
WAS1 05 006

Improvement of Waad Al Shamal Industrial City Fence Gates

Baseline Time Schedule

CONSOLIDATED CONSULTANTS GROUP


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
Improvement of Waad Al Shamal Industrial City Fence & Gates -		7	28-Sep-26	05-Oct-26	0%	100%
Key Milestones		6	28-Sep-26	05-Oct-26	0%	0%
General Milestones		0	05-Oct-26	05-Oct-26	0%	0%
WAD.S.6490	Project Finish	0		05-Oct-26	0%	100%
Contractual Milestones		6	28-Sep-26	05-Oct-26	0%	0%
WAD.S.6250	Completion of Procurment Works	0		28-Sep-26	0%	100%
WAD.S.7560	Testing & Commissioning	0		05-Oct-26	0%	100%
Construction		4	28-Sep-26	01-Oct-26	0%	100%
GUARD HOUSE 1		4	28-Sep-26	01-Oct-26	0%	100%
ELECTRICAL WORKS		4	28-Sep-26	01-Oct-26	0%	100%
ELECTRICAL WORKS - Final Fix		4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6170	12-Port CAT6A UTP fully loaded patch panel	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6420	20A, ATS (Automatic transfer switch) for UPS	2	30-Sep-26	01-Oct-26	0%	100%
WAD.S.6270	Access control panel - Final Fix	2	29-Sep-26	30-Sep-26	0%	100%
WAD.S.6330	Analog addressable fire alarm control panel with battery	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6160	card reader IN/OUT - Final Fix	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6300	CCTV cameras - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6200	CCTV storage system, as specified	4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6280	Central (Headend) System Components	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6180	COMPUTERS AND RELATED PERIPHERALS	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6310	ELECTRICAL GATE BARRIER	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6320	fire alarm system including wires, conduit and other materials - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6150	installation of Wiring devices includes switches and Receptacle outlets	2	28-Sep-26	29-Sep-26	0%	100%
WAD.S.6440	Intelligent Ionization / Photoelectric smoke and heat detector with base	2	30-Sep-26	01-Oct-26	0%	100%
WAD.S.6340	LIGHTING AND POWER TYPE PANELBOARDS - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6430	LIGHTNING PROTECTION	2	30-Sep-26	01-Oct-26	0%	100%
WAD.S.6140	UNDERGROUND DISTRIBUTION SYSTEM - Final Fix	2	28-Sep-26	29-Sep-26	0%	100%
WAD.S.6190	VIDEO SURVEILLANCE	4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6290	VSS System, as specified	3	29-Sep-26	01-Oct-26	0%	100%
DOORS & WINDOWS		3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6120	Install aluminum framed double glazed windows	3	28-Sep-26	30-Sep-26	0%	100%
SPECIALTIES		4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6410	PANEL SIGNAGE	2	30-Sep-26	01-Oct-26	0%	100%
WAD.S.6130	TOILET ACCESSROIES	2	28-Sep-26	29-Sep-26	0%	100%
FURNISHINGS		1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6470	Roller blind	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6480	Waste Receptacle	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6450	Workstation chair	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6460	Workstation table	1	01-Oct-26	01-Oct-26	0%	100%
GUARD HOUSE 2		1	28-Sep-26	28-Sep-26	0%	100%
FURNISHINGS		1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6230	Roller blind	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6240	Waste Receptacle	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6210	Workstation chair	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6220	Workstation table	1	28-Sep-26	28-Sep-26	0%	100%
GUARD HOUSE 3		1	28-Sep-26	28-Sep-26	0%	100%
FURNISHINGS		1	28-Sep-26	28-Sep-26	0%	100%

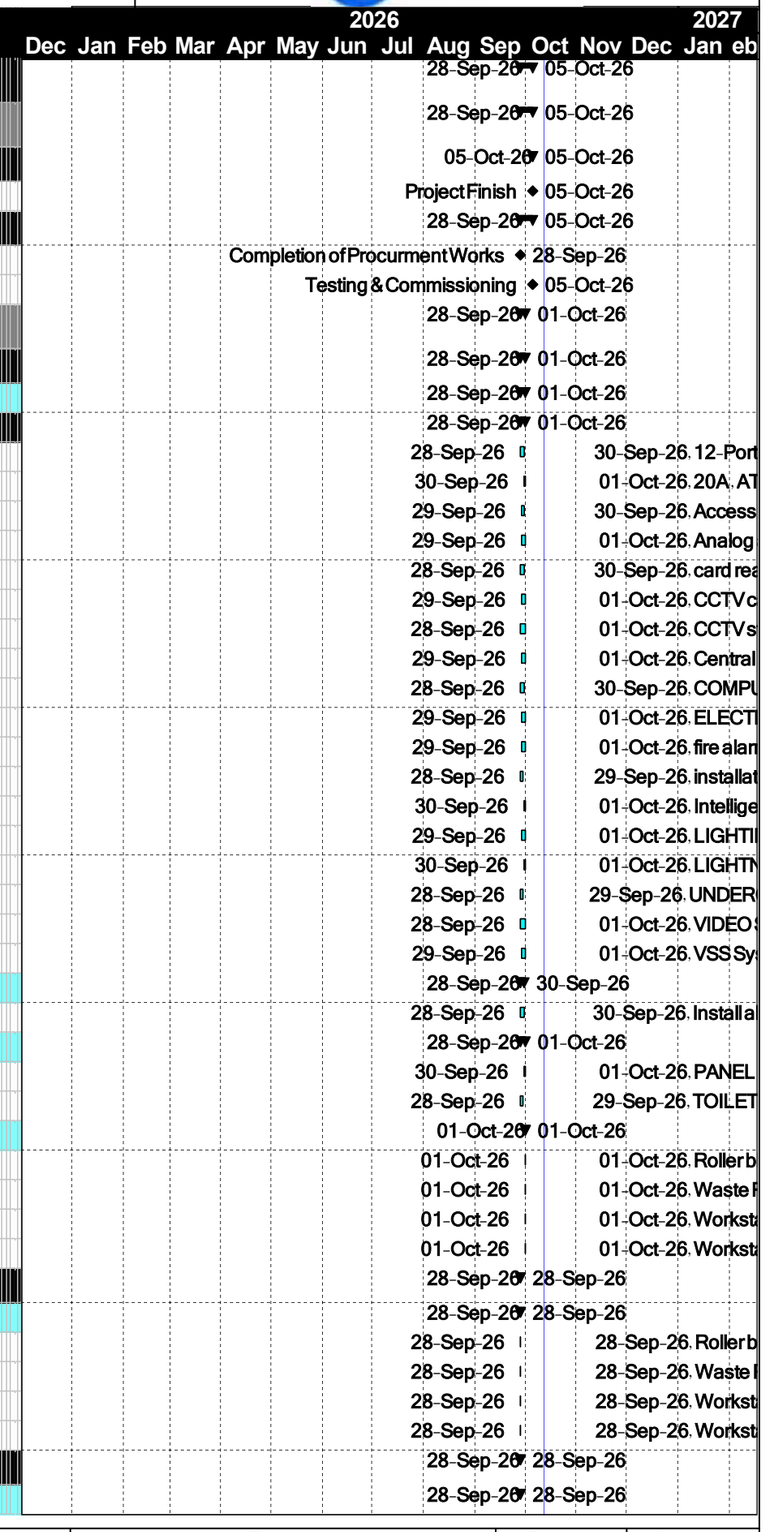

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.6880	Roller blind	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6890	Waste Receptacle	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6860	Workstation chair	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6870	Workstation table	1	28-Sep-26	28-Sep-26	0%	100%
Testing & Commissioning		7	28-Sep-26	05-Oct-26	0%	100%
Engineering		7	28-Sep-26	05-Oct-26	0%	100%
As-Built Drawings		6	28-Sep-26	04-Oct-26	0%	100%
WAD.S.6260	Review & Approve	6	28-Sep-26	04-Oct-26	0%	100%
Operational Spares		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6370	Acceptance	5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6350	Inspection	5	30-Sep-26	05-Oct-26	0%	100%
Warranties and Guarantees		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6360	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
Training and Manuals		5	30-Sep-26	05-Oct-26	0%	100%
Training		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6400	Fabrication & Delivery	5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6380	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
Manuals		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6390	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%

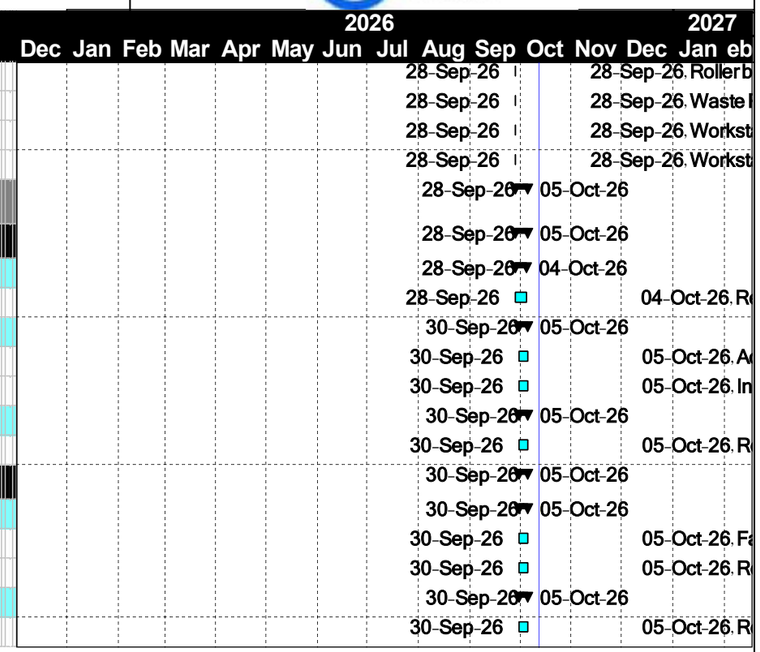

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		
