Development of the Technology City in Dammam

تطوير المناطق التقنية - الدمام

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Ansab Contracting	EGIS	Engr. Afat Elanzey	23-Dec-2025	22-Feb-2027

Scope: collector and local roads, potable water, sewage, storm drainage, irrigation, TSE, medium voltage, street lighting and telecom networks, a sewage pump station, storm drainage ponds, the boundary fence and guard room, and utility buildings, in the 2nd Industrial City in Dammam.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The weekly report (WPR-39) gives 37.09% actual against 68.43% planned in the original baseline and 54.12% in the revised plan. Against last week's report (32.47%) the project gained 4.62% this week.

PHYSICAL % COMPLETE

37.09% / 68.43% plan

▼ SPI 0.54 −31.34% · revised plan 54.12%, SPI 0.69

PROGRESS THIS WEEK

+4.62% / +3.89% plan

▲ 0.73% above the weekly plan

CONTRACT TIME ELAPSED

73.9% · day 315 of 426

▼ Forecast finish 15-Jun-2027

INVOICED TO DATE (GROSS)

11.2% · 7.6M SAR

Last invoice period ends 05-Oct-2026

The forecast delay grew to 113 days.

The weekly report and the P6 update both now forecast completion on 15-Jun-2027, a week later than last week, against the contract date of 22-Feb-2027; the completion milestone has −86 days of float in P6. The networks are moving: sewage, storm drainage and potable water pipes were laid for the first time (331 m, 500 m and 390 m). To finish on 22-Feb-2027 the remaining 62.91% must be done in 15 weeks, about 4.19% a week.

Site photos this week

The four photos added in the WPR-39 upload. The photos carry no date or GPS stamp.
Select a photo to view it larger, then use the arrows to move between photos.



Circular concrete ring

Concrete ring cast around a central sand mound.



Circular concrete ring, second view

The ring from the opposite side, with the formwork removed.



Pipe laying in trench

Large-diameter pipe laid in a deep open trench.



Foundation slab pour

Concrete pumped onto the reinforced slab shown last week.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet of WPR-39.



WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
29-Oct-2026	68.43	32.47	-35.96%	–	0.47
03-Nov-2026	**68.43**	**37.09**	**-31.34%**	**+4.62%**	**0.54**

The table uses the cover sheets of WPR-38 and WPR-39; earlier weeks were not uploaded. Revised plan: 50.23% last week and 54.12% this week. The chart sheet uses the full P6 budget of 151,920 man-hours, so its latest actual is 36.08%, plotted at October. The weekly figure on the cover sheet itself is 2.93% against 3.35% planned; see Data notes.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours. Planned is the revised (P6) plan to date. Source: P6 extract on the Progress sheet of WPR-39.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	20.0%	88.9%	63.3%	-25.5%	0.71	▼ Behind
Sewage network	2.7%	86.8%	17.1%	-69.8%	0.20	▼ Behind
Storm drainage network	6.4%	64.6%	25.6%	-39.0%	0.40	▼ Behind
Potable water network	3.1%	64.7%	11.4%	-53.3%	0.18	▼ Behind
Irrigation network	2.3%	17.7%	0.0%	-17.7%	0.00	▼ Not started
TSE network	1.2%	15.7%	0.0%	-15.7%	0.00	▼ Not started
Medium voltage network	0.6%	1.7%	0.0%	-1.7%	0.00	▼ Not started
Telecom network	1.8%	0.0%	0.0%	0.0%	–	● Not yet due
Street lighting network	2.2%	0.5%	0.0%	-0.5%	0.00	▼ Not started
Roads network	4.8%	66.7%	65.3%	-1.4%	0.98	▼ Slightly behind
Fence and guard room	30.2%	56.7%	38.2%	-18.5%	0.67	▼ Behind
Utility buildings	11.7%	20.8%	28.0%	+7.2%	1.35	▲ Ahead

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Testing & commissioning	10.0%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**52.7%**	**36.1%**	**-16.6%**	**0.69**	▼ Behind

Weights are each phase's share of the 18,990 budgeted man-days in P6. The P6 update (data date 03-Nov-2026) has 873 activities: 344 completed, 71 in progress and 458 not started. Failed-start activities rose from 77 to 84 this week.

Scope of work: quantities

Total, finished and remaining quantity for the items with recorded progress. Network pipe lengths are from the Conclusion sheet of WPR-39; the other items are from its Major Quantities sheet. "This week" is the change since WPR-38.

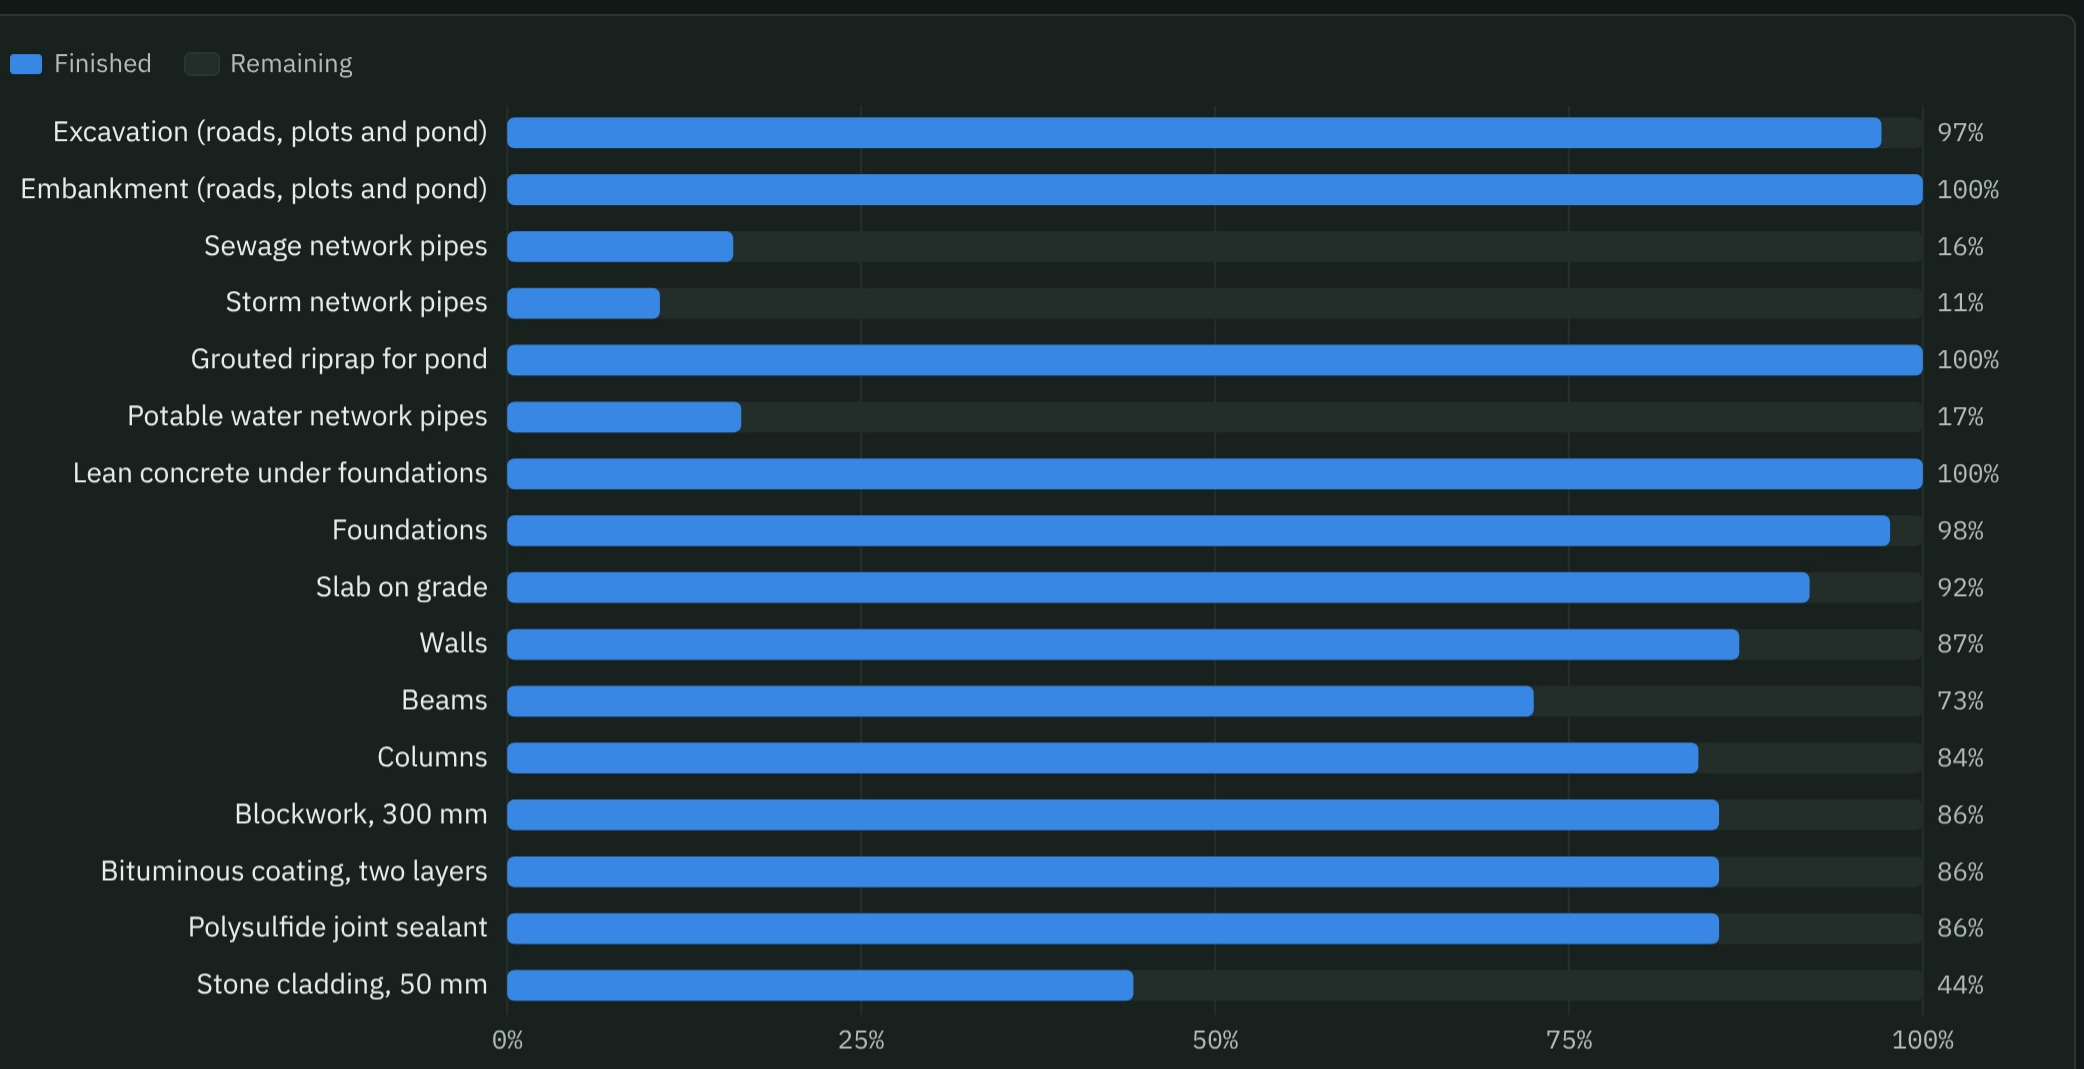

SCOPE ITEM	NETWORK	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation (roads, plots and pond)	Roads	m³	502,417	487,746	+41,861	14,671	97.1%	–
Embankment (roads, plots and pond)	Roads	m³	314,650	314,650	+39,772	0	100.0%	–
Sewage network pipes	Sewage	LM	2,073	331	+331	1,742	16.0%	–
Storm network pipes	Storm drainage	LM	4,635	500	+500	4,135	10.8%	–
Grouted riprap for pond	Storm drainage	m²	3,720	3,720	0	0	100.0%	–
Potable water network pipes	Potable water	LM	2,359	390	+390	1,969	16.5%	–
Lean concrete under foundations	Fence and guard room	m³	1,500	1,500	+138.2	0	100.0%	–
Foundations	Fence and guard room	m³	7,310	7,141	+325	169	97.7%	–
Slab on grade	Fence and guard room	m³	20	18.4	+18.4	1.6	92.0%	–
Walls	Fence and guard room	m³	1,960	1,706	+562.1	254.2	87.0%	–
Beams	Fence and guard room	m³	288	208.8	+88.5	79.2	72.5%	–
Columns	Fence and guard room	m³	372	313	+126.1	59	84.1%	–
Blockwork, 300 mm	Fence and guard room	m²	8,775	7,512	+2,247	1,263	85.6%	–

SCOPE ITEM	NETWORK	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Bituminous coating, two layers	Fence and guard room	m²	39,170	33,532	+10,030	5,638	85.6%	–
Polysulfide joint sealant	Fence and guard room	LM	415	355.3	+106.3	59.7	85.6%	–
Stone cladding, 50 mm	Fence and guard room	m²	14,317	6,333	+6,333	7,984	44.2%	–

First pipe laying on three networks

Sewage (331 m, 16.0%), storm drainage (500 m, 10.8%) and potable water (390 m, 16.5%) pipes appear for the first time. Irrigation, TSE, telecom, medium voltage and street lighting are still at 0.

Earthworks and fence near completion

Embankment is complete and excavation is at 97.1%. Lean concrete is complete, foundations are at 97.7% and the fence walls at 87.0%; stone cladding of the fence has started (44.2%).

Milestones

Baseline and forecast dates from the weekly report; forecast dates and float from the P6 update (data date 03-Nov-2026). Days in brackets are the delay against the baseline.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	23-Dec-2025	23-Dec-2025	23-Dec-2025 (actual)	–	✓ Done
Execution plan and baseline schedule	17-Mar-2026	17-Mar-2026	18-Jan-2026 (actual)	–	✓ Done
Shop drawing and material approvals	13-Apr-2026	13-Apr-2026	21-Aug-2026 (actual)	–	✓ Done late
Mobilisation and site preparation	19-May-2026	19-May-2026	18-Jan-2026 (actual)	–	✓ Done
Storm drainage network	06-Jan-2027	21-Apr-2027 (+105 d)	05-Apr-2027	−66.5	▼ Late
Sewage network	06-Jan-2027	04-Mar-2027 (+57 d)	04-Mar-2027	−33.9	▼ Late
Medium voltage network	07-Mar-2027	02-May-2027 (+56 d)	02-May-2027	−78.5	▼ Late
Street lighting network	18-Mar-2027	06-May-2027 (+49 d)	06-May-2027	−70	▼ Late
Telecom network	18-Mar-2027	10-May-2027 (+53 d)	10-May-2027	−86	▼ Late
Road works	18-Mar-2027	30-May-2027 (+73 d)	30-May-2027	−71.5	▼ Late
Potable water network	22-Mar-2027	27-Apr-2027 (+36 d)	27-Apr-2027	−55.8	▼ Late
Irrigation network	22-Mar-2027	11-Apr-2027 (+20 d)	11-Apr-2027	−42	▼ Late
TSE network	22-Mar-2027	25-Apr-2027 (+34 d)	25-Apr-2027	−53.5	▼ Late
Project completion	22-Feb-2027	15-Jun-2027 (+113 d)	15-Jun-2027	−86	▼ Late

The weekly report and P6 now agree on every milestone except storm drainage.

The weekly report forecasts the storm drainage network on 21-Apr-2027, 16 days after P6 (05-Apr-2027). Sewage moved forward from 01-May-2027 to 04-Mar-2027, while medium voltage, street lighting, telecom and project completion moved later. Telecom and project completion carry the most negative float (−86 days).

Procurement of key materials

Share of total quantity delivered to site. Source: procurement tracker updated 03-Nov-2026, item summary sheet.



Electrical, telecom and irrigation materials: 0% delivered


Purchase orders for MV cables and telecom ducts and manholes are still not issued; the contractor will raise an RFI for MV and links the telecom orders to payment of the invoice. Every tracked item remains behind its baseline delivery date, by 1 to 217 days.

Storm, TSE and potable water deliveries moved

Storm main-line pipes are at 95.8% (4,772 of 4,982 m) and storm manholes complete; TSE pipes at 86.1%, potable water valves at 93.5% and surface boxes complete; storm catch basins rose from 12 to 60 of 195. Fence concrete is still 8,300 of 12,500 m³.

Manpower

Manual head count on site this week by trade, planned vs actual. Source: Manpower sheet of WPR-39.

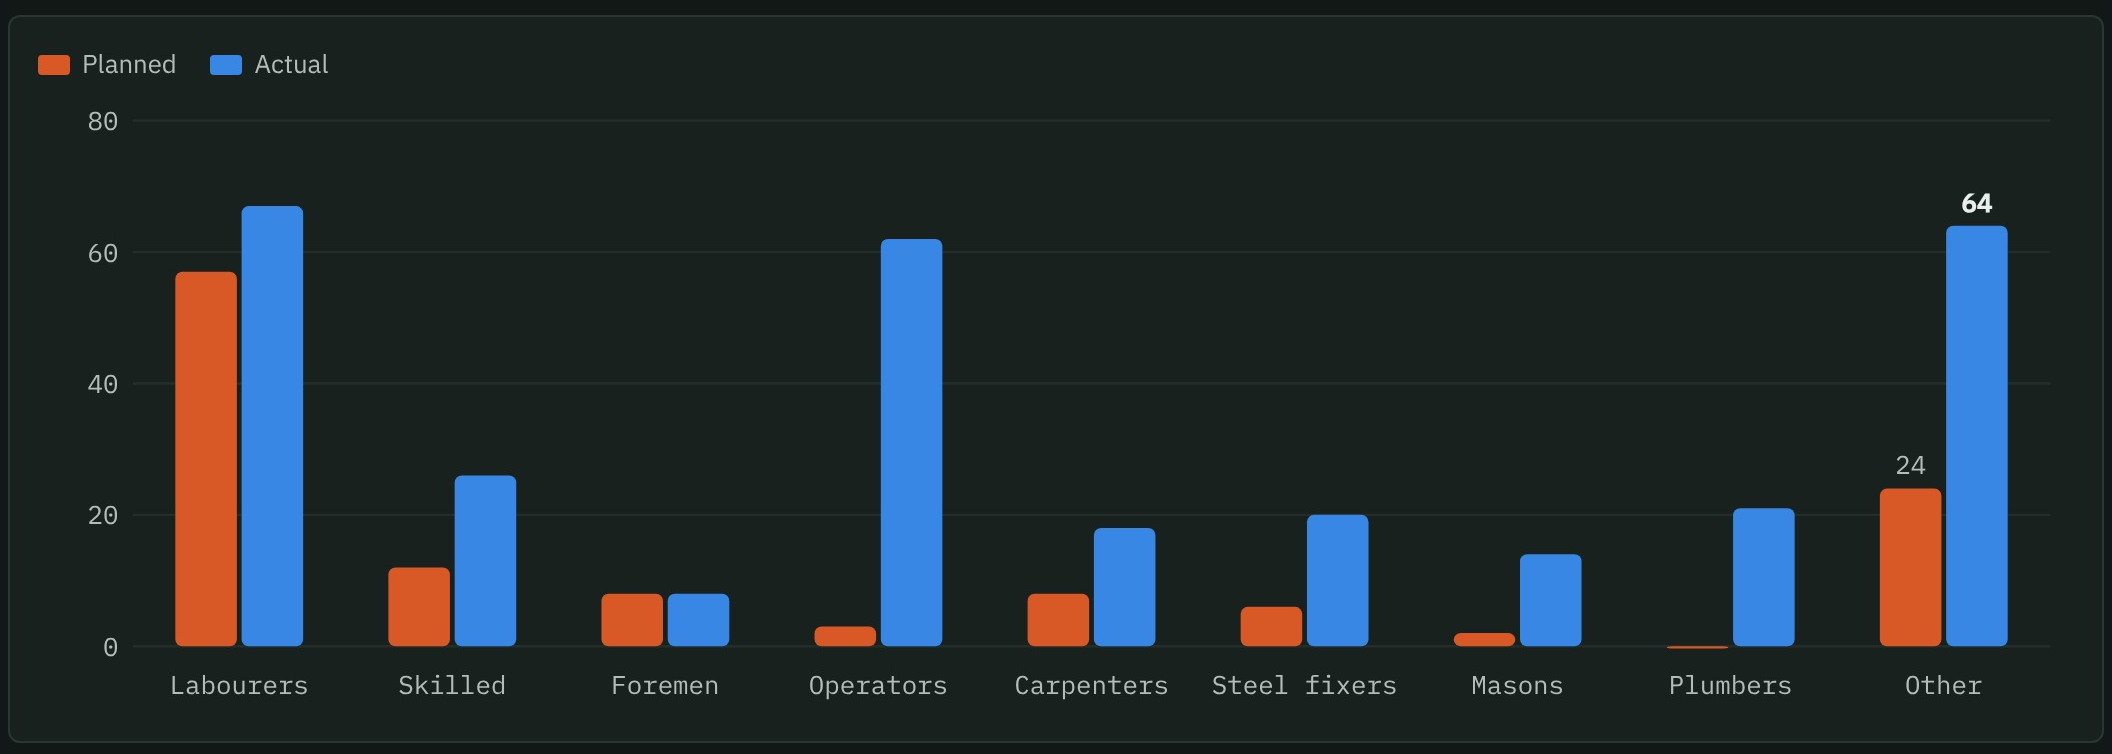

300 manual workers against 120 planned (260 last week), plus 19 staff against 9 planned: 319 in total against 129. Equipment on site: 175 against 117 planned (145 last week), none idle.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	**67,768,369.77**
Contract value incl. 15% VAT	77,933,625.23
Change orders	0
Advance payment (10%)	6,776,836.98

All values in SAR. The value including VAT is from the Conclusion sheet. The change order log is empty.

Invoices

Invoices submitted (invoice log / cover sheet)	3 / 2
Gross value submitted	7,617,509.90
Approved by MODON PM	7,617,509.90
Paid (invoice log / cover sheet)	3,596,613.90 / 0
Retention	0
Deductions and penalties	0

No change from last week. Invoicing is 11.2% of the contract value against 37.09% physical progress. The cover sheet and the invoice log still disagree on the number of invoices and on payments.

Health, safety and quality

Safety Score 0.82

Safe man-hours (cumulative)	222,884
Man-hours this week	18,000
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	1
Toolbox talks (sessions / attendees)	169 / 2,554

Quality Score 0.90

FIRs issued / closed / pending	477 / 390 / 87
MIRs issued / closed / pending	15 / 8 / 7
NCRs issued / closed / open	16 / 15 / 1
Site instructions	0
Method statements approved	8 of 20

QC inspection 03-Nov-2026. 83 FIRs were issued this week.

Open issues and risks

ISSUE	OWNER	DETAIL
Land ownership dispute	MODON	A citizen disputes ownership of the project land. Open since 01-Jan-2026; the police advised the dispute is outside their jurisdiction, and the target date of 20-Apr-2026 has passed.
Late purchase orders	Contractor	Purchase orders are still outstanding (open since 10-Apr-2026), including MV cables, joints and telecom materials.
Late start of the networks	Contractor	Risk 07, score 20. The networks started late and progress slowly while resources focus on the fence; network activities carry about −75 to −84 days of float.
MV consultant and subcontractor	Contractor / Consultant	Risk 08, score 16. MV procurement and works cannot proceed until the specialised MV consultant and subcontractor are approved.
Groundwater	Contractor	Risk 05, score 16. Excavations need continuous dewatering.
Material supply	Contractor	Risk 01, score 15. Late material supply can stop or delay activities.

The issue log and risk register are unchanged from last week. Other open risks: delays in advance and invoice payments, delay or failure of tests, and readiness of existing infrastructure for tie-ins.

Data notes

- Data date: WPR-39, the P6 update, the procurement tracker and the look-ahead are all dated 03-Nov-2026 (a Tuesday), five days after last week's 29-Oct-2026. The Milestones sheet now shows "Contract Weeks 0 of 0", so the week number is (03-Nov-2026 – 23-Dec-2025) ÷ 7 = 315 days, week 45.
- Man-hour total: the cover and Progress sheets still drop Sewage's 516 man-days (total 18,474 instead of 18,990 in P6). With the full budget, physical progress is 36.08%, as on the Physical-Chart Data sheet. The headline uses the reported 37.09%. The P6 update itself gives 6,711.7 earned man-days (35.34%) against 6,852 in the weekly report; the 140 man-day gap is all in procurement.
- This week's gain: the cumulative figure rose by 853 man-days (4.62%), but the cover sheet's weekly column gives 542 earned against 619 planned (2.93% against 3.35%).
- The original-plan figure is unchanged at 68.43% (12,641.76 man-days) for the second week, so the baseline SPI does not move with time. The chart sheet's baseline is 73.84% at the end of October and 85.41% at the end of November.
- The Milestones sheet's "latest plan" dates are now earlier than the baseline for most networks (for example medium voltage 11-Jan-2027 against 07-Mar-2027), and its days-change column is measured against them; the table above measures against the baseline.
- The Conclusion sheet labels cost-based progress as "actual"; it is not used in this report. Its storm network total changed from 5,560 m to 4,635 m and its potable water total from 2,439 m to 2,359 m, and its roads earthworks (637,536 m³) is unchanged from last week against 802,396 m³ on the Major Quantities sheet.
- Quantities: on the Major Quantities sheet the network pipes, manholes, blockwork, bituminous coating and joint sealant are pro-rated (each line in a group carries the same percentage, for example 85.6% for blockwork, coating and sealant), so they are not measured values. Network lengths are taken from the Conclusion sheet instead.
- Procurement tracker: sewage manhole covers fell from 42 of 42 last week to 0 of 42; the fire hydrant total changed from 45 to 18; several expected delivery dates are in December 2027 or in the past (telecom ducts 30-Jan-2026); the fence concrete figure (8,300 m³) and its 30% note are unchanged. The quantity-details sheet was not included this week.
- Safety: "this month" man-hours (9,000) are lower than this week's (18,000). The HSE inspection sheet still carries project ID DAMT-02-001.
- Invoices: the cover sheet shows 2 invoices and 0 paid; the invoice log lists 3 invoices with the first two paid (3,596,613.90 SAR), references DAMT-02-001 and gives a revised contract value of 21,100,000. Unchanged from last week.
- The "major activities this week" list on the photo summary sheet is the same as last week apart from two lines.
- The photos have no date or GPS stamp. Two of the four new photos show the same concrete ring from two sides. The PowerPoint file in the upload could not be opened (damaged archive), and a temporary Excel lock file (~$) was uploaded by mistake.

Compiled 04-Nov-2026 from weekly report WPR-39, the P6 update and the procurement tracker (all dated 03-Nov-2026), with WPR-38 (29-Oct-2026) for the weekly change.
