
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026		285	17-Feb-26	16-Dec-26	17-Feb-26 A	27-Jan-27	25,385,865.43	21,615,212.55	35,709,993.00	71.43%	60.82%	-35
MILESTONES		285	17-Feb-2	16-Dec-26	17-Feb-26 A	27-Jan-27	0.00	0.00	0.00	0%	0%	-35
GENERAL MILESTONES		285	17-Feb-2	16-Dec-26	17-Feb-26 A	27-Jan-27	0.00	0.00	0.00	0%	0%	-35
PG-GN-MS-10	Project Commencement Date	0	17-Feb-2		17-Feb-26 A		0.00	0.00	0.00	100%	100%	0
PG-GN-MS-30	Project Durations(Completed)	101	17-Feb-2	24-Jun-26	17-Feb-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	20-Dec-26	0.00	0.00	0.00	52.88%	50%	1
PG-GN-MS-20	Project Completion Date	0		16-Dec-26		27-Jan-27	0.00	0.00	0.00	0%	0%	0
CONTRACUAL MILESTONES		223	05-May-2	16-Dec-26	05-May-26 A	27-Jan-27	0.00	0.00	0.00	0%	0%	-35
PG-IN-MS-20	Completion of Earthworks (Cut and fill) For Site Layout	0		05-May-26		05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-IN-MS-10	Site Preparation, Work Plans, Schedule ,Drawings Submittals	0		04-Aug-26		16-Sep-26 A	0.00	0.00	0.00	100%	100%	0
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26		17-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-50	Completion of Playground Works	0		07-Dec-26		06-Dec-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-40	Completion of Landscape Works	0		16-Dec-26		20-Jan-27	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-60	Substantial Completion - All Works	0		16-Dec-26		27-Jan-27	0.00	0.00	0.00	0%	0%	0
QASSIM		278	17-Feb-2	16-Dec-26	17-Feb-26 A	19-Jan-27	12,967,898.99	10,799,415.87	17,537,540.00	74.67%	62.19%	-28
MOBILIZATION		29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-MOB-CAM-10	Temporary Underground Utilities works	28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-CAM-20	Temporary Porta-Cabins	21	26-Feb-2	28-Mar-26	26-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-CAM-30	Temporary Toilets	21	26-Feb-2	28-Mar-26	26-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-CAM-40	Temporary Mosque	13	08-Mar-2	28-Mar-26	08-Mar-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
SITE OFFICES		29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-MOB-SO-10	Temporary Underground Utilities works	29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-20	Temporary Porta-Cabins	22	26-Feb-2	29-Mar-26	26-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-30	Temporary Toilets	22	26-Feb-2	29-Mar-26	26-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-40	Temporary Mosque	16	05-Mar-2	29-Mar-26	05-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-50	Car Parking Area	10	12-Mar-2	29-Mar-26	12-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
GENERAL REQUIEREMENTS		57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-GEN-20	HSSE Submission Plan	57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-GEN-30	Surveying report Submission Plan	57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-GEN-40	Baseline Submission	6	28-Feb-2	07-Mar-26	28-Feb-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-GEN-10	QA/QC Submission Plan	16	12-Mar-2	04-Apr-26	12-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	100%	100%	0
ENGINEERING		199	17-Feb-2	16-Aug-26	17-Feb-26 A	18-Oct-26	526,126.20	525,770.51	526,126.20	100%	99.93%	-53
SHOP DRAWINGS SUBMITTALS		168	17-Feb-2	04-Aug-26	17-Feb-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-45
STRUCTURAL DRAWINGS		125	17-Feb-2	06-Jul-26	17-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	-4
PROJECT FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-10	Excavation Drawings	19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-20	Foundation Drawings	19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-30	Excavation Drawings	19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-40	Foundation Drawings	19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		10	25-Jun-26	06-Jul-26	01-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	1
PG-Q-EN-ST-SD-SB-50	Excavation Drawings	8	25-Jun-26	04-Jul-26	01-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%	6
PG-Q-EN-ST-SD-SB-60	Foundation Drawings	10	25-Jun-26	06-Jul-26	07-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	100%	100%	6
TOILET BUILDING		43	17-Feb-2	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-70	Excavation Drawings	43	17-Feb-2	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-80	Foundation Drawings	41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-90	Excavation Drawings	41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-100	Foundation Drawings	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		13	28-Apr-26	13-May-26	28-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-110	Reinforcement Detail Drawings	13	28-Apr-26	13-May-26	28-Apr-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-120	Concrete Detail Drawings	13	28-Apr-26	13-May-26	28-Apr-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		158	19-Feb-2	23-Jul-26	19-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
TOILET BUILDING		42	19-Feb-2	15-Apr-26	19-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-AR-SD-SB-10	Ground Floor Plan	40	19-Feb-2	13-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-20	Roof Floor Plan	37	25-Feb-2	14-Apr-26	25-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-50	Floor Finish Layout	36	25-Feb-2	13-Apr-26	25-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-60	Reflected Ceiling Layout	37	25-Feb-2	13-Apr-26	25-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-70	Enlarged Toilets Layout	38	25-Feb-2	15-Apr-26	25-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-30	Elevations	34	01-Mar-2	14-Apr-26	01-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-80	Doors & Windows Schedule	35	01-Mar-2	15-Apr-26	01-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-90	Aluminum Work	35	01-Mar-2	15-Apr-26	01-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-100	Cladding Details	34	01-Mar-2	14-Apr-26	01-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-40	Sections	32	03-Mar-2	13-Apr-26	03-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-9
PG-Q-EN-AR-SD-SB-110	Membrane & Insulation Details	15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-9
PG-Q-EN-AR-SD-SB-120	Steel Cable System	15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-9
PG-Q-EN-AR-SD-SB-130	Doors & Access Sytem Drawings	15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-9
LANDSCAPE DRAWINGS		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-LS-SD-SB-10	Hardscape Layout Plan	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-20	Interlock Tile Details	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-30	Stamped Concrete Pattern & Section	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0

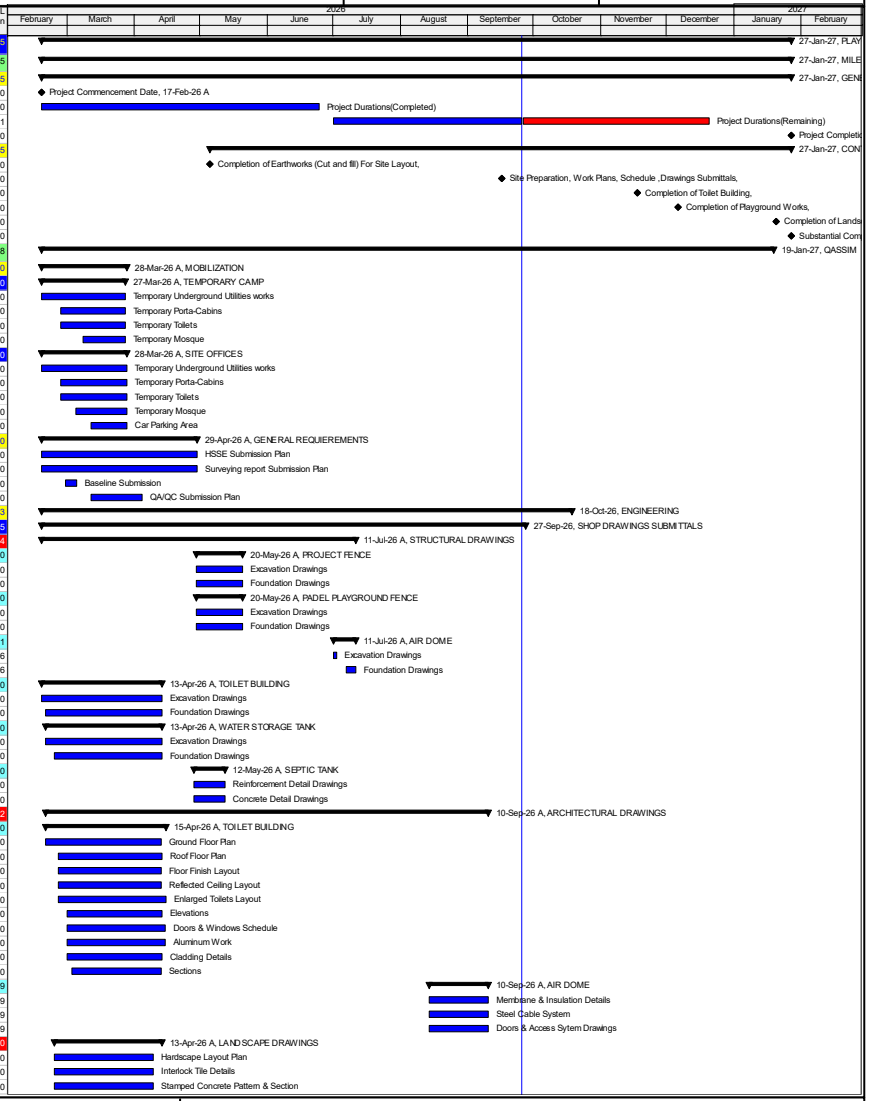


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-EN-LS-SD-SB-40	Tartan Flooring Layout & Details	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-50	Bike Path Layout & Details	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-60	Walking Path layout & Details	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-70	Tree Planting Plan & Details	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-80	Traffic Sign Location & Details	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-90	Football Playground Layout	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-100	Padel Playground Layout	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-110	Basketball Playground Layout	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-120	Playground Details	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-130	Padel Fence Elevation & Details	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		143	28-Feb-2	15-Jul-26	28-Feb-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-62
WATER SUPPLY SYSTEM		32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-SB-20	Pump Room Layout	32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-10	Cold & Hot Water Piping Layout	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-30	Booster Pump Details	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-40	GRP Water Tank Details	24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-SB-50	Drainage Layout	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-60	Floor Drains & Cleanouts Details	24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-70	Inspection Chamber Details	21	12-Mar-2	11-Apr-26	12-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-SB-80	HDPE Pipe Routing	24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-90	Irrigation Network Layout	21	12-Mar-2	11-Apr-26	12-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-32
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	100%	90%	-32
ELECTRICAL DRAWINGS		102	11-May-2	04-Aug-26	11-May-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-45
POWER AND LIGHTING SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-SB-10	Main Distribution Board (MDB) Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-20	Pump Room Power Panel	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-30	Street Lighting Power Panel	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-40	Site Lighting Pole Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-SB-50	Telecom & Data Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-60	CCTV Camera Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-70	Access Control Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-80	AV System Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-SB-90	Fire Alarm Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-100	Detector & Manual Call Point Details	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-110	Control Panel Wiring Diagram	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-33
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	26-Sep-26	0.00	0.00	0.00	100%	90%	-39
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	100%	90%	-35
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	100%	90%	-33
SHOP DRAWINGS APPROVALS		172	19-Feb-2	16-Aug-26	19-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
STRUCTURAL DRAWINGS		130	19-Feb-2	14-Jul-26	19-Feb-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	2
PROJECT FENCE		7	13-May-2	21-May-26	13-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-10	Excavation Drawings	7	13-May-2	21-May-26	13-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-20	Foundation Drawings	7	13-May-2	21-May-26	13-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		9	11-May-2	21-May-26	11-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-30	Excavation Drawings	9	11-May-2	21-May-26	11-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-40	Foundation Drawings	9	11-May-2	21-May-26	11-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		9	05-Jul-26	14-Jul-26	06-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	3
PG-Q-EN-ST-SD-AP-50	Excavation Drawings	4	05-Jul-26	08-Jul-26	06-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	100%	100%	2
PG-Q-EN-ST-SD-AP-60	Foundation Drawings	7	07-Jul-26	14-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	100%	100%	3
TOILET BUILDING		44	19-Feb-2	18-Apr-26	19-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-70	Excavation Drawings	44	19-Feb-2	18-Apr-26	19-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-80	Foundation Drawings	36	02-Mar-2	18-Apr-26	02-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-90	Excavation Drawings	42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-100	Foundation Drawings	34	04-Mar-2	18-Apr-26	04-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		3	11-May-2	14-May-26	11-May-26 A	13-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-110	Reinforcement Detail Drawings	3	11-May-2	14-May-26	11-May-26 A	13-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-120	Concrete Detail Drawings	3	11-May-2	14-May-26	11-May-26 A	13-May-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		166	25-Feb-2	01-Aug-26	25-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
TOILET BUILDING		40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-AR-SD-AP-10	Ground Floor Plan	40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-20	Roof Floor Plan	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-50	Floor Finish Layout	35	03-Mar-2	18-Apr-26	03-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-60	Reflected Ceiling Layout	35	03-Mar-2	18-Apr-26	03-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-70	Enlarged Toilets Layout	35	03-Mar-2	18-Apr-26	03-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-30	Elevations	34	04-Mar-2	18-Apr-26	04-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-80	Doors & Windows Schedule	34	04-Mar-2	18-Apr-26	04-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0

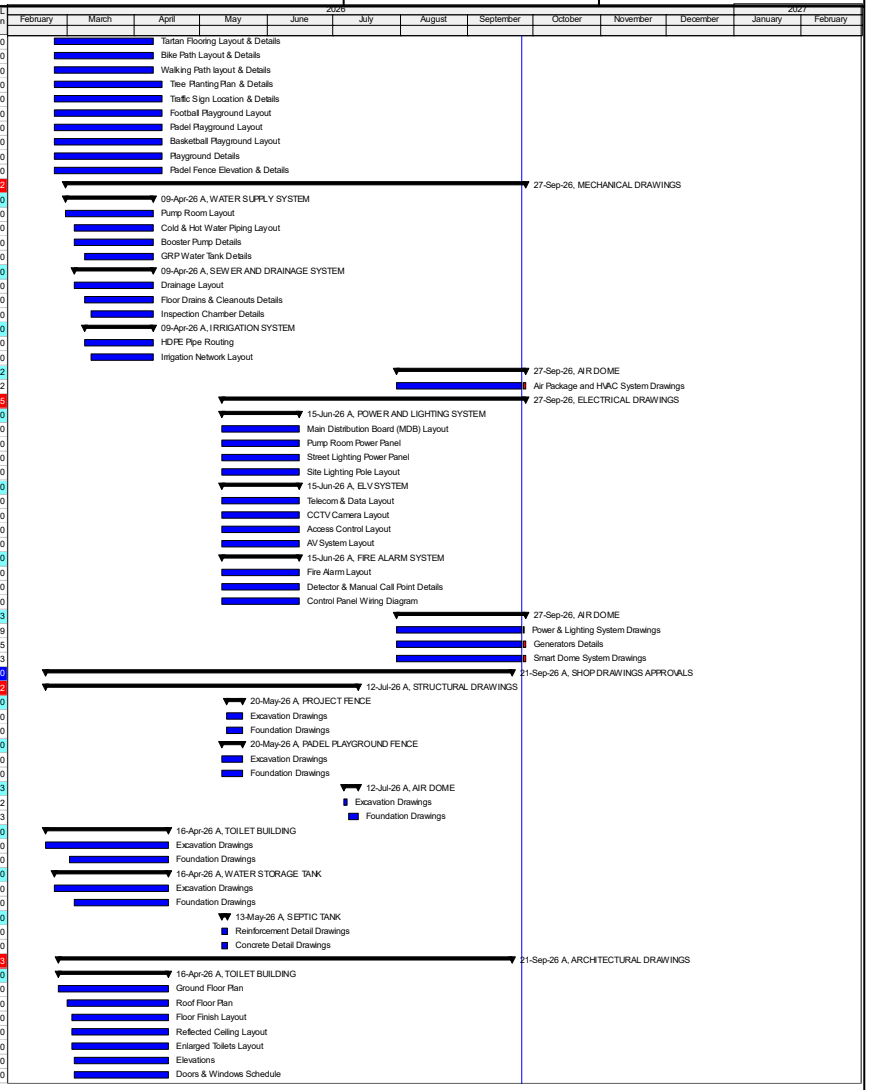


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-EN-AR-SD-AP-90	Aluminum Work	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-100	Cladding Details	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-40	Sections	31	08-Mar-2	18-Apr-26	08-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-20
PG-Q-EN-AR-SD-AP-110	Membrane & Insulation Details	7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-20
PG-Q-EN-AR-SD-AP-120	Steel Cable System	7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-20
PG-Q-EN-AR-SD-AP-130	Doors & Access Sytem Drawings	7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-20
LANDSCAPE DRAWINGS		39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-LS-SD-AP-50	Bike Path Layout & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-60	Walking Path layout & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-80	Tsaffic Sign Location & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-130	Padel Fence Elevation & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-10	Hardscape Layout Plan	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-40	Tartan Flooring Layout & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-70	Tree Planting Plan & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-90	Football Playground Layout	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-100	Padel Playground Layout	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-110	Basketball Playground Layout	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-120	Playground Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-20	Interlock Tile Details	28	11-Mar-2	18-Apr-26	11-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-30	Stamped Concrete Pattern & Section	18	28-Mar-2	18-Apr-26	28-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		154	09-Mar-2	27-Jul-26	09-Mar-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
WATER SUPPLY SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-AP-10	Cold & Hot Water Piping Layout	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-30	Booster Pump Details	26	10-Mar-2	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-40	GRP Water Tank Details	22	14-Mar-2	13-Apr-26	14-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-20	Pump Room Layout	21	16-Mar-2	14-Apr-26	16-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-AP-50	Drainage Layout	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-60	Floor Drains & Cleanouts Details	21	16-Mar-2	14-Apr-26	16-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-70	Inspection Chamber Details	21	16-Mar-2	14-Apr-26	16-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		24	12-Mar-2	14-Apr-26	12-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-AP-80	HDPE Pipe Routing	24	12-Mar-2	14-Apr-26	12-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-90	Irrigation Network Layout	20	17-Mar-2	14-Apr-26	17-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		10	16-Jul-26	27-Jul-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
PG-Q-EN-ME-SD-AP-100	Air Package and HVAC System Drawings	10	16-Jul-26	27-Jul-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-17
ELECTRICAL DRAWINGS		100	20-May-2	16-Aug-26	20-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
POWER AND LIGHTING SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-AP-10	Main Distribution Board (MDB) Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-20	Pump Room Power Panel	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-30	Street Lighting Power Panel	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-40	Site Lighting Pole Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-AP-50	Telecom & Data Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-60	CCTV Camera Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-70	Access Control Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-80	AV System Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-AP-90	Fire Alarm Layout	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-100	Detector & Manual Call Point Details	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-110	Control Panel Wiring Diagram	20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		17	28-Jul-26	16-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-10
PG-Q-EN-EL-SD-AP-120	Power & Lighting System Drawings	17	28-Jul-26	16-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-EN-EL-SD-AP-130	Generators Details	8	03-Aug-2	11-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-19
PG-Q-EN-EL-SD-AP-140	Smart Dome System Drawings	6	05-Aug-2	11-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-21
MATERIAL SUBMITTALS		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
LONG LEAD ITEMS		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
EXTERNAL / LANDSCAPE WORK		56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-LS-MS-20	Benches, Seats (Rectangular & Circular)	56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MS-30	Fence, gates and accessories	49	05-Mar-2	06-May-26	05-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MS-10	Bike and Walk Path Materials	49	05-Mar-2	06-May-26	05-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
PG-Q-PR-LL-SPMS-50	Air Dome Materials(Completed)	101	17-Feb-2	25-Jun-26	17-Feb-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-40	Tartan Floor	48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-50_R	Air Dome Materials(Remaining)	19	25-Jun-26	16-Jul-26	30-Jun-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%	-26
CONCRETE WORK		43	04-Mar-2	28-Apr-26	04-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-CO-MS-10	Autoclaved Aerated Panel	43	04-Mar-2	28-Apr-26	04-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MS-10	Metal Doors	47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-MS-20	Curtain Wall	47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0

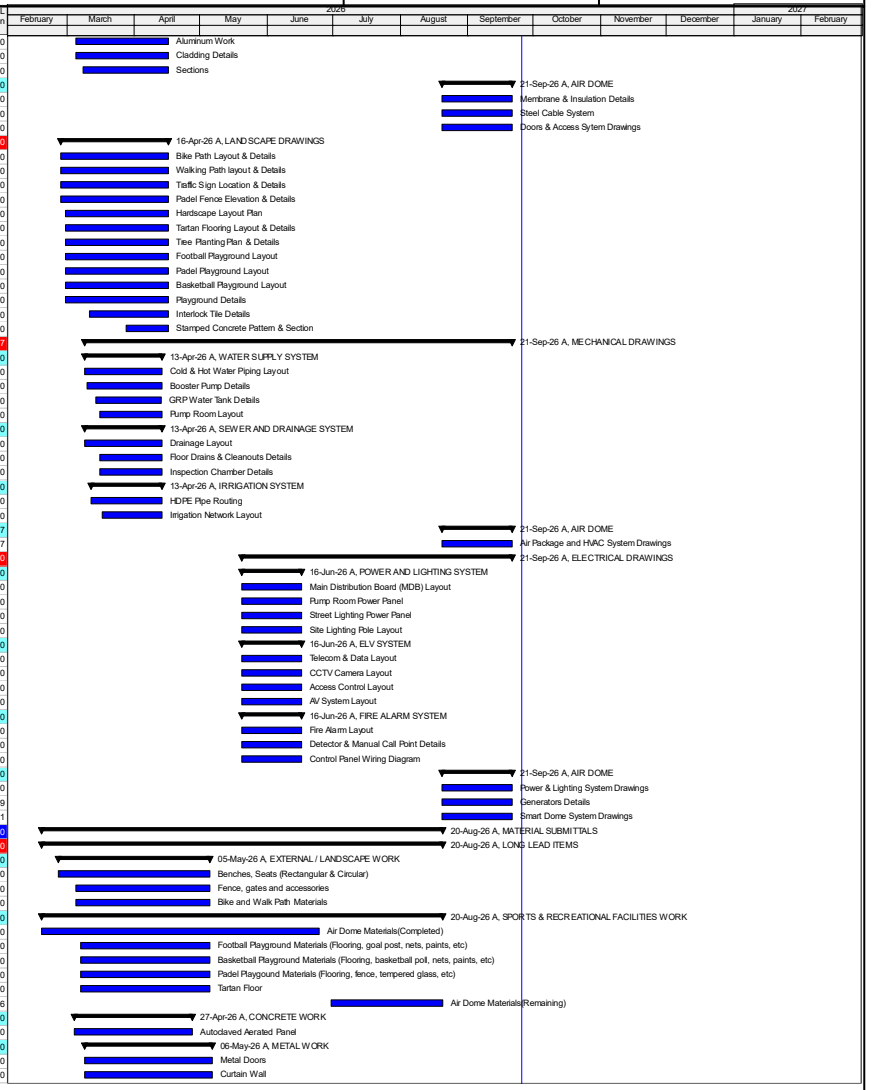


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLUMBING WORK		46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-PB-MS-10	Booster Pump	46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-MS-20	GRP Sectional Panel Water Tanks (4x3x3m)	42	15-Mar-2	07-May-26	15-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-IR-MS-10	HDPE Pipes	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-MS-20	Irrigation Control System	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-EL-MS-10	Main Distribution Board	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-20	Power Panels (Pump, Street Light)	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-30	Site Lighting Poles	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-40	Lighting Fixtures	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-50	Grounding System Materials (Earth pit rod, LPS, etc)	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-70	Security and Access Control System Materials	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-80	Fire Alarm System Materials	26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
SHORT LEAD ITEMS		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-LS-MS-10	Backfilling Materials	23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-30	Compacted Natural Ground Soil	20	21-Feb-2	17-Mar-26	21-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-20	Interlock tiles	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-40	Curb Stone	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-50	Thermoplastic pavement road marking	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-60	Traffic Signages	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-70	Trees	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-80	Lawn	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-CO-MS-10	Steel Rebar	17	17-Feb-2	10-Mar-26	17-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-20	Concrete	13	23-Feb-2	10-Mar-26	23-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-40	CMU Block	19	01-Mar-2	28-Mar-26	01-Mar-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-50	Concrete Repair & Protection Materials	19	01-Mar-2	28-Mar-26	01-Mar-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-30	Screed	9	12-Mar-2	28-Mar-26	12-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		18	21-Feb-2	15-Mar-26	21-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AR-MS-40	Cement Plaster	18	21-Feb-2	15-Mar-26	21-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-50	Acrylic Paint	15	25-Feb-2	15-Mar-26	25-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-80	Phenolic Partition	10	03-Mar-2	15-Mar-26	03-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-90	Glass Partition	10	03-Mar-2	15-Mar-26	03-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-10	Ceramic tiles	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-20	Anti-slip Granite tiles	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-30	Epoxy Paint	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-60	Stone Cladding	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-70	Aluminum Plates	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-100	Gypsum Boards	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-120	Waterproofing System Materials	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-MT-MS-20	Galvanized Steel Roof Scupper	11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-MS-30	Galvanized Steel Cover with frame	11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-MS-10	Galvanized Steel Ladder	8	08-Mar-2	17-Mar-26	08-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AC-MS-10	Split Air Conditioning Unit	19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-MS-20	Air Duct	15	28-Feb-2	17-Mar-26	28-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-MS-30	Diffusers and Grills	11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-MS-40	Exhaust fans	11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-PB-MS-10	PPR Pipes & Valves	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-MS-20	UPCV Pipes	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-MS-30	Sanitary Drainage Fixtures	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		17	25-Feb-2	17-Mar-26	25-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-IR-MS-10	Gate Valve including valve box	17	25-Feb-2	17-Mar-26	25-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-IR-MS-20	Bubblers and Sprayers	12	03-Mar-2	17-Mar-26	03-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-EL-MS-10	Wiring Devices Materials	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-FF-MS-10	Fire Extinguishers	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
MATERIAL APPROVALS		196	21-Feb-2	18-Jul-26	21-Feb-26 A	18-Oct-26	526,126.20	525,770.51	526,126.20	100%	99.93%	-78
LONG LEAD ITEMS		189	02-Mar-2	18-Jul-26	02-Mar-26 A	18-Oct-26	358,885.26	358,529.57	358,885.26	100%	99.9%	-78
EXTERNAL / LANDSCAPE WORK		2	11-May-2	12-May-26	11-May-26 A	12-May-26 A	19,812.18	19,812.18	19,812.18	100%	100%	0
PG-Q-PR-LL-LS-MA-20	Benches, Seats (Rectangular & Circular)	2	11-May-2	12-May-26	11-May-26 A	12-May-26 A	4,007.97	4,007.97	4,007.97	100%	100%	0
PG-Q-PR-LL-LS-MA-30	Fence, gates and accessories	2	11-May-2	12-May-26	11-May-26 A	12-May-26 A	2,529.21	2,529.21	2,529.21	100%	100%	0
PG-Q-PR-LL-LS-MA-10	Bike and Walk Path Materials	2	11-May-2	12-May-26	11-May-26 A	12-May-26 A	13,275.00	13,275.00	13,275.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		110	02-Mar-2	30-Jun-26	02-Mar-26 A	19-Sep-26 A	273,522.54	273,522.54	273,522.54	100%	100%	-69
PG-Q-PR-LL-SP-MA-50	Air Dome Materials(Completed)	91	02-Mar-2	24-Jun-26	02-Mar-26 A	24-Jun-26 A	62,622.07	62,622.07	62,622.07	100%	100%	0
PG-Q-PR-LL-SP-MA-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	8	12-May-2	20-May-26	12-May-26 A	20-May-26 A	13,051.50	13,051.50	13,051.50	100%	100%	0

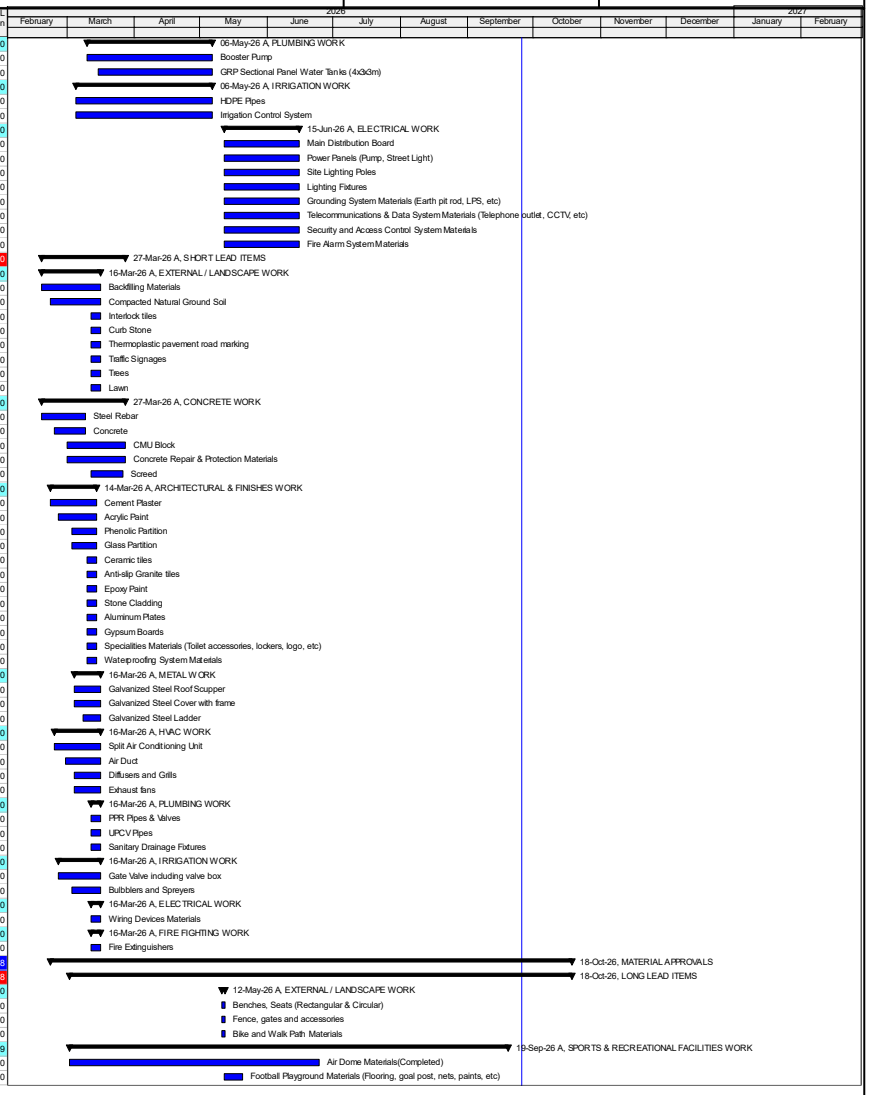


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-SP-MA-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	8	12-May-26	20-May-26	12-May-26 A	20-May-26 A	2,256.00	2,256.00	2,256.00	100%	100%	0
PG-Q-PR-LL-SP-MA-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	8	12-May-26	20-May-26	12-May-26 A	20-May-26 A	5,950.80	5,950.80	5,950.80	100%	100%	0
PG-Q-PR-LL-SP-MA-40	Tartan Floor	8	12-May-26	20-May-26	12-May-26 A	20-May-26 A	43,524.00	43,524.00	43,524.00	100%	100%	0
PG-Q-PR-LL-SP-MA-50_R	Air Dome Materials(Remaining)	5	25-Jun-26	30-Jun-26	02-Jul-26 A	19-Sep-26 A	146,118.17	146,118.17	146,118.17	100%	100%	-63
CONCRETE WORK		40	09-Mar-26	28-Apr-26	09-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
PG-Q-PR-LL-CO-MA-10	Autoclaved Aerated Panel	40	09-Mar-26	28-Apr-26	09-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		112	09-Jun-26	18-Jul-26	09-Jun-26 A	18-Oct-26	889.23	533.54	889.23	100%	60%	-78
PG-Q-PR-LL-MT-MA-10	Metal Doors(Completed)	14	09-Jun-26	24-Jun-26	09-Jun-26 A	24-Jun-26 A	76.52	76.52	76.52	100%	100%	0
PG-Q-PR-LL-MT-MA-20	Curtain Wall(Completed)	14	09-Jun-26	24-Jun-26	09-Jun-26 A	24-Jun-26 A	457.02	457.02	457.02	100%	100%	0
PG-Q-PR-LL-MT-MA-10_R	Metal Doors(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26	12-Oct-26	51.01	0.00	51.01	100%	0%	0
PG-Q-PR-LL-MT-MA-20_R	Curtain Wall(Remaining)	20	25-Jun-26	18-Jul-26	26-Sep-26	18-Oct-26	304.68	0.00	304.68	100%	0%	0
PLUMBING WORK		48	09-Jun-26	18-Jul-26	20-May-26 A	24-Jun-26 A	3,553.95	3,553.95	3,553.95	100%	100%	7
PG-Q-PR-LL-PB-MA-10	Booster Pump(Completed)	14	09-Jun-26	24-Jun-26	09-Jun-26 A	24-Jun-26 A	1,090.98	1,090.98	1,090.98	100%	100%	0
PG-Q-PR-LL-PB-MA-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	14	09-Jun-26	24-Jun-26	09-Jun-26 A	24-Jun-26 A	1,041.39	1,041.39	1,041.39	100%	100%	0
PG-Q-PR-LL-PB-MA-10_R	Booster Pump(Remaining)	20	25-Jun-26	18-Jul-26	20-May-26 A	21-May-26 A	727.32	727.32	727.32	100%	100%	18
PG-Q-PR-LL-PB-MA-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jun-26	12-Jul-26	03-Jun-26 A	06-Jun-26 A	694.26	694.26	694.26	100%	100%	12
IRRIGATION WORK		45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	24,486.75	24,486.75	24,486.75	100%	100%	0
PG-Q-PR-LL-IR-MA-10	HDPE Pipes	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	19,941.00	19,941.00	19,941.00	100%	100%	0
PG-Q-PR-LL-IR-MA-20	Irrigation Control System	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	4,545.75	4,545.75	4,545.75	100%	100%	0
ELECTRICAL WORK		96	12-May-26	02-Jul-26	12-May-26 A	16-Sep-26 A	35,203.11	35,203.11	35,203.11	100%	100%	-64
PG-Q-PR-LL-EL-MA-10	Main Distribution Board(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	297.54	297.54	297.54	100%	100%	0
PG-Q-PR-LL-EL-MA-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	238.03	238.03	238.03	100%	100%	0
PG-Q-PR-LL-EL-MA-30	Site Lighting Poles(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	17,405.28	17,405.28	17,405.28	100%	100%	0
PG-Q-PR-LL-EL-MA-40	Lighting Fixtures(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	769.70	769.70	769.70	100%	100%	0
PG-Q-PR-LL-EL-MA-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	602.51	602.51	602.51	100%	100%	0
PG-Q-PR-LL-EL-MA-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	587.63	587.63	587.63	100%	100%	0
PG-Q-PR-LL-EL-MA-70	Security and Access Control System Materials(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	743.94	743.94	743.94	100%	100%	0
PG-Q-PR-LL-EL-MA-80	Fire Alarm System Materials(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	477.23	477.23	477.23	100%	100%	0
PG-Q-PR-LL-EL-MA-10_R	Main Distribution Board(Remaining)	7	25-Jun-26	02-Jul-26	30-Jul-26 A	16-Sep-26 A	198.36	198.36	198.36	100%	100%	-34
PG-Q-PR-LL-EL-MA-20_R	Power Panels (Pump, Street Light)(Remaining)	7	25-Jun-26	02-Jul-26	30-Jul-26 A	16-Sep-26 A	158.69	158.69	158.69	100%	100%	-34
PG-Q-PR-LL-EL-MA-30_R	Site Lighting Poles(Remaining)	7	25-Jun-26	02-Jul-26	30-Jul-26 A	16-Sep-26 A	11,603.52	11,603.52	11,603.52	100%	100%	-34
PG-Q-PR-LL-EL-MA-40_R	Lighting Fixtures(Remaining)	7	25-Jun-26	02-Jul-26	12-Jul-26 A	23-Jul-26 A	513.13	513.13	513.13	100%	100%	-4
PG-Q-PR-LL-EL-MA-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	7	25-Jun-26	02-Jul-26	30-Jul-26 A	16-Sep-26 A	401.68	401.68	401.68	100%	100%	-34
PG-Q-PR-LL-EL-MA-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	7	25-Jun-26	02-Jul-26	30-Jul-26 A	16-Sep-26 A	391.75	391.75	391.75	100%	100%	-34
PG-Q-PR-LL-EL-MA-70_R	Security and Access Control System Materials(Remaining)	7	25-Jun-26	02-Jul-26	27-Aug-26 A	16-Sep-26 A	495.96	495.96	495.96	100%	100%	-10
PG-Q-PR-LL-EL-MA-80_R	Fire Alarm System Materials(Remaining)	7	25-Jun-26	02-Jul-26	27-Aug-26 A	16-Sep-26 A	318.16	318.16	318.16	100%	100%	-10
SHORT LEAD ITEMS		25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	167,240.94	167,240.94	167,240.94	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	139,867.29	139,867.29	139,867.29	100%	100%	0
PG-Q-PR-SL-LS-MA-10	Backfilling Materials	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	36,450.00	36,450.00	36,450.00	100%	100%	0
PG-Q-PR-SL-LS-MA-30	Compacted Natural Ground Soil	22	25-Feb-26	26-Mar-26	25-Feb-26 A	26-Mar-26 A	8,580.00	8,580.00	8,580.00	100%	100%	0
PG-Q-PR-SL-LS-MA-20	Interlock tiles	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	29,832.00	29,832.00	29,832.00	100%	100%	0
PG-Q-PR-SL-LS-MA-40	Curb Stone	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	43,185.00	43,185.00	43,185.00	100%	100%	0
PG-Q-PR-SL-LS-MA-50	Thermoplastic pavement road marking	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	525.63	525.63	525.63	100%	100%	0
PG-Q-PR-SL-LS-MA-60	Traffic Signages	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	198.36	198.36	198.36	100%	100%	0
PG-Q-PR-SL-LS-MA-70	Trees	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	9,546.30	9,546.30	9,546.30	100%	100%	0
PG-Q-PR-SL-LS-MA-80	Lawn	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	11,550.00	11,550.00	11,550.00	100%	100%	0
CONCRETE WORK		24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
PG-Q-PR-SL-CO-MA-10	Steel Rebar	14	23-Feb-26	10-Mar-26	23-Feb-26 A	10-Mar-26 A	476.82	476.82	476.82	100%	100%	0
PG-Q-PR-SL-CO-MA-20	Concrete	9	01-Mar-26	10-Mar-26	01-Mar-26 A	10-Mar-26 A	518.85	518.85	518.85	100%	100%	0
PG-Q-PR-SL-CO-MA-40	CMU Block	15	05-Mar-26	26-Mar-26	05-Mar-26 A	26-Mar-26 A	124.20	124.20	124.20	100%	100%	0
PG-Q-PR-SL-CO-MA-50	Concrete Repair & Protection Materials	15	05-Mar-26	26-Mar-26	05-Mar-26 A	26-Mar-26 A	372.00	372.00	372.00	100%	100%	0
PG-Q-PR-SL-CO-MA-30	Screed	1	26-Mar-26	26-Mar-26	26-Mar-26 A	26-Mar-26 A	117.60	117.60	117.60	100%	100%	0
ARCHITECTURAL & FINISHES WORK		17	25-Feb-26	16-Mar-26	25-Feb-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
PG-Q-PR-SL-AR-MA-40	Cement Plaster	17	25-Feb-26	16-Mar-26	25-Feb-26 A	16-Mar-26 A	221.37	221.37	221.37	100%	100%	0
PG-Q-PR-SL-AR-MA-50	Acrylic Paint	14	01-Mar-26	16-Mar-26	01-Mar-26 A	16-Mar-26 A	147.90	147.90	147.90	100%	100%	0
PG-Q-PR-SL-AR-MA-10	Ceramic tiles	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	571.95	571.95	571.95	100%	100%	0
PG-Q-PR-SL-AR-MA-20	Anti-slip Granite tiles	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	535.50	535.50	535.50	100%	100%	0
PG-Q-PR-SL-AR-MA-30	Epoxy Paint	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	111.18	111.18	111.18	100%	100%	0
PG-Q-PR-SL-AR-MA-60	Stone Cladding	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	1,852.20	1,852.20	1,852.20	100%	100%	0
PG-Q-PR-SL-AR-MA-70	Aluminum Plates	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MA-80	Phenolic Partition	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	1,340.40	1,340.40	1,340.40	100%	100%	0
PG-Q-PR-SL-AR-MA-90	Glass Partition	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	155.40	155.40	155.40	100%	100%	0
PG-Q-PR-SL-AR-MA-100	Gypsum Boards	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	188.58	188.58	188.58	100%	100%	0
PG-Q-PR-SL-AR-MA-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	2,262.87	2,262.87	2,262.87	100%	100%	0
PG-Q-PR-SL-AR-MA-120	Waterproofing System Materials	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	544.20	544.20	544.20	100%	100%	0
METAL WORK		12	09-Mar-26	26-Mar-26	09-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
PG-Q-PR-SL-MT-MA-20	Galvanized Steel Roof Scupper	12	09-Mar-26	26-Mar-26	09-Mar-26 A	26-Mar-26 A	31.32	31.32	31.32	100%	100%	0
PG-Q-PR-SL-MT-MA-30	Galvanized Steel Cover with frame	12	09-Mar-26	26-Mar-26	09-Mar-26 A	26-Mar-26 A	85.71	85.71	85.71	100%	100%	0
PG-Q-PR-SL-MT-MA-10	Galvanized Steel Ladder	9	12-Mar-26	26-Mar-26	12-Mar-26 A	26-Mar-26 A	361.86	361.86	361.86	100%	100%	0
HVAC WORK		20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
PG-Q-PR-SL-AC-MA-10	Split Air Conditioning Unit	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	309.93	309.93	309.93	100%	100%	0
PG-Q-PR-SL-AC-MA-20	Air Duct	16	04-Mar-26	26-Mar-26	04-Mar-26 A	26-Mar-26 A	156.00	156.00	156.00	100%	100%	0
PG-Q-PR-SL-AC-MA-30	Diffusers and Grills	11	10-Mar-26	26-Mar-26	10-Mar-26 A	26-Mar-26 A	74.31	74.31	74.31	100%	100%	0

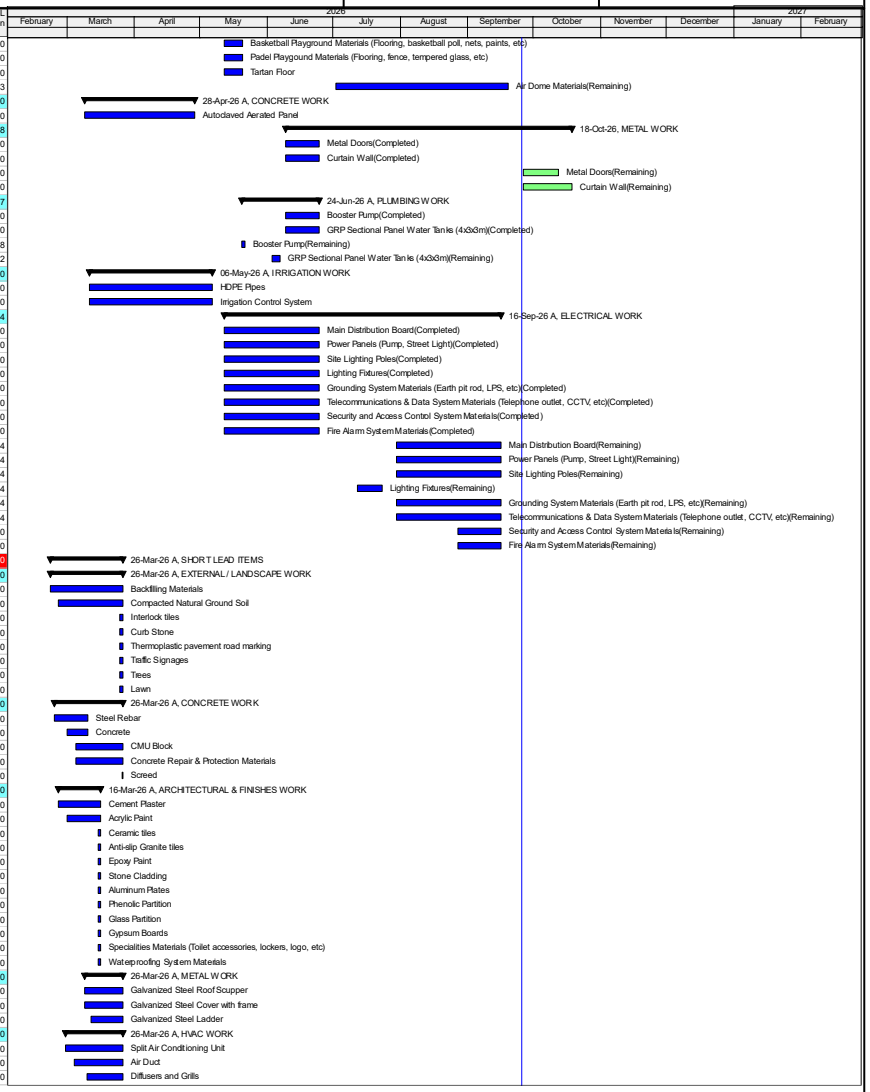


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-SL-AC-MA-40	Exhaust fans	11	10-Mar-26	26-Mar-26	10-Mar-26 A	26-Mar-26 A	66.12	66.12	66.12	100%	100%	0
PLUMBING WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
PG-Q-PR-SL-PB-MA-10	PPR Pipes & Valves	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	265.20	265.20	265.20	100%	100%	0
PG-Q-PR-SL-PB-MA-20	UPCV Pipes	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	335.19	335.19	335.19	100%	100%	0
PG-Q-PR-SL-PB-MA-30	Sanitary Drainage Fixtures	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	2,546.64	2,546.64	2,546.64	100%	100%	0
IRRIGATION WORK		17	03-Mar-26	26-Mar-26	03-Mar-26 A	26-Mar-26 A	13,170.12	13,170.12	13,170.12	100%	100%	0
PG-Q-PR-SL-IR-MA-10	Gate Valve including valve box	17	03-Mar-26	26-Mar-26	03-Mar-26 A	26-Mar-26 A	1,330.74	1,330.74	1,330.74	100%	100%	0
PG-Q-PR-SL-IR-MA-20	Bubblers and Spreyers	12	09-Mar-26	26-Mar-26	09-Mar-26 A	26-Mar-26 A	11,839.38	11,839.38	11,839.38	100%	100%	0
ELECTRICAL WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
PG-Q-PR-SL-EL-MA-10	Wiring Devices Materials	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PG-Q-PR-SL-FF-MA-10	Fire Extinguishers	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PROCUREMENT		208	03-Mar-26	27-Aug-26	03-Mar-26 A	10-Nov-26	4,735,135.80	3,188,145.25	4,735,135.80	100%	67.33%	-63
LONG LEAD ITEMS		195	18-Mar-26	27-Aug-26	18-Mar-26 A	10-Nov-26	3,229,967.34	1,764,284.78	3,229,967.34	100%	54.62%	-63
PURCHASE ORDER		147	18-Mar-26	12-Jul-26	18-Mar-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
EXTERNAL / LANDSCAPE WORK		5	06-May-26	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-LS-PO-20	Benches, Seats (Rectangular & Circular)	5	06-May-26	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-PO-30	Fence, gates and accessories	5	06-May-26	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-PO-10	Bike and Walk Path Materials	5	06-May-26	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		101	26-Mar-26	09-Jul-26	26-Mar-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-SP-PO-40	Tartan Floor	36	26-Mar-26	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-50	Air Dome Materials	8	01-Jul-26	09-Jul-26	08-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	6
CONCRETE WORK		39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-CO-PO-10	Autoclaved Aerated Panel	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		36	26-Mar-26	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-PO-10	Metal Doors	36	26-Mar-26	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-PO-20	Curtain Wall	36	26-Mar-26	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-PB-PO-10	Booster Pump	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-PO-20	GRP Sectional Panel Water Tanks (4x3x3m)	30	02-Apr-26	07-May-26	02-Apr-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		37	25-Mar-26	07-May-26	25-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-IR-PO-10	HDPE Pipes	37	25-Mar-26	07-May-26	25-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-PO-20	Irrigation Control System	37	25-Mar-26	07-May-26	25-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		103	13-May-26	12-Jul-26	13-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
PG-Q-PR-LL-EL-PO-10	Main Distribution Board(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-30	Site Lighting Poles(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-40	Lighting Fixtures(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-70	Security and Access Control System Materials(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-80	Fire Alarm System Materials(Completed)	33	13-May-26	25-Jun-26	13-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-10_R	Main Distribution Board(Remaining)	8	04-Jul-26	12-Jul-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-21
PG-Q-PR-LL-EL-PO-20_R	Power Panels (Pump, Street Light)(Remaining)	8	04-Jul-26	12-Jul-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-21
PG-Q-PR-LL-EL-PO-30_R	Site Lighting Poles(Remaining)	8	04-Jul-26	12-Jul-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-21
PG-Q-PR-LL-EL-PO-40_R	Lighting Fixtures(Remaining)	8	04-Jul-26	12-Jul-26	23-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-40
PG-Q-PR-LL-EL-PO-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	04-Jul-26	12-Jul-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-PR-LL-EL-PO-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	8	04-Jul-26	12-Jul-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-PR-LL-EL-PO-70_R	Security and Access Control System Materials(Remaining)	8	04-Jul-26	12-Jul-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-PR-LL-EL-PO-80_R	Fire Alarm System Materials(Remaining)	8	04-Jul-26	12-Jul-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-10
MANUFACTURE / FABRICATION		143	05-May-26	11-Aug-26	05-May-26 A	24-Oct-26	0.00	0.00	0.00	0%	0%	-62
EXTERNAL / LANDSCAPE WORK		109	05-May-26	23-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
PG-Q-PR-LL-LS-MF-20	Benches, Seats (Rectangular & Circular)(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MF-30	Fence, gates and accessories(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MF-10	Bike and Walk Path Materials(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26	23-Jul-26	30-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-17
PG-Q-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	25	25-Jun-26	23-Jul-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	10	25-Jun-26	06-Jul-26	30-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-32
SPORTS & RECREATIONAL FACILITIES WORK		123	05-May-26	11-Aug-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
PG-Q-PR-LL-SP-MF-10	Football Playground Materials (Flooring, goal post, nets, paints,	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-30	Padel Playgound Materials (Flooring, fence, tempered glass,	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-40	Tartan Floor(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26	23-Jul-26	30-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-17
PG-Q-PR-LL-SP-MF-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	25	25-Jun-26	23-Jul-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-SP-MF-30_R	Padel Playgound Materials (Flooring, fence, tempered glass,	15	25-Jun-26	12-Jul-26	30-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-27
PG-Q-PR-LL-SP-MF-40_R	Tartan Floor(Remaining)	25	25-Jun-26	23-Jul-26	22-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-24
PG-Q-PR-LL-SP-MF-50	Air Dome Materials	28	11-Jul-26	11-Aug-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	11
CONCRETE WORK		69	05-May-26	12-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	15
PG-Q-PR-LL-CO-MF-10	Autoclaved Aerated Panel(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0

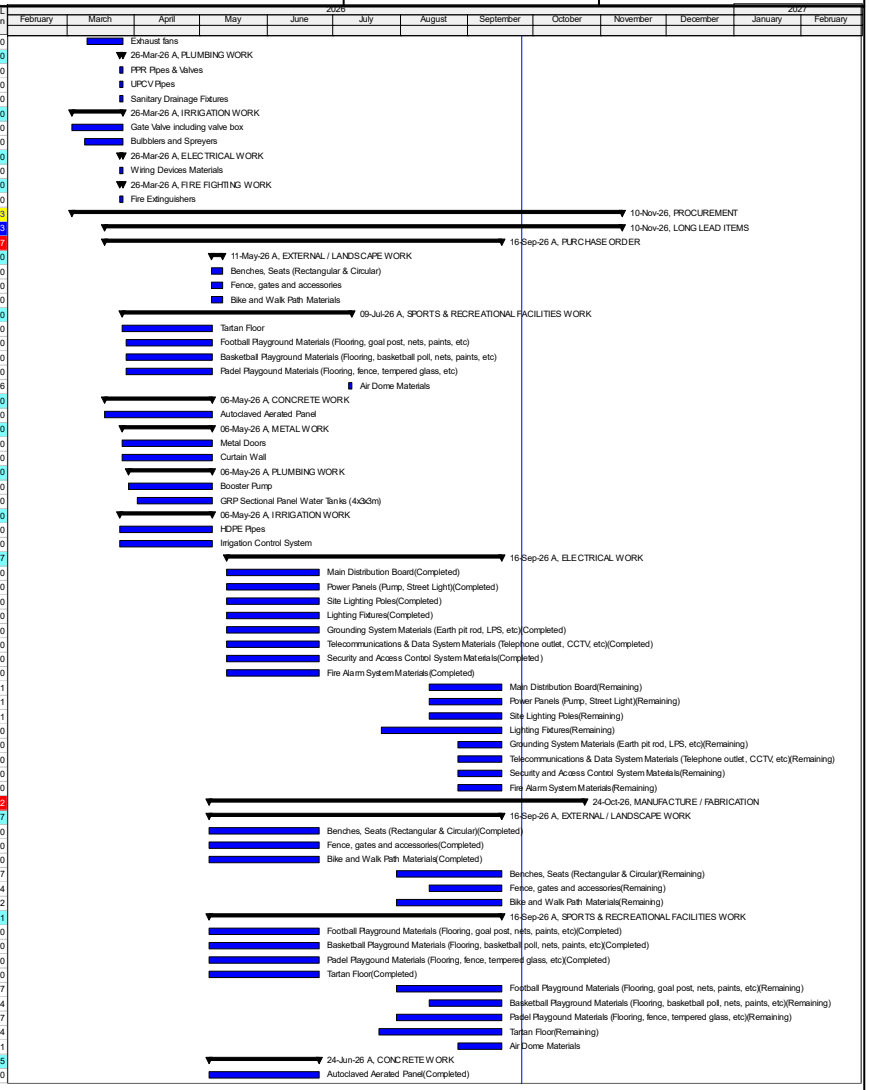


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-CO-MF-10_R	Autoclaved Aerated Panel(Remaining)	15	25-Jun-26	12-Jul-26	01-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	11
METAL WORK		143	05-May-26	23-Jul-26	05-May-26 A	24-Oct-26	0.00	0.00	0.00	0%	0%	-78
PG-Q-PR-LL-MT-MF-10	Metal Doors(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-MF-20	Curtain Wall(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
PLUMBING WORK		79	05-May-26	23-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	25
PG-Q-PR-LL-PB-MF-10	Booster Pump(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-MF-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-MF-10_R	Booster Pump(Remaining)	25	25-Jun-26	23-Jul-26	11-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	21
PG-Q-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26	23-Jul-26	06-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	21
IRRIGATION WORK		82	05-May-26	06-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-62
PG-Q-PR-LL-IR-MF-10	HDPE Pipes(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-MF-20	Irrigation Control System(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-MF-10_R	HDPE Pipes(Remaining)	10	25-Jun-26	06-Jul-26	02-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	7
PG-Q-PR-LL-IR-MF-20_R	Irrigation Control System(Remaining)	10	25-Jun-26	06-Jul-26	30-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-32
ELECTRICAL WORK		129	12-May-26	10-Aug-26	12-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-32
PG-Q-PR-LL-EL-MF-10	Main Distribution Board(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-30	Site Lighting Poles(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-40	Lighting Fixtures(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-70	Security and Access Control System Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-80	Fire Alarm System Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	25	13-Jul-26	10-Aug-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-14
PG-Q-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	13-Jul-26	10-Aug-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	13-Jul-26	10-Aug-26	14-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	8
PG-Q-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	13-Jul-26	10-Aug-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	8
PG-Q-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	8
PG-Q-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	8
DELIVERY TO SITE		157	06-May-26	27-Aug-26	06-May-26 A	10-Nov-26	3,229,967.34	1,764,284.78	3,229,967.34	100%	54.62%	-63
EXTERNAL / LANDSCAPE WORK		123	06-May-26	10-Aug-26	06-May-26 A	30-Sep-26	178,309.62	165,787.58	178,309.62	100%	92.98%	-43
PG-Q-PR-LL-LS-DL-20	Benches, Seats (Rectangular & Circular)(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	21,643.04	21,643.04	21,643.04	100%	100%	0
PG-Q-PR-LL-LS-DL-30	Fence, gates and accessories(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	11,381.45	11,381.45	11,381.45	100%	100%	0
PG-Q-PR-LL-LS-DL-10	Bike and Walk Path Materials(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	71,685.00	71,685.00	71,685.00	100%	100%	0
PG-Q-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	9	07-Jul-26	16-Jul-26	14-Aug-26 A	26-Sep-26	47,790.00	43,011.00	47,790.00	100%	90%	-27
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	14,428.69	10,100.08	14,428.69	100%	70%	-25
PG-Q-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	11,381.45	7,967.01	11,381.45	100%	70%	-25
SPORTS & RECREATIONAL FACILITIES WORK		127	06-May-26	23-Aug-26	06-May-26 A	05-Oct-26	2,461,702.86	1,098,518.87	2,461,702.86	100%	44.62%	-36
PG-Q-PR-LL-SP-DL-10	Football Playground Materials (Flooring, goal post, nets, paints,	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	70,478.10	70,478.10	70,478.10	100%	100%	0
PG-Q-PR-LL-SP-DL-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	10,152.00	10,152.00	10,152.00	100%	100%	0
PG-Q-PR-LL-SP-DL-30	Padel Playgound Materials (Fence, tempered glass, etc)(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	26,778.60	26,778.60	26,778.60	100%	100%	0
PG-Q-PR-LL-SP-DL-40	Tartan Floor(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	235,029.60	235,029.60	235,029.60	100%	100%	0
PG-Q-PR-LL-SP-DL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	28-Sep-26	26,778.60	21,422.88	26,778.60	100%	80%	-23
PG-Q-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	28-Sep-26	46,985.40	37,588.32	46,985.40	100%	80%	-23
PG-Q-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	28-Sep-26	10,152.00	8,121.60	10,152.00	100%	80%	-23
PG-Q-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	28-Sep-26	156,686.40	125,349.12	156,686.40	100%	80%	-23
PG-Q-PR-LL-SP-DL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	25-Aug-26 A	05-Oct-26	1,878,662.16	563,598.65	1,878,662.16	100%	30%	-25
CONCRETE WORK		78	06-May-26	23-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	16
PG-Q-PR-LL-CO-DL-10	Autoclaved Aerated Panel(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	7,654.50	7,654.50	7,654.50	100%	100%	0
PG-Q-PR-LL-CO-DL-10_R	Autoclaved Aerated Panel(Remaining)	10	13-Jul-26	23-Jul-26	04-Jul-26 A	05-Jul-26 A	5,103.00	5,103.00	5,103.00	100%	100%	8
METAL WORK		157	06-May-26	10-Aug-26	06-May-26 A	10-Nov-26	8,003.07	4,288.48	8,003.07	100%	53.59%	-78
PG-Q-PR-LL-MT-DL-10	Metal Doors(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	573.89	573.89	573.89	100%	100%	0
PG-Q-PR-LL-MT-DL-20	Curtain Wall(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	3,427.65	3,427.65	3,427.65	100%	100%	0
PG-Q-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	15	25-Jul-26	10-Aug-26	27-Aug-26 A	02-Nov-26	573.89	286.94	573.89	100%	50%	-42
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26	10-Aug-26	25-Oct-26	10-Nov-26	3,427.65	0.00	3,427.65	100%	0%	0
PLUMBING WORK		104	06-May-26	10-Aug-26	06-May-26 A	30-Sep-26	31,985.55	27,187.72	31,985.55	100%	85%	-43
PG-Q-PR-LL-PB-DL-10	Booster Pump(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	8,182.35	8,182.35	8,182.35	100%	100%	0
PG-Q-PR-LL-PB-DL-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	7,810.43	7,810.43	7,810.43	100%	100%	0
PG-Q-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	15	25-Jul-26	10-Aug-26	20-Aug-26 A	30-Sep-26	8,182.35	5,727.65	8,182.35	100%	70%	-20
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	7,810.43	5,467.30	7,810.43	100%	70%	-25
IRRIGATION WORK		102	06-May-26	15-Jul-26	06-May-26 A	27-Sep-26	220,380.75	216,289.58	220,380.75	100%	98.14%	-62
PG-Q-PR-LL-IR-DL-10	HDPE Pipes(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	89,734.50	89,734.50	89,734.50	100%	100%	0
PG-Q-PR-LL-IR-DL-20	Irrigation Control System(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	20,455.88	20,455.88	20,455.88	100%	100%	0
PG-Q-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	7	07-Jul-26	14-Jul-26	14-Aug-26 A	27-Aug-26 A	89,734.50	89,734.50	89,734.50	100%	100%	-5
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	27-Sep-26	20,455.88	16,364.70	20,455.88	100%	80%	-24
ELECTRICAL WORK		143	13-May-26	27-Aug-26	13-May-26 A	01-Oct-26	316,827.99	239,455.07	316,827.99	100%	75.58%	-28
PG-Q-PR-LL-EL-DL-10	Main Distribution Board(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	1,338.93	1,338.93	1,338.93	100%	100%	0
PG-Q-PR-LL-EL-DL-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	1,785.24	1,785.24	1,785.24	100%	100%	0
PG-Q-PR-LL-EL-DL-30	Site Lighting Poles(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	78,323.76	78,323.76	78,323.76	100%	100%	0

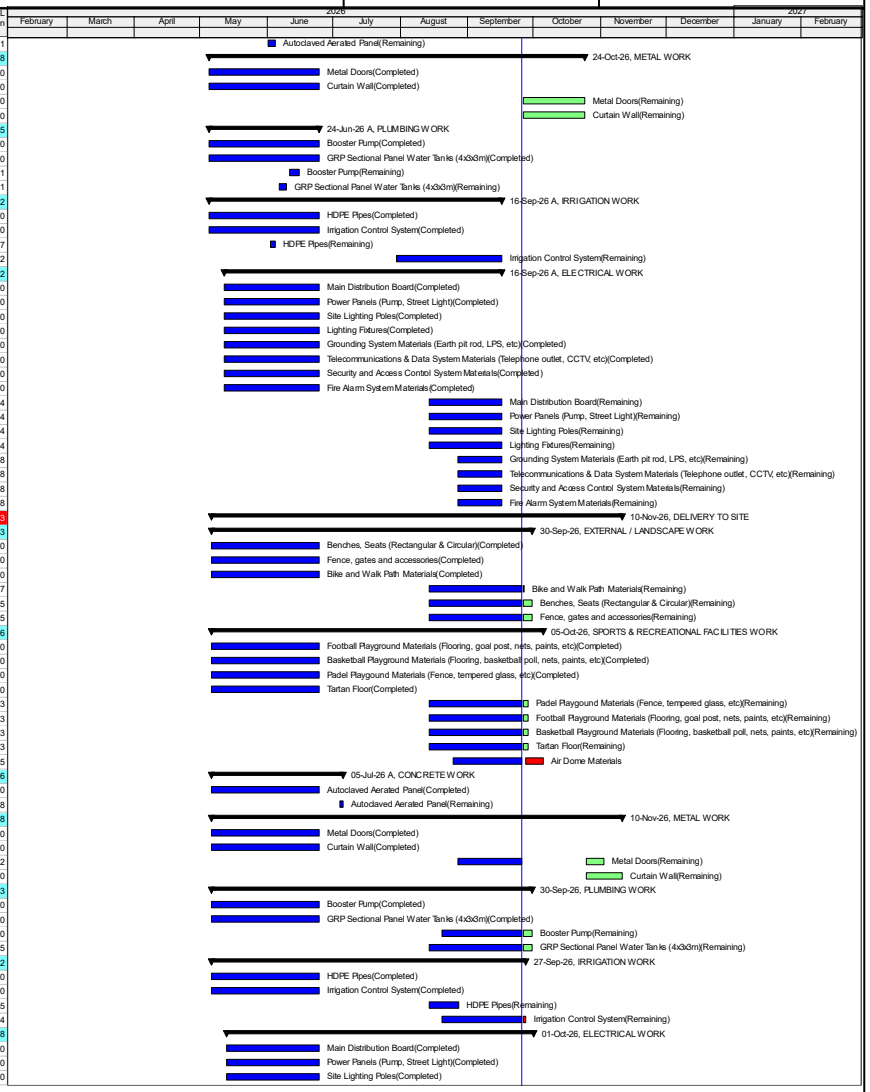


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-EL-DL-40	Lighting Fixtures(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	3,463.64	3,463.64	3,463.64	100%	100%	0
PG-Q-PR-LL-EL-DL-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,711.31	2,711.31	2,711.31	100%	100%	0
PG-Q-PR-LL-EL-DL-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,644.33	2,644.33	2,644.33	100%	100%	0
PG-Q-PR-LL-EL-DL-70	Security and Access Control System Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	3,347.73	3,347.73	3,347.73	100%	100%	0
PG-Q-PR-LL-EL-DL-80	Fire Alarm System Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,147.55	2,147.55	2,147.55	100%	100%	0
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	29-Sep-26	1,785.24	1,160.41	1,785.24	100%	65%	-29
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Oct-26	3,124.17	2,030.71	3,124.17	100%	65%	-25
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Oct-26	182,755.44	118,791.04	182,755.44	100%	65%	-25
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Oct-26	8,081.83	5,253.19	8,081.83	100%	65%	-25
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	6,326.40	4,112.16	6,326.40	100%	65%	-14
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	6,170.09	4,010.56	6,170.09	100%	65%	-14
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	7,811.37	5,077.39	7,811.37	100%	65%	-14
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	5,010.96	3,257.12	5,010.96	100%	65%	-14
SHORT LEAD ITEMS		183	03-Mar-26	12-Jul-26	03-Mar-26 A	12-Oct-26	1,505,168.46	1,423,860.47	1,505,168.46	100%	94.6%	-78
PURCHASE ORDER		64	03-Mar-26	21-May-26	03-Mar-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		57	03-Mar-26	13-May-26	03-Mar-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-LS-PO-10	Backfilling Materials	40	03-Mar-26	23-Apr-26	03-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-30	Compacted Natural Ground Soil	37	07-Mar-26	23-Apr-26	07-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-40	Curb Stone	28	29-Mar-26	30-Apr-26	29-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-20	Interlock tiles	25	01-Apr-26	30-Apr-26	01-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-50	Thermoplastic pavement road marking	2	11-May-26	13-May-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-60	Traffic Signages	2	11-May-26	13-May-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-70	Trees	2	11-May-26	13-May-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-80	Lawn	2	11-May-26	13-May-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		39	04-Mar-26	23-Apr-26	04-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-CO-PO-10	Steel Rebar	39	04-Mar-26	23-Apr-26	04-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-20	Concrete	34	10-Mar-26	23-Apr-26	10-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-40	CMU Block	30	15-Mar-26	23-Apr-26	15-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-50	Concrete Repair & Protection Materials	30	15-Mar-26	23-Apr-26	15-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-30	Screed	19	01-Apr-26	23-Apr-26	01-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		48	07-Mar-26	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AR-PO-40	Cement Plaster	48	07-Mar-26	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-50	Acrylic Paint	45	10-Mar-26	06-May-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-80	Phenolic Partition	40	16-Mar-26	06-May-26	16-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-90	Glass Partition	40	16-Mar-26	06-May-26	16-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-10	Ceramic tiles	32	30-Mar-26	06-May-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-20	Anti-slip Granite tiles	32	30-Mar-26	06-May-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-30	Epoxy Paint	32	30-Mar-26	06-May-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-100	Gypsum Boards	32	30-Mar-26	06-May-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	32	30-Mar-26	06-May-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-120	Waterproofing System Materials	32	30-Mar-26	06-May-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-60	Stone Cladding	30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-70	Aluminum Plates	30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		36	25-Mar-26	06-May-26	25-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-MT-PO-10	Galvanized Steel Ladder	36	25-Mar-26	06-May-26	25-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-PO-20	Galvanized Steel Roof Scupper	2	04-May-26	06-May-26	04-May-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-PO-30	Galvanized Steel Cover with frame	2	04-May-26	06-May-26	04-May-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		46	09-Mar-26	06-May-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AC-PO-10	Split Air Conditioning Unit	46	09-Mar-26	06-May-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-PO-20	Air Duct	42	14-Mar-26	06-May-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-PO-30	Diffusers and Grills	34	28-Mar-26	06-May-26	28-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-PO-40	Exhaust fans	27	05-Apr-26	06-May-26	05-Apr-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		33	29-Mar-26	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-PB-PO-10	PPR Pipes & Valves	33	29-Mar-26	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-PO-20	UPCV Pipes	33	29-Mar-26	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-PO-30	Sanitary Drainage Fixtures	33	29-Mar-26	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		43	12-Mar-26	06-May-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-IR-PO-10	Gate Valve including valve box	43	12-Mar-26	06-May-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-IR-PO-20	Bubblers and Spreyers	38	18-Mar-26	06-May-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		8	12-May-26	21-May-26	12-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-EL-PO-10	Wiring Devices Materials	8	12-May-26	21-May-26	12-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-FF-PO-10	Fire Extinguishers	30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
DELIVERY TO SITE		181	05-Mar-26	12-Jul-26	05-Mar-26 A	12-Oct-26	1,505,168.46	1,423,860.47	1,505,168.46	100%	94.6%	-78
EXTERNAL / LANDSCAPE WORK		155	05-Mar-26	08-Jul-26	05-Mar-26 A	04-Oct-26	1,258,805.61	1,207,746.13	1,258,805.61	100%	95.94%	-74
PG-Q-PR-SL-LS-DL-10	Backfilling Materials	39	05-Mar-26	23-Apr-26	05-Mar-26 A	24-Apr-26 A	328,050.00	328,050.00	328,050.00	100%	100%	0
PG-Q-PR-SL-LS-DL-30	Compacted Natural Ground Soil	12	30-Apr-26	13-May-26	30-Apr-26 A	13-May-26 A	77,220.00	77,220.00	77,220.00	100%	100%	0
PG-Q-PR-SL-LS-DL-20	Interlock tiles	12	30-Apr-26	13-May-26	30-Apr-26 A	13-May-26 A	268,488.00	268,488.00	268,488.00	100%	100%	0
PG-Q-PR-SL-LS-DL-40	Curb Stone	12	30-Apr-26	13-May-26	30-Apr-26 A	13-May-26 A	388,665.00	388,665.00	388,665.00	100%	100%	0
PG-Q-PR-SL-LS-DL-50	Thermoplastic pavement road marking(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	2,838.40	2,838.40	2,838.40	100%	100%	0
PG-Q-PR-SL-LS-DL-60	Traffic Signages(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	1,071.14	1,071.14	1,071.14	100%	100%	0
PG-Q-PR-SL-LS-DL-70	Trees(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	51,550.02	51,550.02	51,550.02	100%	100%	0
PG-Q-PR-SL-LS-DL-80	Lawn(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	62,370.00	62,370.00	62,370.00	100%	100%	0

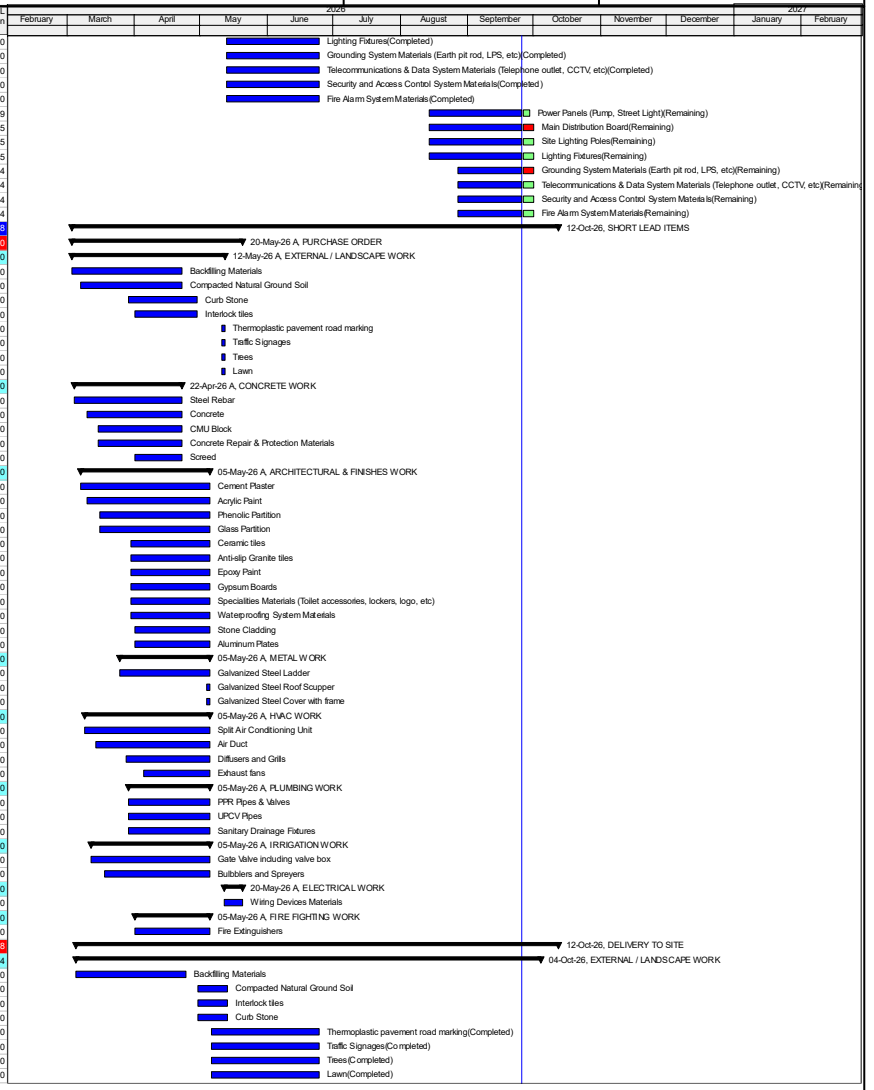


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-SL-LS-DL-60_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	1,892.27	662.29	1,892.27	100%	35%	-20
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	714.10	249.93	714.10	100%	35%	-20
PG-Q-PR-SL-LS-DL-70_R	Tiees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	34,366.68	12,028.34	34,366.68	100%	35%	-20
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	41,580.00	14,553.00	41,580.00	100%	35%	-20
CONCRETE WORK		50	12-Mar-26	13-May-26	12-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
PG-Q-PR-SL-CO-DL-20	Concrete	50	12-Mar-26	13-May-26	12-Mar-26 A	13-May-26 A	4,669.65	4,669.65	4,669.65	100%	100%	0
PG-Q-PR-SL-CO-DL-10	Steel Rebar	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	4,291.38	4,291.38	4,291.38	100%	100%	0
PG-Q-PR-SL-CO-DL-30	Screed	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	1,058.40	1,058.40	1,058.40	100%	100%	0
PG-Q-PR-SL-CO-DL-40	CMU Block	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	1,117.80	1,117.80	1,117.80	100%	100%	0
PG-Q-PR-SL-CO-DL-50	Concrete Repair & Protection Materials	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	3,348.00	3,348.00	3,348.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
PG-Q-PR-SL-AR-DL-10	Ceramic tiles	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	5,147.55	5,147.55	5,147.55	100%	100%	0
PG-Q-PR-SL-AR-DL-20	Anti-slip Granite tiles	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	4,819.50	4,819.50	4,819.50	100%	100%	0
PG-Q-PR-SL-AR-DL-30	Epoxy Paint	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,000.62	1,000.62	1,000.62	100%	100%	0
PG-Q-PR-SL-AR-DL-40	Cement Plaster	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,992.33	1,992.33	1,992.33	100%	100%	0
PG-Q-PR-SL-AR-DL-50	Acrylic Paint	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,331.10	1,331.10	1,331.10	100%	100%	0
PG-Q-PR-SL-AR-DL-60	Stone Cladding	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	16,669.80	16,669.80	16,669.80	100%	100%	0
PG-Q-PR-SL-AR-DL-70	Aluminum Plates	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-DL-80	Phenolic Partition	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	12,063.60	12,063.60	12,063.60	100%	100%	0
PG-Q-PR-SL-AR-DL-90	Glass Partition	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,398.60	1,398.60	1,398.60	100%	100%	0
PG-Q-PR-SL-AR-DL-100	Gypsum Boards	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,697.22	1,697.22	1,697.22	100%	100%	0
PG-Q-PR-SL-AR-DL-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	20,365.83	20,365.83	20,365.83	100%	100%	0
PG-Q-PR-SL-AR-DL-120	Waterproofing System Materials	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	4,897.80	4,897.80	4,897.80	100%	100%	0
METAL WORK		129	06-May-26	08-Jul-26	06-May-26 A	08-Oct-26	4,310.01	2,586.01	4,310.01	100%	60%	-78
PG-Q-PR-SL-MT-DL-10	Galvanized Steel Ladder(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	1,954.04	1,954.04	1,954.04	100%	100%	0
PG-Q-PR-SL-MT-DL-20	Galvanized Steel Roof Scupper(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	169.13	169.13	169.13	100%	100%	0
PG-Q-PR-SL-MT-DL-30	Galvanized Steel Cover with frame(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	462.83	462.83	462.83	100%	100%	0
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	1,302.70	0.00	1,302.70	100%	0%	0
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	112.75	0.00	112.75	100%	0%	0
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	308.56	0.00	308.56	100%	0%	0
HVAC WORK		106	06-May-26	08-Jul-26	06-May-26 A	04-Oct-26	5,457.24	4,147.50	5,457.24	100%	76%	-73
PG-Q-PR-SL-AC-DL-10	Split Air Conditioning Unit(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	1,673.62	1,673.62	1,673.62	100%	100%	0
PG-Q-PR-SL-AC-DL-20	Air Duct(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	842.40	842.40	842.40	100%	100%	0
PG-Q-PR-SL-AC-DL-30	Diffusers and Grills(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	401.27	401.27	401.27	100%	100%	0
PG-Q-PR-SL-AC-DL-40	Exhaust fans(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	357.05	357.05	357.05	100%	100%	0
PG-Q-PR-SL-AC-DL-10_R	Split Air Conditioning Unit(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	1,115.75	446.30	1,115.75	100%	40%	-19
PG-Q-PR-SL-AC-DL-20_R	Air Duct(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	561.60	224.64	561.60	100%	40%	-19
PG-Q-PR-SL-AC-DL-30_R	Diffusers and Grills(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	267.52	107.01	267.52	100%	40%	-19
PG-Q-PR-SL-AC-DL-40_R	Exhaust fans(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	238.03	95.21	238.03	100%	40%	-19
PLUMBING WORK		7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
PG-Q-PR-SL-PB-DL-10	PPR Pipes & Valves	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	2,386.80	2,386.80	2,386.80	100%	100%	0
PG-Q-PR-SL-PB-DL-20	UPCV Pipes	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	3,016.71	3,016.71	3,016.71	100%	100%	0
PG-Q-PR-SL-PB-DL-30	Sanitary Drainage Fixtures	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	22,919.76	22,919.76	22,919.76	100%	100%	0
IRRIGATION WORK		101	06-May-26	08-Jul-26	06-May-26 A	30-Sep-26	118,531.08	93,639.55	118,531.08	100%	79%	-70
PG-Q-PR-SL-IR-DL-10	Gate Valve including valve box(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	4,790.66	4,790.66	4,790.66	100%	100%	0
PG-Q-PR-SL-IR-DL-20	Bubblers and Spreyers(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	42,621.77	42,621.77	42,621.77	100%	100%	0
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	30-Sep-26	7,186.00	4,670.90	7,186.00	100%	65%	-27
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	30-Sep-26	63,932.65	41,556.22	63,932.65	100%	65%	-22
ELECTRICAL WORK		128	11-May-26	12-Jul-26	11-May-26 A	12-Oct-26	3,667.68	1,467.07	3,667.68	100%	40%	-78
PG-Q-PR-SL-EL-DL-10	Wiring Devices Materials(Completed)	35	11-May-26	24-Jun-26	11-May-26 A	24-Jun-26 A	1,467.07	1,467.07	1,467.07	100%	100%	0
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26	12-Oct-26	2,200.61	0.00	2,200.61	100%	0%	0
FIRE FIGHTING WORK		129	06-May-26	08-Jul-26	06-May-26 A	08-Oct-26	204.39	81.76	204.39	100%	40%	-78
PG-Q-PR-SL-FF-DL-10	Fire Extinguishers(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	81.76	81.76	81.76	100%	100%	0
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	122.63	0.00	122.63	100%	0%	0
CONSTRUCTION STAGE		246	24-Mar-26	16-Dec-26	24-Mar-26 A	11-Jan-27	7,654,024.37	6,784,731.30	10,522,524.00	73.95%	65.55%	-21
PLAYGROUND AND LANDSCAPING WORKS		246	24-Mar-26	16-Dec-26	24-Mar-26 A	11-Jan-27	4,860,629.12	5,087,338.62	6,019,638.42	83.12%	86.99%	-21
CUT AND FILL		38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	729,000.00	729,000.00	900,600.00	100%	100%	0
PG-Q-CON-EX-CF-10	Existing Soil Excavation Works	36	24-Mar-26	04-May-26	24-Mar-26 A	04-May-26 A	233,280.00	233,280.00	233,280.00	100%	100%	0
PG-Q-CON-EX-CF-30	Levelling & Backfilling Works	18	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	495,720.00	495,720.00	495,720.00	100%	100%	0
PG-Q-CON-EX-CF-39	Soil Replacement Works	27			05-Apr-26 A	05-May-26 A	0.00	0.00	171,600.00	0%	100%	-27
PLAYGROUND WORKS		197	21-Apr-26	02-Dec-26	21-Apr-26 A	06-Dec-26	971,857.63	1,201,903.58	1,318,471.20	73.71%	91.16%	-3
FOOTBALL PLAYGROUND WORKS		155	21-Apr-26	17-Nov-26	21-Apr-26 A	25-Oct-26	452,560.74	564,692.16	611,282.16	74.03%	92.38%	21
PG-Q-CON-EX-FB-10	Subgrade Preparation and Compaction	14	21-Apr-26	06-May-26	21-Apr-26 A	06-May-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-Q-CON-EX-FB-20	Sub-Base Laying and Compaction	10	26-Apr-26	06-May-26	26-Apr-26 A	06-May-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-Q-CON-EX-FB-30	Base Course Laying and Compaction	33	06-May-26	17-Jun-26	06-May-26 A	17-Jun-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-Q-CON-EX-FB-40	Tartan flooring(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	104,457.60	104,457.60	104,457.60	100%	100%	0
PG-Q-CON-EX-FB-80	Fine Grading & Leveling	10	25-Jun-26	06-Jul-26	09-Jul-26 A	11-Jul-26 A	23,667.00	23,667.00	23,667.00	100%	100%	8
PG-Q-CON-EX-FB-70	Topsoil Placement	12	07-Jul-26	20-Jul-26	12-Jul-26 A	14-Aug-26 A	23,667.00	23,667.00	23,667.00	100%	100%	-17
PG-Q-CON-EX-FB-50	Goal Post Foundation	25	21-Jul-26	18-Aug-26	06-Aug-26 A	27-Aug-26 A	35,500.50	35,500.50	35,500.50	100%	100%	6
PG-Q-CON-EX-FB-120	Installation of Lighting System	12	19-Aug-26	01-Sep-26	20-Aug-26 A	27-Sep-26	24,360.00	20,706.00	24,360.00	100%	85%	-20
PG-Q-CON-EX-FB-90	Turfing / Seeding Works	10	02-Sep-26	13-Sep-26	14-Aug-26 A	30-Sep-26	23,667.00	17,750.25	23,667.00	100%	75%	-29
PG-Q-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	14-Sep-26	01-Oct-26	12-Jul-26 A	14-Aug-26 A	146,240.64	243,734.40	243,734.40	60%	100%	-14
PG-Q-CON-EX-FB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	06-Oct-26	0.00	23,075.33	35,500.50	0%	65%	-19

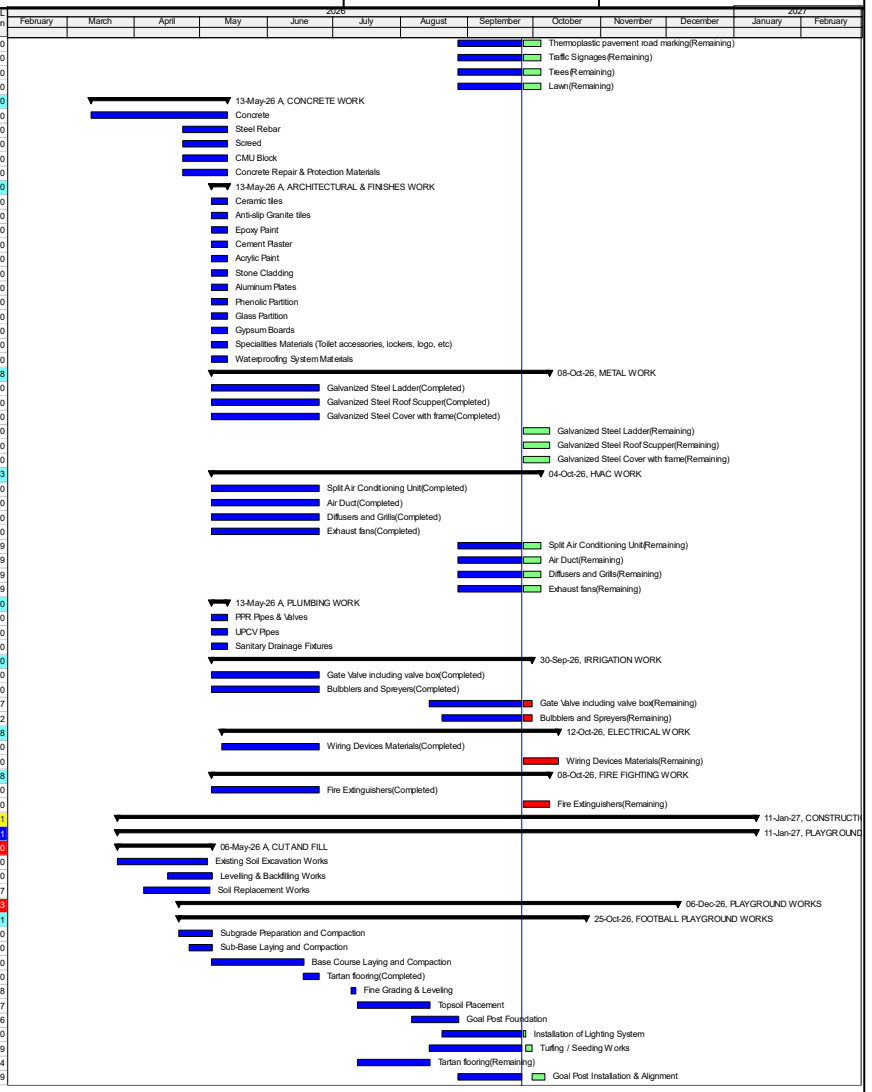

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EXFB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	15-Oct-26	0.00	1,133.09	2,060.16	0%	55%	-24
PG-Q-CON-EXFB-100	Markings and Signages	8	09-Nov-2	17-Nov-26	15-Oct-26	25-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		166	30-Apr-26	17-Nov-26	30-Apr-26 A	16-Nov-26	357,056.89	361,355.47	381,705.12	93.54%	94.67%	2
PG-Q-CON-EXBB-10	Subgrade Preparation and Compaction	6	30-Apr-26	06-May-26	30-Apr-26 A	06-May-26 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-Q-CON-EXBB-20	Sub-Base Laying and Compaction	1	05-May-2	06-May-26	05-May-26 A	06-May-26 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-Q-CON-EXBB-30	Base Course Laying and Compaction	33	06-May-2	17-Jun-26	06-May-26 A	17-Jun-26 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-Q-CON-EXBB-70	Floor Surface Curing(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	4,641.62	4,641.62	4,641.62	100%	100%	0
PG-Q-CON-EXBB-50	Basketball Pole Foundation	25	25-Jun-26	23-Jul-26	06-Aug-26 A	13-Aug-26 A	15,472.08	15,472.08	15,472.08	100%	100%	18
PG-Q-CON-EXBB-70_R	Floor Surface Curing(Remaining)	15	25-Jul-26	10-Aug-26	06-Aug-26 A	14-Aug-26 A	10,830.46	10,830.46	10,830.46	100%	100%	8
PG-Q-CON-EXBB-40	Tartan flooring	17	11-Aug-2	30-Aug-26	30-Jul-26 A	14-Aug-26 A	261,144.00	261,144.00	261,144.00	100%	100%	4
PG-Q-CON-EXBB-80	Court Line Marking	15	31-Aug-2	16-Sep-26	20-Aug-26 A	01-Oct-26	13,091.76	10,473.41	13,091.76	100%	80%	-21
PG-Q-CON-EXBB-60	Basketball Pole Installation & Alignment	17	17-Sep-2	07-Oct-26	20-Aug-26 A	06-Oct-26	5,460.73	12,377.66	15,472.08	35.29%	80%	-22
PG-Q-CON-EXBB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	06-Oct-26	26-Oct-26	0.00	0.00	13,091.76	0%	0%	0
PG-Q-CON-EXBB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	26-Oct-26	16-Nov-26	0.00	0.00	1,545.12	0%	0%	0
PADEL PLAYGROUND WORKS		184	06-May-2	02-Dec-26	06-May-26 A	06-Dec-26	162,239.99	275,855.94	325,483.92	49.85%	84.75%	-3
PG-Q-CON-EXPD-10	Excavation For Fence Footing(Completed)	39	06-May-2	24-Jun-26	06-May-26 A	24-Jun-26 A	16,243.20	16,243.20	16,243.20	100%	100%	0
PG-Q-CON-EXPD-20	RC Foundations For Fence(Completed)	27	20-May-2	24-Jun-26	20-May-26 A	24-Jun-26 A	1,767.48	1,767.48	1,767.48	100%	100%	0
PG-Q-CON-EXPD-30	Tartan Flooring Layers(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	130,572.00	130,572.00	130,572.00	100%	100%	0
PG-Q-CON-EXPD-10_R	Excavation For Fence Footing(Remaining)	7	25-Jun-26	02-Jul-26	06-Aug-26 A	14-Aug-26 A	1,804.80	1,804.80	1,804.80	100%	100%	0
PG-Q-CON-EXPD-20_R	RC Foundations For Fence(Remaining)	20	04-Jul-26	26-Jul-26	07-Aug-26 A	27-Aug-26 A	1,767.48	1,767.48	1,767.48	100%	100%	2
PG-Q-CON-EXPD-40	Steel Structure & Fence Supports Installation	18	11-Aug-2	31-Aug-26	20-Aug-26 A	06-Oct-26	3,534.96	2,474.47	3,534.96	100%	70%	-22
PG-Q-CON-EXPD-60	Chain Link Fence & Gates Installation	16	01-Sep-2	19-Sep-26	20-Aug-26 A	12-Oct-26	5,302.44	3,711.71	5,302.44	100%	70%	-29
PG-Q-CON-EXPD-50	Tempered Glass Installation	17	20-Sep-2	10-Oct-26	12-Oct-26	01-Nov-26	1,247.63	0.00	5,302.44	23.53%	0%	0
PG-Q-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	01-Nov-26	0.00	117,514.80	130,572.00	0%	90%	-58
PG-Q-CON-EXPD-70	Court Accessories Installation	15	29-Oct-26	15-Nov-26	01-Nov-26	18-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-Q-CON-EXPD-80	Install Playground Benches	15	16-Nov-2	02-Dec-26	18-Nov-26	06-Dec-26	0.00	0.00	1,545.12	0%	0%	0
GENERAL SITE WORKS		226	16-Apr-26	16-Dec-26	16-Apr-26 A	11-Jan-27	1,471,030.62	1,263,485.97	1,617,941.82	90.92%	78.09%	-21
FENCE WORKS		161	16-Apr-26	13-Sep-26	16-Apr-26 A	26-Oct-26	32,909.40	18,758.36	32,909.40	100%	57%	-36
PG-Q-CON-EXGN-FN-10	Excavation for fence foundation	3	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	6,581.88	6,581.88	6,581.88	100%	100%	0
PG-Q-CON-EXGN-FN-20	Concrete Foundations for Fence	10	21-Jul-26	01-Aug-26	13-Aug-26 A	20-Aug-26 A	6,581.88	6,581.88	6,581.88	100%	100%	3
PG-Q-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-2	15-Aug-26	20-Aug-26 A	27-Sep-26	6,581.88	5,594.60	6,581.88	100%	85%	-20
PG-Q-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-2	01-Sep-26	27-Sep-26	14-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
PG-Q-CON-EXGN-FN-50	Installation of Gates	10	02-Sep-2	13-Sep-26	14-Oct-26	26-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		137	12-May-2	18-Aug-26	12-May-26 A	25-Oct-26	780,707.34	636,981.23	780,707.34	100%	81.59%	-56
STORM WATER AND UTILITY WORK		135	12-May-2	16-Aug-26	12-May-26 A	22-Oct-26	27,252.00	18,086.40	27,252.00	100%	66.37%	-56
PG-Q-CON-EXGN-M-10	Excavation	2	12-May-2	13-May-26	12-May-26 A	13-May-26 A	3,096.00	3,096.00	3,096.00	100%	100%	0
PG-Q-CON-EXGN-M-20	Bedding preparation & level control(Completed)	27	20-May-2	24-Jun-26	20-May-26 A	24-Jun-26 A	1,651.20	1,651.20	1,651.20	100%	100%	0
PG-Q-CON-EXGN-M-30	Manhole Installation(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	1,032.00	1,032.00	1,032.00	100%	100%	0
PG-Q-CON-EXGN-M-20_R	Bedding preparation & level control(Remaining)	8	25-Jun-26	04-Jul-26	07-Aug-26 A	27-Aug-26 A	412.80	412.80	412.80	100%	100%	-10
PG-Q-CON-EXGN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	27-Sep-26	4,128.00	3,302.40	4,128.00	100%	80%	-25
PG-Q-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	28-Sep-26	10,740.00	8,592.00	10,740.00	100%	80%	-26
PG-Q-CON-EXGN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	28-Sep-26	06-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	06-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-2	16-Aug-26	15-Oct-26	22-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		86	17-Jun-26	09-Aug-26	17-Jun-26 A	15-Oct-26	753,137.40	618,894.83	753,137.40	100%	82.18%	-56
PG-Q-CON-EXGN-M-80	Installation of HDPE Irrigation Pipe Network with Gate Valve and	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	148,902.18	148,902.18	148,902.18	100%	100%	0
PG-Q-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	3	30-Jul-26	02-Aug-26	06-Aug-26 A	13-Oct-26	276,532.62	243,348.71	276,532.62	100%	88%	-55
PG-Q-CON-EXGN-M-90	Installation of Irrigation Control System	3	03-Aug-2	05-Aug-26	20-Aug-26 A	13-Oct-26	90,915.00	72,732.00	90,915.00	100%	80%	-43
PG-Q-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-2	09-Aug-26	27-Aug-26 A	15-Oct-26	236,787.60	153,911.94	236,787.60	100%	65%	-38
FIRE PROTECTION SYSTEM		2	17-Aug-2	18-Aug-26	22-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-Q-CON-EXGN-M-110	Fire Extinguisher Installation	2	17-Aug-2	18-Aug-26	22-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		180	20-May-2	01-Nov-26	20-May-26 A	22-Dec-26	637,514.88	519,487.58	693,965.28	91.87%	74.86%	-43
POWER, LIGHTING & GROUNDING		145	20-May-2	20-Sep-26	20-May-26 A	11-Nov-26	636,895.08	519,487.58	636,895.08	100%	81.57%	-43
PG-Q-CON-EXGN-E-10	Excavation(Completed)	27	20-May-2	24-Jun-26	20-May-26 A	24-Jun-26 A	121,836.96	121,836.96	121,836.96	100%	100%	0
PG-Q-CON-EXGN-E-20	Foundation Work for Site Lighting Poles(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	69,621.12	69,621.12	69,621.12	100%	100%	0
PG-Q-CON-EXGN-E-10_R	Excavation(Remaining)	3	13-Aug-2	16-Aug-26	16-Jul-26 A	27-Aug-26 A	52,215.84	52,215.84	52,215.84	100%	100%	-34
PG-Q-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-2	17-Aug-26	20-Aug-26 A	22-Oct-26	162,449.28	129,959.42	162,449.28	100%	80%	-50
PG-Q-CON-EXGN-E-30	Lightning Protection System (LPS)	3	29-Aug-2	31-Aug-26	27-Aug-26 A	25-Oct-26	8,265.00	6,612.00	8,265.00	100%	80%	-47
PG-Q-CON-EXGN-E-40	KWH Meter and MDB Installation	2	01-Sep-2	02-Sep-26	25-Oct-26	27-Oct-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-Q-CON-EXGN-E-50	Power Panels and Distribution Boards	5	03-Sep-2	08-Sep-26	27-Oct-26	02-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-Q-CON-EXGN-E-60	Site Lighting Poles Installation	3	09-Sep-2	12-Sep-26	20-Aug-26 A	03-Nov-26	174,052.80	139,242.24	174,052.80	100%	80%	-60
PG-Q-CON-EXGN-E-70	Wiring Works	3	13-Sep-2	15-Sep-26	03-Nov-26	07-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-Q-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	4	16-Sep-2	20-Sep-26	07-Nov-26	11-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-2	20-Oct-26	11-Nov-26	10-Dec-26	619.80	0.00	43,146.00	1.44%	0%	0
PG-Q-CON-EXGN-E-90	ELV Containment & Cabling Works	3	21-Sep-2	24-Sep-26	11-Nov-26	15-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-Q-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	26-Sep-2	28-Sep-26	15-Nov-26	18-Nov-26	0.00	0.00	619.80	0%	0%	0
PG-Q-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	29-Sep-2	03-Oct-26	18-Nov-26	23-Nov-26	0.00	0.00	3,718.80	0%	0%	0
PG-Q-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26	07-Oct-26	23-Nov-26	28-Nov-26	0.00	0.00	15,249.12	0%	0%	0
PG-Q-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	08-Oct-26	12-Oct-26	28-Nov-26	02-Dec-26	0.00	0.00	1,446.48	0%	0%	0
PG-Q-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	13-Oct-26	17-Oct-26	02-Dec-26	07-Dec-26	0.00	0.00	6,612.00	0%	0%	0
PG-Q-CON-EXGN-E-150	IP Camera Installation	3	18-Oct-26	20-Oct-26	07-Dec-26	10-Dec-26	0.00	0.00	14,880.00	0%	0%	0
FIRE ALARM SYSTEM		32	26-Sep-2	01-Nov-26	15-Nov-26	22-Dec-26	0.00	0.00	13,924.20	0%	0%	0
PG-Q-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	26-Sep-2	04-Oct-26	15-Nov-26	24-Nov-26	0.00	0.00	1,983.60	0%	0%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26	13-Oct-26	24-Nov-26	03-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-Q-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26	22-Oct-26	03-Dec-26	13-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-Q-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	24-Oct-26	01-Nov-26	13-Dec-26	22-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		160	17-Jun-26	09-Nov-26	17-Jun-26 A	22-Dec-26	19,899.00	84,018.00	102,919.80	19.33%	81.63%	-36
PG-Q-CON-EXGN-PR-20	Interlock tiles(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	19,899.00	19,899.00	19,899.00	100%	100%	0
PG-Q-CON-EXGN-PR-10	Installation of Parking Accessories	5	29-Oct-26	03-Nov-26	20-Aug-26 A	10-Dec-26	0.00	39,798.00	44,220.00	0%	90%	-91
PG-Q-CON-EXGN-PR-20_R	Interlock tiles(Remaining)	3	01-Nov-2	03-Nov-26	06-Jul-26 A	10-Jul-26 A	0.00	24,321.00	24,321.00	0%	100%	-1
PG-Q-CON-EXGN-PR-30	Marking & Signages	5	04-Nov-2	09-Nov-26	16-Dec-26	22-Dec-26	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		44	10-Nov-2	16-Dec-26	12-Jul-26 A	11-Jan-27	0.00	4,240.80	7,440.00	0%	57%	-124
PG-Q-CON-EXGN-SC-10	Excavation & Trench Preparation	8	10-Nov-2	18-Nov-26	12-Jul-26 A	20-Aug-26 A	0.00	2,232.00	2,232.00	0%	100%	-27
PG-Q-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-2	28-Nov-26	14-Aug-26 A	23-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-103
PG-Q-CON-EXGN-SC-30	Connection to City Network	8	29-Nov-2	07-Dec-26	23-Dec-26	02-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-Q-CON-EXGN-SC-40	Backfilling	8	08-Dec-2	16-Dec-26	02-Jan-27	11-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		163	31-May-2	14-Dec-26	30-May-26 A	07-Dec-26	1,640,450.47	1,879,371.68	2,134,335.00	76.86%	88.05%	6
HARDSCAPE WORK		163	31-May-2	14-Dec-26	30-May-26 A	07-Dec-26	1,524,950.47	1,683,021.68	1,712,409.00	89.05%	98.28%	6
PG-Q-CON-EXLS-HS-10	Curbstone Installation(Completed)	22	31-May-2	24-Jun-26	30-May-26 A	24-Jun-26 A	604,590.00	604,590.00	604,590.00	100%	100%	0
PG-Q-CON-EXLS-HS-20	Interlock Tiles Grey Scale with Black Marble Chips(Completed)	22	31-May-2	24-Jun-26	30-May-26 A	24-Jun-26 A	36,960.00	36,960.00	36,960.00	100%	100%	0
PG-Q-CON-EXLS-HS-40	Bike Path and Walking Path Construction(Completed)	22	31-May-2	24-Jun-26	30-May-26 A	24-Jun-26 A	146,025.00	146,025.00	146,025.00	100%	100%	0
PG-Q-CON-EXLS-HS-30	Stamped Concrete Floor(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	207,900.00	207,900.00	207,900.00	100%	100%	0
PG-Q-CON-EXLS-HS-50	Install Recycled Precast Concrete Seats(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	6,959.70	6,959.70	6,959.70	100%	100%	0
PG-Q-CON-EXLS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	17	18-Jul-26	05-Aug-26	08-Jul-26 A	14-Aug-26 A	119,475.00	119,475.00	119,475.00	100%	100%	-15
PG-Q-CON-EXLS-HS-10_R	Curbstone Installation(Remaining)	10	02-Sep-2	13-Sep-26	07-Jul-26 A	14-Aug-26 A	259,110.00	259,110.00	259,110.00	100%	100%	-23
PG-Q-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	13	14-Sep-2	29-Sep-26	31-Jul-26 A	27-Aug-26 A	143,930.77	207,900.00	207,900.00	69.23%	100%	-11
PG-Q-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-2	14-Oct-26	27-Aug-26 A	28-Oct-26	0.00	47,124.00	55,440.00	0%	85%	-40
PG-Q-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-2	02-Dec-26	20-Aug-26 A	25-Nov-26	0.00	46,977.98	62,637.30	0%	75%	-73
PG-Q-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-2	14-Dec-26	25-Nov-26	07-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		141	10-Jun-26	21-Nov-26	10-Jun-26 A	23-Nov-26	115,500.00	196,350.00	421,926.00	27.37%	46.54%	-1
PG-Q-CON-EXLS-SS-20	Lawn Area Preparation & Planting / Turfing(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	115,500.00	115,500.00	115,500.00	100%	100%	0
PG-Q-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	03-Nov-26	0.00	80,850.00	115,500.00	0%	70%	-42
PG-Q-CON-EXLS-SS-10	Planting Trees	17	02-Nov-2	21-Nov-26	03-Nov-26	23-Nov-26	0.00	0.00	190,926.00	0%	0%	0
TANK WORKS		124	13-May-2	19-Aug-26	13-May-26 A	10-Oct-26	48,290.40	13,577.40	48,290.40	100%	28.12%	-43
SEPTIC TANK		33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	7,475.22	7,475.22	7,475.22	100%	100%	0
PG-Q-CON-EXTW-ST-10	Excavation	29	13-May-2	20-Jun-26	13-May-26 A	20-Jun-26 A	252.18	252.18	252.18	100%	100%	0
PG-Q-CON-EXTW-ST-20	PCC / Lean Concrete laying	24	20-May-2	21-Jun-26	20-May-26 A	21-Jun-26 A	168.12	168.12	168.12	100%	100%	0
PG-Q-CON-EXTW-ST-40	RCC Wall	4	20-Jun-26	23-Jun-26	20-Jun-26 A	23-Jun-26 A	2,757.60	2,757.60	2,757.60	100%	100%	0
PG-Q-CON-EXTW-ST-30	RCC Foundation	2	21-Jun-26	22-Jun-26	21-Jun-26 A	22-Jun-26 A	1,277.64	1,277.64	1,277.64	100%	100%	0
PG-Q-CON-EXTW-ST-50	RCC Slab	4	21-Jun-26	24-Jun-26	21-Jun-26 A	24-Jun-26 A	2,599.38	2,599.38	2,599.38	100%	100%	0
PG-Q-CON-EXTW-ST-60	Finishing Work	3	22-Jun-26	24-Jun-26	22-Jun-26 A	24-Jun-26 A	252.18	252.18	252.18	100%	100%	0
PG-Q-CON-EXTW-ST-70	Backfilling	2	23-Jun-26	24-Jun-26	23-Jun-26 A	24-Jun-26 A	168.12	168.12	168.12	100%	100%	0
WATER STORAGE TANK		124	13-May-2	19-Aug-26	13-May-26 A	10-Oct-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-43
PG-Q-CON-EXTW-IR-10	Excavation(Completed)	33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	766.58	766.58	766.58	100%	100%	0
PG-Q-CON-EXTW-IR-10_R	Excavation(Remaining)	7	25-Jun-26	02-Jul-26	07-Jul-26 A	08-Jul-26 A	85.18	85.18	85.18	100%	100%	5
PG-Q-CON-EXTW-IR-20	RCC Foundation	15	04-Jul-26	20-Jul-26	09-Jul-26 A	26-Aug-26 A	4,136.40	4,136.40	4,136.40	100%	100%	-27
PG-Q-CON-EXTW-IR-30	Backfilling	7	21-Jul-26	28-Jul-26	20-Aug-26 A	27-Aug-26 A	1,114.02	1,114.02	1,114.02	100%	100%	0
PG-Q-CON-EXTW-IR-40	GRP Water Tank Installation	8	11-Aug-2	19-Aug-26	30-Sep-26	10-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		193	13-May-2	26-Nov-26	13-May-26 A	30-Dec-26	2,623,169.02	1,411,084.02	4,178,041.20	62.78%	33.77%	-28
CIVIL WORK		132	13-May-2	10-Sep-26	13-May-26 A	20-Oct-26	1,711,669.97	1,160,595.73	1,711,669.97	100%	67.8%	-32
PG-Q-CON-EXAD-CL-10	Excavation For Footing(Completed)	33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	25,048.83	25,048.83	25,048.83	100%	100%	0
PG-Q-CON-EXAD-CL-10_R	Excavation For Footing(Remaining)	6	09-Jul-26	15-Jul-26	09-Jul-26 A	10-Jul-26 A	225,439.46	225,439.46	225,439.46	100%	100%	5
PG-Q-CON-EXAD-CL-20	Anti-Termite Treatment	2	16-Jul-26	18-Jul-26	11-Jul-26 A	12-Jul-26 A	83,496.10	83,496.10	83,496.10	100%	100%	0
PG-Q-CON-EXAD-CL-30	PCC / Blinding Concrete	3	19-Jul-26	21-Jul-26	23-Jul-26 A	06-Aug-26 A	125,244.14	125,244.14	125,244.14	100%	100%	-10
PG-Q-CON-EXAD-CL-40	RCC Foundation Works	12	22-Jul-26	04-Aug-26	31-Jul-26 A	13-Aug-26 A	250,488.29	250,488.29	250,488.29	100%	100%	0
PG-Q-CON-EXAD-CL-50	Backfilling with Compaction	6	05-Aug-2	11-Aug-26	06-Aug-26 A	14-Aug-26 A	250,488.29	250,488.29	250,488.29	100%	100%	-1
PG-Q-CON-EXAD-CL-60	Installation of Anchorage System	8	12-Aug-2	20-Aug-26	27-Aug-26 A	29-Sep-26	250,488.29	200,390.63	250,488.29	100%	80%	-19
PG-Q-CON-EXAD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-2	01-Sep-26	29-Sep-26	11-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXAD-CL-80	Installation of Membrane System	8	02-Sep-2	10-Sep-26	11-Oct-26	20-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		22	27-Oct-26	26-Nov-26	27-Aug-26 A	30-Dec-26	0.00	125,244.14	712,953.22	0%	17.57%	-79
PG-Q-CON-EXAD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	08-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-79
PG-Q-CON-EXAD-AR-40	Final Fixing of Accessories & Finishes	8	05-Nov-2	14-Nov-26	08-Dec-26	17-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EXAD-AR-20	Installation of Doors & Access Systems	6	15-Nov-2	21-Nov-26	17-Dec-26	24-Dec-26	0.00	0.00	250,488.29	0%	0%	0
PG-Q-CON-EXAD-AR-30	Installation of Logo	5	22-Nov-2	26-Nov-26	24-Dec-26	30-Dec-26	0.00	0.00	3,236.40	0%	0%	0
MECHANICAL WORK		16	12-Sep-2	30-Sep-26	20-Oct-26	08-Nov-26	494,018.57	0.00	667,968.77	73.96%	0%	0
PG-Q-CON-EXAD-ME-10	Installation of Main Air Package Units	5	12-Sep-2	16-Sep-26	20-Oct-26	26-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXAD-ME-20	Installation of Backup Air Package Unit	5	17-Sep-2	22-Sep-26	26-Oct-26	01-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXAD-ME-30	Installation of Complete HVAC System	6	24-Sep-2	30-Sep-26	01-Nov-26	08-Nov-26	34,790.04	0.00	208,740.24	16.67%	0%	0
ELECTRICAL WORK		67	17-Aug-2	26-Oct-26	27-Aug-26 A	03-Dec-26	417,480.48	125,244.14	1,085,449.25	38.46%	11.54%	-23
PG-Q-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-2	30-Aug-26	27-Aug-26 A	01-Oct-26	208,740.24	125,244.14	208,740.24	100%	60%	-18
PG-Q-CON-EXAD-EL-20	Installation of Lighting System	12	31-Aug-2	13-Sep-26	01-Oct-26	15-Oct-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXAD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	01-Oct-26	06-Oct-26	08-Nov-26	14-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EXAD-EL-40	Installation of Backup Generator	6	07-Oct-26	13-Oct-26	14-Nov-26	21-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EXAD-EL-50	Installation of Smart Dome System	11	14-Oct-26	26-Oct-26	21-Nov-26	03-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		163	06-May-2	20-Oct-26	06-May-26 A	17-Nov-26	170,226.24	286,308.66	324,844.38	52.4%	88.14%	-24
CIVIL WORK		162	06-May-2	19-Oct-26	06-May-26 A	16-Nov-26	72,635.70	199,628.64	227,117.58	31.98%	87.9%	-24

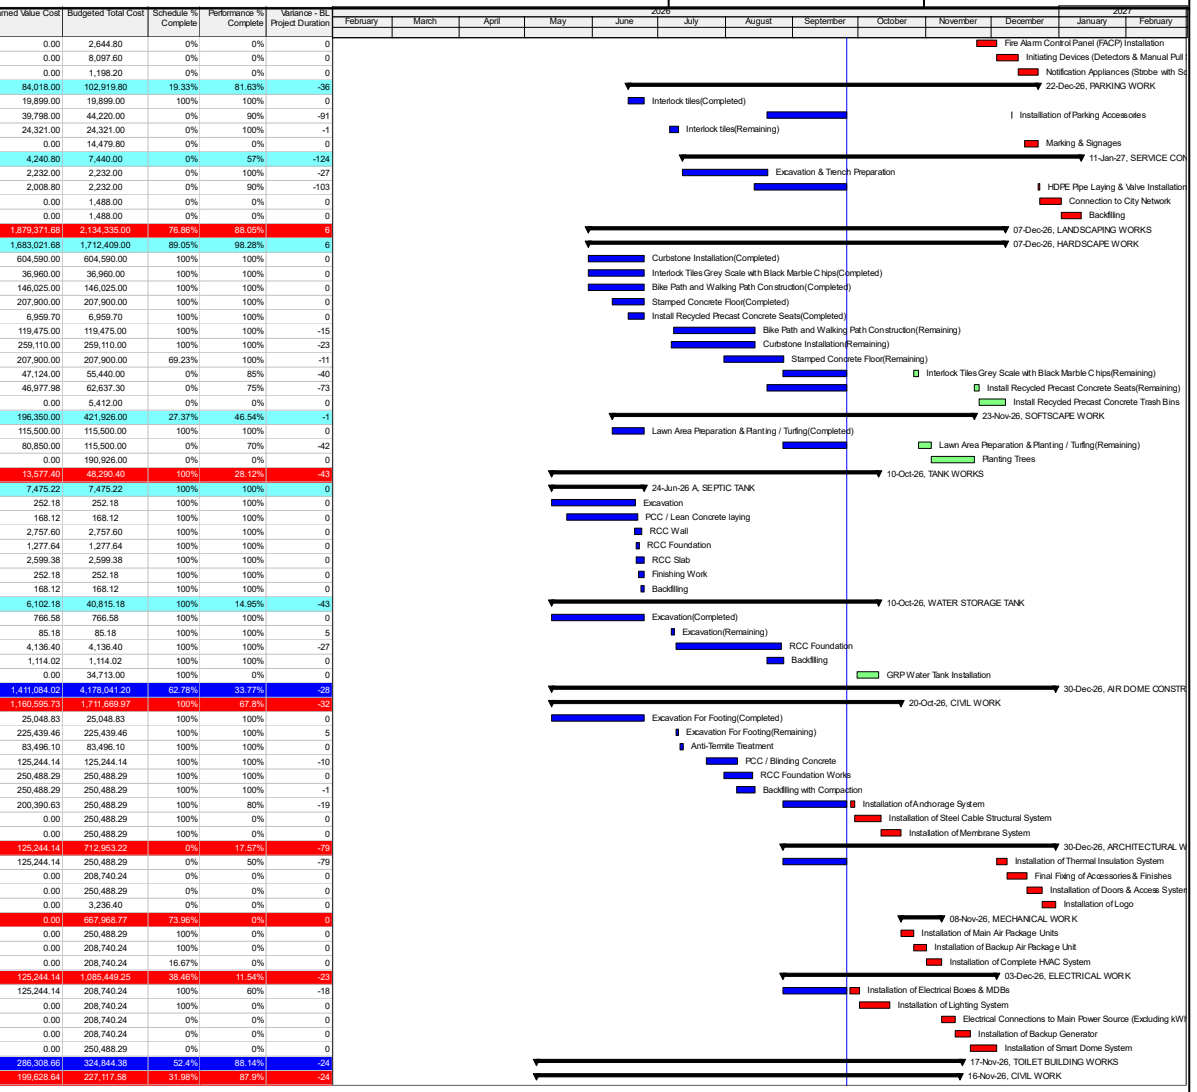


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
STRUCTURAL WORK		85	06-May-26	04-Aug-26	06-May-26 A	10-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	22
PG-Q-CON-B-STR-10	Excavation up to bottom of footing	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-Q-CON-B-STR-20	Anti-termite treatment and Polyethene Sheet	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	3,294.00	3,294.00	3,294.00	100%	100%	0
PG-Q-CON-B-STR-30	Backfilling with selected fill material (under footing)	1	13-May-26	13-May-26	13-May-26 A	13-May-26 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-Q-CON-B-STR-40	Raft Foundation Work	21	13-May-26	10-Jun-26	13-May-26 A	10-Jun-26 A	2,534.40	2,534.40	2,534.40	100%	100%	0
PG-Q-CON-B-STR-50	Autoclaved aerated panel (walls)	4	25-Jul-26	28-Jul-26	08-Jul-26 A	09-Jul-26 A	11,340.00	11,340.00	11,340.00	100%	100%	2
PG-Q-CON-B-STR-60	Autoclaved aerated panel (ceiling)	3	29-Jul-26	01-Aug-26	09-Jul-26 A	10-Jul-26 A	8,505.00	8,505.00	8,505.00	100%	100%	2
PG-Q-CON-B-STR-70	Autoclaved aerated panel (parapet)	3	02-Aug-26	04-Aug-26	09-Jul-26 A	10-Jul-26 A	8,505.00	8,505.00	8,505.00	100%	100%	2
ARCHITECTURAL WORK		107	05-Aug-26	19-Oct-26	12-Jul-26 A	16-Nov-26	34,655.70	161,648.64	189,137.58	18.32%	85.47%	-45
GENERAL FINISHES		107	05-Aug-26	19-Oct-26	12-Jul-26 A	16-Nov-26	9,510.50	72,586.26	84,120.00	11.31%	86.29%	-45
PG-Q-CON-B-AR-GF-10	Block Works	6	05-Aug-26	11-Aug-26	12-Jul-26 A	16-Jul-26 A	2,484.00	2,484.00	2,484.00	100%	100%	1
PG-Q-CON-B-AR-GF-20	Plaster	7	12-Aug-26	19-Aug-26	22-Jul-26 A	05-Aug-26 A	4,427.40	4,427.40	4,427.40	100%	100%	-6
PG-Q-CON-B-AR-GF-30	False Ceiling Installation & Finishing	7	20-Aug-26	27-Aug-26	20-Aug-26 A	10-Sep-26 A	873.60	873.60	873.60	100%	100%	-11
PG-Q-CON-B-AR-GF-40	Wall Paint	12	16-Sep-26	30-Sep-26	20-Aug-26 A	06-Sep-26 A	1,725.50	2,958.00	2,958.00	58.33%	100%	-3
PG-Q-CON-B-AR-GF-50	Epoxy Flooring	6	01-Oct-26	07-Oct-26	20-Aug-26 A	23-Sep-26 A	0.00	273.60	273.60	0%	100%	-23
PG-Q-CON-B-AR-GF-80	Facade Finishing Work	8	01-Oct-26	10-Oct-26	20-Aug-26 A	10-Sep-26 A	0.00	52,278.00	52,278.00	0%	100%	-11
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	03-Nov-26	0.00	9,291.66	13,273.80	0%	70%	-53
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	11-Nov-26	16-Nov-26	0.00	0.00	7,551.60	0%	0%	0
WET AREA FINISHES		59	20-Aug-26	14-Oct-26	06-Aug-26 A	08-Nov-26	25,145.20	75,762.18	81,123.78	31%	93.39%	-33
PG-Q-CON-B-AR-WF-10	False Ceiling Installation & Finishing	7	20-Aug-26	27-Aug-26	27-Aug-26 A	04-Sep-26 A	2,898.00	2,898.00	2,898.00	100%	100%	0
PG-Q-CON-B-AR-WF-20	Wall Tiles and Partition Work	6	16-Sep-26	22-Sep-26	06-Aug-26 A	14-Aug-26 A	21,283.20	21,283.20	21,283.20	100%	100%	-1
PG-Q-CON-B-AR-WF-30	Waterproofing on Floor	6	24-Sep-26	30-Sep-26	14-Aug-26 A	07-Sep-26 A	964.00	5,784.00	5,784.00	16.67%	100%	-15
PG-Q-CON-B-AR-WF-40	Floor Tiles Works	6	01-Oct-26	07-Oct-26	14-Aug-26 A	07-Sep-26 A	0.00	6,489.00	6,489.00	0%	100%	-15
PG-Q-CON-B-AR-WF-50	Toilet accessories Installation Works	6	08-Oct-26	14-Oct-26	27-Aug-26 A	10-Sep-26 A	0.00	39,307.98	39,307.98	0%	100%	-6
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	02-Nov-26	08-Nov-26	0.00	0.00	5,361.60	0%	0%	0
ROOF FINISHES		29	01-Oct-26	19-Oct-26	20-Aug-26 A	16-Nov-26	0.00	13,300.20	23,893.80	0%	55.66%	-59
PG-Q-CON-B-AR-RF-10	Waterproofing on Floor	4	01-Oct-26	05-Oct-26	20-Aug-26 A	08-Sep-26 A	0.00	4,158.00	4,158.00	0%	100%	-13
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	15-Oct-26	0.00	9,142.20	10,158.00	0%	90%	-42
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26	19-Oct-26	16-Nov-26	16-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		132	16-Jun-26	20-Oct-26	16-Jun-26 A	17-Nov-26	97,590.54	86,680.02	97,726.80	99.86%	88.7%	-24
MECANICAL WORKS		132	16-Jun-26	20-Oct-26	16-Jun-26 A	17-Nov-26	79,343.22	68,432.70	79,479.48	99.83%	86.1%	-24
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	17-Nov-26	17-Nov-26	0.00	0.00	136.26	0%	0%	0
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	17-Nov-26	17-Nov-26	0.00	0.00	136.26	0%	0%	0
SEWER AND DRAINAGE SYSTEM		103	16-Jun-26	02-Sep-26	16-Jun-26 A	14-Oct-26	11,290.02	8,064.30	11,290.02	100%	71.43%	-35
PG-Q-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	16-Jun-26	17-Jun-26	16-Jun-26 A	17-Jun-26 A	3,225.72	3,225.72	3,225.72	100%	100%	0
PG-Q-CON-B-GF-DR-20	Sewer and Drainge System Pipes and fittings Installation	2	16-Jun-26	17-Jun-26	16-Jun-26 A	17-Jun-26 A	4,838.58	4,838.58	4,838.58	100%	100%	0
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	13-Oct-26	14-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		26	12-Aug-26	23-Aug-26	13-Aug-26 A	07-Oct-26	12,127.20	4,442.40	12,127.20	100%	36.63%	-36
PG-Q-CON-B-GF-AC-10	Duct Work and Exhaust Fan Installation	7	12-Aug-26	19-Aug-26	13-Aug-26 A	20-Aug-26 A	4,442.40	4,442.40	4,442.40	100%	100%	0
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26	23-Aug-26	04-Oct-26	07-Oct-26	7,684.80	0.00	7,684.80	100%	0%	0
WATER SUPPLY SYSTEM		80	16-Jun-26	31-Aug-26	16-Jun-26 A	07-Sep-26 A	55,926.00	55,926.00	55,926.00	100%	100%	-5
PG-Q-CON-B-GF-WS-10	Water Supply Main Lines Installation	2	16-Jun-26	17-Jun-26	16-Jun-26 A	17-Jun-26 A	5,702.40	5,702.40	5,702.40	100%	100%	0
PG-Q-CON-B-GF-WS-20	Water Supply Pipes Installation (Cold and Hot Water)	2	24-Aug-26	25-Aug-26	22-Jul-26 A	31-Jul-26 A	13,857.60	13,857.60	13,857.60	100%	100%	-6
PG-Q-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	29-Aug-26	31-Aug-26	20-Aug-26 A	07-Sep-26 A	36,366.00	36,366.00	36,366.00	100%	100%	-12
ELECTRICAL WORKS		47	13-Jul-26	15-Sep-26	22-Jul-26 A	08-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	14
PG-Q-CON-B-GF-EL-10	Pipes & Conduits Installation	8	13-Jul-26	21-Jul-26	22-Jul-26 A	23-Jul-26 A	1,983.60	1,983.60	1,983.60	100%	100%	6
PG-Q-CON-B-GF-EL-50	Electrical Light Fixtures Installation	2	03-Sep-26	05-Sep-26	20-Aug-26 A	08-Sep-26 A	7,337.52	7,337.52	7,337.52	100%	100%	-15
PG-Q-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	06-Sep-26	08-Sep-26	20-Aug-26 A	08-Sep-26 A	1,983.60	1,983.60	1,983.60	100%	100%	-14
PG-Q-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	08-Sep-26 A	4,959.00	4,959.00	4,959.00	100%	100%	-14
PG-Q-CON-B-GF-EL-20	Electrical & ELV Wiring Works	3	13-Sep-26	15-Sep-26	20-Aug-26 A	08-Sep-26 A	1,983.60	1,983.60	1,983.60	100%	100%	-14
PROJECT CLOSOUT		202	23-May-26	16-Dec-26	22-May-26 A	19-Jan-27	52,612.62	300,768.81	1,753,754.00	3%	17.15%	-28
PG-Q-PCL-10	Testing, Commissioning for All Systems(Completed)	25	23-May-26	24-Jun-26	22-May-26 A	24-Jun-26 A	52,612.62	52,612.62	52,612.62	100%	100%	0
PG-Q-PCL-20	As-Built Drawings	15	15-Nov-26	02-Dec-26	23-Sep-26 A	06-Jan-27	0.00	35,075.08	175,375.40	0%	20%	-74
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	15-Nov-26	26-Nov-26	06-Aug-26 A	30-Dec-26	0.00	213,081.11	473,513.58	0%	45%	-114
PG-Q-PCL-30	Snag list Submission	3	28-Nov-26	30-Nov-26	30-Dec-26	03-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-40	Snag list Closeout	10	01-Dec-26	12-Dec-26	03-Jan-27	14-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-50	Issuing Approvals	3	13-Dec-26	15-Dec-26	14-Jan-27	18-Jan-27	0.00	0.00	175,375.40	0%	0%	0
PG-Q-PCL-60	Handing Over	1	16-Dec-26	16-Dec-26	18-Jan-27	19-Jan-27	0.00	0.00	175,375.40	0%	0%	0
HAIL		269	17-Feb-26	16-Dec-26	17-Feb-26 A	09-Jan-27	5,099,974.88	5,139,514.80	6,814,652.00	74.84%	75.42%	-20
MOBILIZATION		29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-HMOB-CAM-10	Temporary Underground Utilities works	28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-CAM-20	Temporary Porta-Cabins	21	26-Feb-26	28-Mar-26	26-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-CAM-30	Temporary Toilets	21	26-Feb-26	28-Mar-26	26-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-CAM-40	Temporary Mosque	13	08-Mar-26	28-Mar-26	08-Mar-26 A	27-Mar-26 A	0.00	0.00	0.00	100%	100%	0
SITE OFFICES		29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-HMOB-SO-10	Temporary Underground Utilities works	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-20	Temporary Porta-Cabins	23	25-Feb-26	29-Mar-26	25-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-30	Temporary Toilets	23	25-Feb-26	29-Mar-26	25-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-40	Temporary Mosque	17	04-Mar-26	29-Mar-26	04-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-50	Car Parking Area	10	12-Mar-26	29-Mar-26	12-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
GENERAL REQUIEREMENTS		51	17-Feb-26	23-Apr-26	17-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-GEN-20	HSSE Submission Plan	51	17-Feb-26	23-Apr-26	17-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0

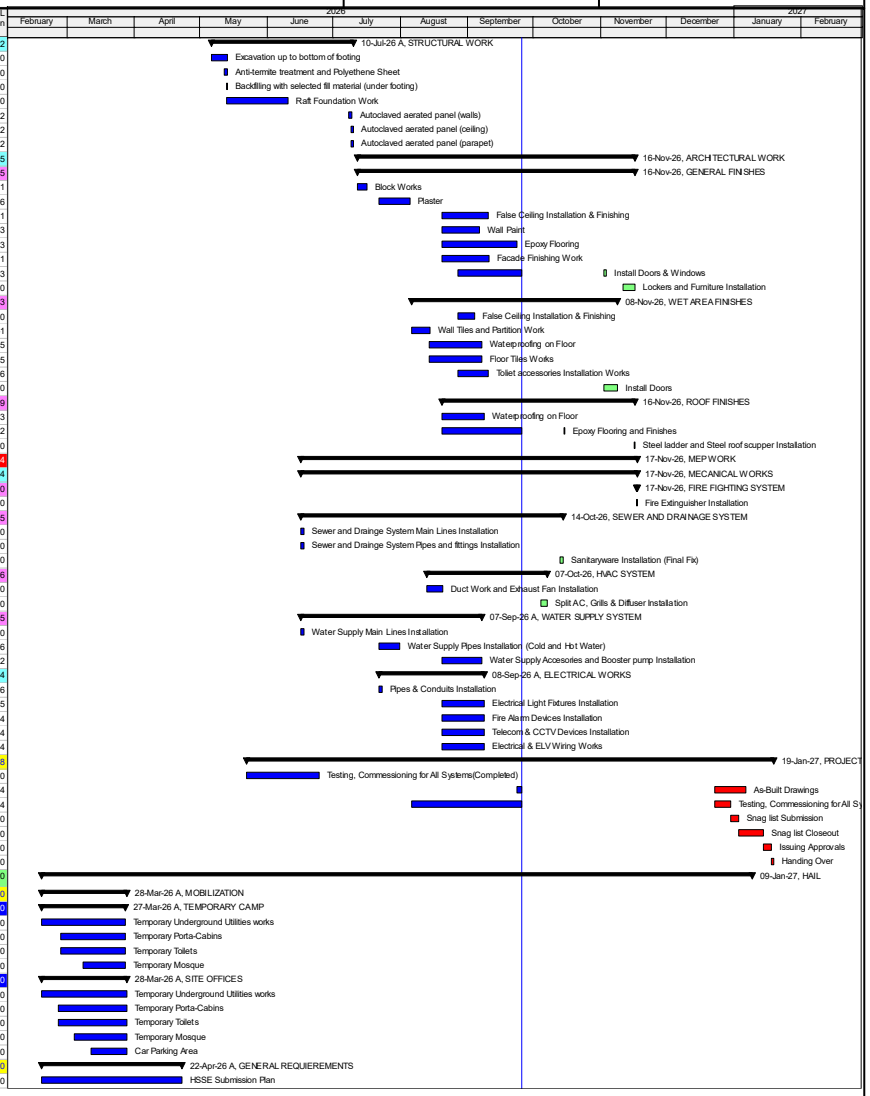


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-GEN-30	Surveying report Submission Plan	51	17-Feb-2	23-Apr-26	17-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-GEN-40	Baseline Submission	6	28-Feb-2	07-Mar-26	28-Feb-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-GEN-10	QA/QC Submission Plan	16	12-Mar-2	05-Apr-26	12-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	100%	100%	0
ENGINEERING		168	17-Feb-2	14-Jul-26	17-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
SHOP DRAWINGS SUBMITTALS		93	17-Feb-2	16-Jun-26	17-Feb-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
STRUCTURAL DRAWINGS		61	17-Feb-2	05-May-26	17-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
PROJECT FENCE		57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-10	Excavation Drawings	57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-20	Foundation Drawings	55	19-Feb-2	30-Apr-26	19-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
TOILET BUILDING		41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-30	Excavation Drawings	41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-40	Foundation Drawings	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-60	Excavation Drawings	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-50	Foundation Drawings	37	25-Feb-2	14-Apr-26	25-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		55	25-Feb-2	05-May-26	25-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-70	Reinforcement Detail Drawings	55	25-Feb-2	05-May-26	25-Feb-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-80	Concrete Detail Drawings	52	01-Mar-2	05-May-26	01-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
TOILET BUILDING		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-AR-SD-SB-10	Ground Floor Plan	36	23-Feb-2	11-Apr-26	23-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-20	Roof Floor Plan	35	28-Feb-2	14-Apr-26	28-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-50	Floor Finish Layout	32	28-Feb-2	09-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-60	Reflected Ceiling Layout	32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-70	Enlarged Toilets Layout	35	28-Feb-2	14-Apr-26	28-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-30	Elevations	29	03-Mar-2	11-Apr-26	03-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-80	Doors & Windows Schedule	32	03-Mar-2	14-Apr-26	03-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-90	Aluminum Work	32	03-Mar-2	14-Apr-26	03-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-100	Cladding Details	32	03-Mar-2	14-Apr-26	03-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-40	Sections	27	05-Mar-2	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
LANDSCAPE DRAWINGS		38	24-Feb-2	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-LS-SD-SB-10	Hardscape Layout Plan	38	24-Feb-2	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-20	Interlock Tile Details	35	24-Feb-2	11-Apr-26	24-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-30	Stamped Concrete Pattern & Section	38	24-Feb-2	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-40	Tartan Flooring Layout & Details	38	24-Feb-2	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-50	Bike Path Layout & Details	35	24-Feb-2	11-Apr-26	24-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-60	Walking Path layout & Details	35	24-Feb-2	11-Apr-26	24-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-70	Tree Planting Plan & Details	35	24-Feb-2	11-Apr-26	24-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-80	Traffic Sign Location & Details	38	24-Feb-2	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-90	Football Playground Layout	38	24-Feb-2	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-100	Playground Details	35	24-Feb-2	11-Apr-26	24-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		52	01-Mar-2	05-May-26	01-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
WATER SUPPLY SYSTEM		31	01-Mar-2	11-Apr-26	01-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-SB-20	Pump Room Layout	31	01-Mar-2	11-Apr-26	01-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-10	Cold & Hot Water Piping Layout	27	05-Mar-2	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-30	Booster Pump Details	27	05-Mar-2	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-40	GRP Water Tank Details	23	10-Mar-2	11-Apr-26	10-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		27	05-Mar-2	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-SB-50	Drainage Layout	27	05-Mar-2	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-60	Floor Drains & Cleanouts Details	23	10-Mar-2	11-Apr-26	10-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-70	Inspection Chamber Details	20	14-Mar-2	11-Apr-26	14-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		44	10-Mar-2	05-May-26	10-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-SB-80	HDPE Pipe Routing	44	10-Mar-2	05-May-26	10-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-90	Irrigation Network Layout	41	14-Mar-2	05-May-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL DRAWINGS		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
POWER AND LIGHTING SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-SB-10	Main Distribution Board (MDB) Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-20	Pump Room Power Panel	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-30	Street Lighting Power Panel	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-40	Site Lighting Pole Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-SB-50	Telecom & Data Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-60	CCTV Camera Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-70	Access Control Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-80	AV System Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-SB-90	Fire Alarm Layout	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-100	Detector & Manual Call Point Details	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-110	Control Panel Wiring Diagram	27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	0
SHOP DRAWINGS APPROVALS		92	19-Feb-2	17-Jun-26	19-Feb-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
STRUCTURAL DRAWINGS		61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PROJECT FENCE		55	19-Feb-2	30-Apr-26	19-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-10	Excavation Drawings	55	19-Feb-2	30-Apr-26	19-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0

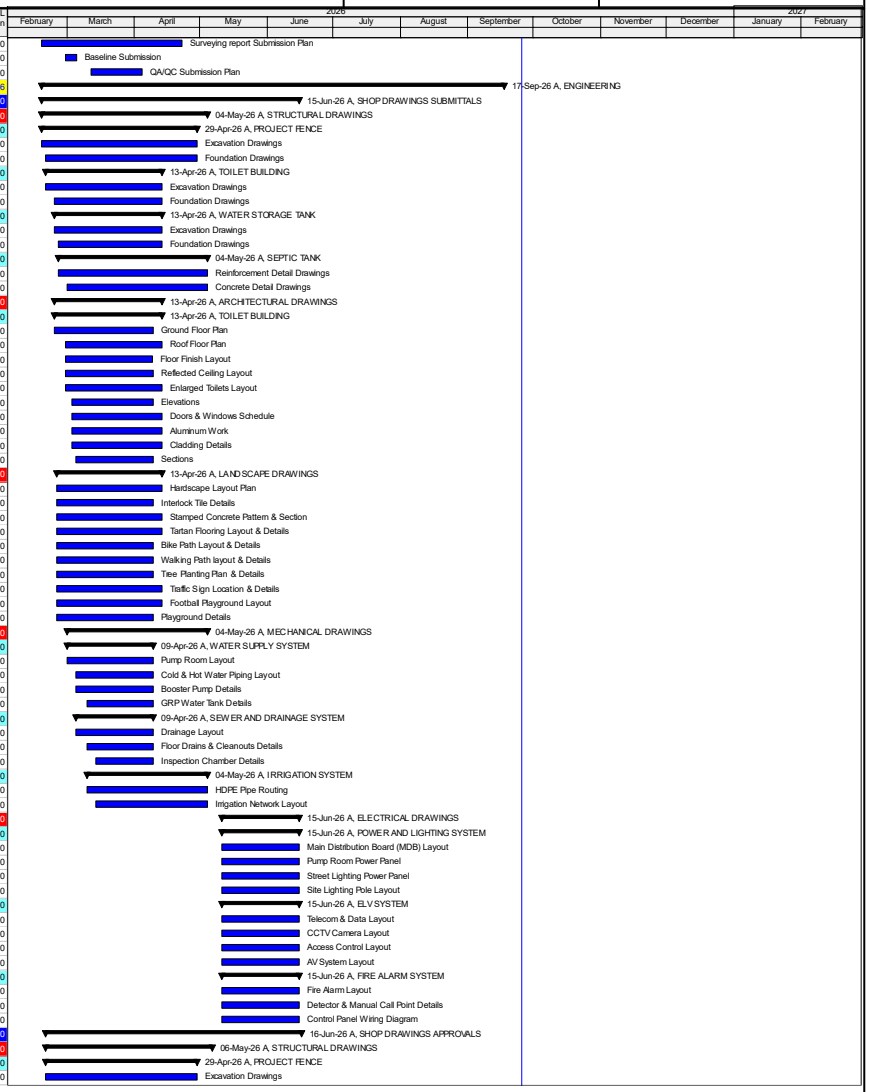


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-EN-ST-SD-AP-20	Foundation Drawings	52	24-Feb-2	30-Apr-26	24-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
TOILET BUILDING		42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-30	Excavation Drawings	42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-40	Foundation Drawings	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-50	Excavation Drawings	40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-60	Foundation Drawings	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-70	Reinforcement Detail Drawings	54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-80	Concrete Detail Drawings	51	04-Mar-2	07-May-26	04-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		38	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
TOILET BUILDING		38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-AR-SD-AP-10	Ground Floor Plan	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-20	Roof Floor Plan	35	03-Mar-2	18-Apr-26	03-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-50	Floor Finish Layout	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-60	Reflected Ceiling Layout	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-70	Enlarged Toilets Layout	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-30	Elevations	32	07-Mar-2	18-Apr-26	07-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-80	Doors & Windows Schedule	32	07-Mar-2	18-Apr-26	07-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-90	Aluminum Work	31	08-Mar-2	18-Apr-26	08-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-100	Cladding Details	31	08-Mar-2	18-Apr-26	08-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-40	Sections	29	10-Mar-2	18-Apr-26	10-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
LANDSCAPE DRAWINGS		38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-LS-SD-AP-50	Bike Path Layout & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-60	Walking Path layout & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-80	Traffic Sign Location & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-10	Hardscape Layout Plan	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-40	Tartan Flooring Layout & Details	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-70	Tree Planting Plan & Details	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-90	Football Playground Layout	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-100	Playground Details	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-20	Interlock Tile Details	29	10-Mar-2	18-Apr-26	10-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-30	Stamped Concrete Pattern & Section	23	17-Mar-2	18-Apr-26	17-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
WATER SUPPLY SYSTEM		26	10-Mar-2	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-AP-10	Cold & Hot Water Piping Layout	26	10-Mar-2	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-30	Booster Pump Details	25	11-Mar-2	14-Apr-26	11-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-40	GRP Water Tank Details	22	15-Mar-2	14-Apr-26	15-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-20	Pump Room Layout	20	17-Mar-2	14-Apr-26	17-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		26	10-Mar-2	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-AP-50	Drainage Layout	26	10-Mar-2	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-60	Floor Drains & Cleanouts Details	20	17-Mar-2	14-Apr-26	17-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-70	Inspection Chamber Details	20	17-Mar-2	14-Apr-26	17-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		43	14-Mar-2	07-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-AP-80	HDPE Pipe Routing	43	14-Mar-2	07-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-90	Irrigation Network Layout	39	18-Mar-2	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL DRAWINGS		27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
POWER AND LIGHTING SYSTEM		27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-AP-10	Main Distribution Board (MDB) Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-20	Pump Room Power Panel	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-30	Street Lighting Power Panel	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-40	Site Lighting Pole Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-AP-50	Telecom & Data Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-60	CCTV Camera Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-70	Access Control Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-80	AV System Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-AP-90	Fire Alarm Layout	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-100	Detector & Manual Call Point Details	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-110	Control Panel Wiring Diagram	27	12-May-2	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
MATERIAL SUBMITTALS		166	17-Feb-2	06-Jul-26	17-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
LONG LEAD ITEMS		163	21-Feb-2	06-Jul-26	21-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
EXTERNAL / LANDSCAPE WORK		56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-LS-MS-20	Benches, Seats (Rectangular & Circular)	56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MS-30	Fence, gates and accessories	56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MS-10	Bike and Walk Path Materials	48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		47	08-Mar-2	06-May-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-SP-MS-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	47	08-Mar-2	06-May-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-MS-20	Tartan Floor	47	08-Mar-2	06-May-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-CO-MS-10	Autoclaved Aerated Panel	41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		44	11-Mar-2	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0

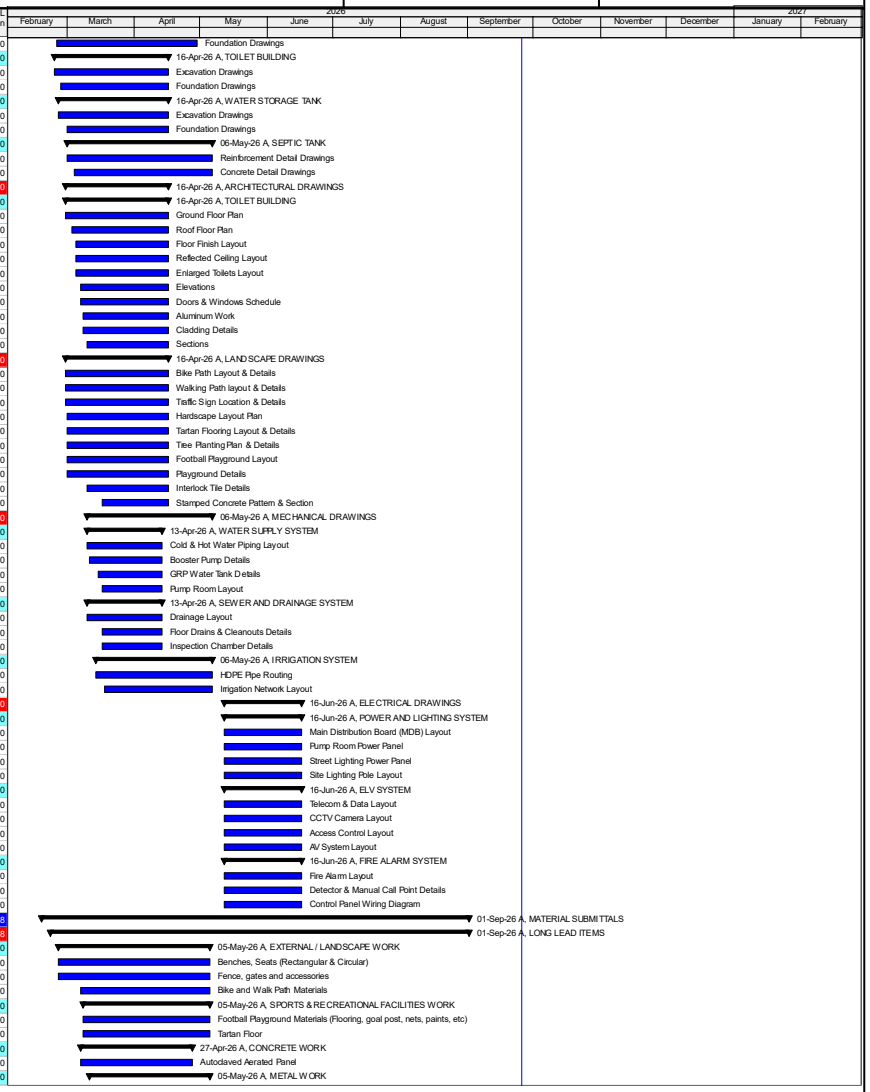


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-LL-MT-MS-10	Metal Doors	44	11-Mar-2	05-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-MS-20	Curtain Wall	44	11-Mar-2	05-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		44	11-Mar-2	05-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-PB-MS-10	Booster Pump	44	11-Mar-2	05-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-MS-20	GRP Sectional Panel Water Tanks (4x3x3m)	40	16-Mar-2	06-May-26	16-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		60	21-Feb-2	07-May-26	21-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-IR-MS-10	HDPE Pipes	60	21-Feb-2	07-May-26	21-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MS-20	Irrigation Control System	60	21-Feb-2	07-May-26	21-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		99	12-May-2	06-Jul-26	12-May-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-LL-EL-MS-10	Main Distribution Board(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-30	Site Lighting Poles(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-40	Lighting Fixtures(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-70	Security and Access Control System Materials(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-80	Fire Alarm System Materials(Completed)	34	12-May-2	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-10_R	Main Distribution Board(Remaining)	8	25-Jun-26	04-Jul-26	11-Jul-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	-13
PG-H-PR-LL-EL-MS-20_R	Power Panels (Pump, Street Light)(Remaining)	8	25-Jun-26	04-Jul-26	11-Jul-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	-13
PG-H-PR-LL-EL-MS-30_R	Site Lighting Poles(Remaining)	10	25-Jun-26	06-Jul-26	11-Jul-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-EL-MS-40_R	Lighting Fixtures(Remaining)	10	25-Jun-26	06-Jul-26	11-Jul-26 A	23-Jul-26 A	0.00	0.00	0.00	100%	100%	-2
PG-H-PR-LL-EL-MS-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	7	25-Jun-26	02-Jul-26	11-Jul-26 A	01-Sep-26 A	0.00	0.00	0.00	100%	100%	-38
PG-H-PR-LL-EL-MS-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	10	25-Jun-26	06-Jul-26	11-Jul-26 A	01-Sep-26 A	0.00	0.00	0.00	100%	100%	-35
PG-H-PR-LL-EL-MS-70_R	Security and Access Control System Materials(Remaining)	10	25-Jun-26	06-Jul-26	11-Jul-26 A	01-Sep-26 A	0.00	0.00	0.00	100%	100%	-35
PG-H-PR-LL-EL-MS-80_R	Fire Alarm System Materials(Remaining)	10	25-Jun-26	06-Jul-26	27-Aug-26 A	01-Sep-26 A	0.00	0.00	0.00	100%	100%	6
SHORT LEAD ITEMS		28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-LS-MS-10	Backfilling Materials	23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-30	Compacted Natural Ground Soil	20	21-Feb-2	17-Mar-26	21-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-60	Traffic Signages	8	08-Mar-2	17-Mar-26	08-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-20	Interlock tiles	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-40	Curb Stone	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-50	Thermoplastic pavement road marking	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-70	Trees	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-80	Lawn	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-CO-MS-10	Steel Rebar	17	17-Feb-2	10-Mar-26	17-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-20	Concrete	13	23-Feb-2	10-Mar-26	23-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-40	CMU Block	19	01-Mar-2	28-Mar-26	01-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-50	Concrete Repair & Protection Materials	19	01-Mar-2	28-Mar-26	01-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-30	Screed	10	11-Mar-2	28-Mar-26	11-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AR-MS-10	Ceramic tiles	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-20	Anti-slip Granite tiles	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-30	Epoxy Paint	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-40	Cement Plaster	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-50	Acrylic Paint	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-60	Stone Cladding	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-70	Aluminum Plates	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-80	Phenolic Partition	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-90	Glass Partition	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-100	Gypsum Boards	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-120	Waterproofing System Materials	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		9	07-Mar-2	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-MT-MS-20	Galvanized Steel Roof Scupper	9	07-Mar-2	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-MS-30	Galvanized Steel Cover with frame	9	07-Mar-2	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-MS-10	Galvanized Steel Ladder	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AC-MS-10	Split Air Conditioning Unit	19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-MS-20	Air Duct	15	28-Feb-2	17-Mar-26	28-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-MS-30	Diffusers and Grills	11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-MS-40	Exhaust fans	11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-PB-MS-10	PPR Pipes & Valves	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-MS-20	UPCV Pipes	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-MS-30	Sanitary Drainage Fixtures	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-IR-MS-10	Gate Valve including valve box	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-MS-20	Bubblers and Sprayers	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-EL-MS-10	Wiring Devices Materials	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0

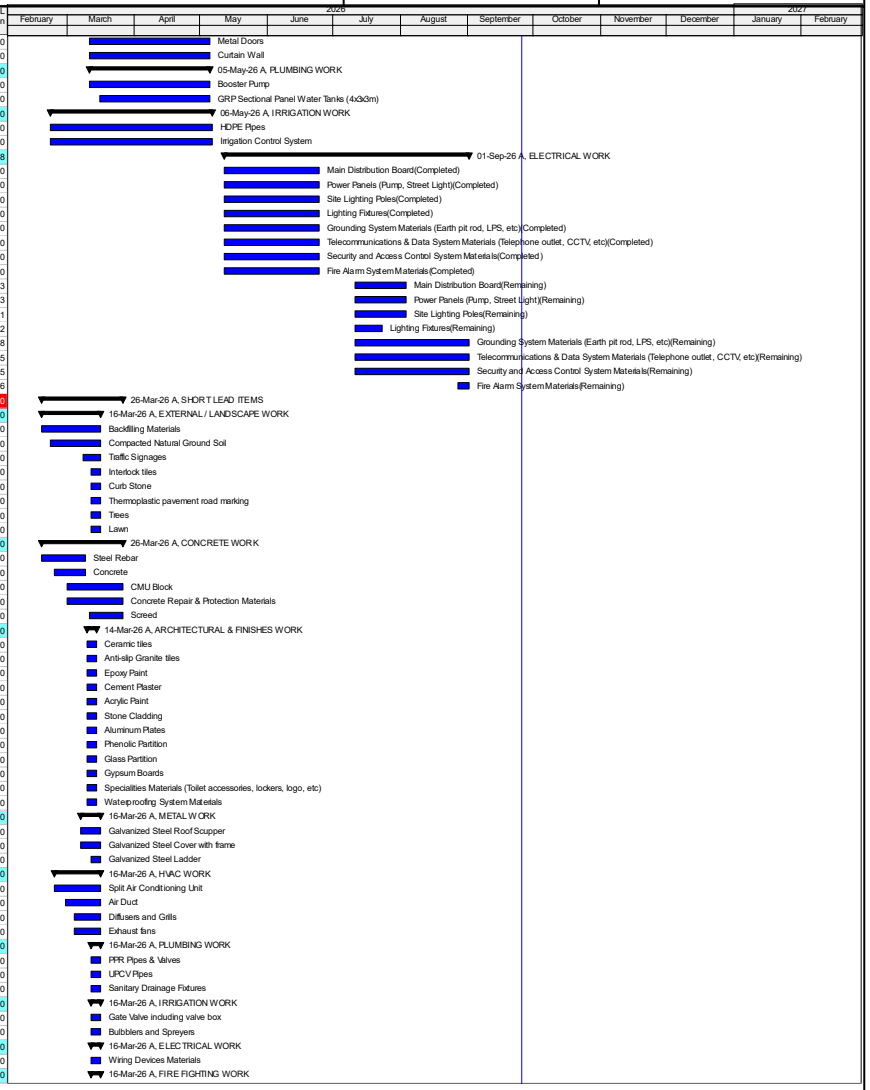


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-SL-FF-MS-10	Fire Extinguishers	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
MATERIAL APPROVALS		165	21-Feb-26	14-Jul-26	21-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
LONG LEAD ITEMS		162	25-Feb-26	14-Jul-26	25-Feb-26 A	17-Sep-26 A	111,065.49	111,065.49	111,065.49	100%	100%	-56
EXTERNAL / LANDSCAPE WORK		57	25-Feb-26	06-May-26	25-Feb-26 A	06-May-26 A	26,079.63	26,079.63	26,079.63	100%	100%	0
PG-H-PR-LL-LS-MA-20	Benches, Seats (Rectangular & Circular)	57	25-Feb-26	06-May-26	25-Feb-26 A	06-May-26 A	6,327.69	6,327.69	6,327.69	100%	100%	0
PG-H-PR-LL-LS-MA-30	Fence, gates and accessories	51	04-Mar-26	06-May-26	04-Mar-26 A	06-May-26 A	3,290.94	3,290.94	3,290.94	100%	100%	0
PG-H-PR-LL-LS-MA-10	Bike and Walk Path Materials	41	16-Mar-26	06-May-26	16-Mar-26 A	06-May-26 A	16,461.00	16,461.00	16,461.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		43	14-Mar-26	06-May-26	14-Mar-26 A	06-May-26 A	38,839.50	38,839.50	38,839.50	100%	100%	0
PG-H-PR-LL-SP-MA-20	Tartan Floor	43	14-Mar-26	06-May-26	14-Mar-26 A	06-May-26 A	24,570.00	24,570.00	24,570.00	100%	100%	0
PG-H-PR-LL-SP-MA-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	14,269.50	14,269.50	14,269.50	100%	100%	0
CONCRETE WORK		45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
PG-H-PR-LL-CO-MA-10	Autoclaved Aerated Panel	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
PG-H-PR-LL-MT-MA-10	Metal Doors	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	127.53	127.53	127.53	100%	100%	0
PG-H-PR-LL-MT-MA-20	Curtain Wall	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	761.70	761.70	761.70	100%	100%	0
PLUMBING WORK		41	16-Mar-26	06-May-26	16-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
PG-H-PR-LL-PB-MA-10	Booster Pump	41	16-Mar-26	06-May-26	16-Mar-26 A	06-May-26 A	1,818.30	1,818.30	1,818.30	100%	100%	0
PG-H-PR-LL-PB-MA-20	GRP Sectional Panel Water Tanks (4x3x3m)	38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	1,735.65	1,735.65	1,735.65	100%	100%	0
IRRIGATION WORK		55	28-Feb-26	06-May-26	28-Feb-26 A	06-May-26 A	12,818.25	12,818.25	12,818.25	100%	100%	0
PG-H-PR-LL-IR-MA-10	HDPE Pipes	55	28-Feb-26	06-May-26	28-Feb-26 A	06-May-26 A	8,272.50	8,272.50	8,272.50	100%	100%	0
PG-H-PR-LL-IR-MA-20	Irrigation Control System	55	28-Feb-26	06-May-26	28-Feb-26 A	06-May-26 A	4,545.75	4,545.75	4,545.75	100%	100%	0
ELECTRICAL WORK		101	12-May-26	14-Jul-26	12-May-26 A	17-Sep-26 A	27,467.43	27,467.43	27,467.43	100%	100%	-56
PG-H-PR-LL-EL-MA-10	Main Distribution Board(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	347.13	347.13	347.13	100%	100%	0
PG-H-PR-LL-EL-MA-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	277.70	277.70	277.70	100%	100%	0
PG-H-PR-LL-EL-MA-30	Site Lighting Poles(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	14,891.18	14,891.18	14,891.18	100%	100%	0
PG-H-PR-LL-EL-MA-40	Lighting Fixtures(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	897.98	897.98	897.98	100%	100%	0
PG-H-PR-LL-EL-MA-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	702.93	702.93	702.93	100%	100%	0
PG-H-PR-LL-EL-MA-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	685.57	685.57	685.57	100%	100%	0
PG-H-PR-LL-EL-MA-70	Security and Access Control System Materials(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	867.93	867.93	867.93	100%	100%	0
PG-H-PR-LL-EL-MA-80	Fire Alarm System Materials(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	556.77	556.77	556.77	100%	100%	0
PG-H-PR-LL-EL-MA-10_R	Main Distribution Board(Remaining)	10	25-Jun-26	06-Jul-26	30-Jul-26 A	17-Sep-26 A	148.77	148.77	148.77	100%	100%	-33
PG-H-PR-LL-EL-MA-20_R	Power Panels (Pump, Street Light)(Remaining)	10	25-Jun-26	06-Jul-26	30-Jul-26 A	17-Sep-26 A	119.02	119.02	119.02	100%	100%	-33
PG-H-PR-LL-EL-MA-30_R	Site Lighting Poles(Remaining)	10	25-Jun-26	06-Jul-26	30-Jul-26 A	17-Sep-26 A	6,381.94	6,381.94	6,381.94	100%	100%	-33
PG-H-PR-LL-EL-MA-40_R	Lighting Fixtures(Remaining)	10	25-Jun-26	06-Jul-26	23-Jul-26 A	23-Jul-26 A	384.85	384.85	384.85	100%	100%	9
PG-H-PR-LL-EL-MA-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	10	25-Jun-26	06-Jul-26	27-Aug-26 A	17-Sep-26 A	293.81	293.81	293.81	100%	100%	-9
PG-H-PR-LL-EL-MA-70_R	Security and Access Control System Materials(Remaining)	10	25-Jun-26	06-Jul-26	27-Aug-26 A	17-Sep-26 A	371.97	371.97	371.97	100%	100%	-9
PG-H-PR-LL-EL-MA-80_R	Fire Alarm System Materials(Remaining)	10	25-Jun-26	06-Jul-26	27-Aug-26 A	17-Sep-26 A	238.62	238.62	238.62	100%	100%	-9
PG-H-PR-LL-EL-MA-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	10	04-Jul-26	14-Jul-26	27-Aug-26 A	17-Sep-26 A	301.26	301.26	301.26	100%	100%	-9
SHORT LEAD ITEMS		25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	93,374.07	93,374.07	93,374.07	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	72,133.44	72,133.44	72,133.44	100%	100%	0
PG-H-PR-SL-LS-MA-10	Backfilling Materials	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	19,575.00	19,575.00	19,575.00	100%	100%	0
PG-H-PR-SL-LS-MA-30	Compacted Natural Ground Soil	22	25-Feb-26	26-Mar-26	25-Feb-26 A	26-Mar-26 A	3,120.00	3,120.00	3,120.00	100%	100%	0
PG-H-PR-SL-LS-MA-60	Traffic Signages	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	198.36	198.36	198.36	100%	100%	0
PG-H-PR-SL-LS-MA-70	Trees	7	15-Mar-26	26-Mar-26	15-Mar-26 A	26-Mar-26 A	4,831.95	4,831.95	4,831.95	100%	100%	0
PG-H-PR-SL-LS-MA-80	Lawn	7	15-Mar-26	26-Mar-26	15-Mar-26 A	26-Mar-26 A	5,460.00	5,460.00	5,460.00	100%	100%	0
PG-H-PR-SL-LS-MA-20	Interlock tiles	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	17,494.50	17,494.50	17,494.50	100%	100%	0
PG-H-PR-SL-LS-MA-40	Curb Stone	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	20,928.00	20,928.00	20,928.00	100%	100%	0
PG-H-PR-SL-LS-MA-50	Thermoplastic pavement road marking	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	525.63	525.63	525.63	100%	100%	0
CONCRETE WORK		24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
PG-H-PR-SL-CO-MA-10	Steel Rebar	14	23-Feb-26	10-Mar-26	23-Feb-26 A	10-Mar-26 A	476.82	476.82	476.82	100%	100%	0
PG-H-PR-SL-CO-MA-20	Concrete	9	01-Mar-26	10-Mar-26	01-Mar-26 A	10-Mar-26 A	518.85	518.85	518.85	100%	100%	0
PG-H-PR-SL-CO-MA-40	CMU Block	15	05-Mar-26	26-Mar-26	05-Mar-26 A	26-Mar-26 A	124.20	124.20	124.20	100%	100%	0
PG-H-PR-SL-CO-MA-50	Concrete Repair & Protection Materials	15	05-Mar-26	26-Mar-26	05-Mar-26 A	26-Mar-26 A	372.00	372.00	372.00	100%	100%	0
PG-H-PR-SL-CO-MA-30	Screed	1	26-Mar-26	26-Mar-26	26-Mar-26 A	26-Mar-26 A	117.60	117.60	117.60	100%	100%	0
ARCHITECTURAL & FINISHES WORK		2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	8,114.01	8,114.01	8,114.01	100%	100%	0
PG-H-PR-SL-AR-MA-10	Ceramic tiles	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	571.95	571.95	571.95	100%	100%	0
PG-H-PR-SL-AR-MA-20	Anti-slip Granite tiles	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	535.50	535.50	535.50	100%	100%	0
PG-H-PR-SL-AR-MA-30	Epoxy Paint	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	111.18	111.18	111.18	100%	100%	0
PG-H-PR-SL-AR-MA-40	Cement Plaster	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	221.37	221.37	221.37	100%	100%	0
PG-H-PR-SL-AR-MA-50	Acrylic Paint	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	147.90	147.90	147.90	100%	100%	0
PG-H-PR-SL-AR-MA-60	Stone Cladding	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	1,852.20	1,852.20	1,852.20	100%	100%	0
PG-H-PR-SL-AR-MA-70	Aluminum Plates	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	182.46	182.46	182.46	100%	100%	0
PG-H-PR-SL-AR-MA-80	Phenolic Partition	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	1,340.40	1,340.40	1,340.40	100%	100%	0
PG-H-PR-SL-AR-MA-90	Glass Partition	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	155.40	155.40	155.40	100%	100%	0
PG-H-PR-SL-AR-MA-100	Gypsum Boards	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	188.58	188.58	188.58	100%	100%	0
PG-H-PR-SL-AR-MA-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	2,262.87	2,262.87	2,262.87	100%	100%	0
PG-H-PR-SL-AR-MA-120	Waterproofing System Materials	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	544.20	544.20	544.20	100%	100%	0
METAL WORK		10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
PG-H-PR-SL-MT-MA-20	Galvanized Steel Roof Scupper	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	31.32	31.32	31.32	100%	100%	0
PG-H-PR-SL-MT-MA-30	Galvanized Steel Cover with frame	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	85.71	85.71	85.71	100%	100%	0
PG-H-PR-SL-MT-MA-10	Galvanized Steel Ladder	7	15-Mar-26	26-Mar-26	15-Mar-26 A	26-Mar-26 A	361.86	361.86	361.86	100%	100%	0
HVAC WORK		20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
PG-H-PR-SL-AC-MA-10	Split Air Conditioning Unit	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	309.93	309.93	309.93	100%	100%	0

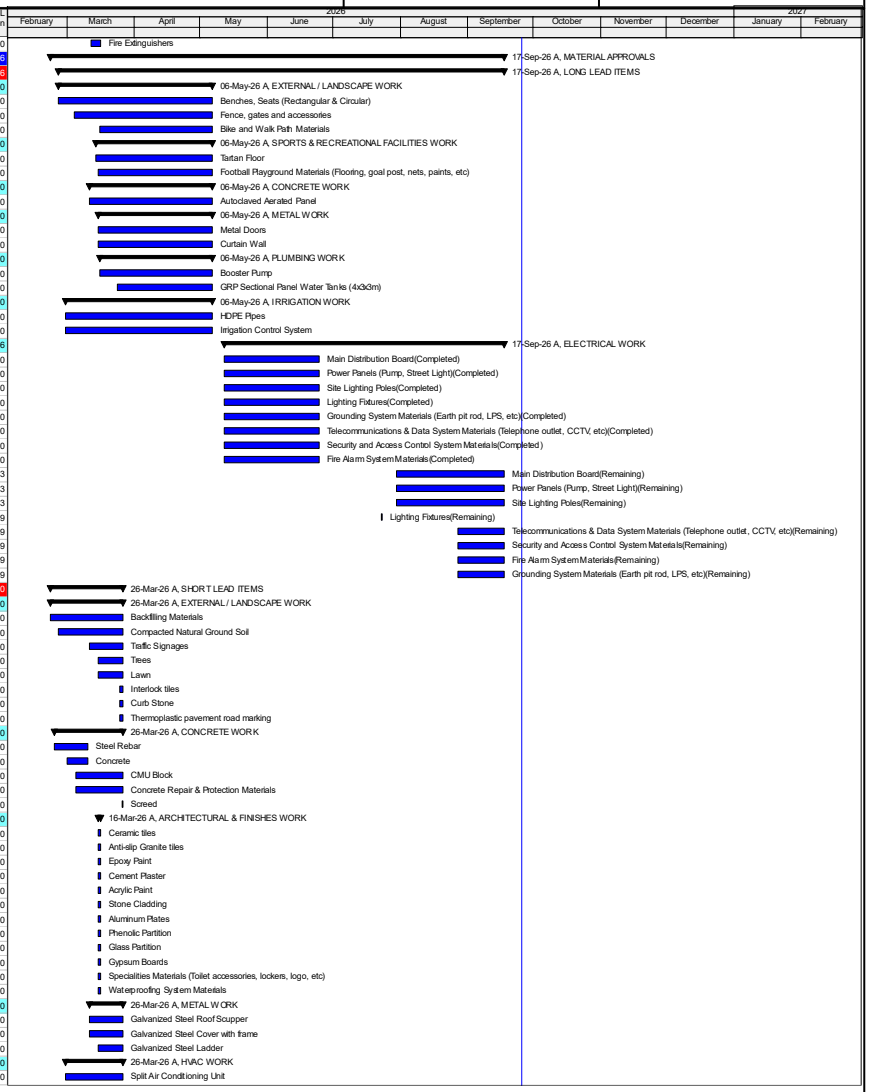


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-SL-AC-MA-20	Air Duct	16	04-Mar-26	26-Mar-26	04-Mar-26 A	26-Mar-26 A	156.00	156.00	156.00	100%	100%	0
PG-H-PR-SL-AC-MA-30	Diffusers and Grills	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	74.31	74.31	74.31	100%	100%	0
PG-H-PR-SL-AC-MA-40	Exhaust fans	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	66.12	66.12	66.12	100%	100%	0
PLUMBING WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
PG-H-PR-SL-PB-MA-10	PPR Pipes & Valves	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	265.20	265.20	265.20	100%	100%	0
PG-H-PR-SL-PB-MA-20	UPCV Pipes	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	335.19	335.19	335.19	100%	100%	0
PG-H-PR-SL-PB-MA-30	Sanitary Drainage Fixtures	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	2,546.64	2,546.64	2,546.64	100%	100%	0
IRRIGATION WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	6,854.64	6,854.64	6,854.64	100%	100%	0
PG-H-PR-SL-IR-MA-10	Gate Valve including valve box	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	756.30	756.30	756.30	100%	100%	0
PG-H-PR-SL-IR-MA-20	Bubblers and Spreyers	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	6,098.34	6,098.34	6,098.34	100%	100%	0
ELECTRICAL WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
PG-H-PR-SL-EL-MA-10	Wiring Devices Materials	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PG-H-PR-SL-FF-MA-10	Fire Extinguishers	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PROCUREMENT		203	26-Feb-26	26-Aug-26	26-Feb-26 A	27-Oct-26	1,839,956.04	1,774,029.58	1,839,956.04	100%	96.42%	-52
LONG LEAD ITEMS		197	05-Mar-26	26-Aug-26	05-Mar-26 A	27-Oct-26	999,589.41	958,872.01	999,589.41	100%	95.93%	-52
PURCHASE ORDER		162	05-Mar-26	22-Jul-26	05-Mar-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
EXTERNAL / LANDSCAPE WORK		49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-LS-PO-20	Benches, Seats (Rectangular & Circular)	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-PO-30	Fence, gates and accessories	43	14-Mar-26	07-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-PO-10	Bike and Walk Path Materials	33	30-Mar-26	07-May-26	30-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-SP-PO-20	Tartan Floor	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-PO-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-CO-PO-10	Autoclaved Aerated Panel	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-PO-10	Metal Doors	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-PO-20	Curtain Wall	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-PB-PO-10	Booster Pump	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-PO-20	GRP Sectional Panel Water Tanks (4x3x3m)	33	30-Mar-26	07-May-26	30-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		50	05-Mar-26	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-IR-PO-20	Irrigation Control System	50	05-Mar-26	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-PO-10	HDPE Pipes	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		109	11-May-26	22-Jul-26	11-May-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
PG-H-PR-LL-EL-PO-10	Main Distribution Board(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-20	Power Panels (Pump, Street Light)(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-30	Site Lighting Poles(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-40	Lighting Fixtures(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-70	Security and Access Control System Materials(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-80	Fire Alarm System Materials(Completed)	35	11-May-26	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-10_R	Main Distribution Board(Remaining)	7	07-Jul-26	14-Jul-26	05-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-22
PG-H-PR-LL-EL-PO-20_R	Power Panels (Pump, Street Light)(Remaining)	7	07-Jul-26	14-Jul-26	05-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-22
PG-H-PR-LL-EL-PO-30_R	Site Lighting Poles(Remaining)	7	07-Jul-26	14-Jul-26	05-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-22
PG-H-PR-LL-EL-PO-40_R	Lighting Fixtures(Remaining)	7	07-Jul-26	14-Jul-26	23-Jul-26 A	23-Jul-26 A	0.00	0.00	0.00	100%	100%	6
PG-H-PR-LL-EL-PO-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	7	07-Jul-26	14-Jul-26	27-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-3
PG-H-PR-LL-EL-PO-70_R	Security and Access Control System Materials(Remaining)	7	07-Jul-26	14-Jul-26	27-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-3
PG-H-PR-LL-EL-PO-80_R	Fire Alarm System Materials(Remaining)	7	07-Jul-26	14-Jul-26	27-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-3
PG-H-PR-LL-EL-PO-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	7	15-Jul-26	22-Jul-26	27-Aug-26 A	08-Sep-26 A	0.00	0.00	0.00	100%	100%	-3
MANUFACTURE / FABRICATION		172	01-Apr-26	12-Aug-26	01-Apr-26 A	24-Oct-26	0.00	0.00	0.00	0%	0%	-61
EXTERNAL / LANDSCAPE WORK		103	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
PG-H-PR-LL-LS-MF-20	Benches, Seats (Rectangular & Circular)(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MF-30	Fence, gates and accessories(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MF-10	Bike and Walk Path Materials(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-6
PG-H-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	5	25-Jun-26	30-Jun-26	23-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-37
PG-H-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	25	25-Jun-26	23-Jul-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-11
SPORTS & RECREATIONAL FACILITIES WORK		97	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
PG-H-PR-LL-SP-MF-10	Football Playground Materials (Flooring, goal post, nets, paints,	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-MF-20	Tartan Floor(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-MF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26	23-Jul-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-SP-MF-20_R	Tartan Floor(Remaining)	25	25-Jun-26	23-Jul-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-11
CONCRETE WORK		93	01-Apr-26	06-Jul-26	01-Apr-26 A	27-Jun-26 A	0.00	0.00	0.00	0%	0%	8
PG-H-PR-LL-CO-MF-10	Autoclaved Aerated Panel(Completed)	69	01-Apr-26	25-Jun-26	01-Apr-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-CO-MF-10_R	Autoclaved Aerated Panel(Remaining)	10	25-Jun-26	06-Jul-26	24-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	100%	100%	7
METAL WORK		143	05-May-26	23-Jul-26	05-May-26 A	24-Oct-26	0.00	0.00	0.00	0%	0%	-78
PG-H-PR-LL-MT-MF-10	Metal Doors(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-MF-20	Curtain Wall(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
PG-H-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0

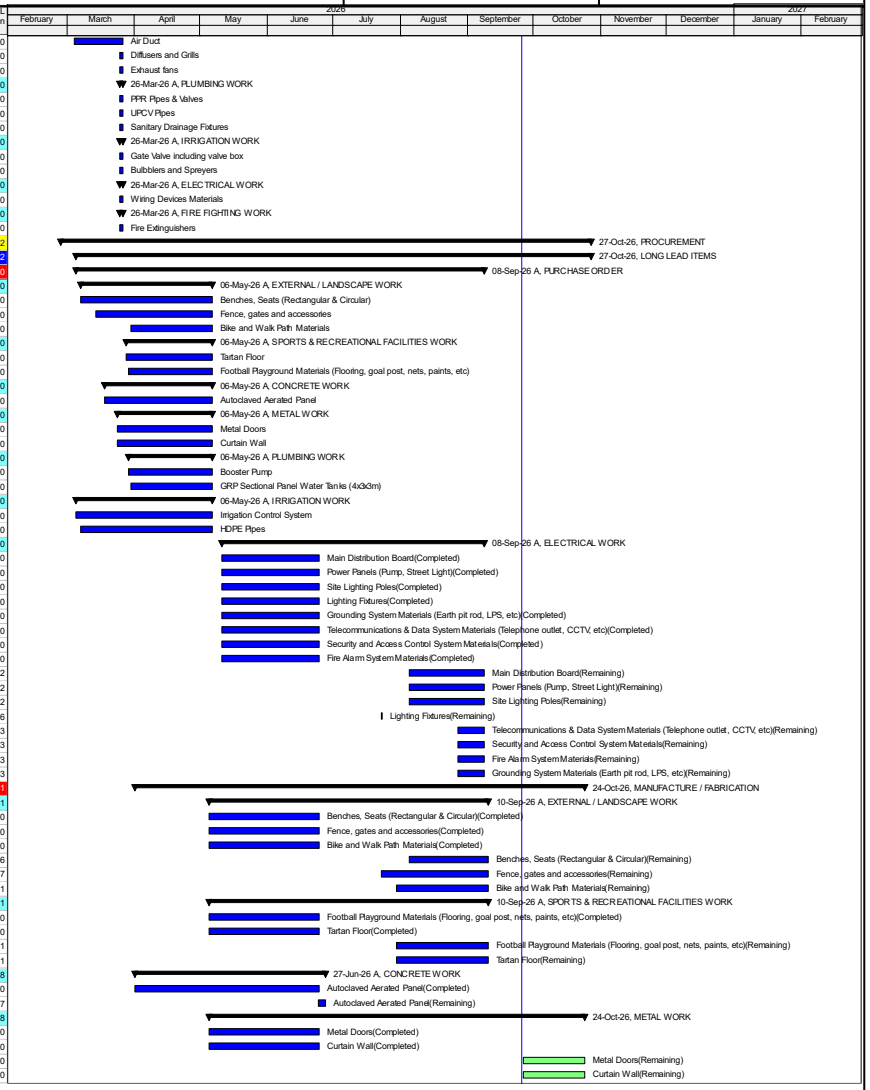


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLUMBING WORK		120	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
PG-H-PR-LL-PB-MF-10	Booster Pump(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-MF-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-MF-10_R	Booster Pump(Remaining)	25	25-Jun-26	23-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26	23-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	13
IRRIGATION WORK		107	05-May-26	08-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-54
PG-H-PR-LL-IR-MF-10	HDPE Pipes(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MF-20	Irrigation Control System(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MF-10_R	HDPE Pipes(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MF-20_R	Irrigation Control System(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		131	12-May-26	12-Aug-26	12-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-25
PG-H-PR-LL-EL-MF-10	Main Distribution Board(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-30	Site Lighting Poles(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-40	Lighting Fixtures(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-70	Security and Access Control System Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-80	Fire Alarm System Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	13	15-Jul-26	29-Jul-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-24
PG-H-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	13	15-Jul-26	29-Jul-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-24
PG-H-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	15-Jul-26	12-Aug-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	15-Jul-26	12-Aug-26	30-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	15-Jul-26	12-Aug-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	15-Jul-26	12-Aug-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	15-Jul-26	12-Aug-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	13	23-Jul-26	06-Aug-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	1
DELIVERY TO SITE		147	07-May-26	26-Aug-26	06-May-26 A	27-Oct-26	999,589.41	958,872.01	999,589.41	100%	95.93%	-52
EXTERNAL / LANDSCAPE WORK		118	07-May-26	06-Aug-26	06-May-26 A	27-Sep-26	234,716.67	226,001.01	234,716.67	100%	96.29%	-43
PG-H-PR-LL-LS-DL-20	Benches, Seats (Rectangular & Circular)(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	28,474.61	28,474.61	28,474.61	100%	100%	0
PG-H-PR-LL-LS-DL-30	Fence, gates and accessories(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	11,847.38	11,847.38	11,847.38	100%	100%	0
PG-H-PR-LL-LS-DL-10	Bike and Walk Path Materials(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	103,704.30	103,704.30	103,704.30	100%	100%	0
PG-H-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	5	01-Jul-26	06-Jul-26	22-Jul-26 A	19-Sep-26 A	17,771.08	17,771.08	17,771.08	100%	100%	-46
PG-H-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	20-Aug-26 A	27-Sep-26	28,474.61	24,203.41	28,474.61	100%	85%	-20
PG-H-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	44,444.70	40,000.23	44,444.70	100%	90%	-31
SPORTS & RECREATIONAL FACILITIES WORK		106	07-May-26	06-Aug-26	06-May-26 A	27-Sep-26	349,555.50	333,183.38	349,555.50	100%	95.32%	-42
PG-H-PR-LL-SP-DL-10	Football Playground Materials (Flooring, goal post, nets, paints,	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	64,212.75	64,212.75	64,212.75	100%	100%	0
PG-H-PR-LL-SP-DL-20	Tartan Floor(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	121,621.50	121,621.50	121,621.50	100%	100%	0
PG-H-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	64,212.75	57,791.48	64,212.75	100%	90%	-31
PG-H-PR-LL-SP-DL-20_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	99,508.50	89,557.65	99,508.50	100%	90%	-31
CONCRETE WORK		67	07-May-26	12-Jul-26	06-May-26 A	07-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	4
PG-H-PR-LL-CO-DL-10	Autoclaved Aerated Panel(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	7,654.50	7,654.50	7,654.50	100%	100%	0
PG-H-PR-LL-CO-DL-10_R	Autoclaved Aerated Panel(Remaining)	5	07-Jul-26	12-Jul-26	06-Jul-26 A	07-Jul-26 A	5,103.00	5,103.00	5,103.00	100%	100%	3
METAL WORK		130	07-May-26	06-Aug-26	06-May-26 A	27-Oct-26	8,003.07	6,802.61	8,003.07	100%	85%	-69
PG-H-PR-LL-MT-DL-10	Metal Doors(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	459.11	459.11	459.11	100%	100%	0
PG-H-PR-LL-MT-DL-20	Curtain Wall(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	2,742.12	2,742.12	2,742.12	100%	100%	0
PG-H-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	27-Oct-26	688.66	516.50	688.66	100%	75%	-40
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	27-Oct-26	4,113.18	3,084.89	4,113.18	100%	75%	-40
PLUMBING WORK		130	07-May-26	06-Aug-26	06-May-26 A	28-Sep-26	31,985.55	30,111.05	31,985.55	100%	94.14%	-43
PG-H-PR-LL-PB-DL-10	Booster Pump(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	6,545.88	6,545.88	6,545.88	100%	100%	0
PG-H-PR-LL-PB-DL-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	6,248.34	6,248.34	6,248.34	100%	100%	0
PG-H-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	21-Sep-26 A	9,818.82	9,818.82	9,818.82	100%	100%	-10
PG-H-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	28-Sep-26	9,372.51	7,498.01	9,372.51	100%	80%	-14
IRRIGATION WORK		108	07-May-26	18-Jul-26	06-May-26 A	04-Sep-26 A	115,364.25	115,364.25	115,364.25	100%	100%	-41
PG-H-PR-LL-IR-DL-10	HDPE Pipes(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	37,226.25	37,226.25	37,226.25	100%	100%	0
PG-H-PR-LL-IR-DL-20	Irrigation Control System(Completed)	38	07-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	16,364.70	16,364.70	16,364.70	100%	100%	0
PG-H-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	8	09-Jul-26	18-Jul-26	20-Aug-26 A	27-Aug-26 A	37,226.25	37,226.25	37,226.25	100%	100%	1
PG-H-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	09-Jul-26	18-Jul-26	20-Aug-26 A	04-Sep-26 A	24,547.05	24,547.05	24,547.05	100%	100%	-5
ELECTRICAL WORK		142	13-May-26	26-Aug-26	13-May-26 A	27-Sep-26	247,206.87	234,652.21	247,206.87	100%	94.92%	-26
PG-H-PR-LL-EL-DL-10	Main Distribution Board(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	1,338.93	1,338.93	1,338.93	100%	100%	0
PG-H-PR-LL-EL-DL-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	1,071.14	1,071.14	1,071.14	100%	100%	0
PG-H-PR-LL-EL-DL-30	Site Lighting Poles(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	57,437.42	57,437.42	57,437.42	100%	100%	0
PG-H-PR-LL-EL-DL-40	Lighting Fixtures(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	3,463.64	3,463.64	3,463.64	100%	100%	0
PG-H-PR-LL-EL-DL-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,711.31	2,711.31	2,711.31	100%	100%	0
PG-H-PR-LL-EL-DL-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,644.33	2,644.33	2,644.33	100%	100%	0
PG-H-PR-LL-EL-DL-70	Security and Access Control System Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	3,347.73	3,347.73	3,347.73	100%	100%	0
PG-H-PR-LL-EL-DL-80	Fire Alarm System Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,147.55	2,147.55	2,147.55	100%	100%	0
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	27-Sep-26	3,124.17	2,655.54	3,124.17	100%	85%	-17
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	27-Sep-26	2,499.34	2,124.44	2,499.34	100%	85%	-17
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	27-Sep-26	6,326.40	5,377.44	6,326.40	100%	85%	-17
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	26-Sep-26	134,020.66	127,319.62	134,020.66	100%	95%	-19
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	27-Sep-26	8,081.83	6,869.55	8,081.83	100%	85%	-20
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	27-Sep-26	6,170.09	5,244.58	6,170.09	100%	85%	-14

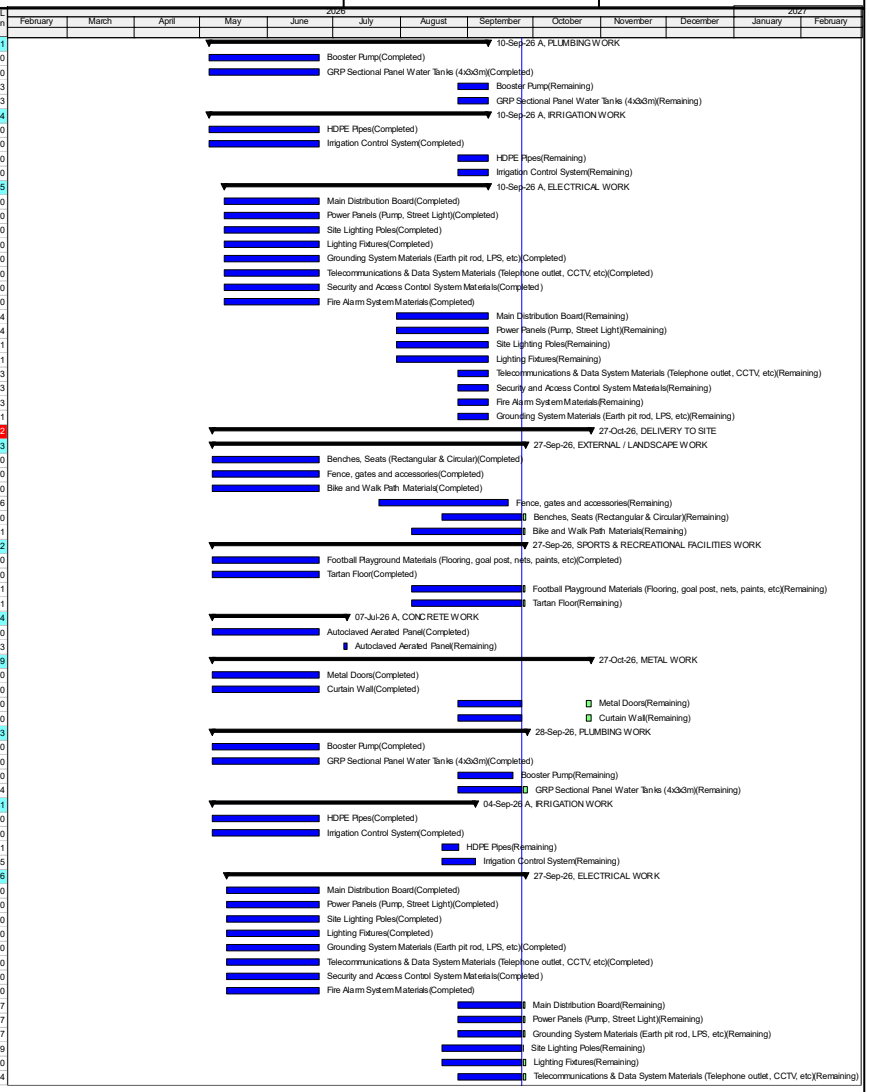


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	27-Sep-26	7,811.37	6,639.66	7,811.37	100%	85%	-14
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	27-Sep-26	5,010.96	4,259.31	5,010.96	100%	85%	-14
SHORT LEAD ITEMS		184	26-Feb-26	16-Jul-26	26-Feb-26 A	08-Oct-26	840,366.63	815,157.57	840,366.63	100%	97%	-71
PURCHASE ORDER		156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
EXTERNAL / LANDSCAPE WORK		156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-LS-PO-10	Backfilling Materials	44	26-Feb-26	23-Apr-26	26-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-30	Compacted Natural Ground Soil	42	01-Mar-26	23-Apr-26	01-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-20	Interlock tiles	27	30-Mar-26	30-Apr-26	30-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-40	Curb Stone	22	05-Apr-26	30-Apr-26	05-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-50	Thermoplastic pavement road marking(Completed)	36	10-May-26	25-Jun-26	10-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-60	Traffic Signages(Completed)	36	10-May-26	25-Jun-26	10-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-70	Trees(Completed)	36	10-May-26	25-Jun-26	10-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-80	Lawn(Completed)	36	10-May-26	25-Jun-26	10-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-50_R	Thermoplastic pavement road marking(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-60_R	Traffic Signages(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-70_R	Trees(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-80_R	Lawn(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-CO-PO-10	Steel Rebar	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-20	Concrete	36	08-Mar-26	23-Apr-26	08-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-40	CMU Block	33	11-Mar-26	23-Apr-26	11-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-50	Concrete Repair & Protection Materials	32	12-Mar-26	23-Apr-26	12-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-30	Screed	23	28-Mar-26	23-Apr-26	28-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AR-PO-10	Ceramic tiles	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-20	Anti-slip Granite tiles	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-30	Epoxy Paint	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-40	Cement Plaster	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-50	Acrylic Paint	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-60	Stone Cladding	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-70	Aluminum Plates	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-80	Phenolic Partition	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-90	Glass Partition	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-100	Gypsum Boards	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-120	Waterproofing System Materials	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-MT-PO-10	Galvanized Steel Ladder	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-PO-20	Galvanized Steel Roof Scupper	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-PO-30	Galvanized Steel Cover with frame	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AC-PO-10	Split Air Conditioning Unit	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-PO-20	Air Duct	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-PO-30	Diffusers and Grills	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-PO-40	Exhaust fans	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-PB-PO-10	PPR Pipes & Valves	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-PO-20	UPCV Pipes	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-PO-30	Sanitary Drainage Fixtures	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		102	05-May-26	02-Jul-26	05-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-IR-PO-10	Gate Valve including valve box(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-PO-20	Bubblers and Spreyers(Completed)	40	05-May-26	25-Jun-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-PO-10_R	Gate Valve including valve box(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-PO-20_R	Bubblers and Spreyers(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-EL-PO-10	Wiring Devices Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-EL-PO-10_R	Wiring Devices Materials(Remaining)	7	25-Jun-26	02-Jul-26	27-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	6
FIRE FIGHTING WORK		96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-FF-PO-10	Fire Extinguishers(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-FF-PO-10_R	Fire Extinguishers(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
DELIVERY TO SITE		182	01-Mar-26	16-Jul-26	01-Mar-26 A	08-Oct-26	840,366.63	815,157.57	840,366.63	100%	97%	-71
EXTERNAL / LANDSCAPE WORK		166	01-Mar-26	16-Jul-26	01-Mar-26 A	29-Sep-26	649,200.96	631,329.23	649,200.96	100%	97.25%	-63
PG-H-PR-SL-LS-DL-10	Backfilling Materials	43	01-Mar-26	23-Apr-26	01-Mar-26 A	24-Apr-26 A	176,175.00	176,175.00	176,175.00	100%	100%	0
PG-H-PR-SL-LS-DL-30	Compacted Natural Ground Soil	41	03-Mar-26	23-Apr-26	03-Mar-26 A	24-Apr-26 A	28,080.00	28,080.00	28,080.00	100%	100%	0
PG-H-PR-SL-LS-DL-20	Interlock tiles	12	30-Apr-26	13-May-26	30-Apr-26 A	13-May-26 A	157,450.50	157,450.50	157,450.50	100%	100%	0
PG-H-PR-SL-LS-DL-40	Curb Stone	12	30-Apr-26	13-May-26	30-Apr-26 A	13-May-26 A	188,352.00	188,352.00	188,352.00	100%	100%	0
PG-H-PR-SL-LS-DL-50	Thermoplastic pavement road marking(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	1,419.20	1,419.20	1,419.20	100%	100%	0
PG-H-PR-SL-LS-DL-60	Traffic Signages(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	535.57	535.57	535.57	100%	100%	0
PG-H-PR-SL-LS-DL-70	Trees(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	13,046.27	13,046.27	13,046.27	100%	100%	0
PG-H-PR-SL-LS-DL-80	Lawn(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	24,570.00	24,570.00	24,570.00	100%	100%	0
PG-H-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	3,311.47	2,318.03	3,311.47	100%	70%	-16
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	1,249.67	874.77	1,249.67	100%	70%	-16
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	30,441.29	21,308.90	30,441.29	100%	70%	-16

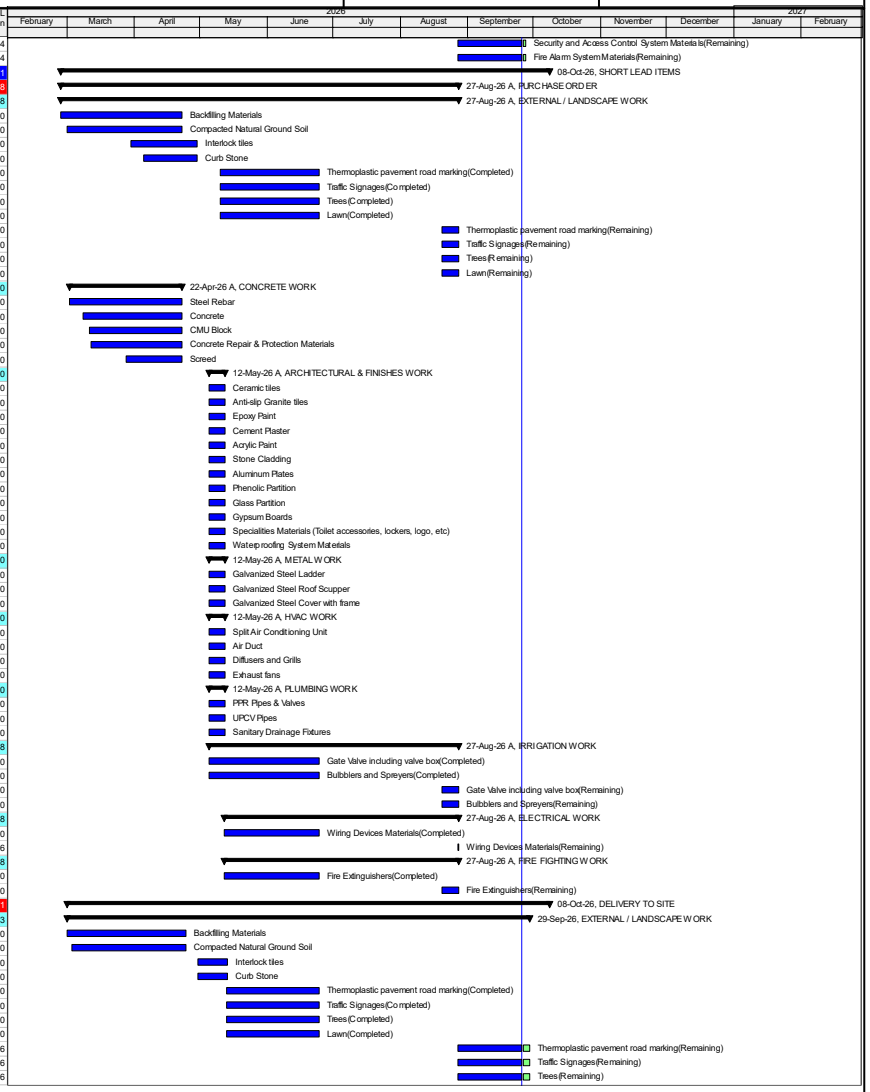


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	24,570.00	17,199.00	24,570.00	100%	70%	-16
CONCRETE WORK		52	10-Mar-2	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
PG-H-PR-SL-CO-DL-20	Concrete	35	10-Mar-2	23-Apr-26	10-Mar-26 A	24-Apr-26 A	4,669.65	4,669.65	4,669.65	100%	100%	0
PG-H-PR-SL-CO-DL-10	Steel Rebar	12	23-Apr-26	06-May-26	23-Apr-26 A	06-May-26 A	4,291.38	4,291.38	4,291.38	100%	100%	0
PG-H-PR-SL-CO-DL-30	Screed	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	1,058.40	1,058.40	1,058.40	100%	100%	0
PG-H-PR-SL-CO-DL-40	CMU Block	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	1,117.80	1,117.80	1,117.80	100%	100%	0
PG-H-PR-SL-CO-DL-50	Concrete Repair & Protection Materials	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	3,348.00	3,348.00	3,348.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	73,026.09	73,026.09	73,026.09	100%	100%	0
PG-H-PR-SL-AR-DL-10	Ceramic tiles	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	5,147.55	5,147.55	5,147.55	100%	100%	0
PG-H-PR-SL-AR-DL-20	Anti-slip Granite tiles	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	4,819.50	4,819.50	4,819.50	100%	100%	0
PG-H-PR-SL-AR-DL-30	Epoxy Paint	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,000.62	1,000.62	1,000.62	100%	100%	0
PG-H-PR-SL-AR-DL-40	Cement Plaster	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,992.33	1,992.33	1,992.33	100%	100%	0
PG-H-PR-SL-AR-DL-50	Acrylic Paint	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,331.10	1,331.10	1,331.10	100%	100%	0
PG-H-PR-SL-AR-DL-60	Stone Cladding	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	16,669.80	16,669.80	16,669.80	100%	100%	0
PG-H-PR-SL-AR-DL-70	Aluminum Plates	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,642.14	1,642.14	1,642.14	100%	100%	0
PG-H-PR-SL-AR-DL-80	Phenolic Partition	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	12,063.60	12,063.60	12,063.60	100%	100%	0
PG-H-PR-SL-AR-DL-90	Glass Partition	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,398.60	1,398.60	1,398.60	100%	100%	0
PG-H-PR-SL-AR-DL-100	Gypsum Boards	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,697.22	1,697.22	1,697.22	100%	100%	0
PG-H-PR-SL-AR-DL-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	20,365.83	20,365.83	20,365.83	100%	100%	0
PG-H-PR-SL-AR-DL-120	Waterproofing System Materials	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	4,897.80	4,897.80	4,897.80	100%	100%	0
METAL WORK		6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	4,310.01	4,310.01	4,310.01	100%	100%	0
PG-H-PR-SL-MT-DL-10	Galvanized Steel Ladder	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	3,256.74	3,256.74	3,256.74	100%	100%	0
PG-H-PR-SL-MT-DL-20	Galvanized Steel Roof Scupper	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	281.88	281.88	281.88	100%	100%	0
PG-H-PR-SL-MT-DL-30	Galvanized Steel Cover with frame	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	771.39	771.39	771.39	100%	100%	0
HVAC WORK		6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
PG-H-PR-SL-AC-DL-10	Split Air Conditioning Unit	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	2,789.37	2,789.37	2,789.37	100%	100%	0
PG-H-PR-SL-AC-DL-20	Air Duct	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	1,404.00	1,404.00	1,404.00	100%	100%	0
PG-H-PR-SL-AC-DL-30	Diffusers and Grills	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	668.79	668.79	668.79	100%	100%	0
PG-H-PR-SL-AC-DL-40	Exhaust fans	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	595.08	595.08	595.08	100%	100%	0
PLUMBING WORK		6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
PG-H-PR-SL-PB-DL-10	PPR Pipes & Valves	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	2,386.80	2,386.80	2,386.80	100%	100%	0
PG-H-PR-SL-PB-DL-20	UPCV Pipes	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	3,016.71	3,016.71	3,016.71	100%	100%	0
PG-H-PR-SL-PB-DL-30	Sanitary Drainage Fixtures	6	06-May-2	12-May-26	06-May-26 A	12-May-26 A	22,919.76	22,919.76	22,919.76	100%	100%	0
IRRIGATION WORK		113	06-May-2	16-Jul-26	06-May-26 A	27-Sep-26	61,691.76	57,064.88	61,691.76	100%	92.5%	-61
PG-H-PR-SL-IR-DL-10	Gate Valve including valve box(Completed)	39	06-May-2	24-Jun-26	06-May-26 A	24-Jun-26 A	3,403.35	3,403.35	3,403.35	100%	100%	0
PG-H-PR-SL-IR-DL-20	Bulbblers and Spreyers(Completed)	39	06-May-2	24-Jun-26	06-May-26 A	24-Jun-26 A	27,442.53	27,442.53	27,442.53	100%	100%	0
PG-H-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26	16-Jul-26	20-Aug-26 A	27-Sep-26	3,403.35	2,892.85	3,403.35	100%	85%	-20
PG-H-PR-SL-IR-DL-20_R	Bulbblers and Spreyers(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	27-Sep-26	27,442.53	23,326.15	27,442.53	100%	85%	-14
ELECTRICAL WORK		117	20-May-2	16-Jul-26	20-May-26 A	08-Oct-26	3,667.68	1,100.30	3,667.68	100%	30%	-71
PG-H-PR-SL-EL-DL-10	Wiring Devices Materials(Completed)	27	20-May-2	24-Jun-26	20-May-26 A	24-Jun-26 A	1,100.30	1,100.30	1,100.30	100%	100%	0
PG-H-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26	08-Oct-26	2,567.38	0.00	2,567.38	100%	0%	0
FIRE FIGHTING WORK		117	20-May-2	16-Jul-26	20-May-26 A	08-Oct-26	204.39	61.32	204.39	100%	30%	-71
PG-H-PR-SL-FF-DL-10	Fire Extinguishers(Completed)	27	20-May-2	24-Jun-26	20-May-26 A	24-Jun-26 A	61.32	61.32	61.32	100%	100%	0
PG-H-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26	08-Oct-26	143.07	0.00	143.07	100%	0%	0
CONSTRUCTION STAGE		231	05-Apr-26	26-Nov-26	05-Apr-26 A	09-Jan-27	3,035,135.32	3,085,403.02	4,088,791.20	74.23%	75.46%	-36
PLAYGROUND AND LANDSCAPING WORKS		231	05-Apr-26	26-Nov-26	05-Apr-26 A	09-Jan-27	2,836,878.60	2,856,507.02	3,760,297.62	75.44%	75.96%	-36
CUT AND FILL		28	05-Apr-26	06-May-26	05-Apr-26 A	06-May-26 A	453,900.00	453,900.00	453,900.00	100%	100%	0
PG-H-CON-EX-CF-10	Existing Soil Excavation Works	26	05-Apr-26	04-May-26	05-Apr-26 A	04-May-26 A	125,280.00	125,280.00	125,280.00	100%	100%	0
PG-H-CON-EX-CF-20	Soil Replacement Works	21	12-Apr-26	05-May-26	12-Apr-26 A	05-May-26 A	62,400.00	62,400.00	62,400.00	100%	100%	0
PG-H-CON-EX-CF-30	Levelling & Backfilling Works	18	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	266,220.00	266,220.00	266,220.00	100%	100%	0
PLAYGROUND WORKS		164	19-Apr-26	17-Nov-26	19-Apr-26 A	01-Nov-26	534,166.50	676,551.06	781,940.40	68.31%	86.52%	14
FOOTBALL PLAYGROUND WORKS		164	19-Apr-26	17-Nov-26	19-Apr-26 A	01-Nov-26	534,166.50	676,551.06	781,940.40	68.31%	86.52%	14
PG-H-CON-EX-FB-10	Subgrade Preparation and Compaction	16	19-Apr-26	06-May-26	19-Apr-26 A	06-May-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-H-CON-EX-FB-20	Sub-Base Laying and Compaction	12	23-Apr-26	06-May-26	23-Apr-26 A	06-May-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-H-CON-EX-FB-30	Base Course Laying and Compaction	33	06-May-2	17-Jun-26	06-May-26 A	17-Jun-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-H-CON-EX-FB-70	Topsoil Placement(Completed)	33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	7,100.10	7,100.10	7,100.10	100%	100%	0
PG-H-CON-EX-FB-40	Tartan flooring(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	147,420.00	147,420.00	147,420.00	100%	100%	0
PG-H-CON-EX-FB-80	Fine Grading & Leveling	15	25-Jun-26	12-Jul-26	12-Jul-26 A	14-Aug-26 A	23,667.00	23,667.00	23,667.00	100%	100%	-14
PG-H-CON-EX-FB-70_R	Topsoil Placement(Remaining)	14	13-Jul-26	28-Jul-26	30-Jul-26 A	14-Aug-26 A	16,566.90	16,566.90	16,566.90	100%	100%	1
PG-H-CON-EX-FB-50	Goal Post Foundation	17	29-Jul-26	17-Aug-26	20-Aug-26 A	30-Sep-26	35,500.50	26,625.38	35,500.50	100%	75%	-17
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-2	01-Sep-26	27-Aug-26 A	06-Oct-26	48,720.00	29,232.00	48,720.00	100%	60%	-20
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-2	15-Sep-26	14-Aug-26 A	08-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-35
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-2	04-Oct-26	06-Aug-26 A	08-Oct-26	160,524.00	309,582.00	343,980.00	46.67%	90%	-39
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	14-Oct-26	0.00	23,075.33	35,500.50	0%	65%	-33
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	20-Oct-26	0.00	3,347.76	5,150.40	0%	65%	-31
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-2	17-Nov-26	20-Oct-26	01-Nov-26	0.00	0.00	23,667.00	0%	0%	0
GENERAL SITE WORKS		221	16-Apr-26	26-Nov-26	16-Apr-26 A	09-Jan-27	1,026,961.56	674,323.23	1,224,114.42	83.89%	55.09%	-36
FENCE WORKS		148	16-Apr-26	16-Aug-26	16-Apr-26 A	11-Oct-26	65,818.80	36,858.53	65,818.80	100%	56%	-47
PG-H-CON-EX-GN-FN-10	Excavation for fence foundation	3	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	13,163.76	13,163.76	13,163.76	100%	100%	0
PG-H-CON-EX-GN-FN-20	Concrete Foundations for Fence	9	13-Jul-26	22-Jul-26	13-Aug-26 A	20-Aug-26 A	13,163.76	13,163.76	13,163.76	100%	100%	2
PG-H-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26	02-Aug-26	27-Aug-26 A	27-Sep-26	13,163.76	10,531.01	13,163.76	100%	80%	-17
PG-H-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-2	11-Aug-26	27-Sep-26	06-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
PG-H-CON-EX-GN-FN-50	Installation of Gates	4	12-Aug-2	16-Aug-26	06-Oct-26	11-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0

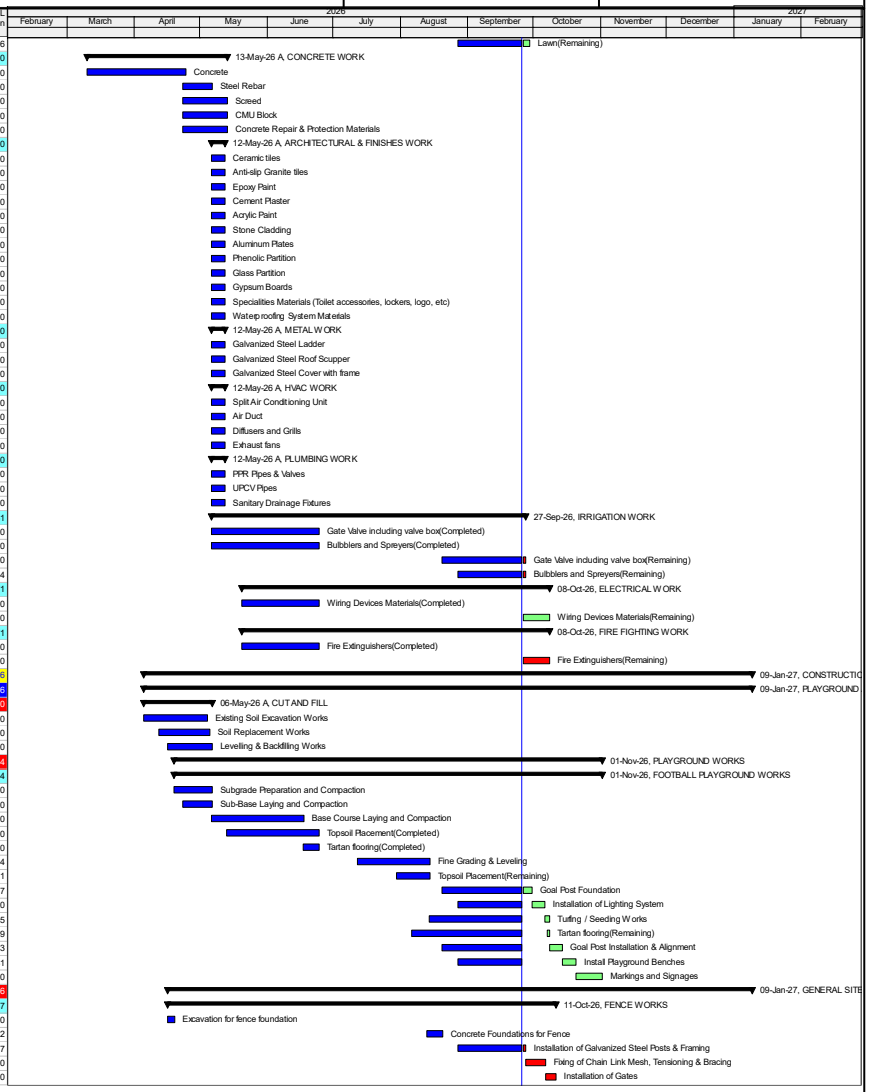

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
MECHANICAL WORK		135	12-May-26	05-Aug-26	12-May-26 A	21-Oct-26	421,027.74	227,748.36	421,027.74	100%	54.09%	-64
STORM WATER AND UTILITY WORK		133	12-May-26	04-Aug-26	12-May-26 A	19-Oct-26	27,252.00	8,875.20	27,252.00	100%	32.57%	-64
PG-H-CON-EX-GN-M-10	Excavation	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	3,096.00	3,096.00	3,096.00	100%	100%	0
PG-H-CON-EX-GN-M-20	Bedding preparation & level control(Completed)	27	20-May-26	24-Jun-26	20-May-26 A	24-Jun-26 A	1,032.00	1,032.00	1,032.00	100%	100%	0
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	27-Sep-26	1,032.00	877.20	1,032.00	100%	85%	-27
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	28-Sep-26	5,160.00	3,870.00	5,160.00	100%	75%	-22
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	28-Sep-26	03-Oct-26	10,740.00	0.00	10,740.00	100%	0%	0
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	03-Oct-26	06-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	06-Oct-26	10-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	14-Oct-26	19-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		115	02-Jun-26	30-Jul-26	02-Jun-26 A	14-Oct-26	393,457.80	218,873.16	393,457.80	100%	55.63%	-64
PG-H-CON-EX-GN-M-80	Installation of HDPE Irrigation Pipe Network with Gate Valve and	20	02-Jun-26	24-Jun-26	02-Jun-26 A	24-Jun-26 A	72,230.40	72,230.40	72,230.40	100%	100%	0
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	10-Oct-26	108,345.60	92,093.76	108,345.60	100%	85%	-45
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	11-Oct-26	90,915.00	54,549.00	90,915.00	100%	60%	-36
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	11-Oct-26	14-Oct-26	121,966.80	0.00	121,966.80	100%	0%	0
FIRE PROTECTION SYSTEM		2	05-Aug-26	06-Aug-26	19-Oct-26	21-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-H-CON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-26	06-Aug-26	19-Oct-26	21-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		183	20-May-26	20-Oct-26	20-May-26 A	24-Dec-26	501,221.52	262,084.84	539,251.68	92.95%	48.6%	-56
POWER, LIGHTING & GROUNDING		148	20-May-26	08-Sep-26	20-May-26 A	14-Nov-26	482,181.48	262,084.84	482,181.48	100%	54.35%	-56
PG-H-CON-EX-GN-E-10	Excavation(Completed)	27	20-May-26	24-Jun-26	20-May-26 A	24-Jun-26 A	63,819.36	63,819.36	63,819.36	100%	100%	0
PG-H-CON-EX-GN-E-20	Foundation Work for Site Lighting Poles(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	51,055.49	51,055.49	51,055.49	100%	100%	0
PG-H-CON-EX-GN-E-10_R	Excavation(Remaining)	1	04-Aug-26	04-Aug-26	16-Jul-26 A	27-Aug-26 A	63,819.36	63,819.36	63,819.36	100%	100%	-36
PG-H-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-26	09-Aug-26	20-Aug-26 A	20-Oct-26	119,129.47	83,390.63	119,129.47	100%	70%	-49
PG-H-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-26	19-Aug-26	21-Oct-26	25-Oct-26	8,265.00	0.00	8,265.00	100%	0%	0
PG-H-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-26	22-Aug-26	25-Oct-26	27-Oct-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-H-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-26	27-Aug-26	27-Oct-26	02-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-H-CON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-26	31-Aug-26	02-Nov-26	05-Nov-26	127,638.72	0.00	127,638.72	100%	0%	0
PG-H-CON-EX-GN-E-70	Wiring Works	3	01-Sep-26	03-Sep-26	05-Nov-26	09-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-H-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-26	08-Sep-26	09-Nov-26	14-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-26	08-Oct-26	14-Nov-26	13-Dec-26	16,395.24	0.00	43,146.00	38%	0%	0
PG-H-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-26	12-Sep-26	14-Nov-26	17-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-H-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-26	15-Sep-26	17-Nov-26	21-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-H-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-26	20-Sep-26	21-Nov-26	25-Nov-26	3,718.80	0.00	3,718.80	100%	0%	0
PG-H-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-26	26-Sep-26	25-Nov-26	30-Nov-26	11,436.84	0.00	15,249.12	75%	0%	0
PG-H-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-26	30-Sep-26	30-Nov-26	05-Dec-26	0.00	0.00	1,446.48	0%	0%	0
PG-H-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-26	05-Oct-26	05-Dec-26	09-Dec-26	0.00	0.00	6,612.00	0%	0%	0
PG-H-CON-EX-GN-E-150	IP Camera Installation	3	06-Oct-26	08-Oct-26	09-Dec-26	13-Dec-26	0.00	0.00	14,880.00	0%	0%	0
FIRE ALARM SYSTEM		32	13-Sep-26	20-Oct-26	17-Nov-26	24-Dec-26	2,644.80	0.00	13,924.20	18.99%	0%	0
PG-H-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-26	21-Sep-26	17-Nov-26	26-Nov-26	1,983.60	0.00	1,983.60	100%	0%	0
PG-H-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-26	01-Oct-26	26-Nov-26	06-Dec-26	661.20	0.00	2,644.80	25%	0%	0
PG-H-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-26	11-Oct-26	06-Dec-26	15-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-H-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-26	20-Oct-26	15-Dec-26	24-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		163	17-Jun-26	20-Oct-26	17-Jun-26 A	24-Dec-26	38,893.50	142,609.50	190,576.20	20.41%	74.83%	-56
PG-H-CON-EX-GN-PR-20	Interlock tiles(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	38,893.50	38,893.50	38,893.50	100%	100%	0
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	15-Dec-26	0.00	56,179.50	86,430.00	0%	65%	-95
PG-H-CON-EX-GN-PR-20_R	Interlock tiles(Remaining)	3	12-Oct-26	14-Oct-26	11-Jul-26 A	30-Jul-26 A	0.00	47,536.50	47,536.50	0%	100%	-15
PG-H-CON-EX-GN-PR-30	Marking & Signages	5	15-Oct-26	20-Oct-26	19-Dec-26	24-Dec-26	0.00	0.00	17,716.20	0%	0%	0
SERVICE CONNECTION		34	21-Oct-26	26-Nov-26	30-Jul-26 A	09-Jan-27	0.00	5,022.00	7,440.00	0%	67.5%	-106
PG-H-CON-EX-GN-SC-10	Excavation & Trench Preparation	8	21-Oct-26	29-Oct-26	30-Jul-26 A	27-Aug-26 A	0.00	2,232.00	2,232.00	0%	100%	-17
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	27-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-101
PG-H-CON-EX-GN-SC-30	Connection to City Network	8	09-Nov-26	17-Nov-26	27-Dec-26	05-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26	26-Nov-26	27-Aug-26 A	09-Jan-27	0.00	892.80	1,488.00	0%	60%	-106
LANDSCAPING WORKS		162	31-May-26	09-Nov-26	30-May-26 A	06-Dec-26	773,560.14	1,040,312.69	1,252,052.40	61.78%	83.09%	-23
HARDSCAPE WORK		162	31-May-26	09-Nov-26	30-May-26 A	06-Dec-26	718,960.14	947,492.69	1,046,213.40	68.72%	90.56%	-23
PG-H-CON-EX-LS-HS-10	Curbstone Installation(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	251,136.00	251,136.00	251,136.00	100%	100%	0
PG-H-CON-EX-LS-HS-20	Interlock Tiles Grey Scale with Black Marble Chips(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	36,036.00	36,036.00	36,036.00	100%	100%	0
PG-H-CON-EX-LS-HS-40	Bike Path and Walking Path Construction(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	181,071.00	181,071.00	181,071.00	100%	100%	0
PG-H-CON-EX-LS-HS-50	Install Recycled Precast Concrete Seats(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	11,599.14	11,599.14	11,599.14	100%	100%	0
PG-H-CON-EX-LS-HS-30	Stamped Concrete Floor(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	43,470.00	43,470.00	43,470.00	100%	100%	0
PG-H-CON-EX-LS-HS-10_R	Curbstone Installation(Remaining)	8	10-Sep-26	19-Sep-26	22-Jul-26 A	27-Aug-26 A	167,424.00	167,424.00	167,424.00	100%	100%	-24
PG-H-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-26	05-Oct-26	27-Aug-26 A	07-Nov-26	16,632.00	35,135.10	54,054.00	30.77%	65%	-47
PG-H-CON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-26	07-Oct-26	30-Jul-26 A	07-Nov-26	11,592.00	39,123.00	43,470.00	26.67%	90%	-69
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	18-Nov-26	0.00	140,741.55	148,149.00	0%	95%	-104
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	24-Nov-26	0.00	41,756.90	104,392.26	0%	40%	-90
PG-H-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	29-Oct-26	09-Nov-26	24-Nov-26	06-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		155	03-Jun-26	09-Nov-26	03-Jun-26 A	06-Dec-26	54,600.00	92,820.00	205,839.00	26.53%	45.09%	-23
PG-H-CON-EX-LS-SS-20	Lawn Area Preparation & Planting / Turfing(Completed)	19	03-Jun-26	24-Jun-26	03-Jun-26 A	24-Jun-26 A	54,600.00	54,600.00	54,600.00	100%	100%	0
PG-H-CON-EX-LS-SS-10	Planting Trees	10	06-Oct-26	17-Oct-26	07-Nov-26	18-Nov-26	0.00	0.00	96,639.00	0%	0%	0
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-26	09-Nov-26	27-Aug-26 A	06-Dec-26	0.00	38,220.00	54,600.00	0%	70%	-79
TANK WORKS		143	13-May-26	19-Sep-26	13-May-26 A	01-Nov-26	48,290.40	11,420.04	48,290.40	100%	23.65%	-36
SEPTIC TANK		138	13-May-26	31-Aug-26	13-May-26 A	26-Oct-26	7,475.22	5,317.86	7,475.22	100%	71.14%	-47
PG-H-CON-EX-TW-ST-10	Excavation	32	13-May-26	23-Jun-26	13-May-26 A	23-Jun-26 A	252.18	252.18	252.18	100%	100%	0
PG-H-CON-EX-TW-ST-20	PCC / Lean Concrete laying	27	20-May-26	24-Jun-26	20-May-26 A	24-Jun-26 A	168.12	168.12	168.12	100%	100%	0



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-TW-ST-30	RCC Foundation(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	766.58	766.58	766.58	100%	100%	0
PG-H-CON-EX-TW-ST-30_R	RCC Foundation(Remaining)	6	25-Jun-26	01-Jul-26	30-Jul-26 A	27-Aug-26 A	511.06	511.06	511.06	100%	100%	-19
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26	09-Jul-26	14-Aug-26 A	28-Sep-26	2,757.60	1,930.32	2,757.60	100%	70%	-30
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26	18-Jul-26	27-Aug-26 A	30-Sep-26	2,599.38	1,689.60	2,599.38	100%	65%	-22
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-26	24-Aug-26	11-Oct-26	19-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-26	31-Aug-26	19-Oct-26	26-Oct-26	168.12	0.00	168.12	100%	0%	0
WATER STORAGE TANK		143	13-May-26	19-Sep-26	13-May-26 A	01-Nov-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-36
PG-H-CON-EX-TW-IR-10	Excavation(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	766.58	766.58	766.58	100%	100%	0
PG-H-CON-EX-TW-IR-10_R	Excavation(Remaining)	3	29-Aug-26	31-Aug-26	08-Jul-26 A	09-Jul-26 A	85.18	85.18	85.18	100%	100%	1
PG-H-CON-EX-TW-IR-20	RCC Foundation	6	01-Sep-26	07-Sep-26	23-Jul-26 A	27-Aug-26 A	4,136.40	4,136.40	4,136.40	100%	100%	-25
PG-H-CON-EX-TW-IR-30	Backfilling	5	08-Sep-26	13-Sep-26	14-Aug-26 A	27-Aug-26 A	1,114.02	1,114.02	1,114.02	100%	100%	-7
PG-H-CON-EX-TW-IR-40	GRP Water Tank Installation	5	14-Sep-26	19-Sep-26	26-Oct-26	01-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
TOILET BUILDING WORKS		165	12-May-26	12-Oct-26	12-May-26 A	08-Nov-26	198,256.72	228,896.00	328,493.58	60.35%	69.68%	-23
CIVIL WORK		165	12-May-26	12-Oct-26	12-May-26 A	07-Nov-26	100,666.18	154,230.90	230,766.78	43.62%	66.83%	-22
STRUCTURAL WORK		59	12-May-26	22-Jul-26	12-May-26 A	23-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-1
PG-H-CON-B-STR-10	Excavation up to bottom of footing	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-H-CON-B-STR-20	Anti-termite treatment and Polyethene Sheet	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	3,294.00	3,294.00	3,294.00	100%	100%	0
PG-H-CON-B-STR-30	Backfilling with selected fill material (under footing)	1	13-May-26	13-May-26	13-May-26 A	13-May-26 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-H-CON-B-STR-40	Raft Foundation Work	27	13-May-26	17-Jun-26	13-May-26 A	17-Jun-26 A	2,534.40	2,534.40	2,534.40	100%	100%	0
PG-H-CON-B-STR-50	Autoclaved aerated panel (walls)	4	13-Jul-26	16-Jul-26	11-Jul-26 A	12-Jul-26 A	11,340.00	11,340.00	11,340.00	100%	100%	2
PG-H-CON-B-STR-60	Autoclaved aerated panel (ceiling)	3	18-Jul-26	20-Jul-26	12-Jul-26 A	16-Jul-26 A	8,505.00	8,505.00	8,505.00	100%	100%	-2
PG-H-CON-B-STR-70	Autoclaved aerated panel (parapet)	2	21-Jul-26	22-Jul-26	12-Jul-26 A	23-Jul-26 A	8,505.00	8,505.00	8,505.00	100%	100%	-9
ARCHITECTURAL WORK		99	23-Jul-26	12-Oct-26	31-Jul-26 A	07-Nov-26	62,686.18	116,250.90	192,786.78	32.52%	60.3%	-15
GENERAL FINISHES		99	23-Jul-26	12-Oct-26	31-Jul-26 A	07-Nov-26	20,239.48	26,890.38	87,769.20	23.06%	30.64%	-15
PG-H-CON-B-AR-GF-10	Block Works	4	23-Jul-26	27-Jul-26	31-Jul-26 A	05-Aug-26 A	2,484.00	2,484.00	2,484.00	100%	100%	-1
PG-H-CON-B-AR-GF-20	Plaster	4	08-Aug-26	11-Aug-26	06-Aug-26 A	07-Aug-26 A	4,427.40	4,427.40	4,427.40	100%	100%	3
PG-H-CON-B-AR-GF-30	False Ceiling Installation & Finishing	8	20-Aug-26	29-Aug-26	20-Aug-26 A	15-Sep-26 A	873.60	873.60	873.60	100%	100%	-14
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-26	12-Sep-26	20-Aug-26 A	10-Oct-26	2,958.00	2,070.60	2,958.00	100%	70%	-40
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-26	20-Sep-26	20-Aug-26 A	12-Oct-26	273.60	191.52	273.60	100%	70%	-38
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-26	27-Sep-26	27-Aug-26 A	29-Oct-26	7,964.28	9,291.66	13,273.80	60%	70%	-49
PG-H-CON-B-AR-GF-70	Facade Finishing Work	18	21-Sep-26	12-Oct-26	20-Aug-26 A	16-Sep-26 A	1,258.60	7,551.60	7,551.60	16.67%	100%	-6
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-26	05-Oct-26	29-Oct-26	07-Nov-26	0.00	0.00	55,927.20	0%	0%	0
WET AREA FINISHES		61	12-Aug-26	11-Oct-26	07-Aug-26 A	29-Oct-26	33,209.70	79,247.22	81,123.78	40.94%	97.69%	-19
PG-H-CON-B-AR-WF-10	False Ceiling Installation & Finishing	4	12-Aug-26	16-Aug-26	20-Aug-26 A	16-Sep-26 A	2,898.00	2,898.00	2,898.00	100%	100%	-20
PG-H-CON-B-AR-WF-20	Wall Tiles and Partition Work	3	13-Sep-26	15-Sep-26	07-Aug-26 A	14-Aug-26 A	21,283.20	21,283.20	21,283.20	100%	100%	-3
PG-H-CON-B-AR-WF-30	Waterproofing on Floor	2	16-Sep-26	17-Sep-26	14-Aug-26 A	16-Sep-26 A	5,784.00	5,784.00	5,784.00	100%	100%	-27
PG-H-CON-B-AR-WF-40	Floor Tiles Works	10	19-Sep-26	30-Sep-26	14-Aug-26 A	16-Sep-26 A	3,244.50	6,489.00	6,489.00	50%	100%	-19
PG-H-CON-B-AR-WF-50	Toilet accessories Installation Works	9	01-Oct-26	11-Oct-26	27-Aug-26 A	16-Sep-26 A	0.00	39,307.98	39,307.98	0%	100%	-9
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26	05-Oct-26	27-Aug-26 A	29-Oct-26	0.00	3,485.04	5,361.60	0%	65%	-49
ROOF FINISHES		40	19-Sep-26	05-Oct-26	20-Aug-26 A	07-Nov-26	9,237.00	10,113.30	23,893.80	38.66%	42.33%	-53
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-26	22-Sep-26	20-Aug-26 A	12-Oct-26	4,158.00	2,494.80	4,158.00	100%	60%	-41
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-26	26-Sep-26	27-Aug-26 A	12-Oct-26	5,079.00	7,618.50	10,158.00	50%	75%	-37
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-26	05-Oct-26	04-Nov-26	07-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		77	28-Jul-26	05-Oct-26	22-Jul-26 A	08-Nov-26	97,590.54	74,665.10	97,726.80	99.86%	76.4%	-33
MECANICAL WORKS		77	28-Jul-26	05-Oct-26	22-Jul-26 A	08-Nov-26	79,343.22	58,857.34	79,479.48	99.83%	74.05%	-33
FIRE FIGHTING SYSTEM		1	06-Oct-26	06-Oct-26	07-Nov-26	08-Nov-26	0.00	0.00	136.26	0%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-26	06-Oct-26	07-Nov-26	08-Nov-26	0.00	0.00	136.26	0%	0%	0
SEWER AND DRAINAGE SYSTEM		43	03-Aug-26	23-Aug-26	22-Jul-26 A	01-Oct-26	11,290.02	7,580.44	11,290.02	100%	67.14%	-43
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-26	04-Aug-26	30-Jul-26 A	26-Sep-26	3,225.72	2,741.86	3,225.72	100%	85%	-46
PG-H-CON-B-GF-DR-20	Sewer and Drainge System Pipes and fittings Installation	2	18-Aug-26	19-Aug-26	22-Jul-26 A	05-Aug-26 A	4,838.58	4,838.58	4,838.58	100%	100%	-11
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-26	23-Aug-26	29-Sep-26	01-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		31	28-Jul-26	15-Aug-26	13-Aug-26 A	28-Sep-26	12,127.20	4,442.40	12,127.20	100%	36.63%	-23
PG-H-CON-B-GF-AC-10	Duct Work and Exhaust Fan Installation	3	28-Jul-26	30-Jul-26	13-Aug-26 A	20-Aug-26 A	4,442.40	4,442.40	4,442.40	100%	100%	-4
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-26	15-Aug-26	26-Sep-26	28-Sep-26	7,684.80	0.00	7,684.80	100%	0%	0
WATER SUPPLY SYSTEM		56	01-Aug-26	20-Aug-26	30-Jul-26 A	29-Sep-26	55,926.00	46,834.50	55,926.00	100%	83.74%	-34
PG-H-CON-B-GF-WS-10	Water Supply Main Lines Installation	2	01-Aug-26	02-Aug-26	30-Jul-26 A	31-Jul-26 A	5,702.40	5,702.40	5,702.40	100%	100%	1
PG-H-CON-B-GF-WS-20	Water Supply Pipes Installation (Cold and Hot Water)	2	16-Aug-26	17-Aug-26	30-Jul-26 A	06-Aug-26 A	13,857.60	13,857.60	13,857.60	100%	100%	-5
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-26	20-Aug-26	27-Aug-26 A	29-Sep-26	36,366.00	27,274.50	36,366.00	100%	75%	-25
ELECTRICAL WORKS		40	05-Aug-26	08-Sep-26	12-Aug-26 A	04-Oct-26	18,247.32	15,807.76	18,247.32	100%	86.63%	-14
PG-H-CON-B-GF-EL-10	Pipes & Conduits Installation	2	05-Aug-26	06-Aug-26	12-Aug-26 A	14-Aug-26 A	1,983.60	1,983.60	1,983.60	100%	100%	0
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-26	29-Aug-26	20-Aug-26 A	03-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-34
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-26	01-Sep-26	20-Aug-26 A	03-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-34
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-26	05-Sep-26	20-Aug-26 A	03-Oct-26	4,959.00	4,215.15	4,959.00	100%	85%	-34
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-26	08-Sep-26	20-Aug-26 A	04-Oct-26	7,337.52	6,236.89	7,337.52	100%	85%	-34
PROJECT CLOSOUT		191	25-May-26	16-Dec-26	25-May-26 A	07-Jan-27	20,443.96	75,642.64	681,465.20	3%	11.1%	-20
PG-H-PCL-10	Testing, Commissioning for All Systems(Completed)	23	25-May-26	24-Jun-26	25-May-26 A	24-Jun-26 A	20,443.96	20,443.96	20,443.96	100%	100%	0
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-26	14-Nov-26	06-Aug-26 A	06-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-94
PG-H-PCL-20	As-Built Drawings	18	14-Nov-26	05-Dec-26	06-Dec-26	27-Dec-26	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-30	Snag list Submission	8	14-Nov-26	23-Nov-26	06-Dec-26	15-Dec-26	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-40	Snag list Closeout	14	23-Nov-26	09-Dec-26	15-Dec-26	31-Dec-26	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-50	Issuing Approvals	3	09-Dec-26	13-Dec-26	31-Dec-26	04-Jan-27	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-60	Handing Over	3	13-Dec-26	16-Dec-26	04-Jan-27	07-Jan-27	0.00	0.00	68,146.52	0%	0%	0
TABUK		285	17-Feb-26	16-Dec-26	17-Feb-26 A	27-Jan-27	7,317,991.56	5,676,281.88	11,357,801.00	64.43%	49.98%	-35




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
MOBILIZATION		44	17-Feb-2	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		43	17-Feb-2	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-MOB-CAM-10	Temporary Underground Utilities works	43	17-Feb-2	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-CAM-20	Temporary Porta-Cabins	36	26-Feb-2	14-Apr-26	26-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-CAM-30	Temporary Toilets	36	26-Feb-2	14-Apr-26	26-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-CAM-40	Temporary Mosque	28	08-Mar-2	14-Apr-26	08-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SITE OFFICES		44	17-Feb-2	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-MOB-SO-10	Temporary Underground Utilities works	44	17-Feb-2	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-20	Temporary Porta-Cabins	38	25-Feb-2	15-Apr-26	25-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-30	Temporary Toilets	38	25-Feb-2	15-Apr-26	25-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-40	Temporary Mosque	32	04-Mar-2	15-Apr-26	04-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-50	Car Parking Area	25	12-Mar-2	15-Apr-26	12-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
GENERAL REQUIEREMENTS		44	17-Feb-2	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-GEN-20	HSSE Submission Plan	35	17-Feb-2	05-Apr-26	17-Feb-26 A	04-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-GEN-30	Surveying report Submission Plan	44	17-Feb-2	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-GEN-40	Baseline Submission	6	28-Feb-2	07-Mar-26	28-Feb-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-GEN-10	QA/QC Submission Plan	16	12-Mar-2	05-Apr-26	12-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	100%	100%	0
ENGINEERING		171	17-Feb-2	12-Aug-26	17-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-30
SHOP DRAWINGS SUBMITTALS		163	17-Feb-2	04-Aug-26	17-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
STRUCTURAL DRAWINGS		135	17-Feb-2	18-Jul-26	17-Feb-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	13
PROJECT FENCE		63	17-Feb-2	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-10	Excavation Drawings	63	17-Feb-2	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-20	Foundation Drawings	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		63	17-Feb-2	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-30	Excavation Drawings	63	17-Feb-2	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-40	Foundation Drawings	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		20	25-Jun-26	18-Jul-26	01-Jul-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	18
PG-T-EN-STSD-SB-50	Excavation Drawings	10	25-Jun-26	06-Jul-26	01-Jul-26 A	03-Jul-26 A	0.00	0.00	0.00	100%	100%	8
PG-T-EN-STSD-SB-60	Foundation Drawings	10	07-Jul-26	18-Jul-26	01-Jul-26 A	03-Jul-26 A	0.00	0.00	0.00	100%	100%	8
TOILET BUILDING		41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-70	Excavation Drawings	41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-80	Foundation Drawings	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-90	Excavation Drawings	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-100	Foundation Drawings	37	25-Feb-2	14-Apr-26	25-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-110	Reinforcement Detail Drawings	57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-120	Concrete Detail Drawings	54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		150	23-Feb-2	04-Aug-26	23-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
TOILET BUILDING		40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-AR-SD-SB-10	Ground Floor Plan	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-20	Roof Floor Plan	35	28-Feb-2	14-Apr-26	28-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-50	Floor Finish Layout	36	28-Feb-2	14-Apr-26	28-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-60	Reflected Ceiling Layout	36	28-Feb-2	15-Apr-26	28-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-70	Enlarged Toilets Layout	36	28-Feb-2	15-Apr-26	28-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-30	Elevations	33	03-Mar-2	15-Apr-26	03-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-80	Doors & Windows Schedule	33	03-Mar-2	15-Apr-26	03-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-90	Aluminum Work	33	03-Mar-2	15-Apr-26	03-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-100	Cladding Details	32	03-Mar-2	14-Apr-26	03-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-40	Sections	31	05-Mar-2	15-Apr-26	05-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-16
PG-T-EN-AR-SD-SB-110	Membrane & Insulation Details	15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-16
PG-T-EN-AR-SD-SB-120	Steel Cable System	15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-16
PG-T-EN-AR-SD-SB-130	Doors & Access Sytem Drawings	15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-16
LANDSCAPE DRAWINGS		40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-LS-SD-SB-10	Hardscape Layout Plan	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-20	Interlock Tile Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-30	Stamped Concrete Pattern & Section	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-40	Tartan Flooring Layout & Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-50	Bike Path Layout & Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-60	Walking Path layout & Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-70	Tree Planting Plan & Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-80	Traffic Sign Location & Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-90	Football Playground Layout	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-100	Padel Playground Layout	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-110	Basketball Playground Layout	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-120	Playground Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-130	Padel Fence Elevation & Details	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		140	28-Feb-2	12-Jul-26	28-Feb-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	-1
WATER SUPPLY SYSTEM		32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-SB-20	Pump Room Layout	32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-10	Cold & Hot Water Piping Layout	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-30	Booster Pump Details	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0

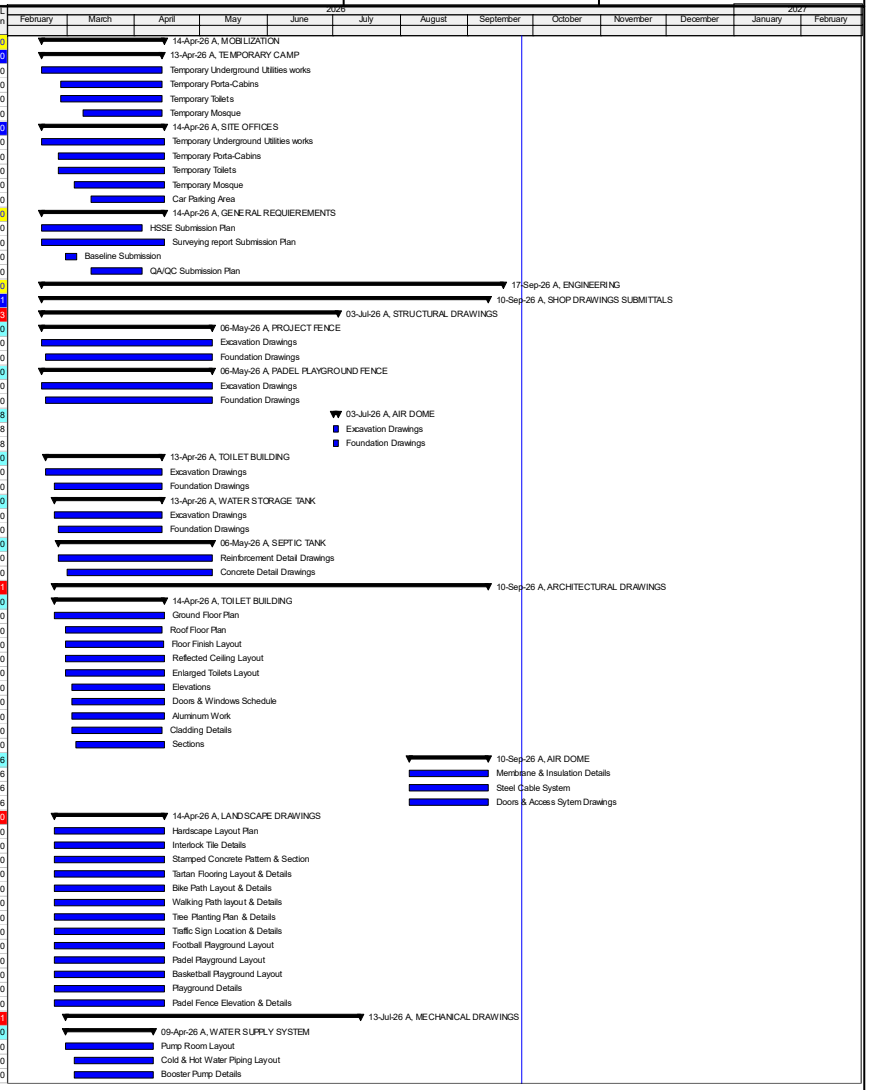


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-EN-ME-SD-SB-40	GRP Water Tank Details	24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-SB-50	Drainage Layout	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-60	Floor Drains & Cleanouts Details	24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-70	Inspection Chamber Details	21	12-Mar-2	11-Apr-26	12-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-SB-80	HDPE Pipe Routing	47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-90	Irrigation Network Layout	44	12-Mar-2	07-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	25-Jun-26	12-Jul-26	02-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	5
PG-T-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	15	25-Jun-26	12-Jul-26	02-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	100%	100%	5
ELECTRICAL DRAWINGS		98	10-May-2	29-Jul-26	10-May-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	15
POWER AND LIGHTING SYSTEM		10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-SB-10	Main Distribution Board (MDB) Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-20	Pump Room Power Panel	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-30	Street Lighting Power Panel	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-40	Site Lighting Pole Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-SB-50	Telecom & Data Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-60	CCTV Camera Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-70	Access Control Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-80	AV System Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-SB-90	Fire Alarm Layout	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-100	Detector & Manual Call Point Details	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-110	Control Panel Wiring Diagram	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		30	25-Jun-26	29-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	26
PG-T-EN-EL-SD-SB-130	Generators Details	15	25-Jun-26	12-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	100%	100%	11
PG-T-EN-EL-SD-SB-120	Power & Lighting System Drawings	15	13-Jul-26	29-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	100%	100%	11
PG-T-EN-EL-SD-SB-140	Smart Dome System Drawings	15	13-Jul-26	29-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	100%	100%	11
SHOP DRAWINGS APPROVALS		169	19-Feb-2	12-Aug-26	19-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
STRUCTURAL DRAWINGS		138	19-Feb-2	23-Jul-26	19-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	12
PROJECT FENCE		61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-10	Excavation Drawings	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-20	Foundation Drawings	58	24-Feb-2	07-May-26	24-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-30	Excavation Drawings	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-40	Foundation Drawings	58	24-Feb-2	07-May-26	24-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	07-Jul-26	23-Jul-26	05-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	10
PG-T-EN-STSD-AP-50	Excavation Drawings	5	07-Jul-26	12-Jul-26	08-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	100%	100%	3
PG-T-EN-STSD-AP-60	Foundation Drawings	5	19-Jul-26	23-Jul-26	05-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	100%	100%	3
TOILET BUILDING		42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-70	Excavation Drawings	42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-80	Foundation Drawings	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-90	Excavation Drawings	40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-100	Foundation Drawings	37	01-Mar-2	18-Apr-26	01-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-110	Reinforcement Detail Drawings	54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-120	Concrete Detail Drawings	51	04-Mar-2	07-May-26	04-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		153	28-Feb-2	12-Aug-26	28-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
TOILET BUILDING		38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-AR-SD-AP-10	Ground Floor Plan	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-20	Roof Floor Plan	35	03-Mar-2	18-Apr-26	03-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-50	Floor Finish Layout	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-60	Reflected Ceiling Layout	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-70	Enlarged Toilets Layout	33	05-Mar-2	18-Apr-26	05-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-30	Elevations	32	07-Mar-2	18-Apr-26	07-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-80	Doors & Windows Schedule	32	07-Mar-2	18-Apr-26	07-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-90	Aluminum Work	31	08-Mar-2	18-Apr-26	08-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-100	Cladding Details	31	08-Mar-2	18-Apr-26	08-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-40	Sections	29	10-Mar-2	18-Apr-26	10-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
PG-T-EN-AR-SD-AP-110	Membrane & Insulation Details	7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	100%	100%	-17
PG-T-EN-AR-SD-AP-120	Steel Cable System	7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	100%	100%	-17
PG-T-EN-AR-SD-AP-130	Doors & Access Sytem Drawings	7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	100%	100%	-17
LANDSCAPE DRAWINGS		39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-LS-SD-AP-50	Bike Path Layout & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-60	Walking Path layout & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-80	Traffic Sign Location & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-130	Padel Fence Elevation & Details	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-10	Hardscape Layout Plan	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-40	Tartan Flooring Layout & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-70	Tree Planting Plan & Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0

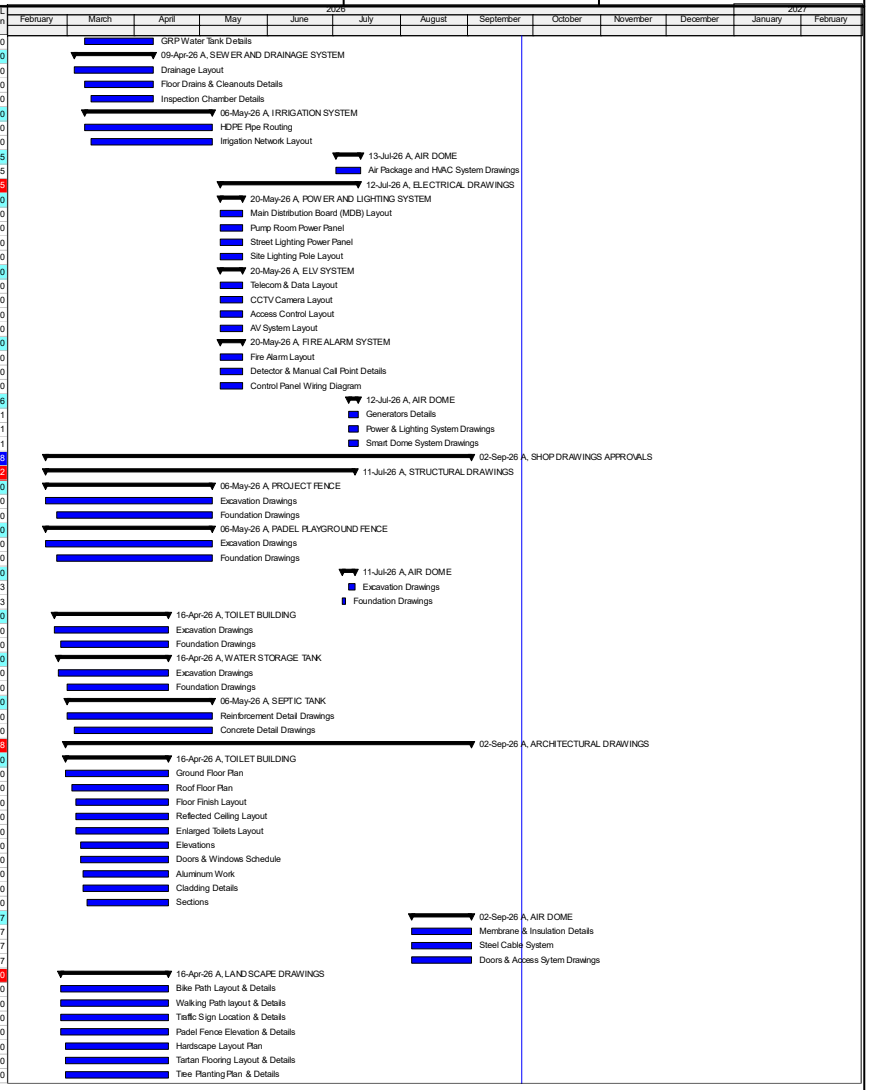


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-EN-LS-SD-AP-90	Football Playground Layout	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-100	Padel Playground Layout	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-110	Basketball Playground Layout	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-120	Playground Details	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-20	Interlock Tile Details	30	09-Mar-2	18-Apr-26	09-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-30	Stamped Concrete Pattern & Section	24	16-Mar-2	18-Apr-26	16-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		142	09-Mar-2	23-Jul-26	09-Mar-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
WATER SUPPLY SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-AP-10	Cold & Hot Water Piping Layout	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-30	Booster Pump Details	26	10-Mar-2	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-40	GRP Water Tank Details	23	14-Mar-2	14-Apr-26	14-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-20	Pump Room Layout	21	16-Mar-2	14-Apr-26	16-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-AP-50	Drainage Layout	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-60	Floor Drains & Cleanouts Details	21	16-Mar-2	14-Apr-26	16-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-70	Inspection Chamber Details	21	16-Mar-2	14-Apr-26	16-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		44	12-Mar-2	07-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-AP-80	HDPE Pipe Routing	44	12-Mar-2	07-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-90	Irrigation Network Layout	40	17-Mar-2	07-May-26	17-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		10	13-Jul-26	23-Jul-26	13-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
PG-T-EN-ME-SD-AP-100	Air Package and HVAC System Drawings	10	13-Jul-26	23-Jul-26	13-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	100%	100%	5
ELECTRICAL DRAWINGS		105	11-May-2	08-Aug-26	11-May-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
POWER AND LIGHTING SYSTEM		28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-AP-10	Main Distribution Board (MDB) Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-20	Pump Room Power Panel	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-30	Street Lighting Power Panel	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-40	Site Lighting Pole Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-AP-50	Telecom & Data Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-60	CCTV Camera Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-70	Access Control Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-80	AV System Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-AP-90	Fire Alarm Layout	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-100	Detector & Manual Call Point Details	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-110	Control Panel Wiring Diagram	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		23	13-Jul-26	08-Aug-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
PG-T-EN-EL-SD-AP-130	Generators Details	8	13-Jul-26	21-Jul-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	100%	100%	2
PG-T-EN-EL-SD-AP-120	Power & Lighting System Drawings	8	30-Jul-26	08-Aug-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	100%	100%	2
PG-T-EN-EL-SD-AP-140	Smart Dome System Drawings	8	30-Jul-26	08-Aug-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	100%	100%	2
MATERIAL SUBMITTALS		166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
LONG LEAD ITEMS		166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
EXTERNAL / LANDSCAPE WORK		57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-LS-MS-20	Benches, Seats (Rectangular & Circular)	57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MS-30	Fence, gates and accessories	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MS-10	Bike and Walk Path Materials	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		124	17-Feb-2	05-Jul-26	17-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-51
PG-T-PR-LL-SPM-S-50	Air Dome Materials(Completed)	101	17-Feb-2	25-Jun-26	17-Feb-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPM-S-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	49	07-Mar-2	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPM-S-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	49	07-Mar-2	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPM-S-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	49	07-Mar-2	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPM-S-40	Tartan Floor	49	07-Mar-2	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPM-S-50_R	Air Dome Materials(Remaining)	9	25-Jun-26	05-Jul-26	07-Jul-26 A	02-Sep-26 A	0.00	0.00	0.00	100%	100%	-41
CONCRETE WORK		41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-CO-MS-10	Autoclaved Aerated Panel	41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		45	11-Mar-2	07-May-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-MT-MS-10	Metal Doors	45	11-Mar-2	07-May-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-MS-20	Curtain Wall	45	11-Mar-2	07-May-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-PB-MS-10	Booster Pump	46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-MS-20	GRP Sectional Panel Water Tanks (4x3x3m)	42	15-Mar-2	07-May-26	15-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-IR-MS-10	HDPE Pipes	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-MS-20	Irrigation Control System	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		100	11-May-2	11-Jul-26	11-May-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
PG-T-PR-LL-EL-MS-10	Main Distribution Board(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-20	Power Panels (Pump, Street Light)(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-30	Site Lighting Poles(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-40	Lighting Fixtures(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-70	Security and Access Control System Materials(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-80	Fire Alarm System Materials(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0

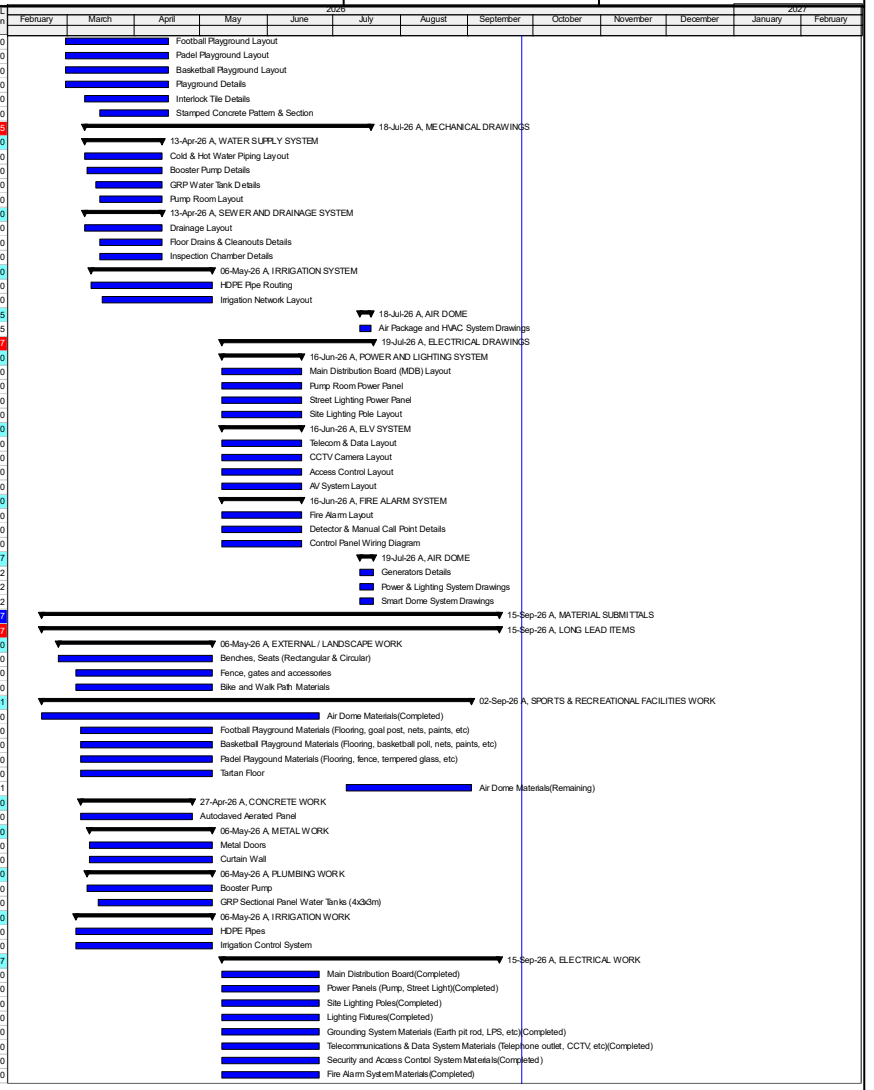


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-EL-MS-10_R	Main Distribution Board(Remaining)	10	25-Jun-26	06-Jul-26	16-Jul-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	-8
PG-T-PR-LL-EL-MS-20_R	Power Panels (Pump, Street Light)(Remaining)	10	25-Jun-26	06-Jul-26	16-Jul-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	-8
PG-T-PR-LL-EL-MS-30_R	Site Lighting Poles(Remaining)	10	25-Jun-26	06-Jul-26	16-Jul-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	-8
PG-T-PR-LL-EL-MS-40_R	Lighting Fixtures(Remaining)	10	25-Jun-26	06-Jul-26	16-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%	4
PG-T-PR-LL-EL-MS-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	10	25-Jun-26	06-Jul-26	16-Jul-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%	-43
PG-T-PR-LL-EL-MS-70_R	Security and Access Control System Materials(Remaining)	10	25-Jun-26	06-Jul-26	16-Jul-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%	-43
PG-T-PR-LL-EL-MS-80_R	Fire Alarm System Materials(Remaining)	10	25-Jun-26	06-Jul-26	27-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%	-7
PG-T-PR-LL-EL-MS-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	5	06-Jul-26	11-Jul-26	16-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	100%	100%	1
SHORT LEAD ITEMS		28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-26	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-LS-MS-10	Backfilling Materials	23	17-Feb-26	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-30	Compacted Natural Ground Soil	20	21-Feb-26	17-Mar-26	21-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-60	Traffic Signages	9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-40	Curb Stone	7	09-Mar-26	17-Mar-26	09-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-20	Interlock tiles	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-50	Thermoplastic pavement road marking	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-70	Tiees	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-80	Lawn	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-CO-MS-10	Steel Rebar	17	17-Feb-26	10-Mar-26	17-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-20	Concrete	13	23-Feb-26	10-Mar-26	23-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-40	CMU Block	19	01-Mar-26	28-Mar-26	01-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-50	Concrete Repair & Protection Materials	19	01-Mar-26	28-Mar-26	01-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-30	Screed	10	11-Mar-26	28-Mar-26	11-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AR-MS-10	Ceramic tiles	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-20	Anti-slip Granite tiles	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-30	Epoxy Paint	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-40	Cement Plaster	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-50	Acrylic Paint	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-60	Stone Cladding	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-70	Phenolic Partition	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-80	Glass Partition	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-90	Gypsum Boards	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-110	Waterproofing System Materials	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-MT-MS-20	Galvanized Steel Roof Scupper	9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-MS-30	Galvanized Steel Cover with frame	9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-MS-10	Galvanized Steel Ladder	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		19	23-Feb-26	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AC-MS-10	Split Air Conditioning Unit	19	23-Feb-26	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-MS-20	Air Duct	15	28-Feb-26	17-Mar-26	28-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-MS-30	Diffusers and Grills	11	04-Mar-26	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-MS-40	Exhaust fans	11	04-Mar-26	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-PB-MS-10	PPR Pipes & Valves	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-MS-20	UPCV Pipes	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-MS-30	Sanitary Drainage Fixtures	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-IR-MS-10	Gate Valve including valve box	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-IR-MS-20	Bubblers and Spreyers	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-EL-MS-10	Wiring Devices Materials	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-FF-MS-10	Fire Extinguishers	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	0
MATERIAL APPROVALS		160	21-Feb-26	13-Jul-26	21-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-56
LONG LEAD ITEMS		157	25-Feb-26	13-Jul-26	25-Feb-26 A	17-Sep-26 A	284,659.98	284,659.98	284,659.98	100%	100%	-56
EXTERNAL / LANDSCAPE WORK		56	25-Feb-26	05-May-26	25-Feb-26 A	05-May-26 A	15,425.28	15,425.28	15,425.28	100%	100%	0
PG-T-PR-LL-LS-MA-20	Benches, Seats (Rectangular & Circular)	56	25-Feb-26	05-May-26	25-Feb-26 A	05-May-26 A	3,869.07	3,869.07	3,869.07	100%	100%	0
PG-T-PR-LL-LS-MA-30	Fence, gates and accessories	43	12-Mar-26	05-May-26	12-Mar-26 A	05-May-26 A	2,529.21	2,529.21	2,529.21	100%	100%	0
PG-T-PR-LL-LS-MA-10	Bike and Walk Path Materials	41	15-Mar-26	05-May-26	15-Mar-26 A	05-May-26 A	9,027.00	9,027.00	9,027.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		119	02-Mar-26	11-Jul-26	02-Mar-26 A	03-Sep-26 A	238,773.54	238,773.54	238,773.54	100%	100%	-47
PG-T-PR-LL-SP-MA-50	Air Dome Materials(Completed)	91	02-Mar-26	24-Jun-26	02-Mar-26 A	24-Jun-26 A	62,622.07	62,622.07	62,622.07	100%	100%	0
PG-T-PR-LL-SP-MA-40	Tartan Floor	43	12-Mar-26	05-May-26	12-Mar-26 A	05-May-26 A	8,775.00	8,775.00	8,775.00	100%	100%	0
PG-T-PR-LL-SP-MA-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	42	14-Mar-26	05-May-26	14-Mar-26 A	05-May-26 A	13,051.50	13,051.50	13,051.50	100%	100%	0
PG-T-PR-LL-SP-MA-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	42	14-Mar-26	05-May-26	14-Mar-26 A	05-May-26 A	2,256.00	2,256.00	2,256.00	100%	100%	0
PG-T-PR-LL-SP-MA-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	42	14-Mar-26	05-May-26	14-Mar-26 A	05-May-26 A	5,950.80	5,950.80	5,950.80	100%	100%	0
PG-T-PR-LL-SP-MA-50_R	Air Dome Materials(Remaining)	5	06-Jul-26	11-Jul-26	09-Jul-26 A	03-Sep-26 A	146,118.17	146,118.17	146,118.17	100%	100%	-44
CONCRETE WORK		38	11-Mar-26	28-Apr-26	11-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
PG-T-PR-LL-CO-MA-10	Autoclaved Aerated Panel	38	11-Mar-26	28-Apr-26	11-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
PG-T-PR-LL-MT-MA-10	Metal Doors	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	127.53	127.53	127.53	100%	100%	0

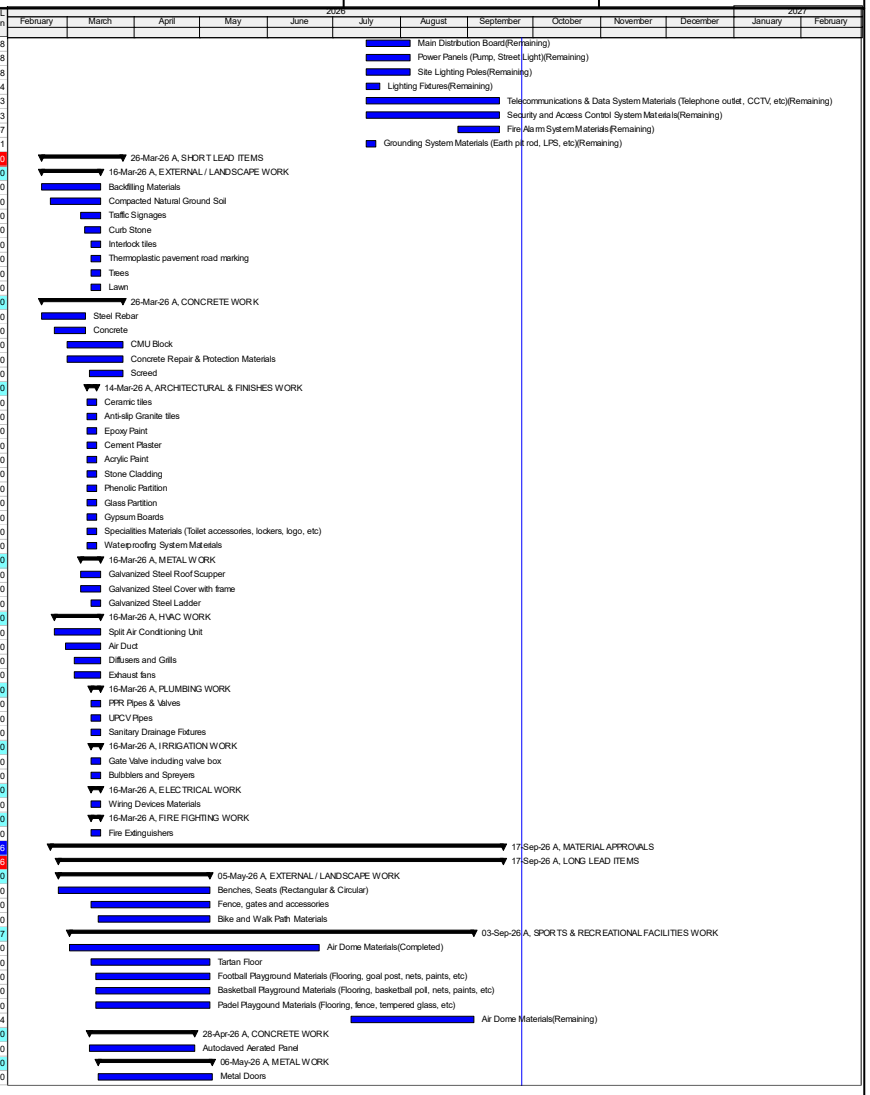


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-MT-MA-20	Curtain Wall	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	761.70	761.70	761.70	100%	100%	0
PLUMBING WORK		42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
PG-T-PR-LL-PB-MA-10	Booster Pump	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	1,818.30	1,818.30	1,818.30	100%	100%	0
PG-T-PR-LL-PB-MA-20	GRP Sectional Panel Water Tanks (4x3x3m)	38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	1,735.65	1,735.65	1,735.65	100%	100%	0
IRRIGATION WORK		45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	6,802.65	6,802.65	6,802.65	100%	100%	0
PG-T-PR-LL-IR-MA-10	HDPE Pipes	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	2,256.90	2,256.90	2,256.90	100%	100%	0
PG-T-PR-LL-IR-MA-20	Irrigation Control System	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	4,545.75	4,545.75	4,545.75	100%	100%	0
ELECTRICAL WORK		96	12-May-26	13-Jul-26	12-May-26 A	17-Sep-26 A	17,797.83	17,797.83	17,797.83	100%	100%	-56
PG-T-PR-LL-EL-MA-10	Main Distribution Board(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	297.54	297.54	297.54	100%	100%	0
PG-T-PR-LL-EL-MA-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	238.03	238.03	238.03	100%	100%	0
PG-T-PR-LL-EL-MA-30	Site Lighting Poles(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	6,962.11	6,962.11	6,962.11	100%	100%	0
PG-T-PR-LL-EL-MA-40	Lighting Fixtures(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	769.70	769.70	769.70	100%	100%	0
PG-T-PR-LL-EL-MA-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	602.51	602.51	602.51	100%	100%	0
PG-T-PR-LL-EL-MA-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	587.63	587.63	587.63	100%	100%	0
PG-T-PR-LL-EL-MA-70	Security and Access Control System Materials(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	743.94	743.94	743.94	100%	100%	0
PG-T-PR-LL-EL-MA-80	Fire Alarm System Materials(Completed)	34	12-May-26	24-Jun-26	12-May-26 A	24-Jun-26 A	477.23	477.23	477.23	100%	100%	0
PG-T-PR-LL-EL-MA-10_R	Main Distribution Board(Remaining)	7	25-Jun-26	02-Jul-26	17-Jul-26 A	06-Aug-26 A	198.36	198.36	198.36	100%	100%	-11
PG-T-PR-LL-EL-MA-20_R	Power Panels (Pump, Street Light)(Remaining)	7	25-Jun-26	02-Jul-26	17-Jul-26 A	06-Aug-26 A	158.69	158.69	158.69	100%	100%	-11
PG-T-PR-LL-EL-MA-30_R	Site Lighting Poles(Remaining)	7	25-Jun-26	02-Jul-26	17-Jul-26 A	06-Aug-26 A	4,641.41	4,641.41	4,641.41	100%	100%	-11
PG-T-PR-LL-EL-MA-40_R	Lighting Fixtures(Remaining)	7	25-Jun-26	02-Jul-26	17-Jul-26 A	23-Jul-26 A	513.13	513.13	513.13	100%	100%	1
PG-T-PR-LL-EL-MA-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	7	25-Jun-26	02-Jul-26	17-Jul-26 A	17-Sep-26 A	391.75	391.75	391.75	100%	100%	-46
PG-T-PR-LL-EL-MA-70_R	Security and Access Control System Materials(Remaining)	7	25-Jun-26	02-Jul-26	17-Jul-26 A	17-Sep-26 A	495.96	495.96	495.96	100%	100%	-46
PG-T-PR-LL-EL-MA-80_R	Fire Alarm System Materials(Remaining)	7	25-Jun-26	02-Jul-26	27-Aug-26 A	17-Sep-26 A	318.16	318.16	318.16	100%	100%	-11
PG-T-PR-LL-EL-MA-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	2	12-Jul-26	13-Jul-26	22-Jul-26 A	28-Jul-26 A	401.68	401.68	401.68	100%	100%	-4
SHORT LEAD ITEMS		25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	56,074.05	56,074.05	56,074.05	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	38,542.29	38,542.29	38,542.29	100%	100%	0
PG-T-PR-SL-LS-MA-10	Backfilling Materials	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	10,125.00	10,125.00	10,125.00	100%	100%	0
PG-T-PR-SL-LS-MA-30	Compacted Natural Ground Soil	22	25-Feb-26	26-Mar-26	25-Feb-26 A	26-Mar-26 A	1,287.00	1,287.00	1,287.00	100%	100%	0
PG-T-PR-SL-LS-MA-60	Traffic Signages	11	10-Mar-26	26-Mar-26	10-Mar-26 A	26-Mar-26 A	198.36	198.36	198.36	100%	100%	0
PG-T-PR-SL-LS-MA-70	Tiees	8	14-Mar-26	26-Mar-26	14-Mar-26 A	26-Mar-26 A	2,306.10	2,306.10	2,306.10	100%	100%	0
PG-T-PR-SL-LS-MA-80	Lawn	8	14-Mar-26	26-Mar-26	14-Mar-26 A	26-Mar-26 A	3,045.00	3,045.00	3,045.00	100%	100%	0
PG-T-PR-SL-LS-MA-50	Thermoplastic pavement road marking	6	16-Mar-26	26-Mar-26	16-Mar-26 A	26-Mar-26 A	525.63	525.63	525.63	100%	100%	0
PG-T-PR-SL-LS-MA-20	Interlock tiles	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	10,715.40	10,715.40	10,715.40	100%	100%	0
PG-T-PR-SL-LS-MA-40	Curb Stone	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	10,339.80	10,339.80	10,339.80	100%	100%	0
CONCRETE WORK		24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
PG-T-PR-SL-CO-MA-10	Steel Rebar	14	23-Feb-26	10-Mar-26	23-Feb-26 A	10-Mar-26 A	476.82	476.82	476.82	100%	100%	0
PG-T-PR-SL-CO-MA-20	Concrete	9	01-Mar-26	10-Mar-26	01-Mar-26 A	10-Mar-26 A	518.85	518.85	518.85	100%	100%	0
PG-T-PR-SL-CO-MA-40	CMU Block	15	05-Mar-26	26-Mar-26	05-Mar-26 A	26-Mar-26 A	124.20	124.20	124.20	100%	100%	0
PG-T-PR-SL-CO-MA-50	Concrete Repair & Protection Materials	15	05-Mar-26	26-Mar-26	05-Mar-26 A	26-Mar-26 A	372.00	372.00	372.00	100%	100%	0
PG-T-PR-SL-CO-MA-30	Screed	1	26-Mar-26	26-Mar-26	26-Mar-26 A	26-Mar-26 A	117.60	117.60	117.60	100%	100%	0
ARCHITECTURAL & FINISHES WORK		2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
PG-T-PR-SL-AR-MA-10	Ceramic tiles	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	571.95	571.95	571.95	100%	100%	0
PG-T-PR-SL-AR-MA-20	Anti-slip Granite tiles	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	535.50	535.50	535.50	100%	100%	0
PG-T-PR-SL-AR-MA-30	Epoxy Paint	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	111.18	111.18	111.18	100%	100%	0
PG-T-PR-SL-AR-MA-40	Cement Plaster	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	221.37	221.37	221.37	100%	100%	0
PG-T-PR-SL-AR-MA-50	Acrylic Paint	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	147.90	147.90	147.90	100%	100%	0
PG-T-PR-SL-AR-MA-60	Stone Cladding	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	1,852.20	1,852.20	1,852.20	100%	100%	0
PG-T-PR-SL-AR-MA-70	Phenolic Partition	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	1,340.40	1,340.40	1,340.40	100%	100%	0
PG-T-PR-SL-AR-MA-80	Glass Partition	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	155.40	155.40	155.40	100%	100%	0
PG-T-PR-SL-AR-MA-90	Gypsum Boards	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	188.58	188.58	188.58	100%	100%	0
PG-T-PR-SL-AR-MA-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	2,262.87	2,262.87	2,262.87	100%	100%	0
PG-T-PR-SL-AR-MA-110	Waterproofing System Materials	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	544.20	544.20	544.20	100%	100%	0
METAL WORK		10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
PG-T-PR-SL-MT-MA-20	Galvanized Steel Roof Scupper	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	31.32	31.32	31.32	100%	100%	0
PG-T-PR-SL-MT-MA-30	Galvanized Steel Cover with frame	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	85.71	85.71	85.71	100%	100%	0
PG-T-PR-SL-MT-MA-10	Galvanized Steel Ladder	7	15-Mar-26	26-Mar-26	15-Mar-26 A	26-Mar-26 A	361.86	361.86	361.86	100%	100%	0
HVAC WORK		20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
PG-T-PR-SL-AC-MA-10	Split Air Conditioning Unit	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	309.93	309.93	309.93	100%	100%	0
PG-T-PR-SL-AC-MA-20	Air Duct	16	04-Mar-26	26-Mar-26	04-Mar-26 A	26-Mar-26 A	156.00	156.00	156.00	100%	100%	0
PG-T-PR-SL-AC-MA-30	Diffusers and Grills	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	74.31	74.31	74.31	100%	100%	0
PG-T-PR-SL-AC-MA-40	Exhaust fans	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	66.12	66.12	66.12	100%	100%	0
PLUMBING WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
PG-T-PR-SL-PB-MA-10	PPR Pipes & Valves	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	265.20	265.20	265.20	100%	100%	0
PG-T-PR-SL-PB-MA-20	UPCV Pipes	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	335.19	335.19	335.19	100%	100%	0
PG-T-PR-SL-PB-MA-30	Sanitary Drainage Fixtures	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	2,546.64	2,546.64	2,546.64	100%	100%	0
IRRIGATION WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,328.23	3,328.23	3,328.23	100%	100%	0
PG-T-PR-SL-IR-MA-10	Gate Valve including valve box	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	413.28	413.28	413.28	100%	100%	0
PG-T-PR-SL-IR-MA-20	Bubblers and Spreyers	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	2,914.95	2,914.95	2,914.95	100%	100%	0
ELECTRICAL WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
PG-T-PR-SL-EL-MA-10	Wiring Devices Materials	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PG-T-PR-SL-FF-MA-10	Fire Extinguishers	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PROCUREMENT		201	26-Feb-26	27-Aug-26	26-Feb-26 A	19-Oct-26	3,066,606.27	1,798,923.19	3,066,606.27	100%	58.66%	-43

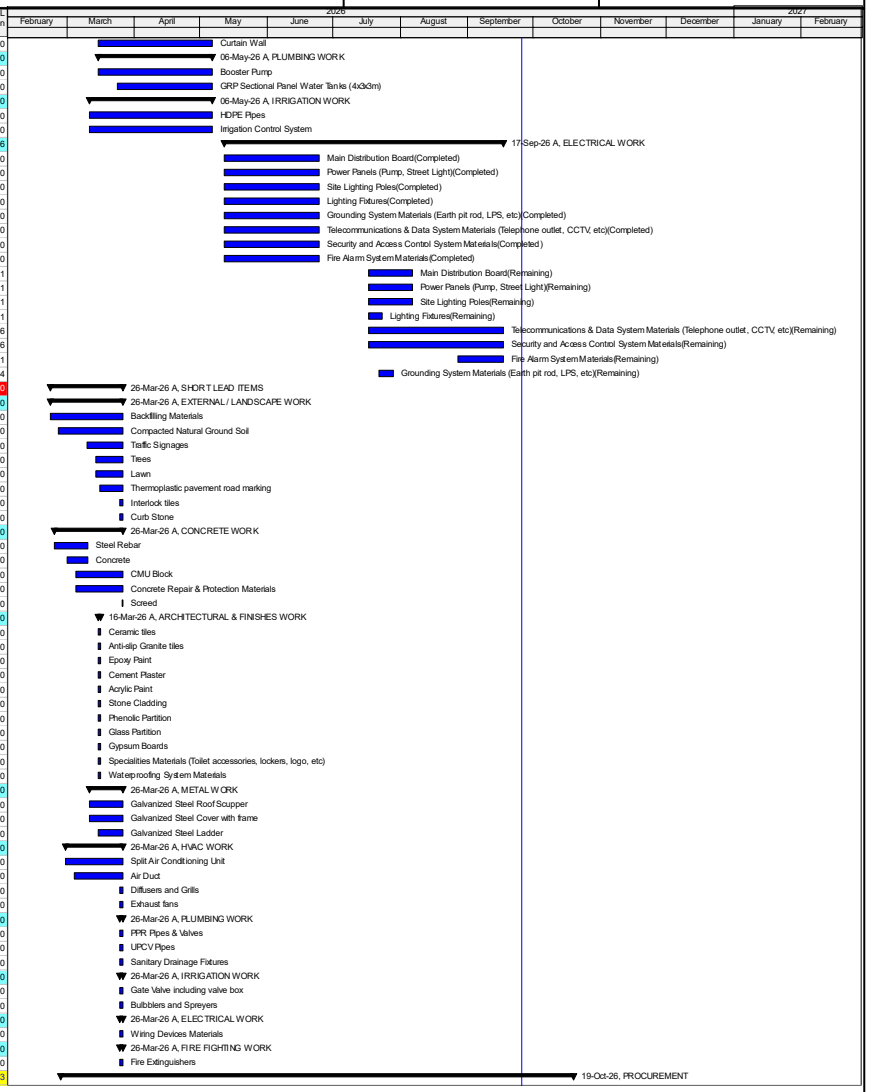


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
LONG LEAD ITEMS		194	07-Mar-2	27-Aug-26	07-Mar-26 A	19-Oct-26	2,561,939.82	1,301,698.09	2,561,939.82	100%	50.81%	-43
PURCHASE ORDER		157	07-Mar-2	16-Jul-26	07-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
EXTERNAL / LANDSCAPE WORK		49	07-Mar-2	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-LS-PO-20	Benches, Seats (Rectangular & Circular)	49	07-Mar-2	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-PO-30	Fence, gates and accessories	36	26-Mar-2	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-PO-10	Bike and Walk Path Materials	34	29-Mar-2	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		119	26-Mar-2	16-Jul-26	26-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
PG-T-PR-LL-SPPO-40	Tartan Floor	36	26-Mar-2	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	35	28-Mar-2	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	35	28-Mar-2	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	35	28-Mar-2	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-50	Air Dome Materials	5	12-Jul-26	16-Jul-26	06-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-26
CONCRETE WORK		39	18-Mar-2	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-CO-PO-10	Autoclaved Aerated Panel	39	18-Mar-2	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		38	24-Mar-2	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-MT-PO-10	Metal Doors	38	24-Mar-2	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-PO-20	Curtain Wall	38	24-Mar-2	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		35	28-Mar-2	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-PB-PO-10	Booster Pump	35	28-Mar-2	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-PO-20	GRP Sectional Panel Water Tanks (4x3x3m)	33	30-Mar-2	07-May-26	30-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		40	17-Mar-2	07-May-26	17-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-IR-PO-20	Irrigation Control System	40	17-Mar-2	07-May-26	17-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-PO-10	HDPE Pipes	39	18-Mar-2	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		105	11-May-2	16-Jul-26	11-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
PG-T-PR-LL-EL-PO-10	Main Distribution Board(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-20	Power Panels (Pump, Street Light)(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-30	Site Lighting Poles(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-40	Lighting Fixtures(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-70	Security and Access Control System Materials(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-80	Fire Alarm System Materials(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-10_R	Main Distribution Board(Remaining)	8	04-Jul-26	12-Jul-26	26-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-32
PG-T-PR-LL-EL-PO-20_R	Power Panels (Pump, Street Light)(Remaining)	8	04-Jul-26	12-Jul-26	26-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-32
PG-T-PR-LL-EL-PO-30_R	Site Lighting Poles(Remaining)	8	04-Jul-26	12-Jul-26	26-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-32
PG-T-PR-LL-EL-PO-40_R	Lighting Fixtures(Remaining)	8	04-Jul-26	12-Jul-26	23-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-34
PG-T-PR-LL-EL-PO-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	8	04-Jul-26	12-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-T-PR-LL-EL-PO-70_R	Security and Access Control System Materials(Remaining)	8	04-Jul-26	12-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-T-PR-LL-EL-PO-80_R	Fire Alarm System Materials(Remaining)	8	04-Jul-26	12-Jul-26	27-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-4
PG-T-PR-LL-EL-PO-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	3	14-Jul-26	16-Jul-26	26-Jul-26 A	10-Sep-26 A	0.00	0.00	0.00	100%	100%	-37
MANUFACTURE / FABRICATION		140	29-Apr-26	16-Aug-26	29-Apr-26 A	12-Oct-26	0.00	0.00	0.00	0%	0%	-48
EXTERNAL / LANDSCAPE WORK		102	06-May-2	23-Jul-26	06-May-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-61
PG-T-PR-LL-LS-MF-20	Benches, Seats (Rectangular & Circular)(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MF-30	Fence, gates and accessories(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MF-10	Bike and Walk Path Materials(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	04-Oct-26	0.00	0.00	0.00	100%	70%	-26
PG-T-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	6	25-Jun-26	01-Jul-26	22-Jul-26 A	26-Sep-26	0.00	0.00	0.00	100%	90%	-50
PG-T-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
SPORTS & RECREATIONAL FACILITIES WORK		124	06-May-2	16-Aug-26	06-May-26 A	07-Oct-26	0.00	0.00	0.00	0%	0%	-43
PG-T-PR-LL-SPMF-10	Football Playground Materials (Flooring, goal post, nets, paints,	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-30	Padel Playgound Materials (Flooring, fence, tempered glass,	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-40	Tartan Floor(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-30_R	Padel Playgound Materials (Flooring, fence, tempered glass,	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-40_R	Tartan Floor(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26	16-Aug-26	27-Aug-26 A	07-Oct-26	0.00	0.00	0.00	100%	60%	-8
CONCRETE WORK		64	29-Apr-26	30-Jun-26	29-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	0%	0%	-2
PG-T-PR-LL-CO-MF-10	Autoclaved Aerated Panel(Completed)	45	29-Apr-26	25-Jun-26	29-Apr-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-CO-MF-10_R	Autoclaved Aerated Panel(Remaining)	5	25-Jun-26	30-Jun-26	01-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%	3
METAL WORK		119	06-May-2	23-Jul-26	06-May-26 A	12-Oct-26	0.00	0.00	0.00	0%	0%	-68
PG-T-PR-LL-MT-MF-10	Metal Doors(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-MF-20	Curtain Wall(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26	23-Jul-26	27-Aug-26 A	10-Oct-26	0.00	0.00	0.00	100%	50%	-12
PG-T-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	27-Aug-26 A	12-Oct-26	0.00	0.00	0.00	100%	40%	-14
PLUMBING WORK		102	06-May-2	23-Jul-26	06-May-26 A	30-Sep-26	0.00	0.00	0.00	0%	0%	-58
PG-T-PR-LL-PB-MF-10	Booster Pump(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-MF-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-MF-10_R	Booster Pump(Remaining)	25	25-Jun-26	23-Jul-26	25-Jun-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%	18
PG-T-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-23
IRRIGATION WORK		99	06-May-2	01-Jul-26	06-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-70
PG-T-PR-LL-IR-MF-10	HDPE Pipes(Completed)	39	06-May-2	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0

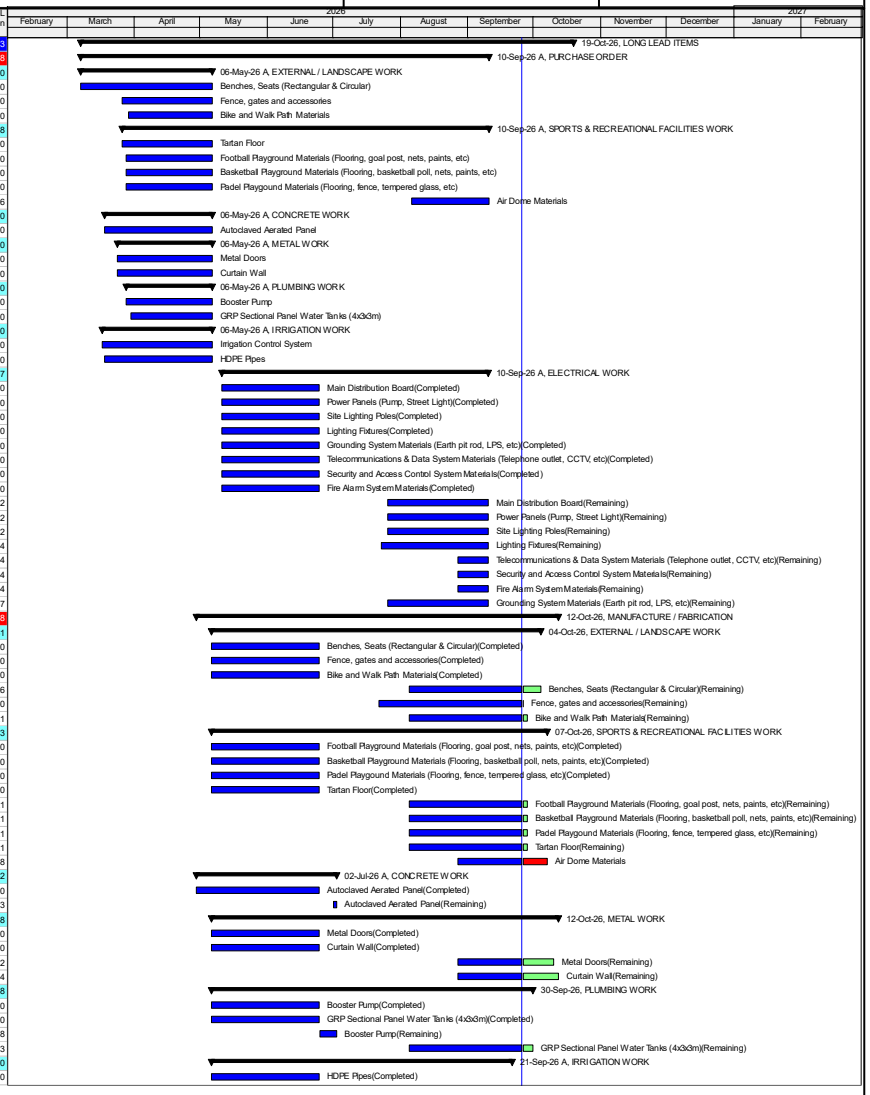


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-IR-MF-20	Irrigation Control System(Completed)	39	06-May-26	25-Jun-26	06-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-MF-10_R	HDPE Pipes(Remaining)	5	25-Jun-26	01-Jul-26	14-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	-7
PG-T-PR-LL-IR-MF-20_R	Irrigation Control System(Remaining)	5	25-Jun-26	01-Jul-26	27-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	-16
ELECTRICAL WORK		129	12-May-26	10-Aug-26	12-May-26 A	30-Sep-26	0.00	0.00	0.00	0%	0%	-43
PG-T-PR-LL-EL-MF-10	Main Distribution Board(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-30	Site Lighting Poles(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-40	Lighting Fixtures(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-70	Security and Access Control System Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-80	Fire Alarm System Materials(Completed)	34	12-May-26	25-Jun-26	12-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	25	13-Jul-26	10-Aug-26	06-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-22
PG-T-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	25	13-Jul-26	10-Aug-26	06-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-22
PG-T-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	13-Jul-26	10-Aug-26	06-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-22
PG-T-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	13-Jul-26	10-Aug-26	23-Jul-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-34
PG-T-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	13-Jul-26	10-Aug-26	27-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-4
PG-T-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-4
PG-T-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-4
PG-T-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	6	18-Jul-26	23-Jul-26	27-Aug-26 A	27-Sep-26	0.00	0.00	0.00	100%	80%	-19
DELIVERY TO SITE		146	06-May-26	27-Aug-26	06-May-26 A	19-Oct-26	2,561,939.82	1,301,698.09	2,561,939.82	100%	50.81%	-43
EXTERNAL / LANDSCAPE WORK		114	06-May-26	06-Aug-26	06-May-26 A	27-Sep-26	138,827.52	136,216.01	138,827.52	100%	98.12%	-42
PG-T-PR-LL-LS-DL-20	Benches, Seats (Rectangular & Circular)(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	20,892.98	20,892.98	20,892.98	100%	100%	0
PG-T-PR-LL-LS-DL-30	Fence, gates and accessories(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	11,381.45	11,381.45	11,381.45	100%	100%	0
PG-T-PR-LL-LS-DL-10	Bike and Walk Path Materials(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	56,870.10	56,870.10	56,870.10	100%	100%	0
PG-T-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	5	02-Jul-26	07-Jul-26	23-Jul-26 A	19-Sep-26 A	11,381.45	11,381.45	11,381.45	100%	100%	-45
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	13,928.65	12,535.79	13,928.65	100%	90%	-24
PG-T-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	26-Sep-26	24,372.90	23,154.26	24,372.90	100%	95%	-31
SPORTS & RECREATIONAL FACILITIES WORK		129	06-May-26	27-Aug-26	06-May-26 A	14-Oct-26	2,148,961.86	914,316.47	2,148,961.86	100%	42.55%	-40
PG-T-PR-LL-SPDL-10	Football Playground Materials (Flooring, goal post, nets, paints,	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	58,731.75	58,731.75	58,731.75	100%	100%	0
PG-T-PR-LL-SPDL-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	10,152.00	10,152.00	10,152.00	100%	100%	0
PG-T-PR-LL-SPDL-30	Padel Playground Materials (Fence, tempered glass, etc)(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	26,778.60	26,778.60	26,778.60	100%	100%	0
PG-T-PR-LL-SPDL-40	Tartan Floor(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	39,487.50	39,487.50	39,487.50	100%	100%	0
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	58,731.75	52,858.58	58,731.75	100%	90%	-24
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	10,152.00	9,136.80	10,152.00	100%	90%	-24
PG-T-PR-LL-SPDL-30_R	Padel Playground Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	26,778.60	24,100.74	26,778.60	100%	90%	-24
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	39,487.50	35,538.75	39,487.50	100%	90%	-31
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-26	27-Aug-26	20-Aug-26 A	14-Oct-26	1,878,662.16	657,531.76	1,878,662.16	100%	35%	-37
CONCRETE WORK		63	06-May-26	06-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	1
PG-T-PR-LL-CO-DL-10	Autoclaved Aerated Panel(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	8,930.25	8,930.25	8,930.25	100%	100%	0
PG-T-PR-LL-CO-DL-10_R	Autoclaved Aerated Panel(Remaining)	5	01-Jul-26	06-Jul-26	04-Jul-26 A	05-Jul-26 A	3,827.25	3,827.25	3,827.25	100%	100%	3
METAL WORK		131	06-May-26	05-Aug-26	06-May-26 A	19-Oct-26	8,003.07	6,259.77	8,003.07	100%	78.22%	-61
PG-T-PR-LL-MT-DL-10	Metal Doors(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	573.89	573.89	573.89	100%	100%	0
PG-T-PR-LL-MT-DL-20	Curtain Wall(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	3,427.65	3,427.65	3,427.65	100%	100%	0
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	14-Oct-26	573.89	373.03	573.89	100%	65%	-29
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	19-Oct-26	3,427.65	1,885.21	3,427.65	100%	55%	-32
PLUMBING WORK		108	06-May-26	06-Aug-26	06-May-26 A	28-Sep-26	31,985.55	30,423.47	31,985.55	100%	95.12%	-44
PG-T-PR-LL-PB-DL-10	Booster Pump(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	9,818.82	9,818.82	9,818.82	100%	100%	0
PG-T-PR-LL-PB-DL-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	9,372.51	9,372.51	9,372.51	100%	100%	0
PG-T-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	26-Sep-26 A	6,545.88	6,545.88	6,545.88	100%	100%	-12
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	28-Sep-26	6,248.34	4,686.26	6,248.34	100%	75%	-26
IRRIGATION WORK		98	06-May-26	06-Jul-26	06-May-26 A	27-Sep-26	61,223.85	52,240.52	61,223.85	100%	85.33%	-71
PG-T-PR-LL-IR-DL-10	HDPE Pipes(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	12,187.26	12,187.26	12,187.26	100%	100%	0
PG-T-PR-LL-IR-DL-20	Irrigation Control System(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	24,547.05	24,547.05	24,547.05	100%	100%	0
PG-T-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	4	01-Jul-26	06-Jul-26	07-Aug-26 A	27-Sep-26	8,124.84	5,687.39	8,124.84	100%	70%	-38
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	06-Jul-26	20-Aug-26 A	27-Sep-26	16,364.70	9,818.82	16,364.70	100%	60%	-28
ELECTRICAL WORK		140	13-May-26	24-Aug-26	13-May-26 A	04-Oct-26	160,180.47	149,484.36	160,180.47	100%	93.32%	-34
PG-T-PR-LL-EL-DL-10	Main Distribution Board(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,677.86	2,677.86	2,677.86	100%	100%	0
PG-T-PR-LL-EL-DL-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	2,142.29	2,142.29	2,142.29	100%	100%	0
PG-T-PR-LL-EL-DL-30	Site Lighting Poles(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	62,659.01	62,659.01	62,659.01	100%	100%	0
PG-T-PR-LL-EL-DL-40	Lighting Fixtures(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	6,927.28	6,927.28	6,927.28	100%	100%	0
PG-T-PR-LL-EL-DL-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	5,422.63	5,422.63	5,422.63	100%	100%	0
PG-T-PR-LL-EL-DL-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	5,288.65	5,288.65	5,288.65	100%	100%	0
PG-T-PR-LL-EL-DL-70	Security and Access Control System Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	6,695.46	6,695.46	6,695.46	100%	100%	0
PG-T-PR-LL-EL-DL-80	Fire Alarm System Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	4,295.11	4,295.11	4,295.11	100%	100%	0
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	27-Sep-26	3,615.08	3,072.82	3,615.08	100%	85%	-32
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	27-Sep-26	1,785.24	1,517.45	1,785.24	100%	85%	-25
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	27-Sep-26	1,428.19	1,213.96	1,428.19	100%	85%	-25
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	27-Sep-26	41,772.67	35,506.77	41,772.67	100%	85%	-25
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	27-Sep-26	4,618.19	3,925.46	4,618.19	100%	85%	-25
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-26	24-Aug-26	27-Aug-26 A	04-Oct-26	3,525.77	2,644.33	3,525.77	100%	75%	-20
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-26	24-Aug-26	27-Aug-26 A	04-Oct-26	4,463.64	3,347.73	4,463.64	100%	75%	-20
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-26	24-Aug-26	27-Aug-26 A	04-Oct-26	2,863.40	2,147.55	2,863.40	100%	75%	-20

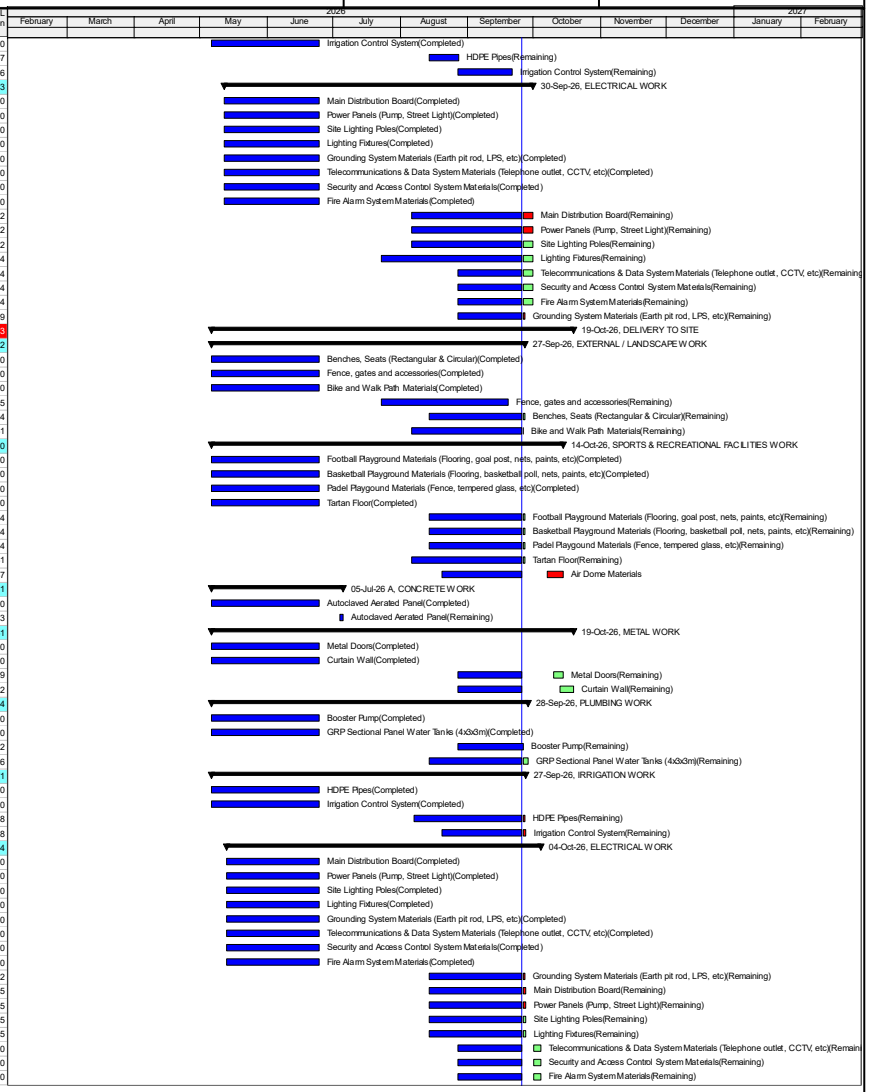


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
SHORT LEAD ITEMS		184	26-Feb-2	22-Jul-26	26-Feb-26 A	08-Oct-26	504,666.45	497,225.10	504,666.45	100%	98.53%	-66
PURCHASE ORDER		163	26-Feb-2	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
EXTERNAL / LANDSCAPE WORK		163	26-Feb-2	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
PG-T-PR-SL-LS-PO-10	Backfilling Materials	44	26-Feb-2	23-Apr-26	26-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-30	Compacted Natural Ground Soil	42	01-Mar-2	23-Apr-26	01-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-20	Interlock tiles	28	29-Mar-2	30-Apr-26	29-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-40	Curb Stone	23	04-Apr-26	30-Apr-26	04-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-50	Thermoplastic pavement road marking(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-60	Traffic Signages(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-70	Trees(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-80	Lawn(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-50_R	Thermoplastic pavement road marking(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-70_R	Trees(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-80_R	Lawn(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-60_R	Traffic Signages(Remaining)	7	04-Jul-26	11-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		41	02-Mar-2	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-CO-PO-10	Steel Rebar	41	02-Mar-2	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-20	Concrete	36	08-Mar-2	23-Apr-26	08-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-40	CMU Block	33	11-Mar-2	23-Apr-26	11-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-50	Concrete Repair & Protection Materials	32	12-Mar-2	23-Apr-26	12-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-30	Screed	23	28-Mar-2	23-Apr-26	28-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AR-PO-10	Ceramic tiles	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-20	Anti-slip Granite tiles	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-30	Epoxy Paint	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-40	Cement Plaster	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-50	Acrylic Paint	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-60	Stone Cladding	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-70	Phenolic Partition	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-80	Glass Partition	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-90	Gypsum Boards	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-110	Waterproofing System Materials	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-MT-PO-10	Galvanized Steel Ladder	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-PO-20	Galvanized Steel Roof Scupper	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-PO-30	Galvanized Steel Cover with frame	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AC-PO-10	Split Air Conditioning Unit	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-PO-20	Air Duct	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-PO-30	Diffusers and Grills	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-PO-40	Exhaust fans	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-PB-PO-10	PPR Pipes & Valves	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-PO-20	UPCV Pipes	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-PO-30	Sanitary Drainage Fixtures	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-IR-PO-10	Gate Valve including valve box	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-IR-PO-20	Bubblers and Spreyers	7	05-May-2	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		97	11-May-2	02-Jul-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
PG-T-PR-SL-EL-PO-10	Wiring Devices Materials(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-EL-PO-10_R	Wiring Devices Materials(Remaining)	7	25-Jun-26	02-Jul-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		94	11-May-2	29-Jun-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-51
PG-T-PR-SL-FF-PO-10	Fire Extinguishers(Completed)	35	11-May-2	25-Jun-26	11-May-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-FF-PO-10_R	Fire Extinguishers(Remaining)	4	25-Jun-26	29-Jun-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	-3
DELIVERY TO SITE		182	01-Mar-2	22-Jul-26	01-Mar-26 A	08-Oct-26	504,666.45	497,225.10	504,666.45	100%	98.53%	-66
EXTERNAL / LANDSCAPE WORK		171	01-Mar-2	22-Jul-26	01-Mar-26 A	27-Sep-26	346,880.61	343,883.90	346,880.61	100%	99.14%	-56
PG-T-PR-SL-LS-DL-10	Backfilling Materials	43	01-Mar-2	23-Apr-26	01-Mar-26 A	24-Apr-26 A	91,125.00	91,125.00	91,125.00	100%	100%	0
PG-T-PR-SL-LS-DL-30	Compacted Natural Ground Soil	41	03-Mar-2	23-Apr-26	03-Mar-26 A	24-Apr-26 A	11,583.00	11,583.00	11,583.00	100%	100%	0
PG-T-PR-SL-LS-DL-20	Interlock tiles	13	29-Apr-26	13-May-26	29-Apr-26 A	13-May-26 A	96,438.60	96,438.60	96,438.60	100%	100%	0
PG-T-PR-SL-LS-DL-40	Curb Stone	13	29-Apr-26	13-May-26	29-Apr-26 A	13-May-26 A	93,058.20	93,058.20	93,058.20	100%	100%	0
PG-T-PR-SL-LS-DL-50	Thermoplastic pavement road marking	1	13-May-2	13-May-26	13-May-26 A	13-May-26 A	4,730.67	4,730.67	4,730.67	100%	100%	0
PG-T-PR-SL-LS-DL-60	Traffic Signages(Completed)	33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	1,071.14	1,071.14	1,071.14	100%	100%	0
PG-T-PR-SL-LS-DL-70	Trees(Completed)	33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	12,452.94	12,452.94	12,452.94	100%	100%	0
PG-T-PR-SL-LS-DL-80	Lawn(Completed)	33	13-May-2	24-Jun-26	13-May-26 A	24-Jun-26 A	16,443.00	16,443.00	16,443.00	100%	100%	0
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	714.10	606.98	714.10	100%	85%	-16
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	8,301.96	7,056.67	8,301.96	100%	85%	-16
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	10,962.00	9,317.70	10,962.00	100%	85%	-16
CONCRETE WORK		52	10-Mar-2	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
PG-T-PR-SL-CO-DL-20	Concrete	35	10-Mar-2	23-Apr-26	10-Mar-26 A	24-Apr-26 A	4,669.65	4,669.65	4,669.65	100%	100%	0
PG-T-PR-SL-CO-DL-10	Steel Rebar	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	4,291.38	4,291.38	4,291.38	100%	100%	0
PG-T-PR-SL-CO-DL-30	Screed	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	1,058.40	1,058.40	1,058.40	100%	100%	0
PG-T-PR-SL-CO-DL-40	CMU Block	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	1,117.80	1,117.80	1,117.80	100%	100%	0

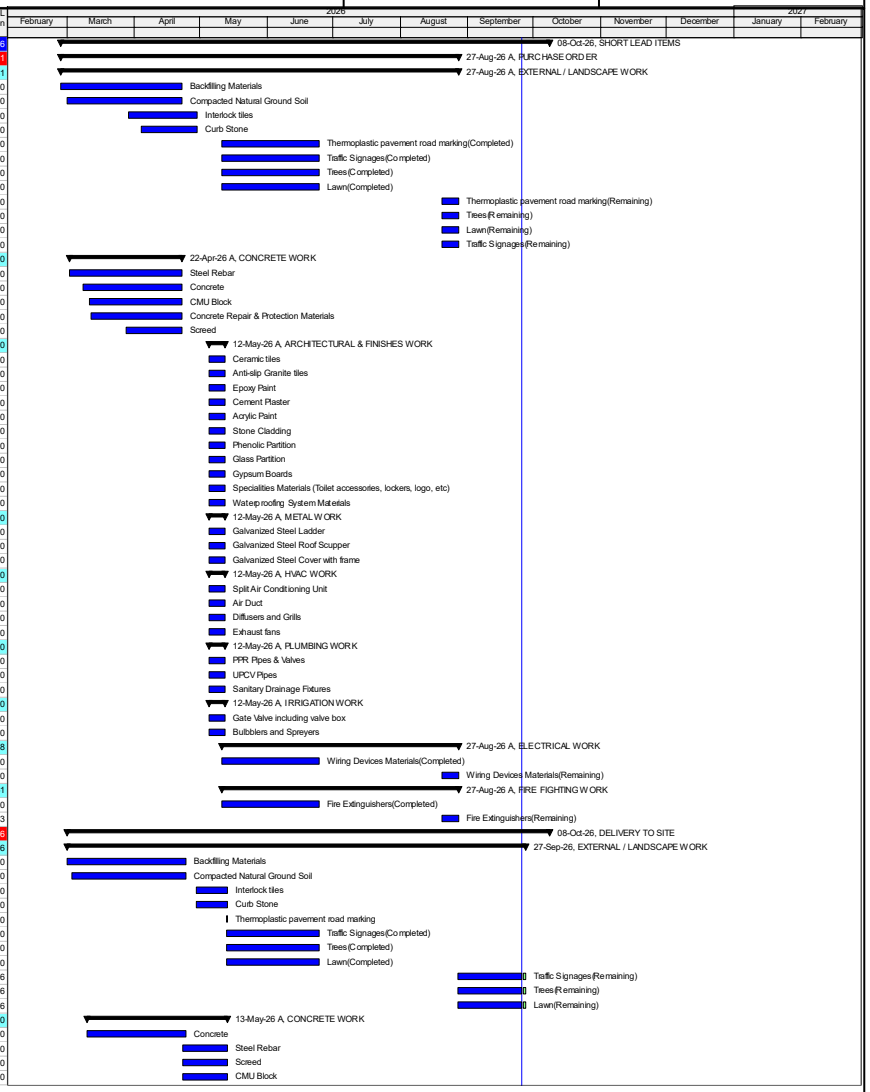


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-SL-CO-DL-50	Concrete Repair & Protection Materials	18	23-Apr-26	13-May-26	23-Apr-26 A	13-May-26 A	3,348.00	3,348.00	3,348.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
PG-T-PR-SL-AR-DL-10	Ceramic tiles	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	5,147.55	5,147.55	5,147.55	100%	100%	0
PG-T-PR-SL-AR-DL-20	Anti-slip Granite tiles	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	4,819.50	4,819.50	4,819.50	100%	100%	0
PG-T-PR-SL-AR-DL-30	Epoxy Paint	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,000.62	1,000.62	1,000.62	100%	100%	0
PG-T-PR-SL-AR-DL-40	Cement Plaster	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,992.33	1,992.33	1,992.33	100%	100%	0
PG-T-PR-SL-AR-DL-50	Acrylic Paint	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,331.10	1,331.10	1,331.10	100%	100%	0
PG-T-PR-SL-AR-DL-60	Stone Cladding	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	16,669.80	16,669.80	16,669.80	100%	100%	0
PG-T-PR-SL-AR-DL-70	Phenolic Partition	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	12,063.60	12,063.60	12,063.60	100%	100%	0
PG-T-PR-SL-AR-DL-80	Glass Partition	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,398.60	1,398.60	1,398.60	100%	100%	0
PG-T-PR-SL-AR-DL-90	Gypsum Boards	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,697.22	1,697.22	1,697.22	100%	100%	0
PG-T-PR-SL-AR-DL-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	20,365.83	20,365.83	20,365.83	100%	100%	0
PG-T-PR-SL-AR-DL-110	Waterproofing System Materials	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	4,897.80	4,897.80	4,897.80	100%	100%	0
METAL WORK		129	06-May-26	08-Jul-26	06-May-26 A	08-Oct-26	4,310.01	2,586.01	4,310.01	100%	60%	-78
PG-T-PR-SL-MT-DL-10	Galvanized Steel Ladder(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	1,954.04	1,954.04	1,954.04	100%	100%	0
PG-T-PR-SL-MT-DL-20	Galvanized Steel Roof Scupper(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	169.13	169.13	169.13	100%	100%	0
PG-T-PR-SL-MT-DL-30	Galvanized Steel Cover with frame(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	462.83	462.83	462.83	100%	100%	0
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	1,302.70	0.00	1,302.70	100%	0%	0
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	112.75	0.00	112.75	100%	0%	0
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	308.56	0.00	308.56	100%	0%	0
HVAC WORK		7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
PG-T-PR-SL-AC-DL-10	Split Air Conditioning Unit	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	2,789.37	2,789.37	2,789.37	100%	100%	0
PG-T-PR-SL-AC-DL-20	Air Duct	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	1,404.00	1,404.00	1,404.00	100%	100%	0
PG-T-PR-SL-AC-DL-30	Diffusers and Grills	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	668.79	668.79	668.79	100%	100%	0
PG-T-PR-SL-AC-DL-40	Exhaust fans	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	595.08	595.08	595.08	100%	100%	0
PLUMBING WORK		7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
PG-T-PR-SL-PB-DL-10	PPR Pipes & Valves	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	2,386.80	2,386.80	2,386.80	100%	100%	0
PG-T-PR-SL-PB-DL-20	UPCV Pipes	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	3,016.71	3,016.71	3,016.71	100%	100%	0
PG-T-PR-SL-PB-DL-30	Sanitary Drainage Fixtures	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	22,919.76	22,919.76	22,919.76	100%	100%	0
IRRIGATION WORK		97	06-May-26	05-Jul-26	06-May-26 A	26-Sep-26	29,954.07	28,456.37	29,954.07	100%	95%	-70
PG-T-PR-SL-IR-DL-10	Gate Valve including valve box(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	1,859.76	1,859.76	1,859.76	100%	100%	0
PG-T-PR-SL-IR-DL-20	Bubblers and Spreyers(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	13,117.28	13,117.28	13,117.28	100%	100%	0
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	26-Sep-26	1,859.76	1,673.78	1,859.76	100%	90%	-33
PG-T-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	26-Sep-26	13,117.28	11,805.55	13,117.28	100%	90%	-22
ELECTRICAL WORK		118	13-May-26	16-Jul-26	13-May-26 A	01-Oct-26	3,667.68	2,567.38	3,667.68	100%	70%	-65
PG-T-PR-SL-EL-DL-10	Wiring Devices Materials(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	1,467.07	1,467.07	1,467.07	100%	100%	0
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	19-Sep-26 A	01-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	1
FIRE FIGHTING WORK		120	13-May-26	09-Jul-26	13-May-26 A	05-Oct-26	204.39	81.76	204.39	100%	40%	-74
PG-T-PR-SL-FF-DL-10	Fire Extinguishers(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	81.76	81.76	81.76	100%	100%	0
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26	09-Jul-26	26-Sep-26	05-Oct-26	122.63	0.00	122.63	100%	0%	0
CONSTRUCTION STAGE		254	24-Mar-26	14-Dec-26	24-Mar-26 A	20-Jan-27	3,876,577.86	3,341,838.37	6,814,680.60	56.89%	49.04%	-31
PLAYGROUND AND LANDSCAPING WORKS		254	24-Mar-26	14-Dec-26	24-Mar-26 A	20-Jan-27	1,649,127.72	1,841,440.55	2,311,795.02	71.34%	79.65%	-31
CUT AND FILL		38	24-Mar-26	05-May-26	24-Mar-26 A	06-May-26 A	228,240.00	228,240.00	228,240.00	100%	100%	0
PG-T-CON-EXCF-10	Existing Soil Excavation Works	22	24-Mar-26	18-Apr-26	24-Mar-26 A	18-Apr-26 A	64,800.00	64,800.00	64,800.00	100%	100%	0
PG-T-CON-EXCF-20	Soil Replacement Works	18	07-Apr-26	27-Apr-26	07-Apr-26 A	27-Apr-26 A	25,740.00	25,740.00	25,740.00	100%	100%	0
PG-T-CON-EXCF-30	Levelling & Backfilling Works	17	18-Apr-26	06-May-26	18-Apr-26 A	06-May-26 A	137,700.00	137,700.00	137,700.00	100%	100%	0
PLAYGROUND WORKS		171	23-Apr-26	07-Dec-26	23-Apr-26 A	17-Nov-26	434,971.56	522,857.41	623,491.20	69.76%	83.86%	17
FOOTBALL PLAYGROUND WORKS		152	23-Apr-26	17-Nov-26	23-Apr-26 A	22-Oct-26	229,942.50	289,692.25	333,290.16	68.99%	86.92%	22
PG-T-CON-EXFB-10	Subgrade Preparation and Compaction	12	23-Apr-26	06-May-26	23-Apr-26 A	06-May-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-T-CON-EXFB-20	Sub-Base Laying and Compaction	8	28-Apr-26	06-May-26	28-Apr-26 A	06-May-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-T-CON-EXFB-30	Base Course Laying and Compaction	33	06-May-26	17-Jun-26	06-May-26 A	17-Jun-26 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-T-CON-EXFB-70	Topsoil Placement(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	9,466.80	9,466.80	9,466.80	100%	100%	0
PG-T-CON-EXFB-80	Fine Grading & Leveling	15	25-Jun-26	12-Jul-26	07-Jul-26 A	12-Jul-26 A	23,667.00	23,667.00	23,667.00	100%	100%	10
PG-T-CON-EXFB-70_R	Topsoil Placement(Remaining)	15	13-Jul-26	29-Jul-26	09-Jul-26 A	12-Jul-26 A	14,200.20	14,200.20	14,200.20	100%	100%	12
PG-T-CON-EXFB-60	Goal Post Foundation	17	30-Jul-26	18-Aug-26	23-Jul-26 A	14-Aug-26 A	35,500.50	35,500.50	35,500.50	100%	100%	-2
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	29-Sep-26	24,360.00	18,270.00	24,360.00	100%	75%	-20
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	30-Sep-26	23,667.00	21,300.30	23,667.00	100%	90%	-27
PG-T-CON-EXFB-40	Tartan flooring	15	17-Sep-26	05-Oct-26	14-Aug-26 A	14-Aug-26 A	28,080.00	70,200.00	70,200.00	40%	100%	15
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	05-Oct-26	0.00	24,850.35	35,500.50	0%	70%	-24
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	11-Oct-26	0.00	1,236.10	2,060.16	0%	60%	-26
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	11-Oct-26	22-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		142	06-May-26	17-Nov-26	06-May-26 A	27-Oct-26	147,399.96	154,055.81	173,211.12	85.1%	88.94%	19
PG-T-CON-EXBB-10	Subgrade Preparation and Compaction	1	06-May-26	06-May-26	06-May-26 A	06-May-26 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-T-CON-EXBB-20	Sub-Base Laying and Compaction	1	06-May-26	06-May-26	06-May-26 A	06-May-26 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-T-CON-EXBB-30	Base Course Laying and Compaction	33	06-May-26	17-Jun-26	06-May-26 A	17-Jun-26 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-T-CON-EXBB-70	Floor Surface Curing(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	7,736.04	7,736.04	7,736.04	100%	100%	0
PG-T-CON-EXBB-50	Basketball Pole Foundation	25	25-Jun-26	23-Jul-26	06-Aug-26 A	14-Aug-26 A	15,472.08	15,472.08	15,472.08	100%	100%	18
PG-T-CON-EXBB-70_R	Floor Surface Curing(Remaining)	15	25-Jul-26	10-Aug-26	09-Jul-26 A	12-Jul-26 A	7,736.04	7,736.04	7,736.04	100%	100%	12
PG-T-CON-EXBB-40	Tartan flooring	17	11-Aug-26	30-Aug-26	12-Jul-26 A	14-Aug-26 A	52,650.00	52,650.00	52,650.00	100%	100%	-12
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	29-Sep-26	13,091.76	11,128.00	13,091.76	100%	85%	-18
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	05-Oct-26	4,297.80	11,604.06	15,472.08	27.78%	75%	-20
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	05-Oct-26	25-Oct-26	0.00	0.00	13,091.76	0%	0%	0
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	27-Oct-26	0.00	1,313.35	1,545.12	0%	85%	-36

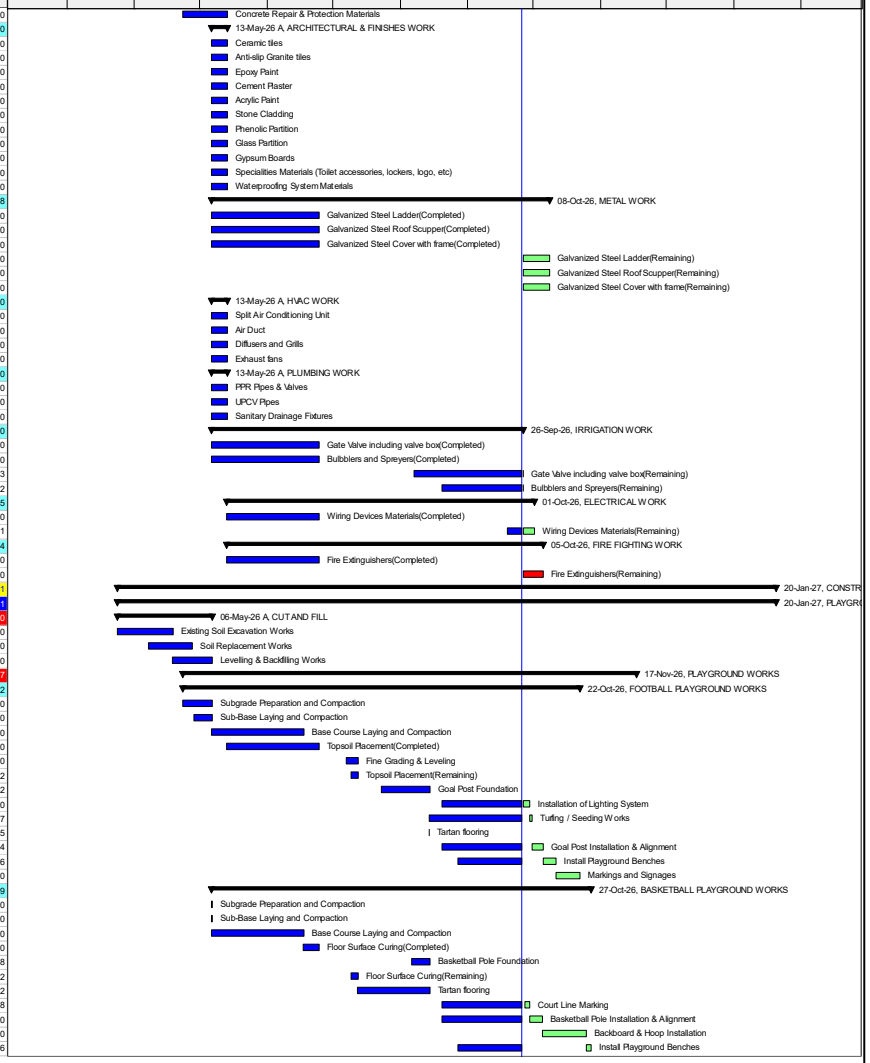


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PADEL PLAYGROUND WORKS		160	06-May-26	07-Dec-26	06-May-26 A	17-Nov-26	57,629.10	79,109.35	116,989.92	49.26%	67.62%	17
PG-T-CON-EXPD-10	Excavation For Fence Footing(Completed)	39	06-May-26	24-Jun-26	06-May-26 A	24-Jun-26 A	16,243.20	16,243.20	16,243.20	100%	100%	0
PG-T-CON-EXPD-20	RC Foundations For Fence(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	1,767.48	1,767.48	1,767.48	100%	100%	0
PG-T-CON-EXPD-30	Tartan Flooring Layers(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	26,325.00	26,325.00	26,325.00	100%	100%	0
PG-T-CON-EXPD-10_R	Excavation For Fence Footing(Remaining)	8	25-Jun-26	04-Jul-26	06-Aug-26 A	14-Aug-26 A	1,804.80	1,804.80	1,804.80	100%	100%	1
PG-T-CON-EXPD-20_R	RC Foundations For Fence(Remaining)	20	05-Jul-26	27-Jul-26	14-Aug-26 A	27-Aug-26 A	1,767.48	1,767.48	1,767.48	100%	100%	8
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	30-Sep-26	3,534.96	3,004.72	3,534.96	100%	85%	-14
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	03-Oct-26	5,302.44	4,507.07	5,302.44	100%	85%	-19
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	03-Oct-26	24-Oct-26	883.74	0.00	5,302.44	16.67%	0%	0
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	27-Oct-26	0.00	22,376.25	26,325.00	0%	85%	-40
PG-T-CON-EXPD-70	Court Accessories Installation	16	02-Nov-26	19-Nov-26	27-Oct-26	15-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	17-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-55
GENERAL SITE WORKS		234	16-Apr-26	14-Dec-26	16-Apr-26 A	20-Jan-27	550,929.66	412,798.28	656,604.42	83.91%	62.87%	-31
FENCE WORKS		146	16-Apr-26	17-Aug-26	16-Apr-26 A	08-Oct-26	32,909.40	20,403.83	32,909.40	100%	62%	-44
PG-T-CON-EXGN-FN-10	Excavation for fence foundation	3	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	6,581.88	6,581.88	6,581.88	100%	100%	0
PG-T-CON-EXGN-FN-20	Concrete Foundations for Fence	12	13-Jul-26	26-Jul-26	13-Aug-26 A	20-Aug-26 A	6,581.88	6,581.88	6,581.88	100%	100%	5
PG-T-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26	03-Aug-26	20-Aug-26 A	27-Sep-26	6,581.88	5,594.60	6,581.88	100%	85%	-24
PG-T-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-26	10-Aug-26	20-Sep-26 A	01-Oct-26	6,581.88	1,645.47	6,581.88	100%	25%	-4
PG-T-CON-EXGN-FN-50	Installation of Gates	6	11-Aug-26	17-Aug-26	01-Oct-26	08-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		133	12-May-26	10-Aug-26	12-May-26 A	19-Oct-26	230,187.54	188,479.27	230,187.54	100%	81.88%	-59
STORM WATER AND UTILITY WORK		128	12-May-26	04-Aug-26	12-May-26 A	13-Oct-26	27,252.00	11,715.00	27,252.00	100%	42.99%	-59
PG-T-CON-EXGN-M-10	Excavation	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	3,096.00	3,096.00	3,096.00	100%	100%	0
PG-T-CON-EXGN-M-20	Bedding preparation & level control(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	1,548.00	1,548.00	1,548.00	100%	100%	0
PG-T-CON-EXGN-M-20_R	Bedding preparation & level control(Remaining)	5	25-Jun-26	30-Jun-26	12-Jul-26 A	27-Aug-26 A	516.00	516.00	516.00	100%	100%	-36
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	27-Sep-26	5,160.00	3,870.00	5,160.00	100%	75%	-26
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	30-Sep-26	10,740.00	2,685.00	10,740.00	100%	25%	-4
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	30-Sep-26	04-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	04-Oct-26	07-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	08-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		96	02-Jun-26	30-Jul-26	02-Jun-26 A	08-Oct-26	202,617.60	176,764.27	202,617.60	100%	87.24%	-59
PG-T-CON-EXGN-M-80	Installation of HDPE Irrigation Pipe Network with Gate Valve and	20	02-Jun-26	24-Jun-26	02-Jun-26 A	24-Jun-26 A	18,691.26	18,691.26	18,691.26	100%	100%	0
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	07-Oct-26	34,712.34	31,241.11	34,712.34	100%	90%	-70
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	08-Oct-26	90,915.00	77,277.75	90,915.00	100%	85%	-35
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	08-Oct-26	58,299.00	49,554.15	58,299.00	100%	85%	-37
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	13-Oct-26	19-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	13-Oct-26	19-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		175	08-Jun-26	07-Nov-26	08-Jun-26 A	30-Dec-26	281,374.32	175,987.59	345,859.68	81.36%	50.88%	-45
POWER, LIGHTING & GROUNDING		141	08-Jun-26	27-Sep-26	08-Jun-26 A	19-Nov-26	281,374.32	171,672.99	288,789.48	97.43%	59.45%	-46
PG-T-CON-EXGN-E-10	Excavation	3	08-Jun-26	10-Jun-26	08-Jun-26 A	10-Jun-26 A	69,621.12	69,621.12	69,621.12	100%	100%	0
PG-T-CON-EXGN-E-20	Foundation Work for Site Lighting Poles(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	37,131.26	37,131.26	37,131.26	100%	100%	0
PG-T-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	01-Oct-26	55,696.90	41,772.67	55,696.90	100%	75%	-14
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	21-Oct-26	8,265.00	7,025.25	8,265.00	100%	85%	-44
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	26-Oct-26	4,586.70	458.67	4,586.70	100%	10%	-28
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	02-Nov-26	17,397.90	1,739.79	17,397.90	100%	10%	-32
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	08-Nov-26	69,621.12	13,924.22	69,621.12	100%	20%	-38
PG-T-CON-EXGN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	08-Nov-26	12-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-T-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	6	20-Sep-26	27-Sep-26	12-Nov-26	19-Nov-26	14,830.32	0.00	22,245.48	66.67%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	16-Dec-26	0.00	4,314.60	43,146.00	0%	10%	-47
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	23-Nov-26	0.00	61.98	619.80	0%	10%	-49
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	26-Nov-26	0.00	61.98	619.80	0%	10%	-52
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	30-Nov-26	0.00	371.88	3,718.80	0%	10%	-55
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	05-Dec-26	0.00	1,524.91	15,249.12	0%	10%	-58
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	08-Dec-26	0.00	144.65	1,446.48	0%	10%	-62
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	13-Dec-26	0.00	661.20	6,612.00	0%	10%	-65
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	16-Dec-26	0.00	1,488.00	14,880.00	0%	10%	-69
FIRE ALARM SYSTEM		32	01-Oct-26	07-Nov-26	23-Nov-26	30-Dec-26	0.00	0.00	13,924.20	0%	0%	0
PG-T-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	01-Oct-26	10-Oct-26	23-Nov-26	02-Dec-26	0.00	0.00	1,983.60	0%	0%	0
PG-T-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26	19-Oct-26	02-Dec-26	12-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-T-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26	28-Oct-26	12-Dec-26	21-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-T-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26	07-Nov-26	21-Dec-26	30-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		167	17-Jun-26	11-Nov-26	17-Jun-26 A	30-Dec-26	5,788.80	23,798.40	40,207.80	14.4%	59.19%	-41
PG-T-CON-EXGN-PR-20	Interlock tiles(Completed)	7	17-Jun-26	24-Jun-26	17-Jun-26 A	24-Jun-26 A	5,788.80	5,788.80	5,788.80	100%	100%	0
PG-T-CON-EXGN-PR-10	Installation of Parking Accessories	7	27-Oct-26	03-Nov-26	20-Aug-26 A	17-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-94
PG-T-CON-EXGN-PR-20_R	Interlock tiles(Remaining)	7	27-Oct-26	03-Nov-26	12-Jul-26 A	27-Aug-26 A	0.00	7,075.20	7,075.20	0%	100%	-34
PG-T-CON-EXGN-PR-30	Marking & Signages	7	04-Nov-26	11-Nov-26	22-Dec-26	30-Dec-26	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		191	10-Jun-26	14-Dec-26	10-Jun-26 A	20-Jan-27	669.60	4,129.20	7,440.00	9%	55.5%	-31
PG-T-CON-EXGN-S-C-10	Excavation & Trench Preparation(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	669.60	669.60	669.60	100%	100%	0
PG-T-CON-EXGN-S-C-10_R	Excavation & Trench Preparation(Remaining)	7	04-Nov-26	11-Nov-26	12-Jul-26 A	23-Jul-26 A	0.00	1,562.40	1,562.40	0%	100%	-4
PG-T-CON-EXGN-S-C-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	30-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-107
PG-T-CON-EXGN-S-C-30	Connection to City Network	10	24-Nov-26	05-Dec-26	30-Dec-26	11-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-T-CON-EXGN-S-C-40	Backfilling	8	06-Dec-26	14-Dec-26	11-Jan-27	20-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		156	31-May-26	22-Nov-26	30-May-26 A	02-Dec-26	400,581.30	669,576.62	755,169.00	53.05%	88.67%	-8
HARDSCAPE WORK		156	31-May-26	22-Nov-26	30-May-26 A	02-Dec-26	376,221.30	609,545.42	648,147.00	58.05%	94.04%	-8

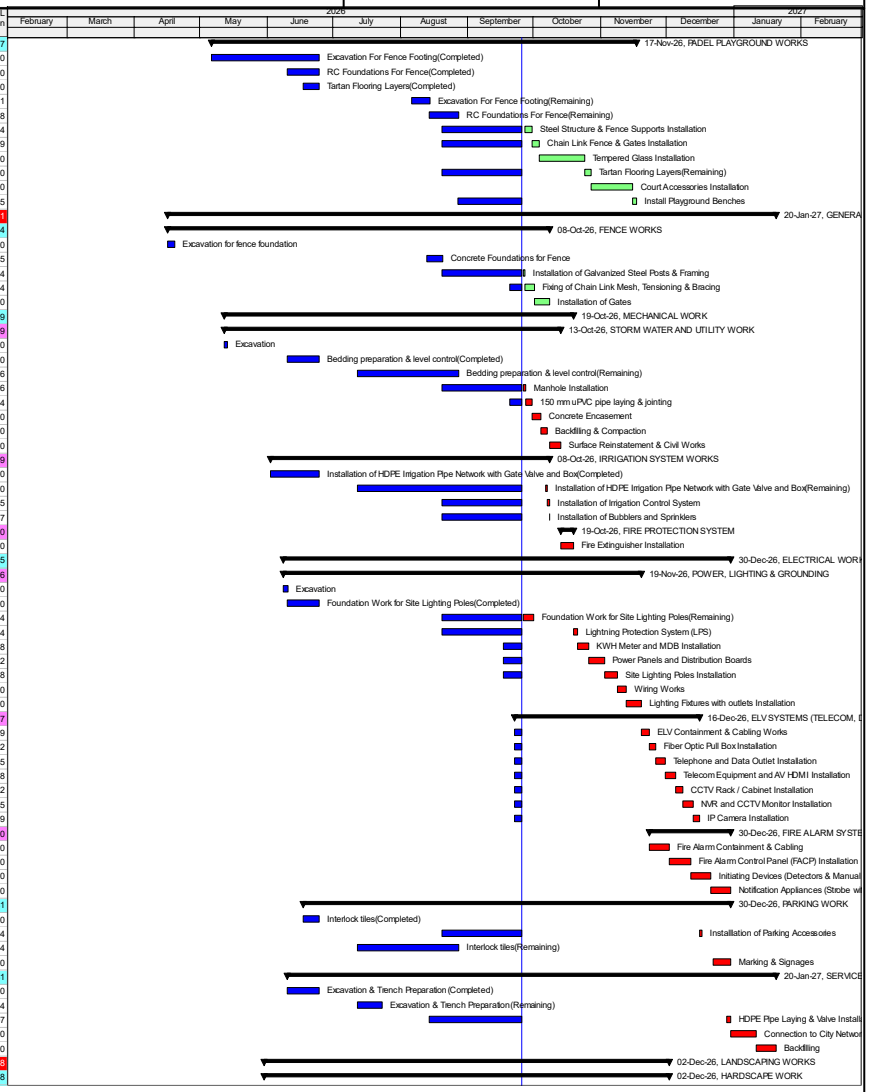

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXLS-HS-10	Curbstone Installation(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	124,077.60	124,077.60	124,077.60	100%	100%	0
PG-T-CON-EXLS-HS-20	Interlock Tiles Grey Scale with Black Marble Chips(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	40,656.00	40,656.00	40,656.00	100%	100%	0
PG-T-CON-EXLS-HS-40	Bike Path and Walking Path Construction(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	99,297.00	99,297.00	99,297.00	100%	100%	0
PG-T-CON-EXLS-HS-50	Install Recycled Precast Concrete Seats(Completed)	22	31-May-26	24-Jun-26	30-May-26 A	24-Jun-26 A	6,681.90	6,681.90	6,681.90	100%	100%	0
PG-T-CON-EXLS-HS-30	Stamped Concrete Floor(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	43,470.00	43,470.00	43,470.00	100%	100%	0
PG-T-CON-EXLS-HS-10_R	Curbstone Installation(Remaining)	8	17-Sep-26	27-Sep-26	12-Jul-26 A	27-Aug-26 A	62,038.80	82,718.40	82,718.40	75%	100%	-33
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	07-Nov-26	0.00	51,836.40	60,984.00	0%	85%	-51
PG-T-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26	20-Oct-26	30-Jul-26 A	07-Nov-26	0.00	39,123.00	43,470.00	0%	90%	-75
PG-T-CON-EXLS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	21-Oct-26	29-Oct-26	23-Jul-26 A	27-Aug-26 A	0.00	81,243.00	81,243.00	0%	100%	-23
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	23-Nov-26	0.00	39,089.12	60,137.10	0%	65%	-89
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	02-Dec-26	0.00	1,353.00	5,412.00	0%	25%	-49
SOFTSCAPE WORK		143	10-Jun-26	22-Nov-26	10-Jun-26 A	02-Dec-26	24,360.00	60,031.20	107,022.00	22.76%	56.09%	-8
PG-T-CON-EXLS-SS-20	Lawn Area Preparation & Planting / Turfing(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	24,360.00	24,360.00	24,360.00	100%	100%	0
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	19-Nov-26	0.00	4,612.20	46,122.00	0%	10%	-37
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	31,059.00	36,540.00	0%	85%	-116
TANK WORKS		146	13-May-26	27-Sep-26	13-May-26 A	04-Nov-26	34,405.20	7,968.24	48,290.40	71.25%	16.5%	-33
SEPTIC TANK		141	13-May-26	03-Sep-26	13-May-26 A	29-Oct-26	7,475.22	1,866.06	7,475.22	100%	24.96%	-47
PG-T-CON-EXTW-ST-10	Excavation	21	13-May-26	10-Jun-26	13-May-26 A	10-Jun-26 A	252.18	252.18	252.18	100%	100%	0
PG-T-CON-EXTW-ST-20	PCC / Lean Concrete laying	27	20-May-26	24-Jun-26	20-May-26 A	24-Jun-26 A	168.12	168.12	168.12	100%	100%	0
PG-T-CON-EXTW-ST-30	RCC Foundation(Completed)	1	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	894.35	894.35	894.35	100%	100%	0
PG-T-CON-EXTW-ST-30_R	RCC Foundation(Remaining)	10	25-Jun-26	06-Jul-26	12-Jul-26 A	27-Aug-26 A	383.29	383.29	383.29	100%	100%	-31
PG-T-CON-EXTW-ST-40	RCC Wall	9	07-Jul-26	16-Jul-26	14-Aug-26 A	05-Oct-26	2,757.60	0.00	2,757.60	100%	0%	-35
PG-T-CON-EXTW-ST-50	RCC Slab	13	18-Jul-26	01-Aug-26	20-Aug-26 A	20-Oct-26	2,599.38	0.00	2,599.38	100%	0%	-39
PG-T-CON-EXTW-ST-60	Finishing Work	8	18-Aug-26	26-Aug-26	21-Oct-26	29-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-T-CON-EXTW-ST-70	Backfilling	7	27-Aug-26	03-Sep-26	20-Aug-26 A	24-Aug-26 A	168.12	168.12	168.12	100%	100%	3
WATER STORAGE TANK		146	13-May-26	27-Sep-26	13-May-26 A	04-Nov-26	26,929.98	6,102.18	40,815.18	65.98%	14.95%	-33
PG-T-CON-EXTW-WR-10	Excavation(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	766.58	766.58	766.58	100%	100%	0
PG-T-CON-EXTW-WR-20	RCC Foundation(Completed)	13	10-Jun-26	24-Jun-26	10-Jun-26 A	24-Jun-26 A	1,654.56	1,654.56	1,654.56	100%	100%	0
PG-T-CON-EXTW-WR-10_R	Excavation(Remaining)	6	29-Aug-26	03-Sep-26	08-Jul-26 A	09-Jul-26 A	85.18	85.18	85.18	100%	100%	4
PG-T-CON-EXTW-WR-20_R	RCC Foundation(Remaining)	8	05-Sep-26	13-Sep-26	16-Jul-26 A	27-Aug-26 A	2,481.84	2,481.84	2,481.84	100%	100%	-29
PG-T-CON-EXTW-WR-30	Backfilling	6	14-Sep-26	20-Sep-26	14-Aug-26 A	25-Aug-26 A	1,114.02	1,114.02	1,114.02	100%	100%	-4
PG-T-CON-EXTW-WR-40	GRP Water Tank Installation	5	21-Sep-26	27-Sep-26	31-Oct-26	04-Nov-26	20,827.80	0.00	34,713.00	60%	0%	0
AIR DOME CONSTRUCTION		206	13-May-26	03-Dec-26	13-May-26 A	14-Jan-27	2,087,402.40	1,210,693.39	4,178,041.20	49.96%	28.98%	-35
CIVIL WORK		138	13-May-26	14-Sep-26	13-May-26 A	27-Oct-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-35
PG-T-CON-EXAD-CL-10	Excavation For Footing(Completed)	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	25,048.83	25,048.83	25,048.83	100%	100%	0
PG-T-CON-EXAD-CL-10_R	Excavation For Footing(Remaining)	7	05-Jul-26	12-Jul-26	08-Jul-26 A	10-Jul-26 A	225,439.46	225,439.46	225,439.46	100%	100%	5
PG-T-CON-EXAD-CL-20	Anti-Termite Treatment	1	13-Jul-26	13-Jul-26	10-Jul-26 A	10-Jul-26 A	83,496.10	83,496.10	83,496.10	100%	100%	1
PG-T-CON-EXAD-CL-30	PCC / Blinding Concrete	3	25-Jul-26	27-Jul-26	22-Jul-26 A	23-Jul-26 A	125,244.14	125,244.14	125,244.14	100%	100%	1
PG-T-CON-EXAD-CL-40	RCC Foundation Works	9	28-Jul-26	06-Aug-26	23-Jul-26 A	13-Aug-26 A	250,488.29	250,488.29	250,488.29	100%	100%	-10
PG-T-CON-EXAD-CL-50	Backfilling with Compaction	8	08-Aug-26	16-Aug-26	07-Aug-26 A	14-Aug-26 A	250,488.29	250,488.29	250,488.29	100%	100%	2
PG-T-CON-EXAD-CL-60	Installation of Anchorage System	8	17-Aug-26	25-Aug-26	27-Aug-26 A	23-Sep-26 A	250,488.29	250,488.29	250,488.29	100%	100%	-15
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-26	05-Sep-26	07-Oct-26	18-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-80	Installation of Membrane System	8	06-Sep-26	14-Sep-26	18-Oct-26	27-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		25	05-Nov-26	03-Dec-26	16-Dec-26	14-Jan-27	0.00	0.00	712,953.22	0%	0%	0
PG-T-CON-EXAD-AR-10	Installation of Thermal Insulation System	7	05-Nov-26	12-Nov-26	16-Dec-26	24-Dec-26	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-40	Final Fixing of Accessories & Finishes	7	14-Nov-26	21-Nov-26	24-Dec-26	02-Jan-27	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-AR-20	Installation of Doors & Access Systems	6	22-Nov-26	28-Nov-26	02-Jan-27	09-Jan-27	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-30	Installation of Logo	5	29-Nov-26	03-Dec-26	09-Jan-27	14-Jan-27	0.00	0.00	3,236.40	0%	0%	0
MECHANICAL WORK		23	15-Sep-26	12-Oct-26	27-Oct-26	23-Nov-26	375,732.43	0.00	667,988.77	56.25%	0%	0
PG-T-CON-EXAD-ME-10	Installation of Main Air Package Units	5	15-Sep-26	20-Sep-26	27-Oct-26	02-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-ME-20	Installation of Backup Air Package Unit	5	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	125,244.14	0.00	208,740.24	60%	0%	0
PG-T-CON-EXAD-ME-30	Installation of Complete HVAC System	6	06-Oct-26	12-Oct-26	16-Nov-26	23-Nov-26	0.00	0.00	208,740.24	0%	0%	0
ELECTRICAL WORK		33	28-Sep-26	04-Nov-26	08-Nov-26	16-Dec-26	0.00	0.00	1,085,449.25	0%	0%	0
PG-T-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	7	28-Sep-26	05-Oct-26	08-Nov-26	16-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-20	Installation of Lighting System	7	06-Oct-26	13-Oct-26	16-Nov-26	24-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	14-Oct-26	19-Oct-26	24-Nov-26	30-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-40	Installation of Backup Generator	6	20-Oct-26	26-Oct-26	30-Nov-26	07-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-50	Installation of Smart Dome System	8	27-Oct-26	04-Nov-26	07-Dec-26	16-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		143	12-May-26	28-Oct-26	12-May-26 A	20-Oct-26	140,047.74	289,704.44	324,844.38	43.11%	89.18%	7
CIVIL WORK		143	12-May-26	26-Oct-26	12-May-26 A	19-Oct-26	50,142.00	216,870.81	227,117.58	22.08%	95.49%	7
STRUCTURAL WORK		59	12-May-26	01-Aug-26	12-May-26 A	12-Aug-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-10
PG-T-CON-B-STR-10	Excavation up to bottom of footing	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-T-CON-B-STR-20	Anti-termite treatment and Polyethene Sheet	2	12-May-26	13-May-26	12-May-26 A	13-May-26 A	3,294.00	3,294.00	3,294.00	100%	100%	0
PG-T-CON-B-STR-30	Backfilling with selected fill material (under footing)	1	13-May-26	13-May-26	13-May-26 A	13-May-26 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-T-CON-B-STR-40	Raft Foundation Work	27	13-May-26	17-Jun-26	13-May-26 A	17-Jun-26 A	2,534.40	2,534.40	2,534.40	100%	100%	0
PG-T-CON-B-STR-50	Autoclaved aerated panel (walls)	9	07-Jul-26	16-Jul-26	07-Jul-26 A	09-Jul-26 A	11,340.00	11,340.00	11,340.00	100%	100%	6
PG-T-CON-B-STR-60	Autoclaved aerated panel (ceiling)	9	18-Jul-26	27-Jul-26	09-Jul-26 A	31-Jul-26 A	8,505.00	8,505.00	8,505.00	100%	100%	-10
PG-T-CON-B-STR-70	Autoclaved aerated panel (parapet)	4	28-Jul-26	01-Aug-26	11-Jul-26 A	12-Aug-26 A	8,505.00	8,505.00	8,505.00	100%	100%	-25
ARCHITECTURAL WORK		76	02-Aug-26	26-Oct-26	01-Aug-26 A	19-Oct-26	12,162.00	178,890.81	189,137.58	6.43%	94.58%	6
GENERAL FINISHES		76	02-Aug-26	21-Oct-26	01-Aug-26 A	07-Sep-26 A	9,264.00	84,120.00	84,120.00	11.01%	100%	37
PG-T-CON-B-ARGF-10	Block Works	6	02-Aug-26	08-Aug-26	01-Aug-26 A	06-Aug-26 A	2,484.00	2,484.00	2,484.00	100%	100%	0
PG-T-CON-B-ARGF-20	Plaster	7	18-Aug-26	25-Aug-26	06-Aug-26 A	07-Aug-26 A	4,427.40	4,427.40	4,427.40	100%	100%	6
PG-T-CON-B-ARGF-30	False Ceiling Installation & Finishing	8	26-Aug-26	03-Sep-26	20-Aug-26 A	07-Sep-26 A	873.60	873.60	873.60	100%	100%	-7



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-B-ARGF-40	Wall Paint	10	19-Sep-26	30-Sep-26	20-Aug-26 A	07-Sep-26 A	1,479.00	2,958.00	2,958.00	50%	100%	-5
PG-T-CON-B-ARGF-50	Epoxy Flooring	7	01-Oct-26	08-Oct-26	20-Aug-26 A	07-Sep-26 A	0.00	273.60	273.60	0%	100%	-8
PG-T-CON-B-ARGF-60	Install Doors & Windows	4	10-Oct-26	13-Oct-26	27-Aug-26 A	07-Sep-26 A	0.00	13,273.80	13,273.80	0%	100%	-5
PG-T-CON-B-ARGF-80	Facade Finishing Work	9	10-Oct-26	19-Oct-26	20-Aug-26 A	07-Sep-26 A	0.00	52,278.00	52,278.00	0%	100%	-6
PG-T-CON-B-ARGF-70	Lockers and Furniture Installation	2	20-Oct-26	21-Oct-26	27-Aug-26 A	07-Sep-26 A	0.00	7,551.60	7,551.60	0%	100%	-7
WET AREA FINISHES		37	26-Aug-26	13-Oct-26	06-Aug-26 A	17-Oct-26	2,898.00	77,102.58	81,123.78	3.57%	95.04%	-19
PG-T-CON-B-ARWF-10	False Ceiling Installation & Finishing	4	26-Aug-26	30-Aug-26	20-Aug-26 A	10-Sep-26 A	2,898.00	2,898.00	2,898.00	100%	100%	-15
PG-T-CON-B-ARWF-20	Wall Tiles and Partition Work	3	01-Oct-26	04-Oct-26	06-Aug-26 A	14-Aug-26 A	0.00	21,283.20	21,283.20	0%	100%	-4
PG-T-CON-B-ARWF-30	Waterproofing on Floor	2	05-Oct-26	06-Oct-26	14-Aug-26 A	10-Sep-26 A	0.00	5,784.00	5,784.00	0%	100%	-22
PG-T-CON-B-ARWF-40	Floor Tiles Works	3	07-Oct-26	10-Oct-26	14-Aug-26 A	10-Sep-26 A	0.00	6,489.00	6,489.00	0%	100%	-21
PG-T-CON-B-ARWF-50	Toilet accessories Installation Works	3	11-Oct-26	13-Oct-26	20-Aug-26 A	10-Sep-26 A	0.00	39,307.98	39,307.98	0%	100%	-16
PG-T-CON-B-ARWF-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	17-Oct-26	0.00	1,340.40	5,361.60	0%	25%	-17
ROOF FINISHES		46	07-Oct-26	26-Oct-26	14-Aug-26 A	19-Oct-26	0.00	17,668.23	23,893.80	0%	73.94%	-38
PG-T-CON-B-ARRF-10	Waterproofing on Floor	7	07-Oct-26	14-Oct-26	14-Aug-26 A	12-Sep-26 A	0.00	4,158.00	4,158.00	0%	100%	-18
PG-T-CON-B-ARRF-20	Epoxy Flooring and Finishes	7	15-Oct-26	22-Oct-26	20-Aug-26 A	12-Sep-26 A	0.00	10,158.00	10,158.00	0%	100%	-13
PG-T-CON-B-ARRF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	19-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-22
MEP WORK		103	16-Jun-26	28-Oct-26	16-Jun-26 A	20-Oct-26	89,905.74	72,833.63	97,726.80	92%	74.53%	7
MECANICAL WORKS		103	16-Jun-26	28-Oct-26	16-Jun-26 A	20-Oct-26	71,658.42	54,586.31	79,479.48	90.16%	68.68%	7
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	20-Oct-26	0.00	34.07	136.26	0%	25%	-21
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	20-Oct-26	0.00	34.07	136.26	0%	25%	-21
SEWER AND DRAINAGE SYSTEM		92	16-Jun-26	05-Sep-26	16-Jun-26 A	05-Oct-26	11,290.02	9,677.16	11,290.02	100%	85.71%	-25
PG-T-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation(Completed)	8	16-Jun-26	24-Jun-26	16-Jun-26 A	24-Jun-26 A	967.72	967.72	967.72	100%	100%	0
PG-T-CON-B-GF-DR-20	Sewer and Drainge System Pipes and fittings Installation(Completed)	8	16-Jun-26	24-Jun-26	16-Jun-26 A	24-Jun-26 A	1,451.57	1,451.57	1,451.57	100%	100%	0
PG-T-CON-B-GF-DR-10_R	Sewer and Drainge System Main Lines Installation(Remaining)	1	12-Aug-26	13-Aug-26	23-Jul-26 A	10-Sep-26 A	2,258.00	2,258.00	2,258.00	100%	100%	-41
PG-T-CON-B-GF-DR-20_R	Sewer and Drainge System Pipes and fittings Installation(Remaining)	1	15-Aug-26	16-Aug-26	23-Jul-26 A	31-Jul-26 A	3,387.01	3,387.01	3,387.01	100%	100%	-6
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-26	05-Sep-26	23-Sep-26 A	05-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-8
HVAC SYSTEM		42	09-Aug-26	12-Oct-26	13-Aug-26 A	06-Oct-26	4,442.40	7,132.08	12,127.20	36.63%	58.81%	9
PG-T-CON-B-GF-AC-10	Duct Work and Exhaust Fan Installation	3	09-Aug-26	11-Aug-26	13-Aug-26 A	20-Aug-26 A	4,442.40	4,442.40	4,442.40	100%	100%	-4
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	06-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-12
WATER SUPPLY SYSTEM		45	12-Aug-26	02-Sep-26	22-Jul-26 A	04-Oct-26	55,926.00	37,743.00	55,926.00	100%	67.49%	-44
PG-T-CON-B-GF-WS-10	Water Supply Main Lines Installation	2	12-Aug-26	13-Aug-26	22-Jul-26 A	10-Sep-26 A	5,702.40	5,702.40	5,702.40	100%	100%	-41
PG-T-CON-B-GF-WS-20	Water Supply Pipes Installation (Cold and Hot Water)	2	15-Aug-26	16-Aug-26	23-Jul-26 A	30-Jul-26 A	13,857.60	13,857.60	13,857.60	100%	100%	-5
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-26	02-Sep-26	23-Sep-26 A	04-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-6
ELECTRICAL WORKS		38	15-Aug-26	17-Sep-26	22-Jul-26 A	16-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	-18
PG-T-CON-B-GF-EL-10	Pipes & Conduits Installation	3	15-Aug-26	17-Aug-26	22-Jul-26 A	23-Jul-26 A	1,983.60	1,983.60	1,983.60	100%	100%	1
PG-T-CON-B-GF-EL-50	Electrical Light Fixtures Installation	2	06-Sep-26	07-Sep-26	20-Aug-26 A	16-Sep-26 A	7,337.52	7,337.52	7,337.52	100%	100%	-21
PG-T-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	08-Sep-26	10-Sep-26	20-Aug-26 A	16-Sep-26 A	1,983.60	1,983.60	1,983.60	100%	100%	-20
PG-T-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	12-Sep-26	14-Sep-26	20-Aug-26 A	16-Sep-26 A	4,959.00	4,959.00	4,959.00	100%	100%	-20
PG-T-CON-B-GF-EL-20	Electrical & ELV Wiring Works	3	15-Sep-26	17-Sep-26	20-Aug-26 A	16-Sep-26 A	1,983.60	1,983.60	1,983.60	100%	100%	-20
PROJECT CLOSOUT		207	25-May-26	16-Dec-26	25-May-26 A	27-Jan-27	34,073.40	194,786.29	1,135,780.10	3%	17.15%	-35
PG-T-PCL-10	Testing, Commissioning for All Systems(Completed)	23	25-May-26	24-Jun-26	25-May-26 A	24-Jun-26 A	34,073.40	34,073.40	34,073.40	100%	100%	0
PG-T-PCL-20	As-Built Drawings	15	22-Nov-26	09-Dec-26	23-Sep-26 A	21-Jan-27	0.00	22,715.60	113,578.01	0%	20%	-87
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-26	03-Dec-26	06-Aug-26 A	14-Jan-27	0.00	137,997.28	306,660.63	0%	45%	-127
PG-T-PCL-30	Snag list Submission	2	05-Dec-26	06-Dec-26	14-Jan-27	17-Jan-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-40	Snag list Closeout	7	07-Dec-26	14-Dec-26	17-Jan-27	25-Jan-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-50	Issuing Approvals	1	15-Dec-26	15-Dec-26	25-Jan-27	26-Jan-27	0.00	0.00	113,578.01	0%	0%	0
PG-T-PCL-60	Handing Over	1	16-Dec-26	16-Dec-26	26-Jan-27	27-Jan-27	0.00	0.00	113,578.01	0%	0%	0



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
