
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026		170	25-Jun-26	16-Dec-26	01-Jul-26 A	27-Jan-27	10,691,597.39	6,211,039.07	20,134,219.53	53.1%	30.85%	-30
MILESTONES		170	25-Jun-26	16-Dec-26	01-Jul-26 A	27-Jan-27	0.00	0.00	0.00	0%	0%	-30
GENERAL MILESTONES		170	25-Jun-26	16-Dec-26	01-Jul-26 A	27-Jan-27	0.00	0.00	0.00	0%	0%	-30
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	20-Dec-26	0.00	0.00	0.00	52.88%	50%	1
PG-GN-MS-20	Project Completion Date	0		16-Dec-26		27-Jan-27	0.00	0.00	0.00	0%	0%	0
CONTRACUAL MILESTONES		60	28-Oct-26	16-Dec-26	17-Nov-26	27-Jan-27	0.00	0.00	0.00	0%	0%	-18
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26		17-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-50	Completion of Playground Works	0		07-Dec-26		06-Dec-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-40	Completion of Landscape Works	0		16-Dec-26		20-Jan-27	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-60	Substantial Completion - All Works	0		16-Dec-26		27-Jan-27	0.00	0.00	0.00	0%	0%	0
QASSIM		145	25-Jun-26	16-Dec-26	30-Jul-26 A	19-Jan-27	5,435,089.62	2,970,031.43	9,536,555.56	56.99%	31.14%	2
ENGINEERING		66	25-Jun-26	04-Aug-26	30-Jul-26 A	18-Oct-26	355.69	0.00	355.69	100%	0%	-33
SHOP DRAWINGS SUBMITTALS		35	25-Jun-26	04-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-15
MECHANICAL DRAWINGS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-32
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-32
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	100%	90%	-32
ELECTRICAL DRAWINGS		17	16-Jul-26	04-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-33
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	0%	0%	-33
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	26-Sep-26	0.00	0.00	0.00	100%	90%	-39
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	100%	90%	-35
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	27-Sep-26	0.00	0.00	0.00	100%	90%	-33
MATERIAL APPROVALS		20	25-Jun-26	18-Jul-26	26-Sep-26	18-Oct-26	355.69	0.00	355.69	100%	0%	0
LONG LEAD ITEMS		20	25-Jun-26	18-Jul-26	26-Sep-26	18-Oct-26	355.69	0.00	355.69	100%	0%	0
METAL WORK		20	25-Jun-26	18-Jul-26	26-Sep-26	18-Oct-26	355.69	0.00	355.69	100%	0%	0
PG-Q-PR-LL-MT-MA-10_R	Metal Doors(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26	12-Oct-26	51.01	0.00	51.01	100%	0%	0
PG-Q-PR-LL-MT-MA-20_R	Curtain Wall(Remaining)	20	25-Jun-26	18-Jul-26	26-Sep-26	18-Oct-26	304.68	0.00	304.68	100%	0%	0
PROCUREMENT		74	25-Jun-26	27-Aug-26	14-Aug-26 A	10-Nov-26	2,610,282.21	1,063,291.67	2,610,282.21	100%	40.73%	-20
LONG LEAD ITEMS		74	25-Jun-26	27-Aug-26	14-Aug-26 A	10-Nov-26	2,454,380.38	988,697.82	2,454,380.38	100%	40.28%	-20
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		74	07-Jul-26	27-Aug-26	14-Aug-26 A	10-Nov-26	2,454,380.38	988,697.82	2,454,380.38	100%	40.28%	-30
EXTERNAL / LANDSCAPE WORK		35	07-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	73,600.14	61,078.10	73,600.14	100%	82.99%	-10
PG-Q-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	9	07-Jul-26	16-Jul-26	14-Aug-26 A	26-Sep-26	47,790.00	43,011.00	47,790.00	100%	90%	-27
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	14,428.69	10,100.08	14,428.69	100%	70%	-25
PG-Q-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	11,381.45	7,967.01	11,381.45	100%	70%	-25
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	05-Oct-26	2,119,264.56	756,080.57	2,119,264.56	100%	35.68%	-8
PG-Q-PR-LL-SP-DL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	28-Sep-26	26,778.60	21,422.88	26,778.60	100%	80%	-23
PG-Q-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	28-Sep-26	46,985.40	37,588.32	46,985.40	100%	80%	-23
PG-Q-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	28-Sep-26	10,152.00	8,121.60	10,152.00	100%	80%	-23
PG-Q-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	28-Sep-26	156,686.40	125,349.12	156,686.40	100%	80%	-23
PG-Q-PR-LL-SP-DL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	25-Aug-26 A	05-Oct-26	1,878,662.16	563,598.65	1,878,662.16	100%	30%	-25
METAL WORK		38	25-Jul-26	10-Aug-26	27-Aug-26 A	10-Nov-26	4,001.54	286.94	4,001.54	100%	7.17%	-49
PG-Q-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	15	25-Jul-26	10-Aug-26	27-Aug-26 A	02-Nov-26	573.89	286.94	573.89	100%	50%	-42
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26	10-Aug-26	25-Oct-26	10-Nov-26	3,427.65	0.00	3,427.65	100%	0%	0
PLUMBING WORK		21	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	15,992.78	11,194.94	15,992.78	100%	70%	-25
PG-Q-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	15	25-Jul-26	10-Aug-26	20-Aug-26 A	30-Sep-26	8,182.35	5,727.65	8,182.35	100%	70%	-20
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x0x3m)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	30-Sep-26	7,810.43	5,467.30	7,810.43	100%	70%	-25
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	27-Sep-26	20,455.88	16,364.70	20,455.88	100%	80%	-24
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	27-Sep-26	20,455.88	16,364.70	20,455.88	100%	80%	-24
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	01-Oct-26	221,065.50	143,692.57	221,065.50	100%	65%	-15
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	29-Sep-26	1,785.24	1,160.41	1,785.24	100%	65%	-29
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Oct-26	3,124.17	2,030.71	3,124.17	100%	65%	-25
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Oct-26	182,755.44	118,791.04	182,755.44	100%	65%	-25
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Oct-26	8,081.83	5,253.19	8,081.83	100%	65%	-25
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	6,326.40	4,112.16	6,326.40	100%	65%	-14
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	6,170.09	4,010.56	6,170.09	100%	65%	-14
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	7,811.37	5,077.39	7,811.37	100%	65%	-14
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Oct-26	5,010.96	3,257.12	5,010.96	100%	65%	-14
SHORT LEAD ITEMS		49	25-Jun-26	12-Jul-26	14-Aug-26 A	12-Oct-26	155,901.83	74,593.85	155,901.83	100%	47.85%	-35
DELIVERY TO SITE		49	25-Jun-26	12-Jul-26	14-Aug-26 A	12-Oct-26	155,901.83	74,593.85	155,901.83	100%	47.85%	-35
EXTERNAL / LANDSCAPE WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	78,553.04	27,493.57	78,553.04	100%	35%	-20
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	1,892.27	662.29	1,892.27	100%	35%	-20
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	714.10	249.93	714.10	100%	35%	-20
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	34,366.68	12,028.34	34,366.68	100%	35%	-20
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	41,580.00	14,553.00	41,580.00	100%	35%	-20
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	1,724.00	0.00	1,724.00	100%	0%	0
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	1,302.70	0.00	1,302.70	100%	0%	0
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	112.75	0.00	112.75	100%	0%	0
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	308.56	0.00	308.56	100%	0%	0
HVAC WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	2,182.90	873.16	2,182.90	100%	40%	-19
PG-Q-PR-SL-AC-DL-10_R	Split Air Conditioning Unit(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	1,115.75	446.30	1,115.75	100%	40%	-19

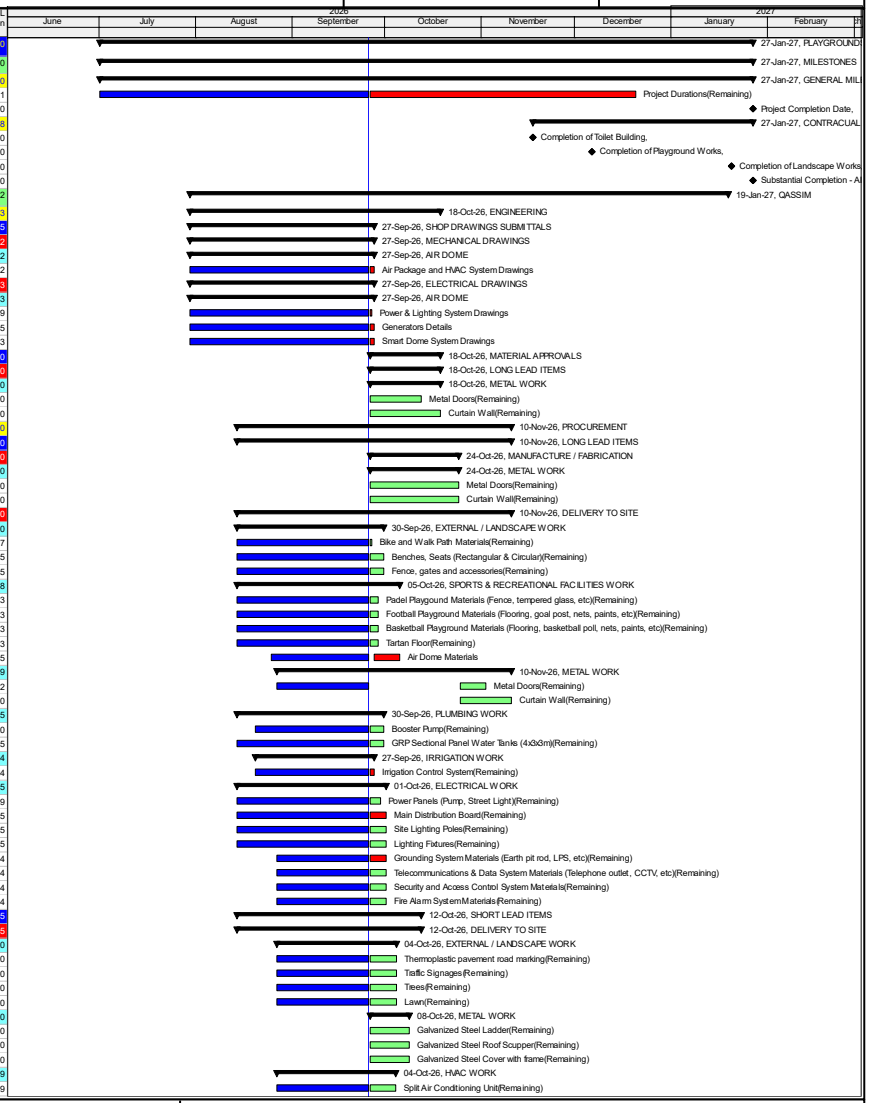

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-SL-AC-DL-20_R	Air Duct(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	561.60	224.64	561.60	100%	40%	-19
PG-Q-PR-SL-AC-DL-30_R	Diffusers and Grills(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	267.52	107.01	267.52	100%	40%	-19
PG-Q-PR-SL-AC-DL-40_R	Exhaust fans(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	04-Oct-26	238.03	95.21	238.03	100%	40%	-19
IRRIGATION WORK		18	25-Jun-26	08-Jul-26	14-Aug-26 A	30-Sep-26	71,118.65	46,227.12	71,118.65	100%	65%	-27
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	30-Sep-26	7,186.00	4,670.90	7,186.00	100%	65%	-27
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	30-Sep-26	63,932.65	41,556.22	63,932.65	100%	65%	-22
ELECTRICAL WORK		15	25-Jun-26	12-Jul-26	26-Sep-26	12-Oct-26	2,200.61	0.00	2,200.61	100%	0%	0
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26	12-Oct-26	2,200.61	0.00	2,200.61	100%	0%	0
FIRE FIGHTING WORK		12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	122.63	0.00	122.63	100%	0%	0
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	122.63	0.00	122.63	100%	0%	0
CONSTRUCTION STAGE		121	05-Jul-26	16-Dec-26	06-Aug-26 A	11-Jan-27	2,824,451.72	1,658,583.56	5,224,776.28	54.06%	31.74%	7
PLAYGROUND AND LANDSCAPING WORKS		121	05-Jul-26	16-Dec-26	06-Aug-26 A	11-Jan-27	1,150,577.29	1,189,270.80	1,949,970.60	59%	60.99%	7
PLAYGROUND WORKS		96	11-Aug-26	02-Dec-26	06-Aug-26 A	06-Dec-26	76,664.53	209,216.72	325,784.34	23.53%	64.22%	-7
FOOTBALL PLAYGROUND WORKS		49	19-Aug-26	17-Nov-26	14-Aug-26 A	25-Oct-26	48,027.00	62,664.66	109,254.66	43.96%	57.36%	17
PG-Q-CON-EXFB-120	Installation of Lighting System	12	19-Aug-26	01-Sep-26	20-Aug-26 A	27-Sep-26	24,360.00	20,706.00	24,360.00	100%	85%	-20
PG-Q-CON-EXFB-90	Turfing / Seeding Works	10	02-Sep-26	13-Sep-26	14-Aug-26 A	30-Sep-26	23,667.00	17,750.25	23,667.00	100%	75%	-29
PG-Q-CON-EXFB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	06-Oct-26	0.00	23,075.33	35,500.50	0%	65%	-19
PG-Q-CON-EXFB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	15-Oct-26	0.00	1,133.09	2,060.16	0%	55%	-24
PG-Q-CON-EXFB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	15-Oct-26	25-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		73	31-Aug-26	17-Nov-26	20-Aug-26 A	16-Nov-26	18,552.49	22,851.07	43,200.72	42.94%	52.9%	-7
PG-Q-CON-EXBB-80	Court Line Marking	15	31-Aug-26	16-Sep-26	20-Aug-26 A	01-Oct-26	13,091.76	10,473.41	13,091.76	100%	80%	-21
PG-Q-CON-EXBB-60	Basketball Pole Installation & Alignment	17	17-Sep-26	07-Oct-26	20-Aug-26 A	06-Oct-26	5,460.73	12,377.66	15,472.08	35.29%	80%	-22
PG-Q-CON-EXBB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	06-Oct-26	26-Oct-26	0.00	0.00	13,091.76	0%	0%	0
PG-Q-CON-EXBB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	26-Oct-26	16-Nov-26	0.00	0.00	1,545.12	0%	0%	0
PADEL PLAYGROUND WORKS		86	11-Aug-26	02-Dec-26	06-Aug-26 A	06-Dec-26	10,085.03	123,700.98	173,328.96	5.82%	71.37%	-7
PG-Q-CON-EXPD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26	31-Aug-26	20-Aug-26 A	06-Oct-26	3,534.96	2,474.47	3,534.96	100%	70%	-22
PG-Q-CON-EXPD-60	Chain Link Fence & Gates Installation	16	01-Sep-26	19-Sep-26	20-Aug-26 A	12-Oct-26	5,302.44	3,711.71	5,302.44	100%	70%	-29
PG-Q-CON-EXPD-50	Tempered Glass Installation	17	20-Sep-26	10-Oct-26	12-Oct-26	01-Nov-26	1,247.63	0.00	5,302.44	23.53%	0%	0
PG-Q-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	01-Nov-26	0.00	117,514.80	130,572.00	0%	90%	-58
PG-Q-CON-EXPD-70	Court Accessories Installation	15	29-Oct-26	15-Nov-26	01-Nov-26	18-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-Q-CON-EXPD-80	Install Playground Benches	15	16-Nov-26	02-Dec-26	18-Nov-26	06-Dec-26	0.00	0.00	1,545.12	0%	0%	0
GENERAL SITE WORKS		121	05-Jul-26	16-Dec-26	06-Aug-26 A	11-Jan-27	1,039,199.76	805,102.11	1,159,557.96	89.62%	69.43%	7
FENCE WORKS		56	02-Aug-26	13-Sep-26	20-Aug-26 A	26-Oct-26	19,745.64	5,594.60	19,745.64	100%	28.33%	-20
PG-Q-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-26	15-Aug-26	20-Aug-26 A	27-Sep-26	6,581.88	5,594.60	6,581.88	100%	85%	-20
PG-Q-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-26	01-Sep-26	27-Sep-26	14-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
PG-Q-CON-EXGN-FN-50	Installation of Gates	10	02-Sep-26	13-Sep-26	14-Oct-26	26-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		52	05-Jul-26	18-Aug-26	06-Aug-26 A	25-Oct-26	625,613.16	481,887.05	625,613.16	100%	77.03%	-28
STORM WATER AND UTILITY WORK		50	05-Jul-26	16-Aug-26	20-Aug-26 A	22-Oct-26	21,060.00	11,894.40	21,060.00	100%	56.48%	-16
PG-Q-CON-EXGN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	27-Sep-26	4,128.00	3,302.40	4,128.00	100%	80%	-25
PG-Q-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	28-Sep-26	10,740.00	8,592.00	10,740.00	100%	80%	-26
PG-Q-CON-EXGN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	28-Sep-26	06-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	06-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-26	16-Aug-26	15-Oct-26	22-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		10	30-Jul-26	09-Aug-26	06-Aug-26 A	15-Oct-26	604,235.22	469,992.65	604,235.22	100%	77.78%	-50
PG-Q-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	3	30-Jul-26	02-Aug-26	06-Aug-26 A	13-Oct-26	276,532.62	243,348.71	276,532.62	100%	88%	-55
PG-Q-CON-EXGN-M-90	Installation of Irrigation Control System	3	03-Aug-26	05-Aug-26	20-Aug-26 A	13-Oct-26	90,915.00	72,732.00	90,915.00	100%	80%	-43
PG-Q-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-26	09-Aug-26	27-Aug-26 A	15-Oct-26	236,787.60	153,911.94	236,787.60	100%	65%	-38
FIRE PROTECTION SYSTEM		2	17-Aug-26	18-Aug-26	22-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-Q-CON-EXGN-M-110	Fire Extinguisher Installation	2	17-Aug-26	18-Aug-26	22-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		66	13-Aug-26	01-Nov-26	20-Aug-26 A	22-Dec-26	393,840.96	275,813.66	450,291.36	87.46%	61.25%	-37
POWER, LIGHTING & GROUNDING		31	13-Aug-26	20-Sep-26	20-Aug-26 A	11-Nov-26	393,221.16	275,813.66	393,221.16	100%	70.14%	-37
PG-Q-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-26	17-Aug-26	20-Aug-26 A	22-Oct-26	162,449.28	129,959.42	162,449.28	100%	80%	-50
PG-Q-CON-EXGN-E-30	Lightning Protection System (LPS)	3	29-Aug-26	31-Aug-26	27-Aug-26 A	25-Oct-26	8,265.00	6,612.00	8,265.00	100%	80%	-47
PG-Q-CON-EXGN-E-40	KWH Meter and MDB Installation	2	01-Sep-26	02-Sep-26	25-Oct-26	27-Oct-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-Q-CON-EXGN-E-50	Power Panels and Distribution Boards	5	03-Sep-26	08-Sep-26	27-Oct-26	02-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-Q-CON-EXGN-E-60	Site Lighting Poles Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	03-Nov-26	174,052.80	139,242.24	174,052.80	100%	80%	-60
PG-Q-CON-EXGN-E-70	Wiring Works	3	13-Sep-26	15-Sep-26	03-Nov-26	07-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-Q-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	4	16-Sep-26	20-Sep-26	07-Nov-26	11-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-26	20-Oct-26	11-Nov-26	10-Dec-26	619.80	0.00	43,146.00	1.44%	0%	0
PG-Q-CON-EXGN-E-90	ELV Containment & Cabling Works	3	21-Sep-26	24-Sep-26	11-Nov-26	15-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-Q-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	26-Sep-26	28-Sep-26	15-Nov-26	18-Nov-26	0.00	0.00	619.80	0%	0%	0
PG-Q-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	29-Sep-26	03-Oct-26	18-Nov-26	23-Nov-26	0.00	0.00	3,718.80	0%	0%	0
PG-Q-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26	07-Oct-26	23-Nov-26	28-Nov-26	0.00	0.00	15,249.12	0%	0%	0
PG-Q-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	08-Oct-26	12-Oct-26	28-Nov-26	02-Dec-26	0.00	0.00	1,446.48	0%	0%	0
PG-Q-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	13-Oct-26	17-Oct-26	02-Dec-26	07-Dec-26	0.00	0.00	6,612.00	0%	0%	0
PG-Q-CON-EXGN-E-150	IP Camera Installation	3	18-Oct-26	20-Oct-26	07-Dec-26	10-Dec-26	0.00	0.00	14,880.00	0%	0%	0
FIRE ALARM SYSTEM		32	26-Sep-26	01-Nov-26	15-Nov-26	22-Dec-26	0.00	0.00	13,924.20	0%	0%	0
PG-Q-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	26-Sep-26	04-Oct-26	15-Nov-26	24-Nov-26	0.00	0.00	1,983.60	0%	0%	0
PG-Q-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26	13-Oct-26	24-Nov-26	03-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-Q-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26	22-Oct-26	03-Dec-26	13-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-Q-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	24-Oct-26	01-Nov-26	13-Dec-26	22-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		8	29-Oct-26	09-Nov-26	20-Aug-26 A	22-Dec-26	0.00	39,798.00	58,699.80	0%	67.8%	-95
PG-Q-CON-EXGN-PR-10	Installation of Parking Accessories	5	29-Oct-26	03-Nov-26	20-Aug-26 A	10-Dec-26	0.00	39,798.00	44,220.00	0%	90%	-91



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EX-GN-PR-30	Marking & Signages	5	04-Nov-2	09-Nov-26	16-Dec-26	22-Dec-26	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		20	19-Nov-2	16-Dec-26	14-Aug-26 A	11-Jan-27	0.00	2,008.80	5,208.00	0%	38.57%	-103
PG-Q-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-2	28-Nov-26	14-Aug-26 A	23-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-103
PG-Q-CON-EX-GN-SC-30	Connection to City Network	8	29-Nov-2	07-Dec-26	23-Dec-26	02-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-Q-CON-EX-GN-SC-40	Backfilling	8	08-Dec-2	16-Dec-26	02-Jan-27	11-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		54	30-Sep-2	14-Dec-26	20-Aug-26 A	07-Dec-26	0.00	174,951.98	429,915.30	0%	40.69%	-28
HARDSCAPE WORK		54	30-Sep-2	14-Dec-26	20-Aug-26 A	07-Dec-26	0.00	94,101.98	123,489.30	0%	76.2%	-28
PG-Q-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-2	14-Oct-26	27-Aug-26 A	28-Oct-26	0.00	47,124.00	55,440.00	0%	85%	-40
PG-Q-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-2	02-Dec-26	20-Aug-26 A	25-Nov-26	0.00	46,977.98	62,637.30	0%	75%	-73
PG-Q-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-2	14-Dec-26	25-Nov-26	07-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		28	15-Oct-26	21-Nov-26	27-Aug-26 A	23-Nov-26	0.00	80,850.00	306,426.00	0%	26.38%	-42
PG-Q-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	03-Nov-26	0.00	80,850.00	115,500.00	0%	70%	-42
PG-Q-CON-EX-LS-SS-10	Planting Trees	17	02-Nov-2	21-Nov-26	03-Nov-26	23-Nov-26	0.00	0.00	190,926.00	0%	0%	0
TANK WORKS		8	11-Aug-2	19-Aug-26	30-Sep-26	10-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
WATER STORAGE TANK		8	11-Aug-2	19-Aug-26	30-Sep-26	10-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-Q-CON-EX-TW-IR-40	GRP Water Tank Installation	8	11-Aug-2	19-Aug-26	30-Sep-26	10-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		90	12-Aug-2	26-Nov-26	27-Aug-26 A	30-Dec-26	1,662,963.91	450,878.92	3,217,836.10	51.68%	14.01%	-15
CIVIL WORK		25	12-Aug-2	10-Sep-26	27-Aug-26 A	20-Oct-26	751,464.86	200,390.63	751,464.86	100%	26.67%	-19
PG-Q-CON-EX-AD-CL-60	Installation of Anchorage System	8	12-Aug-2	20-Aug-26	27-Aug-26 A	29-Sep-26	250,488.29	200,390.63	250,488.29	100%	80%	-19
PG-Q-CON-EX-AD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-2	01-Sep-26	29-Sep-26	11-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EX-AD-CL-80	Installation of Membrane System	8	02-Sep-2	10-Sep-26	11-Oct-26	20-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		22	27-Oct-26	26-Nov-26	27-Aug-26 A	30-Dec-26	0.00	125,244.14	712,953.22	0%	17.57%	-79
PG-Q-CON-EX-AD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	08-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-79
PG-Q-CON-EX-AD-AR-40	Final Fixing of Accessories & Finishes	8	05-Nov-2	14-Nov-26	08-Dec-26	17-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EX-AD-AR-20	Installation of Doors & Access Systems	6	15-Nov-2	21-Nov-26	17-Dec-26	24-Dec-26	0.00	0.00	250,488.29	0%	0%	0
PG-Q-CON-EX-AD-AR-30	Installation of Logo	5	22-Nov-2	26-Nov-26	24-Dec-26	30-Dec-26	0.00	0.00	3,236.40	0%	0%	0
MECHANICAL WORK		16	12-Sep-2	30-Sep-26	20-Oct-26	08-Nov-26	494,018.57	0.00	667,968.77	73.96%	0%	0
PG-Q-CON-EX-AD-ME-10	Installation of Main Air Package Units	5	12-Sep-2	16-Sep-26	20-Oct-26	26-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EX-AD-ME-20	Installation of Backup Air Package Unit	5	17-Sep-2	22-Sep-26	26-Oct-26	01-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EX-AD-ME-30	Installation of Complete HVAC System	6	24-Sep-2	30-Sep-26	01-Nov-26	08-Nov-26	34,790.04	0.00	208,740.24	16.67%	0%	0
ELECTRICAL WORK		67	17-Aug-2	26-Oct-26	27-Aug-26 A	03-Dec-26	417,480.48	125,244.14	1,085,449.25	38.46%	11.54%	-23
PG-Q-CON-EX-AD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-2	30-Aug-26	27-Aug-26 A	01-Oct-26	208,740.24	125,244.14	208,740.24	100%	60%	-18
PG-Q-CON-EX-AD-EL-20	Installation of Lighting System	12	31-Aug-2	13-Sep-26	01-Oct-26	15-Oct-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EX-AD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	01-Oct-26	06-Oct-26	08-Nov-26	14-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EX-AD-EL-40	Installation of Backup Generator	6	07-Oct-26	13-Oct-26	14-Nov-26	21-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EX-AD-EL-50	Installation of Smart Dome System	11	14-Oct-26	26-Oct-26	21-Nov-26	03-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		39	20-Aug-2	20-Oct-26	20-Aug-26 A	17-Nov-26	10,910.52	18,433.86	56,969.58	19.15%	32.36%	-24
CIVIL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	16-Nov-26	0.00	18,433.86	45,922.80	0%	40.14%	-63
ARCHITECTURAL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	16-Nov-26	0.00	18,433.86	45,922.80	0%	40.14%	-63
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	16-Nov-26	0.00	9,291.66	20,825.40	0%	44.62%	-59
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	03-Nov-26	0.00	9,291.66	13,273.80	0%	70%	-53
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	11-Nov-26	16-Nov-26	0.00	0.00	7,551.60	0%	0%	0
WET AREA FINISHES		5	08-Oct-26	13-Oct-26	02-Nov-26	08-Nov-26	0.00	0.00	5,361.60	0%	0%	0
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	02-Nov-26	08-Nov-26	0.00	0.00	5,361.60	0%	0%	0
ROOF FINISHES		29	06-Oct-26	19-Oct-26	20-Aug-26 A	16-Nov-26	0.00	9,142.20	19,735.80	0%	46.32%	-63
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	15-Oct-26	0.00	9,142.20	10,158.00	0%	90%	-42
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26	19-Oct-26	16-Nov-26	16-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		39	20-Aug-2	20-Oct-26	04-Oct-26	17-Nov-26	10,910.52	0.00	11,046.78	98.77%	0%	13
MECANICAL WORKS		39	20-Aug-2	20-Oct-26	04-Oct-26	17-Nov-26	10,910.52	0.00	11,046.78	98.77%	0%	13
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	17-Nov-26	17-Nov-26	0.00	0.00	136.26	0%	0%	0
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	17-Nov-26	17-Nov-26	0.00	0.00	136.26	0%	0%	0
SEWER AND DRAINAGE SYSTEM		2	01-Sep-2	02-Sep-26	13-Oct-26	14-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-2	02-Sep-26	13-Oct-26	14-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	20-Aug-2	23-Aug-26	04-Oct-26	07-Oct-26	7,684.80	0.00	7,684.80	100%	0%	0
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-2	23-Aug-26	04-Oct-26	07-Oct-26	7,684.80	0.00	7,684.80	100%	0%	0
PROJECT CLOSOUT		31	15-Nov-2	16-Dec-26	06-Aug-26 A	19-Jan-27	0.00	248,156.19	1,701,141.38	0%	14.59%	-114
PG-Q-PCL-20	As-Built Drawings	15	15-Nov-2	02-Dec-26	23-Sep-26 A	06-Jan-27	0.00	35,075.08	175,375.40	0%	20%	-74
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	15-Nov-2	26-Nov-26	06-Aug-26 A	30-Dec-26	0.00	213,081.11	473,513.58	0%	45%	-114
PG-Q-PCL-30	Snag list Submission	3	28-Nov-2	30-Nov-26	30-Dec-26	03-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-40	Snag list Closeout	10	01-Dec-2	12-Dec-26	03-Jan-27	14-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-50	Issuing Approvals	3	13-Dec-2	15-Dec-26	14-Jan-27	18-Jan-27	0.00	0.00	175,375.40	0%	0%	0
PG-Q-PCL-60	Handing Over	1	16-Dec-2	16-Dec-26	18-Jan-27	19-Jan-27	0.00	0.00	175,375.40	0%	0%	0
HAIL		127	25-Jun-26	16-Dec-26	09-Jul-26 A	09-Jan-27	1,648,001.02	1,588,926.96	3,264,064.16	50.49%	48.68%	-8
PROCUREMENT		59	25-Jun-26	26-Aug-26	06-Aug-26 A	27-Oct-26	516,988.47	451,062.01	516,988.47	100%	87.25%	-16
LONG LEAD ITEMS		59	25-Jun-26	26-Aug-26	06-Aug-26 A	27-Oct-26	423,859.72	383,142.31	423,859.72	100%	90.39%	-16
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
PG-H-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	26-Sep-26	24-Oct-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		59	25-Jul-26	26-Aug-26	06-Aug-26 A	27-Oct-26	423,859.72	383,142.31	423,859.72	100%	90.39%	-41
EXTERNAL / LANDSCAPE WORK		29	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	72,919.30	64,203.64	72,919.30	100%	88.05%	-32
PG-H-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	05-Aug-26	20-Aug-26 A	27-Sep-26	28,474.61	24,203.41	28,474.61	100%	85%	-20
PG-H-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	44,444.70	40,000.23	44,444.70	100%	90%	-31




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
SPORTS & RECREATIONAL FACILITIES WORK		12	25-Jul-26	05-Aug-26	06-Aug-26 A	27-Sep-26	163,721.25	147,349.13	163,721.25	100%	90%	-31
PG-H-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	05-Aug-26	06-Aug-26 A	27-Sep-26	64,212.75	57,791.48	64,212.75	100%	90%	-31
PG-H-PR-LL-SP-DL-20_R	Tartan Floor(Remaining)	12	25-Jul-26	05-Aug-26	06-Aug-26 A	27-Sep-26	99,508.50	89,557.65	99,508.50	100%	90%	-31
METAL WORK		12	25-Jul-26	05-Aug-26	27-Aug-26 A	27-Oct-26	4,801.84	3,601.38	4,801.84	100%	75%	-40
PG-H-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	05-Aug-26	27-Aug-26 A	27-Oct-26	688.66	516.50	688.66	100%	75%	-40
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	05-Aug-26	27-Aug-26 A	27-Oct-26	4,113.18	3,084.89	4,113.18	100%	75%	-40
PLUMBING WORK		12	25-Jul-26	05-Aug-26	27-Aug-26 A	28-Sep-26	9,372.51	7,498.01	9,372.51	100%	80%	-14
PG-H-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	05-Aug-26	27-Aug-26 A	28-Sep-26	9,372.51	7,498.01	9,372.51	100%	80%	-14
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	27-Sep-26	173,044.81	160,490.15	173,044.81	100%	92.74%	-8
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	27-Sep-26	3,124.17	2,655.54	3,124.17	100%	85%	-17
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	27-Sep-26	2,499.34	2,124.44	2,499.34	100%	85%	-17
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	27-Sep-26	6,326.40	5,377.44	6,326.40	100%	85%	-17
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	26-Sep-26	134,020.66	127,319.62	134,020.66	100%	95%	-19
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	27-Sep-26	8,081.83	6,869.55	8,081.83	100%	85%	-20
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	27-Sep-26	6,170.09	5,244.58	6,170.09	100%	85%	-14
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	27-Sep-26	7,811.37	6,639.66	7,811.37	100%	85%	-14
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	27-Sep-26	5,010.96	4,259.31	5,010.96	100%	85%	-14
SHORT LEAD ITEMS		33	04-Jul-26	16-Jul-26	20-Aug-26 A	08-Oct-26	93,128.75	67,919.69	93,128.75	100%	72.93%	-30
DELIVERY TO SITE		33	04-Jul-26	16-Jul-26	20-Aug-26 A	08-Oct-26	93,128.75	67,919.69	93,128.75	100%	72.93%	-30
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	59,572.42	41,700.70	59,572.42	100%	70%	-16
PG-H-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	3,311.47	2,318.03	3,311.47	100%	70%	-16
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	1,249.67	874.77	1,249.67	100%	70%	-16
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	30,441.29	21,308.90	30,441.29	100%	70%	-16
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	29-Sep-26	24,570.00	17,199.00	24,570.00	100%	70%	-16
IRRIGATION WORK		17	04-Jul-26	16-Jul-26	20-Aug-26 A	27-Sep-26	30,845.88	26,219.00	30,845.88	100%	85%	-20
PG-H-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26	16-Jul-26	20-Aug-26 A	27-Sep-26	3,403.35	2,892.85	3,403.35	100%	85%	-20
PG-H-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	27-Sep-26	27,442.53	23,326.15	27,442.53	100%	85%	-14
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	26-Sep-26	08-Oct-26	2,567.38	0.00	2,567.38	100%	0%	0
PG-H-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26	08-Oct-26	2,567.38	0.00	2,567.38	100%	0%	0
FIRE FIGHTING WORK		12	04-Jul-26	16-Jul-26	26-Sep-26	08-Oct-26	143.07	0.00	143.07	100%	0%	0
PG-H-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26	08-Oct-26	143.07	0.00	143.07	100%	0%	0
CONSTRUCTION STAGE		124	25-Jun-26	26-Nov-26	09-Jul-26 A	09-Jan-27	1,131,012.55	1,082,666.27	2,086,054.45	54.22%	51.9%	-24
PLAYGROUND AND LANDSCAPING WORKS		121	25-Jun-26	26-Nov-26	09-Jul-26 A	09-Jan-27	1,043,813.71	1,013,673.63	1,917,464.23	54.44%	52.87%	-24
PLAYGROUND WORKS		60	29-Jul-26	17-Nov-26	06-Aug-26 A	01-Nov-26	268,411.50	410,796.06	516,185.40	52%	79.58%	21
FOOTBALL PLAYGROUND WORKS		60	29-Jul-26	17-Nov-26	06-Aug-26 A	01-Nov-26	268,411.50	410,796.06	516,185.40	52%	79.58%	21
PG-H-CON-EX-FB-50	Goal Post Foundation	17	29-Jul-26	17-Aug-26	20-Aug-26 A	30-Sep-26	35,500.50	26,625.38	35,500.50	100%	75%	-17
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26	01-Sep-26	27-Aug-26 A	06-Oct-26	48,720.00	29,232.00	48,720.00	100%	60%	-20
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26	15-Sep-26	14-Aug-26 A	08-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-35
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26	04-Oct-26	06-Aug-26 A	08-Oct-26	160,524.00	309,582.00	343,980.00	46.67%	90%	-39
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	14-Oct-26	0.00	23,075.33	35,500.50	0%	65%	-33
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	20-Oct-26	0.00	3,347.76	5,150.40	0%	65%	-31
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	20-Oct-26	01-Nov-26	0.00	0.00	23,667.00	0%	0%	0
GENERAL SITE WORKS		121	25-Jun-26	26-Nov-26	14-Aug-26 A	09-Jan-27	706,687.93	304,281.10	854,072.29	82.74%	35.63%	7
FENCE WORKS		36	23-Jul-26	16-Aug-26	27-Aug-26 A	11-Oct-26	39,491.28	10,531.01	39,491.28	100%	26.67%	-17
PG-H-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26	02-Aug-26	27-Aug-26 A	27-Sep-26	13,163.76	10,531.01	13,163.76	100%	80%	-17
PG-H-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-26	11-Aug-26	27-Sep-26	06-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
PG-H-CON-EX-GN-FN-50	Installation of Gates	4	12-Aug-26	16-Aug-26	06-Oct-26	11-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
MECHANICAL WORK		57	25-Jun-26	06-Aug-26	14-Aug-26 A	21-Oct-26	344,669.34	151,389.96	344,669.34	100%	43.92%	-21
STORM WATER AND UTILITY WORK		55	25-Jun-26	04-Aug-26	14-Aug-26 A	19-Oct-26	23,124.00	4,747.20	23,124.00	100%	20.53%	-21
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	27-Sep-26	1,032.00	877.20	1,032.00	100%	85%	-27
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	28-Sep-26	5,160.00	3,870.00	5,160.00	100%	75%	-22
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	28-Sep-26	03-Oct-26	10,740.00	0.00	10,740.00	100%	0%	0
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	03-Oct-26	06-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	06-Oct-26	10-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	14-Oct-26	19-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		28	21-Jul-26	30-Jul-26	14-Aug-26 A	14-Oct-26	321,227.40	146,642.76	321,227.40	100%	45.65%	-44
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	10-Oct-26	108,345.60	92,093.76	108,345.60	100%	85%	-45
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	11-Oct-26	90,915.00	54,549.00	90,915.00	100%	60%	-36
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	11-Oct-26	14-Oct-26	121,966.80	0.00	121,966.80	100%	0%	0
FIRE PROTECTION SYSTEM		2	05-Aug-26	06-Aug-26	19-Oct-26	21-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-H-CON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-26	06-Aug-26	19-Oct-26	21-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		74	05-Aug-26	20-Oct-26	20-Aug-26 A	24-Dec-26	322,527.31	83,390.63	360,557.47	89.45%	23.13%	-43
POWER, LIGHTING & GROUNDING		39	05-Aug-26	08-Sep-26	20-Aug-26 A	14-Nov-26	303,487.27	83,390.63	303,487.27	100%	27.48%	-43
PG-H-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-26	09-Aug-26	20-Aug-26 A	20-Oct-26	119,129.47	83,390.63	119,129.47	100%	70%	-49
PG-H-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-26	19-Aug-26	21-Oct-26	25-Oct-26	8,265.00	0.00	8,265.00	100%	0%	0
PG-H-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-26	22-Aug-26	25-Oct-26	27-Oct-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-H-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-26	27-Aug-26	27-Oct-26	02-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-H-CON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-26	31-Aug-26	02-Nov-26	05-Nov-26	127,638.72	0.00	127,638.72	100%	0%	0
PG-H-CON-EX-GN-E-70	Wiring Works	3	01-Sep-26	03-Sep-26	05-Nov-26	09-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-H-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-26	08-Sep-26	09-Nov-26	14-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-26	08-Oct-26	14-Nov-26	13-Dec-26	16,395.24	0.00	43,146.00	38%	0%	0
PG-H-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-26	12-Sep-26	14-Nov-26	17-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-H-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-26	15-Sep-26	17-Nov-26	21-Nov-26	619.80	0.00	619.80	100%	0%	0

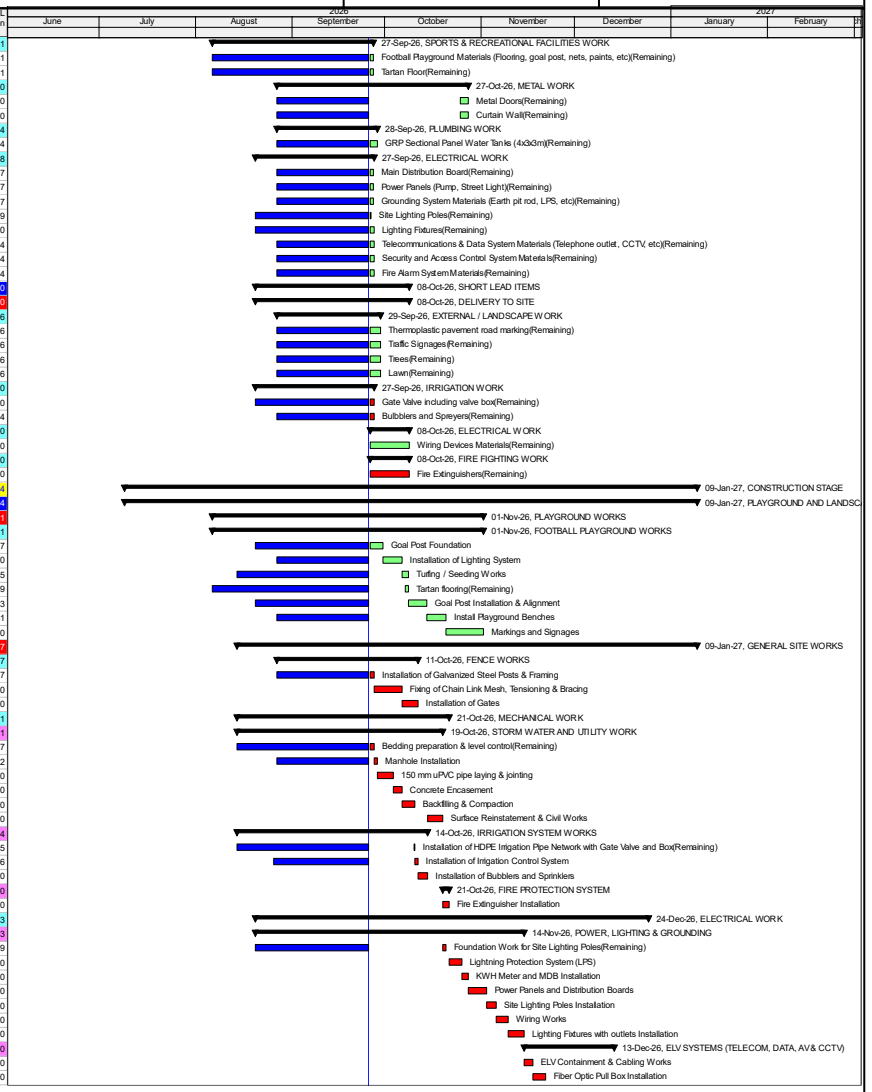

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-26	20-Sep-26	21-Nov-26	25-Nov-26	3,718.80	0.00	3,718.80	100%	0%	0
PG-H-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-26	26-Sep-26	25-Nov-26	30-Nov-26	11,436.84	0.00	15,249.12	75%	0%	0
PG-H-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-26	30-Sep-26	30-Nov-26	05-Dec-26	0.00	0.00	1,446.48	0%	0%	0
PG-H-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-26	05-Oct-26	05-Dec-26	09-Dec-26	0.00	0.00	6,612.00	0%	0%	0
PG-H-CON-EX-GN-E-150	IP Camera Installation	3	06-Oct-26	08-Oct-26	09-Dec-26	13-Dec-26	0.00	0.00	14,880.00	0%	0%	0
FIRE ALARM SYSTEM		32	13-Sep-26	20-Oct-26	17-Nov-26	24-Dec-26	2,644.80	0.00	13,924.20	18.99%	0%	0
PG-H-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-26	21-Sep-26	17-Nov-26	26-Nov-26	1,983.60	0.00	1,983.60	100%	0%	0
PG-H-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-26	01-Oct-26	26-Nov-26	06-Dec-26	661.20	0.00	2,644.80	25%	0%	0
PG-H-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-26	11-Oct-26	06-Dec-26	15-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-H-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-26	20-Oct-26	15-Dec-26	24-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		21	10-Oct-26	20-Oct-26	20-Aug-26 A	24-Dec-26	0.00	56,179.50	104,146.20	0%	53.94%	-98
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	15-Dec-26	0.00	56,179.50	86,430.00	0%	65%	-95
PG-H-CON-EX-GN-PR-30	Marking & Signages	5	15-Oct-26	20-Oct-26	19-Dec-26	24-Dec-26	0.00	0.00	17,716.20	0%	0%	0
SERVICE CONNECTION		22	31-Oct-26	26-Nov-26	20-Aug-26 A	09-Jan-27	0.00	2,790.00	5,208.00	0%	53.57%	-96
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	27-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-101
PG-H-CON-EX-GN-SC-30	Connection to City Network	8	09-Nov-26	17-Nov-26	27-Dec-26	05-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26	26-Nov-26	27-Aug-26 A	09-Jan-27	0.00	892.80	1,488.00	0%	60%	-106
LANDSCAPING WORKS		46	20-Sep-26	09-Nov-26	09-Jul-26 A	06-Dec-26	28,224.00	294,976.55	506,716.26	5.57%	58.21%	-85
HARDSCAPE WORK		46	20-Sep-26	09-Nov-26	09-Jul-26 A	06-Dec-26	28,224.00	256,756.55	355,477.26	7.94%	72.23%	-85
PG-H-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-26	05-Oct-26	27-Aug-26 A	07-Nov-26	16,632.00	35,135.10	54,054.00	30.77%	65%	-47
PG-H-CON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-26	07-Oct-26	30-Jul-26 A	07-Nov-26	11,592.00	39,123.00	43,470.00	26.67%	90%	-69
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	18-Nov-26	0.00	140,741.55	148,149.00	0%	95%	-104
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	24-Nov-26	0.00	41,756.90	104,392.26	0%	40%	-90
PG-H-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	29-Oct-26	09-Nov-26	24-Nov-26	06-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		22	06-Oct-26	09-Nov-26	27-Aug-26 A	06-Dec-26	0.00	38,220.00	151,239.00	0%	25.27%	-56
PG-H-CON-EX-LS-SS-10	Planting Trees	10	06-Oct-26	17-Oct-26	07-Nov-26	18-Nov-26	0.00	0.00	96,639.00	0%	0%	0
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-26	09-Nov-26	27-Aug-26 A	06-Dec-26	0.00	38,220.00	54,600.00	0%	70%	-79
TANK WORKS		65	02-Jul-26	19-Sep-26	14-Aug-26 A	01-Nov-26	40,490.28	3,619.92	40,490.28	100%	8.94%	1
SEPTIC TANK		60	02-Jul-26	31-Aug-26	14-Aug-26 A	26-Oct-26	5,777.28	3,619.92	5,777.28	100%	62.66%	-10
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26	09-Jul-26	14-Aug-26 A	28-Sep-26	2,757.60	1,930.32	2,757.60	100%	70%	-30
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26	18-Jul-26	27-Aug-26 A	30-Sep-26	2,599.38	1,689.60	2,599.38	100%	65%	-22
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-26	24-Aug-26	11-Oct-26	19-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-26	31-Aug-26	19-Oct-26	26-Oct-26	168.12	0.00	168.12	100%	0%	0
WATER STORAGE TANK		5	14-Sep-26	19-Sep-26	26-Oct-26	01-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-H-CON-EX-TW-IR-40	GRP Water Tank Installation	5	14-Sep-26	19-Sep-26	26-Oct-26	01-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
TOILET BUILDING WORKS		75	03-Aug-26	06-Oct-26	30-Jul-26 A	08-Nov-26	87,198.84	68,992.64	168,590.22	51.72%	40.92%	-31
CIVIL WORK		40	09-Sep-26	05-Oct-26	20-Aug-26 A	07-Nov-26	20,432.88	25,152.12	101,688.00	20.09%	24.73%	-45
ARCHITECTURAL WORK		40	09-Sep-26	05-Oct-26	20-Aug-26 A	07-Nov-26	20,432.88	25,152.12	101,688.00	20.09%	24.73%	-45
GENERAL FINISHES		23	09-Sep-26	05-Oct-26	20-Aug-26 A	07-Nov-26	11,195.88	11,553.78	72,432.60	15.46%	15.95%	-45
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-26	12-Sep-26	20-Aug-26 A	10-Oct-26	2,958.00	2,070.60	2,958.00	100%	70%	-40
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-26	20-Sep-26	20-Aug-26 A	12-Oct-26	273.60	191.52	273.60	100%	70%	-38
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-26	27-Sep-26	27-Aug-26 A	29-Oct-26	7,964.28	9,291.66	13,273.80	60%	70%	-49
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-26	05-Oct-26	29-Oct-26	07-Nov-26	0.00	0.00	55,927.20	0%	0%	0
WET AREA FINISHES		4	01-Oct-26	05-Oct-26	27-Aug-26 A	29-Oct-26	0.00	3,485.04	5,361.60	0%	65%	-49
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26	05-Oct-26	27-Aug-26 A	29-Oct-26	0.00	3,485.04	5,361.60	0%	65%	-49
ROOF FINISHES		40	19-Sep-26	05-Oct-26	20-Aug-26 A	07-Nov-26	9,237.00	10,113.30	23,893.80	38.66%	42.33%	-53
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-26	22-Sep-26	20-Aug-26 A	12-Oct-26	4,158.00	2,494.80	4,158.00	100%	60%	-41
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-26	26-Sep-26	27-Aug-26 A	12-Oct-26	5,079.00	7,618.50	10,158.00	50%	75%	-37
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-26	05-Oct-26	04-Nov-26	07-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		75	03-Aug-26	06-Oct-26	30-Jul-26 A	08-Nov-26	66,763.96	43,840.52	66,902.22	99.8%	65.53%	-31
MECANICAL WORKS		75	03-Aug-26	06-Oct-26	30-Jul-26 A	08-Nov-26	50,502.24	30,016.36	50,638.50	99.73%	59.28%	-31
FIRE FIGHTING SYSTEM		1	06-Oct-26	06-Oct-26	07-Nov-26	08-Nov-26	0.00	0.00	136.26	0%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-26	06-Oct-26	07-Nov-26	08-Nov-26	0.00	0.00	136.26	0%	0%	0
SEWER AND DRAINAGE SYSTEM		43	03-Aug-26	23-Aug-26	30-Jul-26 A	01-Oct-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-36
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-26	04-Aug-26	30-Jul-26 A	26-Sep-26	3,225.72	2,741.86	3,225.72	100%	85%	-46
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-26	23-Aug-26	29-Sep-26	01-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-26	15-Aug-26	26-Sep-26	28-Sep-26	7,684.80	0.00	7,684.80	100%	0%	0
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-26	15-Aug-26	26-Sep-26	28-Sep-26	7,684.80	0.00	7,684.80	100%	0%	0
WATER SUPPLY SYSTEM		3	18-Aug-26	20-Aug-26	27-Aug-26 A	29-Sep-26	36,366.00	27,274.50	36,366.00	100%	75%	-25
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-26	20-Aug-26	27-Aug-26 A	29-Sep-26	36,366.00	27,274.50	36,366.00	100%	75%	-25
ELECTRICAL WORKS		11	27-Aug-26	08-Sep-26	20-Aug-26 A	04-Oct-26	16,263.72	13,824.16	16,263.72	100%	85%	-26
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-26	29-Aug-26	20-Aug-26 A	03-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-34
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-26	01-Sep-26	20-Aug-26 A	03-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-34
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-26	05-Sep-26	20-Aug-26 A	03-Oct-26	4,959.00	4,215.15	4,959.00	100%	85%	-34
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-26	08-Sep-26	20-Aug-26 A	04-Oct-26	7,337.52	6,236.89	7,337.52	100%	85%	-34
PROJECT CLOSOUT		36	02-Nov-26	16-Dec-26	06-Aug-26 A	07-Jan-27	0.00	55,198.68	661,021.24	0%	8.35%	-94
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-26	14-Nov-26	06-Aug-26 A	06-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-94
PG-H-PCL-20	As-Built Drawings	18	14-Nov-26	05-Dec-26	06-Dec-26	27-Dec-26	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-30	Snag list Submission	8	14-Nov-26	23-Nov-26	06-Dec-26	15-Dec-26	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-40	Snag list Closeout	14	23-Nov-26	09-Dec-26	15-Dec-26	31-Dec-26	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-50	Issuing Approvals	3	09-Dec-26	13-Dec-26	31-Dec-26	04-Jan-27	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-60	Handing Over	3	13-Dec-26	16-Dec-26	04-Jan-27	07-Jan-27	0.00	0.00	68,146.52	0%	0%	0
TABUK		158	25-Jun-26	16-Dec-26	12-Jul-26 A	27-Jan-27	3,608,506.75	1,652,080.68	7,333,599.80	49.21%	22.53%	-21




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PROCUREMENT		81	25-Jun-26	27-Aug-26	22-Jul-26 A	19-Oct-26	2,189,927.50	922,244.42	2,189,927.50	100%	42.11%	-20
LONG LEAD ITEMS		81	25-Jun-26	27-Aug-26	22-Jul-26 A	19-Oct-26	2,150,925.17	890,683.44	2,150,925.17	100%	41.41%	-20
MANUFACTURE / FABRICATION		69	25-Jun-26	16-Aug-26	22-Jul-26 A	12-Oct-26	0.00	0.00	0.00	0%	0%	-25
EXTERNAL / LANDSCAPE WORK		37	25-Jun-26	23-Jul-26	22-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-38
PG-T-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	04-Oct-26	0.00	0.00	0.00	100%	70%	-26
PG-T-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	6	25-Jun-26	01-Jul-26	22-Jul-26 A	26-Sep-26	0.00	0.00	0.00	100%	90%	-50
PG-T-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
SPORTS & RECREATIONAL FACILITIES WORK		47	25-Jun-26	16-Aug-26	05-Aug-26 A	07-Oct-26	0.00	0.00	0.00	0%	0%	-8
PG-T-PR-LL-SPMF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-30_R	Padel Playground Materials (Flooring, fence, tempered glass,	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-40_R	Tartan Floor(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	28-Sep-26	0.00	0.00	0.00	100%	90%	-21
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26	16-Aug-26	27-Aug-26 A	07-Oct-26	0.00	0.00	0.00	100%	60%	-8
METAL WORK		25	25-Jun-26	23-Jul-26	27-Aug-26 A	12-Oct-26	0.00	0.00	0.00	0%	0%	-14
PG-T-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26	23-Jul-26	27-Aug-26 A	10-Oct-26	0.00	0.00	0.00	100%	50%	-12
PG-T-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	27-Aug-26 A	12-Oct-26	0.00	0.00	0.00	100%	40%	-14
PLUMBING WORK		25	25-Jun-26	23-Jul-26	05-Aug-26 A	30-Sep-26	0.00	0.00	0.00	0%	0%	-23
PG-T-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26	23-Jul-26	05-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-23
ELECTRICAL WORK		55	13-Jul-26	10-Aug-26	23-Jul-26 A	30-Sep-26	0.00	0.00	0.00	0%	0%	-34
PG-T-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	25	13-Jul-26	10-Aug-26	06-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-22
PG-T-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	25	13-Jul-26	10-Aug-26	06-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-22
PG-T-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	13-Jul-26	10-Aug-26	06-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-22
PG-T-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	13-Jul-26	10-Aug-26	23-Jul-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-34
PG-T-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	13-Jul-26	10-Aug-26	27-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-4
PG-T-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-4
PG-T-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	13-Jul-26	10-Aug-26	27-Aug-26 A	30-Sep-26	0.00	0.00	0.00	100%	80%	-4
PG-T-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	6	18-Jul-26	23-Jul-26	27-Aug-26 A	27-Sep-26	0.00	0.00	0.00	100%	80%	-19
DELIVERY TO SITE		58	01-Jul-26	27-Aug-26	06-Aug-26 A	19-Oct-26	2,150,925.17	890,683.44	2,150,925.17	100%	41.41%	-13
EXTERNAL / LANDSCAPE WORK		14	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	38,301.55	35,690.04	38,301.55	100%	93.18%	-31
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	13,928.65	12,535.79	13,928.65	100%	90%	-24
PG-T-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	26-Sep-26	24,372.90	23,154.26	24,372.90	100%	95%	-31
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	14-Oct-26	2,013,812.01	779,166.62	2,013,812.01	100%	38.69%	-29
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	58,731.75	52,858.58	58,731.75	100%	90%	-24
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	10,152.00	9,136.80	10,152.00	100%	90%	-24
PG-T-PR-LL-SPDL-30_R	Padel Playground Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	27-Sep-26	26,778.60	24,100.74	26,778.60	100%	90%	-24
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	27-Sep-26	39,487.50	35,538.75	39,487.50	100%	90%	-31
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-2	27-Aug-26	20-Aug-26 A	14-Oct-26	1,878,662.16	657,531.76	1,878,662.16	100%	35%	-37
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	19-Oct-26	4,001.54	2,258.23	4,001.54	100%	56.43%	-32
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	14-Oct-26	573.89	373.03	573.89	100%	65%	-29
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	19-Oct-26	3,427.65	1,885.21	3,427.65	100%	55%	-32
PLUMBING WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	28-Sep-26	6,248.34	4,686.26	6,248.34	100%	75%	-26
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	28-Sep-26	6,248.34	4,686.26	6,248.34	100%	75%	-26
IRRIGATION WORK		10	01-Jul-26	06-Jul-26	07-Aug-26 A	27-Sep-26	24,489.54	15,506.21	24,489.54	100%	63.32%	-39
PG-T-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	4	01-Jul-26	06-Jul-26	07-Aug-26 A	27-Sep-26	8,124.84	5,687.39	8,124.84	100%	70%	-38
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	06-Jul-26	20-Aug-26 A	27-Sep-26	16,364.70	9,818.82	16,364.70	100%	60%	-28
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	04-Oct-26	64,072.19	53,376.08	64,072.19	100%	83.31%	-16
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	27-Sep-26	3,615.08	3,072.82	3,615.08	100%	85%	-32
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	27-Sep-26	1,785.24	1,517.45	1,785.24	100%	85%	-25
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	27-Sep-26	1,428.19	1,213.96	1,428.19	100%	85%	-25
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	27-Sep-26	41,772.67	35,506.77	41,772.67	100%	85%	-25
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	27-Sep-26	4,618.19	3,925.46	4,618.19	100%	85%	-25
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-2	24-Aug-26	27-Aug-26 A	04-Oct-26	3,525.77	2,644.33	3,525.77	100%	75%	-20
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	04-Oct-26	4,463.64	3,347.73	4,463.64	100%	75%	-20
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	04-Oct-26	2,863.40	2,147.55	2,863.40	100%	75%	-20
SHORT LEAD ITEMS		46	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Oct-26	39,002.34	31,560.98	39,002.34	100%	80.92%	-29
DELIVERY TO SITE		46	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Oct-26	39,002.34	31,560.98	39,002.34	100%	80.92%	-29
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	19,978.06	16,981.35	19,978.06	100%	85%	-16
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	714.10	606.98	714.10	100%	85%	-16
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	8,301.96	7,056.67	8,301.96	100%	85%	-16
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Sep-26	10,962.00	9,317.70	10,962.00	100%	85%	-16
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	1,724.00	0.00	1,724.00	100%	0%	0
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	1,302.70	0.00	1,302.70	100%	0%	0
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	112.75	0.00	112.75	100%	0%	0
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26	08-Oct-26	308.56	0.00	308.56	100%	0%	0
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	26-Sep-26	14,977.04	13,479.33	14,977.04	100%	90%	-33
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	26-Sep-26	1,859.76	1,673.78	1,859.76	100%	90%	-33
PG-T-PR-SL-IR-DL-20_R	Bulbblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	26-Sep-26	13,117.28	11,805.55	13,117.28	100%	90%	-22
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	19-Sep-26 A	01-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	1
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	19-Sep-26 A	01-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	1
FIRE FIGHTING WORK		9	30-Jun-26	09-Jul-26	26-Sep-26	05-Oct-26	122.63	0.00	122.63	100%	0%	0
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26	09-Jul-26	26-Sep-26	05-Oct-26	122.63	0.00	122.63	100%	0%	0
CONSTRUCTION STAGE		146	25-Jun-26	14-Dec-26	12-Jul-26 A	20-Jan-27	1,418,579.24	569,123.38	4,041,965.60	35.1%	14.08%	-17
PLAYGROUND AND LANDSCAPING WORKS		146	25-Jun-26	14-Dec-26	12-Jul-26 A	20-Jan-27	502,278.52	541,911.14	1,012,265.62	49.62%	53.53%	-17

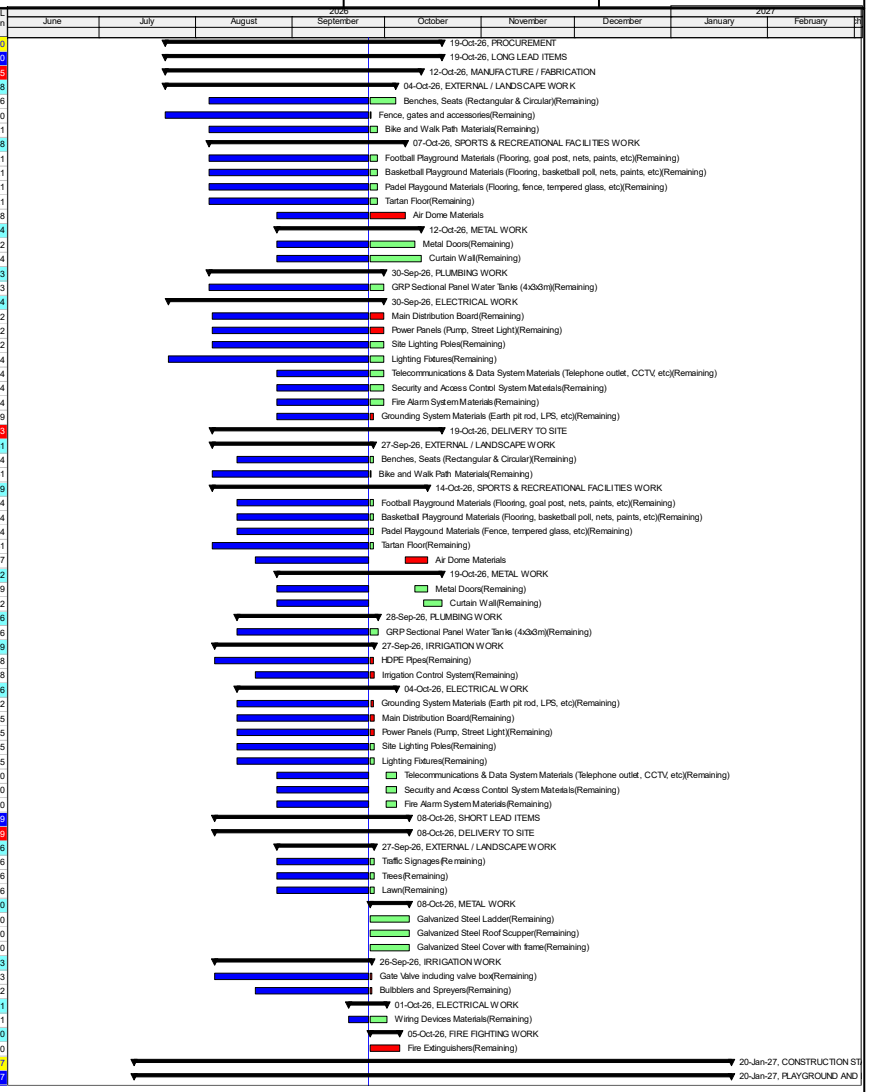


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUND WORKS		71	08-Aug-26	07-Dec-26	14-Aug-26 A	17-Nov-26	75,137.70	120,903.55	221,537.34	33.92%	54.57%	23
FOOTBALL PLAYGROUND WORKS		52	19-Aug-26	17-Nov-26	14-Aug-26 A	22-Oct-26	48,027.00	65,656.75	109,254.66	43.96%	60.1%	18
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	29-Sep-26	24,360.00	18,270.00	24,360.00	100%	75%	-20
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	30-Sep-26	23,667.00	21,300.30	23,667.00	100%	90%	-27
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	05-Oct-26	0.00	24,850.35	35,500.50	0%	70%	-24
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	11-Oct-26	0.00	1,236.10	2,060.16	0%	60%	-26
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	11-Oct-26	22-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		46	31-Aug-26	17-Nov-26	20-Aug-26 A	27-Oct-26	17,389.56	24,045.41	43,200.72	40.25%	55.66%	10
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	29-Sep-26	13,091.76	11,128.00	13,091.76	100%	85%	-18
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	05-Oct-26	4,297.80	11,604.06	15,472.08	27.78%	75%	-20
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	05-Oct-26	25-Oct-26	0.00	0.00	13,091.76	0%	0%	0
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	27-Oct-26	0.00	1,313.35	1,545.12	0%	85%	-36
PADEL PLAYGROUND WORKS		57	08-Aug-26	07-Dec-26	20-Aug-26 A	17-Nov-26	9,721.14	31,201.39	69,081.96	14.07%	45.17%	28
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	30-Sep-26	3,534.96	3,004.72	3,534.96	100%	85%	-14
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	03-Oct-26	5,302.44	4,507.07	5,302.44	100%	85%	-19
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	03-Oct-26	24-Oct-26	883.74	0.00	5,302.44	16.67%	0%	0
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	27-Oct-26	0.00	22,376.25	26,325.00	0%	85%	-40
PG-T-CON-EXPD-70	Court Accessories Installation	16	02-Nov-26	19-Nov-26	27-Oct-26	15-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	17-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-55
GENERAL SITE WORKS		146	25-Jun-26	14-Dec-26	12-Jul-26 A	20-Jan-27	400,703.86	253,934.88	497,741.02	80.5%	51.02%	-17
FENCE WORKS		40	27-Jul-26	17-Aug-26	20-Aug-26 A	08-Oct-26	19,745.64	7,240.07	19,745.64	100%	36.67%	-23
PG-T-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26	03-Aug-26	20-Aug-26 A	27-Sep-26	6,581.88	5,594.60	6,581.88	100%	85%	-24
PG-T-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-26	10-Aug-26	20-Sep-26 A	01-Oct-26	6,581.88	1,645.47	6,581.88	100%	25%	-4
PG-T-CON-EXGN-FN-50	Installation of Gates	6	11-Aug-26	17-Aug-26	01-Oct-26	08-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		67	01-Jul-26	10-Aug-26	12-Jul-26 A	19-Oct-26	206,336.28	164,628.01	206,336.28	100%	79.79%	-50
STORM WATER AND UTILITY WORK		44	01-Jul-26	04-Aug-26	20-Aug-26 A	13-Oct-26	22,092.00	6,555.00	22,092.00	100%	29.67%	-16
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	27-Sep-26	5,160.00	3,870.00	5,160.00	100%	75%	-26
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	30-Sep-26	10,740.00	2,685.00	10,740.00	100%	25%	-4
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	30-Sep-26	04-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	04-Oct-26	07-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	08-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	08-Oct-26	183,926.34	158,073.01	183,926.34	100%	85.94%	-61
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	07-Oct-26	34,712.34	31,241.11	34,712.34	100%	90%	-70
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	08-Oct-26	90,915.00	77,277.75	90,915.00	100%	85%	-35
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	08-Oct-26	58,299.00	49,554.15	58,299.00	100%	85%	-37
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	13-Oct-26	19-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	13-Oct-26	19-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		110	25-Jun-26	07-Nov-26	20-Aug-26 A	30-Dec-26	174,621.94	69,235.21	239,107.30	73.03%	28.96%	3
POWER, LIGHTING & GROUNDING		76	25-Jun-26	27-Sep-26	20-Aug-26 A	19-Nov-26	174,621.94	64,920.61	182,037.10	95.93%	35.66%	2
PG-T-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	01-Oct-26	55,696.90	41,772.67	55,696.90	100%	75%	-14
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	21-Oct-26	8,265.00	7,025.25	8,265.00	100%	85%	-44
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	26-Oct-26	4,586.70	458.67	4,586.70	100%	10%	-28
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	02-Nov-26	17,397.90	1,739.79	17,397.90	100%	10%	-32
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	08-Nov-26	69,621.12	13,924.22	69,621.12	100%	20%	-38
PG-T-CON-EXGN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	08-Nov-26	12-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-T-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	6	20-Sep-26	27-Sep-26	12-Nov-26	19-Nov-26	14,830.32	0.00	22,245.48	66.67%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	16-Dec-26	0.00	4,314.60	43,146.00	0%	10%	-47
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	23-Nov-26	0.00	61.98	619.80	0%	10%	-49
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	26-Nov-26	0.00	61.98	619.80	0%	10%	-52
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	30-Nov-26	0.00	371.88	3,718.80	0%	10%	-55
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	05-Dec-26	0.00	1,524.91	15,249.12	0%	10%	-58
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	08-Dec-26	0.00	144.65	1,446.48	0%	10%	-62
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	13-Dec-26	0.00	661.20	6,612.00	0%	10%	-65
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	16-Dec-26	0.00	1,488.00	14,880.00	0%	10%	-69
FIRE ALARM SYSTEM		32	01-Oct-26	07-Nov-26	23-Nov-26	30-Dec-26	0.00	0.00	13,924.20	0%	0%	0
PG-T-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	01-Oct-26	10-Oct-26	23-Nov-26	02-Dec-26	0.00	0.00	1,983.60	0%	0%	0
PG-T-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26	19-Oct-26	02-Dec-26	12-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-T-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26	28-Oct-26	12-Dec-26	21-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-T-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26	07-Nov-26	21-Dec-26	30-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		14	27-Oct-26	11-Nov-26	20-Aug-26 A	30-Dec-26	0.00	10,934.40	27,343.80	0%	39.99%	-98
PG-T-CON-EXGN-PR-10	Installation of Parking Accessories	7	27-Oct-26	03-Nov-26	20-Aug-26 A	17-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-94
PG-T-CON-EXGN-PR-30	Marking & Signages	7	04-Nov-26	11-Nov-26	22-Dec-26	30-Dec-26	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		24	12-Nov-26	14-Dec-26	14-Aug-26 A	20-Jan-27	0.00	1,897.20	5,208.00	0%	36.43%	-107
PG-T-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	30-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-107
PG-T-CON-EXGN-SC-30	Connection to City Network	10	24-Nov-26	05-Dec-26	30-Dec-26	11-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-T-CON-EXGN-SC-40	Backfilling	8	06-Dec-26	14-Dec-26	11-Jan-27	20-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		38	28-Sep-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	167,072.72	252,665.10	0%	66.12%	-74
HARDSCAPE WORK		38	28-Sep-26	22-Nov-26	30-Jul-26 A	02-Dec-26	0.00	131,401.52	170,003.10	0%	77.29%	-58
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	07-Nov-26	0.00	51,836.40	60,984.00	0%	85%	-51
PG-T-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26	20-Oct-26	30-Jul-26 A	07-Nov-26	0.00	39,123.00	43,470.00	0%	90%	-75
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	23-Nov-26	0.00	39,089.12	60,137.10	0%	65%	-89
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	02-Dec-26	0.00	1,353.00	5,412.00	0%	25%	-49
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	35,671.20	82,662.00	0%	43.15%	-84

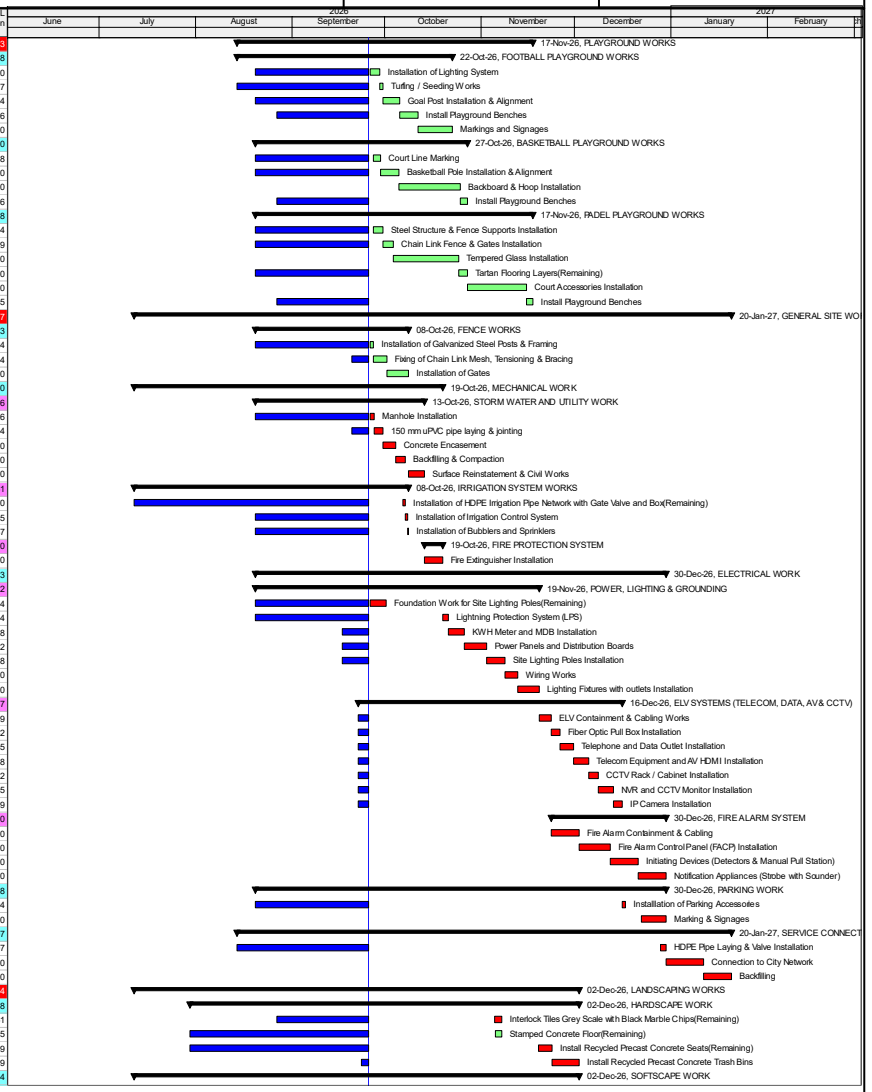


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 27-Sep-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	19-Nov-26	0.00	4,612.20	46,122.00	0%	10%	-37
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-2	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	31,059.00	36,540.00	0%	85%	-116
TANK WORKS		69	07-Jul-26	27-Sep-26	14-Aug-26 A	04-Nov-26	26,436.96	0.00	40,322.16	65.56%	0%	0
SEPTIC TANK		64	07-Jul-26	26-Aug-26	14-Aug-26 A	29-Oct-26	5,609.16	0.00	5,609.16	100%	0%	-21
PG-T-CON-EXTW-ST-40	RCC Wall	9	07-Jul-26	16-Jul-26	14-Aug-26 A	05-Oct-26	2,757.60	0.00	2,757.60	100%	0%	-35
PG-T-CON-EXTW-ST-50	RCC Slab	13	18-Jul-26	01-Aug-26	20-Aug-26 A	20-Oct-26	2,599.38	0.00	2,599.38	100%	0%	-39
PG-T-CON-EXTW-ST-60	Finishing Work	8	18-Aug-2	26-Aug-26	21-Oct-26	29-Oct-26	252.18	0.00	252.18	100%	0%	0
WATER STORAGE TANK		5	21-Sep-2	27-Sep-26	31-Oct-26	04-Nov-26	20,827.80	0.00	34,713.00	60%	0%	0
PG-T-CON-EXTW-4R-40	GRP Water Tank Installation	5	21-Sep-2	27-Sep-26	31-Oct-26	04-Nov-26	20,827.80	0.00	34,713.00	60%	0%	0
AIR DOME CONSTRUCTION		85	26-Aug-2	03-Dec-26	07-Oct-26	14-Jan-27	876,709.01	0.00	2,967,347.81	29.55%	0%	0
CIVIL WORK		17	26-Aug-2	14-Sep-26	07-Oct-26	27-Oct-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-2	05-Sep-26	07-Oct-26	18-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-80	Installation of Membrane System	8	06-Sep-2	14-Sep-26	18-Oct-26	27-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		25	05-Nov-2	03-Dec-26	16-Dec-26	14-Jan-27	0.00	0.00	712,953.22	0%	0%	0
PG-T-CON-EXAD-AR-10	Installation of Thermal Insulation System	7	05-Nov-2	12-Nov-26	16-Dec-26	24-Dec-26	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-40	Final Fixing of Acessories & Finishes	7	14-Nov-2	21-Nov-26	24-Dec-26	02-Jan-27	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-AR-20	Installation of Doors & Access Systems	6	22-Nov-2	28-Nov-26	02-Jan-27	09-Jan-27	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-30	Installation of Logo	5	29-Nov-2	03-Dec-26	09-Jan-27	14-Jan-27	0.00	0.00	3,236.40	0%	0%	0
MECHANICAL WORK		23	15-Sep-2	12-Oct-26	27-Oct-26	23-Nov-26	375,732.43	0.00	667,968.77	56.25%	0%	0
PG-T-CON-EXAD-ME-10	Installation of Main Air Package Units	5	15-Sep-2	20-Sep-26	27-Oct-26	02-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-ME-20	Installation of Backup Air Packag e Unit	5	21-Sep-2	27-Sep-26	02-Nov-26	08-Nov-26	125,244.14	0.00	208,740.24	60%	0%	0
PG-T-CON-EXAD-ME-30	Installation of Complete HVAC System	6	06-Oct-26	12-Oct-26	16-Nov-26	23-Nov-26	0.00	0.00	208,740.24	0%	0%	0
ELECTRICAL WORK		33	28-Sep-2	04-Nov-26	08-Nov-26	16-Dec-26	0.00	0.00	1,085,449.25	0%	0%	0
PG-T-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	7	28-Sep-2	05-Oct-26	08-Nov-26	16-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-20	Installation of Lighting System	7	06-Oct-26	13-Oct-26	16-Nov-26	24-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	14-Oct-26	19-Oct-26	24-Nov-26	30-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-40	Installation of Backup Generator	6	20-Oct-26	26-Oct-26	30-Nov-26	07-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-50	Installation of Smart Dome System	8	27-Oct-26	04-Nov-26	07-Dec-26	16-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		16	31-Aug-2	28-Oct-26	19-Sep-26 A	20-Oct-26	39,591.72	27,212.24	62,352.18	63.5%	43.64%	24
CIVIL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	19-Oct-26	0.00	4,692.63	14,939.40	0%	31.41%	-11
ARCHITECTURAL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	19-Oct-26	0.00	4,692.63	14,939.40	0%	31.41%	-11
WET AREA FINISHES		2	11-Oct-26	12-Oct-26	23-Sep-26 A	17-Oct-26	0.00	1,340.40	5,361.60	0%	25%	-17
PG-T-CON-BARW F-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	17-Oct-26	0.00	1,340.40	5,361.60	0%	25%	-17
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	19-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-22
PG-T-CON-BARRF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	19-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-22
MEP WORK		16	31-Aug-2	28-Oct-26	20-Sep-26 A	20-Oct-26	39,591.72	22,519.61	47,412.78	83.5%	47.5%	24
MECANICAL WORKS		16	31-Aug-2	28-Oct-26	20-Sep-26 A	20-Oct-26	39,591.72	22,519.61	47,412.78	83.5%	47.5%	24
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	20-Oct-26	0.00	34.07	136.26	0%	25%	-21
PG-T-CON-BGF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	20-Oct-26	0.00	34.07	136.26	0%	25%	-21
SEWER AND DRAINAGE SYSTEM		2	03-Sep-2	05-Sep-26	23-Sep-26 A	05-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-8
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-2	05-Sep-26	23-Sep-26 A	05-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-8
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	06-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-12
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	06-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-12
WATER SUPPLY SYSTEM		3	31-Aug-2	02-Sep-26	23-Sep-26 A	04-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-6
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-2	02-Sep-26	23-Sep-26 A	04-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-6
PROJECT CLOSOUT		148	22-Nov-2	16-Dec-26	06-Aug-26 A	27-Jan-27	0.00	160,712.88	1,101,706.70	0%	14.59%	-127
PG-T-PCL-20	As-Built Drawings	15	22-Nov-2	09-Dec-26	23-Sep-26 A	21-Jan-27	0.00	22,715.60	113,578.01	0%	20%	-87
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-2	03-Dec-26	06-Aug-26 A	14-Jan-27	0.00	137,997.28	306,660.63	0%	45%	-127
PG-T-PCL-30	Snag list Submission	2	05-Dec-2	06-Dec-26	14-Jan-27	17-Jan-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-40	Snag list Closeout	7	07-Dec-2	14-Dec-26	17-Jan-27	25-Jan-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-50	Issuing Approvals	1	15-Dec-2	15-Dec-26	25-Jan-27	26-Jan-27	0.00	0.00	113,578.01	0%	0%	0
PG-T-PCL-60	Handing Over	1	16-Dec-2	16-Dec-26	26-Jan-27	27-Jan-27	0.00	0.00	113,578.01	0%	0%	0

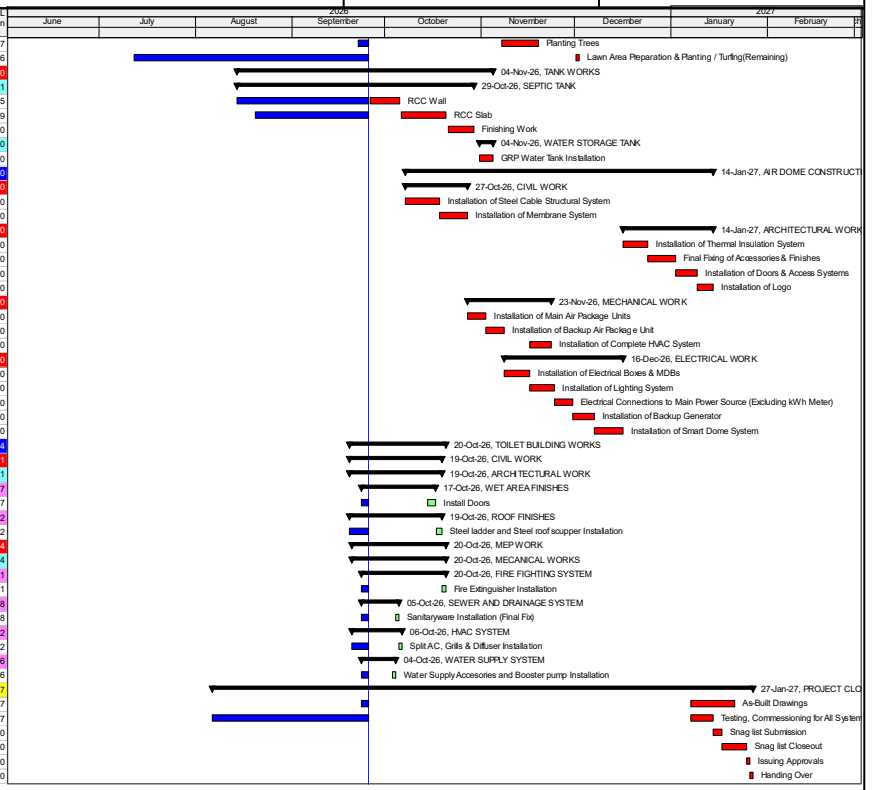

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
