
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026		162	25-Jun-26	15-Dec-26	01-Jul-26 A	08-Feb-27	10,800,089.08	8,582,617.64	12,683,975.77	83.57%	67.67%	-42
MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Dec-26	0.00	0.00	0.00	0%	0%	5
GENERAL MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Dec-26	0.00	0.00	0.00	0%	0%	5
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Dec-26	0.00	0.00	0.00	72.97%	73%	5
CONTRACUAL MILESTONES		0	28-Oct-26	28-Oct-26	12-Nov-26	12-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26		12-Nov-26	0.00	0.00	0.00	100%	0%	0
QASSIM		138	25-Jun-26	14-Dec-26	30-Jul-26 A	06-Feb-27	4,863,690.46	3,979,729.21	6,013,343.52	80.88%	66.18%	-15
ENGINEERING		37	25-Jun-26	04-Aug-26	30-Jul-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-47
SHOP DRAWINGS SUBMITTALS		35	25-Jun-26	04-Aug-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-45
MECHANICAL DRAWINGS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-62
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-62
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	100%	90%	-62
ELECTRICAL DRAWINGS		17	16-Jul-26	04-Aug-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-63
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-63
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	31-Oct-26	0.00	0.00	0.00	100%	90%	-69
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	100%	90%	-65
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	100%	90%	-63
SHOP DRAWINGS APPROVALS		10	16-Jul-26	27-Jul-26	20-Aug-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-54
MECHANICAL DRAWINGS		10	16-Jul-26	27-Jul-26	20-Aug-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-54
AIR DOME		10	16-Jul-26	27-Jul-26	20-Aug-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-54
PG-Q-EN-ME-SD-AP-100	Air Package and HVAC System Drawings	10	16-Jul-26	27-Jul-26	20-Aug-26 A	03-Nov-26	0.00	0.00	0.00	100%	80%	-54
PROCUREMENT		92	25-Jun-26	27-Aug-26	14-Aug-26 A	05-Nov-26	2,532,361.21	2,103,626.26	2,532,361.21	100%	83.07%	-16
LONG LEAD ITEMS		85	07-Jul-26	27-Aug-26	14-Aug-26 A	05-Nov-26	2,378,642.27	1,965,279.21	2,378,642.27	100%	82.62%	-26
DELIVERY TO SITE		85	07-Jul-26	27-Aug-26	14-Aug-26 A	05-Nov-26	2,378,642.27	1,965,279.21	2,378,642.27	100%	82.62%	-26
EXTERNAL / LANDSCAPE WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	01-Nov-26	14,428.69	12,985.82	14,428.69	100%	90%	-52
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	01-Nov-26	14,428.69	12,985.82	14,428.69	100%	90%	-52
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	05-Nov-26	2,119,264.56	1,731,502.01	2,119,264.56	100%	81.7%	-35
PG-Q-PR-LL-SP-DL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	31-Oct-26	26,778.60	25,439.67	26,778.60	100%	95%	-51
PG-Q-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	31-Oct-26	46,985.40	44,636.13	46,985.40	100%	95%	-51
PG-Q-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	31-Oct-26	10,152.00	9,644.40	10,152.00	100%	95%	-51
PG-Q-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	31-Oct-26	156,686.40	148,852.08	156,686.40	100%	95%	-51
PG-Q-PR-LL-SP-DL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	29-Oct-26 A	05-Nov-26	1,878,662.16	1,502,929.73	1,878,662.16	100%	80%	3
METAL WORK		15	25-Jul-26	10-Aug-26	05-Oct-26 A	04-Nov-26	3,427.65	2,399.36	3,427.65	100%	70%	-12
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26	10-Aug-26	05-Oct-26 A	04-Nov-26	3,427.65	2,399.36	3,427.65	100%	70%	-12
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	31-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-52
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	31-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-52
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	01-Nov-26	221,065.50	198,958.95	221,065.50	100%	90%	-42
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	31-Oct-26	1,785.24	1,606.72	1,785.24	100%	90%	-56
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Nov-26	3,124.17	2,811.75	3,124.17	100%	90%	-52
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Nov-26	182,755.44	164,479.90	182,755.44	100%	90%	-52
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	01-Nov-26	8,081.83	7,273.65	8,081.83	100%	90%	-52
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Nov-26	6,326.40	5,693.76	6,326.40	100%	90%	-41
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Nov-26	6,170.09	5,553.08	6,170.09	100%	90%	-41
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Nov-26	7,811.37	7,030.23	7,811.37	100%	90%	-41
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	01-Nov-26	5,010.96	4,509.86	5,010.96	100%	90%	-41
SHORT LEAD ITEMS		49	25-Jun-26	12-Jul-26	14-Aug-26 A	01-Nov-26	153,718.94	138,347.04	153,718.94	100%	90%	-52
DELIVERY TO SITE		49	25-Jun-26	12-Jul-26	14-Aug-26 A	01-Nov-26	153,718.94	138,347.04	153,718.94	100%	90%	-52
EXTERNAL / LANDSCAPE WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	01-Nov-26	78,553.04	70,697.74	78,553.04	100%	90%	-43
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	01-Nov-26	1,892.27	1,703.04	1,892.27	100%	90%	-43
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	01-Nov-26	714.10	642.69	714.10	100%	90%	-43
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	01-Nov-26	34,366.68	30,930.01	34,366.68	100%	90%	-43
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	01-Nov-26	41,580.00	37,422.00	41,580.00	100%	90%	-43
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	01-Nov-26	1,724.00	1,551.60	1,724.00	100%	90%	-19
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	01-Nov-26	1,302.70	1,172.43	1,302.70	100%	90%	-19
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	01-Nov-26	112.75	101.48	112.75	100%	90%	-19
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	01-Nov-26	308.56	277.70	308.56	100%	90%	-19
IRRIGATION WORK		18	25-Jun-26	08-Jul-26	14-Aug-26 A	01-Nov-26	71,118.65	64,006.78	71,118.65	100%	90%	-54
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	01-Nov-26	7,186.00	6,467.40	7,186.00	100%	90%	-54
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Sprayers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	01-Nov-26	63,932.65	57,539.39	63,932.65	100%	90%	-49
ELECTRICAL WORK		15	25-Jun-26	12-Jul-26	26-Sep-26 A	01-Nov-26	2,200.61	1,980.55	2,200.61	100%	90%	-17
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26 A	01-Nov-26	2,200.61	1,980.55	2,200.61	100%	90%	-17
FIRE FIGHTING WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	01-Nov-26	122.63	110.37	122.63	100%	90%	-19
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	01-Nov-26	122.63	110.37	122.63	100%	90%	-19
CONSTRUCTION STAGE		121	05-Jul-26	14-Dec-26	06-Aug-26 A	12-Jan-27	2,331,329.25	1,486,769.56	2,832,093.32	82.32%	52.5%	3
PLAYGROUND AND LANDSCAPING WORKS		121	05-Jul-26	14-Dec-26	06-Aug-26 A	16-Dec-26	1,261,969.50	1,195,328.75	1,606,178.40	78.57%	74.42%	27
PLAYGROUND WORKS		103	11-Aug-26	02-Dec-26	06-Aug-26 A	03-Dec-26	272,962.09	259,374.95	325,784.34	83.79%	79.62%	-4
FOOTBALL PLAYGROUND WORKS		72	19-Aug-26	17-Nov-26	14-Aug-26 A	15-Nov-26	84,618.17	82,739.63	109,254.66	77.45%	75.73%	-2
PG-Q-CON-EX-FB-120	Installation of Lighting System	12	19-Aug-26	01-Sep-26	20-Aug-26 A	01-Nov-26	24,360.00	21,924.00	24,360.00	100%	90%	-49
PG-Q-CON-EX-FB-90	Turfing / Seeding Works	10	02-Sep-26	13-Sep-26	14-Aug-26 A	03-Nov-26	23,667.00	18,933.60	23,667.00	100%	80%	-58
PG-Q-CON-EX-FB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	07-Nov-26	35,500.50	28,400.40	35,500.50	100%	80%	-45
PG-Q-CON-EX-FB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	10-Nov-26	1,090.67	1,648.13	2,060.16	52.94%	80%	-47

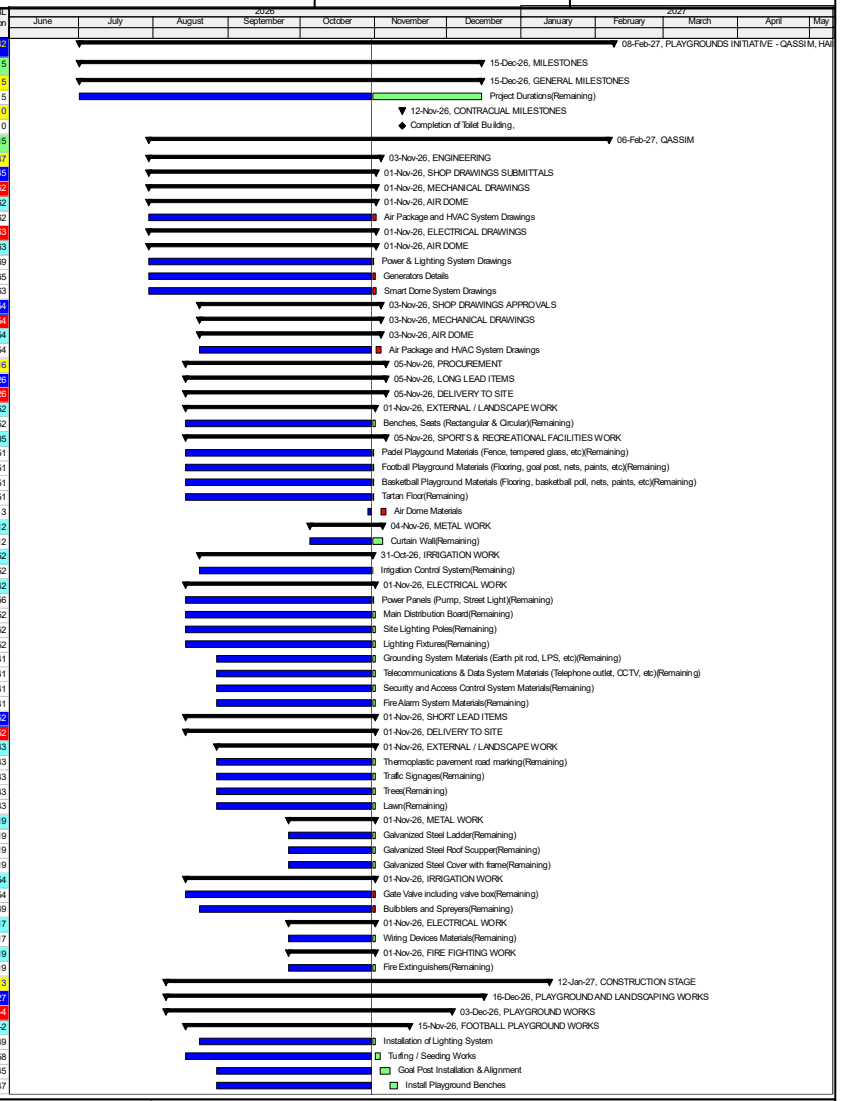

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00


PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EX-FB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	25-Oct-26 A	15-Nov-26	0.00	11,833.50	23,667.00	0%	50%	-11
BASKETBALL PLAYGROUND WORKS		70	31-Aug-26	17-Nov-26	20-Aug-26 A	16-Nov-26	41,827.28	34,560.58	43,200.72	96.82%	80%	-7
PG-Q-CON-EX-BB-80	Court Line Marking	15	31-Aug-26	16-Sep-26	20-Aug-26 A	03-Nov-26	13,091.76	10,473.41	13,091.76	100%	80%	-49
PG-Q-CON-EX-BB-60	Basketball Pole Installation & Alignment	17	17-Sep-26	07-Oct-26	20-Aug-26 A	08-Nov-26	15,472.08	12,377.66	15,472.08	100%	80%	-50
PG-Q-CON-EX-BB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	01-Oct-26 A	11-Nov-26	13,091.76	10,473.41	13,091.76	100%	80%	-18
PG-Q-CON-EX-BB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	27-Sep-26 A	16-Nov-26	171.68	1,236.10	1,545.12	11.11%	80%	-25
PADEL PLAYGROUND WORKS		93	11-Aug-26	02-Dec-26	06-Aug-26 A	03-Dec-26	146,516.64	142,074.74	173,328.96	84.53%	81.97%	-4
PG-Q-CON-EX-PD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26	31-Aug-26	20-Aug-26 A	04-Nov-26	3,534.96	2,827.97	3,534.96	100%	80%	-46
PG-Q-CON-EX-PD-60	Chain Link Fence & Gates Installation	16	01-Sep-26	19-Sep-26	20-Aug-26 A	08-Nov-26	5,302.44	4,241.95	5,302.44	100%	80%	-52
PG-Q-CON-EX-PD-50	Tempered Glass Installation	17	20-Sep-26	10-Oct-26	12-Oct-26 A	16-Nov-26	5,302.44	3,181.46	5,302.44	100%	60%	-13
PG-Q-CON-EX-PD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	16-Nov-26	130,572.00	117,514.80	130,572.00	100%	90%	-70
PG-Q-CON-EX-PD-70	Court Accessories Installation	15	29-Oct-26	15-Nov-26	22-Oct-26 A	24-Nov-26	1,804.80	13,536.00	27,072.00	6.67%	50%	-14
PG-Q-CON-EX-PD-80	Install Playground Benches	15	16-Nov-26	02-Dec-26	25-Oct-26 A	03-Dec-26	0.00	772.56	1,545.12	0%	50%	-19
GENERAL SITE WORKS		119	05-Jul-26	28-Nov-26	14-Aug-26 A	16-Dec-26	798,754.41	617,067.36	815,765.76	97.91%	75.64%	20
MECHANICAL WORK		79	05-Jul-26	16-Aug-26	20-Aug-26 A	24-Nov-26	348,762.60	275,543.28	348,762.60	100%	79.01%	-44
STORM WATER AND UTILITY WORK		79	05-Jul-26	16-Aug-26	20-Aug-26 A	24-Nov-26	21,060.00	13,381.20	21,060.00	100%	63.54%	-44
PG-Q-CON-EX-GNM-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	31-Oct-26	4,128.00	3,715.20	4,128.00	100%	90%	-55
PG-Q-CON-EX-GNM-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	01-Nov-26	10,740.00	9,666.00	10,740.00	100%	90%	-55
PG-Q-CON-EX-GNM-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	01-Nov-26	09-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GNM-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	09-Nov-26	16-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GNM-70	Surface Reinstatement & Civil Works	6	10-Aug-26	16-Aug-26	17-Nov-26	24-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		5	03-Aug-26	09-Aug-26	20-Aug-26 A	17-Nov-26	327,702.60	262,162.08	327,702.60	100%	80%	-69
PG-Q-CON-EX-GNM-90	Installation of Irrigation Control System	3	03-Aug-26	05-Aug-26	20-Aug-26 A	16-Nov-26	90,915.00	72,732.00	90,915.00	100%	80%	-72
PG-Q-CON-EX-GNM-100	Installation of Bubblers and Sprinklers	3	06-Aug-26	09-Aug-26	27-Aug-26 A	17-Nov-26	236,787.60	189,430.08	236,787.60	100%	80%	-66
ELECTRICAL WORK		82	13-Aug-26	01-Nov-26	20-Aug-26 A	15-Dec-26	449,991.81	332,275.38	450,291.36	99.93%	73.79%	-32
POWER, LIGHTING & GROUNDING		47	13-Aug-26	20-Sep-26	20-Aug-26 A	03-Dec-26	393,221.16	292,326.24	393,221.16	100%	74.34%	-56
PG-Q-CON-EX-GNE-20_R	Foundation Wok for Site Lighting Poles(Remaining)	4	13-Aug-26	17-Aug-26	20-Aug-26 A	25-Nov-26	162,449.28	129,959.42	162,449.28	100%	80%	-78
PG-Q-CON-EX-GNE-30	Lightning Protection System (LPS)	3	29-Aug-26	31-Aug-26	27-Aug-26 A	26-Nov-26	8,265.00	6,612.00	8,265.00	100%	80%	-75
PG-Q-CON-EX-GNE-40	KWH Meter and MDB Installation	2	01-Sep-26	02-Sep-26	13-Oct-26 A	28-Nov-26	4,586.70	3,210.69	4,586.70	100%	70%	-38
PG-Q-CON-EX-GNE-50	Power Panels and Distribution Boards	5	03-Sep-26	08-Sep-26	14-Oct-26 A	30-Nov-26	17,397.90	12,178.53	17,397.90	100%	70%	-35
PG-Q-CON-EX-GNE-60	Site Lighting Poles Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	30-Nov-26	174,052.80	121,836.96	174,052.80	100%	70%	-84
PG-Q-CON-EX-GNE-70	Wiring Works	3	13-Sep-26	15-Sep-26	10-Oct-26 A	01-Dec-26	4,224.00	2,956.80	4,224.00	100%	70%	-43
PG-Q-CON-EX-GNE-80	Lighting Fixtures with outlets Installation	4	16-Sep-26	20-Sep-26	12-Oct-26 A	03-Dec-26	22,245.48	15,571.84	22,245.48	100%	70%	-41
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-26	20-Oct-26	07-Oct-26 A	12-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-32
PG-Q-CON-EX-GNE-90	ELV Containment & Cabling Works	3	21-Sep-26	24-Sep-26	07-Oct-26 A	03-Dec-26	619.80	433.86	619.80	100%	70%	-47
PG-Q-CON-EX-GNE-100	Fiber Optic Pull Box Installation	3	26-Sep-26	28-Sep-26	10-Oct-26 A	05-Dec-26	619.80	433.86	619.80	100%	70%	-46
PG-Q-CON-EX-GNE-110	Telephone and Data Outlet Installation	4	29-Sep-26	03-Oct-26	10-Oct-26 A	07-Dec-26	3,718.80	2,603.16	3,718.80	100%	70%	-46
PG-Q-CON-EX-GNE-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26	07-Oct-26	12-Oct-26 A	08-Dec-26	15,249.12	10,674.38	15,249.12	100%	70%	-45
PG-Q-CON-EX-GNE-130	CCTV Rack / Cabinet Installation	4	08-Oct-26	12-Oct-26	11-Oct-26 A	09-Dec-26	1,446.48	1,012.54	1,446.48	100%	70%	-48
PG-Q-CON-EX-GNE-140	NVR and CCTV Monitor Installation	4	13-Oct-26	17-Oct-26	13-Oct-26 A	10-Dec-26	6,612.00	4,628.40	6,612.00	100%	70%	-47
PG-Q-CON-EX-GNE-150	IP Camera Installation	3	18-Oct-26	20-Oct-26	14-Oct-26 A	12-Dec-26	14,880.00	10,416.00	14,880.00	100%	70%	-48
FIRE ALARM SYSTEM		32	26-Sep-26	01-Nov-26	11-Oct-26 A	15-Dec-26	13,624.65	9,746.94	13,924.20	97.85%	70%	-25
PG-Q-CON-EX-GNE-160	Fire Alarm Containment & Cabling	8	26-Sep-26	04-Oct-26	11-Oct-26 A	07-Dec-26	1,983.60	1,388.52	1,983.60	100%	70%	-41
PG-Q-CON-EX-GNE-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26	13-Oct-26	12-Oct-26 A	09-Dec-26	2,644.80	1,851.36	2,644.80	100%	70%	-43
PG-Q-CON-EX-GNE-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26	22-Oct-26	13-Oct-26 A	13-Dec-26	8,097.60	5,668.32	8,097.60	100%	70%	-44
PG-Q-CON-EX-GNE-190	Notification Appliances (Strobe with Sounder)	8	24-Oct-26	01-Nov-26	15-Oct-26 A	15-Dec-26	898.65	838.74	1,198.20	75%	70%	-45
PARKING WORK		5	04-Nov-26	09-Nov-26	27-Oct-26 A	15-Dec-26	0.00	7,239.90	14,479.80	0%	50%	-38
PG-Q-CON-EX-GN-PR-30	Marking & Signages	5	04-Nov-26	09-Nov-26	27-Oct-26 A	15-Dec-26	0.00	7,239.90	14,479.80	0%	50%	-38
SERVICE CONNECTION		8	19-Nov-26	28-Nov-26	14-Aug-26 A	16-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-97
PG-Q-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-26	28-Nov-26	14-Aug-26 A	16-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-97
LANDSCAPING WORKS		58	30-Sep-26	14-Dec-26	20-Aug-26 A	23-Nov-26	155,540.00	291,116.04	429,915.30	36.18%	67.71%	-15
HARDSCAPE WORK		58	30-Sep-26	14-Dec-26	20-Aug-26 A	23-Nov-26	55,440.00	103,253.04	123,489.30	44.89%	83.61%	-15
PG-Q-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-26	14-Oct-26	27-Aug-26 A	02-Nov-26	55,440.00	49,896.00	55,440.00	100%	90%	-44
PG-Q-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-26	02-Dec-26	20-Aug-26 A	18-Nov-26	0.00	50,109.84	62,637.30	0%	80%	-66
PG-Q-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-26	14-Dec-26	12-Oct-26 A	23-Nov-26	0.00	3,247.20	5,412.00	0%	60%	-26
SOFTSCAPE WORK		31	15-Oct-26	21-Nov-26	27-Aug-26 A	16-Nov-26	100,100.00	187,863.00	306,426.00	32.67%	61.31%	-36
PG-Q-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	05-Nov-26	100,100.00	92,400.00	115,500.00	86.67%	80%	-45
PG-Q-CON-EX-LS-SS-10	Planting Trees	17	02-Nov-26	21-Nov-26	25-Oct-26 A	16-Nov-26	0.00	95,463.00	190,926.00	0%	50%	-2
TANK WORKS		8	11-Aug-26	19-Aug-26	14-Oct-26 A	01-Nov-26	34,713.00	27,770.40	34,713.00	100%	80%	-8
WATER STORAGE TANK		8	11-Aug-26	19-Aug-26	14-Oct-26 A	01-Nov-26	34,713.00	27,770.40	34,713.00	100%	80%	-8
PG-Q-CON-EX-TW-IR-40	GRP Water Tank Installation	8	11-Aug-26	19-Aug-26	14-Oct-26 A	01-Nov-26	34,713.00	27,770.40	34,713.00	100%	80%	-8
AIR DOME CONSTRUCTION		76	17-Aug-26	04-Nov-26	27-Aug-26 A	12-Jan-27	1,012,390.16	250,488.29	1,168,945.34	86.61%	21.43%	-50
CIVIL WORK		18	22-Aug-26	10-Sep-26	03-Nov-26	24-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-Q-CON-EX-AD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26	01-Sep-26	03-Nov-26	15-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EX-AD-CL-80	Installation of Membrane System	8	02-Sep-26	10-Sep-26	15-Nov-26	24-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		8	27-Oct-26	04-Nov-26	27-Aug-26 A	12-Jan-27	93,933.11	125,244.14	250,488.29	37.5%	50%	-110
PG-Q-CON-EX-AD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	12-Jan-27	93,933.11	125,244.14	250,488.29	37.5%	50%	-110
ELECTRICAL WORK		56	17-Aug-26	13-Sep-26	27-Aug-26 A	19-Nov-26	417,480.48	125,244.14	417,480.48	100%	30%	-48
PG-Q-CON-EX-AD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26	30-Aug-26	27-Aug-26 A	05-Nov-26	208,740.24	125,244.14	208,740.24	100%	60%	-48
PG-Q-CON-EX-AD-EL-20	Installation of Lighting System	12	31-Aug-26	13-Sep-26	05-Nov-26	19-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
TOILET BUILDING WORKS		39	20-Aug-26	20-Oct-26	20-Aug-26 A	07-Nov-26	56,969.58	40,952.53	56,969.58	100%	71.88%	-14

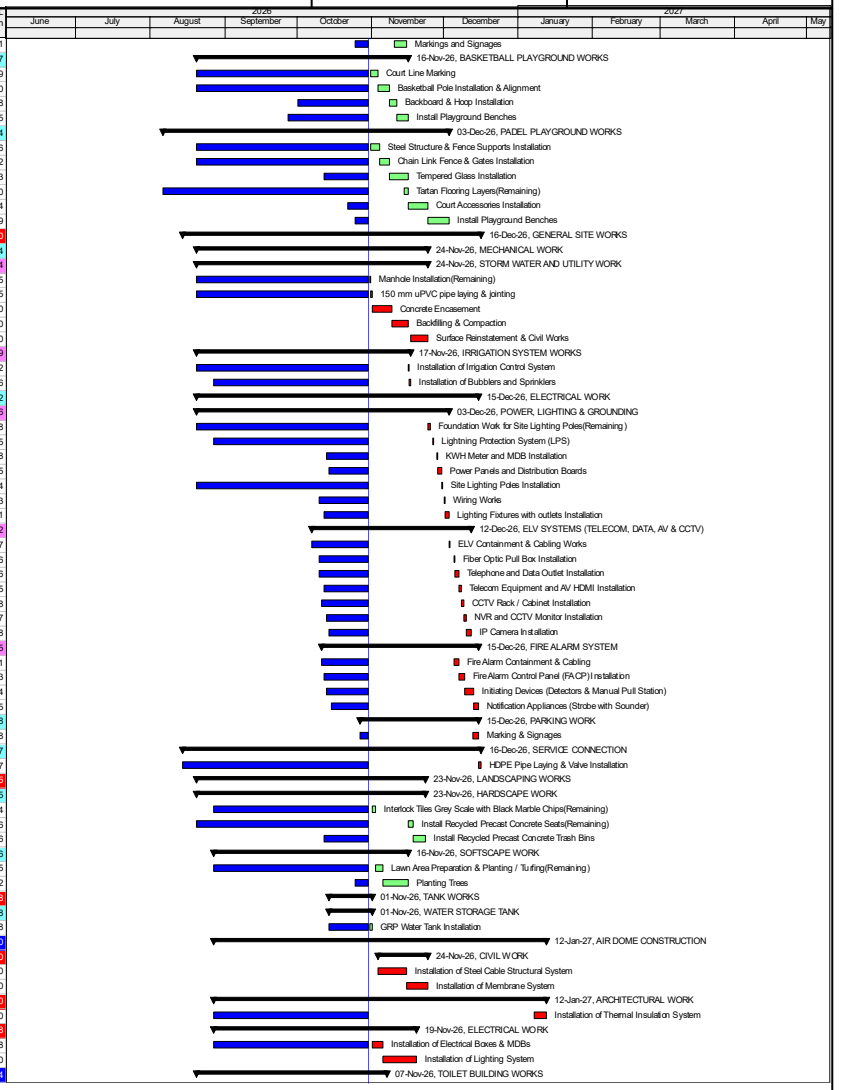


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
CIVIL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	05-Nov-26	45,922.80	33,219.78	45,922.80	100%	72.34%	-54
ARCHITECTURAL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	05-Nov-26	45,922.80	33,219.78	45,922.80	100%	72.34%	-54
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	05-Nov-26	20,825.40	14,577.78	20,825.40	100%	70%	-50
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	03-Nov-26	13,273.80	9,291.66	13,273.80	100%	70%	-53
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	19-Sep-26 A	05-Nov-26	7,551.60	5,286.12	7,551.60	100%	70%	-36
WET AREA FINISHES		5	08-Oct-26	13-Oct-26	01-Oct-26 A	03-Nov-26	5,361.60	3,753.12	5,361.60	100%	70%	-23
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	01-Oct-26 A	03-Nov-26	5,361.60	3,753.12	5,361.60	100%	70%	-23
ROOF FINISHES		14	06-Oct-26	19-Oct-26	20-Aug-26 A	05-Nov-26	19,735.80	14,888.88	19,735.80	100%	75.44%	-54
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	02-Nov-26	10,158.00	9,142.20	10,158.00	100%	90%	-57
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26	19-Oct-26	14-Oct-26 A	05-Nov-26	9,577.80	5,746.68	9,577.80	100%	60%	-19
MEP WORK		39	20-Aug-26	20-Oct-26	01-Oct-26 A	07-Nov-26	11,046.78	7,732.75	11,046.78	100%	70%	21
MECANICAL WORKS		39	20-Aug-26	20-Oct-26	01-Oct-26 A	07-Nov-26	11,046.78	7,732.75	11,046.78	100%	70%	21
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	01-Oct-26 A	07-Nov-26	136.26	95.38	136.26	100%	70%	-30
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	01-Oct-26 A	07-Nov-26	136.26	95.38	136.26	100%	70%	-30
SEWER AND DRAINAGE SYSTEM		2	01-Sep-26	02-Sep-26	01-Oct-26 A	02-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-25
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	01-Oct-26 A	02-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-25
HVAC SYSTEM		3	20-Aug-26	23-Aug-26	01-Oct-26 A	31-Oct-26	7,684.80	5,379.36	7,684.80	100%	70%	-23
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26	23-Aug-26	01-Oct-26 A	31-Oct-26	7,684.80	5,379.36	7,684.80	100%	70%	-23
PROJECT CLOSOUT		18	16-Nov-26	02-Dec-26	29-Oct-26 A	06-Feb-27	0.00	389,333.39	648,888.98	0%	60%	-70
PG-Q-PCL-20	As-Built Drawings	15	16-Nov-26	02-Dec-26	29-Oct-26 A	06-Feb-27	0.00	105,225.24	175,375.40	0%	60%	-70
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	16-Nov-26	26-Nov-26	29-Oct-26 A	03-Feb-27	0.00	284,108.15	473,513.58	0%	60%	-74
HAIL		130	25-Jun-26	03-Dec-26	09-Jul-26 A	20-Dec-26	2,046,495.47	1,837,443.37	2,382,684.76	85.89%	77.12%	-2
PROCUREMENT		48	04-Jul-26	26-Aug-26	20-Aug-26 A	02-Nov-26	233,418.94	209,665.73	233,418.94	100%	89.82%	-15
LONG LEAD ITEMS		48	25-Jul-26	26-Aug-26	20-Aug-26 A	02-Nov-26	177,157.99	159,030.87	177,157.99	100%	89.77%	-33
DELIVERY TO SITE		48	25-Jul-26	26-Aug-26	20-Aug-26 A	02-Nov-26	177,157.99	159,030.87	177,157.99	100%	89.77%	-33
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	02-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-44
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	02-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-44
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	01-Nov-26	173,044.81	155,740.33	173,044.81	100%	90%	-37
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	31-Oct-26	3,124.17	2,811.75	3,124.17	100%	90%	-47
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	31-Oct-26	2,499.34	2,249.40	2,499.34	100%	90%	-47
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	31-Oct-26	6,326.40	5,693.76	6,326.40	100%	90%	-47
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	01-Nov-26	134,020.66	120,618.59	134,020.66	100%	90%	-49
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	01-Nov-26	8,081.83	7,273.65	8,081.83	100%	90%	-49
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	01-Nov-26	6,170.09	5,553.08	6,170.09	100%	90%	-43
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	01-Nov-26	7,811.37	7,030.23	7,811.37	100%	90%	-43
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	01-Nov-26	5,010.96	4,509.86	5,010.96	100%	90%	-43
SHORT LEAD ITEMS		12	04-Jul-26	16-Jul-26	27-Aug-26 A	01-Nov-26	56,260.95	50,634.86	56,260.95	100%	90%	-43
DELIVERY TO SITE		12	04-Jul-26	16-Jul-26	27-Aug-26 A	01-Nov-26	56,260.95	50,634.86	56,260.95	100%	90%	-43
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	01-Nov-26	56,260.95	50,634.86	56,260.95	100%	90%	-43
PG-H-PR-SL-LS-DL-60_R	Trafic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	01-Nov-26	1,249.67	1,124.70	1,249.67	100%	90%	-43
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	01-Nov-26	30,441.29	27,397.16	30,441.29	100%	90%	-43
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	01-Nov-26	24,570.00	22,113.00	24,570.00	100%	90%	-43
CONSTRUCTION STAGE		130	25-Jun-26	26-Nov-26	09-Jul-26 A	20-Dec-26	1,813,076.53	1,476,492.36	1,897,123.69	95.57%	77.83%	-8
PLAYGROUND AND LANDSCAPING WORKS		127	25-Jun-26	26-Nov-26	09-Jul-26 A	20-Dec-26	1,648,644.31	1,364,362.30	1,732,691.47	95.15%	78.74%	-8
PLAYGROUND WORKS		65	18-Aug-26	17-Nov-26	06-Aug-26 A	23-Nov-26	454,957.74	400,012.32	480,684.90	94.65%	83.22%	-15
FOOTBALL PLAYGROUND WORKS		65	18-Aug-26	17-Nov-26	06-Aug-26 A	23-Nov-26	454,957.74	400,012.32	480,684.90	94.65%	83.22%	-15
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26	01-Sep-26	27-Aug-26 A	02-Nov-26	48,720.00	38,976.00	48,720.00	100%	80%	-44
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26	15-Sep-26	14-Aug-26 A	04-Nov-26	23,667.00	18,933.60	23,667.00	100%	80%	-58
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26	04-Oct-26	06-Aug-26 A	04-Nov-26	343,980.00	309,582.00	343,980.00	100%	90%	-62
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	08-Nov-26	35,500.50	28,400.40	35,500.50	100%	80%	-55
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	11-Nov-26	3,090.24	4,120.32	5,150.40	60%	80%	-50
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	11-Nov-26	23-Nov-26	0.00	0.00	23,667.00	0%	0%	0
GENERAL SITE WORKS		127	25-Jun-26	26-Nov-26	14-Aug-26 A	20-Dec-26	809,373.01	627,267.32	813,093.01	99.54%	77.15%	23
MECHANICAL WORK		78	25-Jun-26	06-Aug-26	14-Aug-26 A	16-Nov-26	344,669.34	282,172.04	344,669.34	100%	81.87%	-42
STORM WATER AND UTILITY WORK		78	25-Jun-26	04-Aug-26	14-Aug-26 A	15-Nov-26	23,124.00	14,164.80	23,124.00	100%	61.26%	-44
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	31-Oct-26	1,032.00	928.80	1,032.00	100%	90%	-56
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	01-Nov-26	5,160.00	4,644.00	5,160.00	100%	90%	-51
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	13-Oct-26 A	02-Nov-26	10,740.00	8,592.00	10,740.00	100%	80%	-13
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	02-Nov-26	05-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	05-Nov-26	09-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	10-Nov-26	15-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		46	21-Jul-26	30-Jul-26	14-Aug-26 A	10-Nov-26	321,227.40	267,816.48	321,227.40	100%	83.37%	-66
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	09-Nov-26	108,345.60	97,511.04	108,345.60	100%	90%	-70
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	09-Nov-26	90,915.00	72,732.00	90,915.00	100%	80%	-61
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	10-Oct-26 A	10-Nov-26	121,966.80	97,573.44	121,966.80	100%	80%	-25
FIRE PROTECTION SYSTEM		2	05-Aug-26	06-Aug-26	11-Oct-26 A	16-Nov-26	317.94	190.76	317.94	100%	60%	-29
PG-H-CON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-26	06-Aug-26	11-Oct-26 A	16-Nov-26	317.94	190.76	317.94	100%	60%	-29
ELECTRICAL WORK		89	05-Aug-26	20-Oct-26	20-Aug-26 A	05-Dec-26	360,557.47	264,303.18	360,557.47	100%	73.3%	-26
POWER, LIGHTING & GROUNDING		54	05-Aug-26	08-Sep-26	20-Aug-26 A	23-Nov-26	303,487.27	224,354.04	303,487.27	100%	73.93%	-50
PG-H-CON-EX-GN-E-20_R	Foundation Wok for Site Lighting Poles(Remaining)	4	05-Aug-26	09-Aug-26	20-Aug-26 A	16-Nov-26	119,129.47	95,303.58	119,129.47	100%	80%	-70
PG-H-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-26	19-Aug-26	10-Oct-26 A	17-Nov-26	8,265.00	5,785.50	8,265.00	100%	70%	-30

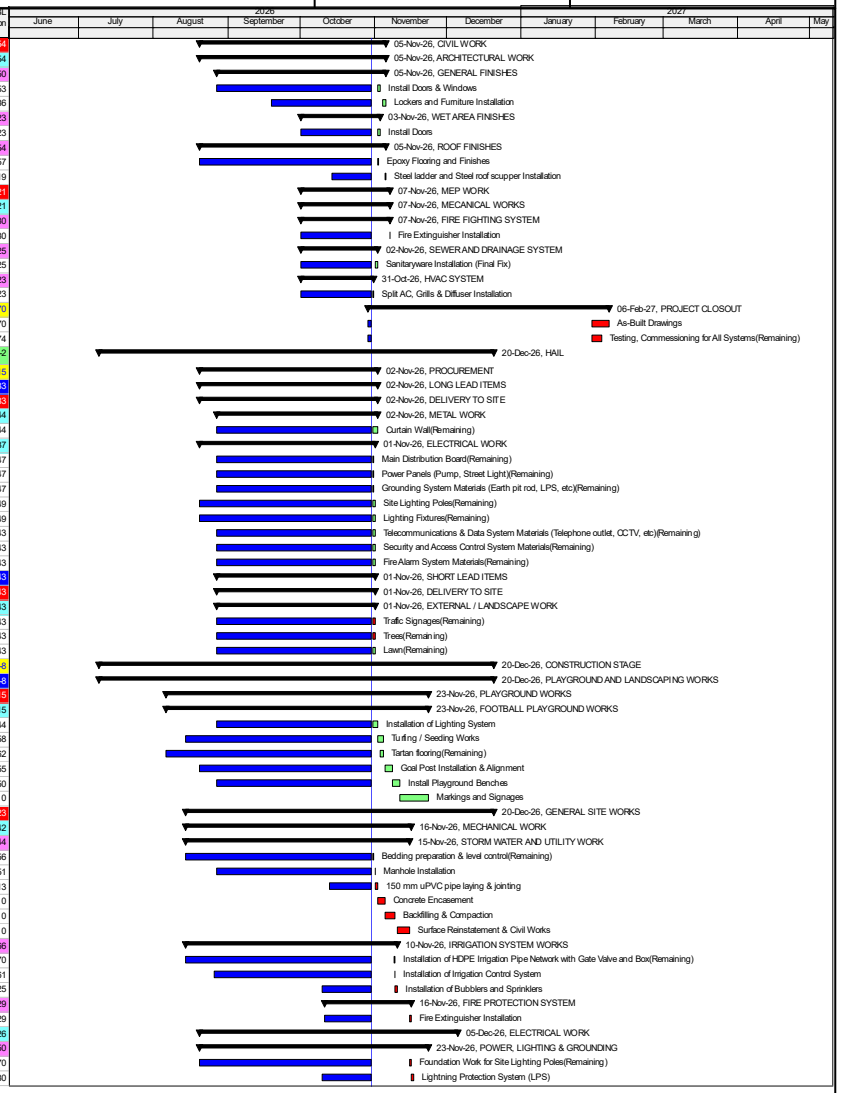


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-26	22-Aug-26	11-Oct-26 A	17-Nov-26	4,586.70	3,210.69	4,586.70	100%	70%	-31
PG-H-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-26	27-Aug-26	11-Oct-26 A	19-Nov-26	17,397.90	12,178.53	17,397.90	100%	70%	-29
PG-H-CON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-26	31-Aug-26	12-Oct-26 A	21-Nov-26	127,638.72	89,347.10	127,638.72	100%	70%	-31
PG-H-CON-EX-GN-E-70	Wiring Works	3	01-Sep-26	03-Sep-26	10-Oct-26 A	22-Nov-26	4,224.00	2,956.80	4,224.00	100%	70%	-34
PG-H-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-26	08-Sep-26	13-Oct-26 A	23-Nov-26	22,245.48	15,571.84	22,245.48	100%	70%	-31
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-26	08-Oct-26	10-Oct-26 A	01-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-21
PG-H-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-26	12-Sep-26	11-Oct-26 A	24-Nov-26	619.80	433.86	619.80	100%	70%	-35
PG-H-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-26	15-Sep-26	12-Oct-26 A	25-Nov-26	619.80	433.86	619.80	100%	70%	-35
PG-H-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-26	20-Sep-26	12-Oct-26 A	26-Nov-26	3,718.80	2,603.16	3,718.80	100%	70%	-35
PG-H-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-26	26-Sep-26	13-Oct-26 A	28-Nov-26	15,249.12	10,674.38	15,249.12	100%	70%	-36
PG-H-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-26	30-Sep-26	10-Oct-26 A	29-Nov-26	1,446.48	1,012.54	1,446.48	100%	70%	-40
PG-H-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-26	05-Oct-26	10-Oct-26 A	30-Nov-26	6,612.00	4,628.40	6,612.00	100%	70%	-41
PG-H-CON-EX-GN-E-150	IP Camera Installation	3	06-Oct-26	08-Oct-26	10-Oct-26 A	01-Dec-26	14,880.00	10,416.00	14,880.00	100%	70%	-43
FIRE ALARM SYSTEM		32	13-Sep-26	20-Oct-26	10-Oct-26 A	05-Dec-26	13,924.20	9,746.94	13,924.20	100%	70%	-17
PG-H-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-26	21-Sep-26	10-Oct-26 A	26-Nov-26	1,983.60	1,388.52	1,983.60	100%	70%	-34
PG-H-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-26	01-Oct-26	10-Oct-26 A	29-Nov-26	2,644.80	1,851.36	2,644.80	100%	70%	-36
PG-H-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-26	11-Oct-26	10-Oct-26 A	02-Dec-26	8,097.60	5,668.32	8,097.60	100%	70%	-38
PG-H-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-26	20-Oct-26	10-Oct-26 A	05-Dec-26	1,198.20	838.74	1,198.20	100%	70%	-41
PARKING WORK		11	10-Oct-26	20-Oct-26	20-Aug-26 A	06-Dec-26	104,146.20	78,002.10	104,146.20	100%	74.9%	-81
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	02-Dec-26	86,430.00	69,144.00	86,430.00	100%	80%	-84
PG-H-CON-EX-GN-PR-30	Marking & Signages	5	15-Oct-26	20-Oct-26	27-Oct-26 A	06-Dec-26	17,716.20	8,858.10	17,716.20	100%	50%	-29
SERVICE CONNECTION		11	31-Oct-26	26-Nov-26	20-Aug-26 A	20-Dec-26	0.00	2,790.00	3,720.00	0%	75%	-80
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	07-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-85
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26	26-Nov-26	27-Aug-26 A	20-Dec-26	0.00	892.80	1,488.00	0%	60%	-90
LANDSCAPING WORKS		34	06-Oct-26	09-Nov-26	09-Jul-26 A	06-Dec-26	349,180.26	316,254.86	403,780.26	86.48%	78.32%	-98
HARDSCAPE WORK		24	08-Oct-26	28-Oct-26	09-Jul-26 A	24-Nov-26	252,541.26	224,255.36	252,541.26	100%	88.8%	-100
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	22-Nov-26	148,149.00	140,741.55	148,149.00	100%	95%	-108
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	24-Nov-26	104,392.26	83,513.81	104,392.26	100%	80%	-90
SOFTSCAPE WORK		14	06-Oct-26	09-Nov-26	27-Aug-26 A	06-Dec-26	96,639.00	91,999.50	151,239.00	63.9%	60.83%	-56
PG-H-CON-EX-LS-SS-10	Planting Trees	10	06-Oct-26	17-Oct-26	26-Oct-26 A	22-Nov-26	96,639.00	48,319.50	96,639.00	100%	50%	-14
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-26	09-Nov-26	27-Aug-26 A	06-Dec-26	0.00	43,680.00	54,600.00	0%	80%	-79
TANK WORKS		13	17-Aug-26	19-Sep-26	17-Oct-26 A	16-Nov-26	35,133.30	20,827.80	35,133.30	100%	59.28%	2
SEPTIC TANK		13	17-Aug-26	31-Aug-26	31-Oct-26	14-Nov-26	420.30	0.00	420.30	100%	0%	0
PG-H-CON-EX-TW-ST-60	Finishing Wok	7	17-Aug-26	24-Aug-26	31-Oct-26	07-Nov-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-26	31-Aug-26	08-Nov-26	14-Nov-26	168.12	0.00	168.12	100%	0%	0
WATER STORAGE TANK		5	14-Sep-26	19-Sep-26	17-Oct-26 A	16-Nov-26	34,713.00	20,827.80	34,713.00	100%	60%	-22
PG-H-CON-EX-TW-R-40	GRP Water Tank Installation	5	14-Sep-26	19-Sep-26	17-Oct-26 A	16-Nov-26	34,713.00	20,827.80	34,713.00	100%	60%	-22
TOILET BUILDING WORKS		83	03-Aug-26	06-Oct-26	30-Jul-26 A	12-Nov-26	164,432.22	112,130.06	164,432.22	100%	68.19%	-35
CIVIL WORK		50	09-Sep-26	05-Oct-26	20-Aug-26 A	11-Nov-26	97,530.00	61,091.88	97,530.00	100%	62.64%	-49
ARCHITECTURAL WORK		50	09-Sep-26	05-Oct-26	20-Aug-26 A	11-Nov-26	97,530.00	61,091.88	97,530.00	100%	62.64%	-49
GENERAL FINISHES		32	09-Sep-26	05-Oct-26	20-Aug-26 A	11-Nov-26	72,432.60	46,760.64	72,432.60	100%	64.56%	-49
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-26	12-Sep-26	20-Aug-26 A	05-Nov-26	2,958.00	2,366.40	2,958.00	100%	80%	-63
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-26	20-Sep-26	20-Aug-26 A	08-Nov-26	273.60	218.88	273.60	100%	80%	-60
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-26	27-Sep-26	27-Aug-26 A	09-Nov-26	13,273.80	10,619.04	13,273.80	100%	80%	-57
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-26	05-Oct-26	04-Oct-26 A	11-Nov-26	55,927.20	33,556.32	55,927.20	100%	60%	-27
WET AREA FINISHES		4	01-Oct-26	05-Oct-26	27-Aug-26 A	07-Nov-26	5,361.60	4,289.28	5,361.60	100%	80%	-57
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26	05-Oct-26	27-Aug-26 A	07-Nov-26	5,361.60	4,289.28	5,361.60	100%	80%	-57
ROOF FINISHES		45	24-Sep-26	05-Oct-26	27-Aug-26 A	11-Nov-26	19,735.80	10,041.96	19,735.80	100%	50.88%	-55
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-26	26-Sep-26	27-Aug-26 A	07-Nov-26	10,158.00	8,126.40	10,158.00	100%	80%	-58
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-26	05-Oct-26	27-Oct-26 A	11-Nov-26	9,577.80	1,915.56	9,577.80	100%	20%	-12
MEP WORK		79	03-Aug-26	06-Oct-26	30-Jul-26 A	12-Nov-26	66,902.22	51,038.18	66,902.22	100%	76.29%	-35
MECANICAL WORKS		79	03-Aug-26	06-Oct-26	30-Jul-26 A	12-Nov-26	50,638.50	37,214.02	50,638.50	100%	73.49%	-35
FIRE FIGHTING SYSTEM		1	06-Oct-26	06-Oct-26	11-Nov-26	12-Nov-26	136.26	0.00	136.26	100%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-26	06-Oct-26	11-Nov-26	12-Nov-26	136.26	0.00	136.26	100%	0%	0
SEWER AND DRAINAGE SYSTEM		71	03-Aug-26	23-Aug-26	30-Jul-26 A	03-Nov-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-64
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-26	04-Aug-26	30-Jul-26 A	31-Oct-26	3,225.72	2,741.86	3,225.72	100%	85%	-76
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-26	23-Aug-26	01-Nov-26	03-Nov-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-26	15-Aug-26	26-Sep-26 A	31-Oct-26	7,684.80	5,379.36	7,684.80	100%	70%	-28
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-26	15-Aug-26	26-Sep-26 A	31-Oct-26	7,684.80	5,379.36	7,684.80	100%	70%	-28
WATER SUPPLY SYSTEM		3	18-Aug-26	20-Aug-26	27-Aug-26 A	01-Nov-26	36,366.00	29,092.80	36,366.00	100%	80%	-53
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-26	20-Aug-26	27-Aug-26 A	01-Nov-26	36,366.00	29,092.80	36,366.00	100%	80%	-53
ELECTRICAL WORKS		11	27-Aug-26	08-Sep-26	20-Aug-26 A	05-Nov-26	16,263.72	13,824.16	16,263.72	100%	85%	-54
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-26	29-Aug-26	20-Aug-26 A	03-Nov-26	1,983.60	1,686.06	1,983.60	100%	85%	-62
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-26	01-Sep-26	20-Aug-26 A	04-Nov-26	1,983.60	1,686.06	1,983.60	100%	85%	-61
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-26	05-Sep-26	20-Aug-26 A	04-Nov-26	4,959.00	4,215.15	4,959.00	100%	85%	-62
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-26	08-Sep-26	20-Aug-26 A	05-Nov-26	7,337.52	6,236.89	7,337.52	100%	85%	-62
PROJECT CLOSOUT		31	02-Nov-26	03-Dec-26	20-Oct-26 A	14-Dec-26	0.00	151,285.27	252,142.12	0%	60%	-20
PG-H-PCL-10_R	Testing, Commessioning for All Systems(Remaining)	10	02-Nov-26	12-Nov-26	29-Oct-26 A	06-Dec-26	0.00	110,397.36	183,995.60	0%	60%	-23
PG-H-PCL-20	As-Built Drawings	18	14-Nov-26	03-Dec-26	20-Oct-26 A	14-Dec-26	0.00	40,887.91	68,146.52	0%	60%	-30
TABUK		144	25-Jun-26	08-Dec-26	12-Jul-26 A	08-Feb-27	3,689,903.15	2,765,445.07	4,287,947.49	86.05%	64.49%	-39
PROCUREMENT		63	25-Jun-26	27-Aug-26	06-Aug-26 A	03-Nov-26	2,148,284.30	1,744,361.48	2,148,284.30	100%	81.2%	-21

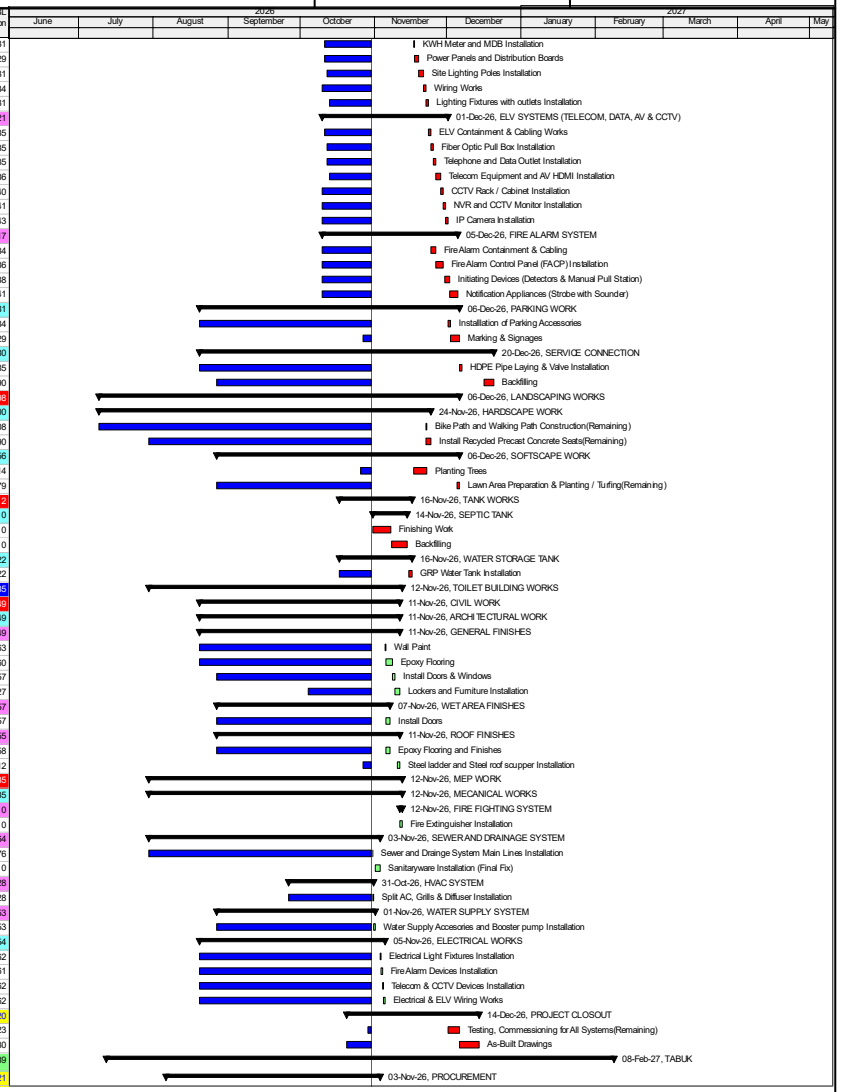

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00


PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
LONG LEAD ITEMS		54	01-Jul-26	27-Aug-26	06-Aug-26 A	03-Nov-26	2,111,605.20	1,711,350.29	2,111,605.20	100%	81.04%	-26
DELIVERY TO SITE		54	01-Jul-26	27-Aug-26	06-Aug-26 A	03-Nov-26	2,111,605.20	1,711,350.29	2,111,605.20	100%	81.04%	-26
EXTERNAL / LANDSCAPE WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	01-Nov-26	13,928.65	12,535.79	13,928.65	100%	90%	-54
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	01-Nov-26	13,928.65	12,535.79	13,928.65	100%	90%	-54
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	01-Nov-26	2,013,812.01	1,624,564.59	2,013,812.01	100%	80.67%	-44
PG-T-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	01-Nov-26	58,731.75	52,858.58	58,731.75	100%	90%	-54
PG-T-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	01-Nov-26	10,152.00	9,136.80	10,152.00	100%	90%	-54
PG-T-PR-LL-SP-DL-30_R	Padel Playground Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	01-Nov-26	26,778.60	24,100.74	26,778.60	100%	90%	-54
PG-T-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	01-Nov-26	39,487.50	35,538.75	39,487.50	100%	90%	-61
PG-T-PR-LL-SP-DL-50	Air Dome Materials	10	17-Aug-26	27-Aug-26	29-Oct-26 A	01-Nov-26	1,878,662.16	1,502,929.73	1,878,662.16	100%	80%	7
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	03-Nov-26	3,427.65	2,399.36	3,427.65	100%	70%	-46
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	03-Nov-26	3,427.65	2,399.36	3,427.65	100%	70%	-46
IRRIGATION WORK		4	01-Jul-26	05-Jul-26	20-Aug-26 A	31-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-56
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	05-Jul-26	20-Aug-26 A	31-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-56
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	01-Nov-26	64,072.19	57,122.33	64,072.19	100%	89.15%	-40
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	31-Oct-26	3,615.08	3,253.58	3,615.08	100%	90%	-61
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	01-Nov-26	1,785.24	1,606.72	1,785.24	100%	90%	-54
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	01-Nov-26	1,428.19	1,285.37	1,428.19	100%	90%	-54
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	01-Nov-26	41,772.67	37,595.40	41,772.67	100%	90%	-54
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-26	24-Aug-26	14-Aug-26 A	01-Nov-26	4,618.19	4,156.37	4,618.19	100%	90%	-54
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-26	24-Aug-26	27-Aug-26 A	01-Nov-26	3,525.77	2,996.90	3,525.77	100%	85%	-44
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-26	24-Aug-26	27-Aug-26 A	01-Nov-26	4,463.64	3,794.09	4,463.64	100%	85%	-44
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-26	24-Aug-26	27-Aug-26 A	01-Nov-26	2,863.40	2,433.89	2,863.40	100%	85%	-44
SHORT LEAD ITEMS		52	25-Jun-26	22-Jul-26	07-Aug-26 A	01-Nov-26	36,679.10	33,011.19	36,679.10	100%	90%	-48
DELIVERY TO SITE		52	25-Jun-26	22-Jul-26	07-Aug-26 A	01-Nov-26	36,679.10	33,011.19	36,679.10	100%	90%	-48
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	31-Oct-26	19,978.06	17,980.25	19,978.06	100%	90%	-45
PG-T-PR-SL-LS-DL-60_R	Trafic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	31-Oct-26	714.10	642.69	714.10	100%	90%	-45
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	31-Oct-26	8,301.96	7,471.76	8,301.96	100%	90%	-45
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	31-Oct-26	10,962.00	9,865.80	10,962.00	100%	90%	-45
METAL WORK		12	25-Jun-26	08-Jul-26	23-Sep-26 A	01-Nov-26	1,724.00	1,551.60	1,724.00	100%	90%	-20
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	23-Sep-26 A	01-Nov-26	1,302.70	1,172.43	1,302.70	100%	90%	-20
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	01-Nov-26	112.75	101.48	112.75	100%	90%	-20
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	01-Nov-26	308.56	277.70	308.56	100%	90%	-20
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	31-Oct-26	14,977.04	13,479.33	14,977.04	100%	90%	-63
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	31-Oct-26	1,859.76	1,673.78	1,859.76	100%	90%	-63
PG-T-PR-SL-IR-DL-20_R	Bulbblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	31-Oct-26	13,117.28	11,805.55	13,117.28	100%	90%	-52
CONSTRUCTION STAGE		133	25-Jun-26	07-Dec-26	12-Jul-26 A	20-Dec-26	1,541,618.86	768,940.41	1,719,424.56	89.66%	44.72%	4
PLAYGROUND AND LANDSCAPING WORKS		133	25-Jun-26	07-Dec-26	12-Jul-26 A	20-Dec-26	727,801.81	725,307.51	905,607.52	80.37%	80.09%	4
PLAYGROUND WORKS		92	08-Aug-26	07-Dec-26	14-Aug-26 A	05-Dec-26	163,580.96	154,600.61	221,537.34	73.84%	69.79%	8
FOOTBALL PLAYGROUND WORKS		76	19-Aug-26	17-Nov-26	14-Aug-26 A	16-Nov-26	84,557.58	80,372.93	109,254.66	77.39%	73.56%	-3
PG-T-CON-EX-FB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	01-Nov-26	24,360.00	21,924.00	24,360.00	100%	90%	-48
PG-T-CON-EX-FB-90	Turfing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	02-Nov-26	23,667.00	21,300.30	23,667.00	100%	90%	-56
PG-T-CON-EX-FB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	05-Nov-26	35,500.50	28,400.40	35,500.50	100%	80%	-51
PG-T-CON-EX-FB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	08-Nov-26	1,030.08	1,648.13	2,060.16	50%	80%	-50
PG-T-CON-EX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	27-Oct-26 A	16-Nov-26	0.00	7,100.10	23,667.00	0%	30%	-8
BASKETBALL PLAYGROUND WORKS		72	31-Aug-26	17-Nov-26	20-Aug-26 A	21-Nov-26	41,655.60	31,025.59	43,200.72	96.42%	71.82%	-11
PG-T-CON-EX-BB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	02-Nov-26	13,091.76	11,782.58	13,091.76	100%	90%	-47
PG-T-CON-EX-BB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	04-Nov-26	15,472.08	13,924.87	15,472.08	100%	90%	-47
PG-T-CON-EX-BB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	28-Oct-26 A	18-Nov-26	13,091.76	3,927.53	13,091.76	100%	30%	-2
PG-T-CON-EX-BB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	21-Nov-26	0.00	1,390.61	1,545.12	0%	90%	-56
PADEL PLAYGROUND WORKS		78	08-Aug-26	07-Dec-26	20-Aug-26 A	05-Dec-26	37,367.78	43,202.09	69,081.96	54.09%	62.54%	13
PG-T-CON-EX-PD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	03-Nov-26	3,534.96	3,181.46	3,534.96	100%	90%	-43
PG-T-CON-EX-PD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	04-Nov-26	5,302.44	4,772.20	5,302.44	100%	90%	-47
PG-T-CON-EX-PD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	20-Oct-26 A	17-Nov-26	5,302.44	2,120.98	5,302.44	100%	40%	-7
PG-T-CON-EX-PD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	19-Nov-26	23,227.94	23,692.50	26,325.00	88.24%	90%	-61
PG-T-CON-EX-PD-70	Court Accessories Installation	16	02-Nov-26	19-Nov-26	26-Oct-26 A	02-Dec-26	0.00	8,121.60	27,072.00	0%	30%	-17
PG-T-CON-EX-PD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	05-Dec-26	0.00	1,313.35	1,545.12	0%	85%	-70
GENERAL SITE WORKS		133	25-Jun-26	23-Nov-26	12-Jul-26 A	20-Dec-26	422,149.67	359,214.61	439,909.90	95.96%	81.66%	-8
MECHANICAL WORK		94	01-Jul-26	10-Aug-26	12-Jul-26 A	21-Nov-26	206,336.28	177,179.71	206,336.28	100%	85.87%	-77
STORM WATER AND UTILITY WORK		72	01-Jul-26	04-Aug-26	20-Aug-26 A	15-Nov-26	22,092.00	11,646.00	22,092.00	100%	52.72%	-43
PG-T-CON-EX-GNM-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	31-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-56
PG-T-CON-EX-GNM-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	02-Nov-26	10,740.00	7,518.00	10,740.00	100%	70%	-32
PG-T-CON-EX-GNM-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	02-Nov-26	05-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EX-GNM-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	05-Nov-26	09-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EX-GNM-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	10-Nov-26	15-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	10-Nov-26	183,926.34	165,533.71	183,926.34	100%	90%	-88
PG-T-CON-EX-GNM-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	09-Nov-26	34,712.34	31,241.11	34,712.34	100%	90%	-98
PG-T-CON-EX-GNM-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	09-Nov-26	90,915.00	81,823.50	90,915.00	100%	90%	-63
PG-T-CON-EX-GNM-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	10-Nov-26	58,299.00	52,469.10	58,299.00	100%	90%	-64
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	15-Nov-26	21-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EX-GNM-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	15-Nov-26	21-Nov-26	317.94	0.00	317.94	100%	0%	0

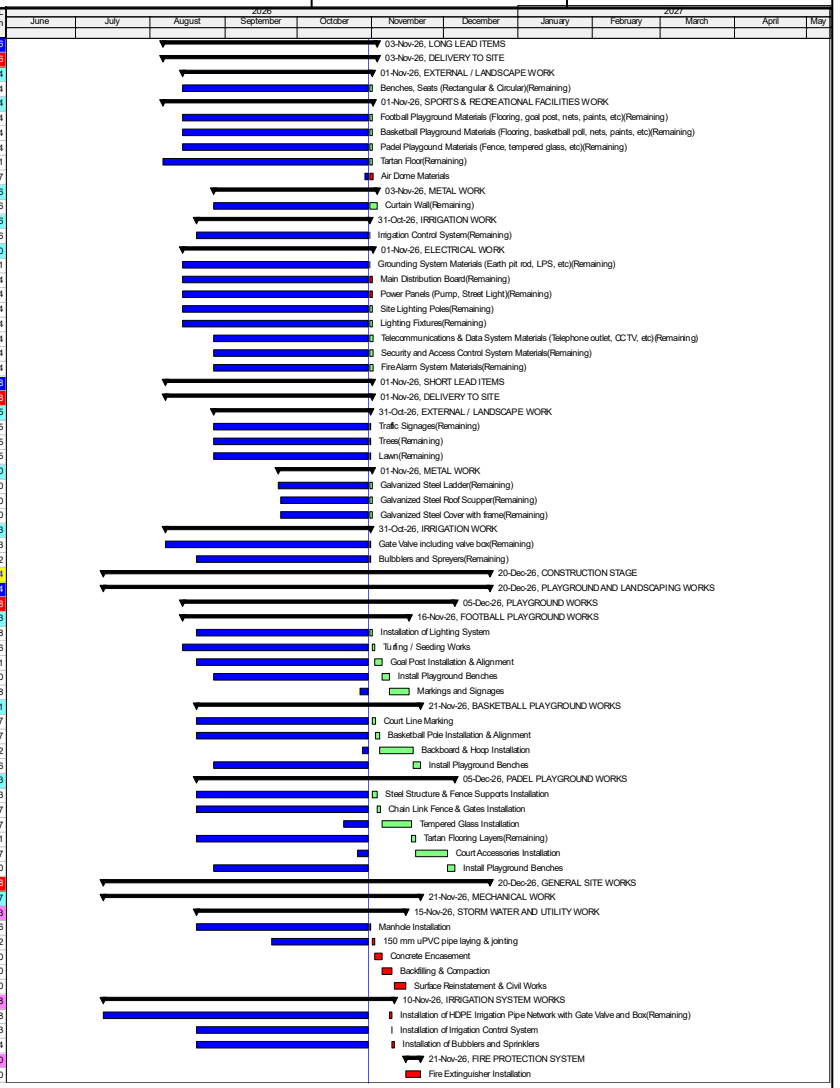


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
ELECTRICAL WORK		115	25-Jun-26	07-Nov-26	20-Aug-26 A	20-Dec-26	215,813.39	172,786.20	216,861.82	99.52%	79.68%	12
POWER, LIGHTING & GROUNDING		79	25-Jun-26	19-Sep-26	20-Aug-26 A	26-Nov-26	159,791.62	134,229.48	159,791.62	100%	84%	-10
PG-T-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	02-Nov-26	55,696.90	50,127.21	55,696.90	100%	90%	-41
PG-T-CON-EX-GN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	22-Nov-26	8,265.00	7,438.50	8,265.00	100%	90%	-71
PG-T-CON-EX-GN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	23-Nov-26	4,586.70	3,669.36	4,586.70	100%	80%	-51
PG-T-CON-EX-GN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	24-Nov-26	17,397.90	13,918.32	17,397.90	100%	80%	-50
PG-T-CON-EX-GN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	25-Nov-26	69,621.12	55,696.90	69,621.12	100%	80%	-53
PG-T-CON-EX-GN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	04-Oct-26 A	26-Nov-26	4,224.00	3,379.20	4,224.00	100%	80%	-43
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	12-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-44
PG-T-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	05-Dec-26	619.80	433.86	619.80	100%	70%	-59
PG-T-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	06-Dec-26	619.80	433.86	619.80	100%	70%	-60
PG-T-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	07-Dec-26	3,718.80	2,603.16	3,718.80	100%	70%	-60
PG-T-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	08-Dec-26	15,249.12	10,674.38	15,249.12	100%	70%	-62
PG-T-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	09-Dec-26	1,446.48	1,012.54	1,446.48	100%	70%	-63
PG-T-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	12-Dec-26	6,612.00	4,628.40	6,612.00	100%	70%	-64
PG-T-CON-EX-GN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	12-Dec-26	14,880.00	10,416.00	14,880.00	100%	70%	-66
FIRE ALARM SYSTEM		32	01-Oct-26	07-Nov-26	13-Oct-26 A	20-Dec-26	12,875.78	8,354.52	13,924.20	92.47%	60%	-26
PG-T-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	01-Oct-26	10-Oct-26	13-Oct-26 A	08-Dec-26	1,983.60	1,190.16	1,983.60	100%	60%	-41
PG-T-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26	19-Oct-26	14-Oct-26 A	12-Dec-26	2,644.80	1,586.88	2,644.80	100%	60%	-43
PG-T-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26	28-Oct-26	15-Oct-26 A	15-Dec-26	8,097.60	4,858.56	8,097.60	100%	60%	-45
PG-T-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26	07-Nov-26	17-Oct-26 A	20-Dec-26	149.78	718.92	1,198.20	12.5%	60%	-47
PARKING WORK		7	04-Nov-26	11-Nov-26	26-Oct-26 A	20-Dec-26	0.00	7,239.90	14,479.80	0%	50%	-40
PG-T-CON-EX-GN-PR-30	Marking & Signages	7	04-Nov-26	11-Nov-26	26-Oct-26 A	20-Dec-26	0.00	7,239.90	14,479.80	0%	50%	-40
SERVICE CONNECTION		10	12-Nov-26	23-Nov-26	14-Aug-26 A	20-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-98
PG-T-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	20-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-98
LANDSCAPING WORKS		38	28-Sep-26	22-Nov-26	12-Jul-26 A	17-Nov-26	107,106.00	187,193.19	209,195.10	51.2%	89.48%	-62
HARDSCAPE WORK		38	28-Sep-26	22-Nov-26	30-Jul-26 A	17-Nov-26	60,984.00	112,797.39	126,533.10	48.2%	89.14%	-46
PG-T-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	11-Nov-26	60,984.00	54,885.60	60,984.00	100%	90%	-55
PG-T-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	14-Nov-26	0.00	54,123.39	60,137.10	0%	90%	-81
PG-T-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	17-Nov-26	0.00	3,788.40	5,412.00	0%	70%	-37
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	17-Nov-26	46,122.00	74,395.80	82,662.00	55.8%	90%	-72
PG-T-CON-EX-LS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	12-Nov-26	46,122.00	41,509.80	46,122.00	100%	90%	-32
PG-T-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-26	22-Nov-26	12-Jul-26 A	17-Nov-26	0.00	32,886.00	36,540.00	0%	90%	-104
TANK WORKS		9	18-Aug-26	27-Sep-26	13-Oct-26 A	10-Nov-26	34,965.18	24,299.10	34,965.18	100%	69.5%	10
SEPTIC TANK		8	18-Aug-26	26-Aug-26	31-Oct-26	08-Nov-26	252.18	0.00	252.18	100%	0%	0
PG-T-CON-EX-TW-ST-60	Finishing Work	8	18-Aug-26	26-Aug-26	31-Oct-26	08-Nov-26	252.18	0.00	252.18	100%	0%	0
WATER STORAGE TANK		5	21-Sep-26	27-Sep-26	13-Oct-26 A	10-Nov-26	34,713.00	24,299.10	34,713.00	100%	70%	-20
PG-T-CON-EX-TW-IR-40	GRP Water Tank Installation	5	21-Sep-26	27-Sep-26	13-Oct-26 A	10-Nov-26	34,713.00	24,299.10	34,713.00	100%	70%	-20
AIR DOME CONSTRUCTION		22	26-Aug-26	20-Sep-26	31-Oct-26	24-Nov-26	751,464.86	0.00	751,464.86	100%	0%	0
CIVIL WORK		17	26-Aug-26	14-Sep-26	31-Oct-26	18-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-T-CON-EX-AD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-26	05-Sep-26	31-Oct-26	09-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EX-AD-CL-80	Installation of Membrane System	8	06-Sep-26	14-Sep-26	10-Nov-26	18-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
MECHANICAL WORK		5	15-Sep-26	20-Sep-26	19-Nov-26	24-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EX-AD-ME-10	Installation of Main Air Package Units	5	15-Sep-26	20-Sep-26	19-Nov-26	24-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
TOILET BUILDING WORKS		16	31-Aug-26	28-Oct-26	19-Sep-26 A	04-Nov-26	62,352.18	43,632.90	62,352.18	100%	69.98%	11
CIVIL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	03-Nov-26	14,939.40	10,457.58	14,939.40	100%	70%	-24
ARCHITECTURAL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	03-Nov-26	14,939.40	10,457.58	14,939.40	100%	70%	-24
WET AREA FINISHES		2	11-Oct-26	12-Oct-26	23-Sep-26 A	02-Nov-26	5,361.60	3,753.12	5,361.60	100%	70%	-31
PG-T-CON-B-AR-WF-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	02-Nov-26	5,361.60	3,753.12	5,361.60	100%	70%	-31
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	03-Nov-26	9,577.80	6,704.46	9,577.80	100%	70%	-35
PG-T-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	03-Nov-26	9,577.80	6,704.46	9,577.80	100%	70%	-35
MEP WORK		16	31-Aug-26	28-Oct-26	20-Sep-26 A	04-Nov-26	47,412.78	33,175.32	47,412.78	100%	69.97%	12
MECANICAL WORKS		16	31-Aug-26	28-Oct-26	20-Sep-26 A	04-Nov-26	47,412.78	33,175.32	47,412.78	100%	69.97%	12
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	04-Nov-26	136.26	81.76	136.26	100%	60%	-33
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	04-Nov-26	136.26	81.76	136.26	100%	60%	-33
SEWER AND DRAINAGE SYSTEM		2	03-Sep-26	05-Sep-26	23-Sep-26 A	01-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-31
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-26	05-Sep-26	23-Sep-26 A	01-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-31
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	02-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-34
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	02-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-34
WATER SUPPLY SYSTEM		3	31-Aug-26	02-Sep-26	23-Sep-26 A	31-Oct-26	36,366.00	25,456.20	36,366.00	100%	70%	-29
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-26	02-Sep-26	23-Sep-26 A	31-Oct-26	36,366.00	25,456.20	36,366.00	100%	70%	-29
PROJECT CLOSOUT		140	22-Nov-26	08-Dec-26	29-Oct-26 A	08-Feb-27	0.00	252,143.18	420,238.64	0%	60%	-73
PG-TPCL-20	As-Built Drawings	15	22-Nov-26	08-Dec-26	29-Oct-26 A	08-Feb-27	0.00	68,146.81	113,578.01	0%	60%	-73
PG-TPCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-26	03-Dec-26	29-Oct-26 A	06-Feb-27	0.00	183,996.38	306,660.63	0%	60%	-75

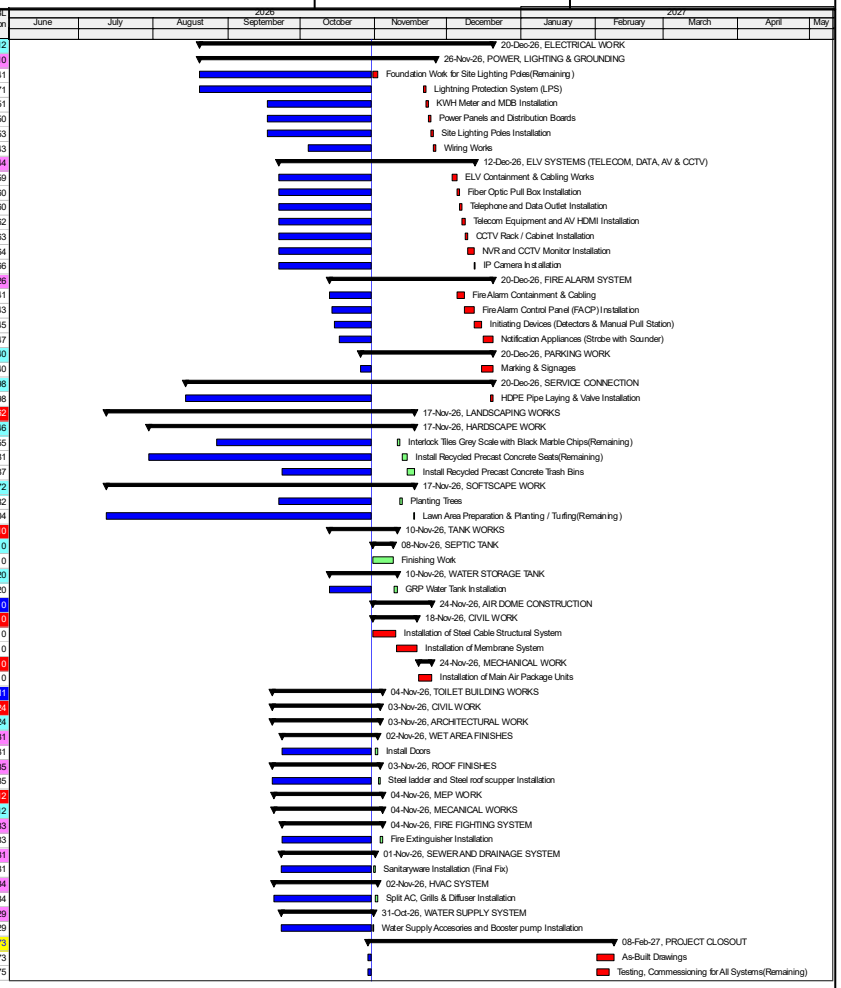

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
