
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026		309	17-Feb-26	16-Dec-26	17-Feb-26 A	23-Feb-27	30,064,337.39	25,416,334.47	35,709,993.00	84.19%	71.17%	-59
MILESTONES		309	17-Feb-26	16-Dec-26	17-Feb-26 A	23-Feb-27	0.00	0.00	0.00	0%	0%	-59
GENERAL MILESTONES		309	17-Feb-26	16-Dec-26	17-Feb-26 A	23-Feb-27	0.00	0.00	0.00	0%	0%	-59
CONTRACUAL MILESTONES		247	05-May-26	16-Dec-26	05-May-26 A	23-Feb-27	0.00	0.00	0.00	0%	0%	-59
QASSIM		309	17-Feb-26	16-Dec-26	17-Feb-26 A	23-Feb-27	14,808,264.61	12,649,976.89	17,537,540.00	84.44%	72.13%	-59
MOBILIZATION		29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
SITE OFFICES		29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
GENERAL REQUIEREMENTS		57	17-Feb-26	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
ENGINEERING		199	17-Feb-26	16-Aug-26	17-Feb-26 A	03-Nov-26	526,126.20	526,126.20	526,126.20	100%	100%	-67
SHOP DRAWINGS SUBMITTALS		168	17-Feb-26	04-Aug-26	17-Feb-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-75
STRUCTURAL DRAWINGS		125	17-Feb-26	06-Jul-26	17-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	-4
PROJECT FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	25-Jun-26	06-Jul-26	01-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	1
TOILET BUILDING		43	17-Feb-26	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		41	19-Feb-26	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		13	28-Apr-26	13-May-26	28-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		158	19-Feb-26	23-Jul-26	19-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
TOILET BUILDING		42	19-Feb-26	15-Apr-26	19-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-9
LANDSCAPE DRAWINGS		39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		143	28-Feb-26	15-Jul-26	28-Feb-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-92
WATER SUPPLY SYSTEM		32	28-Feb-26	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-26	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	09-Mar-26	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-62
ELECTRICAL DRAWINGS		102	11-May-26	04-Aug-26	11-May-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-75
POWER AND LIGHTING SYSTEM		27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	01-Nov-26	0.00	0.00	0.00	0%	0%	-63
SHOP DRAWINGS APPROVALS		172	19-Feb-26	16-Aug-26	19-Feb-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-67
STRUCTURAL DRAWINGS		130	19-Feb-26	14-Jul-26	19-Feb-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	2
PROJECT FENCE		7	13-May-26	21-May-26	13-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		9	11-May-26	21-May-26	11-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		9	05-Jul-26	14-Jul-26	06-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	3
TOILET BUILDING		44	19-Feb-26	18-Apr-26	19-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		42	23-Feb-26	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		3	11-May-26	14-May-26	11-May-26 A	13-May-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		166	25-Feb-26	01-Aug-26	25-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
TOILET BUILDING		40	25-Feb-26	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-20
LANDSCAPE DRAWINGS		39	26-Feb-26	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		154	09-Mar-26	27-Jul-26	09-Mar-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-84
WATER SUPPLY SYSTEM		27	09-Mar-26	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-26	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	12-Mar-26	14-Apr-26	12-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	16-Jul-26	27-Jul-26	20-Aug-26 A	03-Nov-26	0.00	0.00	0.00	0%	0%	-54
ELECTRICAL DRAWINGS		100	20-May-26	16-Aug-26	20-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
POWER AND LIGHTING SYSTEM		20	20-May-26	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		20	20-May-26	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		20	20-May-26	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	28-Jul-26	16-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-10
MATERIAL SUBMITTALS		134	17-Feb-26	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
LONG LEAD ITEMS		134	17-Feb-26	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
EXTERNAL / LANDSCAPE WORK		56	25-Feb-26	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
SPORTS & RECREATIONAL FACILITIES WORK		134	17-Feb-26	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
CONCRETE WORK		43	04-Mar-26	28-Apr-26	04-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		47	09-Mar-26	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		46	10-Mar-26	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		50	05-Mar-26	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		26	12-May-26	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
SHORT LEAD ITEMS		28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-26	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
CONCRETE WORK		28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL & FINISHES WORK		18	21-Feb-26	15-Mar-26	21-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		11	04-Mar-26	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
HVAC WORK		19	23-Feb-26	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		17	25-Feb-26	17-Mar-26	25-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0

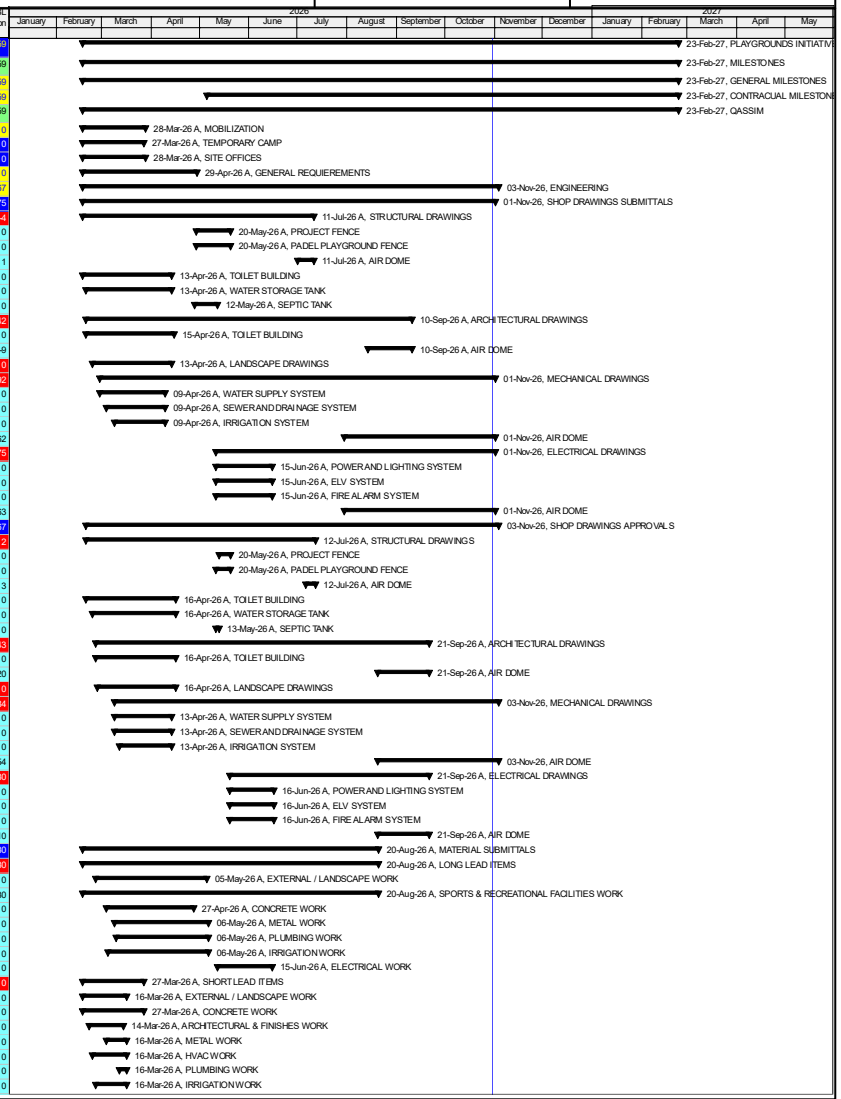


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ELECTRICAL WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	196	21-Feb-2	18-Jul-26	21-Feb-26 A	01-Oct-26 A	526,126.20	526,126.20	526,126.20	100%	100%	-64
	LONG LEAD ITEMS	189	02-Mar-2	18-Jul-26	02-Mar-26 A	01-Oct-26 A	358,885.26	358,885.26	358,885.26	100%	100%	-64
	EXTERNAL / LANDSCAPE WORK	2	11-May-2	12-May-26	11-May-26 A	12-May-26 A	19,812.18	19,812.18	19,812.18	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	110	02-Mar-2	30-Jun-26	02-Mar-26 A	19-Sep-26 A	273,522.54	273,522.54	273,522.54	100%	100%	-69
	CONCRETE WORK	40	09-Mar-2	28-Apr-26	09-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	112	09-Jun-2	18-Jul-26	09-Jun-26 A	01-Oct-26 A	889.23	889.23	889.23	100%	100%	-64
	PLUMBING WORK	48	09-Jun-2	18-Jul-26	20-May-26 A	24-Jun-26 A	3,553.95	3,553.95	3,553.95	100%	100%	7
	IRRIGATION WORK	45	11-Mar-2	06-May-26	11-Mar-26 A	06-May-26 A	24,486.75	24,486.75	24,486.75	100%	100%	0
	ELECTRICAL WORK	96	12-May-2	02-Jul-26	12-May-26 A	16-Sep-26 A	35,203.11	35,203.11	35,203.11	100%	100%	-64
	SHORT LEAD ITEMS	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	167,240.94	167,240.94	167,240.94	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	139,867.29	139,867.29	139,867.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-2	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	17	25-Feb-2	16-Mar-26	25-Feb-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	12	09-Mar-2	26-Mar-26	09-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-2	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	17	03-Mar-2	26-Mar-26	03-Mar-26 A	26-Mar-26 A	13,170.12	13,170.12	13,170.12	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	226	03-Mar-2	27-Aug-26	03-Mar-26 A	05-Nov-26	4,735,135.80	4,306,400.85	4,735,135.80	100%	90.95%	-59
	LONG LEAD ITEMS	213	18-Mar-2	27-Aug-26	18-Mar-26 A	05-Nov-26	3,229,967.34	2,816,604.28	3,229,967.34	100%	87.2%	-59
	PURCHASE ORDER	147	18-Mar-2	12-Jul-26	18-Mar-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	5	06-May-2	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	101	26-Mar-2	09-Jul-26	26-Mar-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-2	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	36	26-Mar-2	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-2	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	37	25-Mar-2	07-May-26	25-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	103	13-May-2	12-Jul-26	13-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	MANUFACTURE / FABRICATION	161	05-May-2	11-Aug-26	05-May-26 A	04-Oct-26 A	0.00	0.00	0.00	0%	0%	-45
	EXTERNAL / LANDSCAPE WORK	109	05-May-2	23-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
	SPORTS & RECREATIONAL FACILITIES WORK	123	05-May-2	11-Aug-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	CONCRETE WORK	69	05-May-2	12-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	15
	METAL WORK	161	05-May-2	23-Jul-26	05-May-26 A	04-Oct-26 A	0.00	0.00	0.00	0%	0%	-61
	PLUMBING WORK	79	05-May-2	23-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	25
	IRRIGATION WORK	82	05-May-2	06-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-62
	ELECTRICAL WORK	129	12-May-2	10-Aug-26	12-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-32
	DELIVERY TO SITE	175	06-May-2	27-Aug-26	06-May-26 A	05-Nov-26	3,229,967.34	2,816,604.28	3,229,967.34	100%	87.2%	-59
	EXTERNAL / LANDSCAPE WORK	123	06-May-2	10-Aug-26	06-May-26 A	01-Nov-26	178,309.62	176,866.75	178,309.62	100%	99.19%	-70
	SPORTS & RECREATIONAL FACILITIES WORK	127	06-May-2	23-Aug-26	06-May-26 A	05-Nov-26	2,461,702.86	2,073,940.31	2,461,702.86	100%	84.25%	-63
	CONCRETE WORK	78	06-May-2	23-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	16
	METAL WORK	175	06-May-2	10-Aug-26	06-May-26 A	04-Nov-26	8,003.07	6,974.78	8,003.07	100%	87.15%	-73
	PLUMBING WORK	104	06-May-2	10-Aug-26	06-May-26 A	13-Oct-26 A	31,985.55	31,985.55	31,985.55	100%	100%	-54
	IRRIGATION WORK	102	06-May-2	15-Jul-26	06-May-26 A	31-Oct-26	220,380.75	219,357.96	220,380.75	100%	99.54%	-90
	ELECTRICAL WORK	143	13-May-2	27-Aug-26	13-May-26 A	01-Nov-26	316,827.99	294,721.44	316,827.99	100%	93.02%	-55
	SHORT LEAD ITEMS	183	03-Mar-2	12-Jul-26	03-Mar-26 A	01-Nov-26	1,505,168.46	1,489,796.57	1,505,168.46	100%	98.98%	-95
	PURCHASE ORDER	64	03-Mar-2	21-May-26	03-Mar-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	57	03-Mar-2	13-May-26	03-Mar-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	04-Mar-2	23-Apr-26	04-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	36	25-Mar-2	06-May-26	25-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	46	09-Mar-2	06-May-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	33	29-Mar-2	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	43	12-Mar-2	06-May-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	8	12-May-2	21-May-26	12-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	DELIVERY TO SITE	181	05-Mar-2	12-Jul-26	05-Mar-26 A	01-Nov-26	1,505,168.46	1,489,796.57	1,505,168.46	100%	98.98%	-95
	EXTERNAL / LANDSCAPE WORK	155	05-Mar-2	08-Jul-26	05-Mar-26 A	01-Nov-26	1,258,805.61	1,250,950.31	1,258,805.61	100%	99.38%	-97
	CONCRETE WORK	50	12-Mar-2	13-May-26	12-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-2	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	129	06-May-2	08-Jul-26	06-May-26 A	01-Nov-26	4,310.01	4,137.61	4,310.01	100%	96%	-97
	HVAC WORK	106	06-May-2	08-Jul-26	06-May-26 A	02-Oct-26 A	5,457.24	5,457.24	5,457.24	100%	100%	-72
	PLUMBING WORK	7	06-May-2	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	101	06-May-2	08-Jul-26	06-May-26 A	01-Nov-26	118,531.08	111,419.22	118,531.08	100%	94%	-97
	ELECTRICAL WORK	128	11-May-2	12-Jul-26	11-May-26 A	01-Nov-26	3,667.68	3,447.62	3,667.68	100%	94%	-95
	FIRE FIGHTING WORK	129	06-May-2	08-Jul-26	06-May-26 A	01-Nov-26	204.39	192.13	204.39	100%	94%	-97
	CONSTRUCTION STAGE	267	24-Mar-2	16-Dec-26	24-Mar-26 A	03-Feb-27	9,494,389.99	7,375,503.83	10,522,524.00	90.23%	70.09%	-42
	PLAYGROUND AND LANDSCAPING WORKS	246	24-Mar-2	16-Dec-26	24-Mar-26 A	04-Jan-27	5,610,524.52	5,605,494.83	6,019,638.42	93.2%	93.12%	-15
	CUT AND FILL	38	24-Mar-2	06-May-26	24-Mar-26 A	06-May-26 A	900,600.00	900,600.00	900,600.00	100%	100%	0

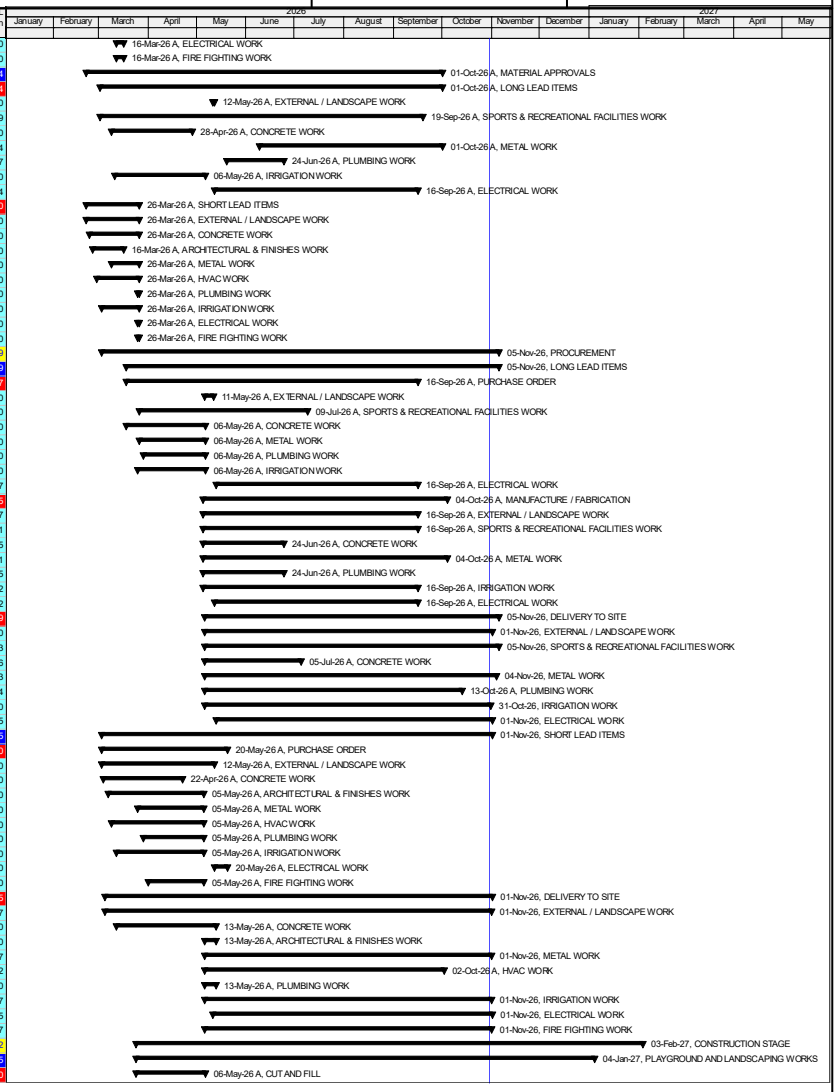


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	PLAYGROUND WORKS	204	21-Apr-26	02-Dec-26	21-Apr-26 A	03-Dec-26	1,265,648.95	1,252,061.81	1,318,471.20	95.99%	94.96%	0
	FOOTBALL PLAYGROUND WORKS	178	21-Apr-26	17-Nov-26	21-Apr-26 A	15-Nov-26	586,645.67	584,767.13	611,282.16	95.97%	95.66%	2
	BASKETBALL PLAYGROUND WORKS	163	30-Apr-26	17-Nov-26	30-Apr-26 A	16-Nov-26	380,331.68	373,064.98	381,705.12	99.64%	97.74%	2
	PADEL PLAYGROUND WORKS	191	06-May-26	02-Dec-26	06-May-26 A	03-Dec-26	298,671.60	294,229.70	325,483.92	91.76%	90.4%	0
	GENERAL SITE WORKS	226	16-Apr-26	16-Dec-26	16-Apr-26 A	04-Jan-27	1,536,025.47	1,415,949.48	1,617,941.82	94.94%	87.52%	-15
	FENCE WORKS	168	16-Apr-26	13-Sep-26	16-Apr-26 A	20-Oct-26 A	32,909.40	32,909.40	32,909.40	100%	100%	-31
	MECHANICAL WORK	165	12-May-26	18-Aug-26	12-May-26 A	26-Nov-26	780,707.34	707,170.08	780,707.34	100%	90.58%	-84
	STORM WATER AND UTILITY WORK	163	12-May-26	16-Aug-26	12-May-26 A	24-Nov-26	27,252.00	19,573.20	27,252.00	100%	71.82%	-84
	IRRIGATION SYSTEM WORKS	86	17-Jun-26	09-Aug-26	17-Jun-26 A	17-Nov-26	753,137.40	687,596.88	753,137.40	100%	91.3%	-84
	FIRE PROTECTION SYSTEM	2	17-Aug-26	18-Aug-26	24-Nov-26	26-Nov-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	197	20-May-26	01-Nov-26	20-May-26 A	15-Dec-26	693,665.73	575,949.30	693,965.28	99.96%	82.99%	-38
	POWER, LIGHTING & GROUNDING	162	20-May-26	20-Sep-26	20-May-26 A	03-Dec-26	636,895.08	536,000.16	636,895.08	100%	84.16%	-62
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	21-Sep-26	20-Oct-26	07-Oct-26 A	12-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-32
	FIRE ALARM SYSTEM	32	26-Sep-26	01-Nov-26	11-Oct-26 A	15-Dec-26	13,624.65	9,746.94	13,924.20	97.85%	70%	-25
	PARKING WORK	160	17-Jun-26	09-Nov-26	17-Jun-26 A	15-Dec-26	28,743.00	95,679.90	102,919.80	27.93%	92.97%	-31
	SERVICE CONNECTION	38	10-Nov-26	16-Dec-26	12-Jul-26 A	04-Jan-27	0.00	4,240.80	7,440.00	0%	57%	-118
	LANDSCAPING WORKS	168	31-May-26	14-Dec-26	30-May-26 A	23-Nov-26	1,859,959.70	1,995,535.74	2,134,335.00	87.14%	93.5%	19
	HARDSCAPE WORK	168	31-May-26	14-Dec-26	30-May-26 A	23-Nov-26	1,644,359.70	1,692,172.74	1,712,409.00	96.03%	98.82%	19
	SOFTSCAPE WORK	144	10-Jun-26	21-Nov-26	10-Jun-26 A	16-Nov-26	215,600.00	303,363.00	421,926.00	51.1%	71.9%	5
	TANK WORKS	138	13-May-26	19-Aug-26	13-May-26 A	01-Nov-26	48,290.40	41,347.80	48,290.40	100%	85.62%	-62
	SEPTIC TANK	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	7,475.22	7,475.22	7,475.22	100%	100%	0
	WATER STORAGE TANK	138	13-May-26	19-Aug-26	13-May-26 A	01-Nov-26	40,815.18	33,872.58	40,815.18	100%	82.99%	-62
	AIR DOME CONSTRUCTION	224	13-May-26	26-Nov-26	13-May-26 A	03-Feb-27	3,559,021.09	1,461,181.68	4,178,041.20	85.18%	34.97%	-59
	CIVIL WORK	163	13-May-26	10-Sep-26	13-May-26 A	24-Nov-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-63
	ARCHITECTURAL WORK	53	27-Oct-26	26-Nov-26	27-Aug-26 A	03-Feb-27	93,933.11	125,244.14	712,953.22	13.18%	17.57%	-110
	MECHANICAL WORK	16	12-Sep-26	30-Sep-26	24-Nov-26	13-Dec-26	667,968.77	0.00	667,968.77	100%	0%	0
	ELECTRICAL WORK	98	17-Aug-26	26-Oct-26	27-Aug-26 A	07-Jan-27	1,085,449.25	125,244.14	1,085,449.25	100%	11.54%	-54
	TOILET BUILDING WORKS	163	06-May-26	20-Oct-26	06-May-26 A	07-Nov-26	324,844.38	308,827.33	324,844.38	100%	95.07%	-14
	CIVIL WORK	162	06-May-26	19-Oct-26	06-May-26 A	05-Nov-26	227,117.58	214,414.56	227,117.58	100%	94.41%	-15
	STRUCTURAL WORK	85	06-May-26	04-Aug-26	06-May-26 A	10-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	22
	ARCHITECTURAL WORK	107	05-Aug-26	19-Oct-26	12-Jul-26 A	05-Nov-26	189,137.58	176,434.56	189,137.58	100%	93.28%	-36
	GENERAL FINISHES	107	05-Aug-26	19-Oct-26	12-Jul-26 A	05-Nov-26	84,120.00	77,872.38	84,120.00	100%	92.57%	-36
	WET AREA FINISHES	59	20-Aug-26	14-Oct-26	06-Aug-26 A	03-Nov-26	81,123.78	79,515.30	81,123.78	100%	98.02%	-29
	ROOF FINISHES	14	01-Oct-26	19-Oct-26	20-Aug-26 A	05-Nov-26	23,893.80	19,046.88	23,893.80	100%	79.71%	-50
	MEP WORK	132	16-Jun-26	20-Oct-26	16-Jun-26 A	07-Nov-26	97,726.80	94,412.77	97,726.80	100%	96.61%	-14
	MECANICAL WORKS	132	16-Jun-26	20-Oct-26	16-Jun-26 A	07-Nov-26	79,479.48	76,165.45	79,479.48	100%	95.83%	-14
	FIRE FIGHTING SYSTEM	1	20-Oct-26	20-Oct-26	01-Oct-26 A	07-Nov-26	136.26	95.38	136.26	100%	70%	-30
	SEWER AND DRAINAGE SYSTEM	103	16-Jun-26	02-Sep-26	16-Jun-26 A	02-Nov-26	11,290.02	10,322.30	11,290.02	100%	91.43%	-50
	HVAC SYSTEM	26	12-Aug-26	23-Aug-26	13-Aug-26 A	31-Oct-26	12,127.20	9,821.76	12,127.20	100%	80.99%	-57
	WATER SUPPLY SYSTEM	80	16-Jun-26	31-Aug-26	16-Jun-26 A	07-Sep-26 A	55,926.00	55,926.00	55,926.00	100%	100%	-5
	ELECTRICAL WORKS	47	13-Jul-26	15-Sep-26	22-Jul-26 A	08-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	14
	PROJECT CLOSOUT	233	23-May-26	16-Dec-26	22-May-26 A	23-Feb-27	52,612.62	441,946.01	1,753,754.00	3%	25.2%	-59
	HAIL	272	17-Feb-26	15-Dec-26	17-Feb-26 A	07-Jan-27	6,063,224.80	5,853,631.49	6,814,652.00	88.97%	85.9%	-20
	MOBILIZATION	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	51	17-Feb-26	23-Apr-26	17-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	168	17-Feb-26	14-Jul-26	17-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	SHOP DRAWINGS SUBMITTALS	93	17-Feb-26	16-Jun-26	17-Feb-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	17-Feb-26	05-May-26	17-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	57	17-Feb-26	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	41	19-Feb-26	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	55	25-Feb-26	05-May-26	25-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	24-Feb-26	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	52	01-Mar-26	05-May-26	01-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	31	01-Mar-26	11-Apr-26	01-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	05-Mar-26	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	10-Mar-26	05-May-26	10-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	SHOP DRAWINGS APPROVALS	92	19-Feb-26	17-Jun-26	19-Feb-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	19-Feb-26	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	55	19-Feb-26	30-Apr-26	19-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	42	23-Feb-26	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-26	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-26	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0

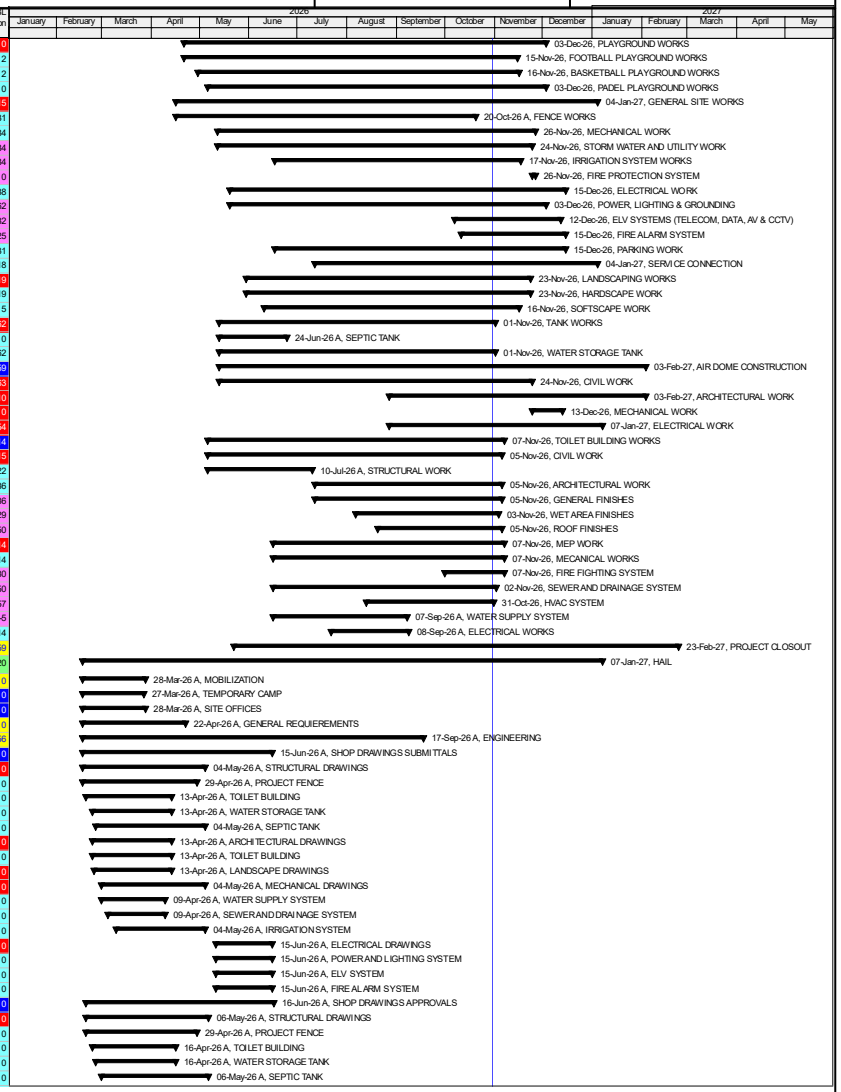


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ARCHITECTURAL DRAWINGS	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	46	10-Mar-26	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	26	10-Mar-26	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	26	10-Mar-26	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	43	14-Mar-26	07-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL SUBMITTALS	166	17-Feb-26	06-Jul-26	17-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	LONG LEAD ITEMS	163	21-Feb-26	06-Jul-26	21-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-26	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	47	08-Mar-26	06-May-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	41	07-Mar-26	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	44	11-Mar-26	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	44	11-Mar-26	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	60	21-Feb-26	07-May-26	21-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	99	12-May-26	06-Jul-26	12-May-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	SHORT LEAD ITEMS	28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-26	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-26	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	165	21-Feb-26	14-Jul-26	21-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	LONG LEAD ITEMS	162	25-Feb-26	14-Jul-26	25-Feb-26 A	17-Sep-26 A	111,065.49	111,065.49	111,065.49	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-26	06-May-26	25-Feb-26 A	06-May-26 A	26,079.63	26,079.63	26,079.63	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	43	14-Mar-26	06-May-26	14-Mar-26 A	06-May-26 A	38,839.50	38,839.50	38,839.50	100%	100%	0
	CONCRETE WORK	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	41	16-Mar-26	06-May-26	16-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	55	28-Feb-26	06-May-26	28-Feb-26 A	06-May-26 A	12,818.25	12,818.25	12,818.25	100%	100%	0
	ELECTRICAL WORK	101	12-May-26	14-Jul-26	12-May-26 A	17-Sep-26 A	27,467.43	27,467.43	27,467.43	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	93,374.07	93,374.07	93,374.07	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	72,133.44	72,133.44	72,133.44	100%	100%	0
	CONCRETE WORK	24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	8,114.01	8,114.01	8,114.01	100%	100%	0
	METAL WORK	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	6,854.64	6,854.64	6,854.64	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	215	26-Feb-26	26-Aug-26	26-Feb-26 A	02-Nov-26	1,839,956.04	1,816,202.83	1,839,956.04	100%	98.71%	-56
	LONG LEAD ITEMS	209	05-Mar-26	26-Aug-26	05-Mar-26 A	02-Nov-26	999,589.41	981,462.29	999,589.41	100%	98.19%	-56
	PURCHASE ORDER	162	05-Mar-26	22-Jul-26	05-Mar-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-26	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	109	11-May-26	22-Jul-26	11-May-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
	MANUFACTURE / FABRICATION	190	01-Apr-26	12-Aug-26	01-Apr-26 A	02-Oct-26 A	0.00	0.00	0.00	0%	0%	-42
	EXTERNAL / LANDSCAPE WORK	103	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	SPORTS & RECREATIONAL FACILITIES WORK	97	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	93	01-Apr-26	06-Jul-26	01-Apr-26 A	27-Jun-26 A	0.00	0.00	0.00	0%	0%	8
	METAL WORK	161	05-May-26	23-Jul-26	05-May-26 A	02-Oct-26 A	0.00	0.00	0.00	0%	0%	-59
	PLUMBING WORK	120	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	IRRIGATION WORK	107	05-May-26	08-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-54
	ELECTRICAL WORK	131	12-May-26	12-Aug-26	12-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-25
	DELIVERY TO SITE	147	07-May-26	26-Aug-26	06-May-26 A	02-Nov-26	999,589.41	981,462.29	999,589.41	100%	98.19%	-56
	EXTERNAL / LANDSCAPE WORK	118	07-May-26	06-Aug-26	06-May-26 A	15-Oct-26 A	234,716.67	234,716.67	234,716.67	100%	100%	-59
	SPORTS & RECREATIONAL FACILITIES WORK	106	07-May-26	06-Aug-26	06-May-26 A	15-Oct-26 A	349,555.50	349,555.50	349,555.50	100%	100%	-59
	CONCRETE WORK	67	07-May-26	12-Jul-26	06-May-26 A	07-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	4

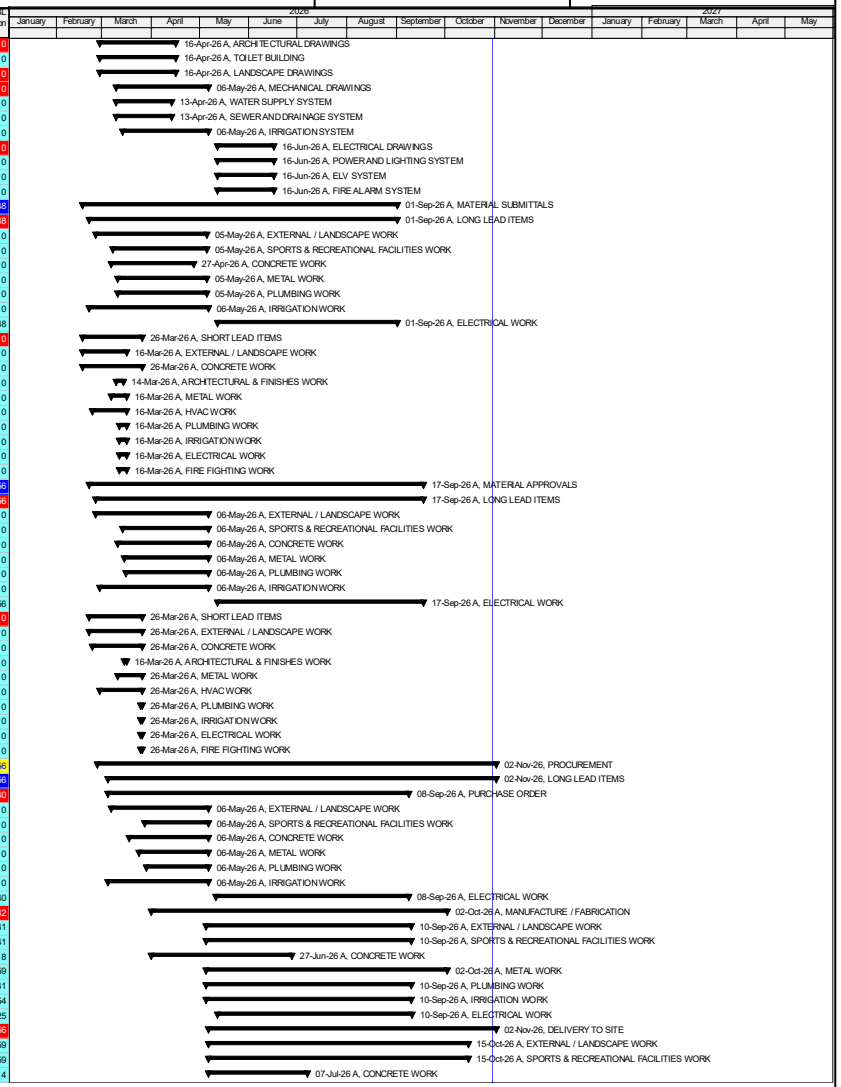


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	METAL WORK	130	07-May-26	06-Aug-26	06-May-26 A	02-Nov-26	8,003.07	7,180.43	8,003.07	100%	89.72%	-73
	PLUMBING WORK	130	07-May-26	06-Aug-26	06-May-26 A	15-Oct-26 A	31,985.55	31,985.55	31,985.55	100%	100%	-59
	IRRIGATION WORK	108	07-May-26	18-Jul-26	06-May-26 A	04-Sep-26 A	115,364.25	115,364.25	115,364.25	100%	100%	-41
	ELECTRICAL WORK	142	13-May-26	26-Aug-26	13-May-26 A	01-Nov-26	247,206.87	229,902.39	247,206.87	100%	93%	-55
	SHORT LEAD ITEMS	196	26-Feb-26	16-Jul-26	26-Feb-26 A	01-Nov-26	840,366.63	834,740.53	840,366.63	100%	99.33%	-90
	PURCHASE ORDER	156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	102	05-May-26	02-Jul-26	05-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	ELECTRICAL WORK	96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	DELIVERY TO SITE	194	01-Mar-26	16-Jul-26	01-Mar-26 A	01-Nov-26	840,366.63	834,740.53	840,366.63	100%	99.33%	-90
	EXTERNAL / LANDSCAPE WORK	166	01-Mar-26	16-Jul-26	01-Mar-26 A	01-Nov-26	649,200.96	643,574.86	649,200.96	100%	99.13%	-90
	CONCRETE WORK	52	10-Mar-26	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	73,026.09	73,026.09	73,026.09	100%	100%	0
	METAL WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	4,310.01	4,310.01	4,310.01	100%	100%	0
	HVAC WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	113	06-May-26	16-Jul-26	06-May-26 A	15-Oct-26 A	61,691.76	61,691.76	61,691.76	100%	100%	-77
	ELECTRICAL WORK	117	20-May-26	16-Jul-26	20-May-26 A	15-Oct-26 A	3,667.68	3,667.68	3,667.68	100%	100%	-77
	FIRE FIGHTING WORK	129	20-May-26	16-Jul-26	20-May-26 A	15-Oct-26 A	204.39	204.39	204.39	100%	100%	-77
	CONSTRUCTION STAGE	237	05-Apr-26	26-Nov-26	05-Apr-26 A	20-Dec-26	3,998,385.24	3,661,259.87	4,088,791.20	97.79%	89.54%	-20
	PLAYGROUND AND LANDSCAPING WORKS	237	05-Apr-26	26-Nov-26	05-Apr-26 A	20-Dec-26	3,669,891.66	3,385,068.45	3,760,297.62	97.6%	90.02%	-20
	CUT AND FILL	28	05-Apr-26	06-May-26	05-Apr-26 A	06-May-26 A	453,900.00	453,900.00	453,900.00	100%	100%	0
	PLAYGROUND WORKS	183	19-Apr-26	17-Nov-26	19-Apr-26 A	23-Nov-26	756,213.24	701,267.82	781,940.40	96.71%	89.68%	-5
	FOOTBALL PLAYGROUND WORKS	183	19-Apr-26	17-Nov-26	19-Apr-26 A	23-Nov-26	756,213.24	701,267.82	781,940.40	96.71%	89.68%	-5
	GENERAL SITE WORKS	227	16-Apr-26	26-Nov-26	16-Apr-26 A	20-Dec-26	1,218,906.42	1,036,800.73	1,224,114.42	99.57%	84.7%	-20
	FENCE WORKS	159	16-Apr-26	16-Aug-26	16-Apr-26 A	15-Oct-26 A	65,818.80	65,818.80	65,818.80	100%	100%	-51
	MECHANICAL WORK	156	12-May-26	06-Aug-26	12-May-26 A	16-Nov-26	421,027.74	358,530.44	421,027.74	100%	85.16%	-85
	STORM WATER AND UTILITY WORK	156	12-May-26	04-Aug-26	12-May-26 A	15-Nov-26	27,252.00	18,292.80	27,252.00	100%	67.12%	-87
	IRRIGATION SYSTEM WORKS	132	02-Jun-26	30-Jul-26	02-Jun-26 A	10-Nov-26	393,457.80	340,046.88	393,457.80	100%	86.43%	-87
	FIRE PROTECTION SYSTEM	2	05-Aug-26	06-Aug-26	11-Oct-26 A	16-Nov-26	317.94	190.76	317.94	100%	60%	-29
	ELECTRICAL WORK	198	20-May-26	20-Oct-26	20-May-26 A	05-Dec-26	539,251.68	442,997.39	539,251.68	100%	82.15%	-39
	POWER, LIGHTING & GROUNDING	163	20-May-26	08-Sep-26	20-May-26 A	23-Nov-26	482,181.48	403,048.25	482,181.48	100%	83.59%	-63
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	09-Sep-26	08-Oct-26	10-Oct-26 A	01-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-21
	FIRE ALARM SYSTEM	32	13-Sep-26	20-Oct-26	10-Oct-26 A	05-Dec-26	13,924.20	9,746.94	13,924.20	100%	70%	-17
	PARKING WORK	153	17-Jun-26	20-Oct-26	17-Jun-26 A	06-Dec-26	190,576.20	164,432.10	190,576.20	100%	86.28%	-39
	SERVICE CONNECTION	23	21-Oct-26	26-Nov-26	30-Jul-26 A	20-Dec-26	2,232.00	5,022.00	7,440.00	30%	67.5%	-90
	LANDSCAPING WORKS	162	31-May-26	09-Nov-26	30-May-26 A	06-Dec-26	1,192,581.60	1,159,115.00	1,252,052.40	95.25%	92.58%	-23
	HARDSCAPE WORK	162	31-May-26	09-Nov-26	30-May-26 A	06-Dec-26	1,041,342.60	1,012,515.50	1,046,213.40	99.53%	96.78%	-23
	SOFTSCAPE WORK	155	03-Jun-26	09-Nov-26	03-Jun-26 A	06-Dec-26	151,239.00	146,599.50	205,839.00	73.47%	71.22%	-23
	TANK WORKS	154	13-May-26	19-Sep-26	13-May-26 A	16-Nov-26	48,290.40	33,984.90	48,290.40	100%	70.38%	-49
	SEPTIC TANK	154	13-May-26	31-Aug-26	13-May-26 A	14-Nov-26	7,475.22	7,054.92	7,475.22	100%	94.38%	-63
	WATER STORAGE TANK	148	13-May-26	19-Sep-26	13-May-26 A	16-Nov-26	40,815.18	26,929.98	40,815.18	100%	65.98%	-49
	TOILET BUILDING WORKS	165	12-May-26	12-Oct-26	12-May-26 A	12-Nov-26	328,493.58	276,191.42	328,493.58	100%	84.08%	-27
	CIVIL WORK	165	12-May-26	12-Oct-26	12-May-26 A	11-Nov-26	230,766.78	194,328.66	230,766.78	100%	84.21%	-26
	STRUCTURAL WORK	59	12-May-26	22-Jul-26	12-May-26 A	23-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-1
	ARCHITECTURAL WORK	99	23-Jul-26	12-Oct-26	31-Jul-26 A	11-Nov-26	192,786.78	156,348.66	192,786.78	100%	81.1%	-19
	GENERAL FINISHES	99	23-Jul-26	12-Oct-26	31-Jul-26 A	11-Nov-26	87,769.20	62,097.24	87,769.20	100%	70.75%	-19
	WET AREA FINISHES	61	12-Aug-26	11-Oct-26	07-Aug-26 A	07-Nov-26	81,123.78	80,051.46	81,123.78	100%	98.68%	-27
	ROOF FINISHES	45	19-Sep-26	05-Oct-26	20-Aug-26 A	11-Nov-26	23,893.80	14,199.96	23,893.80	100%	59.43%	-57
	MEP WORK	81	28-Jul-26	06-Oct-26	22-Jul-26 A	12-Nov-26	97,726.80	81,862.76	97,726.80	100%	83.77%	-37
	MECANICAL WORKS	81	28-Jul-26	06-Oct-26	22-Jul-26 A	12-Nov-26	79,479.48	66,055.00	79,479.48	100%	83.11%	-37
	FIRE FIGHTING SYSTEM	1	06-Oct-26	06-Oct-26	11-Nov-26	12-Nov-26	136.26	0.00	136.26	100%	0%	0
	SEWER AND DRAINAGE SYSTEM	71	03-Aug-26	23-Aug-26	22-Jul-26 A	03-Nov-26	11,290.02	7,580.44	11,290.02	100%	67.14%	-71
	HVAC SYSTEM	31	28-Jul-26	15-Aug-26	13-Aug-26 A	31-Oct-26	12,127.20	9,821.76	12,127.20	100%	80.99%	-51
	WATER SUPPLY SYSTEM	56	01-Aug-26	20-Aug-26	30-Jul-26 A	01-Nov-26	55,926.00	48,652.80	55,926.00	100%	86.99%	-62
	ELECTRICAL WORKS	40	05-Aug-26	08-Sep-26	12-Aug-26 A	05-Nov-26	18,247.32	15,807.76	18,247.32	100%	86.63%	-42
	PROJECT CLOSOUT	190	25-May-26	15-Dec-26	25-May-26 A	07-Jan-27	20,443.96	171,729.23	681,465.20	3%	25.2%	-20
	TABUK	305	17-Feb-26	16-Dec-26	17-Feb-26 A	18-Feb-27	9,192,847.97	6,912,726.09	11,357,801.00	80.94%	60.86%	-55
	MOBILIZATION	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	43	17-Feb-26	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	171	17-Feb-26	12-Aug-26	17-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-30
	SHOP DRAWINGS SUBMITTALS	163	17-Feb-26	04-Aug-26	17-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	STRUCTURAL DRAWINGS	135	17-Feb-26	18-Jul-26	17-Feb-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	13

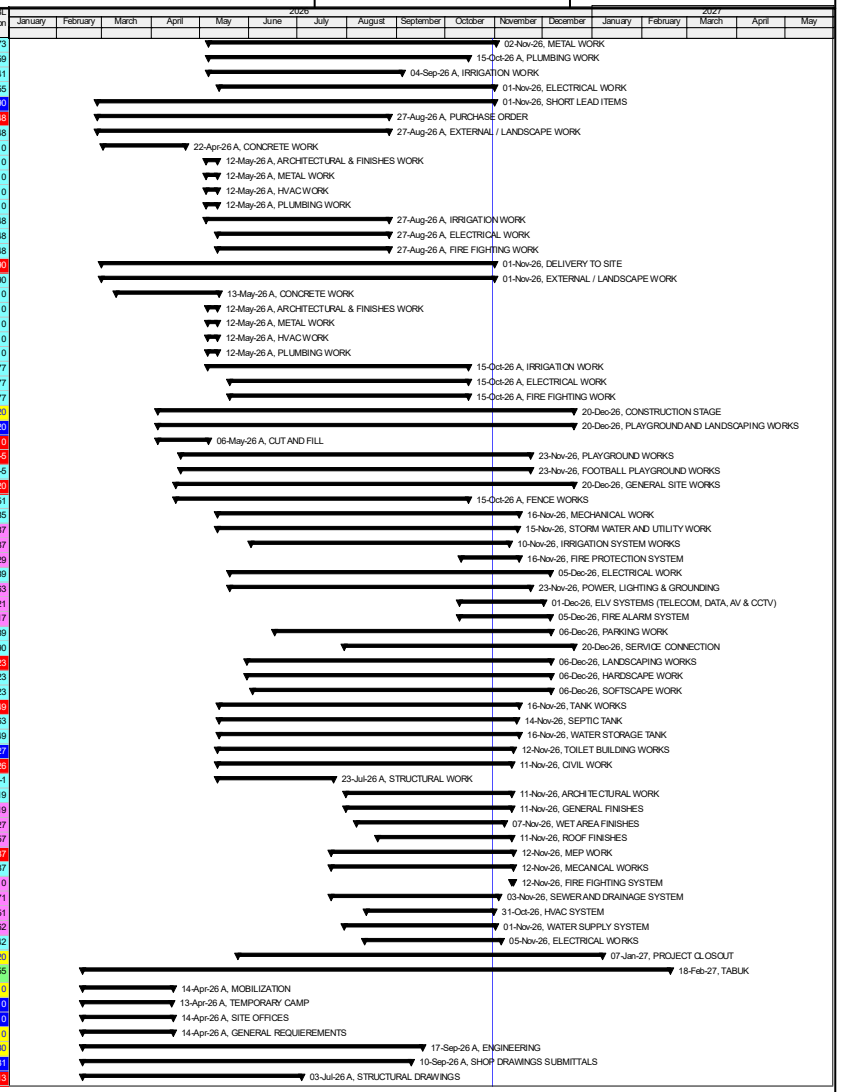


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	PROJECT FENCE	63	17-Feb-2	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	63	17-Feb-2	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	20	25-Jun-2	18-Jul-26	01-Jul-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	18
	TOILET BUILDING	41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	150	23-Feb-2	04-Aug-26	23-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	TOILET BUILDING	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-16
	LANDSCAPE DRAWINGS	40	23-Feb-2	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	140	28-Feb-2	12-Jul-26	28-Feb-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	-1
	WATER SUPPLY SYSTEM	32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	25-Jun-2	12-Jul-26	02-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	98	10-May-2	29-Jul-26	10-May-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	15
	POWER AND LIGHTING SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	30	25-Jun-2	29-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	26
	SHOP DRAWINGS APPROVALS	169	19-Feb-2	12-Aug-26	19-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
	STRUCTURAL DRAWINGS	138	19-Feb-2	23-Jul-26	19-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	12
	PROJECT FENCE	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	07-Jul-26	23-Jul-26	05-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	10
	TOILET BUILDING	42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	153	28-Feb-2	12-Aug-26	28-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
	TOILET BUILDING	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
	LANDSCAPE DRAWINGS	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	142	09-Mar-2	23-Jul-26	09-Mar-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	WATER SUPPLY SYSTEM	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	12-Mar-2	07-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	10	13-Jul-26	23-Jul-26	13-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	105	11-May-2	08-Aug-26	11-May-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
	POWER AND LIGHTING SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	23	13-Jul-26	08-Aug-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
	MATERIAL SUBMITTALS	166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	LONG LEAD ITEMS	166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	124	17-Feb-2	05-Jul-26	17-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-51
	CONCRETE WORK	41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	45	11-Mar-2	07-May-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	100	11-May-2	11-Jul-26	11-May-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	SHORT LEAD ITEMS	28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-2	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	160	21-Feb-2	13-Jul-26	21-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-56
	LONG LEAD ITEMS	157	25-Feb-2	13-Jul-26	25-Feb-26 A	17-Sep-26 A	284,659.98	284,659.98	284,659.98	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-2	05-May-26	25-Feb-26 A	05-May-26 A	15,425.28	15,425.28	15,425.28	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	02-Mar-2	11-Jul-26	02-Mar-26 A	03-Sep-26 A	238,773.54	238,773.54	238,773.54	100%	100%	-47
	CONCRETE WORK	38	11-Mar-2	28-Apr-26	11-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-2	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	42	15-Mar-2	06-May-26	15-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	45	11-Mar-2	06-May-26	11-Mar-26 A	06-May-26 A	6,802.65	6,802.65	6,802.65	100%	100%	0
	ELECTRICAL WORK	96	12-May-2	13-Jul-26	12-May-26 A	17-Sep-26 A	17,797.83	17,797.83	17,797.83	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	56,074.05	56,074.05	56,074.05	100%	100%	0

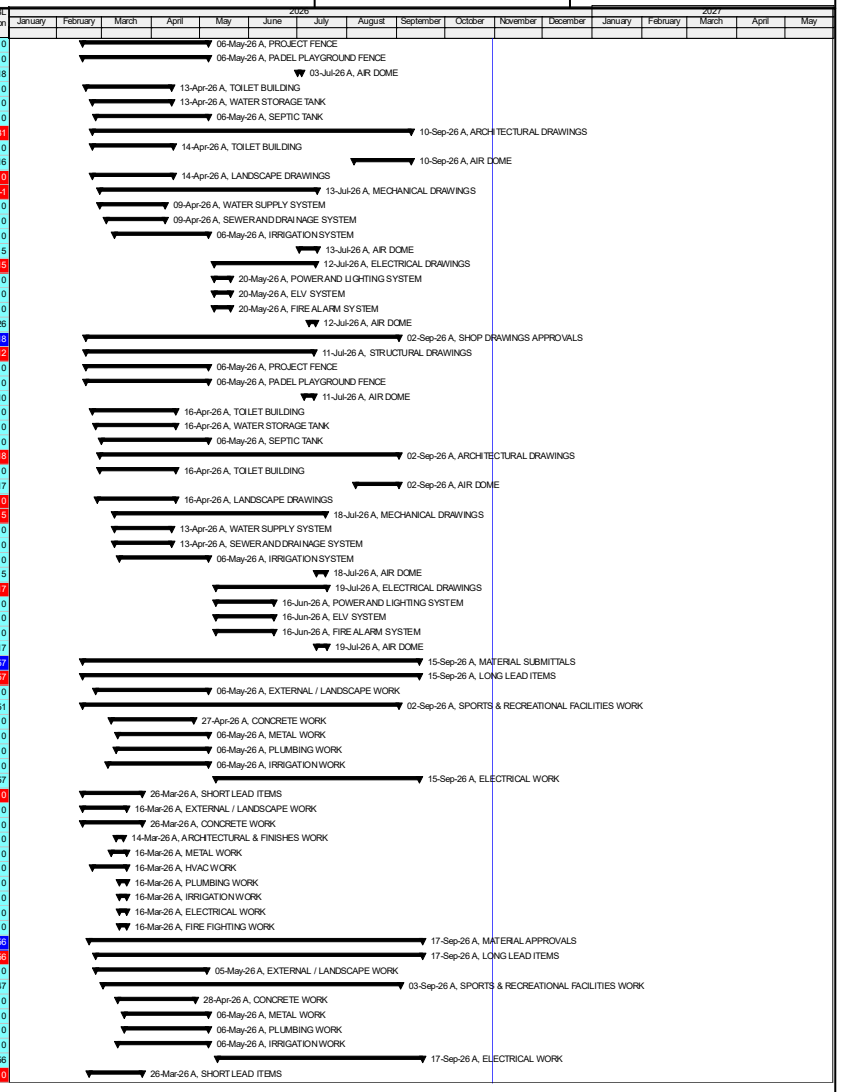

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	38,542.29	38,542.29	38,542.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,328.23	3,328.23	3,328.23	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	201	26-Feb-26	27-Aug-26	26-Feb-26 A	03-Nov-26	3,066,606.27	2,662,683.45	3,066,606.27	100%	86.83%	-57
	LONG LEAD ITEMS	194	07-Mar-26	27-Aug-26	07-Mar-26 A	03-Nov-26	2,561,939.82	2,161,684.91	2,561,939.82	100%	84.38%	-57
	PURCHASE ORDER	157	07-Mar-26	16-Jul-26	07-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	26-Mar-26	16-Jul-26	26-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	40	17-Mar-26	07-May-26	17-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	105	11-May-26	16-Jul-26	11-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
	MANUFACTURE / FABRICATION	140	29-Apr-26	16-Aug-26	29-Apr-26 A	15-Oct-26 A	0.00	0.00	0.00	0%	0%	-51
	EXTERNAL / LANDSCAPE WORK	102	06-May-26	23-Jul-26	06-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
	SPORTS & RECREATIONAL FACILITIES WORK	124	06-May-26	16-Aug-26	06-May-26 A	15-Oct-26 A	0.00	0.00	0.00	0%	0%	-51
	CONCRETE WORK	64	29-Apr-26	30-Jun-26	29-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	0%	0%	-2
	METAL WORK	119	06-May-26	23-Jul-26	06-May-26 A	27-Sep-26 A	0.00	0.00	0.00	0%	0%	-55
	PLUMBING WORK	102	06-May-26	23-Jul-26	06-May-26 A	14-Sep-26 A	0.00	0.00	0.00	0%	0%	-45
	IRRIGATION WORK	99	06-May-26	30-Jun-26	06-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-71
	ELECTRICAL WORK	129	12-May-26	10-Aug-26	12-May-26 A	30-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
	DELIVERY TO SITE	146	06-May-26	27-Aug-26	06-May-26 A	03-Nov-26	2,561,939.82	2,161,684.91	2,561,939.82	100%	84.38%	-57
	EXTERNAL / LANDSCAPE WORK	114	06-May-26	06-Aug-26	06-May-26 A	01-Nov-26	138,827.52	137,434.65	138,827.52	100%	99%	-72
	SPORTS & RECREATIONAL FACILITIES WORK	129	06-May-26	27-Aug-26	06-May-26 A	01-Nov-26	2,148,961.86	1,759,714.44	2,148,961.86	100%	81.89%	-55
	CONCRETE WORK	63	06-May-26	06-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	1
	METAL WORK	131	06-May-26	06-Aug-26	06-May-26 A	03-Nov-26	8,003.07	6,974.78	8,003.07	100%	87.15%	-75
	PLUMBING WORK	108	06-May-26	06-Aug-26	06-May-26 A	15-Oct-26 A	31,985.55	31,985.55	31,985.55	100%	100%	-59
	IRRIGATION WORK	98	06-May-26	05-Jul-26	06-May-26 A	31-Oct-26	61,223.85	59,587.38	61,223.85	100%	97.33%	-99
	ELECTRICAL WORK	140	13-May-26	24-Aug-26	13-May-26 A	01-Nov-26	160,180.47	153,230.61	160,180.47	100%	95.66%	-58
	SHORT LEAD ITEMS	190	26-Feb-26	22-Jul-26	26-Feb-26 A	01-Nov-26	504,666.45	500,998.54	504,666.45	100%	99.27%	-85
	PURCHASE ORDER	163	26-Feb-26	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
	EXTERNAL / LANDSCAPE WORK	163	26-Feb-26	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	97	11-May-26	02-Jul-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	94	11-May-26	29-Jun-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-51
	DELIVERY TO SITE	188	01-Mar-26	22-Jul-26	01-Mar-26 A	01-Nov-26	504,666.45	500,998.54	504,666.45	100%	99.27%	-85
	EXTERNAL / LANDSCAPE WORK	171	01-Mar-26	22-Jul-26	01-Mar-26 A	31-Oct-26	346,880.61	344,882.80	346,880.61	100%	99.42%	-85
	CONCRETE WORK	52	10-Mar-26	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	135	06-May-26	08-Jul-26	06-May-26 A	01-Nov-26	4,310.01	4,137.61	4,310.01	100%	96%	-97
	HVAC WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	97	06-May-26	05-Jul-26	06-May-26 A	31-Oct-26	29,954.07	28,456.37	29,954.07	100%	95%	-100
	ELECTRICAL WORK	118	13-May-26	16-Jul-26	13-May-26 A	15-Oct-26 A	3,667.68	3,667.68	3,667.68	100%	100%	-77
	FIRE FIGHTING WORK	126	13-May-26	09-Jul-26	13-May-26 A	15-Oct-26 A	204.39	204.39	204.39	100%	100%	-83
	CONSTRUCTION STAGE	269	24-Mar-26	14-Dec-26	24-Mar-26 A	06-Feb-27	5,751,434.27	3,623,092.02	6,814,680.60	84.4%	53.17%	-46
	PLAYGROUND AND LANDSCAPING WORKS	245	24-Mar-26	14-Dec-26	24-Mar-26 A	10-Jan-27	2,118,057.09	2,106,273.53	2,311,795.02	91.62%	91.11%	-22
	CUT AND FILL	38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	228,240.00	228,240.00	228,240.00	100%	100%	0
	PLAYGROUND WORKS	192	23-Apr-26	07-Dec-26	23-Apr-26 A	05-Dec-26	565,534.82	556,554.47	623,491.20	90.7%	89.26%	2
	FOOTBALL PLAYGROUND WORKS	176	23-Apr-26	17-Nov-26	23-Apr-26 A	16-Nov-26	308,593.08	304,408.43	333,290.16	92.59%	91.33%	1
	BASKETBALL PLAYGROUND WORKS	169	06-May-26	17-Nov-26	06-May-26 A	21-Nov-26	171,666.00	161,035.99	173,211.12	99.11%	92.97%	-2
	PADEL PLAYGROUND WORKS	181	06-May-26	07-Dec-26	06-May-26 A	05-Dec-26	85,275.74	91,110.05	116,989.92	72.89%	77.88%	2
	GENERAL SITE WORKS	225	16-Apr-26	14-Dec-26	16-Apr-26 A	10-Jan-27	622,911.97	550,687.65	656,604.42	94.87%	83.87%	-22
	FENCE WORKS	160	16-Apr-26	17-Aug-26	16-Apr-26 A	15-Oct-26 A	32,909.40	32,909.40	32,909.40	100%	100%	-50
	MECHANICAL WORK	160	12-May-26	10-Aug-26	12-May-26 A	21-Nov-26	230,187.54	201,030.97	230,187.54	100%	87.33%	-86
	STORM WATER AND UTILITY WORK	155	12-May-26	04-Aug-26	12-May-26 A	15-Nov-26	27,252.00	16,806.00	27,252.00	100%	61.67%	-86
	IRRIGATION SYSTEM WORKS	96	02-Jun-26	30-Jul-26	02-Jun-26 A	10-Nov-26	202,617.60	184,224.97	202,617.60	100%	90.92%	-86
	FIRE PROTECTION SYSTEM	5	05-Aug-26	10-Aug-26	15-Nov-26	21-Nov-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	180	08-Jun-26	07-Nov-26	08-Jun-26 A	20-Dec-26	344,811.26	279,538.59	345,859.68	99.7%	80.82%	-36
	POWER, LIGHTING & GROUNDING	153	08-Jun-26	27-Sep-26	08-Jun-26 A	03-Dec-26	288,789.48	240,981.87	288,789.48	100%	83.45%	-58




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 01-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	28-Sep-26	26-Oct-26	22-Sep-26 A	12-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-44
	FIRE ALARM SYSTEM	32	01-Oct-26	07-Nov-26	13-Oct-26 A	20-Dec-26	12,875.78	8,354.52	13,924.20	92.47%	60%	-26
	PARKING WORK	165	17-Jun-26	11-Nov-26	17-Jun-26 A	20-Dec-26	14,334.17	32,967.90	40,207.80	35.65%	81.99%	-32
	SERVICE CONNECTION	182	10-Jun-26	14-Dec-26	10-Jun-26 A	10-Jan-27	669.60	4,240.80	7,440.00	9%	57%	-22
	LANDSCAPING WORKS	156	31-May-26	22-Nov-26	30-May-26 A	17-Nov-26	653,079.90	733,167.09	755,169.00	86.46%	97.09%	4
	HARDSCAPE WORK	156	31-May-26	22-Nov-26	30-May-26 A	17-Nov-26	582,597.90	634,411.29	648,147.00	89.89%	97.88%	4
	SOFTSCAPE WORK	143	10-Jun-26	22-Nov-26	10-Jun-26 A	17-Nov-26	70,482.00	98,755.80	107,022.00	65.86%	92.28%	4
	TANK WORKS	150	13-May-26	27-Sep-26	13-May-26 A	10-Nov-26	48,290.40	37,624.32	48,290.40	100%	77.91%	-38
	SEPTIC TANK	149	13-May-26	03-Sep-26	13-May-26 A	08-Nov-26	7,475.22	7,223.04	7,475.22	100%	96.63%	-55
	WATER STORAGE TANK	150	13-May-26	27-Sep-26	13-May-26 A	10-Nov-26	40,815.18	30,401.28	40,815.18	100%	74.49%	-38
	AIR DOME CONSTRUCTION	226	13-May-26	03-Dec-26	13-May-26 A	06-Feb-27	3,308,532.80	1,210,693.39	4,178,041.20	79.19%	28.98%	-55
	CIVIL WORK	158	13-May-26	14-Sep-26	13-May-26 A	18-Nov-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-55
	ARCHITECTURAL WORK	25	05-Nov-26	03-Dec-26	09-Jan-27	06-Feb-27	0.00	0.00	712,953.22	0%	0%	0
	MECHANICAL WORK	23	15-Sep-26	12-Oct-26	19-Nov-26	15-Dec-26	667,968.77	0.00	667,968.77	100%	0%	0
	ELECTRICAL WORK	33	28-Sep-26	04-Nov-26	01-Dec-26	07-Jan-27	928,894.07	0.00	1,085,449.25	85.58%	0%	0
	TOILET BUILDING WORKS	143	12-May-26	28-Oct-26	12-May-26 A	04-Nov-26	324,844.38	306,125.10	324,844.38	100%	94.24%	-5
	CIVIL WORK	143	12-May-26	26-Oct-26	12-May-26 A	03-Nov-26	227,117.58	222,635.76	227,117.58	100%	98.03%	-7
	STRUCTURAL WORK	59	12-May-26	01-Aug-26	12-May-26 A	12-Aug-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-10
	ARCHITECTURAL WORK	76	02-Aug-26	26-Oct-26	01-Aug-26 A	03-Nov-26	189,137.58	184,655.76	189,137.58	100%	97.63%	-8
	GENERAL FINISHES	76	02-Aug-26	21-Oct-26	01-Aug-26 A	07-Sep-26 A	84,120.00	84,120.00	84,120.00	100%	100%	37
	WET AREA FINISHES	37	26-Aug-26	13-Oct-26	06-Aug-26 A	02-Nov-26	81,123.78	79,515.30	81,123.78	100%	98.02%	-33
	ROOF FINISHES	46	07-Oct-26	26-Oct-26	14-Aug-26 A	03-Nov-26	23,893.80	21,020.46	23,893.80	100%	87.97%	-52
	MEP WORK	103	16-Jun-26	28-Oct-26	16-Jun-26 A	04-Nov-26	97,726.80	83,489.34	97,726.80	100%	85.43%	-5
	MECANICAL WORKS	103	16-Jun-26	28-Oct-26	16-Jun-26 A	04-Nov-26	79,479.48	65,242.02	79,479.48	100%	82.09%	-5
	FIRE FIGHTING SYSTEM	2	27-Oct-26	28-Oct-26	23-Sep-26 A	04-Nov-26	136.26	81.76	136.26	100%	60%	-33
	SEWER AND DRAINAGE SYSTEM	92	16-Jun-26	05-Sep-26	16-Jun-26 A	01-Nov-26	11,290.02	10,322.30	11,290.02	100%	91.43%	-48
	HVAC SYSTEM	42	09-Aug-26	12-Oct-26	13-Aug-26 A	02-Nov-26	12,127.20	9,821.76	12,127.20	100%	80.99%	-13
	WATER SUPPLY SYSTEM	45	12-Aug-26	02-Sep-26	22-Jul-26 A	31-Oct-26	55,926.00	45,016.20	55,926.00	100%	80.49%	-67
	ELECTRICAL WORKS	38	15-Aug-26	17-Sep-26	22-Jul-26 A	16-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	-18
	PROJECT CLOSOUT	227	25-May-26	16-Dec-26	25-May-26 A	18-Feb-27	34,073.40	286,216.59	1,135,780.10	3%	25.2%	-55

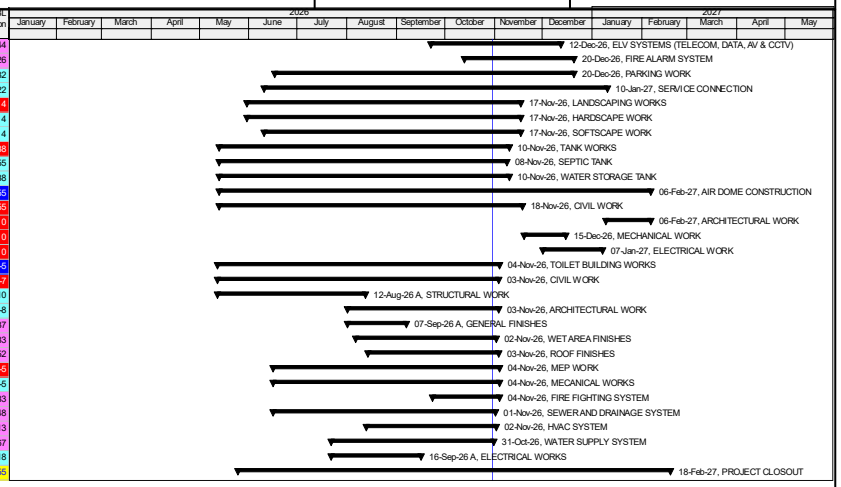

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
