
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oa		314	43.81%	44.23%	03-Mar-26	02-Jan-27	03-Mar-26 A	15-Mar-27	13,142,789.86	13,266,772.75	29,997,851.67	-57
KEY MILESTONES		312	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	15-Mar-27	0.00	0.00	0.00	-57
GENERAL MILESTONES		312	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	15-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-MS-1010	Project Commencement Date	0	100%	100%	03-Mar-26		03-Mar-26 A		0.00	0.00	0.00	0
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		15-Mar-27	0.00	0.00	0.00	-57
CONTRACTUAL MILESTONE		279	0%	0%	11-Apr-26	02-Jan-27	02-Apr-26 A	09-Mar-27	0.00	0.00	0.00	-55
MLTX-02-005-MS-1050	Completion of Mobilization	0	100%	100%		14-Apr-26		02-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-MS-1060	Baseline Programme Approval	0	100%	100%		11-Apr-26		04-Apr-26 A	0.00	0.00	0.00	6
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		02-Jan-27		09-Mar-27	0.00	0.00	0.00	-55
MLTX-02-005-MS-1100	Completion of Engineering	0	0%	0%		17-Dec-26		06-Jan-27	0.00	0.00	0.00	-16
MLTX-02-005-MS-1120	Completion of Levelling Works	0	100%	100%		06-Jul-26		02-May-26 A	0.00	0.00	0.00	53
MLTX-02-005-MS-1130	Completion of Toilet Building	0	0%	0%		31-Dec-26		23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		31-Dec-26		23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		31-Dec-26		09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		31-Dec-26		09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		31-Dec-26		23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		31-Dec-26		06-Mar-27	0.00	0.00	0.00	-53
ARAR		314	43.29%	40.54%	03-Mar-26	02-Jan-27	04-Mar-26 A	09-Mar-27	4,426,788.65	4,146,313.28	10,226,640.03	-55
MOBILIZATION		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	9
TOPOGRAPHIC SURVEY		4	0%	0%	03-Mar-26	07-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1320	Site Survey Works	4	100%	100%	03-Mar-26	07-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-1
SITE FACILITIES & OFFICES		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-MB-1340	Site Layout Plan	3	100%	100%	03-Mar-26	05-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-1350	Clear & Grub for Offices & Access Road	3	100%	100%	19-Mar-26	25-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-MB-1360	Construct Site Access Roads	3	100%	100%	07-Mar-26	09-Mar-26	09-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	-3
MLTX-02-005-MB-1370	Construct Temporary Fence	5	100%	100%	26-Mar-26	31-Mar-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-1380	Construct Site Offices & Storage	10	100%	100%	26-Mar-26	06-Apr-26	14-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	4
MLTX-02-005-MB-1390	Install Project Signs	8	100%	100%	10-Mar-26	18-Mar-26	14-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	-3
MLTX-02-005-MB-1400	Install Site Facilities	4	100%	100%	01-Apr-26	05-Apr-26	16-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-1410	Electrical Works & Connections	6	100%	100%	01-Apr-26	07-Apr-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-1420	Construct Parking Sheds	6	100%	100%	01-Apr-26	07-Apr-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-1430	Equipment Mobalization	5	100%	100%	19-Mar-26	28-Mar-26	26-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-MB-1440	Manpower Mobalization	3	100%	100%	12-Apr-26	14-Apr-26	24-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	10
PRELIMINARY SUBMITTALS		28	0%	0%	07-Mar-26	11-Apr-26	09-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	6
PREPARATIONS & SUBMITTAL BY CONTRACTORS		18	0%	0%	07-Mar-26	30-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-154	Preparation and Submittal of Detailed Work Order	10	100%	100%	16-Mar-26	30-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-155	Preparation and Submittal of Project Execution Plan	8	100%	100%	07-Mar-26	15-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-156	Submission of Contractor Project Quality Plan	8	100%	100%	16-Mar-26	28-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-157	Submission of Construction Safety & Environmental	8	100%	100%	16-Mar-26	28-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-158	Preparation and Submittal of Organization Chart	8	100%	100%	16-Mar-26	28-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-159	Preparation and Submittal of Communication Plan	8	100%	100%	16-Mar-26	28-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	6
APPROVALS BY EMPLOYERS		20	0%	0%	16-Mar-26	11-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-168	Approval of Detailed Work Order Programme (Baseline)	10	100%	100%	31-Mar-26	11-Apr-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-169	Approval of Project Execution Plan	10	100%	100%	16-Mar-26	30-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-170	Approval of Contractor Project Quality Plan	10	100%	100%	31-Mar-26	11-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-171	Approval of Construction Safety & Environmental	10	100%	100%	31-Mar-26	11-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-172	Approval of Organization Chart	10	100%	100%	31-Mar-26	11-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-173	Approval of Communication Plan	10	100%	100%	31-Mar-26	11-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	8
ENGINEERING		258	0%	0%	07-Mar-26	13-Dec-26	07-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	31
SHOP DRAWINGS		257	0%	0%	08-Mar-26	13-Dec-26	07-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	31
SHOP DRAWINGS SUBMISSION		233	0%	0%	08-Mar-26	08-Nov-26	07-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	1
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		46	0%	0%	08-Mar-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN-1	Shop DWG Submittal for Layout Plan	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-1	Shop DWG Submittal for Setting Out	16	100%	100%	08-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Grading Layout Plan	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN-1	Shop DWG Submittal for Curb Setting Out Points	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-1	Shop DWG Submittal for Signing & Marking Layout Plan	15	100%	100%	29-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN-1	Shop DWG Submittal for Standards Details	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		189	0%	0%	29-Mar-26	08-Nov-26	07-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	85
ARCHITECTURE WORKS		31	0%	0%	29-Mar-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN	Shop DWG Submittal for Floor Plan	15	100%	100%	29-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Shop DWG Submittal for Elevations	15	100%	100%	29-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40

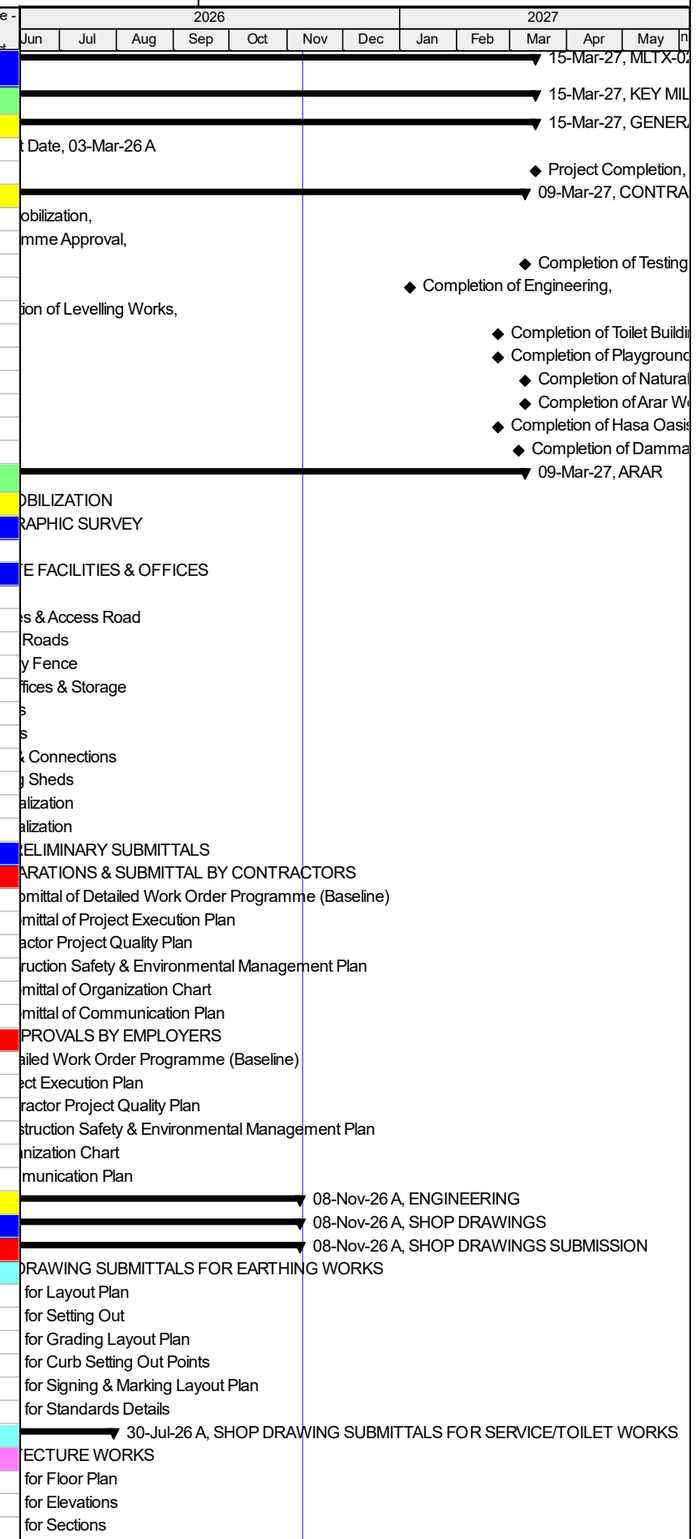

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Shop DWG Submittal for Ceiling Plan	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Finishes Plan	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Toilet Details	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Doors/Windows Schedule	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
STRUCTURE WORKS		67	0%	0%	04-May-26	23-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	102
MLTX-02-005-EM	Shop DWG Submittal for Foundation Plan	15	100%	100%	04-May-26	20-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	50
MLTX-02-005-EM	Shop DWG Submittal for Ground Floor Framing Plan	21	100%	100%	04-May-26	31-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	56
MLTX-02-005-EM	Shop DWG Submittal for Sections/Details	21	100%	100%	30-Jun-26	23-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	102
MECHANCAL WORKS		158	0%	0%	04-May-26	08-Nov-26	07-Mar-26 A	07-May-26 A	0.00	0.00	0.00	154
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Shop DWG Submittal for HVAC Equipment Schedule	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Shop DWG Submittal for Drainage Layout	30	100%	100%	04-May-26	10-Jun-26	07-Mar-26 A	07-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Drainage Details	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EM	Shop DWG Submittal for Dut Routing Layout	30	100%	100%	30-Jun-26	03-Aug-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	75
MLTX-02-005-EM	Shop DWG Submittal for Diffusers Layout	30	100%	100%	16-Jul-26	19-Aug-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	87
MLTX-02-005-EM	Shop DWG Submittal for Fire Fighting Layout	30	100%	100%	05-Oct-26	08-Nov-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	193
MLTX-02-005-EM	Shop DWG Submittal for Water Supply Layout	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Shop DWG Submittal for Water Supply Details	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
ELECTRICAL WORKS		90	0%	0%	04-May-26	19-Aug-26	12-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	30	100%	100%	23-May-26	29-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	81
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	30	100%	100%	30-Jun-26	03-Aug-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	74
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	09-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Shop DWG Submittal for Lighting Installation Details	30	100%	100%	30-Jun-26	03-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Cable Tray Installation Details	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	28
MLTX-02-005-EM	Shop DWG Submittal for Manhole & Ductbank Details	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	07-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Grounding Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	30	100%	100%	11-Jun-26	15-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	95
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection System Layout	30	100%	100%	11-Jun-26	15-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	95
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	30	100%	100%	11-Jun-26	15-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	95
MLTX-02-005-EM	Shop DWG Submittal for CCTV Details	30	100%	100%	04-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Shop DWG Submittal for CCTV Layout	30	100%	100%	11-Jun-26	15-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Layout	30	100%	100%	16-Jul-26	19-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	125
MLTX-02-005-EM	Shop DWG Submittal for Grounding Layout	30	100%	100%	11-Jun-26	15-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	95
MLTX-02-005-EM	Shop DWG Submittal for CCTV Riser Diagram	30	100%	100%	30-Jun-26	03-Aug-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	19
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Riser Diagram	30	100%	100%	16-Jul-26	19-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	125
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		233	0%	0%	08-Mar-26	07-Nov-26	08-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EM	Shop DWG Submittal for Playground Plan/Layout	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Furniture & Marking	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Shop DWG Submittal for Sections	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Interlock Pattern Plan	30	100%	100%	08-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Shop DWG Submittal for Doors/Windows Schedule	30	100%	100%	08-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Shop DWG Submittal for Dome Internal Layout	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
STRUCTURE WORKS		60	0%	0%	15-Apr-26	27-Jun-26	14-Mar-26 A	14-Jul-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Submittal for Air Dome System	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	07-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Foundation of Air Dome	30	100%	100%	04-May-26	10-Jun-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	30	100%	100%	20-May-26	27-Jun-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-15
AIR DOME SYSTEM		30	0%	0%	20-May-26	27-Jun-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Air Dome Structural Layout	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	07-May-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Membrane Panel Layout	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Cable Tension Layout	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Airlock Door Details	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Emergency Exit Details	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	26
SPORTS EQUIPMENT		30	0%	0%	20-May-26	27-Jun-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Shop DWG Submittal for Football Turf Installation	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Shop DWG Submittal for Basketball Court Marking	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Shop DWG Submittal for Padel Court Structure	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	25
MECHANCAL WORKS		30	0%	0%	20-May-26	27-Jun-26	14-Mar-26 A	03-May-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	03-May-26 A	0.00	0.00	0.00	44

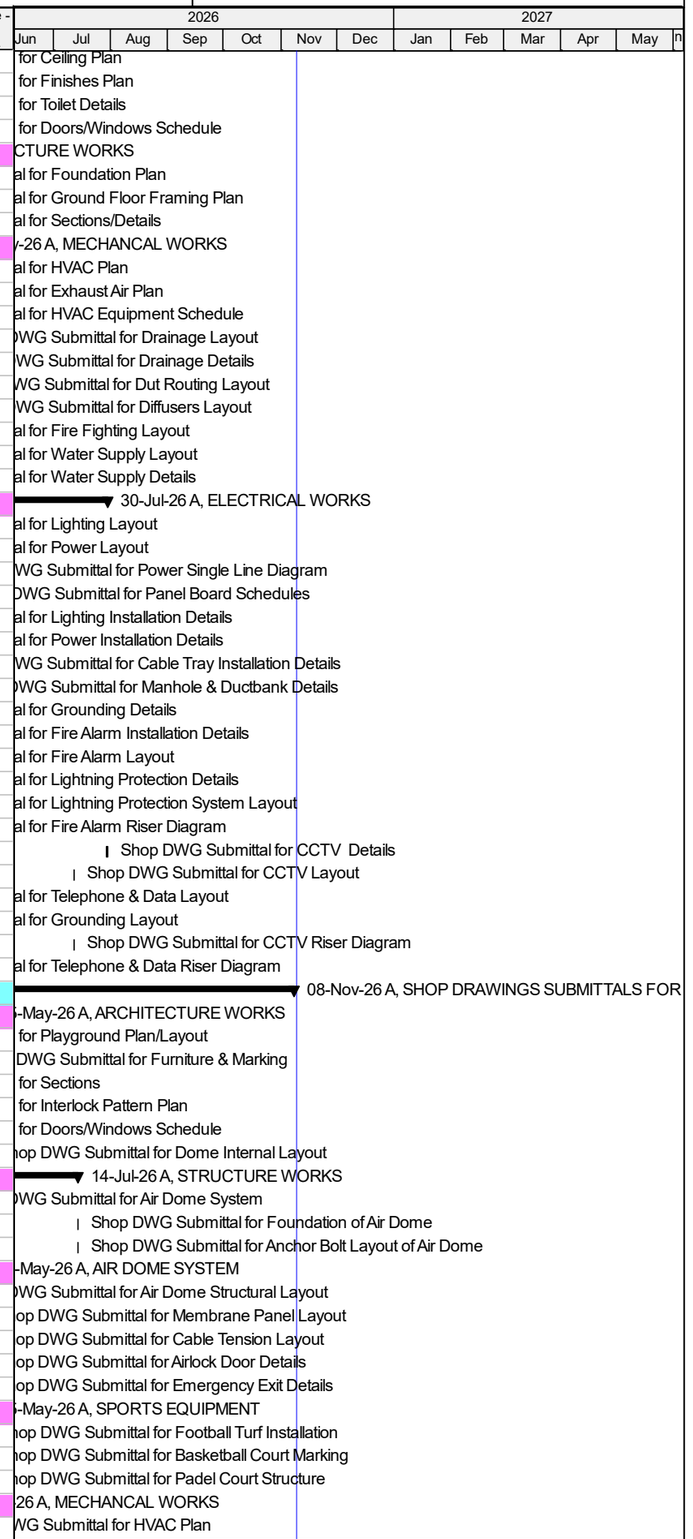

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	03-May-26 A	0.00	0.00	0.00	44
ELECTRICAL WORKS		173	0%	0%	20-May-26	07-Nov-26	14-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	27	100%	100%	19-Sep-26	20-Oct-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	30	100%	100%	30-Aug-26	04-Oct-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	98
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Installation Details	30	100%	100%	30-Aug-26	04-Oct-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Layout	15	100%	100%	19-Sep-26	06-Oct-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	30	100%	100%	20-May-26	27-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	30	100%	100%	20-May-26	27-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	15	100%	100%	21-Oct-26	07-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Shop DWG Submittal for CCTV Details	30	100%	100%	20-May-26	27-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN	Shop DWG Submittal for CCTV Layout	30	100%	100%	16-Jul-26	19-Aug-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN	Shop DWG Submittal for CCTV Riser Diagram	30	100%	100%	16-Jul-26	19-Aug-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-1
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		136	0%	0%	08-Mar-26	19-Aug-26	08-Mar-26 A	13-Jul-26 A	0.00	0.00	0.00	32
ARCHITECTURE WORKS		45	0%	0%	15-Apr-26	09-Jun-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Submittal for Landscape Layout	21	100%	100%	04-May-26	31-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	61
MLTX-02-005-EN	Shop DWG Submittal for Hardscape Plan	21	100%	100%	04-May-26	31-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	61
MLTX-02-005-EN	Shop DWG Submittal for Planting Plan	15	100%	100%	20-May-26	09-Jun-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Submittal for Landscape Details	15	100%	100%	15-Apr-26	02-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	39
MECHANCAL WORKS		60	0%	0%	08-Mar-26	19-May-26	08-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Details	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Layout	30	100%	100%	15-Apr-26	19-May-26	08-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	-10
ELECTRICAL WORKS		136	0%	0%	08-Mar-26	19-Aug-26	12-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Shop DWG Submittal for Lighting Details	30	100%	100%	16-Jul-26	19-Aug-26	13-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Shop DWG Submittal for Lighting Single Line Diagram	30	100%	100%	16-Jul-26	19-Aug-26	13-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Shop DWG Submittal for Lighting General Arrangement	30	100%	100%	08-Mar-26	14-Apr-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-73
MLTX-02-005-EN	Shop DWG Submittal for Lighting Network Layout	30	100%	100%	16-Jul-26	19-Aug-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	33
SHOP DRAWINGS APPROVALS		242	0%	0%	29-Mar-26	13-Dec-26	14-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	31
SHOP DRAWING APPROVAL FOR EARTHING WORKS		47	0%	0%	29-Mar-26	21-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN-2	Shop DWG Approval for Layout Plan	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-2	Shop DWG Approval for Setting Out	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-2	Shop DWG Approval for Grading Layout Plan	16	100%	100%	04-May-26	21-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN-2	Shop DWG Approval for Curb Setting Out Points	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-2	Shop DWG Approval for Signing & Marking Layout Plan	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	29
MLTX-02-005-EN-2	Shop DWG Approval for Standards Details	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		188	0%	0%	04-May-26	13-Dec-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	115
ARCHITECTURE WORKS		74	0%	0%	04-May-26	01-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	104
MLTX-02-005-EN	Shop DWG Approval for Floor Plan	30	100%	100%	25-Jun-26	29-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	102
MLTX-02-005-EN	Shop DWG Approval for Elevations	30	100%	100%	25-Jun-26	29-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	102
MLTX-02-005-EN	Shop DWG Approval for Sections	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Ceiling Plan	30	100%	100%	28-Jun-26	01-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	104
MLTX-02-005-EN	Shop DWG Approval for Finishes Plan	30	100%	100%	25-Jun-26	29-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	102
MLTX-02-005-EN	Shop DWG Approval for Toilet Details	30	100%	100%	25-Jun-26	29-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	102
MLTX-02-005-EN	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	25-Jun-26	29-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	102
STRUCTURE WORKS		76	0%	0%	01-Jun-26	27-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	122
MLTX-02-005-EN	Shop DWG Approval for Foundation Plan	4	100%	100%	24-Aug-26	27-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	122
MLTX-02-005-EN	Shop DWG Approval for Ground Floor Framing Plan	21	100%	100%	01-Jun-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN	Shop DWG Approval for Sections/Details	21	100%	100%	30-Jul-26	23-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	118
MECHANCAL WORKS		158	0%	0%	11-Jun-26	13-Dec-26	18-Mar-26 A	10-May-26 A	0.00	0.00	0.00	182
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EN	Shop DWG Approval for HVAC Equipment Schedule	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EN	Shop DWG Approval for Drainage Layout	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	09-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Drainage Details	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	09-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Duct Routing Layout	30	100%	100%	04-Aug-26	07-Sep-26	18-Mar-26 A	10-May-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Shop DWG Approval for Diffusers Layout	30	100%	100%	20-Aug-26	24-Sep-26	18-Mar-26 A	10-May-26 A	0.00	0.00	0.00	114
MLTX-02-005-EN	Shop DWG Approval for Fire Fighting Layout	30	0.33%	100%	09-Nov-26	13-Dec-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	213
MLTX-02-005-EN	Shop DWG Approval for Water Supply Layout	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EN	Shop DWG Approval for Water Supply Details	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
ELECTRICAL WORKS		143	0%	0%	11-Jun-26	25-Nov-26	18-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	30	100%	100%	30-Jun-26	03-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	101
MLTX-02-005-EN	Shop DWG Approval for Power Layout	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	30	100%	100%	04-Aug-26	07-Sep-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	104
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	30	100%	100%	04-Aug-26	07-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	45

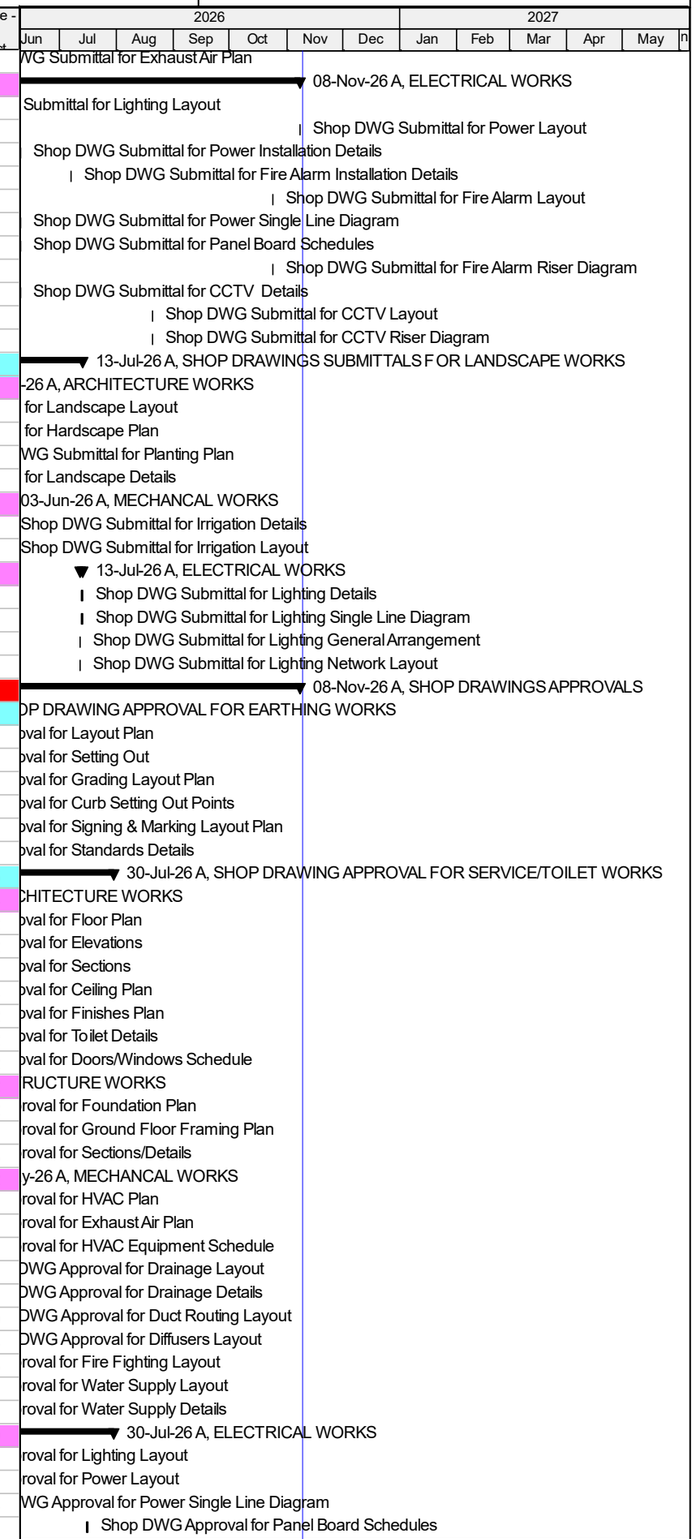

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Shop DWG Approval for Lighting Installation Details	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EI	Shop DWG Approval for Cable Tray Installation Details	30	100%	100%	04-Aug-26	07-Sep-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	104
MLTX-02-005-EI	Shop DWG Approval for Manhole & Ductbank Details	30	100%	100%	04-Aug-26	07-Sep-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	104
MLTX-02-005-EI	Shop DWG Approval for Grounding Details	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Installation Details	30	50.33%	100%	22-Oct-26	25-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	198
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Layout	30	50.33%	100%	22-Oct-26	25-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	198
MLTX-02-005-EI	Shop DWG Approval for Lightning Protection Details	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EI	Shop DWG Approval for Lightning Protection System Layout	30	100%	100%	04-Aug-26	07-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	131
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Riser Diagram	30	50.33%	100%	22-Oct-26	25-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	198
MLTX-02-005-EI	Shop DWG Approval for CCTV Details	30	100%	100%	11-Jun-26	15-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EI	Shop DWG Approval for CCTV Layout	30	100%	100%	16-Jul-26	19-Aug-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	17
MLTX-02-005-EI	Shop DWG Approval for Telephone & Data Layout	30	100%	100%	20-Aug-26	24-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	145
MLTX-02-005-EI	Shop DWG Approval for Grounding Layout	30	100%	100%	16-Jul-26	19-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	115
MLTX-02-005-EI	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	20-Aug-26	24-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	47
MLTX-02-005-EI	Shop DWG Approval for Telephone & Data Riser Diagram	30	100%	100%	20-Aug-26	24-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	145
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		212	0%	0%	03-May-26	13-Dec-26	14-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	31
ARCHITECTURE WORKS		187	0%	0%	03-May-26	17-Sep-26	14-Mar-26 A	24-Oct-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EI	Shop DWG Approval for Playground Plan/Layout	15	100%	100%	03-May-26	19-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	44
MLTX-02-005-EI	Shop DWG Approval for Furniture & Marking	30	100%	100%	20-May-26	27-Jun-26	14-Mar-26 A	12-May-26 A	0.00	0.00	0.00	36
MLTX-02-005-EI	Shop DWG Approval for Sections	15	100%	100%	11-Jun-26	28-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	75
MLTX-02-005-EI	Shop DWG Approval for Interlock Pattern Plan	30	100%	100%	15-Aug-26	17-Sep-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	145
MLTX-02-005-EI	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	15-Jul-26	18-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	119
MLTX-02-005-EI	Shop DWG Approval for Dome Internal Layout	26	100%	100%	15-Jul-26	13-Aug-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-60
STRUCTURE WORKS		38	0%	0%	15-Aug-26	28-Sep-26	19-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	62
MLTX-02-005-EI	Shop DWG Approval for Air Dome System	30	100%	100%	15-Aug-26	17-Sep-26	19-Mar-26 A	09-May-26 A	0.00	0.00	0.00	110
MLTX-02-005-EI	Shop DWG Approval for Foundation of Air Dome	30	100%	100%	24-Aug-26	28-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	62
MLTX-02-005-EI	Shop DWG Approval for Foundation of Air Dome	30	100%	100%	24-Aug-26	28-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	62
MLTX-02-005-EI	Shop DWG Approval for Anchor Bolt Layout of Air Dome	30	100%	100%	24-Aug-26	28-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	62
AIR DOME SYSTEM		101	0%	0%	28-Jun-26	17-Sep-26	19-Mar-26 A	24-Oct-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EI	Shop DWG Approval for Air Dome Structural Layout	30	100%	100%	15-Aug-26	17-Sep-26	19-Mar-26 A	09-May-26 A	0.00	0.00	0.00	110
MLTX-02-005-EI	Shop DWG Approval for Membrane Panel Layout	15	100%	100%	28-Jun-26	14-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-86
MLTX-02-005-EI	Shop DWG Approval for Cable Tension Layout	13	100%	100%	30-Jun-26	14-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-86
MLTX-02-005-EI	Shop DWG Approval for Airlock Door Details	13	100%	100%	15-Jul-26	29-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-73
MLTX-02-005-EI	Shop DWG Approval for Emergency Exit Details	13	100%	100%	30-Jul-26	13-Aug-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-60
SPORTS EQUIPMENT		84	0%	0%	15-Aug-26	13-Dec-26	20-Jul-26 A	24-Oct-26 A	0.00	0.00	0.00	43
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	13	100%	100%	15-Aug-26	29-Aug-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EI	Shop DWG Approval for Basketball Court Marking	30	100%	100%	19-Sep-26	24-Oct-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	50
MLTX-02-005-EI	Shop DWG Approval for Padel Court Structure	30	0.33%	100%	09-Nov-26	13-Dec-26	20-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	124
MECHANCAL WORKS		60	0%	0%	30-Aug-26	08-Nov-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	157
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	30	100%	100%	30-Aug-26	04-Oct-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	30	100%	100%	05-Oct-26	08-Nov-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	157
ELECTRICAL WORKS		167	0%	0%	28-Jun-26	08-Dec-26	13-Jun-26 A	08-Nov-26 A	0.00	0.00	0.00	27
MLTX-02-005-EI	Shop DWG Approval for Lighting Layout	23	100%	100%	26-Sep-26	21-Oct-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Shop DWG Approval for Power Layout	13	0.77%	100%	09-Nov-26	23-Nov-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	14
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	13	0%	100%	24-Nov-26	08-Dec-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	27
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	30	100%	100%	21-Jul-26	24-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	33
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	20	100%	100%	28-Jun-26	20-Jul-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	32
MLTX-02-005-EI	Shop DWG Approval for CCTV Details	25	100%	100%	21-Jul-26	18-Aug-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EI	Shop DWG Approval for CCTV Layout	3	100%	100%	20-Aug-26	23-Aug-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	20-Aug-26	24-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	25
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		140	0%	0%	15-Apr-26	29-Sep-26	15-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	63
ARCHITECTURE WORKS		30	0%	0%	20-May-26	27-Jun-26	15-Mar-26 A	19-May-26 A	0.00	0.00	0.00	30
MLTX-02-005-EI	Shop DWG Approval for Landscape Layout	21	100%	100%	01-Jun-26	24-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	72
MLTX-02-005-EI	Shop DWG Approval for Hardscape Plan	21	100%	100%	01-Jun-26	24-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	72
MLTX-02-005-EI	Shop DWG Approval for Planting Plan	15	100%	100%	10-Jun-26	27-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	30
MLTX-02-005-EI	Shop DWG Approval for Landscape Details	21	100%	100%	20-May-26	16-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	65
MECHANCAL WORKS		60	0%	0%	15-Apr-26	27-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EI	Shop DWG Approval for Irrigation Details	30	100%	100%	15-Apr-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EI	Shop DWG Approval for Irrigation Layout	30	100%	100%	20-May-26	27-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
ELECTRICAL WORKS		140	0%	0%	15-Apr-26	29-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	63
MLTX-02-005-EI	Shop DWG Approval for Lighting Details	30	100%	100%	20-Aug-26	24-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	59
MLTX-02-005-EI	Shop DWG Approval for Lighting Single Line Diagram	30	100%	100%	25-Aug-26	29-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	63
MLTX-02-005-EI	Shop DWG Approval for Lighting General Arrangement	30	100%	100%	15-Apr-26	19-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-47

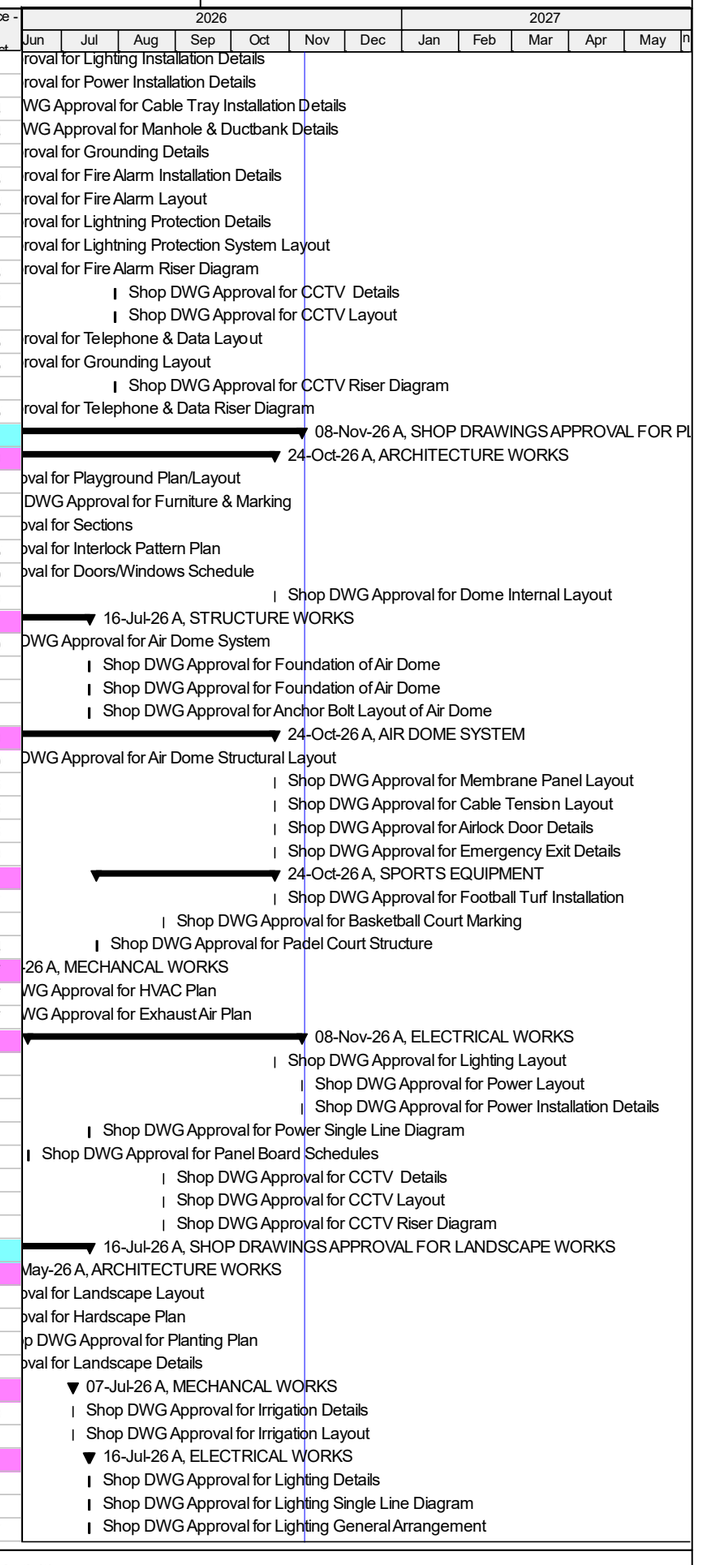

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Approval for Lighting Network Layout	30	100%	100%	20-Aug-26	24-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	59
METHOD STATEMENTS		219	0%	0%	07-Mar-26	24-Nov-26	07-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	62
METHOD STATEMENT SUBMITTAL		156	0%	0%	07-Mar-26	10-Sep-26	07-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	84
CIVIL WORKS		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Concrete	30	100%	100%	07-Mar-26	13-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	21	100%	100%	07-Mar-26	02-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	14
ARCHITECTURE WORKS		156	0%	0%	07-Mar-26	10-Sep-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	86
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Plastering	15	100%	100%	02-May-26	18-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	53
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	19-May-26	25-Jun-26	07-Mar-26 A	11-May-26 A	0.00	0.00	0.00	36
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Tilling	30	100%	100%	21-Jul-26	24-Aug-26	07-Mar-26 A	17-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	21-Jul-26	24-Aug-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	71
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	04-Jul-26	06-Aug-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Parking	30	100%	100%	08-Aug-26	10-Sep-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Soft	30	100%	100%	16-Jun-26	20-Jul-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	41
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Fence	30	100%	100%	19-May-26	25-Jun-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Air Dome	30	100%	100%	19-May-26	25-Jun-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Metal	30	100%	100%	19-May-26	25-Jun-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Partitions	30	100%	100%	19-May-26	25-Jun-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Gypsum	30	100%	100%	09-May-26	15-Jun-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	11
MECHANICAL WORKS		111	0%	0%	28-Mar-26	06-Aug-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	54
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	28-Mar-26	30-Apr-26	12-Mar-26 A	02-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Water	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	02-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Fire	30	100%	100%	04-Apr-26	07-May-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Irrigation	15	100%	100%	19-May-26	08-Jun-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for HVAC	30	100%	100%	04-Jul-26	06-Aug-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	54
ELECTRICAL WORKS		120	0%	0%	14-Apr-26	03-Sep-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	96
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	27-Jun-26	30-Jul-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for CCTV	30	100%	100%	27-Jun-26	30-Jul-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Lighting	30	100%	100%	27-Jun-26	30-Jul-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	27-Jun-26	30-Jul-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	70
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Panel	30	100%	100%	27-Jun-26	30-Jul-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Electrical	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Lighting	30	100%	100%	01-Aug-26	03-Sep-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	96
METHOD STATEMENT APPROVAL		174	0%	0%	02-May-26	24-Nov-26	12-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	62
CIVIL WORKS		66	0%	0%	09-Jun-26	24-Aug-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	96
MLTX-02-005-EN-4	Approval of Method Statement for Earthwork	15	100%	100%	04-Jul-26	20-Jul-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-4	Approval of Method Statement for Concrete Works	30	100%	100%	21-Jul-26	24-Aug-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	96
MLTX-02-005-EN-4	Approval of Method Statement for Waterproofing	21	100%	100%	09-Jun-26	02-Jul-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	51
ARCHITECTURE WORKS		120	0%	0%	27-Jun-26	14-Nov-26	12-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	53
MLTX-02-005-EN-4	Approval of Method Statement for Plastering Works	30	100%	100%	06-Aug-26	09-Sep-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	110
MLTX-02-005-EN-4	Approval of Method Statement for Masonary Works	30	100%	100%	27-Jun-26	30-Jul-26	12-Mar-26 A	24-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN-4	Approval of Method Statement for Tilling Works	30	100%	100%	25-Aug-26	29-Sep-26	12-Mar-26 A	24-May-26 A	0.00	0.00	0.00	106
MLTX-02-005-EN-4	Approval of Method Statement for Seats/Benches Works	30	100%	100%	10-Sep-26	15-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	28
MLTX-02-005-EN-4	Approval of Method Statement for Doors/Windows Works	30	100%	100%	08-Aug-26	10-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN-4	Approval of Method Statement for Interlock/Curbstone Works	30	100%	100%	06-Aug-26	09-Sep-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	106
MLTX-02-005-EN-4	Approval of Method Statement for Parking Works	30	100%	100%	12-Sep-26	17-Oct-26	20-May-26 A	20-May-26 A	0.00	0.00	0.00	124
MLTX-02-005-EN-4	Approval of Method Statement for Soft Scape Works	30	100%	100%	06-Aug-26	09-Sep-26	19-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN-4	Approval of Method Statement for Fence Works	20	100%	100%	14-Jul-26	05-Aug-26	19-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-4	Approval of Method Statement for Air Dome Works	30	100%	100%	10-Sep-26	15-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	28
MLTX-02-005-EN-4	Approval of Method Statement for Partitions Works	30	100%	100%	05-Sep-26	10-Oct-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN-4	Approval of Method Statement for Gypsum Board Works	30	83.67%	100%	11-Oct-26	14-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	72
MECHANICAL WORKS		174	0%	0%	02-May-26	24-Nov-26	14-Jun-26 A	26-Aug-26 A	0.00	0.00	0.00	76
MLTX-02-005-EN-4	Approval of Method Statement for Sewage/Drainage System	30	100%	100%	02-May-26	08-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN-4	Approval of Method Statement for Water Supply System	30	100%	100%	06-Aug-26	09-Sep-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-4	Approval of Method Statement for Fire Fighting System	30	53.67%	100%	21-Oct-26	24-Nov-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	76
MLTX-02-005-EN-4	Approval of Method Statement for Irrigation System	15	100%	100%	09-Jun-26	25-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-4	Approval of Method Statement for HVAC System	30	100%	100%	08-Aug-26	10-Sep-26	14-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	43
ELECTRICAL WORKS		120	0%	0%	19-May-26	10-Oct-26	06-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN-4	Approval of Method Statement for Electrical Conduits/Pulling	30	100%	100%	19-May-26	25-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	17
MLTX-02-005-EN-4	Approval of Method Statement for Lighting Poles Installation	30	100%	100%	05-Sep-26	10-Oct-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN-4	Approval of Method Statement for Telecommunication & Data	30	100%	100%	06-Aug-26	09-Sep-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-4	Approval of Method Statement for CCTV System	30	100%	100%	06-Aug-26	09-Sep-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	75

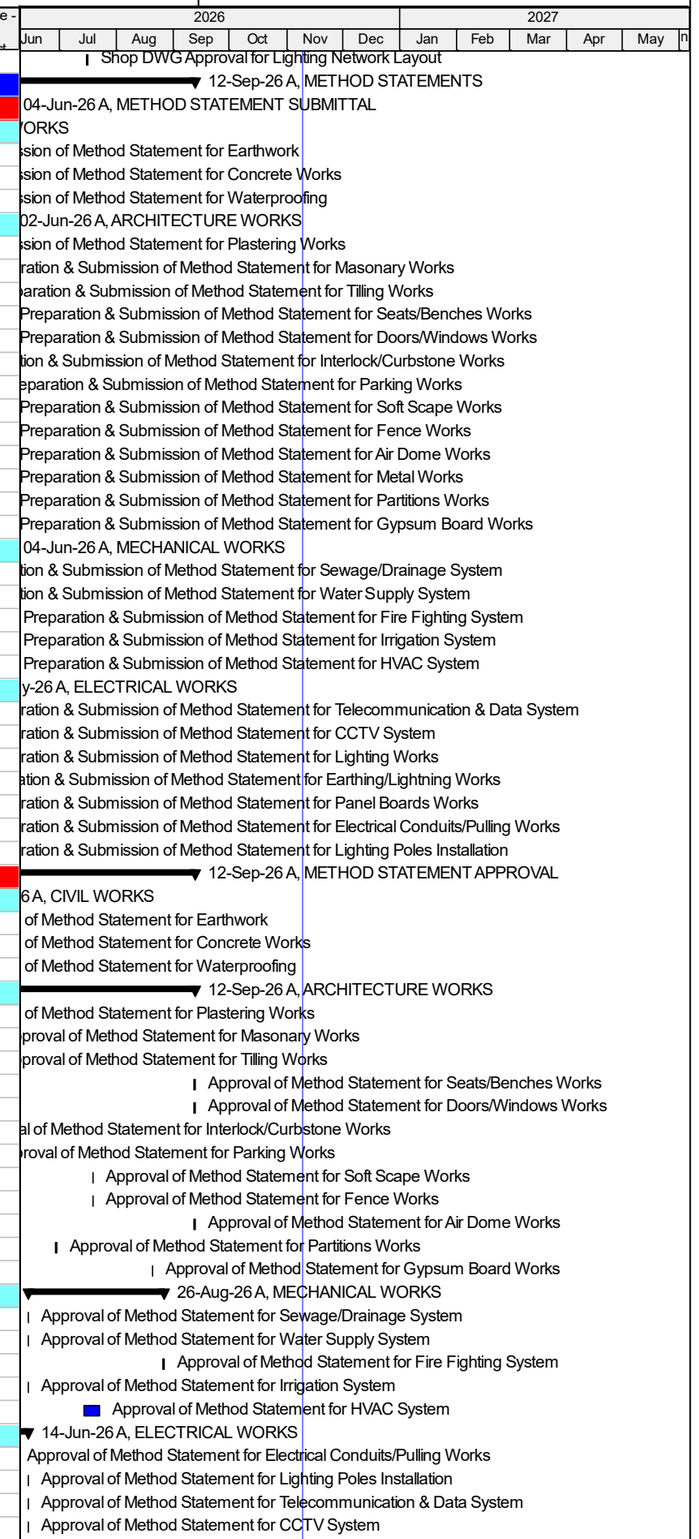

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-4	Approval of Method Statement for Lighting Works	30	100%	100%	06-Aug-26	09-Sep-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-4	Approval of Method Statement for Earthing/Lightning Works	30	100%	100%	01-Aug-26	03-Sep-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	70
MLTX-02-005-EN-4	Approval of Method Statement for Panel Boards Works	30	100%	100%	01-Aug-26	03-Sep-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	70
PRE-QUALIFICATION & MATERIAL		174	0%	0%	07-Mar-26	03-Oct-26	07-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	17
PRE-QUALIFICATION		138	0%	0%	07-Mar-26	20-Aug-26	07-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	64
TOILET/SERVICE WORKS		138	0%	0%	07-Mar-26	20-Aug-26	07-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	64
STEEL REINFORCEMENT		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Reinforcement	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Steel Reinforcement	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
READY MIX CONCRETE		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Ready Mixed Concrete	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval of Ready Mixed Concrete	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
CONCRETE BLOCKS		90	0%	0%	07-Mar-26	25-Jun-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
MLTX-02-005-EN	Pre-Qualification Submittal for Concrete Blocks	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	09-Jun-26	25-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
WATER PROOFING		90	0%	0%	07-Mar-26	25-Jun-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
MLTX-02-005-EN	Pre-Qualification Submittal for Water Proofing	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Water Proofing	30	100%	100%	19-May-26	25-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
FLOOR/WALL TILES		90	0%	0%	07-Mar-26	25-Jun-26	07-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	65
MLTX-02-005-EN	Pre-Qualification Submittal for Tilling Materials	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EN	Pre-Qualification Approval for Tailling Material	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	65
SUSPENDED CEILING		90	0%	0%	07-Mar-26	25-Jun-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
MLTX-02-005-EN	Pre-Qualification Submittal for Suspend Ceiling	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Suspend Ceiling	15	100%	100%	09-Jun-26	25-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
DOORS/WINDOWS		90	0%	0%	07-Mar-26	25-Jun-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
MLTX-02-005-EN	Pre-Qualification Submittal for Doors/Windows	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Doors/Windows	15	100%	100%	09-Jun-26	25-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	78
FURNITURES		90	0%	0%	07-Mar-26	25-Jun-26	07-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	65
MLTX-02-005-EN	Pre-Qualification Submittal for Furnitures	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Approval for Furnitures	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	65
SANITARY FIXTURES		45	0%	0%	07-Mar-26	30-Apr-26	07-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Sanitary Fixtures	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	05-Apr-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Approval for Sanitary Fixtures	15	100%	100%	14-Apr-26	30-Apr-26	10-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	18
WATER SUPPLY PIPES		90	0%	0%	07-Mar-26	25-Jun-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	73
MLTX-02-005-EN	Pre-Qualification Submittal for Water Supply Pipes	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	23-Mar-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Approval for Water Supply Pipes	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	73
SEWAGE/DRAINAGE PIPES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	23-Mar-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	13
PACKAGE AC UNITS		30	0%	0%	02-May-26	08-Jun-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	02-May-26	18-May-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	19-May-26	08-Jun-26	14-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	50
AIR DIFUSSERS/GRILLS		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Pre-Qualification Submittal for Air Diffusers/Grills	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN	Pre-Qualification Approval for Air Diffusers/Grills	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	16
GALVANIZED DUCTS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Ducts	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Ducts	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	19
LIGHTING FIXTURES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting Fixtures	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EN	Pre-Qualification Approval for Lighting Fixtures	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
SWITCHES/SOCKETS		30	0%	0%	09-Jun-26	13-Jul-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Pre-Qualification Submittal for Switches/Sockets	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Pre-Qualification Approval for Switches/Sockets	15	100%	100%	27-Jun-26	13-Jul-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	31
EARTHING SYSTEM		30	0%	0%	09-Jun-26	13-Jul-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Pre-Qualification Submittal for Earthing System	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	38
MLTX-02-005-EN	Pre-Qualification Approval for Earthing System	15	100%	100%	27-Jun-26	13-Jul-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	51
DISTRIBUTION PANNELS		33	0%	0%	14-Jul-26	20-Aug-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	88
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Panels	15	100%	100%	14-Jul-26	30-Jul-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Panels	15	100%	100%	04-Aug-26	20-Aug-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	88
PLAYGROUND WORKS		126	0%	0%	07-Mar-26	06-Aug-26	07-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	52

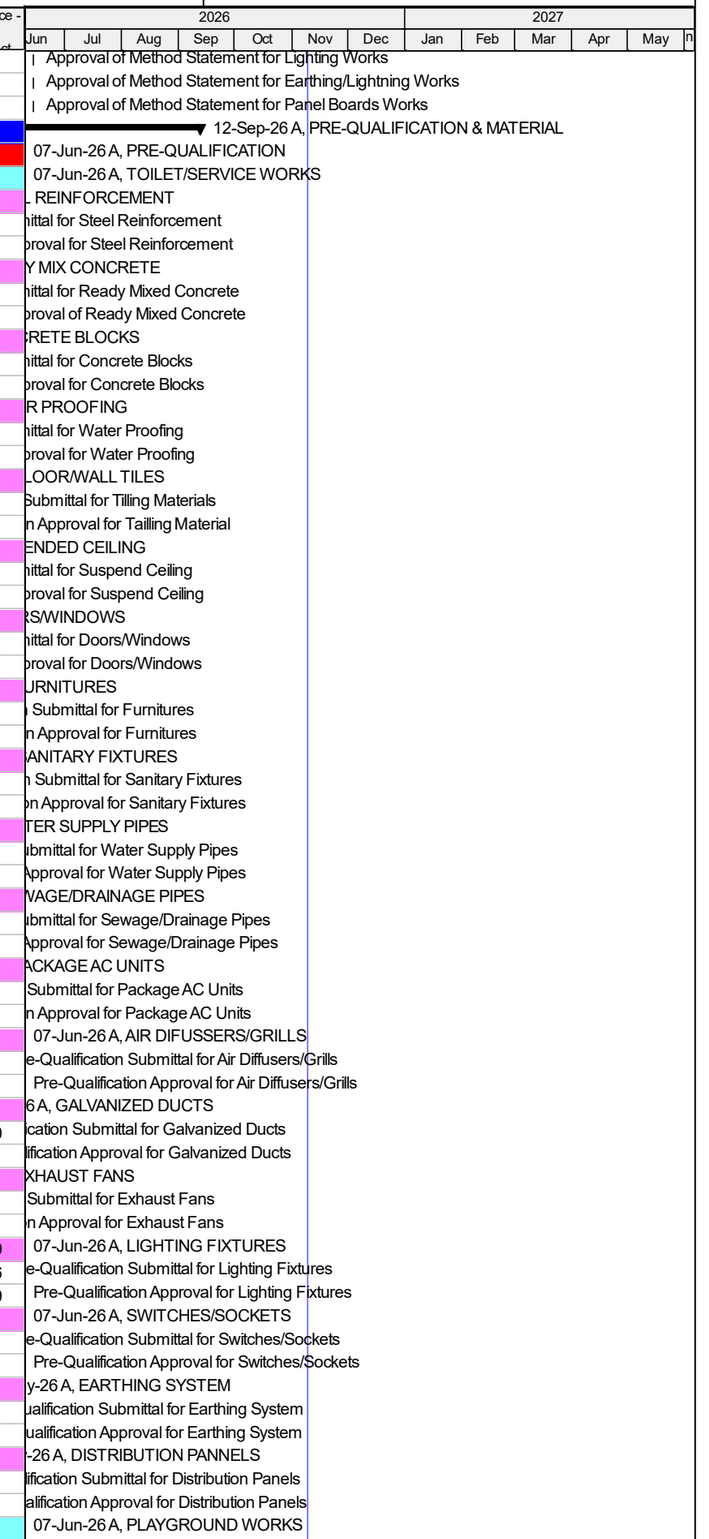

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PVC MEMBRANE		126	0%	0%	07-Mar-26	06-Aug-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	61
MLTX-02-005-EI	Pre-Qualification Submittal for PVC Membrane	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-50
MLTX-02-005-EI	Pre-Qualification Approval for PVC Membrane	21	100%	100%	14-Jul-26	06-Aug-26	10-Mar-26 A	20-May-26 A	0.00	0.00	0.00	64
STEEL TENSION CABLES		60	0%	0%	02-May-26	13-Jul-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Pre-Qualification Submittal for Steel Tension Cables	15	100%	100%	02-May-26	18-May-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Pre-Qualification Approval for Steel Tension Cables	15	100%	100%	27-Jun-26	13-Jul-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	40
EMERGENCY DOORS		33	0%	0%	19-May-26	29-Jun-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	28
MLTX-02-005-EI	Pre-Qualification Submittal for Emergency Doors	15	100%	100%	19-May-26	08-Jun-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EI	Pre-Qualification Approval for Emergency Doors	15	100%	100%	13-Jun-26	29-Jun-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	28
PRESSURE UNITS		45	0%	0%	02-May-26	25-Jun-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EI	Pre-Qualification Submittal for Pressure Units	15	100%	100%	02-May-26	18-May-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Pre-Qualification Approval for Pressure Units	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	25
AIR LOCK DOORS		45	0%	0%	02-May-26	25-Jun-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EI	Pre-Qualification Submittal for Lock Doors	15	100%	100%	02-May-26	18-May-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Pre-Qualification Approval for Lock Doors	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	25
ARTIFICIAL TURF		45	0%	0%	07-Mar-26	30-Apr-26	07-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	18
MLTX-02-005-EI	Pre-Qualification Submittal for Artificial TURF	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Pre-Qualification Approval for Artificial TURF	30	100%	100%	28-Mar-26	30-Apr-26	10-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	18
RUBBER GRANULES		81	0%	0%	02-May-26	06-Aug-26	07-Mar-26 A	10-May-26 A	0.00	0.00	0.00	73
MLTX-02-005-EI	Pre-Qualification Submittal for Rubber Granules	15	100%	100%	02-May-26	18-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EI	Pre-Qualification Approval for Rubber Granules	21	100%	100%	14-Jul-26	06-Aug-26	10-Mar-26 A	10-May-26 A	0.00	0.00	0.00	73
PADEL GLASS		60	0%	0%	02-May-26	13-Jul-26	07-Mar-26 A	10-May-26 A	0.00	0.00	0.00	52
MLTX-02-005-EI	Pre-Qualification Submittal for Padel Glass	15	100%	100%	02-May-26	18-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EI	Pre-Qualification Approval for Padel Glass	15	100%	100%	27-Jun-26	13-Jul-26	10-Mar-26 A	10-May-26 A	0.00	0.00	0.00	52
PADEL WIRE MESH/STEEL SETS		105	0%	0%	07-Mar-26	13-Jul-26	07-Mar-26 A	10-May-26 A	0.00	0.00	0.00	52
MLTX-02-005-EI	Pre-Qualification Submittal for Wire Mesh/Steel Sets	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Wire Mesh/Steel Sets	15	100%	100%	27-Jun-26	13-Jul-26	10-Mar-26 A	10-May-26 A	0.00	0.00	0.00	52
AGGREGATE BASE COURSE		36	0%	0%	07-Mar-26	20-Apr-26	07-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EI	Pre-Qualification Submittal for Aggregate Base Course	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EI	Pre-Qualification Approval for Aggregate Base Course	21	100%	100%	28-Mar-26	20-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-5
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	4
MLTX-02-005-EI	Pre-Qualification Submittal for Bituminous Base & Wearing	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EI	Pre-Qualification Approval for the Site	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	4
INTERLOCKING PAVING		30	0%	0%	19-May-26	25-Jun-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	77
MLTX-02-005-EI	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	19-May-26	08-Jun-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	67
MLTX-02-005-EI	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	09-Jun-26	25-Jun-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	77
MARKING PAINT		30	0%	0%	30-Jun-26	03-Aug-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	71
MLTX-02-005-EI	Pre-Qualification Submittal for Marking Paint	15	100%	100%	30-Jun-26	16-Jul-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	59
MLTX-02-005-EI	Pre-Qualification Approval for Marking Paint	15	100%	100%	18-Jul-26	03-Aug-26	14-Mar-26 A	09-May-26 A	0.00	0.00	0.00	71
PACKAGE AC UNITS		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	65
MLTX-02-005-EI	Pre-Qualification Submittal for Package AC Units	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	55
MLTX-02-005-EI	Pre-Qualification Approval for Package AC Units	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	65
AIR DIFUSSERS/GRILLS		30	0%	0%	09-Jun-26	13-Jul-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	60
MLTX-02-005-EI	Pre-Qualification Submittal for Air Difussers/Grills	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	49
MLTX-02-005-EI	Pre-Qualification Approval for Air Difussers/Grills	15	100%	100%	27-Jun-26	13-Jul-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	60
GALVANIZED DUCTS		30	0%	0%	09-Jun-26	13-Jul-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	60
MLTX-02-005-EI	Pre-Qualification Submittal for Galvanized Duct	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	49
MLTX-02-005-EI	Pre-Qualification Approval for Galvanized Duct	15	100%	100%	27-Jun-26	13-Jul-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	60
EXHAUST FANS		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	64
MLTX-02-005-EI	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	55
MLTX-02-005-EI	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	64
DISTRIBUTION BOARDS		30	0%	0%	09-Jun-26	13-Jul-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	31
MLTX-02-005-EI	Pre-Qualification Submittal for Distribution Boards	15	100%	100%	09-Jun-26	25-Jun-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	24
MLTX-02-005-EI	Pre-Qualification Approval for Distribution Boards	15	100%	100%	27-Jun-26	13-Jul-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	31
POWER CABLES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EI	Pre-Qualification Submittal for Power Cables	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Pre-Qualification Approval for Power Cables	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
LIGHT FIXTURES		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	16
MLTX-02-005-EI	Pre-Qualification Submittal for Light Fixtures	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EI	Pre-Qualification Approval for Light Fixtures	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	16
CCTV MATERIALS		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	16
MLTX-02-005-EI	Pre-Qualification Submittal for CCTV	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EI	Pre-Qualification Approval for CCTV	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	16
POWER OUTLETS/SWITCHES		30	0%	0%	14-Apr-26	18-May-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-14

2026: Jun | Jul | Aug | Sep | Oct | Nov | Dec
2027: Jan | Feb | Mar | Apr | May

-May-26 A, PVC MEMBRANE
e-Qualification Submittal for PVC Membrane
-Qualification Approval for PVC Membrane
-May-26 A, STEEL TENSION CABLES
-Qualification Submittal for Steel Tension Cables
e-Qualification Approval for Steel Tension Cables
-May-26 A, EMERGENCY DOORS
-Qualification Submittal for Emergency Doors
e-Qualification Approval for Emergency Doors
-May-26 A, PRESSURE UNITS
-Qualification Submittal for Pressure Units
e-Qualification Approval for Pressure Units
-May-26 A, AIR LOCK DOORS
-Qualification Submittal for Lock Doors
e-Qualification Approval for Lock Doors
RTIFICIAL TURF
Submittal for Artificial TURF
n Approval for Artificial TURF
y-26 A, RUBBER GRANULES
alification Submittal for Rubber Granules
ualification Approval for Rubber Granules
y-26 A, PADEL GLASS
alification Submittal for Padel Glass
ualification Approval for Padel Glass
y-26 A, PADEL WIRE MESH/STEEL SETS
alification Submittal for Wire Mesh/Steel Sets
ualification Approval for Wire Mesh/Steel Sets
A, AGGREGATE BASE COURSE
ation Submittal for Aggregate Base Course
ication Approval for Aggregate Base Course
A, BITUMINOUS BASE & WEARING COURSE
ation Submittal for Bituminous Base & Wearing Cource
ication Approval for the Site
RLOCKING PAVING
mittal for Interlocking Block Pavers
proval for Interlocking Block Pavers
y-26 A, MARKING PAINT
alification Submittal for Marking Paint
ualification Approval for Marking Paint
ACKAGE AC UNITS
Submittal for Package AC Units
n Approval for Package AC Units
6 A, AIR DIFUSSERS/GRILLS
ication Submittal for Air Difussers/Grills
ification Approval for Air Difussers/Grills
6 A, GALVANIZED DUCTS
ication Submittal for Galvanized Duct
ification Approval for Galvanized Duct
XHAUST FANS
Submittal for Exhaust Fans
n Approval for Exhaust Fans
07-Jun-26 A, DISTRIBUTION BOARDS
e-Qualification Submittal for Distribution Boards
Pre-Qualification Approval for Distribution Boards
y-26 A, POWER CABLES
ualification Submittal for Power Cables
ualification Approval for Power Cables
07-Jun-26 A, LIGHT FIXTURES
e-Qualification Submittal for Light Fixtures
Pre-Qualification Approval for Light Fixtures
07-Jun-26 A, CCTV MATERIALS
e-Qualification Submittal for CCTV
Pre-Qualification Approval for CCTV
07-Jun-26 A, POWER OUTLETS/SWITCHES

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Power Outlets/Switches	15	100%	100%	14-Apr-26	30-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Approval for Power Outlets/Switches	15	100%	100%	02-May-26	18-May-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-14
LANDSCAPE WORKS		75	0%	0%	28-Mar-26	25-Jun-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	36
INTERLOCKING PAVING		30	0%	0%	14-Apr-26	18-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	14-Apr-26	30-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	02-May-26	18-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	47
CURBSTONE		30	0%	0%	28-Mar-26	30-Apr-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Pre-Qualification Submittal for Curbstone	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Pre-Qualification Approval for Curbstone	15	100%	100%	14-Apr-26	30-Apr-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
PAVEMENT MARKING		30	0%	0%	14-Apr-26	18-May-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Pre-Qualification Submittal for Pavement Markings	15	100%	100%	14-Apr-26	30-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Approval for Pavement Markings	15	100%	100%	02-May-26	18-May-26	14-Mar-26 A	09-May-26 A	0.00	0.00	0.00	8
TRAFFIC SIGNS		30	0%	0%	02-May-26	08-Jun-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Submittal for Traffic Signs	15	100%	100%	02-May-26	18-May-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Traffic Signs	15	100%	100%	19-May-26	08-Jun-26	14-Mar-26 A	09-May-26 A	0.00	0.00	0.00	23
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
AGRICULTURE SOIL		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EN	Pre-Qualification Submittal for Agriculture Soil	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	44
MLTX-02-005-EN	Pre-Qualification Approval for Agriculture Soil	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	41
TRACK SURFACE		30	0%	0%	14-Apr-26	18-May-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Submittal for Track Surface	15	100%	100%	14-Apr-26	30-Apr-26	10-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Track Surface	15	100%	100%	02-May-26	18-May-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
GRASS/TREES		30	0%	0%	02-May-26	08-Jun-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Submittal for Grass/Trees	15	100%	100%	02-May-26	18-May-26	10-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	29
MLTX-02-005-EN	Pre-Qualification Approval for Grass/Trees	15	100%	100%	19-May-26	08-Jun-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	26
CABLES		30	0%	0%	19-May-26	25-Jun-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	36
MLTX-02-005-EN	Pre-Qualification Submittal for Cables	15	100%	100%	19-May-26	08-Jun-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Approval for Cables	15	100%	100%	09-Jun-26	25-Jun-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	36
LIGHT POLES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting poles	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN	Pre-Qualification Approval for Lighting poles	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MATERIAL SUBMITTAL & APPROVAL		144	0%	0%	14-Apr-26	03-Oct-26	18-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	17
TOILET/SERVICE WORKS		138	0%	0%	14-Apr-26	26-Sep-26	18-Mar-26 A	11-Jul-26 A	0.00	0.00	0.00	65
STEEL REINFORCEMENT		90	0%	0%	14-Apr-26	30-Jul-26	18-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN	Material Submittal for Steel Reinforcement	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Material Approval for Steel Reinforcement	15	100%	100%	14-Jul-26	30-Jul-26	25-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	91
READY MIX CONCRETE		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Submittal for Ready Mixed Concrete	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Material Approval of Ready Mixed Concrete	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
CONCRETE BLOCKS		30	0%	0%	27-Jun-26	30-Jul-26	18-Mar-26 A	11-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Material Submittal for Concrete Blocks	15	100%	100%	27-Jun-26	13-Jul-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Material Approval for Concrete Blocks	15	100%	100%	14-Jul-26	30-Jul-26	25-Mar-26 A	11-May-26 A	0.00	0.00	0.00	66
FLOOR/WALL TILES		30	0%	0%	27-Jun-26	30-Jul-26	18-Mar-26 A	17-May-26 A	0.00	0.00	0.00	61
MLTX-02-005-EN	Material Submittal for Tilling Materials	15	100%	100%	27-Jun-26	13-Jul-26	18-Mar-26 A	13-May-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN	Material Approval for Tilling Material	15	100%	100%	14-Jul-26	30-Jul-26	25-Mar-26 A	17-May-26 A	0.00	0.00	0.00	61
SUSPENDED CEILING		30	0%	0%	14-Jul-26	17-Aug-26	18-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Material Submittal for Suspend Ceiling	15	100%	100%	14-Jul-26	30-Jul-26	18-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	88
MLTX-02-005-EN	Material Approval for Suspend Ceiling	15	100%	100%	01-Aug-26	17-Aug-26	25-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	100
DOORS/WINDOWS		30	0%	0%	14-Jul-26	17-Aug-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Material Submittal for Doors/Windows	15	100%	100%	14-Jul-26	30-Jul-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	70
MLTX-02-005-EN	Material Approval for Doors/Windows	15	100%	100%	01-Aug-26	17-Aug-26	25-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	106
FURNITURES		30	0%	0%	14-Jul-26	17-Aug-26	18-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	110
MLTX-02-005-EN	Material Submittal for Furnitures	15	100%	100%	14-Jul-26	30-Jul-26	18-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	99
MLTX-02-005-EN	Material Approval for Furnitures	15	100%	100%	01-Aug-26	17-Aug-26	25-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	110
SANITARY FIXTURES		30	0%	0%	02-May-26	08-Jun-26	18-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	42
MLTX-02-005-EN	Material Submittal for Sanitary Fixtures	15	100%	100%	02-May-26	18-May-26	18-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Material Approval for Sanitary Fixtures	15	100%	100%	19-May-26	08-Jun-26	25-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	42
WATER SUPPLY PIPES		45	0%	0%	27-Jun-26	17-Aug-26	18-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	102
MLTX-02-005-EN	Material Submittal for Water Supply Pipes	15	100%	100%	27-Jun-26	13-Jul-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	83
MLTX-02-005-EN	Material Approval for Water Supply Pipes	15	100%	100%	01-Aug-26	17-Aug-26	25-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	102
SEWAGE/DRAINAGE PIPES		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Material Submittal for Sewage/Drainage Pipes	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	23



© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Sewage/Drainage Pipes	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
PACKAGE AC UNITS		33	0%	0%	18-Aug-26	26-Sep-26	21-Jun-26 A	02-Jul-26 A	0.00	0.00	0.00	72
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	18-Aug-26	03-Sep-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	64
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	08-Sep-26	26-Sep-26	02-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	72
AIR DIFUSSERS/GRILLS		30	0%	0%	14-Jul-26	17-Aug-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	57
MLTX-02-005-EM	Material Submittal for Air Diffusers/Grills	15	100%	100%	14-Jul-26	30-Jul-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	42
MLTX-02-005-EM	Material Approval for Air Diffusers/Grills	15	100%	100%	01-Aug-26	17-Aug-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	57
GALVANIZED DUCTS		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-EM	Material Submittal for Galvanized Ducts	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Material Approval for Galvanized Ducts	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
EXHAUST FANS		30	0%	0%	02-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	02-May-26	18-May-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	19-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
LIGHTING FIXTURES		30	0%	0%	02-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Material Submittal for Lighting Fixtures	15	100%	100%	02-May-26	18-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Approval for Lighting Fixtures	15	100%	100%	19-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
SWITCHES/SOCKETS		30	0%	0%	14-Jul-26	17-Aug-26	25-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Material Submittal for Switches/Sockets	15	100%	100%	14-Jul-26	30-Jul-26	25-Jun-26 A	25-Jun-26 A	0.00	0.00	0.00	30
MLTX-02-005-EM	Material Approval for Switches/Sockets	15	100%	100%	01-Aug-26	17-Aug-26	27-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	44
EARTHING SYSTEM		30	0%	0%	14-Jul-26	17-Aug-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	74
MLTX-02-005-EM	Material Submittal for Earthing System	15	100%	100%	14-Jul-26	30-Jul-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EM	Material Approval for Earthing System	15	100%	100%	01-Aug-26	17-Aug-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	74
DISTRIBUTION PANNELS		30	0%	0%	22-Aug-26	26-Sep-26	19-Mar-26 A	18-Jun-26 A	0.00	0.00	0.00	84
MLTX-02-005-EM	Material Submittal for Distribution Panels	15	100%	100%	22-Aug-26	07-Sep-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	99
MLTX-02-005-EM	Material Approval for Distribution Panels	15	100%	100%	08-Sep-26	26-Sep-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	84
PLAYGROUND WORKS		138	0%	0%	21-Apr-26	03-Oct-26	18-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	17
PVC MEMBRANE		42	0%	0%	08-Aug-26	26-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Material Submittal for PVC Membrane	21	100%	100%	08-Aug-26	31-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	4
MLTX-02-005-EM	Material Approval for PVC Membrane	21	100%	100%	01-Sep-26	26-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	25
STEEL TENSION CABLES		30	0%	0%	14-Jul-26	17-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EM	Material Submittal for Steel Tension Cables	15	100%	100%	14-Jul-26	30-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Approval for Steel Tension Cables	15	100%	100%	01-Aug-26	17-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-8
EMERGENCY DOORS		30	0%	0%	14-Jul-26	17-Aug-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Submittal for Emergency Doors	15	100%	100%	14-Jul-26	30-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Approval for Emergency Doors	15	100%	100%	01-Aug-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
PRESSURE UNITS		30	0%	0%	14-Jul-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Submittal for Pressure Units	15	100%	100%	14-Jul-26	30-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-37
MLTX-02-005-EM	Material Approval for Pressure Units	15	100%	100%	01-Aug-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-21
AIR LOCK DOORS		30	0%	0%	14-Jul-26	17-Aug-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Submittal for Lock Doors	15	100%	100%	14-Jul-26	30-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Approval for Lock Doors	15	100%	100%	01-Aug-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
ARTIFICIAL TURF		60	0%	0%	02-May-26	13-Jul-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Material Submittal for Artificial TURF	30	100%	100%	02-May-26	08-Jun-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EM	Material Approval for Artificial TURF	30	100%	100%	09-Jun-26	13-Jul-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	44
RUBBER GRANULES		48	0%	0%	08-Aug-26	03-Oct-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	113
MLTX-02-005-EM	Material Submittal for Rubber Granules	21	100%	100%	08-Aug-26	31-Aug-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	90
MLTX-02-005-EM	Material Approval for Rubber Granules	21	100%	100%	08-Sep-26	03-Oct-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	113
PADEL GLASS		30	0%	0%	14-Jul-26	17-Aug-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	74
MLTX-02-005-EM	Material Submittal for Padel Glass	15	100%	100%	14-Jul-26	30-Jul-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EM	Material Approval for Padel Glass	15	100%	100%	01-Aug-26	17-Aug-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	74
PADEL WIRE MESH/STEEL SETS		30	0%	0%	14-Jul-26	17-Aug-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	74
MLTX-02-005-EM	Material Submittal for Wire Mesh/Steel Sets	15	100%	100%	14-Jul-26	30-Jul-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EM	Material Approval for Wire Mesh/Steel Sets	15	100%	100%	01-Aug-26	17-Aug-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	74
AGGREGATE BASE COURSE		42	0%	0%	21-Apr-26	11-Jun-26	18-Mar-26 A	03-May-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Submittal for Aggregate Base Course	21	100%	100%	21-Apr-26	14-May-26	18-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Approval for Aggregate Base Course	21	100%	100%	16-May-26	11-Jun-26	25-Mar-26 A	03-May-26 A	0.00	0.00	0.00	31
BITUMINOUS BASE & WEARING COURSE		33	0%	0%	16-May-26	25-Jun-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	42
MLTX-02-005-EM	Material Submittal for Bituminous Base & Wearing Cource	15	100%	100%	16-May-26	04-Jun-26	19-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	27
MLTX-02-005-EM	Material Approval for the Site	15	100%	100%	09-Jun-26	25-Jun-26	26-Mar-26 A	04-May-26 A	0.00	0.00	0.00	42
INTERLOCKING PAVING		30	0%	0%	14-Jul-26	17-Aug-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	14-Jul-26	30-Jul-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	71
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	01-Aug-26	17-Aug-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	82
MARKING PAINT		30	0%	0%	04-Aug-26	07-Sep-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	93
MLTX-02-005-EM	Material Submittal for Marking Paint	15	100%	100%	04-Aug-26	20-Aug-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	82




© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Marking Paint	15	100%	100%	22-Aug-26	07-Sep-26	26-Mar-26 A	18-May-26 A	0.00	0.00	0.00	93
PACKAGE AC UNITS		30	0%	0%	14-Jul-26	17-Aug-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	32
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	14-Jul-26	30-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	01-Aug-26	17-Aug-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	32
AIR DIFUSSERS/GRILLS		30	0%	0%	14-Jul-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Submittal for Air Difussers/Grills	15	100%	100%	14-Jul-26	30-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-37
MLTX-02-005-EM	Material Approval for Air Difussers/Grills	15	100%	100%	01-Aug-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
GALVANIZED DUCTS		30	0%	0%	14-Jul-26	17-Aug-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EM	Material Submittal for Galvanized Duct	15	100%	100%	14-Jul-26	30-Jul-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	70
MLTX-02-005-EM	Material Approval for Galvanized Duct	15	100%	100%	01-Aug-26	17-Aug-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	82
EXHAUST FANS		30	0%	0%	14-Jul-26	17-Aug-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	57
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	14-Jul-26	30-Jul-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	42
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	01-Aug-26	17-Aug-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	57
DISTRIBUTION BOARDS		30	0%	0%	14-Jul-26	17-Aug-26	15-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Material Submittal for Distribution Boards	15	100%	100%	14-Jul-26	30-Jul-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Material Approval for Distribution Boards	15	100%	100%	01-Aug-26	17-Aug-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	51
POWER CABLES		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Power Cables	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Power Cables	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
LIGHT FIXTURES		30	0%	0%	14-Jul-26	17-Aug-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	32
MLTX-02-005-EM	Material Submittal for Light Fixtures	15	100%	100%	14-Jul-26	30-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Approval for Light Fixtures	15	100%	100%	01-Aug-26	17-Aug-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	32
CCTV MATERIALS		30	0%	0%	14-Jul-26	17-Aug-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Submittal for CCTV	15	100%	100%	14-Jul-26	30-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Approval for CCTV	15	100%	100%	01-Aug-26	17-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-22
POWER OUTLETS/SWITCHES		30	0%	0%	19-May-26	25-Jun-26	25-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EM	Material Submittal for Power Outlets/Switches	15	100%	100%	19-May-26	08-Jun-26	25-Jun-26 A	25-Jun-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EM	Material Approval for Power Outlets/Switches	15	100%	100%	09-Jun-26	25-Jun-26	27-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	-1
LANDSCAPE WORKS		75	0%	0%	02-May-26	30-Jul-26	19-Mar-26 A	11-Jul-26 A	0.00	0.00	0.00	17
INTERLOCKING PAVING		30	0%	0%	19-May-26	25-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	37
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	19-May-26	08-Jun-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	09-Jun-26	25-Jun-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	37
CURBSTONE		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Submittal for Curbstone	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Curbstone	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	21
PAVEMENT MARKING		30	0%	0%	19-May-26	25-Jun-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	30
MLTX-02-005-EM	Material Submittal for Pavement Markings	15	100%	100%	19-May-26	08-Jun-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	20
MLTX-02-005-EM	Material Approval for Pavement Markings	15	100%	100%	09-Jun-26	25-Jun-26	26-Mar-26 A	18-May-26 A	0.00	0.00	0.00	30
TRAFFIC SIGNS		30	0%	0%	09-Jun-26	13-Jul-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Material Submittal for Traffic Signs	15	100%	100%	09-Jun-26	25-Jun-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	35
MLTX-02-005-EM	Material Approval for Traffic Signs	15	100%	100%	27-Jun-26	13-Jul-26	26-Mar-26 A	18-May-26 A	0.00	0.00	0.00	45
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	02-May-26	08-Jun-26	16-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Material Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	02-May-26	18-May-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Approval for Irrigation Pipes/Sprinkles	15	100%	100%	19-May-26	08-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
AGRICULTURE SOIL		30	0%	0%	27-Jun-26	30-Jul-26	19-Mar-26 A	21-May-26 A	0.00	0.00	0.00	57
MLTX-02-005-EM	Material Submittal for Agriculture Soil	15	100%	100%	27-Jun-26	13-Jul-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	48
MLTX-02-005-EM	Material Approval for Agriculture Soil	15	100%	100%	14-Jul-26	30-Jul-26	26-Mar-26 A	21-May-26 A	0.00	0.00	0.00	57
TRACK SURFACE		30	0%	0%	19-May-26	25-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	29
MLTX-02-005-EM	Material Submittal for Track Surface	15	100%	100%	19-May-26	08-Jun-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EM	Material Approval for Track Surface	15	100%	100%	09-Jun-26	25-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	29
GRASS/TREES		30	0%	0%	09-Jun-26	13-Jul-26	19-Mar-26 A	21-May-26 A	0.00	0.00	0.00	42
MLTX-02-005-EM	Material Submittal for Grass/Trees	15	100%	100%	09-Jun-26	25-Jun-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	33
MLTX-02-005-EM	Material Approval for Grass/Trees	15	100%	100%	27-Jun-26	13-Jul-26	26-Mar-26 A	21-May-26 A	0.00	0.00	0.00	42
CABLES		30	0%	0%	27-Jun-26	30-Jul-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	59
MLTX-02-005-EM	Material Submittal for Cables	15	100%	100%	27-Jun-26	13-Jul-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	48
MLTX-02-005-EM	Material Approval for Cables	15	100%	100%	14-Jul-26	30-Jul-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	59
LIGHT POLES		30	0%	0%	02-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Material Submittal for Lighting poles	15	100%	100%	02-May-26	18-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Approval for Lighting poles	15	100%	100%	19-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
PROCUREMENT		210	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	10-Feb-27	0.00	0.00	0.00	-48
SHORT LEAD ITEM		210	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	10-Feb-27	0.00	0.00	0.00	-48
TOILET/SERVICE WORKS		199	0%	0%	09-Jun-26	28-Nov-26	02-Apr-26 A	28-Jan-27	0.00	0.00	0.00	-52
STEEL REINFORCEMENT		20	0%	0%	01-Aug-26	23-Aug-26	02-Apr-26 A	24-May-26 A	0.00	0.00	0.00	75
MLTX-02-005-PR-7	PO for Steel Reinforcement	5	100%	100%	01-Aug-26	05-Aug-26	02-Apr-26 A	10-May-26 A	0.00	0.00	0.00	72

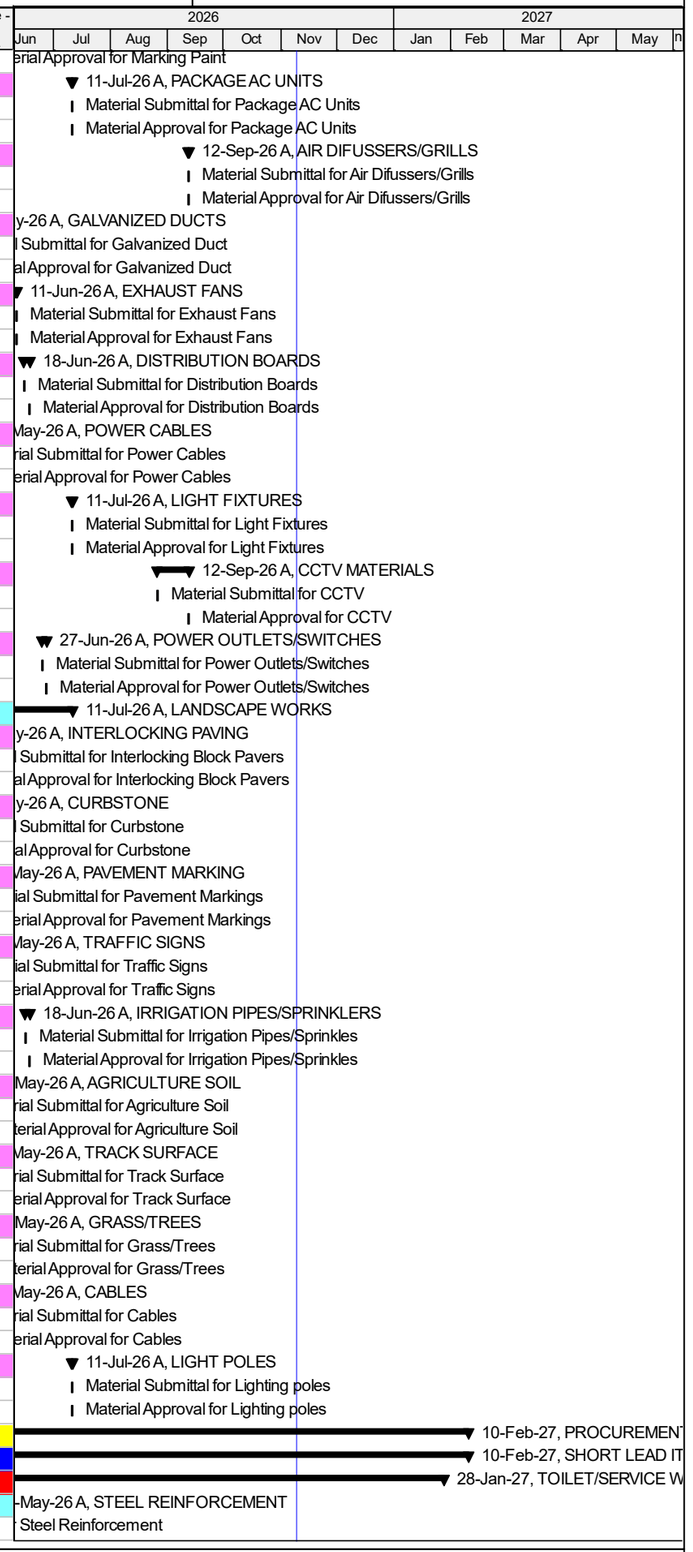

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-7	Material Delivery of Steel Reinforcement	5	100%	100%	18-Aug-26	23-Aug-26	24-May-26 A	24-May-26 A	0.00	0.00	0.00	75
CONCRETE BLOCKS		18	0%	0%	06-Aug-26	26-Aug-26	08-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	43
MLTX-02-005-PR-7	PO for Concrete Blocks	5	100%	100%	06-Aug-26	11-Aug-26	08-Apr-26 A	10-May-26 A	0.00	0.00	0.00	77
MLTX-02-005-PR-7	Material Delivery of Concrete Blocks	8	100%	100%	18-Aug-26	26-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	43
FLOOR/WALL TILES		28	0%	0%	12-Aug-26	13-Sep-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	20
MLTX-02-005-PR-8	PO for Tilling Materials	5	100%	100%	12-Aug-26	17-Aug-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-1
MLTX-02-005-PR-8	Material Delivery of Tailling Material	13	100%	100%	30-Aug-26	13-Sep-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	20
SUSPENDED CEILING		18	0%	0%	21-Oct-26	10-Nov-26	26-Jul-26 A	20-Aug-26 A	0.00	0.00	0.00	69
MLTX-02-005-PR-8	PO for Suspend Ceiling	5	100%	100%	21-Oct-26	26-Oct-26	26-Jul-26 A	26-Jul-26 A	0.00	0.00	0.00	78
MLTX-02-005-PR-8	Material Delivery of Suspend Ceiling	13	85.38%	100%	27-Oct-26	10-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	69
DOORS/WINDOWS		20	0%	0%	18-Aug-26	09-Sep-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-9
MLTX-02-005-PR-8	PO for Doors/Windows	5	100%	100%	18-Aug-26	23-Aug-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-20
MLTX-02-005-PR-8	Material Delivery for Doors/Windows	15	100%	100%	24-Aug-26	09-Sep-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-9
WATER SUPPLY PIPES		22	0%	0%	24-Aug-26	17-Sep-26	28-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	62
MLTX-02-005-PR-8	PO for Water Supply Pipes	5	100%	100%	24-Aug-26	29-Aug-26	28-Apr-26 A	03-May-26 A	0.00	0.00	0.00	98
MLTX-02-005-PR-8	Material Delivery for Water Supply Pipes	7	100%	100%	10-Sep-26	17-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	62
SEWAGE/DRAINAGE PIPES		22	0%	0%	09-Jun-26	04-Jul-26	26-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-3
MLTX-02-005-PR-8	PO for Sewage/Drainage Pipes	5	100%	100%	09-Jun-26	14-Jun-26	26-Apr-26 A	10-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-8	Material Delivery for Sewage/Drainage Pipes	7	100%	100%	27-Jun-26	04-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-3
SANITARY FIXTURES		88	0%	0%	15-Jun-26	26-Sep-26	28-Jul-26 A	20-Aug-26 A	0.00	0.00	0.00	30
MLTX-02-005-PR-8	PO for Sanitary Fixtures	5	100%	100%	15-Jun-26	20-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-33
MLTX-02-005-PR-8	Material Delivery for Sanitary Fixtures	13	100%	100%	10-Sep-26	26-Sep-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	30
PACKAGE AC UNITS		20	0%	0%	15-Jun-26	07-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-005-PR-8	PO for Package AC Units	5	100%	100%	15-Jun-26	20-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-15
MLTX-02-005-PR-8	Material Delivery for Package AC Units	15	100%	100%	21-Jun-26	07-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		30	0%	0%	22-Oct-26	25-Nov-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	82
MLTX-02-005-PR-8	PO for Air Diffusers/Grills	5	100%	100%	22-Oct-26	27-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	59
MLTX-02-005-PR-8	Material Delivery for Air Diffusers/Grills	15	0.67%	100%	09-Nov-26	25-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	82
GALVANIZED DUCTS		20	0%	0%	28-Oct-26	19-Nov-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	77
MLTX-02-005-PR-8	PO for Galvanized Ducts	5	100%	100%	28-Oct-26	02-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	64
MLTX-02-005-PR-8	Material Delivery for Galvanized Ducts	15	34%	100%	03-Nov-26	19-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	77
EXHAUST FANS		80	0%	0%	21-Jun-26	21-Sep-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-8	PO for Exhaust Fans	5	100%	100%	21-Jun-26	25-Jun-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-48
MLTX-02-005-PR-8	Material Delivery for Exhaust Fans	10	100%	100%	10-Sep-26	21-Sep-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	27
LIGHTING FIXTURES		165	0%	0%	15-Jun-26	11-Aug-26	07-Jul-26 A	08-Nov-26 A	0.00	0.00	0.00	-74
MLTX-02-005-PR-8	PO for Lighting Fixtures	5	100%	100%	15-Jun-26	20-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-15
MLTX-02-005-PR-8	Material Delivery for Lighting Fixtures	40	100%	100%	27-Jun-26	11-Aug-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-74
SWITCHES/SOCKETS		40	0%	0%	22-Sep-26	28-Nov-26	13-Oct-26 A	10-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-8	PO for Switches/Sockets	15	100%	100%	22-Sep-26	10-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-3
MLTX-02-005-PR-8	Material Delivery for Switches/Sockets	27	37.41%	0%	28-Oct-26	28-Nov-26	09-Nov-26	10-Dec-26	0.00	0.00	0.00	-10
EARTHING SYSTEM		20	0%	0%	18-Aug-26	09-Sep-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	51
MLTX-02-005-PR-8	PO for Earthing System	5	100%	100%	18-Aug-26	23-Aug-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	36
MLTX-02-005-PR-8	Material Delivery for Earthing System	15	100%	100%	24-Aug-26	09-Sep-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	51
DISTRIBUTION PANNELS		57	0%	0%	27-Sep-26	20-Oct-26	13-Oct-26 A	30-Dec-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-8	PO for Distribution Panels	5	100%	100%	27-Sep-26	01-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-8	Material Delivery for Distribution Panels	15	100%	0%	04-Oct-26	20-Oct-26	13-Dec-26	30-Dec-26	0.00	0.00	0.00	-60
FURNITURES		69	0%	0%	30-Aug-26	19-Nov-26	09-Nov-26	28-Jan-27	0.00	0.00	0.00	-59
MLTX-02-005-PR-8	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	09-Nov-26	13-Dec-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-8	Material Delivery for Furnitures	40	75.25%	0%	05-Oct-26	19-Nov-26	13-Dec-26	28-Jan-27	0.00	0.00	0.00	-59
PLAYGROUND WORKS		207	0%	0%	13-Jun-26	15-Dec-26	02-Apr-26 A	10-Feb-27	0.00	0.00	0.00	-48
PVC MEMBRANE		81	0%	0%	16-Sep-26	22-Oct-26	02-Apr-26 A	21-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	PO for PVC Membrane	10	100%	100%	16-Sep-26	28-Sep-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	109
MLTX-02-005-PR-8	Material Delivery for PVC Membrane	21	100%	0%	29-Sep-26	22-Oct-26	26-Nov-26	21-Dec-26	0.00	0.00	0.00	-50
ARTIFICIAL TURF		65	0%	0%	20-Oct-26	08-Nov-26	02-Apr-26 A	04-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-8	PO for Artificial TURF	5	100%	100%	20-Oct-26	25-Oct-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	132
MLTX-02-005-PR-8	Material Delivery for Artificial TURF	12	100%	0%	26-Oct-26	08-Nov-26	21-Dec-26	04-Jan-27	0.00	0.00	0.00	-48
RUBBER GRANULES		78	0%	0%	04-Oct-26	15-Nov-26	02-Apr-26 A	03-Jan-27	0.00	0.00	0.00	-41
MLTX-02-005-PR-8	PO for Rubber Granules	5	100%	100%	04-Oct-26	08-Oct-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	118
MLTX-02-005-PR-8	Material Delivery for Rubber Granules	32	81.56%	0%	10-Oct-26	15-Nov-26	26-Nov-26	03-Jan-27	0.00	0.00	0.00	-41
PADEL GLASS		135	0%	0%	19-Aug-26	06-Dec-26	02-Apr-26 A	25-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-8	PO for Padel Glass	5	100%	100%	19-Aug-26	24-Aug-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-PR-8	Material Delivery for Padel Glass	18	0%	0%	16-Nov-26	06-Dec-26	04-Jan-27	25-Jan-27	0.00	0.00	0.00	-42
PADEL WIRE MESH/STEEL SETS		79	0%	0%	25-Aug-26	16-Sep-26	08-Apr-26 A	26-Nov-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-8	PO for Wire Mesh/Steel Sets	5	100%	100%	25-Aug-26	30-Aug-26	08-Apr-26 A	19-May-26 A	0.00	0.00	0.00	85

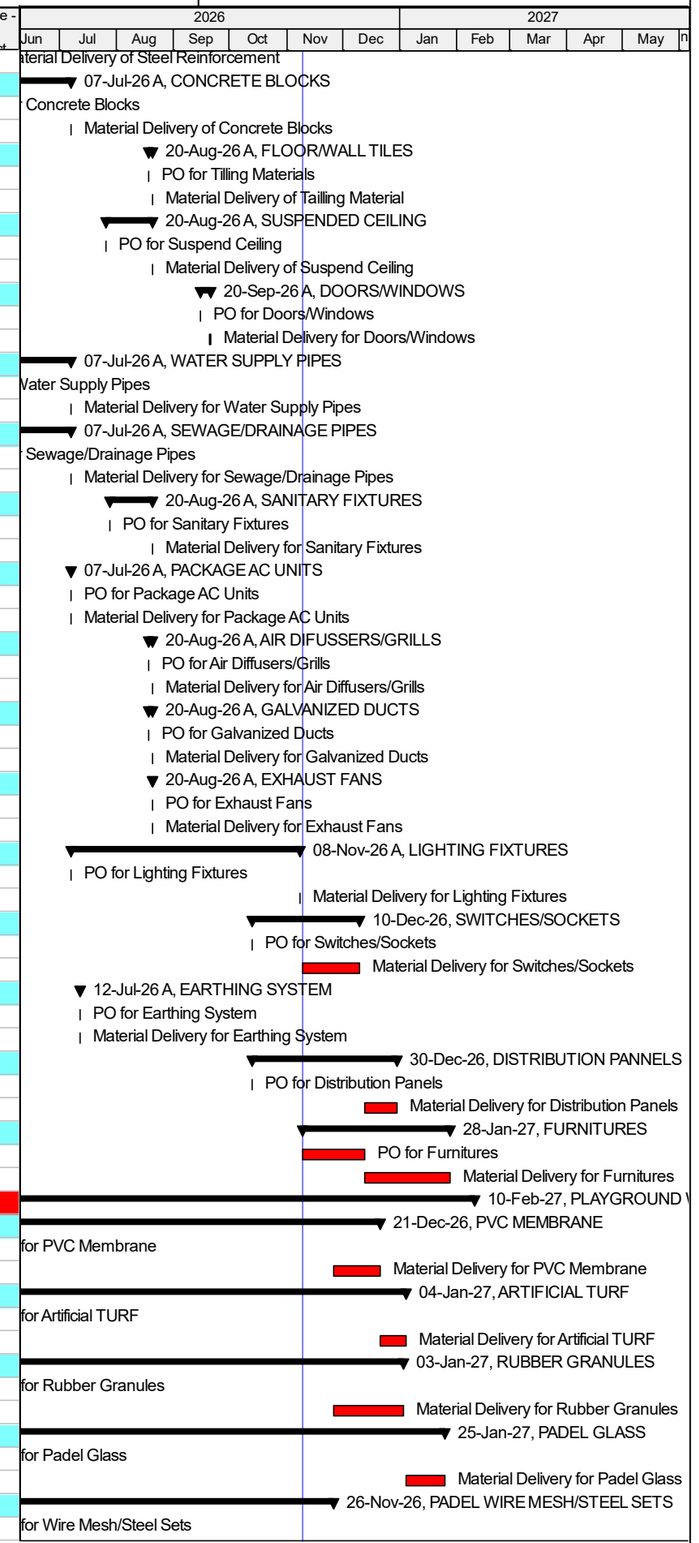

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-8	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-59
AGGREGATE BASE COURSE		12	0%	0%	13-Jun-26	25-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-8	PO for Aggregate Base Course	5	100%	100%	13-Jun-26	17-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-17
MLTX-02-005-PR-8	Material Delivery for Aggregate Base Course	7	100%	100%	18-Jun-26	25-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-10
BITUMINOUS BASE & WEARING COURSE		157	0%	0%	27-Jun-26	29-Oct-26	02-Apr-26 A	28-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	PO for Bituminous Base & Wearing Course	5	100%	100%	27-Jun-26	01-Jul-26	02-Apr-26 A	14-May-26 A	0.00	0.00	0.00	38
MLTX-02-005-PR-8	Material Delivery for the Site	27	100%	0%	29-Sep-26	29-Oct-26	26-Nov-26	28-Dec-26	0.00	0.00	0.00	-50
INTERLOCKING PAVING		76	0%	0%	25-Oct-26	30-Nov-26	15-Sep-26 A	03-Nov-26 A	0.00	0.00	0.00	24
MLTX-02-005-PR-8	PO for Interlocking Block Pavers	15	87.33%	100%	25-Oct-26	10-Nov-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	47
MLTX-02-005-PR-8	Material Delivery for Interlocking Block Pavers	17	0%	100%	11-Nov-26	30-Nov-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	24
MARKING PAINT		32	0%	0%	10-Sep-26	19-Oct-26	09-Nov-26	16-Dec-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-8	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	Material Delivery for Marking Paint	17	100%	0%	30-Sep-26	19-Oct-26	26-Nov-26	16-Dec-26	0.00	0.00	0.00	-49
PACKAGE AC UNITS		20	0%	0%	16-Sep-26	10-Oct-26	04-Jul-26 A	10-Jul-26 A	0.00	0.00	0.00	78
MLTX-02-005-PR-8	PO for Package AC Units	5	100%	100%	16-Sep-26	21-Sep-26	04-Jul-26 A	04-Jul-26 A	0.00	0.00	0.00	68
MLTX-02-005-PR-8	Material Delivery for Package AC Units	15	100%	100%	22-Sep-26	10-Oct-26	10-Jul-26 A	10-Jul-26 A	0.00	0.00	0.00	78
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Sep-26	21-Oct-26	26-Nov-26	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	PO for Air Difussers/Grills	5	100%	0%	29-Sep-26	04-Oct-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	Material Delivery for Air Difussers/Grills	15	100%	0%	05-Oct-26	21-Oct-26	02-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
GALVANIZED DUCTS		20	0%	0%	29-Sep-26	21-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	7
MLTX-02-005-PR-8	PO for Galvanized Duct	5	100%	100%	29-Sep-26	04-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-7
MLTX-02-005-PR-8	Material Delivery for Galvanized Duct	15	100%	100%	05-Oct-26	21-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	7
EXHAUST FANS		20	0%	0%	16-Sep-26	10-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-3
MLTX-02-005-PR-8	PO for Exhaust Fans	5	100%	100%	16-Sep-26	21-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-18
MLTX-02-005-PR-8	Material Delivery for Exhaust Fans	15	100%	100%	22-Sep-26	10-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-3
DISTRIBUTION BOARDS		20	0%	0%	29-Sep-26	21-Oct-26	26-Nov-26	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	PO for Distribution Boards	5	100%	0%	29-Sep-26	04-Oct-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	Material Delivery for Distribution Boards	15	100%	0%	05-Oct-26	21-Oct-26	02-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
POWER CABLES		60	0%	0%	05-Oct-26	15-Dec-26	02-Dec-26	10-Feb-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-8	PO for Power Cables	5	100%	0%	05-Oct-26	10-Oct-26	02-Dec-26	08-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	Material Delivery for Power Cables	30	0%	0%	11-Nov-26	15-Dec-26	06-Jan-27	10-Feb-27	0.00	0.00	0.00	-48
LIGHT FIXTURES		85	0%	0%	10-Sep-26	21-Oct-26	07-Jul-26 A	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	PO for Light Fixtures	5	100%	100%	10-Sep-26	15-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	60
MLTX-02-005-PR-8	Material Delivery for Light Fixtures	10	100%	0%	11-Oct-26	21-Oct-26	08-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
CCTV MATERIALS		50	0%	0%	26-Sep-26	10-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-8	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-38
MLTX-02-005-PR-8	Material Delivery for CCTV	15	87.33%	0%	25-Oct-26	10-Nov-26	20-Dec-26	06-Jan-27	0.00	0.00	0.00	-48
POWER OUTLETS/SWITCHES		135	0%	0%	08-Jul-26	18-Aug-26	07-Jul-26 A	14-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-8	PO for Power Outlets/Switches	6	100%	100%	08-Jul-26	14-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-8	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-99
LANDSCAPE WORKS		192	0%	0%	09-Jun-26	23-Nov-26	16-May-26 A	20-Jan-27	0.00	0.00	0.00	-49
INTERLOCKING PAVING		17	0%	0%	15-Jul-26	03-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-20
MLTX-02-005-PR-8	PO for Interlocking Block Pavers	5	100%	100%	15-Jul-26	20-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-32
MLTX-02-005-PR-8	Material Delivery for Interlocking Block Pavers	12	100%	100%	21-Jul-26	03-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-20
CURBSTONE		17	0%	0%	09-Jun-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-PR-8	PO for Curbstone	5	100%	100%	09-Jun-26	14-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-PR-8	Material Delivery for Curbstone	12	100%	100%	15-Jun-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
PAVEMENT MARKING		62	0%	0%	15-Jul-26	23-Nov-26	09-Nov-26	20-Jan-27	0.00	0.00	0.00	-49
MLTX-02-005-PR-8	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-8	Material Delivery for Pavement Markings	30	57%	0%	20-Oct-26	23-Nov-26	16-Dec-26	20-Jan-27	0.00	0.00	0.00	-49
TRAFFIC SIGNS		18	0%	0%	27-Jul-26	16-Sep-26	13-Oct-26 A	08-Nov-26 A	0.00	0.00	0.00	-43
MLTX-02-005-PR-8	PO for Traffic Signs	15	100%	100%	27-Jul-26	12-Aug-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-52
MLTX-02-005-PR-8	Material Delivery for Traffic Signs	10	100%	100%	13-Aug-26	16-Sep-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-43
IRRIGATION PIPES/SPRINKLERS		13	0%	0%	09-Jun-26	23-Jun-26	10-Jun-26 A	02-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-PR-8	PO for Irrigation Pipes/Sprinkles	5	100%	100%	09-Jun-26	14-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-PR-8	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	100%	15-Jun-26	23-Jun-26	02-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	-8
AGRICULTURE SOIL		35	0%	0%	01-Aug-26	12-Sep-26	13-Oct-26 A	08-Nov-26 A	0.00	0.00	0.00	-47
MLTX-02-005-PR-8	PO for Agriculture Soil	15	100%	100%	01-Aug-26	17-Aug-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-48
MLTX-02-005-PR-8	Material Delivery for Agriculture Soil	22	100%	100%	18-Aug-26	12-Sep-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-47
TRACK SURFACE		127	0%	0%	30-Jun-26	29-Sep-26	16-May-26 A	26-Nov-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-8	PO for Track Surface	5	100%	100%	30-Jun-26	05-Jul-26	16-May-26 A	19-May-26 A	0.00	0.00	0.00	37
MLTX-02-005-PR-8	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-49
GRASS/TREES		119	0%	0%	21-Jul-26	17-Nov-26	17-May-26 A	08-Dec-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-8	PO for Grass/Trees	5	100%	100%	21-Jul-26	26-Jul-26	17-May-26 A	20-May-26 A	0.00	0.00	0.00	54

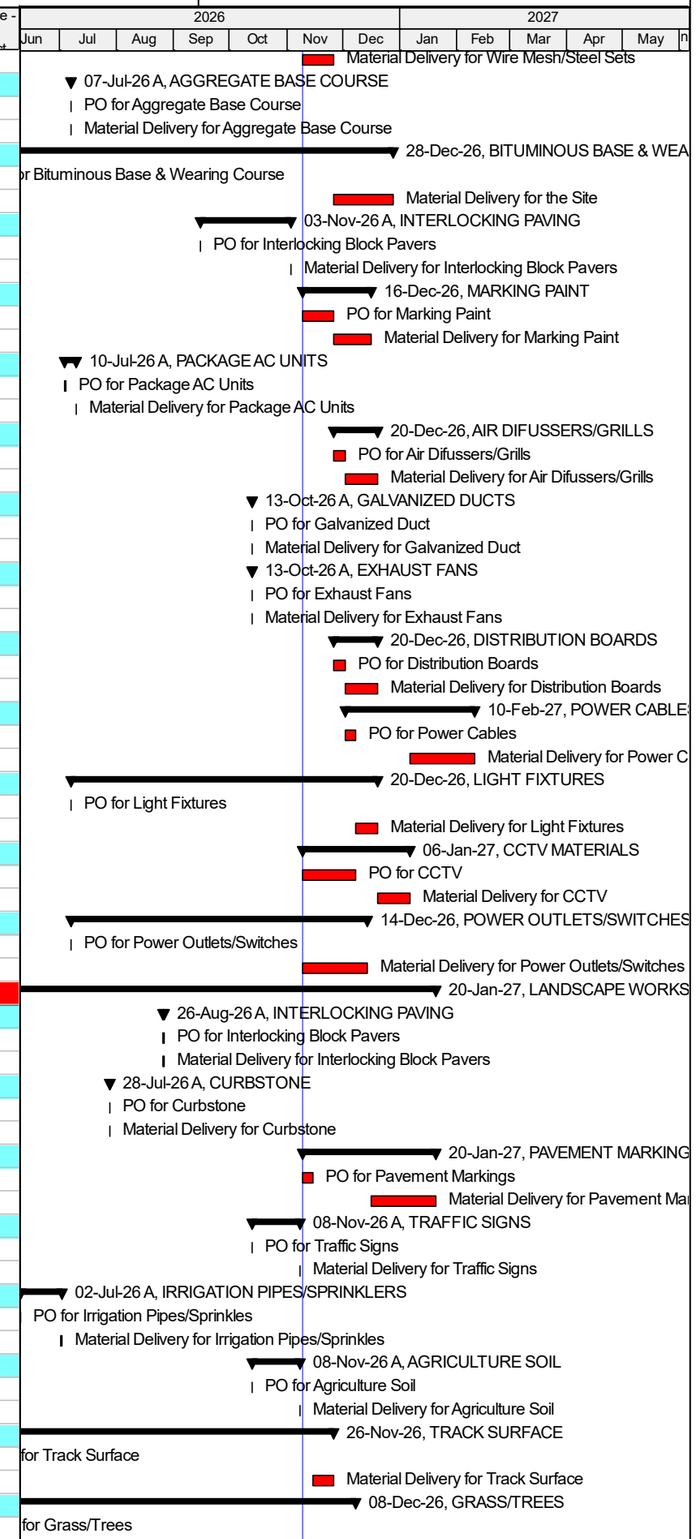


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-S	Material Delivery for Grass/Trees	25	68.4%	0%	20-Oct-26	17-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-17
CABLES		20	0%	0%	17-Sep-26	11-Oct-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	21
MLTX-02-005-PR-S	PO for Cables	5	100%	100%	17-Sep-26	22-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-S	Material Delivery for Cables	15	100%	100%	24-Sep-26	11-Oct-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	21
LONG LEAD ITEM		173	0%	0%	05-Jul-26	10-Dec-26	07-Jul-26 A	24-Jan-27	0.00	0.00	0.00	-37
PLAYGROUND WORKS		78	0%	0%	18-Aug-26	10-Dec-26	13-Oct-26 A	24-Jan-27	0.00	0.00	0.00	-37
STEEL TENSION CABLES		49	0%	0%	18-Aug-26	27-Oct-26	13-Oct-26 A	10-Dec-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-E	PO for Steel Tension Cables	7	100%	100%	18-Aug-26	25-Aug-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-41
MLTX-02-005-PR-E	Material Fabrication for Steel Tension Cables	15	100%	100%	08-Sep-26	26-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-15
MLTX-02-005-PR-E	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-S	Staging time	12	100%	0%	14-Oct-26	27-Oct-26	26-Nov-26	10-Dec-26	0.00	0.00	0.00	-37
EMERGENCY DOORS		78	0%	0%	08-Sep-26	05-Dec-26	13-Oct-26 A	24-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-E	PO for Emergency Doors	20	100%	100%	08-Sep-26	01-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-E	Material Fabrication for Emergency Doors	20	100%	100%	03-Oct-26	25-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-E	Material Delivery for Emergency Doors	20	60.5%	0%	26-Oct-26	17-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-S	Staging time	15	0%	0%	18-Nov-26	05-Dec-26	06-Jan-27	24-Jan-27	0.00	0.00	0.00	-42
PRESSURE UNITS		43	0%	0%	08-Sep-26	29-Nov-26	13-Oct-26 A	14-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-E	PO for Pressure Units	10	100%	100%	08-Sep-26	19-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-20
MLTX-02-005-PR-E	Material Fabrication for Pressure Units	20	100%	100%	03-Oct-26	25-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-E	Material Delivery for Pressure Units	25	48.4%	0%	26-Oct-26	23-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-S	Staging time	5	0%	0%	24-Nov-26	29-Nov-26	08-Dec-26	14-Dec-26	0.00	0.00	0.00	-12
AIR LOCK DOORS		50	0%	0%	03-Oct-26	10-Dec-26	13-Oct-26 A	06-Jan-27	0.00	0.00	0.00	-22
MLTX-02-005-PR-E	PO for Lock Doors	10	100%	100%	03-Oct-26	13-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	0
MLTX-02-005-PR-E	Material Fabrication for Lock Doors	20	100%	0%	14-Oct-26	05-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-E	Material Delivery for Lock Doors	25	8.4%	0%	07-Nov-26	05-Dec-26	02-Dec-26	31-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-S	Staging time	5	0%	0%	06-Dec-26	10-Dec-26	31-Dec-26	06-Jan-27	0.00	0.00	0.00	-22
LANDSCAPE WORKS		91	0%	0%	05-Jul-26	19-Oct-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	24
LIGHT POLES		91	0%	0%	05-Jul-26	19-Oct-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	24
MLTX-02-005-PR-S	PO for Lighting poles	10	100%	100%	05-Jul-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
MLTX-02-005-PR-S	Material Fabrication for Lighting poles	30	100%	100%	04-Aug-26	07-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-S	Material Delivery for Lighting poles	20	100%	100%	08-Sep-26	01-Oct-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	9
MLTX-02-005-PR-S	Staging time	15	100%	100%	03-Oct-26	19-Oct-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	24
CONSTRUCTION PHASE		280	43.29%	40.54%	15-Apr-26	31-Dec-26	04-Apr-26 A	09-Mar-27	4,426,788.65	4,146,313.28	10,226,640.03	-56
SITE WORKS		276	39.9%	36.6%	15-Apr-26	30-Dec-26	04-Apr-26 A	09-Mar-27	3,614,296.25	3,315,861.28	9,058,565.25	-57
EARTH WORKS		68	100%	100%	15-Apr-26	06-Jul-26	04-Apr-26 A	05-Aug-26 A	494,887.02	494,887.02	494,887.02	-25
MLTX-02-005-CN-993	Excavation (in all types of soil) including Compaction	12	100%	100%	15-Apr-26	28-Apr-26	06-Apr-26 A	12-Apr-26 A	126,481.53	126,481.53	126,481.53	15
MLTX-02-005-CN-994	Excavation (in all types of soil) including Compaction	14	100%	100%	15-Apr-26	30-Apr-26	04-Apr-26 A	02-Aug-26 A	14,053.50	14,053.50	14,053.50	-76
MLTX-02-005-CN-995	Excavation (in all types of soil) including Compaction	7	100%	100%	28-Jun-26	05-Jul-26	28-Jun-26 A	05-Aug-26 A	189,722.30	189,722.30	189,722.30	-26
MLTX-02-005-CN-996	Backfilling on Layers (Selected Soil) including Compaction	21	100%	100%	29-Apr-26	23-May-26	13-Apr-26 A	30-Apr-26 A	63,049.67	63,049.67	63,049.67	20
MLTX-02-005-CN-997	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	24-May-26	18-Jun-26	06-Apr-26 A	08-Apr-26 A	7,005.52	7,005.52	7,005.52	58
MLTX-02-005-CN-998	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	28-Jun-26	06-Jul-26	21-Apr-26 A	05-Aug-26 A	94,574.50	94,574.50	94,574.50	-25
LANDSCAPE WORKS		243	36.4%	32.48%	24-May-26	30-Dec-26	17-May-26 A	09-Mar-27	3,095,514.70	2,762,480.93	8,505,184.90	-57
PLAYGROUND AREA		224	54.93%	53.84%	24-May-26	27-Dec-26	19-May-26 A	08-Feb-27	752,566.34	737,620.36	1,369,978.66	-36
FOOTBALL PLAYGROUND		215	35%	35%	24-May-26	13-Dec-26	19-May-26 A	03-Feb-27	110,897.50	110,897.50	316,849.99	-44
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Football Playground)	20	100%	100%	24-May-26	18-Jun-26	19-May-26 A	01-Jun-26 A	79,212.50	79,212.50	79,212.50	15
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Football	21	100%	100%	20-Jun-26	13-Jul-26	01-Jun-26 A	22-Jun-26 A	15,842.50	15,842.50	15,842.50	19
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	15	0%	0%	17-Nov-26	03-Dec-26	26-Dec-26	12-Jan-27	0.00	0.00	158,424.99	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	31,685.00	-44
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	15,842.50	-44
MLTX-02-005-CI	Aggregate base course layer (Football Playground)	21	100%	100%	01-Sep-26	26-Sep-26	02-Aug-26 A	06-Aug-26 A	15,842.50	15,842.50	15,842.50	42
PADEL PLAYGROUND		195	45%	70%	20-Jun-26	19-Dec-26	19-May-26 A	03-Feb-27	105,292.80	163,788.80	233,984.00	-39
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Padel Playground)	21	100%	100%	20-Jun-26	13-Jul-26	19-May-26 A	01-Jun-26 A	81,894.40	81,894.40	81,894.40	36
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Padel	21	100%	100%	14-Jul-26	06-Aug-26	01-Jun-26 A	14-Jun-26 A	11,699.20	11,699.20	11,699.20	47
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Padel Playground)	21	0%	100%	17-Nov-26	10-Dec-26	29-Aug-26 A	31-Aug-26 A	0.00	58,496.00	58,496.00	87
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	58,496.00	-39
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	11,699.20	-39
MLTX-02-005-CI	Aggregate base course layer (Padel Playground)	21	100%	100%	08-Aug-26	31-Aug-26	15-Jun-26 A	28-Jun-26 A	11,699.20	11,699.20	11,699.20	56
BASKETBALL PLAYGROUND		178	69.52%	69.52%	14-Jul-26	23-Dec-26	19-May-26 A	08-Feb-27	221,133.58	221,133.58	318,089.68	-39
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Basketball	20	100%	100%	14-Jul-26	05-Aug-26	19-May-26 A	01-Jun-26 A	92,913.27	92,913.27	92,913.27	56
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Basketball	21	100%	100%	06-Aug-26	30-Aug-26	01-Jun-26 A	14-Jun-26 A	15,795.26	15,795.26	15,795.26	67
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Basketball	21	100%	100%	27-Sep-26	20-Oct-26	19-Aug-26 A	31-Aug-26 A	96,629.80	96,629.80	96,629.80	43
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	80,796.75	-39
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	4	0%	0%	20-Dec-26	23-Dec-26	03-Feb-27	08-Feb-27	0.00	0.00	16,159.35	-39
MLTX-02-005-CI	Aggregate base course layer (Basketball Playground)	21	100%	100%	01-Sep-26	26-Sep-26	15-Jun-26 A	28-Jun-26 A	15,795.26	15,795.26	15,795.26	77

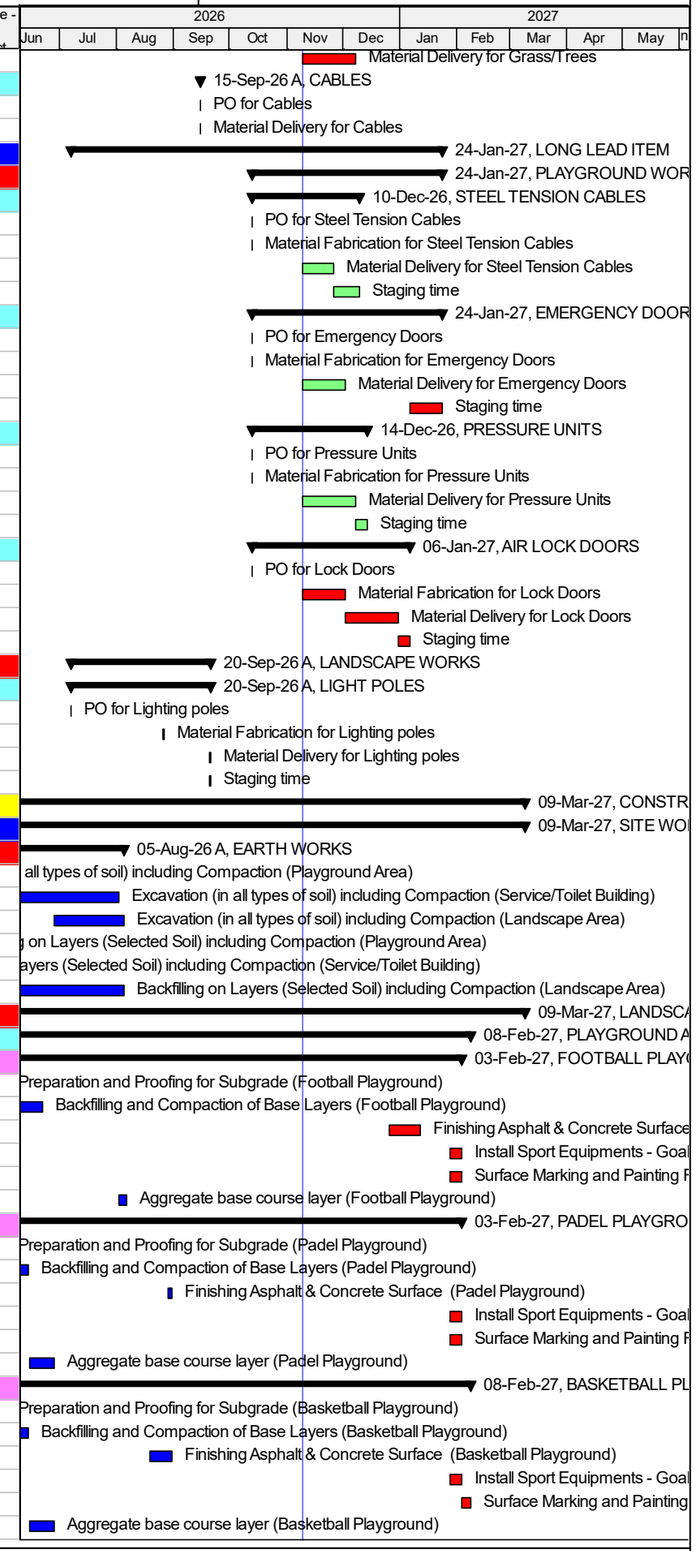

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PADEL FENCE		98	96.19%	4.22%	01-Sep-26	16-Nov-26	08-Aug-26 A	26-Dec-26	133,458.11	5,859.94	138,749.98	-33
MLTX-02-005-CI	Excavation for Fence	8	100%	100%	01-Sep-26	09-Sep-26	08-Aug-26 A	08-Aug-26 A	1,196.57	1,196.57	1,196.57	28
MLTX-02-005-CI	Concrete Foundation for Fence including Posts Fixation	7	100%	100%	02-Sep-26	09-Sep-26	15-Aug-26 A	19-Aug-26 A	828.69	828.69	828.69	18
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	17	100%	100%	10-Sep-26	30-Sep-26	13-Oct-26 A	13-Oct-26 A	3,834.68	3,834.68	3,834.68	-11
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	09-Nov-26	02-Dec-26	30,677.48	0.00	30,677.48	-33
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	20	65.5%	0%	25-Oct-26	16-Nov-26	02-Dec-26	26-Dec-26	10,046.88	0.00	15,338.75	-33
MLTX-02-005-CI	Install of Fence Gates	12	42.5%	0%	03-Nov-26	16-Nov-26	12-Dec-26	26-Dec-26	86,873.81	0.00	86,873.81	-33
CURBSTOEN/INTERLOCK		112	50.17%	65.12%	06-Oct-26	27-Dec-26	15-Aug-26 A	02-Dec-26	181,784.34	235,940.54	362,305.01	22
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	30%	05-Dec-26	27-Dec-26	04-Nov-26 A	02-Dec-26	0.00	54,156.20	180,520.67	22
MLTX-02-005-CI	Concrete Works Under Curbstone	7	100%	100%	06-Oct-26	13-Oct-26	15-Aug-26 A	15-Aug-26 A	54,535.30	54,535.30	54,535.30	50
MLTX-02-005-CI	Curbstone Installation	4	100%	100%	14-Oct-26	18-Oct-26	19-Aug-26 A	05-Sep-26 A	127,249.04	127,249.04	127,249.04	36
AIR DOME		121	23.18%	23.18%	26-Sep-26	21-Dec-26	17-May-26 A	14-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-46
CIVIL WORKS		107	48.29%	48.29%	26-Sep-26	07-Dec-26	17-May-26 A	28-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-44
MLTX-02-005-CI	Excavation for Foundation (Air Dome)	6	100%	100%	26-Sep-26	01-Oct-26	17-May-26 A	31-May-26 A	167,650.30	167,650.30	167,650.30	105
MLTX-02-005-CI	Concrete Works for Foundations including Anchor Bolts (Air	13	100%	100%	03-Oct-26	17-Oct-26	29-Jul-26 A	21-Sep-26 A	228,008.77	228,008.77	228,008.77	21
MLTX-02-005-CI	Cable System Installation (Air Dome)	7	100%	100%	03-Oct-26	10-Oct-26	21-Sep-26 A	21-Sep-26 A	350,921.95	350,921.95	350,921.95	15
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	942,830.33	-44
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-44
MLTX-02-005-CI	Perimeter Clamping System Installation	7	100%	100%	03-Oct-26	10-Oct-26	21-Sep-26 A	28-Sep-26 A	552,946.49	552,946.49	552,946.49	10
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	1,233,296.81	-43
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	728,766.30	-43
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	336,353.67	-43
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	168,176.84	-43
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	01-Feb-27	13-Feb-27	0.00	0.00	1,513,591.54	-46
MLTX-02-005-CI	Light Fixture Works (Air Dome)	7	0%	0%	13-Dec-26	20-Dec-26	01-Feb-27	09-Feb-27	0.00	0.00	224,235.78	-43
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	03-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-43
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	03-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-43
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	3	0%	0%	17-Dec-26	20-Dec-26	06-Feb-27	09-Feb-27	0.00	0.00	504,530.51	-43
MLTX-02-005-CI	Control System Installation (Air Dome)	2	0%	0%	19-Dec-26	20-Dec-26	10-Feb-27	13-Feb-27	0.00	0.00	448,471.57	-46
FINISHES WORKS		9	0%	0%	15-Dec-26	21-Dec-26	03-Feb-27	14-Feb-27	0.00	0.00	168,176.84	-46
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	5	0%	0%	15-Dec-26	20-Dec-26	03-Feb-27	09-Feb-27	0.00	0.00	112,117.89	-43
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	1	0%	0%	21-Dec-26	21-Dec-26	13-Feb-27	14-Feb-27	0.00	0.00	56,058.95	-46
IRRIGATION NETWORK		145	83.53%	83.53%	28-Jun-26	30-Nov-26	18-Aug-26 A	15-Dec-26	127,308.67	127,308.67	152,414.87	-12
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	4	100%	100%	28-Jun-26	01-Jul-26	18-Aug-26 A	02-Sep-26 A	53,620.00	53,620.00	53,620.00	-54
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	4	100%	100%	02-Jul-26	06-Jul-26	03-Sep-26 A	10-Sep-26 A	50,127.83	50,127.83	50,127.83	-57
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	4	100%	100%	07-Jul-26	11-Jul-26	10-Sep-26 A	13-Oct-26 A	23,560.84	23,560.84	23,560.84	-80
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	28-Nov-26	30-Nov-26	12-Dec-26	15-Dec-26	0.00	0.00	25,106.20	-12
NATURAL GROUND		20	0%	30.51%	17-Nov-26	30-Nov-26	27-Oct-26 A	15-Dec-26	0.00	58,500.00	191,740.00	-12
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	6	0%	0%	24-Nov-26	30-Nov-26	08-Dec-26	15-Dec-26	0.00	0.00	126,740.00	-12
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	90%	17-Nov-26	23-Nov-26	27-Oct-26 A	16-Nov-26	0.00	58,500.00	65,000.00	7
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	16-Nov-26	347,251.46	104,175.44	347,251.46	-13
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	100%	30%	17-Sep-26	24-Sep-26	31-Oct-26 A	16-Nov-26	104,175.44	31,252.63	104,175.44	-44
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	4	100%	30%	27-Oct-26	31-Oct-26	31-Oct-26 A	14-Nov-26	141,732.50	42,519.75	141,732.50	-11
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	100%	30%	26-Sep-26	30-Sep-26	31-Oct-26 A	15-Nov-26	101,343.52	30,403.06	101,343.52	-38
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	367,633.90	183,816.95	367,633.90	-21
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	26-Nov-26	187,554.12	93,777.06	187,554.12	-33
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	100%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	180,079.78	90,039.89	180,079.78	-21
GENERAL/FURNITURE		120	42.79%	53.49%	19-Oct-26	30-Dec-26	03-Oct-26 A	09-Mar-27	201,226.82	251,532.00	470,271.40	-57
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	100%	0%	02-Nov-26	07-Nov-26	26-Nov-26	02-Dec-26	93,594.00	0.00	93,594.00	-21
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	14-Dec-26	30-Dec-26	18-Feb-27	09-Mar-27	0.00	0.00	9,749.30	-57
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	100%	0%	27-Oct-26	03-Nov-26	20-Jan-27	28-Jan-27	17,274.79	0.00	17,274.79	-73
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	23-Nov-26	30-Nov-26	28-Jan-27	06-Feb-27	0.00	0.00	40,307.84	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	23-Nov-26	30-Nov-26	28-Jan-27	06-Feb-27	0.00	0.00	32,757.76	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	23-Nov-26	30-Nov-26	28-Jan-27	06-Feb-27	0.00	0.00	12,869.04	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	01-Dec-26	13-Dec-26	06-Feb-27	18-Feb-27	0.00	0.00	12,186.67	-57
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	7	100%	100%	19-Oct-26	26-Oct-26	03-Oct-26 A	15-Oct-26 A	75,459.60	75,459.60	75,459.60	9
MLTX-02-005-CN-1	Installing of Site Light Poles	13	8.46%	100%	08-Nov-26	22-Nov-26	18-Oct-26 A	03-Nov-26 A	14,898.43	176,072.40	176,072.40	17
PARKING		24	40.85%	100%	01-Nov-26	28-Nov-26	16-May-26 A	12-Oct-26 A	23,894.53	58,493.33	58,493.33	40
MLTX-02-005-CN-106	Interlock Installation (8 Cm) for Parking Area (Including	20	15.5%	100%	05-Nov-26	28-Nov-26	03-Oct-26 A	12-Oct-26 A	6,346.53	40,945.33	40,945.33	40
MLTX-02-005-CN-107	Site Preparation & Compaction Under Interlock for Parking	3	100%	100%	01-Nov-26	03-Nov-26	16-May-26 A	22-Jul-26 A	17,548.00	17,548.00	17,548.00	89
TOILET/SERVICE BUILDING		216	69.56%	71.1%	02-Jul-26	31-Dec-26	21-May-26 A	06-Feb-27	812,492.40	830,452.00	1,168,074.78	-30
STRUCTURE WORKS		58	100%	100%	02-Jul-26	07-Sep-26	21-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	31
CONCRETE WORKS		32	100%	100%	02-Aug-26	07-Sep-26	20-Jun-26 A	12-Jul-26 A	118,454.85	118,454.85	118,454.85	49
SUB-STRUCTURE		9	100%	100%	29-Aug-26	07-Sep-26	20-Jun-26 A	25-Jun-26 A	38,022.35	38,022.35	38,022.35	63

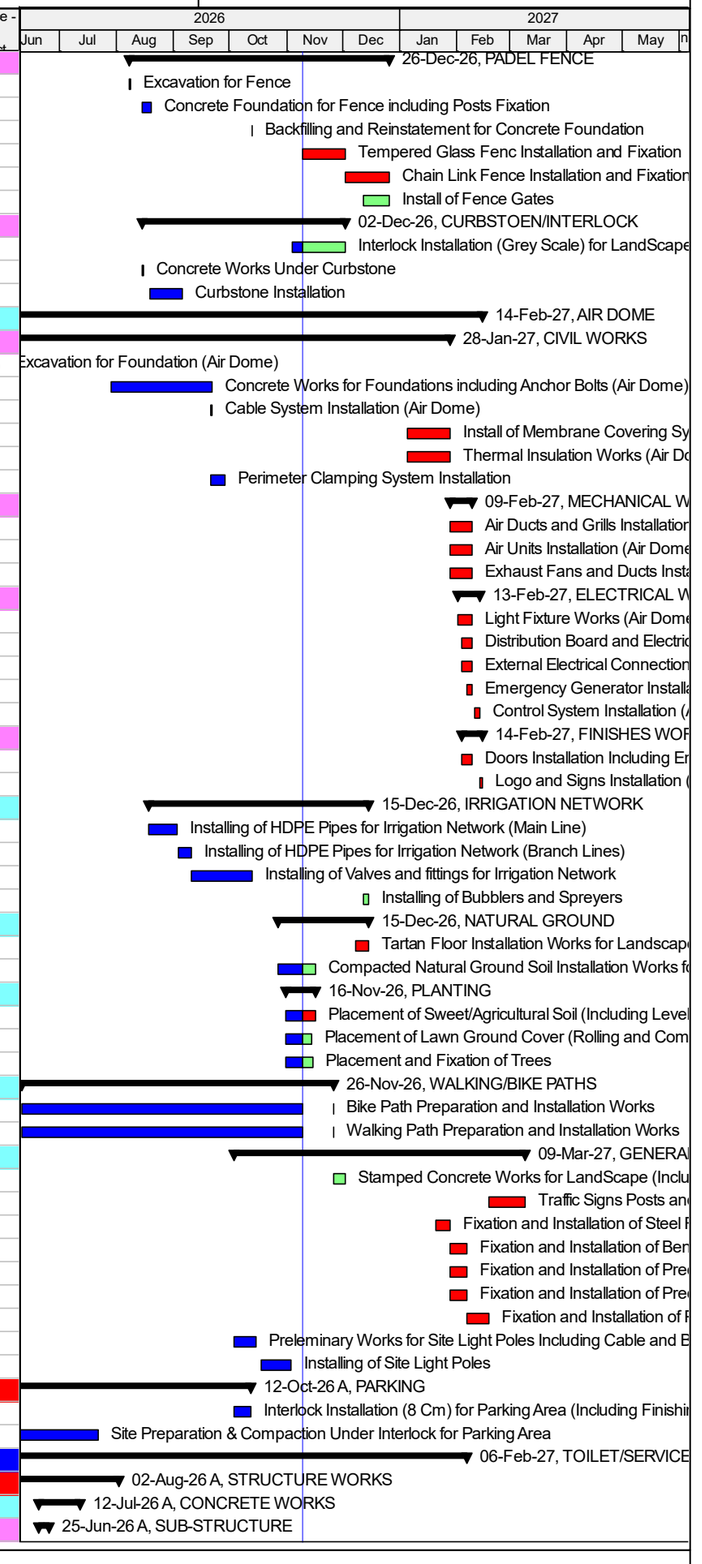

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Plain Concrete Under Footing	4	100%	100%	29-Aug-26	01-Sep-26	20-Jun-26 A	21-Jun-26 A	1,462.40	1,462.40	1,462.40	62
MLTX-02-005-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	02-Sep-26	07-Sep-26	22-Jun-26 A	25-Jun-26 A	36,559.95	36,559.95	36,559.95	63
SUPER-STRUCTURE		14	100%	100%	02-Aug-26	17-Aug-26	07-Jul-26 A	12-Jul-26 A	80,432.50	80,432.50	80,432.50	31
MLTX-02-005-CI	AAC Panels Works for Walls	7	100%	100%	02-Aug-26	09-Aug-26	07-Jul-26 A	08-Jul-26 A	48,259.50	48,259.50	48,259.50	27
MLTX-02-005-CI	AAC Panels Works for Slabs	3	100%	100%	10-Aug-26	12-Aug-26	09-Jul-26 A	11-Jul-26 A	16,086.50	16,086.50	16,086.50	28
MLTX-02-005-CI	Parpet Works and Lintels	4	100%	100%	13-Aug-26	17-Aug-26	11-Jul-26 A	12-Jul-26 A	16,086.50	16,086.50	16,086.50	31
UNDER GROUND SEPTIC TANK		33	100%	100%	05-Jul-26	11-Aug-26	31-May-26 A	24-Jun-26 A	34,208.09	34,208.09	34,208.09	41
MLTX-02-005-CN-1	Plain Concrete Under Footing	3	100%	100%	05-Jul-26	07-Jul-26	31-May-26 A	01-Jun-26 A	1,462.40	1,462.40	1,462.40	31
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Foundation Including	8	100%	100%	08-Jul-26	16-Jul-26	10-Jun-26 A	13-Jun-26 A	7,604.46	7,604.46	7,604.46	29
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	11	100%	100%	19-Jul-26	30-Jul-26	07-Jun-26 A	11-Jun-26 A	16,366.86	16,366.86	16,366.86	42
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Slab Including	10	100%	100%	01-Aug-26	11-Aug-26	20-Jun-26 A	24-Jun-26 A	8,774.37	8,774.37	8,774.37	41
THERMAL & MOISTER PROTECTION		49	100%	100%	02-Jul-26	27-Aug-26	21-May-26 A	02-Aug-26 A	10,236.80	10,236.80	10,236.80	22
ANTI TERMIT CONTROL		41	100%	100%	02-Jul-26	18-Aug-26	21-May-26 A	25-May-26 A	4,387.50	4,387.50	4,387.50	70
MLTX-02-005-CI	Anti Termite Works Under Foundation	1	100%	100%	02-Jul-26	02-Jul-26	24-May-26 A	25-May-26 A	1,755.00	1,755.00	1,755.00	30
MLTX-02-005-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	18-Aug-26	18-Aug-26	21-May-26 A	21-May-26 A	2,632.50	2,632.50	2,632.50	74
POLYETHYLENE SHEET		40	100%	100%	04-Jul-26	18-Aug-26	25-May-26 A	21-Jun-26 A	2,193.30	2,193.30	2,193.30	50
MLTX-02-005-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	04-Jul-26	04-Jul-26	25-May-26 A	31-May-26 A	877.32	877.32	877.32	29
MLTX-02-005-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	18-Aug-26	18-Aug-26	21-Jun-26 A	21-Jun-26 A	1,315.98	1,315.98	1,315.98	50
EPOXY		8	100%	100%	19-Aug-26	27-Aug-26	12-Jul-26 A	02-Aug-26 A	3,656.00	3,656.00	3,656.00	22
MLTX-02-005-CI	Surface Preparation for Epoxy Coating	3	100%	100%	19-Aug-26	22-Aug-26	12-Jul-26 A	12-Jul-26 A	1,096.80	1,096.80	1,096.80	35
MLTX-02-005-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	23-Aug-26	27-Aug-26	25-Jul-26 A	02-Aug-26 A	2,559.20	2,559.20	2,559.20	22
MASONARY WORK		5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
MLTX-02-005-CN-11C	CMU Masonary Works Including all Accessories	5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
THERMAL & MOISTER PROTECTION		54	100%	100%	29-Aug-26	21-Sep-26	26-Sep-26 A	07-Nov-26 A	34,698.32	34,698.32	34,698.32	-39
MLTX-02-005-CN-11C	Preparing Surface and Preliminary Works for Toilets	2	100%	100%	29-Aug-26	30-Aug-26	26-Sep-26 A	26-Sep-26 A	2,105.86	2,105.86	2,105.86	-22
MLTX-02-005-CN-11C	Preparing Surface and Preliminary Works for Roofing and	5	100%	100%	07-Sep-26	12-Sep-26	30-Sep-26 A	30-Sep-26 A	11,071.52	11,071.52	11,071.52	-15
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Toilets	6	100%	100%	31-Aug-26	06-Sep-26	19-Oct-26 A	19-Oct-26 A	4,913.66	4,913.66	4,913.66	-36
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	100%	13-Sep-26	21-Sep-26	03-Oct-26 A	07-Nov-26 A	16,607.28	16,607.28	16,607.28	-39
MECHANICAL WORK		167	62.8%	79%	16-Jul-26	19-Dec-26	18-Jul-26 A	31-Dec-26	166,205.09	209,102.06	264,673.10	-10
HVAC SYSTEM		72	47.55%	100%	26-Sep-26	07-Dec-26	19-Jul-26 A	03-Nov-26 A	13,259.41	27,883.37	27,883.37	30
MLTX-02-005-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	26-Sep-26	28-Sep-26	19-Jul-26 A	22-Jul-26 A	9,359.69	9,359.69	9,359.69	57
MLTX-02-005-CN-1	Exhaust, Air Ducts Installation with all Accessories	6	100%	100%	29-Sep-26	05-Oct-26	12-Sep-26 A	12-Sep-26 A	3,899.72	3,899.72	3,899.72	19
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	0%	100%	05-Dec-26	07-Dec-26	03-Nov-26 A	03-Nov-26 A	0.00	14,623.96	14,623.96	30
WATER SUPPLY SYSTEM		112	67.4%	68.53%	19-Sep-26	19-Dec-26	28-Jul-26 A	31-Dec-26	104,415.30	106,170.17	154,916.69	-10
MLTX-02-005-CN-1	Installing of Valves and Fittings	2	100%	100%	29-Sep-26	30-Sep-26	05-Sep-26 A	05-Sep-26 A	6,499.60	6,499.60	6,499.60	21
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	100%	01-Oct-26	04-Oct-26	29-Sep-26 A	17-Oct-26 A	25,998.40	25,998.40	25,998.40	-11
MLTX-02-005-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	19-Sep-26	21-Sep-26	28-Jul-26 A	02-Aug-26 A	6,921.94	6,921.94	6,921.94	43
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	0%	0%	12-Dec-26	19-Dec-26	23-Dec-26	31-Dec-26	0.00	0.00	48,746.52	-10
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	100%	01-Oct-26	10-Oct-26	28-Sep-26 A	13-Oct-26 A	64,995.36	64,995.36	64,995.36	-3
MLTX-02-005-CN-1	Installing of Water Heater	4	0%	100%	08-Dec-26	12-Dec-26	20-Oct-26 A	20-Oct-26 A	0.00	1,754.87	1,754.87	45
SEWER/DRAINAGE SYSTEM		134	60.72%	93.9%	16-Jul-26	12-Dec-26	18-Jul-26 A	15-Nov-26	48,530.38	75,048.52	79,923.17	24
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	100%	05-Oct-26	08-Oct-26	07-Nov-26 A	07-Nov-26 A	14,217.67	14,217.67	14,217.67	-25
MLTX-02-005-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	16-Jul-26	18-Jul-26	18-Jul-26 A	22-Jul-26 A	11,767.40	11,767.40	11,767.40	-4
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	100%	15-Oct-26	17-Oct-26	05-Nov-26 A	07-Nov-26 A	10,358.68	10,358.68	10,358.68	-17
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	15-Nov-26	12,186.63	7,311.98	12,186.63	-35
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	0%	100%	08-Dec-26	12-Dec-26	03-Nov-26 A	07-Nov-26 A	0.00	31,392.79	31,392.79	30
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	09-Nov-26	11-Nov-26	0.00	0.00	1,949.87	30
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	0%	0%	14-Dec-26	15-Dec-26	09-Nov-26	11-Nov-26	0.00	0.00	1,949.87	30
ELECTRICAL WORKS		124	53.82%	53.29%	13-Sep-26	19-Dec-26	19-Jul-26 A	06-Feb-27	208,264.67	206,217.32	386,998.59	-41
ROUGH-IN WORKS		12	100%	100%	13-Sep-26	27-Sep-26	19-Jul-26 A	09-Aug-26 A	206,217.32	206,217.32	206,217.32	42
MLTX-02-005-CN-1	Preleminary Works for Earthing Works	2	100%	100%	15-Sep-26	16-Sep-26	19-Jul-26 A	09-Aug-26 A	32,172.69	32,172.69	32,172.69	34
MLTX-02-005-CN-1	Preleminary Works for Panel Boards	2	100%	100%	13-Sep-26	14-Sep-26	19-Jul-26 A	20-Jul-26 A	68,245.12	68,245.12	68,245.12	48
MLTX-02-005-CN-1	Preleminary Works for Cable Works	2	100%	100%	15-Sep-26	16-Sep-26	19-Jul-26 A	22-Jul-26 A	12,488.92	12,488.92	12,488.92	48
MLTX-02-005-CN-1	Preleminary Works for Sockets and Power Points	2	100%	100%	15-Sep-26	16-Sep-26	19-Jul-26 A	20-Jul-26 A	15,990.55	15,990.55	15,990.55	50
MLTX-02-005-CN-1	Preleminary Works for Lightning Works	2	100%	100%	15-Sep-26	16-Sep-26	19-Jul-26 A	09-Aug-26 A	21,935.93	21,935.93	21,935.93	34
MLTX-02-005-CN-1	Preleminary Works for Data & Telecommunication System	2	100%	100%	26-Sep-26	27-Sep-26	19-Jul-26 A	09-Aug-26 A	24,470.75	24,470.75	24,470.75	42
MLTX-02-005-CN-1	Preleminary Works for Security and Access Control System	2	100%	100%	15-Sep-26	16-Sep-26	19-Jul-26 A	09-Aug-26 A	30,913.36	30,913.36	30,913.36	34
FIXTURE WORKS		45	1.13%	0%	09-Nov-26	19-Dec-26	15-Dec-26	06-Feb-27	2,047.35	0.00	180,781.27	-41
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	2%	0%	09-Nov-26	14-Nov-26	30-Dec-26	05-Jan-27	2,047.35	0.00	102,367.69	-44
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	13-Dec-26	16-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	6,239.59	-5
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	07-Dec-26	10-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	7,085.10	-10
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	0%	0%	01-Dec-26	03-Dec-26	15-Dec-26	19-Dec-26	0.00	0.00	6,824.51	-12
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	15-Dec-26	19-Dec-26	01-Feb-27	06-Feb-27	0.00	0.00	34,317.53	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	07-Dec-26	10-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	14,259.43	-10

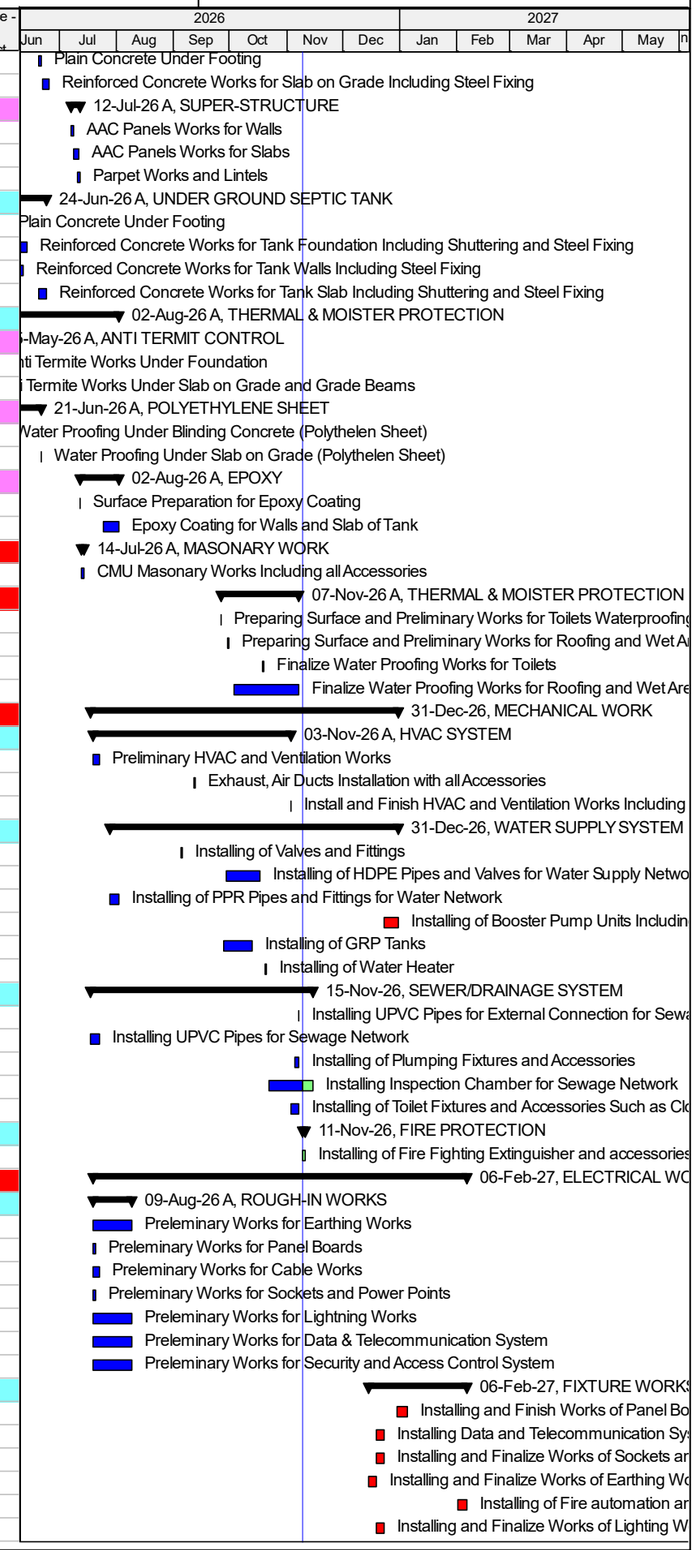

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	05-Dec-26	10-Dec-26	19-Dec-26	26-Dec-26	0.00	0.00	2,437.33	-12
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	0%	0%	05-Dec-26	08-Dec-26	06-Jan-27	11-Jan-27	0.00	0.00	7,250.09	-28
DOORS/WINDOWS		120	88.57%	100%	17-Sep-26	31-Dec-26	20-Oct-26 A	02-Nov-26 A	60,445.68	68,245.12	68,245.12	52
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	100%	17-Sep-26	19-Sep-26	02-Nov-26 A	02-Nov-26 A	52,646.24	52,646.24	52,646.24	-36
MLTX-02-005-CN-111	Preliminary Works For Doors	3	100%	100%	20-Sep-26	22-Sep-26	20-Oct-26 A	20-Oct-26 A	7,799.44	7,799.44	7,799.44	-23
MLTX-02-005-CN-111	Finalize Metal Doors for Toilets Building	9	0%	100%	22-Dec-26	31-Dec-26	20-Oct-26 A	20-Oct-26 A	0.00	1,949.86	1,949.86	62
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	0%	100%	05-Dec-26	12-Dec-26	02-Nov-26 A	02-Nov-26 A	0.00	5,849.58	5,849.58	35
METAL WORKS		75	57.14%	71.43%	14-Sep-26	23-Nov-26	16-Sep-26 A	19-Nov-26	7,799.44	9,749.30	13,649.02	4
MLTX-02-005-CN-111	Installation of Galvanized Steel Ladder	10	0%	100%	12-Nov-26	23-Nov-26	22-Oct-26 A	22-Oct-26 A	0.00	5,849.58	5,849.58	27
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	15-Nov-26	19-Nov-26	3,899.72	0.00	3,899.72	-52
MLTX-02-005-CN-111	Installation of Galvanized Steel Roof Scupper	4	100%	100%	28-Sep-26	01-Oct-26	16-Sep-26 A	16-Sep-26 A	3,899.72	3,899.72	3,899.72	12
FINISHING WORKS		102	87.44%	76.6%	22-Sep-26	12-Dec-26	10-Aug-26 A	14-Jan-27	145,271.41	127,256.05	166,130.97	-28
FLOOR FINISHES		71	93.18%	76.14%	04-Oct-26	12-Dec-26	17-Oct-26 A	14-Jan-27	15,989.09	13,064.27	17,159.03	-28
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	100%	04-Oct-26	05-Oct-26	17-Oct-26 A	18-Oct-26 A	11,894.39	11,894.39	11,894.39	-11
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	09-Nov-26	14-Nov-26	2,924.82	0.00	2,924.82	-29
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	09-Dec-26	12-Dec-26	11-Jan-27	14-Jan-27	0.00	0.00	1,169.94	-28
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	100%	11-Oct-26	14-Oct-26	19-Oct-26 A	19-Oct-26 A	1,169.88	1,169.88	1,169.88	-4
WALL FINISHES		102	92.17%	74.04%	22-Sep-26	06-Dec-26	10-Aug-26 A	23-Nov-26	123,510.80	99,220.88	134,001.04	12
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	100%	14-Oct-26	19-Oct-26	13-Oct-26 A	13-Oct-26 A	2,275.00	2,275.00	2,275.00	5
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	100%	100%	01-Nov-26	08-Nov-26	02-Nov-26 A	02-Nov-26 A	13,649.02	13,649.02	13,649.02	6
MLTX-02-005-CN-1	Granite Capping for Parpet	2	0%	100%	10-Nov-26	11-Nov-26	25-Oct-26 A	25-Oct-26 A	0.00	8,150.24	8,150.24	15
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works including Plastering	5	100%	100%	28-Sep-26	03-Oct-26	10-Aug-26 A	19-Aug-26 A	18,315.62	18,315.62	18,315.62	37
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works (External)	4	100%	100%	22-Sep-26	27-Sep-26	15-Aug-26 A	29-Aug-26 A	6,551.63	6,551.63	6,551.63	25
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	17-Nov-26	35,825.58	32,243.02	35,825.58	-29
MLTX-02-005-CN-1	Ceramic Finish Works for Walls	5	100%	100%	06-Oct-26	11-Oct-26	20-Sep-26 A	26-Sep-26 A	15,696.35	15,696.35	15,696.35	13
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	24-Oct-26	31-Oct-26	15-Nov-26	23-Nov-26	31,197.60	0.00	31,197.60	-19
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	0%	100%	05-Dec-26	06-Dec-26	21-Oct-26 A	25-Oct-26 A	0.00	2,340.00	2,340.00	36
CELLING FINISHES		49	38.55%	100%	12-Oct-26	09-Dec-26	19-Oct-26 A	25-Oct-26 A	5,771.52	14,970.90	14,970.90	39
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	15	0%	100%	15-Nov-26	01-Dec-26	24-Oct-26 A	25-Oct-26 A	0.00	5,771.52	5,771.52	32
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	0%	100%	07-Dec-26	09-Dec-26	25-Oct-26 A	25-Oct-26 A	0.00	3,427.86	3,427.86	39
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	100%	12-Oct-26	19-Oct-26	19-Oct-26 A	22-Oct-26 A	5,771.52	5,771.52	5,771.52	-3
SPECIALTIES WORK		75	25%	0%	18-Oct-26	17-Dec-26	09-Nov-26	04-Feb-27	14,623.96	0.00	58,495.83	-41
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	0%	0%	15-Dec-26	17-Dec-26	01-Feb-27	04-Feb-27	0.00	0.00	24,373.26	-41
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	15-Nov-26	14,623.96	0.00	14,623.96	-19
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	0%	0%	12-Dec-26	14-Dec-26	28-Jan-27	01-Feb-27	0.00	0.00	19,498.61	-41
TESTING & COMMISSIONING		26	0%	0%	20-Dec-26	02-Jan-27	06-Feb-27	09-Mar-27	0.00	0.00	0.00	-55
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	2	0%	0%	30-Dec-26	31-Dec-26	14-Feb-27	16-Feb-27	0.00	0.00	0.00	-39
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	12	0%	0%	20-Dec-26	02-Jan-27	06-Feb-27	20-Feb-27	0.00	0.00	0.00	-41
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	27-Dec-26	31-Dec-26	03-Mar-27	09-Mar-27	0.00	0.00	0.00	-56
HASA OASIS		312	44.72%	48.06%	03-Mar-26	02-Jan-27	04-Mar-26 A	03-Mar-27	4,451,927.78	4,785,309.30	9,955,979.43	-50
MOBILIZATION		32	0%	0%	03-Mar-26	12-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
TOPOGRAPHIC SURVEY		5	0%	0%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-1860	Site Survey Works	5	100%	100%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
SITE FACILITIES & OFFICES		29	0%	0%	03-Mar-26	08-Apr-26	04-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-1740	Manpower Mobalization	5	100%	100%	30-Mar-26	04-Apr-26	29-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	1
MLTX-02-005-MB-1750	Equipment Mobalization	7	100%	100%	01-Apr-26	08-Apr-26	26-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-1770	Site Layout Plan	4	100%	100%	03-Mar-26	07-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1780	Clear & Grub for Offices & Access Road	3	100%	100%	08-Mar-26	10-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1790	Construct Site Access Roads	4	100%	100%	11-Mar-26	15-Mar-26	09-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	2
MLTX-02-005-MB-1800	Construct Temporary Fence	7	100%	100%	11-Mar-26	18-Mar-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1810	Construct Site Offices & Storage	14	100%	100%	19-Mar-26	07-Apr-26	14-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-1820	Install Project Signs	8	100%	100%	19-Mar-26	31-Mar-26	14-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-1830	Install Site Facilities	4	100%	100%	19-Mar-26	26-Mar-26	24-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1840	Electrical Works & Connections	6	100%	100%	30-Mar-26	05-Apr-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-1850	Construct Parking Sheds	6	100%	100%	19-Mar-26	29-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	-1
PRELIMINARY SUBMITTALS		28	0%	0%	08-Mar-26	12-Apr-26	09-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
PREPARATIONS & SUBMITTAL BY CONTRACTORS		16	0%	0%	08-Mar-26	29-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-176	Preparation and Submittal of Detailed Work Order	10	100%	100%	08-Mar-26	18-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-187	Preparation and Submittal of Project Execution Plan	8	100%	100%	17-Mar-26	29-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-188	Submission of Contractor Project Quality Plan	8	100%	100%	08-Mar-26	16-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-189	Submission of Construction Safety & Environmental	8	100%	100%	17-Mar-26	29-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-190	Preparation and Submittal of Organization Chart	8	100%	100%	17-Mar-26	29-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	7
MLTX-02-005-MB-191	Preparation and Submittal of Communication Plan	8	100%	100%	17-Mar-26	29-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	7
APPROVALS BY EMPLOYERS		20	0%	0%	17-Mar-26	12-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7

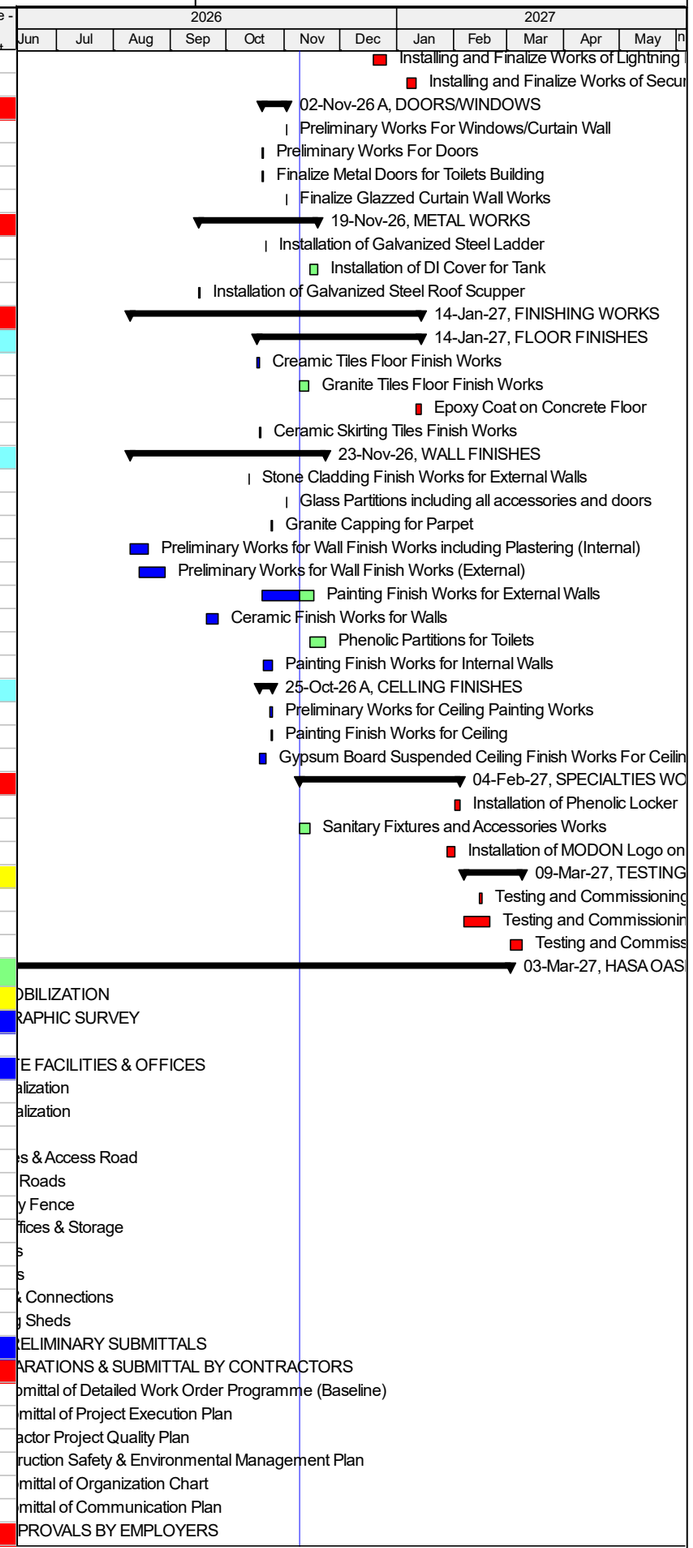

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-MB-192	Approval of Detailed Work Order Programme (Baseline)	10	100%	100%	19-Mar-26	02-Apr-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-193	Approval of Project Execution Plan	10	100%	100%	01-Apr-26	12-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	9
MLTX-02-005-MB-194	Approval of Contractor Project Quality Plan	10	100%	100%	17-Mar-26	31-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-195	Approval of Construction Safety & Environmental	10	100%	100%	01-Apr-26	12-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	9
MLTX-02-005-MB-196	Approval of Organization Chart	10	100%	100%	01-Apr-26	12-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	9
MLTX-02-005-MB-197	Approval of Communication Plan	10	100%	100%	01-Apr-26	12-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	9
ENGINEERING		254	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	06-Jan-27	0.00	0.00	0.00	-16
SHOP DRAWINGS		253	0%	0%	09-Mar-26	07-Dec-26	09-Mar-26 A	06-Jan-27	0.00	0.00	0.00	-25
SHOP DRAWINGS SUBMISSION		245	0%	0%	09-Mar-26	01-Dec-26	09-Mar-26 A	08-Dec-26	0.00	0.00	0.00	-5
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		135	0%	0%	09-Mar-26	19-Aug-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	130
MLTX-02-005-EN-7	Shop DWG Submittal for Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Setting Out	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Grading Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Curb Setting Out Points	15	100%	100%	16-Jul-26	02-Aug-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	115
MLTX-02-005-EN-7	Shop DWG Submittal for Signing & Marking Layout Plan	15	100%	100%	03-Aug-26	19-Aug-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	130
MLTX-02-005-EN-7	Shop DWG Submittal for Standards Details	15	100%	100%	03-Aug-26	19-Aug-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	130
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		192	0%	0%	09-Mar-26	26-Oct-26	09-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	74
ARCHITECTURE WORKS		15	0%	0%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Floor Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Elevations	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Ceiling Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Finishes Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Toilet Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Doors/Windows Schedule	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
STRUCTURE WORKS		21	0%	0%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Foundation Plan	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Ground Floor Framing Plan	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Sections/Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MECHANCAL WORKS		87	0%	0%	16-Jul-26	26-Oct-26	15-Mar-26 A	07-Jul-26 A	0.00	0.00	0.00	94
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	100%	07-Sep-26	01-Oct-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	161
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	100%	10-Aug-26	02-Sep-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	137
MLTX-02-005-EN	Shop DWG Submittal for HVAC Equipment Schedule	21	100%	100%	03-Sep-26	28-Sep-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	158
MLTX-02-005-EN	Shop DWG Submittal for Fire Fighting Layout	21	100%	100%	03-Oct-26	26-Oct-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	182
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Layout	21	100%	100%	16-Jul-26	09-Aug-26	15-Mar-26 A	20-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Details	21	100%	100%	16-Jul-26	09-Aug-26	15-Mar-26 A	20-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Shop DWG Submittal for Drainage Layout	21	100%	100%	22-Jul-26	15-Aug-26	15-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	63
MLTX-02-005-EN	Shop DWG Submittal for Drainage Details	21	100%	100%	16-Jul-26	09-Aug-26	15-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	58
MLTX-02-005-EN	Shop DWG Submittal for Dut Routing Layout	21	100%	100%	10-Aug-26	02-Sep-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	137
MLTX-02-005-EN	Shop DWG Submittal for Diffusers Layout	21	100%	100%	07-Sep-26	01-Oct-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	73
ELECTRICAL WORKS		153	0%	0%	30-Mar-26	28-Sep-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	21	100%	100%	16-Jul-26	09-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	116
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	100%	22-Jul-26	15-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	121
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	21	100%	100%	03-Sep-26	28-Sep-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	93
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	15	100%	100%	01-Jun-26	17-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN	Shop DWG Submittal for Lighting Installation Details	21	100%	100%	16-Jul-26	09-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	116
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Cable Tray Installation Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Manhole & Ductbank Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Grounding Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Lightning Protection Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Installation Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for CCTV Details	15	100%	100%	22-Jul-26	08-Aug-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN	Shop DWG Submittal for Grounding Layout	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Lightning Protection System Layout	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Layout	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for CCTV Layout	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for CCTV Riser Diagram	15	100%	100%	05-Jul-26	21-Jul-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Shop DWG Submittal for Telephone & Data Layout	21	100%	100%	04-May-26	31-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Submittal for Telephone & Data Riser Diagram	21	100%	100%	16-Jul-26	09-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	116
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		245	0%	0%	09-Mar-26	01-Dec-26	09-Mar-26 A	08-Dec-26	0.00	0.00	0.00	-5
ARCHITECTURE WORKS		152	0%	0%	09-Mar-26	08-Sep-26	09-Mar-26 A	13-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN	Shop DWG Submittal for Playground Plan/Layout	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10

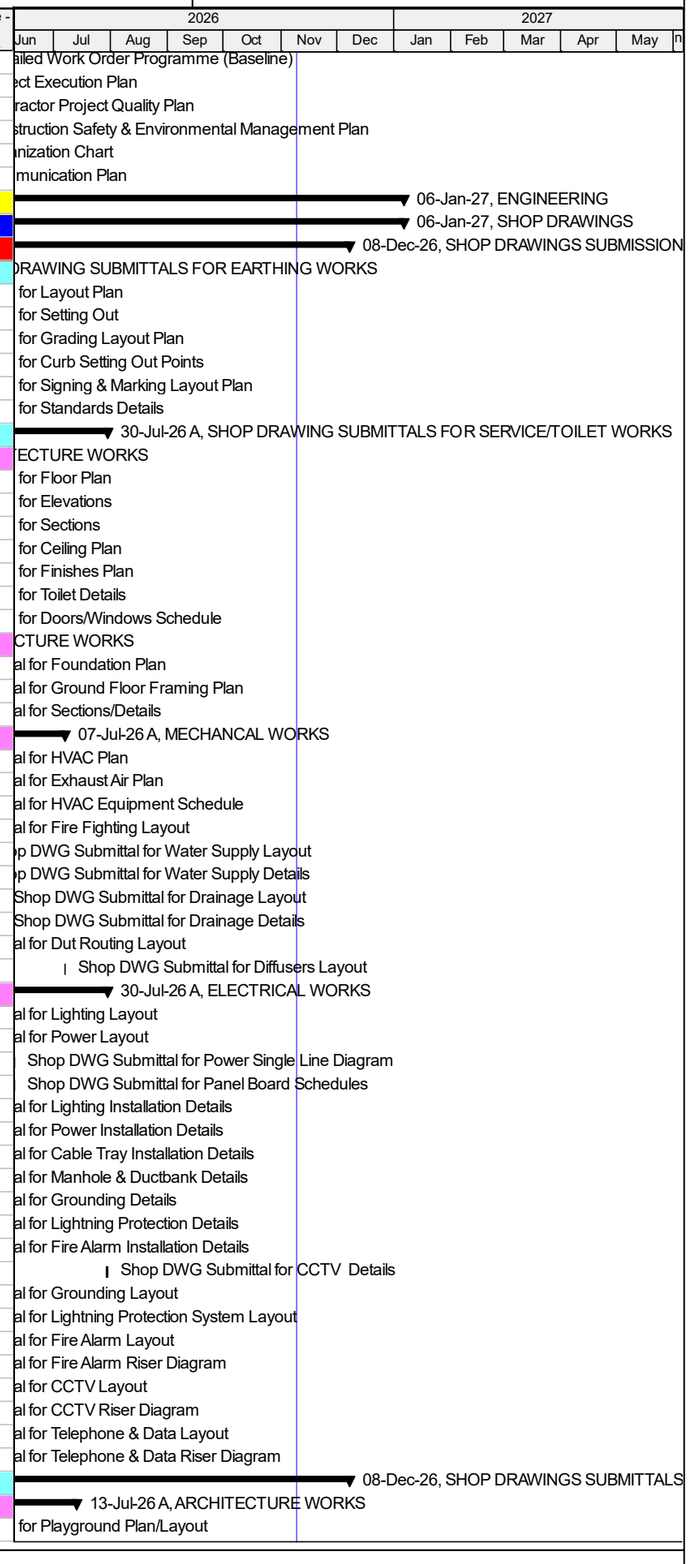


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Submittal for Furniture & Marking	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	28-Apr-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Interlock Pattern Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Shop DWG Submittal for Doors/Windows Schedule	21	100%	100%	16-Aug-26	08-Sep-26	13-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN	Shop DWG Submittal for Dome Internal Layout	21	100%	100%	06-Apr-26	29-Apr-26	09-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-18
STRUCTURE WORKS		63	0%	0%	30-Apr-26	15-Jul-26	15-Mar-26 A	14-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN	Shop DWG Submittal for Air Dome System	21	100%	100%	30-Apr-26	24-May-26	15-Mar-26 A	10-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Shop DWG Submittal for Foundation of Air Dome	21	100%	100%	22-Jun-26	15-Jul-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	21	100%	100%	22-Jun-26	15-Jul-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	1
AIR DOME SYSTEM		21	0%	0%	25-May-26	21-Jun-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Air Dome Structural Layout	21	100%	100%	25-May-26	21-Jun-26	15-Mar-26 A	10-May-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Shop DWG Submittal for Membrane Panel Layout	21	100%	100%	25-May-26	21-Jun-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Cable Tension Layout	21	100%	100%	25-May-26	21-Jun-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Airlock Door Details	21	100%	100%	25-May-26	21-Jun-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Emergency Exit Details	21	100%	100%	25-May-26	21-Jun-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	20
SPORTS EQUIPMENT		108	0%	0%	25-May-26	01-Oct-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	80
MLTX-02-005-EN	Shop DWG Submittal for Football Turf Installation	21	100%	100%	25-May-26	21-Jun-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Shop DWG Submittal for Basketball Court Marking	21	100%	100%	25-May-26	21-Jun-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Shop DWG Submittal for Padel Court Structure	21	100%	100%	07-Sep-26	01-Oct-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	80
MECHANCAL WORKS		25	0%	0%	26-Sep-26	24-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	25	100%	100%	26-Sep-26	24-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	25	100%	100%	26-Sep-26	24-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	8
ELECTRICAL WORKS		200	0%	0%	04-May-26	01-Dec-26	20-Aug-26 A	08-Dec-26	0.00	0.00	0.00	-5
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	25	100%	100%	26-Sep-26	24-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	25	100%	100%	29-Sep-26	27-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	25	100%	100%	29-Sep-26	27-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	25	100%	100%	29-Sep-26	27-Oct-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Installation Details	30	43.67%	100%	25-Oct-26	28-Nov-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	38
MLTX-02-005-EN	Shop DWG Submittal for CCTV Details	21	100%	100%	04-May-26	31-May-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-70
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Layout	30	43.67%	100%	25-Oct-26	28-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	30	33.67%	100%	28-Oct-26	01-Dec-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Shop DWG Submittal for CCTV Layout	21	100%	100%	29-Sep-26	22-Oct-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	53
MLTX-02-005-EN	Shop DWG Submittal for CCTV Riser Diagram	21	100%	100%	29-Sep-26	22-Oct-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	53
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		135	0%	0%	09-Mar-26	19-Aug-26	09-Mar-26 A	29-Jul-26 A	0.00	0.00	0.00	18
ARCHITECTURE WORKS		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Landscape Layout	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Shop DWG Submittal for Hardscape Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Shop DWG Submittal for Planting Plan	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Landscape Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MECHANCAL WORKS		30	0%	0%	16-Jul-26	19-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	38
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Details	30	100%	100%	16-Jul-26	19-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	38
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Layout	30	100%	100%	16-Jul-26	19-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	38
ELECTRICAL WORKS		135	0%	0%	09-Mar-26	19-Aug-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Shop DWG Submittal for Lighting General Arrangement	30	100%	100%	16-Jul-26	19-Aug-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Shop DWG Submittal for Lighting Network Layout	30	100%	100%	09-Mar-26	15-Apr-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
MLTX-02-005-EN	Shop DWG Submittal for Lighting Details	30	100%	100%	16-Jul-26	19-Aug-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Shop DWG Submittal for Lighting Single Line Diagram	30	100%	100%	16-Jul-26	19-Aug-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	18
SHOP DRAWINGS APPROVALS		238	0%	0%	30-Mar-26	07-Dec-26	15-Mar-26 A	06-Jan-27	0.00	0.00	0.00	-25
SHOP DRAWING APPROVAL FOR EARTHING WORKS		90	0%	0%	11-Jun-26	24-Sep-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	150
MLTX-02-005-EN-1	Shop DWG Approval for Layout Plan	15	100%	100%	11-Jun-26	28-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-1	Shop DWG Approval for Setting Out	15	100%	100%	29-Jun-26	15-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	90
MLTX-02-005-EN-1	Shop DWG Approval for Grading Layout Plan	15	100%	100%	16-Jul-26	02-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	105
MLTX-02-005-EN-1	Shop DWG Approval for Curb Setting Out Points	15	100%	100%	03-Aug-26	19-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	120
MLTX-02-005-EN-1	Shop DWG Approval for Signing & Marking Layout Plan	15	100%	100%	20-Aug-26	06-Sep-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	135
MLTX-02-005-EN-1	Shop DWG Approval for Standards Details	15	100%	100%	07-Sep-26	24-Sep-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	150
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		198	0%	0%	30-Mar-26	19-Nov-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	95
ARCHITECTURE WORKS		60	0%	0%	30-Mar-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Floor Plan	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Elevations	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Sections	30	100%	100%	22-Apr-26	30-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN	Shop DWG Approval for Ceiling Plan	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Finishes Plan	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Toilet Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60

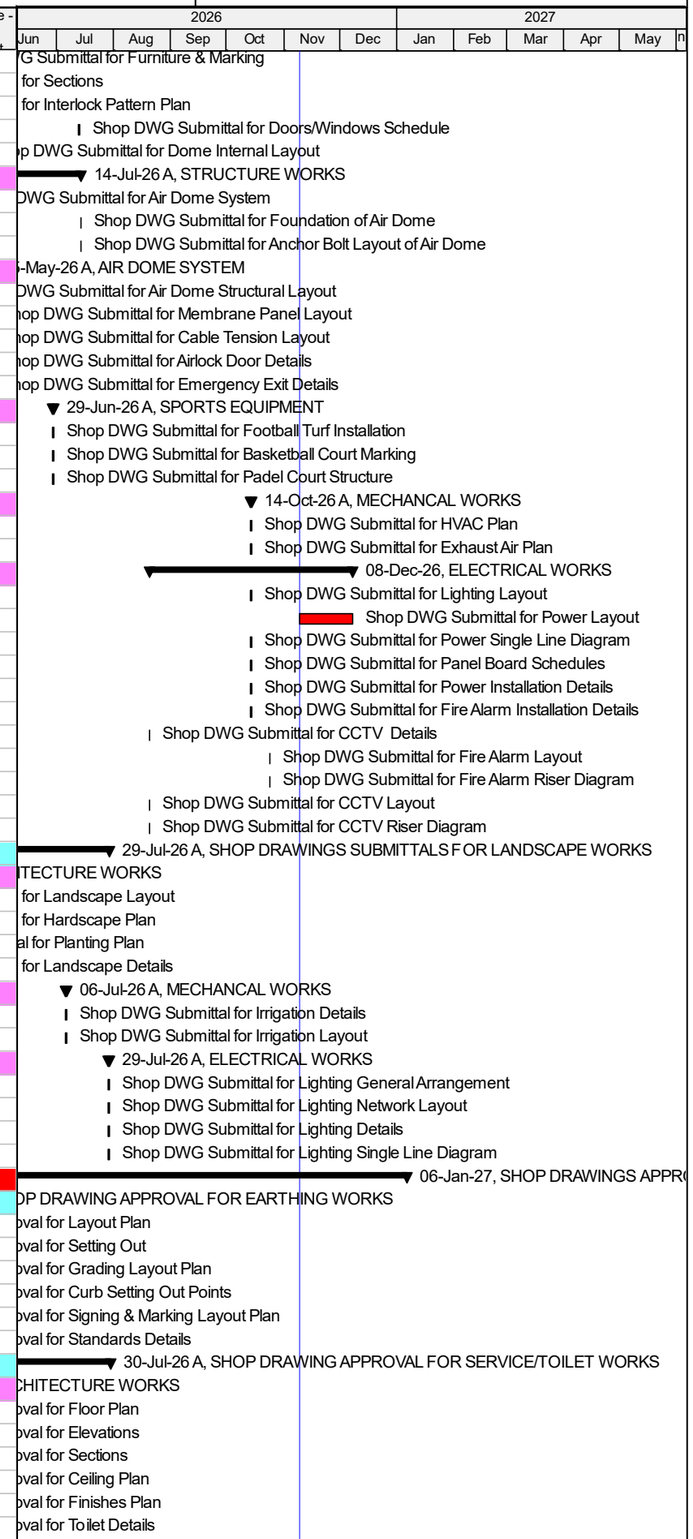


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	29-Apr-26	06-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	56
STRUCTURE WORKS		24	0%	0%	23-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Foundation Plan	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Ground Floor Framing Plan	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Sections/Details	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MECHANCAL WORKS		87	0%	0%	10-Aug-26	19-Nov-26	24-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	95
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	21	62.38%	100%	25-Oct-26	17-Nov-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	93
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	21	100%	100%	14-Sep-26	08-Oct-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	157
MLTX-02-005-EI	Shop DWG Approval for HVAC Equipment Schedule	21	100%	100%	10-Oct-26	02-Nov-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	80
MLTX-02-005-EI	Shop DWG Approval for Fire Fighting Layout	21	52.86%	100%	27-Oct-26	19-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	193
MLTX-02-005-EI	Shop DWG Approval for Water Supply Layout	21	100%	100%	20-Aug-26	13-Sep-26	03-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	87
MLTX-02-005-EI	Shop DWG Approval for Water Supply Details	21	100%	100%	20-Aug-26	13-Sep-26	03-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	87
MLTX-02-005-EI	Shop DWG Approval for Drainage Layout	21	100%	100%	16-Aug-26	08-Sep-26	30-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	82
MLTX-02-005-EI	Shop DWG Approval for Drainage Details	21	100%	100%	10-Aug-26	02-Sep-26	30-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	77
MLTX-02-005-EI	Shop DWG Approval for Duct Routing Layout	21	100%	100%	14-Sep-26	08-Oct-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	157
MLTX-02-005-EI	Shop DWG Approval for Diffusers Layout	21	62.38%	100%	25-Oct-26	17-Nov-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	93
ELECTRICAL WORKS		141	0%	0%	01-Jun-26	12-Nov-26	24-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	89
MLTX-02-005-EI	Shop DWG Approval for Lighting Layout	21	100%	100%	10-Aug-26	02-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Power Layout	21	100%	100%	16-Aug-26	08-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	132
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	21	100%	100%	29-Sep-26	22-Oct-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	71
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	30	100%	100%	29-Jun-26	02-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	9
MLTX-02-005-EI	Shop DWG Approval for Lighting Installation Details	21	100%	100%	10-Aug-26	02-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	30	100%	100%	27-Jul-26	30-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	124
MLTX-02-005-EI	Shop DWG Approval for Cable Tray Installation Details	30	100%	100%	25-Jun-26	29-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EI	Shop DWG Approval for Manhole & Ductbank Details	30	100%	100%	25-Jun-26	29-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EI	Shop DWG Approval for Grounding Details	30	100%	100%	30-Jul-26	02-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Lightning Protection Details	30	100%	100%	30-Jul-26	02-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Installation Details	30	87%	100%	10-Oct-26	12-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	187
MLTX-02-005-EI	Shop DWG Approval for CCTV Details	30	100%	100%	09-Aug-26	12-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Grounding Layout	30	100%	100%	30-Jul-26	02-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Lightning Protection System Layout	30	100%	100%	30-Jul-26	02-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	127
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Layout	30	87%	100%	10-Oct-26	12-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	187
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Riser Diagram	30	87%	100%	10-Oct-26	12-Nov-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	187
MLTX-02-005-EI	Shop DWG Approval for CCTV Layout	30	100%	100%	30-Jul-26	02-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	29
MLTX-02-005-EI	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	30-Jul-26	02-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	29
MLTX-02-005-EI	Shop DWG Approval for Telephone & Data Layout	21	100%	100%	01-Jun-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MLTX-02-005-EI	Shop DWG Approval for Telephone & Data Riser Diagram	21	100%	100%	10-Aug-26	02-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	29
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		238	0%	0%	30-Mar-26	07-Dec-26	15-Mar-26 A	06-Jan-27	0.00	0.00	0.00	-25
ARCHITECTURE WORKS		150	0%	0%	30-Mar-26	24-Sep-26	15-Mar-26 A	24-May-26 A	0.00	0.00	0.00	102
MLTX-02-005-EI	Shop DWG Approval for Playground Plan/Layout	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EI	Shop DWG Approval for Furniture & Marking	30	100%	100%	20-Aug-26	24-Sep-26	15-Mar-26 A	14-May-26 A	0.00	0.00	0.00	110
MLTX-02-005-EI	Shop DWG Approval for Sections	20	100%	100%	30-Mar-26	21-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EI	Shop DWG Approval for Interlock Pattern Plan	30	100%	100%	16-Jul-26	19-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	120
MLTX-02-005-EI	Shop DWG Approval for Doors/Windows Schedule	20	100%	100%	06-Apr-26	28-Apr-26	15-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Shop DWG Approval for Dome Internal Layout	30	100%	100%	11-Jun-26	15-Jul-26	15-Mar-26 A	24-May-26 A	0.00	0.00	0.00	42
STRUCTURE WORKS		31	0%	0%	05-Jul-26	09-Aug-26	24-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	20
MLTX-02-005-EI	Shop DWG Approval for Air Dome System	21	100%	100%	05-Jul-26	28-Jul-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	60
MLTX-02-005-EI	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	16-Jul-26	09-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	20
MLTX-02-005-EI	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	16-Jul-26	09-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	20
MLTX-02-005-EI	Shop DWG Approval for Anchor Bolt Layout of Air Dome	21	100%	100%	16-Jul-26	09-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	20
AIR DOME SYSTEM		21	0%	0%	22-Jun-26	15-Jul-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EI	Shop DWG Approval for Air Dome Structural Layout	21	100%	100%	22-Jun-26	15-Jul-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	49
MLTX-02-005-EI	Shop DWG Approval for Membrane Panel Layout	21	100%	100%	22-Jun-26	15-Jul-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EI	Shop DWG Approval for Cable Tension Layout	21	100%	100%	22-Jun-26	15-Jul-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EI	Shop DWG Approval for Airlock Door Details	21	100%	100%	22-Jun-26	15-Jul-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EI	Shop DWG Approval for Emergency Exit Details	21	100%	100%	22-Jun-26	15-Jul-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	41
SPORTS EQUIPMENT		144	0%	0%	22-Jun-26	07-Dec-26	20-Jul-26 A	24-Oct-26 A	0.00	0.00	0.00	38
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	21	100%	100%	10-Oct-26	02-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	8
MLTX-02-005-EI	Shop DWG Approval for Basketball Court Marking	30	100%	100%	22-Jun-26	26-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EI	Shop DWG Approval for Padel Court Structure	30	17%	100%	03-Nov-26	07-Dec-26	20-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	119
MECHANCAL WORKS		23	0%	0%	25-Oct-26	19-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	23
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	23	56.96%	100%	25-Oct-26	19-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	23
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	23	56.96%	100%	25-Oct-26	19-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	23
ELECTRICAL WORKS		55	0%	0%	06-Jun-26	26-Nov-26	25-Aug-26 A	06-Jan-27	0.00	0.00	0.00	-34

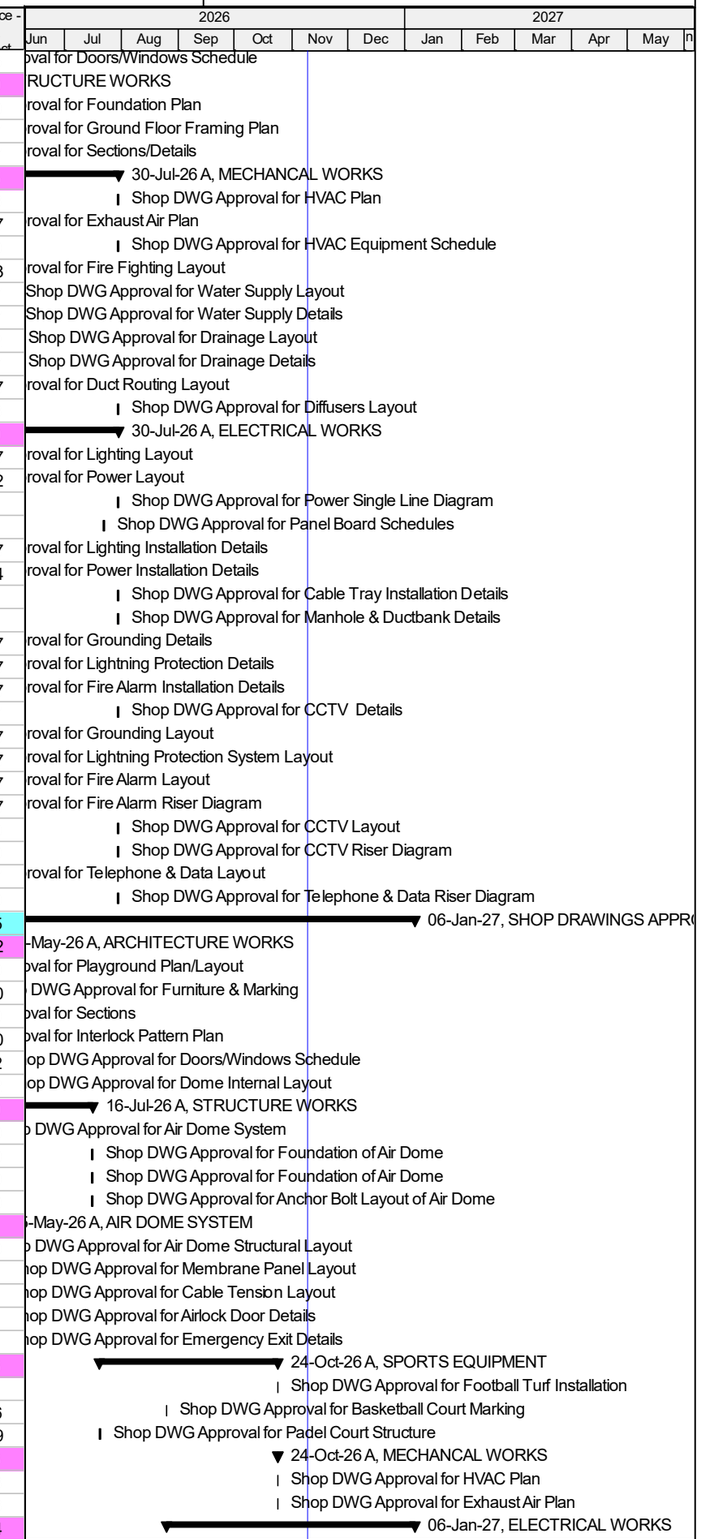


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	25	52.4%	100%	25-Oct-26	22-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Shop DWG Approval for Power Layout	25	100%	0%	06-Jun-26	04-Jul-26	08-Dec-26	06-Jan-27	0.00	0.00	0.00	-158
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	25	40.4%	100%	28-Oct-26	25-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	28
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	25	40.4%	100%	28-Oct-26	25-Nov-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	28
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	25	40.4%	0%	28-Oct-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-EN	Shop DWG Approval for CCTV Details	21	24.29%	100%	03-Nov-26	26-Nov-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	79
MLTX-02-005-EN	Shop DWG Approval for CCTV Layout	21	24.29%	100%	03-Nov-26	26-Nov-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	79
MLTX-02-005-EN	Shop DWG Approval for CCTV Riser Diagram	21	24.29%	100%	03-Nov-26	26-Nov-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	79
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		150	0%	0%	30-Mar-26	24-Sep-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	47
ARCHITECTURE WORKS		30	0%	0%	30-Mar-26	03-May-26	15-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Shop DWG Approval for Landscape Layout	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Hardscape Plan	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Planting Plan	15	100%	100%	16-Apr-26	03-May-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Shop DWG Approval for Landscape Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	21
MECHANCAL WORKS		30	0%	0%	20-Aug-26	24-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Shop DWG Approval for Irrigation Details	30	100%	100%	20-Aug-26	24-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Shop DWG Approval for Irrigation Layout	30	100%	100%	20-Aug-26	24-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	66
ELECTRICAL WORKS		135	0%	0%	16-Apr-26	24-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN	Shop DWG Approval for Lighting General Arrangement	30	100%	100%	20-Aug-26	24-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN	Shop DWG Approval for Lighting Network Layout	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Details	30	100%	100%	20-Aug-26	24-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN	Shop DWG Approval for Lighting Single Line Diagram	30	100%	100%	20-Aug-26	24-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	47
METHOD STATEMENTS		238	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	82
METHOD STATEMENT SUBMITTAL		196	0%	0%	08-Mar-26	29-Oct-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	125
CIVIL WORKS		36	0%	0%	08-Mar-26	21-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Concrete	21	100%	100%	29-Mar-26	21-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for	21	100%	100%	08-Mar-26	04-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	15
ARCHITECTURE WORKS		178	0%	0%	08-Mar-26	08-Oct-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	109
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Plastering	15	100%	100%	29-Jun-26	15-Jul-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-32
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Tilling	30	100%	100%	01-Jul-26	04-Aug-26	08-Mar-26 A	17-May-26 A	0.00	0.00	0.00	65
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	30	100%	100%	16-Jul-26	19-Aug-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	30	100%	100%	03-Sep-26	08-Oct-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	109
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Parking	30	100%	100%	31-Aug-26	05-Oct-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	111
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Soft	21	100%	100%	16-Jul-26	09-Aug-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	58
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Fence	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Air Dome	30	100%	100%	24-May-26	30-Jun-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Metal	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-48
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Partitions	21	100%	100%	05-Apr-26	28-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Gypsum	21	100%	100%	01-Jul-26	25-Jul-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	45
MECHANICAL WORKS		90	0%	0%	16-Jul-26	29-Oct-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	125
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	21	100%	100%	16-Jul-26	09-Aug-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Water	21	100%	100%	16-Jul-26	09-Aug-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Fire	21	100%	100%	06-Oct-26	29-Oct-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	125
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Irrigation	15	100%	100%	05-Aug-26	22-Aug-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for HVAC	21	100%	100%	10-Aug-26	02-Sep-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	77
ELECTRICAL WORKS		127	0%	0%	05-Apr-26	02-Sep-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	95
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Electrical	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Lighting	21	100%	100%	10-Aug-26	02-Sep-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	95
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for CCTV	30	100%	100%	01-Jul-26	04-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	70
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Lighting	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	21	100%	100%	29-Apr-26	23-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Panel	21	100%	100%	26-Jul-26	18-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	82
METHOD STATEMENT APPROVAL		223	0%	0%	29-Mar-26	17-Dec-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	82
CIVIL WORKS		51	0%	0%	29-Mar-26	30-May-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN-1	Approval of Method Statement for Earthwork	15	100%	100%	29-Mar-26	14-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN-1	Approval of Method Statement for Concrete Works	30	100%	100%	22-Apr-26	30-May-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN-1	Approval of Method Statement for Waterproofing	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-2
ARCHITECTURE WORKS		196	0%	0%	29-Apr-26	17-Dec-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN-1	Approval of Method Statement for Plastering Works	30	100%	100%	05-Aug-26	08-Sep-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	109
MLTX-02-005-EN-1	Approval of Method Statement for Masonary Works	30	100%	100%	29-Apr-26	06-Jun-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	10

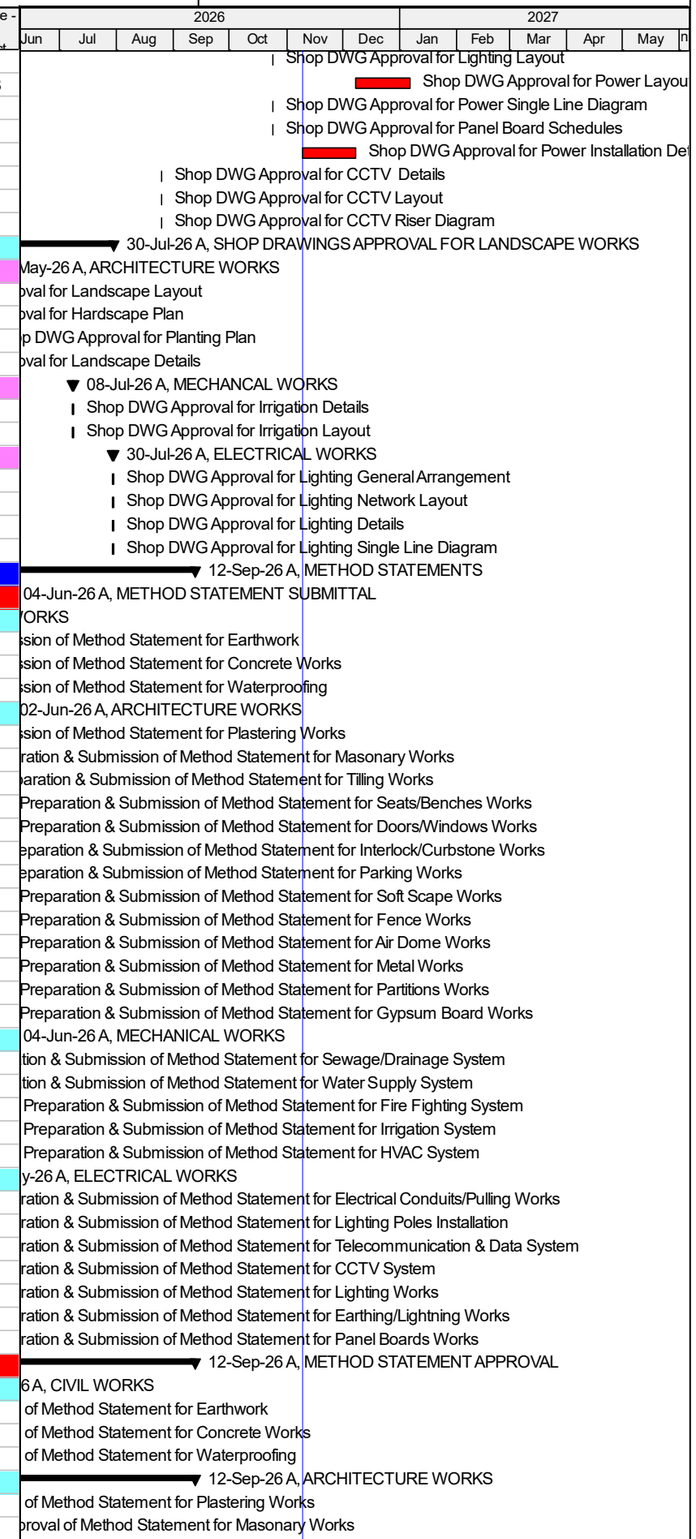

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-1	Approval of Method Statement for Tilling Works	30	100%	100%	05-Aug-26	08-Sep-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN-1	Approval of Method Statement for Seats/Benches Works	30	100%	100%	09-Sep-26	14-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN-1	Approval of Method Statement for Doors/Windows Works	30	0%	100%	14-Nov-26	17-Dec-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN-1	Approval of Method Statement for Interlock/Curbstone Works	30	100%	100%	05-Aug-26	08-Sep-26	15-Aug-26 A	15-Aug-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Approval of Method Statement for Parking Works	30	87%	100%	10-Oct-26	12-Nov-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-1	Approval of Method Statement for Soft Scape Works	30	100%	100%	09-Sep-26	14-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN-1	Approval of Method Statement for Fence Works	30	47%	100%	24-Oct-26	26-Nov-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	92
MLTX-02-005-EN-1	Approval of Method Statement for Air Dome Works	30	100%	100%	01-Jul-26	04-Aug-26	11-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN-1	Approval of Method Statement for Partitions Works	30	100%	100%	09-Sep-26	14-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN-1	Approval of Method Statement for Gypsum Board Works	30	100%	100%	09-Sep-26	14-Oct-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	46
MECHANICAL WORKS		90	0%	0%	10-Aug-26	23-Nov-26	02-Jun-26 A	26-Aug-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-1	Approval of Method Statement for Sewage/Drainage System	21	100%	100%	10-Aug-26	02-Sep-26	09-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	73
MLTX-02-005-EN-1	Approval of Method Statement for Water Supply System	21	100%	100%	23-Aug-26	15-Sep-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	90
MLTX-02-005-EN-1	Approval of Method Statement for Fire Fighting System	21	38.57%	100%	31-Oct-26	23-Nov-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-1	Approval of Method Statement for Irrigation System	15	100%	100%	09-Sep-26	27-Sep-26	28-Jun-26 A	28-Jun-26 A	0.00	0.00	0.00	77
MLTX-02-005-EN-1	Approval of Method Statement for HVAC System	21	100%	100%	03-Sep-26	28-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	28
ELECTRICAL WORKS		132	0%	0%	29-Apr-26	04-Oct-26	12-Jul-26 A	26-Aug-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN-1	Approval of Method Statement for Electrical Conduits/Pulling	21	100%	100%	05-Aug-26	29-Aug-26	12-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Poles Installation	21	100%	100%	09-Sep-26	04-Oct-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN-1	Approval of Method Statement for Telecommunication & Data	30	100%	100%	20-May-26	27-Jun-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Approval of Method Statement for CCTV System	30	100%	100%	05-Aug-26	08-Sep-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Works	21	100%	100%	29-Apr-26	23-May-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-65
MLTX-02-005-EN-1	Approval of Method Statement for Earthing/Lightning Works	21	100%	100%	24-May-26	20-Jun-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EN-1	Approval of Method Statement for Panel Boards Works	21	100%	100%	19-Aug-26	12-Sep-26	12-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	44
PRE-QUALIFICATION & MATERIAL		171	0%	0%	08-Mar-26	30-Sep-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	15
PRE-QUALIFICATION		141	0%	0%	08-Mar-26	25-Aug-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	68
TOILET/SERVICE WORKS		141	0%	0%	08-Mar-26	25-Aug-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	68
STEEL REINFORCEMENT		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Approval for Steel Reinforcement	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Reinforcement	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
READY MIX CONCRETE		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Ready Mixed Concrete	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval of Ready Mixed Concrete	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
CONCRETE BLOCKS		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Concrete Blocks	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
WATER PROOFING		51	0%	0%	08-Mar-26	09-May-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN	Pre-Qualification Submittal for Water Proofing	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Water Proofing	21	100%	100%	15-Apr-26	09-May-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	40
FLOOR/WALL TILES		105	0%	0%	08-Mar-26	14-Jul-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	53
MLTX-02-005-EN	Pre-Qualification Submittal for Tilling Materials	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Tailling Material	15	100%	100%	28-Jun-26	14-Jul-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	53
SUSPENDED CEILING		141	0%	0%	08-Mar-26	25-Aug-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	130
MLTX-02-005-EN	Pre-Qualification Submittal for Suspend Ceiling	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Suspend Ceiling	15	100%	100%	09-Aug-26	25-Aug-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	130
DOORS/WINDOWS		126	0%	0%	08-Mar-26	08-Aug-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	115
MLTX-02-005-EN	Pre-Qualification Submittal for Doors/Windows	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Doors/Windows	15	100%	100%	22-Jul-26	08-Aug-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	115
FURNITURES		45	0%	0%	08-Mar-26	02-May-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Furnitures	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Furnitures	15	100%	100%	15-Apr-26	02-May-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-7
SANITARY FIXTURES		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Sanitary Fixtures	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Sanitary Fixtures	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
WATER SUPPLY PIPES		105	0%	0%	08-Mar-26	14-Jul-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	94
MLTX-02-005-EN	Pre-Qualification Submittal for Water Supply Pipes	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Water Supply Pipes	15	100%	100%	28-Jun-26	14-Jul-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	94
SEWAGE/DRAINAGE PIPES		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
PACKAGE AC UNITS		30	0%	0%	29-Mar-26	02-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	15-Apr-26	02-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
AIR DIFUSSERS/GRILLS		45	0%	0%	05-Jul-26	25-Aug-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	93

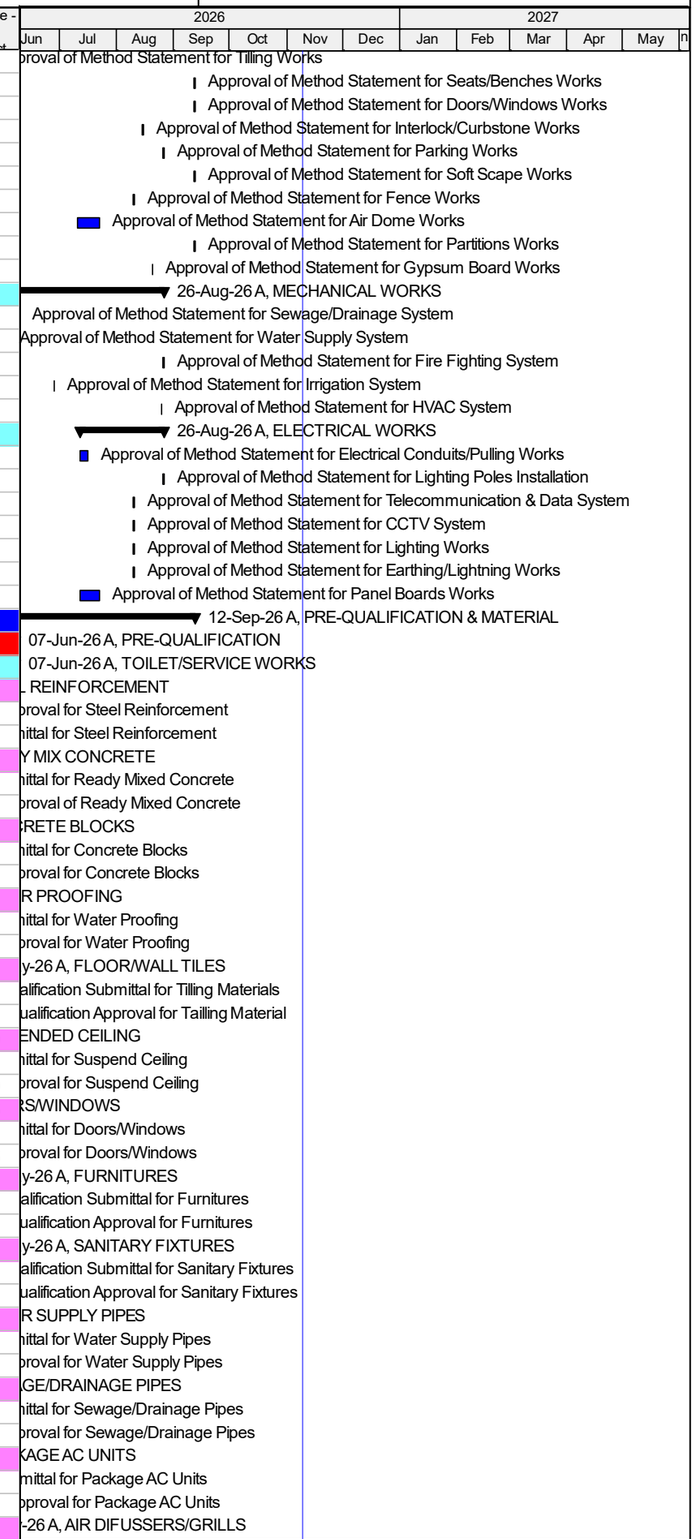

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Pre-Qualification Submittal for Air Diffusers/Grills	15	100%	100%	05-Jul-26	21-Jul-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EM	Pre-Qualification Approval for Air Diffusers/Grills	15	100%	100%	09-Aug-26	25-Aug-26	16-Mar-26 A	06-May-26 A	0.00	0.00	0.00	93
GALVANIZED DUCTS		30	0%	0%	10-Jun-26	14-Jul-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	61
MLTX-02-005-EM	Pre-Qualification Submittal for Galvanized Ducts	15	100%	100%	10-Jun-26	27-Jun-26	11-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Pre-Qualification Approval for Galvanized Ducts	15	100%	100%	28-Jun-26	14-Jul-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	61
EXHAUST FANS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EM	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
LIGHTING FIXTURES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Pre-Qualification Submittal for Lighting Fixtures	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EM	Pre-Qualification Approval for Lighting Fixtures	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
SWITCHES/SOCKETS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Pre-Qualification Submittal for Switches/Sockets	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EM	Pre-Qualification Approval for Switches/Sockets	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
EARTHING SYSTEM		39	0%	0%	31-May-26	14-Jul-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	52
MLTX-02-005-EM	Pre-Qualification Submittal for Earthing System	15	100%	100%	31-May-26	16-Jun-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	30
MLTX-02-005-EM	Pre-Qualification Approval for Earthing System	15	100%	100%	28-Jun-26	14-Jul-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	52
DISTRIBUTION PANNELS		36	0%	0%	20-May-26	04-Jul-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	23
MLTX-02-005-EM	Pre-Qualification Submittal for Distribution Panels	15	100%	100%	20-May-26	09-Jun-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Pre-Qualification Approval for Distribution Panels	15	100%	100%	17-Jun-26	04-Jul-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	23
PLAYGROUND WORKS		136	0%	0%	08-Mar-26	19-Aug-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	63
PVC MEMBRANE		51	0%	0%	08-Mar-26	09-May-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EM	Pre-Qualification Submittal for PVC Membrane	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EM	Pre-Qualification Approval for PVC Membrane	15	100%	100%	22-Apr-26	09-May-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-13
STEEL TENSION CABLES		72	0%	0%	22-Apr-26	18-Jul-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Pre-Qualification Submittal for Steel Tension Cables	15	100%	100%	22-Apr-26	09-May-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Pre-Qualification Approval for Steel Tension Cables	15	100%	100%	01-Jul-26	18-Jul-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	44
EMERGENCY DOORS		30	0%	0%	29-Mar-26	02-May-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EM	Pre-Qualification Submittal for Emergency Doors	15	100%	100%	29-Mar-26	14-Apr-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-31
MLTX-02-005-EM	Pre-Qualification Approval for Emergency Doors	15	100%	100%	15-Apr-26	02-May-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-19
PRESSURE UNITS		42	0%	0%	14-Jun-26	01-Aug-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	56
MLTX-02-005-EM	Pre-Qualification Submittal for Pressure Units	15	100%	100%	14-Jun-26	30-Jun-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	32
MLTX-02-005-EM	Pre-Qualification Approval for Pressure Units	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	56
AIR LOCK DOORS		45	0%	0%	20-May-26	14-Jul-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EM	Pre-Qualification Submittal for Lock Doors	15	100%	100%	20-May-26	09-Jun-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Pre-Qualification Approval for Lock Doors	15	100%	100%	28-Jun-26	14-Jul-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	41
ARTIFICIAL TURF		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Pre-Qualification Submittal for Artificial TURF	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EM	Pre-Qualification Approval for Artificial TURF	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
RUBBER GRANULES		36	0%	0%	08-Mar-26	21-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EM	Pre-Qualification Submittal for Rubber Granules	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EM	Pre-Qualification Approval for Rubber Granules	21	100%	100%	29-Mar-26	21-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-16
PADEL GLASS		36	0%	0%	29-Mar-26	09-May-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EM	Pre-Qualification Submittal for Padel Glass	15	100%	100%	29-Mar-26	14-Apr-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EM	Pre-Qualification Approval for Padel Glass	15	100%	100%	22-Apr-26	09-May-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-1
PADEL WIRE MESH/STEEL SETS		120	0%	0%	08-Mar-26	01-Aug-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	68
MLTX-02-005-EM	Pre-Qualification Submittal for Wire Mesh/Steel Sets	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EM	Pre-Qualification Approval for Wire Mesh/Steel Sets	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	68
AGGREGATE BASE COURSE		36	0%	0%	08-Mar-26	21-Apr-26	08-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EM	Pre-Qualification Submittal for Aggregate Base Course	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-25
MLTX-02-005-EM	Pre-Qualification Approval for Aggregate Base Course	21	100%	100%	29-Mar-26	21-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-8
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Pre-Qualification Submittal for Bituminous Base & Wearing	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Pre-Qualification Approval for the Site	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
INTERLOCKING PAVING		30	0%	0%	10-May-26	16-Jun-26	11-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	10-May-26	30-May-26	11-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	31-May-26	16-Jun-26	15-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	51
MARKING PAINT		30	0%	0%	15-Apr-26	19-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Pre-Qualification Submittal for Marking Paint	15	100%	100%	15-Apr-26	02-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EM	Pre-Qualification Approval for Marking Paint	15	100%	100%	03-May-26	19-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	9
PACKAGE AC UNITS		30	0%	0%	15-Jul-26	18-Aug-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	62
MLTX-02-005-EM	Pre-Qualification Submittal for Package AC Units	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EM	Pre-Qualification Approval for Package AC Units	15	100%	100%	02-Aug-26	18-Aug-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	62
AIR DIFUSSERS/GRILLS		30	0%	0%	15-Jul-26	18-Aug-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	62

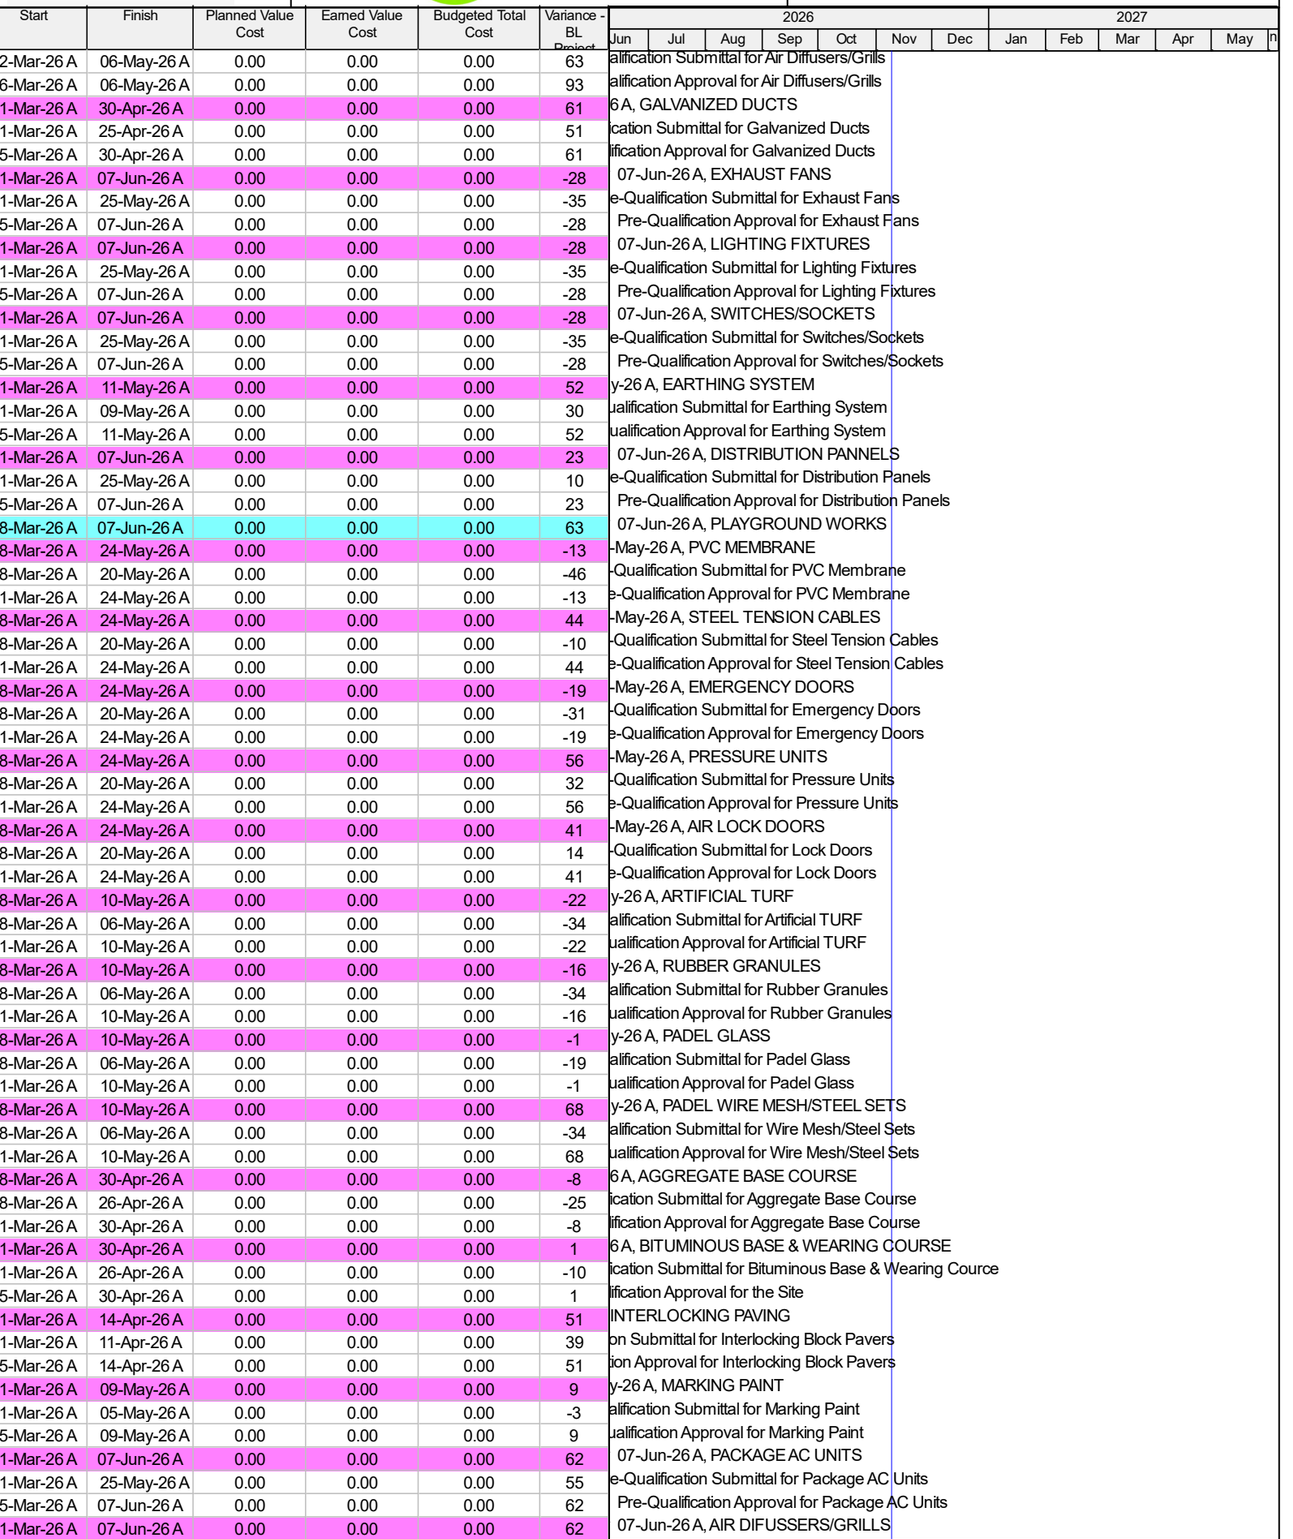

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Air Difussers/Grills	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Pre-Qualification Approval for Air Difussers/Grills	15	100%	100%	02-Aug-26	18-Aug-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	62
GALVANIZED DUCTS		30	0%	0%	15-Jul-26	18-Aug-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Duct	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	76
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Duct	15	100%	100%	02-Aug-26	18-Aug-26	15-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	96
EXHAUST FANS		30	0%	0%	01-Jul-26	04-Aug-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	01-Jul-26	18-Jul-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	43
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	19-Jul-26	04-Aug-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	50
DISTRIBUTION BOARDS		31	0%	0%	15-Jul-26	19-Aug-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	63
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Boards	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Boards	15	100%	100%	03-Aug-26	19-Aug-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	63
POWER CABLES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Submittal for Power Cables	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Approval for Power Cables	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
LIGHT FIXTURES		30	0%	0%	15-Apr-26	19-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Pre-Qualification Submittal for Light Fixtures	15	100%	100%	15-Apr-26	02-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Light Fixtures	15	100%	100%	03-May-26	19-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-13
CCTV MATERIALS		30	0%	0%	15-Apr-26	19-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Pre-Qualification Submittal for CCTV	15	100%	100%	15-Apr-26	02-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for CCTV	15	100%	100%	03-May-26	19-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-13
POWER OUTLETS/SWITCHES		30	0%	0%	22-Apr-26	30-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Power Outlets/Switches	15	100%	100%	22-Apr-26	09-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Pre-Qualification Approval for Power Outlets/Switches	15	100%	100%	10-May-26	30-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-7
LANDSCAPE WORKS		123	0%	0%	29-Mar-26	22-Aug-26	11-Mar-26 A	18-May-26 A	0.00	0.00	0.00	79
INTERLOCKING PAVING		30	0%	0%	29-Mar-26	02-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	15-Apr-26	02-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
CURBSTONE		30	0%	0%	10-Jun-26	14-Jul-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	93
MLTX-02-005-EN	Pre-Qualification Submittal for Curbstone	15	100%	100%	10-Jun-26	27-Jun-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	83
MLTX-02-005-EN	Pre-Qualification Approval for Curbstone	15	100%	100%	28-Jun-26	14-Jul-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	93
PAVEMENT MARKING		36	0%	0%	20-May-26	04-Jul-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN	Pre-Qualification Submittal for Pavement Markings	15	100%	100%	20-May-26	09-Jun-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Pre-Qualification Approval for Pavement Markings	15	100%	100%	17-Jun-26	04-Jul-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	45
TRAFFIC SIGNS		30	0%	0%	17-Jun-26	21-Jul-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Pre-Qualification Submittal for Traffic Signs	15	100%	100%	17-Jun-26	04-Jul-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	48
MLTX-02-005-EN	Pre-Qualification Approval for Traffic Signs	15	100%	100%	05-Jul-26	21-Jul-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	60
IRRIGATION PIPES/SPRINKLERS		33	0%	0%	15-Jul-26	22-Aug-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	86
MLTX-02-005-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	15-Jul-26	01-Aug-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	71
MLTX-02-005-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	15	100%	100%	05-Aug-26	22-Aug-26	15-Mar-26 A	10-May-26 A	0.00	0.00	0.00	86
AGRICULTURE SOIL		33	0%	0%	28-Jun-26	04-Aug-26	11-Mar-26 A	14-May-26 A	0.00	0.00	0.00	68
MLTX-02-005-EN	Pre-Qualification Submittal for Agriculture Soil	15	100%	100%	28-Jun-26	14-Jul-26	11-Mar-26 A	07-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Pre-Qualification Approval for Agriculture Soil	15	100%	100%	19-Jul-26	04-Aug-26	15-Mar-26 A	14-May-26 A	0.00	0.00	0.00	68
TRACK SURFACE		33	0%	0%	10-Jun-26	18-Jul-26	11-Mar-26 A	13-May-26 A	0.00	0.00	0.00	53
MLTX-02-005-EN	Pre-Qualification Submittal for Track Surface	15	100%	100%	10-Jun-26	27-Jun-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	38
MLTX-02-005-EN	Pre-Qualification Approval for Track Surface	15	100%	100%	01-Jul-26	18-Jul-26	15-Mar-26 A	13-May-26 A	0.00	0.00	0.00	53
GRASS/TREES		39	0%	0%	31-May-26	14-Jul-26	11-Mar-26 A	18-May-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN	Pre-Qualification Submittal for Grass/Trees	15	100%	100%	31-May-26	16-Jun-26	11-Mar-26 A	13-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Approval for Grass/Trees	15	100%	100%	28-Jun-26	14-Jul-26	15-Mar-26 A	18-May-26 A	0.00	0.00	0.00	46
CABLES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Submittal for Cables	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Approval for Cables	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
LIGHT POLES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting poles	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Pre-Qualification Approval for Lighting poles	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-2
MATERIAL SUBMITTAL		141	0%	0%	15-Apr-26	30-Sep-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	15
TOILET/SERVICE WORKS		141	0%	0%	15-Apr-26	30-Sep-26	19-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	52
STEEL REINFORCEMENT		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Submittal for Steel Reinforcement	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Approval for Steel Reinforcement	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
READY MIX CONCRETE		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Submittal for Ready Mixed Concrete	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Approval of Ready Mixed Concrete	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
CONCRETE BLOCKS		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Submittal for Concrete Blocks	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31

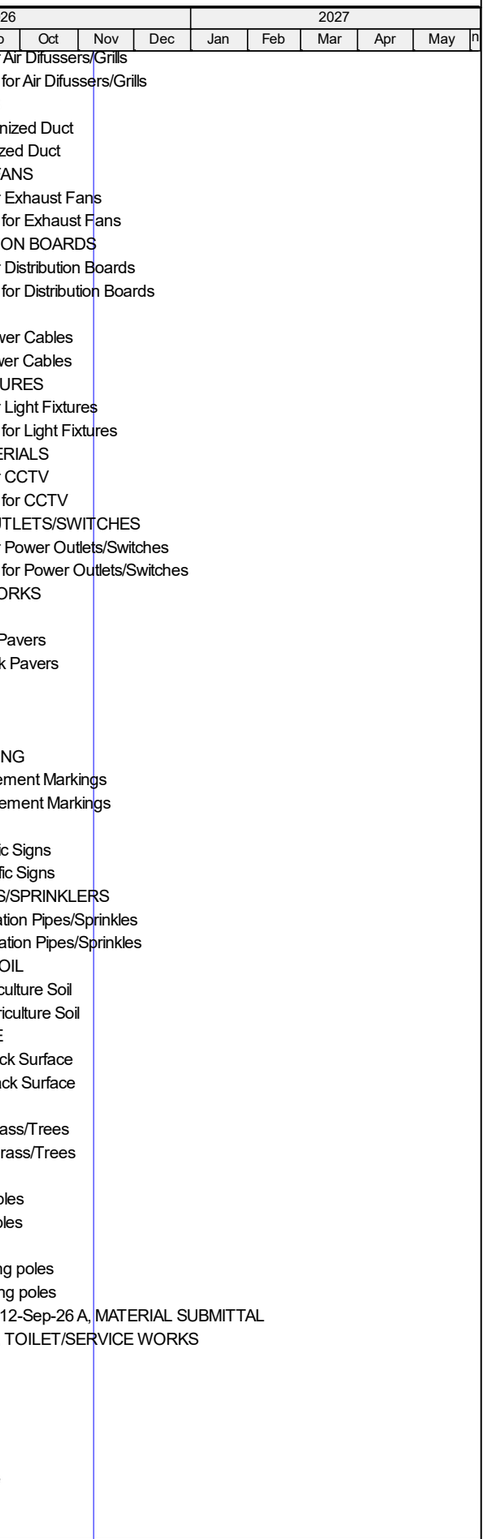


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Material Approval for Concrete Blocks	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
FLOOR/WALL TILES		30	0%	0%	15-Jul-26	18-Aug-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	77
MLTX-02-005-EN	Material Submittal for Tilling Materials	15	100%	100%	15-Jul-26	01-Aug-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Material Approval for Tilling Material	15	100%	100%	02-Aug-26	18-Aug-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	77
SUSPENDED CEILING		30	0%	0%	26-Aug-26	30-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	150
MLTX-02-005-EN	Material Submittal for Suspend Ceiling	15	100%	100%	26-Aug-26	12-Sep-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	142
MLTX-02-005-EN	Material Approval for Suspend Ceiling	15	100%	100%	13-Sep-26	30-Sep-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	150
DOORS/WINDOWS		30	0%	0%	19-Aug-26	22-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	144
MLTX-02-005-EN	Material Submittal for Doors/Windows	15	100%	100%	19-Aug-26	05-Sep-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	136
MLTX-02-005-EN	Material Approval for Doors/Windows	15	100%	100%	06-Sep-26	22-Sep-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	144
FURNITURES		30	0%	0%	03-May-26	09-Jun-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EN	Material Submittal for Furnitures	15	100%	100%	03-May-26	19-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Material Approval for Furnitures	15	100%	100%	20-May-26	09-Jun-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	17
SANITARY FIXTURES		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
MLTX-02-005-EN	Material Submittal for Sanitary Fixtures	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Material Approval for Sanitary Fixtures	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
WATER SUPPLY PIPES		30	0%	0%	15-Jul-26	18-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	114
MLTX-02-005-EN	Material Submittal for Water Supply Pipes	15	100%	100%	15-Jul-26	01-Aug-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	106
MLTX-02-005-EN	Material Approval for Water Supply Pipes	15	100%	100%	02-Aug-26	18-Aug-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	114
SEWAGE/DRAINAGE PIPES		30	0%	0%	15-Apr-26	19-May-26	08-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Material Submittal for Sewage/Drainage Pipes	15	100%	100%	15-Apr-26	02-May-26	08-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Material Approval for Sewage/Drainage Pipes	15	100%	100%	03-May-26	19-May-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	-20
PACKAGE AC UNITS		30	0%	0%	03-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EN	Material Submittal for Package AC Units	15	100%	100%	03-May-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN	Material Approval for Package AC Units	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
AIR DIFUSSERS/GRILLS		30	0%	0%	26-Aug-26	30-Sep-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	52
MLTX-02-005-EN	Material Submittal for Air Diffusers/Grills	15	100%	100%	26-Aug-26	12-Sep-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN	Material Approval for Air Diffusers/Grills	15	100%	100%	13-Sep-26	30-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	52
GALVANIZED DUCTS		30	0%	0%	15-Jul-26	18-Aug-26	24-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN	Material Submittal for Galvanized Ducts	15	100%	100%	15-Jul-26	01-Aug-26	24-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	81
MLTX-02-005-EN	Material Approval for Galvanized Ducts	15	100%	100%	02-Aug-26	18-Aug-26	28-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	91
EXHAUST FANS		30	0%	0%	03-May-26	09-Jun-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EN	Material Submittal for Exhaust Fans	15	100%	100%	03-May-26	19-May-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Material Approval for Exhaust Fans	15	100%	100%	20-May-26	09-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
LIGHTING FIXTURES		30	0%	0%	03-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EN	Material Submittal for Lighting Fixtures	15	100%	100%	03-May-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN	Material Approval for Lighting Fixtures	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
SWITCHES/SOCKETS		30	0%	0%	03-May-26	09-Jun-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EN	Material Submittal for Switches/Sockets	15	100%	100%	03-May-26	19-May-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Material Approval for Switches/Sockets	15	100%	100%	20-May-26	09-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
EARTHING SYSTEM		30	0%	0%	15-Jul-26	18-Aug-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	76
MLTX-02-005-EN	Material Submittal for Earthing System	15	100%	100%	15-Jul-26	01-Aug-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	64
MLTX-02-005-EN	Material Approval for Earthing System	15	100%	100%	02-Aug-26	18-Aug-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	76
DISTRIBUTION PANNELS		30	0%	0%	19-Aug-26	22-Sep-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN	Material Submittal for Distribution Panels	15	100%	100%	19-Aug-26	05-Sep-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	34
MLTX-02-005-EN	Material Approval for Distribution Panels	15	100%	100%	06-Sep-26	22-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	46
PLAYGROUND WORKS		136	0%	0%	15-Apr-26	24-Sep-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	10
PVC MEMBRANE		30	0%	0%	17-May-26	23-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Material Submittal for PVC Membrane	15	100%	100%	17-May-26	06-Jun-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	58
MLTX-02-005-EN	Material Approval for PVC Membrane	15	100%	100%	07-Jun-26	23-Jun-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	66
STEEL TENSION CABLES		30	0%	0%	19-Jul-26	22-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Material Submittal for Steel Tension Cables	15	100%	100%	19-Jul-26	04-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Material Approval for Steel Tension Cables	15	100%	100%	05-Aug-26	22-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-4
EMERGENCY DOORS		30	0%	0%	03-May-26	09-Jun-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EN	Material Submittal for Emergency Doors	15	100%	100%	03-May-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EN	Material Approval for Emergency Doors	15	100%	100%	20-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
PRESSURE UNITS		30	0%	0%	03-Aug-26	06-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Material Submittal for Pressure Units	15	100%	100%	03-Aug-26	19-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Material Approval for Pressure Units	15	100%	100%	20-Aug-26	06-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-5
AIR LOCK DOORS		30	0%	0%	16-Jul-26	19-Aug-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Material Submittal for Lock Doors	15	100%	100%	16-Jul-26	02-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Material Approval for Lock Doors	15	100%	100%	03-Aug-26	19-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-20
ARTIFICIAL TURF		135	0%	0%	15-Apr-26	22-Sep-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	105
MLTX-02-005-EN	Material Submittal for Artificial TURF	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-11

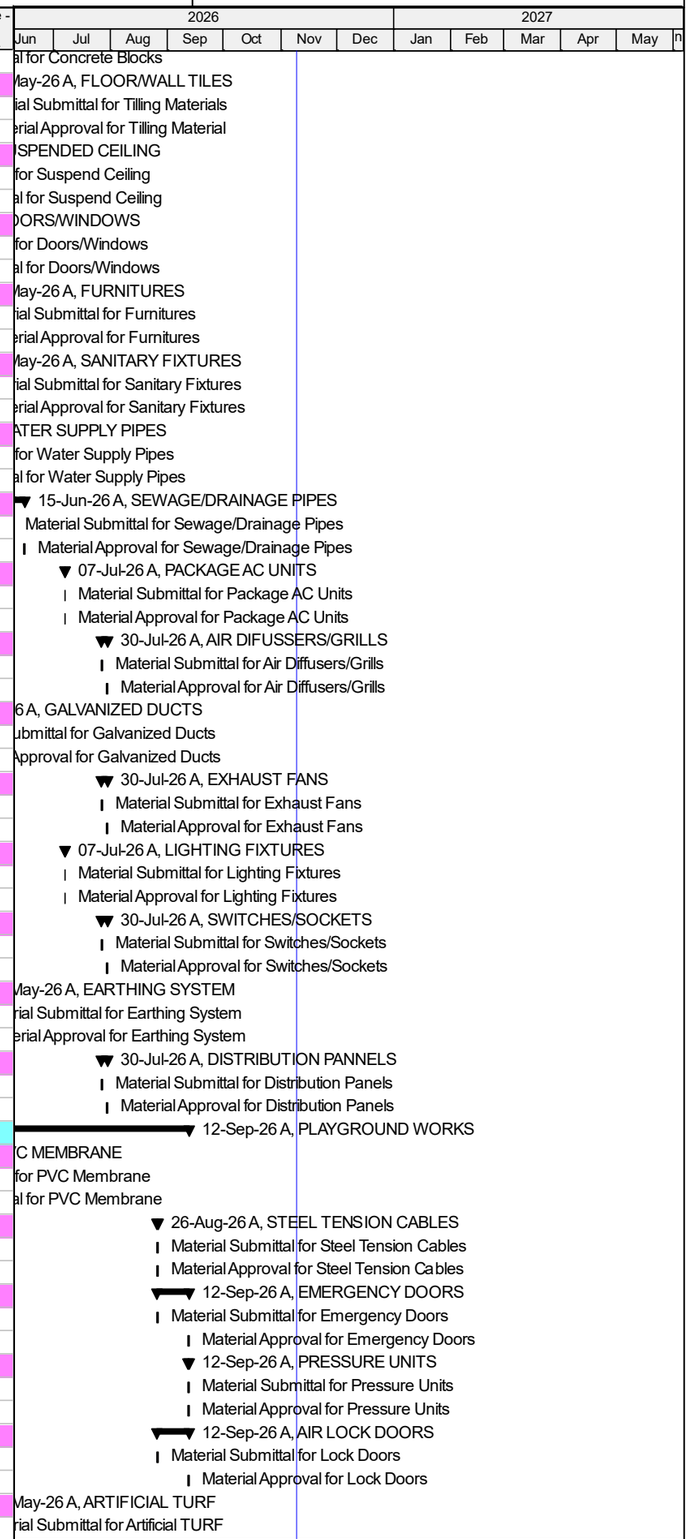

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Artificial TURF	15	100%	100%	06-Sep-26	22-Sep-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	105
RUBBER GRANULES		42	0%	0%	22-Apr-26	13-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EM	Material Submittal for Rubber Granules	21	100%	100%	22-Apr-26	16-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Approval for Rubber Granules	21	100%	100%	17-May-26	13-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	18
PADEL GLASS		33	0%	0%	17-May-26	27-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	30
MLTX-02-005-EM	Material Submittal for Padel Glass	15	100%	100%	17-May-26	06-Jun-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Approval for Padel Glass	15	100%	100%	10-Jun-26	27-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	30
PADEL WIRE MESH/STEEL SETS		30	0%	0%	03-Aug-26	06-Sep-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	91
MLTX-02-005-EM	Material Submittal for Wire Mesh/Steel Sets	15	100%	100%	03-Aug-26	19-Aug-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-EM	Material Approval for Wire Mesh/Steel Sets	15	100%	100%	20-Aug-26	06-Sep-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	91
AGGREGATE BASE COURSE		42	0%	0%	22-Apr-26	13-Jun-26	19-Mar-26 A	07-May-26 A	0.00	0.00	0.00	28
MLTX-02-005-EM	Material Submittal for Aggregate Base Course	21	100%	100%	22-Apr-26	16-May-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Material Approval for Aggregate Base Course	21	100%	100%	17-May-26	13-Jun-26	26-Mar-26 A	07-May-26 A	0.00	0.00	0.00	28
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Material Submittal for Bituminous Base & Wearing Cource	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	04-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Material Approval for the Site	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	07-May-26 A	0.00	0.00	0.00	25
INTERLOCKING PAVING		33	0%	0%	24-Jun-26	01-Aug-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	70
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	24-Jun-26	11-Jul-26	24-Mar-26 A	04-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	15-Jul-26	01-Aug-26	28-Mar-26 A	07-May-26 A	0.00	0.00	0.00	70
MARKING PAINT		30	0%	0%	20-May-26	27-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Submittal for Marking Paint	15	100%	100%	20-May-26	09-Jun-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Approval for Marking Paint	15	100%	100%	10-Jun-26	27-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	31
PACKAGE AC UNITS		30	0%	0%	20-Aug-26	24-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	67
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	20-Aug-26	06-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	52
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	07-Sep-26	24-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	67
AIR DIFUSSERS/GRILLS		30	0%	0%	19-Aug-26	22-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Material Submittal for Air Difussers/Grills	15	100%	100%	19-Aug-26	05-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EM	Material Approval for Air Difussers/Grills	15	100%	100%	06-Sep-26	22-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	9
GALVANIZED DUCTS		30	0%	0%	19-Aug-26	22-Sep-26	24-Mar-26 A	10-May-26 A	0.00	0.00	0.00	113
MLTX-02-005-EM	Material Submittal for Galvanized Duct	15	100%	100%	19-Aug-26	05-Sep-26	24-Mar-26 A	05-May-26 A	0.00	0.00	0.00	102
MLTX-02-005-EM	Material Approval for Galvanized Duct	15	100%	100%	06-Sep-26	22-Sep-26	28-Mar-26 A	10-May-26 A	0.00	0.00	0.00	113
EXHAUST FANS		30	0%	0%	05-Aug-26	08-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	05-Aug-26	22-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	23-Aug-26	08-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-3
DISTRIBUTION BOARDS		30	0%	0%	20-Aug-26	24-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Material Submittal for Distribution Boards	15	100%	100%	20-Aug-26	06-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Material Approval for Distribution Boards	15	100%	100%	07-Sep-26	24-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	24
POWER CABLES		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Material Submittal for Power Cables	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EM	Material Approval for Power Cables	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
LIGHT FIXTURES		30	0%	0%	20-May-26	27-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Material Submittal for Light Fixtures	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EM	Material Approval for Light Fixtures	15	100%	100%	10-Jun-26	27-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
CCTV MATERIALS		30	0%	0%	20-May-26	27-Jun-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-66
MLTX-02-005-EM	Material Submittal for CCTV	15	100%	100%	20-May-26	09-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-67
MLTX-02-005-EM	Material Approval for CCTV	15	100%	100%	10-Jun-26	27-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-66
POWER OUTLETS/SWITCHES		33	0%	0%	07-Jun-26	14-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-37
MLTX-02-005-EM	Material Submittal for Power Outlets/Switches	15	100%	100%	07-Jun-26	23-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-55
MLTX-02-005-EM	Material Approval for Power Outlets/Switches	15	100%	100%	28-Jun-26	14-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-37
LANDSCAPE WORKS		123	0%	0%	03-May-26	27-Sep-26	24-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	12
INTERLOCKING PAVING		30	0%	0%	03-May-26	09-Jun-26	25-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	54
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	03-May-26	19-May-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	20-May-26	09-Jun-26	29-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	54
CURBSTONE		30	0%	0%	22-Jul-26	25-Aug-26	25-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	120
MLTX-02-005-EM	Material Submittal for Curbstone	15	100%	100%	22-Jul-26	08-Aug-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	111
MLTX-02-005-EM	Material Approval for Curbstone	15	100%	100%	09-Aug-26	25-Aug-26	29-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	120
PAVEMENT MARKING		30	0%	0%	05-Jul-26	08-Aug-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	67
MLTX-02-005-EM	Material Submittal for Pavement Markings	15	100%	100%	05-Jul-26	21-Jul-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	57
MLTX-02-005-EM	Material Approval for Pavement Markings	15	100%	100%	22-Jul-26	08-Aug-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	67
TRAFFIC SIGNS		30	0%	0%	22-Jul-26	25-Aug-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EM	Material Submittal for Traffic Signs	15	100%	100%	22-Jul-26	08-Aug-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	72
MLTX-02-005-EM	Material Approval for Traffic Signs	15	100%	100%	09-Aug-26	25-Aug-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	82
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	23-Aug-26	27-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	23-Aug-26	08-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-3

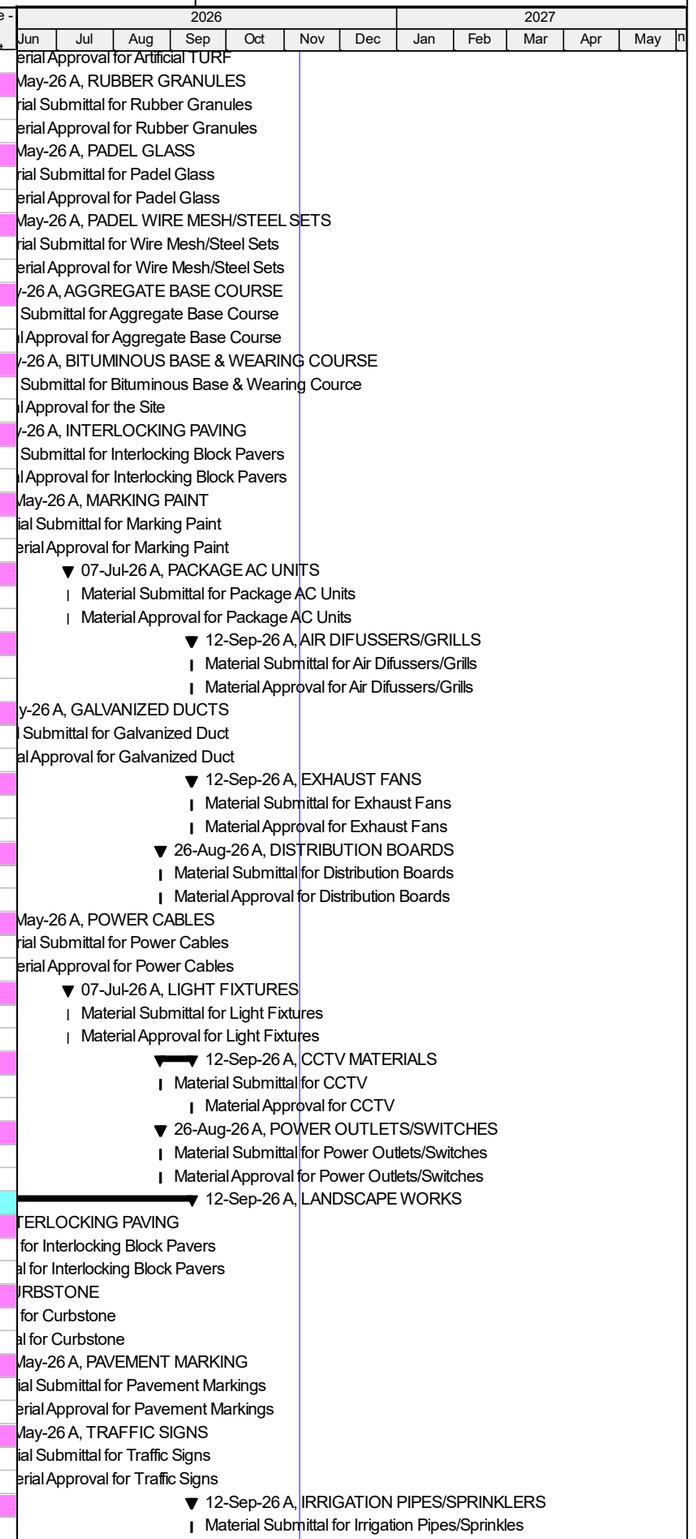

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Material Approval for Irrigation Pipes/Sprinkles	15	100%	100%	09-Sep-26	27-Sep-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	12
AGRICULTURE SOIL		30	0%	0%	05-Aug-26	08-Sep-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	91
MLTX-02-005-EI	Material Submittal for Agriculture Soil	15	100%	100%	05-Aug-26	22-Aug-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	81
MLTX-02-005-EI	Material Approval for Agriculture Soil	15	100%	100%	23-Aug-26	08-Sep-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	91
TRACK SURFACE		30	0%	0%	19-Jul-26	22-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EI	Material Submittal for Track Surface	15	100%	100%	19-Jul-26	04-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EI	Material Approval for Track Surface	15	100%	100%	05-Aug-26	22-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-18
GRASS/TREES		33	0%	0%	15-Jul-26	22-Aug-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	76
MLTX-02-005-EI	Material Submittal for Grass/Trees	15	100%	100%	15-Jul-26	01-Aug-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EI	Material Approval for Grass/Trees	15	100%	100%	05-Aug-26	22-Aug-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	76
CABLES		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EI	Material Submittal for Cables	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EI	Material Approval for Cables	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
LIGHT POLES		30	0%	0%	03-May-26	09-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EI	Material Submittal for Lighting poles	15	100%	100%	03-May-26	19-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EI	Material Approval for Lighting poles	15	100%	100%	20-May-26	09-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-27
PROCUREMENT		220	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	31-Jan-27	0.00	0.00	0.00	-51
SHORT LEAD ITEM		215	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	31-Jan-27	0.00	0.00	0.00	-51
TOILET/SERVICE WORKS		193	0%	0%	20-May-26	16-Nov-26	04-Apr-26 A	09-Nov-26 A	0.00	0.00	0.00	7
STEEL REINFORCEMENT		10	0%	0%	20-May-26	03-Jun-26	04-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	Material Delivery of Steel Reinforcement	5	100%	100%	30-May-26	03-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-9	PO for Steel Reinforcement	5	100%	100%	20-May-26	25-May-26	04-Apr-26 A	18-May-26 A	0.00	0.00	0.00	6
CONCRETE BLOCKS		13	0%	0%	30-May-26	13-Jun-26	09-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-21
MLTX-02-005-PR-1	PO for Concrete Blocks	5	100%	100%	30-May-26	03-Jun-26	09-Apr-26 A	18-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	Material Delivery of Concrete Blocks	8	100%	100%	04-Jun-26	13-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-21
FLOOR/WALL TILES		18	0%	0%	22-Aug-26	10-Sep-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	18
MLTX-02-005-PR-1	PO for Tilling Materials	5	100%	100%	22-Aug-26	26-Aug-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Material Delivery of Tailling Material	13	100%	100%	27-Aug-26	10-Sep-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	18
SUSPENDED CEILING		18	0%	0%	01-Oct-26	21-Oct-26	28-Jul-26 A	18-Aug-26 A	0.00	0.00	0.00	54
MLTX-02-005-PR-1	PO for Suspend Ceiling	5	100%	100%	01-Oct-26	06-Oct-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	59
MLTX-02-005-PR-1	Material Delivery of Suspend Ceiling	13	100%	100%	07-Oct-26	21-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	54
DOORS/WINDOWS		40	0%	0%	01-Oct-26	16-Nov-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	48
MLTX-02-005-PR-1	PO for Doors/Windows	15	100%	100%	01-Oct-26	18-Oct-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-1	Material Delivery for Doors/Windows	25	72.4%	100%	19-Oct-26	16-Nov-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	48
WATER SUPPLY PIPES		12	0%	0%	27-Aug-26	09-Sep-26	07-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	54
MLTX-02-005-PR-1	PO for Water Supply Pipes	5	100%	100%	27-Aug-26	01-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	48
MLTX-02-005-PR-1	Material Delivery for Water Supply Pipes	7	100%	100%	02-Sep-26	09-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	54
SEWAGE/DRAINAGE PIPES		87	0%	0%	20-May-26	01-Sep-26	13-Jun-26 A	20-Jun-26 A	0.00	0.00	0.00	63
MLTX-02-005-PR-1	PO for Sewage/Drainage Pipes	5	100%	100%	20-May-26	25-May-26	20-Jun-26 A	20-Jun-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Sewage/Drainage Pipes	7	100%	100%	25-Aug-26	01-Sep-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	69
SANITARY FIXTURES		102	0%	0%	30-May-26	26-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	50
MLTX-02-005-PR-1	PO for Sanitary Fixtures	5	100%	100%	30-May-26	03-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-47
MLTX-02-005-PR-1	Material Delivery for Sanitary Fixtures	13	100%	100%	10-Sep-26	26-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	50
PACKAGE AC UNITS		20	0%	0%	10-Jun-26	02-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	10-Jun-26	15-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	100%	100%	16-Jun-26	02-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-4
AIR DIFUSSERS/GRILLS		20	0%	0%	19-Oct-26	10-Nov-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	69
MLTX-02-005-PR-1	PO for Air Diffusers/Grills	5	100%	100%	19-Oct-26	24-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	56
MLTX-02-005-PR-1	Material Delivery for Air Diffusers/Grills	15	87.33%	100%	25-Oct-26	10-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	69
GALVANIZED DUCTS		20	0%	0%	19-Oct-26	10-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	69
MLTX-02-005-PR-1	PO for Galvanized Ducts	5	100%	100%	19-Oct-26	24-Oct-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	54
MLTX-02-005-PR-1	Material Delivery for Galvanized Ducts	15	87.33%	100%	25-Oct-26	10-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	69
EXHAUST FANS		121	0%	0%	10-Jun-26	29-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	61
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	100%	10-Jun-26	15-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-55
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	10	100%	100%	19-Oct-26	29-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	61
LIGHTING FIXTURES		142	0%	0%	10-Jun-26	08-Jul-26	07-Jul-26 A	31-Oct-26 A	0.00	0.00	0.00	-96
MLTX-02-005-PR-1	PO for Lighting Fixtures	5	100%	100%	10-Jun-26	15-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	20	100%	100%	16-Jun-26	08-Jul-26	31-Oct-26 A	31-Oct-26 A	0.00	0.00	0.00	-96
SWITCHES/SOCKETS		32	0%	0%	16-Jun-26	22-Jul-26	28-Oct-26 A	28-Oct-26 A	0.00	0.00	0.00	-82
MLTX-02-005-PR-1	PO for Switches/Sockets	15	100%	100%	16-Jun-26	02-Jul-26	28-Oct-26 A	28-Oct-26 A	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	17	100%	100%	04-Jul-26	22-Jul-26	28-Oct-26 A	28-Oct-26 A	0.00	0.00	0.00	-82
EARTHING SYSTEM		20	0%	0%	19-Aug-26	10-Sep-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-1	PO for Earthing System	5	100%	100%	19-Aug-26	24-Aug-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	12
MLTX-02-005-PR-1	Material Delivery for Earthing System	15	100%	100%	25-Aug-26	10-Sep-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	27

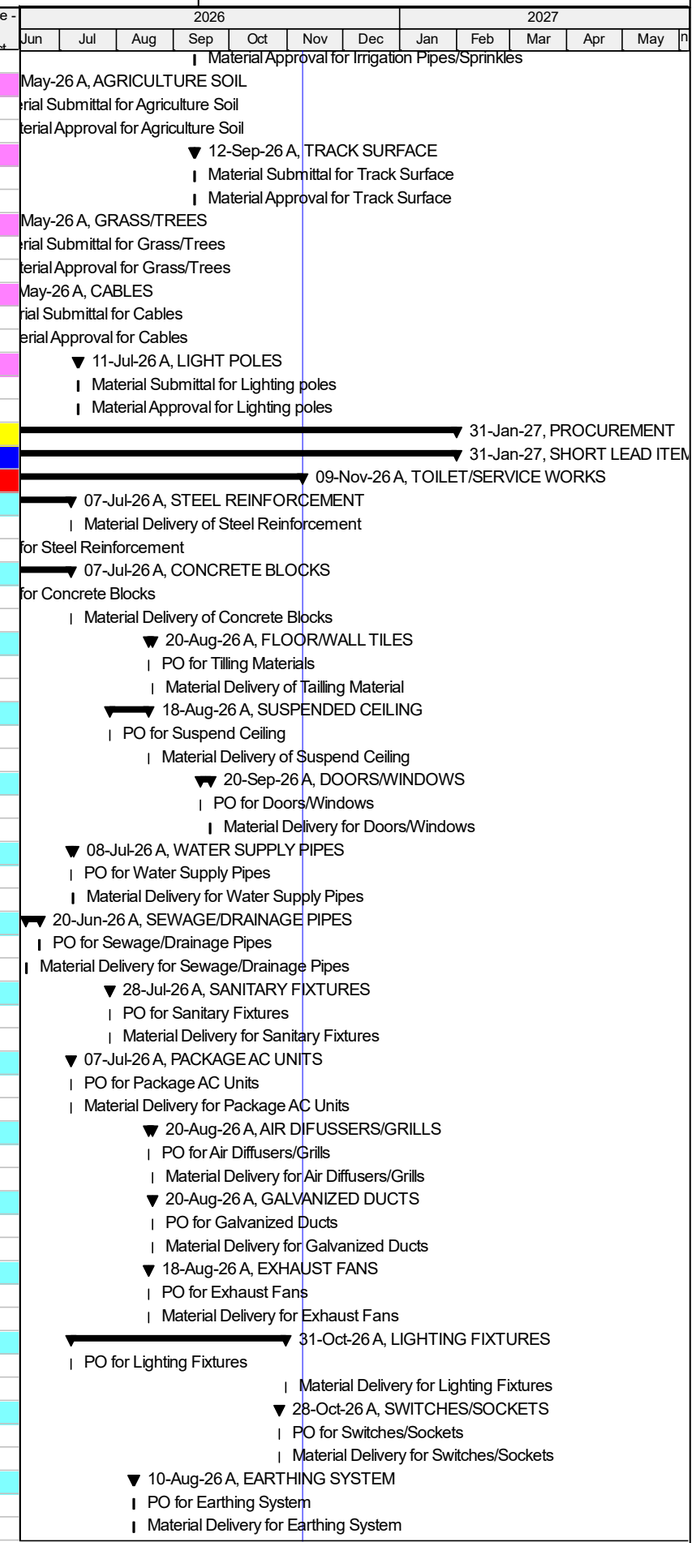

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	100%	27-Sep-26	01-Oct-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	100%	03-Oct-26	19-Oct-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	-12
FURNITURES		49	0%	0%	16-Jun-26	11-Aug-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	PO for Furnitures	19	100%	100%	16-Jun-26	07-Jul-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for Furnitures	30	100%	100%	08-Jul-26	11-Aug-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-75
PLAYGROUND WORKS		200	0%	0%	10-Jun-26	01-Dec-26	04-Apr-26 A	31-Jan-27	0.00	0.00	0.00	-51
PVC MEMBRANE		162	0%	0%	24-Jun-26	02-Nov-26	04-Apr-26 A	31-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	PO for PVC Membrane	4	100%	100%	24-Jun-26	28-Jun-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	31
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	30	100%	0%	29-Sep-26	02-Nov-26	26-Nov-26	31-Dec-26	0.00	0.00	0.00	-50
ARTIFICIAL TURF		69	0%	0%	24-Sep-26	03-Nov-26	04-Apr-26 A	14-Dec-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	PO for Artificial TURF	5	100%	100%	24-Sep-26	29-Sep-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	110
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	30	100%	0%	30-Sep-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
RUBBER GRANULES		156	0%	0%	14-Jun-26	25-Oct-26	04-Apr-26 A	14-Dec-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-1	PO for Rubber Granules	5	100%	100%	14-Jun-26	18-Jun-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-42
PADEL GLASS		144	0%	0%	28-Jun-26	21-Oct-26	04-Apr-26 A	14-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Padel Glass	5	100%	100%	28-Jun-26	02-Jul-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	35
MLTX-02-005-PR-1	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-45
PADEL WIRE MESH/STEEL SETS		65	0%	0%	10-Sep-26	04-Oct-26	09-Apr-26 A	26-Nov-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Wire Mesh/Steel Sets	5	100%	100%	10-Sep-26	15-Sep-26	09-Apr-26 A	19-May-26 A	0.00	0.00	0.00	99
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-45
AGGREGATE BASE COURSE		12	0%	0%	14-Jun-26	27-Jun-26	04-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
MLTX-02-005-PR-9	PO for Aggregate Base Course	5	100%	100%	14-Jun-26	18-Jun-26	04-Apr-26 A	14-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-9	Material Delivery for Aggregate Base Course	7	100%	100%	20-Jun-26	27-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
BITUMINOUS BASE & WEARING COURSE		57	0%	0%	10-Jun-26	15-Aug-26	15-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	-32
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	15	100%	100%	10-Jun-26	27-Jun-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-69
MLTX-02-005-PR-1	Material Delivery for the Site	27	100%	100%	15-Jul-26	15-Aug-26	21-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	-32
INTERLOCKING PAVING		32	0%	0%	04-Aug-26	09-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-5
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	15	100%	100%	04-Aug-26	20-Aug-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	17	100%	100%	22-Aug-26	09-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-5
MARKING PAINT		32	0%	0%	28-Jun-26	03-Aug-26	09-Nov-26	16-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	15-Jul-26	03-Aug-26	26-Nov-26	16-Dec-26	0.00	0.00	0.00	-114
PACKAGE AC UNITS		34	0%	0%	04-Oct-26	11-Nov-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	108
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	04-Oct-26	08-Oct-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	79
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	80.67%	100%	26-Oct-26	11-Nov-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	108
AIR DIFUSSERS/GRILLS		40	0%	0%	24-Sep-26	09-Nov-26	09-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	96.4%	0%	12-Oct-26	09-Nov-26	26-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
GALVANIZED DUCTS		40	0%	0%	24-Sep-26	09-Nov-26	09-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	96.4%	0%	12-Oct-26	09-Nov-26	26-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
EXHAUST FANS		40	0%	0%	10-Sep-26	02-Nov-26	09-Nov-26	26-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	100%	0%	05-Oct-26	02-Nov-26	26-Nov-26	26-Dec-26	0.00	0.00	0.00	-45
DISTRIBUTION BOARDS		20	0%	0%	10-Oct-26	01-Nov-26	26-Nov-26	20-Dec-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	10-Oct-26	14-Oct-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	15-Oct-26	01-Nov-26	02-Dec-26	20-Dec-26	0.00	0.00	0.00	-41
POWER CABLES		35	0%	0%	22-Oct-26	01-Dec-26	14-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Power Cables	15	100%	0%	22-Oct-26	08-Nov-26	14-Dec-26	31-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	Material Delivery for Power Cables	20	0.5%	0%	09-Nov-26	01-Dec-26	31-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
LIGHT FIXTURES		179	0%	0%	28-Jun-26	01-Dec-26	07-Jul-26 A	24-Jan-27	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Light Fixtures	5	100%	100%	28-Jun-26	02-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0.5%	0%	09-Nov-26	01-Dec-26	31-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
CCTV MATERIALS		71	0%	0%	04-Jul-26	29-Nov-26	09-Nov-26	31-Jan-27	0.00	0.00	0.00	-53
MLTX-02-005-PR-1	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	12-Nov-26	29-Nov-26	13-Jan-27	31-Jan-27	0.00	0.00	0.00	-53
POWER OUTLETS/SWITCHES		41	0%	0%	23-Jul-26	10-Nov-26	26-Nov-26	13-Jan-27	0.00	0.00	0.00	-54
MLTX-02-005-PR-1	PO for Power Outlets/Switches	16	100%	0%	23-Jul-26	10-Aug-26	26-Nov-26	15-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	92.4%	0%	13-Oct-26	10-Nov-26	15-Dec-26	13-Jan-27	0.00	0.00	0.00	-54
LANDSCAPE WORKS		193	0%	0%	10-Jun-26	04-Nov-26	16-May-26 A	23-Jan-27	0.00	0.00	0.00	-67
INTERLOCKING PAVING		17	0%	0%	10-Jun-26	29-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	100%	10-Jun-26	15-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-62

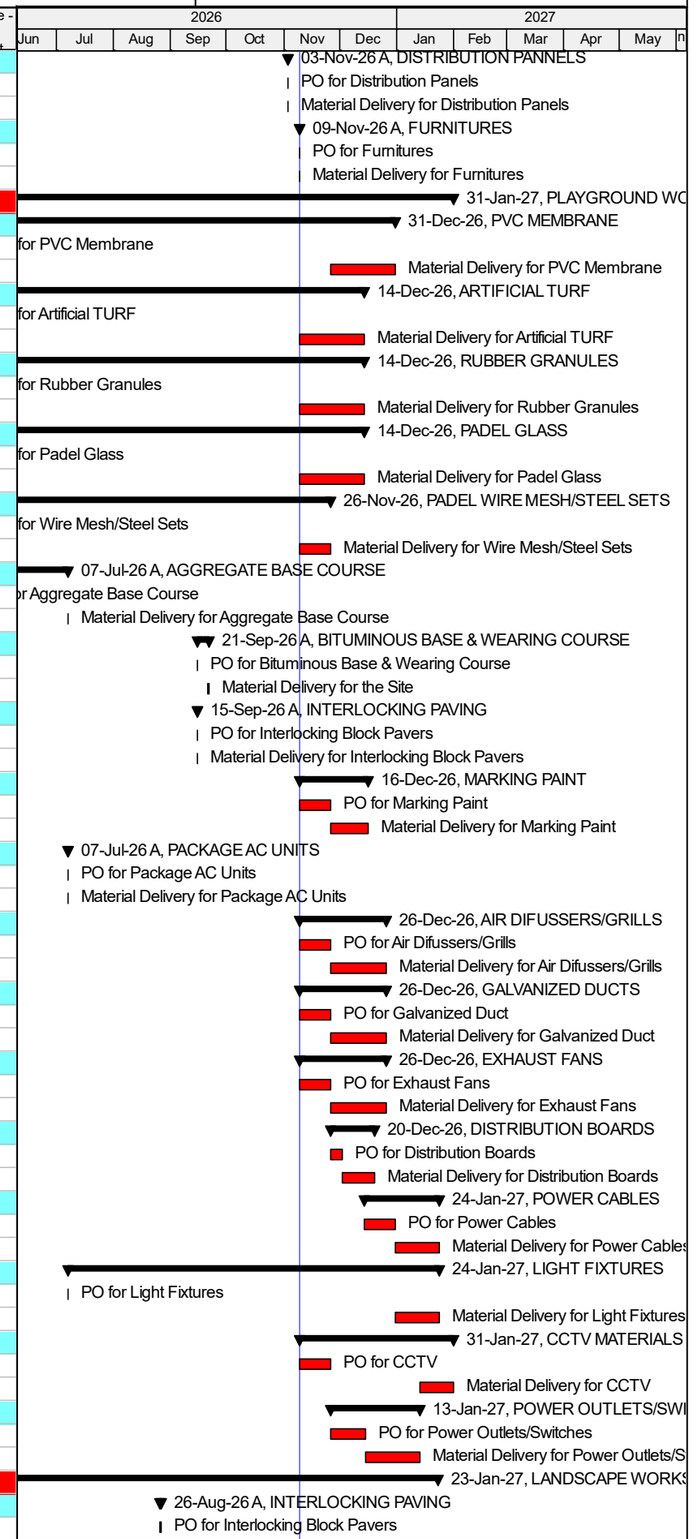

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	12	100%	100%	16-Jun-26	29-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-50
CURBSTONE		17	0%	0%	31-Aug-26	19-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	45
MLTX-02-005-PR-1	PO for Curbstone	5	100%	100%	31-Aug-26	05-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	33
MLTX-02-005-PR-1	Material Delivery for Curbstone	12	100%	100%	06-Sep-26	19-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	45
PAVEMENT MARKING		33	0%	0%	11-Aug-26	04-Nov-26	15-Dec-26	23-Jan-27	0.00	0.00	0.00	-67
MLTX-02-005-PR-1	PO for Pavement Markings	13	100%	0%	11-Aug-26	25-Aug-26	15-Dec-26	30-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	20	100%	0%	13-Oct-26	04-Nov-26	30-Dec-26	23-Jan-27	0.00	0.00	0.00	-67
TRAFFIC SIGNS		63	0%	0%	03-Sep-26	27-Sep-26	13-Oct-26 A	09-Nov-26 A	0.00	0.00	0.00	-36
MLTX-02-005-PR-1	PO for Traffic Signs	15	100%	100%	03-Sep-26	20-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	5	100%	100%	21-Sep-26	27-Sep-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-36
IRRIGATION PIPES/SPRINKLERS		13	0%	0%	28-Sep-26	12-Oct-26	17-Jun-26 A	21-Jul-26 A	0.00	0.00	0.00	70
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	100%	28-Sep-26	03-Oct-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	91
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	100%	04-Oct-26	12-Oct-26	21-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	70
AGRICULTURE SOIL		37	0%	0%	09-Sep-26	22-Oct-26	01-Oct-26 A	03-Oct-26 A	0.00	0.00	0.00	17
MLTX-02-005-PR-1	PO for Agriculture Soil	15	100%	100%	09-Sep-26	27-Sep-26	01-Oct-26 A	01-Oct-26 A	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	22	100%	100%	28-Sep-26	22-Oct-26	03-Oct-26 A	03-Oct-26 A	0.00	0.00	0.00	17
TRACK SURFACE		112	0%	0%	23-Aug-26	30-Aug-26	16-May-26 A	02-Jan-27	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	PO for Track Surface	5	100%	100%	23-Aug-26	27-Aug-26	16-May-26 A	19-May-26 A	0.00	0.00	0.00	83
MLTX-02-005-PR-1	Material Delivery for Track Surface	2	100%	0%	29-Aug-26	30-Aug-26	30-Dec-26	02-Jan-27	0.00	0.00	0.00	-105
GRASS/TREES		86	0%	0%	29-Aug-26	26-Oct-26	17-May-26 A	08-Dec-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-1	PO for Grass/Trees	5	100%	100%	29-Aug-26	02-Sep-26	17-May-26 A	20-May-26 A	0.00	0.00	0.00	87
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-36
CABLES		83	0%	0%	10-Jun-26	14-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	16
MLTX-02-005-PR-1	PO for Cables	5	100%	100%	10-Jun-26	15-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-62
MLTX-02-005-PR-1	Material Delivery for Cables	15	100%	100%	29-Aug-26	14-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	16
LONG LEAD ITEM		205	0%	0%	10-Jun-26	16-Nov-26	07-Jul-26 A	15-Dec-26	0.00	0.00	0.00	-24
PLAYGROUND WORKS		89	0%	0%	10-Jun-26	16-Nov-26	13-Oct-26 A	15-Dec-26	0.00	0.00	0.00	-24
STEEL TENSION CABLES		63	0%	0%	01-Sep-26	21-Oct-26	13-Oct-26 A	09-Dec-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	PO for Steel Tension Cables	7	100%	100%	01-Sep-26	08-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	09-Nov-26	28-Nov-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	10	100%	100%	09-Sep-26	20-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Staging time	10	100%	0%	11-Oct-26	21-Oct-26	28-Nov-26	09-Dec-26	0.00	0.00	0.00	-41
EMERGENCY DOORS		43	0%	0%	10-Jun-26	18-Aug-26	13-Oct-26 A	14-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	100%	10-Jun-26	21-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-97
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	100%	22-Jun-26	14-Jul-26	13-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-77
MLTX-02-005-PR-1	Staging time	5	100%	0%	13-Aug-26	18-Aug-26	08-Dec-26	14-Dec-26	0.00	0.00	0.00	-99
PRESSURE UNITS		76	0%	0%	07-Sep-26	16-Nov-26	13-Oct-26 A	14-Dec-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	100%	07-Sep-26	17-Sep-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-21
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	92.4%	0%	13-Oct-26	10-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	100%	19-Sep-26	12-Oct-26	13-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-1
MLTX-02-005-PR-1	Staging time	5	0%	0%	11-Nov-26	16-Nov-26	08-Dec-26	14-Dec-26	0.00	0.00	0.00	-23
AIR LOCK DOORS		66	0%	0%	20-Aug-26	05-Nov-26	13-Oct-26 A	15-Dec-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	100%	20-Aug-26	31-Aug-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-36
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	03-Oct-26	31-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-32
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	100%	08-Sep-26	01-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	Staging time	5	100%	0%	01-Nov-26	05-Nov-26	09-Dec-26	15-Dec-26	0.00	0.00	0.00	-33
LANDSCAPE WORKS		92	0%	0%	10-Jun-26	26-Sep-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	4
LIGHT POLES		92	0%	0%	10-Jun-26	26-Sep-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	4
MLTX-02-005-PR-1	Staging time	15	100%	100%	08-Sep-26	26-Sep-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	4
MLTX-02-005-PR-9	PO for Lighting poles	10	100%	100%	10-Jun-26	21-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-14
MLTX-02-005-PR-9	Material Fabrication for Lighting poles	30	100%	100%	30-Jun-26	03-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-20
MLTX-02-005-PR-9	Material Delivery for Lighting poles	30	100%	100%	04-Aug-26	07-Sep-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-11
CONSTRUCTION PHASE		293	44.72%	48.06%	29-Mar-26	31-Dec-26	04-Apr-26 A	23-Feb-27	4,451,927.78	4,785,309.30	9,955,979.43	-44
SITE WORKS		292	40.4%	42.81%	29-Mar-26	31-Dec-26	04-Apr-26 A	23-Feb-27	3,551,206.88	3,763,219.05	8,789,975.14	-44
EARTH WORKS		43	100%	100%	29-Mar-26	17-May-26	04-Apr-26 A	08-Aug-26 A	294,826.31	294,826.31	294,826.31	-67
MLTX-02-005-CN-118	Excavation (in all types of soil) including Compaction	21	100%	100%	29-Mar-26	21-Apr-26	06-Apr-26 A	12-Apr-26 A	112,428.03	112,428.03	112,428.03	9
MLTX-02-005-CN-118	Excavation (in all types of soil) including Compaction	20	100%	100%	15-Apr-26	07-May-26	04-Apr-26 A	02-Aug-26 A	14,053.50	14,053.50	14,053.50	-70
MLTX-02-005-CN-119	Excavation (in all types of soil) including Compaction	12	100%	100%	04-May-26	17-May-26	06-Apr-26 A	05-Aug-26 A	70,267.52	70,267.52	70,267.52	-66
MLTX-02-005-CN-119	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	22-Apr-26	14-May-26	13-Apr-26 A	03-May-26 A	56,044.15	56,044.15	56,044.15	11
MLTX-02-005-CN-119	Backfilling on Layers (Selected Soil) including Compaction	19	100%	100%	16-Apr-26	07-May-26	06-Apr-26 A	08-Apr-26 A	7,005.52	7,005.52	7,005.52	25
MLTX-02-005-CN-119	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	09-May-26	17-May-26	21-Apr-26 A	08-Aug-26 A	35,027.59	35,027.59	35,027.59	-67
LANDSCAPE WORKS		251	38.6%	40.42%	16-May-26	31-Dec-26	16-May-26 A	23-Feb-27	3,256,380.57	3,409,899.41	8,436,655.50	-44
PLAYGROUND AREA		251	74.56%	76.9%	16-May-26	31-Dec-26	18-May-26 A	23-Feb-27	970,403.66	1,000,815.42	1,301,449.27	-44

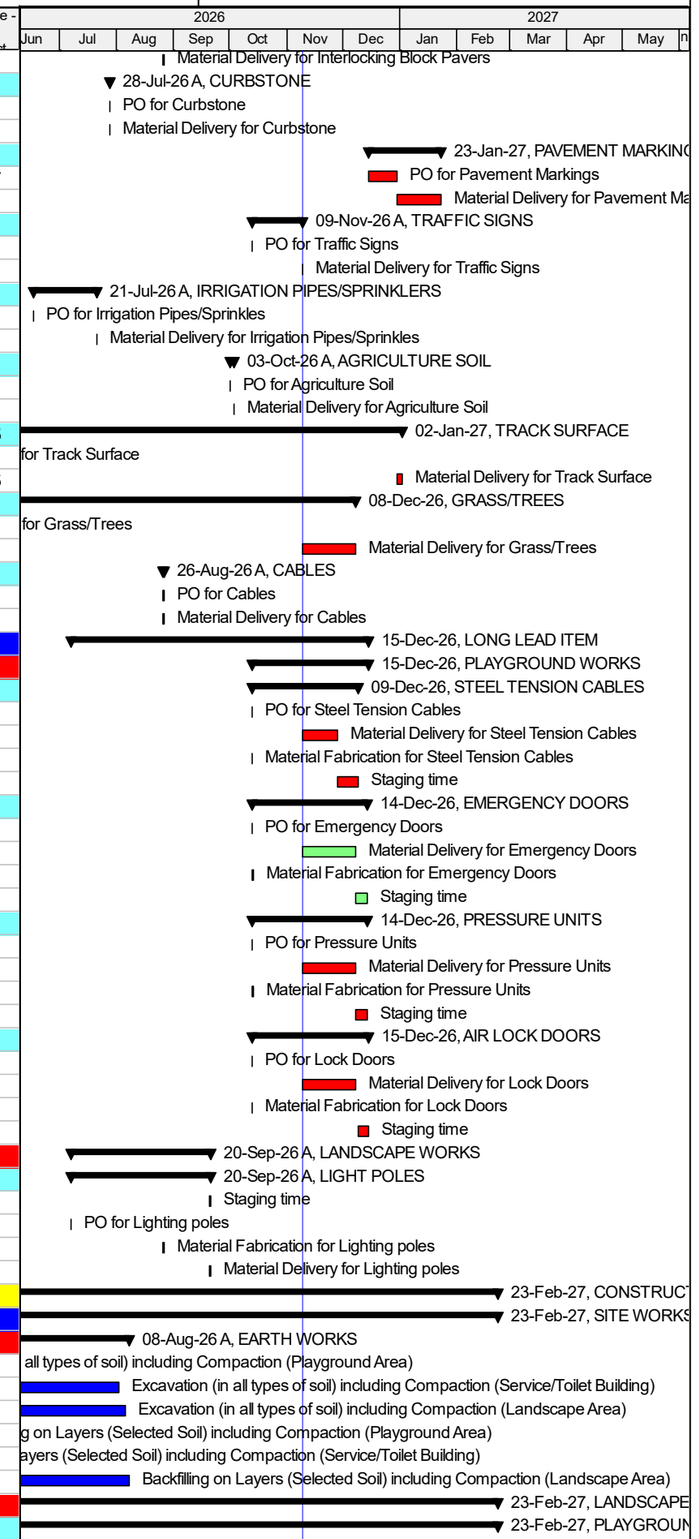

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
FOOTBALL PLAYGROUND		200	84.07%	85%	16-May-26	09-Dec-26	18-May-26 A	09-Jan-27	266,380.31	269,322.49	316,849.99	-25
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Football Playground)	20	100%	100%	16-May-26	10-Jun-26	18-May-26 A	31-May-26 A	79,212.50	79,212.50	79,212.50	9
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Football	21	100%	100%	11-Jun-26	05-Jul-26	01-Jun-26 A	23-Jun-26 A	15,842.50	15,842.50	15,842.50	10
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	21	100%	100%	06-Jul-26	29-Jul-26	14-Sep-26 A	21-Sep-26 A	158,424.99	158,424.99	158,424.99	-46
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	0%	0%	17-Nov-26	09-Dec-26	12-Dec-26	04-Jan-27	0.00	0.00	31,685.00	-21
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	3	0%	0%	17-Nov-26	19-Nov-26	05-Jan-27	09-Jan-27	0.00	0.00	15,842.50	-42
MLTX-02-005-CI	Aggregate basecourse layer (Football Playground)	21	81.43%	100%	20-Oct-26	12-Nov-26	24-Jun-26 A	27-Jun-26 A	12,900.32	15,842.50	15,842.50	118
PADEL PLAYGROUND		198	45%	70%	11-Jun-26	31-Dec-26	18-May-26 A	30-Jan-27	105,292.80	163,788.80	233,984.00	-24
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Padel Playground)	20	100%	100%	11-Jun-26	04-Jul-26	18-May-26 A	31-May-26 A	81,894.40	81,894.40	81,894.40	29
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Padel	21	100%	100%	06-Jul-26	29-Jul-26	01-Jun-26 A	23-Jun-26 A	11,699.20	11,699.20	11,699.20	31
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Padel Playground)	21	0%	100%	17-Nov-26	10-Dec-26	30-Aug-26 A	30-Aug-26 A	0.00	58,496.00	58,496.00	87
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	12-Dec-26	28-Dec-26	09-Jan-27	26-Jan-27	0.00	0.00	58,496.00	-24
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	3	0%	0%	29-Dec-26	31-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	11,699.20	-24
MLTX-02-005-CI	Aggregate basecourse layer (Padel Playground)	21	100%	100%	30-Jul-26	23-Aug-26	23-Jun-26 A	28-Jun-26 A	11,699.20	11,699.20	11,699.20	48
BASKETBALL PLAYGROUND		176	70.92%	70.92%	07-Jul-26	31-Dec-26	18-May-26 A	30-Jan-27	236,425.54	236,425.54	333,381.64	-24
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Basketball	20	100%	100%	07-Jul-26	29-Jul-26	18-May-26 A	31-May-26 A	92,913.27	92,913.27	92,913.27	51
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Basketball	21	100%	100%	11-Oct-26	03-Nov-26	01-Jun-26 A	23-Jun-26 A	15,795.26	15,795.26	15,795.26	113
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Basketball	21	100%	100%	24-Aug-26	16-Sep-26	29-Aug-26 A	30-Aug-26 A	96,629.80	96,629.80	96,629.80	15
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	17-Nov-26	28-Nov-26	12-Dec-26	23-Dec-26	0.00	0.00	80,796.75	-21
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	3	0%	0%	29-Dec-26	31-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	16,159.35	-24
MLTX-02-005-CI	Aggregate basecourse layer (Basketball Playground)	21	100%	100%	30-Jul-26	23-Aug-26	23-Jun-26 A	28-Jun-26 A	31,087.21	31,087.21	31,087.21	48
PADEL FENCE		87	0%	9.24%	28-Nov-26	31-Dec-26	06-Aug-26 A	23-Feb-27	0.00	5,077.72	54,928.63	-44
MLTX-02-005-CI	Excavation for Fence	8	0%	100%	28-Nov-26	06-Dec-26	06-Aug-26 A	06-Aug-26 A	0.00	414.35	414.35	103
MLTX-02-005-CI	Concrete Foundation for Fence including Posts Fixation	7	0%	100%	29-Nov-26	06-Dec-26	15-Aug-26 A	19-Aug-26 A	0.00	828.69	828.69	92
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	18	0%	100%	29-Nov-26	19-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	3,834.68	3,834.68	57
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	09-Jan-27	26-Jan-27	0.00	0.00	30,677.48	-32
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	09-Jan-27	26-Jan-27	0.00	0.00	15,338.75	-32
MLTX-02-005-CI	Install of Fence Gates	26	0%	0%	02-Dec-26	31-Dec-26	23-Jan-27	23-Feb-27	0.00	0.00	3,834.68	-44
CURBSTOEN/INTERLOCK		19	100%	90.03%	09-Sep-26	01-Oct-26	12-Aug-26 A	12-Nov-26	362,305.01	326,200.88	362,305.01	-35
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	12-Nov-26	180,520.67	144,416.54	180,520.67	-35
MLTX-02-005-CI	Concrete Works Under Curbstone	12	100%	100%	09-Sep-26	22-Sep-26	12-Aug-26 A	12-Aug-26 A	54,535.30	54,535.30	54,535.30	35
MLTX-02-005-CI	Curbstone Installation	4	100%	100%	24-Sep-26	28-Sep-26	12-Aug-26 A	23-Aug-26 A	127,249.04	127,249.04	127,249.04	30
AIR DOME		165	23.18%	23.18%	30-Jul-26	10-Dec-26	16-May-26 A	09-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-51
CIVIL WORKS		155	48.29%	48.29%	30-Jul-26	07-Dec-26	16-May-26 A	28-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-44
MLTX-02-005-CI	Excavation for Foundation (Air Dome)	15	100%	100%	30-Jul-26	16-Aug-26	16-May-26 A	01-Jun-26 A	167,650.30	167,650.30	167,650.30	65
MLTX-02-005-CI	Concrete Works for Foundations including Anchor Bolts (Air	15	100%	100%	17-Aug-26	02-Sep-26	22-Jul-26 A	21-Sep-26 A	228,008.77	228,008.77	228,008.77	-16
MLTX-02-005-CI	Cable System Installation (Air Dome)	10	100%	100%	03-Sep-26	14-Sep-26	21-Sep-26 A	21-Sep-26 A	350,921.95	350,921.95	350,921.95	-6
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	942,830.33	-44
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-44
MLTX-02-005-CI	Perimeter Clamping System Installation	13	100%	100%	03-Sep-26	17-Sep-26	21-Sep-26 A	28-Sep-26 A	552,946.49	552,946.49	552,946.49	-8
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	1,233,296.81	-39
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	15	0%	0%	21-Nov-26	07-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	728,766.30	-39
MLTX-02-005-CI	Air Units Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	13-Jan-27	23-Jan-27	0.00	0.00	336,353.67	-39
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	13-Jan-27	23-Jan-27	0.00	0.00	168,176.84	-39
ELECTRICAL WORKS		14	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	09-Feb-27	0.00	0.00	1,513,591.54	-51
MLTX-02-005-CI	Light Fixture Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	224,235.78	-45
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-45
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-45
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	504,530.51	-45
MLTX-02-005-CI	Control System Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	31-Jan-27	09-Feb-27	0.00	0.00	448,471.57	-51
FINISHES WORKS		30	0%	0%	15-Nov-26	10-Dec-26	05-Jan-27	09-Feb-27	0.00	0.00	168,176.84	-51
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	15-Nov-26	01-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	112,117.89	-44
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	09-Dec-26	10-Dec-26	07-Feb-27	09-Feb-27	0.00	0.00	56,058.95	-51
IRRIGATION NETWORK		111	52.94%	83.53%	03-Sep-26	07-Dec-26	18-Jul-26 A	12-Jan-27	80,689.03	127,308.67	152,414.87	-30
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	15	100%	100%	03-Sep-26	20-Sep-26	18-Jul-26 A	20-Jul-26 A	53,620.00	53,620.00	53,620.00	53
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	15	54%	100%	31-Oct-26	16-Nov-26	24-Aug-26 A	01-Sep-26 A	27,069.03	50,127.83	50,127.83	64
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	10	0%	100%	17-Nov-26	28-Nov-26	10-Sep-26 A	13-Oct-26 A	0.00	23,560.84	23,560.84	39
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	05-Dec-26	07-Dec-26	09-Jan-27	12-Jan-27	0.00	0.00	25,106.20	-30
NATURAL GROUND		15	0%	80.17%	29-Nov-26	07-Dec-26	13-Oct-26 A	12-Nov-26	0.00	153,718.00	191,740.00	22
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	70%	05-Dec-26	07-Dec-26	14-Oct-26 A	12-Nov-26	0.00	88,718.00	126,740.00	22
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	100%	29-Nov-26	03-Dec-26	13-Oct-26 A	03-Nov-26 A	0.00	65,000.00	65,000.00	27
PLANTING		101	100%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	12-Nov-26	347,251.46	240,773.38	347,251.46	-8
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	100%	95%	24-Oct-26	26-Oct-26	03-Oct-26 A	12-Nov-26	104,175.44	98,966.67	104,175.44	-14
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	100%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	12-Nov-26	141,732.50	70,866.25	141,732.50	-8

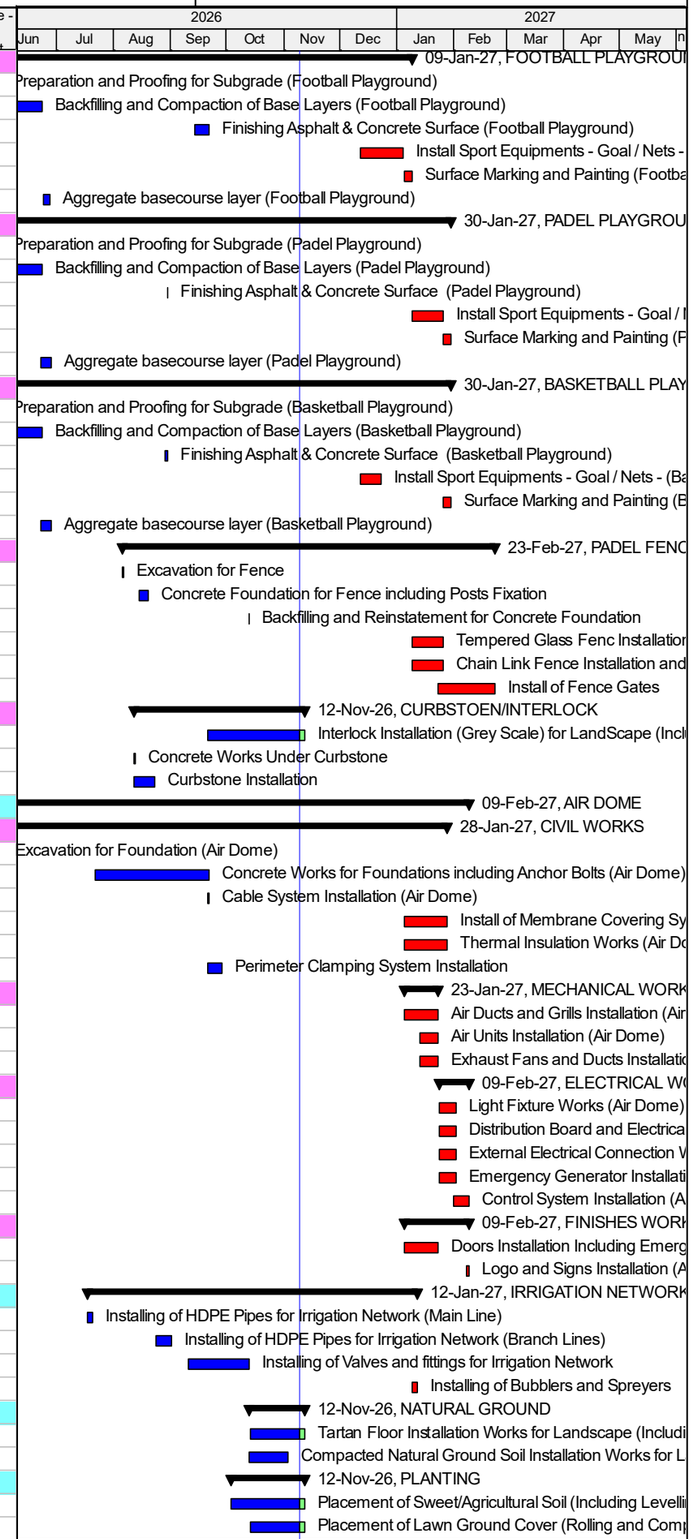

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Placement and Fixation of Trees	3	100%	70%	27-Oct-26	29-Oct-26	14-Oct-26 A	12-Nov-26	101,343.52	70,940.46	101,343.52	-11
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	09-Nov-26	367,633.90	294,107.12	367,633.90	-19
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	09-Nov-26	187,554.12	150,043.30	187,554.12	-27
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	09-Nov-26	180,079.78	144,063.82	180,079.78	-19
GENERAL/FURNITURE		103	40.59%	62.44%	06-Oct-26	24-Dec-26	03-Sep-26 A	03-Feb-27	190,875.01	293,649.30	470,271.40	-34
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	100%	45%	18-Oct-26	07-Nov-26	14-Oct-26 A	30-Nov-26	93,594.00	42,117.30	93,594.00	-19
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	3	0%	0%	20-Dec-26	22-Dec-26	28-Jan-27	01-Feb-27	0.00	0.00	9,749.30	-34
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	28	75.36%	0%	15-Oct-26	16-Nov-26	09-Nov-26	12-Dec-26	13,017.79	0.00	17,274.79	-21
MLTX-02-005-CN-1	Fixation and Installation of Benches	14	0%	0%	17-Nov-26	02-Dec-26	12-Dec-26	28-Dec-26	0.00	0.00	40,307.84	-21
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	14	0%	0%	03-Dec-26	19-Dec-26	12-Dec-26	28-Dec-26	0.00	0.00	32,757.76	-7
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	14	0%	0%	03-Dec-26	19-Dec-26	28-Dec-26	13-Jan-27	0.00	0.00	12,869.04	-21
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	2	0%	0%	23-Dec-26	24-Dec-26	01-Feb-27	03-Feb-27	0.00	0.00	12,186.67	-34
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	8	100%	100%	06-Oct-26	14-Oct-26	03-Sep-26 A	07-Sep-26 A	75,459.60	75,459.60	75,459.60	31
MLTX-02-005-CN-1	Installing of Site Light Poles	22	5%	100%	08-Nov-26	02-Dec-26	01-Oct-26 A	26-Oct-26 A	8,803.62	176,072.40	176,072.40	33
PARKING		12	0%	100%	24-Nov-26	07-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	68
MLTX-02-005-CN-119	Interlock Installation (8 Cm) for Parking Area (Including	7	0%	100%	30-Nov-26	07-Dec-26	10-Sep-26 A	19-Sep-26 A	0.00	40,945.33	40,945.33	68
MLTX-02-005-CN-119	Site Preparation & Compaction Under Interlock for Parking	5	0%	100%	24-Nov-26	29-Nov-26	14-May-26 A	30-Jun-26 A	0.00	17,548.00	17,548.00	129
TOILET/SERVICE BUILDING		258	77.25%	87.66%	09-May-26	23-Dec-26	24-May-26 A	04-Feb-27	900,720.90	1,022,090.25	1,166,004.29	-36
STRUCTURE WORKS		45	100%	100%	09-May-26	02-Jul-26	24-May-26 A	10-Aug-26 A	162,899.73	162,899.73	162,899.73	-33
CONCRETE WORKS		29	100%	100%	31-May-26	02-Jul-26	25-May-26 A	02-Jul-26 A	118,454.85	118,454.85	118,454.85	0
SUB-STRUCTURE		9	100%	100%	31-May-26	09-Jun-26	25-May-26 A	06-Jun-26 A	38,022.35	38,022.35	38,022.35	3
MLTX-02-005-CI	Plain Concrete Under Footing	2	100%	100%	31-May-26	01-Jun-26	25-May-26 A	31-May-26 A	1,462.40	1,462.40	1,462.40	1
MLTX-02-005-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	04-Jun-26	09-Jun-26	03-Jun-26 A	06-Jun-26 A	36,559.95	36,559.95	36,559.95	3
SUPER-STRUCTURE		12	100%	100%	20-Jun-26	02-Jul-26	28-Jun-26 A	02-Jul-26 A	80,432.50	80,432.50	80,432.50	0
MLTX-02-005-CI	AAC Panels Works for Walls	7	100%	100%	20-Jun-26	27-Jun-26	28-Jun-26 A	30-Jun-26 A	48,259.50	48,259.50	48,259.50	-3
MLTX-02-005-CI	Parpet Works and Lintels	3	100%	100%	30-Jun-26	02-Jul-26	02-Jul-26 A	02-Jul-26 A	16,086.50	16,086.50	16,086.50	0
MLTX-02-005-CI	AAC Panels Works for Slabs	2	100%	100%	28-Jun-26	29-Jun-26	01-Jul-26 A	01-Jul-26 A	16,086.50	16,086.50	16,086.50	-2
UNDER GROUND SEPTIC TANK		28	100%	100%	11-May-26	15-Jun-26	04-Jun-26 A	06-Jul-26 A	34,208.09	34,208.09	34,208.09	-18
MLTX-02-005-CN-1	Plain Concrete Under Footing	3	100%	100%	11-May-26	13-May-26	04-Jun-26 A	06-Jun-26 A	1,462.40	1,462.40	1,462.40	-17
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Slab Including	8	100%	100%	07-Jun-26	15-Jun-26	02-Jul-26 A	06-Jul-26 A	8,774.37	8,774.37	8,774.37	-18
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Foundation Including	7	100%	100%	14-May-26	21-May-26	18-Jun-26 A	20-Jun-26 A	7,604.46	7,604.46	7,604.46	-22
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	10	100%	100%	23-May-26	06-Jun-26	20-Jun-26 A	29-Jun-26 A	16,366.86	16,366.86	16,366.86	-20
THERMAL & MOISTER PROTECTION		38	100%	100%	09-May-26	24-Jun-26	24-May-26 A	10-Aug-26 A	10,236.80	10,236.80	10,236.80	-40
ANTI TERMIT CONTROL		13	100%	100%	09-May-26	23-May-26	24-May-26 A	03-Jun-26 A	4,387.50	4,387.50	4,387.50	-7
MLTX-02-005-CI	Anti Termite Works Under Foundation	1	100%	100%	09-May-26	09-May-26	31-May-26 A	03-Jun-26 A	1,755.00	1,755.00	1,755.00	-19
MLTX-02-005-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	23-May-26	23-May-26	24-May-26 A	25-May-26 A	2,632.50	2,632.50	2,632.50	-2
POLYETHYLENE SHEET		13	100%	100%	10-May-26	24-May-26	25-May-26 A	04-Jun-26 A	2,193.30	2,193.30	2,193.30	-7
MLTX-02-005-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	10-May-26	10-May-26	01-Jun-26 A	04-Jun-26 A	877.32	877.32	877.32	-19
MLTX-02-005-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	24-May-26	24-May-26	25-May-26 A	31-May-26 A	1,315.98	1,315.98	1,315.98	-3
EPOXY		8	100%	100%	16-Jun-26	24-Jun-26	11-Jul-26 A	10-Aug-26 A	3,656.00	3,656.00	3,656.00	-40
MLTX-02-005-CI	Surface Preparation for Epoxy Coating	3	100%	100%	16-Jun-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	1,096.80	1,096.80	1,096.80	-19
MLTX-02-005-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	20-Jun-26	24-Jun-26	28-Jul-26 A	10-Aug-26 A	2,559.20	2,559.20	2,559.20	-40
MASONARY WORK		5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
MLTX-02-005-CN-126	CMU Masonary Works Including all Accessories	5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
THERMAL & MOISTER PROTECTION		41	100%	95.21%	04-Jul-26	19-Aug-26	10-Sep-26 A	30-Nov-26	34,698.32	33,037.59	34,698.32	-86
MLTX-02-005-CN-126	Preparing Surface and Preliminary Works for Toilets	2	100%	100%	04-Jul-26	05-Jul-26	10-Sep-26 A	10-Sep-26 A	2,105.86	2,105.86	2,105.86	-58
MLTX-02-005-CN-126	Finalize Water Proofing Works for Toilets	5	100%	100%	06-Jul-26	11-Jul-26	12-Sep-26 A	12-Sep-26 A	4,913.66	4,913.66	4,913.66	-54
MLTX-02-005-CN-126	Preparing Surface and Preliminary Works for Roofing and	16	100%	100%	12-Jul-26	29-Jul-26	20-Sep-26 A	20-Sep-26 A	11,071.52	11,071.52	11,071.52	-45
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	30-Nov-26	16,607.28	14,946.55	16,607.28	-86
MECHANICAL WORK		112	99.26%	99.26%	24-Aug-26	21-Dec-26	12-Jul-26 A	03-Jan-27	262,723.23	262,723.23	264,673.10	-10
HVAC SYSTEM		10	100%	100%	04-Oct-26	14-Oct-26	12-Jul-26 A	08-Oct-26 A	27,883.37	27,883.37	27,883.37	5
MLTX-02-005-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	12-Oct-26	14-Oct-26	12-Jul-26 A	12-Jul-26 A	9,359.69	9,359.69	9,359.69	80
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	4	100%	100%	06-Oct-26	10-Oct-26	08-Oct-26 A	08-Oct-26 A	14,623.96	14,623.96	14,623.96	1
MLTX-02-005-CN-1	Exhaust, Air Ducts Installation with all Accessories	6	100%	100%	04-Oct-26	10-Oct-26	25-Aug-26 A	29-Aug-26 A	3,899.72	3,899.72	3,899.72	35
WATER SUPPLY SYSTEM		46	100%	100%	24-Aug-26	17-Oct-26	21-Jul-26 A	08-Oct-26 A	154,916.69	154,916.69	154,916.69	7
MLTX-02-005-CN-1	Installing of PPR Pipes and Fittings for Water Network	6	100%	100%	16-Sep-26	22-Sep-26	21-Jul-26 A	21-Jul-26 A	6,921.94	6,921.94	6,921.94	54
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	7	100%	100%	10-Oct-26	17-Oct-26	19-Sep-26 A	08-Oct-26 A	25,998.40	25,998.40	25,998.40	7
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	20	100%	100%	27-Aug-26	19-Sep-26	04-Oct-26 A	04-Oct-26 A	48,746.52	48,746.52	48,746.52	-12
MLTX-02-005-CN-1	Installing of GRP Tanks	20	100%	100%	12-Sep-26	05-Oct-26	06-Sep-26 A	14-Sep-26 A	64,995.36	64,995.36	64,995.36	17
MLTX-02-005-CN-1	Installing of Valves and Fittings	5	100%	100%	24-Sep-26	29-Sep-26	05-Sep-26 A	05-Sep-26 A	6,499.60	6,499.60	6,499.60	20
MLTX-02-005-CN-1	Installing of Water Heater	3	100%	100%	24-Aug-26	26-Aug-26	29-Sep-26 A	29-Sep-26 A	1,754.87	1,754.87	1,754.87	-28
SEWER/DRAINAGE SYSTEM		46	100%	100%	27-Aug-26	20-Oct-26	21-Jul-26 A	12-Oct-26 A	79,923.17	79,923.17	79,923.17	7
MLTX-02-005-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	09-Sep-26	10-Sep-26	21-Jul-26 A	22-Jul-26 A	11,767.40	11,767.40	11,767.40	43
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	5	100%	100%	15-Oct-26	20-Oct-26	04-Oct-26 A	12-Oct-26 A	10,358.68	10,358.68	10,358.68	7

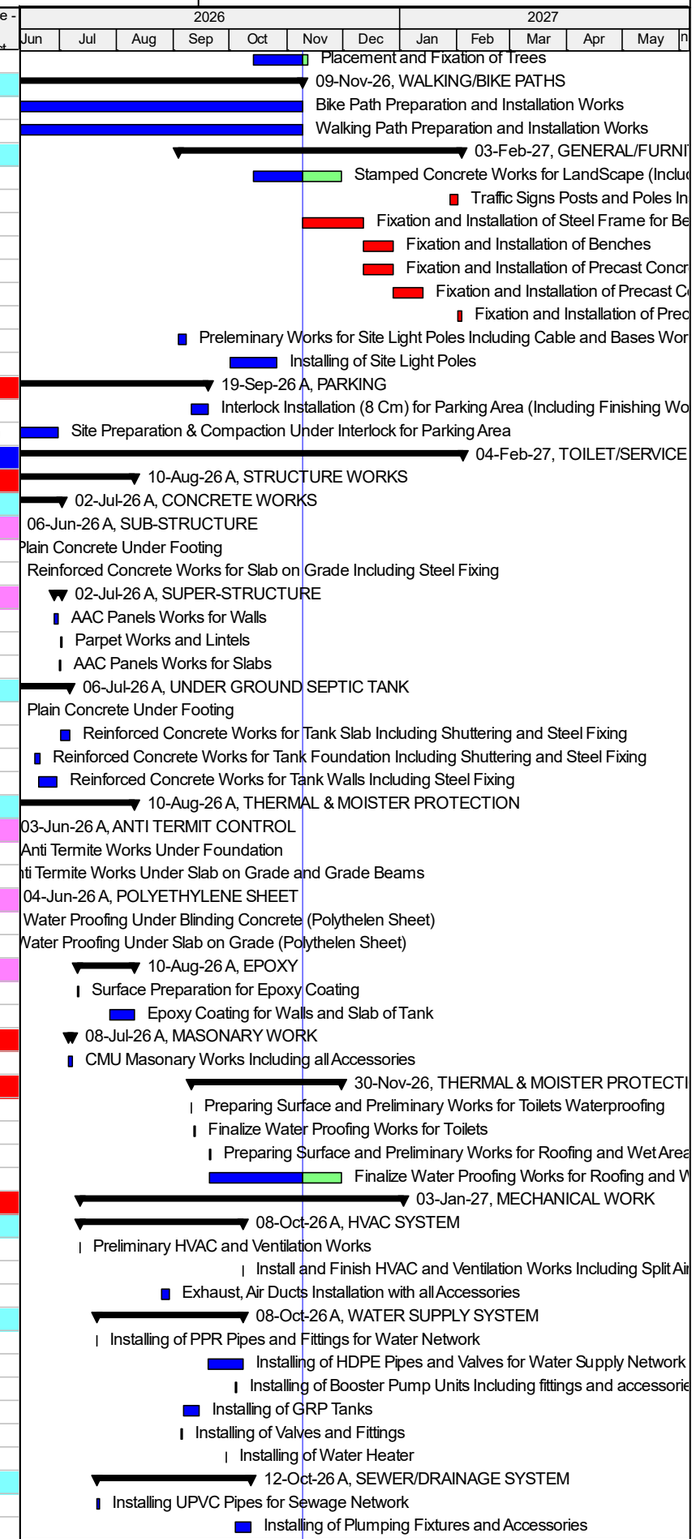

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	8	100%	100%	24-Sep-26	03-Oct-26	08-Oct-26 A	08-Oct-26 A	14,217.67	14,217.67	14,217.67	-5
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	10	100%	100%	12-Sep-26	22-Sep-26	03-Oct-26 A	03-Oct-26 A	12,186.63	12,186.63	12,186.63	-8
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	21	100%	100%	27-Aug-26	20-Sep-26	08-Oct-26 A	12-Oct-26 A	31,392.79	31,392.79	31,392.79	-18
FIRE PROTECTION		21	0%	0%	28-Nov-26	21-Dec-26	09-Dec-26	03-Jan-27	0.00	0.00	1,949.87	-10
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	0%	0%	28-Nov-26	21-Dec-26	09-Dec-26	03-Jan-27	0.00	0.00	1,949.87	-10
ELECTRICAL WORKS		128	58.71%	71.78%	03-Sep-26	21-Dec-26	14-Jul-26 A	01-Feb-27	227,202.96	277,771.03	386,998.85	-35
ROUGH-IN WORKS		10	100%	100%	03-Sep-26	14-Sep-26	14-Jul-26 A	17-Aug-26 A	206,217.58	206,217.58	206,217.58	24
MLTX-02-005-CN-1	Preleminary Works for Panel Boards	2	100%	100%	13-Sep-26	14-Sep-26	22-Jul-26 A	09-Aug-26 A	68,245.12	68,245.12	68,245.12	31
MLTX-02-005-CN-1	Preleminary Works for Cable Works	2	100%	100%	06-Sep-26	07-Sep-26	22-Jul-26 A	09-Aug-26 A	12,488.95	12,488.95	12,488.95	26
MLTX-02-005-CN-1	Preleminary Works for Sockets and Power Points	2	100%	100%	06-Sep-26	07-Sep-26	14-Jul-26 A	09-Aug-26 A	15,990.55	15,990.55	15,990.55	25
MLTX-02-005-CN-1	Preleminary Works for Lightning Works	2	100%	100%	03-Sep-26	05-Sep-26	09-Aug-26 A	17-Aug-26 A	21,935.93	21,935.93	21,935.93	16
MLTX-02-005-CN-1	Preleminary Works for Data & Telecommunication System	2	100%	100%	06-Sep-26	07-Sep-26	09-Aug-26 A	17-Aug-26 A	24,470.75	24,470.75	24,470.75	18
MLTX-02-005-CN-1	Preleminary Works for Security and Access Control System	2	100%	100%	13-Sep-26	14-Sep-26	09-Aug-26 A	17-Aug-26 A	30,913.59	30,913.59	30,913.59	24
MLTX-02-005-CN-1	Preleminary Works for Earthing Works	2	100%	100%	12-Sep-26	13-Sep-26	09-Aug-26 A	17-Aug-26 A	32,172.69	32,172.69	32,172.69	23
FIXTURE WORKS		57	11.61%	39.58%	04-Nov-26	21-Dec-26	29-Oct-26 A	01-Feb-27	20,985.38	71,553.45	180,781.27	-35
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	18	0%	0%	28-Nov-26	17-Dec-26	02-Dec-26	23-Dec-26	0.00	0.00	34,317.53	-4
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	20.5%	40%	04-Nov-26	26-Nov-26	03-Nov-26 A	02-Dec-26	20,985.38	40,947.08	102,367.69	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	0%	100%	28-Nov-26	20-Dec-26	29-Oct-26 A	31-Oct-26 A	0.00	7,085.10	7,085.10	44
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	0%	100%	28-Nov-26	21-Dec-26	01-Nov-26 A	01-Nov-26 A	0.00	14,259.43	14,259.43	44
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	28-Nov-26	20-Dec-26	02-Dec-26	26-Dec-26	0.00	0.00	6,239.59	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	0%	0%	21-Nov-26	13-Dec-26	09-Jan-27	01-Feb-27	0.00	0.00	7,250.09	-42
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	0%	100%	28-Nov-26	20-Dec-26	03-Nov-26 A	03-Nov-26 A	0.00	6,824.51	6,824.51	41
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	0%	100%	21-Nov-26	13-Dec-26	01-Nov-26 A	01-Nov-26 A	0.00	2,437.33	2,437.33	37
DOORS/WINDOWS		213	14.29%	100%	04-Jul-26	16-Dec-26	28-Sep-26 A	28-Oct-26 A	9,749.30	68,245.12	68,245.12	43
MLTX-02-005-CN-126	Preliminary Works For Doors	13	100%	100%	04-Jul-26	18-Jul-26	28-Sep-26 A	28-Sep-26 A	7,799.44	7,799.44	7,799.44	-61
MLTX-02-005-CN-126	Finalize Metal Doors for Toilets Building	11	100%	100%	19-Jul-26	30-Jul-26	29-Sep-26 A	29-Sep-26 A	1,949.86	1,949.86	1,949.86	-51
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	11	0%	100%	05-Dec-26	16-Dec-26	27-Oct-26 A	28-Oct-26 A	0.00	5,849.58	5,849.58	43
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	12	0%	100%	21-Nov-26	03-Dec-26	24-Oct-26 A	27-Oct-26 A	0.00	52,646.24	52,646.24	33
METAL WORKS		65	100%	71.43%	03-Sep-26	20-Oct-26	06-Sep-26 A	19-Dec-26	13,649.02	9,749.30	13,649.02	-50
MLTX-02-005-CN-126	Installation of Galvanized Steel Ladder	14	100%	100%	03-Sep-26	19-Sep-26	18-Oct-26 A	18-Oct-26 A	5,849.58	5,849.58	5,849.58	-24
MLTX-02-005-CN-125	Installation of DI Cover for Tank	14	100%	0%	05-Oct-26	20-Oct-26	02-Dec-26	19-Dec-26	3,899.72	0.00	3,899.72	-50
MLTX-02-005-CN-125	Installation of Galvanized Steel Roof Scupper	4	100%	100%	04-Oct-26	07-Oct-26	06-Sep-26 A	06-Sep-26 A	3,899.72	3,899.72	3,899.72	26
FINISHING WORKS		121	99.29%	97.1%	20-Aug-26	16-Dec-26	17-Aug-26 A	04-Feb-27	162,890.28	159,307.72	164,060.22	-42
FLOOR FINISHES		114	93.18%	93.18%	24-Sep-26	16-Dec-26	15-Sep-26 A	04-Feb-27	15,989.09	15,989.09	17,159.03	-42
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	100%	24-Sep-26	26-Sep-26	15-Sep-26 A	16-Sep-26 A	11,894.39	11,894.39	11,894.39	7
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	6	100%	100%	27-Sep-26	03-Oct-26	25-Oct-26 A	25-Oct-26 A	2,924.82	2,924.82	2,924.82	-19
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	23	0%	0%	21-Nov-26	16-Dec-26	09-Jan-27	04-Feb-27	0.00	0.00	1,169.94	-42
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	100%	11-Oct-26	14-Oct-26	04-Oct-26 A	04-Oct-26 A	1,169.88	1,169.88	1,169.88	9
WALL FINISHES		82	100%	97.33%	20-Aug-26	03-Nov-26	17-Aug-26 A	12-Nov-26	134,001.04	130,418.48	134,001.04	-7
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works including Plastering	3	100%	100%	15-Sep-26	17-Sep-26	17-Aug-26 A	19-Aug-26 A	18,315.62	18,315.62	18,315.62	25
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works (External)	6	100%	100%	27-Sep-26	03-Oct-26	19-Aug-26 A	31-Aug-26 A	6,551.63	6,551.63	6,551.63	27
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	12-Nov-26	35,825.58	32,243.02	35,825.58	-19
MLTX-02-005-CN-1	Ceramic Finish Works for Walls	5	100%	100%	20-Sep-26	26-Sep-26	01-Sep-26 A	03-Sep-26 A	15,696.35	15,696.35	15,696.35	18
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	100%	21-Oct-26	28-Oct-26	03-Nov-26 A	07-Nov-26 A	31,197.60	31,197.60	31,197.60	-8
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	100%	27-Sep-26	01-Oct-26	04-Oct-26 A	04-Oct-26 A	2,275.00	2,275.00	2,275.00	-2
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	100%	100%	29-Oct-26	03-Nov-26	24-Oct-26 A	28-Oct-26 A	13,649.02	13,649.02	13,649.02	6
MLTX-02-005-CN-1	Granite Capping for Parpet	12	100%	100%	20-Aug-26	02-Sep-26	25-Oct-26 A	25-Oct-26 A	8,150.24	8,150.24	8,150.24	-44
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	100%	04-Oct-26	05-Oct-26	29-Sep-26 A	06-Oct-26 A	2,340.00	2,340.00	2,340.00	-1
CELLING FINISHES		16	100%	100%	15-Sep-26	04-Oct-26	28-Sep-26 A	01-Oct-26 A	12,900.15	12,900.15	12,900.15	2
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	13	100%	100%	15-Sep-26	30-Sep-26	30-Sep-26 A	01-Oct-26 A	1,357.11	1,357.11	1,357.11	-1
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	5	100%	100%	27-Sep-26	01-Oct-26	28-Sep-26 A	29-Sep-26 A	5,771.52	5,771.52	5,771.52	2
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	13	100%	100%	19-Sep-26	04-Oct-26	28-Sep-26 A	29-Sep-26 A	5,771.52	5,771.52	5,771.52	4
SPECIALTIES WORK		74	25%	61.67%	27-Sep-26	23-Dec-26	04-Oct-26 A	22-Dec-26	14,623.96	36,072.43	58,495.83	2
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	12-Nov-26	14,623.96	11,699.17	14,623.96	-37
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	17	0%	0%	05-Dec-26	23-Dec-26	02-Dec-26	22-Dec-26	0.00	0.00	19,498.61	2
MLTX-02-005-CN-131	Installation of Phenolic Locker	12	0%	100%	28-Nov-26	10-Dec-26	07-Nov-26 A	07-Nov-26 A	0.00	24,373.26	24,373.26	29
TESTING & COMMISSIONING		28	0%	0%	08-Dec-26	02-Jan-27	28-Jan-27	03-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	18	0%	0%	12-Dec-26	31-Dec-26	09-Feb-27	03-Mar-27	0.00	0.00	0.00	-51
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	7	0%	0%	26-Dec-26	02-Jan-27	14-Feb-27	23-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	21	0%	0%	08-Dec-26	31-Dec-26	28-Jan-27	23-Feb-27	0.00	0.00	0.00	-44
DAMMAM		307	43.44%	44.17%	03-Mar-26	02-Jan-27	04-Mar-26 A	06-Mar-27	4,264,073.43	4,335,150.18	9,815,232.20	-52
MOBILIZATION		33	0%	0%	03-Mar-26	13-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
TOPOGRAPHIC SURVEY		5	0%	0%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2100	Site Survey Works	5	100%	100%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0

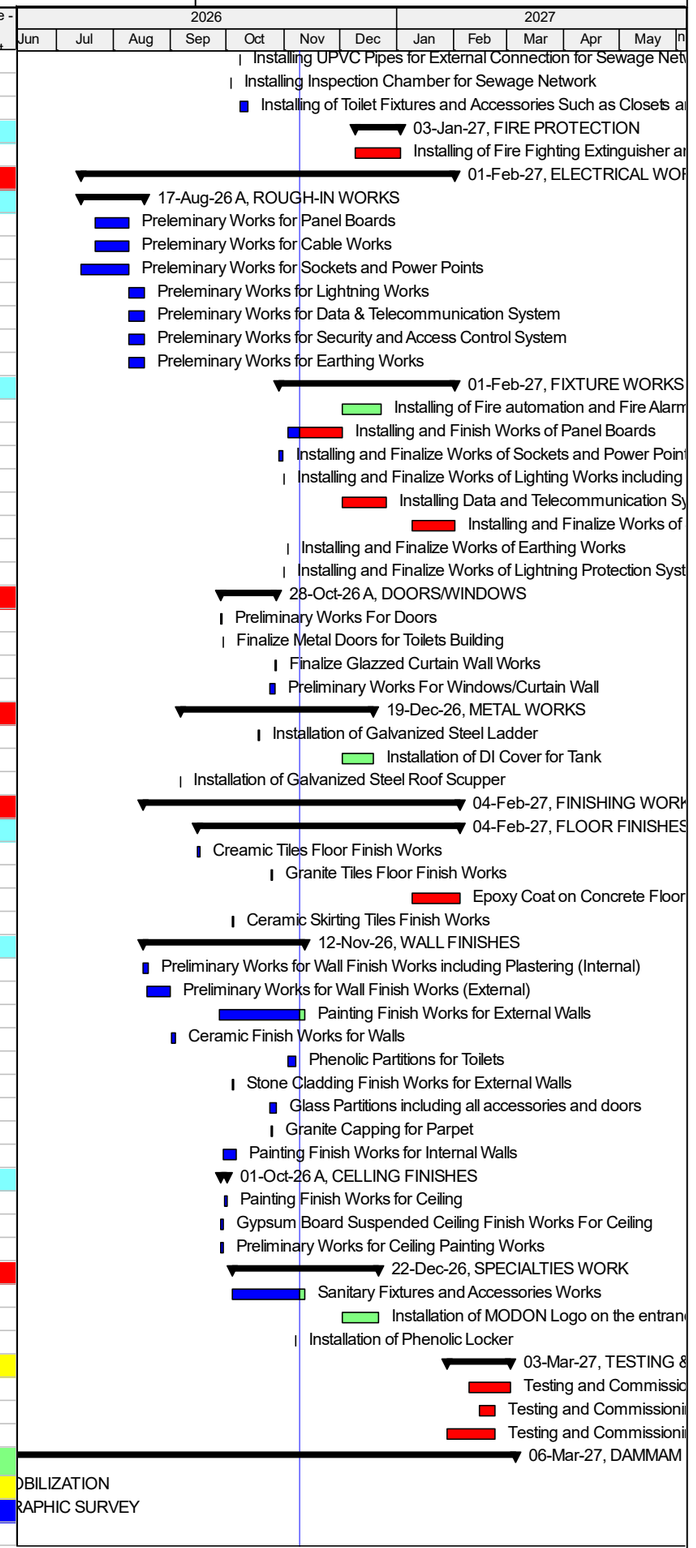

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SITE FACILITIES & OFFICES		29	0%	0%	03-Mar-26	08-Apr-26	04-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	5
MLTX-02-005-MB-1980	Manpower Mobalization	5	100%	100%	29-Mar-26	02-Apr-26	29-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-1990	Equipment Mobalization	7	100%	100%	26-Mar-26	02-Apr-26	26-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2010	Site Layout Plan	5	100%	100%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2020	Clear & Grub for Offices & Access Road	3	100%	100%	09-Mar-26	11-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2030	Construct Site Access Roads	4	100%	100%	09-Mar-26	12-Mar-26	09-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2040	Construct Temporary Fence	7	100%	100%	12-Mar-26	19-Mar-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2050	Construct Site Offices & Storage	14	100%	100%	24-Mar-26	08-Apr-26	14-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-2060	Install Project Signs	8	100%	100%	14-Mar-26	25-Mar-26	14-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2070	Install Site Facilities	4	100%	100%	24-Mar-26	28-Mar-26	24-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2080	Electrical Works & Connections	6	100%	100%	29-Mar-26	04-Apr-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	4
MLTX-02-005-MB-2090	Construct Parking Sheds	6	100%	100%	29-Mar-26	04-Apr-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	4
PRELIMINARY SUBMITTALS		28	0%	0%	09-Mar-26	13-Apr-26	09-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
PREPARATIONS & SUBMITTAL BY CONTRACTORS		16	0%	0%	09-Mar-26	30-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	6
MLTX-02-005-MB-200	Preparation and Submittal of Detailed Work Order	10	100%	100%	09-Mar-26	19-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-211	Preparation and Submittal of Project Execution Plan	8	100%	100%	09-Mar-26	17-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-212	Submission of Contractor Project Quality Plan	8	100%	100%	18-Mar-26	30-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-213	Submission of Construction Safety & Environmental	8	100%	100%	18-Mar-26	30-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-214	Preparation and Submittal of Organization Chart	8	100%	100%	18-Mar-26	30-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-215	Preparation and Submittal of Communication Plan	8	100%	100%	18-Mar-26	30-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	8
APPROVALS BY EMPLOYERS		20	0%	0%	18-Mar-26	13-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
MLTX-02-005-MB-216	Approval of Detailed Work Order Programme (Baseline)	10	100%	100%	24-Mar-26	04-Apr-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-217	Approval of Project Execution Plan	10	100%	100%	18-Mar-26	01-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-218	Approval of Contractor Project Quality Plan	10	100%	100%	02-Apr-26	13-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-MB-219	Approval of Construction Safety & Environmental	10	100%	100%	02-Apr-26	13-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-MB-220	Approval of Organization Chart	10	100%	100%	02-Apr-26	13-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-MB-221	Approval of Communication Plan	10	100%	100%	02-Apr-26	13-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
ENGINEERING		253	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	30
SHOP DRAWINGS		253	0%	0%	09-Mar-26	06-Oct-26	08-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-27
SHOP DRAWINGS SUBMISSION		233	0%	0%	09-Mar-26	06-Sep-26	08-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-52
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		40	0%	0%	09-Mar-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN-1	Shop DWG Submittal for Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Setting Out	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Grading Layout Plan	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN-1	Shop DWG Submittal for Curb Setting Out Points	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Signing & Marking Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Standards Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		135	0%	0%	30-Mar-26	06-Sep-26	09-Mar-26 A	08-Jul-26 A	0.00	0.00	0.00	51
ARCHITECTURE WORKS		25	0%	0%	30-Mar-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Floor Plan	15	100%	100%	30-Mar-26	15-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Shop DWG Submittal for Elevations	15	100%	100%	30-Mar-26	15-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Ceiling Plan	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Finishes Plan	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Toilet Details	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Doors/Windows Schedule	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
STRUCTURE WORKS		21	0%	0%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for Foundation Plan	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN	Shop DWG Submittal for Ground Floor Framing Plan	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for Sections/Details	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MECHANCAL WORKS		110	0%	0%	28-Apr-26	06-Sep-26	12-Mar-26 A	08-Jul-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	100%	13-Aug-26	06-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	100%	11-Aug-26	03-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN	Shop DWG Submittal for HVAC Equipment Schedule	21	100%	100%	11-Aug-26	03-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN	Shop DWG Submittal for Fire Fighting Layout	21	100%	100%	28-Apr-26	21-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Layout	21	100%	100%	11-Aug-26	03-Sep-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Details	21	100%	100%	11-Aug-26	03-Sep-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN	Shop DWG Submittal for Drainage Layout	21	100%	100%	11-Aug-26	03-Sep-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN	Shop DWG Submittal for Drainage Details	21	100%	100%	11-Aug-26	03-Sep-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	82
MLTX-02-005-EN	Shop DWG Submittal for Dut Routing Layout	21	100%	100%	11-Aug-26	03-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN	Shop DWG Submittal for Diffusers Layout	21	100%	100%	11-Aug-26	03-Sep-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	49
ELECTRICAL WORKS		93	0%	0%	28-Apr-26	17-Aug-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	21	100%	100%	25-Jul-26	17-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	123
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	100%	25-Jul-26	17-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	123

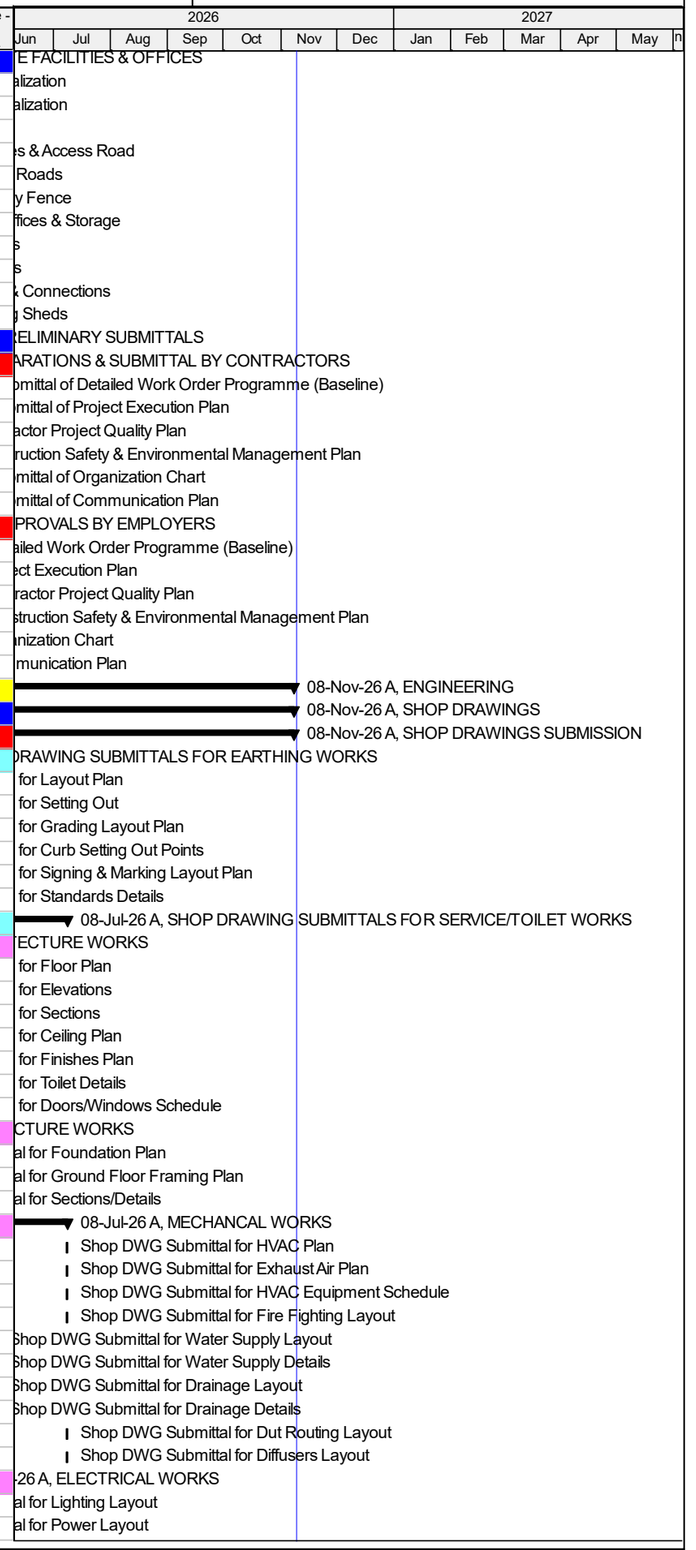

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	21	100%	100%	25-Jul-26	17-Aug-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	87
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	15	100%	100%	28-Apr-26	14-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Lighting Installation Details	21	100%	100%	25-Jul-26	17-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	123
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Cable Tray Installation Details	15	100%	100%	28-Apr-26	14-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Manhole & Ductbank Details	15	100%	100%	28-Apr-26	14-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Grounding Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for CCTV Details	15	100%	100%	25-Jul-26	10-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	117
MLTX-02-005-EM	Shop DWG Submittal for Grounding Layout	15	100%	100%	16-May-26	04-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection System Layout	15	100%	100%	16-May-26	04-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	15	100%	100%	16-May-26	04-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	15	100%	100%	16-May-26	04-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EM	Shop DWG Submittal for CCTV Layout	15	100%	100%	25-Jul-26	10-Aug-26	15-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	121
MLTX-02-005-EM	Shop DWG Submittal for CCTV Riser Diagram	15	100%	100%	25-Jul-26	10-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	107
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Layout	21	100%	100%	25-Jul-26	17-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	123
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Riser Diagram	21	100%	100%	25-Jul-26	17-Aug-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	123
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		233	0%	0%	09-Mar-26	17-Aug-26	08-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-69
ARCHITECTURE WORKS		21	0%	0%	09-Mar-26	05-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EM	Shop DWG Submittal for Playground Plan/Layout	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Furniture & Marking	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Sections	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Interlock Pattern Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Shop DWG Submittal for Doors/Windows Schedule	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EM	Shop DWG Submittal for Dome Internal Layout	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
STRUCTURE WORKS		21	0%	0%	06-Apr-26	29-Apr-26	14-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Air Dome System	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Shop DWG Submittal for Foundation of Air Dome	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-26
AIR DOME SYSTEM		199	0%	0%	06-Apr-26	07-Jun-26	14-Mar-26 A	13-Oct-26 A	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Submittal for Air Dome Structural Layout	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Shop DWG Submittal for Membrane Panel Layout	21	100%	100%	06-Apr-26	29-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EM	Shop DWG Submittal for Cable Tension Layout	15	100%	100%	16-Apr-26	03-May-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-136
MLTX-02-005-EM	Shop DWG Submittal for Airlock Door Details	25	100%	100%	30-Apr-26	01-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-114
MLTX-02-005-EM	Shop DWG Submittal for Emergency Exit Details	30	100%	100%	30-Apr-26	07-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-109
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Shop DWG Submittal for Football Turf Installation	21	100%	100%	30-Apr-26	24-May-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Shop DWG Submittal for Basketball Court Marking	21	100%	100%	30-Apr-26	24-May-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Shop DWG Submittal for Padel Court Structure	21	100%	100%	30-Apr-26	24-May-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-28
MECHANCAL WORKS		15	0%	0%	30-Apr-26	14-Jun-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-104
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	15	100%	100%	30-Apr-26	17-May-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-125
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	15	100%	100%	25-May-26	14-Jun-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-104
ELECTRICAL WORKS		191	0%	0%	30-Apr-26	17-Aug-26	14-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-69
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	21	100%	100%	25-May-26	21-Jun-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	25	100%	100%	25-May-26	25-Jun-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-114
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	25	100%	100%	25-May-26	25-Jun-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-94
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	25	100%	100%	25-May-26	25-Jun-26	14-Oct-26 A	14-Oct-26 A	0.00	0.00	0.00	-94
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	30	100%	100%	25-May-26	01-Jul-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	100%	30-Jun-26	23-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Shop DWG Submittal for CCTV Details	21	100%	100%	25-May-26	21-Jun-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	21	100%	100%	30-Apr-26	24-May-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	100%	02-Jul-26	26-Jul-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	68
MLTX-02-005-EM	Shop DWG Submittal for CCTV Layout	21	100%	100%	25-Jul-26	17-Aug-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EM	Shop DWG Submittal for CCTV Riser Diagram	21	100%	100%	25-Jul-26	17-Aug-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-7
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		132	0%	0%	09-Mar-26	16-Aug-26	08-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	14
ARCHITECTURE WORKS		51	0%	0%	09-Mar-26	10-May-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	41
MLTX-02-005-EM	Shop DWG Submittal for Landscape Layout	21	100%	100%	30-Mar-26	22-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Shop DWG Submittal for Hardscape Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Shop DWG Submittal for Planting Plan	15	100%	100%	23-Apr-26	10-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	41
MLTX-02-005-EM	Shop DWG Submittal for Landscape Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MECHANCAL WORKS		21	0%	0%	09-Mar-26	05-Apr-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Irrigation Details	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Irrigation Layout	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-49

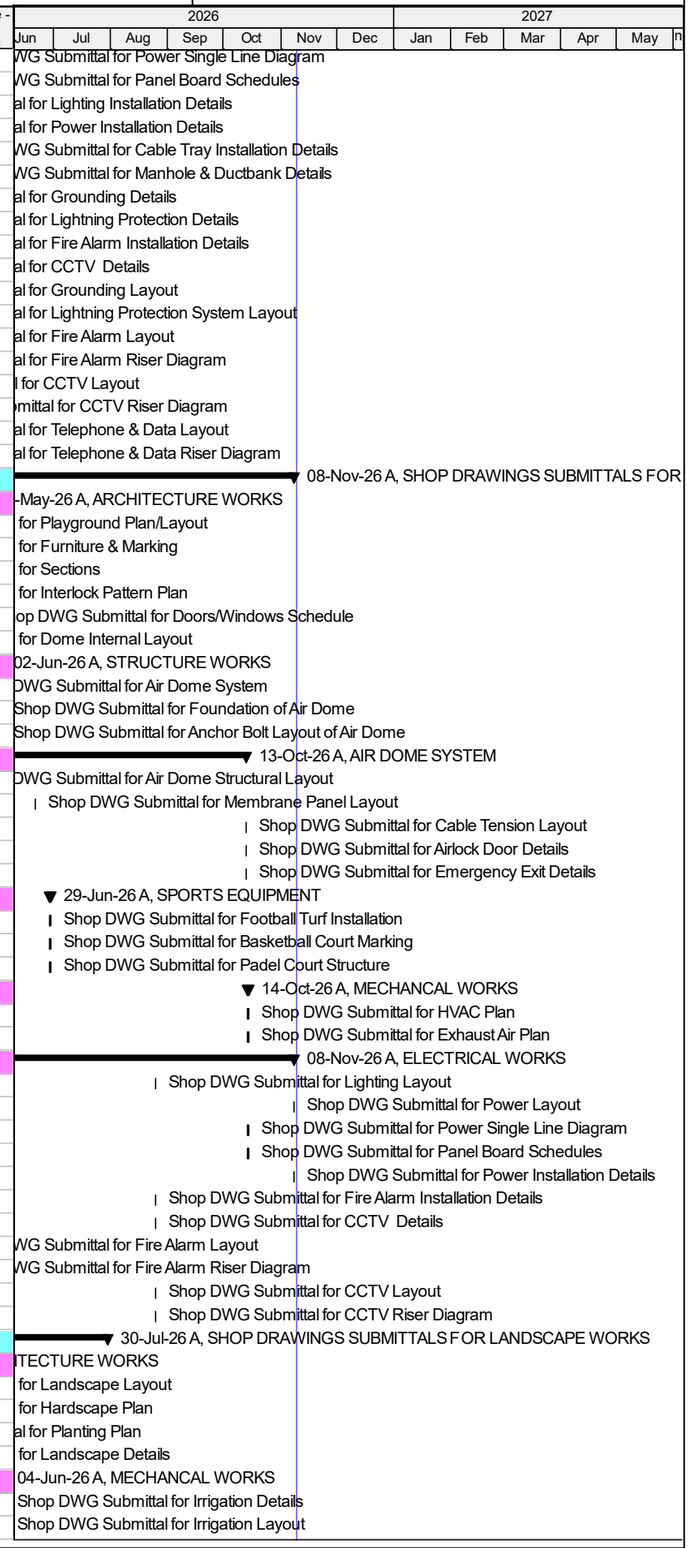

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
ELECTRICAL WORKS		132	0%	0%	09-Mar-26	16-Aug-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN	Shop DWG Submittal for Lighting General Arrangement	30	100%	100%	13-Jul-26	16-Aug-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN	Shop DWG Submittal for Lighting Network Layout	30	100%	100%	09-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Submittal for Lighting Details	30	100%	100%	22-Jun-26	26-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Shop DWG Submittal for Lighting Single Line Diagram	30	100%	100%	22-Jun-26	26-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-4
SHOP DRAWINGS APPROVALS		238	0%	0%	30-Mar-26	06-Oct-26	14-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-27
SHOP DRAWING APPROVAL FOR EARTHING WORKS		114	0%	0%	30-Mar-26	12-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	114
MLTX-02-005-EN-1	Shop DWG Approval for Layout Plan	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Shop DWG Approval for Setting Out	10	100%	100%	30-Mar-26	09-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Approval for Grading Layout Plan	16	100%	100%	26-Jul-26	12-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	114
MLTX-02-005-EN-1	Shop DWG Approval for Curb Setting Out Points	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Shop DWG Approval for Signing & Marking Layout Plan	10	100%	100%	30-Mar-26	09-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Approval for Standards Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		133	0%	0%	30-Apr-26	06-Oct-26	15-Mar-26 A	28-Jul-26 A	0.00	0.00	0.00	59
ARCHITECTURE WORKS		64	0%	0%	30-Apr-26	16-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN	Shop DWG Approval for Floor Plan	30	100%	100%	13-Jun-26	16-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN	Shop DWG Approval for Elevations	30	100%	100%	08-Jun-26	12-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN	Shop DWG Approval for Sections	30	100%	100%	30-Apr-26	07-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	57
MLTX-02-005-EN	Shop DWG Approval for Ceiling Plan	30	100%	100%	08-Jun-26	12-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN	Shop DWG Approval for Finishes Plan	30	100%	100%	08-Jun-26	12-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN	Shop DWG Approval for Toilet Details	30	100%	100%	08-Jun-26	12-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	08-Jun-26	12-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	87
STRUCTURE WORKS		26	0%	0%	23-May-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN	Shop DWG Approval for Foundation Plan	15	100%	100%	08-Jun-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN	Shop DWG Approval for Ground Floor Framing Plan	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Sections/Details	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MECHANCAL WORKS		114	0%	0%	23-May-26	06-Oct-26	18-Mar-26 A	11-Jul-26 A	0.00	0.00	0.00	74
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	21	100%	100%	07-Sep-26	01-Oct-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	70
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	21	100%	100%	05-Sep-26	29-Sep-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	68
MLTX-02-005-EN	Shop DWG Approval for HVAC Equipment Schedule	21	100%	100%	05-Sep-26	29-Sep-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	68
MLTX-02-005-EN	Shop DWG Approval for Fire Fighting Layout	21	100%	100%	23-May-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Shop DWG Approval for Water Supply Layout	21	100%	100%	05-Sep-26	29-Sep-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Shop DWG Approval for Water Supply Details	21	100%	100%	05-Sep-26	29-Sep-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Shop DWG Approval for Drainage Layout	21	100%	100%	12-Sep-26	06-Oct-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	106
MLTX-02-005-EN	Shop DWG Approval for Drainage Details	21	100%	100%	05-Sep-26	29-Sep-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN	Shop DWG Approval for Duct Routing Layout	21	100%	100%	05-Sep-26	29-Sep-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	68
MLTX-02-005-EN	Shop DWG Approval for Diffusers Layout	21	100%	100%	05-Sep-26	29-Sep-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	68
ELECTRICAL WORKS		108	0%	0%	16-May-26	21-Sep-26	18-Mar-26 A	28-Jul-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
MLTX-02-005-EN	Shop DWG Approval for Power Layout	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	21	100%	100%	18-Aug-26	10-Sep-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	105
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	21	100%	100%	18-Aug-26	10-Sep-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	105
MLTX-02-005-EN	Shop DWG Approval for Lighting Installation Details	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
MLTX-02-005-EN	Shop DWG Approval for Cable Tray Installation Details	21	100%	100%	18-Aug-26	10-Sep-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	105
MLTX-02-005-EN	Shop DWG Approval for Manhole & Ductbank Details	21	100%	100%	16-May-26	11-Jun-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Grounding Details	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Lightning Protection Details	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
MLTX-02-005-EN	Shop DWG Approval for Fire Alarm Installation Details	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for CCTV Details	30	100%	100%	11-Aug-26	14-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	41
MLTX-02-005-EN	Shop DWG Approval for Grounding Layout	21	100%	100%	11-Aug-26	03-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	128
MLTX-02-005-EN	Shop DWG Approval for Lightning Protection System Layout	21	100%	100%	06-Jun-26	29-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	71
MLTX-02-005-EN	Shop DWG Approval for Fire Alarm Layout	21	100%	100%	06-Jun-26	29-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	71
MLTX-02-005-EN	Shop DWG Approval for Fire Alarm Riser Diagram	21	100%	100%	06-Jun-26	29-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	71
MLTX-02-005-EN	Shop DWG Approval for CCTV Layout	30	100%	100%	11-Aug-26	14-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	137
MLTX-02-005-EN	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	18-Aug-26	21-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	143
MLTX-02-005-EN	Shop DWG Approval for Telephone & Data Layout	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
MLTX-02-005-EN	Shop DWG Approval for Telephone & Data Riser Diagram	21	100%	100%	18-Aug-26	10-Sep-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	134
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		238	0%	0%	30-Mar-26	20-Sep-26	14-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-40
ARCHITECTURE WORKS		128	0%	0%	30-Mar-26	29-Aug-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	84
MLTX-02-005-EN	Shop DWG Approval for Playground Plan/Layout	15	100%	100%	30-Mar-26	15-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Shop DWG Approval for Furniture & Marking	30	100%	100%	26-Jul-26	29-Aug-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	84
MLTX-02-005-EN	Shop DWG Approval for Sections	15	100%	100%	30-Mar-26	15-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Shop DWG Approval for Interlock Pattern Plan	21	100%	100%	03-Aug-26	26-Aug-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	82

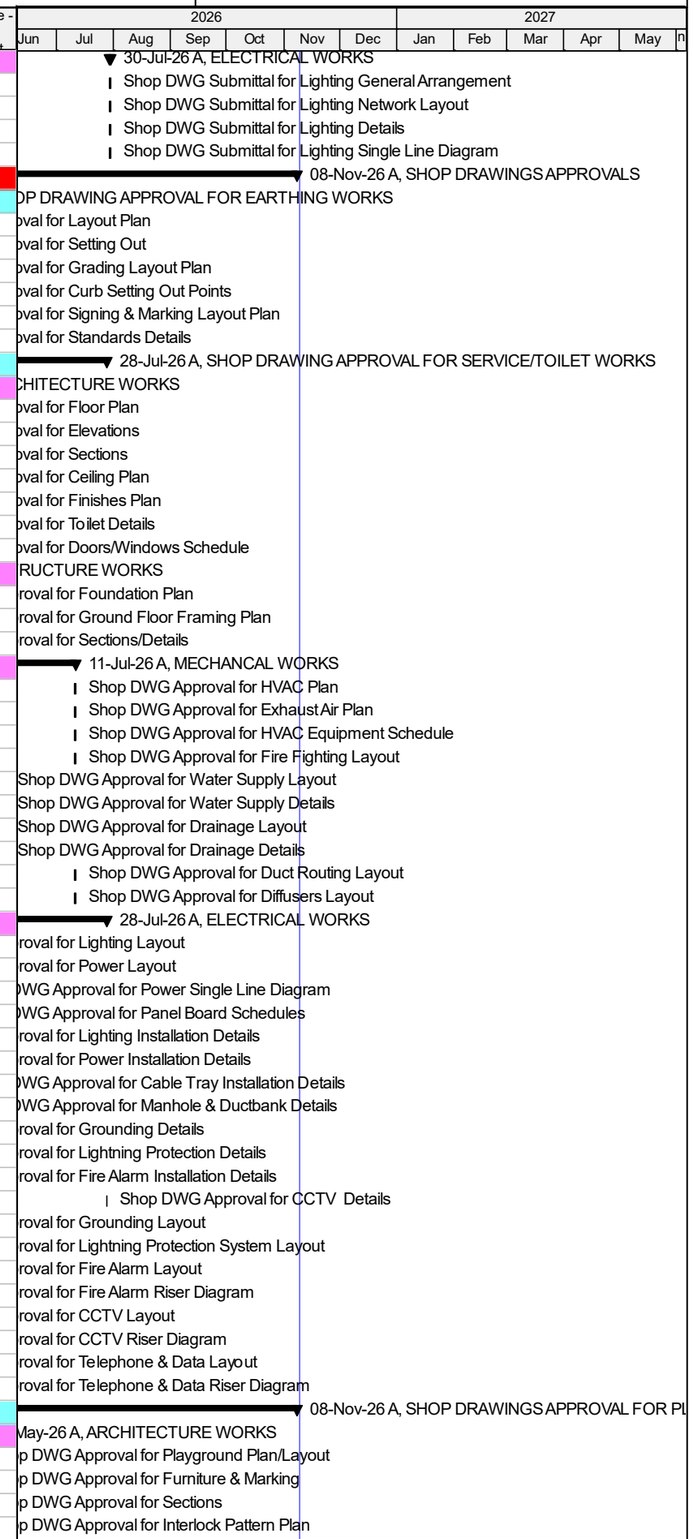

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Approval for Doors/Windows Schedule	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EN	Shop DWG Approval for Dome Internal Layout	21	100%	100%	30-Apr-26	24-May-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	4
STRUCTURE WORKS		21	0%	0%	27-Aug-26	20-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Air Dome System	21	100%	100%	27-Aug-26	20-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	27-Aug-26	20-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	27-Aug-26	20-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Anchor Bolt Layout of Air Dome	21	100%	100%	27-Aug-26	20-Sep-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	56
AIR DOME SYSTEM		60	0%	0%	30-Apr-26	12-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Approval for Air Dome Structural Layout	15	100%	100%	30-Apr-26	17-May-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-133
MLTX-02-005-EN	Shop DWG Approval for Membrane Panel Layout	15	100%	100%	18-May-26	07-Jun-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-118
MLTX-02-005-EN	Shop DWG Approval for Cable Tension Layout	15	100%	100%	18-May-26	07-Jun-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-118
MLTX-02-005-EN	Shop DWG Approval for Airlock Door Details	15	100%	100%	08-Jun-26	24-Jun-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-103
MLTX-02-005-EN	Shop DWG Approval for Emergency Exit Details	15	100%	100%	25-Jun-26	12-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-88
SPORTS EQUIPMENT		157	0%	0%	25-May-26	01-Jul-26	20-Jul-26 A	24-Oct-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EN	Shop DWG Approval for Football Turf Installation	30	100%	100%	25-May-26	01-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EN	Shop DWG Approval for Basketball Court Marking	21	100%	100%	25-May-26	21-Jun-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Shop DWG Approval for Padel Court Structure	21	100%	100%	25-May-26	21-Jun-26	20-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	-25
MECHANCAL WORKS		40	0%	0%	18-May-26	06-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-93
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	25	100%	100%	18-May-26	18-Jun-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-108
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	15	100%	100%	20-Jun-26	06-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-93
ELECTRICAL WORKS		211	0%	0%	30-Apr-26	10-Sep-26	19-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	-48
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	21	100%	100%	30-Apr-26	24-May-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Shop DWG Approval for Power Layout	25	100%	100%	02-Jul-26	30-Jul-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-84
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	25	100%	100%	27-Jun-26	25-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-77
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	25	100%	100%	27-Jun-26	25-Jul-26	24-Oct-26 A	24-Oct-26 A	0.00	0.00	0.00	-77
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	15	100%	100%	16-Jul-26	02-Aug-26	08-Nov-26 A	08-Nov-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EN	Shop DWG Approval for CCTV Details	21	100%	100%	22-Jun-26	15-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Shop DWG Approval for CCTV Layout	21	100%	100%	18-Aug-26	10-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN	Shop DWG Approval for CCTV Riser Diagram	21	100%	100%	18-Aug-26	10-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	14
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		148	0%	0%	30-Mar-26	21-Sep-26	14-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	45
ARCHITECTURE WORKS		51	0%	0%	30-Mar-26	31-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Shop DWG Approval for Landscape Layout	21	100%	100%	23-Apr-26	17-May-26	14-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	28
MLTX-02-005-EN	Shop DWG Approval for Hardscape Plan	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Planting Plan	15	100%	100%	11-May-26	31-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Shop DWG Approval for Landscape Details	21	100%	100%	30-Mar-26	22-Apr-26	14-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	7
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-76
MLTX-02-005-EN	Shop DWG Approval for Irrigation Details	21	100%	100%	06-Apr-26	29-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-76
MLTX-02-005-EN	Shop DWG Approval for Irrigation Layout	21	100%	100%	06-Apr-26	29-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-76
ELECTRICAL WORKS		50	0%	0%	26-Jul-26	21-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN	Shop DWG Approval for Lighting General Arrangement	30	100%	100%	18-Aug-26	21-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN	Shop DWG Approval for Lighting Network Layout	30	100%	100%	26-Jul-26	29-Aug-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Shop DWG Approval for Lighting Details	30	100%	100%	01-Aug-26	03-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Lighting Single Line Diagram	30	100%	100%	01-Aug-26	03-Sep-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	30
METHOD STATEMENTS		232	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	77
METHOD STATEMENT SUBMITTAL		197	0%	0%	09-Mar-26	01-Nov-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	127
CIVIL WORKS		42	0%	0%	09-Mar-26	29-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Concrete	21	100%	100%	06-Apr-26	29-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
ARCHITECTURE WORKS		197	0%	0%	09-Mar-26	01-Nov-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	129
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Plastering	15	100%	100%	23-Jul-26	09-Aug-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	121
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	30-Apr-26	24-May-26	08-Mar-26 A	17-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Tilling	21	100%	100%	26-Jul-26	18-Aug-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	70
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	19-Aug-26	12-Sep-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	08-Oct-26	01-Nov-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	129
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	29-Jun-26	22-Jul-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Parking	21	100%	100%	10-Aug-26	02-Sep-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	83
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Soft	21	100%	100%	29-Jun-26	22-Jul-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	43
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Fence	30	100%	100%	09-Mar-26	15-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Air Dome	30	100%	100%	21-May-26	28-Jun-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Metal	21	100%	100%	29-Jun-26	22-Jul-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	43
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Partitions	21	100%	100%	29-Jun-26	22-Jul-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	43
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Gypsum	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MECHANICAL WORKS		85	0%	0%	25-Jul-26	01-Nov-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	127

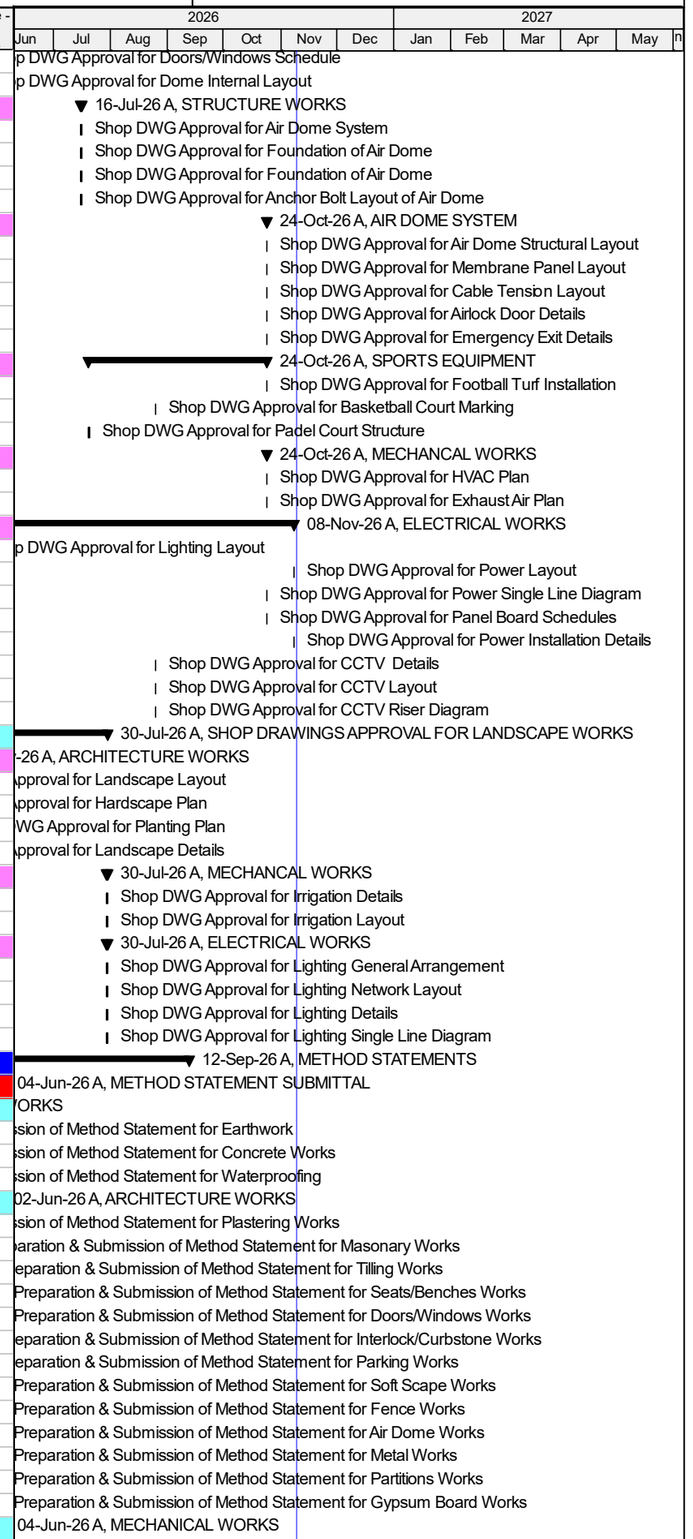

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	03-Aug-26	26-Aug-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	95
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Water	21	100%	100%	25-Jul-26	17-Aug-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Fire	21	100%	100%	08-Oct-26	01-Nov-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	127
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Irrigation	15	100%	100%	08-Oct-26	25-Oct-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	121
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for HVAC	21	100%	100%	13-Sep-26	07-Oct-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	106
ELECTRICAL WORKS		120	0%	0%	06-Apr-26	26-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	89
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Electrical	21	100%	100%	03-Aug-26	26-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	89
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Lighting	21	100%	100%	23-Jul-26	16-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	30	100%	100%	16-Apr-26	20-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for CCTV	30	100%	100%	29-Jun-26	02-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	68
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Lighting	21	100%	100%	23-Jul-26	16-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	23-Jul-26	16-Aug-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	80
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Panel	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-10
METHOD STATEMENT APPROVAL		217	0%	0%	30-Mar-26	12-Dec-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	77
CIVIL WORKS		57	0%	0%	30-Mar-26	07-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	57
MLTX-02-005-EN-1	Approval of Method Statement for Earthwork	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-1	Approval of Method Statement for Concrete Works	30	100%	100%	30-Apr-26	07-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	57
MLTX-02-005-EN-1	Approval of Method Statement for Waterproofing	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	27
ARCHITECTURE WORKS		164	0%	0%	25-May-26	06-Dec-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	72
MLTX-02-005-EN-1	Approval of Method Statement for Plastering Works	30	100%	100%	17-Aug-26	20-Sep-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	147
MLTX-02-005-EN-1	Approval of Method Statement for Masonary Works	21	100%	100%	25-May-26	21-Jun-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN-1	Approval of Method Statement for Tilling Works	21	100%	100%	27-Aug-26	20-Sep-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	101
MLTX-02-005-EN-1	Approval of Method Statement for Seats/Benches Works	21	100%	100%	13-Sep-26	07-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Approval of Method Statement for Doors/Windows Works	21	0%	100%	12-Nov-26	06-Dec-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	72
MLTX-02-005-EN-1	Approval of Method Statement for Interlock/Curbstone Works	21	100%	100%	23-Jul-26	16-Aug-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN-1	Approval of Method Statement for Parking Works	21	100%	100%	10-Sep-26	05-Oct-26	15-May-26 A	15-May-26 A	0.00	0.00	0.00	119
MLTX-02-005-EN-1	Approval of Method Statement for Soft Scape Works	21	62.38%	100%	25-Oct-26	17-Nov-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN-1	Approval of Method Statement for Fence Works	30	90.33%	100%	08-Oct-26	11-Nov-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100
MLTX-02-005-EN-1	Approval of Method Statement for Air Dome Works	30	100%	100%	10-Sep-26	15-Oct-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	81
MLTX-02-005-EN-1	Approval of Method Statement for Partitions Works	21	100%	100%	30-Sep-26	24-Oct-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN-1	Approval of Method Statement for Gypsum Board Works	21	100%	100%	08-Oct-26	01-Nov-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	61
MECHANICAL WORKS		99	0%	0%	18-Aug-26	12-Dec-26	24-Jun-26 A	26-Aug-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN-1	Approval of Method Statement for Sewage/Drainage System	21	100%	100%	10-Sep-26	05-Oct-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN-1	Approval of Method Statement for Water Supply System	21	100%	100%	18-Aug-26	10-Sep-26	12-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN-1	Approval of Method Statement for Fire Fighting System	21	0%	100%	18-Nov-26	12-Dec-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	91
MLTX-02-005-EN-1	Approval of Method Statement for Irrigation System	15	80.67%	100%	26-Oct-26	11-Nov-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN-1	Approval of Method Statement for HVAC System	21	100%	100%	08-Oct-26	01-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	63
ELECTRICAL WORKS		120	0%	0%	30-Apr-26	20-Sep-26	14-Jul-26 A	26-Aug-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Approval of Method Statement for Electrical Conduits/Pulling	21	100%	100%	27-Aug-26	20-Sep-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	58
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Poles Installation	21	100%	100%	17-Aug-26	09-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN-1	Approval of Method Statement for Telecommunication & Data	30	100%	100%	21-May-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN-1	Approval of Method Statement for CCTV System	30	100%	100%	17-Aug-26	20-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Works	21	100%	100%	17-Aug-26	09-Sep-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EN-1	Approval of Method Statement for Earthing/Lightning Works	21	100%	100%	18-Aug-26	10-Sep-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN-1	Approval of Method Statement for Panel Boards Works	21	100%	100%	30-Apr-26	24-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-41
PRE-QUALIFICATION & MATERIAL		180	0%	0%	09-Mar-26	12-Oct-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	25
PRE-QUALIFICATION		150	0%	0%	09-Mar-26	06-Sep-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	78
TOILET/SERVICE WORKS		150	0%	0%	09-Mar-26	06-Sep-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	78
STEEL REINFORCEMENT		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Reinforcement	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Steel Reinforcement	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
READY MIX CONCRETE		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Ready Mixed Concrete	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval of Ready Mixed Concrete	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
CONCRETE BLOCKS		45	0%	0%	09-Mar-26	03-May-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Pre-Qualification Submittal for Concrete Blocks	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	16-Apr-26	03-May-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	35
WATER PROOFING		36	0%	0%	09-Mar-26	22-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Submittal for Water Proofing	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Water Proofing	21	100%	100%	30-Mar-26	22-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
FLOOR/WALL TILES		45	0%	0%	09-Mar-26	03-May-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EN	Pre-Qualification Submittal for Tilling Materials	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Tailling Material	15	100%	100%	16-Apr-26	03-May-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-6
SUSPENDED CEILING		75	0%	0%	09-Mar-26	10-Jun-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65

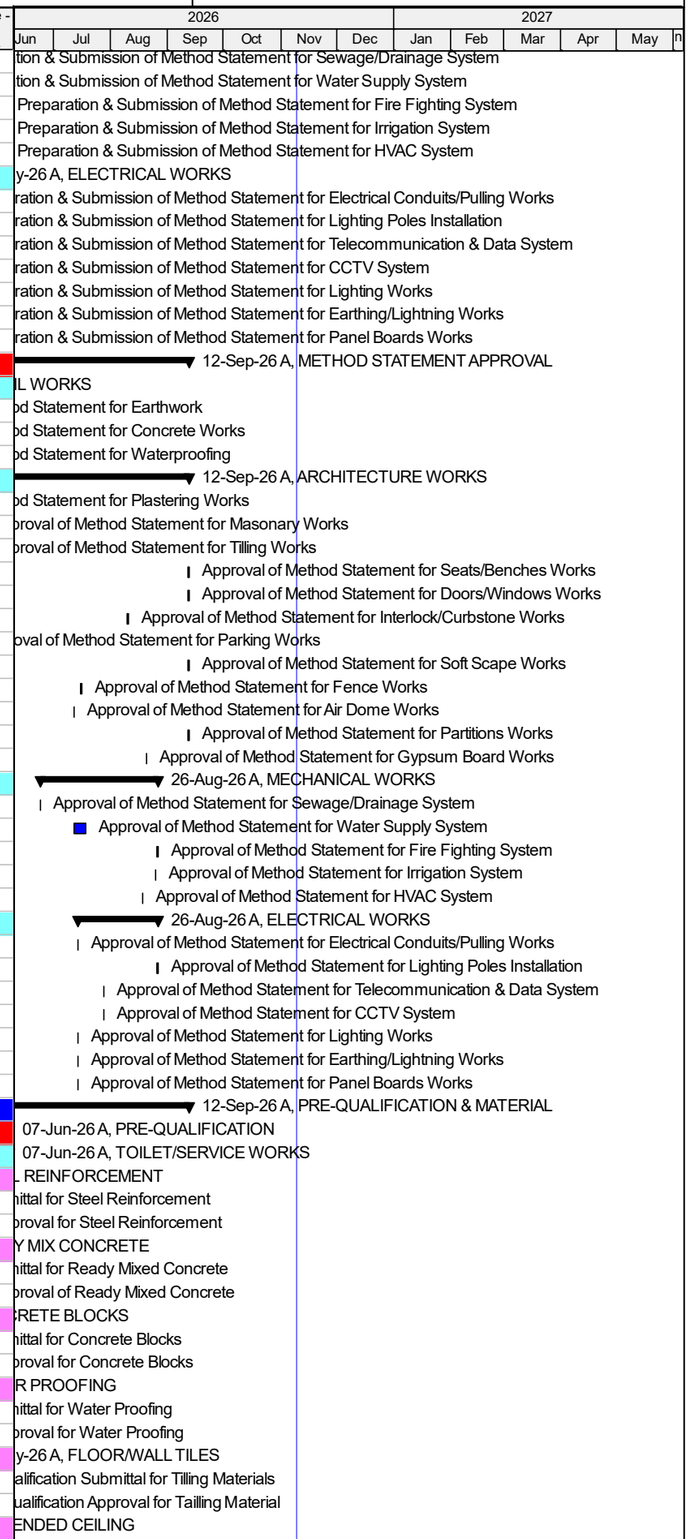

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Suspend Ceiling	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Suspend Ceiling	15	100%	100%	21-May-26	10-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
DOORS/WINDOWS		75	0%	0%	09-Mar-26	10-Jun-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EN	Pre-Qualification Submittal for Doors/Windows	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Doors/Windows	15	100%	100%	21-May-26	10-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
FURNITURES		45	0%	0%	09-Mar-26	03-May-26	08-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Submittal for Furnitures	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	07-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Furnitures	15	100%	100%	16-Apr-26	03-May-26	11-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-8
SANITARY FIXTURES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Submittal for Sanitary Fixtures	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Sanitary Fixtures	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
WATER SUPPLY PIPES		75	0%	0%	09-Mar-26	10-Jun-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Water Supply Pipes	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Pre-Qualification Approval for Water Supply Pipes	15	100%	100%	21-May-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
SEWAGE/DRAINAGE PIPES		120	0%	0%	09-Mar-26	02-Aug-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	48
MLTX-02-005-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	15	100%	100%	16-Jul-26	02-Aug-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	48
PACKAGE AC UNITS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
AIR DIFUSSERS/GRILLS		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Air Diffusers/Grills	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Approval for Air Diffusers/Grills	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
GALVANIZED DUCTS		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Ducts	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Ducts	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	32
EXHAUST FANS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
LIGHTING FIXTURES		39	0%	0%	23-Apr-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting Fixtures	15	100%	100%	23-Apr-26	10-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Pre-Qualification Approval for Lighting Fixtures	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
SWITCHES/SOCKETS		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Switches/Sockets	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Approval for Switches/Sockets	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
EARTHING SYSTEM		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Earthing System	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Earthing System	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
DISTRIBUTION PANNELS		30	0%	0%	03-Aug-26	06-Sep-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	78
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Panels	15	100%	100%	03-Aug-26	19-Aug-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	71
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Panels	15	100%	100%	20-Aug-26	06-Sep-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	78
PLAYGROUND WORKS		90	0%	0%	09-Mar-26	28-Jun-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	18
PVC MEMBRANE		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for PVC Membrane	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for PVC Membrane	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
STEEL TENSION CABLES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Tension Cables	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Steel Tension Cables	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
EMERGENCY DOORS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for Emergency Doors	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Emergency Doors	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
PRESSURE UNITS		42	0%	0%	16-Apr-26	07-Jun-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN	Pre-Qualification Submittal for Pressure Units	15	100%	100%	16-Apr-26	03-May-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EN	Pre-Qualification Approval for Pressure Units	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	9
AIR LOCK DOORS		87	0%	0%	09-Mar-26	24-Jun-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Pre-Qualification Submittal for Lock Doors	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Lock Doors	15	100%	100%	08-Jun-26	24-Jun-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	24
ARTIFICIAL TURF		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Submittal for Artificial TURF	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Artificial TURF	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
RUBBER GRANULES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Rubber Granules	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Rubber Granules	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
PADEL GLASS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22

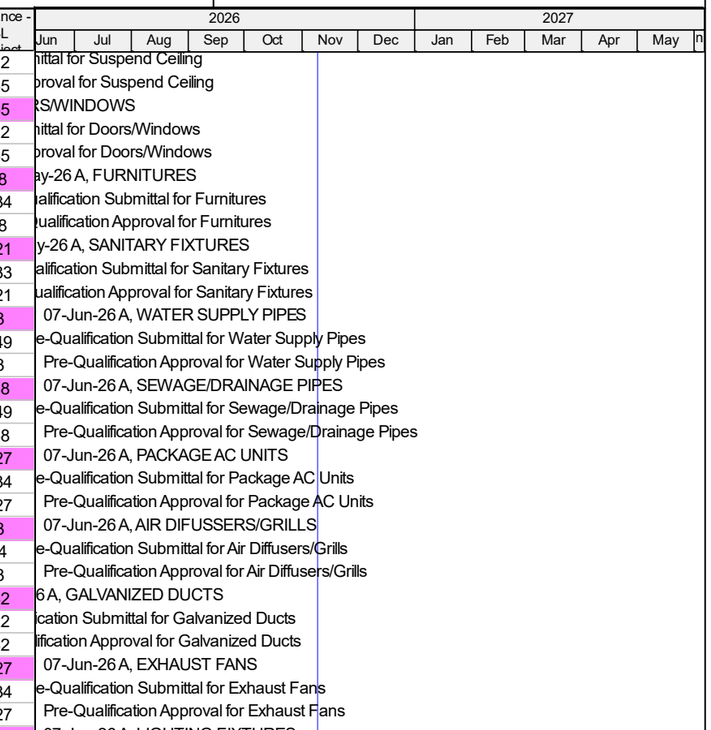

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Padel Glass	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Padel Glass	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
PADEL WIRE MESH/STEEL SETS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Wire Mesh/Steel Sets	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Wire Mesh/Steel Sets	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
AGGREGATE BASE COURSE		30	0%	0%	30-Apr-26	07-Jun-26	08-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	29
MLTX-02-005-EN	Pre-Qualification Submittal for Aggregate Base Course	15	100%	100%	30-Apr-26	17-May-26	08-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Approval for Aggregate Base Course	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	29
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
MLTX-02-005-EN	Pre-Qualification Submittal for Bituminous Base & Wearing	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Pre-Qualification Approval for the Site	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
INTERLOCKING PAVING		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	04-May-26 A	0.00	0.00	0.00	29
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	17
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	04-May-26 A	0.00	0.00	0.00	29
MARKING PAINT		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Pre-Qualification Submittal for Marking Paint	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EN	Pre-Qualification Approval for Marking Paint	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
PACKAGE AC UNITS		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
AIR DIFUSSERS/GRILLS		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Pre-Qualification Submittal for Air Difussers/Grills	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Pre-Qualification Approval for Air Difussers/Grills	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	15
GALVANIZED DUCTS		30	0%	0%	21-May-26	28-Jun-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	47
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Duct	15	100%	100%	21-May-26	10-Jun-26	11-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Duct	15	100%	100%	11-Jun-26	28-Jun-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	47
EXHAUST FANS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
DISTRIBUTION BOARDS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Boards	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Boards	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
POWER CABLES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Power Cables	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Power Cables	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
LIGHT FIXTURES		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Light Fixtures	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Approval for Light Fixtures	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
CCTV MATERIALS		30	0%	0%	04-May-26	10-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for CCTV	15	100%	100%	04-May-26	20-May-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Approval for CCTV	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	3
POWER OUTLETS/SWITCHES		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Pre-Qualification Submittal for Power Outlets/Switches	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Pre-Qualification Approval for Power Outlets/Switches	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	15
LANDSCAPE WORKS		33	0%	0%	18-May-26	28-Jun-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	29
INTERLOCKING PAVING		30	0%	0%	18-May-26	24-Jun-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	76
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	18-May-26	07-Jun-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	08-Jun-26	24-Jun-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	76
CURBSTONE		30	0%	0%	18-May-26	24-Jun-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	76
MLTX-02-005-EN	Pre-Qualification Submittal for Curbstone	15	100%	100%	18-May-26	07-Jun-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	66
MLTX-02-005-EN	Pre-Qualification Approval for Curbstone	15	100%	100%	08-Jun-26	24-Jun-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	76
PAVEMENT MARKING		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN	Pre-Qualification Submittal for Pavement Markings	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Pre-Qualification Approval for Pavement Markings	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	37
TRAFFIC SIGNS		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	37
MLTX-02-005-EN	Pre-Qualification Submittal for Traffic Signs	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Pre-Qualification Approval for Traffic Signs	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	37
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
AGRICULTURE SOIL		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Submittal for Agriculture Soil	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Agriculture Soil	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
TRACK SURFACE		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26

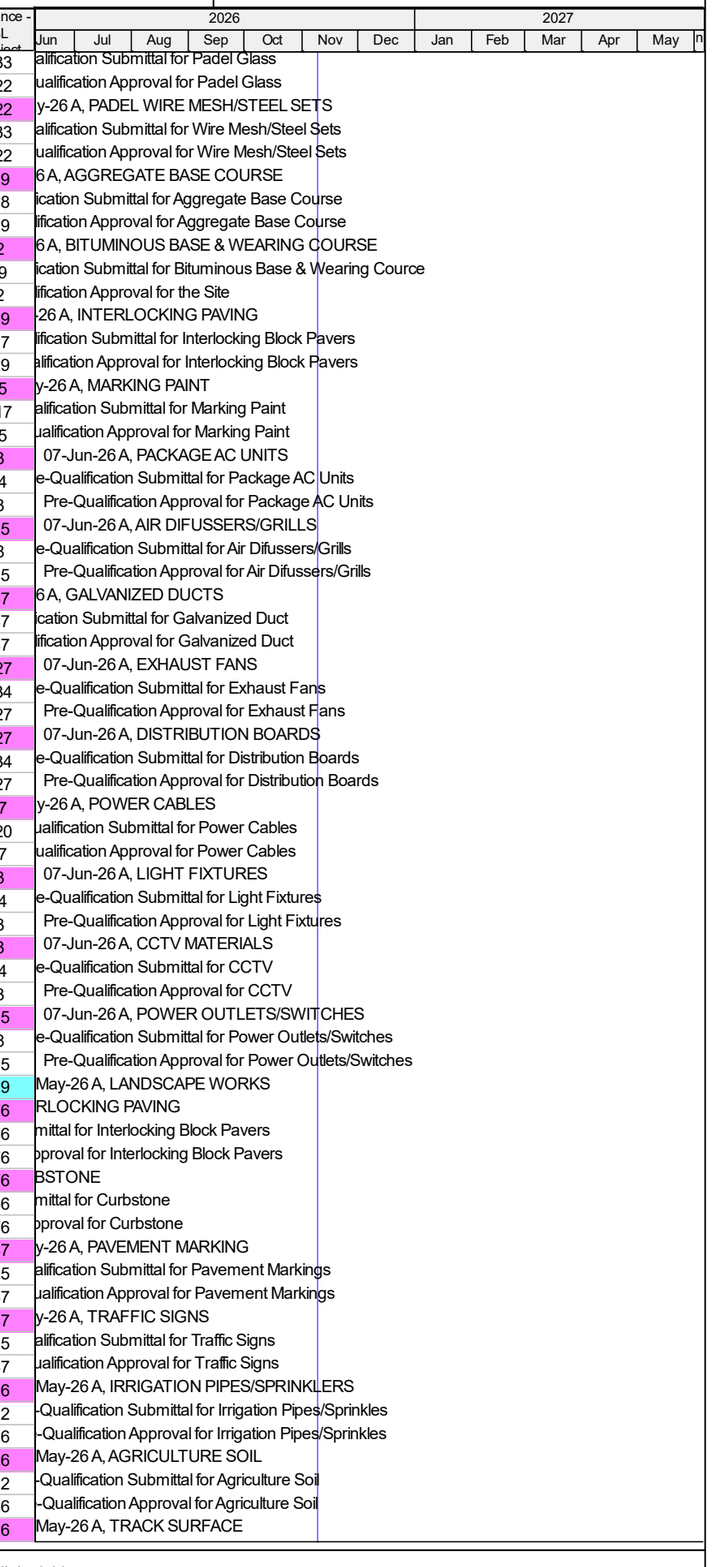

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Track Surface	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Track Surface	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
GRASS/TREES		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Submittal for Grass/Trees	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Grass/Trees	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	26
CABLES		30	0%	0%	18-May-26	24-Jun-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Pre-Qualification Submittal for Cables	15	100%	100%	18-May-26	07-Jun-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Pre-Qualification Approval for Cables	15	100%	100%	08-Jun-26	24-Jun-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	35
LIGHT POLES		30	0%	0%	21-May-26	28-Jun-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting poles	15	100%	100%	21-May-26	10-Jun-26	11-Mar-26 A	17-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Approval for Lighting poles	15	100%	100%	11-Jun-26	28-Jun-26	15-Mar-26 A	20-May-26 A	0.00	0.00	0.00	30
MATERIAL SUBMITTAL		150	0%	0%	16-Apr-26	12-Oct-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	25
TOILET/SERVICE WORKS		150	0%	0%	16-Apr-26	12-Oct-26	19-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	62
STEEL REINFORCEMENT		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Material Submittal for Steel Reinforcement	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Material Approval for Steel Reinforcement	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
READY MIX CONCRETE		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Material Submittal for Ready Mixed Concrete	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Material Approval of Ready Mixed Concrete	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
CONCRETE BLOCKS		30	0%	0%	04-May-26	10-Jun-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Material Submittal for Concrete Blocks	15	100%	100%	04-May-26	20-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Material Approval for Concrete Blocks	15	100%	100%	21-May-26	10-Jun-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	23
FLOOR/WALL TILES		30	0%	0%	04-May-26	10-Jun-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Material Submittal for Tilling Materials	15	100%	100%	04-May-26	20-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN	Material Approval for Tilling Material	15	100%	100%	21-May-26	10-Jun-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	18
SUSPENDED CEILING		30	0%	0%	11-Jun-26	15-Jul-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Material Submittal for Suspend Ceiling	15	100%	100%	11-Jun-26	28-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Approval for Suspend Ceiling	15	100%	100%	29-Jun-26	15-Jul-26	26-Mar-26 A	13-May-26 A	0.00	0.00	0.00	51
DOORS/WINDOWS		30	0%	0%	11-Jun-26	15-Jul-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	52
MLTX-02-005-EN	Material Submittal for Doors/Windows	15	100%	100%	11-Jun-26	28-Jun-26	19-Mar-26 A	07-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EN	Material Approval for Doors/Windows	15	100%	100%	29-Jun-26	15-Jul-26	26-Mar-26 A	12-May-26 A	0.00	0.00	0.00	52
FURNITURES		30	0%	0%	04-May-26	10-Jun-26	19-Mar-26 A	20-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Material Submittal for Furnitures	15	100%	100%	04-May-26	20-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Material Approval for Furnitures	15	100%	100%	21-May-26	10-Jun-26	26-Mar-26 A	20-May-26 A	0.00	0.00	0.00	15
SANITARY FIXTURES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN	Material Submittal for Sanitary Fixtures	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Material Approval for Sanitary Fixtures	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
WATER SUPPLY PIPES		30	0%	0%	11-Jun-26	15-Jul-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	53
MLTX-02-005-EN	Material Submittal for Water Supply Pipes	15	100%	100%	11-Jun-26	28-Jun-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	42
MLTX-02-005-EN	Material Approval for Water Supply Pipes	15	100%	100%	29-Jun-26	15-Jul-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	53
SEWAGE/DRAINAGE PIPES		30	0%	0%	03-Aug-26	06-Sep-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	98
MLTX-02-005-EN	Material Submittal for Sewage/Drainage Pipes	15	100%	100%	03-Aug-26	19-Aug-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	87
MLTX-02-005-EN	Material Approval for Sewage/Drainage Pipes	15	100%	100%	20-Aug-26	06-Sep-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	98
PACKAGE AC UNITS		30	0%	0%	04-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EN	Material Submittal for Package AC Units	15	100%	100%	04-May-26	20-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Material Approval for Package AC Units	15	100%	100%	21-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
AIR DIFUSSERS/GRILLS		30	0%	0%	11-Jun-26	15-Jul-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Material Submittal for Air Diffusers/Grills	15	100%	100%	11-Jun-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN	Material Approval for Air Diffusers/Grills	15	100%	100%	29-Jun-26	15-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
GALVANIZED DUCTS		30	0%	0%	11-Jun-26	15-Jul-26	24-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Material Submittal for Galvanized Ducts	15	100%	100%	11-Jun-26	28-Jun-26	24-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	52
MLTX-02-005-EN	Material Approval for Galvanized Ducts	15	100%	100%	29-Jun-26	15-Jul-26	28-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	62
EXHAUST FANS		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Material Submittal for Exhaust Fans	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Material Approval for Exhaust Fans	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
LIGHTING FIXTURES		30	0%	0%	11-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN	Material Submittal for Lighting Fixtures	15	100%	100%	11-Jun-26	28-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Material Approval for Lighting Fixtures	15	100%	100%	29-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
SWITCHES/SOCKETS		30	0%	0%	11-Jun-26	15-Jul-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Material Submittal for Switches/Sockets	15	100%	100%	11-Jun-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN	Material Approval for Switches/Sockets	15	100%	100%	29-Jun-26	15-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
EARTHING SYSTEM		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EN	Material Submittal for Earthing System	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Material Approval for Earthing System	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17




© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
DISTRIBUTION PANNELS		30	0%	0%	07-Sep-26	12-Oct-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	62
MLTX-02-005-EM	Material Submittal for Distribution Panels	15	100%	100%	07-Sep-26	24-Sep-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	49
MLTX-02-005-EM	Material Approval for Distribution Panels	15	100%	100%	26-Sep-26	12-Oct-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	62
PLAYGROUND WORKS		90	0%	0%	16-Apr-26	02-Aug-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-35
PVC MEMBRANE		30	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for PVC Membrane	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for PVC Membrane	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
STEEL TENSION CABLES		30	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for Steel Tension Cables	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Steel Tension Cables	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
EMERGENCY DOORS		30	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Submittal for Emergency Doors	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Emergency Doors	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
PRESSURE UNITS		30	0%	0%	11-Jun-26	15-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-50
MLTX-02-005-EM	Material Submittal for Pressure Units	15	100%	100%	11-Jun-26	28-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-65
MLTX-02-005-EM	Material Approval for Pressure Units	15	100%	100%	29-Jun-26	15-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-50
AIR LOCK DOORS		30	0%	0%	25-Jun-26	29-Jul-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EM	Material Submittal for Lock Doors	15	100%	100%	25-Jun-26	12-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Material Approval for Lock Doors	15	100%	100%	13-Jul-26	29-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-38
ARTIFICIAL TURF		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Artificial TURF	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Artificial TURF	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
RUBBER GRANULES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Rubber Granules	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Rubber Granules	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
PADEL GLASS		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Padel Glass	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Padel Glass	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
PADEL WIRE MESH/STEEL SETS		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Wire Mesh/Steel Sets	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Wire Mesh/Steel Sets	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
AGGREGATE BASE COURSE		30	0%	0%	08-Jun-26	12-Jul-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Material Submittal for Aggregate Base Course	15	100%	100%	08-Jun-26	24-Jun-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Material Approval for Aggregate Base Course	15	100%	100%	25-Jun-26	12-Jul-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	51
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	10-May-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Material Submittal for Bituminous Base & Wearing Cource	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	05-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Material Approval for the Site	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	10-May-26 A	0.00	0.00	0.00	24
INTERLOCKING PAVING		30	0%	0%	11-Jun-26	15-Jul-26	24-Mar-26 A	13-May-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	11-Jun-26	28-Jun-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	41
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	29-Jun-26	15-Jul-26	28-Mar-26 A	13-May-26 A	0.00	0.00	0.00	51
MARKING PAINT		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Submittal for Marking Paint	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Approval for Marking Paint	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
PACKAGE AC UNITS		30	0%	0%	11-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	11-Jun-26	28-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	29-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
AIR DIFUSSERS/GRILLS		30	0%	0%	25-Jun-26	29-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EM	Material Submittal for Air Difussers/Grills	15	100%	100%	25-Jun-26	12-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-53
MLTX-02-005-EM	Material Approval for Air Difussers/Grills	15	100%	100%	13-Jul-26	29-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-38
GALVANIZED DUCTS		30	0%	0%	29-Jun-26	02-Aug-26	24-Mar-26 A	10-May-26 A	0.00	0.00	0.00	69
MLTX-02-005-EM	Material Submittal for Galvanized Duct	15	100%	100%	29-Jun-26	15-Jul-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	57
MLTX-02-005-EM	Material Approval for Galvanized Duct	15	100%	100%	16-Jul-26	02-Aug-26	28-Mar-26 A	10-May-26 A	0.00	0.00	0.00	69
EXHAUST FANS		30	0%	0%	04-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	21-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
DISTRIBUTION BOARDS		30	0%	0%	04-May-26	10-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-66
MLTX-02-005-EM	Material Submittal for Distribution Boards	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Approval for Distribution Boards	15	100%	100%	21-May-26	10-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-66
POWER CABLES		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Power Cables	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EM	Material Approval for Power Cables	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	16
LIGHT FIXTURES		30	0%	0%	11-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Submittal for Light Fixtures	15	100%	100%	11-Jun-26	28-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EM	Material Approval for Light Fixtures	15	100%	100%	29-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7

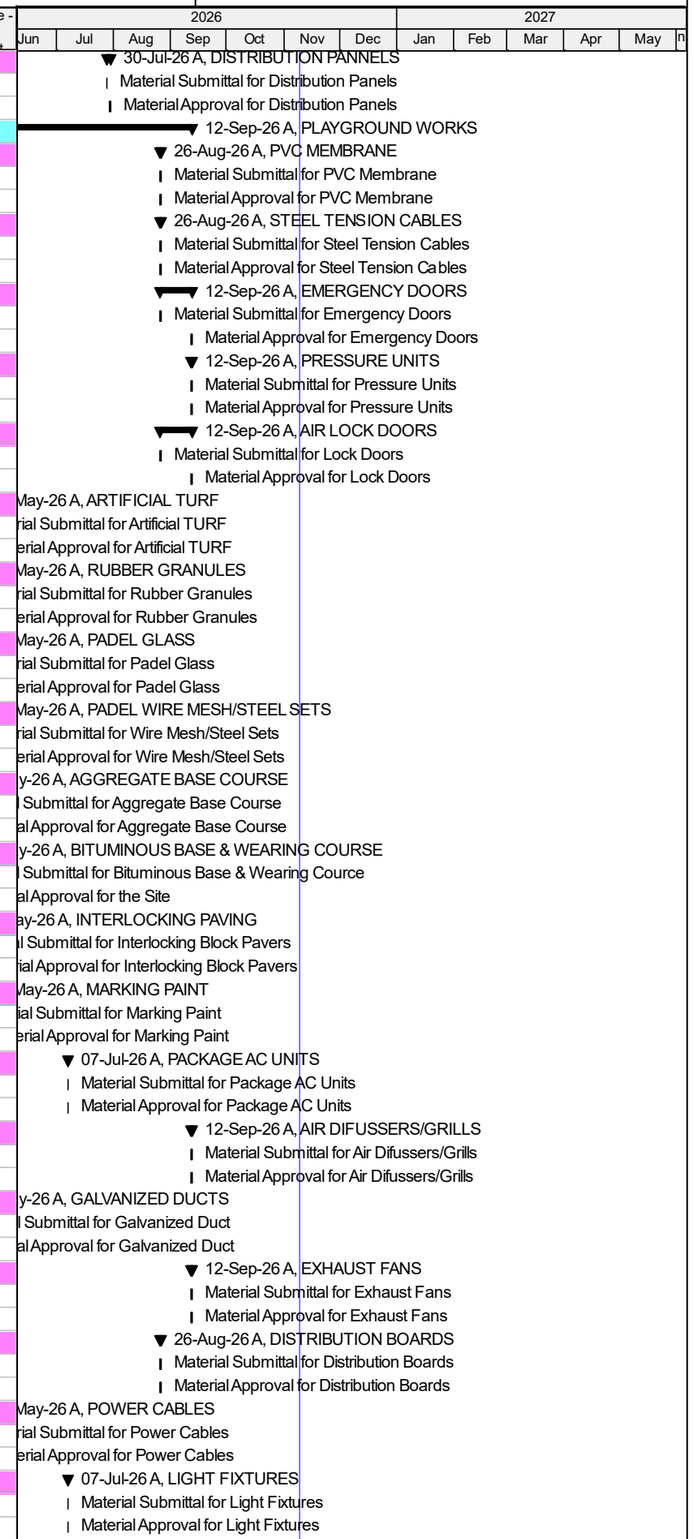

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CCTV MATERIALS		30	0%	0%	11-Jun-26	15-Jul-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-50
MLTX-02-005-EM	Material Submittal for CCTV	15	100%	100%	11-Jun-26	28-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-51
MLTX-02-005-EM	Material Approval for CCTV	15	100%	100%	29-Jun-26	15-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-50
POWER OUTLETS/SWITCHES		30	0%	0%	25-Jun-26	29-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EM	Material Submittal for Power Outlets/Switches	15	100%	100%	25-Jun-26	12-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-53
MLTX-02-005-EM	Material Approval for Power Outlets/Switches	15	100%	100%	13-Jul-26	29-Jul-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-38
LANDSCAPE WORKS		33	0%	0%	25-Jun-26	02-Aug-26	24-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	2
INTERLOCKING PAVING		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	13-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	53
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	13-May-26 A	0.00	0.00	0.00	63
CURBSTONE		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	13-May-26 A	0.00	0.00	0.00	63
MLTX-02-005-EM	Material Submittal for Curbstone	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	53
MLTX-02-005-EM	Material Approval for Curbstone	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	13-May-26 A	0.00	0.00	0.00	63
PAVEMENT MARKING		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	59
MLTX-02-005-EM	Material Submittal for Pavement Markings	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	49
MLTX-02-005-EM	Material Approval for Pavement Markings	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	59
TRAFFIC SIGNS		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	59
MLTX-02-005-EM	Material Submittal for Traffic Signs	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	49
MLTX-02-005-EM	Material Approval for Traffic Signs	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	59
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	25-Jun-26	29-Jul-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EM	Material Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	25-Jun-26	12-Jul-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EM	Material Approval for Irrigation Pipes/Sprinkles	15	100%	100%	13-Jul-26	29-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-1
AGRICULTURE SOIL		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	56
MLTX-02-005-EM	Material Submittal for Agriculture Soil	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	46
MLTX-02-005-EM	Material Approval for Agriculture Soil	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	56
TRACK SURFACE		33	0%	0%	25-Jun-26	02-Aug-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	2
MLTX-02-005-EM	Material Submittal for Track Surface	15	100%	100%	25-Jun-26	12-Jul-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EM	Material Approval for Track Surface	15	100%	100%	16-Jul-26	02-Aug-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	2
GRASS/TREES		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	56
MLTX-02-005-EM	Material Submittal for Grass/Trees	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	46
MLTX-02-005-EM	Material Approval for Grass/Trees	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	56
CABLES		30	0%	0%	25-Jun-26	29-Jul-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	58
MLTX-02-005-EM	Material Submittal for Cables	15	100%	100%	25-Jun-26	12-Jul-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	47
MLTX-02-005-EM	Material Approval for Cables	15	100%	100%	13-Jul-26	29-Jul-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	58
LIGHT POLES		30	0%	0%	29-Jun-26	02-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	22
MLTX-02-005-EM	Material Submittal for Lighting poles	15	100%	100%	29-Jun-26	15-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Approval for Lighting poles	15	100%	100%	16-Jul-26	02-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	22
PROCUREMENT		251	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	04-Jan-27	0.00	0.00	0.00	-11
SHORT LEAD ITEM		251	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	04-Jan-27	0.00	0.00	0.00	-11
TOILET/SERVICE WORKS		179	0%	0%	21-May-26	28-Nov-26	04-Apr-26 A	09-Nov-26 A	0.00	0.00	0.00	17
STEEL REINFORCEMENT		30	0%	0%	21-May-26	28-Jun-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	31
MLTX-02-005-PR-1	PO for Steel Reinforcement	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	18-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Material Delivery of Steel Reinforcement	5	100%	100%	23-Jun-26	28-Jun-26	09-Apr-26 A	19-May-26 A	0.00	0.00	0.00	31
CONCRETE BLOCKS		18	0%	0%	11-Jun-26	01-Jul-26	09-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-5
MLTX-02-005-PR-1	PO for Concrete Blocks	5	100%	100%	11-Jun-26	16-Jun-26	09-Apr-26 A	18-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-PR-1	Material Delivery of Concrete Blocks	8	100%	100%	23-Jun-26	01-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-5
FLOOR/WALL TILES		93	0%	0%	17-Jun-26	04-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	39
MLTX-02-005-PR-1	PO for Tilling Materials	5	100%	100%	17-Jun-26	22-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-49
MLTX-02-005-PR-1	Material Delivery of Tailling Material	13	100%	100%	19-Sep-26	04-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	39
SUSPENDED CEILING		18	0%	0%	19-Oct-26	08-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	69
MLTX-02-005-PR-1	PO for Suspend Ceiling	5	100%	100%	19-Oct-26	24-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	56
MLTX-02-005-PR-1	Material Delivery of Suspend Ceiling	13	100%	100%	25-Oct-26	08-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	69
DOORS/WINDOWS		40	0%	0%	03-Aug-26	17-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	2
MLTX-02-005-PR-1	PO for Doors/Windows	15	100%	100%	03-Aug-26	19-Aug-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	Material Delivery for Doors/Windows	25	100%	100%	20-Aug-26	17-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	2
WATER SUPPLY PIPES		12	0%	0%	19-Sep-26	03-Oct-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	74
MLTX-02-005-PR-1	PO for Water Supply Pipes	5	100%	100%	19-Sep-26	24-Sep-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	67
MLTX-02-005-PR-1	Material Delivery for Water Supply Pipes	7	100%	100%	26-Sep-26	03-Oct-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	74
SEWAGE/DRAINAGE PIPES		17	0%	0%	19-Sep-26	08-Oct-26	02-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	102
MLTX-02-005-PR-1	PO for Sewage/Drainage Pipes	5	100%	100%	19-Sep-26	24-Sep-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	97
MLTX-02-005-PR-1	Material Delivery for Sewage/Drainage Pipes	7	100%	100%	01-Oct-26	08-Oct-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	102
SANITARY FIXTURES		18	0%	0%	26-Sep-26	15-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	49
MLTX-02-005-PR-1	PO for Sanitary Fixtures	5	100%	100%	26-Sep-26	30-Sep-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	36
MLTX-02-005-PR-1	Material Delivery for Sanitary Fixtures	13	100%	100%	01-Oct-26	15-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	49



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PACKAGE AC UNITS		49	0%	0%	11-Jun-26	06-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	26
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	11-Jun-26	16-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-18
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	100%	100%	21-Jul-26	06-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	26
AIR DIFUSSERS/GRILLS		20	0%	0%	17-Oct-26	08-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	69
MLTX-02-005-PR-1	PO for Air Diffusers/Grills	5	100%	100%	17-Oct-26	21-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	54
MLTX-02-005-PR-1	Material Delivery for Air Diffusers/Grills	15	100%	100%	22-Oct-26	08-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	69
GALVANIZED DUCTS		20	0%	0%	25-Oct-26	16-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	76
MLTX-02-005-PR-1	PO for Galvanized Ducts	5	100%	100%	25-Oct-26	29-Oct-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	61
MLTX-02-005-PR-1	Material Delivery for Galvanized Ducts	15	54%	100%	31-Oct-26	16-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	76
EXHAUST FANS		125	0%	0%	11-Jun-26	04-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	66
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	100%	11-Jun-26	16-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-54
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	10	100%	100%	25-Oct-26	04-Nov-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	66
LIGHTING FIXTURES		133	0%	0%	16-Jul-26	02-Aug-26	07-Jul-26 A	03-Nov-26 A	0.00	0.00	0.00	-78
MLTX-02-005-PR-1	PO for Lighting Fixtures	5	100%	100%	16-Jul-26	21-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	12
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	100%	22-Jul-26	02-Aug-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	-78
SWITCHES/SOCKETS		12	0%	0%	22-Jul-26	04-Aug-26	31-Oct-26 A	31-Oct-26 A	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	100%	22-Jul-26	27-Jul-26	31-Oct-26 A	31-Oct-26 A	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	100%	28-Jul-26	04-Aug-26	31-Oct-26 A	31-Oct-26 A	0.00	0.00	0.00	-73
EARTHING SYSTEM		20	0%	0%	11-Jun-26	04-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-005-PR-1	PO for Earthing System	5	100%	100%	11-Jun-26	16-Jun-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Earthing System	15	100%	100%	17-Jun-26	04-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-7
DISTRIBUTION PANNELS		40	0%	0%	13-Oct-26	28-Nov-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	22
MLTX-02-005-PR-1	PO for Distribution Panels	15	100%	100%	13-Oct-26	29-Oct-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	25	32.4%	100%	31-Oct-26	28-Nov-26	03-Nov-26 A	03-Nov-26 A	0.00	0.00	0.00	22
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Furnitures	9	100%	100%	17-Jun-26	27-Jun-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	100%	28-Jun-26	20-Jul-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-94
PLAYGROUND WORKS		251	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	04-Jan-27	0.00	0.00	0.00	-11
PVC MEMBRANE		188	0%	0%	23-Apr-26	17-Jun-26	04-Apr-26 A	03-Dec-26	0.00	0.00	0.00	-143
MLTX-02-005-PR-1	PO for PVC Membrane	10	100%	100%	23-Apr-26	04-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	-13
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	09-Nov-26	03-Dec-26	0.00	0.00	0.00	-143
ARTIFICIAL TURF		176	0%	0%	21-May-26	01-Jul-26	04-Apr-26 A	17-Dec-26	0.00	0.00	0.00	-143
MLTX-02-005-PR-1	PO for Artificial TURF	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	18-Jun-26	01-Jul-26	03-Dec-26	17-Dec-26	0.00	0.00	0.00	-143
RUBBER GRANULES		155	0%	0%	21-May-26	13-Jun-26	04-Apr-26 A	23-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-PR-1	PO for Rubber Granules	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-138
PADEL GLASS		171	0%	0%	21-May-26	19-Nov-26	04-Apr-26 A	12-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-1	PO for Padel Glass	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-1	Material Delivery for Padel Glass	28	64.64%	0%	19-Oct-26	19-Nov-26	09-Nov-26	12-Dec-26	0.00	0.00	0.00	-18
PADEL WIRE MESH/STEEL SETS		153	0%	0%	31-May-26	22-Jun-26	09-Apr-26 A	26-Nov-26	0.00	0.00	0.00	-133
MLTX-02-005-PR-1	PO for Wire Mesh/Steel Sets	5	100%	100%	31-May-26	04-Jun-26	09-Apr-26 A	19-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-133
AGGREGATE BASE COURSE		12	0%	0%	16-Jul-26	29-Jul-26	04-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	19
MLTX-02-005-PR-1	PO for Aggregate Base Course	5	100%	100%	16-Jul-26	21-Jul-26	04-Apr-26 A	14-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-PR-1	Material Delivery for Aggregate Base Course	7	100%	100%	22-Jul-26	29-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	19
BITUMINOUS BASE & WEARING COURSE		32	0%	0%	15-Jun-26	21-Jul-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	15	100%	100%	15-Jun-26	01-Jul-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for the Site	17	100%	100%	02-Jul-26	21-Jul-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	-93
INTERLOCKING PAVING		32	0%	0%	09-Aug-26	14-Sep-26	15-Oct-26 A	15-Oct-26 A	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	15	100%	100%	09-Aug-26	25-Aug-26	15-Oct-26 A	15-Oct-26 A	0.00	0.00	0.00	-43
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	17	100%	100%	26-Aug-26	14-Sep-26	15-Oct-26 A	15-Oct-26 A	0.00	0.00	0.00	-26
MARKING PAINT		32	0%	0%	02-Jul-26	08-Aug-26	09-Nov-26	16-Dec-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	20-Jul-26	08-Aug-26	26-Nov-26	16-Dec-26	0.00	0.00	0.00	-110
PACKAGE AC UNITS		20	0%	0%	04-Nov-26	26-Nov-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	121
MLTX-02-005-PR-1	PO for Package AC Units	5	82%	100%	04-Nov-26	09-Nov-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	106
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	0%	100%	10-Nov-26	26-Nov-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	121
AIR DIFUSSERS/GRILLS		40	0%	0%	01-Oct-26	02-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	43
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	100%	01-Oct-26	18-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	4
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	16.4%	100%	04-Nov-26	02-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	43
GALVANIZED DUCTS		40	0%	0%	19-Oct-26	03-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	44
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	100%	19-Oct-26	04-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	19
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	12.4%	100%	05-Nov-26	03-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	44

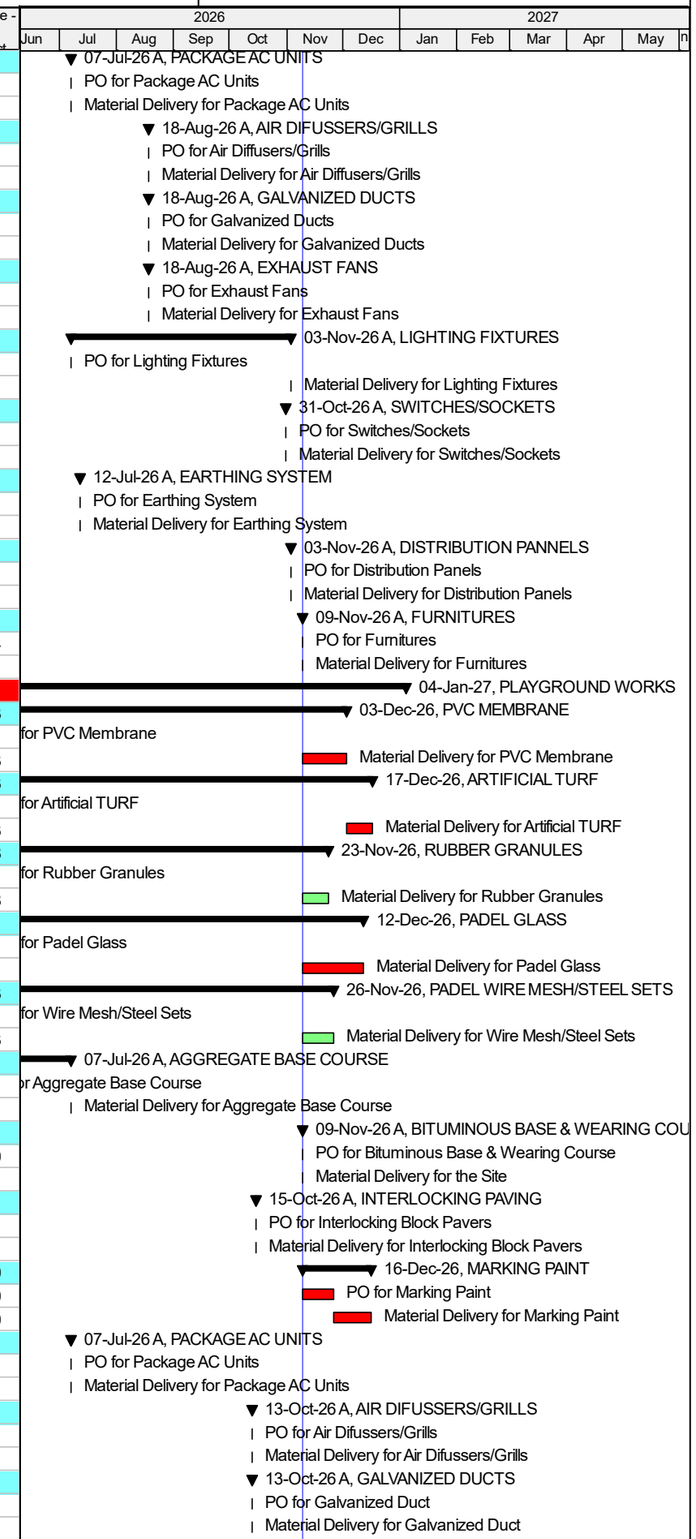

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
EXHAUST FANS		40	0%	0%	17-Jun-26	02-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	43
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	100%	17-Jun-26	04-Jul-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	16.4%	100%	04-Nov-26	02-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	43
DISTRIBUTION BOARDS		20	0%	0%	23-Jun-26	26-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	38
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	100%	23-Jun-26	28-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-91
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	0%	100%	10-Nov-26	26-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	38
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-113
LIGHT FIXTURES		118	0%	0%	22-Jul-26	02-Dec-26	07-Jul-26 A	08-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	PO for Light Fixtures	5	100%	100%	22-Jul-26	27-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	17
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	15-Nov-26	08-Dec-26	0.00	0.00	0.00	-4
CCTV MATERIALS		48	0%	0%	30-Jul-26	21-Dec-26	09-Nov-26	04-Jan-27	0.00	0.00	0.00	-11
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	05-Dec-26	21-Dec-26	17-Dec-26	04-Jan-27	0.00	0.00	0.00	-11
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	15-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	15-Nov-26	22-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	22-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
LANDSCAPE WORKS		164	0%	0%	30-Jul-26	13-Dec-26	16-May-26 A	21-Dec-26	0.00	0.00	0.00	-6
INTERLOCKING PAVING		22	0%	0%	30-Jul-26	24-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-2
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	100%	30-Jul-26	04-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	12	100%	100%	11-Aug-26	24-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-2
CURBSTONE		32	0%	0%	30-Jul-26	05-Sep-26	14-Jul-26 A	23-Jul-26 A	0.00	0.00	0.00	37
MLTX-02-005-PR-1	PO for Curbstone	5	100%	100%	30-Jul-26	04-Aug-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	18
MLTX-02-005-PR-1	Material Delivery for Curbstone	12	100%	100%	23-Aug-26	05-Sep-26	23-Jul-26 A	23-Jul-26 A	0.00	0.00	0.00	37
PAVEMENT MARKING		15	0%	0%	15-Aug-26	31-Aug-26	22-Nov-26	09-Dec-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	22-Nov-26	28-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	20-Aug-26	31-Aug-26	28-Nov-26	09-Dec-26	0.00	0.00	0.00	-84
TRAFFIC SIGNS		18	0%	0%	04-Nov-26	13-Dec-26	13-Oct-26 A	09-Nov-26 A	0.00	0.00	0.00	30
MLTX-02-005-PR-1	PO for Traffic Signs	15	27.33%	100%	04-Nov-26	21-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	33
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	10	0%	100%	22-Nov-26	13-Dec-26	09-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	30
IRRIGATION PIPES/SPRINKLERS		15	0%	0%	10-Nov-26	30-Nov-26	13-Oct-26 A	09-Nov-26 A	0.00	0.00	0.00	19
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	0%	100%	10-Nov-26	15-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	28
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	0%	100%	22-Nov-26	30-Nov-26	08-Nov-26 A	09-Nov-26 A	0.00	0.00	0.00	19
AGRICULTURE SOIL		37	0%	0%	05-Aug-26	05-Dec-26	21-Oct-26 A	21-Oct-26 A	0.00	0.00	0.00	38
MLTX-02-005-PR-1	PO for Agriculture Soil	15	100%	100%	05-Aug-26	22-Aug-26	21-Oct-26 A	21-Oct-26 A	0.00	0.00	0.00	-51
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	22	0%	100%	10-Nov-26	05-Dec-26	21-Oct-26 A	21-Oct-26 A	0.00	0.00	0.00	38
TRACK SURFACE		122	0%	0%	30-Jul-26	21-Nov-26	16-May-26 A	21-Dec-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	PO for Track Surface	5	100%	100%	30-Jul-26	04-Aug-26	16-May-26 A	20-May-26 A	0.00	0.00	0.00	62
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	0%	0%	10-Nov-26	21-Nov-26	09-Dec-26	21-Dec-26	0.00	0.00	0.00	-25
GRASS/TREES		159	0%	0%	05-Aug-26	08-Dec-26	17-May-26 A	07-Nov-26 A	0.00	0.00	0.00	28
MLTX-02-005-PR-1	PO for Grass/Trees	5	100%	100%	05-Aug-26	10-Aug-26	17-May-26 A	20-May-26 A	0.00	0.00	0.00	67
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	100%	22-Nov-26	08-Dec-26	25-Oct-26 A	07-Nov-26 A	0.00	0.00	0.00	28
CABLES		33	0%	0%	30-Jul-26	06-Sep-26	26-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	-8
MLTX-02-005-PR-1	PO for Cables	5	100%	100%	30-Jul-26	04-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Cables	15	100%	100%	20-Aug-26	06-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-8
LONG LEAD ITEM		131	0%	0%	21-May-26	30-Nov-26	26-Aug-26 A	05-Dec-26	0.00	0.00	0.00	-3
PLAYGROUND WORKS		63	0%	0%	21-May-26	30-Nov-26	13-Oct-26 A	05-Dec-26	0.00	0.00	0.00	-3
STEEL TENSION CABLES		35	0%	0%	21-May-26	19-Oct-26	13-Oct-26 A	05-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	100%	21-May-26	02-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-53
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	10	100%	100%	03-Jun-26	14-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Staging time	7	100%	0%	12-Oct-26	19-Oct-26	26-Nov-26	05-Dec-26	0.00	0.00	0.00	-39
EMERGENCY DOORS		35	0%	0%	15-Jun-26	24-Nov-26	13-Oct-26 A	30-Nov-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	100%	15-Jun-26	25-Jun-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	15	27.33%	0%	04-Nov-26	21-Nov-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	100%	27-Jun-26	19-Jul-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	Staging time	3	0%	0%	22-Nov-26	24-Nov-26	26-Nov-26	30-Nov-26	0.00	0.00	0.00	-4
PRESSURE UNITS		50	0%	0%	12-Oct-26	30-Nov-26	13-Oct-26 A	05-Dec-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	100%	12-Oct-26	22-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	8
MLTX-02-005-PR-1	Material Delivery for Pressure Units	10	31%	0%	05-Nov-26	16-Nov-26	09-Nov-26	21-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	10	100%	100%	24-Oct-26	03-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	18
MLTX-02-005-PR-1	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	23-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
AIR LOCK DOORS		45	0%	0%	30-Sep-26	26-Nov-26	13-Oct-26 A	02-Dec-26	0.00	0.00	0.00	-4

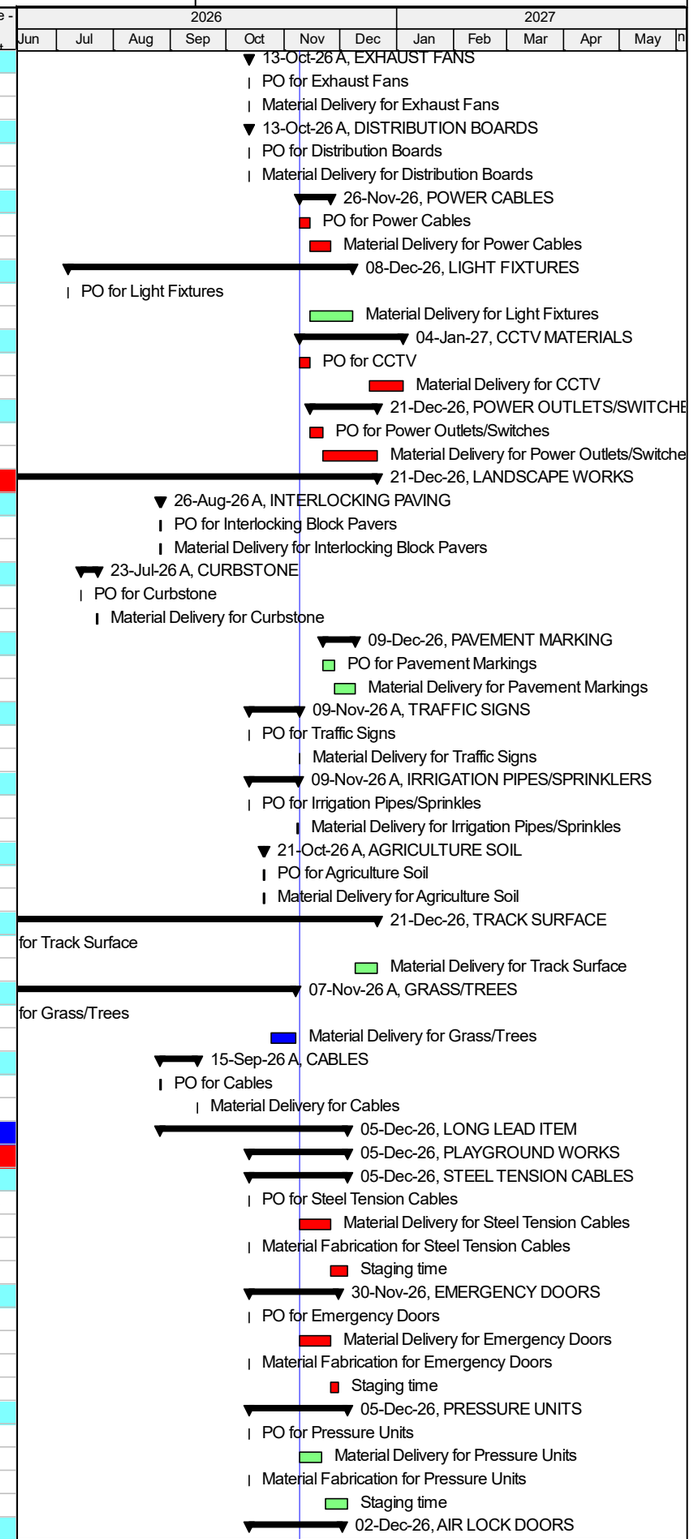

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	100%	30-Sep-26	11-Oct-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	-2
MLTX-02-005-PR-1	Material Delivery for Lock Doors	12	25.83%	0%	05-Nov-26	18-Nov-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	15	100%	100%	19-Oct-26	04-Nov-26	13-Oct-26 A	13-Oct-26 A	0.00	0.00	0.00	19
MLTX-02-005-PR-1	Staging time	5	0%	0%	22-Nov-26	26-Nov-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-4
LANDSCAPE WORKS		92	0%	0%	05-Aug-26	21-Nov-26	26-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	56
LIGHT POLES		92	0%	0%	05-Aug-26	21-Nov-26	26-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	56
MLTX-02-005-PR-1	PO for Lighting poles	10	100%	100%	05-Aug-26	16-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-9
MLTX-02-005-PR-1	Material Fabrication for Lighting poles	30	100%	100%	25-Aug-26	29-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	28
MLTX-02-005-PR-1	Material Delivery for Lighting poles	30	100%	100%	30-Sep-26	03-Nov-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	41
MLTX-02-005-PR-1	Staging time	15	27.33%	100%	04-Nov-26	21-Nov-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	56
CONSTRUCTION PHASE		272	43.44%	44.17%	16-Apr-26	31-Dec-26	04-Apr-26 A	06-Mar-27	4,264,073.43	4,335,150.18	9,815,232.20	-53
SITE WORKS		272	38.81%	38.33%	16-Apr-26	31-Dec-26	04-Apr-26 A	06-Mar-27	3,356,401.70	3,315,131.98	8,649,227.95	-53
EARTH WORKS		44	100%	100%	16-Apr-26	09-Jun-26	04-Apr-26 A	13-Aug-26 A	263,237.78	263,237.78	263,237.78	-55
MLTX-02-005-CN-133	Excavation (in all types of soil) including Compaction	12	100%	100%	16-Apr-26	29-Apr-26	06-Apr-26 A	12-Apr-26 A	98,374.53	98,374.53	98,374.53	15
MLTX-02-005-CN-133	Excavation (in all types of soil) including Compaction	9	100%	100%	16-Apr-26	26-Apr-26	04-Apr-26 A	02-Aug-26 A	14,053.50	14,053.50	14,053.50	-81
MLTX-02-005-CN-133	Excavation (in all types of soil) including Compaction	7	100%	100%	01-Jun-26	08-Jun-26	06-Apr-26 A	05-Aug-26 A	63,240.77	63,240.77	63,240.77	-49
MLTX-02-005-CN-133	Backfilling on Layers (Selected Soil) including Compaction	10	100%	100%	30-Apr-26	11-May-26	13-Apr-26 A	30-Apr-26 A	49,038.63	49,038.63	49,038.63	10
MLTX-02-005-CN-133	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	30-Apr-26	23-May-26	06-Apr-26 A	08-Apr-26 A	7,005.52	7,005.52	7,005.52	38
MLTX-02-005-CN-133	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	01-Jun-26	09-Jun-26	21-Apr-26 A	13-Aug-26 A	31,524.83	31,524.83	31,524.83	-55
LANDSCAPE WORKS		250	36.44%	35.95%	12-May-26	31-Dec-26	19-May-26 A	06-Mar-27	3,034,670.59	2,993,400.87	8,327,496.85	-53
PLAYGROUND AREA		239	78.93%	71.01%	12-May-26	31-Dec-26	19-May-26 A	17-Feb-27	1,015,120.79	913,315.20	1,286,157.31	-40
FOOTBALL PLAYGROUND		227	85%	85%	12-May-26	15-Dec-26	19-May-26 A	06-Feb-27	269,322.49	269,322.49	316,849.99	-44
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Football Playground)	10	100%	100%	12-May-26	23-May-26	19-May-26 A	31-May-26 A	79,212.50	79,212.50	79,212.50	-4
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Football	16	100%	100%	30-Jul-26	17-Aug-26	01-Jun-26 A	18-Jun-26 A	15,842.50	15,842.50	15,842.50	52
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	100%	02-Jul-26	25-Jul-26	08-Nov-26 A	09-Nov-26 A	158,424.99	158,424.99	158,424.99	-90
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	10-Dec-26	15-Dec-26	31-Jan-27	06-Feb-27	0.00	0.00	31,685.00	-44
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	2	0%	0%	08-Dec-26	09-Dec-26	28-Jan-27	31-Jan-27	0.00	0.00	15,842.50	-44
MLTX-02-005-CI	Aggregate basecourse layer (Football Playground)	21	100%	100%	18-Aug-26	10-Sep-26	20-Jun-26 A	28-Jun-26 A	15,842.50	15,842.50	15,842.50	65
PADEL PLAYGROUND		225	70%	70%	24-May-26	24-Dec-26	19-May-26 A	15-Feb-27	163,788.80	163,788.80	233,984.00	-44
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Padel Playground)	7	100%	100%	24-May-26	03-Jun-26	19-May-26 A	31-May-26 A	81,894.40	81,894.40	81,894.40	3
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Padel	16	100%	100%	19-Aug-26	06-Sep-26	01-Jun-26 A	18-Jun-26 A	11,699.20	11,699.20	11,699.20	69
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Padel Playground)	21	100%	100%	13-Sep-26	07-Oct-26	24-Aug-26 A	25-Aug-26 A	58,496.00	58,496.00	58,496.00	36
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	09-Feb-27	15-Feb-27	0.00	0.00	58,496.00	-44
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	09-Feb-27	15-Feb-27	0.00	0.00	11,699.20	-44
MLTX-02-005-CI	Aggregate basecourse layer (Padel Playground)	21	100%	100%	22-Sep-26	17-Oct-26	20-Jun-26 A	28-Jun-26 A	11,699.20	11,699.20	11,699.20	95
BASKETBALL PLAYGROUND		176	69.07%	69.52%	26-Jul-26	31-Dec-26	19-May-26 A	17-Feb-27	219,704.49	221,133.58	318,089.68	-40
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Basketball	10	100%	100%	26-Jul-26	05-Aug-26	19-May-26 A	31-May-26 A	92,913.27	92,913.27	92,913.27	57
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Basketball	11	100%	100%	06-Aug-26	18-Aug-26	01-Jun-26 A	18-Jun-26 A	15,795.26	15,795.26	15,795.26	53
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Basketball	21	100%	100%	19-Aug-26	12-Sep-26	20-Aug-26 A	25-Aug-26 A	96,629.80	96,629.80	96,629.80	15
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	2	0%	0%	30-Dec-26	31-Dec-26	15-Feb-27	17-Feb-27	0.00	0.00	80,796.75	-40
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	2	0%	0%	30-Dec-26	31-Dec-26	15-Feb-27	17-Feb-27	0.00	0.00	16,159.35	-40
MLTX-02-005-CI	Aggregate basecourse layer (Basketball Playground)	21	90.95%	100%	18-Oct-26	10-Nov-26	20-Jun-26 A	28-Jun-26 A	14,366.16	15,795.26	15,795.26	116
PADEL FENCE		62	0%	9.24%	25-Nov-26	24-Dec-26	08-Aug-26 A	06-Feb-27	0.00	5,077.72	54,928.63	-36
MLTX-02-005-CI	Excavation for Fence	8	0%	100%	25-Nov-26	03-Dec-26	08-Aug-26 A	08-Aug-26 A	0.00	414.35	414.35	100
MLTX-02-005-CI	Concrete Foundation for Fence including Posts Fixation	7	0%	100%	26-Nov-26	03-Dec-26	15-Aug-26 A	23-Aug-26 A	0.00	828.69	828.69	87
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	2	0%	100%	20-Dec-26	21-Dec-26	13-Oct-26 A	13-Oct-26 A	0.00	3,834.68	3,834.68	59
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	12-Dec-26	10-Jan-27	0.00	0.00	30,677.48	-13
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	12-Dec-26	10-Jan-27	0.00	0.00	15,338.75	-13
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	20-Dec-26	24-Dec-26	31-Jan-27	06-Feb-27	0.00	0.00	3,834.68	-36
CURBSTOEN/INTERLOCK		150	100%	70.1%	27-Aug-26	21-Sep-26	10-Aug-26 A	16-Nov-26	362,305.01	253,992.61	362,305.01	-46
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	6	100%	40%	15-Sep-26	21-Sep-26	21-Oct-26 A	16-Nov-26	180,520.67	72,208.27	180,520.67	-46
MLTX-02-005-CI	Concrete Works Under Curbstone	3	100%	100%	27-Aug-26	30-Aug-26	10-Aug-26 A	10-Aug-26 A	54,535.30	54,535.30	54,535.30	17
MLTX-02-005-CI	Curbstone Installation	4	100%	100%	06-Sep-26	09-Sep-26	11-Aug-26 A	13-Aug-26 A	127,249.04	127,249.04	127,249.04	23
AIR DOME		201	23.18%	23.18%	18-Jun-26	24-Dec-26	14-Jul-26 A	09-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-39
CIVIL WORKS		191	48.29%	48.29%	18-Jun-26	07-Dec-26	14-Jul-26 A	28-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-44
MLTX-02-005-CI	Excavation for Foundation (Air Dome)	10	100%	100%	21-Sep-26	03-Oct-26	14-Jul-26 A	02-Aug-26 A	167,650.30	167,650.30	167,650.30	52
MLTX-02-005-CI	Concrete Works for Foundations including Anchor Bolts (Air	15	100%	100%	04-Oct-26	20-Oct-26	10-Aug-26 A	21-Sep-26 A	228,008.77	228,008.77	228,008.77	24
MLTX-02-005-CI	Cable System Installation (Air Dome)	8	100%	100%	18-Jun-26	27-Jun-26	21-Sep-26 A	21-Sep-26 A	350,921.95	350,921.95	350,921.95	-74
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	942,830.33	-44
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-44
MLTX-02-005-CI	Perimeter Clamping System Installation	8	100%	100%	30-Jun-26	08-Jul-26	21-Sep-26 A	28-Sep-26 A	552,946.49	552,946.49	552,946.49	-69
MECHANICAL WORKS		5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	1,233,296.81	-44
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	4	0%	0%	08-Dec-26	12-Dec-26	28-Jan-27	02-Feb-27	0.00	0.00	728,766.30	-44
MLTX-02-005-CI	Air Units Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	336,353.67	-44

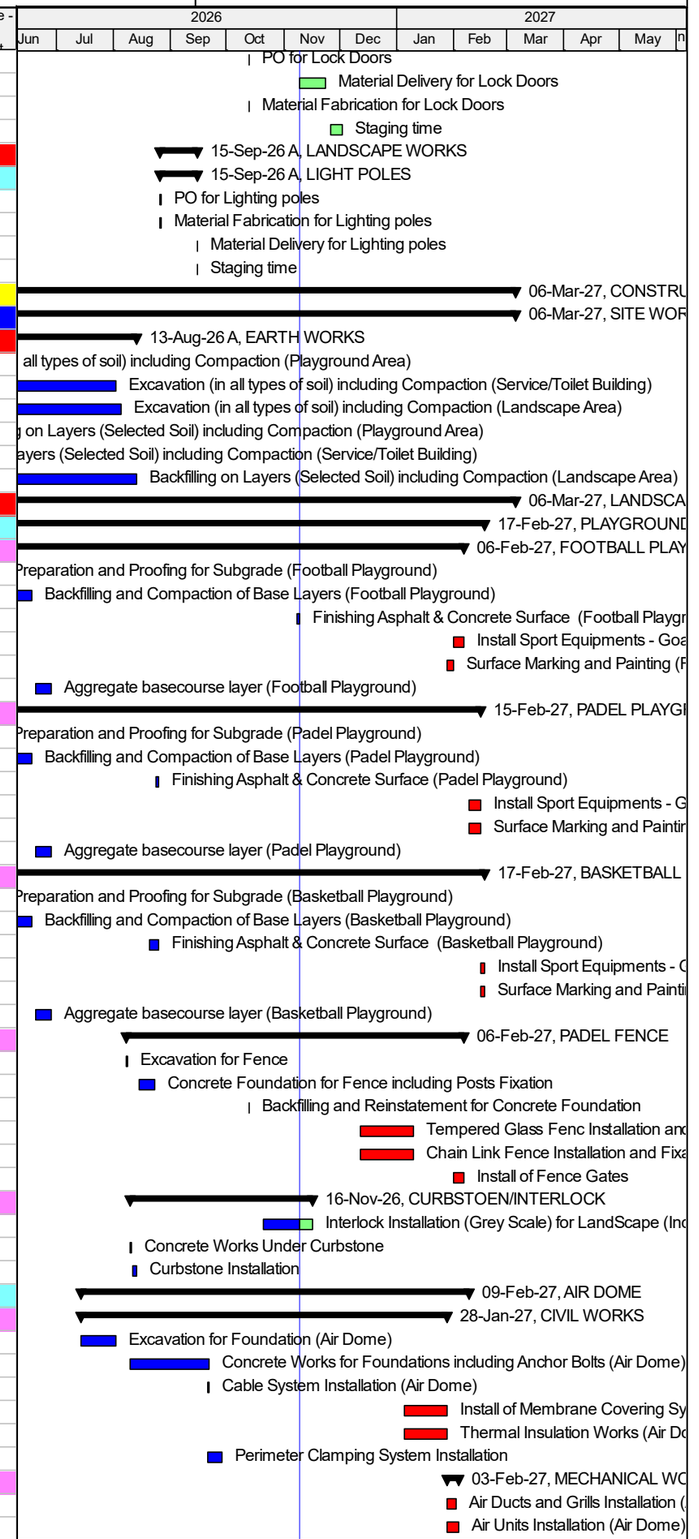

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	168,176.84	-44
ELECTRICAL WORKS		10	0%	0%	08-Dec-26	24-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	1,513,591.54	-39
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	08-Dec-26	19-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	224,235.78	-44
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	12-Dec-26	19-Dec-26	01-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-44
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	13-Dec-26	19-Dec-26	02-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-44
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	15-Dec-26	19-Dec-26	04-Feb-27	09-Feb-27	0.00	0.00	504,530.51	-44
MLTX-02-005-CI	Control System Installation (Air Dome)	3	0%	0%	22-Dec-26	24-Dec-26	06-Feb-27	09-Feb-27	0.00	0.00	448,471.57	-39
FINISHES WORKS		4	0%	0%	12-Dec-26	15-Dec-26	01-Feb-27	06-Feb-27	0.00	0.00	168,176.84	-44
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	2	0%	0%	12-Dec-26	13-Dec-26	01-Feb-27	03-Feb-27	0.00	0.00	112,117.89	-44
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	14-Dec-26	15-Dec-26	03-Feb-27	06-Feb-27	0.00	0.00	56,058.95	-44
IRRIGATION NETWORK		133	83.53%	83.53%	10-Sep-26	02-Dec-26	24-Aug-26 A	14-Feb-27	127,308.67	127,308.67	152,414.87	-62
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	3	100%	100%	10-Sep-26	13-Sep-26	24-Aug-26 A	14-Sep-26 A	53,620.00	53,620.00	53,620.00	-1
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	3	100%	100%	14-Sep-26	16-Sep-26	19-Sep-26 A	29-Sep-26 A	50,127.83	50,127.83	50,127.83	-10
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	3	100%	100%	17-Sep-26	20-Sep-26	19-Sep-26 A	13-Oct-26 A	23,560.84	23,560.84	23,560.84	-19
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	01-Dec-26	02-Dec-26	11-Feb-27	14-Feb-27	0.00	0.00	25,106.20	-62
NATURAL GROUND		46	82.81%	30.51%	10-Oct-26	12-Nov-26	20-Oct-26 A	14-Dec-26	158,787.60	58,500.00	191,740.00	-26
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	74%	0%	27-Oct-26	12-Nov-26	26-Nov-26	14-Dec-26	93,787.60	0.00	126,740.00	-26
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	26-Nov-26	65,000.00	58,500.00	65,000.00	-26
PLANTING		27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	21-Nov-26	0.00	69,450.29	347,251.46	36
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	16-Nov-26	0.00	20,835.09	104,175.44	23
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	20%	24-Dec-26	31-Dec-26	01-Nov-26 A	17-Nov-26	0.00	28,346.50	141,732.50	39
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	20%	13-Dec-26	23-Dec-26	01-Nov-26 A	21-Nov-26	0.00	20,268.70	101,343.52	29
WALKING/BIKE PATHS		31	100%	100%	22-Sep-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	273,767.20	273,767.20	273,767.20	35
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	10	100%	100%	22-Sep-26	04-Oct-26	19-Jul-26 A	16-Sep-26 A	140,620.76	140,620.76	140,620.76	14
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	10	100%	100%	18-Oct-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	133,146.44	133,146.44	133,146.44	35
GENERAL/FURNITURE		139	34.06%	53.49%	22-Sep-26	31-Dec-26	20-Sep-26 A	06-Mar-27	160,158.82	251,532.00	470,271.40	-53
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	39.44%	0%	01-Nov-26	21-Nov-26	29-Dec-26	19-Jan-27	36,917.63	0.00	93,594.00	-50
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	15-Dec-26	31-Dec-26	11-Feb-27	02-Mar-27	0.00	0.00	9,749.30	-50
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	18	100%	0%	11-Oct-26	31-Oct-26	08-Dec-26	29-Dec-26	17,274.79	0.00	17,274.79	-50
MLTX-02-005-CN-1	Fixation and Installation of Benches	20	35.5%	0%	01-Nov-26	23-Nov-26	19-Jan-27	11-Feb-27	14,309.28	0.00	40,307.84	-68
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	20	35.5%	0%	01-Nov-26	23-Nov-26	19-Jan-27	11-Feb-27	11,629.00	0.00	32,757.76	-68
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	20	35.5%	0%	01-Nov-26	23-Nov-26	19-Jan-27	11-Feb-27	4,568.51	0.00	12,869.04	-68
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	18	0%	0%	24-Nov-26	14-Dec-26	11-Feb-27	06-Mar-27	0.00	0.00	12,186.67	-68
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	13	100%	100%	22-Sep-26	07-Oct-26	20-Sep-26 A	30-Sep-26 A	75,459.60	75,459.60	75,459.60	6
MLTX-02-005-CN-1	Installing of Site Light Poles	20	0%	100%	22-Nov-26	14-Dec-26	15-Oct-26 A	28-Oct-26 A	0.00	176,072.40	176,072.40	41
PARKING		15	100%	100%	14-Oct-26	31-Oct-26	18-Jul-26 A	19-Sep-26 A	58,493.33	58,493.33	58,493.33	35
MLTX-02-005-CN-133	Interlock Installation (8 Cm) for Parking Area (Including	11	100%	100%	19-Oct-26	31-Oct-26	10-Sep-26 A	19-Sep-26 A	40,945.33	40,945.33	40,945.33	35
MLTX-02-005-CN-133	Site Preparation & Compaction Under Interlock for Parking	4	100%	100%	14-Oct-26	18-Oct-26	18-Jul-26 A	18-Jul-26 A	17,548.00	17,548.00	17,548.00	78
TOILET/SERVICE BUILDING		218	77.84%	87.48%	01-Jun-26	29-Dec-26	23-May-26 A	11-Feb-27	907,671.73	1,020,018.20	1,166,004.25	-37
STRUCTURE WORKS		54	100%	100%	01-Jun-26	02-Aug-26	23-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	0
CONCRETE WORKS		33	100%	100%	25-Jun-26	02-Aug-26	25-May-26 A	27-Jun-26 A	118,454.85	118,454.85	118,454.85	31
SUB-STRUCTURE		9	100%	100%	25-Jun-26	05-Jul-26	25-May-26 A	07-Jun-26 A	38,022.35	38,022.35	38,022.35	24
MLTX-02-005-CI	Plain Concrete Under Footing	4	100%	100%	25-Jun-26	29-Jun-26	25-May-26 A	31-May-26 A	1,462.40	1,462.40	1,462.40	25
MLTX-02-005-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	30-Jun-26	05-Jul-26	03-Jun-26 A	07-Jun-26 A	36,559.95	36,559.95	36,559.95	24
SUPER-STRUCTURE		14	100%	100%	18-Jul-26	02-Aug-26	20-Jun-26 A	27-Jun-26 A	80,432.50	80,432.50	80,432.50	31
MLTX-02-005-CI	AAC Panels Works for Walls	7	100%	100%	18-Jul-26	25-Jul-26	20-Jun-26 A	20-Jun-26 A	48,259.50	48,259.50	48,259.50	30
MLTX-02-005-CI	Parpet Works and Lintels	3	100%	100%	30-Jul-26	02-Aug-26	25-Jun-26 A	27-Jun-26 A	16,086.50	16,086.50	16,086.50	31
MLTX-02-005-CI	AAC Panels Works for Slabs	4	100%	100%	26-Jul-26	29-Jul-26	21-Jun-26 A	24-Jun-26 A	16,086.50	16,086.50	16,086.50	30
UNDER GROUND SEPTIC TANK		44	100%	100%	02-Jun-26	22-Jul-26	01-Jun-26 A	06-Jul-26 A	34,208.09	34,208.09	34,208.09	14
MLTX-02-005-CN-1	Plain Concrete Under Footing	3	100%	100%	02-Jun-26	04-Jun-26	01-Jun-26 A	06-Jun-26 A	1,462.40	1,462.40	1,462.40	-1
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Slab Including	10	100%	100%	12-Jul-26	22-Jul-26	06-Jul-26 A	06-Jul-26 A	8,774.37	8,774.37	8,774.37	14
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Foundation Including	8	100%	100%	06-Jun-26	14-Jun-26	09-Jun-26 A	13-Jun-26 A	7,604.46	7,604.46	7,604.46	1
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	10	100%	100%	30-Jun-26	11-Jul-26	18-Jun-26 A	05-Jul-26 A	16,366.86	16,366.86	16,366.86	5
THERMAL & MOISTER PROTECTION		53	100%	100%	01-Jun-26	01-Aug-26	23-May-26 A	02-Aug-26 A	10,236.80	10,236.80	10,236.80	-1
ANTI TERMIT CONTROL		13	100%	100%	01-Jun-26	15-Jun-26	23-May-26 A	03-Jun-26 A	4,387.50	4,387.50	4,387.50	10
MLTX-02-005-CI	Anti Termite Works Under Foundation	1	100%	100%	01-Jun-26	01-Jun-26	31-May-26 A	03-Jun-26 A	1,755.00	1,755.00	1,755.00	-2
MLTX-02-005-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	15-Jun-26	15-Jun-26	23-May-26 A	24-May-26 A	2,632.50	2,632.50	2,632.50	16
POLYETHYLENE SHEET		13	100%	100%	01-Jun-26	15-Jun-26	24-May-26 A	04-Jun-26 A	2,193.30	2,193.30	2,193.30	9
MLTX-02-005-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	01-Jun-26	01-Jun-26	31-May-26 A	04-Jun-26 A	877.32	877.32	877.32	-3
MLTX-02-005-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	15-Jun-26	15-Jun-26	24-May-26 A	25-May-26 A	1,315.98	1,315.98	1,315.98	15
EPOXY		8	100%	100%	23-Jul-26	01-Aug-26	11-Jul-26 A	02-Aug-26 A	3,656.00	3,656.00	3,656.00	-1
MLTX-02-005-CI	Surface Preparation for Epoxy Coating	3	100%	100%	23-Jul-26	26-Jul-26	11-Jul-26 A	11-Jul-26 A	1,096.80	1,096.80	1,096.80	13
MLTX-02-005-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	27-Jul-26	01-Aug-26	02-Aug-26 A	02-Aug-26 A	2,559.20	2,559.20	2,559.20	-1
MASONARY WORK		5	100%	100%	06-Jul-26	11-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	2



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-140	CMU Masonary Works Including all Accessories	5	100%	100%	06-Jul-26	11-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	2
THERMAL & MOISTER PROTECTION		21	100%	95.21%	03-Aug-26	26-Aug-26	25-Aug-26 A	18-Nov-26	34,698.32	33,037.59	34,698.32	-70
MLTX-02-005-CN-140	Preparing Surface and Preliminary Works for Toilets	2	100%	100%	03-Aug-26	04-Aug-26	25-Aug-26 A	25-Aug-26 A	2,105.86	2,105.86	2,105.86	-18
MLTX-02-005-CN-140	Finalize Water Proofing Works for Toilets	5	100%	100%	05-Aug-26	10-Aug-26	25-Aug-26 A	29-Aug-26 A	4,913.66	4,913.66	4,913.66	-16
MLTX-02-005-CN-140	Preparing Surface and Preliminary Works for Roofing and	6	100%	100%	11-Aug-26	17-Aug-26	05-Sep-26 A	05-Sep-26 A	11,071.52	11,071.52	11,071.52	-16
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	18-Nov-26	16,607.28	14,946.55	16,607.28	-70
MECHANICAL WORK		71	99.26%	99.26%	09-Sep-26	26-Dec-26	12-Jul-26 A	02-Dec-26	262,723.23	262,723.23	264,673.10	21
HVAC SYSTEM		22	100%	100%	09-Sep-26	05-Oct-26	12-Jul-26 A	03-Oct-26 A	27,883.37	27,883.37	27,883.37	2
MLTX-02-005-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	03-Oct-26	05-Oct-26	12-Jul-26 A	12-Jul-26 A	9,359.69	9,359.69	9,359.69	72
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	13	100%	100%	09-Sep-26	24-Sep-26	03-Oct-26 A	03-Oct-26 A	14,623.96	14,623.96	14,623.96	-7
MLTX-02-005-CN-1	Exhaust, Air Ducts Installation with all Accessories	6	100%	100%	17-Sep-26	24-Sep-26	18-Aug-26 A	23-Aug-26 A	3,899.72	3,899.72	3,899.72	27
WATER SUPPLY SYSTEM		31	100%	100%	15-Sep-26	21-Oct-26	19-Jul-26 A	12-Oct-26 A	154,916.69	154,916.69	154,916.69	8
MLTX-02-005-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	04-Oct-26	06-Oct-26	19-Jul-26 A	22-Jul-26 A	6,921.94	6,921.94	6,921.94	64
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	6	100%	100%	04-Oct-26	10-Oct-26	19-Sep-26 A	12-Oct-26 A	25,998.40	25,998.40	25,998.40	-2
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	20	100%	100%	15-Sep-26	08-Oct-26	04-Oct-26 A	04-Oct-26 A	48,746.52	48,746.52	48,746.52	4
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	100%	08-Oct-26	17-Oct-26	06-Sep-26 A	14-Sep-26 A	64,995.36	64,995.36	64,995.36	27
MLTX-02-005-CN-1	Installing of Valves and Fittings	2	100%	100%	07-Oct-26	08-Oct-26	05-Sep-26 A	05-Sep-26 A	6,499.60	6,499.60	6,499.60	28
MLTX-02-005-CN-1	Installing of Water Heater	4	100%	100%	18-Oct-26	21-Oct-26	15-Sep-26 A	15-Sep-26 A	1,754.87	1,754.87	1,754.87	30
SEWER/DRAINAGE SYSTEM		37	100%	100%	10-Sep-26	24-Oct-26	20-Jul-26 A	15-Oct-26 A	79,923.17	79,923.17	79,923.17	7
MLTX-02-005-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	22-Oct-26	24-Oct-26	20-Jul-26 A	22-Jul-26 A	11,767.40	11,767.40	11,767.40	79
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	4	100%	100%	10-Oct-26	13-Oct-26	04-Oct-26 A	15-Oct-26 A	10,358.68	10,358.68	10,358.68	-2
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	3	100%	100%	01-Oct-26	04-Oct-26	26-Sep-26 A	26-Sep-26 A	14,217.67	14,217.67	14,217.67	7
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	4	100%	100%	27-Sep-26	30-Sep-26	26-Sep-26 A	26-Sep-26 A	12,186.63	12,186.63	12,186.63	4
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	24	100%	100%	10-Sep-26	08-Oct-26	08-Oct-26 A	12-Oct-26 A	31,392.79	31,392.79	31,392.79	-3
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
ELECTRICAL WORKS		117	53.29%	70.01%	12-Sep-26	29-Dec-26	14-Jul-26 A	03-Jan-27	206,217.55	270,946.49	386,998.82	-3
ROUGH-IN WORKS		16	100%	100%	12-Sep-26	30-Sep-26	14-Jul-26 A	17-Aug-26 A	206,217.55	206,217.55	206,217.55	38
MLTX-02-005-CN-1	Preleminary Works for Panel Boards	2	100%	100%	15-Sep-26	16-Sep-26	15-Jul-26 A	22-Jul-26 A	68,245.12	68,245.12	68,245.12	48
MLTX-02-005-CN-1	Preleminary Works for Cable Works	3	100%	100%	28-Sep-26	30-Sep-26	14-Jul-26 A	14-Jul-26 A	12,488.92	12,488.92	12,488.92	66
MLTX-02-005-CN-1	Preleminary Works for Sockets and Power Points	2	100%	100%	15-Sep-26	16-Sep-26	14-Jul-26 A	14-Jul-26 A	15,990.55	15,990.55	15,990.55	55
MLTX-02-005-CN-1	Preleminary Works for Lightning Works	2	100%	100%	15-Sep-26	16-Sep-26	28-Jul-26 A	17-Aug-26 A	21,935.93	21,935.93	21,935.93	27
MLTX-02-005-CN-1	Preleminary Works for Data & Telecommunication System	2	100%	100%	15-Sep-26	16-Sep-26	28-Jul-26 A	17-Aug-26 A	24,470.75	24,470.75	24,470.75	27
MLTX-02-005-CN-1	Preleminary Works for Security and Access Control System	3	100%	100%	22-Sep-26	26-Sep-26	28-Jul-26 A	17-Aug-26 A	30,913.59	30,913.59	30,913.59	34
MLTX-02-005-CN-1	Preleminary Works for Earthing Works	3	100%	100%	12-Sep-26	14-Sep-26	28-Jul-26 A	17-Aug-26 A	32,172.69	32,172.69	32,172.69	25
FIXTURE WORKS		68	0%	35.81%	23-Nov-26	29-Dec-26	01-Nov-26 A	03-Jan-27	0.00	64,728.94	180,781.27	-3
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	15	0%	0%	12-Dec-26	28-Dec-26	16-Dec-26	03-Jan-27	0.00	0.00	34,317.53	-4
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	0%	40%	06-Dec-26	29-Dec-26	03-Nov-26 A	03-Dec-26	0.00	40,947.08	102,367.69	23
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	13	0%	100%	12-Dec-26	26-Dec-26	01-Nov-26 A	01-Nov-26 A	0.00	7,085.10	7,085.10	48
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	14	0%	100%	12-Dec-26	27-Dec-26	02-Nov-26 A	03-Nov-26 A	0.00	14,259.43	14,259.43	47
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	14	0%	0%	12-Dec-26	27-Dec-26	16-Dec-26	02-Jan-27	0.00	0.00	6,239.59	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	14	0%	0%	25-Nov-26	10-Dec-26	30-Nov-26	16-Dec-26	0.00	0.00	7,250.09	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	09-Nov-26	06-Dec-26	0.00	0.00	6,824.51	12
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	15	0%	100%	13-Dec-26	29-Dec-26	03-Nov-26 A	03-Nov-26 A	0.00	2,437.33	2,437.33	49
DOORS/WINDOWS		118	91.43%	100%	19-Sep-26	27-Dec-26	17-Sep-26 A	26-Oct-26 A	62,395.54	68,245.12	68,245.12	53
MLTX-02-005-CN-140	Preliminary Works For Doors	13	100%	100%	19-Sep-26	04-Oct-26	17-Sep-26 A	26-Sep-26 A	7,799.44	7,799.44	7,799.44	7
MLTX-02-005-CN-141	Finalize Metal Doors for Toilets Building	13	100%	100%	26-Sep-26	10-Oct-26	29-Sep-26 A	29-Sep-26 A	1,949.86	1,949.86	1,949.86	9
MLTX-02-005-CN-142	Finalize Glazzed Curtain Wall Works	14	0%	100%	12-Dec-26	27-Dec-26	25-Oct-26 A	26-Oct-26 A	0.00	5,849.58	5,849.58	53
MLTX-02-005-CN-145	Preliminary Works For Windows/Curtain Wall	12	100%	100%	19-Sep-26	03-Oct-26	25-Oct-26 A	25-Oct-26 A	52,646.24	52,646.24	52,646.24	-19
METAL WORKS		77	100%	71.43%	10-Sep-26	26-Oct-26	05-Sep-26 A	24-Dec-26	13,649.02	9,749.30	13,649.02	-50
MLTX-02-005-CN-140	Installation of Galvanized Steel Ladder	14	100%	100%	10-Sep-26	27-Sep-26	21-Oct-26 A	22-Oct-26 A	5,849.58	5,849.58	5,849.58	-22
MLTX-02-005-CN-142	Installation of DI Cover for Tank	14	100%	0%	11-Oct-26	26-Oct-26	08-Dec-26	24-Dec-26	3,899.72	0.00	3,899.72	-50
MLTX-02-005-CN-142	Installation of Galvanized Steel Roof Scupper	4	100%	100%	26-Sep-26	29-Sep-26	05-Sep-26 A	05-Sep-26 A	3,899.72	3,899.72	3,899.72	20
FINISHING WORKS		106	84.23%	100%	27-Aug-26	21-Dec-26	17-Aug-26 A	04-Nov-26 A	138,180.28	164,060.21	164,060.21	41
FLOOR FINISHES		87	93.18%	100%	04-Oct-26	21-Dec-26	01-Sep-26 A	27-Oct-26 A	15,989.09	17,159.03	17,159.03	47
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	4	100%	100%	12-Oct-26	15-Oct-26	01-Sep-26 A	03-Sep-26 A	11,894.39	11,894.39	11,894.39	35
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	100%	17-Oct-26	20-Oct-26	21-Oct-26 A	26-Oct-26 A	2,924.82	2,924.82	2,924.82	-5
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	14	0%	100%	06-Dec-26	21-Dec-26	27-Oct-26 A	27-Oct-26 A	0.00	1,169.94	1,169.94	47
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	2	100%	100%	04-Oct-26	05-Oct-26	26-Sep-26 A	26-Sep-26 A	1,169.88	1,169.88	1,169.88	8
WALL FINISHES		97	81.56%	100%	27-Aug-26	22-Nov-26	17-Aug-26 A	04-Nov-26 A	109,291.05	134,001.04	134,001.04	16
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works including Plastering	3	100%	100%	01-Oct-26	04-Oct-26	17-Aug-26 A	19-Aug-26 A	18,315.62	18,315.62	18,315.62	38
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works (External)	4	100%	100%	12-Oct-26	15-Oct-26	17-Aug-26 A	19-Aug-26 A	6,551.63	6,551.63	6,551.63	48
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	100%	05-Oct-26	07-Oct-26	21-Sep-26 A	26-Sep-26 A	35,825.58	35,825.58	35,825.58	10
MLTX-02-005-CN-1	Ceramic Finish Works for Walls	6	100%	100%	10-Sep-26	16-Sep-26	20-Aug-26 A	23-Aug-26 A	15,696.35	15,696.35	15,696.35	21

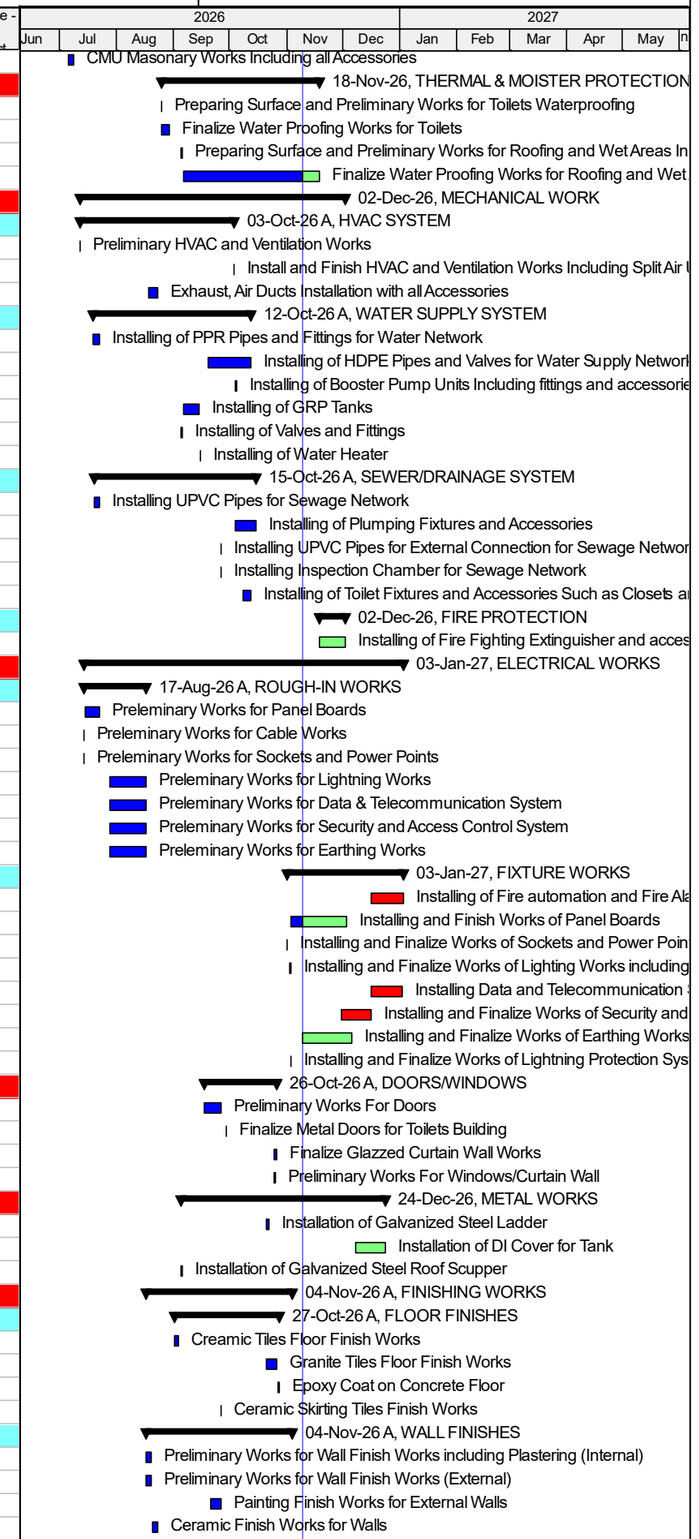


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	64.55%	100%	01-Nov-26	12-Nov-26	03-Nov-26 A	04-Nov-26 A	20,136.63	31,197.60	31,197.60	8
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	100%	05-Oct-26	10-Oct-26	29-Sep-26 A	29-Sep-26 A	2,275.00	2,275.00	2,275.00	9
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	6	0%	100%	16-Nov-26	22-Nov-26	25-Oct-26 A	25-Oct-26 A	0.00	13,649.02	13,649.02	24
MLTX-02-005-CN-1	Granite Capping for Parpet	12	100%	100%	27-Aug-26	09-Sep-26	25-Oct-26 A	25-Oct-26 A	8,150.24	8,150.24	8,150.24	-38
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	12	100%	100%	10-Sep-26	24-Sep-26	19-Sep-26 A	26-Sep-26 A	2,340.00	2,340.00	2,340.00	-1
CELLING FINISHES		23	100%	100%	10-Sep-26	07-Oct-26	15-Sep-26 A	26-Sep-26 A	12,900.14	12,900.14	12,900.14	10
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	15	100%	100%	10-Sep-26	28-Sep-26	26-Sep-26 A	26-Sep-26 A	1,357.11	1,357.11	1,357.11	2
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	6	100%	100%	17-Sep-26	24-Sep-26	16-Sep-26 A	16-Sep-26 A	5,771.52	5,771.52	5,771.52	6
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	100%	05-Oct-26	07-Oct-26	15-Sep-26 A	15-Sep-26 A	5,771.51	5,771.51	5,771.51	18
SPECIALTIES WORK		53	25%	61.67%	27-Oct-26	23-Dec-26	12-Oct-26 A	11-Feb-27	14,623.96	36,072.43	58,495.83	-42
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	24-Dec-26	14,623.96	11,699.17	14,623.96	-46
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	15	0%	0%	07-Dec-26	23-Dec-26	25-Jan-27	11-Feb-27	0.00	0.00	19,498.61	-42
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	0%	100%	14-Nov-26	15-Nov-26	07-Nov-26 A	07-Nov-26 A	0.00	24,373.26	24,373.26	7
TESTING & COMMISSIONING		8	0%	0%	24-Dec-26	02-Jan-27	24-Feb-27	06-Mar-27	0.00	0.00	0.00	-52
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	27-Dec-26	31-Dec-26	24-Feb-27	02-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	3	0%	0%	30-Dec-26	02-Jan-27	27-Feb-27	02-Mar-27	0.00	0.00	0.00	-49
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	7	0%	0%	24-Dec-26	31-Dec-26	25-Feb-27	06-Mar-27	0.00	0.00	0.00	-53
PROJECT CLOSEOUT & DEMOBILIZATION		35	0%	0%	08-Dec-26	02-Jan-27	28-Jan-27	15-Mar-27	0.00	0.00	0.00	-57
As-Built DWGs		27	0%	0%	08-Dec-26	31-Dec-26	28-Jan-27	02-Mar-27	0.00	0.00	0.00	-50
As-Built DWGs Submittals		16	0%	0%	08-Dec-26	27-Dec-26	28-Jan-27	16-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	12-Dec-26	13-Dec-26	09-Feb-27	11-Feb-27	0.00	0.00	0.00	-51
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	26-Dec-26	27-Dec-26	14-Feb-27	16-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	08-Dec-26	12-Dec-26	28-Jan-27	02-Feb-27	0.00	0.00	0.00	-44
As-Built DWGs Approvals		23	0%	0%	15-Dec-26	31-Dec-26	02-Feb-27	02-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	19-Dec-26	21-Dec-26	11-Feb-27	15-Feb-27	0.00	0.00	0.00	-47
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	29-Dec-26	31-Dec-26	27-Feb-27	02-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	15-Dec-26	17-Dec-26	02-Feb-27	06-Feb-27	0.00	0.00	0.00	-42
Demobilization		12	0%	0%	28-Dec-26	02-Jan-27	25-Feb-27	15-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	28-Dec-26	28-Dec-26	25-Feb-27	27-Feb-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	28-Dec-26	28-Dec-26	25-Feb-27	27-Feb-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	09-Mar-27	14-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	14-Mar-27	15-Mar-27	0.00	0.00	0.00	-57

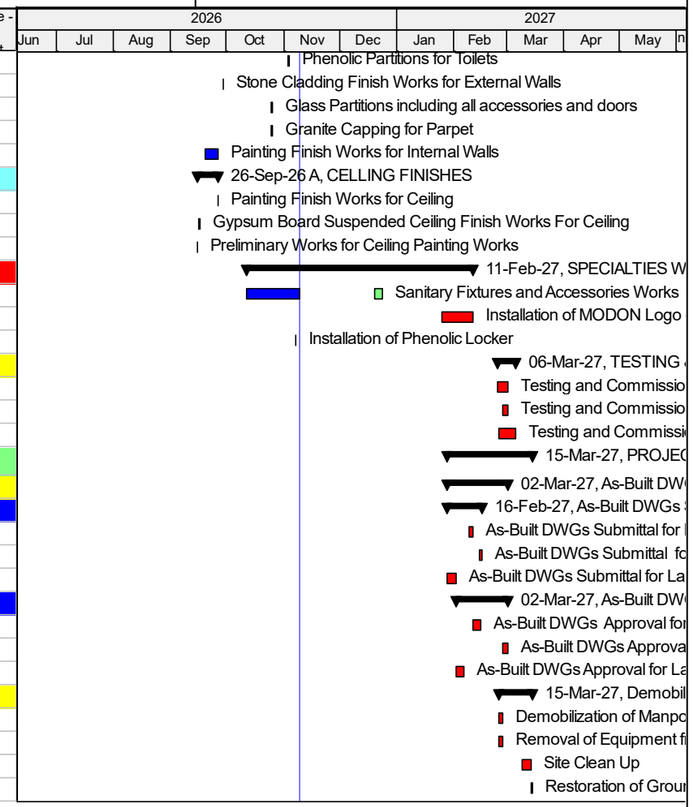

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
