
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R R		186	70.68%	51.67%	04-May-26	31-Dec-26	01-Jun-26 A	24-Dec-26	2,213,033.08	1,617,923.10	3,131,276.46	7
ARAR		113	77.37%	40.25%	15-Jul-26	27-Dec-26	11-Jun-26 A	14-Dec-26	846,221.15	440,203.59	1,093,691.69	12
PROCUREMENT		30	0%	0%	15-Jul-26	28-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-13
SHORT LEAD ITEM		30	0%	0%	15-Jul-26	28-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-13
TOILET/SERVICE WORKS		29	0%	0%	30-Aug-26	28-Nov-26	09-Nov-26	13-Dec-26	0.00	0.00	0.00	-12
SWITCHES/SOCKETS		27	0%	0%	28-Oct-26	28-Nov-26	09-Nov-26	10-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-8530	Material Delivery for Switches/Sockets	27	37.41%	0%	28-Oct-26	28-Nov-26	09-Nov-26	10-Dec-26	0.00	0.00	0.00	-10
FURNITURES		29	0%	0%	30-Aug-26	03-Oct-26	09-Nov-26	13-Dec-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-8150	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	09-Nov-26	13-Dec-26	0.00	0.00	0.00	-60
PLAYGROUND WORKS		30	0%	0%	15-Jul-26	24-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-43
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-8970	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-59
MARKING PAINT		15	0%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9090	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
CCTV MATERIALS		25	0%	0%	26-Sep-26	24-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-38
MLTX-02-005-PR-9410	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-38
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-9470	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-99
LANDSCAPE WORKS		25	0%	0%	15-Jul-26	17-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-17
PAVEMENT MARKING		5	0%	0%	15-Jul-26	20-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-9580	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-99
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9760	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-49
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-9800	Material Delivery for Grass/Trees	25	68.4%	0%	20-Oct-26	17-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-17
LONG LEAD ITEM		25	0%	0%	27-Sep-26	23-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-12
PLAYGROUND WORKS		25	0%	0%	27-Sep-26	23-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-12
STEEL TENSION CABLES		15	0%	0%	27-Sep-26	13-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-8690	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-37
EMERGENCY DOORS		20	0%	0%	26-Oct-26	17-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-8730	Material Delivery for Emergency Doors	20	60.5%	0%	26-Oct-26	17-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-12
PRESSURE UNITS		25	0%	0%	26-Oct-26	23-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-8770	Material Delivery for Pressure Units	25	48.4%	0%	26-Oct-26	23-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-12
AIR LOCK DOORS		20	0%	0%	14-Oct-26	05-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-8800	Material Fabrication for Lock Doors	20	100%	0%	14-Oct-26	05-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-22
CONSTRUCTION PHASE		113	77.37%	40.25%	14-Sep-26	27-Dec-26	11-Jun-26 A	02-Dec-26	846,221.15	440,203.59	1,093,691.69	22
SITE WORKS		113	75.23%	40.43%	17-Sep-26	27-Dec-26	11-Jun-26 A	02-Dec-26	745,562.84	400,648.59	991,083.51	22
LANDSCAPE WORKS		113	75.23%	40.43%	17-Sep-26	27-Dec-26	11-Jun-26 A	02-Dec-26	745,562.84	400,648.59	991,083.51	22
PLAYGROUND AREA		83	14.53%	25.64%	01-Oct-26	27-Dec-26	04-Nov-26 A	02-Dec-26	30,677.48	54,156.20	211,198.15	22
PADEL FENCE		20	100%	0%	01-Oct-26	24-Oct-26	09-Nov-26	02-Dec-26	30,677.48	0.00	30,677.48	-33
MLTX-02-005-CN-1026(	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	09-Nov-26	02-Dec-26	30,677.48	0.00	30,677.48	-33
CURBSTOEN/INTERLOCK		20	0%	30%	05-Dec-26	27-Dec-26	04-Nov-26 A	02-Dec-26	0.00	54,156.20	180,520.67	22
MLTX-02-005-CN-1014(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	20	0%	30%	05-Dec-26	27-Dec-26	04-Nov-26 A	02-Dec-26	0.00	54,156.20	180,520.67	22
NATURAL GROUND		6	0%	90%	17-Nov-26	23-Nov-26	27-Oct-26 A	16-Nov-26	0.00	58,500.00	65,000.00	7
MLTX-02-005-CN-10550	Compacted Natural Ground Soil Installation Works for Landscape	6	0%	90%	17-Nov-26	23-Nov-26	27-Oct-26 A	16-Nov-26	0.00	58,500.00	65,000.00	7
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	16-Nov-26	347,251.46	104,175.44	347,251.46	-13
MLTX-02-005-CN-10570	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	6	100%	30%	17-Sep-26	24-Sep-26	31-Oct-26 A	16-Nov-26	104,175.44	31,252.63	104,175.44	-44
MLTX-02-005-CN-10580	Placement of Lawn Ground Cover (Rolling and Compaction)	4	100%	30%	27-Oct-26	31-Oct-26	31-Oct-26 A	14-Nov-26	141,732.50	42,519.75	141,732.50	-11
MLTX-02-005-CN-10590	Placement and Fixation of Trees	5	100%	30%	26-Sep-26	30-Sep-26	31-Oct-26 A	15-Nov-26	101,343.52	30,403.06	101,343.52	-38
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	367,633.90	183,816.95	367,633.90	-21
MLTX-02-005-CN-10510	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	26-Nov-26	187,554.12	93,777.06	187,554.12	-33
MLTX-02-005-CN-10520	Walking Path Preparation and Installation Works	12	100%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	180,079.78	90,039.89	180,079.78	-21
TOILET/SERVICE BUILDING		28	98.1%	38.55%	14-Sep-26	15-Dec-26	20-Oct-26 A	23-Nov-26	100,658.31	39,555.00	102,608.18	20
MECHANICAL WORK		15	86.21%	51.72%	29-Sep-26	15-Dec-26	22-Oct-26 A	15-Nov-26	12,186.63	7,311.98	14,136.50	27
SEWER/DRAINAGE SYSTEM		5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	15-Nov-26	12,186.63	7,311.98	12,186.63	-35
MLTX-02-005-CN-11850	Installing Inspection Chamber for Sewage Network	5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	15-Nov-26	12,186.63	7,311.98	12,186.63	-35
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	09-Nov-26	11-Nov-26	0.00	0.00	1,949.87	30
MLTX-02-005-CN-11620	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	2	0%	0%	14-Dec-26	15-Dec-26	09-Nov-26	11-Nov-26	0.00	0.00	1,949.87	30
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	15-Nov-26	19-Nov-26	3,899.72	0.00	3,899.72	-52
MLTX-02-005-CN-11160	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	15-Nov-26	19-Nov-26	3,899.72	0.00	3,899.72	-52
FINISHING WORKS		28	100%	46.1%	06-Oct-26	31-Oct-26	20-Oct-26 A	23-Nov-26	69,948.00	32,243.02	69,948.00	-19
FLOOR FINISHES		4	100%	0%	06-Oct-26	10-Oct-26	09-Nov-26	14-Nov-26	2,924.82	0.00	2,924.82	-29
MLTX-02-005-CN-11210	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	09-Nov-26	14-Nov-26	2,924.82	0.00	2,924.82	-29

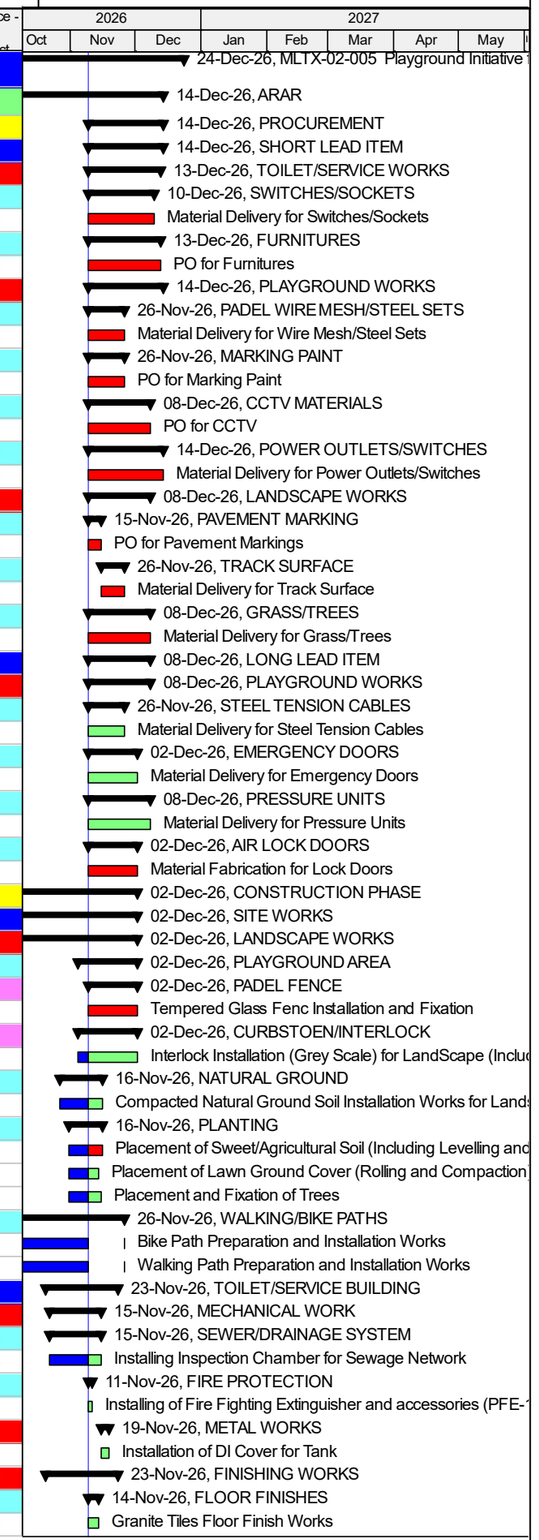

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
WALL FINISHES		28	100%	48.11%	06-Oct-26	31-Oct-26	20-Oct-26 A	23-Nov-26	67,023.18	32,243.02	67,023.18	-19
MLTX-02-005-CN-11300	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	17-Nov-26	35,825.58	32,243.02	35,825.58	-29
MLTX-02-005-CN-11320	Phenolic Partitions for Toilets	7	100%	0%	24-Oct-26	31-Oct-26	15-Nov-26	23-Nov-26	31,197.60	0.00	31,197.60	-19
SPECIALTIES WORK		5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	15-Nov-26	14,623.96	0.00	14,623.96	-19
MLTX-02-005-CN-11390	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	15-Nov-26	14,623.96	0.00	14,623.96	-19
HASA OASIS		186	83.69%	69.87%	04-May-26	07-Dec-26	01-Jun-26 A	14-Dec-26	1,090,060.01	909,968.16	1,302,439.33	-5
ENGINEERING		25	0%	0%	04-May-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
SHOP DRAWINGS		25	0%	0%	04-May-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
ELECTRICAL WORKS		25	0%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
MLTX-02-005-EN-8660	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
SHOP DRAWINGS APPROVALS		25	0%	0%	28-Oct-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		25	0%	0%	28-Oct-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
ELECTRICAL WORKS		25	0%	0%	28-Oct-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-EN-1184(	Shop DWG Approval for Power Installation Details	25	40.4%	0%	28-Oct-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
PROCUREMENT		30	0%	0%	28-Jun-26	10-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-28
SHORT LEAD ITEM		30	0%	0%	28-Jun-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
PLAYGROUND WORKS		30	0%	0%	28-Jun-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-10780	Material Delivery for Artificial TURF	30	100%	0%	30-Sep-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-10800	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-42
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-10820	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-45
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-45
MARKING PAINT		15	0%	0%	28-Jun-26	14-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-10350	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-114
AIR DIFUSSERS/GRILLS		15	0%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-10470	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
GALVANIZED DUCTS		15	0%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-10490	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
EXHAUST FANS		15	0%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-10510	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
CCTV MATERIALS		15	0%	0%	04-Jul-26	20-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-10690	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-109
LANDSCAPE WORKS		25	0%	0%	28-Sep-26	26-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-36
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-10920	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-36
LONG LEAD ITEM		25	0%	0%	15-Jul-26	10-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-23
PLAYGROUND WORKS		25	0%	0%	15-Jul-26	10-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-23
STEEL TENSION CABLES		16	0%	0%	21-Sep-26	10-Oct-26	09-Nov-26	28-Nov-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-10560	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	09-Nov-26	28-Nov-26	0.00	0.00	0.00	-41
EMERGENCY DOORS		25	0%	0%	15-Jul-26	12-Aug-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-10580	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-99
PRESSURE UNITS		25	0%	0%	13-Oct-26	10-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-10600	Material Delivery for Pressure Units	25	92.4%	0%	13-Oct-26	10-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-23
AIR LOCK DOORS		25	0%	0%	03-Oct-26	31-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-32
MLTX-02-005-PR-10620	Material Delivery for Lock Doors	25	100%	0%	03-Oct-26	31-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-32
CONSTRUCTION PHASE		186	83.69%	69.87%	30-Jul-26	07-Dec-26	01-Jun-26 A	12-Dec-26	1,090,060.01	909,968.16	1,302,439.33	-3
SITE WORKS		135	88.44%	71.5%	29-Sep-26	07-Dec-26	01-Jun-26 A	12-Dec-26	1,002,017.82	810,132.34	1,133,014.82	-3
LANDSCAPE WORKS		135	88.44%	71.5%	29-Sep-26	07-Dec-26	01-Jun-26 A	12-Dec-26	1,002,017.82	810,132.34	1,133,014.82	-3
PLAYGROUND AREA		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	12-Nov-26	180,520.67	144,416.54	180,520.67	-35
CURBSTOEN/INTERLOCK		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	12-Nov-26	180,520.67	144,416.54	180,520.67	-35
MLTX-02-005-CN-1196(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	12-Nov-26	180,520.67	144,416.54	180,520.67	-35
NATURAL GROUND		3	0%	70%	05-Dec-26	07-Dec-26	14-Oct-26 A	12-Nov-26	0.00	88,718.00	126,740.00	22
MLTX-02-005-CN-11980	Tartan Floor Installation Works for Landscape (Including Finishing Works)	3	0%	70%	05-Dec-26	07-Dec-26	14-Oct-26 A	12-Nov-26	0.00	88,718.00	126,740.00	22
PLANTING		101	100%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	12-Nov-26	347,251.46	240,773.38	347,251.46	-8
MLTX-02-005-CN-12050	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	3	100%	95%	24-Oct-26	26-Oct-26	03-Oct-26 A	12-Nov-26	104,175.44	98,966.67	104,175.44	-14
MLTX-02-005-CN-12060	Placement of Lawn Ground Cover (Rolling and Compaction)	3	100%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	12-Nov-26	141,732.50	70,866.25	141,732.50	-8
MLTX-02-005-CN-12070	Placement and Fixation of Trees	3	100%	70%	27-Oct-26	29-Oct-26	14-Oct-26 A	12-Nov-26	101,343.52	70,940.46	101,343.52	-11
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	09-Nov-26	367,633.90	294,107.12	367,633.90	-19
MLTX-02-005-CN-12000	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	09-Nov-26	187,554.12	150,043.30	187,554.12	-27

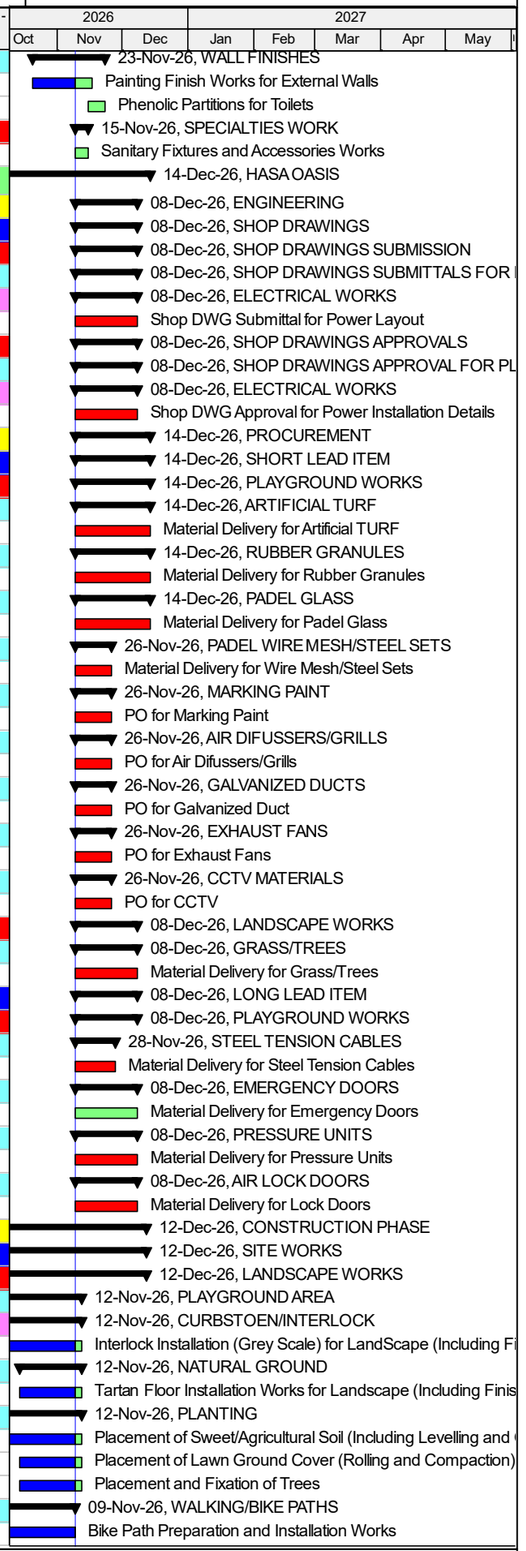

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-12010	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	09-Nov-26	180,079.78	144,063.82	180,079.78	-19
GENERAL/FURNITURE		48	96.16%	37.99%	15-Oct-26	16-Nov-26	14-Oct-26 A	12-Dec-26	106,611.79	42,117.30	110,868.79	-21
MLTX-02-005-CN-11970	Stamped Concrete Works for LandScape (Including Finishing Works)	18	100%	45%	18-Oct-26	07-Nov-26	14-Oct-26 A	30-Nov-26	93,594.00	42,117.30	93,594.00	-19
MLTX-02-005-CN-12440	Fixation and Installation of Steel Frame for Benches	28	75.36%	0%	15-Oct-26	16-Nov-26	09-Nov-26	12-Dec-26	13,017.79	0.00	17,274.79	-21
TOILET/SERVICE BUILDING		121	51.97%	58.93%	30-Jul-26	26-Nov-26	20-Sep-26 A	02-Dec-26	88,042.20	99,835.82	169,424.51	-4
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	30-Nov-26	16,607.28	14,946.55	16,607.28	-86
MLTX-02-005-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	30-Nov-26	16,607.28	14,946.55	16,607.28	-86
ELECTRICAL WORKS		20	20.5%	40%	04-Nov-26	26-Nov-26	03-Nov-26 A	02-Dec-26	20,985.38	40,947.08	102,367.69	-4
FIXTURE WORKS		20	20.5%	40%	04-Nov-26	26-Nov-26	03-Nov-26 A	02-Dec-26	20,985.38	40,947.08	102,367.69	-4
MLTX-02-005-CN-12840	Installing and Finish Works of Panel Boards	20	20.5%	40%	04-Nov-26	26-Nov-26	03-Nov-26 A	02-Dec-26	20,985.38	40,947.08	102,367.69	-4
FINISHING WORKS		3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	12-Nov-26	35,825.58	32,243.02	35,825.58	-19
WALL FINISHES		3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	12-Nov-26	35,825.58	32,243.02	35,825.58	-19
MLTX-02-005-CN-13010	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	12-Nov-26	35,825.58	32,243.02	35,825.58	-19
SPECIALTIES WORK		3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	12-Nov-26	14,623.96	11,699.17	14,623.96	-37
MLTX-02-005-CN-12700	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	12-Nov-26	14,623.96	11,699.17	14,623.96	-37
DAMMAM		167	37.65%	36.42%	21-May-26	31-Dec-26	06-Sep-26 A	24-Dec-26	276,751.91	267,751.36	735,145.44	7
PROCUREMENT		36	0%	0%	21-May-26	08-Dec-26	09-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
SHORT LEAD ITEM		36	0%	0%	21-May-26	08-Dec-26	09-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
PLAYGROUND WORKS		36	0%	0%	21-May-26	08-Dec-26	09-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	09-Nov-26	03-Dec-26	0.00	0.00	0.00	-143
MLTX-02-005-PR-11620	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	09-Nov-26	03-Dec-26	0.00	0.00	0.00	-143
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-PR-11880	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-138
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	09-Nov-26	12-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-11900	Material Delivery for Padel Glass	28	64.64%	0%	19-Oct-26	19-Nov-26	09-Nov-26	12-Dec-26	0.00	0.00	0.00	-18
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-133
MLTX-02-005-PR-11920	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-133
MARKING PAINT		15	0%	0%	02-Jul-26	19-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-11430	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-110
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-11730	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-11740	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-113
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	15-Nov-26	08-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-11760	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	15-Nov-26	08-Dec-26	0.00	0.00	0.00	-4
CCTV MATERIALS		5	0%	0%	30-Jul-26	04-Aug-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-11770	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-86
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	15-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-11790	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	15-Nov-26	22-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-11800	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	22-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
LANDSCAPE WORKS		5	0%	0%	15-Aug-26	19-Aug-26	22-Nov-26	28-Nov-26	0.00	0.00	0.00	-84
PAVEMENT MARKING		5	0%	0%	15-Aug-26	19-Aug-26	22-Nov-26	28-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-11120	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	22-Nov-26	28-Nov-26	0.00	0.00	0.00	-84
LONG LEAD ITEM		22	0%	0%	07-Sep-26	30-Nov-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
PLAYGROUND WORKS		22	0%	0%	07-Sep-26	30-Nov-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
STEEL TENSION CABLES		15	0%	0%	07-Sep-26	24-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-53
MLTX-02-005-PR-11640	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-53
EMERGENCY DOORS		15	0%	0%	04-Nov-26	21-Nov-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-11660	Material Delivery for Emergency Doors	15	27.33%	0%	04-Nov-26	21-Nov-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-4
PRESSURE UNITS		22	0%	0%	05-Nov-26	30-Nov-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-11680	Material Delivery for Pressure Units	10	31%	0%	05-Nov-26	16-Nov-26	09-Nov-26	21-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-12070	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	23-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
AIR LOCK DOORS		12	0%	0%	05-Nov-26	18-Nov-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-11700	Material Delivery for Lock Doors	12	25.83%	0%	05-Nov-26	18-Nov-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-3
CONSTRUCTION PHASE		167	37.65%	36.42%	18-Aug-26	31-Dec-26	06-Sep-26 A	24-Dec-26	276,751.91	267,751.36	735,145.44	7
SITE WORKS		113	41.42%	33.77%	15-Sep-26	31-Dec-26	20-Oct-26 A	26-Nov-26	245,520.67	200,158.56	592,772.13	31
LANDSCAPE WORKS		113	41.42%	33.77%	15-Sep-26	31-Dec-26	20-Oct-26 A	26-Nov-26	245,520.67	200,158.56	592,772.13	31
PLAYGROUND AREA		6	100%	40%	15-Sep-26	21-Sep-26	21-Oct-26 A	16-Nov-26	180,520.67	72,208.27	180,520.67	-46
CURBSTOEN/INTERLOCK		6	100%	40%	15-Sep-26	21-Sep-26	21-Oct-26 A	16-Nov-26	180,520.67	72,208.27	180,520.67	-46
MLTX-02-005-CN-1339(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	6	100%	40%	15-Sep-26	21-Sep-26	21-Oct-26 A	16-Nov-26	180,520.67	72,208.27	180,520.67	-46
NATURAL GROUND		15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	26-Nov-26	65,000.00	58,500.00	65,000.00	-26
MLTX-02-005-CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	26-Nov-26	65,000.00	58,500.00	65,000.00	-26
PLANTING		27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	21-Nov-26	0.00	69,450.29	347,251.46	36
MLTX-02-005-CN-13480	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	16-Nov-26	0.00	20,835.09	104,175.44	23
MLTX-02-005-CN-13490	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	20%	24-Dec-26	31-Dec-26	01-Nov-26 A	17-Nov-26	0.00	28,346.50	141,732.50	39

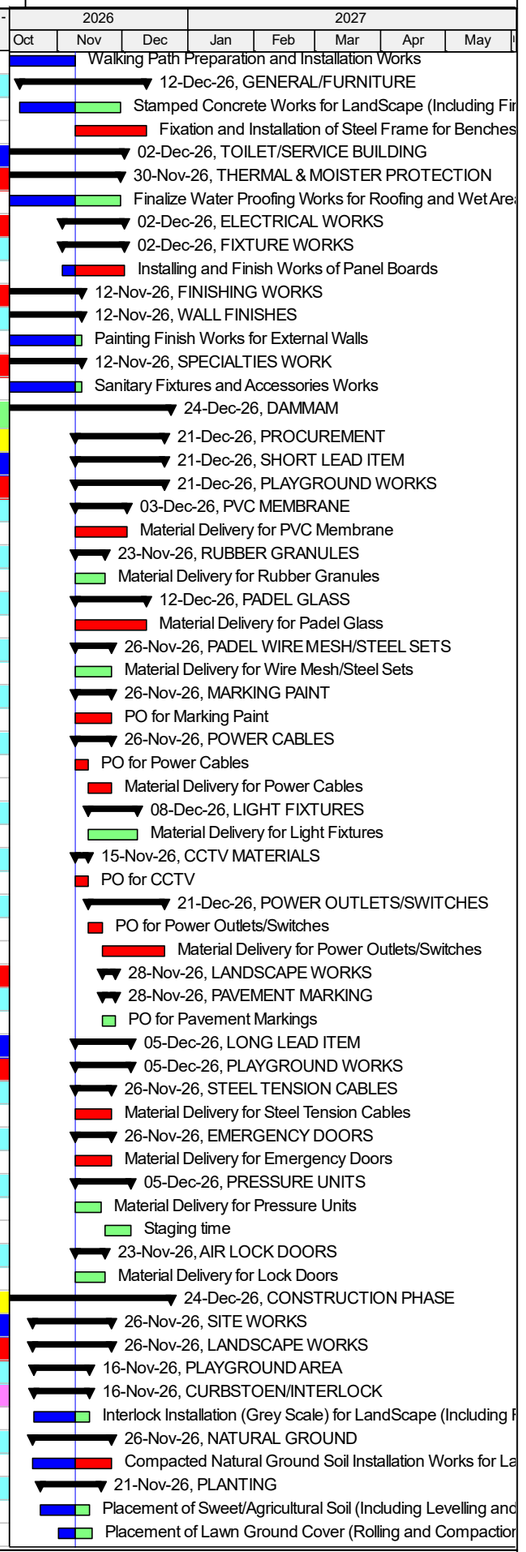

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-13500	Placement and Fixation of Trees	10	0%	20%	13-Dec-26	23-Dec-26	01-Nov-26 A	21-Nov-26	0.00	20,268.70	101,343.52	29
TOILET/SERVICE BUILDING		138	21.94%	47.48%	18-Aug-26	29-Dec-26	06-Sep-26 A	24-Dec-26	31,231.24	67,592.80	142,373.31	5
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	18-Nov-26	16,607.28	14,946.55	16,607.28	-70
MLTX-02-005-CN-14080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	18-Nov-26	16,607.28	14,946.55	16,607.28	-70
MECHANICAL WORK		12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
MLTX-02-005-CN-14240	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
ELECTRICAL WORKS		68	0%	37.5%	23-Nov-26	29-Dec-26	03-Nov-26 A	06-Dec-26	0.00	40,947.08	109,192.20	21
FIXTURE WORKS		68	0%	37.5%	23-Nov-26	29-Dec-26	03-Nov-26 A	06-Dec-26	0.00	40,947.08	109,192.20	21
MLTX-02-005-CN-14270	Installing and Finish Works of Panel Boards	21	0%	40%	06-Dec-26	29-Dec-26	03-Nov-26 A	03-Dec-26	0.00	40,947.08	102,367.69	23
MLTX-02-005-CN-14390	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	09-Nov-26	06-Dec-26	0.00	0.00	6,824.51	12
SPECIALTIES WORK		4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	24-Dec-26	14,623.96	11,699.17	14,623.96	-46
MLTX-02-005-CN-14130	Sanitary Fixtures and Accessories Works	4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	24-Dec-26	14,623.96	11,699.17	14,623.96	-46

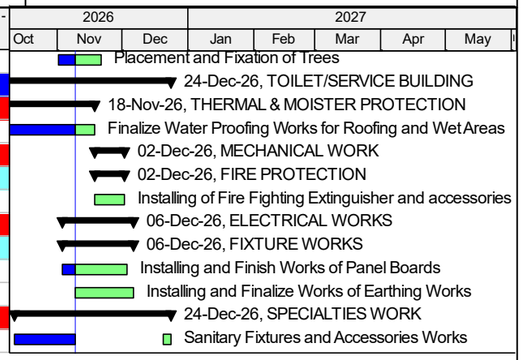

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation
