
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oa	314	43.81%	44.23%	03-Mar-26	02-Jan-27	03-Mar-26 A	15-Mar-27	13,142,789.86	13,266,772.75	29,997,851.67	-57
KEY MILESTONES		312	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	15-Mar-27	0.00	0.00	0.00	-57
GENERAL MILESTONES		312	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	15-Mar-27	0.00	0.00	0.00	-57
CONTRACTUAL MILESTONE		279	0%	0%	11-Apr-26	02-Jan-27	02-Apr-26 A	09-Mar-27	0.00	0.00	0.00	-55
ARAR		314	43.29%	40.54%	03-Mar-26	02-Jan-27	04-Mar-26 A	09-Mar-27	4,426,788.65	4,146,313.28	10,226,640.03	-55
MOBILIZATION		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	9
ENGINEERING		258	0%	0%	07-Mar-26	13-Dec-26	07-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	31
PROCUREMENT		210	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	10-Feb-27	0.00	0.00	0.00	-48
CONSTRUCTION PHASE		280	43.29%	40.54%	15-Apr-26	31-Dec-26	04-Apr-26 A	09-Mar-27	4,426,788.65	4,146,313.28	10,226,640.03	-56
SITE WORKS		276	39.9%	36.6%	15-Apr-26	30-Dec-26	04-Apr-26 A	09-Mar-27	3,614,296.25	3,315,861.28	9,058,565.25	-57
EARTH WORKS		68	100%	100%	15-Apr-26	06-Jul-26	04-Apr-26 A	05-Aug-26 A	494,887.02	494,887.02	494,887.02	-25
LANDSCAPE WORKS		243	36.4%	32.48%	24-May-26	30-Dec-26	17-May-26 A	09-Mar-27	3,095,514.70	2,762,480.93	8,505,184.90	-57
PLAYGROUND AREA		224	54.93%	53.84%	24-May-26	27-Dec-26	19-May-26 A	08-Feb-27	752,566.34	737,620.36	1,369,978.66	-36
FOOTBALL PLAYGROUND		215	35%	35%	24-May-26	13-Dec-26	19-May-26 A	03-Feb-27	110,897.50	110,897.50	316,849.99	-44
PADEL PLAYGROUND		195	45%	70%	20-Jun-26	19-Dec-26	19-May-26 A	03-Feb-27	105,292.80	163,788.80	233,984.00	-39
BASKETBALL PLAYGROUND		178	69.52%	69.52%	14-Jul-26	23-Dec-26	19-May-26 A	08-Feb-27	221,133.58	221,133.58	318,089.68	-39
PADEL FENCE		98	96.19%	4.22%	01-Sep-26	16-Nov-26	08-Aug-26 A	26-Dec-26	133,458.11	5,859.94	138,749.98	-33
CURBSTOEN/INTERLOCK		112	50.17%	65.12%	06-Oct-26	27-Dec-26	15-Aug-26 A	02-Dec-26	181,784.34	235,940.54	362,305.01	22
AIR DOME		121	23.18%	23.18%	26-Sep-26	21-Dec-26	17-May-26 A	14-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-46
CIVIL WORKS		107	48.29%	48.29%	26-Sep-26	07-Dec-26	17-May-26 A	28-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-44
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	1,233,296.81	-43
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	01-Feb-27	13-Feb-27	0.00	0.00	1,513,591.54	-46
FINISHES WORKS		9	0%	0%	15-Dec-26	21-Dec-26	03-Feb-27	14-Feb-27	0.00	0.00	168,176.84	-46
IRRIGATION NETWORK		145	83.53%	83.53%	28-Jun-26	30-Nov-26	18-Aug-26 A	15-Dec-26	127,308.67	127,308.67	152,414.87	-12
NATURAL GROUND		20	0%	30.51%	17-Nov-26	30-Nov-26	27-Oct-26 A	15-Dec-26	0.00	58,500.00	191,740.00	-12
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	16-Nov-26	347,251.46	104,175.44	347,251.46	-13
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	367,633.90	183,816.95	367,633.90	-21
GENERAL/FURNITURE		120	42.79%	53.49%	19-Oct-26	30-Dec-26	03-Oct-26 A	09-Mar-27	201,226.82	251,532.00	470,271.40	-57
PARKING		24	40.85%	100%	01-Nov-26	28-Nov-26	16-May-26 A	12-Oct-26 A	23,894.53	58,493.33	58,493.33	40
TOILET/SERVICE BUILDING		216	69.56%	71.1%	02-Jul-26	31-Dec-26	21-May-26 A	06-Feb-27	812,492.40	830,452.00	1,168,074.78	-30
STRUCTURE WORKS		58	100%	100%	02-Jul-26	07-Sep-26	21-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	31
MASONARY WORK		5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
THERMAL & MOISTER PROTECTION		54	100%	100%	29-Aug-26	21-Sep-26	26-Sep-26 A	07-Nov-26 A	34,698.32	34,698.32	34,698.32	-39
MECHANICAL WORK		167	62.8%	79%	16-Jul-26	19-Dec-26	18-Jul-26 A	31-Dec-26	166,205.09	209,102.06	264,673.10	-10
ELECTRICAL WORKS		124	53.82%	53.29%	13-Sep-26	19-Dec-26	19-Jul-26 A	06-Feb-27	208,264.67	206,217.32	386,998.59	-41
DOORS/WINDOWS		120	88.57%	100%	17-Sep-26	31-Dec-26	20-Oct-26 A	02-Nov-26 A	60,445.68	68,245.12	68,245.12	52
METAL WORKS		75	57.14%	71.43%	14-Sep-26	23-Nov-26	16-Sep-26 A	19-Nov-26	7,799.44	9,749.30	13,649.02	4
FINISHING WORKS		102	87.44%	76.6%	22-Sep-26	12-Dec-26	10-Aug-26 A	14-Jan-27	145,271.41	127,256.05	166,130.97	-28
SPECIALTIES WORK		75	25%	0%	18-Oct-26	17-Dec-26	09-Nov-26	04-Feb-27	14,623.96	0.00	58,495.83	-41
TESTING & COMMISSIONING		26	0%	0%	20-Dec-26	02-Jan-27	06-Feb-27	09-Mar-27	0.00	0.00	0.00	-55
HASA OASIS		312	44.72%	48.06%	03-Mar-26	02-Jan-27	04-Mar-26 A	03-Mar-27	4,451,927.78	4,785,309.30	9,955,979.43	-50
MOBILIZATION		32	0%	0%	03-Mar-26	12-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
ENGINEERING		254	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	06-Jan-27	0.00	0.00	0.00	-16
PROCUREMENT		220	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	31-Jan-27	0.00	0.00	0.00	-51
CONSTRUCTION PHASE		293	44.72%	48.06%	29-Mar-26	31-Dec-26	04-Apr-26 A	23-Feb-27	4,451,927.78	4,785,309.30	9,955,979.43	-44
SITE WORKS		292	40.4%	42.81%	29-Mar-26	31-Dec-26	04-Apr-26 A	23-Feb-27	3,551,206.88	3,763,219.05	8,789,975.14	-44
EARTH WORKS		43	100%	100%	29-Mar-26	17-May-26	04-Apr-26 A	08-Aug-26 A	294,826.31	294,826.31	294,826.31	-67
LANDSCAPE WORKS		251	38.6%	40.42%	16-May-26	31-Dec-26	16-May-26 A	23-Feb-27	3,256,380.57	3,409,899.41	8,436,655.50	-44
PLAYGROUND AREA		251	74.56%	76.9%	16-May-26	31-Dec-26	18-May-26 A	23-Feb-27	970,403.66	1,000,815.42	1,301,449.27	-44
FOOTBALL PLAYGROUND		200	84.07%	85%	16-May-26	09-Dec-26	18-May-26 A	09-Jan-27	266,380.31	269,322.49	316,849.99	-25
PADEL PLAYGROUND		198	45%	70%	11-Jun-26	31-Dec-26	18-May-26 A	30-Jan-27	105,292.80	163,788.80	233,984.00	-24
BASKETBALL PLAYGROUND		176	70.92%	70.92%	07-Jul-26	31-Dec-26	18-May-26 A	30-Jan-27	236,425.54	236,425.54	333,381.64	-24
PADEL FENCE		87	0%	9.24%	28-Nov-26	31-Dec-26	06-Aug-26 A	23-Feb-27	0.00	5,077.72	54,928.63	-44
CURBSTOEN/INTERLOCK		19	100%	90.03%	09-Sep-26	01-Oct-26	12-Aug-26 A	12-Nov-26	362,305.01	326,200.88	362,305.01	-35
AIR DOME		165	23.18%	23.18%	30-Jul-26	10-Dec-26	16-May-26 A	09-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-51
CIVIL WORKS		155	48.29%	48.29%	30-Jul-26	07-Dec-26	16-May-26 A	28-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-44
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	1,233,296.81	-39
ELECTRICAL WORKS		14	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	09-Feb-27	0.00	0.00	1,513,591.54	-51
FINISHES WORKS		30	0%	0%	15-Nov-26	10-Dec-26	05-Jan-27	09-Feb-27	0.00	0.00	168,176.84	-51
IRRIGATION NETWORK		111	52.94%	83.53%	03-Sep-26	07-Dec-26	18-Jul-26 A	12-Jan-27	80,689.03	127,308.67	152,414.87	-30
NATURAL GROUND		15	0%	80.17%	29-Nov-26	07-Dec-26	13-Oct-26 A	12-Nov-26	0.00	153,718.00	191,740.00	22
PLANTING		101	100%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	12-Nov-26	347,251.46	240,773.38	347,251.46	-8
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	09-Nov-26	367,633.90	294,107.12	367,633.90	-19

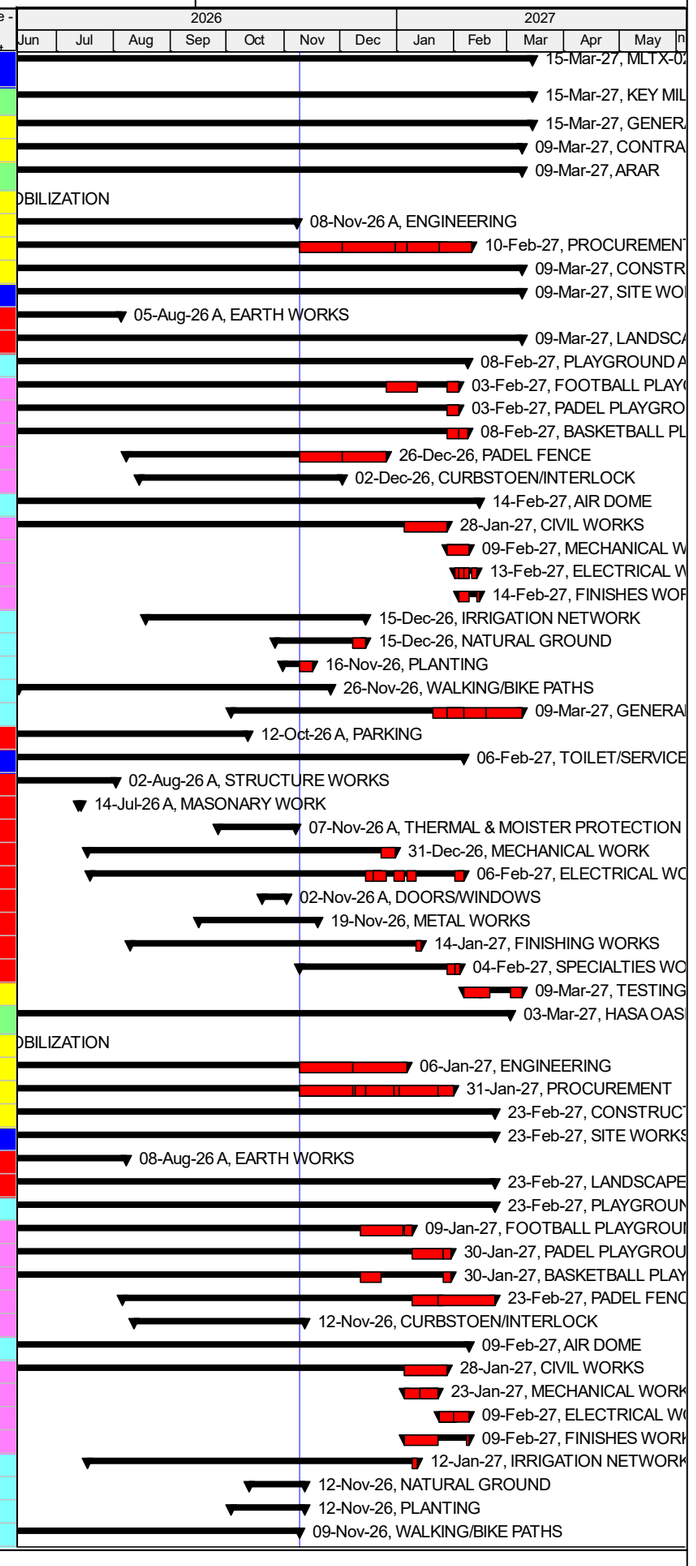

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	103	40.59%	62.44%	06-Oct-26	24-Dec-26	03-Sep-26 A	03-Feb-27	190,875.01	293,649.30	470,271.40	-34
	PARKING	12	0%	100%	24-Nov-26	07-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	68
	TOILET/SERVICE BUILDING	258	77.25%	87.66%	09-May-26	23-Dec-26	24-May-26 A	04-Feb-27	900,720.90	1,022,090.25	1,166,004.29	-36
	STRUCTURE WORKS	45	100%	100%	09-May-26	02-Jul-26	24-May-26 A	10-Aug-26 A	162,899.73	162,899.73	162,899.73	-33
	MASONARY WORK	5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
	THERMAL & MOISTER PROTECTION	41	100%	95.21%	04-Jul-26	19-Aug-26	10-Sep-26 A	30-Nov-26	34,698.32	33,037.59	34,698.32	-86
	MECHANICAL WORK	112	99.26%	99.26%	24-Aug-26	21-Dec-26	12-Jul-26 A	03-Jan-27	262,723.23	262,723.23	264,673.10	-10
	ELECTRICAL WORKS	128	58.71%	71.78%	03-Sep-26	21-Dec-26	14-Jul-26 A	01-Feb-27	227,202.96	277,771.03	386,998.85	-35
	DOORS/WINDOWS	213	14.29%	100%	04-Jul-26	16-Dec-26	28-Sep-26 A	28-Oct-26 A	9,749.30	68,245.12	68,245.12	43
	METAL WORKS	65	100%	71.43%	03-Sep-26	20-Oct-26	06-Sep-26 A	19-Dec-26	13,649.02	9,749.30	13,649.02	-50
	FINISHING WORKS	121	99.29%	97.1%	20-Aug-26	16-Dec-26	17-Aug-26 A	04-Feb-27	162,890.28	159,307.72	164,060.22	-42
	SPECIALTIES WORK	74	25%	61.67%	27-Sep-26	23-Dec-26	04-Oct-26 A	22-Dec-26	14,623.96	36,072.43	58,495.83	2
	TESTING & COMMISSIONING	28	0%	0%	08-Dec-26	02-Jan-27	28-Jan-27	03-Mar-27	0.00	0.00	0.00	-50
	DAMMAM	307	43.44%	44.17%	03-Mar-26	02-Jan-27	04-Mar-26 A	06-Mar-27	4,264,073.43	4,335,150.18	9,815,232.20	-52
	MOBILIZATION	33	0%	0%	03-Mar-26	13-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
	ENGINEERING	253	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	08-Nov-26 A	0.00	0.00	0.00	30
	PROCUREMENT	251	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	04-Jan-27	0.00	0.00	0.00	-11
	CONSTRUCTION PHASE	272	43.44%	44.17%	16-Apr-26	31-Dec-26	04-Apr-26 A	06-Mar-27	4,264,073.43	4,335,150.18	9,815,232.20	-53
	SITE WORKS	272	38.81%	38.33%	16-Apr-26	31-Dec-26	04-Apr-26 A	06-Mar-27	3,356,401.70	3,315,131.98	8,649,227.95	-53
	EARTH WORKS	44	100%	100%	16-Apr-26	09-Jun-26	04-Apr-26 A	13-Aug-26 A	263,237.78	263,237.78	263,237.78	-55
	LANDSCAPE WORKS	250	36.44%	35.95%	12-May-26	31-Dec-26	19-May-26 A	06-Mar-27	3,034,670.59	2,993,400.87	8,327,496.85	-53
	PLAYGROUND AREA	239	78.93%	71.01%	12-May-26	31-Dec-26	19-May-26 A	17-Feb-27	1,015,120.79	913,315.20	1,286,157.31	-40
	FOOTBALL PLAYGROUND	227	85%	85%	12-May-26	15-Dec-26	19-May-26 A	06-Feb-27	269,322.49	269,322.49	316,849.99	-44
	PADEL PLAYGROUND	225	70%	70%	24-May-26	24-Dec-26	19-May-26 A	15-Feb-27	163,788.80	163,788.80	233,984.00	-44
	BASKETBALL PLAYGROUND	176	69.07%	69.52%	26-Jul-26	31-Dec-26	19-May-26 A	17-Feb-27	219,704.49	221,133.58	318,089.68	-40
	PADEL FENCE	62	0%	9.24%	25-Nov-26	24-Dec-26	08-Aug-26 A	06-Feb-27	0.00	5,077.72	54,928.63	-36
	CURBSTOEN/INTERLOCK	150	100%	70.1%	27-Aug-26	21-Sep-26	10-Aug-26 A	16-Nov-26	362,305.01	253,992.61	362,305.01	-46
	AIR DOME	201	23.18%	23.18%	18-Jun-26	24-Dec-26	14-Jul-26 A	09-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-39
	CIVIL WORKS	191	48.29%	48.29%	18-Jun-26	07-Dec-26	14-Jul-26 A	28-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-44
	MECHANICAL WORKS	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	1,233,296.81	-44
	ELECTRICAL WORKS	10	0%	0%	08-Dec-26	24-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	1,513,591.54	-39
	FINISHES WORKS	4	0%	0%	12-Dec-26	15-Dec-26	01-Feb-27	06-Feb-27	0.00	0.00	168,176.84	-44
	IRRIGATION NETWORK	133	83.53%	83.53%	10-Sep-26	02-Dec-26	24-Aug-26 A	14-Feb-27	127,308.67	127,308.67	152,414.87	-62
	NATURAL GROUND	46	82.81%	30.51%	10-Oct-26	12-Nov-26	20-Oct-26 A	14-Dec-26	158,787.60	58,500.00	191,740.00	-26
	PLANTING	27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	21-Nov-26	0.00	69,450.29	347,251.46	36
	WALKING/BIKE PATHS	31	100%	100%	22-Sep-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	273,767.20	273,767.20	273,767.20	35
	GENERAL/FURNITURE	139	34.06%	53.49%	22-Sep-26	31-Dec-26	20-Sep-26 A	06-Mar-27	160,158.82	251,532.00	470,271.40	-53
	PARKING	15	100%	100%	14-Oct-26	31-Oct-26	18-Jul-26 A	19-Sep-26 A	58,493.33	58,493.33	58,493.33	35
	TOILET/SERVICE BUILDING	218	77.84%	87.48%	01-Jun-26	29-Dec-26	23-May-26 A	11-Feb-27	907,671.73	1,020,018.20	1,166,004.25	-37
	STRUCTURE WORKS	54	100%	100%	01-Jun-26	02-Aug-26	23-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	0
	MASONARY WORK	5	100%	100%	06-Jul-26	11-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	2
	THERMAL & MOISTER PROTECTION	21	100%	95.21%	03-Aug-26	26-Aug-26	25-Aug-26 A	18-Nov-26	34,698.32	33,037.59	34,698.32	-70
	MECHANICAL WORK	71	99.26%	99.26%	09-Sep-26	26-Dec-26	12-Jul-26 A	02-Dec-26	262,723.23	262,723.23	264,673.10	21
	ELECTRICAL WORKS	117	53.29%	70.01%	12-Sep-26	29-Dec-26	14-Jul-26 A	03-Jan-27	206,217.55	270,946.49	386,998.82	-3
	DOORS/WINDOWS	118	91.43%	100%	19-Sep-26	27-Dec-26	17-Sep-26 A	26-Oct-26 A	62,395.54	68,245.12	68,245.12	53
	METAL WORKS	77	100%	71.43%	10-Sep-26	26-Oct-26	05-Sep-26 A	24-Dec-26	13,649.02	9,749.30	13,649.02	-50
	FINISHING WORKS	106	84.23%	100%	27-Aug-26	21-Dec-26	17-Aug-26 A	04-Nov-26 A	138,180.28	164,060.21	164,060.21	41
	SPECIALTIES WORK	53	25%	61.67%	27-Oct-26	23-Dec-26	12-Oct-26 A	11-Feb-27	14,623.96	36,072.43	58,495.83	-42
	TESTING & COMMISSIONING	8	0%	0%	24-Dec-26	02-Jan-27	24-Feb-27	06-Mar-27	0.00	0.00	0.00	-52
	PROJECT CLOSEOUT & DEMOBILIZATION	35	0%	0%	08-Dec-26	02-Jan-27	28-Jan-27	15-Mar-27	0.00	0.00	0.00	-57
	As-Built DWGs	27	0%	0%	08-Dec-26	31-Dec-26	28-Jan-27	02-Mar-27	0.00	0.00	0.00	-50
	Demobilization	12	0%	0%	28-Dec-26	02-Jan-27	25-Feb-27	15-Mar-27	0.00	0.00	0.00	-57

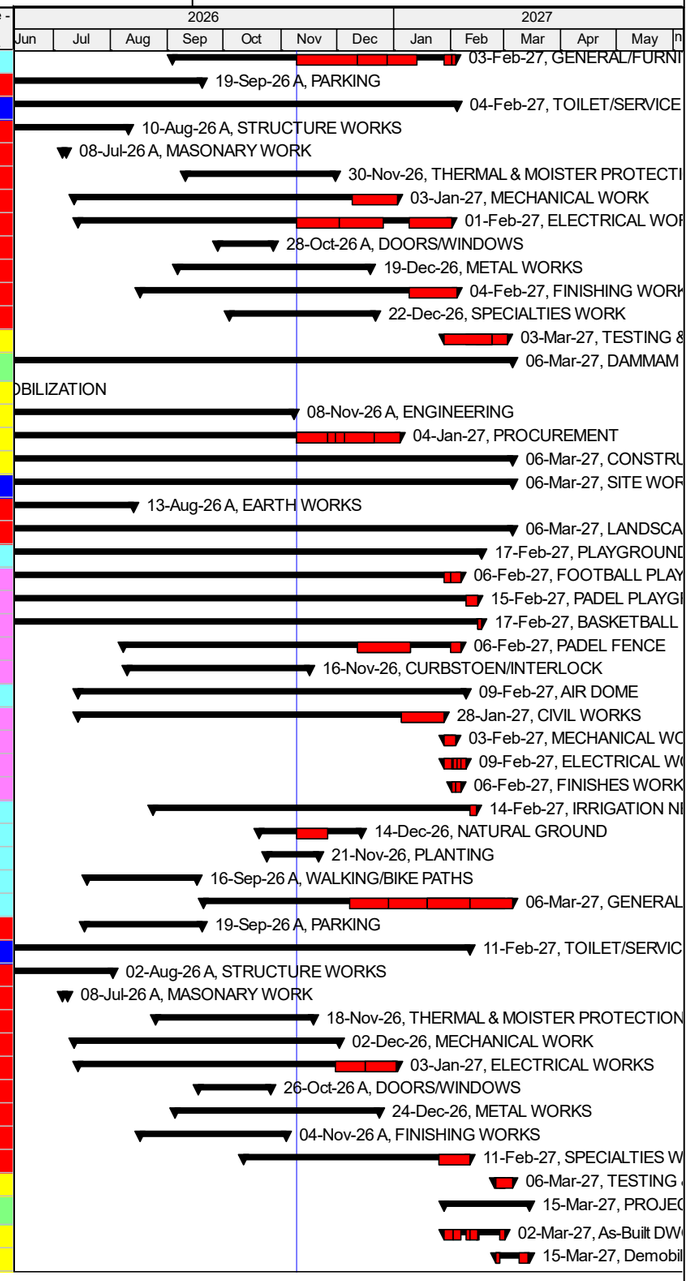

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
