MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oa		190	14.22%	8.82%	04-May-26	02-Jan-27	01-Jun-26 A	15-Mar-27	2,609,156.17	1,617,923.10	18,349,002.01	-57
KEY MILESTONES		54	0%	0%	17-Dec-26	02-Jan-27	06-Jan-27	15-Mar-27	0.00	0.00	0.00	-57
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	15-Mar-27	15-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		15-Mar-27	0.00	0.00	0.00	-57
CONTRACTUAL MILESTONE		52	0%	0%	17-Dec-26	02-Jan-27	06-Jan-27	09-Mar-27	0.00	0.00	0.00	-55
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		02-Jan-27		09-Mar-27	0.00	0.00	0.00	-55
MLTX-02-005-MS-1100	Completion of Engineering	0	0%	0%		17-Dec-26		06-Jan-27	0.00	0.00	0.00	-16
MLTX-02-005-MS-1130	Completion of Toilet Building	0	0%	0%		31-Dec-26		23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		31-Dec-26		23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		31-Dec-26		09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		31-Dec-26		09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		31-Dec-26		23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		31-Dec-26		06-Mar-27	0.00	0.00	0.00	-53
ARAR		132	16.2%	6.75%	15-Jul-26	02-Jan-27	11-Jun-26 A	09-Mar-27	1,056,057.99	440,203.59	6,520,530.33	-55
PROCUREMENT		80	0%	0%	15-Jul-26	15-Dec-26	09-Nov-26	10-Feb-27	0.00	0.00	0.00	-48
SHORT LEAD ITEM		80	0%	0%	15-Jul-26	15-Dec-26	09-Nov-26	10-Feb-27	0.00	0.00	0.00	-48
TOILET/SERVICE WORKS		69	0%	0%	30-Aug-26	28-Nov-26	09-Nov-26	28-Jan-27	0.00	0.00	0.00	-52
SWITCHES/SOCKETS		27	0%	0%	28-Oct-26	28-Nov-26	09-Nov-26	10-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-8	Material Delivery for Switches/Sockets	27	37.41%	0%	28-Oct-26	28-Nov-26	09-Nov-26	10-Dec-26	0.00	0.00	0.00	-10
DISTRIBUTION PANNELS		15	0%	0%	04-Oct-26	20-Oct-26	13-Dec-26	30-Dec-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-8	Material Delivery for Distribution Panels	15	100%	0%	04-Oct-26	20-Oct-26	13-Dec-26	30-Dec-26	0.00	0.00	0.00	-60
FURNITURES		69	0%	0%	30-Aug-26	19-Nov-26	09-Nov-26	28-Jan-27	0.00	0.00	0.00	-59
MLTX-02-005-PR-8	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	09-Nov-26	13-Dec-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-8	Material Delivery for Furnitures	40	75.25%	0%	05-Oct-26	19-Nov-26	13-Dec-26	28-Jan-27	0.00	0.00	0.00	-59
PLAYGROUND WORKS		80	0%	0%	15-Jul-26	15-Dec-26	09-Nov-26	10-Feb-27	0.00	0.00	0.00	-48
PVC MEMBRANE		21	0%	0%	29-Sep-26	22-Oct-26	26-Nov-26	21-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	Material Delivery for PVC Membrane	21	100%	0%	29-Sep-26	22-Oct-26	26-Nov-26	21-Dec-26	0.00	0.00	0.00	-50
ARTIFICIAL TURF		12	0%	0%	26-Oct-26	08-Nov-26	21-Dec-26	04-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-8	Material Delivery for Artificial TURF	12	100%	0%	26-Oct-26	08-Nov-26	21-Dec-26	04-Jan-27	0.00	0.00	0.00	-48
RUBBER GRANULES		32	0%	0%	10-Oct-26	15-Nov-26	26-Nov-26	03-Jan-27	0.00	0.00	0.00	-41
MLTX-02-005-PR-8	Material Delivery for Rubber Granules	32	81.56%	0%	10-Oct-26	15-Nov-26	26-Nov-26	03-Jan-27	0.00	0.00	0.00	-41
PADEL GLASS		18	0%	0%	16-Nov-26	06-Dec-26	04-Jan-27	25-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-8	Material Delivery for Padel Glass	18	0%	0%	16-Nov-26	06-Dec-26	04-Jan-27	25-Jan-27	0.00	0.00	0.00	-42
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-8	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-59
BITUMINOUS BASE & WEARING COURSE		27	0%	0%	29-Sep-26	29-Oct-26	26-Nov-26	28-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	Material Delivery for the Site	27	100%	0%	29-Sep-26	29-Oct-26	26-Nov-26	28-Dec-26	0.00	0.00	0.00	-50
MARKING PAINT		32	0%	0%	10-Sep-26	19-Oct-26	09-Nov-26	16-Dec-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	Material Delivery for Marking Paint	17	100%	0%	30-Sep-26	19-Oct-26	26-Nov-26	16-Dec-26	0.00	0.00	0.00	-49
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Sep-26	21-Oct-26	26-Nov-26	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	PO for Air Difussers/Grills	5	100%	0%	29-Sep-26	04-Oct-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	Material Delivery for Air Difussers/Grills	15	100%	0%	05-Oct-26	21-Oct-26	02-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
DISTRIBUTION BOARDS		20	0%	0%	29-Sep-26	21-Oct-26	26-Nov-26	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	PO for Distribution Boards	5	100%	0%	29-Sep-26	04-Oct-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	Material Delivery for Distribution Boards	15	100%	0%	05-Oct-26	21-Oct-26	02-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
POWER CABLES		60	0%	0%	05-Oct-26	15-Dec-26	02-Dec-26	10-Feb-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-9	PO for Power Cables	5	100%	0%	05-Oct-26	10-Oct-26	02-Dec-26	08-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	Material Delivery for Power Cables	30	0%	0%	11-Nov-26	15-Dec-26	06-Jan-27	10-Feb-27	0.00	0.00	0.00	-48
LIGHT FIXTURES		10	0%	0%	11-Oct-26	21-Oct-26	08-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	100%	0%	11-Oct-26	21-Oct-26	08-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
CCTV MATERIALS		50	0%	0%	26-Sep-26	10-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-9	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-38
MLTX-02-005-PR-9	Material Delivery for CCTV	15	87.33%	0%	25-Oct-26	10-Nov-26	20-Dec-26	06-Jan-27	0.00	0.00	0.00	-48
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-99
LANDSCAPE WORKS		62	0%	0%	15-Jul-26	23-Nov-26	09-Nov-26	20-Jan-27	0.00	0.00	0.00	-49
PAVEMENT MARKING		62	0%	0%	15-Jul-26	23-Nov-26	09-Nov-26	20-Jan-27	0.00	0.00	0.00	-49
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	30	57%	0%	20-Oct-26	23-Nov-26	16-Dec-26	20-Jan-27	0.00	0.00	0.00	-49
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-49
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-17

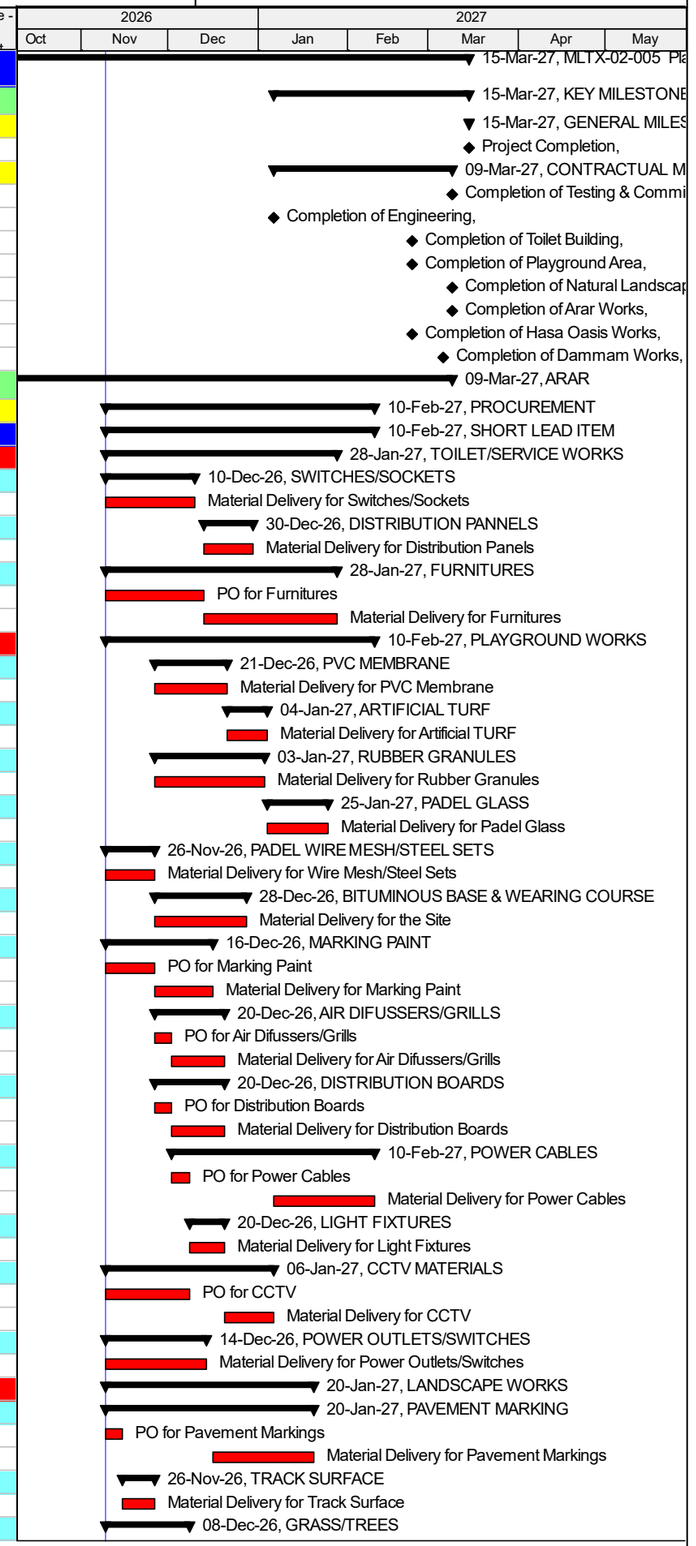

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	25	68.4%	0%	20-Oct-26	17-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-17
LONG LEAD ITEM		65	0%	0%	27-Sep-26	10-Dec-26	09-Nov-26	24-Jan-27	0.00	0.00	0.00	-37
PLAYGROUND WORKS		65	0%	0%	27-Sep-26	10-Dec-26	09-Nov-26	24-Jan-27	0.00	0.00	0.00	-37
STEEL TENSION CABLES		27	0%	0%	27-Sep-26	27-Oct-26	09-Nov-26	10-Dec-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-9	Staging time	12	100%	0%	14-Oct-26	27-Oct-26	26-Nov-26	10-Dec-26	0.00	0.00	0.00	-37
EMERGENCY DOORS		65	0%	0%	26-Oct-26	05-Dec-26	09-Nov-26	24-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	20	60.5%	0%	26-Oct-26	17-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-9	Staging time	15	0%	0%	18-Nov-26	05-Dec-26	06-Jan-27	24-Jan-27	0.00	0.00	0.00	-42
PRESSURE UNITS		30	0%	0%	26-Oct-26	29-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	48.4%	0%	26-Oct-26	23-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-9	Staging time	5	0%	0%	24-Nov-26	29-Nov-26	08-Dec-26	14-Dec-26	0.00	0.00	0.00	-12
AIR LOCK DOORS		50	0%	0%	14-Oct-26	10-Dec-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-22
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	100%	0%	14-Oct-26	05-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	8.4%	0%	07-Nov-26	05-Dec-26	02-Dec-26	31-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-9	Staging time	5	0%	0%	06-Dec-26	10-Dec-26	31-Dec-26	06-Jan-27	0.00	0.00	0.00	-22
CONSTRUCTION PHASE		132	16.2%	6.75%	14-Sep-26	30-Dec-26	11-Jun-26 A	09-Mar-27	1,056,057.99	440,203.59	6,520,530.33	-57
SITE WORKS		132	15.52%	6.52%	17-Sep-26	30-Dec-26	11-Jun-26 A	09-Mar-27	953,352.32	400,648.59	6,143,352.55	-57
LANDSCAPE WORKS		132	15.52%	6.52%	17-Sep-26	30-Dec-26	11-Jun-26 A	09-Mar-27	953,352.32	400,648.59	6,143,352.55	-57
PLAYGROUND AREA		83	18.59%	7.89%	01-Oct-26	27-Dec-26	04-Nov-26 A	08-Feb-27	127,598.17	54,156.20	686,514.50	-36
FOOTBALL PLAYGROUND		34	0%	0%	17-Nov-26	13-Dec-26	26-Dec-26	03-Feb-27	0.00	0.00	205,952.49	-44
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	15	0%	0%	17-Nov-26	03-Dec-26	26-Dec-26	12-Jan-27	0.00	0.00	158,424.99	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	31,685.00	-44
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	15,842.50	-44
PADEL PLAYGROUND		5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	70,195.20	-39
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	58,496.00	-39
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	11,699.20	-39
BASKETBALL PLAYGROUND		9	0%	0%	14-Dec-26	23-Dec-26	28-Jan-27	08-Feb-27	0.00	0.00	96,956.10	-39
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	5	0%	0%	14-Dec-26	19-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	80,796.75	-39
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	4	0%	0%	20-Dec-26	23-Dec-26	03-Feb-27	08-Feb-27	0.00	0.00	16,159.35	-39
PADEL FENCE		40	96.02%	0%	01-Oct-26	16-Nov-26	09-Nov-26	26-Dec-26	127,598.17	0.00	132,890.04	-33
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	09-Nov-26	02-Dec-26	30,677.48	0.00	30,677.48	-33
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	20	65.5%	0%	25-Oct-26	16-Nov-26	02-Dec-26	26-Dec-26	10,046.88	0.00	15,338.75	-33
MLTX-02-005-CI	Install of Fence Gates	12	42.5%	0%	03-Nov-26	16-Nov-26	12-Dec-26	26-Dec-26	86,873.81	0.00	86,873.81	-33
CURBSTOEN/INTERLOCK		20	0%	30%	05-Dec-26	27-Dec-26	04-Nov-26 A	02-Dec-26	0.00	54,156.20	180,520.67	22
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	30%	05-Dec-26	27-Dec-26	04-Nov-26 A	02-Dec-26	0.00	54,156.20	180,520.67	22
AIR DOME		34	0%	0%	15-Nov-26	21-Dec-26	05-Jan-27	14-Feb-27	0.00	0.00	4,306,367.09	-46
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	1,391,301.90	-44
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	942,830.33	-44
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-44
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	1,233,296.81	-43
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	728,766.30	-43
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	336,353.67	-43
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	168,176.84	-43
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	01-Feb-27	13-Feb-27	0.00	0.00	1,513,591.54	-46
MLTX-02-005-CI	Light Fixture Works (Air Dome)	7	0%	0%	13-Dec-26	20-Dec-26	01-Feb-27	09-Feb-27	0.00	0.00	224,235.78	-43
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	03-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-43
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	03-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-43
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	3	0%	0%	17-Dec-26	20-Dec-26	06-Feb-27	09-Feb-27	0.00	0.00	504,530.51	-43
MLTX-02-005-CI	Control System Installation (Air Dome)	2	0%	0%	19-Dec-26	20-Dec-26	10-Feb-27	13-Feb-27	0.00	0.00	448,471.57	-46
FINISHES WORKS		9	0%	0%	15-Dec-26	21-Dec-26	03-Feb-27	14-Feb-27	0.00	0.00	168,176.84	-46
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	5	0%	0%	15-Dec-26	20-Dec-26	03-Feb-27	09-Feb-27	0.00	0.00	112,117.89	-43
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	1	0%	0%	21-Dec-26	21-Dec-26	13-Feb-27	14-Feb-27	0.00	0.00	56,058.95	-46
IRRIGATION NETWORK		3	0%	0%	28-Nov-26	30-Nov-26	12-Dec-26	15-Dec-26	0.00	0.00	25,106.20	-12
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	28-Nov-26	30-Nov-26	12-Dec-26	15-Dec-26	0.00	0.00	25,106.20	-12
NATURAL GROUND		20	0%	30.51%	17-Nov-26	30-Nov-26	27-Oct-26 A	15-Dec-26	0.00	58,500.00	191,740.00	-12
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	6	0%	0%	24-Nov-26	30-Nov-26	08-Dec-26	15-Dec-26	0.00	0.00	126,740.00	-12
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	90%	17-Nov-26	23-Nov-26	27-Oct-26 A	16-Nov-26	0.00	58,500.00	65,000.00	7
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	16-Nov-26	347,251.46	104,175.44	347,251.46	-13
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	100%	30%	17-Sep-26	24-Sep-26	31-Oct-26 A	16-Nov-26	104,175.44	31,252.63	104,175.44	-44
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	4	100%	30%	27-Oct-26	31-Oct-26	31-Oct-26 A	14-Nov-26	141,732.50	42,519.75	141,732.50	-11
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	100%	30%	26-Sep-26	30-Sep-26	31-Oct-26 A	15-Nov-26	101,343.52	30,403.06	101,343.52	-38
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	367,633.90	183,816.95	367,633.90	-21
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	26-Nov-26	187,554.12	93,777.06	187,554.12	-33

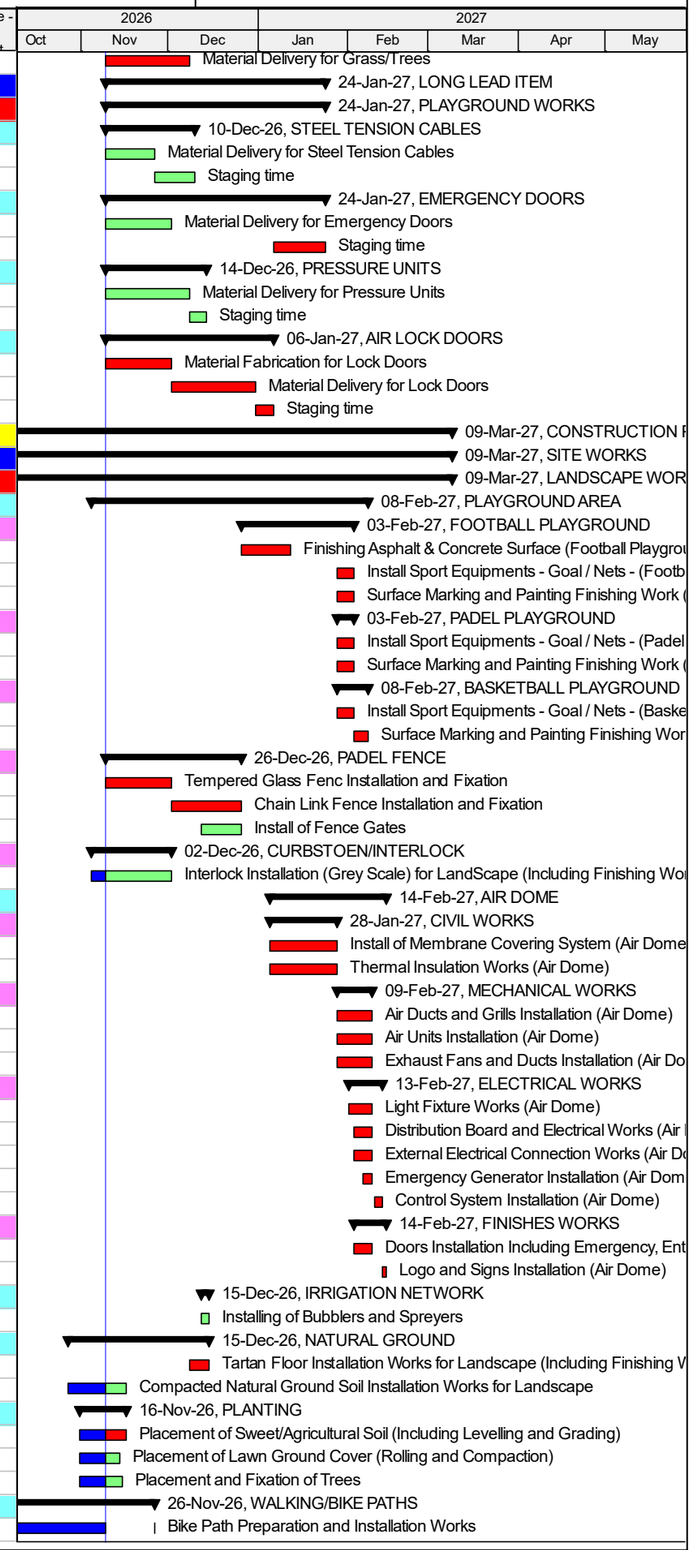

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	100%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	26-Nov-26	180,079.78	90,039.89	180,079.78	-21
GENERAL/FURNITURE		87	50.69%	0%	27-Oct-26	30-Dec-26	26-Nov-26	09-Mar-27	110,868.79	0.00	218,739.40	-57
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	100%	0%	02-Nov-26	07-Nov-26	26-Nov-26	02-Dec-26	93,594.00	0.00	93,594.00	-21
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	14-Dec-26	30-Dec-26	18-Feb-27	09-Mar-27	0.00	0.00	9,749.30	-57
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	100%	0%	27-Oct-26	03-Nov-26	20-Jan-27	28-Jan-27	17,274.79	0.00	17,274.79	-73
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	23-Nov-26	30-Nov-26	28-Jan-27	06-Feb-27	0.00	0.00	40,307.84	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	23-Nov-26	30-Nov-26	28-Jan-27	06-Feb-27	0.00	0.00	32,757.76	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	23-Nov-26	30-Nov-26	28-Jan-27	06-Feb-27	0.00	0.00	12,869.04	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	01-Dec-26	13-Dec-26	06-Feb-27	18-Feb-27	0.00	0.00	12,186.67	-57
TOILET/SERVICE BUILDING		92	27.23%	10.49%	14-Sep-26	19-Dec-26	20-Oct-26 A	06-Feb-27	102,705.66	39,555.00	377,177.78	-41
MECHANICAL WORK		58	19.38%	11.63%	29-Sep-26	19-Dec-26	22-Oct-26 A	31-Dec-26	12,186.63	7,311.98	62,883.02	-10
WATER SUPPLY SYSTEM		7	0%	0%	12-Dec-26	19-Dec-26	23-Dec-26	31-Dec-26	0.00	0.00	48,746.52	-10
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	0%	0%	12-Dec-26	19-Dec-26	23-Dec-26	31-Dec-26	0.00	0.00	48,746.52	-10
SEWER/DRAINAGE SYSTEM		5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	15-Nov-26	12,186.63	7,311.98	12,186.63	-35
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	15-Nov-26	12,186.63	7,311.98	12,186.63	-35
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	09-Nov-26	11-Nov-26	0.00	0.00	1,949.87	30
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	0%	0%	14-Dec-26	15-Dec-26	09-Nov-26	11-Nov-26	0.00	0.00	1,949.87	30
ELECTRICAL WORKS		45	1.13%	0%	09-Nov-26	19-Dec-26	15-Dec-26	06-Feb-27	2,047.35	0.00	180,781.27	-41
FIXTURE WORKS		45	1.13%	0%	09-Nov-26	19-Dec-26	15-Dec-26	06-Feb-27	2,047.35	0.00	180,781.27	-41
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	2%	0%	09-Nov-26	14-Nov-26	30-Dec-26	05-Jan-27	2,047.35	0.00	102,367.69	-44
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	13-Dec-26	16-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	6,239.59	-5
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	07-Dec-26	10-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	7,085.10	-10
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	0%	0%	01-Dec-26	03-Dec-26	15-Dec-26	19-Dec-26	0.00	0.00	6,824.51	-12
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	15-Dec-26	19-Dec-26	01-Feb-27	06-Feb-27	0.00	0.00	34,317.53	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	07-Dec-26	10-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	14,259.43	-10
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	05-Dec-26	10-Dec-26	19-Dec-26	26-Dec-26	0.00	0.00	2,437.33	-12
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	0%	0%	05-Dec-26	08-Dec-26	06-Jan-27	11-Jan-27	0.00	0.00	7,250.09	-28
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	15-Nov-26	19-Nov-26	3,899.72	0.00	3,899.72	-52
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	15-Nov-26	19-Nov-26	3,899.72	0.00	3,899.72	-52
FINISHING WORKS		73	98.35%	45.34%	06-Oct-26	12-Dec-26	20-Oct-26 A	14-Jan-27	69,948.00	32,243.02	71,117.94	-28
FLOOR FINISHES		57	71.43%	0%	06-Oct-26	12-Dec-26	09-Nov-26	14-Jan-27	2,924.82	0.00	4,094.76	-28
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	09-Nov-26	14-Nov-26	2,924.82	0.00	2,924.82	-29
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	09-Dec-26	12-Dec-26	11-Jan-27	14-Jan-27	0.00	0.00	1,169.94	-28
WALL FINISHES		28	100%	48.11%	06-Oct-26	31-Oct-26	20-Oct-26 A	23-Nov-26	67,023.18	32,243.02	67,023.18	-19
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	17-Nov-26	35,825.58	32,243.02	35,825.58	-29
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	24-Oct-26	31-Oct-26	15-Nov-26	23-Nov-26	31,197.60	0.00	31,197.60	-19
SPECIALTIES WORK		75	25%	0%	18-Oct-26	17-Dec-26	09-Nov-26	04-Feb-27	14,623.96	0.00	58,495.83	-41
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	0%	0%	15-Dec-26	17-Dec-26	01-Feb-27	04-Feb-27	0.00	0.00	24,373.26	-41
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	15-Nov-26	14,623.96	0.00	14,623.96	-19
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	0%	0%	12-Dec-26	14-Dec-26	28-Jan-27	01-Feb-27	0.00	0.00	19,498.61	-41
TESTING & COMMISSIONING		26	0%	0%	20-Dec-26	02-Jan-27	06-Feb-27	09-Mar-27	0.00	0.00	0.00	-55
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	2	0%	0%	30-Dec-26	31-Dec-26	14-Feb-27	16-Feb-27	0.00	0.00	0.00	-39
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	12	0%	0%	20-Dec-26	02-Jan-27	06-Feb-27	20-Feb-27	0.00	0.00	0.00	-41
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	27-Dec-26	31-Dec-26	03-Mar-27	09-Mar-27	0.00	0.00	0.00	-56
HASA OASIS		186	17.99%	14.97%	04-May-26	02-Jan-27	01-Jun-26 A	03-Mar-27	1,093,959.73	909,968.16	6,080,638.29	-50
ENGINEERING		50	0%	0%	04-May-26	25-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-35
SHOP DRAWINGS		50	0%	0%	04-May-26	25-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-35
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
ELECTRICAL WORKS		25	0%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-158
SHOP DRAWINGS APPROVALS		50	0%	0%	06-Jun-26	25-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-35
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		50	0%	0%	06-Jun-26	25-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-35
ELECTRICAL WORKS		50	0%	0%	06-Jun-26	25-Nov-26	09-Nov-26	06-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-EM	Shop DWG Approval for Power Layout	25	100%	0%	06-Jun-26	04-Jul-26	08-Dec-26	06-Jan-27	0.00	0.00	0.00	-158
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	25	40.4%	0%	28-Oct-26	25-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-10
PROCUREMENT		71	0%	0%	28-Jun-26	01-Dec-26	09-Nov-26	31-Jan-27	0.00	0.00	0.00	-51
SHORT LEAD ITEM		71	0%	0%	28-Jun-26	01-Dec-26	09-Nov-26	31-Jan-27	0.00	0.00	0.00	-51
PLAYGROUND WORKS		71	0%	0%	28-Jun-26	01-Dec-26	09-Nov-26	31-Jan-27	0.00	0.00	0.00	-51
PVC MEMBRANE		30	0%	0%	29-Sep-26	02-Nov-26	26-Nov-26	31-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	30	100%	0%	29-Sep-26	02-Nov-26	26-Nov-26	31-Dec-26	0.00	0.00	0.00	-50
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	30	100%	0%	30-Sep-26	03-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-34
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-42

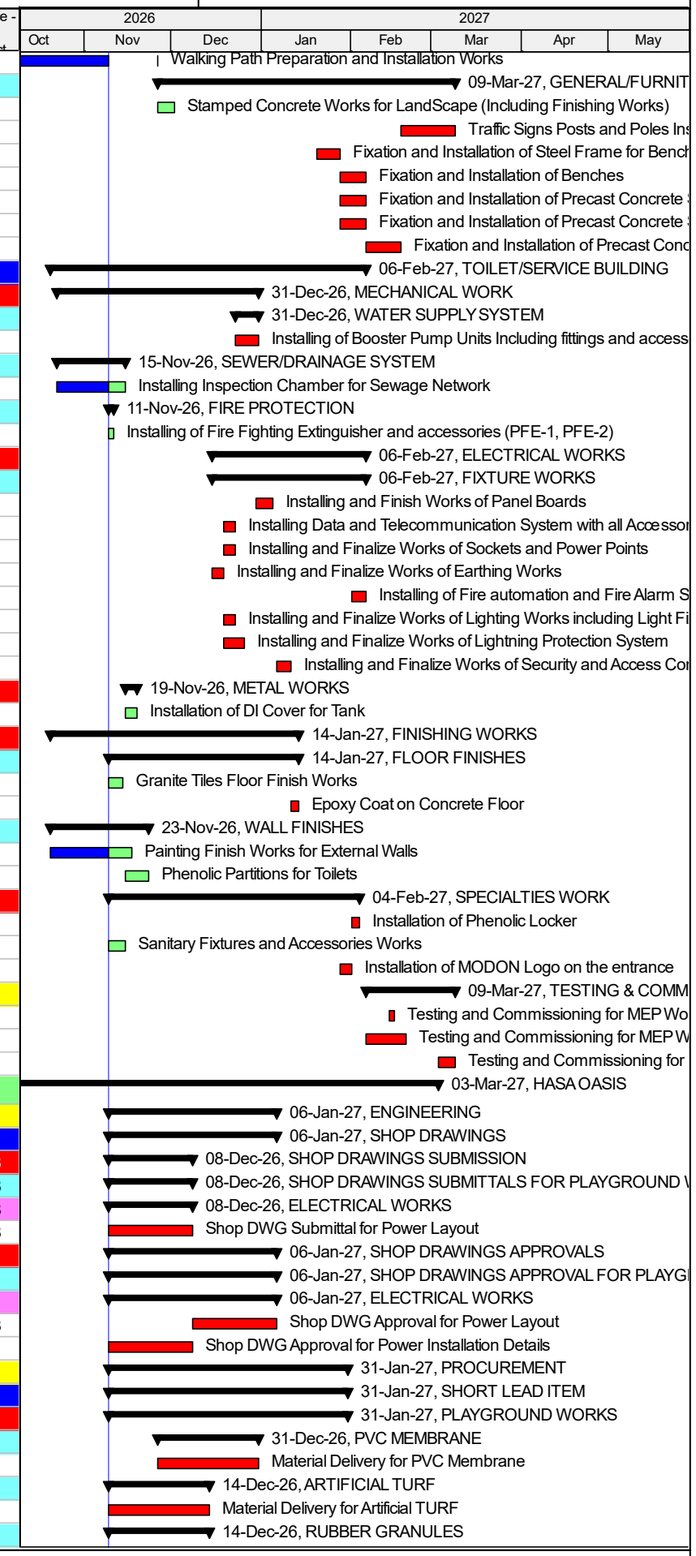

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-42
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-45
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-45
MARKING PAINT		32	0%	0%	28-Jun-26	03-Aug-26	09-Nov-26	16-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	15-Jul-26	03-Aug-26	26-Nov-26	16-Dec-26	0.00	0.00	0.00	-114
AIR DIFUSSERS/GRILLS		40	0%	0%	24-Sep-26	09-Nov-26	09-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	96.4%	0%	12-Oct-26	09-Nov-26	26-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
GALVANIZED DUCTS		40	0%	0%	24-Sep-26	09-Nov-26	09-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	96.4%	0%	12-Oct-26	09-Nov-26	26-Nov-26	26-Dec-26	0.00	0.00	0.00	-39
EXHAUST FANS		40	0%	0%	10-Sep-26	02-Nov-26	09-Nov-26	26-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	100%	0%	05-Oct-26	02-Nov-26	26-Nov-26	26-Dec-26	0.00	0.00	0.00	-45
DISTRIBUTION BOARDS		20	0%	0%	10-Oct-26	01-Nov-26	26-Nov-26	20-Dec-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	10-Oct-26	14-Oct-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	15-Oct-26	01-Nov-26	02-Dec-26	20-Dec-26	0.00	0.00	0.00	-41
POWER CABLES		35	0%	0%	22-Oct-26	01-Dec-26	14-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	PO for Power Cables	15	100%	0%	22-Oct-26	08-Nov-26	14-Dec-26	31-Dec-26	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	Material Delivery for Power Cables	20	0.5%	0%	09-Nov-26	01-Dec-26	31-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
LIGHT FIXTURES		20	0%	0%	09-Nov-26	01-Dec-26	31-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0.5%	0%	09-Nov-26	01-Dec-26	31-Dec-26	24-Jan-27	0.00	0.00	0.00	-45
CCTV MATERIALS		71	0%	0%	04-Jul-26	29-Nov-26	09-Nov-26	31-Jan-27	0.00	0.00	0.00	-53
MLTX-02-005-PR-1	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	12-Nov-26	29-Nov-26	13-Jan-27	31-Jan-27	0.00	0.00	0.00	-53
POWER OUTLETS/SWITCHES		41	0%	0%	23-Jul-26	10-Nov-26	26-Nov-26	13-Jan-27	0.00	0.00	0.00	-54
MLTX-02-005-PR-1	PO for Power Outlets/Switches	16	100%	0%	23-Jul-26	10-Aug-26	26-Nov-26	15-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	92.4%	0%	13-Oct-26	10-Nov-26	15-Dec-26	13-Jan-27	0.00	0.00	0.00	-54
LANDSCAPE WORKS		64	0%	0%	11-Aug-26	04-Nov-26	09-Nov-26	23-Jan-27	0.00	0.00	0.00	-67
PAVEMENT MARKING		33	0%	0%	11-Aug-26	04-Nov-26	15-Dec-26	23-Jan-27	0.00	0.00	0.00	-67
MLTX-02-005-PR-1	PO for Pavement Markings	13	100%	0%	11-Aug-26	25-Aug-26	15-Dec-26	30-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	20	100%	0%	13-Oct-26	04-Nov-26	30-Dec-26	23-Jan-27	0.00	0.00	0.00	-67
TRACK SURFACE		2	0%	0%	29-Aug-26	30-Aug-26	30-Dec-26	02-Jan-27	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for Track Surface	2	100%	0%	29-Aug-26	30-Aug-26	30-Dec-26	02-Jan-27	0.00	0.00	0.00	-105
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-36
LONG LEAD ITEM		31	0%	0%	15-Jul-26	16-Nov-26	09-Nov-26	15-Dec-26	0.00	0.00	0.00	-24
PLAYGROUND WORKS		31	0%	0%	15-Jul-26	16-Nov-26	09-Nov-26	15-Dec-26	0.00	0.00	0.00	-24
STEEL TENSION CABLES		26	0%	0%	21-Sep-26	21-Oct-26	09-Nov-26	09-Dec-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	09-Nov-26	28-Nov-26	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	Staging time	10	100%	0%	11-Oct-26	21-Oct-26	28-Nov-26	09-Dec-26	0.00	0.00	0.00	-41
EMERGENCY DOORS		30	0%	0%	15-Jul-26	18-Aug-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Staging time	5	100%	0%	13-Aug-26	18-Aug-26	08-Dec-26	14-Dec-26	0.00	0.00	0.00	-99
PRESSURE UNITS		30	0%	0%	13-Oct-26	16-Nov-26	09-Nov-26	14-Dec-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	92.4%	0%	13-Oct-26	10-Nov-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	Staging time	5	0%	0%	11-Nov-26	16-Nov-26	08-Dec-26	14-Dec-26	0.00	0.00	0.00	-23
AIR LOCK DOORS		31	0%	0%	03-Oct-26	05-Nov-26	09-Nov-26	15-Dec-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	03-Oct-26	31-Oct-26	09-Nov-26	08-Dec-26	0.00	0.00	0.00	-32
MLTX-02-005-PR-1	Staging time	5	100%	0%	01-Nov-26	05-Nov-26	09-Dec-26	15-Dec-26	0.00	0.00	0.00	-33
CONSTRUCTION PHASE		186	17.99%	14.97%	30-Jul-26	31-Dec-26	01-Jun-26 A	23-Feb-27	1,093,959.73	909,968.16	6,080,638.29	-44
SITE WORKS		135	17.17%	13.88%	29-Sep-26	31-Dec-26	01-Jun-26 A	23-Feb-27	1,002,017.82	810,132.34	5,836,888.43	-44
LANDSCAPE WORKS		135	17.17%	13.88%	29-Sep-26	31-Dec-26	01-Jun-26 A	23-Feb-27	1,002,017.82	810,132.34	5,836,888.43	-44
PLAYGROUND AREA		125	40.56%	32.45%	29-Sep-26	31-Dec-26	21-Sep-26 A	23-Feb-27	180,520.67	144,416.54	445,050.38	-44
FOOTBALL PLAYGROUND		24	0%	0%	17-Nov-26	09-Dec-26	12-Dec-26	09-Jan-27	0.00	0.00	47,527.50	-25
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	0%	0%	17-Nov-26	09-Dec-26	12-Dec-26	04-Jan-27	0.00	0.00	31,685.00	-21
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	3	0%	0%	17-Nov-26	19-Nov-26	05-Jan-27	09-Jan-27	0.00	0.00	15,842.50	-42
PADEL PLAYGROUND		18	0%	0%	12-Dec-26	31-Dec-26	09-Jan-27	30-Jan-27	0.00	0.00	70,195.20	-24
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	12-Dec-26	28-Dec-26	09-Jan-27	26-Jan-27	0.00	0.00	58,496.00	-24
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	3	0%	0%	29-Dec-26	31-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	11,699.20	-24
BASKETBALL PLAYGROUND		42	0%	0%	17-Nov-26	31-Dec-26	12-Dec-26	30-Jan-27	0.00	0.00	96,956.10	-24

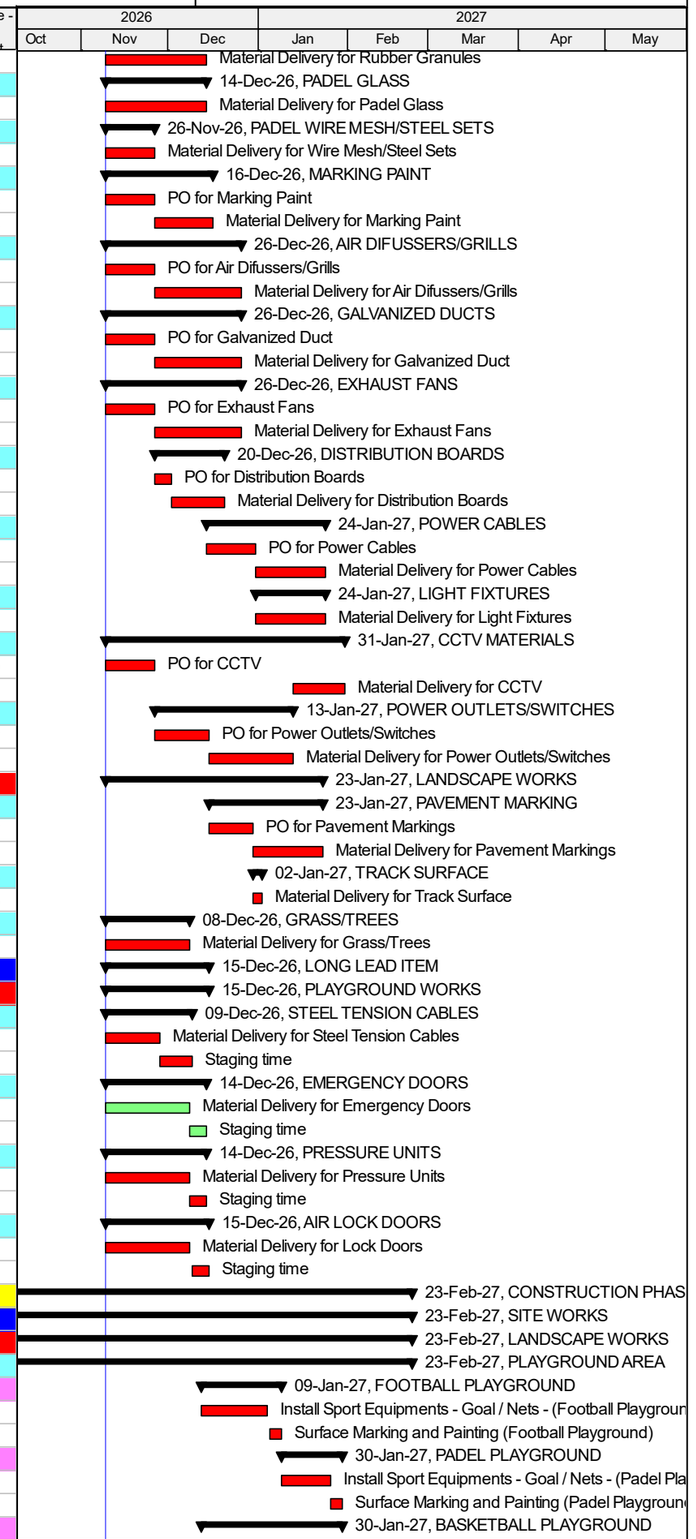

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 9-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	17-Nov-26	28-Nov-26	12-Dec-26	23-Dec-26	0.00	0.00	80,796.75	-21
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	3	0%	0%	29-Dec-26	31-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	16,159.35	-24
PADEL FENCE		38	0%	0%	02-Dec-26	31-Dec-26	09-Jan-27	23-Feb-27	0.00	0.00	49,850.91	-44
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	09-Jan-27	26-Jan-27	0.00	0.00	30,677.48	-32
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	09-Jan-27	26-Jan-27	0.00	0.00	15,338.75	-32
MLTX-02-005-CI	Install of Fence Gates	26	0%	0%	02-Dec-26	31-Dec-26	23-Jan-27	23-Feb-27	0.00	0.00	3,834.68	-44
CURBSTOEN/INTERLOCK		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	12-Nov-26	180,520.67	144,416.54	180,520.67	-35
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	12-Nov-26	180,520.67	144,416.54	180,520.67	-35
AIR DOME		30	0%	0%	15-Nov-26	10-Dec-26	05-Jan-27	09-Feb-27	0.00	0.00	4,306,367.09	-51
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	1,391,301.90	-44
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	942,830.33	-44
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-44
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	1,233,296.81	-39
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	15	0%	0%	21-Nov-26	07-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	728,766.30	-39
MLTX-02-005-CI	Air Units Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	13-Jan-27	23-Jan-27	0.00	0.00	336,353.67	-39
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	13-Jan-27	23-Jan-27	0.00	0.00	168,176.84	-39
ELECTRICAL WORKS		14	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	09-Feb-27	0.00	0.00	1,513,591.54	-51
MLTX-02-005-CI	Light Fixture Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	224,235.78	-45
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-45
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-45
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	504,530.51	-45
MLTX-02-005-CI	Control System Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	31-Jan-27	09-Feb-27	0.00	0.00	448,471.57	-51
FINISHES WORKS		30	0%	0%	15-Nov-26	10-Dec-26	05-Jan-27	09-Feb-27	0.00	0.00	168,176.84	-51
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	15-Nov-26	01-Dec-26	05-Jan-27	23-Jan-27	0.00	0.00	112,117.89	-44
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	09-Dec-26	10-Dec-26	07-Feb-27	09-Feb-27	0.00	0.00	56,058.95	-51
IRRIGATION NETWORK		3	0%	0%	05-Dec-26	07-Dec-26	09-Jan-27	12-Jan-27	0.00	0.00	25,106.20	-30
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	05-Dec-26	07-Dec-26	09-Jan-27	12-Jan-27	0.00	0.00	25,106.20	-30
NATURAL GROUND		3	0%	70%	05-Dec-26	07-Dec-26	14-Oct-26 A	12-Nov-26	0.00	88,718.00	126,740.00	22
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	70%	05-Dec-26	07-Dec-26	14-Oct-26 A	12-Nov-26	0.00	88,718.00	126,740.00	22
PLANTING		101	100%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	12-Nov-26	347,251.46	240,773.38	347,251.46	-8
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	100%	95%	24-Oct-26	26-Oct-26	03-Oct-26 A	12-Nov-26	104,175.44	98,966.67	104,175.44	-14
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	100%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	12-Nov-26	141,732.50	70,866.25	141,732.50	-8
MLTX-02-005-CN-1	Placement and Fixation of Trees	3	100%	70%	27-Oct-26	29-Oct-26	14-Oct-26 A	12-Nov-26	101,343.52	70,940.46	101,343.52	-11
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	09-Nov-26	367,633.90	294,107.12	367,633.90	-19
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	09-Nov-26	187,554.12	150,043.30	187,554.12	-27
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	09-Nov-26	180,079.78	144,063.82	180,079.78	-19
GENERAL/FURNITURE		94	48.74%	19.25%	15-Oct-26	24-Dec-26	14-Oct-26 A	03-Feb-27	106,611.79	42,117.30	218,739.40	-34
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	100%	45%	18-Oct-26	07-Nov-26	14-Oct-26 A	30-Nov-26	93,594.00	42,117.30	93,594.00	-19
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	3	0%	0%	20-Dec-26	22-Dec-26	28-Jan-27	01-Feb-27	0.00	0.00	9,749.30	-34
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	28	75.36%	0%	15-Oct-26	16-Nov-26	09-Nov-26	12-Dec-26	13,017.79	0.00	17,274.79	-21
MLTX-02-005-CN-1	Fixation and Installation of Benches	14	0%	0%	17-Nov-26	02-Dec-26	12-Dec-26	28-Dec-26	0.00	0.00	40,307.84	-21
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	14	0%	0%	03-Dec-26	19-Dec-26	12-Dec-26	28-Dec-26	0.00	0.00	32,757.76	-7
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	14	0%	0%	03-Dec-26	19-Dec-26	28-Dec-26	13-Jan-27	0.00	0.00	12,869.04	-21
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	2	0%	0%	23-Dec-26	24-Dec-26	01-Feb-27	03-Feb-27	0.00	0.00	12,186.67	-34
TOILET/SERVICE BUILDING		161	37.72%	40.96%	30-Jul-26	23-Dec-26	20-Sep-26 A	04-Feb-27	91,941.92	99,835.82	243,749.86	-36
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	30-Nov-26	16,607.28	14,946.55	16,607.28	-86
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	30-Nov-26	16,607.28	14,946.55	16,607.28	-86
MECHANICAL WORK		21	0%	0%	28-Nov-26	21-Dec-26	09-Dec-26	03-Jan-27	0.00	0.00	1,949.87	-10
FIRE PROTECTION		21	0%	0%	28-Nov-26	21-Dec-26	09-Dec-26	03-Jan-27	0.00	0.00	1,949.87	-10
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	0%	0%	28-Nov-26	21-Dec-26	09-Dec-26	03-Jan-27	0.00	0.00	1,949.87	-10
ELECTRICAL WORKS		57	13.97%	27.27%	04-Nov-26	20-Dec-26	03-Nov-26 A	01-Feb-27	20,985.38	40,947.08	150,174.90	-36
FIXTURE WORKS		57	13.97%	27.27%	04-Nov-26	20-Dec-26	03-Nov-26 A	01-Feb-27	20,985.38	40,947.08	150,174.90	-36
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	18	0%	0%	28-Nov-26	17-Dec-26	02-Dec-26	23-Dec-26	0.00	0.00	34,317.53	-4
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	20.5%	40%	04-Nov-26	26-Nov-26	03-Nov-26 A	02-Dec-26	20,985.38	40,947.08	102,367.69	-4
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	28-Nov-26	20-Dec-26	02-Dec-26	26-Dec-26	0.00	0.00	6,239.59	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	0%	0%	21-Nov-26	13-Dec-26	09-Jan-27	01-Feb-27	0.00	0.00	7,250.09	-42
METAL WORKS		14	100%	0%	05-Oct-26	20-Oct-26	02-Dec-26	19-Dec-26	3,899.72	0.00	3,899.72	-50
MLTX-02-005-CN-129	Installation of DI Cover for Tank	14	100%	0%	05-Oct-26	20-Oct-26	02-Dec-26	19-Dec-26	3,899.72	0.00	3,899.72	-50
FINISHING WORKS		94	96.84%	87.15%	18-Oct-26	16-Dec-26	27-Sep-26 A	04-Feb-27	35,825.58	32,243.02	36,995.52	-42
FLOOR FINISHES		23	0%	0%	21-Nov-26	16-Dec-26	09-Jan-27	04-Feb-27	0.00	0.00	1,169.94	-42
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	23	0%	0%	21-Nov-26	16-Dec-26	09-Jan-27	04-Feb-27	0.00	0.00	1,169.94	-42
WALL FINISHES		3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	12-Nov-26	35,825.58	32,243.02	35,825.58	-19
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	12-Nov-26	35,825.58	32,243.02	35,825.58	-19
SPECIALTIES WORK		74	42.86%	34.29%	27-Sep-26	23-Dec-26	04-Oct-26 A	22-Dec-26	14,623.96	11,699.17	34,122.57	2

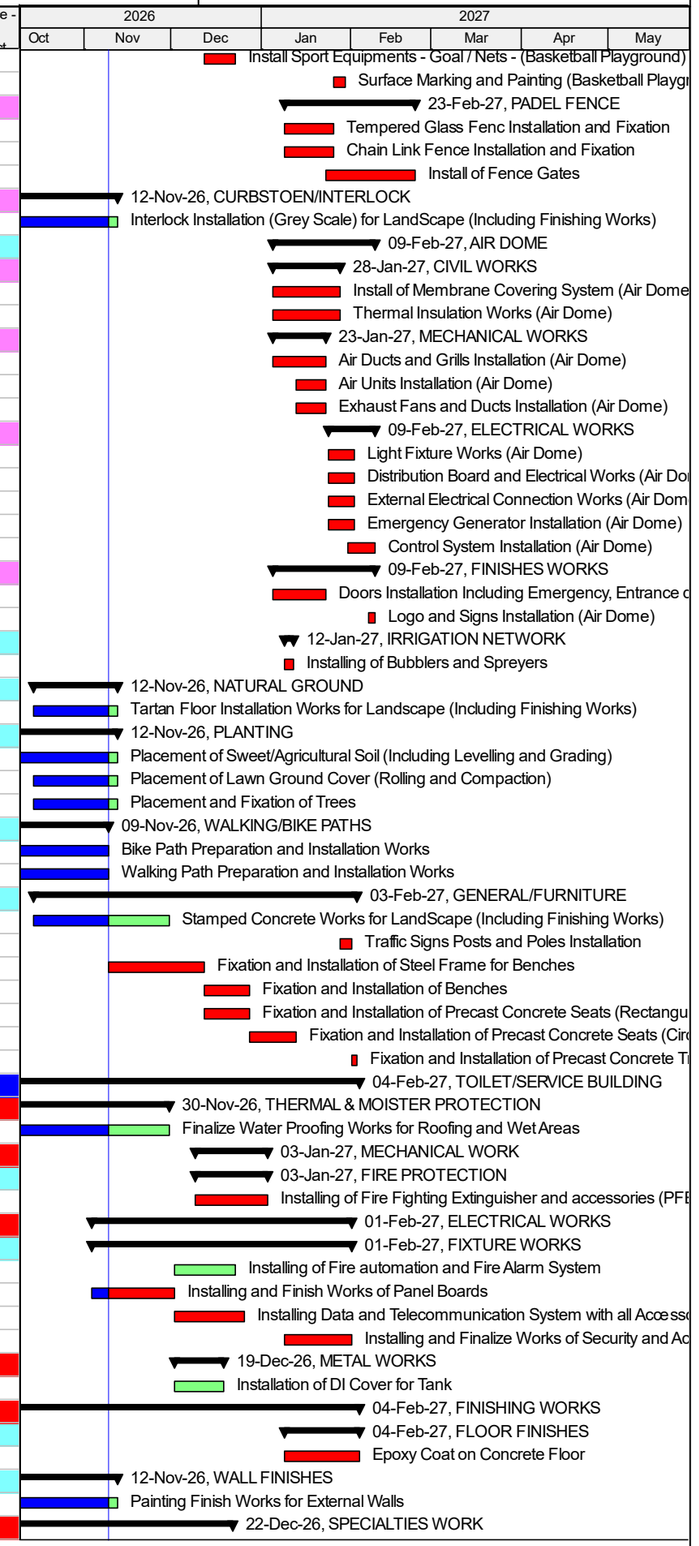

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	12-Nov-26	14,623.96	11,699.17	14,623.96	-37
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	17	0%	0%	05-Dec-26	23-Dec-26	02-Dec-26	22-Dec-26	0.00	0.00	19,498.61	2
TESTING & COMMISSIONING		28	0%	0%	08-Dec-26	02-Jan-27	28-Jan-27	03-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	18	0%	0%	12-Dec-26	31-Dec-26	09-Feb-27	03-Mar-27	0.00	0.00	0.00	-51
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	7	0%	0%	26-Dec-26	02-Jan-27	14-Feb-27	23-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	21	0%	0%	08-Dec-26	31-Dec-26	28-Jan-27	23-Feb-27	0.00	0.00	0.00	-44
DAMMAM		169	7.99%	4.66%	21-May-26	02-Jan-27	06-Sep-26 A	06-Mar-27	459,138.45	267,751.36	5,747,833.38	-52
PROCUREMENT		48	0%	0%	21-May-26	21-Dec-26	09-Nov-26	04-Jan-27	0.00	0.00	0.00	-11
SHORT LEAD ITEM		48	0%	0%	21-May-26	21-Dec-26	09-Nov-26	04-Jan-27	0.00	0.00	0.00	-11
PLAYGROUND WORKS		48	0%	0%	21-May-26	21-Dec-26	09-Nov-26	04-Jan-27	0.00	0.00	0.00	-11
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	09-Nov-26	03-Dec-26	0.00	0.00	0.00	-143
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	09-Nov-26	03-Dec-26	0.00	0.00	0.00	-143
ARTIFICIAL TURF		12	0%	0%	18-Jun-26	01-Jul-26	03-Dec-26	17-Dec-26	0.00	0.00	0.00	-143
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	18-Jun-26	01-Jul-26	03-Dec-26	17-Dec-26	0.00	0.00	0.00	-143
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-138
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	09-Nov-26	12-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-1	Material Delivery for Padel Glass	28	64.64%	0%	19-Oct-26	19-Nov-26	09-Nov-26	12-Dec-26	0.00	0.00	0.00	-18
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-133
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-133
MARKING PAINT		32	0%	0%	02-Jul-26	08-Aug-26	09-Nov-26	16-Dec-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	20-Jul-26	08-Aug-26	26-Nov-26	16-Dec-26	0.00	0.00	0.00	-110
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	15-Nov-26	26-Nov-26	0.00	0.00	0.00	-113
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	15-Nov-26	08-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	15-Nov-26	08-Dec-26	0.00	0.00	0.00	-4
CCTV MATERIALS		48	0%	0%	30-Jul-26	21-Dec-26	09-Nov-26	04-Jan-27	0.00	0.00	0.00	-11
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	09-Nov-26	15-Nov-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	05-Dec-26	21-Dec-26	17-Dec-26	04-Jan-27	0.00	0.00	0.00	-11
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	15-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	15-Nov-26	22-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	22-Nov-26	21-Dec-26	0.00	0.00	0.00	-10
LANDSCAPE WORKS		25	0%	0%	15-Aug-26	21-Nov-26	22-Nov-26	21-Dec-26	0.00	0.00	0.00	-25
PAVEMENT MARKING		15	0%	0%	15-Aug-26	31-Aug-26	22-Nov-26	09-Dec-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	22-Nov-26	28-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	20-Aug-26	31-Aug-26	28-Nov-26	09-Dec-26	0.00	0.00	0.00	-84
TRACK SURFACE		10	0%	0%	10-Nov-26	21-Nov-26	09-Dec-26	21-Dec-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	0%	0%	10-Nov-26	21-Nov-26	09-Dec-26	21-Dec-26	0.00	0.00	0.00	-25
LONG LEAD ITEM		22	0%	0%	07-Sep-26	30-Nov-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
PLAYGROUND WORKS		22	0%	0%	07-Sep-26	30-Nov-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
STEEL TENSION CABLES		22	0%	0%	07-Sep-26	19-Oct-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-53
MLTX-02-005-PR-1	Staging time	7	100%	0%	12-Oct-26	19-Oct-26	26-Nov-26	05-Dec-26	0.00	0.00	0.00	-39
EMERGENCY DOORS		18	0%	0%	04-Nov-26	24-Nov-26	09-Nov-26	30-Nov-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	15	27.33%	0%	04-Nov-26	21-Nov-26	09-Nov-26	26-Nov-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Staging time	3	0%	0%	22-Nov-26	24-Nov-26	26-Nov-26	30-Nov-26	0.00	0.00	0.00	-4
PRESSURE UNITS		22	0%	0%	05-Nov-26	30-Nov-26	09-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Material Delivery for Pressure Units	10	31%	0%	05-Nov-26	16-Nov-26	09-Nov-26	21-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	23-Nov-26	05-Dec-26	0.00	0.00	0.00	-3
AIR LOCK DOORS		20	0%	0%	05-Nov-26	26-Nov-26	09-Nov-26	02-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Lock Doors	12	25.83%	0%	05-Nov-26	18-Nov-26	09-Nov-26	23-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Staging time	5	0%	0%	22-Nov-26	26-Nov-26	26-Nov-26	02-Dec-26	0.00	0.00	0.00	-4
CONSTRUCTION PHASE		169	7.99%	4.66%	18-Aug-26	31-Dec-26	06-Sep-26 A	06-Mar-27	459,138.45	267,751.36	5,747,833.38	-53
SITE WORKS		115	7.66%	3.62%	15-Sep-26	31-Dec-26	20-Oct-26 A	06-Mar-27	424,007.49	200,158.56	5,534,254.53	-53
LANDSCAPE WORKS		115	7.66%	3.62%	15-Sep-26	31-Dec-26	20-Oct-26 A	06-Mar-27	424,007.49	200,158.56	5,534,254.53	-53
PLAYGROUND AREA		60	40.56%	16.22%	15-Sep-26	31-Dec-26	21-Oct-26 A	17-Feb-27	180,520.67	72,208.27	445,050.38	-40
FOOTBALL PLAYGROUND		7	0%	0%	08-Dec-26	15-Dec-26	28-Jan-27	06-Feb-27	0.00	0.00	47,527.50	-44
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	10-Dec-26	15-Dec-26	31-Jan-27	06-Feb-27	0.00	0.00	31,685.00	-44
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	2	0%	0%	08-Dec-26	09-Dec-26	28-Jan-27	31-Jan-27	0.00	0.00	15,842.50	-44
PADEL PLAYGROUND		5	0%	0%	20-Dec-26	24-Dec-26	09-Feb-27	15-Feb-27	0.00	0.00	70,195.20	-44
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	09-Feb-27	15-Feb-27	0.00	0.00	58,496.00	-44
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	09-Feb-27	15-Feb-27	0.00	0.00	11,699.20	-44

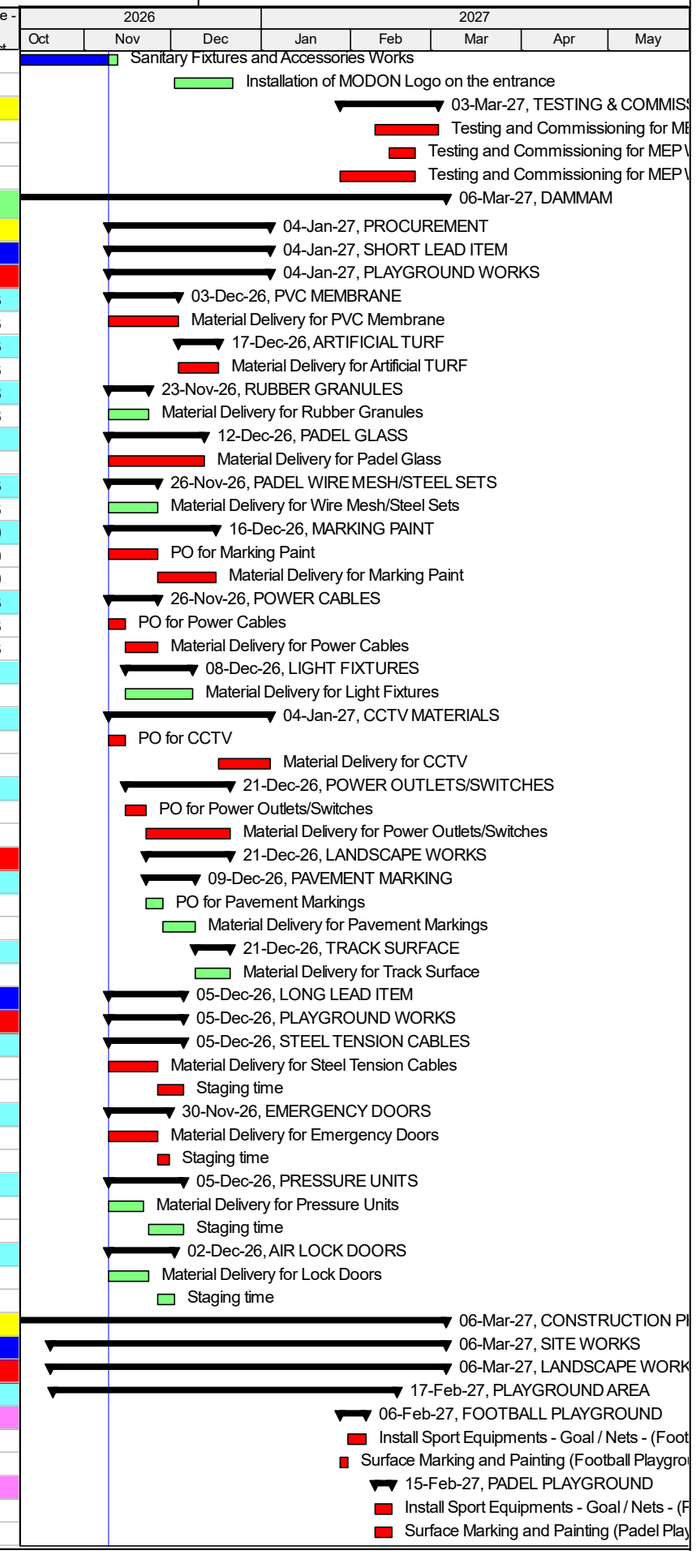

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
BASKETBALL PLAYGROUND		2	0%	0%	30-Dec-26	31-Dec-26	15-Feb-27	17-Feb-27	0.00	0.00	96,956.10	-40
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	2	0%	0%	30-Dec-26	31-Dec-26	15-Feb-27	17-Feb-27	0.00	0.00	80,796.75	-40
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	2	0%	0%	30-Dec-26	31-Dec-26	15-Feb-27	17-Feb-27	0.00	0.00	16,159.35	-40
PADEL FENCE		48	0%	0%	26-Nov-26	24-Dec-26	12-Dec-26	06-Feb-27	0.00	0.00	49,850.91	-36
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	12-Dec-26	10-Jan-27	0.00	0.00	30,677.48	-13
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	12-Dec-26	10-Jan-27	0.00	0.00	15,338.75	-13
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	20-Dec-26	24-Dec-26	31-Jan-27	06-Feb-27	0.00	0.00	3,834.68	-36
CURBSTOEN/INTERLOCK		6	100%	40%	15-Sep-26	21-Sep-26	21-Oct-26 A	16-Nov-26	180,520.67	72,208.27	180,520.67	-46
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	6	100%	40%	15-Sep-26	21-Sep-26	21-Oct-26 A	16-Nov-26	180,520.67	72,208.27	180,520.67	-46
AIR DOME		30	0%	0%	15-Nov-26	24-Dec-26	05-Jan-27	09-Feb-27	0.00	0.00	4,306,367.09	-39
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	1,391,301.90	-44
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	942,830.33	-44
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-44
MECHANICAL WORKS		5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	1,233,296.81	-44
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	4	0%	0%	08-Dec-26	12-Dec-26	28-Jan-27	02-Feb-27	0.00	0.00	728,766.30	-44
MLTX-02-005-CI	Air Units Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	336,353.67	-44
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	28-Jan-27	03-Feb-27	0.00	0.00	168,176.84	-44
ELECTRICAL WORKS		10	0%	0%	08-Dec-26	24-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	1,513,591.54	-39
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	08-Dec-26	19-Dec-26	28-Jan-27	09-Feb-27	0.00	0.00	224,235.78	-44
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	12-Dec-26	19-Dec-26	01-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-44
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	13-Dec-26	19-Dec-26	02-Feb-27	09-Feb-27	0.00	0.00	168,176.84	-44
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	15-Dec-26	19-Dec-26	04-Feb-27	09-Feb-27	0.00	0.00	504,530.51	-44
MLTX-02-005-CI	Control System Installation (Air Dome)	3	0%	0%	22-Dec-26	24-Dec-26	06-Feb-27	09-Feb-27	0.00	0.00	448,471.57	-39
FINISHES WORKS		4	0%	0%	12-Dec-26	15-Dec-26	01-Feb-27	06-Feb-27	0.00	0.00	168,176.84	-44
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	2	0%	0%	12-Dec-26	13-Dec-26	01-Feb-27	03-Feb-27	0.00	0.00	112,117.89	-44
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	14-Dec-26	15-Dec-26	03-Feb-27	06-Feb-27	0.00	0.00	56,058.95	-44
IRRIGATION NETWORK		2	0%	0%	01-Dec-26	02-Dec-26	11-Feb-27	14-Feb-27	0.00	0.00	25,106.20	-62
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	01-Dec-26	02-Dec-26	11-Feb-27	14-Feb-27	0.00	0.00	25,106.20	-62
NATURAL GROUND		46	82.81%	30.51%	10-Oct-26	12-Nov-26	20-Oct-26 A	14-Dec-26	158,787.60	58,500.00	191,740.00	-26
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	74%	0%	27-Oct-26	12-Nov-26	26-Nov-26	14-Dec-26	93,787.60	0.00	126,740.00	-26
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	26-Nov-26	65,000.00	58,500.00	65,000.00	-26
PLANTING		27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	21-Nov-26	0.00	69,450.29	347,251.46	36
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	16-Nov-26	0.00	20,835.09	104,175.44	23
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	20%	24-Dec-26	31-Dec-26	01-Nov-26 A	17-Nov-26	0.00	28,346.50	141,732.50	39
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	20%	13-Dec-26	23-Dec-26	01-Nov-26 A	21-Nov-26	0.00	20,268.70	101,343.52	29
GENERAL/FURNITURE		74	38.72%	0%	11-Oct-26	31-Dec-26	08-Dec-26	06-Mar-27	84,699.22	0.00	218,739.40	-53
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	39.44%	0%	01-Nov-26	21-Nov-26	29-Dec-26	19-Jan-27	36,917.63	0.00	93,594.00	-50
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	15-Dec-26	31-Dec-26	11-Feb-27	02-Mar-27	0.00	0.00	9,749.30	-50
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	18	100%	0%	11-Oct-26	31-Oct-26	08-Dec-26	29-Dec-26	17,274.79	0.00	17,274.79	-50
MLTX-02-005-CN-1	Fixation and Installation of Benches	20	35.5%	0%	01-Nov-26	23-Nov-26	19-Jan-27	11-Feb-27	14,309.28	0.00	40,307.84	-68
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	20	35.5%	0%	01-Nov-26	23-Nov-26	19-Jan-27	11-Feb-27	11,629.00	0.00	32,757.76	-68
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	20	35.5%	0%	01-Nov-26	23-Nov-26	19-Jan-27	11-Feb-27	4,568.51	0.00	12,869.04	-68
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	18	0%	0%	24-Nov-26	14-Dec-26	11-Feb-27	06-Mar-27	0.00	0.00	12,186.67	-68
TOILET/SERVICE BUILDING		151	16.45%	31.65%	18-Aug-26	29-Dec-26	06-Sep-26 A	11-Feb-27	35,130.96	67,592.80	213,578.85	-37
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	18-Nov-26	16,607.28	14,946.55	16,607.28	-70
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	18-Nov-26	16,607.28	14,946.55	16,607.28	-70
MECHANICAL WORK		12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	12	0%	0%	13-Dec-26	26-Dec-26	18-Nov-26	02-Dec-26	0.00	0.00	1,949.87	21
ELECTRICAL WORKS		68	0%	26.08%	23-Nov-26	29-Dec-26	03-Nov-26 A	03-Jan-27	0.00	40,947.08	156,999.41	-3
FIXTURE WORKS		68	0%	26.08%	23-Nov-26	29-Dec-26	03-Nov-26 A	03-Jan-27	0.00	40,947.08	156,999.41	-3
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	15	0%	0%	12-Dec-26	28-Dec-26	16-Dec-26	03-Jan-27	0.00	0.00	34,317.53	-4
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	0%	40%	06-Dec-26	29-Dec-26	03-Nov-26 A	03-Dec-26	0.00	40,947.08	102,367.69	23
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	14	0%	0%	12-Dec-26	27-Dec-26	16-Dec-26	02-Jan-27	0.00	0.00	6,239.59	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	14	0%	0%	25-Nov-26	10-Dec-26	30-Nov-26	16-Dec-26	0.00	0.00	7,250.09	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	09-Nov-26	06-Dec-26	0.00	0.00	6,824.51	12
METAL WORKS		14	100%	0%	11-Oct-26	26-Oct-26	08-Dec-26	24-Dec-26	3,899.72	0.00	3,899.72	-50
MLTX-02-005-CN-144	Installation of DI Cover for Tank	14	100%	0%	11-Oct-26	26-Oct-26	08-Dec-26	24-Dec-26	3,899.72	0.00	3,899.72	-50
SPECIALTIES WORK		25	42.86%	34.29%	27-Oct-26	23-Dec-26	12-Oct-26 A	11-Feb-27	14,623.96	11,699.17	34,122.57	-42
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	24-Dec-26	14,623.96	11,699.17	14,623.96	-46
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	15	0%	0%	07-Dec-26	23-Dec-26	25-Jan-27	11-Feb-27	0.00	0.00	19,498.61	-42
TESTING & COMMISSIONING		8	0%	0%	24-Dec-26	02-Jan-27	24-Feb-27	06-Mar-27	0.00	0.00	0.00	-52
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	27-Dec-26	31-Dec-26	24-Feb-27	02-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	3	0%	0%	30-Dec-26	02-Jan-27	27-Feb-27	02-Mar-27	0.00	0.00	0.00	-49

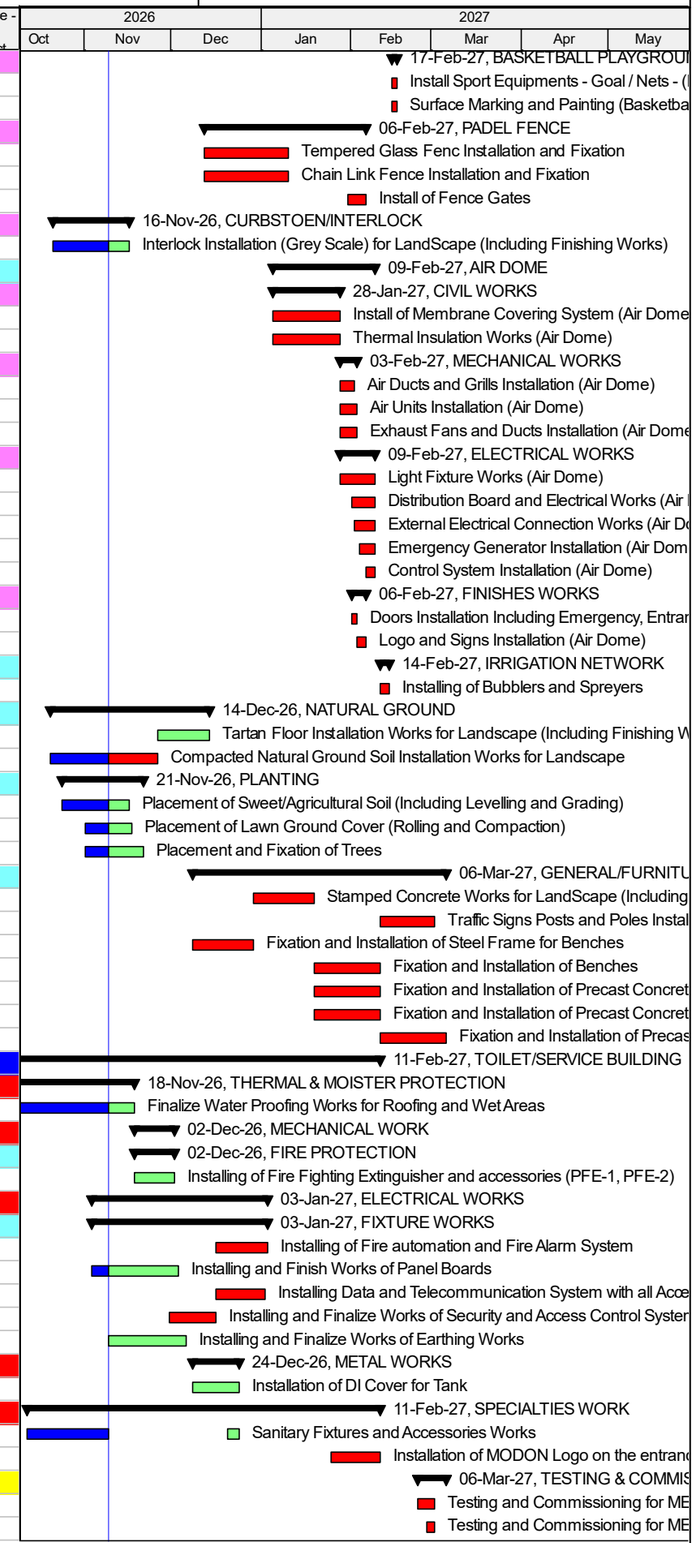

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 9-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	7	0%	0%	24-Dec-26	31-Dec-26	25-Feb-27	06-Mar-27	0.00	0.00	0.00	-53
PROJECT CLOSEOUT & DEMOBILIZATION		35	0%	0%	08-Dec-26	02-Jan-27	28-Jan-27	15-Mar-27	0.00	0.00	0.00	-57
As-Built DWGs		27	0%	0%	08-Dec-26	31-Dec-26	28-Jan-27	02-Mar-27	0.00	0.00	0.00	-50
As-Built DWGs Submittals		16	0%	0%	08-Dec-26	27-Dec-26	28-Jan-27	16-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	12-Dec-26	13-Dec-26	09-Feb-27	11-Feb-27	0.00	0.00	0.00	-51
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	26-Dec-26	27-Dec-26	14-Feb-27	16-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	08-Dec-26	12-Dec-26	28-Jan-27	02-Feb-27	0.00	0.00	0.00	-44
As-Built DWGs Approvals		23	0%	0%	15-Dec-26	31-Dec-26	02-Feb-27	02-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	19-Dec-26	21-Dec-26	11-Feb-27	15-Feb-27	0.00	0.00	0.00	-47
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	29-Dec-26	31-Dec-26	27-Feb-27	02-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	15-Dec-26	17-Dec-26	02-Feb-27	06-Feb-27	0.00	0.00	0.00	-42
Demobilization		12	0%	0%	28-Dec-26	02-Jan-27	25-Feb-27	15-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	28-Dec-26	28-Dec-26	25-Feb-27	27-Feb-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	28-Dec-26	28-Dec-26	25-Feb-27	27-Feb-27	0.00	0.00	0.00	-50
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	09-Mar-27	14-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	14-Mar-27	15-Mar-27	0.00	0.00	0.00	-57

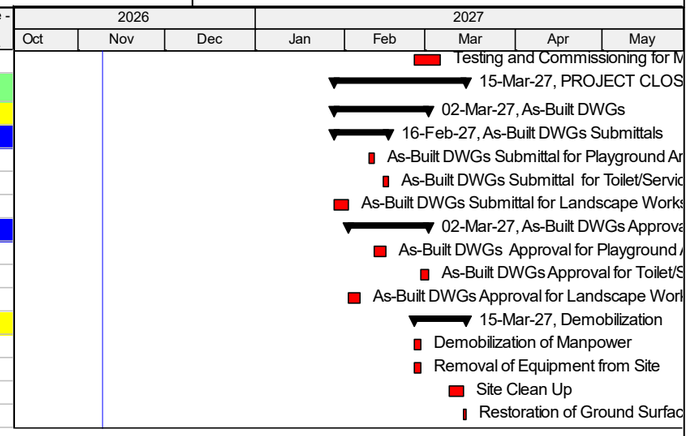

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation
