Completion of Infrastructure Works, Second Industrial City in Makkah

استكمال شبكات البنية التحتية بالمدينة الصناعية الثانية بمكة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Trading & Contracting Co.	EGIS	Engr. Abdallah Aljulaifi	15-Feb-2026	14-Aug-2027

Scope: road works, box culverts, open drain channels and dike walls, street lighting and low-voltage cables, and concrete ducts at road crossings. Contract value 52,025,516 SAR excluding VAT, 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 80.0% against 50.0% planned, the project is 30.1% ahead of plan. This week it gained 0.74% against 1.33% planned, so the weekly pace was below plan.

PHYSICAL % COMPLETE

80.0% / 50.0% plan

▲ SPI 1.60 +30.1%

PROGRESS THIS WEEK

+0.74% / +1.33% plan

▼ 0.59% below the weekly plan

CONTRACT TIME ELAPSED

45.3% · day 247 of 545

▼ Forecast finish 30-Aug-2027

INVOICED TO DATE (GROSS)

57.3% · 29.8M SAR

7 invoices, last period ends 26-Sep-2026

Well ahead of plan, but the forecast finish is 16 days after the contract date.

The weekly report and the P6 update (UP 33, data date 20-Oct-2026) both forecast completion on 30-Aug-2027, 16 days after the contract completion date of 14-Aug-2027, with −14 days of total float. The negative float runs through the asphalt and finishing works on the connection to the 5th Ring Road, testing and commissioning, and close-out. Additional scope on Collector 9 and Road 52 is still open.

Site photos this week

Four photos from the Weekly Photos sheet of the 20-Oct-2026 weekly report, time-stamped 15 and 17-Oct-2026. The photos carry no GPS stamp and are small in the source workbook (about 600 px wide). Select a photo to view it larger, then use the arrows to move between photos.



Cutting works, Collector 9

Excavator on rock cutting. Stamped 17-Oct-2026, 07:09.



Aggregate base course, Non-Muslim Road

Paver and roller on the base course. Stamped 17-Oct-2026, 07:50.



Berm construction, Open Channel 3C

Excavator shaping the berm beside the riprap lining. Stamped 17-Oct-2026, 07:53.




Box culvert 5 base slab

Concrete pour on the base slab. Stamped 15-Oct-2026, 10:14.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

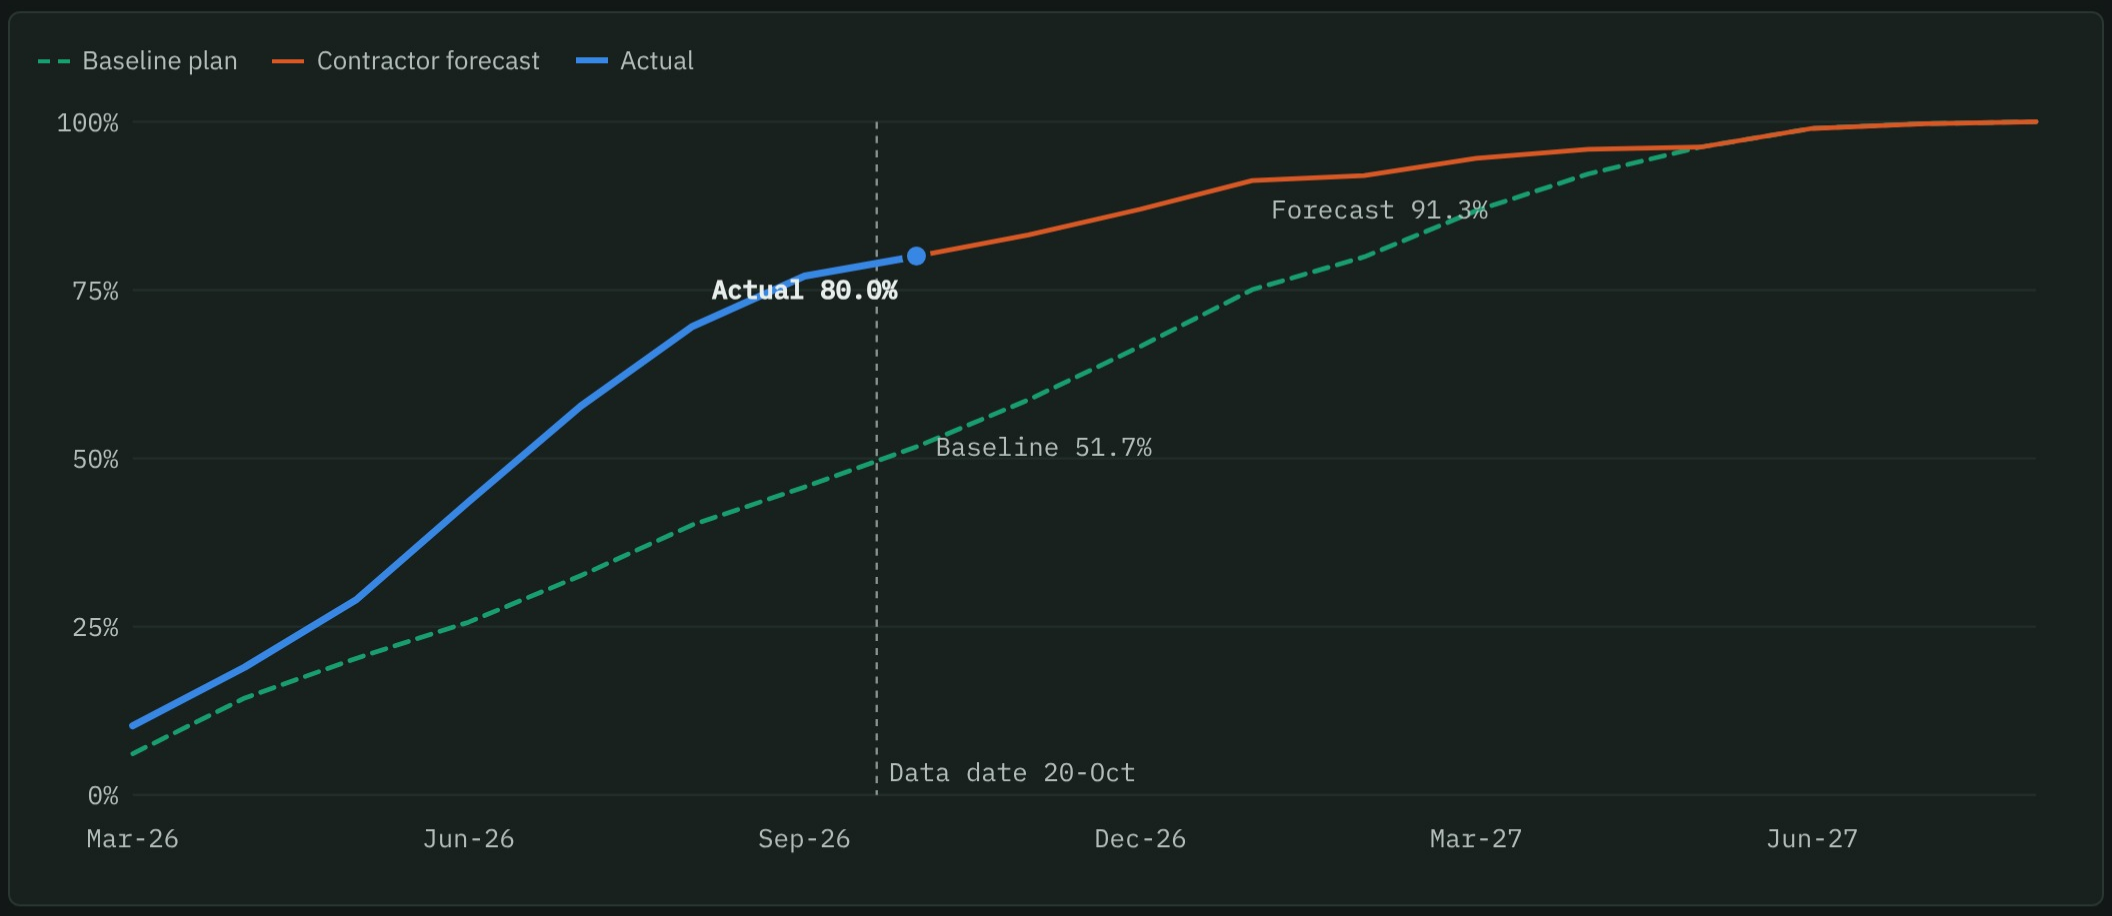

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	48.66	79.31	+30.65	–	1.63
20-Oct-2026	**49.99**	**80.05**	**+30.06**	**+0.74**	**1.60**

Physical % complete from the man-hour totals in the 20-Oct-2026 report, which gives this week's and last week's cumulative values only. The revised plan in the source is identical to the baseline, so the orange line shows the contractor's forecast: actual to September, then the forecast from October.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	12.0%	100.0%	90.5%	-9.5%	0.90	▼ Behind
Road works	24.0%	48.9%	61.4%	+12.5%	1.26	▲ Ahead
Electrical works	8.3%	25.4%	71.8%	+46.4%	2.83	▲ Ahead
Demolition	1.3%	100.0%	67.6%	-32.4%	0.68	▼ Behind
Box culverts	3.5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Open drain channels	37.6%	30.3%	96.2%	+65.9%	3.18	▲ Ahead
Testing & commissioning	3.0%	0.0%	0.0%	0.0%	–	● Not yet due
Close-out & demobilisation	2.0%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**50.0%**	**80.0%**	**+30.1%**	**1.60**	▲ Ahead

The P6 update UP 33 (data date 20-Oct-2026) has 399 activities: 312 completed, 30 in progress and 57 not started. Its scheduled finish is 30-Aug-2027, 16 days after the contract date. Critical-path activities fell from 66 to 43 this week.

Scope of work: quantities

Total, finished and remaining quantity for each network and major item. Network totals come from the Progress Summary sheet and item quantities from the Major Quantities sheet of the 20-Oct-2026 report. "This week" is the quantity listed as executed this week in the summary sheets (files 15 and 16); "–" means the report gives no weekly figure.

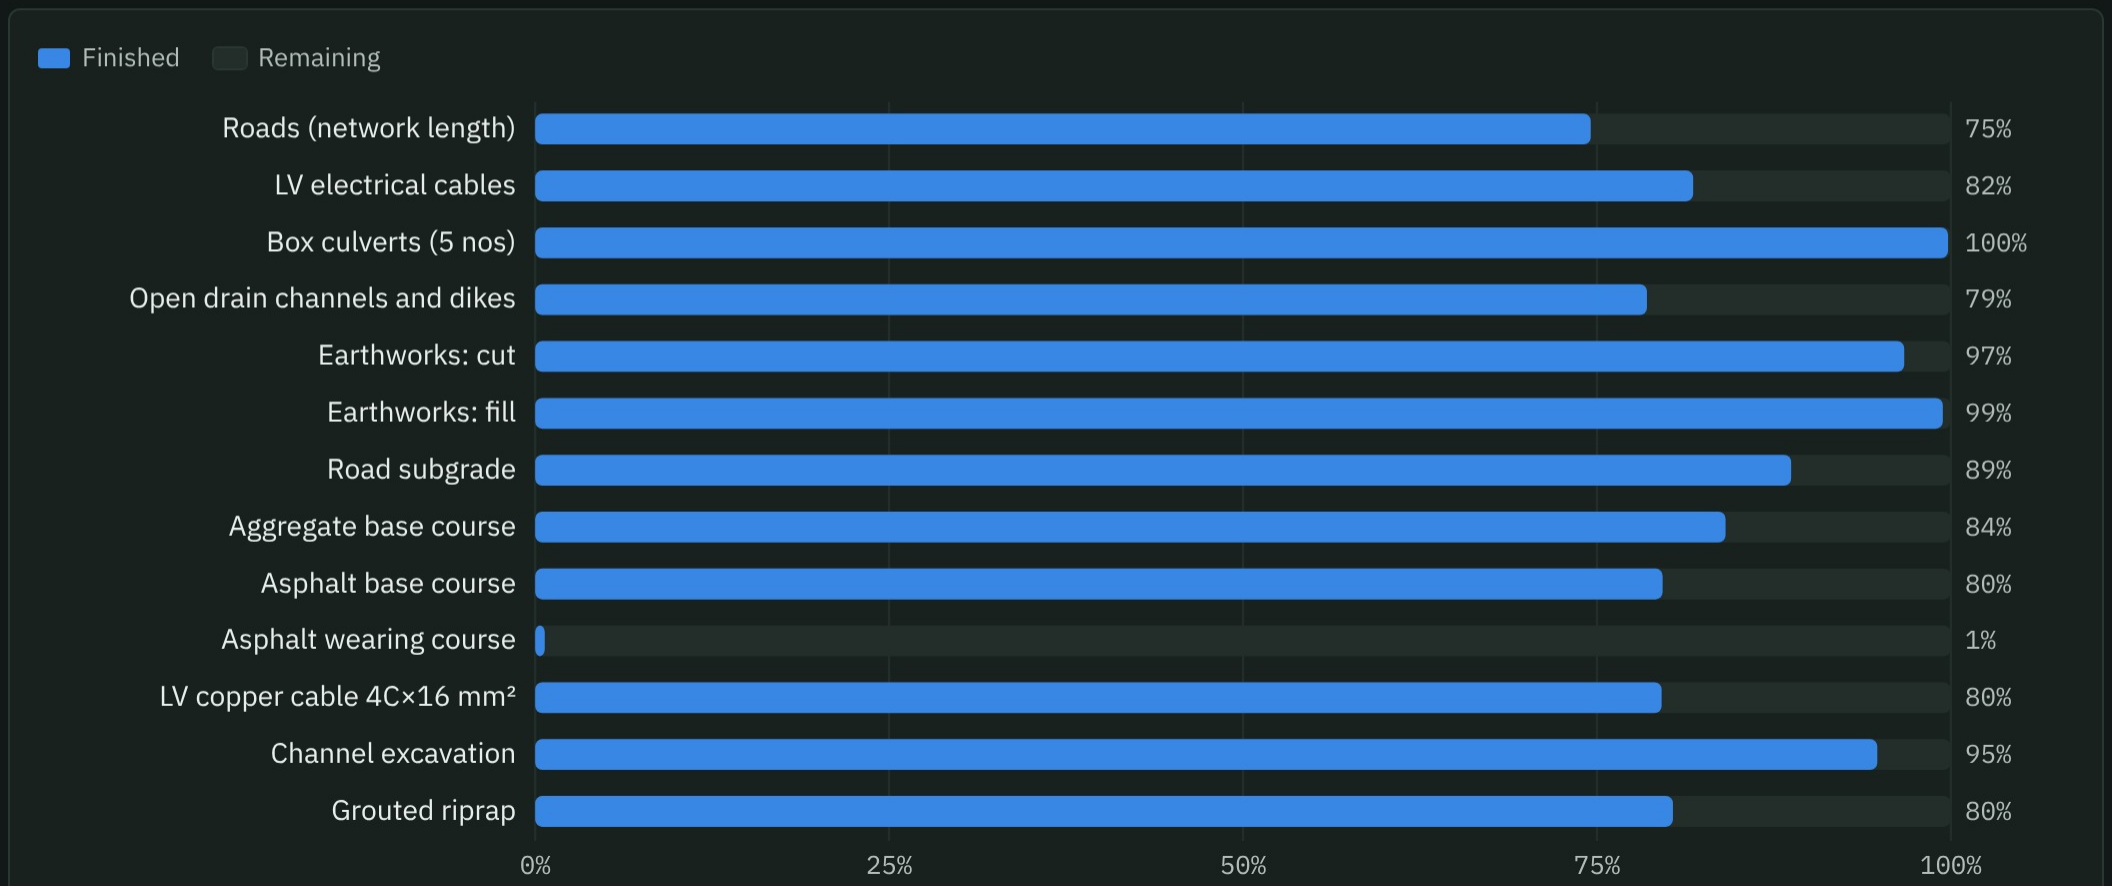

SCOPE ITEM	SOURCE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Roads (network length)	Progress Summary	LM	3,754	2,799	–	955	74.6%
LV electrical cables	Progress Summary	LM	8,464	6,923	–	1,541	81.8%
Box culverts (5 nos)	Progress Summary	%	100	99.8	–	0.2	99.8%
Open drain channels and dikes	Progress Summary	LM	3,921	3,079	–	841.7	78.5%
Earthworks: cut	B1.31 22 00.01	m³	537,044	519,347	+10,548	17,697	96.7%
Earthworks: fill	B1.31 22 00.02	m³	438,397	435,902	+3,240	2,495	99.4%
Road subgrade	B1.31 22 00.03	m³	37,334	33,122	+301	4,212	88.7%
Aggregate base course	B1.32 11 23.01	m³	24,889	20,928	+802	3,961	84.1%
Asphalt base course	B1.32 11 26.01	m³	11,676	9,298	+313	2,377	79.6%
Asphalt wearing course	B1.32 12 16.01	m³	5,253	35.6	–	5,218	0.7%
LV copper cable 4C×16 mm²	B2.26 05 19.01	m	8,007	6,371	–	1,636	79.6%
Channel excavation	B6.31 22 00.04	m³	115,262	109,271	–	5,991	94.8%
Grouted riprap	B6.31 25 00.02	m²	49,594	39,857	–	9,737	80.4%

Box culverts and open channels

The five box culverts are 99.8% complete; the base slab of culvert 5 was poured this week. Channel excavation is 94.8% done and grouted riprap 80.4%.

Not yet started or barely started

The asphalt wearing course is at 0.7% (35.6 of 5,253 m³). This week's work also included 571 m² of interlock paving on Arterial Road 4, but the report has no current total for interlock.

Milestones

Baseline and forecast dates from the weekly report's milestone sheet, with the forecast and float from the P6 update UP 33.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	15-Feb-2026	15-Feb-2026	15-Feb-2026 (actual)	–	✓ Done
Baseline programme approval	14-Mar-2026	01-Mar-2026	01-Mar-2026 (actual)	–	✓ Done
Completion of mobilisation	14-Mar-2026	06-Jun-2026 (+84 d)	06-Jun-2026 (actual)	–	✓ Done
Prequalification and material approval	14-Mar-2026	06-Jun-2026 (+84 d)	06-Jun-2026 (actual)	–	✓ Done
Long-lead materials delivered	16-Aug-2026	29-Aug-2026 (+13 d)	29-Aug-2026 (actual)	–	✓ Done
Completion of road works	14-Dec-2026	11-Jan-2027 (+28 d)	11-Jan-2027	45	▼ Later than baseline
Completion of open drain channels	14-Jun-2027	29-Jun-2027 (+15 d)	29-Jun-2027	3	▼ At risk
Completion of all works	14-Aug-2027	30-Aug-2027 (+16 d)	30-Aug-2027	−14	▼ Late
Final handover	14-Aug-2027	30-Aug-2027 (+16 d)	30-Aug-2027	−14	▼ Late

The weekly report and the P6 update agree on every forecast date.

Both put completion of all works and final handover on 30-Aug-2027, 16 calendar days after the contract date; P6 shows this as −14 days of float. Road works keep 45 days of float but finish 28 days after their baseline date, and the open drain channels have only 3 days of float.

Procurement of key materials

Share of the required quantity procured, per material. Source: Procurement sheet, weekly report 20-Oct-2026.



Pavement markings: no purchase order


5,712 m² required, 0% procured, although the material was required on site from 17-May-2026.

Asphalt and kerbs still being supplied

Bituminous base and wearing course is 55% procured (9,334 of 16,929 m³) and precast kerbs 79% (17,414 of 21,915 m). The report shows 17 of 18 planned materials on site, with the last road-works material due by 10-Nov-2026.

Manpower

Monthly average head count on site, manual and non-manual combined, planned vs actual.
Source: Manpower sheet.

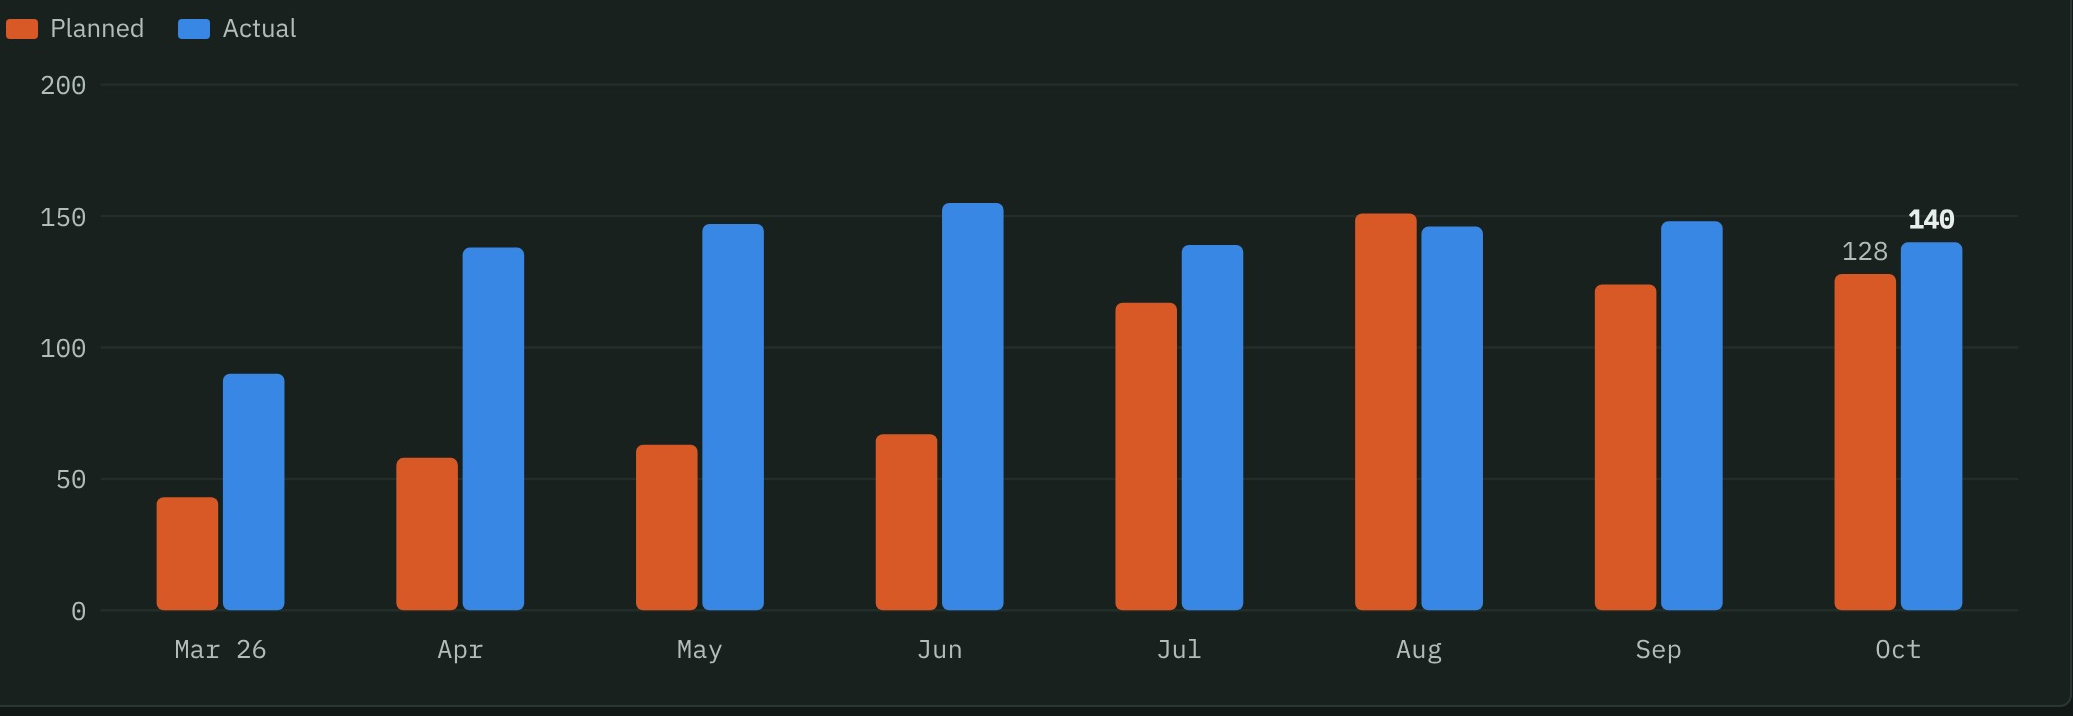

October head count is 140 against 128 planned: 115 manual (116 planned) and 25 staff (12 planned). Equipment on site averages 64 units against 49 planned. The manual plan peaks at 161 in January 2027.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	52,025,516
Contract value incl. 15% VAT	59,829,343
Change orders	0
Potential changes	0
Estimate at completion	52,025,516
FIR value to date	40,386,553

All values in SAR. No change orders are registered. The FIR (field inspection) value to date is 77.6% of the contract value.

Invoices

Invoices submitted	7
Gross value	29,797,667
Deductions and penalties	2,000
Net incl. VAT	34,269,317
Paid (6 invoices)	31,459,715
Approved, awaiting payment	2,809,602

Invoicing is 57.3% of the contract value against 80.0% physical progress. Invoice 7 (24-Aug to 26-Sep-2026) was approved by accounts on 12-Oct-2026 and is not yet paid. No retention or advance payment is recorded.

Health, safety and quality

Safety Score 86.4%

Safe man-hours (cumulative)	196,660
Man-hours this week	4,560
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses (cumulative)	1
Property damage	0
Inductions / toolbox talks	12 / 51

Consultant HSE inspection, 20-Oct-2026. Average score to date 85.2%.

Quality Score 90.0%

FIRs issued / closed	910 / 901
FIRs pending	9
NCRs issued / closed	2 / 2
Site instructions issued / closed	25 / 24
MIRs issued / closed	31 / 31
Shop drawings approved / submitted	28 / 36
Material submittals approved / submitted	63 / 65

Cumulative to 20-Oct-2026. Consultant quality inspection score 89.95% this week; average to date 84.7%.

Open issues and risks

ISSUE	OWNER	DETAIL
Additional works, Collector 9	Contractor / MODON	Scope change adding works on Collector 9. Open in the risk register, target date 14-Nov-2026.
New Road 52	Contractor / MODON	Scope change to build Road 52, rated very high (score 25 after treatment). Open, target date 28-Dec-2026.
New Al Gloud Road	Contractor / MODON	Listed as a project challenge in the Progress Summary. The risk register shows it open; the risk log shows it closed, target date 01-Dec-2026.
Connection to the 5th Ring Road	Contractor	Asphalt works started 08-Oct-2026 and are 8.4% complete; with the finishing works they carry –14 days of float and set the project finish date.

The weekly report's issue log and top-five issues table are empty this week. Other register entries (design of Open Channel 3A, culvert 3, Hajj-period permits) are closed.

Data notes

- The two summary sheets (files 15 and 16) give actual progress as 77.67% (77.08% last week) and planned as 55.76%. These are the cost-based earned-value figures; physical progress weighted by man-hours is 80.05% against 49.99% planned.
- File 15 gives the progress this week as –0.59%, file 16 as +0.59%. Cost-based progress rose from 77.08% to 77.67%, so the sign in file 15 is wrong.
- File 15 names the MODON PM as عبد الله الجليفي and file 16 as عبد الله الشنيفي. File 16 also gives project start 24-Nov-2025 and contract end 23-May-2026, against site handover 15-Feb-2026 and completion 14-Aug-2027 everywhere else.
- Only this week's and last week's cumulative progress are in the report, so the weekly table has two rows and last week's gain is shown as "—".
- The revised plan in the Physical-Chart Data and EV-Chart Data sheets is identical to the baseline.
- The Progress (2) sheet shows schedule % complete above 100% for road works (274%) and box culverts (200%), and puts the whole project earned value (40.4M SAR) against Mobilisation.
- The Major Quantities sheet has an older block of items at zero (subgrade 21,604 m³, base course 14,403 m³, kerbs 23,250 "m³", 15 kV cable 5,632 "m²", substation, RMU, 7 m lighting poles and others) next to the current items with progress. Only the current items are used.
- LV cable: the Major Quantities sheet gives 6,371 of 8,007 m installed; the Progress Summary gives 6,923 of 8,463.65 m.
- Luminaires are 264 in the Procurement sheet and 247 in the Progress Summary; earthing units 17 and 15. Procurement is 90.5% complete by man-hours although 17 of 18 materials are reported on site.
- The invoice summary shows 0 submitted invoices although 7 are logged, and a submitted value (34,267,317) 2,000 SAR below the approved value (34,269,317). The revised contract value and EAC cells also hold 21,100,000 and 20,900,000 next to 52,025,516.
- General Information dates baseline schedule approval 01-Mar-2025, before contract award; the milestone sheet and P6 give 01-Mar-2026. In the FIR summary, FIR-0880 is dated 10-Nov-2026 (after the data date) and FIR-0882 and FIR-0885 are dated June and May 2026, within the 14–20 Oct period.
- Manual head count in October is 115 (116 planned) in the Manpower sheet, but the trade breakdown in the Weekly Progress Report sheet shows 105 planned and 105 actual.
- The risk dashboard (file 17) shows 240 open risks and 133 open issues but zero in every category; the log lists 8 risks, 3 of them open. Culvert 4 and Al Gloud Road are open in the weekly report's risk register but closed in file 17.
- The P6 milestone table inside the Milestones sheet (for example mobilisation 02-Apr-2026) is out of date; milestone forecasts and float are taken from the P6 file UP 33.
- The weekly report measures the delay as 16 calendar days; P6 gives –14 days of float.

Compiled 28-Oct-2026 from the weekly report of 20-Oct-2026 (report no. 36) and its P6 update UP 33.
