Ready-Built Factories Program, Package 3: 20 Factories of 900 m² in Hail

برنامج المصانع الجاهزة و المنتجات الجديدة الحزمة الثالثة (المحفظة الاستثمارية) - حائل 20 مصنع 900 متر

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Saudi Zaas Construction	EGIS	Eng. Bader Alrowaidan	04-Dec-2025	03-Dec-2026

Scope: 20 ready-built factories of 900 m² each in five blocks (A to E), with external utilities, roads, parking and street lighting. Contract value 44,567,415.90 SAR.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. Weekly report No. 43 (data date 01-Nov-2026) reports the project 100.0% complete against 98.8% planned, 1.2% ahead. It gained 1.6% this week against 1.0% planned, closing out the remaining roads, fences, landscaping, building finishes and close-out documents.

PHYSICAL % COMPLETE
100.0% / 98.8% plan
▲ SPI 1.01 +1.2%

PROGRESS THIS WEEK
+1.6% / +1.0% plan
▲ 0.6% above the weekly plan

CONTRACT TIME ELAPSED
91.2% · day 332 of 364
▲ Completed 01-Nov-2026

INVOICED TO DATE (GROSS)
76.4% · 34.0M SAR
10 invoices, all paid; last period ends 06-Oct-2026

All works are reported complete on 01-Nov-2026, 32 days before the contract completion date.

The P6 update records all 1,827 activities complete, with construction finished on 29-Oct-2026, testing and commissioning on 31-Oct-2026 and initial handover on 01-Nov-2026. Close-out went from 0% to 100% in one week, and several activities that were open at the 26-Oct-2026 update now carry actual dates before it (see Data notes). The workbook's own summary still forecasts completion on 03-Dec-2026, and 33 field inspection requests remain pending.

Site photos this week

Four photos from the weekly report workbook No. 43, date-stamped 31-Oct-2026 to 02-Nov-2026. They show the completed buildings, roads, planting and a finished factory hall. Select a photo to view it larger, then use the arrows to move between photos.



Water tank and pump room

Panel water tank and fire-pump room beside the factory blocks. Stamped 31-Oct-2026.



Internal road

Asphalt, curbs, street lighting and new planting along the factories. Stamped 01-Nov-2026.



Completed external works

Planted verge and street lighting in front of the factory row. Stamped 02-Nov-2026.




Completed factory hall

Finished floor, ducting, lighting and office fronts. Stamped 01-Nov-2026.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet, weekly report No. 43.

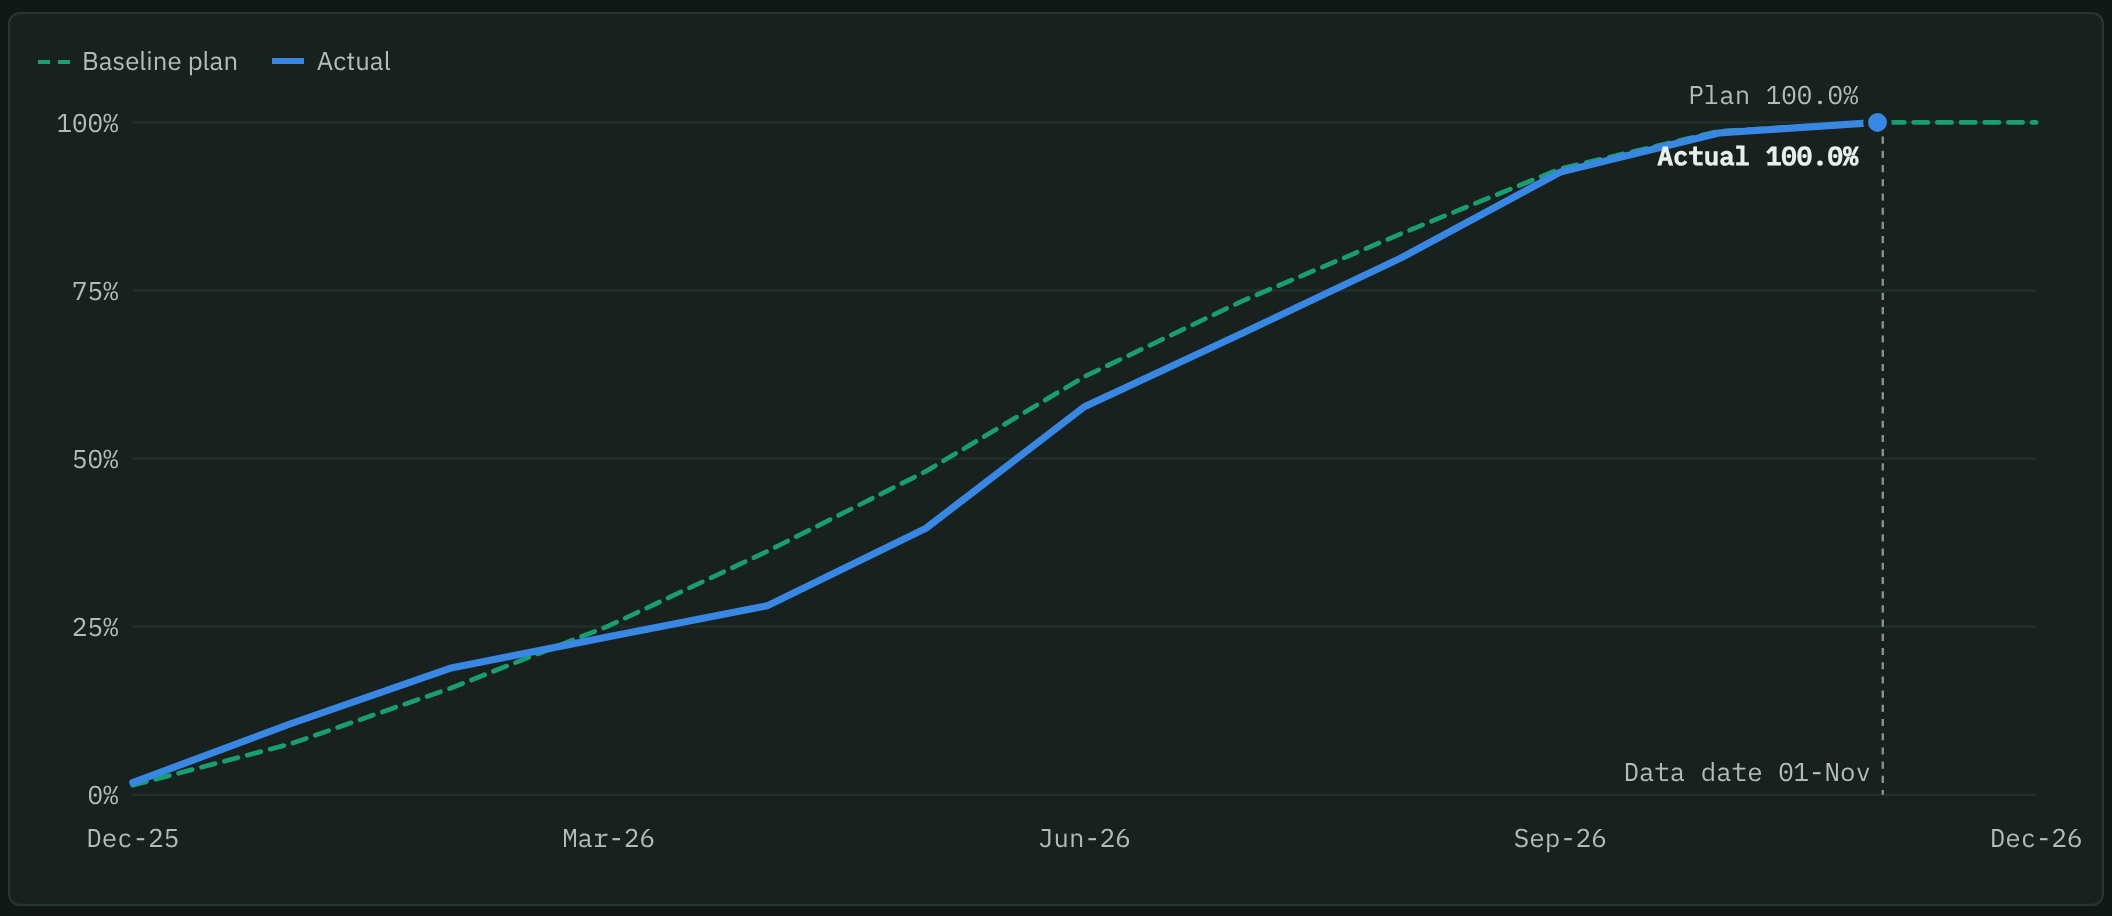

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
26-Oct-2026	97.8	98.4	+0.6	+1.3	1.01
01-Nov-2026	**98.8**	**100.0**	**+1.2**	**+1.6**	**1.01**

Weekly values from workbooks No. 42 and No. 43, both on a budget of 116,776 man-hours. Earlier weeks are not part of this upload. The revised plan in the sheet is identical to the baseline, so only one plan line is drawn.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet, weekly report No. 43.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	12.6%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	23.5%	100.0%	100.0%	0.0	1.00	✓ Complete
Construction	59.1%	97.7%	100.0%	+2.3	1.02	✓ Complete
Testing & commissioning	3.4%	84.6%	100.0%	+15.4	1.18	✓ Complete
Project close-out	0.5%	40.1%	100.0%	+59.9	2.49	✓ Complete
Total	100%	**98.8%**	**100.0%**	**+1.2**	**1.01**	✓ Complete

Weights are each phase's share of the 116,776 budgeted man-hours. The planned figures for construction, testing and close-out are unchanged from last week's workbook. Within construction, planned electrical hours (6,655) exceed the electrical budget (6,304). The P6 update lists all 1,827 activities as completed.

Scope of work: quantities

The 16 quantities tracked in the Major Quantities sheet of weekly report No. 43. "This week" is the change since workbook No. 42.

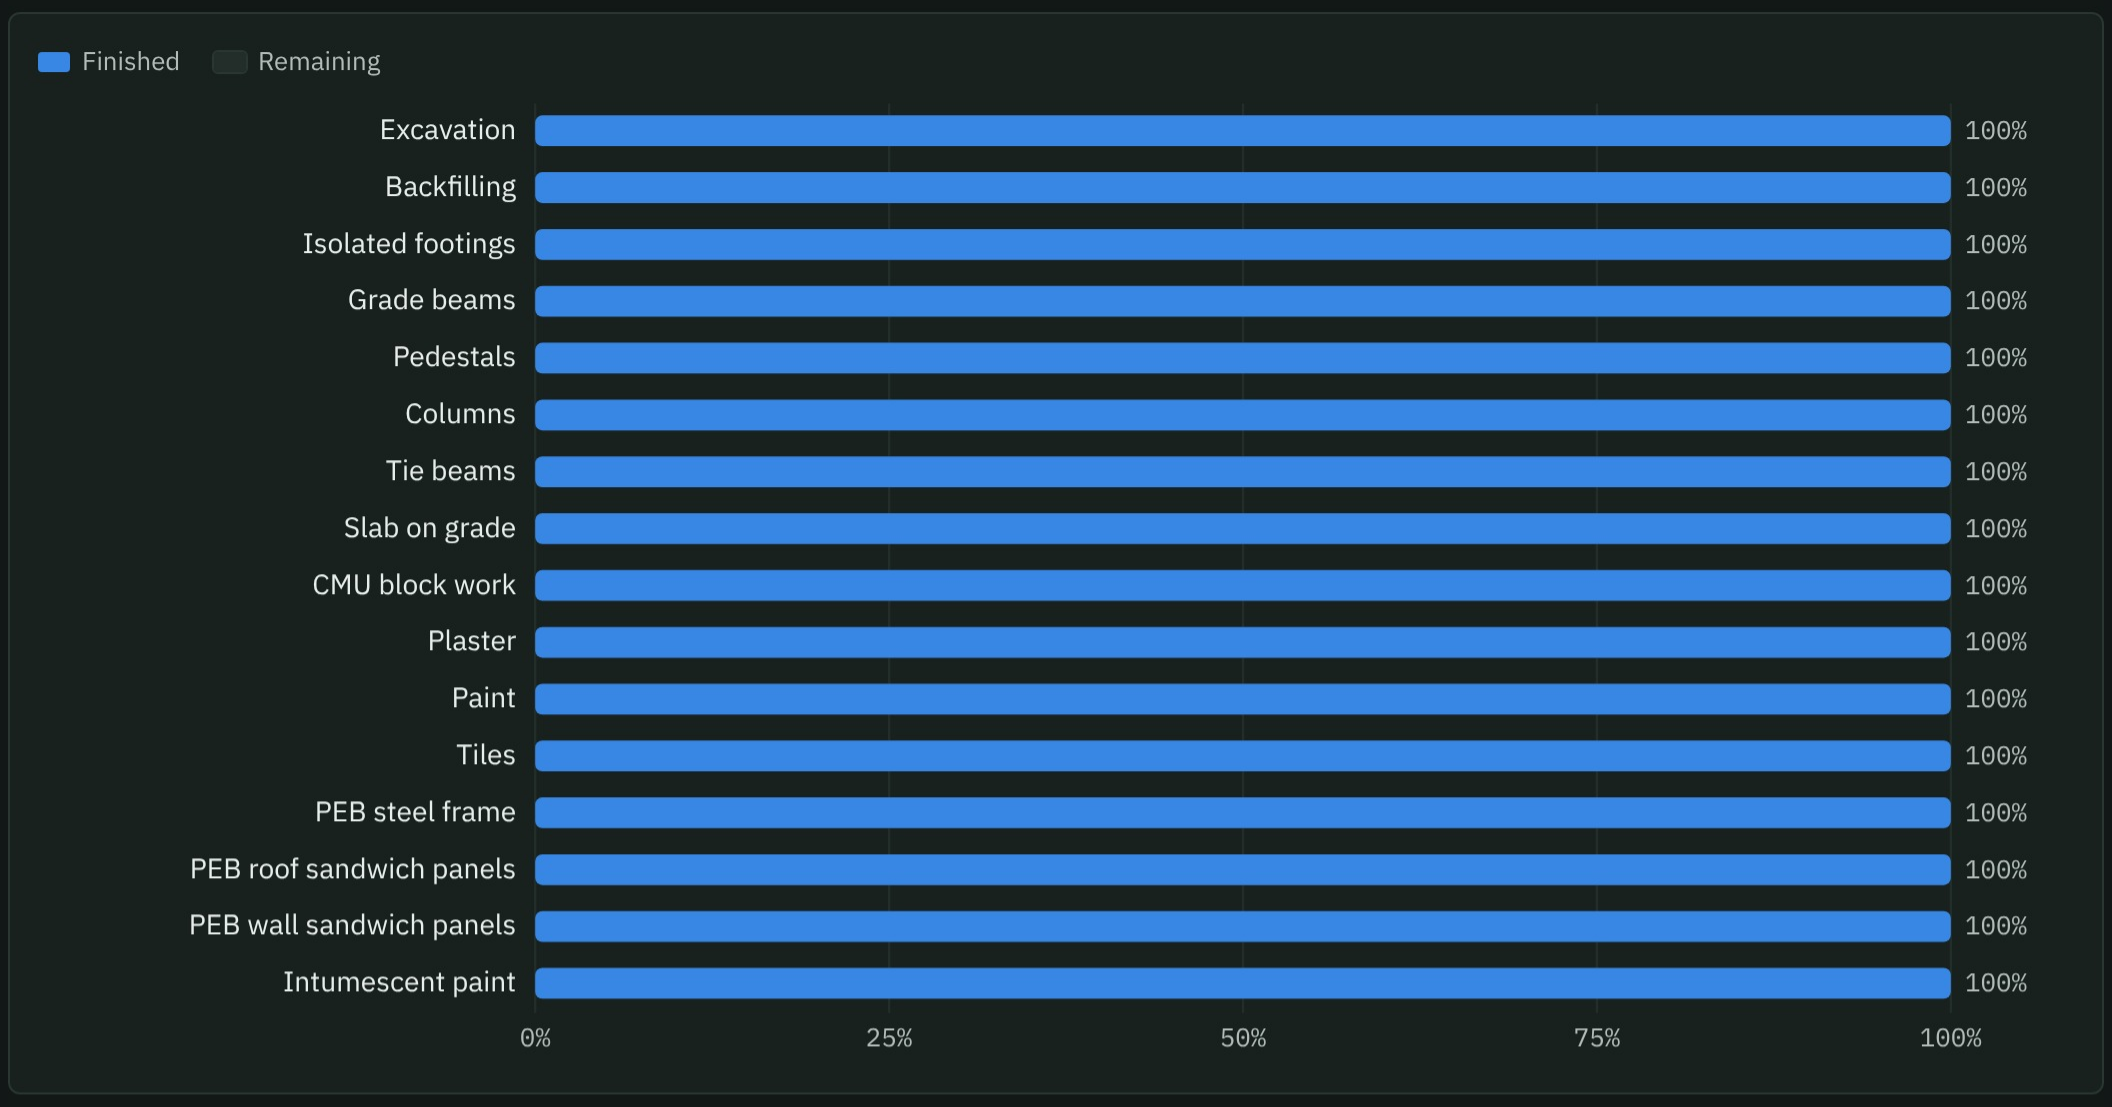

SCOPE ITEM	BOQ ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Excavation	2.1.1	m³	26,030	26,030	0	0	100.0%
Backfilling	2.1.8	m³	11,950	11,950	0	0	100.0%
Isolated footings	3.2.1	m³	1,315	1,315	0	0	100.0%
Grade beams	3.2.2	m³	250	250	0	0	100.0%
Pedestals	3.2.4	m³	220	220	0	0	100.0%
Columns	3.2.5	m³	185	185	0	0	100.0%
Tie beams	3.2.6	m³	75	75	0	0	100.0%
Slab on grade	3.2.10	m³	3,235	3,235	0	0	100.0%
CMU block work	4.1	m²	4,930	4,930	0	0	100.0%
Plaster	9.2.1	m²	5,355	5,355	0	0	100.0%
Paint	9.2.2	m²	5,355	5,355	+535.5	0	100.0%
Tiles	9.2.3	m²	2,600	2,600	0	0	100.0%
PEB steel frame	11.1.1	Nos	5	5	0	0	100.0%
PEB roof sandwich panels	11.1.1	Nos	5	5	0	0	100.0%
PEB wall sandwich panels	11.1.1	Nos	5	5	0	0	100.0%
Intumescent paint	11.1.5	Nos	5	5	0	0	100.0%

All tracked quantities are finished.

Paint was the last open item: 535.5 m² was finished this week, taking it from 4,819.5 m² to the full 5,355 m². The sheet tracks building items only; roads, fences, landscaping and networks have no quantity table.

Milestones

Baseline and forecast from the Milestones sheet of weekly report No. 43, with the actual dates in the P6 update. All milestones are achieved.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE	STATUS
Contract award	09-Nov-2025	09-Nov-2025	–	✓ Done
Contract signing	01-Dec-2025	01-Dec-2025	–	✓ Done
Site handover	04-Dec-2025	04-Dec-2025	04-Dec-2025 (actual)	✓ Done
Existing condition survey and final reports	04-Jan-2026	04-Jan-2026	04-Dec-2025 (actual)	✓ Done
Complete mobilisation	13-Jan-2026	05-Jan-2026 (8 d early)	05-Jan-2026 (actual)	✓ Done
Submittals approved and long-lead items ordered	14-Apr-2026	28-Jun-2026 (75 d late)	–	✓ Done late
Complete earthworks	12-Sep-2026	12-Oct-2026 (30 d late)	–	✓ Done late
All equipment and materials delivered	03-Oct-2026	15-Oct-2026 (12 d late)	19-Oct-2026 (actual)	✓ Done late
Complete civil works	02-Nov-2026	26-Aug-2026 (68 d early)	26-Aug-2026 (actual)	✓ Done
Complete mechanical works	28-Oct-2026	08-Oct-2026 (20 d early)	08-Oct-2026 (actual)	✓ Done
Complete electrical works	19-Sep-2026	31-Oct-2026 (42 d late)	31-Oct-2026 (actual)	✓ Done late
All works complete, ready for initial handover	03-Dec-2026	01-Nov-2026 (32 d early)	01-Nov-2026 (actual)	✓ Done
Complete demobilisation	03-Dec-2026	01-Nov-2026 (32 d early)	29-Oct-2026 (actual)	✓ Done

The workbook's milestone baselines do not match the P6 baseline.

The workbook gives 02-Nov-2026 for civil works, 28-Oct-2026 for mechanical and 19-Sep-2026 for electrical works; the P6 baseline gives 14-Jul-2026, 01-Oct-2026 and 26-Nov-2026. Against the P6 baseline, civil works finished 43 days late and electrical works 26 days early. The P6 "materials" date shown is its "Completion of Engineering and Materials" milestone.

Procurement of key materials

Material items delivered to site, by discipline. Source: Procurement summary, weekly report No. 43.




79 of 81 material items are on site.

All 81 purchase orders are issued. The two civil items with no delivery date are concrete parking bumpers and road markings, although P6 shows traffic lines and wheel bumpers installed on 28–29 Oct and road markings delivered on 15-Oct-2026.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet, weekly report No. 43.

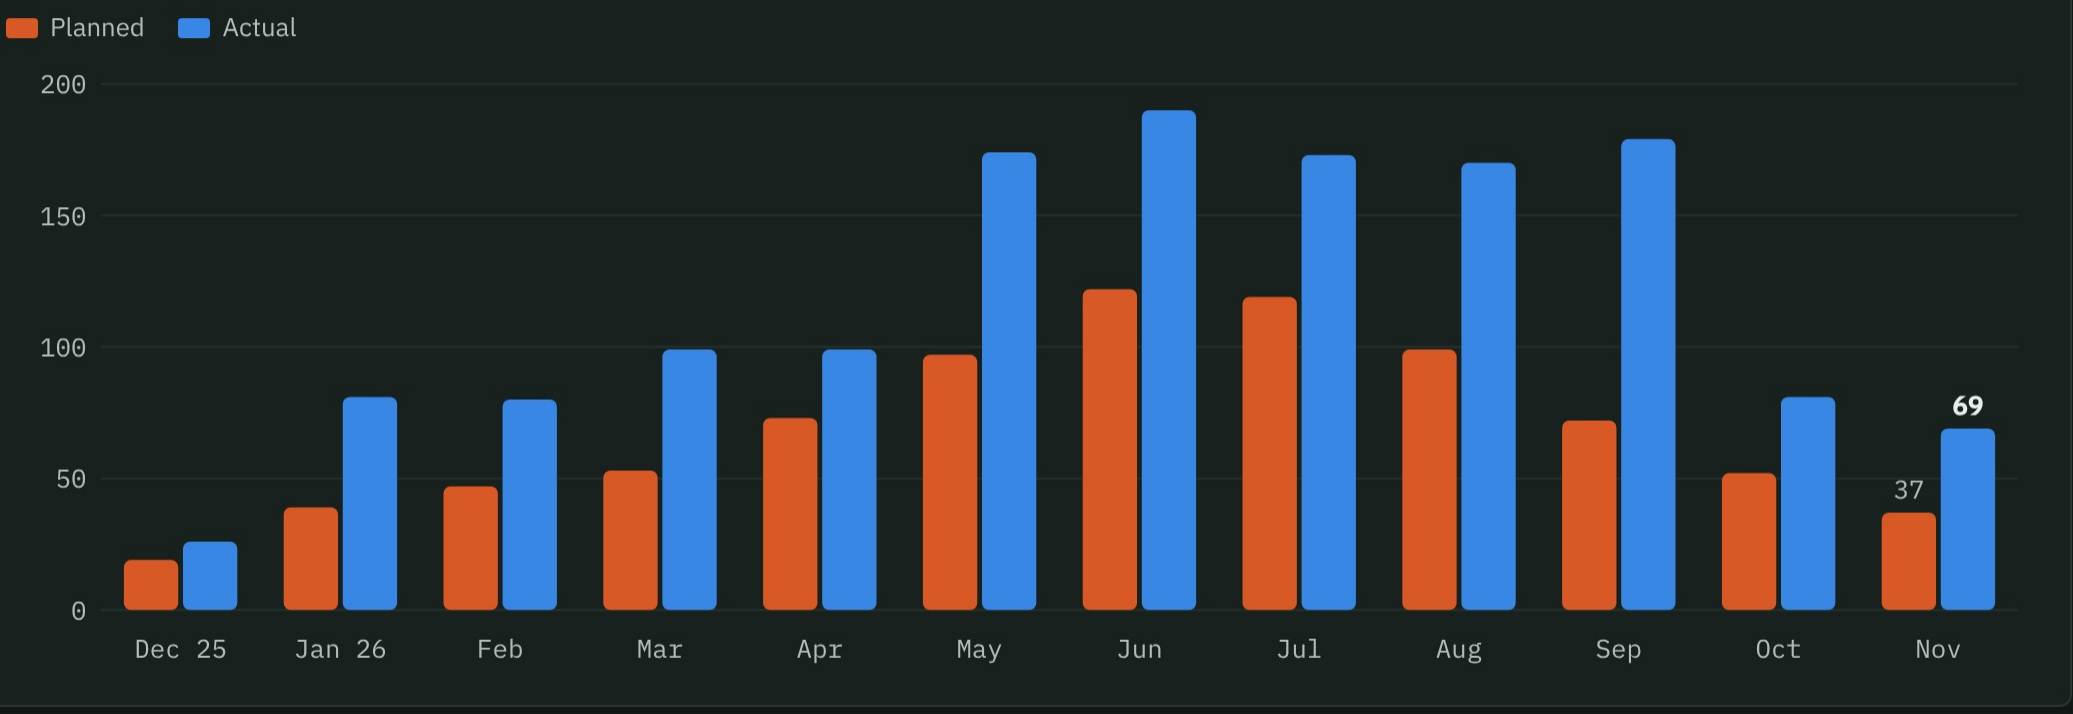

The November head count is 69 against 37 planned (17 staff against 7, and 52 workers against 30), down from 81 in October. Equipment on site: 11 against 2 planned, of which 7 idle. The peak was 190 in June 2026.

Cost and invoicing

Contract value

Original contract value	44,567,415.90
Revised contract value	44,567,415.90
Change orders	0
Potential changes	0
Not yet invoiced	10,523,669.03

All values in SAR. The change order log is empty.

Invoices

Invoices submitted / approved / paid	10 / 10 / 10
Gross value	34,043,746.87
Advance payment recovery	−3,404,374.69
Deductions and penalties	−10,000.00
Retention	0
Paid to date	30,629,372.18

Invoice 10 (08-Sep to 06-Oct-2026, 7,083,278.97 net) was paid on 01-Nov-2026. Invoicing stands at 76.4% of the contract value against 100% physical progress. The log deducts a 10% advance payment recovery although it records no advance payment.

Health, safety and quality

Safety Score 0.92

Safe man-hours (cumulative)	310,512
Man-hours this week	3,844
Lost-time injuries	0
Fatalities	0
First-aid cases (cumulative)	1
Near misses	0
Property damage	0
Inductions / toolbox talks (sessions)	206 / 98

Quality Score 0.95

FIRs issued / closed (cumulative)	2,028 / 1,995
FIRs pending	33
FIRs this week: issued / closed	59 / 80
NCRs issued / closed	6 / 6
Site instructions issued / closed	8 / 8
MIRs issued / closed	229 / 229
Shop drawings approved	166 / 166
Material submittals approved	120 / 120

This-week FIR figures compare with workbook No. 42 (1,969 issued, 1,915 closed).

Open issues and risks

ISSUE	OWNER	DETAIL
Pending field inspections	Consultant	33 field inspection requests are still pending, all less than 10 days old, after all works were reported complete.
Final invoicing	Contractor	76.4% of the contract value is invoiced against 100% physical progress; 10,523,669.03 SAR remains to be invoiced.
Procurement log not closed	Contractor	Concrete parking bumpers and road markings have no delivery date, although the items are installed according to P6.
Completion date not updated	Contractor	The workbook summary still forecasts completion on 03-Dec-2026 with zero variance, while its milestone sheet and P6 show 01-Nov-2026.
Weather	Contractor	The only open risk in the register: rain and sandstorms, rated low after treatment.

The issue log holds one issue, closed on 17-May-2026: removal of electrical panels and an RMU by SEC at Block A (owner: MODON).

Data notes

- The weekly report workbook has no text version in MD Files; it was read directly from the original (.xlsb) file for this report. The P6 update and P6 report were read from MD Files.
- Physical progress and the S-curve use the workbook's man-hour figures (116,776 budgeted). The P6 reports used for weeks 45 and 46 had a budget of 116,740; the 36-hour difference is procurement, where the workbook uses the earned hours as the budget.
- The workbook's weekly physical figures (1,605 planned, 1,504 earned) are the same as in workbook No. 42. This week's gain (+1.6% earned, +1.0% planned) is calculated from the to-date figures of both workbooks.
- Several activities that were open in the 26-Oct-2026 P6 update now carry actual dates on or before that date: steel fence and base plates (21–25 Oct), tree and shrub planting (19–26 Oct), street-lighting feeder pillars (finished 19-Oct-2026) and asphalt wearing course (finished 22-Oct-2026).
- The P6 report now shows cost-based columns only, which are not used here. The P6 update file is coded HAL1-05-13 (HAL1-05-10 last week) and gives a planned start of 14-Mar-2023; its data date is 02-Nov-2026, one day after the workbook.
- The procurement sheet has unit errors (for example fire pumps in m^2 and access control in m^3).
- The workbook summary still forecasts completion on 03-Dec-2026 with zero variance, while its milestone sheet and P6 show completion on 01-Nov-2026.
- Report week: the Milestones sheet states "Current Contract Weeks: 47 of 52", which matches 332 days from site handover (04-Dec-2025). Workbook No. 42 also stated week 47, one week early; last week's report used week 46.
- One photo is stamped 02-Nov-2026, one day after the data date. None has a GPS stamp.

Compiled 05-Nov-2026 from the W06 upload (weekly report No. 43 workbook, P6 update and P6 report, data date 01-Nov-2026), compared with weekly report No. 42.
