
Development of the Technology City in Dammam Project
BL-Update05-10-2026
WBS Summary Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Schedule % Complete	Performance % Complete	Budgeted Total Cost	Planned Value Cost	Earned Value Cost
	Development of the Technology City in Dhahra	436	06-Jan-26 A	17-Jun-27	33.42%	18.13%	93,388,698	31,210,172	16,935,047
	Key Milestones	436	06-Jan-26 A	17-Jun-27	0%	0%	0	0	0
	Preliminaries and Mobilization Works	79	06-Jan-26 A	11-Apr-26 A	0%	0%	0	0	0
	Engineering Works	242	06-Jan-26 A	25-Oct-26	0%	0%	0	0	0
	Procurement Cycle	319	02-May-26 A	23-May-27	0%	0%	0	0	0
	Construction Works	368	10-Mar-26 A	31-May-27	33.42%	18.13%	93,388,698	31,210,172	16,935,047
	Infrastructure Networks	364	10-Mar-26 A	26-May-27	51.15%	23.46%	57,696,530	29,514,560	13,535,825
	Internal	364	10-Mar-26 A	26-May-27	49.78%	9.4%	32,508,953	16,182,294	3,055,456
	Alignment-RD-01	346	10-Mar-26 A	29-Apr-27	52.95%	20.1%	15,199,337	8,048,109	3,055,456
	Alignment-RD-02	176	25-Oct-26	26-May-27	48.92%	0%	7,655,882	3,745,016	0
	Alignment-RD-03-1	172	28-Sep-26	19-Apr-27	36.2%	0%	3,448,486	1,248,299	0
	Alignment-RD-03-2	191	03-Oct-26	22-May-27	52.01%	0%	3,959,670	2,059,402	0
	Alignment-RD-03-3	166	12-Oct-26	26-Apr-27	48.16%	0%	2,245,578	1,081,468	0
	External	316	01-Apr-26 A	13-Apr-27	52.93%	41.61%	25,187,577	13,332,266	10,480,369
	External Road - 1 - 1	315	01-Apr-26 A	12-Apr-27	62.19%	49.95%	5,221,714	3,247,135	2,608,226
	External Road - 1 - 2	302	18-Apr-26 A	13-Apr-27	62.3%	23.4%	7,651,591	4,767,067	1,790,191
	External Road - 2	284	09-May-26 A	13-Apr-27	62.12%	35.19%	3,781,297	2,348,995	1,330,763
	External Road - 3	284	09-May-26 A	13-Apr-27	34.8%	55.68%	8,532,974	2,969,069	4,751,189
	Superstructure Work	206	01-Aug-26 A	31-May-27	4.75%	9.52%	35,692,169	1,695,612	3,399,222
	Testing and Comissioning	24	12-May-27	14-Jun-27	0%	0%	0	0	0
	Handing over and close out	23	23-May-27	17-Jun-27	0%	0%	0	0	0

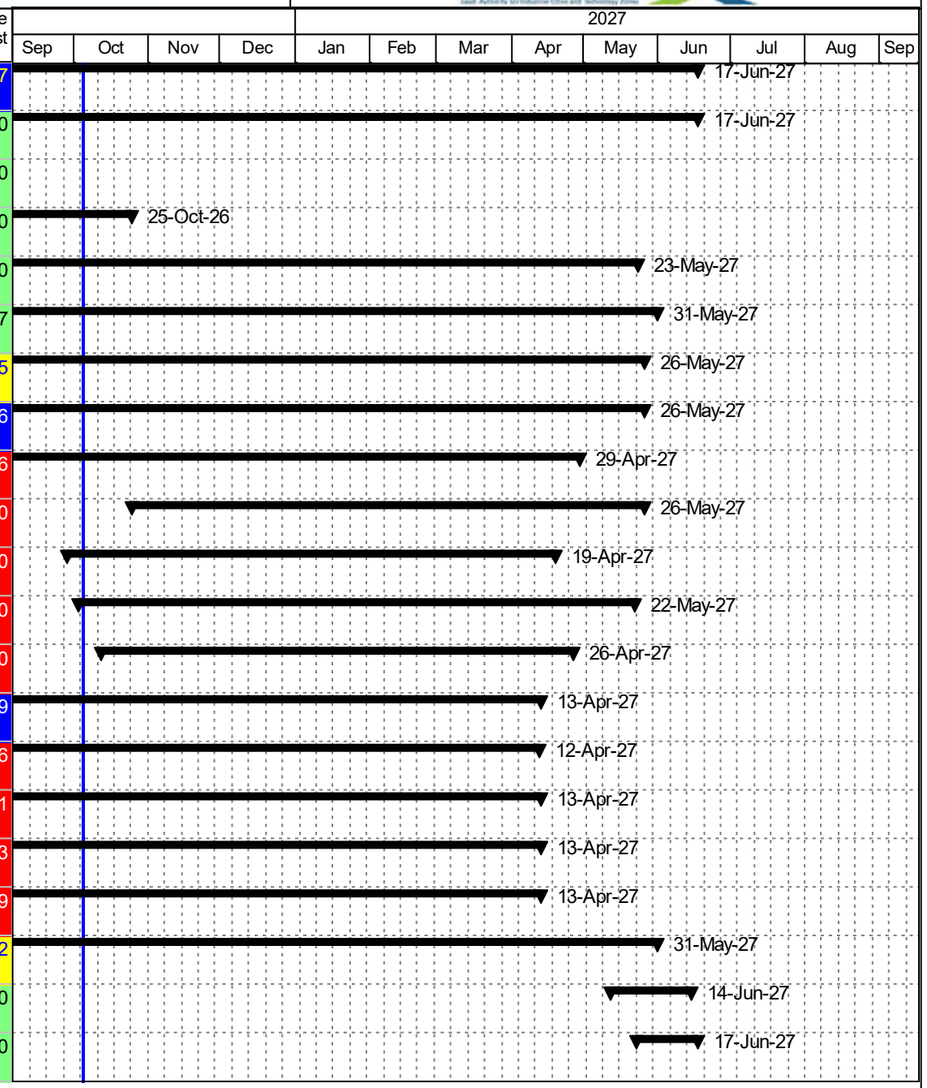

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
05-Oct-26	Third Industrial City		
