
Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
28-09-2026		140d	140d	23-Jun-26	05-Apr-27	29-Sep-26	15-Mar-27	304d	1497	97.8%	0%	30,469,634
JDH3-02-009-Al-Khorayef Factory Roac		18d	18d	23-Jun-26	06-Oct-26	29-Sep-26	19-Oct-26	426d	17	97.45%	0%	54,099
Construction		18d	18d	23-Jun-26	06-Oct-26	29-Sep-26	19-Oct-26	426d	17	97.45%	0%	54,099
JDH3-02-009-KF-Storm Network - ST		18d	18d	23-Jun-26	06-Oct-26	29-Sep-26	19-Oct-26	426d	17	97.45%	0%	54,099
JDH3-02-009-KF-(ST)-MH Works (1200) r		4d	4d	20-Aug-26	12-Sep-26	11-Oct-26	14-Oct-26	198d	2	100%	0%	1,052
JDH	Steel Coverfor MH 1200 mm - de	2d	2d	01-Sep-26	12-Sep-26	13-Oct-26	14-Oct-26	198d	1	100%	0%	351
JDH	Finishing, Benching, Testing Worl	2d	2d	20-Aug-26	31-Aug-26	11-Oct-26	12-Oct-26	198d	1	100%	0%	701
JDH3-02-009-KF-(ST)-MH Works (1200) r		4d	4d	01-Sep-26	24-Sep-26	13-Oct-26	17-Oct-26	198d	2	100%	0%	3,217
JDH	Steel Coverfor MH 1200 mm - de	2d	2d	13-Sep-26	24-Sep-26	15-Oct-26	17-Oct-26	198d	1	100%	0%	1,072
JDH	Finishing, Benching, Testing Worl	2d	2d	01-Sep-26	12-Sep-26	13-Oct-26	14-Oct-26	198d	1	100%	0%	2,144
JDH3-02-009-KF-(ST)-MH Works (1500) r		4d	4d	23-Jun-26	15-Jul-26	29-Sep-26	03-Oct-26	432d	2	100%	0%	4,513
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	05-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	1,504
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	04-Jul-26	29-Sep-26	30-Sep-26	198d	1	100%	0%	3,009
JDH3-02-009-KF-(ST)-MH Works (1500) r		4d	4d	05-Jul-26	27-Jul-26	01-Oct-26	05-Oct-26	432d	2	100%	0%	13,509
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	16-Jul-26	27-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	4,503
JDH	Finishing, Benching, Testing Worl	2d	2d	05-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	198d	1	100%	0%	9,006
JDH3-02-009-KF-(ST)-MH Works (1500) r		4d	4d	13-Sep-26	06-Oct-26	15-Oct-26	19-Oct-26	198d	2	76.67%	0%	1,819
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	26-Sep-26	06-Oct-26	18-Oct-26	19-Oct-26	198d	1	30%	0%	606
JDH	Finishing, Benching, Testing Worl	2d	2d	13-Sep-26	24-Sep-26	15-Oct-26	17-Oct-26	198d	1	100%	0%	1,213
JDH3-02-009-KF-(ST)-MH Works (2000) r		2d	2d	26-Sep-26	06-Oct-26	18-Oct-26	19-Oct-26	198d	1	30%	0%	1,367
JDH	Finishing, Benching, Testing Worl	2d	2d	26-Sep-26	06-Oct-26	18-Oct-26	19-Oct-26	198d	1	30%	0%	1,367
JDH3-02-009-KF-(ST)-MH Works (2000) r		4d	4d	16-Jul-26	08-Aug-26	04-Oct-26	07-Oct-26	432d	2	100%	0%	15,605
JDH	Steel Coverfor MH 2000 mm - de	2d	2d	28-Jul-26	08-Aug-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	5,202
JDH	Finishing, Benching, Testing Worl	2d	2d	16-Jul-26	27-Jul-26	04-Oct-26	05-Oct-26	198d	1	100%	0%	10,403
JDH3-02-009-KF-(ST)-MH Works (2000) r		4d	4d	09-Aug-26	31-Aug-26	08-Oct-26	12-Oct-26	432d	2	100%	0%	2,400
JDH	Steel Coverfor MH 2000 mm - de	2d	2d	20-Aug-26	31-Aug-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	800
JDH	Finishing, Benching, Testing Worl	2d	2d	09-Aug-26	19-Aug-26	08-Oct-26	10-Oct-26	198d	1	100%	0%	1,600
JDH3-02-009-KF-(ST)-MH Works (2000) r		4d	4d	28-Jul-26	19-Aug-26	06-Oct-26	10-Oct-26	432d	2	100%	0%	10,617
JDH	Steel Coverfor MH 2000 mm - de	2d	2d	09-Aug-26	19-Aug-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	3,539
JDH	Finishing, Benching, Testing Worl	2d	2d	28-Jul-26	08-Aug-26	06-Oct-26	07-Oct-26	198d	1	100%	0%	7,078
JDH3-02-009-New Roads - NR		45d	45d	23-Jun-26	30-Sep-26	29-Sep-26	19-Nov-26	399d	108	99.89%	0%	1,532,423
A-MCG		8d	8d	23-Jun-26	29-Sep-26	29-Sep-26	07-Oct-26	388d	7	98.24%	0%	6,023
JDH3-02-009-AMCG-Storm Network- ST		8d	8d	23-Jun-26	29-Sep-26	29-Sep-26	07-Oct-26	388d	7	98.24%	0%	6,023
JDH3-02-009-AMCG-(ST)-MH Works (150		4d	4d	23-Jun-26	10-Aug-26	29-Sep-26	03-Oct-26	388d	2	100%	0%	1,560
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	18-Jul-26	10-Aug-26	01-Oct-26	03-Oct-26	388d	1	100%	0%	557
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	16-Jul-26	29-Sep-26	30-Sep-26	388d	1	100%	0%	1,003
JDH3-02-009-AMCG-(ST)-MH Works (120		4d	4d	18-Jul-26	03-Sep-26	01-Oct-26	05-Oct-26	388d	2	100%	0%	1,112
JDH	Steel Coverfor MH 1200 mm - de	2d	2d	11-Aug-26	03-Sep-26	04-Oct-26	05-Oct-26	388d	1	100%	0%	397
JDH	Finishing, Benching, Testing Worl	2d	2d	18-Jul-26	10-Aug-26	01-Oct-26	03-Oct-26	388d	1	100%	0%	715
JDH3-02-009-AMCG-(ST)-MH Works (150		4d	4d	11-Aug-26	29-Sep-26	04-Oct-26	07-Oct-26	388d	2	98.3%	0%	1,751
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	05-Sep-26	29-Sep-26	06-Oct-26	07-Oct-26	388d	1	95.24%	0%	625
JDH	Finishing, Benching, Testing Worl	2d	2d	11-Aug-26	03-Sep-26	04-Oct-26	05-Oct-26	388d	1	100%	0%	1,126
JDH3-02-009-AMCG-(ST)-MH Works (200		2d	2d	05-Sep-26	29-Sep-26	06-Oct-26	07-Oct-26	388d	1	95.24%	0%	1,600
JDH	Finishing, Benching, Testing Worl	2d	2d	05-Sep-26	29-Sep-26	06-Oct-26	07-Oct-26	388d	1	95.24%	0%	1,600
A-MCH		44d	44d	23-Jun-26	28-Sep-26	29-Sep-26	18-Nov-26	400d	6	100%	0%	38,515
JDH3-02-009-AMCH-Earthworks - EW		2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	399d	1	100%	0%	38
JDH3(	Backfill Layers with Imported Mate	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	399d	1	100%	0%	38
JDH3-02-009-AMCH-Storm Network - ST		6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	438d	4	100%	0%	3,704
JDH3-02-009-AMCH-(ST)-MH Works (150		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	438d	2	100%	0%	1,560
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	557
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	1,003

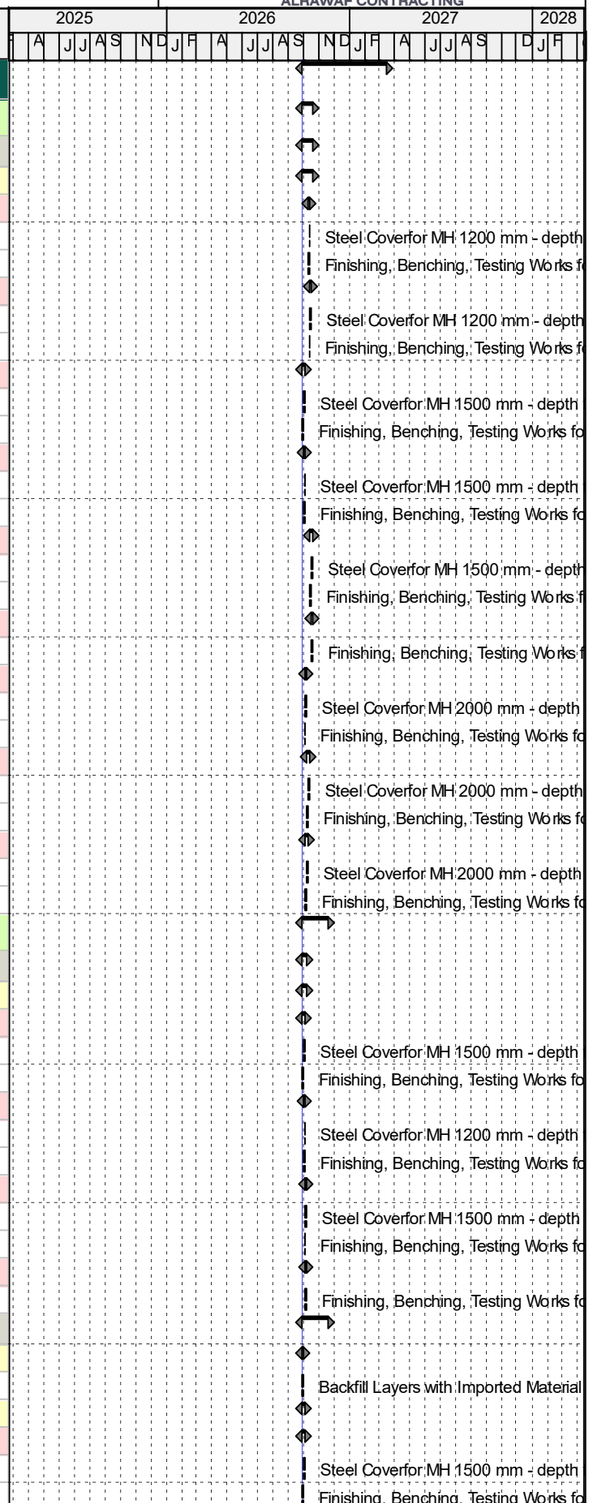


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDH3-02-009-AMCH-(ST)-MH Works (120		4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	438d	2	100%	0%	2,144
JDI	Steel Coverfor MH 1200 mm - dep	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	715
JDI	Finishing, Benching, Testing Work	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	1,430
JDH3-02-009-AMCH-Road Works - RD		2d	2d	27-Sep-26	28-Sep-26	17-Nov-26	18-Nov-26	314d	1	100%	0%	34,773
JDH3-02-009-AMCH-(RD)-Aggregate Bas		2d	2d	27-Sep-26	28-Sep-26	17-Nov-26	18-Nov-26	314d	1	100%	0%	34,773
JDI	Supply, lay and compaction Aggr	2d	2d	27-Sep-26	28-Sep-26	17-Nov-26	18-Nov-26	314d	1	100%	0%	34,773
A-MCA		34d	34d	23-Jun-26	26-Sep-26	29-Sep-26	07-Nov-26	410d	64	100%	0%	762,927
JDH3-02-009-AMCA-Sewage Network - SW		34d	34d	23-Jun-26	26-Sep-26	29-Sep-26	07-Nov-26	410d	21	100%	0%	110,270
JDH3-02-009-AMCA-(SW)-GRP Pipes-15(		20d	20d	23-Jun-26	15-Jul-26	29-Sep-26	21-Oct-26	400d	5	100%	0%	25,222
JDI	Backfilling and warning tape Work	6d	6d	09-Jul-26	15-Jul-26	15-Oct-26	21-Oct-26	400d	1	100%	0%	2,522
JDI	Primary Test for GRP Pipe Line 15	6d	6d	02-Jul-26	08-Jul-26	08-Oct-26	14-Oct-26	392d	1	100%	0%	2,522
JDI	Installing for GRP Pipe Line 150 r	3d	3d	29-Jun-26	01-Jul-26	05-Oct-26	07-Oct-26	392d	1	100%	0%	13,872
JDI	Bedding Works for GRP Pipe Line	3d	3d	25-Jun-26	28-Jun-26	01-Oct-26	04-Oct-26	392d	1	100%	0%	1,261
JDI	Excavation Works for GRP Pipe L	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	392d	1	100%	0%	5,044
JDH3-02-009-AMCA-(SW)-GRP Pipes-15(		20d	20d	09-Jul-26	01-Aug-26	15-Oct-26	07-Nov-26	392d	5	100%	0%	21,230
JDI	Backfilling and warning tape Work	6d	6d	26-Jul-26	01-Aug-26	01-Nov-26	07-Nov-26	392d	1	100%	0%	2,123
JDI	Primary Test for GRP Pipe Line 15	6d	6d	19-Jul-26	25-Jul-26	25-Oct-26	31-Oct-26	392d	1	100%	0%	2,123
JDI	Installing for GRP Pipe Line 150 r	3d	3d	15-Jul-26	18-Jul-26	21-Oct-26	24-Oct-26	392d	1	100%	0%	11,677
JDI	Bedding Works for GRP Pipe Line	3d	3d	12-Jul-26	14-Jul-26	18-Oct-26	20-Oct-26	392d	1	100%	0%	1,062
JDI	Excavation Works for GRP Pipe L	2d	2d	09-Jul-26	11-Jul-26	15-Oct-26	17-Oct-26	392d	1	100%	0%	4,246
JDH3-02-009-AMCA-(SW)-GRP Pipes-20(		6d	6d	04-Aug-26	10-Aug-26	29-Sep-26	05-Oct-26	420d	1	100%	0%	8,738
JDI	Primary Test for GRP Pipe Line 20	6d	6d	04-Aug-26	10-Aug-26	29-Sep-26	05-Oct-26	420d	1	100%	0%	8,738
JDH3-02-009-AMCA-(SW)-GRP Pipes-20(		6d	6d	27-Aug-26	02-Sep-26	29-Sep-26	05-Oct-26	420d	1	100%	0%	11,329
JDI	Primary Test for GRP Pipe Line 20	6d	6d	27-Aug-26	02-Sep-26	29-Sep-26	05-Oct-26	420d	1	100%	0%	11,329
JDH3-02-009-AMCA-(SW)-GRP Pipes-20(		6d	6d	19-Sep-26	26-Sep-26	29-Sep-26	05-Oct-26	420d	1	100%	0%	8,831
JDI	Primary Test for GRP Pipe Line 20	6d	6d	19-Sep-26	26-Sep-26	29-Sep-26	05-Oct-26	420d	1	100%	0%	8,831
JDH3-02-009-AMCA-(SW)-MH Works dep		4d	4d	30-Jun-26	04-Jul-26	30-Sep-26	04-Oct-26	433d	2	100%	0%	17,058
JDI	Steel Cover for MH 1200 mm - de	2d	2d	02-Jul-26	04-Jul-26	03-Oct-26	04-Oct-26	433d	1	100%	0%	5,686
JDI	Finishing, Benching, Testing Work	2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	01-Oct-26	433d	1	100%	0%	11,372
JDH3-02-009-AMCA-(SW)-MH Works dep		4d	4d	02-Jul-26	06-Jul-26	03-Oct-26	06-Oct-26	433d	2	100%	0%	7,316
JDI	Steel Cover for MH 1200 mm - de	2d	2d	05-Jul-26	06-Jul-26	05-Oct-26	06-Oct-26	433d	1	100%	0%	2,439
JDI	Finishing, Benching, Testing Work	2d	2d	02-Jul-26	04-Jul-26	03-Oct-26	04-Oct-26	433d	1	100%	0%	4,877
JDH3-02-009-AMCA-(SW)-MH Works dep		4d	4d	27-Jul-26	30-Jul-26	05-Oct-26	08-Oct-26	433d	2	100%	0%	5,027
JDI	Steel Coverfor MH 1200 mm - dep	2d	2d	29-Jul-26	30-Jul-26	07-Oct-26	08-Oct-26	433d	1	100%	0%	1,676
JDI	Finishing, Benching, Testing Work	2d	2d	27-Jul-26	28-Jul-26	05-Oct-26	06-Oct-26	433d	1	100%	0%	3,351
JDH3-02-009-AMCA-(SW)-MH Works dep		4d	4d	29-Jul-26	02-Aug-26	07-Oct-26	11-Oct-26	433d	2	100%	0%	5,518
JDI	Steel Cover for MH 1200 mm - de	2d	2d	01-Aug-26	02-Aug-26	10-Oct-26	11-Oct-26	433d	1	100%	0%	1,839
JDI	Finishing, Benching, Testing Work	2d	2d	29-Jul-26	30-Jul-26	07-Oct-26	08-Oct-26	433d	1	100%	0%	3,679
JDH3-02-009-AMCA-Storm Network- ST		12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	404d	10	100%	0%	59,914
JDH3-02-009-AMCA-(ST)-MH Works (120		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	404d	2	100%	0%	1,358
JDI	Steel Coverfor MH 1200 mm - dep	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	404d	1	100%	0%	485
JDI	Finishing, Benching, Testing Work	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	404d	1	100%	0%	873
JDH3-02-009-AMCA-(ST)-MH Works (150		4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	404d	2	100%	0%	5,129
JDI	Steel Coverfor MH 1500 mm - dep	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	404d	1	100%	0%	1,751
JDI	Finishing, Benching, Testing Work	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	404d	1	100%	0%	3,377
JDH3-02-009-AMCA-(ST)-MH Works (200		4d	4d	28-Jun-26	01-Jul-26	04-Oct-26	07-Oct-26	404d	2	100%	0%	12,088
JDI	Steel Coverfor MH 2000 mm - dep	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	404d	1	100%	0%	4,089
JDI	Finishing, Benching, Testing Work	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	404d	1	100%	0%	8,000
JDH3-02-009-AMCA-(ST)-MH Works (200		4d	4d	30-Jun-26	04-Jul-26	06-Oct-26	10-Oct-26	404d	2	100%	0%	30,723
JDI	Steel Coverfor MH 2000 mm - dep	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	404d	1	100%	0%	10,241
JDI	Finishing, Benching, Testing Work	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	404d	1	100%	0%	20,482
JDH3-02-009-AMCA-(ST)-MH Works (200		4d	4d	02-Jul-26	06-Jul-26	08-Oct-26	12-Oct-26	404d	2	100%	0%	10,617
JDI	Steel Coverfor MH 2000 mm - dep	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	404d	1	100%	0%	3,539

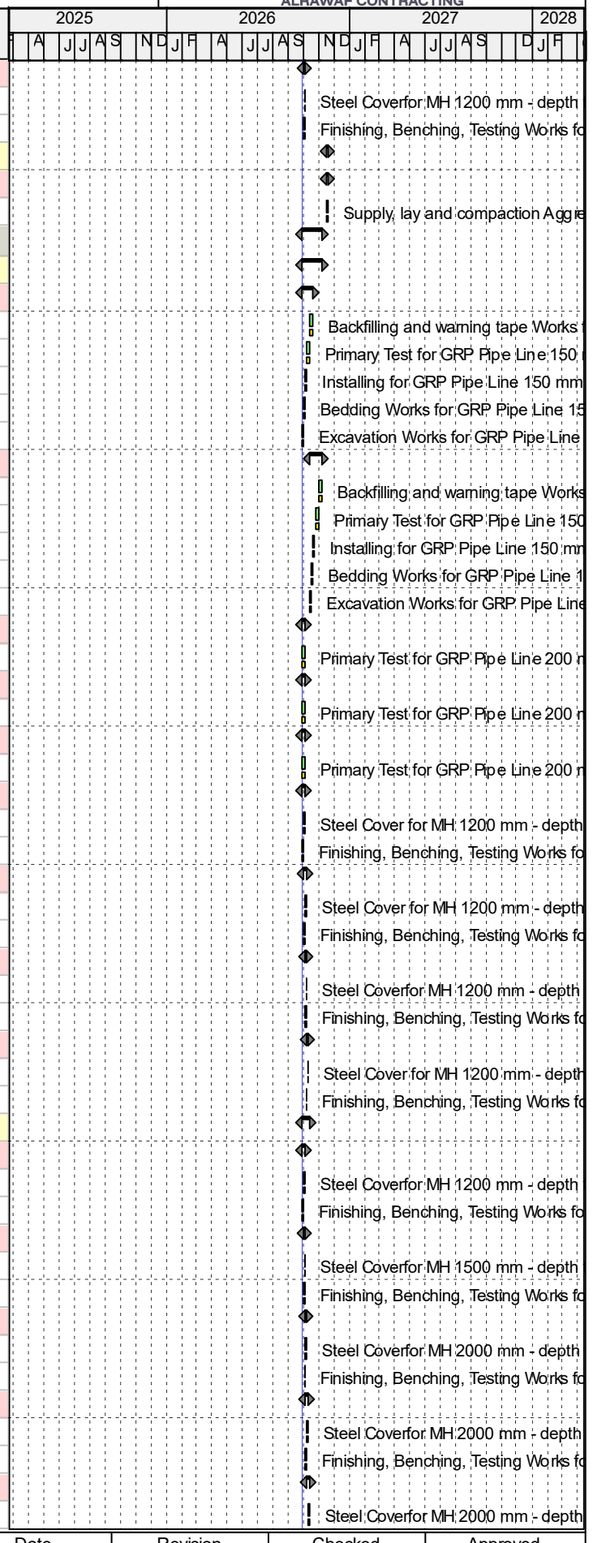


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDI	Finishing, Benching, Testing Work	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	404d	1	100%	0%	7,078
JDH3-02-009-AMCA-Potable Water Network-		25d	25d	23-Jun-26	22-Aug-26	29-Sep-26	27-Oct-26	419d	19	100%	0%	383,110
(WT)-HDPE Pipes-160 mm diameter dept		12d	12d	25-Jul-26	06-Aug-26	29-Sep-26	12-Oct-26	432d	5	100%	0%	5,004
JDI	Backfilling and warning tape Work	2d	2d	05-Aug-26	06-Aug-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	500
JDI	Primary Test for HDPE Pipe Line	2d	2d	03-Aug-26	04-Aug-26	08-Oct-26	10-Oct-26	419d	1	100%	0%	500
JDI	Installing for HDPE Pipe Line 160	4d	4d	29-Jul-26	02-Aug-26	04-Oct-26	07-Oct-26	419d	1	100%	0%	2,752
JDI	Bedding Works for HDPE Pipe Lir	2d	2d	27-Jul-26	28-Jul-26	01-Oct-26	03-Oct-26	419d	1	100%	0%	250
JDI	Excavation Works for HDPE Pipe	2d	2d	25-Jul-26	26-Jul-26	29-Sep-26	30-Sep-26	419d	1	100%	0%	1,001
(WT)-HDPE Pipes-225 mm diameter dept		12d	12d	05-Aug-26	18-Aug-26	11-Oct-26	24-Oct-26	422d	5	100%	0%	236,994
JDI	Backfilling and warning tape Work	2d	2d	17-Aug-26	18-Aug-26	22-Oct-26	24-Oct-26	422d	1	100%	0%	23,699
JDI	Primary Test for HDPE Pipe Line 2	2d	2d	15-Aug-26	16-Aug-26	20-Oct-26	21-Oct-26	422d	1	100%	0%	23,699
JDI	Installing for HDPE Pipe Line 225	4d	4d	10-Aug-26	13-Aug-26	15-Oct-26	19-Oct-26	422d	1	100%	0%	130,347
JDI	Bedding Works for HDPE Pipe Lir	2d	2d	08-Aug-26	09-Aug-26	13-Oct-26	14-Oct-26	422d	1	100%	0%	11,850
JDI	Excavation Works for HDPE Pipe	2d	2d	05-Aug-26	06-Aug-26	11-Oct-26	12-Oct-26	422d	1	100%	0%	47,399
(WT)-Gate Valve-150 mm on pipe dia (16		4d	4d	05-Aug-26	09-Aug-26	11-Oct-26	14-Oct-26	419d	2	100%	0%	3,453
JDI	Stem & Surface box for Gate Valv	2d	2d	08-Aug-26	09-Aug-26	13-Oct-26	14-Oct-26	419d	1	100%	0%	345
JDI	Installation for Gate Valve 150 mr	2d	2d	05-Aug-26	06-Aug-26	11-Oct-26	12-Oct-26	419d	1	100%	0%	3,108
(WT)-Gate Valve-200 mm on pipe dia (22		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	10,638
JDI	Stem & Surface box for Gate Valv	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,064
JDI	Installation for Gate Valve 200 mr	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	9,574
(WT)-Fire Hydrant		11d	11d	10-Aug-26	22-Aug-26	15-Oct-26	27-Oct-26	419d	5	100%	0%	127,021
JDI	Protection Barriers for Fire Hydrar	2d	2d	20-Aug-26	22-Aug-26	26-Oct-26	27-Oct-26	419d	1	100%	0%	6,351
JDI	Fire Installation for Fire Hydrant- (	2d	2d	18-Aug-26	19-Aug-26	24-Oct-26	25-Oct-26	419d	1	100%	0%	44,457
JDI	Stem for Fire Hydrant- (B3.33 14	2d	2d	16-Aug-26	17-Aug-26	21-Oct-26	22-Oct-26	419d	1	100%	0%	38,106
JDI	Valve Installation for Fire Hydrant-	3d	3d	12-Aug-26	15-Aug-26	18-Oct-26	20-Oct-26	419d	1	100%	0%	25,404
JDI	Excavation and Bedding and Pipe	2d	2d	10-Aug-26	11-Aug-26	15-Oct-26	17-Oct-26	419d	1	100%	0%	12,702
JDH3-02-009-AMCA-TSE Network - TSE		22d	22d	23-Jun-26	18-Jul-26	29-Sep-26	24-Oct-26	422d	14	100%	0%	209,632
JDH3-02-009-AMCA-(TSE)-HDPE Pipes-1		22d	22d	23-Jun-26	18-Jul-26	29-Sep-26	24-Oct-26	422d	5	100%	0%	10,898
JDI	Backfilling and warning tape Work	4d	4d	14-Jul-26	18-Jul-26	20-Oct-26	24-Oct-26	422d	1	100%	0%	1,090
JDI	Primary Test for HDPE Pipe Line	4d	4d	09-Jul-26	13-Jul-26	15-Oct-26	19-Oct-26	422d	1	100%	0%	1,090
JDI	Installing for HDPE Pipe Line 110	8d	8d	30-Jun-26	08-Jul-26	06-Oct-26	14-Oct-26	422d	1	100%	0%	5,994
JDI	Bedding Works for HDPE Pipe Lir	3d	3d	27-Jun-26	29-Jun-26	03-Oct-26	05-Oct-26	422d	1	100%	0%	545
JDI	Excavation Works for HDPE Pipe	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	422d	1	100%	0%	2,180
JDH3-02-009-AMCA-(TSE)-HDPE Pipes-1		10d	10d	29-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	434d	5	100%	0%	174,460
JDI	Backfilling and warning tape Work	2d	2d	08-Jul-26	09-Jul-26	08-Oct-26	10-Oct-26	434d	1	100%	0%	17,446
JDI	Primary Test for HDPE Pipe Line	2d	2d	06-Jul-26	07-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	17,446
JDI	Installing for HDPE Pipe Line 160	2d	2d	04-Jul-26	05-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	95,953
JDI	Bedding Works for HDPE Pipe Lir	2d	2d	01-Jul-26	02-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	8,723
JDI	Excavation Works for HDPE Pipe	2d	2d	29-Jun-26	30-Jun-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	34,892
JDH3-02-009-AMCA-(TSE)-Gate Valve-10		4d	4d	09-Jul-26	13-Jul-26	15-Oct-26	19-Oct-26	424d	2	100%	0%	10,147
JDI	Stem & Surface box for Gate Valv	2d	2d	12-Jul-26	13-Jul-26	18-Oct-26	19-Oct-26	424d	1	100%	0%	1,015
JDI	Installation for Gate Valve 100 mr	2d	2d	09-Jul-26	11-Jul-26	15-Oct-26	17-Oct-26	424d	1	100%	0%	9,132
JDH3-02-009-AMCA-(TSE)-Gate Valve-15		4d	4d	12-Jul-26	15-Jul-26	18-Oct-26	21-Oct-26	424d	2	100%	0%	14,128
JDI	Stem & Surface box for Gate Valv	2d	2d	14-Jul-26	15-Jul-26	20-Oct-26	21-Oct-26	424d	1	100%	0%	1,413
JDI	Installation for Gate Valve 150 mr	2d	2d	12-Jul-26	13-Jul-26	18-Oct-26	19-Oct-26	424d	1	100%	0%	12,715
D-MCA		45d	45d	23-Jun-26	29-Sep-26	29-Sep-26	19-Nov-26	399d	5	99.68%	0%	91,982
JDH3-02-009-DMCA-Storm Network- ST		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	1,112
JDH3-02-009-DMCA-(ST)-MH Works (120		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	1,112
JDI	Steel Coverfor MH 1200 mm - dep	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	397
JDI	Finishing, Benching, Testing Work	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	715
JDH3-02-009-DMCA-Road Works - RD		25d	25d	31-Aug-26	29-Sep-26	22-Oct-26	19-Nov-26	362d	3	99.67%	0%	90,870
JDH3-02-009-DMCA-(RD)-Precast Concre		25d	25d	31-Aug-26	29-Sep-26	22-Oct-26	19-Nov-26	362d	3	99.67%	0%	90,870
JDI	Supply and installation Depressed	3d	3d	27-Sep-26	29-Sep-26	17-Nov-26	19-Nov-26	362d	1	66.67%	0%	896

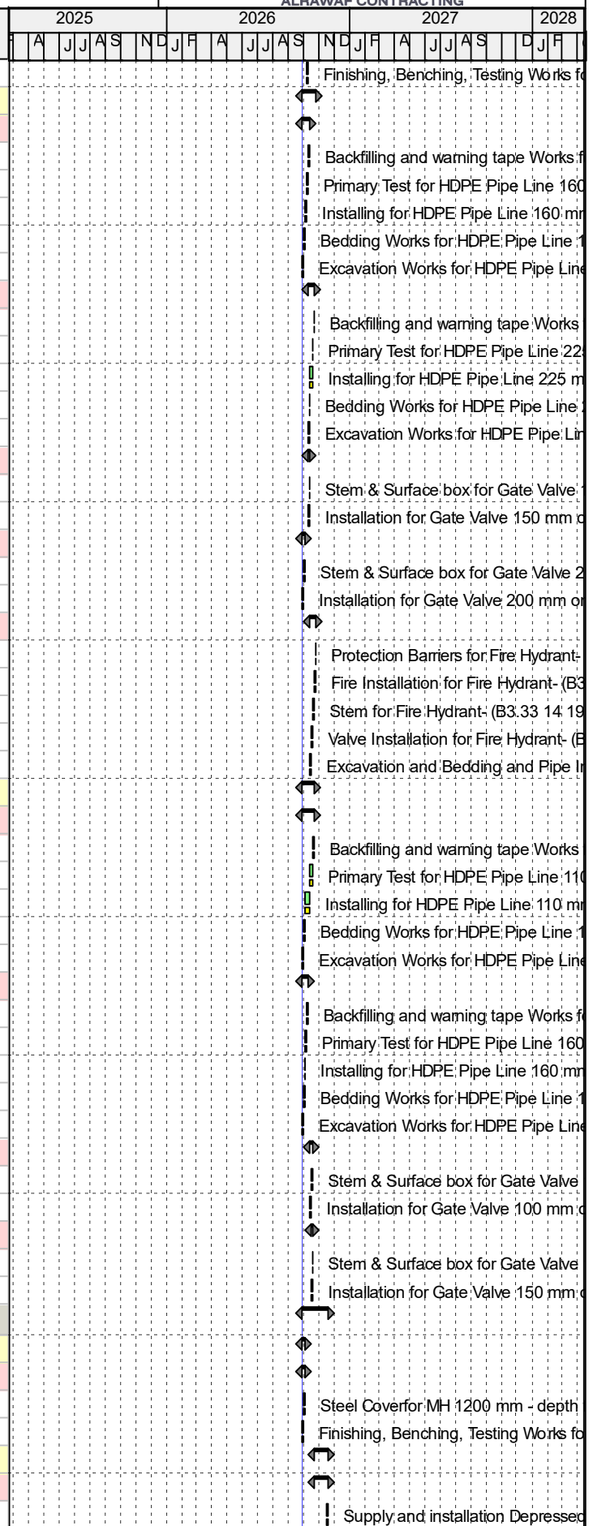


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDH	Supply and installation Precast C	12d	12d	12-Sep-26	26-Sep-26	03-Nov-26	16-Nov-26	314d	1	100%	0%	21,189
JDH	Supply and installation Precast C	10d	10d	31-Aug-26	10-Sep-26	22-Oct-26	02-Nov-26	314d	1	100%	0%	68,785
D-MCE		44d	44d	23-Jun-26	28-Sep-26	29-Sep-26	18-Nov-26	400d	11	100%	0%	523,109
JDH3-02-009-DMCE-Storm Network - ST		6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	438d	4	100%	0%	19,366
JDH3-02-009-DMCE-(ST)-MH Works (200		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	438d	2	100%	0%	12,088
JDH	Steel Coverfor MH 2000 mm - de	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	4,089
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	8,000
JDH3-02-009-DMCE-(ST)-MH Works (150		4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	438d	2	100%	0%	7,278
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	2,426
JDH	Finishing, Benching, Testing Worl	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	4,852
JDH3-02-009-DMCE-Road Works - RD		44d	44d	08-Aug-26	28-Sep-26	29-Sep-26	18-Nov-26	388d	7	100%	0%	503,743
JDH3-02-009-DMCE-(RD)-Bituminous cor		4d	4d	24-Sep-26	28-Sep-26	15-Nov-26	18-Nov-26	367d	1	100%	0%	264,872
JDH	Supply, lay and compaction Asph	4d	4d	24-Sep-26	28-Sep-26	15-Nov-26	18-Nov-26	367d	1	100%	0%	264,872
JDH3-02-009-DMCE-(RD)-Precast Concre		24d	24d	08-Aug-26	03-Sep-26	29-Sep-26	26-Oct-26	367d	3	100%	0%	90,870
JDH	Supply and installation Depresse	4d	4d	31-Aug-26	03-Sep-26	22-Oct-26	26-Oct-26	367d	1	100%	0%	896
JDH	Supply and installation Precast C	12d	12d	17-Aug-26	30-Aug-26	08-Oct-26	21-Oct-26	314d	1	100%	0%	21,189
JDH	Supply and installation Precast C	8d	8d	08-Aug-26	16-Aug-26	29-Sep-26	07-Oct-26	314d	1	100%	0%	68,785
JDH3-02-009-DMCE-(RD)-Precast Interlo		16d	16d	05-Sep-26	22-Sep-26	27-Oct-26	14-Nov-26	367d	1	100%	0%	146,259
JDH	Interlocking block pavers for sidev	16d	16d	05-Sep-26	22-Sep-26	27-Oct-26	14-Nov-26	367d	1	100%	0%	146,259
JDH3-02-009-DMCE-(RD)-Pavement Mark		4d	4d	24-Sep-26	28-Sep-26	15-Nov-26	18-Nov-26	388d	2	100%	0%	1,742
JDH	Thermoplastic continuous 200 mr	2d	2d	27-Sep-26	28-Sep-26	17-Nov-26	18-Nov-26	388d	1	100%	0%	1,146
JDH	Thermoplastic continuous 120 m	2d	2d	24-Sep-26	26-Sep-26	15-Nov-26	16-Nov-26	388d	1	100%	0%	596
C-MCA		8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	6	100%	0%	9,418
JDH3-02-009-CMCA-Storm Network- ST		8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	6	100%	0%	9,418
JDH3-02-009-CMCA-(ST)-MH Works (120		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	436d	2	100%	0%	5,298
JDH	Steel Coverfor MH 1200 mm - de	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	1,792
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	3,506
JDH3-02-009-CMCA-(ST)-MH Works (120		6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	436d	2	100%	0%	1,112
JDH	Steel Coverfor MH 1200 mm - de	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	397
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	715
JDH3-02-009-CMCA-(ST)-MH Works (150		8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	2	100%	0%	3,009
JDH	Steel Coverfor MH 1500 mm - de	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	1,003
JDH	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,006
C-MCB		27d	27d	30-Aug-26	30-Sep-26	29-Sep-26	29-Oct-26	414d	9	98.69%	0%	100,448
JDH3-02-009-CMCB-Storm Network - ST		27d	27d	30-Aug-26	30-Sep-26	29-Sep-26	29-Oct-26	414d	9	98.69%	0%	100,448
JDH3-02-009-CMCB-(ST)-GRP Pipes-400		15d	15d	30-Aug-26	15-Sep-26	29-Sep-26	15-Oct-26	414d	5	100%	0%	82,666
JDH	Backfilling and warning tape Worl	3d	3d	13-Sep-26	15-Sep-26	13-Oct-26	15-Oct-26	414d	1	100%	0%	8,267
JDH	Primary Test for GRP Pipe Line 4(	3d	3d	09-Sep-26	12-Sep-26	10-Oct-26	12-Oct-26	414d	1	100%	0%	8,267
JDH	Installing for GRP Pipe Line 400 r	3d	3d	06-Sep-26	08-Sep-26	06-Oct-26	08-Oct-26	414d	1	100%	0%	45,466
JDH	Bedding Works for GRP Pipe Line	3d	3d	02-Sep-26	05-Sep-26	03-Oct-26	05-Oct-26	414d	1	100%	0%	4,133
JDH	Excavation Works for GRP Pipe L	3d	3d	30-Aug-26	01-Sep-26	29-Sep-26	01-Oct-26	414d	1	100%	0%	16,533
JDH3-02-009-CMCB-(ST)-GRP Pipes-500		12d	12d	16-Sep-26	30-Sep-26	17-Oct-26	29-Oct-26	414d	4	92.59%	0%	17,782
JDH	Primary Test for GRP Pipe Line 5(	3d	3d	28-Sep-26	30-Sep-26	27-Oct-26	29-Oct-26	414d	1	33.33%	0%	1,976
JDH	Installing for GRP Pipe Line 500 r	3d	3d	24-Sep-26	27-Sep-26	24-Oct-26	26-Oct-26	414d	1	100%	0%	10,867
JDH	Bedding Works for GRP Pipe Line	3d	3d	20-Sep-26	22-Sep-26	20-Oct-26	22-Oct-26	414d	1	100%	0%	988
JDH	Excavation Works for GRP Pipe L	3d	3d	16-Sep-26	19-Sep-26	17-Oct-26	19-Oct-26	414d	1	100%	0%	3,952
JDH3-02-009-Infrastructure Networks		122d	122d	23-Jun-26	13-Oct-26	29-Sep-26	17-Feb-27	322d	1175	97.65%	0%	27,026,918
JDH3-02-009-Milestone		0d	0d	02-Sep-26	02-Sep-26	14-Oct-26	14-Oct-26	430d	1	0%	0%	0
Zones Millestones		0d	0d	02-Sep-26	02-Sep-26	14-Oct-26	14-Oct-26	430d	1	0%	0%	0
JDH3(	Finish EX	0d	0d		02-Sep-26		14-Oct-26	430d	1	100%	0%	0
JDH3-02-009-Engineering - EN		2d	2d	23-Jun-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	0%	0%	0
JDH3-02-009-Prequalification and Material		2d	2d	23-Jun-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	0%	0%	0

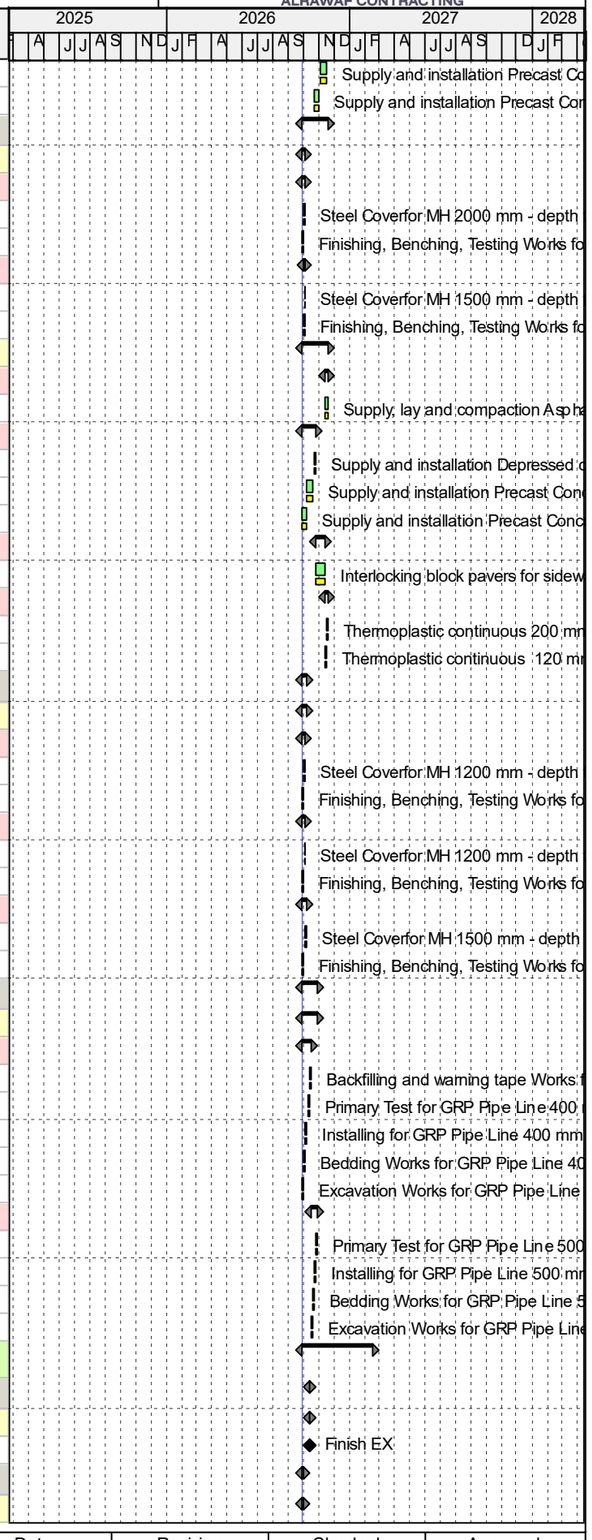

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-Submittals of Material and	2d	2d	23-Jun-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	0%	0%	0
	JDH3-02-009-Submittals of Material a	2d	2d	23-Jun-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	0%	0%	0
	Prepare Material Submittal for Lar	2d	2d	23-Jun-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	0
	JDH3-02-009-Procurement- PR	102d	102d	23-Jun-26	22-Aug-26	29-Sep-26	08-Jan-27	430d	5	100%	0%	1,903,933
	Long Lead Items	10d	10d	23-Jun-26	11-Aug-26	29-Sep-26	08-Oct-26	522d	4	100%	0%	369,797
	JDH3-02-009-Material Delivery and stagi	10d	10d	23-Jun-26	11-Aug-26	29-Sep-26	08-Oct-26	522d	4	100%	0%	369,797
	JDH3-02-009-Material Delivery and st	10d	10d	23-Jun-26	11-Aug-26	29-Sep-26	08-Oct-26	265d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and	10d	10d	23-Jun-26	11-Aug-26	29-Sep-26	08-Oct-26	265d	1	100%	0%	92,449
	delivery and staging for Lighting F	10d	10d	23-Jun-26	11-Aug-26	29-Sep-26	08-Oct-26	265d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and st	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	404d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	404d	1	100%	0%	92,449
	delivery and staging for Lighting F	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	404d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and st	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	466d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	466d	1	100%	0%	92,449
	delivery and staging for Lighting F	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	466d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and st	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	522d	1	100%	0%	92,449
	JDH3-02-009-Material Delivery and	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	522d	1	100%	0%	92,449
	delivery and staging for Lighting F	10d	10d	23-Jun-26	12-Jul-26	29-Sep-26	08-Oct-26	522d	1	100%	0%	92,449
	Short Lead items	10d	10d	13-Aug-26	22-Aug-26	30-Dec-26	08-Jan-27	300d	1	100%	0%	1,534,136
	JDH3-02-009-Material Delivery and stagi	10d	10d	13-Aug-26	22-Aug-26	30-Dec-26	08-Jan-27	300d	1	100%	0%	1,534,136
	JDH3-02-009-Material Delivery and st	10d	10d	13-Aug-26	22-Aug-26	30-Dec-26	08-Jan-27	300d	1	100%	0%	1,534,136
	JDH3-02-009-Material Delivery and	10d	10d	13-Aug-26	22-Aug-26	30-Dec-26	08-Jan-27	300d	1	100%	0%	1,534,136
	delivery and staging for Landscap	10d	10d	13-Aug-26	22-Aug-26	30-Dec-26	08-Jan-27	300d	1	100%	0%	1,534,136
	JDH3-02-009-Execution	122d	122d	23-Jun-26	13-Oct-26	29-Sep-26	17-Feb-27	322d	1158	97.47%	0%	25,122,985
	JDH3-02-009-XX-Execution	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	2	100%	0%	11,854
	Z2	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	8,413
	R102	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	8,413
	JDH3-02-009-XX-R102-Potable Wa	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	8,413
	JDH3-02-009-XX-R102-(WT)-HDF	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	8,413
	Primary Test for HDPE Pipe Line	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	8,413
	Z3	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	3,442
	R103	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	3,442
	JDH3-02-009-XX-R103-Potable Wa	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	3,442
	JDH3-02-009-XX-R103-(WT)-HDF	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	3,442
	Primary Test for HDPE Pipe Line	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	3,442
	Pond - PS	94d	94d	23-Jun-26	11-Oct-26	29-Sep-26	16-Jan-27	350d	13	95.31%	0%	634,059
	JDH3-02-009-ST1-Pond 6 - ST	31d	31d	23-Jun-26	28-Jul-26	29-Sep-26	03-Nov-26	285d	7	100%	0%	152,496
	JDH3-02-009-PN6-Landscape Works	31d	31d	23-Jun-26	28-Jul-26	29-Sep-26	03-Nov-26	285d	7	100%	0%	152,496
	JDH3-02-009-PN6-(LS)-Trees	26d	26d	23-Jun-26	22-Jul-26	29-Sep-26	28-Oct-26	285d	6	100%	0%	151,675
	Ref. FIC REL (Ficus Religiosa) - (E	4d	4d	28-Jun-26	01-Jul-26	04-Oct-26	07-Oct-26	285d	1	100%	0%	28,890
	Ref. DEL REG (Delonix Regia) - (I	6d	6d	02-Jul-26	08-Jul-26	08-Oct-26	14-Oct-26	285d	1	100%	0%	30,204
	Ref. DAL SIS (Dalbergia Sissoo) -	7d	7d	15-Jul-26	22-Jul-26	21-Oct-26	28-Oct-26	285d	1	100%	0%	30,204
	Ref. COR SEB (Cordia Sebestena	5d	5d	09-Jul-26	14-Jul-26	15-Oct-26	20-Oct-26	285d	1	100%	0%	32,502
	Ref. AZA INC (Azadirachta Indica	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	293d	1	100%	0%	9,192
	Ref. ACA AMP (Acacia Ampliceps	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	285d	1	100%	0%	20,683
	JDH3-02-009-PN6-(LS)-Design, Del	5d	5d	23-Jul-26	28-Jul-26	29-Oct-26	03-Nov-26	285d	1	100%	0%	822
	Online pressure compensating er	5d	5d	23-Jul-26	28-Jul-26	29-Oct-26	03-Nov-26	285d	1	100%	0%	822
	JDH3-02-009-ST1-Pond 9 - ST	63d	63d	29-Jul-26	11-Oct-26	04-Nov-26	16-Jan-27	285d	5	84.57%	0%	190,713
	JDH3-02-009-PN9-Landscape Works	63d	63d	29-Jul-26	11-Oct-26	04-Nov-26	16-Jan-27	285d	5	84.57%	0%	190,713
	JDH3-02-009-PN9-(LS)-HDPE for S	63d	63d	29-Jul-26	11-Oct-26	04-Nov-26	16-Jan-27	285d	5	84.57%	0%	190,713
	Pipe linefor Diam 32 mm PN10 -	14d	14d	19-Aug-26	03-Sep-26	25-Nov-26	10-Dec-26	285d	1	100%	0%	64,445
	Pipe linefor Diam 50 mm PN10 -	14d	14d	03-Aug-26	18-Aug-26	09-Nov-26	24-Nov-26	285d	1	100%	0%	56,421

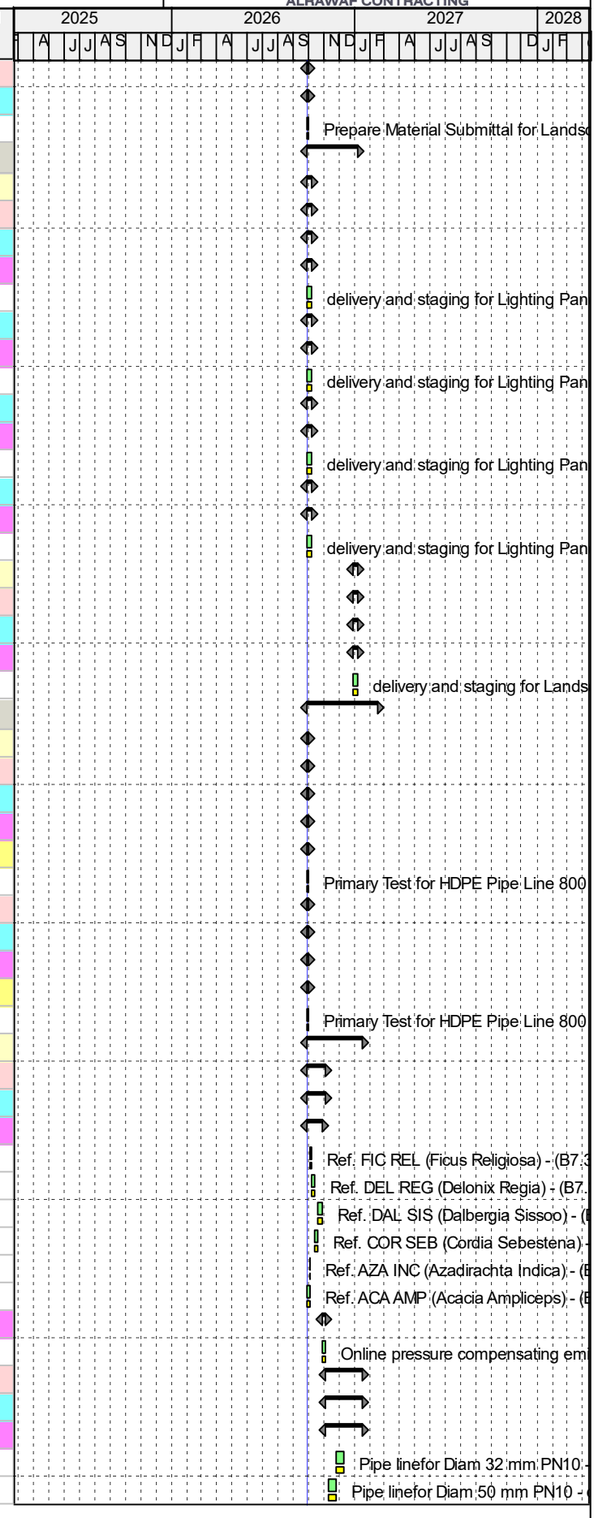

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Pipe linefor Diam 63 mm PN10 -	16d	16d	22-Sep-26	11-Oct-26	29-Dec-26	16-Jan-27	285d	1	31.25%	0%	42,806
	Pipe linefor Diam 75 mm PN10 -	15d	15d	05-Sep-26	21-Sep-26	12-Dec-26	28-Dec-26	285d	1	100%	0%	21,736
	Pipe line with Diam 90 mm PN10	4d	4d	29-Jul-26	02-Aug-26	04-Nov-26	08-Nov-26	285d	1	100%	0%	5,305
JDH3-02-009-ST1-Pond 4 - ST		3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	290,850
JDH3-02-009-BW-Backfilling Works		3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	290,850
	Backfill Layers Works Imported M	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	290,850
Earthworks - EW		15d	15d	16-Aug-26	01-Sep-26	05-Dec-26	21-Dec-26	295d	1	100%	0%	714,729
JDH3-02-009-R01-Road Works - RW		15d	15d	16-Aug-26	01-Sep-26	05-Dec-26	21-Dec-26	295d	1	100%	0%	714,729
Z2		15d	15d	16-Aug-26	01-Sep-26	05-Dec-26	21-Dec-26	295d	1	100%	0%	714,729
JDH3-02-009-Road Works - RWZ2-		15d	15d	16-Aug-26	01-Sep-26	05-Dec-26	21-Dec-26	295d	1	100%	0%	714,729
	Backfill Layers with Imported Mat	15d	15d	16-Aug-26	01-Sep-26	05-Dec-26	21-Dec-26	295d	1	100%	0%	714,729
Z3		64d	64d	23-Jun-26	08-Oct-26	29-Sep-26	12-Dec-26	381d	169	97.03%	0%	3,782,292
R152		33d	33d	28-Jun-26	01-Oct-26	29-Sep-26	05-Nov-26	411d	10	86.15%	0%	423,173
JDH3-02-009-R152-Potable Water Net		2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,862
JDH3-02-009-R152-(WT)-Fire Hydra		2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,862
	Protection Barriers for Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,862
JDH3-02-009-R152-Street Lighting Ne		26d	26d	21-Jul-26	18-Aug-26	29-Sep-26	28-Oct-26	418d	6	100%	0%	56,664
JDH3-02-009-R152-(SL)- LV Cables		16d	16d	21-Jul-26	08-Aug-26	08-Oct-26	26-Oct-26	418d	4	100%	0%	51,873
	Backfilling, Warning Tape Works f	4d	4d	04-Aug-26	08-Aug-26	22-Oct-26	26-Oct-26	418d	1	100%	0%	5,187
	Testing and Commissioning for L	4d	4d	30-Jul-26	03-Aug-26	18-Oct-26	21-Oct-26	418d	1	100%	0%	2,594
	Bedding Layer and Installation fo	4d	4d	26-Jul-26	29-Jul-26	13-Oct-26	17-Oct-26	418d	1	100%	0%	38,905
	Excavation Works for LV Cables	4d	4d	21-Jul-26	25-Jul-26	08-Oct-26	12-Oct-26	418d	1	100%	0%	5,187
JDH3-02-009-R152-(SL)-Lighting P		5d	5d	09-Aug-26	13-Aug-26	29-Sep-26	04-Oct-26	433d	1	100%	0%	3,940
	Cable Connection for Lighting Po	5d	5d	09-Aug-26	13-Aug-26	29-Sep-26	04-Oct-26	433d	1	100%	0%	3,940
JDH3-02-009-R152-(SL)-Earthing S		2d	2d	17-Aug-26	18-Aug-26	27-Oct-26	28-Oct-26	418d	1	100%	0%	852
	Supply, construct, connect and te	2d	2d	17-Aug-26	18-Aug-26	27-Oct-26	28-Oct-26	418d	1	100%	0%	852
JDH3-02-009-R152-Road Works - RD		29d	29d	29-Aug-26	01-Oct-26	04-Oct-26	05-Nov-26	360d	3	83.75%	0%	360,646
JDH3-02-009-R152-(RD)-Precast C		16d	16d	29-Aug-26	15-Sep-26	04-Oct-26	21-Oct-26	360d	2	100%	0%	106,762
	Supply and installation Depressec	11d	11d	03-Sep-26	15-Sep-26	10-Oct-26	21-Oct-26	360d	1	100%	0%	69,333
	Supply and installation Precast C	5d	5d	29-Aug-26	02-Sep-26	04-Oct-26	08-Oct-26	360d	1	100%	0%	37,429
JDH3-02-009-R152-(RD)-Precast In		13d	13d	16-Sep-26	01-Oct-26	22-Oct-26	05-Nov-26	360d	1	76.92%	0%	253,884
	Interlocking block pavers for sidev	13d	13d	16-Sep-26	01-Oct-26	22-Oct-26	05-Nov-26	360d	1	76.92%	0%	253,884
R16		46d	46d	01-Jul-26	23-Aug-26	29-Sep-26	21-Nov-26	398d	18	100%	0%	466,576
JDH3-02-009-R16-Potable Water Netw		2d	2d	10-Aug-26	11-Aug-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	2,931
JDH3-02-009-R16-(WT)-Fire Hydrar		2d	2d	10-Aug-26	11-Aug-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	2,931
	Protection Barriers for Fire Hydrar	2d	2d	10-Aug-26	11-Aug-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	2,931
JDH3-02-009-R16-Street Lighting Netv		4d	4d	05-Jul-26	16-Jul-26	29-Sep-26	04-Oct-26	440d	2	100%	0%	3,534
JDH3-02-009-R16-(SL)- LV Cables -		4d	4d	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	440d	1	100%	0%	2,682
	Testing and Commissioning for L	4d	4d	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	440d	1	100%	0%	2,682
JDH3-02-009-R16-(SL)-Earthing Sy		2d	2d	14-Jul-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	852
	Supply, construct, connect and te	2d	2d	14-Jul-26	16-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	852
JDH3-02-009-R16-Road Works - RD		46d	46d	01-Jul-26	23-Aug-26	29-Sep-26	21-Nov-26	132d	15	100%	0%	460,111
JDH3-02-009-R16-(RD)-Bituminous		4d	4d	27-Jul-26	30-Jul-26	25-Oct-26	28-Oct-26	132d	1	100%	0%	268,601
	Supply, lay and compaction Asph	4d	4d	27-Jul-26	30-Jul-26	25-Oct-26	28-Oct-26	132d	1	100%	0%	268,601
JDH3-02-009-R16-(RD)-Precast Cor		10d	10d	01-Jul-26	12-Jul-26	29-Sep-26	10-Oct-26	132d	2	100%	0%	55,210
	Supply and installation Depressec	8d	8d	04-Jul-26	12-Jul-26	01-Oct-26	10-Oct-26	132d	1	100%	0%	50,487
	Supply and installation Precast C	2d	2d	01-Jul-26	02-Jul-26	29-Sep-26	30-Sep-26	132d	1	100%	0%	4,724
JDH3-02-009-R16-(RD)-Precast Inte		12d	12d	13-Jul-26	26-Jul-26	11-Oct-26	24-Oct-26	132d	1	100%	0%	114,218
	Interlocking block pavers for sidev	12d	12d	13-Jul-26	26-Jul-26	11-Oct-26	24-Oct-26	132d	1	100%	0%	114,218
JDH3-02-009-R16-(RD)-Pavement M		20d	20d	01-Aug-26	23-Aug-26	29-Oct-26	21-Nov-26	132d	10	100%	0%	12,501
	Retroreflective Only Right or Only	2d	2d	22-Aug-26	23-Aug-26	19-Nov-26	21-Nov-26	132d	1	100%	0%	572
	Retroreflective Straight Arrow - (B	2d	2d	19-Aug-26	20-Aug-26	17-Nov-26	18-Nov-26	132d	1	100%	0%	572
	Thermoplastic intermittent 120 mi	2d	2d	17-Aug-26	18-Aug-26	15-Nov-26	16-Nov-26	132d	1	100%	0%	1,121

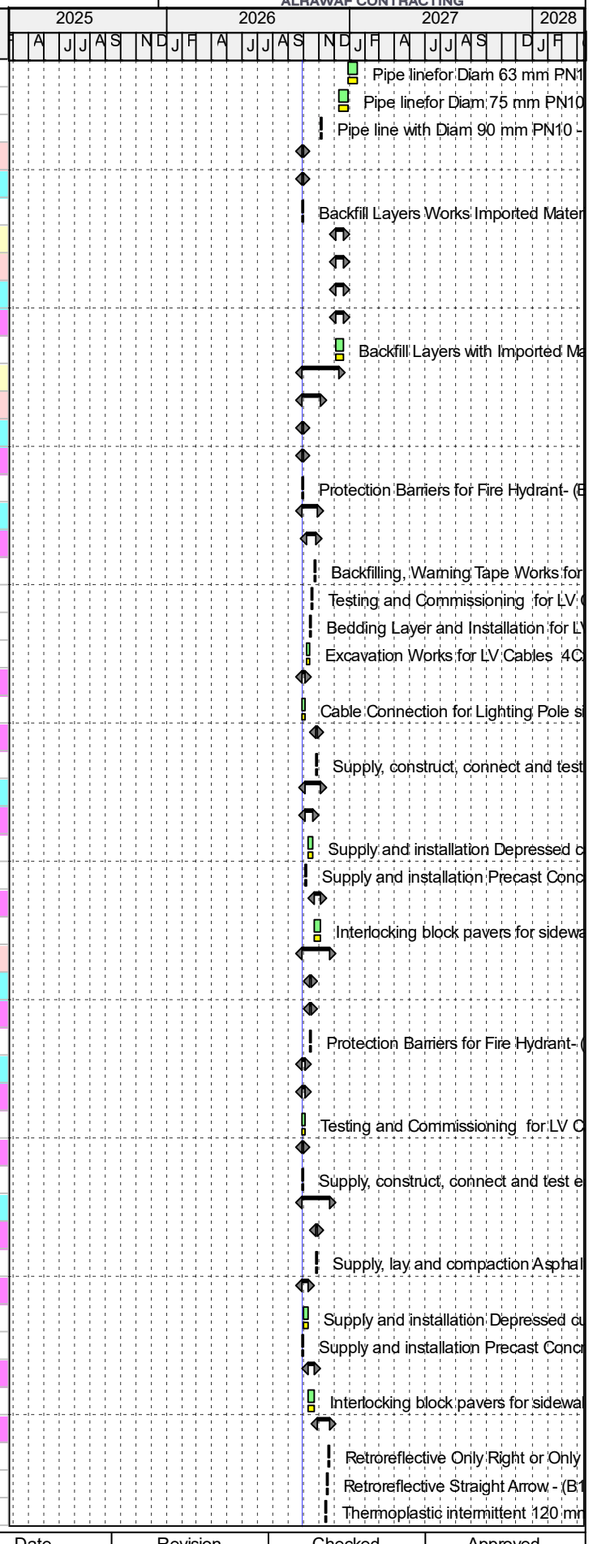


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Thermoplastic intermittent 100 mi	2d	2d	15-Aug-26	16-Aug-26	12-Nov-26	14-Nov-26	132d	1	100%	0%	1,557
	Thermoplastic continuous Retrore	2d	2d	12-Aug-26	13-Aug-26	10-Nov-26	11-Nov-26	132d	1	100%	0%	1,426
	Thermoplastic continuous 100 mi	2d	2d	10-Aug-26	11-Aug-26	08-Nov-26	09-Nov-26	132d	1	100%	0%	1,247
	Thermoplastic continuous 300 mi	2d	2d	08-Aug-26	09-Aug-26	05-Nov-26	07-Nov-26	132d	1	100%	0%	166
	Thermoplastic continuous 200 mi	2d	2d	05-Aug-26	06-Aug-26	03-Nov-26	04-Nov-26	132d	1	100%	0%	1,410
	Thermoplastic continuous 120 mi	2d	2d	03-Aug-26	04-Aug-26	01-Nov-26	02-Nov-26	132d	1	100%	0%	371
	Thermoplastic continuous 120 m	2d	2d	01-Aug-26	02-Aug-26	29-Oct-26	31-Oct-26	132d	1	100%	0%	4,058
	JDH3-02-009-R16-(RD)-Traffic Signa	2d	2d	01-Aug-26	02-Aug-26	29-Oct-26	31-Oct-26	148d	1	100%	0%	9,582
	Supply and installation Traffic sign	2d	2d	01-Aug-26	02-Aug-26	29-Oct-26	31-Oct-26	148d	1	100%	0%	9,582
R17		46d	46d	25-Jun-26	23-Aug-26	29-Sep-26	21-Nov-26	398d	27	100%	0%	558,941
	JDH3-02-009-R17-Potable Water Netw	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	3,908
	JDH3-02-009-R17-(WT)-Fire Hydran	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	3,908
	Protection Barriers for Fire Hydran	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	3,908
	JDH3-02-009-R17-Electrical Network	6d	6d	25-Jun-26	01-Jul-26	29-Sep-26	06-Oct-26	438d	3	100%	0%	68,946
	JDH3-02-009-R17-(EL)-RMU 33 KV	6d	6d	25-Jun-26	01-Jul-26	29-Sep-26	06-Oct-26	438d	3	100%	0%	68,946
	Earthing + Primary Test for RMU 3	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	06-Oct-26	438d	1	100%	0%	4,925
	Cables Connection for RMU 33 K'	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	04-Oct-26	438d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.26	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	438d	1	100%	0%	59,096
	JDH3-02-009-R17-Street Lighting Netv	11d	11d	27-Jun-26	13-Aug-26	29-Sep-26	11-Oct-26	433d	7	100%	0%	20,231
	JDH3-02-009-R17-(SL)- LV Cables -	4d	4d	28-Jun-26	01-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	4,828
	Backfilling, Warning Tape Works f	2d	2d	30-Jun-26	01-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	3,219
	Testing and Commissioning for L	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	1,609
	JDH3-02-009-R17-(SL)- LV Cables -	5d	5d	07-Jul-26	12-Jul-26	29-Sep-26	04-Oct-26	439d	1	100%	0%	3,946
	Testing and Commissioning for L	5d	5d	07-Jul-26	12-Jul-26	29-Sep-26	04-Oct-26	439d	1	100%	0%	3,946
	JDH3-02-009-R17-(SL)-Earthing Sy	2d	2d	27-Jun-26	28-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	27-Jun-26	28-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	1,126
	JDH3-02-009-R17-(SL)- Street Light	11d	11d	01-Jul-26	13-Aug-26	29-Sep-26	11-Oct-26	433d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	12-Aug-26	13-Aug-26	10-Oct-26	11-Oct-26	433d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	04-Jul-26	05-Jul-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	01-Jul-26	02-Jul-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	1,033
	JDH3-02-009-R17-Road Works - RD	46d	46d	01-Jul-26	23-Aug-26	29-Sep-26	21-Nov-26	398d	16	100%	0%	465,856
	JDH3-02-009-R17-(RD)-Bituminous	4d	4d	27-Jul-26	30-Jul-26	25-Oct-26	28-Oct-26	398d	1	100%	0%	268,570
	Supply, lay and compaction Asph	4d	4d	27-Jul-26	30-Jul-26	25-Oct-26	28-Oct-26	398d	1	100%	0%	268,570
	JDH3-02-009-R17-(RD)-Precast Cor	10d	10d	01-Jul-26	12-Jul-26	29-Sep-26	10-Oct-26	398d	2	100%	0%	59,977
	Supply and installation Depressed	8d	8d	04-Jul-26	12-Jul-26	01-Oct-26	10-Oct-26	398d	1	100%	0%	50,487
	Supply and installation Precast C	2d	2d	01-Jul-26	02-Jul-26	29-Sep-26	30-Sep-26	398d	1	100%	0%	9,490
	JDH3-02-009-R17-(RD)-Precast Inte	12d	12d	13-Jul-26	26-Jul-26	11-Oct-26	24-Oct-26	398d	1	100%	0%	114,145
	Interlocking block pavers for sidev	12d	12d	13-Jul-26	26-Jul-26	11-Oct-26	24-Oct-26	398d	1	100%	0%	114,145
	JDH3-02-009-R17-(RD)-Pavement M	20d	20d	01-Aug-26	23-Aug-26	29-Oct-26	21-Nov-26	398d	10	100%	0%	11,948
	Retroreflective Only Right or Only	2d	2d	22-Aug-26	23-Aug-26	19-Nov-26	21-Nov-26	398d	1	100%	0%	572
	Retroreflective Straight Arrow - (B'	2d	2d	19-Aug-26	20-Aug-26	17-Nov-26	18-Nov-26	398d	1	100%	0%	572
	Thermoplastic intermittent 100 mi	2d	2d	17-Aug-26	18-Aug-26	15-Nov-26	16-Nov-26	398d	1	100%	0%	1,493
	Thermoplastic continuous Chevro	2d	2d	15-Aug-26	16-Aug-26	12-Nov-26	14-Nov-26	398d	1	100%	0%	178
	Thermoplastic continuous Retrore	2d	2d	12-Aug-26	13-Aug-26	10-Nov-26	11-Nov-26	398d	1	100%	0%	1,901
	Thermoplastic continuous 100 mi	2d	2d	10-Aug-26	11-Aug-26	08-Nov-26	09-Nov-26	398d	1	100%	0%	1,247
	Thermoplastic continuous 300 mi	2d	2d	08-Aug-26	09-Aug-26	05-Nov-26	07-Nov-26	398d	1	100%	0%	166
	Thermoplastic continuous 200 mi	2d	2d	05-Aug-26	06-Aug-26	03-Nov-26	04-Nov-26	398d	1	100%	0%	1,398
	Thermoplastic continuous 120 mi	2d	2d	03-Aug-26	04-Aug-26	01-Nov-26	02-Nov-26	398d	1	100%	0%	363
	Thermoplastic continuous 120 m	2d	2d	01-Aug-26	02-Aug-26	29-Oct-26	31-Oct-26	398d	1	100%	0%	4,058
	JDH3-02-009-R17-(RD)-Traffic Signa	4d	4d	01-Aug-26	04-Aug-26	29-Oct-26	02-Nov-26	412d	2	100%	0%	11,217
	Supply and installation Traffic sign	2d	2d	03-Aug-26	04-Aug-26	01-Nov-26	02-Nov-26	412d	1	100%	0%	9,582
	Supply and installation Traffic sign	2d	2d	01-Aug-26	02-Aug-26	29-Oct-26	31-Oct-26	412d	1	100%	0%	1,635
R18		26d	26d	23-Jun-26	06-Oct-26	29-Sep-26	29-Oct-26	418d	12	78.04%	0%	207,820

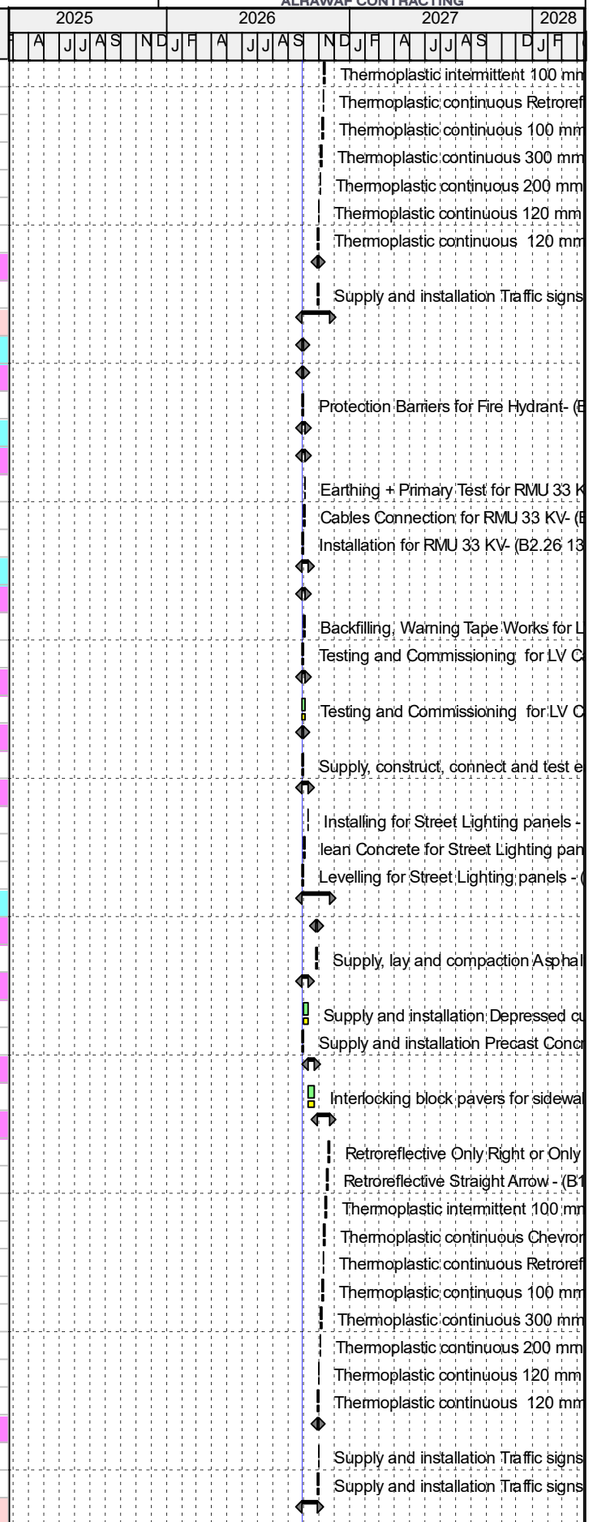


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R18-Potable Water Netw	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R18-(WT)-Fire Hydrar	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	Protection Barriers for Fire Hydrar	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R18-Street Lighting Netv	14d	14d	23-Jun-26	17-Aug-26	29-Sep-26	14-Oct-26	430d	9	100%	0%	116,666
	JDH3-02-009-R18-(SL)- LV Cables -	8d	8d	29-Jun-26	07-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	96,924
	Backfilling, Warning Tape Works f	2d	2d	06-Jul-26	07-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	9,692
	Testing and Commissioning for L	2d	2d	04-Jul-26	05-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	4,846
	Bedding Layer and Installation fo	2d	2d	01-Jul-26	02-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	72,693
	Excavation Works for LV Cables	2d	2d	29-Jun-26	30-Jun-26	29-Sep-26	30-Sep-26	378d	1	100%	0%	9,692
	JDH3-02-009-R18-(SL)- LV Cables -	5d	5d	13-Jul-26	18-Jul-26	01-Oct-26	06-Oct-26	378d	1	100%	0%	3,784
	Testing and Commissioning for L	5d	5d	13-Jul-26	18-Jul-26	01-Oct-26	06-Oct-26	378d	1	100%	0%	3,784
	JDH3-02-009-R18-(SL)-Earthing Sy	3d	3d	15-Aug-26	17-Aug-26	12-Oct-26	14-Oct-26	374d	1	100%	0%	5,628
	Supply, construct, connect and te	3d	3d	15-Aug-26	17-Aug-26	12-Oct-26	14-Oct-26	374d	1	100%	0%	5,628
	JDH3-02-009-R18-(SL)- Street Light	11d	11d	23-Jun-26	13-Aug-26	29-Sep-26	11-Oct-26	374d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	12-Aug-26	13-Aug-26	10-Oct-26	11-Oct-26	374d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	379d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	379d	1	100%	0%	1,033
	JDH3-02-009-R18-Road Works - RD	13d	13d	21-Sep-26	06-Oct-26	14-Oct-26	29-Oct-26	374d	2	47.11%	0%	86,268
	JDH3-02-009-R18-(RD)-Precast Cor	13d	13d	21-Sep-26	06-Oct-26	14-Oct-26	29-Oct-26	374d	2	47.11%	0%	86,268
	Supply and installation Depresse	10d	10d	26-Sep-26	06-Oct-26	18-Oct-26	29-Oct-26	374d	1	30%	0%	65,183
	Supply and installation Precast C	3d	3d	21-Sep-26	24-Sep-26	14-Oct-26	18-Oct-26	374d	1	100%	0%	21,085
R19		64d	64d	23-Jun-26	08-Oct-26	29-Sep-26	12-Dec-26	381d	39	98.88%	0%	725,191
	JDH3-02-009-R19-Potable Water Netw	2d	2d	23-Jun-26	09-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R19-(WT)-Fire Hydrar	2d	2d	23-Jun-26	09-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	Protection Barriers for Fire Hydrar	2d	2d	23-Jun-26	09-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R19-Street Lighting Netv	14d	14d	11-Jul-26	08-Oct-26	29-Sep-26	14-Oct-26	430d	18	90.26%	0%	83,491
	JDH3-02-009-R19-(SL)-Lighting Uni	12d	12d	15-Aug-26	06-Oct-26	01-Oct-26	14-Oct-26	428d	3	96.67%	0%	47,612
	Earthing + Primary Test for Unit su	2d	2d	19-Sep-26	06-Oct-26	13-Oct-26	14-Oct-26	428d	1	53.33%	0%	3,401
	Cables Connection for Unit substa	2d	2d	01-Sep-26	17-Sep-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	3,401
	Installation for Unit substation 33/	2d	2d	15-Aug-26	31-Aug-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	40,810
	JDH3-02-009-R19-(SL)- LV Cables -	12d	12d	11-Jul-26	17-Sep-26	29-Sep-26	12-Oct-26	428d	4	100%	0%	14,828
	Backfilling, Warning Tape Works f	2d	2d	01-Sep-26	17-Sep-26	11-Oct-26	12-Oct-26	428d	1	100%	0%	1,483
	Testing and Commissioning for L	2d	2d	15-Aug-26	31-Aug-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	741
	Bedding Layer and Installation fo	2d	2d	28-Jul-26	13-Aug-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	11,121
	Excavation Works for LV Cables	2d	2d	11-Jul-26	27-Jul-26	29-Sep-26	30-Sep-26	426d	1	100%	0%	1,483
	JDH3-02-009-R19-(SL)- LV Cables -	2d	2d	01-Sep-26	17-Sep-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	1,520
	Installation for LV Cables 3x1Cx5	2d	2d	01-Sep-26	17-Sep-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	1,520
	JDH3-02-009-R19-(SL)- LV Cables -	4d	4d	28-Jul-26	13-Aug-26	29-Sep-26	03-Oct-26	440d	1	100%	0%	2,477
	Testing and Commissioning for L	4d	4d	28-Jul-26	13-Aug-26	29-Sep-26	03-Oct-26	440d	1	100%	0%	2,477
	JDH3-02-009-R19-(SL)- Street Light	9d	9d	17-Aug-26	08-Oct-26	01-Oct-26	11-Oct-26	423d	3	58%	0%	10,331
	Installing for Street Lighting pane	2d	2d	21-Sep-26	08-Oct-26	10-Oct-26	11-Oct-26	423d	1	40%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	03-Sep-26	20-Sep-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	17-Aug-26	02-Sep-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	1,033
	JDH3-02-009-R19-(SL)- LV Distribut	4d	4d	03-Sep-26	08-Oct-26	04-Oct-26	07-Oct-26	426d	2	60%	0%	5,511
	lean Concrete for Street Lighting	2d	2d	21-Sep-26	08-Oct-26	06-Oct-26	07-Oct-26	426d	1	40%	0%	3,674
	Levelling for Street Lighting pane	2d	2d	03-Sep-26	20-Sep-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	1,837
	JDH3-02-009-R19-(SL)- LV Cables -	8d	8d	28-Jul-26	05-Aug-26	01-Oct-26	10-Oct-26	428d	4	100%	0%	1,212
	Backfilling, Warning Tape Works f	2d	2d	04-Aug-26	05-Aug-26	08-Oct-26	10-Oct-26	428d	1	100%	0%	121
	Testing and Commissioning for L	2d	2d	02-Aug-26	03-Aug-26	06-Oct-26	07-Oct-26	428d	1	100%	0%	61
	Bedding Layer and Installation fo	2d	2d	30-Jul-26	01-Aug-26	04-Oct-26	05-Oct-26	428d	1	100%	0%	909
	Excavation Works for LV Cables	2d	2d	28-Jul-26	29-Jul-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	121
	JDH3-02-009-R19-Road Works - RD	60d	60d	01-Jul-26	08-Sep-26	03-Oct-26	12-Dec-26	381d	20	100%	0%	637,303
	JDH3-02-009-R19-(RD)-Bituminous	5d	5d	04-Aug-26	09-Aug-26	05-Nov-26	11-Nov-26	381d	1	100%	0%	307,208

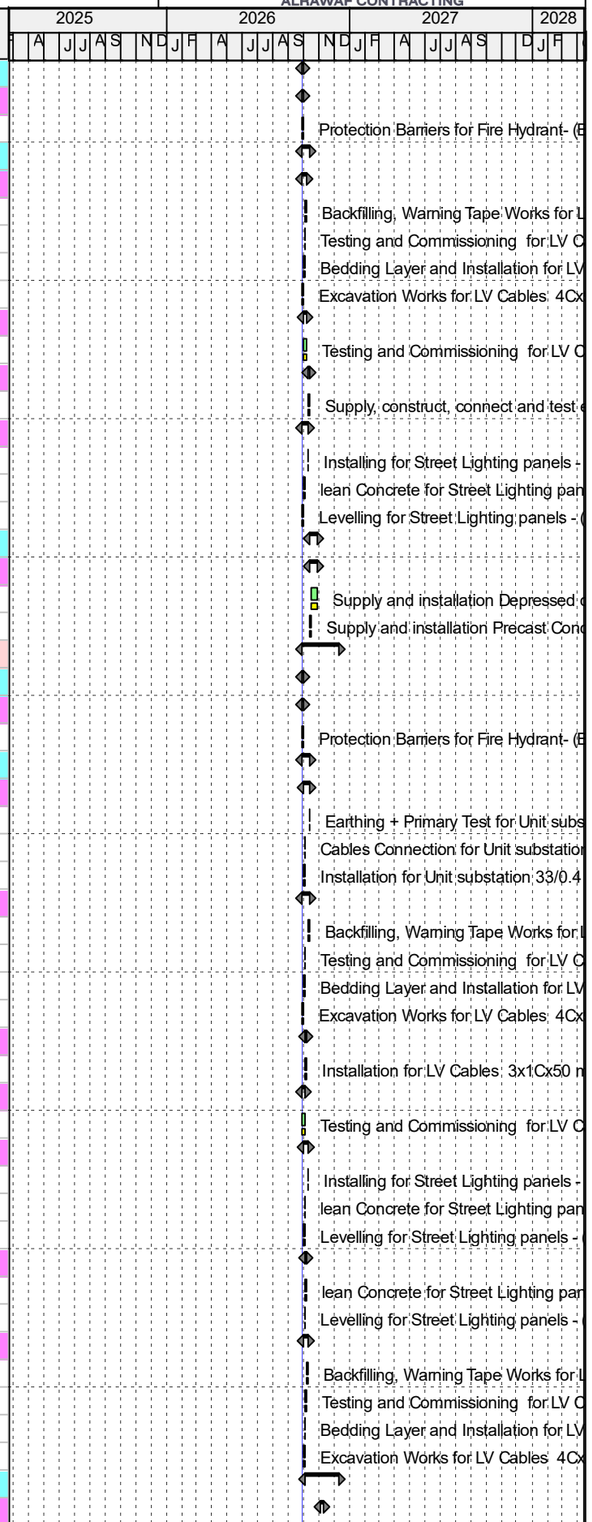


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Supply, lay and compaction Asph	5d	5d	04-Aug-26	09-Aug-26	05-Nov-26	11-Nov-26	381d	1	100%	0%	307,208
	JDH3-02-009-R19-(RD)-Precast Cor	11d	11d	01-Jul-26	13-Jul-26	03-Oct-26	15-Oct-26	381d	2	100%	0%	70,734
	Supply and installation Depressed	9d	9d	04-Jul-26	13-Jul-26	05-Oct-26	15-Oct-26	381d	1	100%	0%	55,656
	Supply and installation Precast C	2d	2d	01-Jul-26	02-Jul-26	03-Oct-26	05-Oct-26	381d	1	100%	0%	15,078
	JDH3-02-009-R19-(RD)-Precast Inte	18d	18d	14-Jul-26	03-Aug-26	15-Oct-26	05-Nov-26	381d	1	100%	0%	185,873
	Interlocking block pavers for sidev	18d	18d	14-Jul-26	03-Aug-26	15-Oct-26	05-Nov-26	381d	1	100%	0%	185,873
	JDH3-02-009-R19-(RD)-Pavement M	26d	26d	10-Aug-26	08-Sep-26	11-Nov-26	12-Dec-26	381d	13	100%	0%	19,912
	Retroreflective Only Right or Only	2d	2d	07-Sep-26	08-Sep-26	09-Dec-26	12-Dec-26	381d	1	100%	0%	572
	Retroreflective Straight-Right or S	2d	2d	05-Sep-26	06-Sep-26	07-Dec-26	09-Dec-26	381d	1	100%	0%	429
	Retroreflective Straight Arrow - (B	2d	2d	02-Sep-26	03-Sep-26	05-Dec-26	07-Dec-26	381d	1	100%	0%	2,146
	Thermoplastic intermittent 500 m	2d	2d	31-Aug-26	01-Sep-26	02-Dec-26	05-Dec-26	381d	1	100%	0%	573
	Thermoplastic intermittent 120 m	2d	2d	29-Aug-26	30-Aug-26	30-Nov-26	02-Dec-26	381d	1	100%	0%	829
	Thermoplastic intermittent 100 m	2d	2d	26-Aug-26	27-Aug-26	28-Nov-26	30-Nov-26	381d	1	100%	0%	988
	Thermoplastic continuous Chevro	2d	2d	24-Aug-26	25-Aug-26	25-Nov-26	28-Nov-26	381d	1	100%	0%	547
	Thermoplastic continuous Retrore	2d	2d	22-Aug-26	23-Aug-26	23-Nov-26	25-Nov-26	381d	1	100%	0%	3,802
	Thermoplastic continuous 100 m	2d	2d	19-Aug-26	20-Aug-26	21-Nov-26	23-Nov-26	381d	1	100%	0%	808
	Thermoplastic continuous 300 m	2d	2d	17-Aug-26	18-Aug-26	18-Nov-26	21-Nov-26	381d	1	100%	0%	458
	Thermoplastic continuous 200 m	2d	2d	15-Aug-26	16-Aug-26	16-Nov-26	18-Nov-26	381d	1	100%	0%	4,392
	Thermoplastic continuous 120 m	2d	2d	12-Aug-26	13-Aug-26	14-Nov-26	16-Nov-26	381d	1	100%	0%	795
	Thermoplastic continuous 120 m	2d	2d	10-Aug-26	11-Aug-26	11-Nov-26	14-Nov-26	381d	1	100%	0%	3,574
	JDH3-02-009-R19-(RD)-Traffic Sign	14d	14d	10-Aug-26	25-Aug-26	11-Nov-26	28-Nov-26	391d	3	100%	0%	53,576
	Supply and installation Traffic sign	2d	2d	24-Aug-26	25-Aug-26	25-Nov-26	28-Nov-26	391d	1	100%	0%	6,730
	Supply and installation Traffic sign	5d	5d	18-Aug-26	23-Aug-26	19-Nov-26	25-Nov-26	391d	1	100%	0%	23,955
	Supply and installation Traffic sign	7d	7d	10-Aug-26	17-Aug-26	11-Nov-26	19-Nov-26	391d	1	100%	0%	22,890
R20		47d	47d	25-Jun-26	28-Sep-26	29-Sep-26	22-Nov-26	397d	30	100%	0%	607,905
JDH3-02-009-R20-TSE Network - TSE		2d	2d	25-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	441d	2	100%	0%	13,452
JDH3-02-009-R20-(TSE)-Butterfly V		2d	2d	25-Jun-26	27-Jun-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	4,839
	Stem & Surface box for Butterfly	2d	2d	25-Jun-26	27-Jun-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	4,839
	JDH3-02-009-R20-(TSE)-Valve Char	2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	8,613
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	8,613
JDH3-02-009-R20-Potable Water Netw		14d	14d	06-Aug-26	02-Sep-26	29-Sep-26	14-Oct-26	430d	13	100%	0%	143,121
JDH3-02-009-R20-(WT)-Wash-Out V		4d	4d	06-Aug-26	10-Aug-26	29-Sep-26	03-Oct-26	434d	2	100%	0%	19,542
	Stem & Surface box for Wash-Ou	2d	2d	09-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	1,954
	Installation for Wash-Out Valve 15	2d	2d	06-Aug-26	08-Aug-26	29-Sep-26	30-Sep-26	430d	1	100%	0%	17,588
	JDH3-02-009-R20-(WT)-Wash-Out C	8d	8d	09-Aug-26	17-Aug-26	01-Oct-26	10-Oct-26	430d	4	100%	0%	27,211
	Backfilling Worksfor Wash-Out Ch	2d	2d	16-Aug-26	17-Aug-26	08-Oct-26	10-Oct-26	430d	1	100%	0%	5,442
	Installationfor Wash-Out Chambe	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	14,966
	PC Worksfor Wash-Out Chamber	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	2,721
	Excavation+Bedding for Wash-Ou	2d	2d	09-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	4,082
	JDH3-02-009-R20-(WT)-Butterfly Va	2d	2d	30-Aug-26	31-Aug-26	13-Oct-26	14-Oct-26	430d	1	100%	0%	2,607
	Stem & Surface box for Butterfly	2d	2d	30-Aug-26	31-Aug-26	13-Oct-26	14-Oct-26	430d	1	100%	0%	2,607
	JDH3-02-009-R20-(WT)-Butterfly Va	2d	2d	27-Aug-26	29-Aug-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	24,658
	Stem & Surface box for Butterfly	2d	2d	27-Aug-26	29-Aug-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	24,658
	JDH3-02-009-R20-(WT)-Valve Chan	2d	2d	25-Aug-26	26-Aug-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	18,359
	Backfilling Worksfor Butterfly Valv	2d	2d	25-Aug-26	26-Aug-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	18,359
	JDH3-02-009-R20-(WT)-Fire Hydran	6d	6d	27-Aug-26	02-Sep-26	29-Sep-26	05-Oct-26	438d	3	100%	0%	47,877
	Protection Barriers for Fire Hydran	2d	2d	01-Sep-26	02-Sep-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	3,420
	Fire Installation for Fire Hydrant- (	2d	2d	30-Aug-26	31-Aug-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	23,939
	Stem for Fire Hydrant- (B3.33 14	2d	2d	27-Aug-26	29-Aug-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	20,519
	JDH3-02-009-R20-(WT)-Valve Chan	2d	2d	27-Aug-26	29-Aug-26	11-Oct-26	13-Oct-26	431d	1	100%	0%	2,867
	Backfilling Worksfor Butterfly Valv	2d	2d	27-Aug-26	29-Aug-26	11-Oct-26	13-Oct-26	431d	1	100%	0%	2,867
JDH3-02-009-R20-Electrical Network		15d	15d	08-Jul-26	25-Jul-26	08-Oct-26	25-Oct-26	391d	4	100%	0%	227,213
JDH3-02-009-R20-(EL)-MV cable tr		15d	15d	08-Jul-26	25-Jul-26	08-Oct-26	25-Oct-26	391d	2	100%	0%	5,593

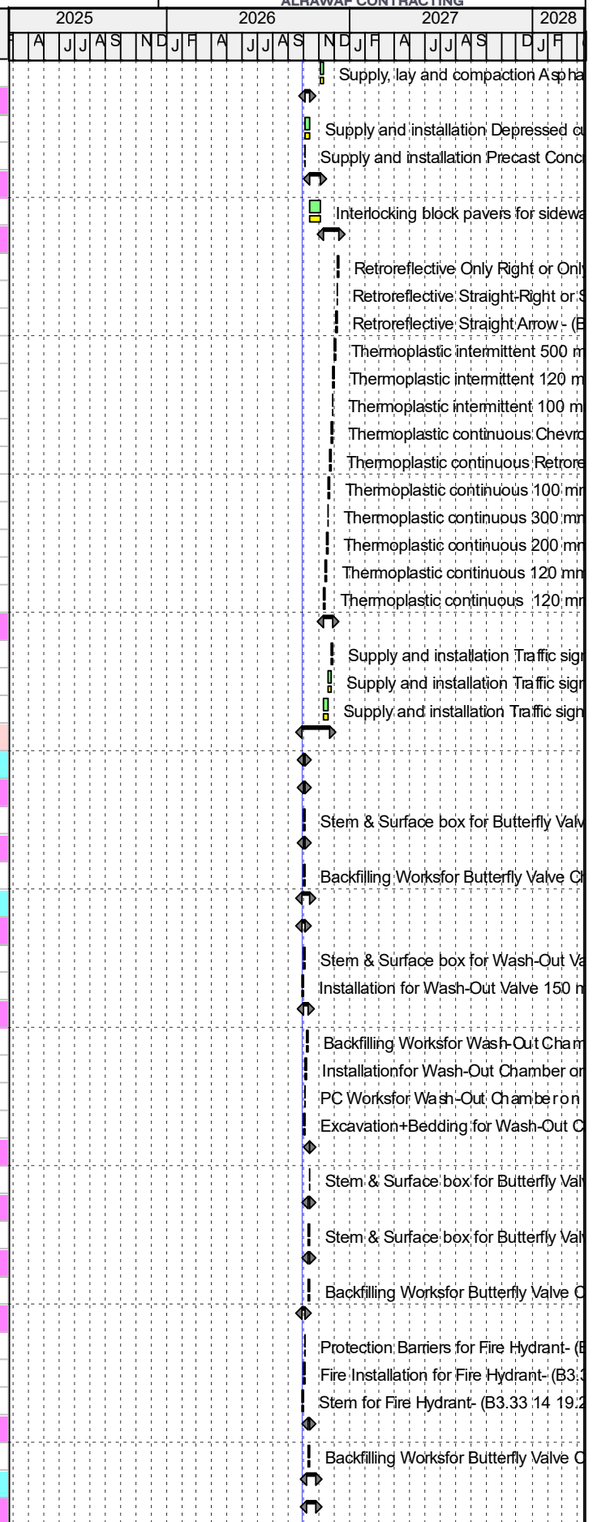

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Backfilling + Warning Tape for MV	3d	3d	22-Jul-26	25-Jul-26	22-Oct-26	25-Oct-26	391d	1	100%	0%	2,237
	Excavation for MV Cable Trench	5d	5d	08-Jul-26	13-Jul-26	08-Oct-26	13-Oct-26	391d	1	100%	0%	3,356
	JDH3-02-009-R20-(EL)-MV cables /	7d	7d	14-Jul-26	21-Jul-26	14-Oct-26	21-Oct-26	391d	2	100%	0%	221,620
	Installing Joints for MV Cables 3C	2d	2d	20-Jul-26	21-Jul-26	20-Oct-26	21-Oct-26	391d	1	100%	0%	8,701
	Installing for MV Cables AL/XLPE	5d	5d	14-Jul-26	19-Jul-26	14-Oct-26	19-Oct-26	391d	1	100%	0%	212,919
	JDH3-02-009-R20-Street Lighting Netv	9d	9d	28-Jul-26	20-Aug-26	26-Oct-26	04-Nov-26	412d	9	100%	0%	87,668
	JDH3-02-009-R20-(SL)- LV Cables -	8d	8d	28-Jul-26	05-Aug-26	26-Oct-26	03-Nov-26	391d	4	100%	0%	68,353
	Backfilling, Warning Tape Works f	2d	2d	04-Aug-26	05-Aug-26	02-Nov-26	03-Nov-26	391d	1	100%	0%	6,835
	Testing and Commissioning for L	2d	2d	02-Aug-26	03-Aug-26	31-Oct-26	01-Nov-26	391d	1	100%	0%	3,418
	Bedding Layer and Installation fo	2d	2d	30-Jul-26	01-Aug-26	28-Oct-26	29-Oct-26	391d	1	100%	0%	51,265
	Excavation Works for LV Cables	2d	2d	28-Jul-26	29-Jul-26	26-Oct-26	27-Oct-26	391d	1	100%	0%	6,835
	JDH3-02-009-R20-(SL)-Earthing Sy	3d	3d	18-Aug-26	20-Aug-26	02-Nov-26	04-Nov-26	412d	1	100%	0%	5,628
	Supply, construct, connect and te	3d	3d	18-Aug-26	20-Aug-26	02-Nov-26	04-Nov-26	412d	1	100%	0%	5,628
	JDH3-02-009-R20-(SL)- Street Ligh	6d	6d	28-Jul-26	13-Aug-26	26-Oct-26	01-Nov-26	412d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	12-Aug-26	13-Aug-26	31-Oct-26	01-Nov-26	412d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	09-Aug-26	10-Aug-26	28-Oct-26	29-Oct-26	412d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	28-Jul-26	29-Jul-26	26-Oct-26	27-Oct-26	412d	1	100%	0%	1,033
	JDH3-02-009-R20-(SL)- LV Cables -	5d	5d	11-Aug-26	16-Aug-26	28-Oct-26	02-Nov-26	392d	1	100%	0%	3,356
	Testing and Commissioning for L	5d	5d	11-Aug-26	16-Aug-26	28-Oct-26	02-Nov-26	392d	1	100%	0%	3,356
	JDH3-02-009-R20-Road Works - RD	12d	12d	14-Sep-26	28-Sep-26	08-Nov-26	22-Nov-26	391d	2	100%	0%	136,451
	JDH3-02-009-R20-(RD)-Precast Cor	12d	12d	14-Sep-26	28-Sep-26	08-Nov-26	22-Nov-26	391d	2	100%	0%	136,451
	Supply and installation Depresse	6d	6d	21-Sep-26	28-Sep-26	15-Nov-26	22-Nov-26	391d	1	100%	0%	83,542
	Supply and installation Precast C	6d	6d	14-Sep-26	20-Sep-26	08-Nov-26	15-Nov-26	391d	1	100%	0%	52,910
R151		63d	63d	04-Jul-26	14-Sep-26	29-Sep-26	12-Dec-26	381d	33	100%	0%	792,686
	JDH3-02-009-R151-Potable Water Net	2d	2d	12-Aug-26	13-Aug-26	18-Oct-26	19-Oct-26	426d	1	100%	0%	4,885
	JDH3-02-009-R151-(WT)-Fire Hydra	2d	2d	12-Aug-26	13-Aug-26	18-Oct-26	19-Oct-26	426d	1	100%	0%	4,885
	Protection Barriers for Fire Hydran	2d	2d	12-Aug-26	13-Aug-26	18-Oct-26	19-Oct-26	426d	1	100%	0%	4,885
	JDH3-02-009-R151-Street Lighting Ne	13d	13d	11-Jul-26	18-Aug-26	29-Sep-26	13-Oct-26	431d	11	100%	0%	101,056
	JDH3-02-009-R151-(SL)- LV Cables	8d	8d	11-Jul-26	20-Jul-26	29-Sep-26	07-Oct-26	432d	4	100%	0%	80,468
	Backfilling, Warning Tape Works f	2d	2d	18-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	8,047
	Testing and Commissioning for L	2d	2d	15-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	4,023
	Bedding Layer and Installation fo	2d	2d	13-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	60,351
	Excavation Works for LV Cables	2d	2d	11-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	432d	1	100%	0%	8,047
	JDH3-02-009-R151-(SL)- LV Cables	5d	5d	25-Jul-26	30-Jul-26	01-Oct-26	06-Oct-26	433d	1	100%	0%	3,858
	Testing and Commissioning for L	5d	5d	25-Jul-26	30-Jul-26	01-Oct-26	06-Oct-26	433d	1	100%	0%	3,858
	JDH3-02-009-R151-(SL)-Earthing S	2d	2d	13-Aug-26	16-Aug-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	426
	Supply, construct, connect and te	2d	2d	13-Aug-26	16-Aug-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	426
	JDH3-02-009-R151-(SL)-Earthing S	2d	2d	16-Aug-26	18-Aug-26	12-Oct-26	13-Oct-26	431d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	16-Aug-26	18-Aug-26	12-Oct-26	13-Oct-26	431d	1	100%	0%	1,126
	JDH3-02-009-R151-(SL)- Street Ligl	9d	9d	08-Aug-26	15-Aug-26	01-Oct-26	11-Oct-26	431d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	12-Aug-26	15-Aug-26	10-Oct-26	11-Oct-26	431d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	10-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	08-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	1,033
	JDH3-02-009-R151-(SL)- LV Cables	2d	2d	02-Aug-26	04-Aug-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	4,847
	Installation for LV Cables 3-1xCx	2d	2d	02-Aug-26	04-Aug-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	4,847
	JDH3-02-009-R151-Road Works - RD	63d	63d	04-Jul-26	14-Sep-26	29-Sep-26	12-Dec-26	381d	21	100%	0%	686,745
	JDH3-02-009-R151-(RD)-Bituminous	5d	5d	08-Aug-26	12-Aug-26	03-Nov-26	09-Nov-26	381d	1	100%	0%	350,054
	Supply, lay and compaction Asph	5d	5d	08-Aug-26	12-Aug-26	03-Nov-26	09-Nov-26	381d	1	100%	0%	350,054
	JDH3-02-009-R151-(RD)-Precast Co	12d	12d	04-Jul-26	16-Jul-26	29-Sep-26	13-Oct-26	381d	2	100%	0%	81,763
	Supply and installation Depresse	10d	10d	06-Jul-26	16-Jul-26	01-Oct-26	13-Oct-26	381d	1	100%	0%	64,950
	Supply and installation Precast C	2d	2d	04-Jul-26	05-Jul-26	29-Sep-26	01-Oct-26	381d	1	100%	0%	16,813
	JDH3-02-009-R151-(RD)-Precast In	18d	18d	18-Jul-26	06-Aug-26	13-Oct-26	03-Nov-26	381d	1	100%	0%	176,695
	Interlocking block pavers for sidev	18d	18d	18-Jul-26	06-Aug-26	13-Oct-26	03-Nov-26	381d	1	100%	0%	176,695

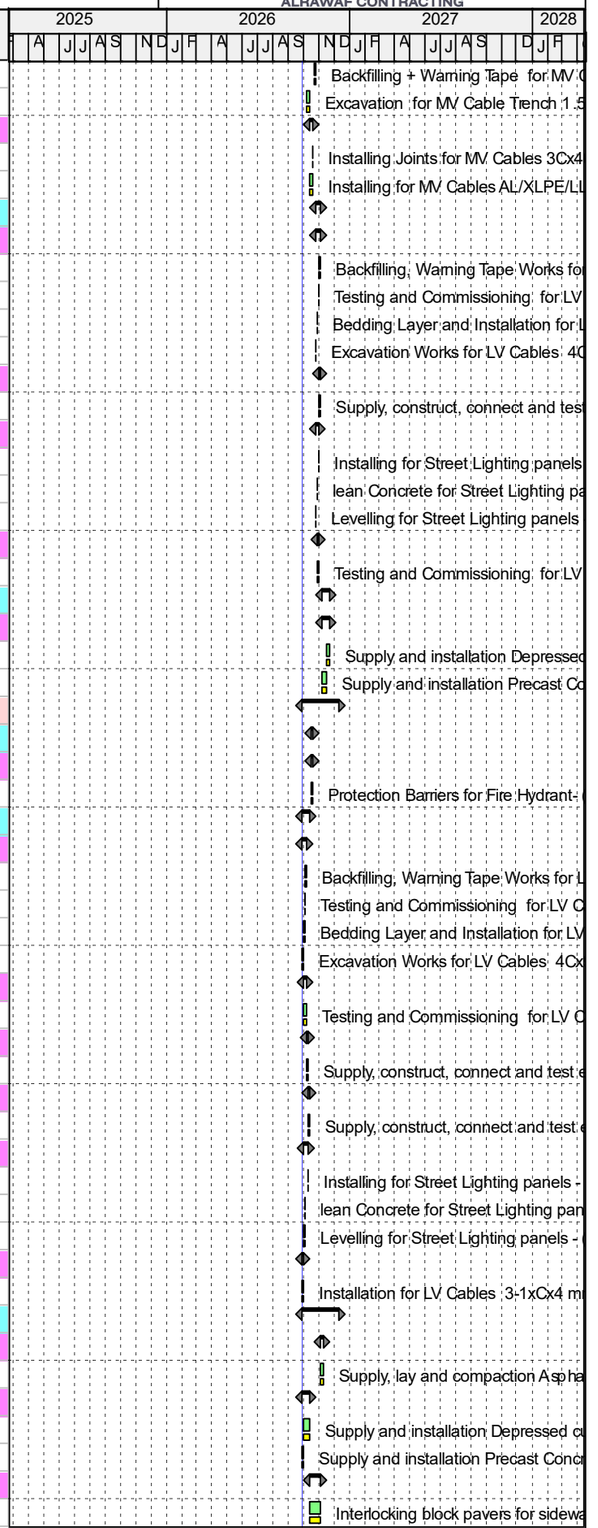


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R151-(RD)-Pavement	28d	28d	13-Aug-26	14-Sep-26	09-Nov-26	12-Dec-26	381d	14	100%	0%	18,118
	Retroreflective Only Right or Only	2d	2d	13-Sep-26	14-Sep-26	09-Dec-26	12-Dec-26	381d	1	100%	0%	286
	Retroreflective Straight-Right or S	2d	2d	10-Sep-26	12-Sep-26	07-Dec-26	09-Dec-26	381d	1	100%	0%	572
	Retroreflective Straight Arrow - (B	2d	2d	08-Sep-26	09-Sep-26	05-Dec-26	07-Dec-26	381d	1	100%	0%	1,717
	Thermoplastic intermittent 500 mi	2d	2d	06-Sep-26	07-Sep-26	02-Dec-26	05-Dec-26	381d	1	100%	0%	495
	Thermoplastic intermittent 120 mi	2d	2d	03-Sep-26	05-Sep-26	30-Nov-26	02-Dec-26	381d	1	100%	0%	970
	Thermoplastic intermittent 100 mi	2d	2d	01-Sep-26	02-Sep-26	28-Nov-26	30-Nov-26	381d	1	100%	0%	1,113
	Thermoplastic continuous Painte	2d	2d	30-Aug-26	31-Aug-26	25-Nov-26	28-Nov-26	381d	1	100%	0%	308
	Thermoplastic continuous Chevro	2d	2d	27-Aug-26	29-Aug-26	23-Nov-26	25-Nov-26	381d	1	100%	0%	355
	Thermoplastic continuous Retrore	2d	2d	25-Aug-26	26-Aug-26	21-Nov-26	23-Nov-26	381d	1	100%	0%	1,426
	Thermoplastic continuous 100 mi	2d	2d	23-Aug-26	24-Aug-26	18-Nov-26	21-Nov-26	381d	1	100%	0%	934
	Thermoplastic continuous 300 mi	2d	2d	20-Aug-26	22-Aug-26	16-Nov-26	18-Nov-26	381d	1	100%	0%	255
	Thermoplastic continuous 200 mi	2d	2d	18-Aug-26	19-Aug-26	14-Nov-26	16-Nov-26	381d	1	100%	0%	5,034
	Thermoplastic continuous 120 mi	2d	2d	16-Aug-26	17-Aug-26	11-Nov-26	14-Nov-26	381d	1	100%	0%	898
	Thermoplastic continuous 120 m	2d	2d	13-Aug-26	15-Aug-26	09-Nov-26	11-Nov-26	381d	1	100%	0%	3,755
	JDH3-02-009-R151-(RD)-Traffic Sig	16d	16d	13-Aug-26	31-Aug-26	09-Nov-26	28-Nov-26	391d	3	100%	0%	60,116
	Supply and installation Traffic sign	2d	2d	30-Aug-26	31-Aug-26	25-Nov-26	28-Nov-26	391d	1	100%	0%	6,730
	Supply and installation Traffic sign	5d	5d	24-Aug-26	29-Aug-26	19-Nov-26	25-Nov-26	391d	1	100%	0%	23,955
	Supply and installation Traffic sign	9d	9d	13-Aug-26	23-Aug-26	09-Nov-26	19-Nov-26	391d	1	100%	0%	29,431
Z2		122d	122d	23-Jun-26	13-Oct-26	29-Sep-26	17-Feb-27	322d	234	93.86%	0%	7,697,055
R07		4d	4d	23-Jun-26	04-Jul-26	29-Sep-26	03-Oct-26	440d	5	100%	0%	36,384
	JDH3-02-009-R07-TSE Network - TSE	4d	4d	23-Jun-26	04-Jul-26	29-Sep-26	03-Oct-26	440d	4	100%	0%	31,010
	JDH3-02-009-R07-(TSE)-Wash-Out	4d	4d	23-Jun-26	29-Jun-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	15,346
	Stem & Surface box for Wash-Ou	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,535
	Installation for Wash-Out Valve 1(	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	13,811
	JDH3-02-009-R07-(TSE)-Wash-Out	4d	4d	28-Jun-26	04-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	15,665
	Backfilling Worksfor Wash-Out Ch	2d	2d	02-Jul-26	04-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	4,177
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	11,487
	JDH3-02-009-R07-Potable Water Netw	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,374
	JDH3-02-009-R07-(WT)-Fire Hydrar	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,374
	Protection Barriers for Fire Hydrar	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,374
R08		92d	92d	23-Jun-26	17-Sep-26	29-Sep-26	13-Jan-27	352d	41	100%	0%	901,490
	JDH3-02-009-R08-Potable Water Netw	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	417d	1	100%	0%	4,397
	JDH3-02-009-R08-(WT)-Fire Hydrar	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	417d	1	100%	0%	4,397
	Protection Barriers for Fire Hydrar	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	417d	1	100%	0%	4,397
	JDH3-02-009-R08-Electrical Network	17d	17d	07-Jul-26	26-Jul-26	01-Oct-26	20-Oct-26	417d	4	100%	0%	164,372
	JDH3-02-009-R08-(EL)-MV cable tr	17d	17d	07-Jul-26	26-Jul-26	01-Oct-26	20-Oct-26	417d	2	100%	0%	8,260
	Backfilling + Warning Tape for MV	5d	5d	21-Jul-26	26-Jul-26	15-Oct-26	20-Oct-26	417d	1	100%	0%	3,304
	Excavation for MV Cable Trench	6d	6d	07-Jul-26	13-Jul-26	01-Oct-26	07-Oct-26	417d	1	100%	0%	4,956
	JDH3-02-009-R08-(EL)-MV cables /	6d	6d	14-Jul-26	20-Jul-26	08-Oct-26	14-Oct-26	417d	2	100%	0%	156,112
	Installing Joints for MV Cables 3C	2d	2d	19-Jul-26	20-Jul-26	13-Oct-26	14-Oct-26	417d	1	100%	0%	5,801
	Installing for MV Cables AL/XLPE	4d	4d	14-Jul-26	18-Jul-26	08-Oct-26	12-Oct-26	417d	1	100%	0%	150,311
	JDH3-02-009-R08-Street Lighting Netv	27d	27d	23-Jun-26	25-Aug-26	29-Sep-26	29-Oct-26	417d	10	100%	0%	96,554
	JDH3-02-009-R08-(SL)- LV Cables -	8d	8d	27-Jul-26	04-Aug-26	21-Oct-26	29-Oct-26	417d	4	100%	0%	75,043
	Backfilling, Warning Tape Works f	2d	2d	03-Aug-26	04-Aug-26	28-Oct-26	29-Oct-26	417d	1	100%	0%	7,504
	Testing and Commissioning for L	2d	2d	01-Aug-26	02-Aug-26	26-Oct-26	27-Oct-26	417d	1	100%	0%	3,752
	Bedding Layer and Installation fo	2d	2d	29-Jul-26	30-Jul-26	24-Oct-26	25-Oct-26	417d	1	100%	0%	56,283
	Excavation Works for LV Cables	2d	2d	27-Jul-26	28-Jul-26	21-Oct-26	22-Oct-26	417d	1	100%	0%	7,504
	JDH3-02-009-R08-(SL)- LV Cables -	10d	10d	10-Aug-26	20-Aug-26	29-Sep-26	10-Oct-26	434d	2	100%	0%	10,054
	Backfilling, Warning Tape Works f	5d	5d	16-Aug-26	20-Aug-26	05-Oct-26	10-Oct-26	434d	1	100%	0%	6,703
	Testing and Commissioning for L	5d	5d	10-Aug-26	15-Aug-26	29-Sep-26	04-Oct-26	434d	1	100%	0%	3,351
	JDH3-02-009-R08-(SL)-Earthing Sy	2d	2d	24-Aug-26	25-Aug-26	12-Oct-26	13-Oct-26	411d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	24-Aug-26	25-Aug-26	12-Oct-26	13-Oct-26	411d	1	100%	0%	1,126

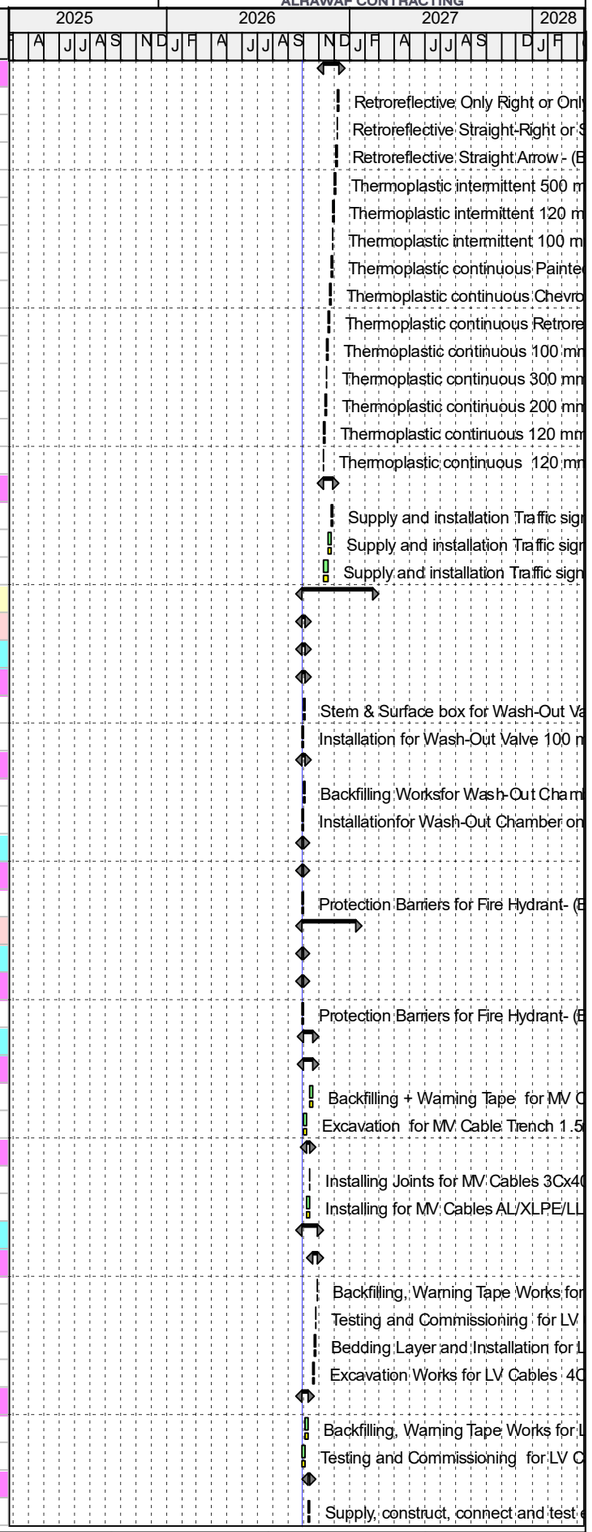

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R08-(SL)- Street Ligh	11d	11d	23-Jun-26	20-Aug-26	29-Sep-26	11-Oct-26	433d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	19-Aug-26	20-Aug-26	10-Oct-26	11-Oct-26	411d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	17-Aug-26	18-Aug-26	29-Sep-26	30-Sep-26	418d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	1,033
	JDH3-02-009-R08-Telecommunicatior	33d	33d	23-Jun-26	17-Sep-26	29-Sep-26	05-Nov-26	411d	8	100%	0%	125,489
	JDH3-02-009-R08-(TEL)-Reinforcec	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	414d	4	100%	0%	1,907
	Backfilling Works for RC Duct 6-w	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	414d	1	100%	0%	191
	Pouring RC Concrete Cover for R	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	414d	1	100%	0%	572
	Installation for RC Duct 6-ways du	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	414d	1	100%	0%	858
	Excavation Works for RC Duct 6-v	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	414d	1	100%	0%	286
	JDH3-02-009-R08-(TEL)-Unreinforc	20d	20d	26-Aug-26	17-Sep-26	14-Oct-26	05-Nov-26	411d	4	100%	0%	123,582
	Backfilling Works for Duct 6-ways	3d	3d	15-Sep-26	17-Sep-26	03-Nov-26	05-Nov-26	411d	1	100%	0%	12,358
	Pouring PC Concrete Cover for D	7d	7d	07-Sep-26	14-Sep-26	26-Oct-26	02-Nov-26	411d	1	100%	0%	24,716
	Installation for Duct 6-ways ducts,	7d	7d	30-Aug-26	06-Sep-26	18-Oct-26	25-Oct-26	411d	1	100%	0%	67,970
	Excavation Works for Duct 6-ways	3d	3d	26-Aug-26	29-Aug-26	14-Oct-26	17-Oct-26	411d	1	100%	0%	18,537
	JDH3-02-009-R08-Road Works - RD	40d	40d	25-Jun-26	02-Aug-26	29-Sep-26	14-Nov-26	399d	17	100%	0%	496,180
	JDH3-02-009-R08-(RD)-Bituminous	5d	5d	02-Jul-26	07-Jul-26	14-Oct-26	19-Oct-26	399d	1	100%	0%	285,288
	Supply, lay and compaction Asph	5d	5d	02-Jul-26	07-Jul-26	14-Oct-26	19-Oct-26	399d	1	100%	0%	285,288
	JDH3-02-009-R08-(RD)-Precast Cor	11d	11d	25-Jun-26	29-Jun-26	29-Sep-26	11-Oct-26	399d	2	100%	0%	62,795
	Supply and installation Depresse	9d	9d	28-Jun-26	29-Jun-26	01-Oct-26	11-Oct-26	399d	1	100%	0%	53,795
	Supply and installation Precast C	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	399d	1	100%	0%	9,001
	JDH3-02-009-R08-(RD)-Precast Inte	2d	2d	30-Jun-26	01-Jul-26	12-Oct-26	13-Oct-26	399d	1	100%	0%	121,560
	Interlocking block pavers for sidev	2d	2d	30-Jun-26	01-Jul-26	12-Oct-26	13-Oct-26	399d	1	100%	0%	121,560
	JDH3-02-009-R08-(RD)-Pavement M	22d	22d	08-Jul-26	02-Aug-26	20-Oct-26	14-Nov-26	399d	11	100%	0%	13,685
	Retroreflective Only Right or Only	2d	2d	01-Aug-26	02-Aug-26	12-Nov-26	14-Nov-26	399d	1	100%	0%	572
	Retroreflective Straight Arrow - (B	2d	2d	29-Jul-26	30-Jul-26	10-Nov-26	11-Nov-26	399d	1	100%	0%	572
	Thermoplastic intermittent 120 m	2d	2d	27-Jul-26	28-Jul-26	08-Nov-26	09-Nov-26	399d	1	100%	0%	1,205
	Thermoplastic intermittent 100 m	2d	2d	25-Jul-26	26-Jul-26	05-Nov-26	07-Nov-26	399d	1	100%	0%	1,604
	Thermoplastic continuous Chevro	2d	2d	22-Jul-26	23-Jul-26	03-Nov-26	04-Nov-26	399d	1	100%	0%	194
	Thermoplastic continuous Retrore	2d	2d	20-Jul-26	21-Jul-26	01-Nov-26	02-Nov-26	399d	1	100%	0%	1,901
	Thermoplastic continuous 100 m	2d	2d	18-Jul-26	19-Jul-26	29-Oct-26	31-Oct-26	399d	1	100%	0%	1,339
	Thermoplastic continuous 300 m	2d	2d	15-Jul-26	16-Jul-26	27-Oct-26	28-Oct-26	399d	1	100%	0%	164
	Thermoplastic continuous 200 m	2d	2d	13-Jul-26	14-Jul-26	25-Oct-26	26-Oct-26	399d	1	100%	0%	1,442
	Thermoplastic continuous 120 m	2d	2d	11-Jul-26	12-Jul-26	22-Oct-26	24-Oct-26	399d	1	100%	0%	355
	Thermoplastic continuous 120 m	2d	2d	08-Jul-26	09-Jul-26	20-Oct-26	21-Oct-26	399d	1	100%	0%	4,337
	JDH3-02-009-R08-(RD)-Traffic Signa	4d	4d	08-Jul-26	12-Jul-26	20-Oct-26	24-Oct-26	399d	2	100%	0%	12,852
	Supply and installation Traffic sigr	2d	2d	11-Jul-26	12-Jul-26	22-Oct-26	24-Oct-26	399d	1	100%	0%	9,582
	Supply and installation Traffic sigr	2d	2d	08-Jul-26	09-Jul-26	20-Oct-26	21-Oct-26	399d	1	100%	0%	3,270
	JDH3-02-009-R08-Landscape Works -	5d	5d	23-Aug-26	27-Aug-26	09-Jan-27	13-Jan-27	352d	1	100%	0%	14,498
	JDH3-02-009-R08-(LS)-HDPE for Se	5d	5d	23-Aug-26	27-Aug-26	09-Jan-27	13-Jan-27	352d	1	100%	0%	14,498
	Pipe line with Diam 110 mm PN1(	5d	5d	23-Aug-26	27-Aug-26	09-Jan-27	13-Jan-27	352d	1	100%	0%	14,498
R09		60d	60d	28-Jun-26	28-Sep-26	29-Sep-26	07-Dec-26	385d	22	100%	0%	334,774
	JDH3-02-009-R09-Potable Water Netw	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R09-(WT)-Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	Protection Barriers for Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R09-Electrical Network	6d	6d	08-Jul-26	14-Jul-26	04-Oct-26	11-Oct-26	255d	1	100%	0%	3,863
	JDH3-02-009-R09-(EL)-MV cable tr	6d	6d	08-Jul-26	14-Jul-26	04-Oct-26	11-Oct-26	255d	1	100%	0%	3,863
	Backfilling + Warning Tape for MV	6d	6d	08-Jul-26	14-Jul-26	04-Oct-26	11-Oct-26	255d	1	100%	0%	3,863
	JDH3-02-009-R09-Street Lighting Netv	32d	32d	15-Jul-26	18-Aug-26	29-Sep-26	04-Nov-26	413d	10	100%	0%	147,293
	JDH3-02-009-R09-(SL)- LV Cables -	16d	16d	15-Jul-26	02-Aug-26	11-Oct-26	29-Oct-26	255d	4	100%	0%	58,752
	Backfilling, Warning Tape Works f	4d	4d	29-Jul-26	02-Aug-26	25-Oct-26	29-Oct-26	255d	1	100%	0%	5,875
	Testing and Commissioning for L	4d	4d	25-Jul-26	28-Jul-26	20-Oct-26	25-Oct-26	255d	1	100%	0%	2,938
	Bedding Layer and Installation fo	4d	4d	20-Jul-26	23-Jul-26	15-Oct-26	20-Oct-26	255d	1	100%	0%	44,064

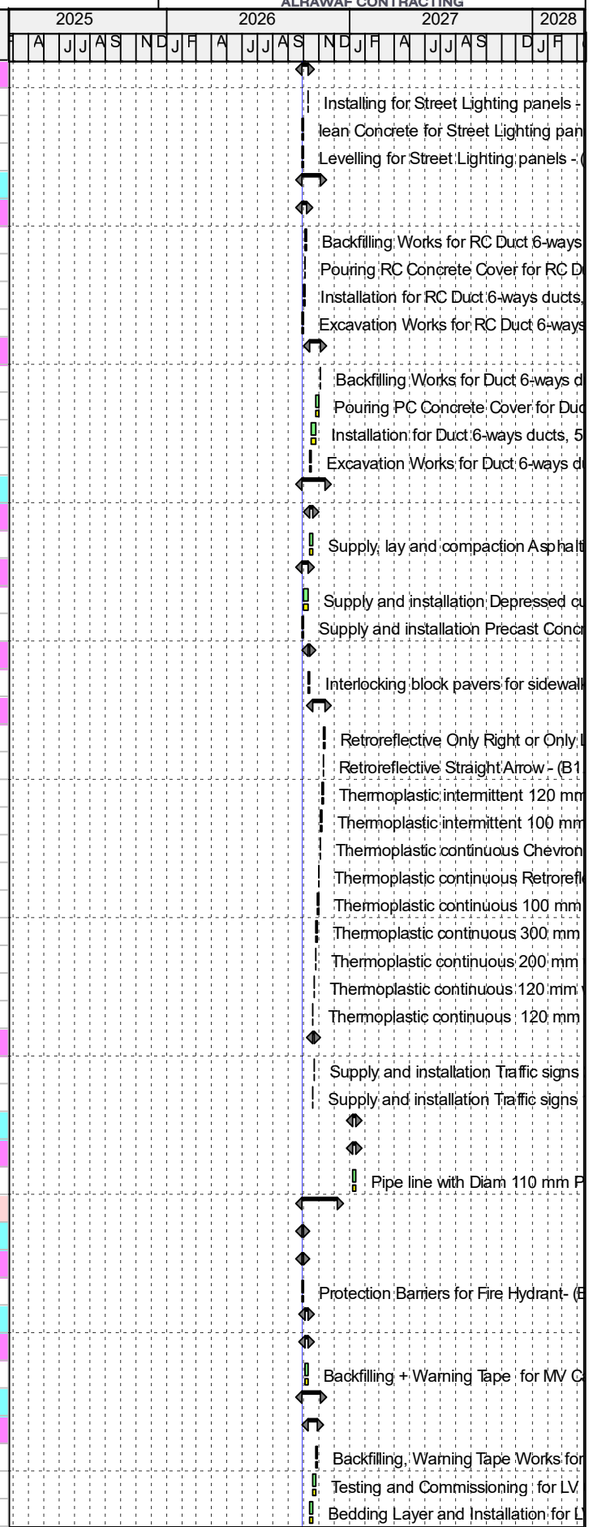


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Excavation Works for LV Cables	4d	4d	15-Jul-26	19-Jul-26	11-Oct-26	15-Oct-26	255d	1	100%	0%	5,875
	JDH3-02-009-R09-(SL)- LV Cables ·	2d	2d	25-Jul-26	26-Jul-26	20-Oct-26	22-Oct-26	260d	1	100%	0%	3,706
	Installation for LV Cables 3-1xCx	2d	2d	25-Jul-26	26-Jul-26	20-Oct-26	22-Oct-26	260d	1	100%	0%	3,706
	JDH3-02-009-R09-(SL)-Lighting Pol	16d	16d	01-Aug-26	18-Aug-26	29-Sep-26	17-Oct-26	428d	2	100%	0%	68,286
	Cable Connection for Lighting Po	8d	8d	10-Aug-26	18-Aug-26	08-Oct-26	17-Oct-26	428d	1	100%	0%	4,878
	Installation Works for Lighting Pol	8d	8d	01-Aug-26	09-Aug-26	29-Sep-26	07-Oct-26	428d	1	100%	0%	63,409
	JDH3-02-009-R09-(SL)-Street Light	11d	11d	27-Jul-26	08-Aug-26	22-Oct-26	04-Nov-26	255d	2	100%	0%	14,844
	Cable Connection for Lighting(LE	3d	3d	05-Aug-26	08-Aug-26	01-Nov-26	04-Nov-26	255d	1	100%	0%	2,969
	Installation for Lighting(LED) Lur	3d	3d	27-Jul-26	29-Jul-26	22-Oct-26	26-Oct-26	260d	1	100%	0%	11,875
	JDH3-02-009-R09-(SL)-Earthing Sy	2d	2d	03-Aug-26	04-Aug-26	29-Oct-26	01-Nov-26	255d	1	100%	0%	1,703
	Supply, construct, connect and te	2d	2d	03-Aug-26	04-Aug-26	29-Oct-26	01-Nov-26	255d	1	100%	0%	1,703
	JDH3-02-009-R09-Telecommunicatior	12d	12d	09-Aug-26	22-Aug-26	04-Nov-26	18-Nov-26	401d	7	100%	0%	99,289
	JDH3-02-009-R09-(TEL)-Unreinforc	12d	12d	09-Aug-26	22-Aug-26	04-Nov-26	18-Nov-26	255d	4	100%	0%	73,561
	Backfilling Works for Duct 6-ways	2d	2d	20-Aug-26	22-Aug-26	16-Nov-26	18-Nov-26	255d	1	100%	0%	7,356
	Pouring PC Concrete Cover for D	4d	4d	16-Aug-26	19-Aug-26	11-Nov-26	16-Nov-26	255d	1	100%	0%	14,712
	Installation for Duct 6-ways ducts,	4d	4d	11-Aug-26	15-Aug-26	07-Nov-26	11-Nov-26	255d	1	100%	0%	40,458
	Excavation Works for Duct 6-ways	2d	2d	09-Aug-26	10-Aug-26	04-Nov-26	07-Nov-26	255d	1	100%	0%	11,034
	JDH3-02-009-R09-(TEL)-Ducts	9d	9d	11-Aug-26	20-Aug-26	07-Nov-26	17-Nov-26	402d	3	100%	0%	25,728
	Backfilling Works for HDPE ducts	2d	2d	19-Aug-26	20-Aug-26	15-Nov-26	17-Nov-26	402d	1	100%	0%	2,573
	Installation for HDPE ducts 2 x 32	5d	5d	13-Aug-26	18-Aug-26	09-Nov-26	15-Nov-26	402d	1	100%	0%	19,296
	Excavation Works for HDPE ducts	2d	2d	11-Aug-26	12-Aug-26	07-Nov-26	09-Nov-26	402d	1	100%	0%	3,859
	JDH3-02-009-R09-Road Works - RD	16d	16d	09-Sep-26	28-Sep-26	18-Nov-26	07-Dec-26	255d	3	100%	0%	79,444
	JDH3-02-009-R09-(RD)-Precast Cor	16d	16d	09-Sep-26	28-Sep-26	18-Nov-26	07-Dec-26	255d	3	100%	0%	79,444
	Supply and installation Depresse	9d	9d	17-Sep-26	28-Sep-26	26-Nov-26	07-Dec-26	255d	1	100%	0%	53,460
	Supply and installation Depresse	4d	4d	13-Sep-26	16-Sep-26	22-Nov-26	26-Nov-26	255d	1	100%	0%	3,998
	Supply and installation Precast C	3d	3d	09-Sep-26	12-Sep-26	18-Nov-26	22-Nov-26	255d	1	100%	0%	21,986
R11		92d	92d	23-Jun-26	15-Sep-26	29-Sep-26	13-Jan-27	352d	44	100%	0%	725,136
	JDH3-02-009-R11-Potable Water Netw	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R11-(WT)-Fire Hydran	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	Protection Barriers for Fire Hydran	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R11-Electrical Network ·	6d	6d	16-Jul-26	22-Jul-26	30-Sep-26	07-Oct-26	437d	4	100%	0%	74,106
	JDH3-02-009-R11-(EL)-MV cables A	2d	2d	16-Jul-26	18-Jul-26	30-Sep-26	03-Oct-26	439d	1	100%	0%	5,160
	Termination for MV Cables 3Cx40	2d	2d	16-Jul-26	18-Jul-26	30-Sep-26	03-Oct-26	439d	1	100%	0%	5,160
	JDH3-02-009-R11-(EL)-RMU 33 KV	6d	6d	16-Jul-26	22-Jul-26	30-Sep-26	07-Oct-26	437d	3	100%	0%	68,946
	Earthing + Primary Test for RMU 3	2d	2d	21-Jul-26	22-Jul-26	05-Oct-26	07-Oct-26	437d	1	100%	0%	4,925
	Cables Connection for RMU 33 K'	2d	2d	19-Jul-26	20-Jul-26	03-Oct-26	05-Oct-26	437d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.2(	2d	2d	16-Jul-26	18-Jul-26	30-Sep-26	03-Oct-26	437d	1	100%	0%	59,096
	JDH3-02-009-R11-Street Lighting Netv	15d	15d	23-Jun-26	05-Aug-26	29-Sep-26	15-Oct-26	427d	17	100%	0%	132,301
	JDH3-02-009-R11-(SL)-RMU 33 KV	4d	4d	02-Aug-26	05-Aug-26	29-Sep-26	04-Oct-26	438d	2	100%	0%	54,621
	Cables Connection for RMU 33 K'	2d	2d	04-Aug-26	05-Aug-26	01-Oct-26	04-Oct-26	438d	1	100%	0%	4,202
	Installation for RMU 33 KV- (B2.2(	2d	2d	02-Aug-26	03-Aug-26	29-Sep-26	01-Oct-26	438d	1	100%	0%	50,420
	JDH3-02-009-R11-(SL)- LV Cables ·	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	430d	4	100%	0%	1,212
	Backfilling, Warning Tape Works f	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	121
	Testing and Commissioning for L	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	61
	Bedding Layer and Installation fo	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	909
	Excavation Works for LV Cables	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	430d	1	100%	0%	121
	JDH3-02-009-R11-(SL)- LV Cables ·	6d	6d	25-Jun-26	01-Jul-26	01-Oct-26	07-Oct-26	432d	3	100%	0%	42,314
	Testing and Commissioning for L	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	2,351
	Bedding Layer and Installation fo	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	35,261
	Excavation Works for LV Cables	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	4,702
	JDH3-02-009-R11-(SL)- LV Cables ·	5d	5d	09-Jul-26	14-Jul-26	29-Sep-26	04-Oct-26	417d	1	100%	0%	3,382
	Testing and Commissioning for L	5d	5d	09-Jul-26	14-Jul-26	29-Sep-26	04-Oct-26	417d	1	100%	0%	3,382
	JDH3-02-009-R11-(SL)- Street Light	11d	11d	28-Jun-26	14-Jul-26	29-Sep-26	11-Oct-26	407d	3	100%	0%	10,331

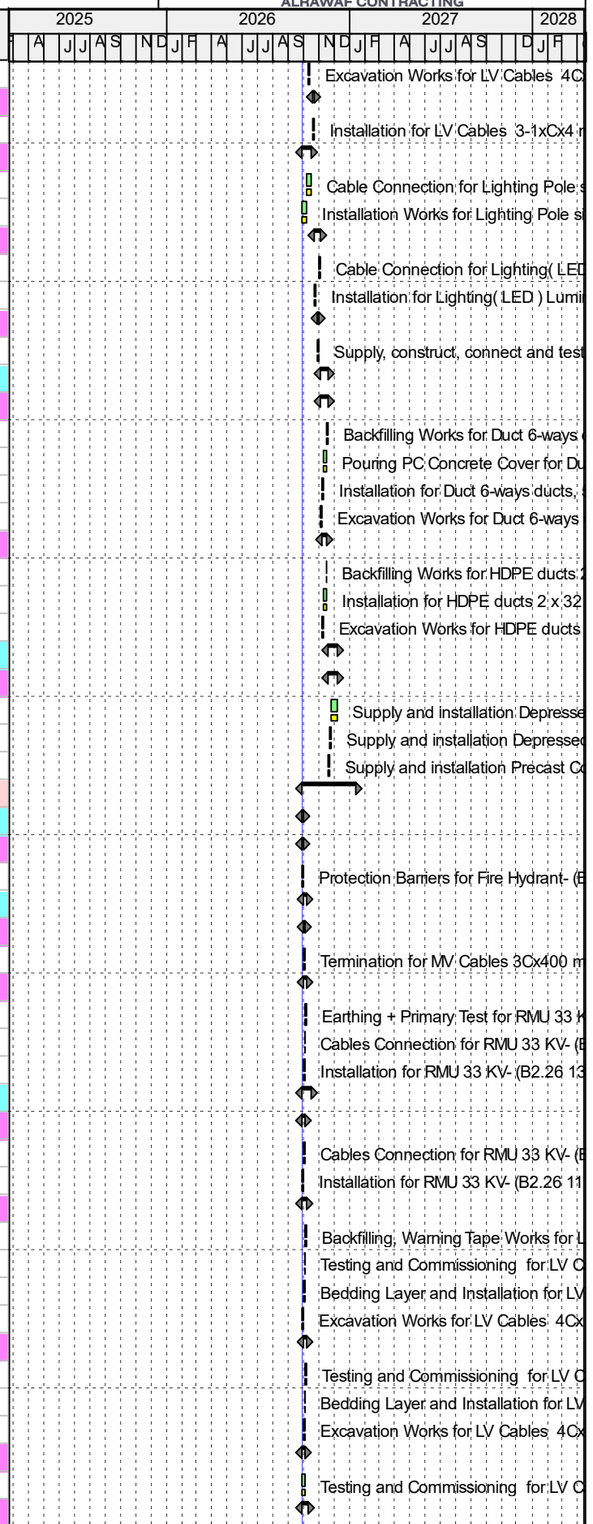


Actual Level of Effort · Remaining Work
Primary Baseline · Critical Remaining Work
Actual Work · Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Installing for Street Lighting pane	2d	2d	13-Jul-26	14-Jul-26	10-Oct-26	11-Oct-26	407d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	30-Jun-26	01-Jul-26	01-Oct-26	04-Oct-26	412d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	01-Oct-26	412d	1	100%	0%	1,033
	JDH3-02-009-R11-(SL)- LV Distribut	11d	11d	30-Jun-26	16-Jul-26	01-Oct-26	13-Oct-26	407d	3	100%	0%	18,369
	Installing for Street Lighting pane	2d	2d	15-Jul-26	16-Jul-26	12-Oct-26	13-Oct-26	407d	1	100%	0%	12,858
	lean Concrete for Street Lighting	2d	2d	02-Jul-26	04-Jul-26	04-Oct-26	06-Oct-26	412d	1	100%	0%	3,674
	Levelling for Street Lighting pane	2d	2d	30-Jun-26	01-Jul-26	01-Oct-26	04-Oct-26	412d	1	100%	0%	1,837
	JDH3-02-009-R11-(SL)-KWH meter	2d	2d	18-Jul-26	19-Jul-26	14-Oct-26	15-Oct-26	407d	1	100%	0%	2,072
	Installation for KWH meter - (B2.2	2d	2d	18-Jul-26	19-Jul-26	14-Oct-26	15-Oct-26	407d	1	100%	0%	2,072
	JDH3-02-009-R11-Telecommunicatior	8d	8d	02-Jul-26	11-Jul-26	08-Oct-26	17-Oct-26	425d	4	100%	0%	1,907
	JDH3-02-009-R11-(TEL)-Reinforced	8d	8d	02-Jul-26	11-Jul-26	08-Oct-26	17-Oct-26	425d	4	100%	0%	1,907
	Backfilling Works for RC Duct 6-w	2d	2d	09-Jul-26	11-Jul-26	15-Oct-26	17-Oct-26	425d	1	100%	0%	191
	Pouring RC Concrete Cover for R	2d	2d	07-Jul-26	08-Jul-26	13-Oct-26	14-Oct-26	425d	1	100%	0%	572
	Installation for RC Duct 6-ways du	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	425d	1	100%	0%	858
	Excavation Works for RC Duct 6-v	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	414d	1	100%	0%	286
	JDH3-02-009-R11-Road Works - RD	50d	50d	14-Jul-26	09-Sep-26	29-Sep-26	25-Nov-26	384d	17	100%	0%	498,139
	JDH3-02-009-R11-(RD)-Bituminous	5d	5d	10-Aug-26	15-Aug-26	26-Oct-26	31-Oct-26	384d	1	100%	0%	285,250
	Supply, lay and compaction Asph	5d	5d	10-Aug-26	15-Aug-26	26-Oct-26	31-Oct-26	384d	1	100%	0%	285,250
	JDH3-02-009-R11-(RD)-Precast Cor	11d	11d	14-Jul-26	26-Jul-26	29-Sep-26	11-Oct-26	384d	2	100%	0%	63,413
	Supply and installation Depresse	9d	9d	16-Jul-26	26-Jul-26	01-Oct-26	11-Oct-26	384d	1	100%	0%	53,809
	Supply and installation Precast C	2d	2d	14-Jul-26	15-Jul-26	29-Sep-26	30-Sep-26	384d	1	100%	0%	9,604
	JDH3-02-009-R11-(RD)-Precast Inte	12d	12d	27-Jul-26	09-Aug-26	12-Oct-26	25-Oct-26	384d	1	100%	0%	122,925
	Interlocking block pavers for sidev	12d	12d	27-Jul-26	09-Aug-26	12-Oct-26	25-Oct-26	384d	1	100%	0%	122,925
	JDH3-02-009-R11-(RD)-Pavement M	22d	22d	16-Aug-26	09-Sep-26	01-Nov-26	25-Nov-26	384d	11	100%	0%	13,699
	Retroreflective Only Right or Only	2d	2d	08-Sep-26	09-Sep-26	24-Nov-26	25-Nov-26	384d	1	100%	0%	572
	Retroreflective Straight Arrow - (B	2d	2d	06-Sep-26	07-Sep-26	22-Nov-26	23-Nov-26	384d	1	100%	0%	572
	Thermoplastic intermittent 120 m	2d	2d	03-Sep-26	05-Sep-26	19-Nov-26	21-Nov-26	384d	1	100%	0%	1,205
	Thermoplastic intermittent 100 m	2d	2d	01-Sep-26	02-Sep-26	17-Nov-26	18-Nov-26	384d	1	100%	0%	1,604
	Thermoplastic continuous Chevro	2d	2d	30-Aug-26	31-Aug-26	15-Nov-26	16-Nov-26	384d	1	100%	0%	189
	Thermoplastic continuous Retrore	2d	2d	27-Aug-26	29-Aug-26	12-Nov-26	14-Nov-26	384d	1	100%	0%	1,901
	Thermoplastic continuous 100 m	2d	2d	25-Aug-26	26-Aug-26	10-Nov-26	11-Nov-26	384d	1	100%	0%	1,339
	Thermoplastic continuous 300 m	2d	2d	23-Aug-26	24-Aug-26	08-Nov-26	09-Nov-26	384d	1	100%	0%	164
	Thermoplastic continuous 200 m	2d	2d	20-Aug-26	22-Aug-26	05-Nov-26	07-Nov-26	384d	1	100%	0%	1,443
	Thermoplastic continuous 120 m	2d	2d	18-Aug-26	19-Aug-26	03-Nov-26	04-Nov-26	384d	1	100%	0%	372
	Thermoplastic continuous 120 m	2d	2d	16-Aug-26	17-Aug-26	01-Nov-26	02-Nov-26	384d	1	100%	0%	4,338
	JDH3-02-009-R11-(RD)-Traffic Signa	4d	4d	16-Aug-26	19-Aug-26	01-Nov-26	04-Nov-26	400d	2	100%	0%	12,852
	Supply and installation Traffic sigr	2d	2d	18-Aug-26	19-Aug-26	03-Nov-26	04-Nov-26	400d	1	100%	0%	9,582
	Supply and installation Traffic sigr	2d	2d	16-Aug-26	17-Aug-26	01-Nov-26	02-Nov-26	400d	1	100%	0%	3,270
	JDH3-02-009-R11-Landscape Works -	5d	5d	10-Sep-26	15-Sep-26	09-Jan-27	13-Jan-27	347d	1	100%	0%	14,288
	JDH3-02-009-R11-(LS)-HDPE for Se	5d	5d	10-Sep-26	15-Sep-26	09-Jan-27	13-Jan-27	347d	1	100%	0%	14,288
	Pipe line with Diam 110 mm PN1(	5d	5d	10-Sep-26	15-Sep-26	09-Jan-27	13-Jan-27	347d	1	100%	0%	14,288
R12		97d	97d	30-Jun-26	21-Sep-26	29-Sep-26	19-Jan-27	347d	29	100%	0%	648,777
	JDH3-02-009-R12-Potable Water Netw	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R12-(WT)-Fire Hydrar	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	Protection Barriers for Fire Hydrar	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R12-Street Lighting Netv	5d	5d	30-Jun-26	12-Jul-26	29-Sep-26	04-Oct-26	439d	2	100%	0%	6,141
	JDH3-02-009-R12-(SL)-Earthing Sy	3d	3d	30-Jun-26	04-Jul-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	2,555
	Supply, construct, connect and te	3d	3d	30-Jun-26	04-Jul-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	2,555
	JDH3-02-009-R12-(SL)- LV Cables -	5d	5d	06-Jul-26	12-Jul-26	29-Sep-26	04-Oct-26	439d	1	100%	0%	3,586
	Testing and Commissioning for L	5d	5d	06-Jul-26	12-Jul-26	29-Sep-26	04-Oct-26	439d	1	100%	0%	3,586
	JDH3-02-009-R12-Telecommunicatior	11d	11d	05-Jul-26	30-Jul-26	11-Oct-26	22-Oct-26	423d	8	100%	0%	125,489
	JDH3-02-009-R12-(TEL)-Reinforcec	8d	8d	05-Jul-26	13-Jul-26	11-Oct-26	19-Oct-26	424d	4	100%	0%	1,907
	Backfilling Works for RC Duct 6-w	2d	2d	12-Jul-26	13-Jul-26	18-Oct-26	19-Oct-26	424d	1	100%	0%	191

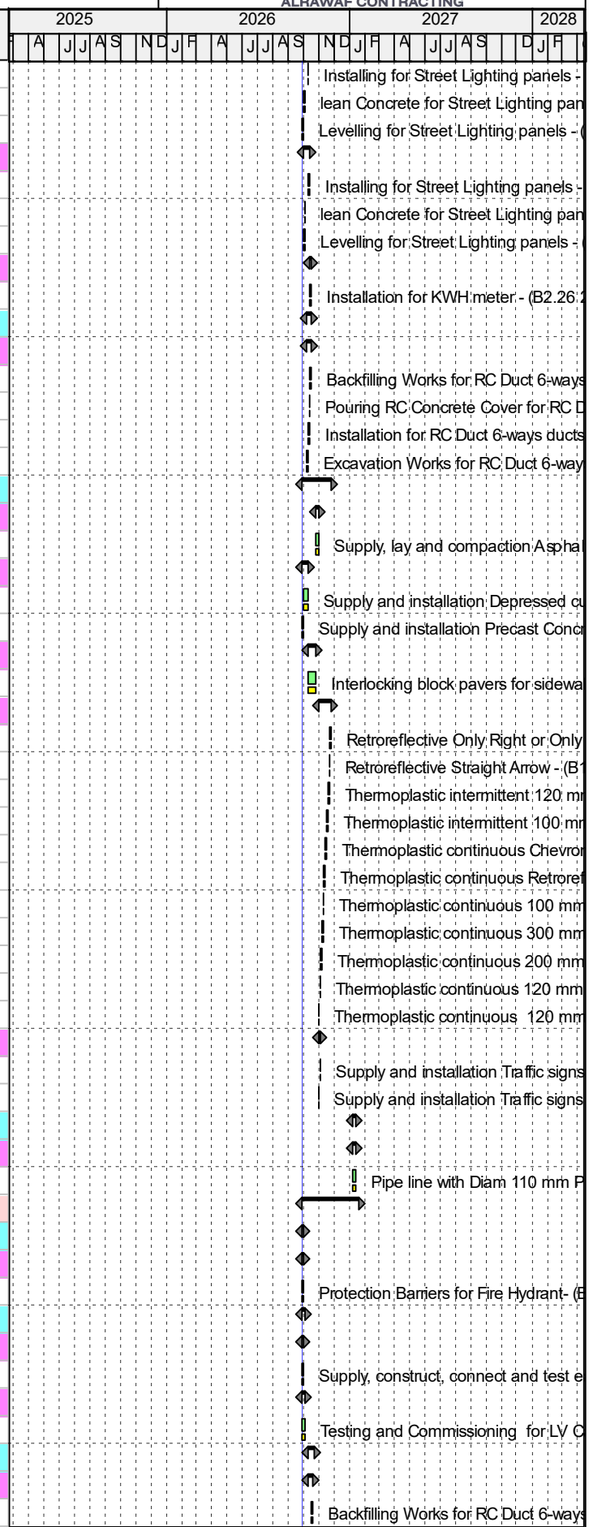


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Pouring RC Concrete Cover for R	2d	2d	09-Jul-26	11-Jul-26	15-Oct-26	17-Oct-26	424d	1	100%	0%	572
	Installation for RC Duct 6-ways du	2d	2d	07-Jul-26	08-Jul-26	13-Oct-26	14-Oct-26	424d	1	100%	0%	858
	Excavation Works for RC Duct 6-v	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	423d	1	100%	0%	286
	JDH3-02-009-R12-(TEL)-Unreinforc	9d	9d	21-Jul-26	30-Jul-26	13-Oct-26	22-Oct-26	423d	4	100%	0%	123,582
	Backfilling Works for Duct 6-ways	2d	2d	28-Jul-26	30-Jul-26	21-Oct-26	22-Oct-26	423d	1	100%	0%	12,358
	Pouring PC Concrete Cover for D	2d	2d	26-Jul-26	28-Jul-26	19-Oct-26	20-Oct-26	423d	1	100%	0%	24,716
	Installation for Duct 6-ways ducts,	2d	2d	23-Jul-26	26-Jul-26	17-Oct-26	18-Oct-26	423d	1	100%	0%	67,970
	Excavation Works for Duct 6-ways	3d	3d	21-Jul-26	23-Jul-26	13-Oct-26	15-Oct-26	423d	1	100%	0%	18,537
	JDH3-02-009-R12-Road Works - RD	35d	35d	28-Jul-26	03-Sep-26	29-Sep-26	08-Nov-26	404d	17	100%	0%	498,462
	JDH3-02-009-R12-(RD)-Bituminous	5d	5d	03-Aug-26	09-Aug-26	08-Oct-26	13-Oct-26	404d	1	100%	0%	285,326
	Supply, lay and compaction Asph	5d	5d	03-Aug-26	09-Aug-26	08-Oct-26	13-Oct-26	404d	1	100%	0%	285,326
	JDH3-02-009-R12-(RD)-Precast Cor	5d	5d	28-Jul-26	03-Aug-26	29-Sep-26	04-Oct-26	404d	2	100%	0%	63,766
	Supply and installation Depressed	3d	3d	30-Jul-26	03-Aug-26	01-Oct-26	04-Oct-26	404d	1	100%	0%	53,846
	Supply and installation Precast C	2d	2d	28-Jul-26	30-Jul-26	29-Sep-26	30-Sep-26	404d	1	100%	0%	9,920
	JDH3-02-009-R12-(RD)-Precast Inte	3d	3d	03-Aug-26	06-Aug-26	05-Oct-26	07-Oct-26	404d	1	100%	0%	122,836
	Interlocking block pavers for sidev	3d	3d	03-Aug-26	06-Aug-26	05-Oct-26	07-Oct-26	404d	1	100%	0%	122,836
	JDH3-02-009-R12-(RD)-Pavement M	22d	22d	09-Aug-26	03-Sep-26	14-Oct-26	08-Nov-26	404d	11	100%	0%	13,682
	Retroreflective Only Right or Only	2d	2d	01-Sep-26	03-Sep-26	07-Nov-26	08-Nov-26	404d	1	100%	0%	572
	Retroreflective Straight Arrow - (B1	2d	2d	30-Aug-26	01-Sep-26	04-Nov-26	05-Nov-26	404d	1	100%	0%	572
	Thermoplastic intermittent 120 mi	2d	2d	27-Aug-26	30-Aug-26	02-Nov-26	03-Nov-26	404d	1	100%	0%	1,205
	Thermoplastic intermittent 100 mi	2d	2d	25-Aug-26	27-Aug-26	31-Oct-26	01-Nov-26	404d	1	100%	0%	1,604
	Thermoplastic continuous Chevro	2d	2d	23-Aug-26	25-Aug-26	28-Oct-26	29-Oct-26	404d	1	100%	0%	189
	Thermoplastic continuous Retrore	2d	2d	20-Aug-26	23-Aug-26	26-Oct-26	27-Oct-26	404d	1	100%	0%	1,901
	Thermoplastic continuous 100 mi	2d	2d	18-Aug-26	20-Aug-26	24-Oct-26	25-Oct-26	404d	1	100%	0%	1,339
	Thermoplastic continuous 300 mi	2d	2d	16-Aug-26	18-Aug-26	21-Oct-26	22-Oct-26	404d	1	100%	0%	164
	Thermoplastic continuous 200 mi	2d	2d	13-Aug-26	16-Aug-26	19-Oct-26	20-Oct-26	404d	1	100%	0%	1,435
	Thermoplastic continuous 120 mi	2d	2d	11-Aug-26	13-Aug-26	17-Oct-26	18-Oct-26	404d	1	100%	0%	364
	Thermoplastic continuous 120 m	2d	2d	09-Aug-26	11-Aug-26	14-Oct-26	15-Oct-26	404d	1	100%	0%	4,338
	JDH3-02-009-R12-(RD)-Traffic Sign	4d	4d	09-Aug-26	13-Aug-26	14-Oct-26	18-Oct-26	404d	2	100%	0%	12,852
	Supply and installation Traffic sign	2d	2d	11-Aug-26	13-Aug-26	17-Oct-26	18-Oct-26	404d	1	100%	0%	9,582
	Supply and installation Traffic sign	2d	2d	09-Aug-26	11-Aug-26	14-Oct-26	15-Oct-26	404d	1	100%	0%	3,270
	JDH3-02-009-R12-Landscape Works -	5d	5d	16-Sep-26	21-Sep-26	14-Jan-27	19-Jan-27	347d	1	100%	0%	14,288
	JDH3-02-009-R12-(LS)-HDPE for Se	5d	5d	16-Sep-26	21-Sep-26	14-Jan-27	19-Jan-27	347d	1	100%	0%	14,288
	Pipe line with Diam 110 mm PN16	5d	5d	16-Sep-26	21-Sep-26	14-Jan-27	19-Jan-27	347d	1	100%	0%	14,288
R131		93d	93d	23-Jun-26	03-Oct-26	29-Sep-26	14-Jan-27	351d	18	75.78%	0%	1,118,819
	JDH3-02-009-R131-Potable Water Net	2d	2d	01-Sep-26	17-Sep-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R131-(WT)-Fire Hydra	2d	2d	01-Sep-26	17-Sep-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	Protection Barriers for Fire Hydrar	2d	2d	01-Sep-26	17-Sep-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R131-Electrical Network	20d	20d	23-Jun-26	15-Jul-26	29-Sep-26	21-Oct-26	412d	4	100%	0%	265,111
	JDH3-02-009-R131-(EL)-MV cable t	20d	20d	23-Jun-26	15-Jul-26	29-Sep-26	21-Oct-26	412d	2	100%	0%	11,379
	Backfilling + Warning Tape for MV	6d	6d	09-Jul-26	15-Jul-26	15-Oct-26	21-Oct-26	412d	1	100%	0%	4,552
	Excavation for MV Cable Trench	6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	402d	1	100%	0%	6,828
	JDH3-02-009-R131-(EL)-MV cables	8d	8d	30-Jun-26	08-Jul-26	06-Oct-26	14-Oct-26	412d	2	100%	0%	253,732
	Installing Joints for MV Cables 3C	2d	2d	07-Jul-26	08-Jul-26	13-Oct-26	14-Oct-26	412d	1	100%	0%	14,502
	Installing for MV Cables AL/XLPE	6d	6d	30-Jun-26	06-Jul-26	06-Oct-26	12-Oct-26	412d	1	100%	0%	239,230
	JDH3-02-009-R131-Street Lighting Ne	12d	12d	28-Jul-26	26-Aug-26	22-Oct-26	04-Nov-26	412d	4	100%	0%	19,218
	JDH3-02-009-R131-(SL)- LV Cables	10d	10d	28-Jul-26	08-Aug-26	22-Oct-26	02-Nov-26	412d	2	100%	0%	11,511
	Backfilling, Warning Tape Works f	5d	5d	03-Aug-26	08-Aug-26	28-Oct-26	02-Nov-26	412d	1	100%	0%	7,674
	Testing and Commissioning for L	5d	5d	28-Jul-26	02-Aug-26	22-Oct-26	27-Oct-26	412d	1	100%	0%	3,837
	JDH3-02-009-R131-(SL)-Lighting Pc	9d	9d	17-Aug-26	26-Aug-26	22-Oct-26	01-Nov-26	415d	1	100%	0%	6,003
	Cable Connection for Lighting Po	9d	9d	17-Aug-26	26-Aug-26	22-Oct-26	01-Nov-26	415d	1	100%	0%	6,003
	JDH3-02-009-R131-(SL)-Earthing S	2d	2d	09-Aug-26	10-Aug-26	03-Nov-26	04-Nov-26	412d	1	100%	0%	1,703
	Supply, construct, connect and te	2d	2d	09-Aug-26	10-Aug-26	03-Nov-26	04-Nov-26	412d	1	100%	0%	1,703

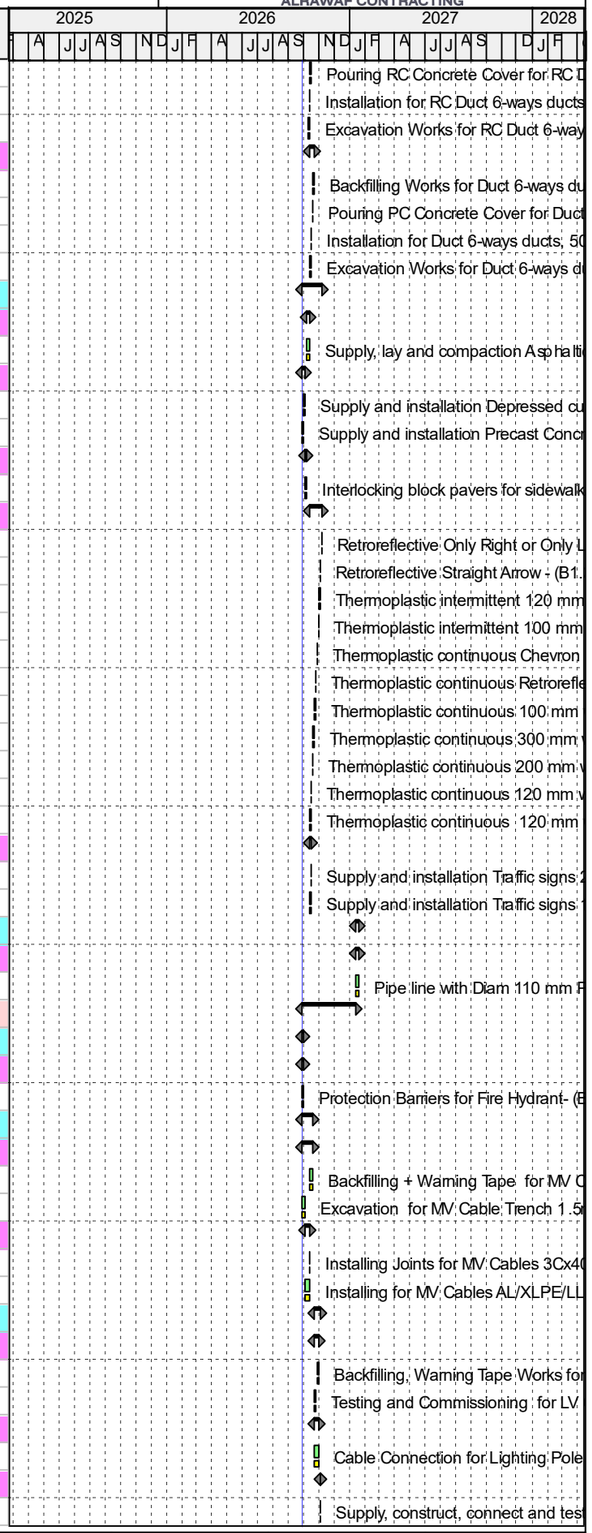


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Primary Baseline
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R131-Telecommunicatic	8d	8d	29-Jun-26	01-Aug-26	29-Sep-26	07-Oct-26	436d	3	100%	0%	19,984
	JDH3-02-009-R131-(TEL)-Ducts	8d	8d	29-Jun-26	01-Aug-26	29-Sep-26	07-Oct-26	436d	3	100%	0%	19,984
	Backfilling Works for HDPE ducts	2d	2d	30-Jul-26	01-Aug-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	1,998
	Installation for HDPE ducts 2 x 32	4d	4d	01-Jul-26	05-Jul-26	01-Oct-26	05-Oct-26	436d	1	100%	0%	14,988
	Excavation Works for HDPE ducts	2d	2d	29-Jun-26	30-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	2,998
	JDH3-02-009-R131-Road Works - RD	41d	41d	16-Aug-26	03-Oct-26	01-Oct-26	18-Nov-26	372d	5	67.29%	0%	791,551
	JDH3-02-009-R131-(RD)-Bituminous	6d	6d	27-Sep-26	03-Oct-26	11-Nov-26	18-Nov-26	372d	1	33.33%	0%	388,354
	Supply, lay and compaction Asph	6d	6d	27-Sep-26	03-Oct-26	11-Nov-26	18-Nov-26	372d	1	33.33%	0%	388,354
	JDH3-02-009-R131-(RD)-Precast C	20d	20d	16-Aug-26	07-Sep-26	01-Oct-26	25-Oct-26	329d	3	100%	0%	110,043
	Supply and installation Depressed	11d	11d	26-Aug-26	07-Sep-26	12-Oct-26	25-Oct-26	329d	1	100%	0%	69,521
	Supply and installation Depressed	4d	4d	22-Aug-26	25-Aug-26	07-Oct-26	12-Oct-26	329d	1	100%	0%	3,238
	Supply and installation Precast C	5d	5d	16-Aug-26	20-Aug-26	01-Oct-26	07-Oct-26	329d	1	100%	0%	37,285
	JDH3-02-009-R131-(RD)-Precast In	15d	15d	08-Sep-26	26-Sep-26	25-Oct-26	11-Nov-26	329d	1	100%	0%	293,154
	Interlocking block pavers for sidev	15d	15d	08-Sep-26	26-Sep-26	25-Oct-26	11-Nov-26	329d	1	100%	0%	293,154
	JDH3-02-009-R131-Landscape Works	6d	6d	27-Sep-26	03-Oct-26	09-Jan-27	14-Jan-27	280d	1	33.33%	0%	18,070
	JDH3-02-009-R131-(LS)-HDPE for S	6d	6d	27-Sep-26	03-Oct-26	09-Jan-27	14-Jan-27	280d	1	33.33%	0%	18,070
	Pipe line with Diam 110 mm PN16	6d	6d	27-Sep-26	03-Oct-26	09-Jan-27	14-Jan-27	280d	1	33.33%	0%	18,070
R132		77d	77d	07-Jul-26	01-Oct-26	29-Sep-26	27-Dec-26	367d	21	98.27%	0%	830,963
	JDH3-02-009-R132-Potable Water Net	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R132-(WT)-Fire Hydra	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	Protection Barriers for Fire Hydran	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R132-Street Lighting Ne	45d	45d	21-Jul-26	16-Aug-26	29-Sep-26	19-Nov-26	399d	12	100%	0%	149,298
	JDH3-02-009-R132-(SL)- LV Cables	12d	12d	21-Jul-26	03-Aug-26	28-Oct-26	10-Nov-26	399d	4	100%	0%	121,516
	Backfilling, Warning Tape Works f	3d	3d	01-Aug-26	03-Aug-26	08-Nov-26	10-Nov-26	399d	1	100%	0%	12,152
	Testing and Commissioning for L	3d	3d	28-Jul-26	30-Jul-26	04-Nov-26	07-Nov-26	399d	1	100%	0%	6,076
	Bedding Layer and Installation fo	3d	3d	25-Jul-26	27-Jul-26	01-Nov-26	03-Nov-26	399d	1	100%	0%	91,137
	Excavation Works for LV Cables	3d	3d	21-Jul-26	23-Jul-26	28-Oct-26	31-Oct-26	399d	1	100%	0%	12,152
	JDH3-02-009-R132-(SL)- LV Cables	13d	13d	03-Aug-26	11-Aug-26	01-Nov-26	15-Nov-26	399d	2	100%	0%	9,419
	Backfilling, Warning Tape Works f	4d	4d	08-Aug-26	11-Aug-26	11-Nov-26	15-Nov-26	399d	1	100%	0%	6,280
	Testing and Commissioning for L	4d	4d	03-Aug-26	06-Aug-26	01-Nov-26	04-Nov-26	404d	1	100%	0%	3,140
	JDH3-02-009-R132-(SL)-Earthing S	2d	2d	12-Aug-26	13-Aug-26	16-Nov-26	17-Nov-26	399d	1	100%	0%	1,278
	Supply, construct, connect and te	2d	2d	12-Aug-26	13-Aug-26	16-Nov-26	17-Nov-26	399d	1	100%	0%	1,278
	JDH3-02-009-R132-(SL)-Earthing S	2d	2d	15-Aug-26	16-Aug-26	18-Nov-26	19-Nov-26	399d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	15-Aug-26	16-Aug-26	18-Nov-26	19-Nov-26	399d	1	100%	0%	1,126
	JDH3-02-009-R132-(SL)- Street Ligl	11d	11d	06-Aug-26	12-Aug-26	29-Sep-26	11-Oct-26	431d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	11-Aug-26	12-Aug-26	10-Oct-26	11-Oct-26	431d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	09-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	06-Aug-26	08-Aug-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	1,033
	JDH3-02-009-R132-(SL)-Lighting P	6d	6d	01-Aug-26	06-Aug-26	29-Sep-26	05-Oct-26	436d	1	100%	0%	5,628
	Cable Connection for Lighting Po	6d	6d	01-Aug-26	06-Aug-26	29-Sep-26	05-Oct-26	436d	1	100%	0%	5,628
	JDH3-02-009-R132-Road Works - RD	53d	53d	01-Aug-26	01-Oct-26	26-Oct-26	27-Dec-26	341d	8	97.88%	0%	676,779
	JDH3-02-009-R132-(RD)-Bituminous	5d	5d	02-Sep-26	07-Sep-26	28-Nov-26	03-Dec-26	338d	1	100%	0%	352,694
	Supply, lay and compaction Asph	5d	5d	02-Sep-26	07-Sep-26	28-Nov-26	03-Dec-26	338d	1	100%	0%	352,694
	JDH3-02-009-R132-(RD)-Precast C	12d	12d	01-Aug-26	13-Aug-26	26-Oct-26	09-Nov-26	338d	2	100%	0%	79,825
	Supply and installation Depressed	10d	10d	03-Aug-26	13-Aug-26	28-Oct-26	09-Nov-26	338d	1	100%	0%	65,115
	Supply and installation Precast C	2d	2d	01-Aug-26	02-Aug-26	26-Oct-26	28-Oct-26	338d	1	100%	0%	14,711
	JDH3-02-009-R132-(RD)-Precast In	16d	16d	15-Aug-26	01-Sep-26	09-Nov-26	28-Nov-26	338d	1	100%	0%	163,408
	Interlocking block pavers for sidev	16d	16d	15-Aug-26	01-Sep-26	09-Nov-26	28-Nov-26	338d	1	100%	0%	163,408
	JDH3-02-009-R132-(RD)-Pavement	4d	4d	08-Sep-26	12-Sep-26	03-Dec-26	08-Dec-26	357d	2	100%	0%	6,325
	Thermoplastic continuous 120 mr	2d	2d	10-Sep-26	12-Sep-26	06-Dec-26	08-Dec-26	357d	1	100%	0%	1,253
	Thermoplastic continuous 120 m	2d	2d	08-Sep-26	09-Sep-26	03-Dec-26	06-Dec-26	357d	1	100%	0%	5,072
	JDH3-02-009-R132-(RD)-Traffic Sig	20d	20d	08-Sep-26	01-Oct-26	03-Dec-26	27-Dec-26	338d	2	80.71%	0%	74,527
	Supply and installation Traffic sigr	6d	6d	26-Sep-26	01-Oct-26	20-Dec-26	27-Dec-26	338d	1	50%	0%	28,746

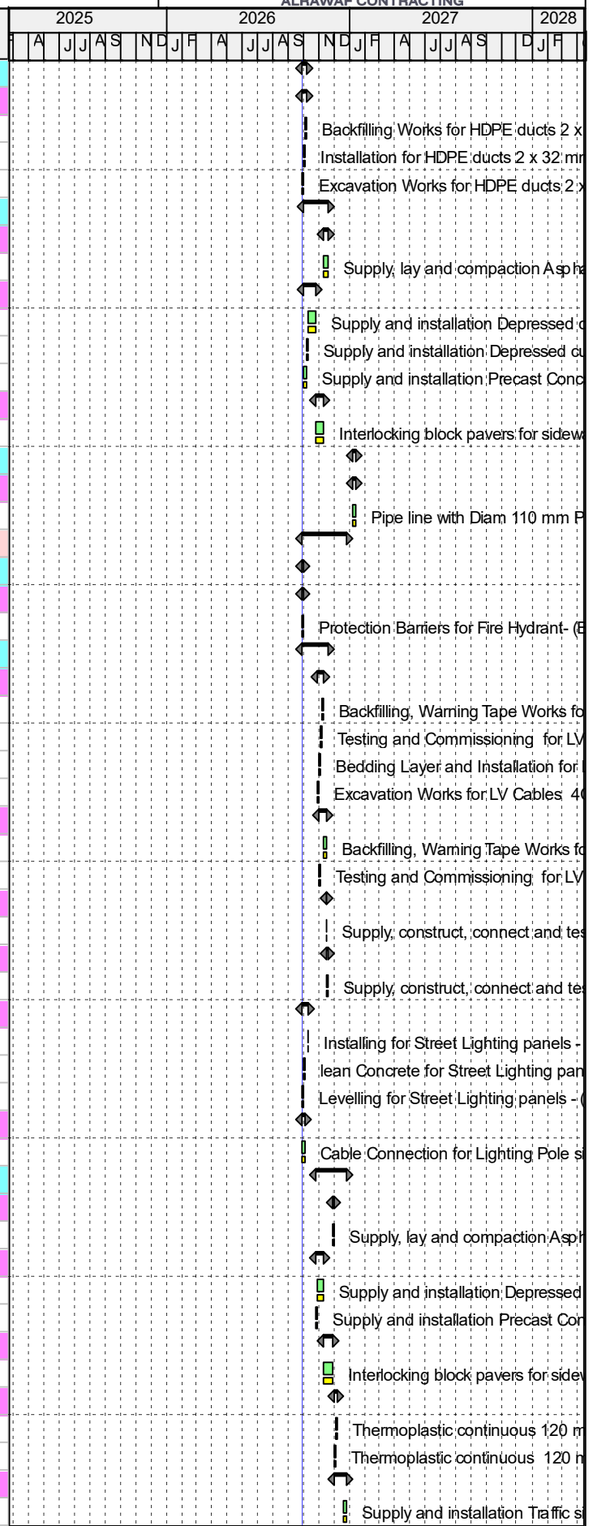


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Supply and installation Traffic sigr	14d	14d	08-Sep-26	24-Sep-26	03-Dec-26	20-Dec-26	338d	1	100%	0%	45,781
R14		122d	122d	23-Jun-26	13-Oct-26	29-Sep-26	17-Feb-27	322d	54	93.97%	0%	3,100,712
JDH3-02-009-R14-Catch Basins (Ston		10d	10d	08-Jul-26	01-Aug-26	29-Sep-26	10-Oct-26	434d	4	100%	0%	39,262
JDH3-02-009-R14-(ST)-Single Catcl		10d	10d	21-Jul-26	01-Aug-26	29-Sep-26	10-Oct-26	434d	2	100%	0%	16,848
	Steel Coverfor single Catch Basin	5d	5d	27-Jul-26	01-Aug-26	05-Oct-26	10-Oct-26	434d	1	100%	0%	5,616
	Finishing and Insulation Works fo	5d	5d	21-Jul-26	26-Jul-26	29-Sep-26	04-Oct-26	434d	1	100%	0%	11,232
JDH3-02-009-R14-(ST)-Double Catc		4d	4d	08-Jul-26	12-Jul-26	29-Sep-26	03-Oct-26	435d	2	100%	0%	22,414
	Steel Coverfor double Catch Basi	2d	2d	11-Jul-26	12-Jul-26	01-Oct-26	03-Oct-26	435d	1	100%	0%	7,471
	Finishing and Insulation Works fo	2d	2d	08-Jul-26	09-Jul-26	29-Sep-26	30-Sep-26	435d	1	100%	0%	14,942
JDH3-02-009-R14-TSE Network - TSE		8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	306d	6	100%	0%	91,453
JDH3-02-009-R14-(TSE)-Butterfly V		4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	306d	2	100%	0%	48,390
	Stem & Surface box for Butterfly '	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	306d	1	100%	0%	4,839
	Installation for Butterfly Valve 300	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	306d	1	100%	0%	43,551
JDH3-02-009-R14-(TSE)-Valve Chai		8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	306d	4	100%	0%	43,064
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	306d	1	100%	0%	8,613
	Installationfor Butterfly Valve Chai	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	306d	1	100%	0%	23,685
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	306d	1	100%	0%	4,306
	Excavation+Bedding for Butterfly	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	306d	1	100%	0%	6,460
JDH3-02-009-R14-Potable Water Netw		10d	10d	30-Jun-26	25-Jul-26	29-Sep-26	11-Oct-26	434d	7	100%	0%	123,903
JDH3-02-009-R14-(WT)-Butterfly Va		2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	419d	1	100%	0%	7,822
	Stem & Surface box for Butterfly '	2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	419d	1	100%	0%	7,822
JDH3-02-009-R14-(WT)-Valve Chan		2d	2d	02-Jul-26	04-Jul-26	03-Oct-26	05-Oct-26	419d	1	100%	0%	8,601
	Backfilling Worksfor Butterfly Valv	2d	2d	02-Jul-26	04-Jul-26	03-Oct-26	05-Oct-26	419d	1	100%	0%	8,601
JDH3-02-009-R14-(WT)-Fire Hydran		10d	10d	14-Jul-26	25-Jul-26	29-Sep-26	11-Oct-26	434d	5	100%	0%	107,479
	Protection Barriers for Fire Hydran	2d	2d	23-Jul-26	25-Jul-26	08-Oct-26	11-Oct-26	434d	1	100%	0%	5,374
	Fire Installation for Fire Hydrant- (I	2d	2d	21-Jul-26	22-Jul-26	06-Oct-26	08-Oct-26	434d	1	100%	0%	37,618
	Stem for Fire Hydrant- (B3.33 14	2d	2d	19-Jul-26	20-Jul-26	04-Oct-26	06-Oct-26	434d	1	100%	0%	32,244
	Valve Installation for Fire Hydrant-	2d	2d	16-Jul-26	18-Jul-26	01-Oct-26	04-Oct-26	434d	1	100%	0%	21,496
	Excavation and Bedding and Pipe	2d	2d	14-Jul-26	15-Jul-26	29-Sep-26	01-Oct-26	434d	1	100%	0%	10,748
JDH3-02-009-R14-Electrical Network		10d	10d	02-Jul-26	13-Jul-26	21-Oct-26	01-Nov-26	295d	3	100%	0%	137,319
JDH3-02-009-R14-(EL)-MV cables /		2d	2d	09-Jul-26	11-Jul-26	28-Oct-26	29-Oct-26	295d	1	100%	0%	134,929
	Installing for MV Cables AL/XLPE	2d	2d	09-Jul-26	11-Jul-26	28-Oct-26	29-Oct-26	295d	1	100%	0%	134,929
JDH3-02-009-R14-(EL)-MV cable tr		10d	10d	02-Jul-26	13-Jul-26	21-Oct-26	01-Nov-26	295d	2	100%	0%	2,390
	Backfilling + Warning Tape for MV	2d	2d	12-Jul-26	13-Jul-26	31-Oct-26	01-Nov-26	295d	1	100%	0%	956
	Excavation for MV Cable Trench	6d	6d	02-Jul-26	08-Jul-26	21-Oct-26	27-Oct-26	295d	1	100%	0%	1,434
JDH3-02-009-R14-Street Lighting Netv		57d	57d	27-Jun-26	15-Aug-26	29-Sep-26	03-Dec-26	387d	22	100%	0%	265,636
JDH3-02-009-R14-(SL)- LV Cables -		8d	8d	14-Jul-26	22-Jul-26	02-Nov-26	10-Nov-26	311d	4	100%	0%	1,141
	Backfilling, Warning Tape Works f	2d	2d	21-Jul-26	22-Jul-26	09-Nov-26	10-Nov-26	311d	1	100%	0%	114
	Testing and Commissioning for L	2d	2d	19-Jul-26	20-Jul-26	07-Nov-26	08-Nov-26	311d	1	100%	0%	57
	Bedding Layer and Installation fo	2d	2d	16-Jul-26	18-Jul-26	04-Nov-26	05-Nov-26	311d	1	100%	0%	855
	Excavation Works for LV Cables	2d	2d	14-Jul-26	15-Jul-26	02-Nov-26	03-Nov-26	295d	1	100%	0%	114
JDH3-02-009-R14-(SL)-Lighting Pol		26d	26d	16-Jul-26	15-Aug-26	04-Nov-26	03-Dec-26	295d	5	100%	0%	131,320
	Cable Connection for Lighting Po	4d	4d	11-Aug-26	15-Aug-26	30-Nov-26	03-Dec-26	295d	1	100%	0%	6,566
	Installation Works for Lighting Pol	4d	4d	23-Jul-26	27-Jul-26	11-Nov-26	15-Nov-26	297d	1	100%	0%	85,358
	Backfilling of RC foundation for Li	2d	2d	21-Jul-26	22-Jul-26	09-Nov-26	10-Nov-26	297d	1	100%	0%	13,132
	Installation of RC foundation for L	2d	2d	19-Jul-26	20-Jul-26	07-Nov-26	08-Nov-26	297d	1	100%	0%	13,132
	Excavation for RC foundation for	2d	2d	16-Jul-26	18-Jul-26	04-Nov-26	05-Nov-26	297d	1	100%	0%	13,132
JDH3-02-009-R14-(SL)-Street Lighti		6d	6d	30-Jul-26	05-Aug-26	18-Nov-26	24-Nov-26	297d	2	100%	0%	51,232
	Cable Connection for Lighting(LE	3d	3d	03-Aug-26	05-Aug-26	22-Nov-26	24-Nov-26	297d	1	100%	0%	10,246
	Installation for Lighting(LED) Lur	3d	3d	30-Jul-26	02-Aug-26	18-Nov-26	21-Nov-26	297d	1	100%	0%	40,986
JDH3-02-009-R14-(SL)-Earthing Sy		2d	2d	09-Aug-26	10-Aug-26	28-Nov-26	29-Nov-26	295d	1	100%	0%	1,703
	Supply, construct, connect and te	2d	2d	09-Aug-26	10-Aug-26	28-Nov-26	29-Nov-26	295d	1	100%	0%	1,703
JDH3-02-009-R14-(SL)-Road Cross		8d	8d	27-Jun-26	05-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	2,161

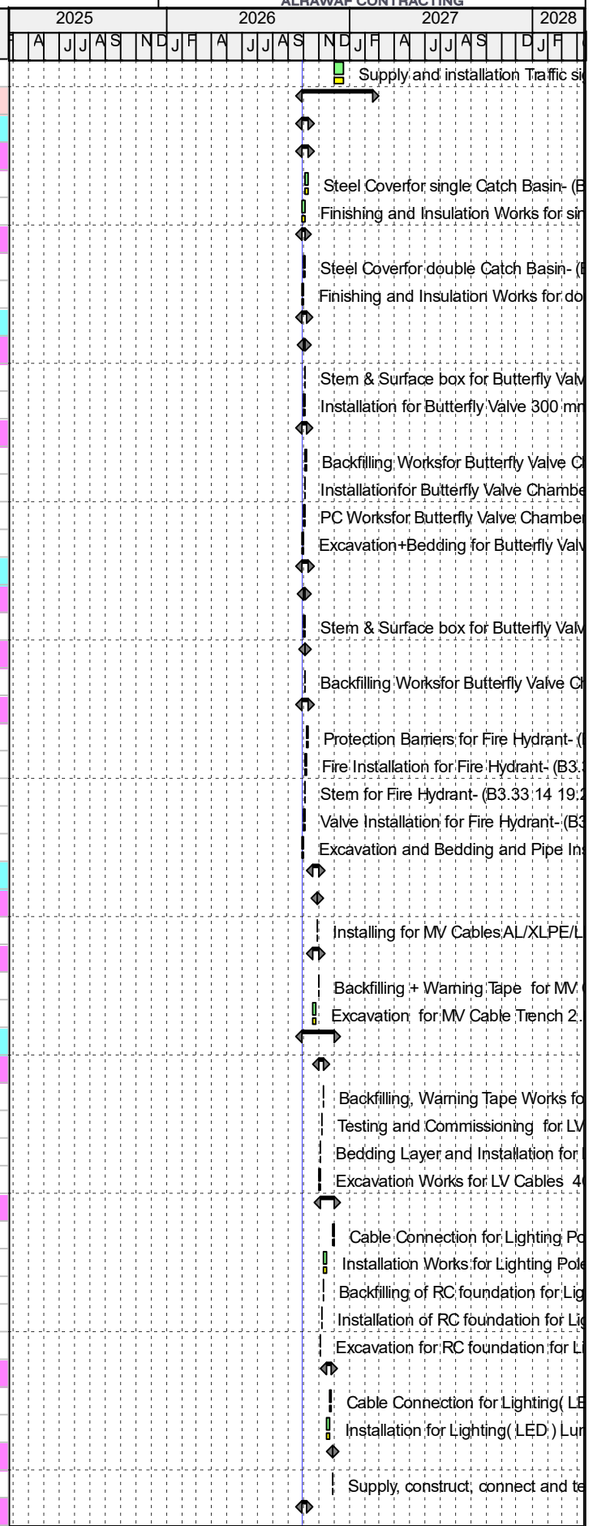


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Testing and Backfilling Works for I	2d	2d	04-Jul-26	05-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	108
	Pouring Concrete Cover for PVC I	2d	2d	01-Jul-26	02-Jul-26	04-Oct-26	05-Oct-26	332d	1	100%	0%	324
	Installation for PVC Pipes 2×100r	2d	2d	29-Jun-26	30-Jun-26	01-Oct-26	03-Oct-26	332d	1	100%	0%	1,297
	Excavation Works for PVC Pipes	2d	2d	27-Jun-26	28-Jun-26	29-Sep-26	30-Sep-26	324d	1	100%	0%	432
	JDH3-02-009-R14-(SL)- LV Cables -	2d	2d	28-Jul-26	29-Jul-26	16-Nov-26	17-Nov-26	297d	1	100%	0%	1,431
	Installation for LV Cables 3x1Cx5	2d	2d	28-Jul-26	29-Jul-26	16-Nov-26	17-Nov-26	297d	1	100%	0%	1,431
	JDH3-02-009-R14-(SL)- LV Cables -	2d	2d	28-Jul-26	29-Jul-26	16-Nov-26	17-Nov-26	297d	1	100%	0%	4,276
	Installation for LV Cables 3-1xCx	2d	2d	28-Jul-26	29-Jul-26	16-Nov-26	17-Nov-26	297d	1	100%	0%	4,276
	JDH3-02-009-R14-(SL)- LV Cables -	20d	20d	16-Jul-26	08-Aug-26	04-Nov-26	26-Nov-26	295d	4	100%	0%	72,371
	Backfilling, Warning Tape Works f	5d	5d	03-Aug-26	08-Aug-26	22-Nov-26	26-Nov-26	295d	1	100%	0%	7,237
	Testing and Commissioning for L	5d	5d	28-Jul-26	02-Aug-26	16-Nov-26	21-Nov-26	295d	1	100%	0%	3,619
	Bedding Layer and Installation fo	5d	5d	22-Jul-26	27-Jul-26	10-Nov-26	15-Nov-26	295d	1	100%	0%	54,279
	Excavation Works for LV Cables	5d	5d	16-Jul-26	21-Jul-26	04-Nov-26	09-Nov-26	295d	1	100%	0%	7,237
	JDH3-02-009-R14-Road Works - RD	98d	98d	01-Jul-26	05-Oct-26	30-Sep-26	23-Jan-27	307d	4	98.23%	0%	2,155,505
	JDH3-02-009-R14-(RD)-Bituminous	5d	5d	01-Jul-26	06-Jul-26	30-Sep-26	06-Oct-26	372d	1	100%	0%	1,898,605
	Supply, lay and Asphaltic base cc	5d	5d	01-Jul-26	06-Jul-26	30-Sep-26	06-Oct-26	372d	1	100%	0%	1,898,605
	JDH3-02-009-R14-(RD)-Precast Cor	28d	28d	02-Sep-26	05-Oct-26	22-Dec-26	23-Jan-27	307d	3	85.18%	0%	256,899
	Supply and installation Depresse	12d	12d	21-Sep-26	05-Oct-26	10-Jan-27	23-Jan-27	307d	1	50%	0%	76,142
	Supply and installation Depresse	4d	4d	16-Sep-26	20-Sep-26	05-Jan-27	09-Jan-27	307d	1	100%	0%	6,186
	Supply and installation Precast C	12d	12d	02-Sep-26	15-Sep-26	22-Dec-26	04-Jan-27	307d	1	100%	0%	174,572
	JDH3-02-009-R14-Landscape Works -	35d	35d	02-Sep-26	13-Oct-26	09-Jan-27	17-Feb-27	280d	8	48.21%	0%	287,634
	JDH3-02-009-R14-(LS)-Miscellanec	17d	17d	24-Sep-26	13-Oct-26	30-Jan-27	17-Feb-27	280d	3	24.44%	0%	169,666
	Concrete heel kerb - PV6- (B7.32	17d	17d	24-Sep-26	13-Oct-26	30-Jan-27	17-Feb-27	280d	1	23.53%	0%	143,408
	200 x 100 x 60 mm Precast Conc	12d	12d	24-Sep-26	07-Oct-26	30-Jan-27	11-Feb-27	280d	1	33.33%	0%	15,797
	200 x 100 x 60 mm Precast Conc	17d	17d	24-Sep-26	13-Oct-26	30-Jan-27	17-Feb-27	280d	1	23.53%	0%	10,461
	JDH3-02-009-R14-(LS)-HDPE for Se	24d	24d	02-Sep-26	30-Sep-26	09-Jan-27	04-Feb-27	280d	5	82.39%	0%	117,968
	Pipe linefor Diam 32 mm PN10 -	6d	6d	24-Sep-26	30-Sep-26	30-Jan-27	04-Feb-27	280d	1	66.67%	0%	62,319
	Pipe linefor Diam 50 mm PN10 -	7d	7d	15-Sep-26	22-Sep-26	21-Jan-27	28-Jan-27	280d	1	100%	0%	35,405
	Pipe linefor Diam 63 mm PN10 -	5d	5d	09-Sep-26	14-Sep-26	16-Jan-27	20-Jan-27	280d	1	100%	0%	16,521
	Pipe linefor Diam 75 mm PN10 -	3d	3d	06-Sep-26	08-Sep-26	12-Jan-27	14-Jan-27	280d	1	100%	0%	939
	Pipe line with Diam 90 mm PN10	3d	3d	02-Sep-26	05-Sep-26	09-Jan-27	11-Jan-27	280d	1	100%	0%	2,784
Z1		70d	70d	23-Jun-26	07-Oct-26	29-Sep-26	19-Dec-26	375d	189	99.05%	0%	1,981,190
R01		10d	10d	25-Jun-26	07-Oct-26	29-Sep-26	10-Oct-26	434d	31	99.48%	0%	210,198
	JDH3-02-009-R01-Storm Network - ST	8d	8d	21-Jul-26	15-Aug-26	29-Sep-26	07-Oct-26	430d	5	100%	0%	3,913
	JDH3-02-009-R01-(ST)-MH Works (	2d	2d	06-Aug-26	08-Aug-26	29-Sep-26	30-Sep-26	430d	1	100%	0%	1,402
	Steel Coverfor MH 1200 mm - de	2d	2d	06-Aug-26	08-Aug-26	29-Sep-26	30-Sep-26	430d	1	100%	0%	1,402
	JDH3-02-009-R01-(ST)-MH Works (	2d	2d	09-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	485
	Steel Coverfor MH 1200 mm - de	2d	2d	09-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	485
	JDH3-02-009-R01-(ST)-MH Works (	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	1,003
	Steel Coverfor MH 1500 mm - de	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	1,003
	JDH3-02-009-R01-(ST)-MH Works (	2d	2d	21-Jul-26	22-Jul-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	625
	Steel Coverfor MH 1500 mm - de	2d	2d	21-Jul-26	22-Jul-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	625
	JDH3-02-009-R01-(ST)-MH Works (	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	397
	Steel Coverfor MH 1200 mm - de	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	397
	JDH3-02-009-R01-TSE Network - TSE	3d	3d	09-Jul-26	08-Aug-26	29-Sep-26	03-Oct-26	439d	2	100%	0%	8,968
	JDH3-02-009-R01-(TSE)-Butterfly V	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	3,226
	Stem & Surface box for Butterfly '	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	3,226
	JDH3-02-009-R01-(TSE)-Valve Chai	2d	2d	06-Aug-26	08-Aug-26	30-Sep-26	03-Oct-26	439d	1	100%	0%	5,742
	Backfilling Worksfor Butterfly Valv	2d	2d	06-Aug-26	08-Aug-26	30-Sep-26	03-Oct-26	439d	1	100%	0%	5,742
	JDH3-02-009-R01-Potable Water Netw	10d	10d	25-Jun-26	15-Jul-26	29-Sep-26	10-Oct-26	434d	20	100%	0%	192,167
	JDH3-02-009-R01-(WT)-Butterfly Va	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	404d	1	100%	0%	9,863
	Stem & Surface box for Butterfly '	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	404d	1	100%	0%	9,863
	JDH3-02-009-R01-(WT)-Wash-Out V	4d	4d	02-Jul-26	06-Jul-26	29-Sep-26	03-Oct-26	404d	2	100%	0%	39,083

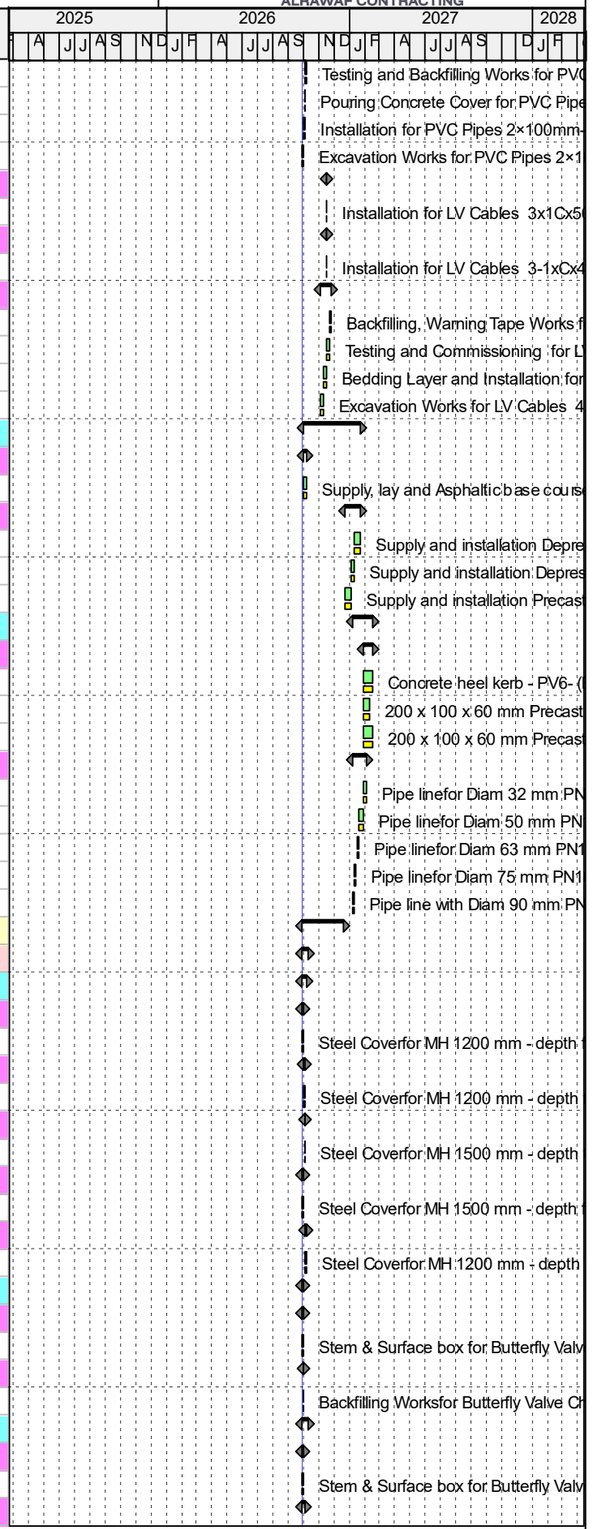


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Stem & Surface box for Wash-Ou	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	404d	1	100%	0%	3,908
	Installation for Wash-Out Valve 1!	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	404d	1	100%	0%	35,175
	JDH3-02-009-R01-(WT)-Air Valve-6!	4d	4d	05-Jul-26	08-Jul-26	01-Oct-26	05-Oct-26	404d	2	100%	0%	17,978
	Stem & Surface box for Air Valve	2d	2d	07-Jul-26	08-Jul-26	04-Oct-26	05-Oct-26	404d	1	100%	0%	1,798
	Installation for Air Valve 65 mm or	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	404d	1	100%	0%	16,180
	JDH3-02-009-R01-(WT)-Valve Cham	2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	437d	1	100%	0%	7,344
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jun-26	01-Jul-26	30-Sep-26	03-Oct-26	437d	1	100%	0%	7,344
	JDH3-02-009-R01-(WT)-Wash-Out C	8d	8d	25-Jun-26	04-Jul-26	29-Sep-26	07-Oct-26	434d	4	100%	0%	54,422
	Backfilling Worksfor Wash-Out Ch	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	10,884
	Installationfor Wash-Out Chambe	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	29,932
	PC Worksfor Wash-Out Chamber	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	5,442
	Excavation+Bedding for Wash-Ou	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	8,163
	JDH3-02-009-R01-(WT)-Air Valve Ch	8d	8d	28-Jun-26	15-Jul-26	01-Oct-26	10-Oct-26	434d	4	100%	0%	7,139
	Backfilling Worksfor Air Valve Cha	2d	2d	14-Jul-26	15-Jul-26	08-Oct-26	10-Oct-26	434d	1	100%	0%	1,428
	Installationfor Air Valve Chamber	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	3,926
	PC Worksfor Air Valve Chamber o	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	714
	Excavation+Bedding for Air Valve	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	1,071
	JDH3-02-009-R01-(WT)-Fire Hydrar	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,443
	Protection Barriers for Fire Hydrar	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,443
	JDH3-02-009-R01-(WT)-Butterfly Va	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	1,613
	Stem & Surface box for Butterfly '	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	1,613
	JDH3-02-009-R01-(WT)-Butterfly Va	2d	2d	07-Jul-26	08-Jul-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	13,151
	Stem & Surface box for Butterfly '	2d	2d	07-Jul-26	08-Jul-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	13,151
	JDH3-02-009-R01-(WT)-Valve Cham	2d	2d	02-Jul-26	04-Jul-26	30-Sep-26	03-Oct-26	439d	1	100%	0%	2,867
	Backfilling Worksfor Butterfly Valv	2d	2d	02-Jul-26	04-Jul-26	30-Sep-26	03-Oct-26	439d	1	100%	0%	2,867
	JDH3-02-009-R01-(WT)-Valve Cham	2d	2d	09-Jul-26	11-Jul-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	12,798
	Backfilling Worksfor Butterfly Valv	2d	2d	09-Jul-26	11-Jul-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	12,798
	JDH3-02-009-R01-(WT)-Butterfly Va	2d	2d	11-Jul-26	12-Jul-26	30-Sep-26	03-Oct-26	433d	1	100%	0%	23,467
	Installation for Butterfly Valve 400	2d	2d	11-Jul-26	12-Jul-26	30-Sep-26	03-Oct-26	433d	1	100%	0%	23,467
	JDH3-02-009-R01-Street Lighting Netv	4d	4d	02-Sep-26	07-Oct-26	29-Sep-26	03-Oct-26	438d	2	64.44%	0%	3,099
	JDH3-02-009-R01-(SL)- Street Ligh	4d	4d	02-Sep-26	07-Oct-26	29-Sep-26	03-Oct-26	438d	2	64.44%	0%	3,099
	lean Concrete for Street Lighting	2d	2d	20-Sep-26	07-Oct-26	01-Oct-26	03-Oct-26	438d	1	46.67%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	02-Sep-26	19-Sep-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	1,033
	JDH3-02-009-R01-Telecommunicatior	4d	4d	30-Jul-26	03-Aug-26	29-Sep-26	03-Oct-26	360d	2	100%	0%	2,051
	JDH3-02-009-R01-(TEL)-Manhole T	2d	2d	30-Jul-26	01-Aug-26	29-Sep-26	30-Sep-26	360d	1	100%	0%	1,367
	Backfilling Works for MH Type 1 D	2d	2d	30-Jul-26	01-Aug-26	29-Sep-26	30-Sep-26	360d	1	100%	0%	1,367
	JDH3-02-009-R01-(TEL)-Manhole T	2d	2d	02-Aug-26	03-Aug-26	01-Oct-26	03-Oct-26	360d	1	100%	0%	684
	Backfilling Works for MH Type 2 D	2d	2d	02-Aug-26	03-Aug-26	01-Oct-26	03-Oct-26	360d	1	100%	0%	684
R02		56d	56d	23-Jun-26	15-Sep-26	29-Sep-26	02-Dec-26	388d	37	100%	0%	457,766
	JDH3-02-009-R02-Potable Water Netv	12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	13	100%	0%	116,265
	JDH3-02-009-R02-(WT)-Air Valve-5(	4d	4d	30-Jun-26	04-Jul-26	06-Oct-26	10-Oct-26	432d	2	100%	0%	6,490
	Stem & Surface box for Air Valve	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	649
	Installation for Air Valve 50 mm or	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	5,841
	JDH3-02-009-R02-(WT)-Air Valve Ch	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	7,139
	Backfilling Worksfor Air Valve Cha	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	1,428
	Installationfor Air Valve Chamber	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	3,926
	PC Worksfor Air Valve Chamber o	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	714
	Excavation+Bedding for Air Valve	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	432d	1	100%	0%	1,071
	JDH3-02-009-R02-(WT)-Fire Hydrar	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	4,885
	Protection Barriers for Fire Hydrar	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	4,885
	JDH3-02-009-R02-(WT)-Butterfly Va	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	438d	2	100%	0%	65,754
	Stem & Surface box for Butterfly '	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	6,575
	Installation for Butterfly Valve 800	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	59,179

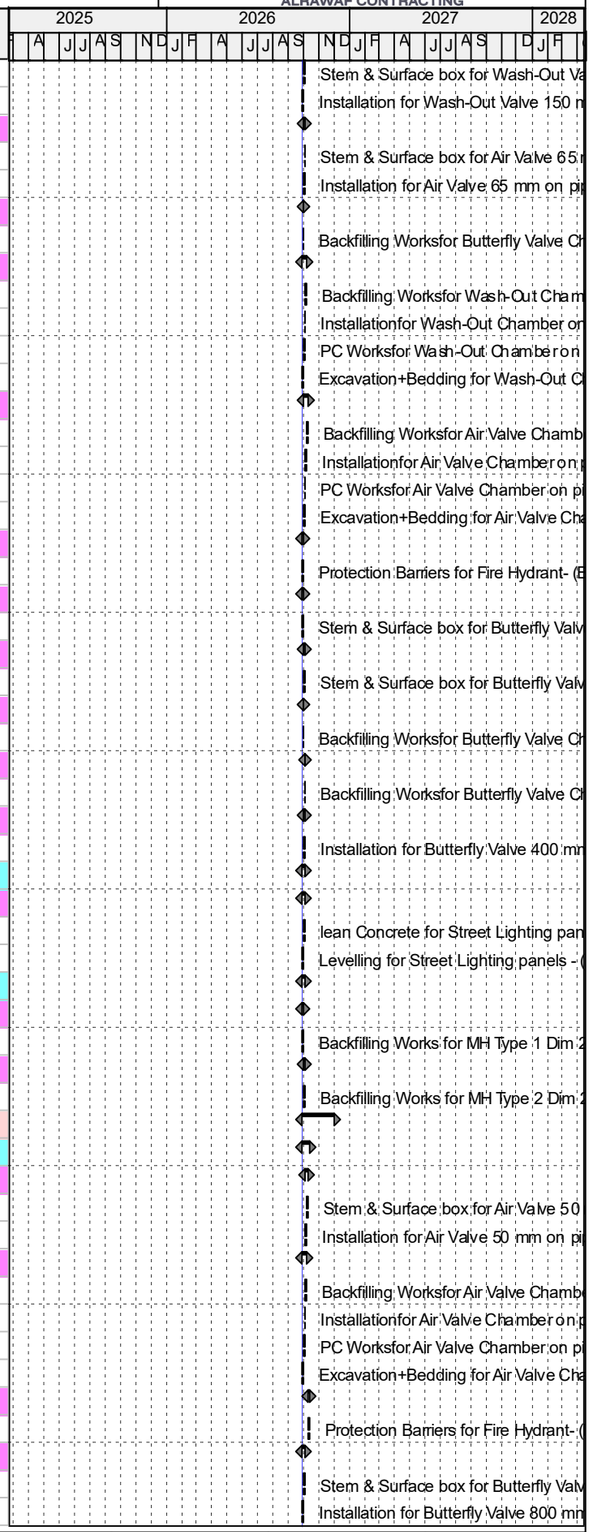


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R02-(WT)-Valve Chan	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	31,996
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	6,399
	Installationfor Butterfly Valve Cha	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	17,598
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	3,200
	Excavation+Bedding for Butterfly	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	4,799
	JDH3-02-009-R02-Electrical Network	6d	6d	05-Jul-26	19-Jul-26	29-Sep-26	05-Oct-26	388d	3	100%	0%	68,946
	JDH3-02-009-R02-(EL)-RMU 33 KV	6d	6d	05-Jul-26	19-Jul-26	29-Sep-26	05-Oct-26	388d	3	100%	0%	68,946
	Earthing + Primary Test for RMU 3	2d	2d	18-Jul-26	19-Jul-26	04-Oct-26	05-Oct-26	388d	1	100%	0%	4,925
	Cables Connection for RMU 33 K'	2d	2d	07-Jul-26	08-Jul-26	01-Oct-26	03-Oct-26	388d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.2(	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	388d	1	100%	0%	59,096
	JDH3-02-009-R02-Street Lighting Netv	30d	30d	20-Jul-26	23-Aug-26	06-Oct-26	09-Nov-26	388d	15	100%	0%	144,871
	JDH3-02-009-R02-(SL)- LV Cables -	8d	8d	20-Jul-26	04-Aug-26	06-Oct-26	14-Oct-26	400d	4	100%	0%	37,974
	Backfilling, Warning Tape Works f	2d	2d	03-Aug-26	04-Aug-26	13-Oct-26	14-Oct-26	400d	1	100%	0%	3,797
	Testing and Commissioning for L	2d	2d	01-Aug-26	02-Aug-26	11-Oct-26	12-Oct-26	400d	1	100%	0%	1,899
	Bedding Layer and Installation fo	2d	2d	29-Jul-26	30-Jul-26	08-Oct-26	10-Oct-26	400d	1	100%	0%	28,480
	Excavation Works for LV Cables	2d	2d	20-Jul-26	21-Jul-26	06-Oct-26	07-Oct-26	388d	1	100%	0%	3,797
	JDH3-02-009-R02-(SL)- LV Cables -	24d	24d	22-Jul-26	18-Aug-26	08-Oct-26	04-Nov-26	388d	4	100%	0%	85,014
	Backfilling, Warning Tape Works f	6d	6d	12-Aug-26	18-Aug-26	29-Oct-26	04-Nov-26	388d	1	100%	0%	8,501
	Testing and Commissioning for L	6d	6d	05-Aug-26	11-Aug-26	22-Oct-26	28-Oct-26	388d	1	100%	0%	4,251
	Bedding Layer and Installation fo	6d	6d	29-Jul-26	04-Aug-26	15-Oct-26	21-Oct-26	388d	1	100%	0%	63,761
	Excavation Works for LV Cables	6d	6d	22-Jul-26	28-Jul-26	08-Oct-26	14-Oct-26	388d	1	100%	0%	8,501
	JDH3-02-009-R02-(SL)- LV Cables -	2d	2d	09-Aug-26	10-Aug-26	08-Oct-26	10-Oct-26	408d	1	100%	0%	4,134
	Installation for LV Cables 3-1xCx	2d	2d	09-Aug-26	10-Aug-26	08-Oct-26	10-Oct-26	408d	1	100%	0%	4,134
	JDH3-02-009-R02-(SL)-Lighting Pol	6d	6d	09-Aug-26	15-Aug-26	08-Oct-26	14-Oct-26	406d	1	100%	0%	5,440
	Cable Connection for Lighting Po	6d	6d	09-Aug-26	15-Aug-26	08-Oct-26	14-Oct-26	406d	1	100%	0%	5,440
	JDH3-02-009-R02-(SL)-Earthing Sy	2d	2d	22-Aug-26	23-Aug-26	08-Nov-26	09-Nov-26	388d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	22-Aug-26	23-Aug-26	08-Nov-26	09-Nov-26	388d	1	100%	0%	1,126
	JDH3-02-009-R02-(SL)-Earthing Sy	2d	2d	19-Aug-26	20-Aug-26	05-Nov-26	07-Nov-26	388d	1	100%	0%	852
	Supply, construct, connect and te	2d	2d	19-Aug-26	20-Aug-26	05-Nov-26	07-Nov-26	388d	1	100%	0%	852
	JDH3-02-009-R02-(SL)- Street Ligh	6d	6d	26-Jul-26	18-Aug-26	08-Oct-26	14-Oct-26	408d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	17-Aug-26	18-Aug-26	13-Oct-26	14-Oct-26	408d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	15-Aug-26	16-Aug-26	11-Oct-26	12-Oct-26	408d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	26-Jul-26	27-Jul-26	08-Oct-26	10-Oct-26	408d	1	100%	0%	1,033
	JDH3-02-009-R02-Telecommunicatior	56d	56d	28-Jun-26	15-Sep-26	29-Sep-26	02-Dec-26	388d	6	100%	0%	127,684
	JDH3-02-009-R02-(TEL)-Unreinforc	20d	20d	24-Aug-26	15-Sep-26	10-Nov-26	02-Dec-26	388d	4	100%	0%	123,582
	Backfilling Works for Duct 6-ways	3d	3d	13-Sep-26	15-Sep-26	30-Nov-26	02-Dec-26	388d	1	100%	0%	12,358
	Pouring PC Concrete Cover for D	7d	7d	05-Sep-26	12-Sep-26	22-Nov-26	29-Nov-26	388d	1	100%	0%	24,716
	Installation for Duct 6-ways ducts,	7d	7d	27-Aug-26	03-Sep-26	14-Nov-26	21-Nov-26	388d	1	100%	0%	67,970
	Excavation Works for Duct 6-ways	3d	3d	24-Aug-26	26-Aug-26	10-Nov-26	12-Nov-26	388d	1	100%	0%	18,537
	JDH3-02-009-R02-(TEL)-Manhole T	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,735
	Backfilling Works for MH Type 1 D	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,735
	JDH3-02-009-R02-(TEL)-Manhole T	2d	2d	30-Jun-26	01-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,367
	Backfilling Works for MH Type 2 D	2d	2d	30-Jun-26	01-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,367
R03		70d	70d	25-Jun-26	04-Oct-26	29-Sep-26	19-Dec-26	375d	60	97.72%	0%	773,311
	JDH3-02-009-R03-Potable Water Netv	14d	14d	25-Jun-26	11-Jul-26	29-Sep-26	14-Oct-26	430d	13	100%	0%	131,172
	JDH3-02-009-R03-(WT)-Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	Protection Barriers for Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R03-(WT)-Butterfly Va	4d	4d	02-Jul-26	06-Jul-26	06-Oct-26	10-Oct-26	430d	2	100%	0%	65,754
	Stem & Surface box for Butterfly '	2d	2d	05-Jul-26	06-Jul-26	08-Oct-26	10-Oct-26	430d	1	100%	0%	6,575
	Installation for Butterfly Valve 800	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	59,179
	JDH3-02-009-R03-(WT)-Wash-Out V	6d	6d	05-Jul-26	11-Jul-26	08-Oct-26	14-Oct-26	430d	2	100%	0%	7,673
	Stem & Surface box for Wash-Ou	2d	2d	09-Jul-26	11-Jul-26	13-Oct-26	14-Oct-26	430d	1	100%	0%	767
	Installation for Wash-Out Valve 1(	2d	2d	05-Jul-26	06-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	6,906

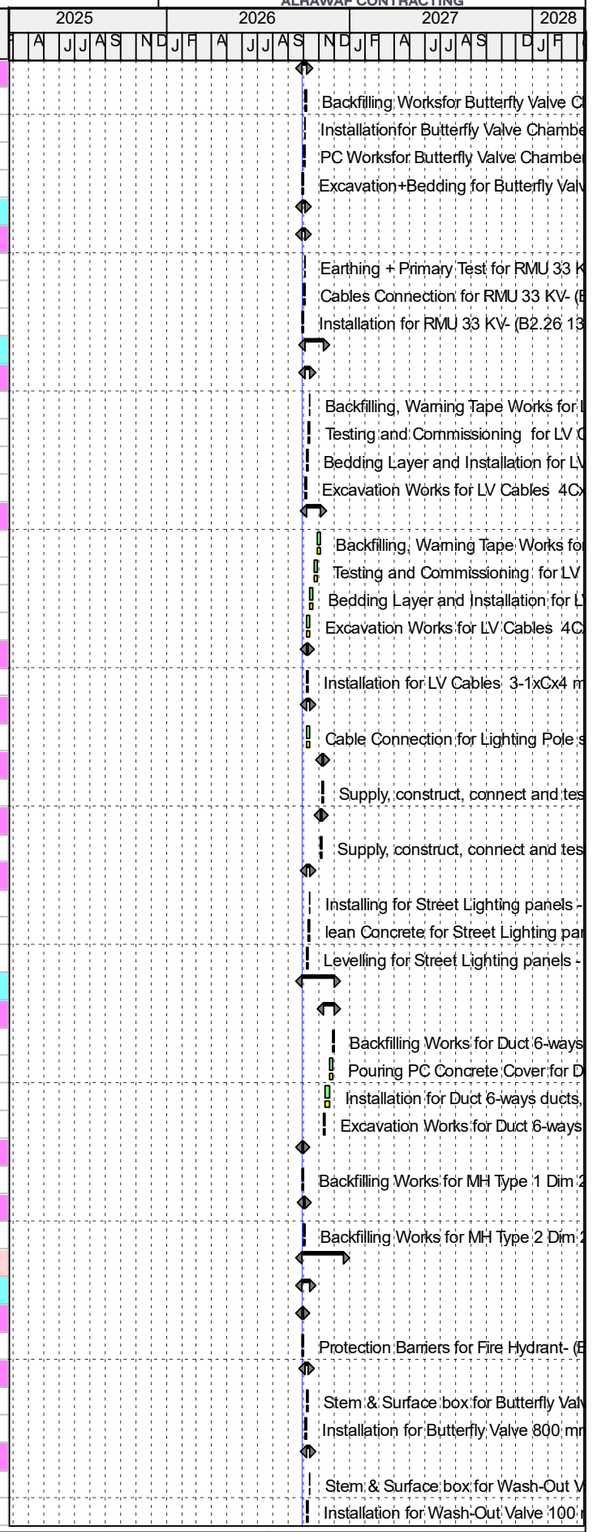


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R03-(WT)-Valve Chan	8d	8d	25-Jun-26	04-Jul-26	29-Sep-26	07-Oct-26	432d	4	100%	0%	31,996
	Backfilling Worksfor Butterfly Valv	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	6,399
	Installationfor Butterfly Valve Cha	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	17,598
	PC Worksfor Butterfly Valve Chan	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	3,200
	Excavation+Bedding for Butterfly	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	430d	1	100%	0%	4,799
	JDH3-02-009-R03-(WT)-Wash-Out C	10d	10d	28-Jun-26	08-Jul-26	01-Oct-26	12-Oct-26	430d	4	100%	0%	20,864
	Backfilling Worksfor Wash-Out Ch	2d	2d	07-Jul-26	08-Jul-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	4,173
	Installationfor Wash-Out Chambe	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	11,475
	PC Worksfor Wash-Out Chamber	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	2,086
	Excavation+Bedding for Wash-Ou	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	3,130
	JDH3-02-009-R03-Electrical Network	13d	13d	15-Jul-26	28-Jul-26	29-Sep-26	13-Oct-26	319d	6	100%	0%	86,800
	JDH3-02-009-R03-(EL)-MV cable tr	6d	6d	18-Jul-26	23-Jul-26	01-Oct-26	08-Oct-26	319d	1	100%	0%	3,992
	Backfilling + Warning Tape for MV	6d	6d	18-Jul-26	23-Jul-26	01-Oct-26	08-Oct-26	319d	1	100%	0%	3,992
	JDH3-02-009-R03-(EL)-RMU 33 KV	13d	13d	18-Jul-26	28-Jul-26	29-Sep-26	13-Oct-26	319d	3	100%	0%	68,946
	Earthing + Primary Test for RMU 3	2d	2d	27-Jul-26	28-Jul-26	11-Oct-26	13-Oct-26	319d	1	100%	0%	4,925
	Cables Connection for RMU 33 K'	2d	2d	20-Jul-26	21-Jul-26	01-Oct-26	03-Oct-26	325d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.26	2d	2d	18-Jul-26	19-Jul-26	29-Sep-26	30-Sep-26	325d	1	100%	0%	59,096
	JDH3-02-009-R03-(EL)-MV cables A	10d	10d	15-Jul-26	26-Jul-26	29-Sep-26	11-Oct-26	319d	2	100%	0%	13,862
	Termination for MV Cables 3Cx40	2d	2d	25-Jul-26	26-Jul-26	08-Oct-26	11-Oct-26	319d	1	100%	0%	5,160
	Installing Joints for MV Cables 3C	2d	2d	15-Jul-26	16-Jul-26	29-Sep-26	01-Oct-26	319d	1	100%	0%	8,701
	JDH3-02-009-R03-Street Lighting Netv	53d	53d	29-Jul-26	13-Sep-26	29-Sep-26	29-Nov-26	319d	36	100%	0%	440,013
	JDH3-02-009-R03-(SL)-Lighting Uni	36d	36d	22-Aug-26	27-Aug-26	29-Sep-26	09-Nov-26	323d	3	100%	0%	47,612
	Earthing + Primary Test for Unit su	2d	2d	26-Aug-26	27-Aug-26	07-Nov-26	09-Nov-26	323d	1	100%	0%	3,401
	Cables Connection for Unit substa	2d	2d	24-Aug-26	25-Aug-26	01-Oct-26	03-Oct-26	352d	1	100%	0%	3,401
	Installation for Unit substation 33/	2d	2d	22-Aug-26	23-Aug-26	29-Sep-26	30-Sep-26	352d	1	100%	0%	40,810
	JDH3-02-009-R03-(SL)-RMU 33 KV	40d	40d	20-Aug-26	01-Sep-26	29-Sep-26	14-Nov-26	323d	3	100%	0%	58,823
	Earthing + Primary Test for RMU 3	2d	2d	31-Aug-26	01-Sep-26	11-Nov-26	14-Nov-26	323d	1	100%	0%	4,202
	Cables Connection for RMU 33 K'	2d	2d	23-Aug-26	24-Aug-26	01-Oct-26	03-Oct-26	356d	1	100%	0%	4,202
	Installation for RMU 33 KV- (B2.26	2d	2d	20-Aug-26	22-Aug-26	29-Sep-26	30-Sep-26	356d	1	100%	0%	50,420
	JDH3-02-009-R03-(SL)- LV Cables -	21d	21d	29-Jul-26	22-Aug-26	13-Oct-26	07-Nov-26	323d	4	100%	0%	1,212
	Backfilling, Warning Tape Works f	2d	2d	20-Aug-26	22-Aug-26	04-Nov-26	07-Nov-26	323d	1	100%	0%	121
	Testing and Commissioning for L	2d	2d	18-Aug-26	19-Aug-26	02-Nov-26	04-Nov-26	323d	1	100%	0%	61
	Bedding Layer and Installation fo	2d	2d	16-Aug-26	17-Aug-26	31-Oct-26	02-Nov-26	323d	1	100%	0%	909
	Excavation Works for LV Cables	2d	2d	29-Jul-26	30-Jul-26	13-Oct-26	15-Oct-26	319d	1	100%	0%	121
	JDH3-02-009-R03-(SL)- LV Cables -	18d	18d	06-Aug-26	30-Aug-26	21-Oct-26	11-Nov-26	323d	4	100%	0%	86,797
	Backfilling, Warning Tape Works f	2d	2d	29-Aug-26	30-Aug-26	09-Nov-26	11-Nov-26	323d	1	100%	0%	8,680
	Testing and Commissioning for L	2d	2d	11-Aug-26	12-Aug-26	26-Oct-26	28-Oct-26	333d	1	100%	0%	4,340
	Bedding Layer and Installation fo	2d	2d	09-Aug-26	10-Aug-26	24-Oct-26	26-Oct-26	333d	1	100%	0%	65,098
	Excavation Works for LV Cables	2d	2d	06-Aug-26	08-Aug-26	21-Oct-26	24-Oct-26	319d	1	100%	0%	8,680
	JDH3-02-009-R03-(SL)- LV Cables -	2d	2d	26-Aug-26	27-Aug-26	04-Oct-26	05-Oct-26	354d	1	100%	0%	1,520
	Installation for LV Cables 3x1Cx5	2d	2d	26-Aug-26	27-Aug-26	04-Oct-26	05-Oct-26	354d	1	100%	0%	1,520
	JDH3-02-009-R03-(SL)- LV Cables -	20d	20d	01-Aug-26	23-Aug-26	15-Oct-26	08-Nov-26	332d	4	100%	0%	77,298
	Backfilling, Warning Tape Works f	5d	5d	18-Aug-26	23-Aug-26	02-Nov-26	08-Nov-26	332d	1	100%	0%	7,730
	Testing and Commissioning for L	5d	5d	12-Aug-26	17-Aug-26	27-Oct-26	02-Nov-26	332d	1	100%	0%	3,865
	Bedding Layer and Installation fo	5d	5d	06-Aug-26	11-Aug-26	21-Oct-26	27-Oct-26	332d	1	100%	0%	57,974
	Excavation Works for LV Cables	5d	5d	01-Aug-26	05-Aug-26	15-Oct-26	21-Oct-26	319d	1	100%	0%	7,730
	JDH3-02-009-R03-(SL)- LV Cables -	2d	2d	26-Aug-26	27-Aug-26	10-Nov-26	12-Nov-26	319d	1	100%	0%	4,134
	Installation for LV Cables 3-1xCx	2d	2d	26-Aug-26	27-Aug-26	10-Nov-26	12-Nov-26	319d	1	100%	0%	4,134
	JDH3-02-009-R03-(SL)-Lighting Pol	24d	24d	09-Aug-26	08-Sep-26	24-Oct-26	21-Nov-26	323d	5	100%	0%	108,808
	Cable Connection for Lighting Po	6d	6d	02-Sep-26	08-Sep-26	14-Nov-26	21-Nov-26	323d	1	100%	0%	5,440
	Installation Works for Lighting Pol	6d	6d	19-Aug-26	25-Aug-26	03-Nov-26	10-Nov-26	319d	1	100%	0%	70,725
	Backfilling of RC foundation for Li	3d	3d	16-Aug-26	18-Aug-26	31-Oct-26	03-Nov-26	319d	1	100%	0%	10,881
	Installation of RC foundation for L	3d	3d	12-Aug-26	15-Aug-26	27-Oct-26	31-Oct-26	319d	1	100%	0%	10,881

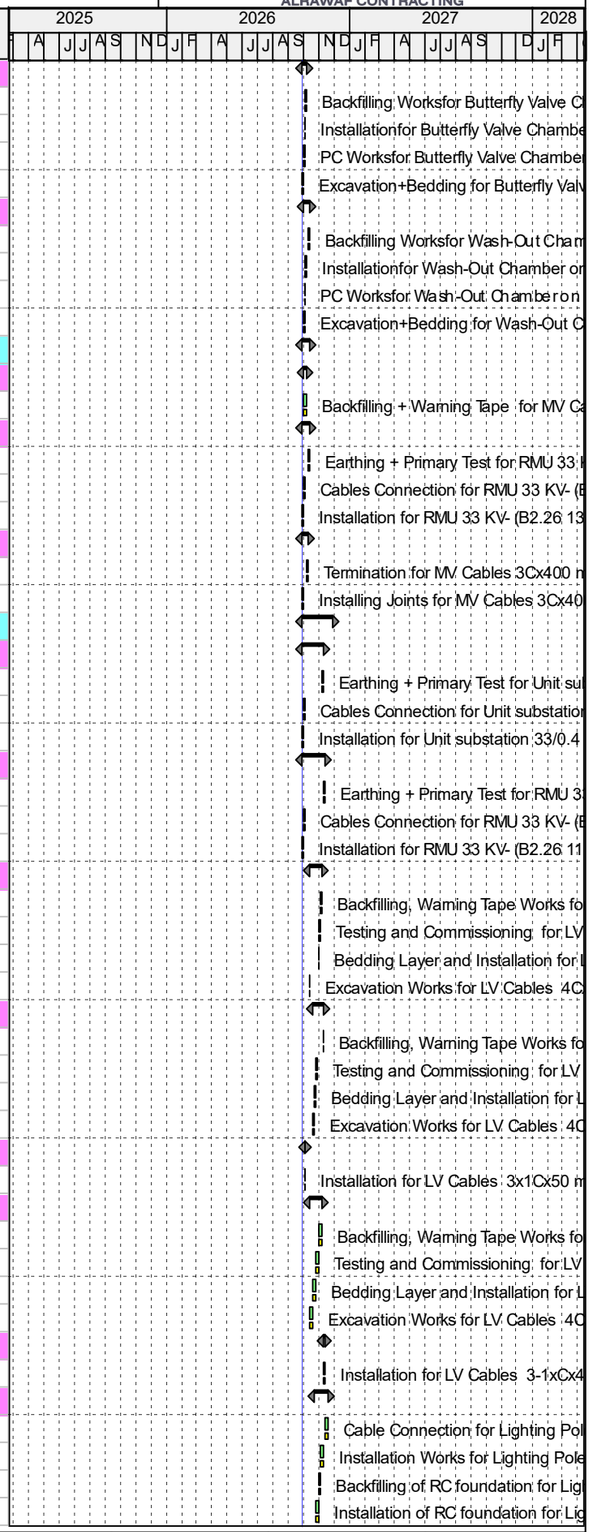


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Excavation for RC foundation for	3d	3d	09-Aug-26	11-Aug-26	24-Oct-26	27-Oct-26	319d	1	100%	0%	10,881
	JDH3-02-009-R03-(SL)-Street Lighti	6d	6d	29-Aug-26	03-Sep-26	12-Nov-26	19-Nov-26	322d	2	100%	0%	16,557
	Cable Connection for Lighting(LE	3d	3d	01-Sep-26	03-Sep-26	16-Nov-26	19-Nov-26	322d	1	100%	0%	3,311
	Installation for Lighting(LED) Lur	3d	3d	29-Aug-26	31-Aug-26	12-Nov-26	16-Nov-26	319d	1	100%	0%	13,246
	JDH3-02-009-R03-(SL)-Earthing Sy	3d	3d	10-Sep-26	13-Sep-26	25-Nov-26	29-Nov-26	319d	1	100%	0%	5,628
	Supply, construct, connect and te	3d	3d	10-Sep-26	13-Sep-26	25-Nov-26	29-Nov-26	319d	1	100%	0%	5,628
	JDH3-02-009-R03-(SL)-Earthing Sy	2d	2d	05-Sep-26	06-Sep-26	19-Nov-26	22-Nov-26	322d	1	100%	0%	852
	Supply, construct, connect and te	2d	2d	05-Sep-26	06-Sep-26	19-Nov-26	22-Nov-26	322d	1	100%	0%	852
	JDH3-02-009-R03-(SL)- Street Light	46d	46d	20-Aug-26	05-Sep-26	29-Sep-26	21-Nov-26	319d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	03-Sep-26	05-Sep-26	18-Nov-26	21-Nov-26	319d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	01-Sep-26	02-Sep-26	16-Nov-26	18-Nov-26	319d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	20-Aug-26	22-Aug-26	29-Sep-26	30-Sep-26	358d	1	100%	0%	1,033
	JDH3-02-009-R03-(SL)- LV Distribut	46d	46d	23-Aug-26	07-Sep-26	01-Oct-26	23-Nov-26	319d	3	100%	0%	18,369
	Installing for Street Lighting pane	2d	2d	06-Sep-26	07-Sep-26	21-Nov-26	23-Nov-26	319d	1	100%	0%	12,858
	lean Concrete for Street Lighting	2d	2d	25-Aug-26	26-Aug-26	04-Oct-26	05-Oct-26	358d	1	100%	0%	3,674
	Levelling for Street Lighting pane	2d	2d	23-Aug-26	24-Aug-26	01-Oct-26	03-Oct-26	358d	1	100%	0%	1,837
	JDH3-02-009-R03-(SL)-KWH meter	2d	2d	08-Sep-26	09-Sep-26	23-Nov-26	25-Nov-26	319d	1	100%	0%	2,072
	Installation for KWH meter - (B2.2	2d	2d	08-Sep-26	09-Sep-26	23-Nov-26	25-Nov-26	319d	1	100%	0%	2,072
	JDH3-02-009-R03-Telecommunicatior	70d	70d	09-Jul-26	04-Oct-26	29-Sep-26	19-Dec-26	375d	5	84.69%	0%	115,326
	JDH3-02-009-R03-(TEL)-Unreinforc	17d	17d	14-Sep-26	04-Oct-26	29-Nov-26	19-Dec-26	319d	3	84.13%	0%	111,224
	Pouring PC Concrete Cover for D	7d	7d	27-Sep-26	04-Oct-26	10-Dec-26	19-Dec-26	319d	1	28.57%	0%	24,716
	Installation for Duct 6-ways ducts,	7d	7d	17-Sep-26	26-Sep-26	02-Dec-26	10-Dec-26	319d	1	100%	0%	67,970
	Excavation Works for Duct 6-ways	3d	3d	14-Sep-26	16-Sep-26	29-Nov-26	02-Dec-26	319d	1	100%	0%	18,537
	JDH3-02-009-R03-(TEL)-Manhole T	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,735
	Backfilling Works for MH Type 1 D	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,735
	JDH3-02-009-R03-(TEL)-Manhole T	2d	2d	12-Jul-26	13-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,367
	Backfilling Works for MH Type 2 D	2d	2d	12-Jul-26	13-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,367
R04		10d	10d	25-Jun-26	10-Aug-26	29-Sep-26	10-Oct-26	434d	15	100%	0%	252,794
JDH3-02-009-R04-Potable Water Netw		10d	10d	25-Jun-26	13-Jul-26	29-Sep-26	10-Oct-26	434d	9	100%	0%	215,780
JDH3-02-009-R04-(WT)-Butterfly Va		4d	4d	02-Jul-26	06-Jul-26	06-Oct-26	10-Oct-26	434d	2	100%	0%	131,509
	Stem & Surface box for Butterfly '	2d	2d	05-Jul-26	06-Jul-26	08-Oct-26	10-Oct-26	434d	1	100%	0%	13,151
	Installation for Butterfly Valve 800	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	118,358
	JDH3-02-009-R04-(WT)-Butterfly Va	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	4,839
	Stem & Surface box for Butterfly '	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	4,839
	JDH3-02-009-R04-(WT)-Valve Chan	2d	2d	12-Jul-26	13-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	8,601
	Backfilling Worksfor Butterfly Valv	2d	2d	12-Jul-26	13-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	8,601
	JDH3-02-009-R04-(WT)-Fire Hydrar	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	6,840
	Protection Barriers for Fire Hydrar	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	6,840
	JDH3-02-009-R04-(WT)-Valve Chan	8d	8d	25-Jun-26	13-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	63,992
	Backfilling Worksfor Butterfly Valv	2d	2d	12-Jul-26	13-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	12,798
	Installationfor Butterfly Valve Cha	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	35,195
	PC Worksfor Butterfly Valve Chan	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	6,399
	Excavation+Bedding for Butterfly	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	9,599
JDH3-02-009-R04-TSE Network - TSE		8d	8d	09-Jul-26	10-Aug-26	29-Sep-26	07-Oct-26	436d	6	100%	0%	37,013
JDH3-02-009-R04-(TSE)-Wash-Out		4d	4d	09-Jul-26	13-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	16,127
	Stem & Surface box for Wash-Ou	2d	2d	12-Jul-26	13-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,613
	Installation for Wash-Out Valve 1(	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	14,515
JDH3-02-009-R04-(TSE)-Wash-Out		8d	8d	02-Aug-26	10-Aug-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	20,886
	Backfilling Worksfor Wash-Out Ch	2d	2d	09-Aug-26	10-Aug-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	4,177
	Installationfor Wash-Out Chambe	2d	2d	06-Aug-26	08-Aug-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	11,487
	PC Worksfor Wash-Out Chamber	2d	2d	04-Aug-26	05-Aug-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,089
	Excavation+Bedding for Wash-Ou	2d	2d	02-Aug-26	03-Aug-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	3,133
R05		8d	8d	23-Jun-26	22-Jul-26	29-Sep-26	07-Oct-26	436d	13	100%	0%	39,431

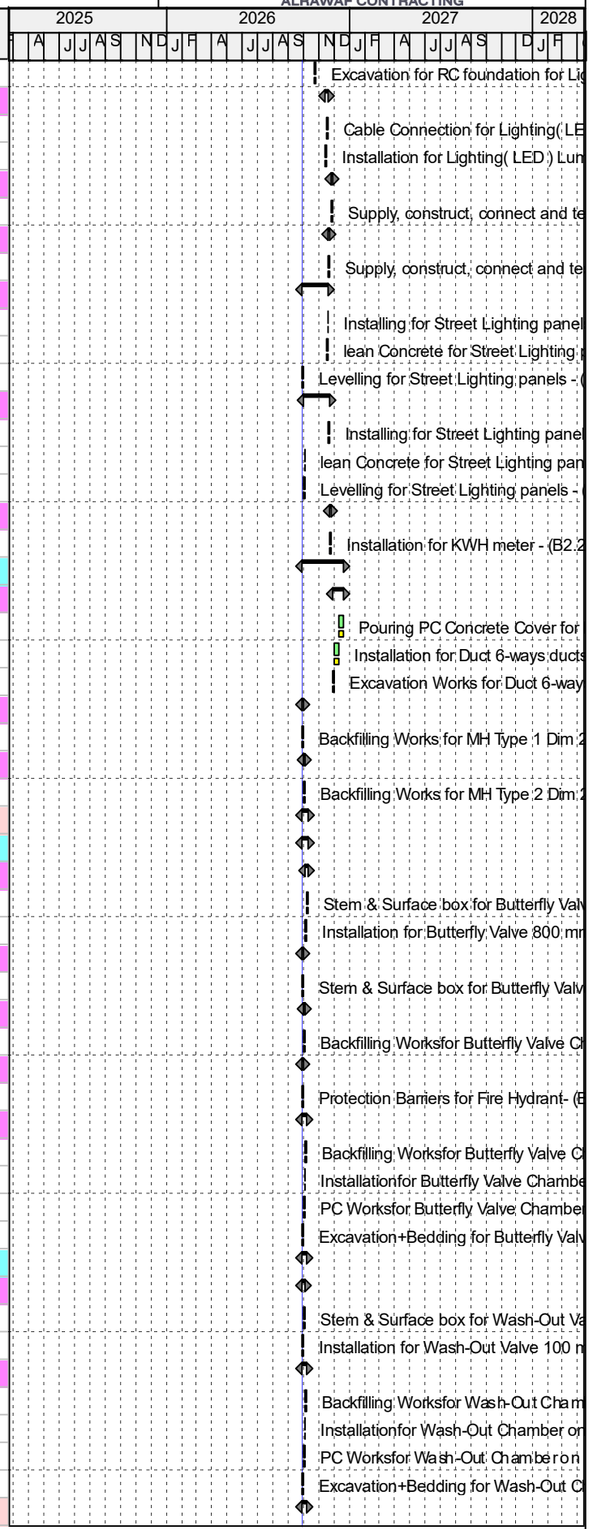


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R05-Potable Water Netw	8d	8d	23-Jun-26	06-Jul-26	29-Sep-26	07-Oct-26	436d	7	100%	0%	33,422
	JDH3-02-009-R05-(WT)-Wash-Out V	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	371d	2	100%	0%	7,673
	Stem & Surface box for Wash-Ou	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	371d	1	100%	0%	767
	Installation for Wash-Out Valve 1(	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	371d	1	100%	0%	6,906
	JDH3-02-009-R05-(WT)-Fire Hydrar	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	371d	1	100%	0%	4,885
	Protection Barriers for Fire Hydrar	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	371d	1	100%	0%	4,885
	JDH3-02-009-R05-(WT)-Wash-Out (	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	20,864
	Backfilling Worksfor Wash-Out Ch	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	4,173
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	11,475
	PC Worksfor Wash-Out Chamber	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,086
	Excavation+Bedding for Wash-Ou	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	3,130
	JDH3-02-009-R05-Telecommunicatior	8d	8d	12-Jul-26	22-Jul-26	29-Sep-26	07-Oct-26	436d	6	100%	0%	6,009
	JDH3-02-009-R05-(TEL)-Reinforcec	8d	8d	12-Jul-26	20-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	1,907
	Backfilling Works for RC Duct 6-w	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	191
	Pouring RC Concrete Cover for R	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	572
	Installation for RC Duct 6-ways du	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	858
	Excavation Works for RC Duct 6-v	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	422d	1	100%	0%	286
	JDH3-02-009-R05-(TEL)-Manhole T	2d	2d	19-Jul-26	20-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,735
	Backfilling Works for MH Type 1 D	2d	2d	19-Jul-26	20-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	2,735
	JDH3-02-009-R05-(TEL)-Manhole T	2d	2d	21-Jul-26	22-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,367
	Backfilling Works for MH Type 2 D	2d	2d	21-Jul-26	22-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,367
R06		25d	25d	25-Jun-26	27-Aug-26	29-Sep-26	27-Oct-26	419d	33	100%	0%	247,691
	JDH3-02-009-R06-Catch Basins (Stori	5d	5d	21-Jul-26	02-Aug-26	29-Sep-26	04-Oct-26	433d	2	100%	0%	23,966
	JDH3-02-009-R06-(ST)-Single Catcl	5d	5d	28-Jul-26	02-Aug-26	29-Sep-26	04-Oct-26	433d	1	100%	0%	10,684
	Finishing and Insulation Works fo	5d	5d	28-Jul-26	02-Aug-26	29-Sep-26	04-Oct-26	433d	1	100%	0%	10,684
	JDH3-02-009-R06-(ST)-Double Catc	2d	2d	21-Jul-26	22-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	13,282
	Finishing and Insulation Works fo	2d	2d	21-Jul-26	22-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	13,282
	JDH3-02-009-R06-TSE Network - TSE	8d	8d	25-Jun-26	15-Jul-26	29-Sep-26	08-Oct-26	435d	8	100%	0%	50,465
	JDH3-02-009-R06-(TSE)-Butterfly V	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	439d	1	100%	0%	4,839
	Stem & Surface box for Butterfly '	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	439d	1	100%	0%	4,839
	JDH3-02-009-R06-(TSE)-Wash-Out	4d	4d	25-Jun-26	29-Jun-26	29-Sep-26	04-Oct-26	439d	2	100%	0%	16,127
	Stem & Surface box for Wash-Ou	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	04-Oct-26	439d	1	100%	0%	1,613
	Installation for Wash-Out Valve 1(	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	439d	1	100%	0%	14,515
	JDH3-02-009-R06-(TSE)-Valve Chai	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	01-Oct-26	439d	1	100%	0%	8,613
	Backfilling Worksfor Butterfly Valv	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	01-Oct-26	439d	1	100%	0%	8,613
	JDH3-02-009-R06-(TSE)-Wash-Out	8d	8d	25-Jun-26	15-Jul-26	29-Sep-26	08-Oct-26	435d	4	100%	0%	20,886
	Backfilling Worksfor Wash-Out Ch	2d	2d	14-Jul-26	15-Jul-26	06-Oct-26	08-Oct-26	435d	1	100%	0%	4,177
	Installationfor Wash-Out Chambe	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	06-Oct-26	435d	1	100%	0%	11,487
	PC Worksfor Wash-Out Chamber	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	04-Oct-26	435d	1	100%	0%	2,089
	Excavation+Bedding for Wash-Ou	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	435d	1	100%	0%	3,133
	JDH3-02-009-R06-Potable Water Netw	8d	8d	25-Jun-26	11-Jul-26	29-Sep-26	07-Oct-26	436d	9	100%	0%	123,951
	JDH3-02-009-R06-(WT)-Butterfly Va	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	14,795
	Stem & Surface box for Butterfly '	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	14,795
	JDH3-02-009-R06-(WT)-Valve Chan	2d	2d	02-Jul-26	04-Jul-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	11,015
	Backfilling Worksfor Butterfly Valv	2d	2d	02-Jul-26	04-Jul-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	11,015
	JDH3-02-009-R06-(WT)-Fire Hydrar	8d	8d	02-Jul-26	11-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	79,144
	Protection Barriers for Fire Hydrar	2d	2d	09-Jul-26	11-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	4,397
	Fire Installation for Fire Hydrant- (	2d	2d	07-Jul-26	08-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	30,778
	Stem for Fire Hydrant- (B3.33 14	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	26,381
	Valve Installation for Fire Hydrant-	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	17,587
	JDH3-02-009-R06-(WT)-Butterfly Va	4d	4d	30-Jun-26	04-Jul-26	29-Sep-26	03-Oct-26	434d	2	100%	0%	16,130
	Stem & Surface box for Butterfly '	2d	2d	02-Jul-26	04-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	1,613
	Installation for Butterfly Valve 300	2d	2d	30-Jun-26	01-Jul-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	14,517

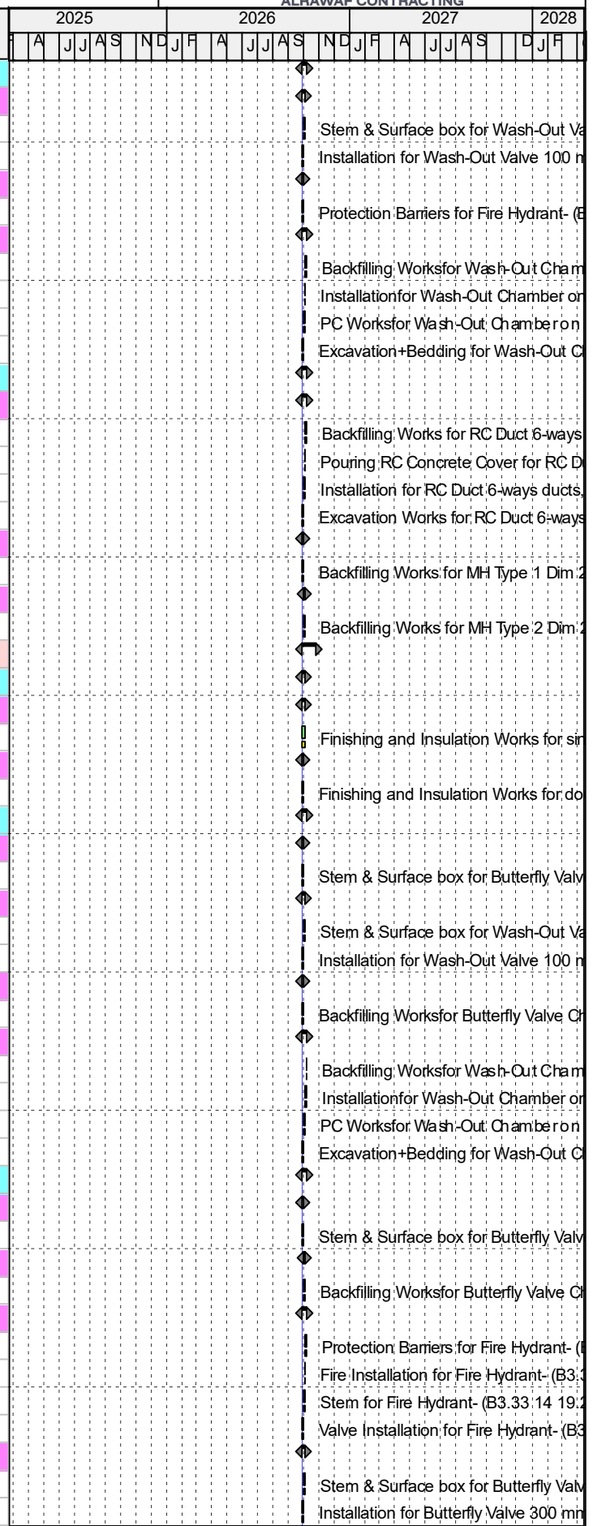


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R06-(WT)-Valve Chan	2d	2d	09-Jul-26	11-Jul-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	2,867
	Backfilling Worksfor Butterfly Valv	2d	2d	09-Jul-26	11-Jul-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	2,867
	JDH3-02-009-R06-Street Lighting Netv	16d	16d	19-Jul-26	17-Aug-26	29-Sep-26	17-Oct-26	334d	11	100%	0%	23,580
	JDH3-02-009-R06-(SL)- LV Cables -	8d	8d	19-Jul-26	27-Jul-26	29-Sep-26	07-Oct-26	334d	4	100%	0%	3,978
	Backfilling, Warning Tape Works f	2d	2d	26-Jul-26	27-Jul-26	06-Oct-26	07-Oct-26	334d	1	100%	0%	398
	Testing and Commissioning for L	2d	2d	23-Jul-26	25-Jul-26	04-Oct-26	05-Oct-26	334d	1	100%	0%	199
	Bedding Layer and Installation fo	2d	2d	21-Jul-26	22-Jul-26	01-Oct-26	03-Oct-26	334d	1	100%	0%	2,984
	Excavation Works for LV Cables	2d	2d	19-Jul-26	20-Jul-26	29-Sep-26	30-Sep-26	334d	1	100%	0%	398
	JDH3-02-009-R06-(SL)- LV Cables -	10d	10d	30-Jul-26	08-Aug-26	01-Oct-26	12-Oct-26	334d	2	100%	0%	7,293
	Backfilling, Warning Tape Works f	4d	4d	04-Aug-26	08-Aug-26	08-Oct-26	12-Oct-26	334d	1	100%	0%	4,862
	Testing and Commissioning for L	4d	4d	30-Jul-26	03-Aug-26	01-Oct-26	05-Oct-26	336d	1	100%	0%	2,431
	JDH3-02-009-R06-(SL)-Earthing Sy	2d	2d	16-Aug-26	17-Aug-26	15-Oct-26	17-Oct-26	334d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	16-Aug-26	17-Aug-26	15-Oct-26	17-Oct-26	334d	1	100%	0%	1,126
	JDH3-02-009-R06-(SL)-Earthing Sy	2d	2d	09-Aug-26	10-Aug-26	13-Oct-26	14-Oct-26	334d	1	100%	0%	852
	Supply, construct, connect and te	2d	2d	09-Aug-26	10-Aug-26	13-Oct-26	14-Oct-26	334d	1	100%	0%	852
	JDH3-02-009-R06-(SL)- Street Ligh	9d	9d	28-Jul-26	15-Aug-26	01-Oct-26	11-Oct-26	337d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	13-Aug-26	15-Aug-26	10-Oct-26	11-Oct-26	337d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	340d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	28-Jul-26	29-Jul-26	01-Oct-26	03-Oct-26	340d	1	100%	0%	1,033
	JDH3-02-009-R06-Telecommunicatior	9d	9d	18-Aug-26	27-Aug-26	18-Oct-26	27-Oct-26	334d	3	100%	0%	25,728
	JDH3-02-009-R06-(TEL)-Ducts	9d	9d	18-Aug-26	27-Aug-26	18-Oct-26	27-Oct-26	334d	3	100%	0%	25,728
	Backfilling Works for HDPE ducts	2d	2d	26-Aug-26	27-Aug-26	26-Oct-26	27-Oct-26	334d	1	100%	0%	2,573
	Installation for HDPE ducts 2 x 32	5d	5d	20-Aug-26	25-Aug-26	20-Oct-26	25-Oct-26	334d	1	100%	0%	19,296
	Excavation Works for HDPE ducts	2d	2d	18-Aug-26	19-Aug-26	18-Oct-26	19-Oct-26	334d	1	100%	0%	3,859
Z4		77d	77d	23-Jun-26	29-Sep-26	29-Sep-26	27-Dec-26	367d	180	99.95%	0%	2,337,829
R21		39d	39d	23-Jun-26	28-Sep-26	29-Sep-26	12-Nov-26	406d	65	100%	0%	616,381
	JDH3-02-009-R21-Sewage Network - S	8d	8d	01-Jul-26	19-Jul-26	30-Sep-26	08-Oct-26	435d	8	100%	0%	6,295
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	01-Jul-26	02-Jul-26	30-Sep-26	01-Oct-26	439d	1	100%	0%	485
	Steel Cover for MH 1200 mm - de	2d	2d	01-Jul-26	02-Jul-26	30-Sep-26	01-Oct-26	439d	1	100%	0%	485
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	04-Jul-26	05-Jul-26	03-Oct-26	04-Oct-26	439d	1	100%	0%	1,019
	Steel Cover for MH 1200 mm - de	2d	2d	04-Jul-26	05-Jul-26	03-Oct-26	04-Oct-26	439d	1	100%	0%	1,019
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	06-Jul-26	07-Jul-26	30-Sep-26	01-Oct-26	429d	1	100%	0%	667
	Steel Coverfor MH 1200 mm - de	2d	2d	06-Jul-26	07-Jul-26	30-Sep-26	01-Oct-26	429d	1	100%	0%	667
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	08-Jul-26	09-Jul-26	03-Oct-26	04-Oct-26	429d	1	100%	0%	783
	Steel Cover for MH 1200 mm - de	2d	2d	08-Jul-26	09-Jul-26	03-Oct-26	04-Oct-26	429d	1	100%	0%	783
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	11-Jul-26	12-Jul-26	30-Sep-26	01-Oct-26	441d	1	100%	0%	732
	Steel Cover for MH 1200 mm - de	2d	2d	11-Jul-26	12-Jul-26	30-Sep-26	01-Oct-26	441d	1	100%	0%	732
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	13-Jul-26	14-Jul-26	30-Sep-26	01-Oct-26	441d	1	100%	0%	852
	Steel Cover for MH 1200 mm - de	2d	2d	13-Jul-26	14-Jul-26	30-Sep-26	01-Oct-26	441d	1	100%	0%	852
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	15-Jul-26	16-Jul-26	05-Oct-26	06-Oct-26	429d	1	100%	0%	818
	Steel Cover for MH 1200 mm - de	2d	2d	15-Jul-26	16-Jul-26	05-Oct-26	06-Oct-26	429d	1	100%	0%	818
	JDH3-02-009-R21-(SW)-MH Works	2d	2d	18-Jul-26	19-Jul-26	07-Oct-26	08-Oct-26	429d	1	100%	0%	938
	Steel Cover for MH 1200 mm - de	2d	2d	18-Jul-26	19-Jul-26	07-Oct-26	08-Oct-26	429d	1	100%	0%	938
	JDH3-02-009-R21-Storm Network - ST	6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	438d	6	100%	0%	11,086
	JDH3-02-009-R21-(ST)-MH Works (	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	2,104
	Steel Coverfor MH 1200 mm - de	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	701
	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	1,402
	JDH3-02-009-R21-(ST)-MH Works (	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	436d	2	100%	0%	6,228
	Steel Coverfor MH 2000 mm - de	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,127
	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	4,101
	JDH3-02-009-R21-(ST)-MH Works (	4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	2,754
	Steel Coverfor MH 1500 mm - de	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	918
	Finishing, Benching, Testing Worl	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	1,836

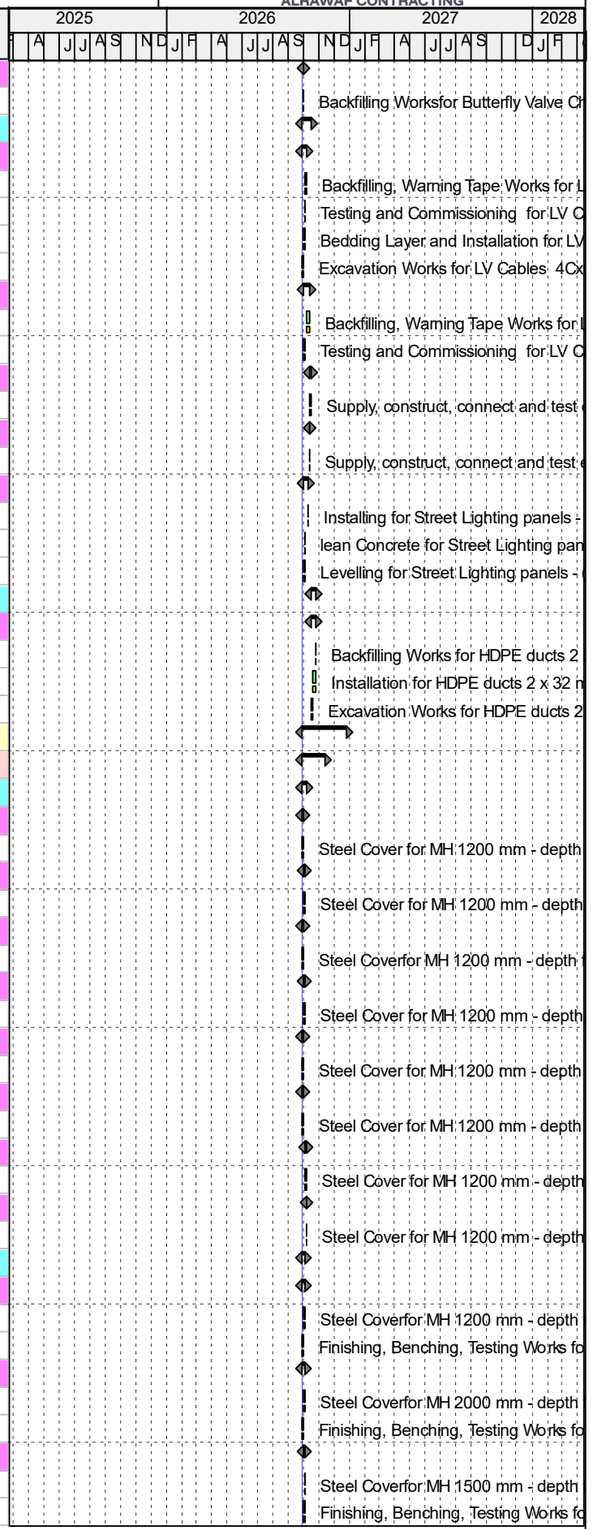


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R21-TSE Network - TSE	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	391d	6	100%	0%	35,502
	JDH3-02-009-R152-(TSE)-Wash-Ou	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	393d	2	100%	0%	14,564
	Stem & Surface box for Wash-Ou	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	393d	1	100%	0%	1,456
	Installation for Wash-Out Valve 1(	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	393d	1	100%	0%	13,108
	JDH3-02-009-R152-(TSE)-Wash-Ou	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	391d	4	100%	0%	20,938
	Backfilling Worksfor Wash-Out Ch	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	391d	1	100%	0%	4,188
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	391d	1	100%	0%	11,516
	PC Worksfor Wash-Out Chamber	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	391d	1	100%	0%	2,094
	Excavation+Bedding for Wash-Ou	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	391d	1	100%	0%	3,141
	JDH3-02-009-R21-Potable Water Netw	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R21-(WT)-Fire Hydrar	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	Protection Barriers for Fire Hydran	2d	2d	05-Jul-26	06-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,397
	JDH3-02-009-R21-Electrical Network	6d	6d	02-Aug-26	08-Aug-26	03-Oct-26	10-Oct-26	406d	3	100%	0%	68,946
	JDH3-02-009-R21-(EL)-RMU 33 KV	6d	6d	02-Aug-26	08-Aug-26	03-Oct-26	10-Oct-26	406d	3	100%	0%	68,946
	Earthing + Primary Test for RMU 3	2d	2d	06-Aug-26	08-Aug-26	07-Oct-26	10-Oct-26	406d	1	100%	0%	4,925
	Cables Connection for RMU 33 K'	2d	2d	04-Aug-26	05-Aug-26	05-Oct-26	07-Oct-26	406d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.2(	2d	2d	02-Aug-26	03-Aug-26	03-Oct-26	05-Oct-26	406d	1	100%	0%	59,096
	JDH3-02-009-R21-Street Lighting Netv	29d	29d	09-Aug-26	10-Sep-26	10-Oct-26	12-Nov-26	406d	32	100%	0%	360,784
	JDH3-02-009-R21-(SL)-Earthing Sy	2d	2d	31-Aug-26	01-Sep-26	01-Nov-26	03-Nov-26	412d	1	100%	0%	852
	Supply, construct, connect and te	2d	2d	31-Aug-26	01-Sep-26	01-Nov-26	03-Nov-26	412d	1	100%	0%	852
	JDH3-02-009-R21-(SL)-Lighting Uni	25d	25d	16-Aug-26	10-Sep-26	14-Oct-26	12-Nov-26	406d	3	100%	0%	47,612
	Earthing + Primary Test for Unit su	2d	2d	09-Sep-26	10-Sep-26	10-Nov-26	12-Nov-26	406d	1	100%	0%	3,401
	Cables Connection for Unit substa	2d	2d	18-Aug-26	19-Aug-26	17-Oct-26	19-Oct-26	411d	1	100%	0%	3,401
	Installation for Unit substation 33/	2d	2d	16-Aug-26	17-Aug-26	14-Oct-26	17-Oct-26	411d	1	100%	0%	40,810
	JDH3-02-009-R21-(SL)- LV Cables -	23d	23d	13-Aug-26	08-Sep-26	14-Oct-26	10-Nov-26	406d	4	100%	0%	113,017
	Backfilling, Warning Tape Works f	3d	3d	06-Sep-26	08-Sep-26	07-Nov-26	10-Nov-26	406d	1	100%	0%	11,302
	Testing and Commissioning for L	3d	3d	20-Aug-26	23-Aug-26	21-Oct-26	25-Oct-26	417d	1	100%	0%	5,651
	Bedding Layer and Installation fo	3d	3d	17-Aug-26	19-Aug-26	18-Oct-26	21-Oct-26	417d	1	100%	0%	84,763
	Excavation Works for LV Cables	3d	3d	13-Aug-26	16-Aug-26	14-Oct-26	18-Oct-26	407d	1	100%	0%	11,302
	JDH3-02-009-R21-(SL)- LV Cables -	2d	2d	20-Aug-26	22-Aug-26	19-Oct-26	21-Oct-26	411d	1	100%	0%	1,431
	Installation for LV Cables 3x1Cx5	2d	2d	20-Aug-26	22-Aug-26	19-Oct-26	21-Oct-26	411d	1	100%	0%	1,431
	JDH3-02-009-R21-(SL)- LV Cables -	12d	12d	17-Aug-26	30-Aug-26	18-Oct-26	01-Nov-26	407d	4	100%	0%	41,554
	Backfilling, Warning Tape Works f	3d	3d	27-Aug-26	30-Aug-26	28-Oct-26	01-Nov-26	407d	1	100%	0%	4,155
	Testing and Commissioning for L	3d	3d	24-Aug-26	26-Aug-26	25-Oct-26	28-Oct-26	407d	1	100%	0%	2,078
	Bedding Layer and Installation fo	3d	3d	20-Aug-26	23-Aug-26	21-Oct-26	25-Oct-26	407d	1	100%	0%	31,166
	Excavation Works for LV Cables	3d	3d	17-Aug-26	19-Aug-26	18-Oct-26	21-Oct-26	407d	1	100%	0%	4,155
	JDH3-02-009-R21-(SL)- LV Cables -	2d	2d	20-Aug-26	22-Aug-26	21-Oct-26	24-Oct-26	406d	1	100%	0%	2,423
	Installation for LV Cables 3-1xCx	2d	2d	20-Aug-26	22-Aug-26	21-Oct-26	24-Oct-26	406d	1	100%	0%	2,423
	JDH3-02-009-R21-(SL)-Lighting Pol	14d	14d	09-Aug-26	24-Aug-26	10-Oct-26	26-Oct-26	412d	5	100%	0%	63,784
	Cable Connection for Lighting Po	4d	4d	20-Aug-26	24-Aug-26	21-Oct-26	26-Oct-26	412d	1	100%	0%	3,189
	Installation Works for Lighting Pol	4d	4d	16-Aug-26	19-Aug-26	17-Oct-26	21-Oct-26	406d	1	100%	0%	41,460
	Backfilling of RC foundation for Li	2d	2d	13-Aug-26	15-Aug-26	14-Oct-26	17-Oct-26	406d	1	100%	0%	6,378
	Installation of RC foundation for L	2d	2d	11-Aug-26	12-Aug-26	12-Oct-26	14-Oct-26	406d	1	100%	0%	6,378
	Excavation for RC foundation for	2d	2d	09-Aug-26	10-Aug-26	10-Oct-26	12-Oct-26	406d	1	100%	0%	6,378
	JDH3-02-009-R21-(SL)-Street Light	9d	9d	23-Aug-26	01-Sep-26	24-Oct-26	03-Nov-26	407d	2	100%	0%	9,706
	Cable Connection for Lighting(LE	2d	2d	31-Aug-26	01-Sep-26	01-Nov-26	03-Nov-26	407d	1	100%	0%	1,941
	Installation for Lighting(LED) Lur	2d	2d	23-Aug-26	24-Aug-26	24-Oct-26	26-Oct-26	406d	1	100%	0%	7,765
	JDH3-02-009-R21-(SL)- LV Distribut	14d	14d	18-Aug-26	29-Aug-26	14-Oct-26	31-Oct-26	406d	3	100%	0%	18,369
	Installing for Street Lighting pane	2d	2d	27-Aug-26	29-Aug-26	28-Oct-26	31-Oct-26	406d	1	100%	0%	12,858
	lean Concrete for Street Lighting	2d	2d	25-Aug-26	26-Aug-26	26-Oct-26	28-Oct-26	406d	1	100%	0%	3,674
	Levelling for Street Lighting pane	2d	2d	18-Aug-26	19-Aug-26	14-Oct-26	17-Oct-26	414d	1	100%	0%	1,837
	JDH3-02-009-R21-(SL)-KWH meter	2d	2d	30-Aug-26	31-Aug-26	31-Oct-26	02-Nov-26	406d	1	100%	0%	2,072
	Installation for KWH meter - (B2.2	2d	2d	30-Aug-26	31-Aug-26	31-Oct-26	02-Nov-26	406d	1	100%	0%	2,072

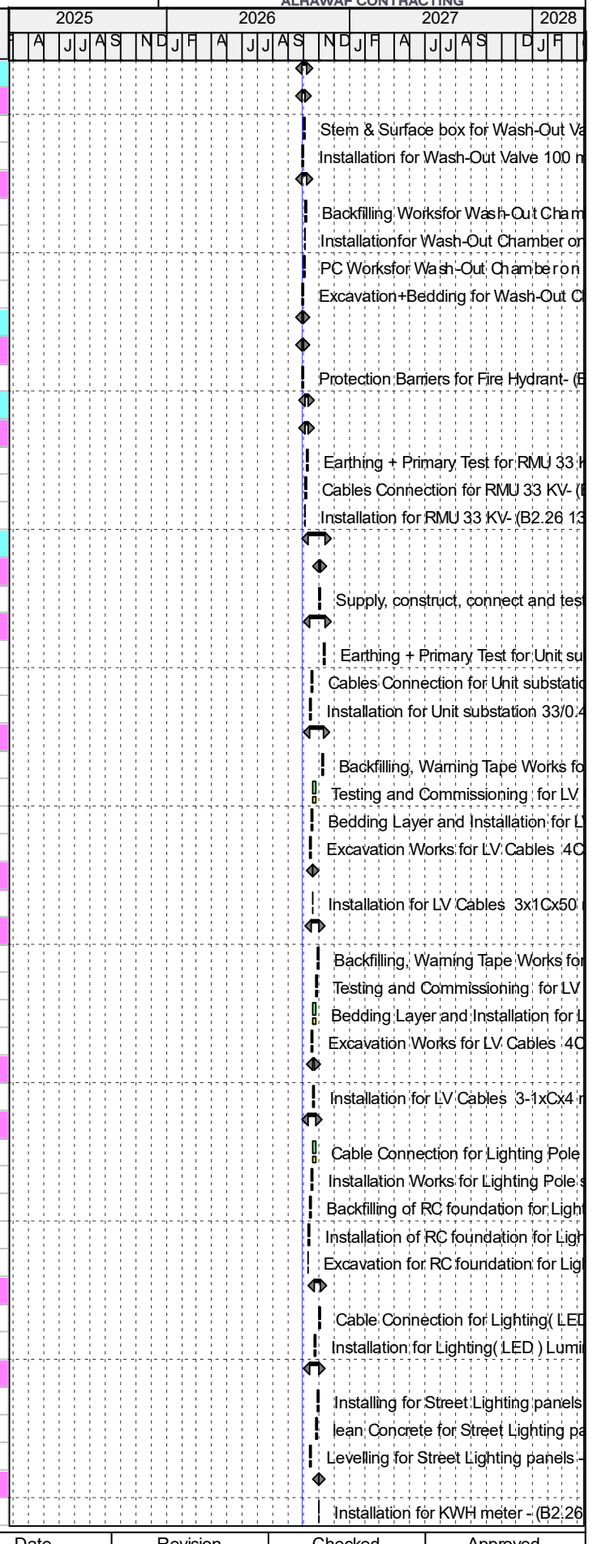

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R21-(SL)- LV Cables -	22d	22d	11-Aug-26	05-Sep-26	12-Oct-26	07-Nov-26	406d	4	100%	0%	1,141
	Backfilling, Warning Tape Works f	2d	2d	03-Sep-26	05-Sep-26	04-Nov-26	07-Nov-26	406d	1	100%	0%	114
	Testing and Commissioning for L	2d	2d	01-Sep-26	02-Sep-26	02-Nov-26	04-Nov-26	406d	1	100%	0%	57
	Bedding Layer and Installation fo	2d	2d	13-Aug-26	15-Aug-26	14-Oct-26	17-Oct-26	420d	1	100%	0%	855
	Excavation Works for LV Cables	2d	2d	11-Aug-26	12-Aug-26	12-Oct-26	14-Oct-26	407d	1	100%	0%	114
	JDH3-02-009-R21-(SL)-RMU 33 KV	8d	8d	18-Aug-26	24-Aug-26	14-Oct-26	24-Oct-26	411d	3	100%	0%	58,823
	Earthing + Primary Test for RMU 3	2d	2d	23-Aug-26	24-Aug-26	21-Oct-26	24-Oct-26	411d	1	100%	0%	4,202
	Cables Connection for RMU 33 K'	2d	2d	20-Aug-26	22-Aug-26	17-Oct-26	19-Oct-26	413d	1	100%	0%	4,202
	Installation for RMU 33 KV- (B2.2(	2d	2d	18-Aug-26	19-Aug-26	14-Oct-26	17-Oct-26	413d	1	100%	0%	50,420
	JDH3-02-009-R21-Telecommunicatior	8d	8d	14-Sep-26	28-Sep-26	29-Sep-26	07-Oct-26	436d	9	100%	0%	129,372
	JDH3-02-009-R21-(TEL)-Ducts	8d	8d	14-Sep-26	22-Sep-26	29-Sep-26	07-Oct-26	436d	3	100%	0%	19,984
	Backfilling Works for HDPE ducts	2d	2d	21-Sep-26	22-Sep-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	1,998
	Installation for HDPE ducts 2 x 32	4d	4d	16-Sep-26	20-Sep-26	01-Oct-26	05-Oct-26	436d	1	100%	0%	14,988
	Excavation Works for HDPE ducts	2d	2d	14-Sep-26	15-Sep-26	29-Sep-26	30-Sep-26	370d	1	100%	0%	2,998
	JDH3-02-009-R21-(TEL)-Manhole T	6d	6d	16-Sep-26	22-Sep-26	01-Oct-26	07-Oct-26	432d	3	100%	0%	54,694
	Backfilling Works for MH Type 1 D	2d	2d	21-Sep-26	22-Sep-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	5,469
	Installation for MH Type 1 Dim 20(	2d	2d	19-Sep-26	20-Sep-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	41,021
	Excavation and Bedding Works fo	2d	2d	16-Sep-26	17-Sep-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	8,204
	JDH3-02-009-R21-(TEL)-Manhole T	6d	6d	16-Sep-26	28-Sep-26	01-Oct-26	07-Oct-26	370d	3	100%	0%	54,694
	Backfilling Works for MH Type 2 D	2d	2d	27-Sep-26	28-Sep-26	06-Oct-26	07-Oct-26	370d	1	100%	0%	5,469
	Installation for MH Type 2 Dim 20(	2d	2d	19-Sep-26	20-Sep-26	04-Oct-26	05-Oct-26	370d	1	100%	0%	41,021
	Excavation and Bedding Works fo	2d	2d	16-Sep-26	17-Sep-26	01-Oct-26	03-Oct-26	370d	1	100%	0%	8,204
R22		55d	55d	23-Jun-26	28-Sep-26	29-Sep-26	01-Dec-26	389d	41	100%	0%	468,433
	JDH3-02-009-R22-Sewage Network - S	4d	4d	20-Jul-26	23-Jul-26	10-Oct-26	13-Oct-26	429d	2	100%	0%	2,960
	JDH3-02-009-R22-(SW)-MH Works	2d	2d	20-Jul-26	21-Jul-26	10-Oct-26	11-Oct-26	429d	1	100%	0%	485
	Steel Cover for MH 1200 mm - de	2d	2d	20-Jul-26	21-Jul-26	10-Oct-26	11-Oct-26	429d	1	100%	0%	485
	JDH3-02-009-R22-(SW)-MH Works	2d	2d	22-Jul-26	23-Jul-26	12-Oct-26	13-Oct-26	429d	1	100%	0%	2,475
	Steel Cover for MH 1200 mm - de	2d	2d	22-Jul-26	23-Jul-26	12-Oct-26	13-Oct-26	429d	1	100%	0%	2,475
	JDH3-02-009-R22-Storm Network - ST	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	8	100%	0%	6,206
	JDH3-02-009-R22-(ST)-MH Works (	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	1,091
	Steel Coverfor MH 1200 mm - de|	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	390
	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	701
	JDH3-02-009-R22-(ST)-MH Works (	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	436d	2	100%	0%	2,127
	Steel Coverfor MH 2000 mm - de|	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	760
	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	1,367
	JDH3-02-009-R22-(ST)-MH Works (	4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	1,428
	Steel Coverfor MH 1500 mm - de|	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	510
	Finishing, Benching, Testing Worl	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	918
	JDH3-02-009-R22-(ST)-MH Works (	4d	4d	28-Jun-26	01-Jul-26	04-Oct-26	07-Oct-26	436d	2	100%	0%	1,560
	Steel Coverfor MH 1500 mm - de|	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	557
	Finishing, Benching, Testing Worl	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	1,003
	JDH3-02-009-R22-Potable Water Netw	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	2,931
	JDH3-02-009-R22-(WT)-Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	2,931
	Protection Barriers for Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	2,931
	JDH3-02-009-R22-Electrical Network	12d	12d	19-Jul-26	08-Aug-26	29-Sep-26	12-Oct-26	345d	8	100%	0%	205,764
	JDH3-02-009-R22-(EL)-MV cable tr	11d	11d	19-Jul-26	30-Jul-26	29-Sep-26	11-Oct-26	346d	2	100%	0%	5,449
	Backfilling + Warning Tape for MV	3d	3d	28-Jul-26	30-Jul-26	08-Oct-26	11-Oct-26	346d	1	100%	0%	2,180
	Excavation for MV Cable Trench	3d	3d	19-Jul-26	21-Jul-26	29-Sep-26	01-Oct-26	345d	1	100%	0%	3,270
	JDH3-02-009-R22-(EL)-MV cables /	7d	7d	22-Jul-26	29-Jul-26	03-Oct-26	10-Oct-26	345d	3	100%	0%	131,369
	Termination for MV Cables 3Cx40	2d	2d	28-Jul-26	29-Jul-26	08-Oct-26	10-Oct-26	345d	1	100%	0%	2,580
	Installing Joints for MV Cables 3C	2d	2d	26-Jul-26	27-Jul-26	06-Oct-26	07-Oct-26	345d	1	100%	0%	8,701
	Installing for MV Cables AL/XLPE	3d	3d	22-Jul-26	25-Jul-26	03-Oct-26	05-Oct-26	345d	1	100%	0%	120,087
	JDH3-02-009-R22-(EL)-RMU 33 KV	6d	6d	02-Aug-26	08-Aug-26	06-Oct-26	12-Oct-26	345d	3	100%	0%	68,946

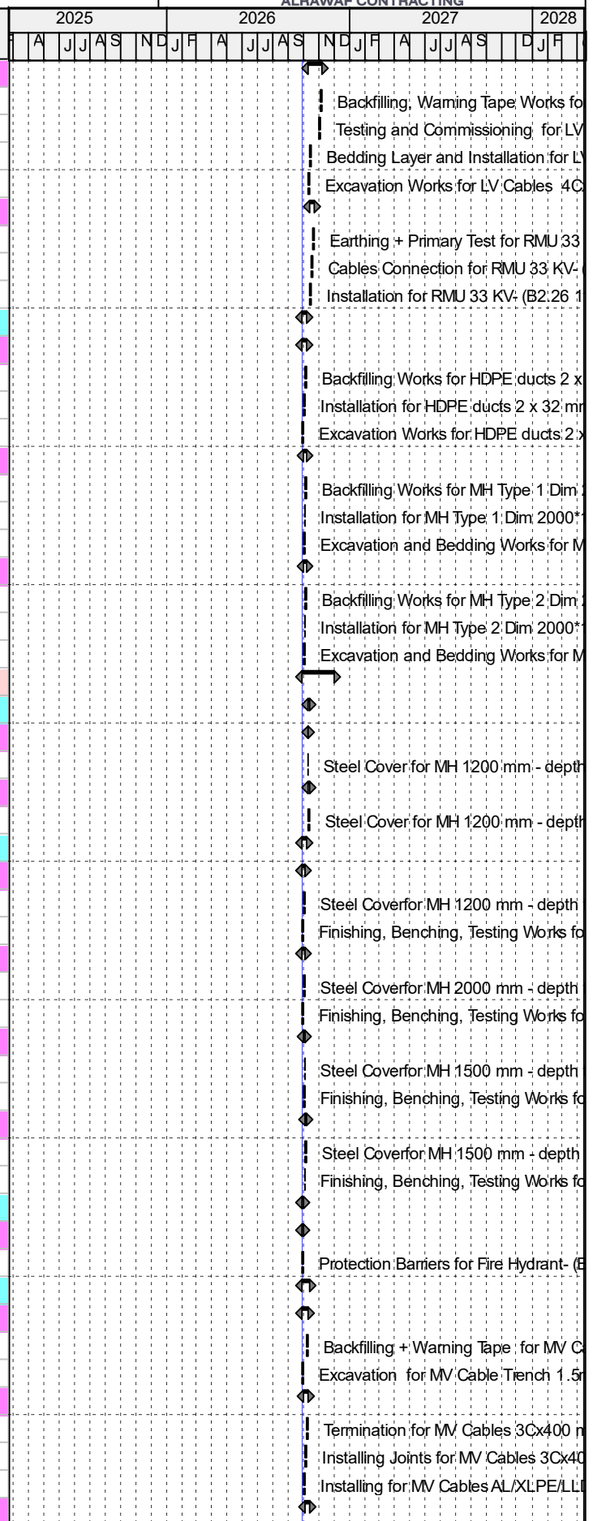


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Earthing + Primary Test for RMU 3	2d	2d	06-Aug-26	08-Aug-26	11-Oct-26	12-Oct-26	345d	1	100%	0%	4,925
	Cables Connection for RMU 33 K'	2d	2d	04-Aug-26	05-Aug-26	08-Oct-26	10-Oct-26	345d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.2(	2d	2d	02-Aug-26	03-Aug-26	06-Oct-26	07-Oct-26	345d	1	100%	0%	59,096
	JDH3-02-009-R22-Street Lighting Netv	31d	31d	09-Aug-26	13-Sep-26	13-Oct-26	17-Nov-26	345d	13	100%	0%	196,405
	JDH3-02-009-R22-(SL)- LV Cables -	20d	20d	09-Aug-26	31-Aug-26	13-Oct-26	04-Nov-26	354d	4	100%	0%	70,094
	Backfilling, Warning Tape Works f	5d	5d	26-Aug-26	31-Aug-26	31-Oct-26	04-Nov-26	354d	1	100%	0%	7,009
	Testing and Commissioning for L	5d	5d	20-Aug-26	25-Aug-26	25-Oct-26	29-Oct-26	354d	1	100%	0%	3,505
	Bedding Layer and Installation fo	5d	5d	15-Aug-26	19-Aug-26	19-Oct-26	24-Oct-26	354d	1	100%	0%	52,570
	Excavation Works for LV Cables	5d	5d	09-Aug-26	13-Aug-26	13-Oct-26	18-Oct-26	345d	1	100%	0%	7,009
	JDH3-02-009-R22-(SL)- LV Cables -	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	07-Nov-26	346d	1	100%	0%	3,991
	Installation for LV Cables 3-1xCx	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	07-Nov-26	346d	1	100%	0%	3,991
	JDH3-02-009-R22-(SL)-Lighting Pol	21d	21d	15-Aug-26	07-Sep-26	19-Oct-26	11-Nov-26	345d	5	100%	0%	105,056
	Cable Connection for Lighting Po	6d	6d	01-Sep-26	07-Sep-26	05-Nov-26	11-Nov-26	345d	1	100%	0%	5,253
	Installation Works for Lighting Pol	6d	6d	25-Aug-26	31-Aug-26	29-Oct-26	04-Nov-26	345d	1	100%	0%	68,286
	Backfilling of RC foundation for Li	3d	3d	22-Aug-26	24-Aug-26	26-Oct-26	28-Oct-26	345d	1	100%	0%	10,506
	Installation of RC foundation for L	3d	3d	18-Aug-26	20-Aug-26	22-Oct-26	25-Oct-26	345d	1	100%	0%	10,506
	Excavation for RC foundation for	3d	3d	15-Aug-26	17-Aug-26	19-Oct-26	21-Oct-26	345d	1	100%	0%	10,506
	JDH3-02-009-R22-(SL)-Street Light	7d	7d	03-Sep-26	10-Sep-26	08-Nov-26	15-Nov-26	345d	2	100%	0%	15,986
	Cable Connection for Lighting(LE	3d	3d	08-Sep-26	10-Sep-26	12-Nov-26	15-Nov-26	345d	1	100%	0%	3,197
	Installation for Lighting(LED) Lur	3d	3d	03-Sep-26	06-Sep-26	08-Nov-26	10-Nov-26	346d	1	100%	0%	12,789
	JDH3-02-009-R22-(SL)-Earthing Sy	2d	2d	12-Sep-26	13-Sep-26	16-Nov-26	17-Nov-26	345d	1	100%	0%	1,278
	Supply, construct, connect and te	2d	2d	12-Sep-26	13-Sep-26	16-Nov-26	17-Nov-26	345d	1	100%	0%	1,278
	JDH3-02-009-R22-Telecommunicatior	12d	12d	14-Sep-26	28-Sep-26	18-Nov-26	01-Dec-26	345d	9	100%	0%	54,168
	JDH3-02-009-R22-(TEL)-Manhole T	6d	6d	14-Sep-26	20-Sep-26	18-Nov-26	24-Nov-26	349d	3	100%	0%	20,510
	Backfilling Works for MH Type 1 D	2d	2d	19-Sep-26	20-Sep-26	23-Nov-26	24-Nov-26	349d	1	100%	0%	2,051
	Installation for MH Type 1 Dim 20	2d	2d	16-Sep-26	17-Sep-26	21-Nov-26	22-Nov-26	349d	1	100%	0%	15,383
	Excavation and Bedding Works fo	2d	2d	14-Sep-26	15-Sep-26	18-Nov-26	19-Nov-26	345d	1	100%	0%	3,077
	JDH3-02-009-R22-(TEL)-Manhole T	6d	6d	16-Sep-26	22-Sep-26	21-Nov-26	26-Nov-26	347d	3	100%	0%	13,674
	Backfilling Works for MH Type 2 D	2d	2d	21-Sep-26	22-Sep-26	25-Nov-26	26-Nov-26	347d	1	100%	0%	1,367
	Installation for MH Type 2 Dim 20	2d	2d	19-Sep-26	20-Sep-26	23-Nov-26	24-Nov-26	347d	1	100%	0%	10,255
	Excavation and Bedding Works fo	2d	2d	16-Sep-26	17-Sep-26	21-Nov-26	22-Nov-26	345d	1	100%	0%	2,051
	JDH3-02-009-R22-(TEL)-Ducts	8d	8d	19-Sep-26	28-Sep-26	23-Nov-26	01-Dec-26	345d	3	100%	0%	19,984
	Backfilling Works for HDPE ducts	2d	2d	27-Sep-26	28-Sep-26	30-Nov-26	01-Dec-26	345d	1	100%	0%	1,998
	Installation for HDPE ducts 2 x 32	4d	4d	21-Sep-26	26-Sep-26	25-Nov-26	29-Nov-26	345d	1	100%	0%	14,988
	Excavation Works for HDPE ducts	2d	2d	19-Sep-26	20-Sep-26	23-Nov-26	24-Nov-26	345d	1	100%	0%	2,998
R231		52d	52d	23-Jun-26	28-Sep-26	29-Sep-26	28-Nov-26	392d	45	100%	0%	492,985
	JDH3-02-009-R231-Sewage Network -	14d	14d	30-Jun-26	26-Jul-26	30-Sep-26	15-Oct-26	429d	3	100%	0%	4,074
	JDH3-02-009-R231-(SW)-MH Works	2d	2d	30-Jun-26	02-Jul-26	30-Sep-26	01-Oct-26	439d	1	100%	0%	1,067
	Steel Cover for MH 1200 mm - de	2d	2d	30-Jun-26	02-Jul-26	30-Sep-26	01-Oct-26	439d	1	100%	0%	1,067
	JDH3-02-009-R231-(SW)-MH Works	2d	2d	02-Jul-26	05-Jul-26	03-Oct-26	04-Oct-26	439d	1	100%	0%	2,425
	Steel Cover for MH 1200 mm - de	2d	2d	02-Jul-26	05-Jul-26	03-Oct-26	04-Oct-26	439d	1	100%	0%	2,425
	JDH3-02-009-R231-(SW)-MH Works	2d	2d	25-Jul-26	26-Jul-26	14-Oct-26	15-Oct-26	429d	1	100%	0%	582
	Steel Cover for MH 1200 mm - de	2d	2d	25-Jul-26	26-Jul-26	14-Oct-26	15-Oct-26	429d	1	100%	0%	582
	JDH3-02-009-R231-Storm Network - S	10d	10d	23-Jun-26	04-Jul-26	29-Sep-26	10-Oct-26	434d	6	100%	0%	10,457
	JDH3-02-009-R231-(ST)-MH Works	6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	434d	2	100%	0%	1,560
	Steel Coverfor MH 1500 mm - de	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	557
	Finishing, Benching, Testing Worl	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	1,003
	JDH3-02-009-R231-(ST)-MH Works	6d	6d	25-Jun-26	01-Jul-26	01-Oct-26	07-Oct-26	434d	2	100%	0%	2,127
	Steel Coverfor MH 2000 mm - de	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	760
	Finishing, Benching, Testing Worl	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	1,367
	JDH3-02-009-R231-(ST)-MH Works	6d	6d	28-Jun-26	04-Jul-26	04-Oct-26	10-Oct-26	434d	2	100%	0%	6,770
	Steel Coverfor MH 2000 mm - de	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	434d	1	100%	0%	2,312
	Finishing, Benching, Testing Worl	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	4,459

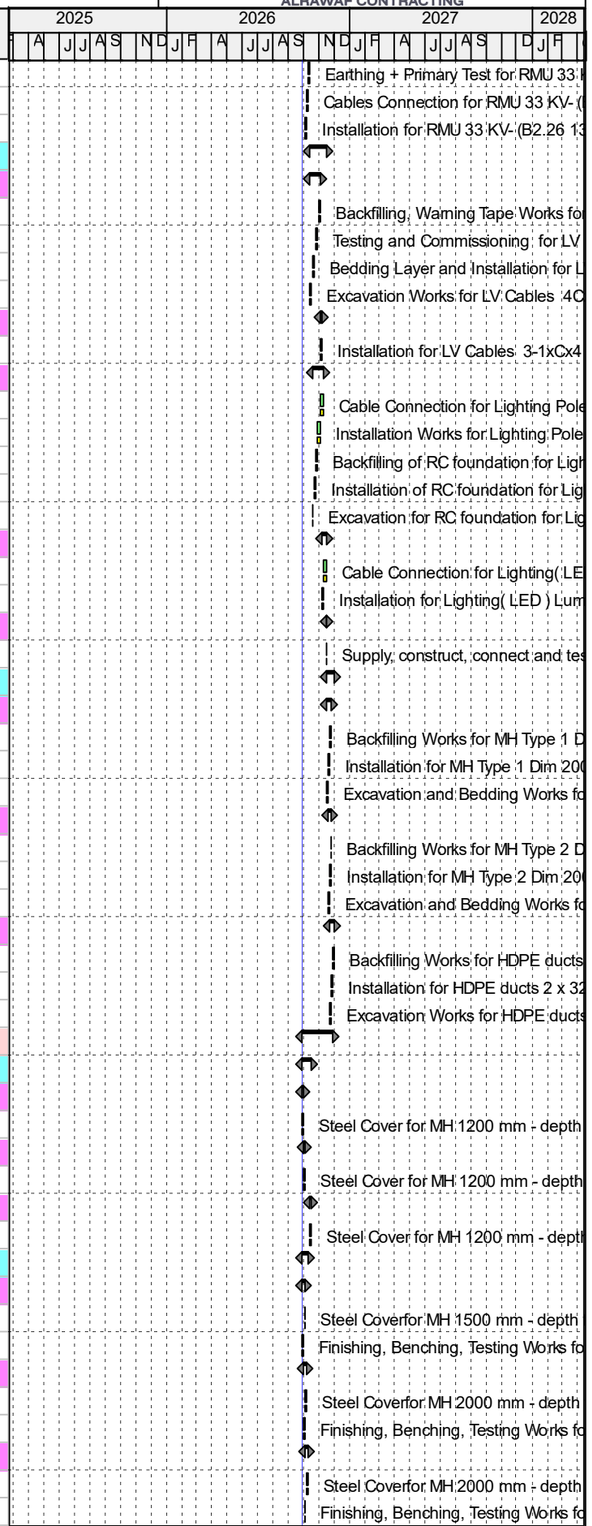


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R231-TSE Network - TSI	6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	438d	6	100%	0%	35,502
	JDH3-02-009-R231-(TSE)-Wash-Ou	6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	438d	4	100%	0%	20,938
	Backfilling Worksfor Wash-Out Ch	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	393d	1	100%	0%	4,188
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	11,516
	PC Worksfor Wash-Out Chamber	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	2,094
	Excavation+Bedding for Wash-Ou	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	3,141
	JDH3-02-009-R231-(TSE)-Wash-Ou	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	393d	2	100%	0%	14,564
	Stem & Surface box for Wash-Ou	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	393d	1	100%	0%	1,456
	Installation for Wash-Out Valve 1(	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	393d	1	100%	0%	13,108
	JDH3-02-009-R231-Potable Water Net	2d	2d	18-Jul-26	19-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R231-(WT)-Fire Hydra	2d	2d	18-Jul-26	19-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	Protection Barriers for Fire Hydran	2d	2d	18-Jul-26	19-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	4,885
	JDH3-02-009-R231-Electrical Network	6d	6d	02-Aug-26	08-Aug-26	06-Oct-26	13-Oct-26	392d	3	100%	0%	68,946
	JDH3-02-009-R231-(EL)-RMU 33 KV	6d	6d	02-Aug-26	08-Aug-26	06-Oct-26	13-Oct-26	392d	3	100%	0%	68,946
	Earthing + Primary Test for RMU 3	2d	2d	06-Aug-26	08-Aug-26	11-Oct-26	13-Oct-26	392d	1	100%	0%	4,925
	Cables Connection for RMU 33 KV	2d	2d	04-Aug-26	05-Aug-26	08-Oct-26	11-Oct-26	392d	1	100%	0%	4,925
	Installation for RMU 33 KV- (B2.26	2d	2d	02-Aug-26	03-Aug-26	06-Oct-26	08-Oct-26	392d	1	100%	0%	59,096
	JDH3-02-009-R231-Street Lighting Ne	29d	29d	09-Aug-26	10-Sep-26	13-Oct-26	16-Nov-26	402d	17	100%	0%	212,402
	JDH3-02-009-R231-(SL)-Earthing S	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	08-Nov-26	409d	1	100%	0%	1,126
	Supply, construct, connect and te	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	08-Nov-26	409d	1	100%	0%	1,126
	JDH3-02-009-R231-(SL)- LV Cables	20d	20d	09-Aug-26	31-Aug-26	13-Oct-26	05-Nov-26	396d	4	100%	0%	75,486
	Backfilling, Warning Tape Works f	5d	5d	26-Aug-26	31-Aug-26	31-Oct-26	05-Nov-26	396d	1	100%	0%	7,549
	Testing and Commissioning for L	5d	5d	20-Aug-26	25-Aug-26	25-Oct-26	31-Oct-26	396d	1	100%	0%	3,774
	Bedding Layer and Installation fo	5d	5d	15-Aug-26	19-Aug-26	19-Oct-26	25-Oct-26	396d	1	100%	0%	56,614
	Excavation Works for LV Cables	5d	5d	09-Aug-26	13-Aug-26	13-Oct-26	19-Oct-26	392d	1	100%	0%	7,549
	JDH3-02-009-R231-(SL)-Street Ligh	7d	7d	03-Sep-26	10-Sep-26	08-Nov-26	16-Nov-26	392d	2	100%	0%	15,986
	Cable Connection for Lighting(LE	3d	3d	08-Sep-26	10-Sep-26	12-Nov-26	16-Nov-26	392d	1	100%	0%	3,197
	Installation for Lighting(LED) Lur	3d	3d	03-Sep-26	06-Sep-26	08-Nov-26	11-Nov-26	393d	1	100%	0%	12,789
	JDH3-02-009-R231-(SL)-Earthing S	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	08-Nov-26	396d	1	100%	0%	426
	Supply, construct, connect and te	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	08-Nov-26	396d	1	100%	0%	426
	JDH3-02-009-R231-(SL)- Street Ligl	6d	6d	15-Aug-26	20-Aug-26	19-Oct-26	26-Oct-26	404d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	19-Aug-26	20-Aug-26	24-Oct-26	26-Oct-26	404d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	17-Aug-26	18-Aug-26	21-Oct-26	24-Oct-26	404d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	15-Aug-26	16-Aug-26	19-Oct-26	21-Oct-26	404d	1	100%	0%	1,033
	JDH3-02-009-R231-(SL)-Lighting Po	21d	21d	15-Aug-26	07-Sep-26	19-Oct-26	12-Nov-26	392d	5	100%	0%	105,056
	Cable Connection for Lighting Po	6d	6d	01-Sep-26	07-Sep-26	05-Nov-26	12-Nov-26	392d	1	100%	0%	5,253
	Installation Works for Lighting Pol	6d	6d	25-Aug-26	31-Aug-26	29-Oct-26	05-Nov-26	392d	1	100%	0%	68,286
	Backfilling of RC foundation for Li	3d	3d	22-Aug-26	24-Aug-26	26-Oct-26	29-Oct-26	392d	1	100%	0%	10,506
	Installation of RC foundation for L	3d	3d	18-Aug-26	20-Aug-26	22-Oct-26	26-Oct-26	392d	1	100%	0%	10,506
	Excavation for RC foundation for	3d	3d	15-Aug-26	17-Aug-26	19-Oct-26	22-Oct-26	392d	1	100%	0%	10,506
	JDH3-02-009-R231-(SL)- LV Cables	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	08-Nov-26	393d	1	100%	0%	3,991
	Installation for LV Cables 3-1xCx	2d	2d	01-Sep-26	02-Sep-26	05-Nov-26	08-Nov-26	393d	1	100%	0%	3,991
	JDH3-02-009-R231-Telecommunicatic	10d	10d	12-Sep-26	28-Sep-26	16-Nov-26	28-Nov-26	392d	9	100%	0%	156,719
	JDH3-02-009-R231-(TEL)-Ducts	8d	8d	12-Sep-26	20-Sep-26	16-Nov-26	25-Nov-26	394d	3	100%	0%	19,984
	Backfilling Works for HDPE ducts	2d	2d	19-Sep-26	20-Sep-26	23-Nov-26	25-Nov-26	394d	1	100%	0%	1,998
	Installation for HDPE ducts 2 x 32	4d	4d	14-Sep-26	17-Sep-26	18-Nov-26	23-Nov-26	394d	1	100%	0%	14,988
	Excavation Works for HDPE ducts	2d	2d	12-Sep-26	13-Sep-26	16-Nov-26	18-Nov-26	392d	1	100%	0%	2,998
	JDH3-02-009-R231-(TEL)-Manhole	6d	6d	14-Sep-26	26-Sep-26	18-Nov-26	25-Nov-26	392d	3	100%	0%	95,715
	Backfilling Works for MH Type 1 D	2d	2d	24-Sep-26	26-Sep-26	23-Nov-26	25-Nov-26	392d	1	100%	0%	9,571
	Installation for MH Type 1 Dim 20	2d	2d	16-Sep-26	17-Sep-26	21-Nov-26	23-Nov-26	392d	1	100%	0%	71,786
	Excavation and Bedding Works fo	2d	2d	14-Sep-26	15-Sep-26	18-Nov-26	21-Nov-26	392d	1	100%	0%	14,357
	JDH3-02-009-R231-(TEL)-Manhole	6d	6d	16-Sep-26	28-Sep-26	21-Nov-26	28-Nov-26	392d	3	100%	0%	41,021
	Backfilling Works for MH Type 2 D	2d	2d	27-Sep-26	28-Sep-26	25-Nov-26	28-Nov-26	392d	1	100%	0%	4,102

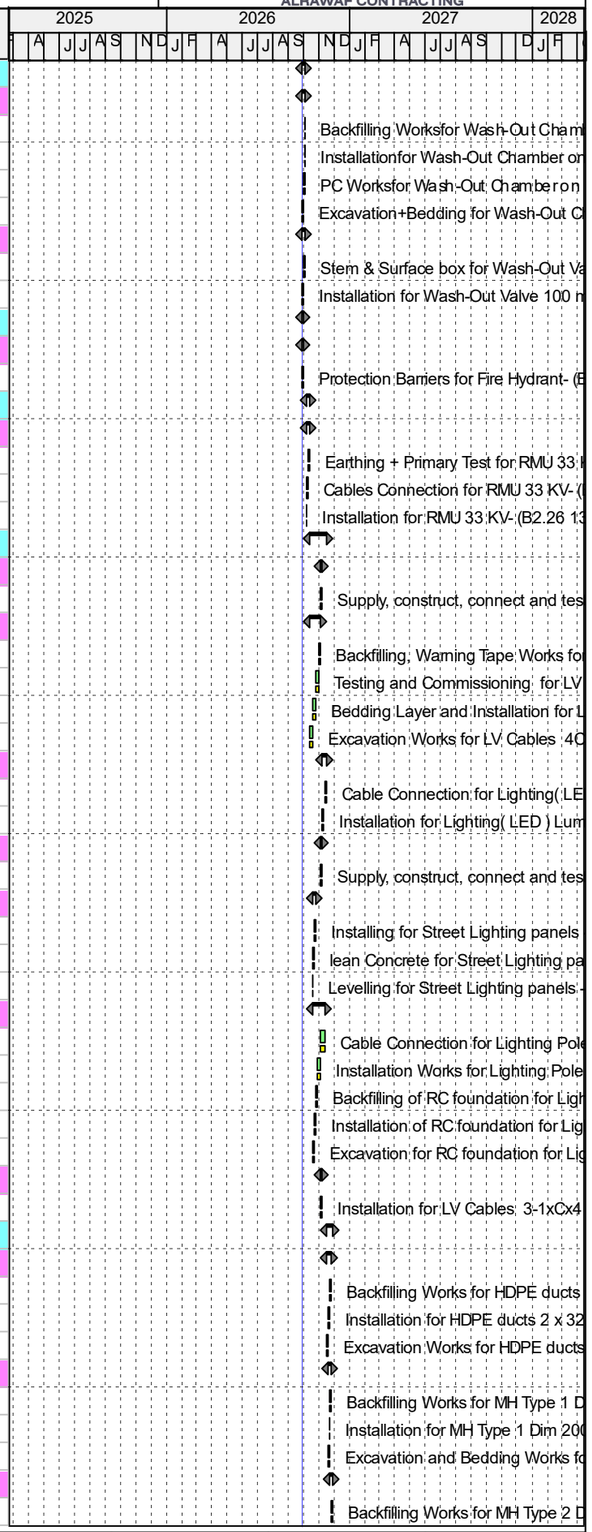

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Installation for MH Type 2 Dim 20	2d	2d	19-Sep-26	20-Sep-26	23-Nov-26	25-Nov-26	392d	1	100%	0%	30,765
	Excavation and Bedding Works fo	2d	2d	16-Sep-26	17-Sep-26	21-Nov-26	23-Nov-26	392d	1	100%	0%	6,153
R232		77d	77d	23-Jun-26	29-Sep-26	29-Sep-26	27-Dec-26	367d	29	99.83%	0%	760,030
JDH3-02-009-R232-Storm Network - S		4d	4d	23-Jun-26	06-Jul-26	29-Sep-26	03-Oct-26	440d	4	100%	0%	8,703
JDH3-02-009-R232-(ST)-MH Works		4d	4d	02-Jul-26	06-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	5,508
	Steel Coverfor MH 1500 mm - dep	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,836
	Finishing, Benching, Testing Work	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	3,672
JDH3-02-009-R232-(ST)-MH Works		4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	434d	2	100%	0%	3,194
	Steel Coverfor MH 1200 mm - dep	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	1,091
	Finishing, Benching, Testing Work	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	2,104
JDH3-02-009-R232-Potable Water Net		2d	2d	06-Jul-26	07-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,374
JDH3-02-009-R232-(WT)-Fire Hydra		2d	2d	06-Jul-26	07-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,374
	Protection Barriers for Fire Hydran	2d	2d	06-Jul-26	07-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	5,374
JDH3-02-009-R232-Street Lighting Ne		21d	21d	28-Jun-26	21-Jul-26	29-Sep-26	22-Oct-26	423d	7	100%	0%	99,427
JDH3-02-009-R232-(SL)-Lighting P		21d	21d	28-Jun-26	21-Jul-26	29-Sep-26	22-Oct-26	361d	5	100%	0%	86,296
	Cable Connection for Lighting Po	6d	6d	15-Jul-26	21-Jul-26	17-Oct-26	22-Oct-26	361d	1	100%	0%	4,315
	Installation Works for Lighting Pol	6d	6d	08-Jul-26	14-Jul-26	10-Oct-26	15-Oct-26	361d	1	100%	0%	56,092
	Backfilling of RC foundation for Li	3d	3d	05-Jul-26	07-Jul-26	06-Oct-26	08-Oct-26	361d	1	100%	0%	8,630
	Installation of RC foundation for L	3d	3d	01-Jul-26	04-Jul-26	03-Oct-26	05-Oct-26	361d	1	100%	0%	8,630
	Excavation for RC foundation for	3d	3d	28-Jun-26	30-Jun-26	29-Sep-26	01-Oct-26	361d	1	100%	0%	8,630
JDH3-02-009-R232-(SL)-Street Ligh		4d	4d	15-Jul-26	19-Jul-26	17-Oct-26	20-Oct-26	425d	2	100%	0%	13,131
	Cable Connection for Lighting(LE	2d	2d	18-Jul-26	19-Jul-26	19-Oct-26	20-Oct-26	425d	1	100%	0%	2,626
	Installation for Lighting(LED) Lur	2d	2d	15-Jul-26	16-Jul-26	17-Oct-26	18-Oct-26	425d	1	100%	0%	10,505
JDH3-02-009-R232-Road Works - RD		56d	56d	26-Jul-26	29-Sep-26	24-Oct-26	27-Dec-26	365d	17	99.8%	0%	646,526
JDH3-02-009-R232-(RD)-Bituminous		5d	5d	03-Sep-26	08-Sep-26	02-Dec-26	07-Dec-26	361d	1	100%	0%	303,743
	Supply, lay and compaction Asph	5d	5d	03-Sep-26	08-Sep-26	02-Dec-26	07-Dec-26	361d	1	100%	0%	303,743
JDH3-02-009-R232-(RD)-Precast C		43d	43d	26-Jul-26	13-Sep-26	24-Oct-26	12-Dec-26	378d	4	100%	0%	127,502
	Supply and installation Depressec	9d	9d	05-Aug-26	15-Aug-26	03-Nov-26	12-Nov-26	361d	1	100%	0%	56,761
	Supply and installation Depressec	4d	4d	09-Sep-26	13-Sep-26	08-Dec-26	12-Dec-26	378d	1	100%	0%	798
	Supply and installation Precast C	2d	2d	03-Aug-26	04-Aug-26	01-Nov-26	02-Nov-26	361d	1	100%	0%	17,561
	Supply and installation Precast C	7d	7d	26-Jul-26	02-Aug-26	24-Oct-26	31-Oct-26	361d	1	100%	0%	52,382
JDH3-02-009-R232-(RD)-Precast In		16d	16d	16-Aug-26	02-Sep-26	14-Nov-26	01-Dec-26	361d	1	100%	0%	163,738
	Interlocking block pavers for sidev	16d	16d	16-Aug-26	02-Sep-26	14-Nov-26	01-Dec-26	361d	1	100%	0%	163,738
JDH3-02-009-R232-(RD)-Pavement		17d	17d	09-Sep-26	29-Sep-26	08-Dec-26	27-Dec-26	361d	8	90.63%	0%	13,538
	Thermoplastic intermittent 100 m	2d	2d	28-Sep-26	29-Sep-26	26-Dec-26	27-Dec-26	361d	1	50%	0%	2,536
	Thermoplastic continuous Painted	2d	2d	26-Sep-26	27-Sep-26	23-Dec-26	24-Dec-26	361d	1	100%	0%	345
	Thermoplastic continuous Retrore	2d	2d	22-Sep-26	24-Sep-26	21-Dec-26	22-Dec-26	361d	1	100%	0%	951
	Thermoplastic continuous 100 m	2d	2d	19-Sep-26	20-Sep-26	17-Dec-26	19-Dec-26	362d	1	100%	0%	1,062
	Thermoplastic continuous 300 m	2d	2d	16-Sep-26	17-Sep-26	15-Dec-26	16-Dec-26	362d	1	100%	0%	183
	Thermoplastic continuous 200 m	2d	2d	14-Sep-26	15-Sep-26	13-Dec-26	14-Dec-26	362d	1	100%	0%	3,858
	Thermoplastic continuous 120 m	2d	2d	12-Sep-26	13-Sep-26	10-Dec-26	12-Dec-26	362d	1	100%	0%	685
	Thermoplastic continuous 120 m	2d	2d	09-Sep-26	10-Sep-26	08-Dec-26	09-Dec-26	362d	1	100%	0%	3,917
JDH3-02-009-R232-(RD)-Traffic Sig		11d	11d	09-Sep-26	21-Sep-26	08-Dec-26	20-Dec-26	361d	3	100%	0%	38,005
	Supply and installation Traffic sign	2d	2d	20-Sep-26	21-Sep-26	19-Dec-26	20-Dec-26	361d	1	100%	0%	3,365
	Supply and installation Traffic sign	5d	5d	14-Sep-26	19-Sep-26	13-Dec-26	17-Dec-26	361d	1	100%	0%	21,560
	Supply and installation Traffic sign	4d	4d	09-Sep-26	13-Sep-26	08-Dec-26	12-Dec-26	361d	1	100%	0%	13,080
R45		12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	9	100%	0%	74,608
R454		12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	9	100%	0%	74,608
JDH3-02-009-R454-Potable Water Net		12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	9	100%	0%	74,608
JDH3-02-009-R454-(WT)-Valve Cha		12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	4	100%	0%	14,336
	Backfilling Worksfor Butterfly Valv	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	2,867
	Installationfor Butterfly Valve Cha	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	7,885
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	1,434

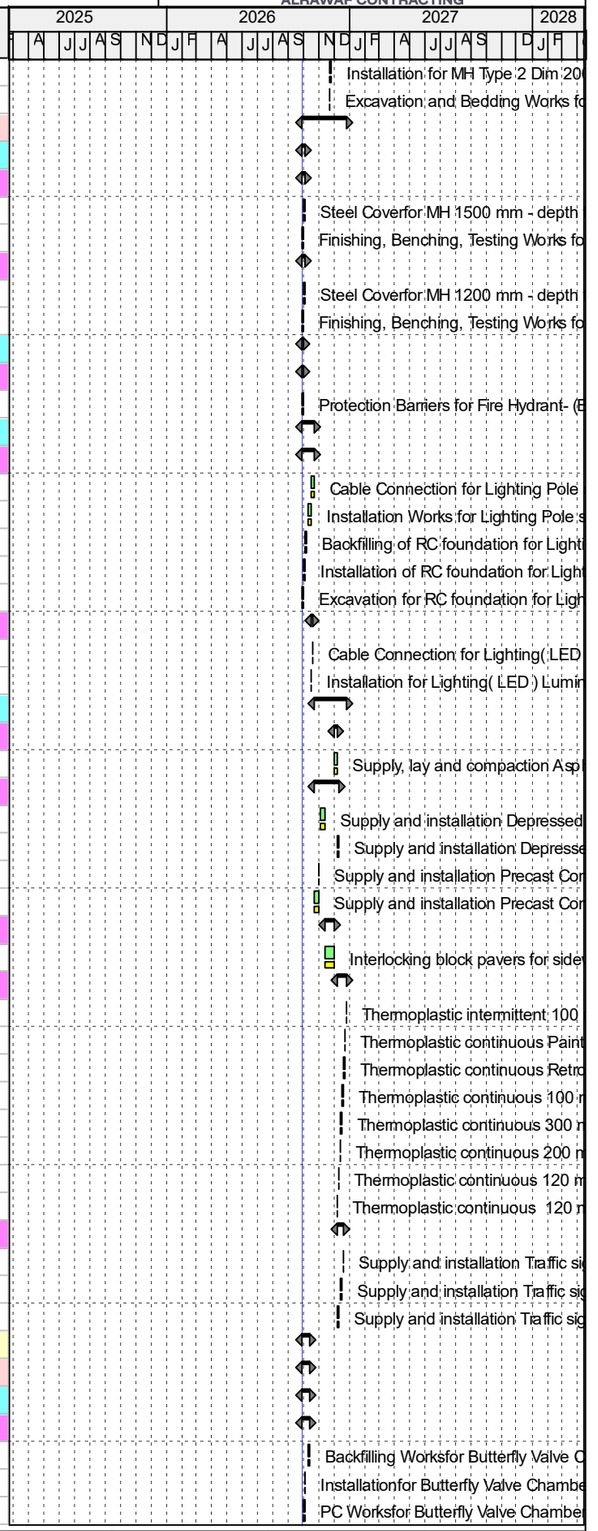

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Excavation+Bedding for Butterfly	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	432d	1	100%	0%	2,150
	JDH3-02-009-R454-(WT)-Fire Hydra	6d	6d	23-Jun-26	29-Jun-26	29-Sep-26	05-Oct-26	434d	3	100%	0%	34,198
	Protection Barriers for Fire Hydrar	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	2,443
	Fire Installation for Fire Hydrant- (	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	17,099
	Stem for Fire Hydrant- (B3.33 14	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	14,656
	JDH3-02-009-R454-(WT)-Butterfly V	4d	4d	30-Jun-26	04-Jul-26	06-Oct-26	10-Oct-26	432d	2	100%	0%	26,074
	Stem & Surface box for Butterfly '	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	2,607
	Installation for Butterfly Valve 400	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	23,467
R10		45d	45d	23-Jun-26	29-Sep-26	29-Sep-26	19-Nov-26	399d	268	99.97%	0%	4,533,823
R103		42d	42d	23-Jun-26	27-Sep-26	29-Sep-26	16-Nov-26	402d	58	100%	0%	1,033,073
	JDH3-02-009-R103-Storm Network - S	7d	7d	12-Jul-26	21-Jul-26	29-Sep-26	06-Oct-26	429d	3	100%	0%	11,377
	JDH3-02-009-R103-(ST)-MH Works	3d	3d	12-Jul-26	15-Jul-26	29-Sep-26	01-Oct-26	429d	1	100%	0%	9,817
	Finishing, Benching, Testing Worl	3d	3d	12-Jul-26	15-Jul-26	29-Sep-26	01-Oct-26	429d	1	100%	0%	9,817
	JDH3-02-009-R103-(ST)-MH Works	4d	4d	15-Jul-26	21-Jul-26	03-Oct-26	06-Oct-26	429d	2	100%	0%	1,560
	Steel Coverfor MH 1500 mm - dep	2d	2d	19-Jul-26	21-Jul-26	05-Oct-26	06-Oct-26	429d	1	100%	0%	557
	Finishing, Benching, Testing Worl	2d	2d	15-Jul-26	18-Jul-26	03-Oct-26	04-Oct-26	429d	1	100%	0%	1,003
	JDH3-02-009-R103-Catch Basins (Sto	4d	4d	05-Sep-26	27-Sep-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	24,514
	JDH3-02-009-R103-(ST)-Single Cat	4d	4d	05-Sep-26	09-Sep-26	29-Sep-26	03-Oct-26	440d	1	100%	0%	11,232
	Finishing and Insulation Works fo	4d	4d	05-Sep-26	09-Sep-26	29-Sep-26	03-Oct-26	440d	1	100%	0%	11,232
	JDH3-02-009-R103-(ST)-Double Cat	2d	2d	24-Sep-26	27-Sep-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	13,282
	Finishing and Insulation Works fo	2d	2d	24-Sep-26	27-Sep-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	13,282
	JDH3-02-009-R103-TSE Network - TSI	10d	10d	23-Jun-26	22-Jul-26	29-Sep-26	10-Oct-26	434d	17	100%	0%	135,563
	JDH3-02-009-R103-(TSE)-Butterfly '	8d	8d	09-Jul-26	22-Jul-26	29-Sep-26	08-Oct-26	435d	2	100%	0%	48,390
	Stem & Surface box for Butterfly '	2d	2d	21-Jul-26	22-Jul-26	06-Oct-26	08-Oct-26	435d	1	100%	0%	4,839
	Installation for Butterfly Valve 300	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	01-Oct-26	439d	1	100%	0%	43,551
	JDH3-02-009-R103-(TSE)-Wash-Ou	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	190d	2	100%	0%	16,127
	Stem & Surface box for Wash-Ou	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	190d	1	100%	0%	1,613
	Installation for Wash-Out Valve 1(	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	190d	1	100%	0%	14,515
	JDH3-02-009-R103-(TSE)-Air Valve	4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	190d	2	100%	0%	6,338
	Stem & Surface box for Air Valve	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	190d	1	100%	0%	634
	Installation for Air Valve 50 mm or	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	190d	1	100%	0%	5,704
	JDH3-02-009-R103-(TSE)-Valve Cha	6d	6d	09-Jul-26	20-Jul-26	29-Sep-26	06-Oct-26	435d	3	100%	0%	36,604
	Backfilling Worksfor Butterfly Valv	2d	2d	19-Jul-26	20-Jul-26	04-Oct-26	06-Oct-26	435d	1	100%	0%	8,613
	Installationfor Butterfly Valve Cha	2d	2d	12-Jul-26	13-Jul-26	01-Oct-26	04-Oct-26	435d	1	100%	0%	23,685
	PC Worksfor Butterfly Valve Chan	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	01-Oct-26	435d	1	100%	0%	4,306
	JDH3-02-009-R103-(TSE)-Wash-Ou	8d	8d	23-Jun-26	07-Jul-26	29-Sep-26	07-Oct-26	190d	4	100%	0%	20,886
	Backfilling Worksfor Wash-Out Ch	2d	2d	06-Jul-26	07-Jul-26	06-Oct-26	07-Oct-26	190d	1	100%	0%	4,177
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	190d	1	100%	0%	11,487
	PC Worksfor Wash-Out Chamber	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	190d	1	100%	0%	2,089
	Excavation+Bedding for Wash-Ou	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	190d	1	100%	0%	3,133
	JDH3-02-009-R103-(TSE)-Air Valve	8d	8d	25-Jun-26	09-Jul-26	01-Oct-26	10-Oct-26	434d	4	100%	0%	7,218
	Backfilling Worksfor Air Valve Cha	2d	2d	08-Jul-26	09-Jul-26	08-Oct-26	10-Oct-26	190d	1	100%	0%	1,444
	Installationfor Air Valve Chamber	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	3,970
	PC Worksfor Air Valve Chamber o	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	722
	Excavation+Bedding for Air Valve	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	1,083
	JDH3-02-009-R103-Potable Water Net	10d	10d	23-Jun-26	28-Jul-26	29-Sep-26	10-Oct-26	434d	10	100%	0%	179,197
	JDH3-02-009-R103-(WT)-HDPE Pipe	6d	6d	16-Jul-26	23-Jul-26	29-Sep-26	05-Oct-26	434d	1	100%	0%	20,256
	Primary Test for HDPE Pipe Line 8	6d	6d	16-Jul-26	23-Jul-26	29-Sep-26	05-Oct-26	434d	1	100%	0%	20,256
	JDH3-02-009-R103-(WT)-HDPE Pipe	4d	4d	23-Jul-26	28-Jul-26	06-Oct-26	10-Oct-26	434d	1	100%	0%	52,791
	Primary Test for HDPE Pipe Line 8	4d	4d	23-Jul-26	28-Jul-26	06-Oct-26	10-Oct-26	434d	1	100%	0%	52,791
	JDH3-02-009-R103-(WT)-HDPE Pipe	4d	4d	23-Jul-26	28-Jul-26	06-Oct-26	10-Oct-26	434d	1	100%	0%	4,981
	Primary Test for HDPE Pipe Line 8	4d	4d	23-Jul-26	28-Jul-26	06-Oct-26	10-Oct-26	434d	1	100%	0%	4,981
	JDH3-02-009-R103-(WT)-Butterfly V	4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	65,754

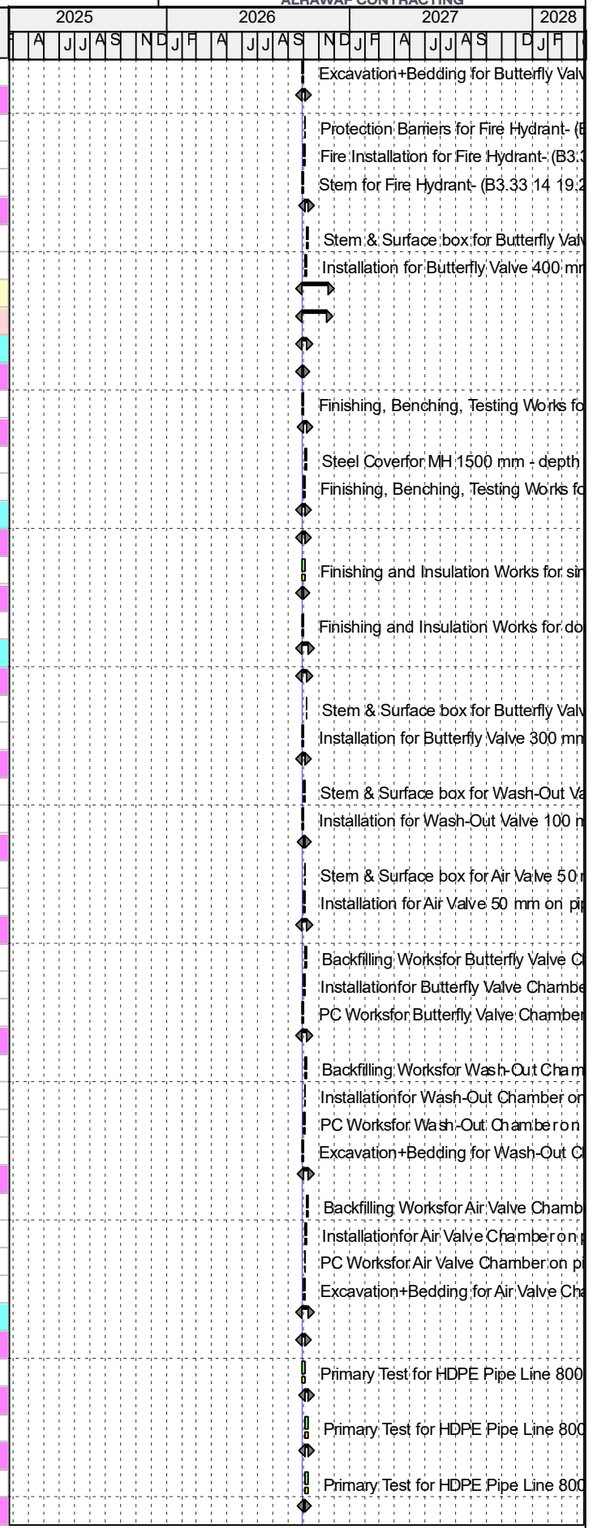


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Stem & Surface box for Butterfly '	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	6,575
	Installation for Butterfly Valve 800	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	59,179
	JDH3-02-009-R103-(WT)-Valve Cha	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	31,996
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	6,399
	Installationfor Butterfly Valve Cha	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	17,598
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	3,200
	Excavation+Bedding for Butterfly	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	4,799
	JDH3-02-009-R103-(WT)-Fire Hydra	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	198d	1	100%	0%	3,420
	Protection Barriers for Fire Hydran	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	198d	1	100%	0%	3,420
	JDH3-02-009-R103-Electrical Network	19d	19d	14-Jul-26	25-Aug-26	11-Oct-26	01-Nov-26	415d	7	100%	0%	478,641
	JDH3-02-009-R103-(EL)-MV cable t	10d	10d	14-Jul-26	25-Jul-26	11-Oct-26	21-Oct-26	190d	2	100%	0%	8,795
	Backfilling + Warning Tape for MV	5d	5d	20-Jul-26	25-Jul-26	17-Oct-26	21-Oct-26	190d	1	100%	0%	3,518
	Excavation for MV Cable Trench	5d	5d	14-Jul-26	19-Jul-26	11-Oct-26	15-Oct-26	190d	1	100%	0%	5,277
	JDH3-02-009-R103-(EL)-MV cable t	4d	4d	26-Jul-26	29-Jul-26	22-Oct-26	26-Oct-26	420d	2	100%	0%	1,291
	Backfilling + Warning Tape for MV	2d	2d	28-Jul-26	29-Jul-26	25-Oct-26	26-Oct-26	420d	1	100%	0%	516
	Excavation for MV Cable Trench	2d	2d	26-Jul-26	27-Jul-26	22-Oct-26	24-Oct-26	420d	1	100%	0%	774
	JDH3-02-009-R103-(EL)-MV cables	14d	14d	20-Jul-26	25-Aug-26	17-Oct-26	01-Nov-26	415d	3	100%	0%	468,555
	Termination for MV Cables 3Cx40	2d	2d	24-Aug-26	25-Aug-26	31-Oct-26	01-Nov-26	415d	1	100%	0%	2,580
	Installing Joints for MV Cables 3C	2d	2d	22-Aug-26	23-Aug-26	28-Oct-26	29-Oct-26	415d	1	100%	0%	20,303
	Installing for MV Cables AL/XLPE	10d	10d	20-Jul-26	30-Jul-26	17-Oct-26	27-Oct-26	415d	1	100%	0%	445,672
	JDH3-02-009-R103-Street Lighting Ne	22d	22d	28-Jul-26	22-Aug-26	21-Oct-26	16-Nov-26	192d	19	100%	0%	203,781
	JDH3-02-009-R103-(SL)-Lighting Ur	10d	10d	12-Aug-26	18-Aug-26	21-Oct-26	02-Nov-26	200d	3	100%	0%	47,612
	Earthing + Primary Test for Unit su	2d	2d	17-Aug-26	18-Aug-26	01-Nov-26	02-Nov-26	200d	1	100%	0%	3,401
	Cables Connection for Unit substa	2d	2d	15-Aug-26	16-Aug-26	24-Oct-26	26-Oct-26	204d	1	100%	0%	3,401
	Installation for Unit substation 33/	2d	2d	12-Aug-26	13-Aug-26	21-Oct-26	24-Oct-26	204d	1	100%	0%	40,810
	JDH3-02-009-R103-(SL)- LV Cables	8d	8d	28-Jul-26	05-Aug-26	22-Oct-26	31-Oct-26	200d	4	100%	0%	46,111
	Backfilling, Warning Tape Works f	2d	2d	04-Aug-26	05-Aug-26	29-Oct-26	31-Oct-26	200d	1	100%	0%	4,611
	Testing and Commissioning for L	2d	2d	02-Aug-26	03-Aug-26	27-Oct-26	28-Oct-26	200d	1	100%	0%	2,306
	Bedding Layer and Installation fo	2d	2d	30-Jul-26	01-Aug-26	25-Oct-26	26-Oct-26	200d	1	100%	0%	34,583
	Excavation Works for LV Cables	2d	2d	28-Jul-26	29-Jul-26	22-Oct-26	24-Oct-26	190d	1	100%	0%	4,611
	JDH3-02-009-R103-(SL)- LV Cables	20d	20d	30-Jul-26	22-Aug-26	25-Oct-26	16-Nov-26	190d	4	100%	0%	75,300
	Backfilling, Warning Tape Works f	5d	5d	17-Aug-26	22-Aug-26	11-Nov-26	16-Nov-26	190d	1	100%	0%	7,530
	Testing and Commissioning for L	5d	5d	11-Aug-26	16-Aug-26	05-Nov-26	10-Nov-26	190d	1	100%	0%	3,765
	Bedding Layer and Installation fo	5d	5d	05-Aug-26	10-Aug-26	31-Oct-26	04-Nov-26	190d	1	100%	0%	56,475
	Excavation Works for LV Cables	5d	5d	30-Jul-26	04-Aug-26	25-Oct-26	29-Oct-26	190d	1	100%	0%	7,530
	JDH3-02-009-R103-(SL)-Lighting Po	3d	3d	05-Aug-26	08-Aug-26	22-Oct-26	25-Oct-26	209d	1	100%	0%	3,987
	Cable Connection for Lighting Po	3d	3d	05-Aug-26	08-Aug-26	22-Oct-26	25-Oct-26	209d	1	100%	0%	3,987
	JDH3-02-009-R103-(SL)- Street Ligl	6d	6d	04-Aug-26	15-Aug-26	21-Oct-26	28-Oct-26	204d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	13-Aug-26	15-Aug-26	26-Oct-26	28-Oct-26	204d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	11-Aug-26	12-Aug-26	24-Oct-26	26-Oct-26	204d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	04-Aug-26	05-Aug-26	21-Oct-26	24-Oct-26	204d	1	100%	0%	1,033
	JDH3-02-009-R103-(SL)- LV Distribu	6d	6d	06-Aug-26	17-Aug-26	24-Oct-26	31-Oct-26	204d	3	100%	0%	18,369
	Installing for Street Lighting pane	2d	2d	16-Aug-26	17-Aug-26	28-Oct-26	31-Oct-26	204d	1	100%	0%	12,858
	lean Concrete for Street Lighting	2d	2d	13-Aug-26	15-Aug-26	26-Oct-26	28-Oct-26	204d	1	100%	0%	3,674
	Levelling for Street Lighting pane	2d	2d	06-Aug-26	08-Aug-26	24-Oct-26	26-Oct-26	204d	1	100%	0%	1,837
	JDH3-02-009-R103-(SL)-KWH mete	2d	2d	18-Aug-26	19-Aug-26	31-Oct-26	02-Nov-26	204d	1	100%	0%	2,072
	Installation for KWH meter - (B2.2	2d	2d	18-Aug-26	19-Aug-26	31-Oct-26	02-Nov-26	204d	1	100%	0%	2,072
R104		40d	40d	23-Jun-26	06-Sep-26	29-Sep-26	14-Nov-26	404d	69	100%	0%	880,406
	JDH3-02-009-R104-Storm Network - S	15d	15d	07-Jul-26	30-Jul-26	29-Sep-26	15-Oct-26	429d	6	100%	0%	27,156
	JDH3-02-009-R104-(ST)-MH Works	11d	11d	07-Jul-26	26-Jul-26	29-Sep-26	11-Oct-26	429d	2	100%	0%	17,919
	Steel Coverfor MH 1200 mm - dep	4d	4d	21-Jul-26	26-Jul-26	07-Oct-26	11-Oct-26	429d	1	100%	0%	5,999
	Finishing, Benching, Testing Worl	4d	4d	07-Jul-26	11-Jul-26	29-Sep-26	03-Oct-26	432d	1	100%	0%	11,920
	JDH3-02-009-R104-(ST)-MH Works	9d	9d	12-Jul-26	28-Jul-26	04-Oct-26	13-Oct-26	429d	2	100%	0%	6,228

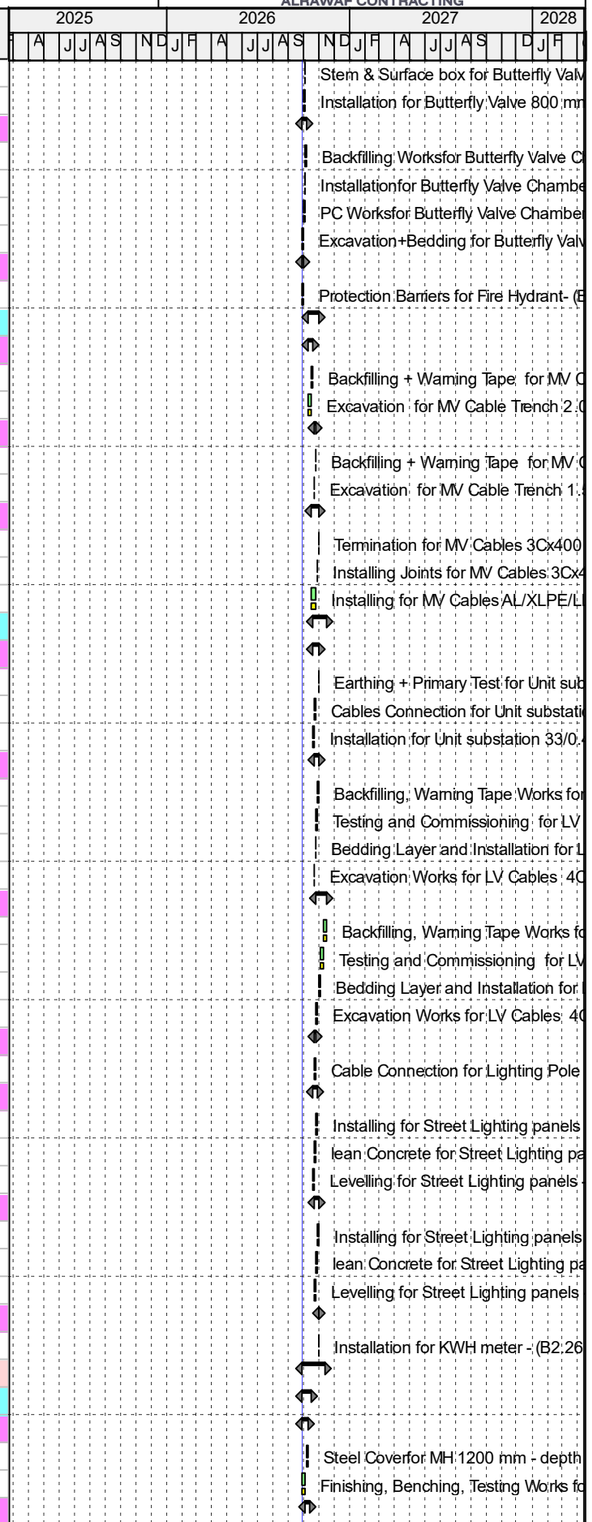


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Steel Coverfor MH 2000 mm - de	2d	2d	26-Jul-26	28-Jul-26	12-Oct-26	13-Oct-26	429d	1	100%	0%	2,127
	Finishing, Benching, Testing Worl	2d	2d	12-Jul-26	13-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	4,101
	JDH3-02-009-R104-(ST)-MH Works	9d	9d	14-Jul-26	30-Jul-26	06-Oct-26	15-Oct-26	429d	2	100%	0%	3,009
	Steel Coverfor MH 1500 mm - de	2d	2d	28-Jul-26	30-Jul-26	14-Oct-26	15-Oct-26	429d	1	100%	0%	1,003
	Finishing, Benching, Testing Worl	2d	2d	14-Jul-26	15-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	2,006
	JDH3-02-009-R104-Catch Basins (Sto	10d	10d	19-Jul-26	06-Sep-26	29-Sep-26	10-Oct-26	434d	6	100%	0%	46,309
	JDH3-02-009-R104-(ST)-For Catch I	7d	7d	19-Jul-26	26-Jul-26	29-Sep-26	07-Oct-26	434d	1	100%	0%	21,304
	Primary Test for CB GRP Pipe Lin	7d	7d	19-Jul-26	26-Jul-26	29-Sep-26	07-Oct-26	434d	1	100%	0%	21,304
	JDH3-02-009-R104-(ST)-For Catch I	2d	2d	12-Aug-26	13-Aug-26	07-Oct-26	10-Oct-26	434d	1	100%	0%	624
	Primary Test for CB GRP Pipe Lin	2d	2d	12-Aug-26	13-Aug-26	07-Oct-26	10-Oct-26	434d	1	100%	0%	624
	JDH3-02-009-R104-(ST)-Single Cat	8d	8d	15-Aug-26	23-Aug-26	29-Sep-26	07-Oct-26	436d	2	100%	0%	10,684
	Steel Coverfor single Catch Basin	4d	4d	19-Aug-26	23-Aug-26	04-Oct-26	07-Oct-26	436d	1	100%	0%	3,561
	Finishing and Insulation Works fo	4d	4d	15-Aug-26	18-Aug-26	29-Sep-26	03-Oct-26	436d	1	100%	0%	7,123
	JDH3-02-009-R104-(ST)-Double Cat	4d	4d	02-Sep-26	06-Sep-26	29-Sep-26	03-Oct-26	190d	2	100%	0%	13,697
	Steel Coverfor double Catch Basi	2d	2d	05-Sep-26	06-Sep-26	01-Oct-26	03-Oct-26	190d	1	100%	0%	4,566
	Finishing and Insulation Works fo	2d	2d	02-Sep-26	03-Sep-26	29-Sep-26	30-Sep-26	190d	1	100%	0%	9,131
	JDH3-02-009-R104-TSE Network - TSI	9d	9d	23-Jun-26	13-Jul-26	29-Sep-26	08-Oct-26	435d	17	100%	0%	106,910
	JDH3-02-009-R104-(TSE)-Butterfly '	4d	4d	30-Jun-26	04-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	32,260
	Stem & Surface box for Butterfly '	2d	2d	02-Jul-26	04-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	3,226
	Installation for Butterfly Valve 300	2d	2d	30-Jun-26	01-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	29,034
	JDH3-02-009-R104-(TSE)-Wash-Ou	4d	4d	07-Jul-26	11-Jul-26	29-Sep-26	03-Oct-26	357d	2	100%	0%	16,127
	Stem & Surface box for Wash-Ou	2d	2d	09-Jul-26	11-Jul-26	01-Oct-26	03-Oct-26	357d	1	100%	0%	1,613
	Installation for Wash-Out Valve 1(	2d	2d	07-Jul-26	08-Jul-26	29-Sep-26	30-Sep-26	357d	1	100%	0%	14,515
	JDH3-02-009-R104-(TSE)-Valve Cha	6d	6d	25-Jun-26	01-Jul-26	30-Sep-26	06-Oct-26	435d	3	100%	0%	24,403
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jun-26	01-Jul-26	05-Oct-26	06-Oct-26	435d	1	100%	0%	5,742
	Installationfor Butterfly Valve Cha	2d	2d	28-Jun-26	29-Jun-26	03-Oct-26	04-Oct-26	435d	1	100%	0%	15,790
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jun-26	27-Jun-26	30-Sep-26	01-Oct-26	435d	1	100%	0%	2,871
	JDH3-02-009-R104-(TSE)-Wash-Ou	8d	8d	23-Jun-26	13-Jul-26	29-Sep-26	07-Oct-26	355d	4	100%	0%	20,886
	Backfilling Worksfor Wash-Out Ch	2d	2d	12-Jul-26	13-Jul-26	06-Oct-26	07-Oct-26	355d	1	100%	0%	4,177
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	355d	1	100%	0%	11,487
	PC Worksfor Wash-Out Chamber	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	355d	1	100%	0%	2,089
	Excavation+Bedding for Wash-Ou	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	355d	1	100%	0%	3,133
	JDH3-02-009-R104-(TSE)-Air Valve	4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	438d	2	100%	0%	6,016
	Stem & Surface box for Air Valve	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	602
	Installation for Air Valve 50 mm or	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	5,415
	JDH3-02-009-R104-(TSE)-Air Valve	9d	9d	23-Jun-26	04-Jul-26	29-Sep-26	08-Oct-26	435d	4	100%	0%	7,218
	Backfilling Worksfor Air Valve Cha	2d	2d	02-Jul-26	04-Jul-26	07-Oct-26	08-Oct-26	435d	1	100%	0%	1,444
	Installationfor Air Valve Chamber	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	3,970
	PC Worksfor Air Valve Chamber o	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	722
	Excavation+Bedding for Air Valve	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	1,083
	JDH3-02-009-R104-Potable Water Net	18d	18d	23-Jun-26	13-Jul-26	29-Sep-26	19-Oct-26	426d	17	100%	0%	256,469
	JDH3-02-009-R104-(WT)-Butterfly V	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	436d	2	100%	0%	78,222
	Stem & Surface box for Butterfly '	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	7,822
	Installation for Butterfly Valve 400	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	70,400
	JDH3-02-009-R104-(WT)-Valve Cha	16d	16d	23-Jun-26	11-Jul-26	29-Sep-26	17-Oct-26	426d	4	100%	0%	43,007
	Backfilling Worksfor Butterfly Valv	2d	2d	09-Jul-26	11-Jul-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	8,601
	Installationfor Butterfly Valve Cha	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	23,654
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	4,301
	Excavation+Bedding for Butterfly	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	426d	1	100%	0%	6,451
	JDH3-02-009-R104-(WT)-Fire Hydra	12d	12d	25-Jun-26	08-Jul-26	01-Oct-26	14-Oct-26	426d	5	100%	0%	78,167
	Protection Barriers for Fire Hydran	2d	2d	07-Jul-26	08-Jul-26	13-Oct-26	14-Oct-26	426d	1	100%	0%	3,908
	Fire Installation for Fire Hydrant- (	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	426d	1	100%	0%	27,358
	Stem for Fire Hydrant- (B3.33 14	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	426d	1	100%	0%	23,450

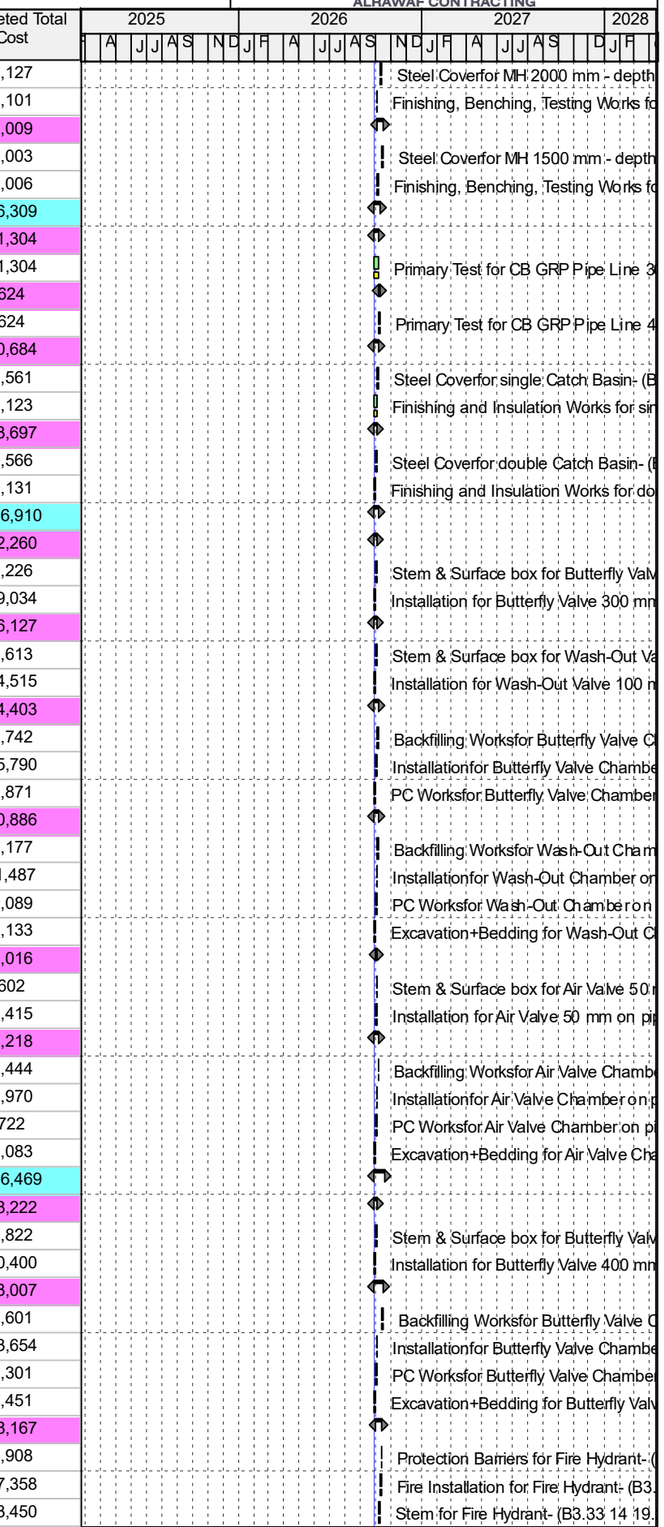

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Valve Installation for Fire Hydrant-	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	426d	1	100%	0%	15,633
	Excavation and Bedding and Pip	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	428d	1	100%	0%	7,817
	JDH3-02-009-R104-(WT)-Wash-Out	4d	4d	25-Jun-26	29-Jun-26	01-Oct-26	05-Oct-26	438d	2	100%	0%	15,346
	Stem & Surface box for Wash-Ou	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	438d	1	100%	0%	1,535
	Installation for Wash-Out Valve 1(	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	13,811
	JDH3-02-009-R104-(WT)-Wash-Out	18d	18d	23-Jun-26	13-Jul-26	29-Sep-26	19-Oct-26	426d	4	100%	0%	41,727
	Backfilling Worksfor Wash-Out Ch	2d	2d	12-Jul-26	13-Jul-26	18-Oct-26	19-Oct-26	426d	1	100%	0%	8,345
	Installationfor Wash-Out Chambe	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	22,950
	PC Worksfor Wash-Out Chamber	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	4,173
	Excavation+Bedding for Wash-Ou	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	6,259
	JDH3-02-009-R104-Electrical Network	4d	4d	14-Jul-26	18-Jul-26	08-Oct-26	12-Oct-26	355d	2	100%	0%	77,785
	JDH3-02-009-R104-(EL)-MV cables	4d	4d	14-Jul-26	18-Jul-26	08-Oct-26	12-Oct-26	355d	2	100%	0%	77,785
	Installing Joints for MV Cables 3C	2d	2d	16-Jul-26	18-Jul-26	11-Oct-26	12-Oct-26	355d	1	100%	0%	8,701
	Installing for MV Cables AL/XLPE	2d	2d	14-Jul-26	15-Jul-26	08-Oct-26	10-Oct-26	355d	1	100%	0%	69,084
	JDH3-02-009-R104-Street Lighting Ne	28d	28d	19-Jul-26	19-Aug-26	13-Oct-26	14-Nov-26	404d	21	100%	0%	365,777
	JDH3-02-009-R104-(SL)- LV Cables	12d	12d	19-Jul-26	01-Aug-26	13-Oct-26	26-Oct-26	359d	4	100%	0%	152,619
	Backfilling, Warning Tape Works f	3d	3d	29-Jul-26	01-Aug-26	24-Oct-26	26-Oct-26	359d	1	100%	0%	15,262
	Testing and Commissioning for L	3d	3d	26-Jul-26	28-Jul-26	20-Oct-26	22-Oct-26	359d	1	100%	0%	7,631
	Bedding Layer and Installation fo	3d	3d	22-Jul-26	25-Jul-26	17-Oct-26	19-Oct-26	359d	1	100%	0%	114,464
	Excavation Works for LV Cables	3d	3d	19-Jul-26	21-Jul-26	13-Oct-26	15-Oct-26	355d	1	100%	0%	15,262
	JDH3-02-009-R104-(SL)-Lighting P	14d	14d	22-Jul-26	06-Aug-26	17-Oct-26	01-Nov-26	358d	5	100%	0%	98,490
	Cable Connection for Lighting Po	4d	4d	03-Aug-26	06-Aug-26	28-Oct-26	01-Nov-26	358d	1	100%	0%	4,925
	Installation Works for Lighting Pol	4d	4d	29-Jul-26	02-Aug-26	24-Oct-26	27-Oct-26	358d	1	100%	0%	64,019
	Backfilling of RC foundation for Li	2d	2d	27-Jul-26	28-Jul-26	21-Oct-26	22-Oct-26	358d	1	100%	0%	9,849
	Installation of RC foundation for L	2d	2d	25-Jul-26	26-Jul-26	19-Oct-26	20-Oct-26	358d	1	100%	0%	9,849
	Excavation for RC foundation for	2d	2d	22-Jul-26	23-Jul-26	17-Oct-26	18-Oct-26	358d	1	100%	0%	9,849
	JDH3-02-009-R104-(SL)-Street Ligh	4d	4d	29-Jul-26	02-Aug-26	24-Oct-26	27-Oct-26	419d	2	100%	0%	24,951
	Cable Connection for Lighting(LE	2d	2d	01-Aug-26	02-Aug-26	26-Oct-26	27-Oct-26	419d	1	100%	0%	4,990
	Installation for Lighting(LED) Lur	2d	2d	29-Jul-26	30-Jul-26	24-Oct-26	25-Oct-26	419d	1	100%	0%	19,961
	JDH3-02-009-R104-(SL)-Earthing S	3d	3d	08-Aug-26	10-Aug-26	02-Nov-26	04-Nov-26	358d	1	100%	0%	5,628
	Supply, construct, connect and te	3d	3d	08-Aug-26	10-Aug-26	02-Nov-26	04-Nov-26	358d	1	100%	0%	5,628
	JDH3-02-009-R104-(SL)-Earthing S	2d	2d	11-Aug-26	12-Aug-26	05-Nov-26	07-Nov-26	404d	1	100%	0%	3,407
	Supply, construct, connect and te	2d	2d	11-Aug-26	12-Aug-26	05-Nov-26	07-Nov-26	404d	1	100%	0%	3,407
	JDH3-02-009-R104-(SL)- Street Ligh	6d	6d	13-Aug-26	19-Aug-26	08-Nov-26	14-Nov-26	404d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	18-Aug-26	19-Aug-26	12-Nov-26	14-Nov-26	404d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	16-Aug-26	17-Aug-26	10-Nov-26	11-Nov-26	404d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	13-Aug-26	15-Aug-26	08-Nov-26	09-Nov-26	404d	1	100%	0%	1,033
	JDH3-02-009-R104-(SL)- LV Cables	2d	2d	03-Aug-26	04-Aug-26	28-Oct-26	29-Oct-26	413d	1	100%	0%	3,279
	Installation for LV Cables 3-1xCx	2d	2d	03-Aug-26	04-Aug-26	28-Oct-26	29-Oct-26	413d	1	100%	0%	3,279
	JDH3-02-009-R104-(SL)- LV Cables	20d	20d	22-Jul-26	13-Aug-26	17-Oct-26	08-Nov-26	355d	4	100%	0%	67,073
	Backfilling, Warning Tape Works f	5d	5d	09-Aug-26	13-Aug-26	03-Nov-26	08-Nov-26	355d	1	100%	0%	6,707
	Testing and Commissioning for L	5d	5d	03-Aug-26	08-Aug-26	28-Oct-26	02-Nov-26	355d	1	100%	0%	3,354
	Bedding Layer and Installation fo	5d	5d	28-Jul-26	02-Aug-26	22-Oct-26	27-Oct-26	355d	1	100%	0%	50,304
	Excavation Works for LV Cables	5d	5d	22-Jul-26	27-Jul-26	17-Oct-26	21-Oct-26	355d	1	100%	0%	6,707
R101		29d	29d	23-Jun-26	05-Sep-26	29-Sep-26	01-Nov-26	415d	50	100%	0%	896,147
	JDH3-02-009-R101-TSE Network - TSI	19d	19d	02-Aug-26	05-Sep-26	29-Sep-26	21-Oct-26	425d	16	100%	0%	161,285
	JDH3-02-009-R101-(TSE)-HDPE Pip	2d	2d	02-Aug-26	03-Aug-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	42,219
	Primary Test for HDPE Pipe Line	2d	2d	02-Aug-26	03-Aug-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	42,219
	JDH3-02-009-R101-(TSE)-HDPE Pip	2d	2d	09-Aug-26	10-Aug-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	943
	Primary Test for HDPE Pipe Line	2d	2d	09-Aug-26	10-Aug-26	30-Sep-26	03-Oct-26	441d	1	100%	0%	943
	JDH3-02-009-R101-(TSE)-Butterfly	2d	2d	23-Aug-26	24-Aug-26	07-Oct-26	10-Oct-26	425d	1	100%	0%	13,037
	Stem & Surface box for Butterfly	2d	2d	23-Aug-26	24-Aug-26	07-Oct-26	10-Oct-26	425d	1	100%	0%	13,037
	JDH3-02-009-R101-(TSE)-Wash-Ou	10d	10d	23-Aug-26	26-Aug-26	30-Sep-26	12-Oct-26	425d	2	100%	0%	33,818

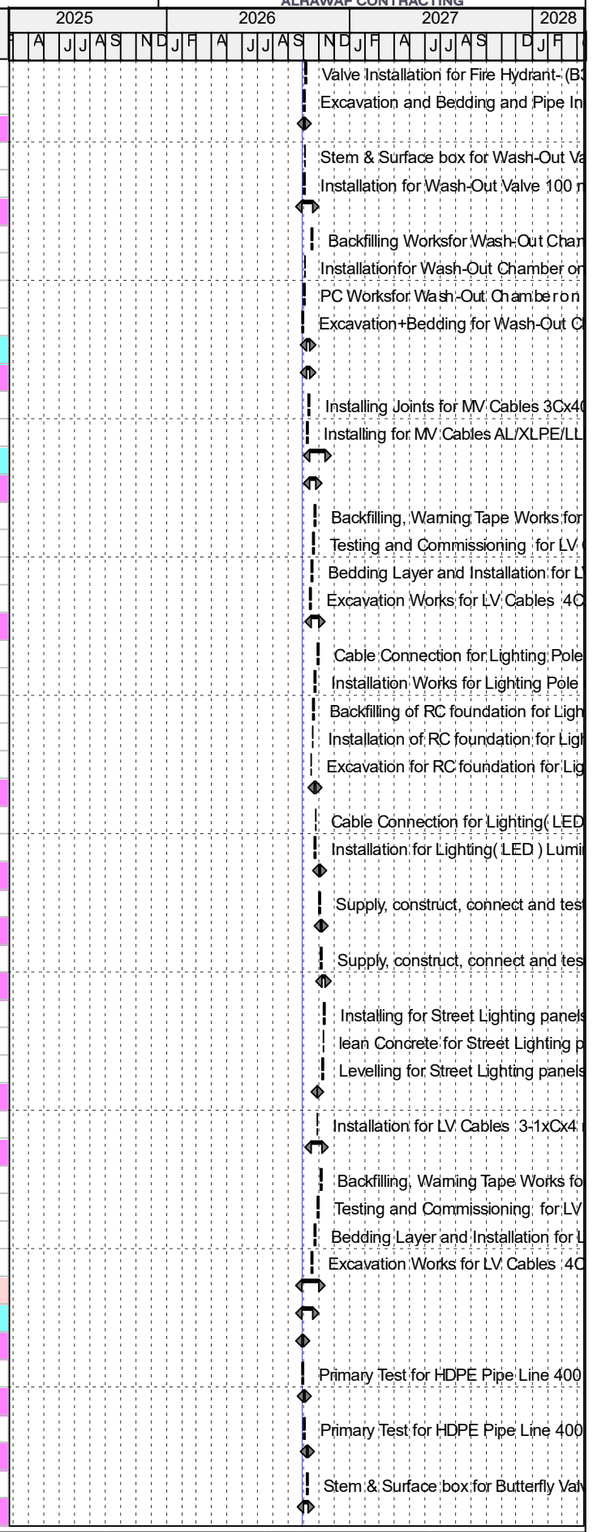


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Stem & Surface box for Wash-Ou	2d	2d	25-Aug-26	26-Aug-26	10-Oct-26	12-Oct-26	425d	1	100%	0%	3,382
	Installation for Wash-Out Valve 1(	2d	2d	23-Aug-26	24-Aug-26	30-Sep-26	03-Oct-26	431d	1	100%	0%	30,436
	JDH3-02-009-R101-(TSE)-Air Valve	10d	10d	25-Aug-26	29-Aug-26	03-Oct-26	14-Oct-26	425d	2	100%	0%	7,790
	Stem & Surface box for Air Valve	2d	2d	27-Aug-26	29-Aug-26	12-Oct-26	14-Oct-26	425d	1	100%	0%	779
	Installation for Air Valve 65 mm or	2d	2d	25-Aug-26	26-Aug-26	03-Oct-26	05-Oct-26	431d	1	100%	0%	7,011
	JDH3-02-009-R101-(TSE)-Valve Cha	2d	2d	30-Aug-26	31-Aug-26	14-Oct-26	17-Oct-26	425d	1	100%	0%	14,395
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Aug-26	31-Aug-26	14-Oct-26	17-Oct-26	425d	1	100%	0%	14,395
	JDH3-02-009-R101-(TSE)-Wash-Ou	16d	16d	04-Aug-26	02-Sep-26	30-Sep-26	19-Oct-26	425d	4	100%	0%	41,949
	Backfilling Worksfor Wash-Out Ch	2d	2d	01-Sep-26	02-Sep-26	17-Oct-26	19-Oct-26	425d	1	100%	0%	8,390
	Installationfor Wash-Out Chambe	2d	2d	09-Aug-26	10-Aug-26	05-Oct-26	07-Oct-26	425d	1	100%	0%	23,072
	PC Worksfor Wash-Out Chamber	2d	2d	06-Aug-26	08-Aug-26	03-Oct-26	05-Oct-26	425d	1	100%	0%	4,195
	Excavation+Bedding for Wash-Ou	2d	2d	04-Aug-26	05-Aug-26	30-Sep-26	03-Oct-26	425d	1	100%	0%	6,292
	JDH3-02-009-R101-(TSE)-Air Valve	16d	16d	06-Aug-26	05-Sep-26	03-Oct-26	21-Oct-26	425d	4	100%	0%	7,134
	Backfilling Worksfor Air Valve Cha	2d	2d	03-Sep-26	05-Sep-26	19-Oct-26	21-Oct-26	425d	1	100%	0%	1,427
	Installationfor Air Valve Chamber	2d	2d	11-Aug-26	12-Aug-26	07-Oct-26	10-Oct-26	433d	1	100%	0%	3,924
	PC Worksfor Air Valve Chamber o	2d	2d	09-Aug-26	10-Aug-26	05-Oct-26	07-Oct-26	433d	1	100%	0%	713
	Excavation+Bedding for Air Valve	2d	2d	06-Aug-26	08-Aug-26	03-Oct-26	05-Oct-26	433d	1	100%	0%	1,070
	JDH3-02-009-R101-Potable Water Net	29d	29d	23-Jun-26	01-Aug-26	29-Sep-26	01-Nov-26	415d	32	100%	0%	717,246
	JDH3-02-009-R101-(WT)-HDPE Pipe	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	1	100%	0%	27,753
	Primary Test for HDPE Pipe Line 8	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	440d	1	100%	0%	27,753
	JDH3-02-009-R101-(WT)-HDPE Pipe	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	36,144
	Primary Test for HDPE Pipe Line 8	3d	3d	23-Jun-26	25-Jun-26	29-Sep-26	01-Oct-26	441d	1	100%	0%	36,144
	JDH3-02-009-R101-(WT)-HDPE Pipe	3d	3d	29-Jun-26	01-Jul-26	29-Sep-26	01-Oct-26	415d	1	100%	0%	59,286
	Primary Test for HDPE Pipe Line 8	3d	3d	29-Jun-26	01-Jul-26	29-Sep-26	01-Oct-26	415d	1	100%	0%	59,286
	JDH3-02-009-R101-(WT)-Butterfly V	4d	4d	29-Jun-26	02-Jul-26	29-Sep-26	03-Oct-26	426d	2	100%	0%	78,222
	Stem & Surface box for Butterfly '	2d	2d	01-Jul-26	02-Jul-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	7,822
	Installation for Butterfly Valve 400	2d	2d	29-Jun-26	30-Jun-26	29-Sep-26	30-Sep-26	426d	1	100%	0%	70,400
	JDH3-02-009-R101-(WT)-Butterfly V	4d	4d	01-Jul-26	05-Jul-26	01-Oct-26	05-Oct-26	426d	2	100%	0%	197,263
	Stem & Surface box for Butterfly '	2d	2d	04-Jul-26	05-Jul-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	19,726
	Installation for Butterfly Valve 800	2d	2d	01-Jul-26	02-Jul-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	177,537
	JDH3-02-009-R101-(WT)-Wash-Out	4d	4d	04-Jul-26	07-Jul-26	04-Oct-26	07-Oct-26	426d	2	100%	0%	27,358
	Stem & Surface box for Wash-Ou	2d	2d	06-Jul-26	07-Jul-26	06-Oct-26	07-Oct-26	426d	1	100%	0%	2,736
	Installation for Wash-Out Valve 2(	2d	2d	04-Jul-26	05-Jul-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	24,622
	JDH3-02-009-R101-(WT)-Air Valve-	4d	4d	06-Jul-26	09-Jul-26	06-Oct-26	10-Oct-26	426d	2	100%	0%	25,013
	Stem & Surface box for Air Valve	2d	2d	08-Jul-26	09-Jul-26	08-Oct-26	10-Oct-26	426d	1	100%	0%	2,501
	Installation for Air Valve 110 mm (	2d	2d	06-Jul-26	07-Jul-26	06-Oct-26	07-Oct-26	426d	1	100%	0%	22,512
	JDH3-02-009-R101-(WT)-Valve Cha	20d	20d	02-Jul-26	25-Jul-26	03-Oct-26	25-Oct-26	415d	4	100%	0%	43,007
	Backfilling Worksfor Butterfly Valv	2d	2d	23-Jul-26	25-Jul-26	24-Oct-26	25-Oct-26	415d	1	100%	0%	8,601
	Installationfor Butterfly Valve Cha	2d	2d	07-Jul-26	08-Jul-26	07-Oct-26	08-Oct-26	427d	1	100%	0%	23,654
	PC Worksfor Butterfly Valve Chan	2d	2d	05-Jul-26	06-Jul-26	05-Oct-26	06-Oct-26	427d	1	100%	0%	4,301
	Excavation+Bedding for Butterfly	2d	2d	02-Jul-26	04-Jul-26	03-Oct-26	04-Oct-26	415d	1	100%	0%	6,451
	JDH3-02-009-R101-(WT)-Valve Cha	20d	20d	05-Jul-26	27-Jul-26	05-Oct-26	27-Oct-26	415d	4	100%	0%	95,987
	Backfilling Worksfor Butterfly Valv	2d	2d	26-Jul-26	27-Jul-26	26-Oct-26	27-Oct-26	415d	1	100%	0%	19,197
	Installationfor Butterfly Valve Cha	2d	2d	09-Jul-26	11-Jul-26	10-Oct-26	11-Oct-26	427d	1	100%	0%	52,793
	PC Worksfor Butterfly Valve Chan	2d	2d	07-Jul-26	08-Jul-26	07-Oct-26	08-Oct-26	427d	1	100%	0%	9,599
	Excavation+Bedding for Butterfly	2d	2d	05-Jul-26	06-Jul-26	05-Oct-26	06-Oct-26	415d	1	100%	0%	14,398
	JDH3-02-009-R101-(WT)-Wash-Out	20d	20d	07-Jul-26	29-Jul-26	07-Oct-26	29-Oct-26	415d	4	100%	0%	32,136
	Backfilling Worksfor Wash-Out Ch	2d	2d	28-Jul-26	29-Jul-26	28-Oct-26	29-Oct-26	415d	1	100%	0%	6,427
	Installationfor Wash-Out Chambe	2d	2d	12-Jul-26	13-Jul-26	12-Oct-26	13-Oct-26	427d	1	100%	0%	17,675
	PC Worksfor Wash-Out Chamber	2d	2d	09-Jul-26	11-Jul-26	10-Oct-26	11-Oct-26	427d	1	100%	0%	3,214
	Excavation+Bedding for Wash-Ou	2d	2d	07-Jul-26	08-Jul-26	07-Oct-26	08-Oct-26	415d	1	100%	0%	4,820
	JDH3-02-009-R101-(WT)-Air Valve (	20d	20d	09-Jul-26	01-Aug-26	10-Oct-26	01-Nov-26	415d	4	100%	0%	7,139
	Backfilling Worksfor Air Valve Cha	2d	2d	30-Jul-26	01-Aug-26	31-Oct-26	01-Nov-26	415d	1	100%	0%	1,428

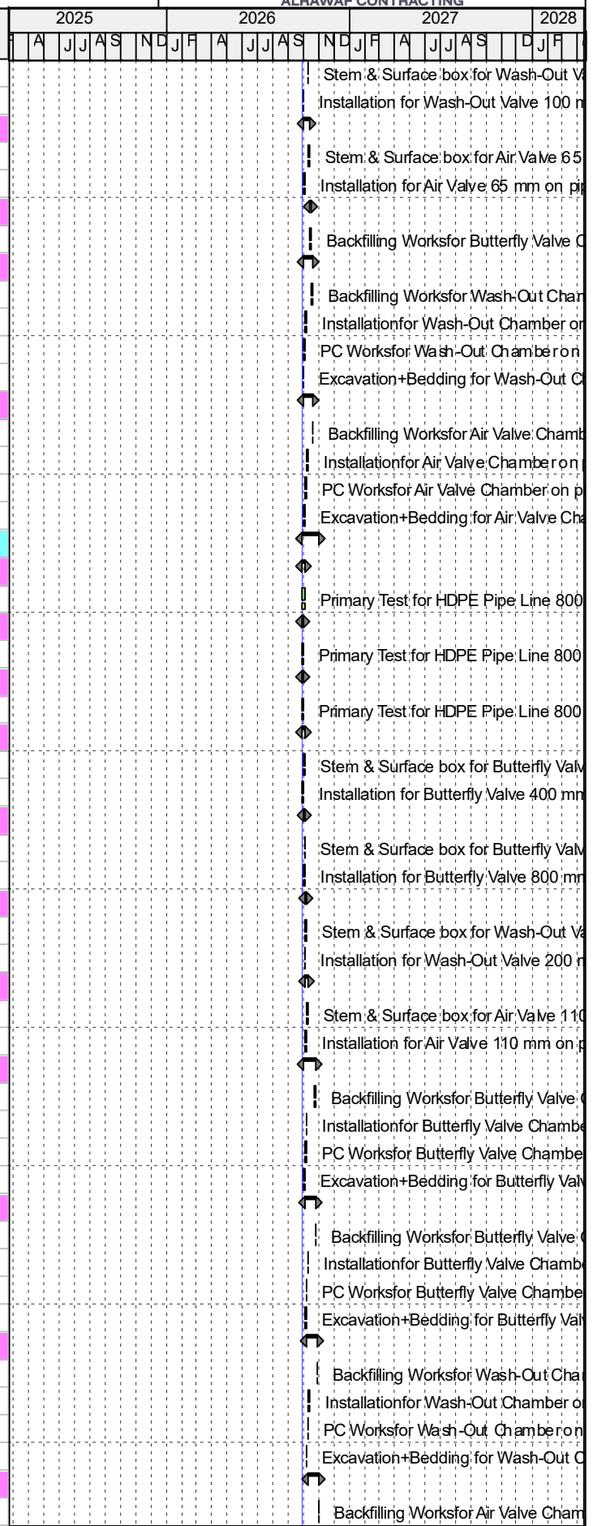

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Installationfor Air Valve Chamber (	2d	2d	14-Jul-26	15-Jul-26	14-Oct-26	15-Oct-26	427d	1	100%	0%	3,926
	PC Worksfor Air Valve Chamber o	2d	2d	12-Jul-26	13-Jul-26	12-Oct-26	13-Oct-26	427d	1	100%	0%	714
	Excavation+Bedding for Air Valve	2d	2d	09-Jul-26	11-Jul-26	10-Oct-26	11-Oct-26	415d	1	100%	0%	1,071
	JDH3-02-009-R101-(WT)-Fire Hydra	10d	10d	12-Jul-26	22-Jul-26	12-Oct-26	22-Oct-26	415d	5	100%	0%	87,937
	Protection Barriers for Fire Hydrar	2d	2d	21-Jul-26	22-Jul-26	21-Oct-26	22-Oct-26	415d	1	100%	0%	4,397
	Fire Installation for Fire Hydrant- (	2d	2d	19-Jul-26	20-Jul-26	19-Oct-26	20-Oct-26	415d	1	100%	0%	30,778
	Stem for Fire Hydrant- (B3.33 14	2d	2d	16-Jul-26	18-Jul-26	17-Oct-26	18-Oct-26	415d	1	100%	0%	26,381
	Valve Installation for Fire Hydrant-	2d	2d	14-Jul-26	15-Jul-26	14-Oct-26	15-Oct-26	415d	1	100%	0%	17,587
	Excavation and Bedding and Pipe	2d	2d	12-Jul-26	13-Jul-26	12-Oct-26	13-Oct-26	415d	1	100%	0%	8,794
	JDH3-02-009-R101-Catch Basins (Sto	5d	5d	27-Jul-26	04-Aug-26	29-Sep-26	04-Oct-26	410d	2	100%	0%	17,616
	JDH3-02-009-R101-(ST)-Single Cat	5d	5d	29-Jul-26	04-Aug-26	29-Sep-26	04-Oct-26	410d	1	100%	0%	9,315
	Finishing and Insulation Works fo	5d	5d	29-Jul-26	04-Aug-26	29-Sep-26	04-Oct-26	410d	1	100%	0%	9,315
	JDH3-02-009-R101-(ST)-Double Cat	2d	2d	27-Jul-26	29-Jul-26	29-Sep-26	30-Sep-26	413d	1	100%	0%	8,301
	Finishing and Insulation Works fo	2d	2d	27-Jul-26	29-Jul-26	29-Sep-26	30-Sep-26	413d	1	100%	0%	8,301
R102		45d	45d	02-Jul-26	29-Sep-26	29-Sep-26	19-Nov-26	399d	81	99.91%	0%	1,493,463
	JDH3-02-009-R102-Catch Basins (Sto	5d	5d	22-Jul-26	03-Aug-26	29-Sep-26	04-Oct-26	405d	2	100%	0%	21,758
	JDH3-02-009-R102-(ST)-Single Cat	5d	5d	29-Jul-26	03-Aug-26	29-Sep-26	04-Oct-26	405d	1	100%	0%	10,136
	Finishing and Insulation Works fo	5d	5d	29-Jul-26	03-Aug-26	29-Sep-26	04-Oct-26	405d	1	100%	0%	10,136
	JDH3-02-009-R102-(ST)-Double Cat	2d	2d	22-Jul-26	23-Jul-26	29-Sep-26	30-Sep-26	408d	1	100%	0%	11,622
	Finishing and Insulation Works fo	2d	2d	22-Jul-26	23-Jul-26	29-Sep-26	30-Sep-26	408d	1	100%	0%	11,622
	JDH3-02-009-R102-TSE Network - TSI	10d	10d	12-Jul-26	10-Aug-26	29-Sep-26	10-Oct-26	434d	24	100%	0%	226,152
	JDH3-02-009-R102-(TSE)-Butterfly '	4d	4d	14-Jul-26	18-Jul-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	78,222
	Stem & Surface box for Butterfly '	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	7,822
	Installation for Butterfly Valve 400	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	70,400
	JDH3-02-009-R102-(TSE)-Wash-Ou	4d	4d	23-Jul-26	27-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	16,127
	Stem & Surface box for Wash-Ou	2d	2d	26-Jul-26	27-Jul-26	01-Oct-26	03-Oct-26	440d	1	100%	0%	1,613
	Installation for Wash-Out Valve 1(	2d	2d	23-Jul-26	25-Jul-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	14,515
	JDH3-02-009-R102-(TSE)-Wash-Ou	8d	8d	02-Aug-26	10-Aug-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	20,886
	Backfilling Worksfor Wash-Out Ch	2d	2d	09-Aug-26	10-Aug-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	4,177
	Installationfor Wash-Out Chambe	2d	2d	06-Aug-26	08-Aug-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	11,487
	PC Worksfor Wash-Out Chamber	2d	2d	04-Aug-26	05-Aug-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,089
	Excavation+Bedding for Wash-Ou	2d	2d	02-Aug-26	03-Aug-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	3,133
	JDH3-02-009-R102-(TSE)-Wash-Ou	4d	4d	12-Jul-26	15-Jul-26	29-Sep-26	03-Oct-26	436d	2	100%	0%	16,909
	Stem & Surface box for Wash-Ou	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	1,691
	Installation for Wash-Out Valve 1(	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	15,218
	JDH3-02-009-R102-(TSE)-Air Valve	4d	4d	14-Jul-26	18-Jul-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	15,581
	Stem & Surface box for Air Valve	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	1,558
	Installation for Air Valve 65 mm or	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	14,023
	JDH3-02-009-R102-(TSE)-Valve Cha	8d	8d	12-Jul-26	20-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	43,184
	Backfilling Worksfor Butterfly Valv	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	8,637
	Installationfor Butterfly Valve Cha	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	23,751
	PC Worksfor Butterfly Valve Chan	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	4,318
	Excavation+Bedding for Butterfly	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	6,478
	JDH3-02-009-R102-(TSE)-Wash-Ou	8d	8d	12-Jul-26	20-Jul-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	20,974
	Backfilling Worksfor Wash-Out Ch	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	4,195
	Installationfor Wash-Out Chambe	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	11,536
	PC Worksfor Wash-Out Chamber	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,097
	Excavation+Bedding for Wash-Ou	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	389d	1	100%	0%	3,146
	JDH3-02-009-R102-(TSE)-Air Valve	8d	8d	14-Jul-26	22-Jul-26	01-Oct-26	10-Oct-26	427d	4	100%	0%	14,269
	Backfilling Worksfor Air Valve Cha	2d	2d	21-Jul-26	22-Jul-26	08-Oct-26	10-Oct-26	427d	1	100%	0%	2,854
	Installationfor Air Valve Chamber (	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	427d	1	100%	0%	7,848
	PC Worksfor Air Valve Chamber o	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	427d	1	100%	0%	1,427
	Excavation+Bedding for Air Valve	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	389d	1	100%	0%	2,140

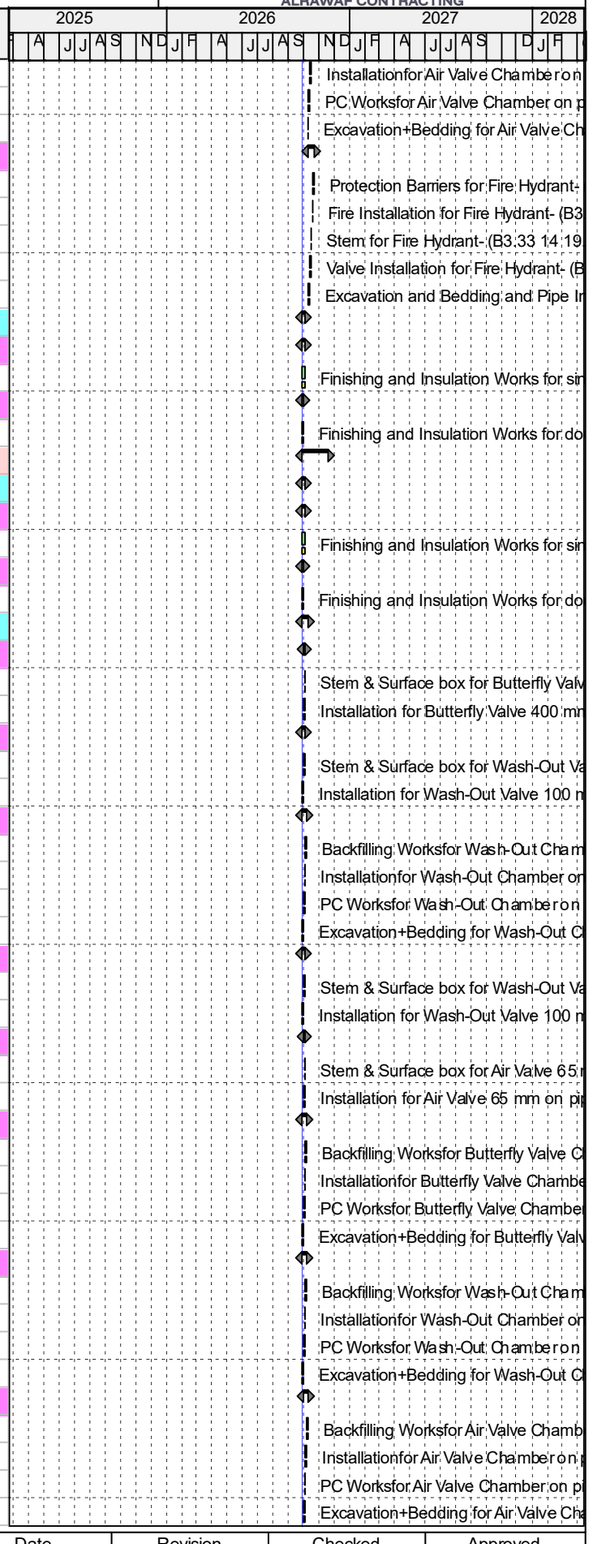

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R102-Potable Water Net	25d	25d	02-Jul-26	02-Sep-26	29-Sep-26	28-Oct-26	419d	33	100%	0%	387,000
	JDH3-02-009-R102-(WT)-Wash-Out	4d	4d	05-Jul-26	08-Jul-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	27,358
	Stem & Surface box for Wash-Ou	2d	2d	07-Jul-26	08-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	2,736
	Installation for Wash-Out Valve 2(	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	24,622
	JDH3-02-009-R102-(WT)-Wash-Out	8d	8d	02-Jul-26	11-Jul-26	29-Sep-26	07-Oct-26	434d	4	100%	0%	32,136
	Backfilling Worksfor Wash-Out Ch	2d	2d	09-Jul-26	11-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	6,427
	Installationfor Wash-Out Chambe	2d	2d	07-Jul-26	08-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	17,675
	PC Worksfor Wash-Out Chamber	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	3,214
	Excavation+Bedding for Wash-Ou	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	4,820
	JDH3-02-009-R102-(WT)-HDPE Pip	2d	2d	06-Aug-26	08-Aug-26	29-Sep-26	30-Sep-26	369d	1	100%	0%	1,257
	Primary Test for HDPE Pipe Line	2d	2d	06-Aug-26	08-Aug-26	29-Sep-26	30-Sep-26	369d	1	100%	0%	1,257
	JDH3-02-009-R102-(WT)-HDPE Pip	9d	9d	18-Jul-26	27-Jul-26	18-Oct-26	28-Oct-26	419d	1	100%	0%	3,141
	Primary Test for HDPE Pipe Line	9d	9d	18-Jul-26	27-Jul-26	18-Oct-26	28-Oct-26	419d	1	100%	0%	3,141
	JDH3-02-009-R102-(WT)-HDPE Pip	9d	9d	07-Jul-26	16-Jul-26	07-Oct-26	18-Oct-26	419d	1	100%	0%	23,070
	Primary Test for HDPE Pipe Line	9d	9d	07-Jul-26	16-Jul-26	07-Oct-26	18-Oct-26	419d	1	100%	0%	23,070
	JDH3-02-009-R102-(WT)-HDPE Pip	2d	2d	05-Jul-26	06-Jul-26	05-Oct-26	07-Oct-26	419d	1	100%	0%	71,275
	Primary Test for HDPE Pipe Line	2d	2d	05-Jul-26	06-Jul-26	05-Oct-26	07-Oct-26	419d	1	100%	0%	71,275
	JDH3-02-009-R102-(WT)-Butterfly V	14d	14d	11-Aug-26	26-Aug-26	04-Oct-26	19-Oct-26	369d	2	100%	0%	16,130
	Stem & Surface box for Butterfly	2d	2d	25-Aug-26	26-Aug-26	18-Oct-26	19-Oct-26	369d	1	100%	0%	1,613
	Installation for Butterfly Valve 300	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	379d	1	100%	0%	14,517
	JDH3-02-009-R102-(WT)-Butterfly V	14d	14d	13-Aug-26	29-Aug-26	06-Oct-26	21-Oct-26	369d	2	100%	0%	65,754
	Stem & Surface box for Butterfly	2d	2d	27-Aug-26	29-Aug-26	20-Oct-26	21-Oct-26	369d	1	100%	0%	6,575
	Installation for Butterfly Valve 800	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	379d	1	100%	0%	59,179
	JDH3-02-009-R102-(WT)-Air Valve-	4d	4d	07-Jul-26	11-Jul-26	04-Oct-26	07-Oct-26	436d	2	100%	0%	25,013
	Stem & Surface box for Air Valve	2d	2d	09-Jul-26	11-Jul-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	2,501
	Installation for Air Valve 110 mm (	2d	2d	07-Jul-26	08-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	22,512
	JDH3-02-009-R102-(WT)-Valve Cha	20d	20d	09-Aug-26	31-Aug-26	01-Oct-26	24-Oct-26	369d	4	100%	0%	14,336
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Aug-26	31-Aug-26	22-Oct-26	24-Oct-26	369d	1	100%	0%	2,867
	Installationfor Butterfly Valve Cha	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	381d	1	100%	0%	7,885
	PC Worksfor Butterfly Valve Chan	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	381d	1	100%	0%	1,434
	Excavation+Bedding for Butterfly	2d	2d	09-Aug-26	10-Aug-26	01-Oct-26	03-Oct-26	369d	1	100%	0%	2,150
	JDH3-02-009-R102-(WT)-Valve Cha	20d	20d	11-Aug-26	02-Sep-26	04-Oct-26	26-Oct-26	369d	4	100%	0%	31,996
	Backfilling Worksfor Butterfly Valv	2d	2d	01-Sep-26	02-Sep-26	25-Oct-26	26-Oct-26	369d	1	100%	0%	6,399
	Installationfor Butterfly Valve Cha	2d	2d	16-Aug-26	17-Aug-26	08-Oct-26	10-Oct-26	381d	1	100%	0%	17,598
	PC Worksfor Butterfly Valve Chan	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	381d	1	100%	0%	3,200
	Excavation+Bedding for Butterfly	2d	2d	11-Aug-26	12-Aug-26	04-Oct-26	05-Oct-26	369d	1	100%	0%	4,799
	JDH3-02-009-R102-(WT)-Air Valve (	8d	8d	05-Jul-26	13-Jul-26	01-Oct-26	10-Oct-26	434d	4	100%	0%	7,139
	Backfilling Worksfor Air Valve Cha	2d	2d	12-Jul-26	13-Jul-26	08-Oct-26	10-Oct-26	434d	1	100%	0%	1,428
	Installationfor Air Valve Chamber	2d	2d	09-Jul-26	11-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	3,926
	PC Worksfor Air Valve Chamber o	2d	2d	07-Jul-26	08-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	714
	Excavation+Bedding for Air Valve	2d	2d	05-Jul-26	06-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	1,071
	JDH3-02-009-R102-(WT)-Fire Hydra	10d	10d	13-Aug-26	24-Aug-26	06-Oct-26	17-Oct-26	369d	5	100%	0%	68,396
	Protection Barriers for Fire Hydrar	2d	2d	23-Aug-26	24-Aug-26	15-Oct-26	17-Oct-26	369d	1	100%	0%	3,420
	Fire Installation for Fire Hydrant- (	2d	2d	20-Aug-26	22-Aug-26	13-Oct-26	14-Oct-26	369d	1	100%	0%	23,939
	Stem for Fire Hydrant- (B3.33 14	2d	2d	18-Aug-26	19-Aug-26	11-Oct-26	12-Oct-26	369d	1	100%	0%	20,519
	Valve Installation for Fire Hydrant-	2d	2d	16-Aug-26	17-Aug-26	08-Oct-26	10-Oct-26	369d	1	100%	0%	13,679
	Excavation and Bedding and Pipe	2d	2d	13-Aug-26	15-Aug-26	06-Oct-26	07-Oct-26	369d	1	100%	0%	6,840
	JDH3-02-009-R102-Electrical Network	21d	21d	03-Sep-26	28-Sep-26	27-Oct-26	19-Nov-26	394d	5	100%	0%	731,338
	JDH3-02-009-R102-(EL)-MV cable t	4d	4d	09-Sep-26	13-Sep-26	02-Nov-26	05-Nov-26	406d	2	100%	0%	1,807
	Backfilling + Warning Tape for MV	2d	2d	12-Sep-26	13-Sep-26	04-Nov-26	05-Nov-26	406d	1	100%	0%	723
	Excavation for MV Cable Trench	2d	2d	09-Sep-26	10-Sep-26	02-Nov-26	03-Nov-26	406d	1	100%	0%	1,084
	JDH3-02-009-R102-(EL)-MV cable t	5d	5d	03-Sep-26	08-Sep-26	27-Oct-26	01-Nov-26	369d	1	100%	0%	6,316
	Excavation for MV Cable Trench	5d	5d	03-Sep-26	08-Sep-26	27-Oct-26	01-Nov-26	369d	1	100%	0%	6,316




Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R102-(EL)-MV cables	16d	16d	09-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	394d	2	100%	0%	723,216
	Installing Joints for MV Cables 3C	2d	2d	27-Sep-26	28-Sep-26	18-Nov-26	19-Nov-26	394d	1	100%	0%	29,004
	Installing for MV Cables AL/XLPE	14d	14d	09-Sep-26	26-Sep-26	02-Nov-26	17-Nov-26	394d	1	100%	0%	694,212
	JDH3-02-009-R102-Street Lighting Ne	12d	12d	03-Sep-26	29-Sep-26	27-Oct-26	09-Nov-26	369d	9	97.67%	0%	58,667
	JDH3-02-009-R102-(SL)- LV Cables	8d	8d	03-Sep-26	12-Sep-26	27-Oct-26	04-Nov-26	369d	4	100%	0%	40,144
	Backfilling, Warning Tape Works f	2d	2d	10-Sep-26	12-Sep-26	03-Nov-26	04-Nov-26	369d	1	100%	0%	4,014
	Testing and Commissioning for L	2d	2d	08-Sep-26	09-Sep-26	01-Nov-26	02-Nov-26	369d	1	100%	0%	2,007
	Bedding Layer and Installation fo	2d	2d	06-Sep-26	07-Sep-26	29-Oct-26	31-Oct-26	369d	1	100%	0%	30,108
	Excavation Works for LV Cables	2d	2d	03-Sep-26	05-Sep-26	27-Oct-26	28-Oct-26	369d	1	100%	0%	4,014
	JDH3-02-009-R102-(SL)- LV Cables	10d	10d	15-Sep-26	29-Sep-26	29-Oct-26	09-Nov-26	369d	2	83.33%	0%	8,192
	Backfilling, Warning Tape Works f	4d	4d	26-Sep-26	29-Sep-26	05-Nov-26	09-Nov-26	369d	1	75%	0%	5,462
	Testing and Commissioning for L	4d	4d	15-Sep-26	19-Sep-26	29-Oct-26	02-Nov-26	371d	1	100%	0%	2,731
	JDH3-02-009-R102-(SL)- Street Ligl	6d	6d	13-Sep-26	19-Sep-26	29-Oct-26	04-Nov-26	369d	3	100%	0%	10,331
	Installing for Street Lighting pane	2d	2d	17-Sep-26	19-Sep-26	03-Nov-26	04-Nov-26	369d	1	100%	0%	7,232
	lean Concrete for Street Lighting	2d	2d	15-Sep-26	16-Sep-26	01-Nov-26	02-Nov-26	369d	1	100%	0%	2,066
	Levelling for Street Lighting pane	2d	2d	13-Sep-26	14-Sep-26	29-Oct-26	31-Oct-26	369d	1	100%	0%	1,033
	JDH3-02-009-R102-Telecommunicatic	20d	20d	27-Jul-26	18-Aug-26	29-Sep-26	21-Oct-26	424d	8	100%	0%	68,547
	JDH3-02-009-R102-(TEL)-Reinforce	8d	8d	27-Jul-26	04-Aug-26	29-Sep-26	07-Oct-26	424d	4	100%	0%	3,766
	Backfilling Works for RC Duct 6-w	2d	2d	03-Aug-26	04-Aug-26	06-Oct-26	07-Oct-26	424d	1	100%	0%	377
	Pouring RC Concrete Cover for R	2d	2d	01-Aug-26	02-Aug-26	04-Oct-26	05-Oct-26	424d	1	100%	0%	1,130
	Installation for RC Duct 6-ways du	2d	2d	29-Jul-26	30-Jul-26	01-Oct-26	03-Oct-26	424d	1	100%	0%	1,695
	Excavation Works for RC Duct 6-w	2d	2d	27-Jul-26	28-Jul-26	29-Sep-26	30-Sep-26	424d	1	100%	0%	565
	JDH3-02-009-R102-(TEL)-Unreinfor	12d	12d	05-Aug-26	18-Aug-26	08-Oct-26	21-Oct-26	424d	4	100%	0%	64,781
	Backfilling Works for Duct 6-ways	2d	2d	17-Aug-26	18-Aug-26	20-Oct-26	21-Oct-26	424d	1	100%	0%	6,478
	Pouring PC Concrete Cover for D	4d	4d	12-Aug-26	16-Aug-26	15-Oct-26	19-Oct-26	424d	1	100%	0%	12,956
	Installation for Duct 6-ways ducts,	4d	4d	08-Aug-26	11-Aug-26	11-Oct-26	14-Oct-26	424d	1	100%	0%	35,629
	Excavation Works for Duct 6-ways	2d	2d	05-Aug-26	06-Aug-26	08-Oct-26	10-Oct-26	424d	1	100%	0%	9,717
	R100	19d	19d	25-Jun-26	24-Sep-26	29-Sep-26	21-Oct-26	425d	10	100%	0%	230,734
	JDH3-02-009-R100-TSE Network - TSI	3d	3d	25-Jun-26	01-Aug-26	29-Sep-26	03-Oct-26	439d	2	100%	0%	4,484
	JDH3-02-009-R100-(TSE)-Butterfly '	2d	2d	25-Jun-26	28-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	1,613
	Stem & Surface box for Butterfly '	2d	2d	25-Jun-26	28-Jun-26	29-Sep-26	30-Sep-26	440d	1	100%	0%	1,613
	JDH3-02-009-R100-(TSE)-Valve Cha	2d	2d	30-Jul-26	01-Aug-26	30-Sep-26	03-Oct-26	425d	1	100%	0%	2,871
	Backfilling Worksfor Butterfly Valv	2d	2d	30-Jul-26	01-Aug-26	30-Sep-26	03-Oct-26	425d	1	100%	0%	2,871
	JDH3-02-009-R100-Potable Water Net	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	1,466
	JDH3-02-009-R100-(WT)-Fire Hydra	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	1,466
	Protection Barriers for Fire Hydran	2d	2d	02-Jul-26	04-Jul-26	29-Sep-26	30-Sep-26	442d	1	100%	0%	1,466
	JDH3-02-009-R100-Street Lighting Ne	19d	19d	02-Aug-26	24-Sep-26	29-Sep-26	21-Oct-26	425d	7	100%	0%	224,785
	JDH3-02-009-R100-(SL)- LV Cables	16d	16d	02-Aug-26	19-Aug-26	03-Oct-26	21-Oct-26	425d	4	100%	0%	207,771
	Backfilling, Warning Tape Works f	4d	4d	16-Aug-26	19-Aug-26	17-Oct-26	21-Oct-26	425d	1	100%	0%	20,777
	Testing and Commissioning for L	4d	4d	11-Aug-26	15-Aug-26	12-Oct-26	17-Oct-26	425d	1	100%	0%	10,389
	Bedding Layer and Installation fo	4d	4d	06-Aug-26	10-Aug-26	07-Oct-26	12-Oct-26	425d	1	100%	0%	155,828
	Excavation Works for LV Cables	4d	4d	02-Aug-26	05-Aug-26	03-Oct-26	07-Oct-26	425d	1	100%	0%	20,777
	JDH3-02-009-R100-(SL)- LV Cables	14d	14d	06-Sep-26	21-Sep-26	29-Sep-26	14-Oct-26	413d	2	100%	0%	15,736
	Backfilling, Warning Tape Works f	7d	7d	14-Sep-26	21-Sep-26	07-Oct-26	14-Oct-26	413d	1	100%	0%	10,491
	Testing and Commissioning for L	7d	7d	06-Sep-26	13-Sep-26	29-Sep-26	06-Oct-26	413d	1	100%	0%	5,245
	JDH3-02-009-R100-(SL)-Earthing S	2d	2d	22-Sep-26	24-Sep-26	15-Oct-26	17-Oct-26	413d	1	100%	0%	1,278
	Supply, construct, connect and te	2d	2d	22-Sep-26	24-Sep-26	15-Oct-26	17-Oct-26	413d	1	100%	0%	1,278
	External Roads - EX	18d	18d	23-Jun-26	19-Aug-26	29-Sep-26	19-Oct-26	426d	93	100%	0%	3,355,546
	R241 - Access Road PW Storage Tanks	18d	18d	23-Jun-26	01-Aug-26	29-Sep-26	19-Oct-26	426d	20	100%	0%	555,912
	JDH3-02-009-R241-Potable Water Net	18d	18d	23-Jun-26	01-Aug-26	29-Sep-26	19-Oct-26	426d	20	100%	0%	555,912
	JDH3-02-009-R241-(WT)-HDPE Pipe	12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	1	100%	0%	71,871
	Primary Test for HDPE Pipe Line 8	12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	1	100%	0%	71,871
	JDH3-02-009-R241-(WT)-HDPE Pipe	12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	1	100%	0%	1,394

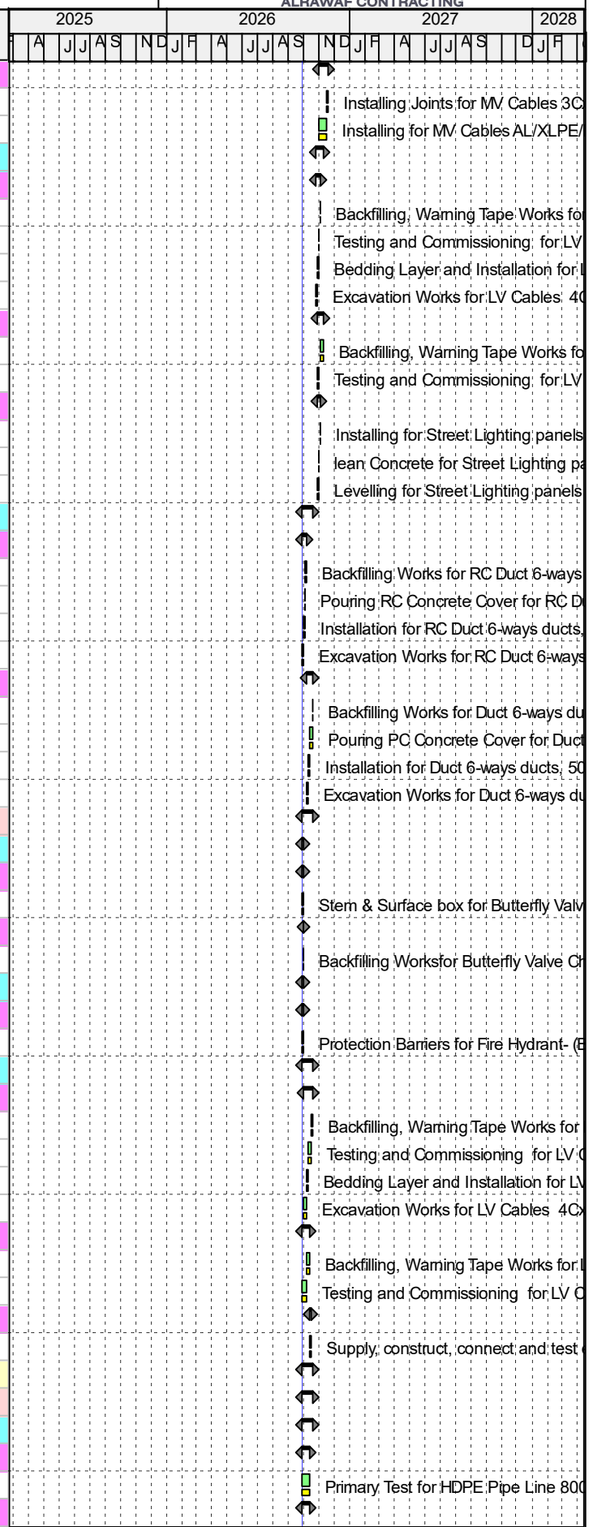

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Primary Test for HDPE Pipe Line	12d	12d	23-Jun-26	06-Jul-26	29-Sep-26	12-Oct-26	432d	1	100%	0%	1,394
	JDH3-02-009-R241-(WT)-Valve Cha	8d	8d	16-Jul-26	25-Jul-26	04-Oct-26	12-Oct-26	432d	4	100%	0%	127,983
	Backfilling Worksfor Butterfly Valv	2d	2d	23-Jul-26	25-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	25,597
	Installationfor Butterfly Valve Cha	2d	2d	21-Jul-26	22-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	70,391
	PC Worksfor Butterfly Valve Chan	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	12,798
	Excavation+Bedding for Butterfly	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	19,197
	JDH3-02-009-R241-(WT)-Butterfly V	4d	4d	16-Jul-26	20-Jul-26	01-Oct-26	05-Oct-26	436d	2	100%	0%	263,018
	Stem & Surface box for Butterfly	2d	2d	19-Jul-26	20-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	26,302
	Installation for Butterfly Valve 800	2d	2d	16-Jul-26	18-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	236,716
	JDH3-02-009-R241-(WT)-Air Valve (	8d	8d	19-Jul-26	27-Jul-26	06-Oct-26	14-Oct-26	430d	4	100%	0%	7,139
	Backfilling Worksfor Air Valve Cha	2d	2d	26-Jul-26	27-Jul-26	13-Oct-26	14-Oct-26	430d	1	100%	0%	1,428
	Installationfor Air Valve Chamber	2d	2d	23-Jul-26	25-Jul-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	3,926
	PC Worksfor Air Valve Chamber o	2d	2d	21-Jul-26	22-Jul-26	08-Oct-26	10-Oct-26	430d	1	100%	0%	714
	Excavation+Bedding for Air Valve	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	426d	1	100%	0%	1,071
	JDH3-02-009-R241-(WT)-Air Valve-	4d	4d	23-Jun-26	27-Jun-26	29-Sep-26	03-Oct-26	438d	2	100%	0%	25,013
	Stem & Surface box for Air Valve	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	438d	1	100%	0%	2,501
	Installation for Air Valve 110 mm	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	438d	1	100%	0%	22,512
	JDH3-02-009-R241-(WT)-Wash-Out	4d	4d	28-Jul-26	01-Aug-26	15-Oct-26	19-Oct-26	426d	2	100%	0%	27,358
	Stem & Surface box for Wash-Ou	2d	2d	30-Jul-26	01-Aug-26	18-Oct-26	19-Oct-26	426d	1	100%	0%	2,736
	Installation for Wash-Out Valve 2(	2d	2d	28-Jul-26	29-Jul-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	24,622
	JDH3-02-009-R241-(WT)-Wash-Out	8d	8d	21-Jul-26	29-Jul-26	08-Oct-26	17-Oct-26	428d	4	100%	0%	32,136
	Backfilling Worksfor Wash-Out Ch	2d	2d	28-Jul-26	29-Jul-26	15-Oct-26	17-Oct-26	428d	1	100%	0%	6,427
	Installationfor Wash-Out Chambe	2d	2d	26-Jul-26	27-Jul-26	13-Oct-26	14-Oct-26	426d	1	100%	0%	17,675
	PC Worksfor Wash-Out Chamber	2d	2d	23-Jul-26	25-Jul-26	11-Oct-26	12-Oct-26	426d	1	100%	0%	3,214
	Excavation+Bedding for Wash-Ou	2d	2d	21-Jul-26	22-Jul-26	08-Oct-26	10-Oct-26	426d	1	100%	0%	4,820
	R242 - Access Road PW Storage Tanks	14d	14d	23-Jun-26	13-Aug-26	29-Sep-26	14-Oct-26	430d	27	100%	0%	1,130,081
JDI	Surveying Works for Road - R242	0d	0d	23-Jun-26	23-Jun-26	29-Sep-26	29-Sep-26	444d	1	100%	0%	0
	JDH3-02-009-R242-Potable Water Net	14d	14d	23-Jun-26	13-Aug-26	29-Sep-26	14-Oct-26	430d	26	100%	0%	1,130,081
	JDH3-02-009-R242-(WT)-HDPE Pipe	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	1	100%	0%	65,924
	Primary Test for HDPE Pipe Line	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	1	100%	0%	65,924
	JDH3-02-009-R242-(WT)-HDPE Pipe	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	1	100%	0%	141,987
	Primary Test for HDPE Pipe Line	8d	8d	23-Jun-26	01-Jul-26	29-Sep-26	07-Oct-26	436d	1	100%	0%	141,987
	JDH3-02-009-R242-(WT)-Wash-Out	4d	4d	19-Jul-26	22-Jul-26	04-Oct-26	07-Oct-26	432d	2	100%	0%	39,083
	Stem & Surface box for Wash-Ou	2d	2d	21-Jul-26	22-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	3,908
	Installation for Wash-Out Valve 2(	2d	2d	19-Jul-26	20-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	35,175
	JDH3-02-009-R242-(WT)-Valve Cha	10d	10d	12-Jul-26	25-Jul-26	29-Sep-26	10-Oct-26	432d	4	100%	0%	191,975
	Backfilling Worksfor Butterfly Valv	2d	2d	23-Jul-26	25-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	38,395
	Installationfor Butterfly Valve Cha	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	105,586
	PC Worksfor Butterfly Valve Chan	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	19,197
	Excavation+Bedding for Butterfly	2d	2d	12-Jul-26	13-Jul-26	29-Sep-26	30-Sep-26	426d	1	100%	0%	28,796
	JDH3-02-009-R242-(WT)-Butterfly V	4d	4d	16-Jul-26	20-Jul-26	01-Oct-26	05-Oct-26	432d	2	100%	0%	493,159
	Stem & Surface box for Butterfly	2d	2d	19-Jul-26	20-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	49,316
	Installation for Butterfly Valve 100	2d	2d	16-Jul-26	18-Jul-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	443,843
	JDH3-02-009-R242-(WT)-Wash-Out	10d	10d	14-Jul-26	27-Jul-26	01-Oct-26	12-Oct-26	432d	4	100%	0%	32,136
	Backfilling Worksfor Wash-Out Ch	2d	2d	26-Jul-26	27-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	6,427
	Installationfor Wash-Out Chambe	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	17,675
	PC Worksfor Wash-Out Chamber	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	3,214
	Excavation+Bedding for Wash-Ou	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	4,820
	JDH3-02-009-R242-(WT)-Valve Cha	8d	8d	16-Jul-26	25-Jul-26	04-Oct-26	12-Oct-26	432d	4	100%	0%	14,336
	Backfilling Worksfor Butterfly Valv	2d	2d	23-Jul-26	25-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	2,867
	Installationfor Butterfly Valve Cha	2d	2d	21-Jul-26	22-Jul-26	08-Oct-26	10-Oct-26	430d	1	100%	0%	7,885
	PC Worksfor Butterfly Valve Chan	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	1,434
	Excavation+Bedding for Butterfly	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	2,150

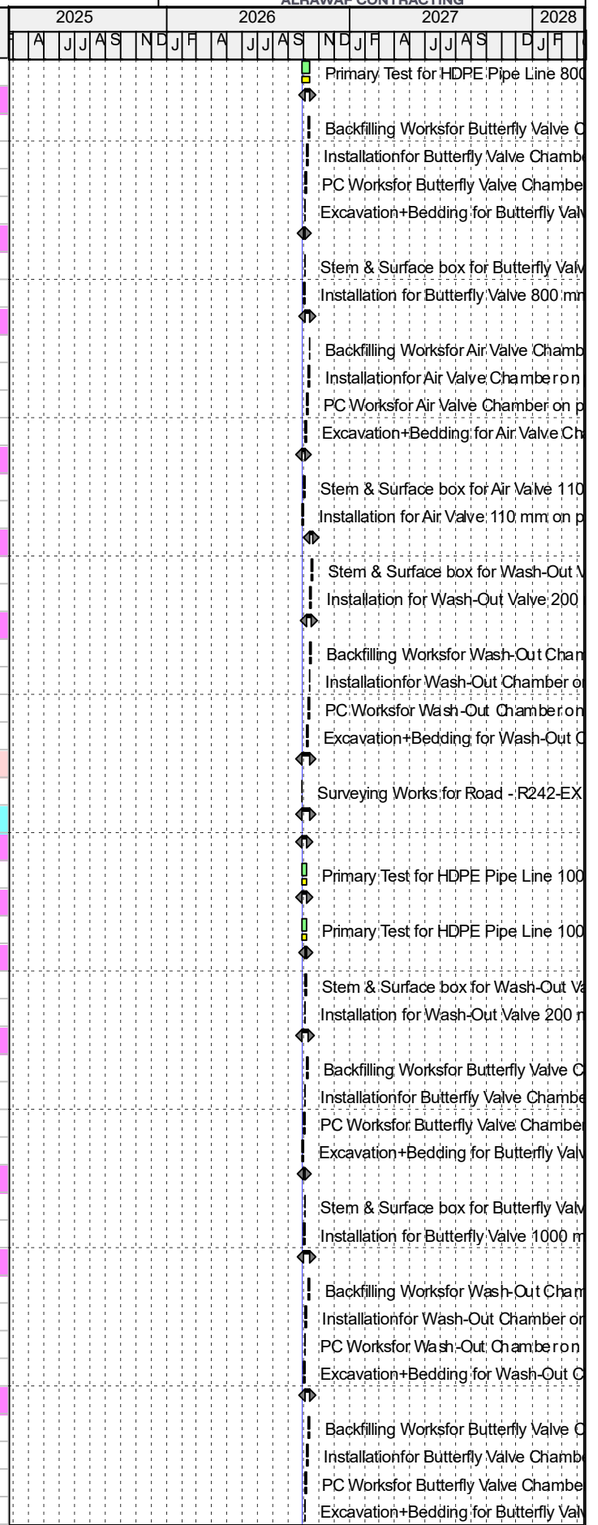


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R242-(WT)-Butterfly V	4d	4d	23-Jul-26	13-Aug-26	11-Oct-26	14-Oct-26	430d	2	100%	0%	16,130
	Stem & Surface box for Butterfly '	2d	2d	12-Aug-26	13-Aug-26	13-Oct-26	14-Oct-26	430d	1	100%	0%	1,613
	Installation for Butterfly Valve 300	2d	2d	23-Jul-26	25-Jul-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	14,517
	JDH3-02-009-R242-(WT)-Butterfly V	4d	4d	14-Jul-26	18-Jul-26	29-Sep-26	03-Oct-26	436d	2	100%	0%	98,633
	Stem & Surface box for Butterfly '	2d	2d	16-Jul-26	18-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	9,863
	Installation for Butterfly Valve 600	2d	2d	14-Jul-26	15-Jul-26	29-Sep-26	30-Sep-26	432d	1	100%	0%	88,769
	JDH3-02-009-R242-(WT)-Valve Cha	8d	8d	14-Jul-26	22-Jul-26	01-Oct-26	10-Oct-26	432d	4	100%	0%	36,718
	Backfilling Worksfor Butterfly Valv	2d	2d	21-Jul-26	22-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	7,344
	Installationfor Butterfly Valve Cha	2d	2d	19-Jul-26	20-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	20,195
	PC Worksfor Butterfly Valve Chan	2d	2d	16-Jul-26	18-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	3,672
	Excavation+Bedding for Butterfly	2d	2d	14-Jul-26	15-Jul-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	5,508
	R251 - Access Road TSE Storage Tanks	14d	14d	05-Jul-26	19-Aug-26	29-Sep-26	14-Oct-26	430d	18	100%	0%	227,022
	JDH3-02-009-R251-TSE Network - TSI	14d	14d	05-Jul-26	19-Aug-26	29-Sep-26	14-Oct-26	430d	18	100%	0%	227,022
	JDH3-02-009-R251-(TSE)-Air Valve	10d	10d	11-Jul-26	19-Jul-26	01-Oct-26	12-Oct-26	432d	4	100%	0%	14,269
	Backfilling Worksfor Air Valve Cha	2d	2d	18-Jul-26	19-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	2,854
	Installationfor Air Valve Chamber	2d	2d	15-Jul-26	16-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	7,848
	PC Worksfor Air Valve Chamber o	2d	2d	13-Jul-26	14-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	1,427
	Excavation+Bedding for Air Valve	2d	2d	11-Jul-26	12-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	2,140
	JDH3-02-009-R251-(TSE)-Wash-Ou	10d	10d	08-Jul-26	16-Jul-26	29-Sep-26	10-Oct-26	432d	4	100%	0%	41,949
	Backfilling Worksfor Wash-Out Ch	2d	2d	15-Jul-26	16-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	8,390
	Installationfor Wash-Out Chambe	2d	2d	13-Jul-26	14-Jul-26	04-Oct-26	05-Oct-26	434d	1	100%	0%	23,072
	PC Worksfor Wash-Out Chamber	2d	2d	11-Jul-26	12-Jul-26	01-Oct-26	03-Oct-26	434d	1	100%	0%	4,195
	Excavation+Bedding for Wash-Ou	2d	2d	08-Jul-26	09-Jul-26	29-Sep-26	30-Sep-26	434d	1	100%	0%	6,292
	JDH3-02-009-R251-(TSE)-Air Valve	4d	4d	07-Jul-26	11-Jul-26	11-Oct-26	14-Oct-26	430d	2	100%	0%	15,581
	Stem & Surface box for Air Valve	2d	2d	09-Jul-26	11-Jul-26	13-Oct-26	14-Oct-26	430d	1	100%	0%	1,558
	Installation for Air Valve 65 mm or	2d	2d	07-Jul-26	08-Jul-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	14,023
	JDH3-02-009-R251-(TSE)-Wash-Ou	4d	4d	05-Jul-26	08-Jul-26	08-Oct-26	12-Oct-26	430d	2	100%	0%	33,818
	Stem & Surface box for Wash-Ou	2d	2d	07-Jul-26	08-Jul-26	11-Oct-26	12-Oct-26	430d	1	100%	0%	3,382
	Installation for Wash-Out Valve 1(	2d	2d	05-Jul-26	06-Jul-26	08-Oct-26	10-Oct-26	430d	1	100%	0%	30,436
	JDH3-02-009-R251-(TSE)-Butterfly '	4d	4d	15-Jul-26	19-Jul-26	06-Oct-26	10-Oct-26	434d	2	100%	0%	78,222
	Stem & Surface box for Butterfly '	2d	2d	18-Jul-26	19-Jul-26	08-Oct-26	10-Oct-26	434d	1	100%	0%	7,822
	Installation for Butterfly Valve 400	2d	2d	15-Jul-26	16-Jul-26	06-Oct-26	07-Oct-26	434d	1	100%	0%	70,400
	JDH3-02-009-R251-(TSE)-Valve Cha	8d	8d	08-Jul-26	19-Aug-26	29-Sep-26	07-Oct-26	436d	4	100%	0%	43,184
	Backfilling Worksfor Butterfly Valv	2d	2d	18-Aug-26	19-Aug-26	06-Oct-26	07-Oct-26	436d	1	100%	0%	8,637
	Installationfor Butterfly Valve Cha	2d	2d	13-Jul-26	14-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	23,751
	PC Worksfor Butterfly Valve Chan	2d	2d	11-Jul-26	12-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	4,318
	Excavation+Bedding for Butterfly	2d	2d	08-Jul-26	09-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	6,478
	R252 - Access Road TSE Storage Tanks	18d	18d	22-Jul-26	11-Aug-26	29-Sep-26	19-Oct-26	426d	18	100%	0%	1,302,210
	JDH3-02-009-R252-TSE Network - TSI	18d	18d	22-Jul-26	11-Aug-26	29-Sep-26	19-Oct-26	426d	18	100%	0%	1,302,210
	JDH3-02-009-R252-(TSE)-Butterfly '	4d	4d	03-Aug-26	06-Aug-26	11-Oct-26	14-Oct-26	426d	2	100%	0%	542,479
	Stem & Surface box for Butterfly '	2d	2d	05-Aug-26	06-Aug-26	13-Oct-26	14-Oct-26	426d	1	100%	0%	54,248
	Installation for Butterfly Valve 600	2d	2d	03-Aug-26	04-Aug-26	11-Oct-26	12-Oct-26	426d	1	100%	0%	488,231
	JDH3-02-009-R252-(TSE)-Wash-Ou	4d	4d	05-Aug-26	09-Aug-26	13-Oct-26	17-Oct-26	426d	2	100%	0%	195,417
	Stem & Surface box for Wash-Ou	2d	2d	08-Aug-26	09-Aug-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	19,542
	Installation for Wash-Out Valve 1	2d	2d	05-Aug-26	06-Aug-26	13-Oct-26	14-Oct-26	426d	1	100%	0%	175,875
	JDH3-02-009-R252-(TSE)-Air Valve	4d	4d	08-Aug-26	11-Aug-26	15-Oct-26	19-Oct-26	426d	2	100%	0%	187,600
	Stem & Surface box for Air Valve	2d	2d	10-Aug-26	11-Aug-26	18-Oct-26	19-Oct-26	426d	1	100%	0%	18,760
	Installation for Air Valve 65 mm or	2d	2d	08-Aug-26	09-Aug-26	15-Oct-26	17-Oct-26	426d	1	100%	0%	168,840
	JDH3-02-009-R252-(TSE)-Valve Cha	8d	8d	22-Jul-26	30-Jul-26	29-Sep-26	07-Oct-26	432d	4	100%	0%	202,721
	Backfilling Worksfor Butterfly Valv	2d	2d	29-Jul-26	30-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	40,544
	Installationfor Butterfly Valve Cha	2d	2d	27-Jul-26	28-Jul-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	111,497
	PC Worksfor Butterfly Valve Chan	2d	2d	25-Jul-26	26-Jul-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	20,272
	Excavation+Bedding for Butterfly	2d	2d	22-Jul-26	23-Jul-26	29-Sep-26	30-Sep-26	426d	1	100%	0%	30,408

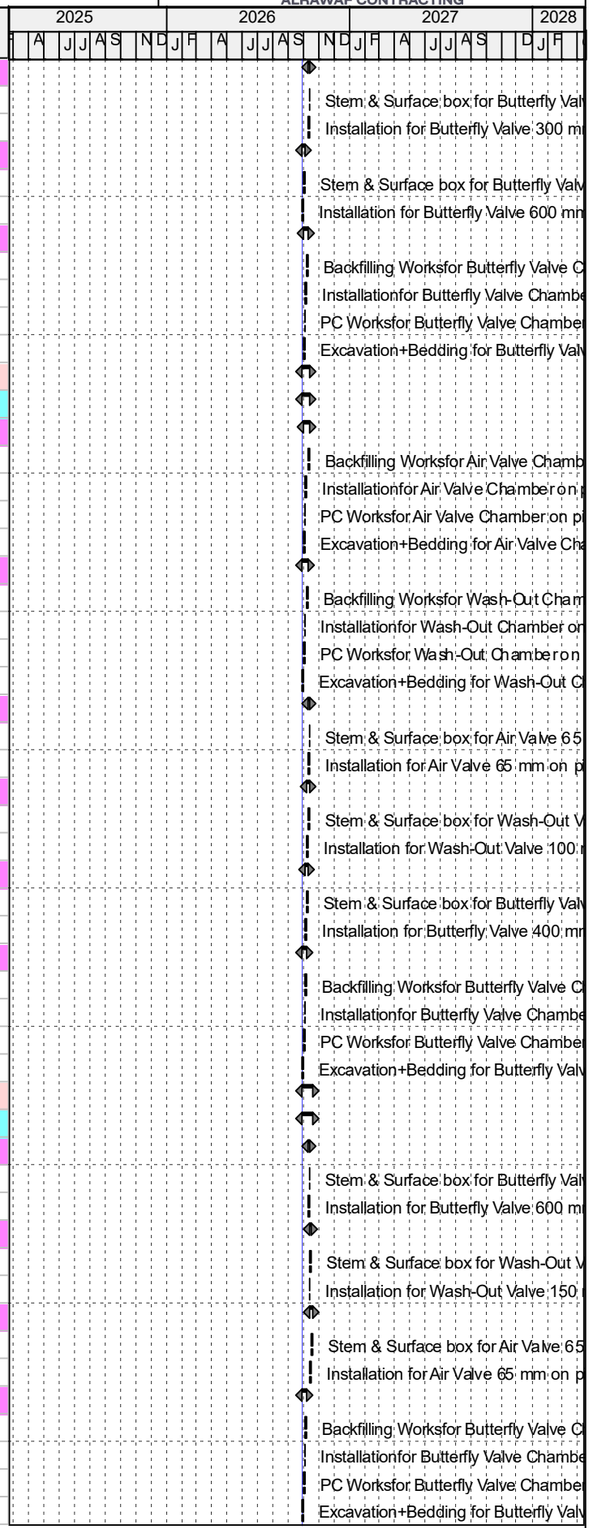


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	JDH3-02-009-R252-(TSE)-Wash-Ou	8d	8d	25-Jul-26	02-Aug-26	01-Oct-26	10-Oct-26	432d	4	100%	0%	137,902
	Backfilling Worksfor Wash-Out Ch	2d	2d	01-Aug-26	02-Aug-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	27,580
	Installationfor Wash-Out Chambe	2d	2d	29-Jul-26	30-Jul-26	06-Oct-26	07-Oct-26	426d	1	100%	0%	75,846
	PC Worksfor Wash-Out Chamber	2d	2d	27-Jul-26	28-Jul-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	13,790
	Excavation+Bedding for Wash-Ou	2d	2d	25-Jul-26	26-Jul-26	01-Oct-26	03-Oct-26	426d	1	100%	0%	20,685
	JDH3-02-009-R252-(TSE)-Air Valve	8d	8d	27-Jul-26	04-Aug-26	04-Oct-26	12-Oct-26	432d	4	100%	0%	36,091
	Backfilling Worksfor Air Valve Cha	2d	2d	03-Aug-26	04-Aug-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	7,218
	Installationfor Air Valve Chamber	2d	2d	01-Aug-26	02-Aug-26	08-Oct-26	10-Oct-26	426d	1	100%	0%	19,850
	PC Worksfor Air Valve Chamber o	2d	2d	29-Jul-26	30-Jul-26	06-Oct-26	07-Oct-26	426d	1	100%	0%	3,609
	Excavation+Bedding for Air Valve	2d	2d	27-Jul-26	28-Jul-26	04-Oct-26	05-Oct-26	426d	1	100%	0%	5,414
	R253 - Access Road TSE Storage Tanks	10d	10d	25-Jun-26	06-Jul-26	29-Sep-26	10-Oct-26	430d	6	100%	0%	121,405
	JDH3-02-009-R253-TSE Network - TSI	10d	10d	25-Jun-26	06-Jul-26	29-Sep-26	10-Oct-26	430d	6	100%	0%	121,405
	JDH3-02-009-R253-(TSE)-Valve Cha	8d	8d	25-Jun-26	04-Jul-26	29-Sep-26	07-Oct-26	432d	4	100%	0%	43,184
	Backfilling Worksfor Butterfly Valv	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	8,637
	Installationfor Butterfly Valve Cha	2d	2d	30-Jun-26	01-Jul-26	04-Oct-26	05-Oct-26	430d	1	100%	0%	23,751
	PC Worksfor Butterfly Valve Chan	2d	2d	28-Jun-26	29-Jun-26	01-Oct-26	03-Oct-26	430d	1	100%	0%	4,318
	Excavation+Bedding for Butterfly	2d	2d	25-Jun-26	27-Jun-26	29-Sep-26	30-Sep-26	430d	1	100%	0%	6,478
	JDH3-02-009-R253-(TSE)-Butterfly	4d	4d	02-Jul-26	06-Jul-26	06-Oct-26	10-Oct-26	430d	2	100%	0%	78,222
	Stem & Surface box for Butterfly	2d	2d	05-Jul-26	06-Jul-26	08-Oct-26	10-Oct-26	430d	1	100%	0%	7,822
	Installation for Butterfly Valve 400	2d	2d	02-Jul-26	04-Jul-26	06-Oct-26	07-Oct-26	430d	1	100%	0%	70,400
	R26	6d	6d	25-Jun-26	04-Jul-26	30-Sep-26	06-Oct-26	437d	4	100%	0%	18,916
	JDH3-02-009-R26-Sewage Network - S	6d	6d	25-Jun-26	04-Jul-26	30-Sep-26	06-Oct-26	437d	4	100%	0%	18,916
	JDH3-02-009-R26-(SW)-MH Works	3d	3d	27-Jun-26	29-Jun-26	30-Sep-26	04-Oct-26	440d	1	100%	0%	9,971
	Steel Cover for MH 1500 mm - de	3d	3d	27-Jun-26	29-Jun-26	30-Sep-26	04-Oct-26	440d	1	100%	0%	9,971
	JDH3-02-009-R26-(SW)-MH Works	2d	2d	25-Jun-26	27-Jun-26	30-Sep-26	01-Oct-26	437d	1	100%	0%	1,761
	Steel Cover for MH 1200 mm - de	2d	2d	25-Jun-26	27-Jun-26	30-Sep-26	01-Oct-26	437d	1	100%	0%	1,761
	JDH3-02-009-R26-(SW)-MH Works	2d	2d	30-Jun-26	01-Jul-26	03-Oct-26	04-Oct-26	437d	1	100%	0%	5,510
	Steel Cover for MH 1500 mm - de	2d	2d	30-Jun-26	01-Jul-26	03-Oct-26	04-Oct-26	437d	1	100%	0%	5,510
	JDH3-02-009-R26-(SW)-MH Works	2d	2d	02-Jul-26	04-Jul-26	05-Oct-26	06-Oct-26	437d	1	100%	0%	1,674
	Steel Cover for MH 2000 mm - de	2d	2d	02-Jul-26	04-Jul-26	05-Oct-26	06-Oct-26	437d	1	100%	0%	1,674
	JDH3-02-009-Close Out	18d	18d	23-Jun-26	24-Aug-26	29-Sep-26	19-Oct-26	414d	10	0%	0%	0
	JDH3-02-009-Engineering - EN	18d	18d	23-Jun-26	24-Aug-26	29-Sep-26	19-Oct-26	414d	10	0%	0%	0
	JDH3-02-009-As Built Drawing Submittal	7d	7d	23-Jun-26	13-Aug-26	29-Sep-26	06-Oct-26	415d	5	0%	0%	0
	JDH3-02-009-As Built Drawing Submi	7d	7d	23-Jun-26	06-Aug-26	29-Sep-26	06-Oct-26	415d	2	0%	0%	0
	Prepare and Submit Drawing for S	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	415d	1	100%	0%	0
	Prepare and Submit Drawing for S	7d	7d	29-Jul-26	06-Aug-26	29-Sep-26	06-Oct-26	415d	1	100%	0%	0
	JDH3-02-009-As Built Drawing Submi	7d	7d	23-Jun-26	06-Aug-26	29-Sep-26	06-Oct-26	415d	2	0%	0%	0
	Prepare and Submit Drawing for S	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	415d	1	100%	0%	0
	Prepare and Submit Drawing for S	7d	7d	29-Jul-26	06-Aug-26	29-Sep-26	06-Oct-26	415d	1	100%	0%	0
	JDH3-02-009-As Built Drawing Submi	7d	7d	06-Aug-26	13-Aug-26	29-Sep-26	06-Oct-26	415d	1	0%	0%	0
	Prepare and Submit Drawing for S	7d	7d	06-Aug-26	13-Aug-26	29-Sep-26	06-Oct-26	415d	1	100%	0%	0
	JDH3-02-009-As Built Drawing Approvals	9d	9d	01-Jul-26	24-Aug-26	07-Oct-26	19-Oct-26	344d	5	0%	0%	0
	JDH3-02-009-As Built Drawing Appro	9d	9d	01-Jul-26	17-Aug-26	07-Oct-26	19-Oct-26	344d	2	0%	0%	0
	Review and Approval for Sewage	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	344d	1	100%	0%	0
	Review and Approval for Storm W	9d	9d	06-Aug-26	17-Aug-26	07-Oct-26	19-Oct-26	344d	1	100%	0%	0
	JDH3-02-009-As Built Drawing Appro	9d	9d	01-Jul-26	17-Aug-26	07-Oct-26	19-Oct-26	344d	2	0%	0%	0
	Review and Approval for Sewage	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	344d	1	100%	0%	0
	Review and Approval for Storm W	9d	9d	06-Aug-26	17-Aug-26	07-Oct-26	19-Oct-26	344d	1	100%	0%	0
	JDH3-02-009-As Built Drawing Appro	9d	9d	15-Aug-26	24-Aug-26	07-Oct-26	19-Oct-26	344d	1	0%	0%	0
	Review and Approval for Storm W	9d	9d	15-Aug-26	24-Aug-26	07-Oct-26	19-Oct-26	344d	1	100%	0%	0
	JDH3-02-009-Linking Road between CI	80d	80d	23-Jun-26	18-Aug-26	29-Sep-26	30-Dec-26	364d	26	100%	0%	561,921
	Construction	80d	80d	23-Jun-26	18-Aug-26	29-Sep-26	30-Dec-26	364d	26	100%	0%	561,921

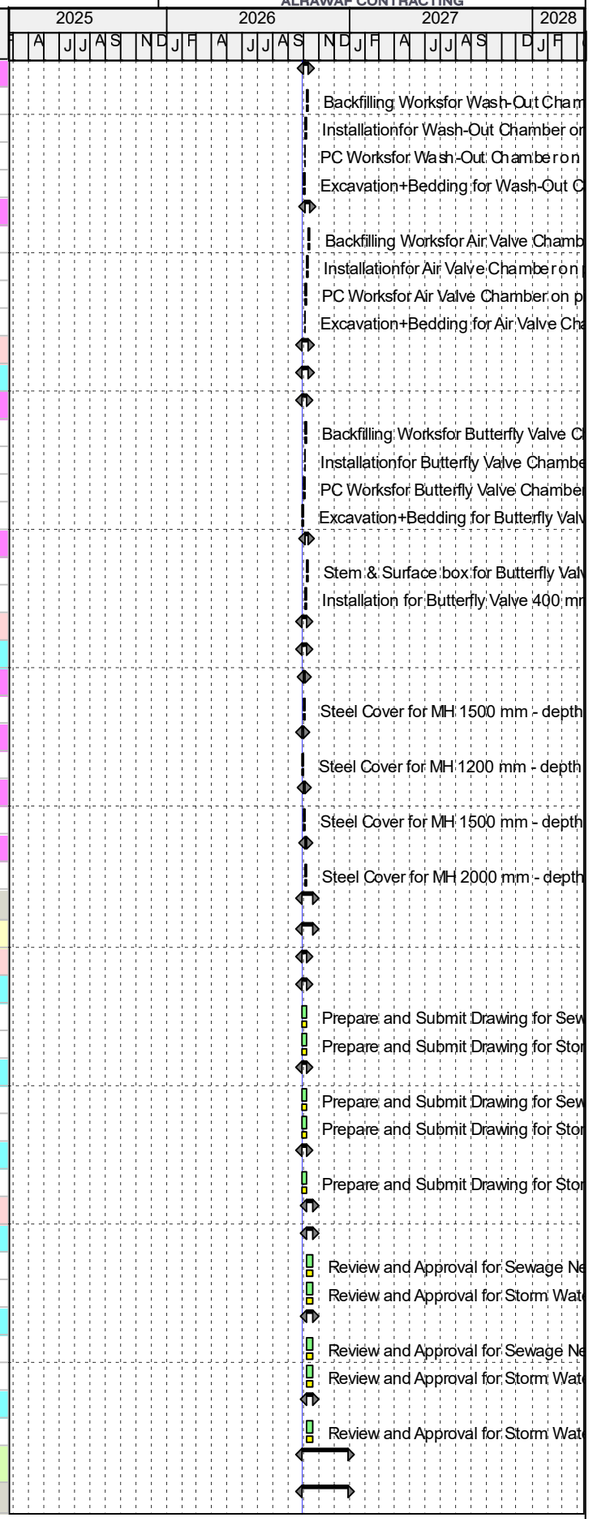


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDH3-02-009-CZ-Street Lighting Network -SL		80d	80d	23-Jun-26	18-Aug-26	29-Sep-26	30-Dec-26	364d	26	100%	0%	561,921
JDH3-02-009-CZ-(SL)-Lighting Pole with		16d	16d	05-Jul-26	22-Jul-26	11-Oct-26	28-Oct-26	383d	1	100%	0%	106,138
JDH	Earthing + Primary Test for Lightir	16d	16d	05-Jul-26	22-Jul-26	11-Oct-26	28-Oct-26	383d	1	100%	0%	106,138
JDH3-02-009-CZ-(SL)-Lighting Pole with		10d	10d	23-Jun-26	04-Jul-26	29-Sep-26	10-Oct-26	383d	4	100%	0%	149,775
JDH	Earthing + Primary Test for Lightir	3d	3d	01-Jul-26	04-Jul-26	07-Oct-26	10-Oct-26	383d	1	100%	0%	18,722
JDH	Installation Works for Lighting Pol	3d	3d	28-Jun-26	30-Jun-26	04-Oct-26	06-Oct-26	383d	1	100%	0%	65,526
JDH	Backfilling of RC foundation for Li	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	383d	1	100%	0%	28,083
JDH	Installation of RC foundation for L	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	383d	1	100%	0%	37,444
JDH3-02-009-CZ-(SL)-Road Crossing Duc		80d	80d	23-Jun-26	27-Jul-26	29-Sep-26	30-Dec-26	364d	4	100%	0%	76,774
JDH	Testing and Backfilling Works for I	20d	20d	16-Jul-26	27-Jul-26	08-Dec-26	30-Dec-26	364d	1	100%	0%	3,839
JDH	Pouring Concrete Cover for PVC I	20d	20d	11-Jul-26	15-Jul-26	15-Nov-26	07-Dec-26	364d	1	100%	0%	11,516
JDH	Installation for PVC Pipes 2×150r	20d	20d	29-Jun-26	09-Jul-26	22-Oct-26	14-Nov-26	364d	1	100%	0%	46,064
JDH	Excavation Works for PVC Pipes	20d	20d	23-Jun-26	28-Jun-26	29-Sep-26	21-Oct-26	364d	1	100%	0%	15,355
JDH3-02-009-CZ-(SL)- LV Cables - Coppe		12d	12d	16-Jul-26	29-Jul-26	29-Sep-26	12-Oct-26	432d	4	100%	0%	9,255
JDH	Backfilling, Warning Tape Works f	2d	2d	28-Jul-26	29-Jul-26	11-Oct-26	12-Oct-26	432d	1	100%	0%	925
JDH	Testing and Commissioning for L	2d	2d	21-Jul-26	22-Jul-26	04-Oct-26	05-Oct-26	436d	1	100%	0%	2,776
JDH	Bedding Layer and Installation fo	2d	2d	19-Jul-26	20-Jul-26	01-Oct-26	03-Oct-26	436d	1	100%	0%	2,776
JDH	Excavation Works for LV Cables	2d	2d	16-Jul-26	18-Jul-26	29-Sep-26	30-Sep-26	432d	1	100%	0%	2,776
JDH3-02-009-CZ-(SL)- LV Cables - Single		8d	8d	19-Jul-26	27-Jul-26	01-Oct-26	10-Oct-26	432d	4	100%	0%	1,376
JDH	Backfilling, Warning Tape Works f	2d	2d	26-Jul-26	27-Jul-26	08-Oct-26	10-Oct-26	432d	1	100%	0%	138
JDH	Testing and Commissioning for L	2d	2d	23-Jul-26	25-Jul-26	06-Oct-26	07-Oct-26	432d	1	100%	0%	413
JDH	Bedding Layer and Installation fo	2d	2d	21-Jul-26	22-Jul-26	04-Oct-26	05-Oct-26	432d	1	100%	0%	413
JDH	Excavation Works for LV Cables	2d	2d	19-Jul-26	20-Jul-26	01-Oct-26	03-Oct-26	432d	1	100%	0%	413
JDH3-02-009-CZ-(SL)-Street Lighting (LE		19d	19d	23-Jun-26	14-Jul-26	29-Sep-26	20-Oct-26	390d	1	100%	0%	76,281
JDH	Earthing & Primary Test for Lightir	19d	19d	23-Jun-26	14-Jul-26	29-Sep-26	20-Oct-26	390d	1	100%	0%	76,281
JDH3-02-009-CZ-(SL)- Street Lighting Pa		9d	9d	23-Jul-26	02-Aug-26	29-Oct-26	08-Nov-26	383d	3	100%	0%	75,211
JDH	Backfilling for Street Lighting pan	3d	3d	30-Jul-26	02-Aug-26	05-Nov-26	08-Nov-26	383d	1	100%	0%	7,521
JDH	Installation for Street Lighting par	3d	3d	27-Jul-26	29-Jul-26	02-Nov-26	04-Nov-26	383d	1	100%	0%	52,648
JDH	Excavation for Street Lighting par	3d	3d	23-Jul-26	26-Jul-26	29-Oct-26	01-Nov-26	383d	1	100%	0%	15,042
JDH3-02-009-CZ-(SL)-Earthing System of		14d	14d	03-Aug-26	18-Aug-26	09-Nov-26	24-Nov-26	383d	1	100%	0%	15,518
JDH	Supply, construct, connect and te	14d	14d	03-Aug-26	18-Aug-26	09-Nov-26	24-Nov-26	383d	1	100%	0%	15,518
JDH3-02-009-CZ-(SL)- Feeder Pillars		6d	6d	03-Aug-26	09-Aug-26	09-Nov-26	15-Nov-26	388d	3	100%	0%	42,978
JDH	Backfilling for Feeder Pillar - (B2.2	2d	2d	08-Aug-26	09-Aug-26	14-Nov-26	15-Nov-26	388d	1	100%	0%	4,298
JDH	Installation for Feeder Pillar - (B2.	2d	2d	05-Aug-26	06-Aug-26	11-Nov-26	12-Nov-26	388d	1	100%	0%	30,085
JDH	Excavation for Feeder Pillar - (B2.	2d	2d	03-Aug-26	04-Aug-26	09-Nov-26	10-Nov-26	388d	1	100%	0%	8,596
JDH3-02-009-CZ-(SL)-KWH meter mounti		3d	3d	10-Aug-26	12-Aug-26	16-Nov-26	18-Nov-26	388d	1	100%	0%	8,617
JDH	Installation for KWH meter - (B2.2	3d	3d	10-Aug-26	12-Aug-26	16-Nov-26	18-Nov-26	388d	1	100%	0%	8,617
JDH3-02-009-Lift Station 01		140d	140d	23-Jun-26	05-Apr-27	29-Sep-26	15-Mar-27	304d	31	0%	0%	0
Engineering		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	348d	10	0%	0%	0
JDH3-02-009-Method of Statement for Lift Static		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	348d	10	0%	0%	0
JDH3-02-009-Pumps		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	344d	2	0%	0%	0
JDH	Review & approval MS for Pumps	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	285d	1	100%	0%	0
JDH	Prepare & Submit MS for Pumps-	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	344d	1	100%	0%	0
JDH3-02-009-Duct Works		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	259d	2	0%	0%	0
JDH	Review & approval MS for Duct W	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	215d	1	100%	0%	0
JDH	Prepare & Submit MS for Duct W	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	260d	1	100%	0%	0
JDH3-02-009-Drainage System		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	316d	2	0%	0%	0
JDH	Review & approval MS for Drainag	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	262d	1	100%	0%	0
JDH	Prepare & Submit MS for Drinage	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	316d	1	100%	0%	0
JDH3-02-009-Data Communication		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	303d	2	0%	0%	0
JDH	Review & approval MS for Data C	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	251d	1	100%	0%	0
JDH	Prepare & Submit MS for Data Cc	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	303d	1	100%	0%	0

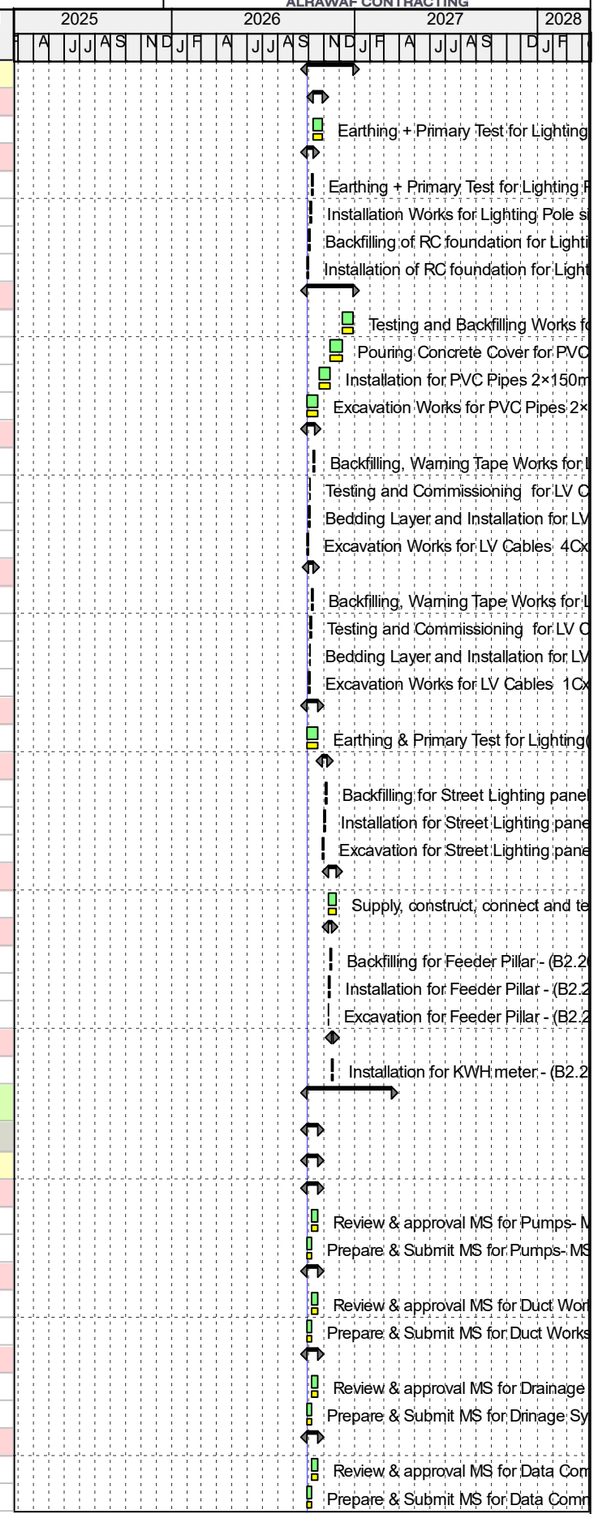


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDH3-02-009-Programing Logical Contrc		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	348d	2	0%	0%	0
JDI	Review & approval MS for Prograi	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	289d	1	100%	0%	0
JDI	Prepare & Submit MS for Progran	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	349d	1	100%	0%	0
Procurement		140d	140d	23-Jun-26	05-Apr-27	29-Sep-26	15-Mar-27	304d	21	0%	0%	0
Long Lead Items		140d	140d	23-Jun-26	05-Apr-27	29-Sep-26	15-Mar-27	304d	21	0%	0%	0
Purchase Order - PO - Lift Station		21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	368d	5	0%	0%	0
JDH3-02-009-LOL-PO-LFT-AR-Architec		21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	368d	2	0%	0%	0
	Material Purchase Order for Steel	21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	368d	1	100%	0%	0
	Material Purchase Order for Chair	21d	21d	23-Jun-26	09-Jul-26	29-Sep-26	22-Oct-26	368d	1	100%	0%	0
JDH3-02-009-LOL-PO-LFT-TC-Telecon		21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	345d	3	0%	0%	0
	Material Purchase Order for Secu	21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	321d	1	100%	0%	0
	Material Purchase Order for Data	21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	345d	1	100%	0%	0
	Material Purchase Order for Addre	21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	345d	1	100%	0%	0
Fabrication - FAB - Lift Station		168d	168d	23-Jun-26	05-Apr-27	29-Sep-26	15-Mar-27	366d	16	0%	0%	0
JDH3-02-009-LOL-MAN-LFT-AR-Archit		70d	70d	11-Jul-26	28-Nov-26	23-Oct-26	31-Dec-26	440d	1	0%	0%	0
	Material Fabrication for Chain link	70d	70d	11-Jul-26	28-Nov-26	23-Oct-26	31-Dec-26	440d	1	56.74%	0%	0
JDH3-02-009-LOL-MAN-LFT-MC-Mech		168d	168d	23-Jun-26	05-Apr-27	29-Sep-26	15-Mar-27	366d	8	0%	0%	0
	Material Fabrication for Fuel Pum	84d	84d	18-Jul-26	05-Apr-27	29-Sep-26	21-Dec-26	387d	1	27.86%	0%	0
	Material Fabrication for Fuel Tank	84d	84d	18-Jul-26	05-Apr-27	29-Sep-26	21-Dec-26	372d	1	27.86%	0%	0
	Material Fabrication for Force Mai	112d	112d	23-Jun-26	19-Jan-27	29-Sep-26	18-Jan-27	422d	1	46.45%	0%	0
	Material Fabrication for Penstok -	140d	140d	23-Jun-26	08-Mar-27	29-Sep-26	15-Feb-27	221d	1	37.84%	0%	0
	Material Fabrication for Basket Sc	112d	112d	23-Jun-26	08-Mar-27	29-Sep-26	18-Jan-27	247d	1	37.84%	0%	0
	Material Fabrication for Chlorinatic	168d	168d	23-Jun-26	08-Mar-27	29-Sep-26	15-Mar-27	212d	1	37.84%	0%	0
	Material Fabrication for Surge Pro	112d	112d	23-Jun-26	08-Mar-27	29-Sep-26	18-Jan-27	277d	1	37.84%	0%	0
	Material Fabrication for Odour Sys	168d	168d	23-Jun-26	08-Mar-27	29-Sep-26	15-Mar-27	212d	1	37.84%	0%	0
JDH3-02-009-LOL-MAN-LFT-EL-Electri		140d	140d	23-Jun-26	08-Mar-27	29-Sep-26	15-Feb-27	394d	4	0%	0%	0
	Material Fabrication for Automatic	84d	84d	23-Jun-26	08-Mar-27	29-Sep-26	21-Dec-26	386d	1	37.84%	0%	0
	Material Fabrication for Generator	140d	140d	23-Jun-26	08-Mar-27	29-Sep-26	15-Feb-27	394d	1	37.84%	0%	0
	Material Fabrication for Programm	112d	112d	23-Jun-26	08-Mar-27	29-Sep-26	18-Jan-27	386d	1	37.84%	0%	0
	Material Fabrication for Motor Cor	84d	84d	23-Jun-26	08-Mar-27	29-Sep-26	21-Dec-26	404d	1	37.84%	0%	0
JDH3-02-009-LOL-MAN-LFT-TC-Telecc		112d	112d	18-Jul-26	25-Nov-26	23-Oct-26	11-Feb-27	386d	3	0%	0%	0
	Material Fabrication for Security S	112d	112d	18-Jul-26	25-Nov-26	23-Oct-26	11-Feb-27	386d	1	55.73%	0%	0
	Material Fabrication for Data Com	84d	84d	18-Jul-26	24-Oct-26	23-Oct-26	14-Jan-27	414d	1	73.74%	0%	0
	Material Fabrication for Addressat	84d	84d	18-Jul-26	24-Oct-26	23-Oct-26	14-Jan-27	414d	1	73.74%	0%	0
JDH3-02-009-Lift Station 03		14d	14d	23-Jun-26	05-Oct-26	29-Sep-26	14-Oct-26	430d	7	58.57%	0%	18,970
Procurement		14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	430d	5	0%	0%	0
Short Lead Items		14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	430d	5	0%	0%	0
Purchase Order - PO - Lift Station		14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	430d	5	0%	0%	0
JDH3-02-009-SHL-PO-LFT-MC-Mechai		14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	393d	3	0%	0%	0
	Material Purchase Order for Exha	14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	393d	1	100%	0%	0
	Material Purchase Order for Wall I	14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	393d	1	100%	0%	0
	Material Purchase Order for Fire F	14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	381d	1	100%	0%	0
JDH3-02-009-SHL-PO-LFT-EL-Electric		14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	430d	2	0%	0%	0
	Material Purchase Order for Wirin	14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	430d	1	100%	0%	0
	Material Purchase Order for Lighti	14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	430d	1	100%	0%	0
Construction		9d	9d	10-Sep-26	05-Oct-26	29-Sep-26	08-Oct-26	391d	2	58.57%	0%	18,970
SEWERAGE PUMP STATION		9d	9d	10-Sep-26	05-Oct-26	29-Sep-26	08-Oct-26	391d	2	58.57%	0%	18,970
JDH3-02-009-BQ4-Sewerage Pumps & M		9d	9d	10-Sep-26	05-Oct-26	29-Sep-26	08-Oct-26	391d	2	58.57%	0%	18,970
JDH3-02-009-BQ4-Plinth for Odour Cc		9d	9d	10-Sep-26	05-Oct-26	29-Sep-26	08-Oct-26	391d	2	58.57%	0%	18,970
	Steel Fixing for Plinth - (Z900.10)-	6d	6d	22-Sep-26	05-Oct-26	03-Oct-26	08-Oct-26	391d	1	42%	0%	13,550
	Shuttering for Plinth - (Z900.10)-L	3d	3d	10-Sep-26	22-Sep-26	29-Sep-26	01-Oct-26	391d	1	100%	0%	5,420
JDH3-02-009-Mosque		44d	44d	23-Jun-26	30-Sep-26	29-Sep-26	18-Nov-26	400d	41	92.7%	0%	293,010

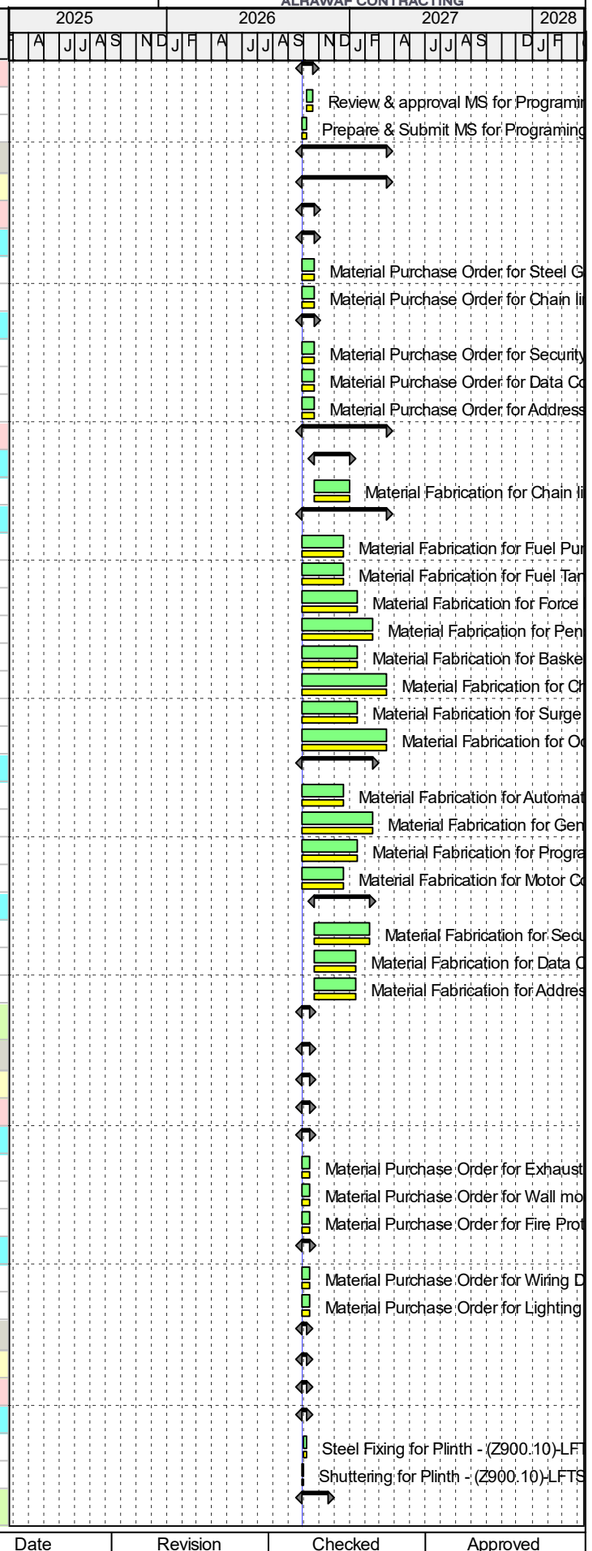

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
Engineering		19d	19d	23-Jun-26	12-Jul-26	29-Sep-26	20-Oct-26	425d	13	100%	0%	15,829
JDH3-02-009-Prequalification and Material Subm		7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	10	0%	0%	0
Architectural		7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	8	0%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	318d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	294d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	342d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
Steel Material		7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	2	0%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
JDI	Submission of P.Q issuance for st	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	437d	1	100%	0%	0
JDH3-02-009-Prequalification and Material Appr		10d	10d	01-Jul-26	12-Jul-26	07-Oct-26	20-Oct-26	283d	3	100%	0%	15,829
Architectural		10d	10d	01-Jul-26	12-Jul-26	07-Oct-26	20-Oct-26	283d	3	100%	0%	15,829
JDI	Approval of Material Submittal for	10d	10d	01-Jul-26	12-Jul-26	07-Oct-26	20-Oct-26	263d	1	100%	0%	5,276
JDI	Approval of Material Submittal for	10d	10d	01-Jul-26	12-Jul-26	07-Oct-26	20-Oct-26	243d	1	100%	0%	5,276
JDI	Approval of Material Submittal for	10d	10d	01-Jul-26	12-Jul-26	07-Oct-26	20-Oct-26	283d	1	100%	0%	5,276
Procurement		39d	39d	23-Jun-26	30-Aug-26	29-Sep-26	12-Nov-26	177d	10	100%	0%	100,916
Short Lead Items		39d	39d	23-Jun-26	30-Aug-26	29-Sep-26	12-Nov-26	177d	10	100%	0%	100,916
Purchase Order - PO-Mosque		30d	30d	23-Jun-26	16-Aug-26	29-Sep-26	02-Nov-26	184d	6	0%	0%	0
Architectural		21d	21d	13-Jul-26	05-Aug-26	29-Sep-26	22-Oct-26	193d	2	0%	0%	0
P.O Issue For Material for Marble		21d	21d	13-Jul-26	05-Aug-26	29-Sep-26	22-Oct-26	193d	1	100%	0%	0
P.O Issue For Material for PORCI		21d	21d	13-Jul-26	05-Aug-26	29-Sep-26	22-Oct-26	177d	1	100%	0%	0
Electrical		21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	142d	2	0%	0%	0
P.O Issue For Material . SOUND S		21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	142d	1	100%	0%	0
P.O Issue For Material . FIRE AL/		21d	21d	23-Jun-26	16-Jul-26	29-Sep-26	22-Oct-26	140d	1	100%	0%	0
Mechanical		30d	30d	23-Jun-26	16-Aug-26	29-Sep-26	02-Nov-26	154d	2	0%	0%	0
P.O Issue For Material . HVAC-P(		21d	21d	23-Jun-26	27-Jul-26	29-Sep-26	22-Oct-26	141d	1	100%	0%	0
P.O Issue For Material . PLUMBII		21d	21d	13-Jul-26	16-Aug-26	10-Oct-26	02-Nov-26	154d	1	100%	0%	0
Delivery and staging on Site - DOS-Mosc		21d	21d	18-Jul-26	30-Aug-26	23-Oct-26	12-Nov-26	216d	4	100%	0%	100,916
Architectural		21d	21d	06-Aug-26	30-Aug-26	23-Oct-26	12-Nov-26	216d	1	100%	0%	25,229
INS&delivery and staging Materia		21d	21d	06-Aug-26	30-Aug-26	23-Oct-26	12-Nov-26	216d	1	100%	0%	25,229
Electrical		21d	21d	18-Jul-26	10-Aug-26	23-Oct-26	12-Nov-26	171d	2	100%	0%	50,458
INS&delivery and staging Materia		21d	21d	18-Jul-26	10-Aug-26	23-Oct-26	12-Nov-26	171d	1	100%	0%	25,229
INS&delivery and staging Materia		21d	21d	18-Jul-26	10-Aug-26	23-Oct-26	12-Nov-26	169d	1	100%	0%	25,229
Mechanical		21d	21d	28-Jul-26	20-Aug-26	23-Oct-26	12-Nov-26	170d	1	100%	0%	25,229
INS&delivery and staging Materia		21d	21d	28-Jul-26	20-Aug-26	23-Oct-26	12-Nov-26	170d	1	100%	0%	25,229
Construction		44d	44d	23-Jun-26	30-Sep-26	29-Sep-26	18-Nov-26	400d	18	87.87%	0%	176,264
Mosque Main Building		44d	44d	06-Jul-26	30-Sep-26	29-Sep-26	18-Nov-26	400d	7	82.17%	0%	84,935
SuperStructure for Building		4d	4d	06-Jul-26	11-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	4,295
Slab For Main Building		4d	4d	06-Jul-26	11-Jul-26	29-Sep-26	03-Oct-26	440d	2	100%	0%	4,295
De Shuttering for RC Steps And F		3d	3d	07-Jul-26	11-Jul-26	30-Sep-26	03-Oct-26	440d	1	100%	0%	541
Pouring for RC Steps And Ramps		1d	1d	06-Jul-26	07-Jul-26	29-Sep-26	29-Sep-26	440d	1	100%	0%	3,754
Finishing of Mosque Building		10d	10d	05-Sep-26	30-Sep-26	29-Sep-26	11-Oct-26	186d	3	80.17%	0%	49,539
Masonary Work - MSW		4d	4d	05-Sep-26	08-Sep-26	29-Sep-26	04-Oct-26	173d	1	100%	0%	13,697
Installation for External Insulated		4d	4d	05-Sep-26	08-Sep-26	29-Sep-26	04-Oct-26	173d	1	100%	0%	13,697
Thermal & Moisture Protection - INS		6d	6d	24-Sep-26	30-Sep-26	04-Oct-26	11-Oct-26	186d	2	72.59%	0%	35,842
Provide and Apply 50 Mm Thk Ri		3d	3d	28-Sep-26	30-Sep-26	07-Oct-26	11-Oct-26	186d	1	33.33%	0%	14,734
Provide and Apply 4mm Thick Me		3d	3d	24-Sep-26	27-Sep-26	04-Oct-26	07-Oct-26	186d	1	100%	0%	21,108
Electrical Works of Mosque Building		5d	5d	24-Sep-26	29-Sep-26	14-Nov-26	18-Nov-26	140d	2	82.9%	0%	31,101

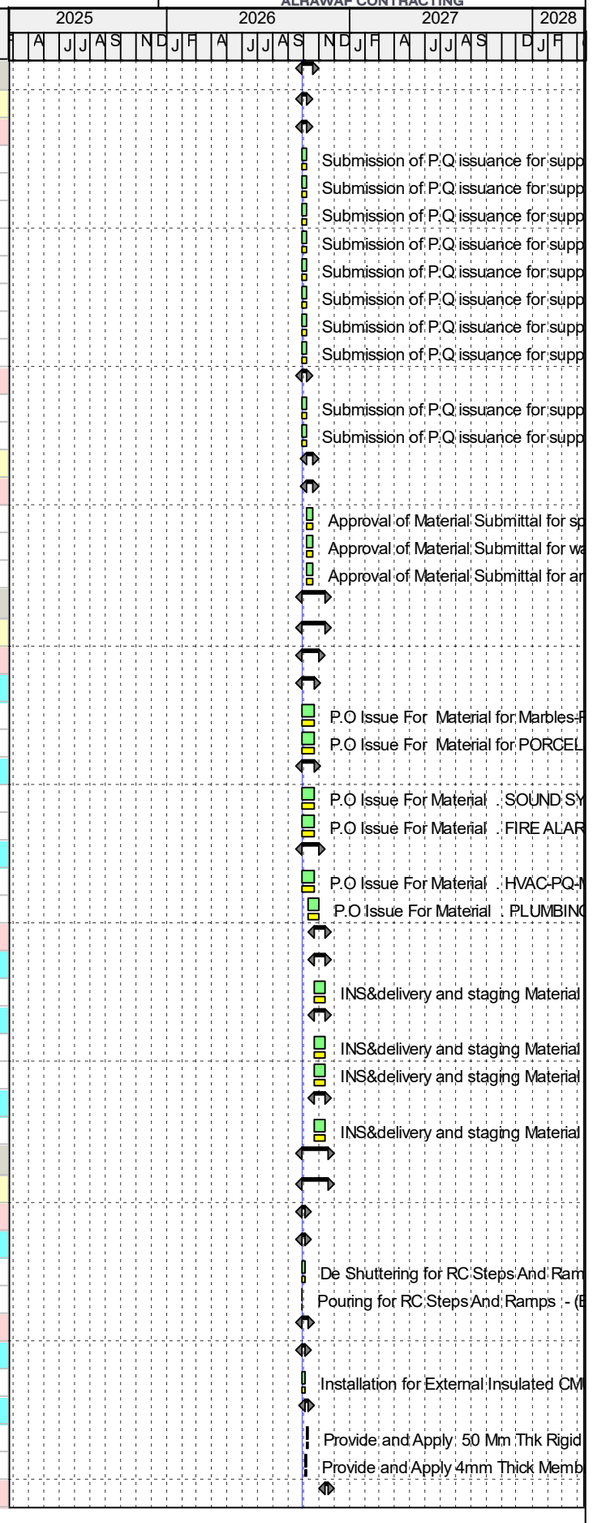

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Low Voltage - LV	5d	5d	24-Sep-26	29-Sep-26	14-Nov-26	18-Nov-26	140d	1	80%	0%	26,595
	Installation of Conduits and wiring	5d	5d	24-Sep-26	29-Sep-26	14-Nov-26	18-Nov-26	140d	1	80%	0%	26,595
	Light Current - LC	3d	3d	24-Sep-26	27-Sep-26	14-Nov-26	16-Nov-26	142d	1	100%	0%	4,505
	Installation of Conduits and wiring	3d	3d	24-Sep-26	27-Sep-26	14-Nov-26	16-Nov-26	142d	1	100%	0%	4,505
	Mosque Wash Room	6d	6d	23-Jun-26	06-Sep-26	29-Sep-26	05-Oct-26	432d	7	100%	0%	9,360
	Finishing of Mosque Wash Room	2d	2d	31-Aug-26	01-Sep-26	29-Sep-26	30-Sep-26	176d	1	100%	0%	1,403
	Masonary Work - MSW	2d	2d	31-Aug-26	01-Sep-26	29-Sep-26	30-Sep-26	176d	1	100%	0%	1,403
	Installation for External Insulated	2d	2d	31-Aug-26	01-Sep-26	29-Sep-26	30-Sep-26	176d	1	100%	0%	1,403
	Electrical Works of Wash Room	6d	6d	23-Jun-26	06-Sep-26	29-Sep-26	05-Oct-26	432d	6	100%	0%	7,957
	Grounding System - GR	4d	4d	23-Jun-26	24-Jun-26	29-Sep-26	03-Oct-26	401d	2	100%	0%	642
	Installation of grounding system	2d	2d	23-Jun-26	24-Jun-26	01-Oct-26	03-Oct-26	401d	1	100%	0%	260
	Installation of grounding system (	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	401d	1	100%	0%	382
	Lightning system - LIG	4d	4d	23-Jun-26	11-Jul-26	29-Sep-26	03-Oct-26	434d	3	100%	0%	3,686
	Installation of lightning protection	2d	2d	09-Jul-26	11-Jul-26	29-Sep-26	30-Sep-26	436d	1	100%	0%	825
	Installation of lightning protection	2d	2d	23-Jun-26	24-Jun-26	01-Oct-26	03-Oct-26	401d	1	100%	0%	203
	Installation of lightning protection	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	401d	1	100%	0%	2,658
	Low Voltage - LV	4d	4d	02-Sep-26	06-Sep-26	01-Oct-26	05-Oct-26	204d	1	100%	0%	3,629
	Installation of Conduits and wiring	4d	4d	02-Sep-26	06-Sep-26	01-Oct-26	05-Oct-26	204d	1	100%	0%	3,629
	Mechanical Works For (Mosque Bldg+ Wash Ar	38d	38d	24-Sep-26	30-Sep-26	04-Oct-26	17-Nov-26	141d	4	92.39%	0%	81,969
	Water Supply System - PW	6d	6d	24-Sep-26	30-Sep-26	04-Oct-26	11-Oct-26	173d	1	66.67%	0%	18,722
JDI	Installation of for cold and hot wa	6d	6d	24-Sep-26	30-Sep-26	04-Oct-26	11-Oct-26	173d	1	66.67%	0%	18,722
	Sewer And Drainage System - SW	4d	4d	24-Sep-26	28-Sep-26	04-Oct-26	08-Oct-26	175d	1	100%	0%	3,902
JDI	Installation of Galvanized iron ver	4d	4d	24-Sep-26	28-Sep-26	04-Oct-26	08-Oct-26	175d	1	100%	0%	3,902
	HVAC System - AC	38d	38d	24-Sep-26	28-Sep-26	04-Oct-26	17-Nov-26	141d	2	100%	0%	59,344
JDI	Installation of Ducted Split Air Cor	4d	4d	24-Sep-26	28-Sep-26	04-Oct-26	08-Oct-26	175d	1	100%	0%	2,439
JDI	Installation of Ducted Split Air Cor	4d	4d	24-Sep-26	28-Sep-26	14-Nov-26	17-Nov-26	141d	1	100%	0%	56,905
JDH3-02-009-TSE Pump Station		87d	87d	23-Jun-26	28-Nov-26	29-Sep-26	08-Jan-27	357d	30	0%	0%	0
Engineering		18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	426d	23	0%	0%	0
	JDH3-02-009-Prequalification and Material Subm	10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	434d	1	0%	0%	0
	JDH3-02-009-Prequalifications and Mate	10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	434d	1	0%	0%	0
JDI	Prepare Material Submittal for Acr	10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	434d	1	100%	0%	0
	JDH3-02-009-Method of Statement for TSE Pump	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	374d	22	0%	0%	0
	JDH3-02-009-Pumps	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	329d	2	0%	0%	0
JDI	Review & approval MS for Pumps	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	273d	1	100%	0%	0
JDI	Prepare & Submit MS for Pumps-	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	330d	1	100%	0%	0
	JDH3-02-009-Duct Works	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	288d	2	0%	0%	0
JDI	Review & approval MS for Duct W	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	239d	1	100%	0%	0
JDI	Prepare & Submit MS for Duct W	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	289d	1	100%	0%	0
	JDH3-02-009-Drainage System	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	227d	2	0%	0%	0
JDI	Review & approval MS for Drainag	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	188d	1	100%	0%	0
JDI	Prepare & Submit MS for Drinage	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	227d	1	100%	0%	0
	JDH3-02-009-Water Supply System	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	252d	2	0%	0%	0
JDI	Review & approval MS for Water S	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	209d	1	100%	0%	0
JDI	Prepare & Submit MS for Water S	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	253d	1	100%	0%	0
	JDH3-02-009-Chlorination System	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	352d	2	0%	0%	0
JDI	Review & approval MS for Chlorin	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	292d	1	100%	0%	0
JDI	Prepare & Submit MS for Chlorina	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	352d	1	100%	0%	0
	JDH3-02-009-Over head Crane	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	205d	2	0%	0%	0
JDI	Review & approval MS for Over h	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	170d	1	100%	0%	0
JDI	Prepare & Submit MS for Over he	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	206d	1	100%	0%	0
	JDH3-02-009-GLS Tank	18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	374d	2	0%	0%	0
JDI	Review & approval MS for GLS Ta	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	310d	1	100%	0%	0

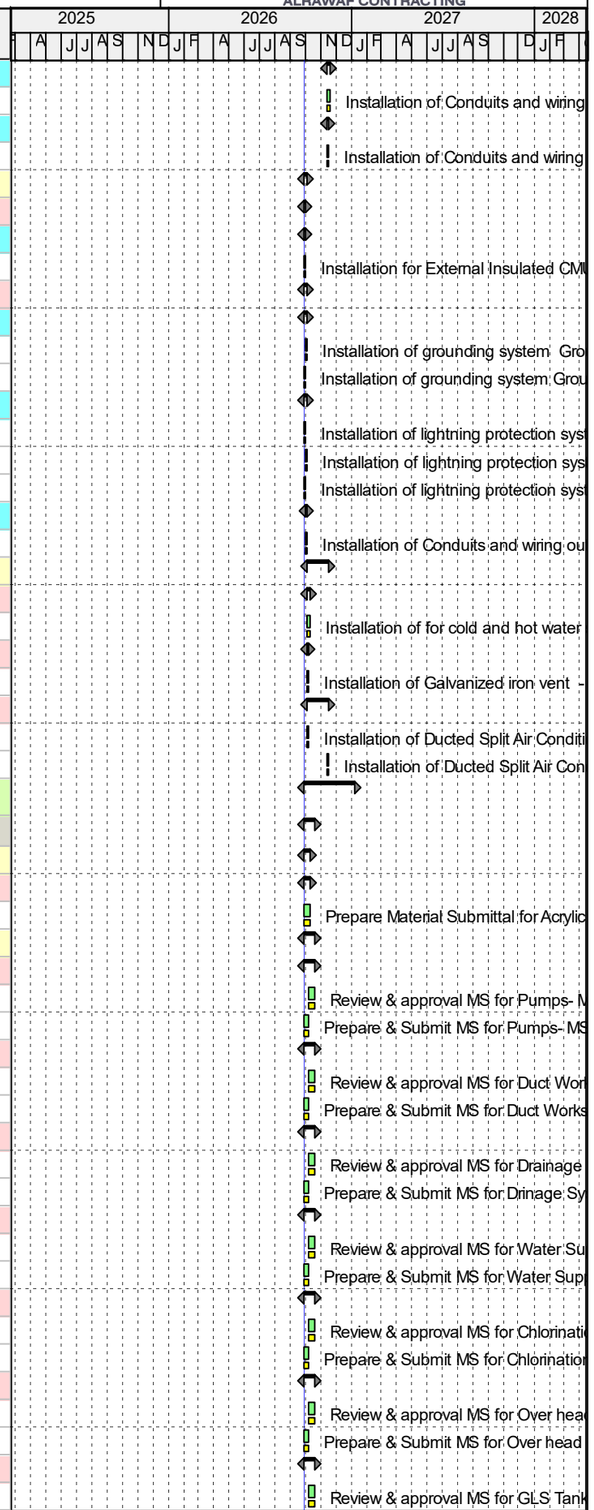


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDI	Prepare & Submit MS for GLS Ta	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	374d	1	100%	0%	0
JDH3-02-009-Access Control		18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	177d	2	0%	0%	0
JDI	Review & approval MS for Access	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	146d	1	100%	0%	0
JDI	Prepare & Submit MS for Access	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	176d	1	100%	0%	0
JDH3-02-009-Data Communication		18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	175d	2	0%	0%	0
JDI	Review & approval MS for Data C	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	145d	1	100%	0%	0
JDI	Prepare & Submit MS for Data Cc	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	175d	1	100%	0%	0
JDH3-02-009-Security System		18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	178d	2	0%	0%	0
JDI	Review & approval MS for Securit	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	147d	1	100%	0%	0
JDI	Prepare & Submit MS for Security	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	177d	1	100%	0%	0
JDH3-02-009-Programing Logical Contrc		18d	18d	23-Jun-26	15-Jul-26	29-Sep-26	19-Oct-26	371d	2	0%	0%	0
JDI	Review & approval MS for Prograi	9d	9d	05-Jul-26	15-Jul-26	07-Oct-26	19-Oct-26	308d	1	100%	0%	0
JDI	Prepare & Submit MS for Progran	7d	7d	23-Jun-26	04-Jul-26	29-Sep-26	06-Oct-26	372d	1	100%	0%	0
Procurement		87d	87d	23-Jun-26	28-Nov-26	29-Sep-26	08-Jan-27	94d	5	0%	0%	0
Long Lead Items		87d	87d	23-Jun-26	28-Nov-26	29-Sep-26	08-Jan-27	94d	5	0%	0%	0
Purchase Order - PO - TSE Pump Statio		10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	107d	3	0%	0%	0
JDH3-02-009-Long Lead Items - LOL-I		10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	107d	3	0%	0%	0
	Material Purchase Order for Data	10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	107d	1	100%	0%	0
	Material Purchase Order for Acce	10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	98d	1	100%	0%	0
	Material Purchase Order for Addre	10d	10d	23-Jun-26	09-Jul-26	29-Sep-26	10-Oct-26	89d	1	100%	0%	0
Fabrication - FAB - TSE Pump Station		90d	90d	11-Jul-26	28-Nov-26	11-Oct-26	08-Jan-27	114d	2	0%	0%	0
JDH3-02-009-Long Lead Items - LOL-I		90d	90d	11-Jul-26	28-Nov-26	11-Oct-26	08-Jan-27	114d	2	0%	0%	0
	Material Fabrication for Access Cc	90d	90d	11-Jul-26	28-Nov-26	11-Oct-26	08-Jan-27	114d	1	56.74%	0%	0
	Material Fabrication for Addressat	90d	90d	11-Jul-26	28-Nov-26	11-Oct-26	08-Jan-27	104d	1	56.74%	0%	0
Authorities Permits & Approval		9d	9d	23-Jun-26	09-Jul-26	29-Sep-26	11-Oct-26	245d	2	0%	0%	0
JDH3ATF	NWC Authorities Permits & Appro	9d	9d	23-Jun-26	09-Jul-26	29-Sep-26	11-Oct-26	220d	1	100%	0%	0
JDH3ATF	SEC Authorities Permits & Approv	9d	9d	23-Jun-26	09-Jul-26	29-Sep-26	11-Oct-26	245d	1	100%	0%	0
JDH3-02-009-PW Pump Station		119d	119d	23-Jun-26	29-Sep-26	29-Sep-26	14-Feb-27	325d	62	99.74%	0%	982,293
Engineering		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	426d	21	0%	0%	0
JDH3-02-009-Prequalification and Material Subm		11d	11d	23-Jun-26	05-Jul-26	29-Sep-26	11-Oct-26	433d	1	0%	0%	0
JDH3-02-009-Prequalifications and Mate		11d	11d	23-Jun-26	05-Jul-26	29-Sep-26	11-Oct-26	433d	1	0%	0%	0
JDI	Prepare Material Submittal for Acr	11d	11d	23-Jun-26	05-Jul-26	29-Sep-26	11-Oct-26	433d	1	100%	0%	0
JDH3-02-009-Method of State me nt for PW Pum		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	406d	20	0%	0%	0
JDH3-02-009-Pumps		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	365d	2	0%	0%	0
JDI	Review & approval MS for Pumps	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	303d	1	100%	0%	0
JDI	Prepare & Submit MS for Pumps-	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	366d	1	100%	0%	0
JDH3-02-009-Duct Works		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	386d	2	0%	0%	0
JDI	Review & approval MS for Duct W	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	320d	1	100%	0%	0
JDI	Prepare & Submit MS for Duct W	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	386d	1	100%	0%	0
JDH3-02-009-Drainage System		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	268d	2	0%	0%	0
JDI	Review & approval MS for Drainag	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	222d	1	100%	0%	0
JDI	Prepare & Submit MS for Drinage	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	268d	1	100%	0%	0
JDH3-02-009-Water Supply System		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	358d	2	0%	0%	0
JDI	Review & approval MS for Water S	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	297d	1	100%	0%	0
JDI	Prepare & Submit MS for Water S	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	358d	1	100%	0%	0
JDH3-02-009-Chlorination System		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	381d	2	0%	0%	0
JDI	Review & approval MS for Chlorin	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	316d	1	100%	0%	0
JDI	Prepare & Submit MS for Chlorina	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	381d	1	100%	0%	0
JDH3-02-009-Over head Crane		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	148d	2	0%	0%	0
JDI	Review & approval MS for Over h	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	123d	1	100%	0%	0
JDI	Prepare & Submit MS for Over he	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	149d	1	100%	0%	0
JDH3-02-009-Access Control		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	275d	2	0%	0%	0

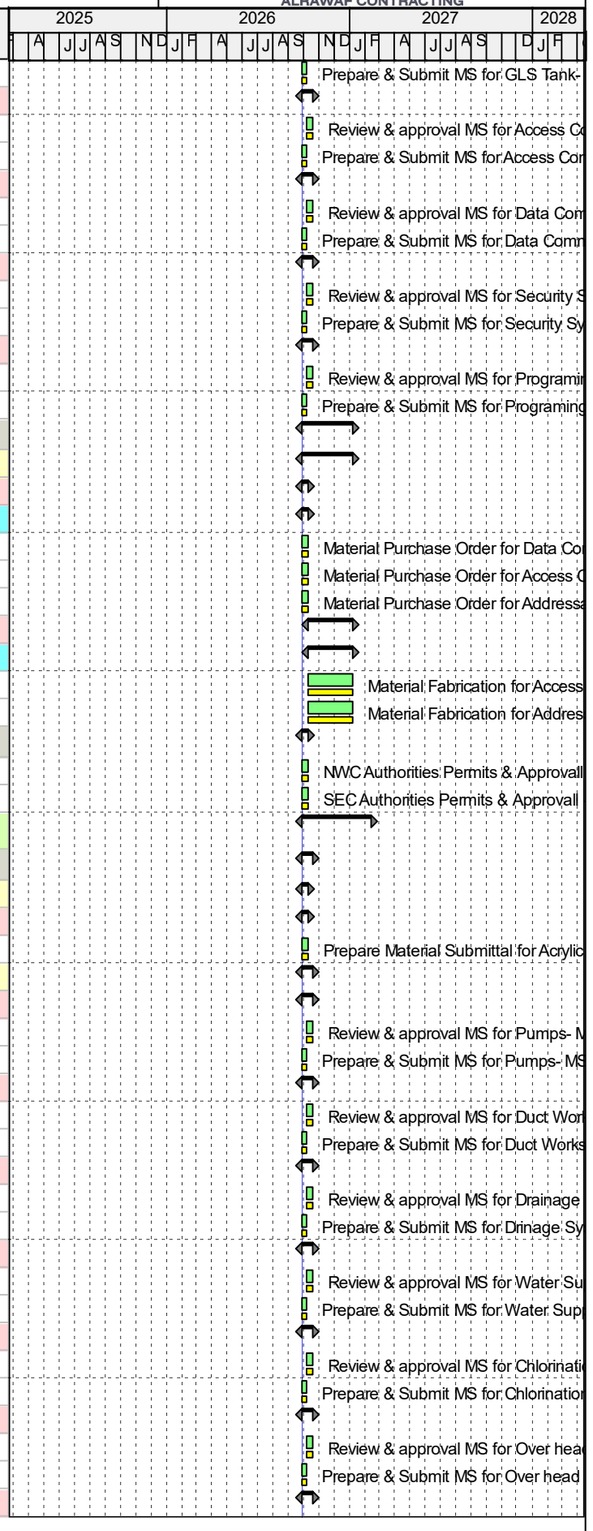


Actual Level of Effort
Actual Work
Remaining Work
Primary Baseline
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
JDI	Review & approval MS for Access	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	228d	1	100%	0%	0
JDI	Prepare & Submit MS for Access	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	275d	1	100%	0%	0
JDH3-02-009-Data Communication		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	227d	2	0%	0%	0
JDI	Review & approval MS for Data C	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	188d	1	100%	0%	0
JDI	Prepare & Submit MS for Data Cc	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	227d	1	100%	0%	0
JDH3-02-009-Security System		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	406d	2	0%	0%	0
JDI	Review & approval MS for Securit	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	337d	1	100%	0%	0
JDI	Prepare & Submit MS for Security	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	406d	1	100%	0%	0
JDH3-02-009-Programing Logical Contrc		18d	18d	23-Jun-26	11-Jul-26	29-Sep-26	19-Oct-26	312d	2	0%	0%	0
JDI	Review & approval MS for Prograi	9d	9d	01-Jul-26	11-Jul-26	07-Oct-26	19-Oct-26	259d	1	100%	0%	0
JDI	Prepare & Submit MS for Progran	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	313d	1	100%	0%	0
Procurement		134d	134d	23-Jun-26	25-Sep-26	29-Sep-26	09-Feb-27	19d	4	100%	0%	657,169
Long Lead Items		134d	134d	23-Jun-26	25-Sep-26	29-Sep-26	09-Feb-27	19d	4	100%	0%	657,169
Fabrication - FAB - PW Pump Station		84d	84d	23-Jun-26	27-Jul-26	29-Sep-26	21-Dec-26	44d	2	0%	0%	0
JDH3-02-009-Long Lead Items - LOL-I		84d	84d	23-Jun-26	27-Jul-26	29-Sep-26	21-Dec-26	44d	2	0%	0%	0
Material Fabrication for Access Cc		84d	84d	23-Jun-26	27-Jul-26	29-Sep-26	21-Dec-26	44d	1	100%	0%	0
Material Fabrication for Addressat		84d	84d	23-Jun-26	27-Jul-26	29-Sep-26	21-Dec-26	19d	1	100%	0%	0
Delivery and staging on Site - DOS - PW		50d	50d	28-Jul-26	25-Sep-26	22-Dec-26	09-Feb-27	19d	2	100%	0%	657,169
JDH3-02-009-Long Lead Items - LOL-I		50d	50d	28-Jul-26	25-Sep-26	22-Dec-26	09-Feb-27	19d	2	100%	0%	657,169
delivery and staging for Access C		25d	25d	27-Aug-26	25-Sep-26	16-Jan-27	09-Feb-27	19d	1	100%	0%	328,585
delivery and staging for Addressa		25d	25d	28-Jul-26	26-Aug-26	22-Dec-26	15-Jan-27	19d	1	100%	0%	328,585
Construction		119d	119d	23-Jun-26	29-Sep-26	29-Sep-26	14-Feb-27	129d	37	99.21%	0%	325,124
JDH3-02-009-B9-PUMP STATION		119d	119d	23-Jun-26	29-Sep-26	29-Sep-26	14-Feb-27	129d	29	99.19%	0%	319,070
JDH3-02-009-B9-Sub Structure		9d	9d	28-Jul-26	12-Aug-26	29-Sep-26	08-Oct-26	98d	4	100%	0%	33,790
JDH3-02-009-B9-Slab on Grade		9d	9d	28-Jul-26	12-Aug-26	29-Sep-26	08-Oct-26	98d	4	100%	0%	33,790
Deshuttering Slab on Grade - (B9		2d	2d	11-Aug-26	12-Aug-26	07-Oct-26	08-Oct-26	98d	1	100%	0%	3,379
RC Casting Slab on Grade - (B9.		2d	2d	09-Aug-26	10-Aug-26	05-Oct-26	06-Oct-26	98d	1	100%	0%	6,758
Steel Fixing Slab on Grade - (B9.		3d	3d	03-Aug-26	08-Aug-26	01-Oct-26	04-Oct-26	98d	1	100%	0%	16,895
Shuttering Slab on Grade - (B9. 3		2d	2d	28-Jul-26	02-Aug-26	29-Sep-26	30-Sep-26	98d	1	100%	0%	6,758
JDH3-02-009-B9-Super Structure		90d	90d	25-Aug-26	28-Sep-26	13-Oct-26	26-Jan-27	145d	15	100%	0%	190,672
JDH3-02-009-B9-Roof Beam		8d	8d	25-Aug-26	02-Sep-26	21-Oct-26	29-Oct-26	209d	4	100%	0%	23,272
Deshuttering Roof Beam - (B9. 3.		2d	2d	01-Sep-26	02-Sep-26	28-Oct-26	29-Oct-26	209d	1	100%	0%	2,327
RC Casting Roof Beam - (B9. 3.2		2d	2d	30-Aug-26	31-Aug-26	26-Oct-26	27-Oct-26	209d	1	100%	0%	4,654
Steel Fixing Roof Beam - (B9. 3.2		2d	2d	27-Aug-26	29-Aug-26	24-Oct-26	25-Oct-26	209d	1	100%	0%	11,636
Shuttering Roof Beam - (B9. 3.2.4		2d	2d	25-Aug-26	26-Aug-26	21-Oct-26	22-Oct-26	209d	1	100%	0%	4,654
JDH3-02-009-B9-Roof Slab		8d	8d	25-Aug-26	02-Sep-26	13-Oct-26	22-Oct-26	98d	4	100%	0%	9,590
Deshuttering Roof Slab - (B9. 3.2		2d	2d	01-Sep-26	02-Sep-26	20-Oct-26	22-Oct-26	98d	1	100%	0%	959
RC Casting Roof Slab - (B9. 3.2.5		2d	2d	30-Aug-26	31-Aug-26	18-Oct-26	20-Oct-26	98d	1	100%	0%	1,918
Steel Fixing Roof Slab - (B9. 3.2.5		2d	2d	27-Aug-26	29-Aug-26	15-Oct-26	18-Oct-26	98d	1	100%	0%	4,795
Shuttering Roof Slab - (B9. 3.2.5)		2d	2d	25-Aug-26	26-Aug-26	13-Oct-26	15-Oct-26	98d	1	100%	0%	1,918
JDH3-02-009-B9-Hollow Core slab		10d	10d	03-Sep-26	14-Sep-26	31-Oct-26	10-Nov-26	209d	2	100%	0%	137,001
Hollow Core Slab Screed Hollow C		8d	8d	06-Sep-26	14-Sep-26	02-Nov-26	10-Nov-26	209d	1	100%	0%	109,601
Hollow Core Slab Installation Holl		2d	2d	03-Sep-26	05-Sep-26	31-Oct-26	01-Nov-26	209d	1	100%	0%	27,400
JDH3-02-009-B9-Entrance and Ramps		2d	2d	27-Sep-26	28-Sep-26	25-Jan-27	26-Jan-27	145d	1	100%	0%	2,725
Shuttering Entrance and Ramps -		2d	2d	27-Sep-26	28-Sep-26	25-Jan-27	26-Jan-27	145d	1	100%	0%	2,725
JDH3-02-009-B9-pump pads		69d	69d	16-Sep-26	26-Sep-26	04-Nov-26	24-Jan-27	145d	4	100%	0%	18,084
Deshuttering Pump Pads - (B9. 3		2d	2d	24-Sep-26	26-Sep-26	23-Jan-27	24-Jan-27	145d	1	100%	0%	1,808
RC Casting Pump Pads - (B9. 3.2		2d	2d	21-Sep-26	22-Sep-26	09-Nov-26	11-Nov-26	206d	1	100%	0%	3,617
Steel Fixing Pump Pads - (B9. 3.2		2d	2d	19-Sep-26	20-Sep-26	07-Nov-26	09-Nov-26	206d	1	100%	0%	9,042
Shuttering Pump Pads - (B9. 3.2.		2d	2d	16-Sep-26	17-Sep-26	04-Nov-26	07-Nov-26	206d	1	100%	0%	3,617
JDH3-02-009-B9-Finishes		34d	34d	23-Jun-26	17-Sep-26	29-Sep-26	07-Nov-26	103d	3	100%	0%	46,860
JDH3-02-009-B9-Masonary		13d	13d	03-Sep-26	17-Sep-26	22-Oct-26	07-Nov-26	103d	2	100%	0%	34,746

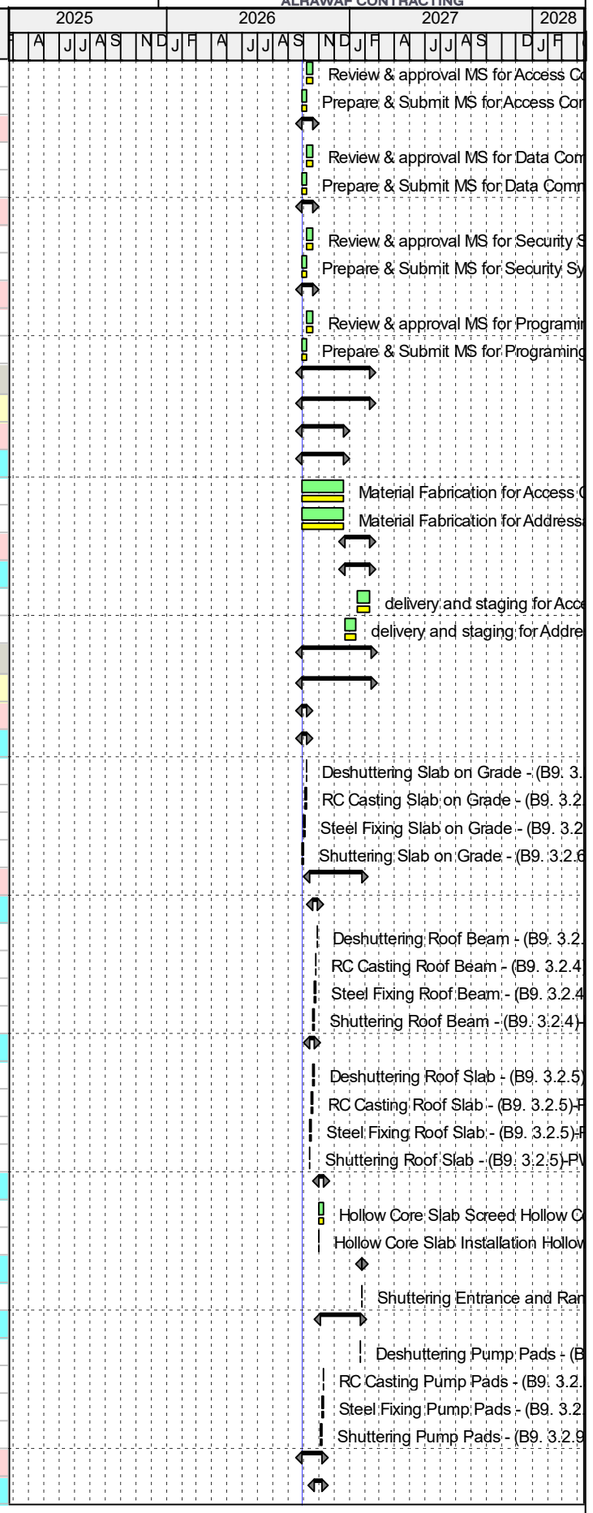

Actual Level of Effort
Actual Work
Remaining Work
Primary Baseline
Critical Remaining Work
Milestone

EGIS Template - Delayed Activities

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Remaining Duration	BL Project Start	BL Project Finish	Start	Finish	Total Float	Activity Count	Schedule % Complete	Performance % Complete	Budgeted Total Cost
	Masonary Block work Block Work	2d	2d	16-Sep-26	17-Sep-26	04-Nov-26	07-Nov-26	103d	1	100%	0%	1,637
	Masonary Block work Insulated Bl	11d	11d	03-Sep-26	15-Sep-26	22-Oct-26	04-Nov-26	98d	1	100%	0%	33,109
JDH3-02-009-B9-Thermal & Moisture		7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	100d	1	100%	0%	12,114
	Applying Bitumen waterproofing F	7d	7d	23-Jun-26	30-Jun-26	29-Sep-26	06-Oct-26	100d	1	100%	0%	12,114
JDH3-02-009-B9-Mechanical Works-pha		10d	10d	13-Aug-26	24-Aug-26	10-Oct-26	20-Oct-26	209d	1	100%	0%	2,845
JDH3-02-009-B9-Soakage Pits (For A(		10d	10d	13-Aug-26	24-Aug-26	10-Oct-26	20-Oct-26	209d	1	100%	0%	2,845
	Soakage Pits Installation 600*60(	10d	10d	13-Aug-26	24-Aug-26	10-Oct-26	20-Oct-26	209d	1	100%	0%	2,845
JDH3-02-009-B9-Electrical Works for Po		110d	110d	16-Aug-26	29-Sep-26	08-Oct-26	14-Feb-27	17d	6	94.24%	0%	44,902
JDH3-02-009-B9-LED Interior Lighting		2d	2d	16-Sep-26	17-Sep-26	04-Nov-26	07-Nov-26	100d	1	100%	0%	4,363
	Electrical Conduits and Pull Box I	2d	2d	16-Sep-26	17-Sep-26	04-Nov-26	07-Nov-26	100d	1	100%	0%	4,363
JDH3-02-009-B9-Grounding and Bond		4d	4d	16-Aug-26	19-Aug-26	08-Oct-26	13-Oct-26	98d	1	100%	0%	20,522
	Copper Conductor Connecting to	4d	4d	16-Aug-26	19-Aug-26	08-Oct-26	13-Oct-26	98d	1	100%	0%	20,522
JDH3-02-009-B9-Addressable Fire-Al		4d	4d	16-Sep-26	20-Sep-26	16-Jan-27	19-Jan-27	37d	1	100%	0%	3,680
	1st Fix, Conduits and Pull Box Ins	4d	4d	16-Sep-26	20-Sep-26	16-Jan-27	19-Jan-27	37d	1	100%	0%	3,680
JDH3-02-009-B9-Data Communicatior		6d	6d	16-Sep-26	22-Sep-26	16-Jan-27	21-Jan-27	37d	1	100%	0%	732
	1st Fix, Conduits and Pull Box Ins	6d	6d	16-Sep-26	22-Sep-26	16-Jan-27	21-Jan-27	37d	1	100%	0%	732
JDH3-02-009-B9-Access control syst		4d	4d	26-Sep-26	29-Sep-26	10-Feb-27	14-Feb-27	15d	1	75%	0%	10,338
	1st Fix, Conduits and Pull Box Ins	4d	4d	26-Sep-26	29-Sep-26	10-Feb-27	14-Feb-27	15d	1	75%	0%	10,338
JDH3-02-009-B9-CCTV system		3d	3d	26-Sep-26	28-Sep-26	10-Feb-27	13-Feb-27	16d	1	100%	0%	5,268
	1st Fix, Conduits and Pull Box Ins	3d	3d	26-Sep-26	28-Sep-26	10-Feb-27	13-Feb-27	16d	1	100%	0%	5,268
JDH3-02-009-B10-GUARD HOUSE		22d	22d	23-Jun-26	18-Jul-26	29-Sep-26	24-Oct-26	222d	8	100%	0%	6,054
JDH3-02-009-B10-Sub Structure		8d	8d	25-Jun-26	04-Jul-26	01-Oct-26	10-Oct-26	222d	4	100%	0%	1,852
JDH3-02-009-B10-Slab on Grade		8d	8d	25-Jun-26	04-Jul-26	01-Oct-26	10-Oct-26	222d	4	100%	0%	1,852
	Deshuttering Slab on Grade - (B1	2d	2d	02-Jul-26	04-Jul-26	08-Oct-26	10-Oct-26	222d	1	100%	0%	185
	RC Casting Slab on Grade - (B10	2d	2d	30-Jun-26	01-Jul-26	06-Oct-26	07-Oct-26	222d	1	100%	0%	370
	Steel Fixing Slab on Grade - (B1(	2d	2d	28-Jun-26	29-Jun-26	04-Oct-26	05-Oct-26	222d	1	100%	0%	926
	Shuttering Slab on Grade - (B10.	2d	2d	25-Jun-26	27-Jun-26	01-Oct-26	03-Oct-26	222d	1	100%	0%	370
JDH3-02-009-B10-Finishes		14d	14d	23-Jun-26	08-Jul-26	29-Sep-26	14-Oct-26	222d	3	100%	0%	2,716
JDH3-02-009-B10-Masonary		4d	4d	05-Jul-26	08-Jul-26	11-Oct-26	14-Oct-26	222d	2	100%	0%	2,616
	Masonary Block work Block Work	2d	2d	07-Jul-26	08-Jul-26	13-Oct-26	14-Oct-26	222d	1	100%	0%	353
	Masonary Block work ACC Block -	2d	2d	05-Jul-26	06-Jul-26	11-Oct-26	12-Oct-26	222d	1	100%	0%	2,263
JDH3-02-009-B10-Thermal & Moisture		2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	222d	1	100%	0%	101
	Applying Polyethylene sheet und	2d	2d	23-Jun-26	24-Jun-26	29-Sep-26	30-Sep-26	222d	1	100%	0%	101
JDH3-02-009-B10-Electrical Works for P		8d	8d	09-Jul-26	18-Jul-26	15-Oct-26	24-Oct-26	222d	1	100%	0%	1,486
JDH3-02-009-B10-LV Cables - Copper		8d	8d	09-Jul-26	18-Jul-26	15-Oct-26	24-Oct-26	222d	1	100%	0%	1,486
	Electrical Conduits and Pull Box I	8d	8d	09-Jul-26	18-Jul-26	15-Oct-26	24-Oct-26	222d	1	100%	0%	1,486

