
Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Development of the Technology City in Dhahran Project Recovery -R		3632.00	06-Jan-26 A	08-Jul-27	93,061,973	34,795,176	23,121,817	22,765,905	37.26%	24.76%
Key Milestones		3632.00	06-Jan-26 A	08-Jul-27	0	0	0	0	0%	0%
Contractual Milestones		3632.00	06-Jan-26 A	08-Jul-27	0	0	0	0	0%	0%
MS-CF-EBL	Completion of Execution Plan and Baseline Schedule	0.00		05-Feb-26 A	0	0	0	0	100%	100%
MS-CF-ENG	Completion of Submitting and Approval of Shopdrawing and Materials	0.00		15-Nov-26	0	0	0	0	100%	0%
MS-CF-IR	Completion of Construction Works for Irrigation Network	0.00		05-May-27	0	0	0	0	0%	0%
MS-CF-LO	Completion of Construction Works for Low Voltage Network	0.00		05-May-27	0	0	0	0	0%	0%
MS-CF-MOB	Completion of Mobilization Works	0.00		07-Mar-26 A	0	0	0	0	100%	100%
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0.00		10-Apr-27	0	0	0	0	0%	0%
MS-CF-PF	Project Completion Date	0.00		08-Jul-27	0	0	0	0	0%	0%
MS-CF-PW	Completion of Construction Works for Potable Water Network	0.00		05-May-27	0	0	0	0	0%	0%
MS-CF-RD	Completion of Construction Works for Road Works	0.00		05-May-27	0	0	0	0	0%	0%
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0.00		04-May-27	0	0	0	0	0%	0%
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0.00		04-May-27	0	0	0	0	0%	0%
MS-CF-SW	Completion of Construction Works for Sewage Network	0.00		25-Feb-27	0	0	0	0	0%	0%
MS-CF-TE	Completion of Construction Works for Telecom and Light Current Networks	0.00		05-May-27	0	0	0	0	0%	0%
MS-CF-TSE	Completion of Construction Works for Treated Sewage Effluent Network	0.00		29-May-27	0	0	0	0	0%	0%
MS-CS-PS	Project Commencement Date (Site Handover)	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-MO-10	Completion of Sewage Pump Station	0.00		16-Jun-27	0	0	0	0	0%	0%
MS-MO-20	Completion of Storm Drainage Ponds	0.00		28-Apr-27	0	0	0	0	0%	0%
MS-MO-40	Completion of Control Room	0.00		05-Jul-27	0	0	0	0	0%	0%
MS-MO-50	Completion of Water Pump Station	0.00		16-Jun-27	0	0	0	0	0%	0%
MS-MO-60	Completion of Irrigation and Potable Tank	0.00		13-Jun-27	0	0	0	0	0%	0%
Control Milestones		1888.00	06-Jan-26 A	19-Oct-26	0	0	0	0	0%	0%
The Employer		1696.00	03-Feb-26 A	19-Oct-26	0	0	0	0	0%	0%
MS-MM-100	Right of Access and Possession of the Site	0.00		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-120	Receipt of Advance Payment for the Project From The Employer	0.00		19-Oct-26	0	0	0	0	100%	0%
MS-MM-130	Receipt the Site Benchmark Coordinates (Original Point) From The Employer	0.00		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-140	Receipt the Site Levels Details From The Employer	0.00		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-150	Receipt of Approved Concept Master Plan for the Project From the Employer	0.00		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-160	Receipt of Master Plan Approval Letter for the Project From the Employer	0.00		03-Feb-26 A	0	0	0	0	100%	100%
NOC's		0.00	06-Jan-26 A	06-Jan-26 A	0	0	0	0	0%	0%
Infrastructure Networks		0.00	06-Jan-26 A	06-Jan-26 A	0	0	0	0	0%	0%
MS-CS-IR	Receipt of Approval NOC From Relevant Authorities For Irrigation Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%

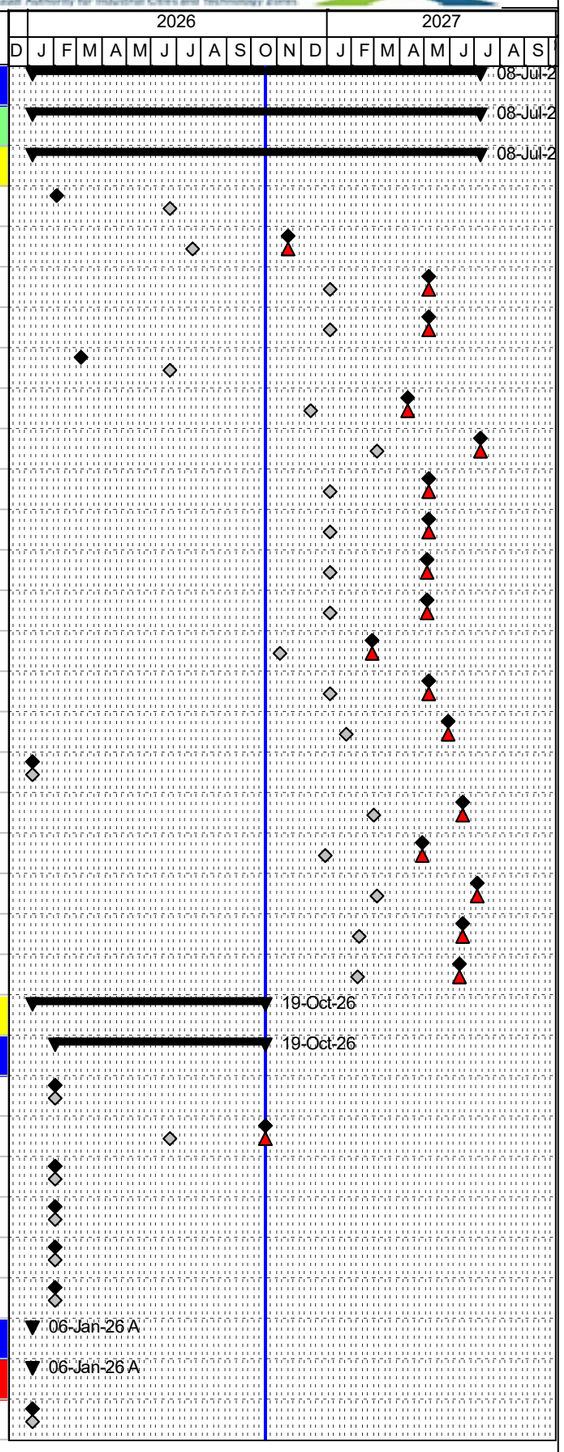

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
MS-CS-LV	Receipt of Approval NOC From Relevant Authorities For Low Voltage Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-MV	Receipt of Approval NOC From Relevant Authorities For Medium Voltage Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-PW	Receipt of Approval NOC From Relevant Authorities For Potable Water Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-RD	Receipt of Approval NOC From Relevant Authorities For Roads Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SD	Receipt of Approval NOC From Relevant Authorities For Storm Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SL	Receipt of Approval NOC From Relevant Authorities For Street Lighting Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SW	Receipt of Approval NOC From Relevant Authorities For Sewage Network	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TE	Receipt of Approval NOC From Relevant Authorities For Telecom and Light Current	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TSE	Receipt of Approval NOC From Relevant Authorities For Treated Sewage Effluent	0.00	06-Jan-26 A		0	0	0	0	100%	100%
Superstructure Works		0.00	06-Jan-26 A	06-Jan-26 A	0	0	0	0	0%	0%
MS-CS-IR10	Receipt of Approval NOC From Relevant Authorities For Sewage Pump Station	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-LV10	Receipt of Approval NOC From Relevant Authorities For Boundary Fence	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-MV10	Receipt of Approval NOC From Relevant Authorities For Water Pump Station	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SL10	Receipt of Approval NOC From Relevant Authorities For Storm Drainage Ponds	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TE10	Receipt of Approval NOC From Relevant Authorities For Storage Tank (TSE)	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TE20	Receipt of Approval NOC From Relevant Authorities For Control Room	0.00	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TSE10	Receipt of Approval NOC From Relevant Authorities For Gaurd Room	0.00	06-Jan-26 A		0	0	0	0	100%	100%
Preliminaries and Mobilization Works		632.00	06-Jan-26 A	11-Apr-26 A	0	0	0	0	0%	0%
Mobilization Works		632.00	06-Jan-26 A	11-Apr-26 A	0	0	0	0	0%	0%
MOB-10	Clear and Grub for Offices and Access Roads	112.00	06-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
MOB-20	Project Site Layout Plan Approval	56.00	21-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
MOB-30	Supply & Install of Temporary Offices for the Project	72.00	01-Apr-26 A	09-Apr-26 A	0	0	0	0	100%	100%
MOB-40	Construction Project Store	80.00	01-Apr-26 A	11-Apr-26 A	0	0	0	0	100%	100%
MOB-50	Mobilization of Major Manpower	48.00	12-Feb-26 A	26-Feb-26 A	0	0	0	0	100%	100%
MOB-60	Mobilization of Major Equipments	48.00	12-Feb-26 A	07-Mar-26 A	0	0	0	0	100%	100%
MOB-70	Installation Project Sign Board	80.00	01-Apr-26 A	11-Apr-26 A	0	0	0	0	100%	100%
MOB-80	Construction Site Access Roads	136.00	28-Jan-26 A	15-Feb-26 A	0	0	0	0	100%	100%
Project Main Documents From The Contractor		224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	0%	0%
PRE-CON-MDC-10	Submission Project Execution Plan	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-20	Submission Project Baseline Schedule	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-30	Submission Project Health & Safety Plan	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-40	Submission Project Quality Control Plan	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-50	Submission Project Surveying Report	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-60	Submission Project Geotechnical Soil Report	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%

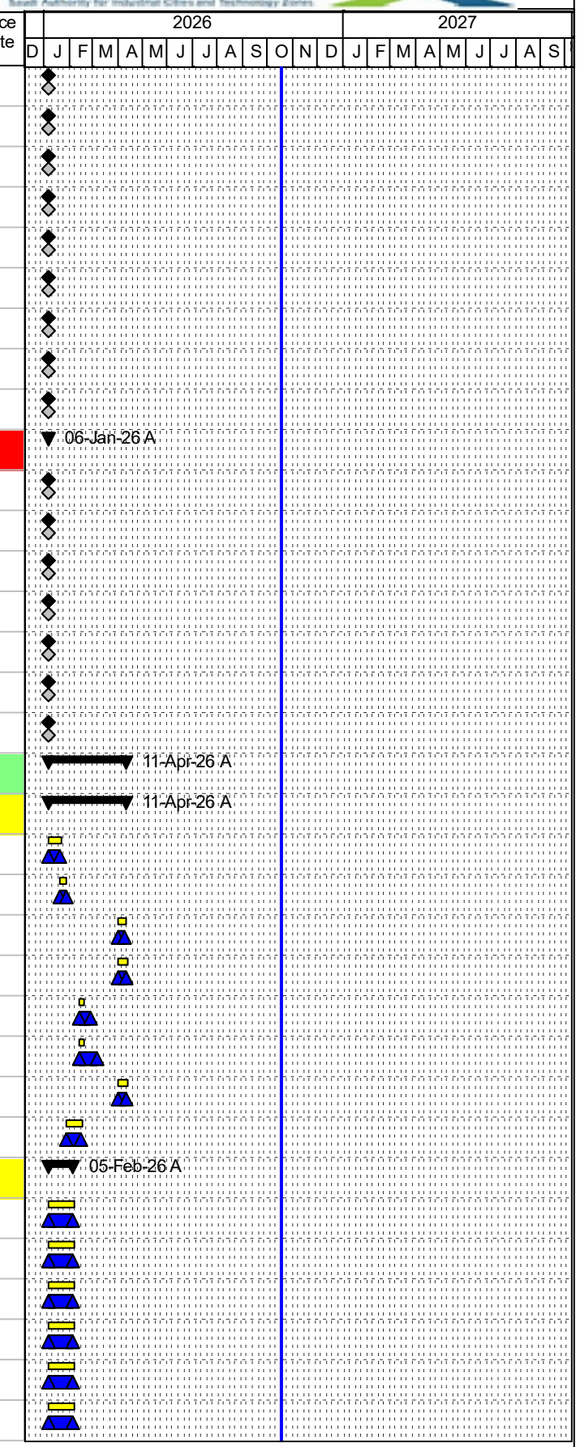

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRE-CON-MDC-70	Submission Project Environmental Plan	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-80	Submission Project Organization Chart and Communications Plan	224.00	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
Engineering Works		2080.00	06-Jan-26 A	15-Nov-26	0	0	0	0	0%	0%
Shop Drawings		216.00	06-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Infrastructure Networks		216.00	06-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Road Works		216.00	06-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
General Road Works		168.00	06-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-SH-RD-A-100	Approval Shop Drawings for Plan and Profile of Road Works	56.00	11-Jan-26 A	17-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-RD-A-110	Approval Shop Drawings for Roads Typical Sections and Pavement Details	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-RD-S-100	Submission Shop Drawings for Plan and Profile of Road Works	40.00	06-Jan-26 A	10-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-RD-S-110	Submission Shop Drawings for Roads Typical Sections and Pavement Details	40.00	18-Jan-26 A	21-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-HS-A-110	Approval Shop Drawings for Landscape Works	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-HS-S-100	Submission Shop Drawings for Landscape Works	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Traffic Sign Boards and Road Marking		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-MRK-A-110	Approval Shop Drawings for Road Markings	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-MRK-S-110	Submission Shop Drawings for Road Markings	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-TSB-A-100	Approval Shop Drawings for Traffic Signs Boards	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-TSB-S-100	Submission Shop Drawings for Traffic Signs Boards	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SD-ML-A-110	Approval Shop Drawings for Main Line and Manholes of Storm Drainage Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SD-ML-S-100	Submission Shop Drawings for Main Line and Manholes of Storm Drainage Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SD-CB-A-110	Approval Shop Drawings for Secondary Line and Catch Basin of Storm Drainage Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SD-CB-S-100	Submission Shop Drawings for Secondary Line and Catch Basin of Storm Drainage	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Ponds		56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-SH-DPO-A-120	Approval Shop Drawings Package for Storm Drainage Ponds	32.00	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-DPO-S-110	Submission Shop Drawings Package for Storm Drainage Ponds	32.00	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
Sewage Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SW-ML-A-110	Approval Shop Drawings for Main Line and Manholes of Sewage Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SW-ML-S-100	Submission Shop Drawings for Main Line and Manholes of Sewage Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Treated Sewage Effluent Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%

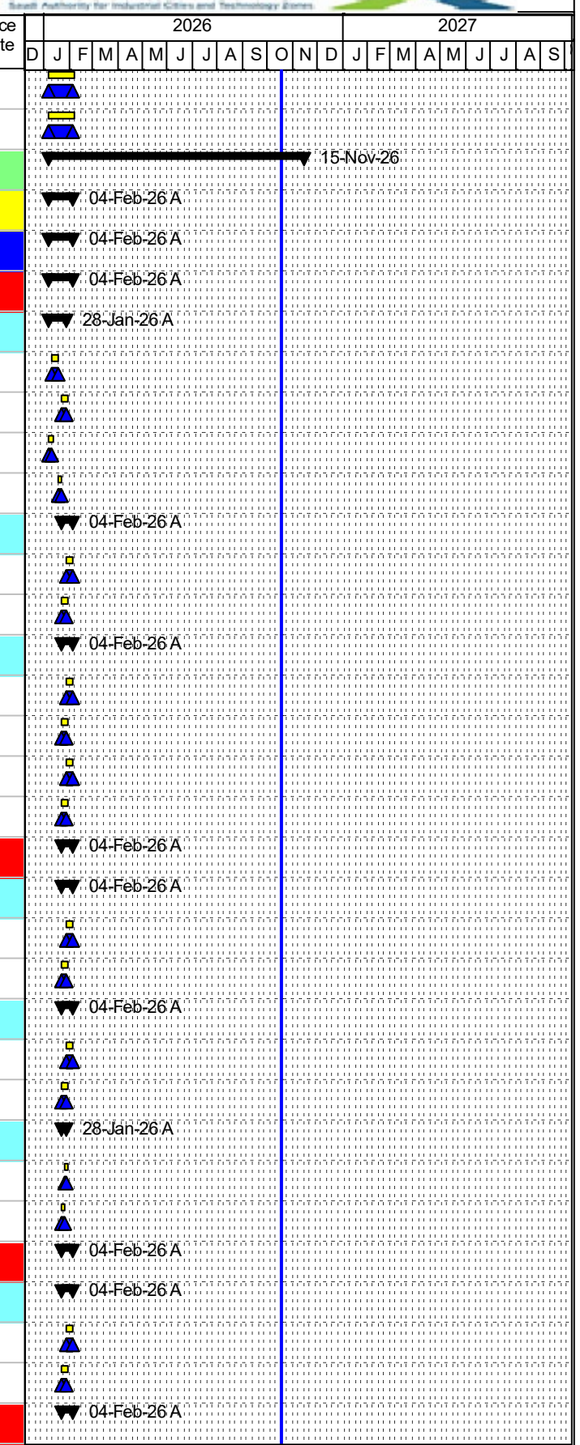

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-SH-TSE-ML-A-120	Approval Shop Drawings for Main Line Treated Sewage Effluent Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-TSE-ML-S-110	Submission Shop Drawings for Main Line Treated Sewage Effluent Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Potable Water Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-PW-ML-A-110	Approval Shop Drawings for Main Line and Valve Chambers of Potable Water Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-PW-ML-S-100	Submission Shop Drawings for Main Line and Valve Chambers of Potable Water Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Fire Hydrant		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-PW-FH-A-110	Approval Shop Drawings for Fire Hydrant Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-PW-FH-S-100	Submission Shop Drawings for Fire Hydrant Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Irrigation Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-IR-ML-A-110	Approval Shop Drawings for Main Line and Valves & Bulbblers and Sprinklers of Irrigation	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-IR-ML-S-100	Submission Shop Drawings for Main Line and Valves & Bulbblers and Sprinklers of Irrigation	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Medium Voltage Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-MV-A-110	Approval Shop Drawings for Medium Voltage Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-MV-S-100	Submission Shop Drawings for Medium Voltage Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Low Voltage Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-LV-A-120	Approval Shop Drawings for Low Voltage Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-LV-S-110	Submission Shop Drawings for Low Voltage Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Street Lighting Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SL-A-110	Approval Shop Drawings for Street Lighting Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SL-S-100	Submission Shop Drawings for Street Lighting Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Telecom Network		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-CTV-A-110	Approval Shop Drawings for CCTV and Telephone Complete Systems	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-CTV-S-100	Submission Shop Drawings for CCTV and Telephone Complete Systems	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-MSN-A-120	Approval Shop Drawings for MSN and Access Control Systems	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-MSN-S-110	Submission Shop Drawings for MSN and Access Control Systems	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-TE-A-110	Approval Shop Drawings for Telecom Network	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-TE-S-100	Submission Shop Drawings for Telecom Network	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Superstructure Works		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Water Pump Station		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-LS-A-170	Approval Shop Drawings Package for Water Pump Station	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-LS-S-160	Submission Shop Drawings Package for Water Pump Station	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Storage Tank (TSE)		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%

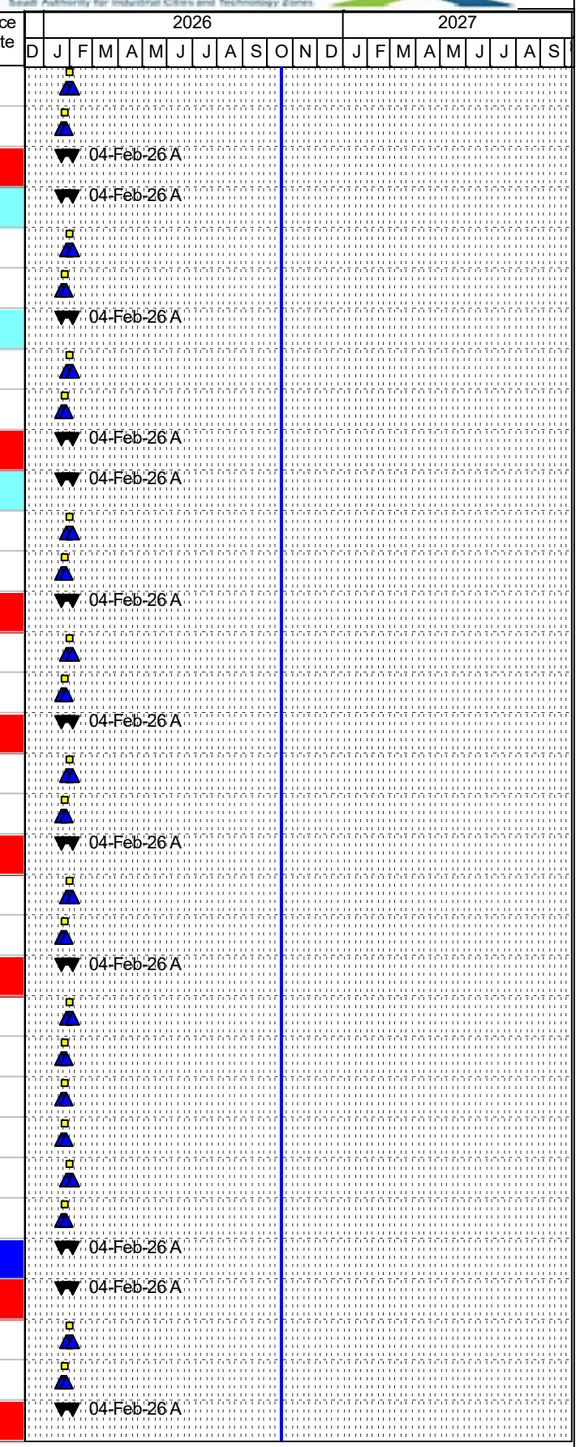

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-SH-ST-A-180	Approval Shop Drawings Package for Storage Tank TSE	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-ST-S-170	Submission Shop Drawings Package for Storage Tank TSE	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Control Room		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-ST-A-190	Approval Shop Drawings Package for Control Room	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-ST-S-180	Submission Shop Drawings Package for Control Room	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Sewage Pump Stations		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SPS-A-160	Approval Shop Drawings Package for Sewage Pump Station	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SPS-S-150	Submission Shop Drawings Package for Sewage Pump Station	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Gaurd Room		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-GR-A-190	Approval Shop Drawings Package for Gaurd Room	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-GR-S-180	Submission Shop Drawings Package for Gaurd Room	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Boundary Fence		104.00	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-GR-A-200	Approval Shop Drawings Package for Boundary Fence	56.00	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-GR-S-190	Submission Shop Drawings Package for Boundary Fence	56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Method Statements		104.00	18-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Infrastructure Networks		104.00	18-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Storm Drainage Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		40.00	25-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SD-ML-A-110	Approval Method Statement for Main Line of Storm Drainage Network	32.00	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SD-ML-S-100	Submission Method Statement for Main Line of Storm Drainage Network	16.00	25-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SD-CB-A-110	Approval Method Statement for Catch Basin of Storm Drainage Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SD-CB-S-100	Submission Method Statement for Catch Basin of Storm Drainage Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Ponds		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-DPO-A-130	Approval Method Statement Package for Storm Drainage Ponds	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-DPO-S-120	Submission Method Statement Package for Storm Drainage Ponds	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Sewage Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SW-ML-A-110	Approval Method Statement for Main Line of Sewage Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SW-ML-S-100	Submission Method Statement for Main Line of Sewage Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Treated Sewage Effluent Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-TSE-ML-A-120	Approval Method Statement for Main Line of Treated Sewage Effluent Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TSE-ML-S-110	Submission Method Statement for Main Line of Treated Sewage Effluent Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Potable Water Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%

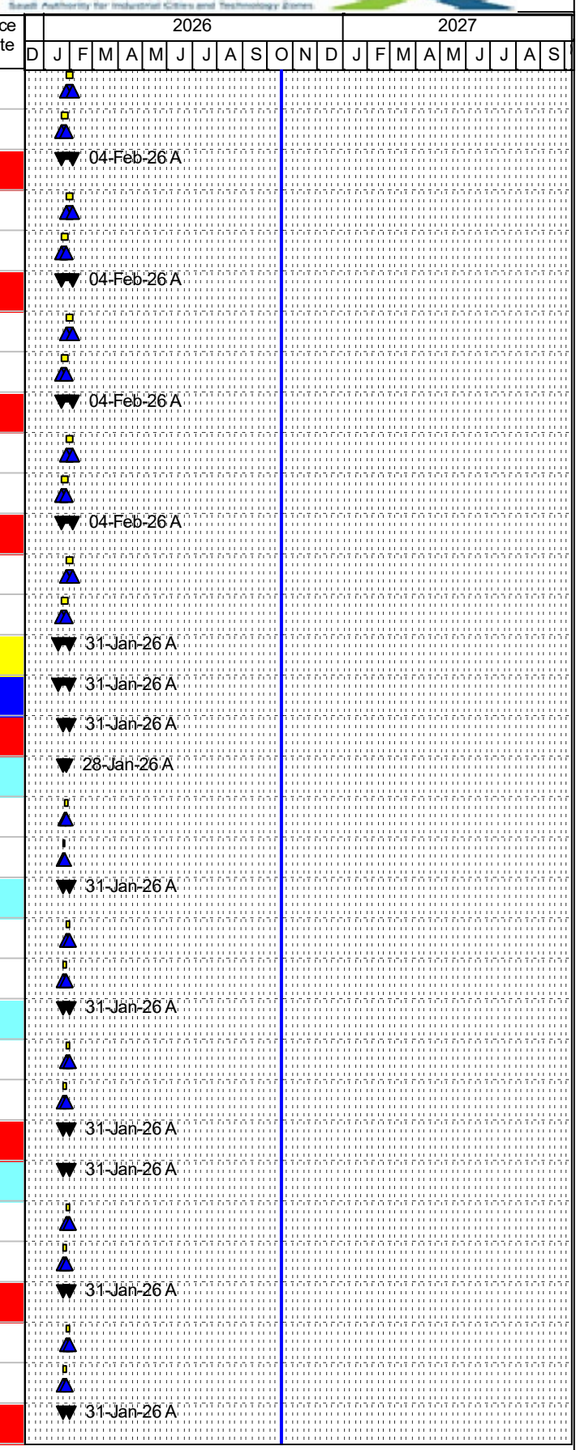

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Main Line Sections		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-PW-ML-A-110	Approval Method Statement for Main Line of Potable Water Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-PW-ML-S-100	Submission Method Statement for Main Line of Potable Water Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Irrigation Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-IR-ML-A-110	Approval Method Statement for Main Line of Irrigation Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-IR-ML-S-100	Submission Method Statement for Main Line of Irrigation Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Medium Voltage Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-MV-A-110	Approval Method Statement for Medium Voltage Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-MV-S-100	Submission Method Statement for Medium Voltage Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Low Voltage Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-MV-A-120	Approval Method Statement for Low Voltage Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-MV-S-110	Submission Method Statement for Low Voltage Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Street Lighting Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SL-A-110	Approval Method Statement for Street Lighting Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SL-S-100	Submission Method Statement for Street Lighting Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Telecom Network		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-CTV-A-110	Approval Method Statement for CCTV, Telephone, MSN, and Access Control	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-CTV-S-100	Submission Method Statement for CCTV, Telephone, MSN, and Access Control	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TE-A-110	Approval Method Statement for Telecom Network	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TE-S-100	Submission Method Statement for Telecom Network	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Road Works		88.00	18-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
General Road Works		88.00	18-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-RD-A-10	Approval Method Statement for Plan and Profile of Road Works	32.00	21-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-A-20	Approval Method Statement for Roads Typical Sections and Pavement Details	32.00	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-A-30	Approval Method Statement of Extraover for Pedestrian ramps	32.00	21-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-A-40	Approval Method Statement for Intersections of Road Works	32.00	21-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-10	Submission Method Statement for Plan and Profile of Road Works	32.00	18-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-20	Submission Method Statement for Roads Typical Sections and Pavement Details	32.00	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-30	Submission Method Statement of Extraover for Pedestrian ramps	32.00	18-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-40	Submission Method Statement for Intersections of Road Works	32.00	18-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-HS-A-10	Approval Method Statement for Landscaping Works	32.00	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-HS-S-10	Submission Method Statement for Landscaping Works	32.00	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%

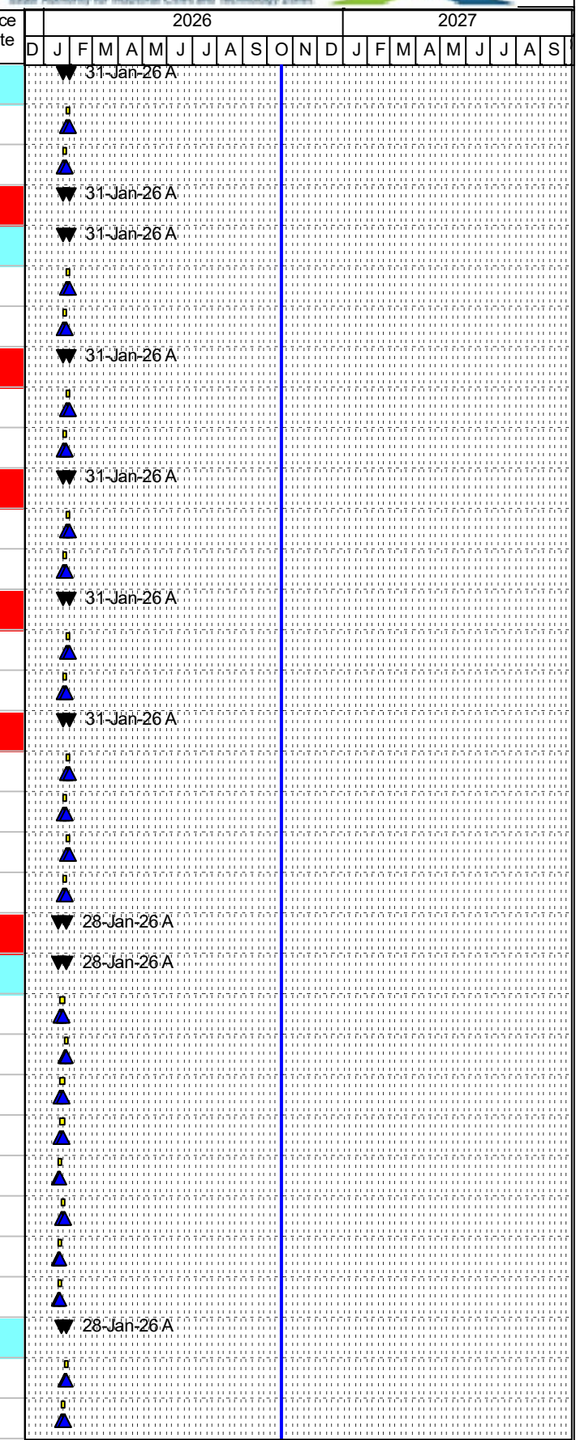

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Traffic Sign Boards and Road Marking		56.00	22-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-MRK-A-10	Approval Method Statement for Roads Markings	32.00	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-MRK-S-10	Submission Method Statement for Roads Markings	32.00	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TSB-A-10	Approval Method Statement for Traffic Signs Boards	32.00	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TSB-S-10	Submission Method Statement for Traffic Signs Boards	32.00	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
Superstructure Works		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Water Pump Station		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-LS-A-180	Approval Method Statement Package for Water Pump Station	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-LS-S-170	Submission Method Statement Package for Water Pump Station	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Storage Tank (TSE)		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-ST-A-190	Approval Method Statement Package for Storage Tank TSE	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-ST-S-180	Submission Method Statement Package for Storage Tank TSE	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Control Room		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-ST-A-200	Approval Method Statement Package for Control Room	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-ST-S-190	Submission Method Statement Package for Control Room	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Sewage Pump Stations		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SPS-A-170	Approval Method Statement Package for Sewage Pump Station	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SPS-S-160	Submission Method Statement Package for Sewage Pump Station	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Gaurd Room		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-GR-A-210	Approval Method Statement Package for Gaurd Room	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-GR-S-200	Submission Method Statement Package for Gaurd Room	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Boundary Fence		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-GR-A-220	Approval Method Statement Package for Boundary Fence	32.00	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-GR-S-210	Submission Method Statement Package for Boundary Fence	32.00	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Material Submittals and Approvals		2080.00	06-Jan-26 A	15-Nov-26	0	0	0	0	0%	0%
Short Lead Time Items		992.00	06-Jan-26 A	13-Jun-26 A	0	0	0	0	0%	0%
Infrastructure Networks		184.00	06-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Storm Drainage Network		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-ML-S-100	Material Submittal for Manholes of Storm Drainage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-ML-S-110	Material Submittal for Main Line Pipes of Storm Drainage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-CB-S-100	Material Submittal for Catch Basins of Storm Drainage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%

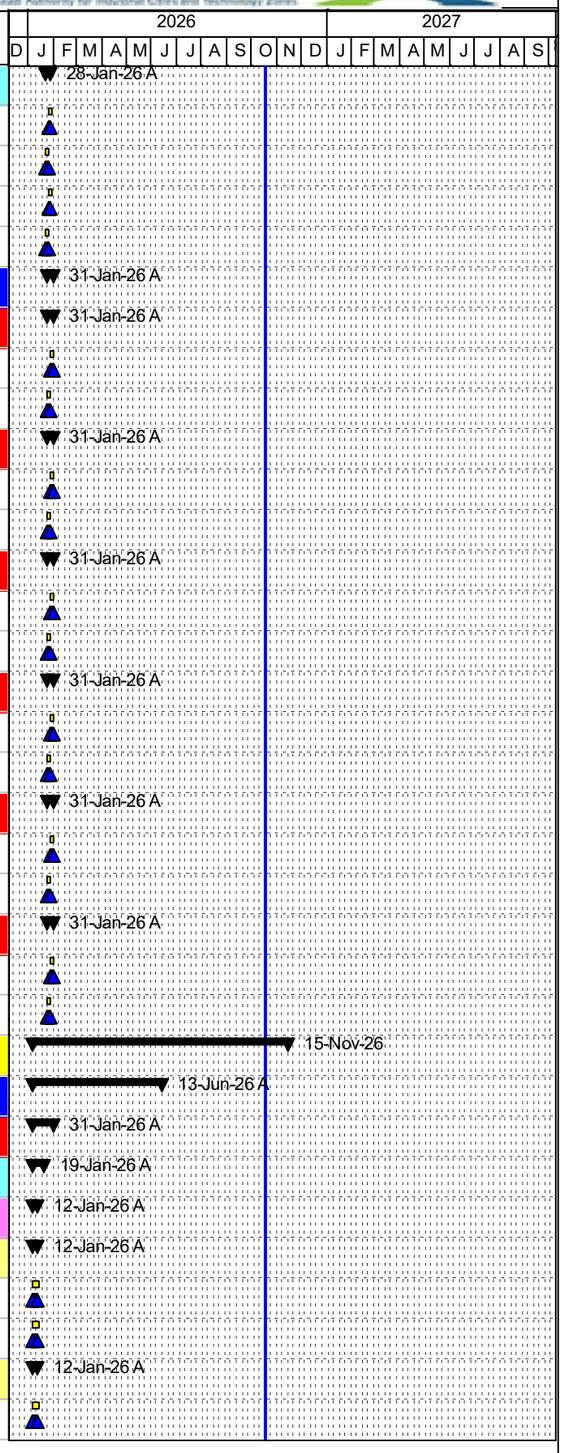

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-MT-SD-CB-S-110	Material Submittal for Catch Basin Pipes of Storm Drainage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Pond		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-DPO-CV-S-100	Material Submittal for Materials of Storm Drainage Ponds	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-TF-S-100	Material Submittal for Manhole Covers of Storm Drainage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-TF-S-110	Material Submittal for Catch Basin Covers of Storm Drainage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-ML-A-100	Material Approval for Manholes of Storm Drainage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-ML-A-110	Material Approval for Main Line Pipes of Storm Drainage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-CB-A-100	Material Approval for Catch Basins of Storm Drainage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-CB-A-110	Material Approval for Catch Basin Pipes of Storm Drainage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Pond		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-DPO-CV-A-110	Material Approval for Materials of Storm Drainage Ponds	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-TF-A-100	Material Approval for Manhole Covers of Storm Drainage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-TF-A-110	Material Approval for Catch Basin Covers of Storm Drainage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Sewage Network		104.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-ML-S-100	Material Submittal for Manholes of Sewage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SW-ML-S-110	Material Submittal for Main Line Pipes of Sewage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-TF-S-100	Material Submittal for Manhole Covers of Sewage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		56.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-ML-A-100	Material Approval for Manholes of Sewage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SW-ML-A-110	Material Approval for Main Line Pipes of Sewage Network	56.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-TF-A-100	Material Approval for Manhole Covers of Sewage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Treated Sewage Effluent (Tse)		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-S-120	Material Submittal for Materials of Treated Sewage Effluent (TSE)	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%

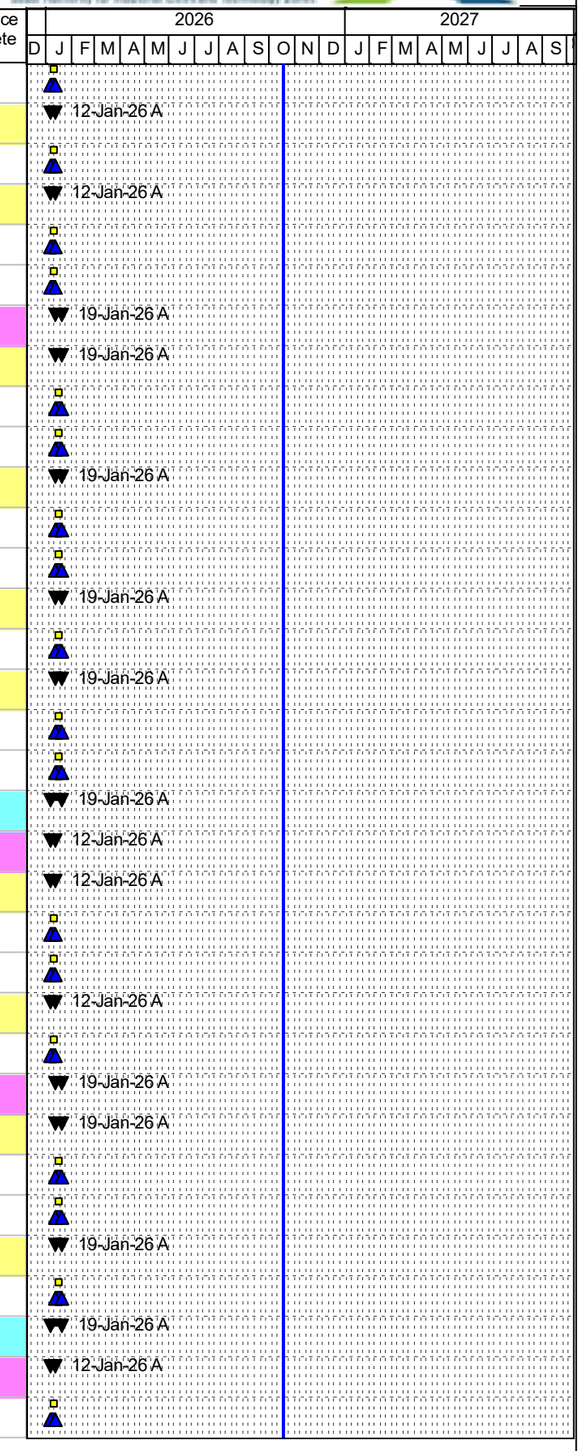


Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-A-120	Material Approval for Materials of Treated Sewage Effluent (TSE)	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Potable Water Network		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-ML-S-100	Material Submittal for Main Line Pipes and Materials of Potable Water Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-PW-ML-S-110	Material Submittal for Main Line Valves of Potable Water Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Fire Hydrant		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-FH-S-100	Material Submittal for Fire Hydrant of Potable Water Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-TF-S-100	Material Submittal for Surface Box of Potable Water Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-ML-A-100	Material Approval for Main Line Pipes and Materials of Potable Water Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-PW-ML-A-110	Material Approval for Valves of Potable Water Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Fire Hydrant		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-FH-A-100	Material Approval for Fire Hydrants of Potable Water Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-TF-A-100	Material Approval for Surface Box of Potable Water Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Irrigation Network		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Pipes		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-S-100	Material Submittal for Main Line Pipes of Irrigation Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-S-110	Material Submittal for Main Line Valves of Irrigation Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Pipes		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-A-100	Material Approval for Main Line Pipes of Irrigation Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-A-110	Material Approval for Valves of Irrigation Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Medium Voltage Network		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-MV-ML-S-100	Material Submittal for Medium Voltage Materials of Medium Voltage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-MV-ML-A-100	Material Approval for Medium Voltage Materials of Medium Voltage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Low Voltage Network		104.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%

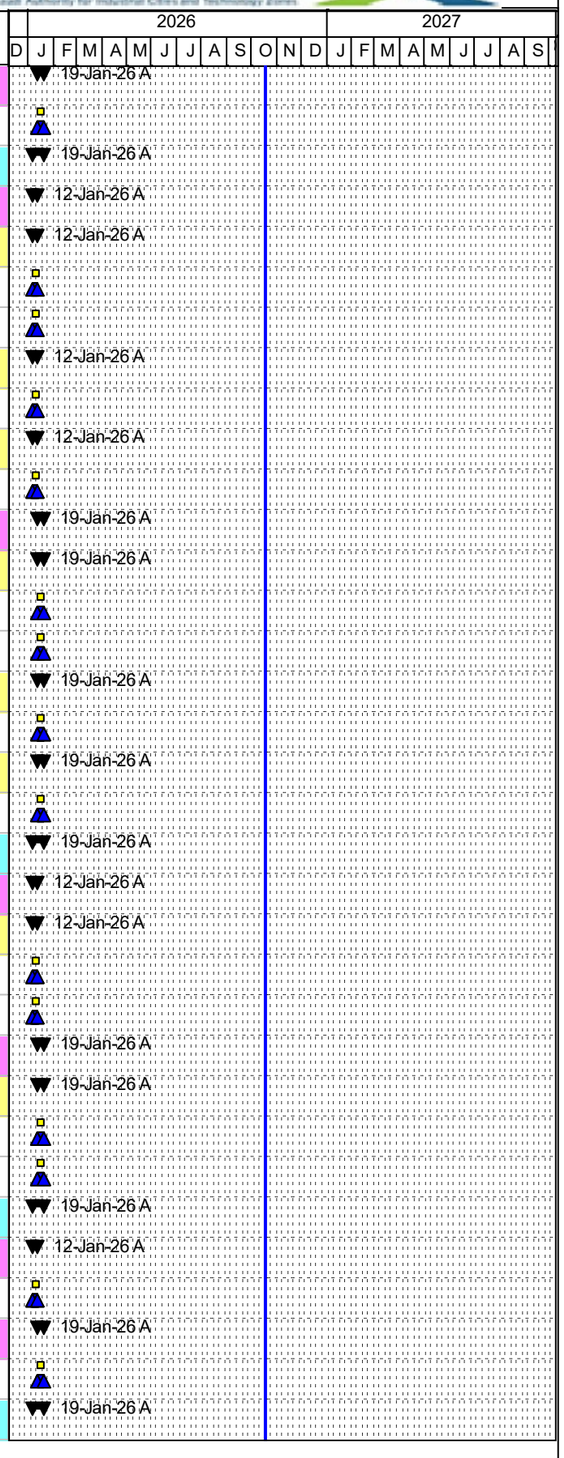

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Low Voltage Cables Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-ML-S-100	Material Submittal for Main Low Voltage Cables of Low Voltage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Service Low Voltage Cables Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-HC-S-100	Material Submittal for Service Low Voltage Cables of Low Voltage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Distribution Pillars Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-DP-S-100	Material Submittal for Distribution Pillars of Low Voltage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
PRO-LV-DP-S-110	Material Submittal for Low Voltage Earthing of Low Voltage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-TT-S-100	Material Submittal for Cable Lugs of Low Voltage Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		56.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Low Voltage Cables Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-ML-A-100	Material Approval for Main Low Voltage Cables of Low Voltage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Service Low Voltage Cables Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-HC-A-100	Material Approval for Service Low Voltage Cables of Low Voltage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Distribution Pillars Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-DP-A-100	Material Approval for Distribution Pillars of Low Voltage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
PRO-LV-DP-A-110	Material Approval for Low Voltage Earthing of Low Voltage Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		56.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-TT-A-100	Material Approval for Cable Lugs of Low Voltage Network	56.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Street Lighting Network		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Cabling Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-ML-S-100	Material Submittal for Lighting Cables of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Lighting Poles Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-S-100	Material Submittal for Lighting Poles Concrete Foundations of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-S-110	Material Submittal for Lighting Poles of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-S-120	Material Submittal for Lighting Fixtures of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Distribution Panel Board		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-DB-S-100	Material Submittal for Lighting Distrubution Panel Boards of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-TF-S-100	Material Submittal for Fuse Boxes of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-TF-S-110	Material Submittal for Cable Lugs of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Earthing System Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%

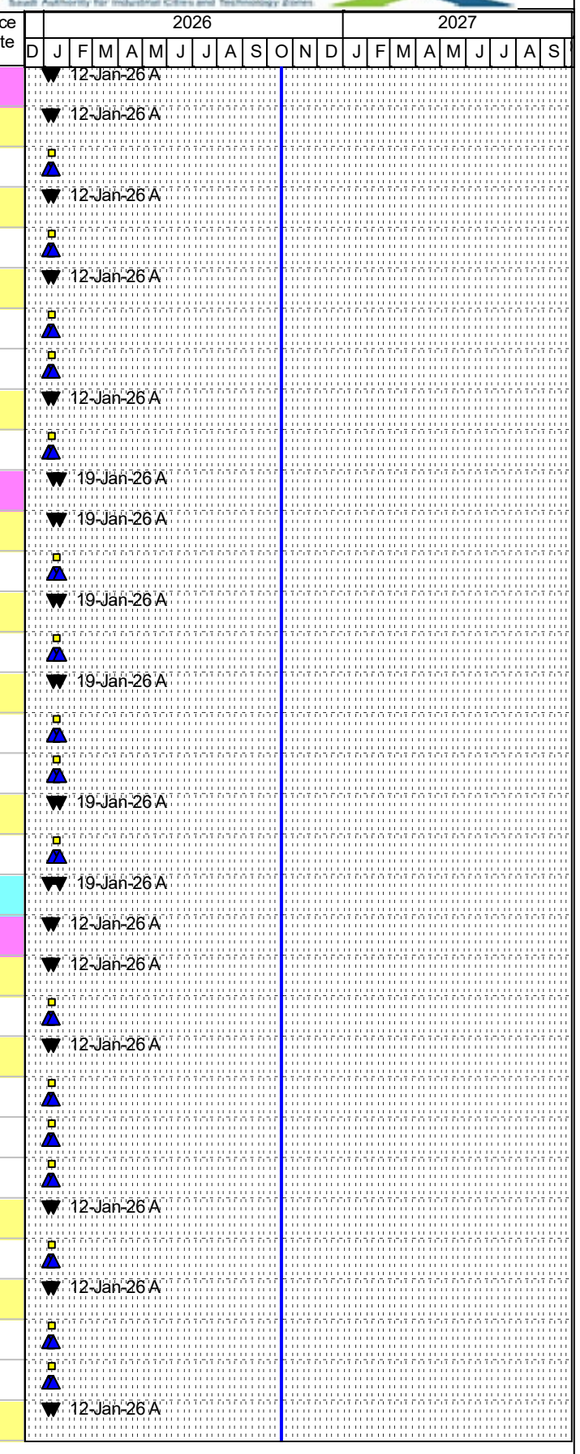

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-MT-SL-ES-S-100	Material Submittal for Lighting Earthing of Street Lighting Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Cabling Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-ML-A-100	Material Approval for Lighting Cables of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Lighting Poles Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-A-100	Material Approval for Lighting Poles Concrete Foundations of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-A-110	Material Approval for Lighting Poles of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-A-120	Material Approval for Lighting Fixtures of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Distribution Panel Board		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-DB-A-100	Material Approval for Distrubution Panel Boards of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-TF-A-100	Material Approval for Fuse Boxes of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-TF-A-110	Material Approval for Cable Lugs of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Earthing System Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-ES-A-100	Material Approval for Lighting Earthing of Street Lighting Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Telecom and Light Current Networks		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Ducts Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-S-100	Material Submittal for Ducts of Telecom Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Manholes Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-S-110	Material Submittal for Manholes of Telecom Network	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
CCTV, Telephone, MSN, ACs System Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-CTV-S-100	Material Submittal for Materials of CCTV, Telephone, MSN, and Access Control	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Ducts Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-A-100	Material Approval for Ducts of Telecom Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Manholes Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-A-110	Material Approval for Manholes of Telecom Network	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
CCTV, Telephone, MSN, ACs System Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-CTV-A-100	Material Approval for for Materials of CCTV, Telephone, MSN, and Access Control	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Road Works		184.00	06-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		136.00	06-Jan-26 A	24-Jan-26 A	0	0	0	0	0%	0%
General Road Works		56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-S-100	Material Submittal for Subgrade of Road Works	56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%

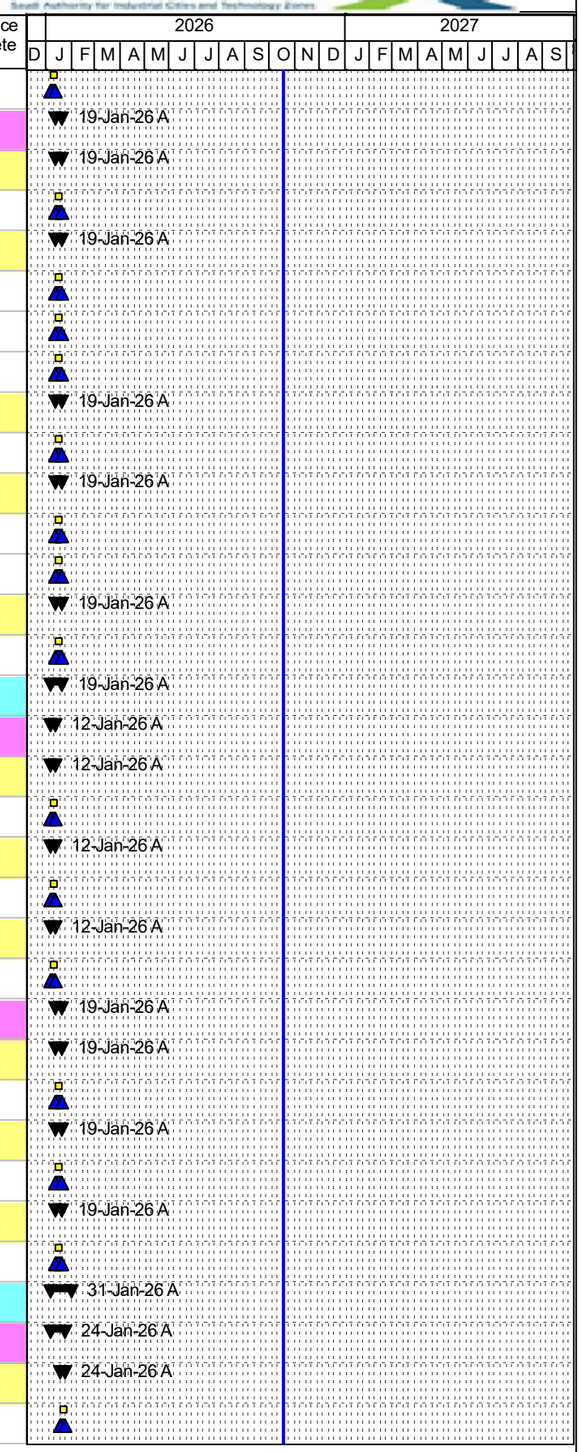

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-MT-RD-S-110	Material Submittal for Aggregate Base Course of Road Works	56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-120	Material Submittal for Prime Coat of Road Works	56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-130	Material Submittal for Asphaltic Base Course Laver of Road Works	56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-160	Material Submittal for Asphaltic Wearing Course Laver for Roads Network	56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-170	Material Submittal for Tack Coat Layer for Roads Network	56.00	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-S-140	Material Submittal for Interlock Tiles of Landscaping	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-150	Material Submittal for Curbstones of Landscaping	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Traffic Signs Boards and Roads Marking		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TS-S-100	Material Submittal for Traffic Signs Boards of Road Works	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-TS-S-110	Material Submittal for Road Markings of Road Works	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		136.00	13-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
General Road Works		56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-A-100	Material Approval for Subgrade of Road Works	48.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-110	Material Approval for Aggregate Base Course of Road Works	48.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-120	Material Approval for Prime Coat of Road Works	48.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-130	Material Approval for Asphaltic Base Course Layer of Road Works	56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-160	Material Approval for Asphaltic Wearing Course Laver for Roads Network	56.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-170	Material Approval for Tack Coat Layer for Roads Network	48.00	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-A-140	Material Approval of Interlock Tiles for Landscaping	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-150	Material Approval of Curbstones for Landscaping	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Traffic Signs Boards and Roads Marking		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TS-A-100	Material Approval for Traffic Signs Boards of Road Works	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-TS-A-110	Material Approval for Road Markings of Road Works	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Softscape and Planting Works		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-S-140	Material Submittal for Softscape and Planting Works	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-S-150	Material Submittal for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-A-140	Material Approval for Softscape and Planting Works	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-A-150	Material Approval for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Superstructure Works		992.00	06-Jan-26 A	13-Jun-26 A	0	0	0	0	0%	0%
Water Pump Station		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%

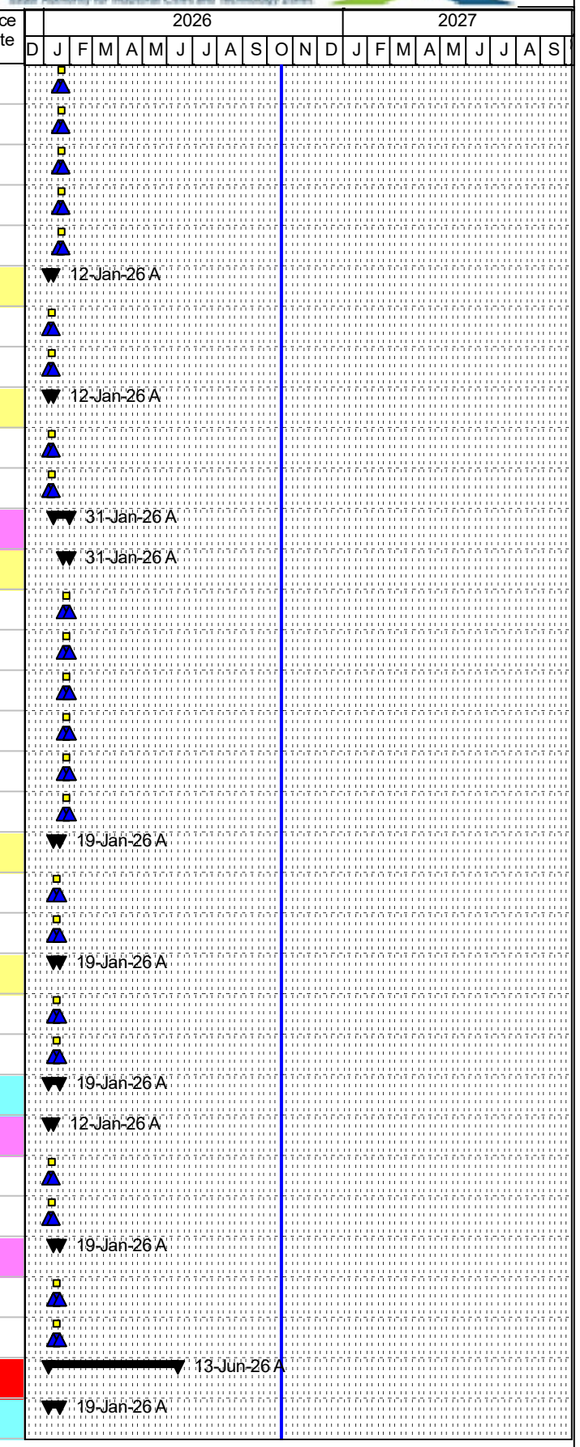


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SLS-CV-S-100	Material Submittal for Works for Water Pump Station	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SLS-CV-A-110	Material Approval for Works for Water Pump Station	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Storage Tank (TSE)		96.00	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-S-130	Material Submittal for Works for Storage Tank (TSE)	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-A-140	Material Approval for Works for Storage Tank (TSE)	48.00	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Control Room		56.00	03-Feb-26 A	10-Feb-26 A	0	0	0	0	0%	0%
Submission of Material		24.00	03-Feb-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-S-140	Material Submittal for Works for Control Room	24.00	03-Feb-26 A	04-Feb-26 A	0	0	0	0	100%	100%
Approval of Material		48.00	04-Feb-26 A	10-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-A-150	Material Approval for Works for Control Room	48.00	04-Feb-26 A	10-Feb-26 A	0	0	0	0	100%	100%
Sewage Pump Stations		288.00	06-Jan-26 A	16-Feb-26 A	0	0	0	0	0%	0%
Submission of Material		56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PS-CV-S-140	Material Submittal for Works of Sewage Pump Station	56.00	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		40.00	11-Feb-26 A	16-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-PS-CV-A-150	Material Approval for Works of Sewage Pump Station	40.00	11-Feb-26 A	16-Feb-26 A	0	0	0	0	100%	100%
Gaurd Room		64.00	18-Feb-26 A	02-Mar-26 A	0	0	0	0	0%	0%
Submission of Material		0.00	18-Feb-26 A	19-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-GR-CV-S-120	Material Submittal for Materials for Gaurd Room	0.00	18-Feb-26 A	19-Feb-26 A	0	0	0	0	100%	100%
Approval of Material		56.00	19-Feb-26 A	02-Mar-26 A	0	0	0	0	0%	0%
ENG-MT-GR-CV-A-130	Material Approval for Materials for Gaurd Room	56.00	19-Feb-26 A	02-Mar-26 A	0	0	0	0	100%	100%
Boundary Fence		656.00	25-Feb-26 A	13-Jun-26 A	0	0	0	0	0%	0%
Submission of Material		0.00	25-Feb-26 A	26-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-FE-CV-S-110	Material Submittal for Materials for Boundary Fence	0.00	25-Feb-26 A	26-Feb-26 A	0	0	0	0	100%	100%
Approval of Material		640.00	28-Feb-26 A	13-Jun-26 A	0	0	0	0	0%	0%
ENG-MT-FE-CV-A-120	Material Approval for Materials for Boundary Fence	640.00	28-Feb-26 A	13-Jun-26 A	0	0	0	0	100%	100%
Long Lead Time Items		192.00	19-Oct-26	15-Nov-26	0	0	0	0	0%	0%
Superstructure Works		192.00	19-Oct-26	15-Nov-26	0	0	0	0	0%	0%
Sewage Pump Stations		96.00	19-Oct-26	01-Nov-26	0	0	0	0	0%	0%
Submission of Material		48.00	19-Oct-26	25-Oct-26	0	0	0	0	0%	0%
ENG-MT-SPS-MC-S-100	Material Submittal for Electromechanical Works for Pump Station	48.00	19-Oct-26	25-Oct-26	0	0	0	0	100%	0%

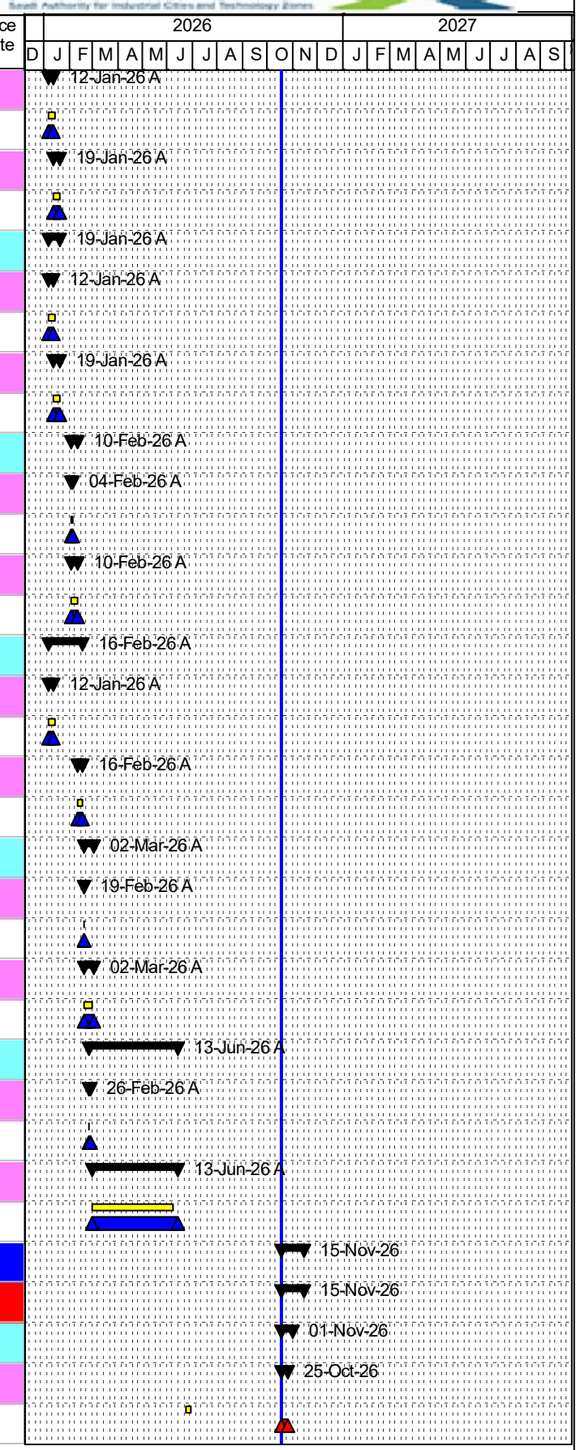

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Approval of Material		48.00	26-Oct-26	01-Nov-26	0	0	0	0	0%	0%
ENG-MT-SPS-MC-A-110	Material Approval for Electromechanical Works for Pump Station	48.00	26-Oct-26	01-Nov-26	0	0	0	0	100%	0%
Storage Tank (TSE)		192.00	19-Oct-26	15-Nov-26	0	0	0	0	0%	0%
Submission of Material		96.00	19-Oct-26	01-Nov-26	0	0	0	0	0%	0%
ENG-MT-TSE-MC-S-110	Material Submittal for Electromechanical Works for Storage Tank (TSE)	96.00	19-Oct-26	01-Nov-26	0	0	0	0	100%	0%
Approval of Material		96.00	02-Nov-26	15-Nov-26	0	0	0	0	0%	0%
ENG-MT-TSE-MC-A-120	Material Approval for Electromechanical Works for Storage Tank (TSE)	96.00	02-Nov-26	15-Nov-26	0	0	0	0	100%	0%
Procurement Cycle		2696.00	02-May-26 A	13-Jun-27	0	0	0	0	0%	0%
Short Lead Time Items		2400.00	02-May-26 A	25-Apr-27	0	0	0	0	0%	0%
Infrastructure Networks		2400.00	02-May-26 A	25-Apr-27	0	0	0	0	0%	0%
Storm Drainage Network		1032.00	01-Jul-26 A	27-Feb-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		376.00	01-Jul-26 A	23-Nov-26	0	0	0	0	0%	0%
Main Line Sections		144.00	01-Jul-26 A	20-Oct-26	0	0	0	0	0%	0%
PRO-SD-PO-100	Issuance of Purchase Order for Manholes of Storm Drainage Network	16.00	19-Oct-26	20-Oct-26	0	0	0	0	100%	0%
PRO-SD-PO-110	Issuance of Purchase Order for Main Line Pipes of Storm Drainage Network	16.00	01-Jul-26 A	02-Jul-26 A	0	0	0	0	100%	100%
Catch Basin Sections		88.00	21-Oct-26	02-Nov-26	0	0	0	0	0%	0%
PRO-SD-PO-130	Issuance of Purchase Order for Catch Basins of Storm Drainage Network	40.00	21-Oct-26	26-Oct-26	0	0	0	0	100%	0%
PRO-SD-PO-150	Issuance of Purchase Order for Catch Basin Pipes of Storm Drainage Network	48.00	27-Oct-26	02-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		96.00	03-Nov-26	16-Nov-26	0	0	0	0	0%	0%
PRO-SD-PO-120	Issuance of Purchase Order for Manhole Covers of Storm Drainage Network	48.00	03-Nov-26	09-Nov-26	0	0	0	0	100%	0%
PRO-SD-PO-140	Issuance of Purchase Order for Catch Basin Covers of Storm Drainage Network	48.00	10-Nov-26	16-Nov-26	0	0	0	0	100%	0%
Storm Drainage Ponds		48.00	17-Nov-26	23-Nov-26	0	0	0	0	0%	0%
PRO-DPO-CV-PO-10	Issuance of Purchase Order for Materials of Storm Drainage Ponds	48.00	17-Nov-26	23-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		872.00	05-Jul-26 A	06-Feb-27	0	0	0	0	0%	0%
Main Line Sections		192.00	05-Jul-26 A	29-Oct-26	0	0	0	0	0%	0%
PRO-SD-MF-100	Manufacturing of Materials for Manholes of Storm Drainage Network	64.00	21-Oct-26	29-Oct-26	0	0	0	0	100%	0%
PRO-SD-MF-110	Manufacturing of Materials for Main Line Pipes of Storm Drainage Network	192.00	05-Jul-26 A	07-Jul-26 A	0	0	0	0	100%	100%
Catch Basin Sections		248.00	27-Oct-26	01-Dec-26	0	0	0	0	0%	0%
PRO-SD-MF-130	Manufacturing of Materials for Catch Basins of Storm Drainage Network	200.00	27-Oct-26	24-Nov-26	0	0	0	0	100%	0%
PRO-SD-MF-150	Manufacturing of Materials for Catch Basin Pipes of Storm Drainage Network	200.00	03-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		400.00	02-Dec-26	28-Jan-27	0	0	0	0	0%	0%
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	160.00	02-Dec-26	24-Dec-26	0	0	0	0	100%	0%
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	240.00	26-Dec-26	28-Jan-27	0	0	0	0	100%	0%
Storm Drainage Ponds		512.00	24-Nov-26	06-Feb-27	0	0	0	0	0%	0%

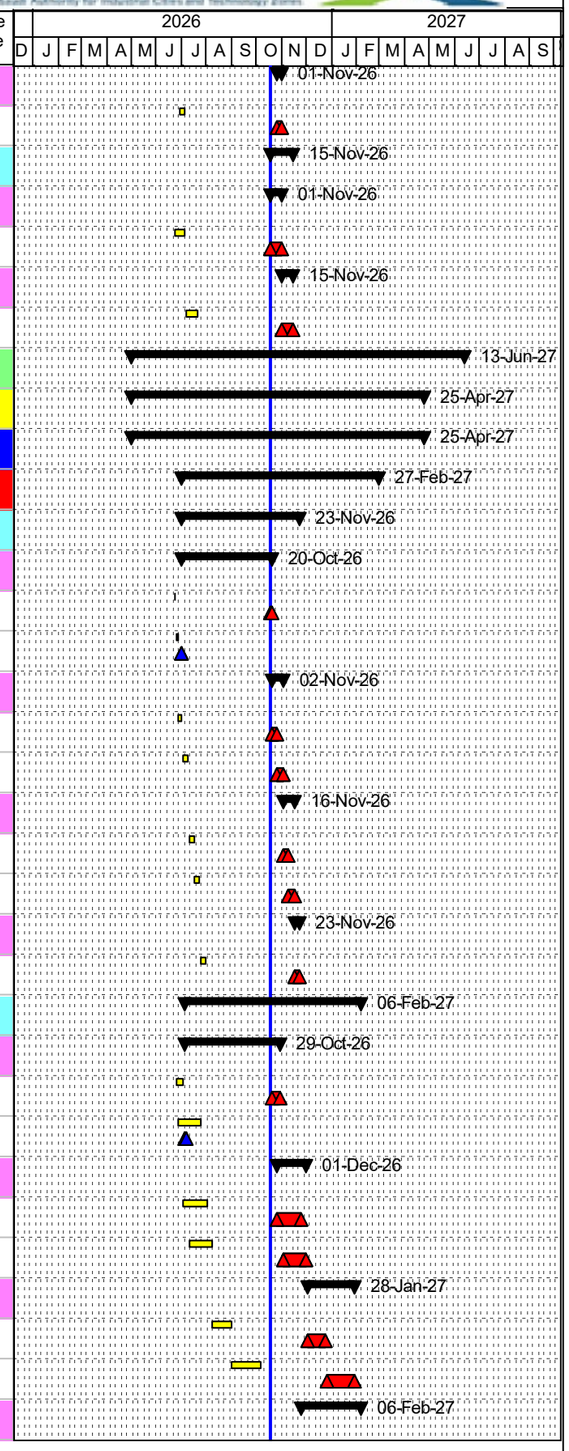


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-DPO-CV-MF-10	Manufacturing of Materials of Storm Drainage Ponds	512.00	24-Nov-26	06-Feb-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		712.00	08-Jul-26 A	10-Feb-27	0	0	0	0	0%	0%
Main Line Sections		32.00	08-Jul-26 A	03-Nov-26	0	0	0	0	0%	0%
PRO-SD-1DL-100	1ST Material Delivery for Manholes of Storm Drainage Network	32.00	31-Oct-26	03-Nov-26	0	0	0	0	100%	0%
PRO-SD-1DL-110	1ST Material Delivery for Main Line Pipes of Storm Drainage Network	32.00	08-Jul-26 A	12-Jul-26 A	0	0	0	0	100%	100%
Catch Basin Sections		80.00	25-Nov-26	06-Dec-26	0	0	0	0	0%	0%
PRO-SD-1DL-120	1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network	32.00	02-Dec-26	06-Dec-26	0	0	0	0	100%	0%
PRO-SD-1DL-130	1ST Material Delivery for Catch Basins of Storm Drainage Network	32.00	25-Nov-26	29-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		272.00	26-Dec-26	02-Feb-27	0	0	0	0	0%	0%
PRO-SD-1DL-140	1ST Material Delivery for Manholes Covers of Storm Drainage Network	32.00	26-Dec-26	29-Dec-26	0	0	0	0	100%	0%
PRO-SD-1DL-150	1ST Material Delivery for Catch Basin Covers of Storm Drainage Network	32.00	30-Jan-27	02-Feb-27	0	0	0	0	100%	0%
Storm Drainage Ponds		32.00	07-Feb-27	10-Feb-27	0	0	0	0	0%	0%
PRO-DPO-CV-1DL-10	1ST Material Delivery for Materials of Drainage Ponds	32.00	07-Feb-27	10-Feb-27	0	0	0	0	75%	0%
Material Delivery & Site Inspection		792.00	20-Jul-26 A	27-Feb-27	0	0	0	0	0%	0%
Main Line Sections		120.00	20-Jul-26 A	02-Dec-26	0	0	0	0	0%	0%
PRO-R25-SD-DL-100	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	80.00	04-Nov-26	15-Nov-26	0	0	0	0	100%	0%
PRO-R25-SD-DL-120	Material Delivery & Site Inspection of Main Line Pipes of Storm Drainage Network	120.00	20-Jul-26 A	02-Dec-26	0	0	0	0	100%	95%
Catch Basin Sections		120.00	30-Nov-26	16-Dec-26	0	0	0	0	0%	0%
PRO-R25-SD-DL-110	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	56.00	09-Dec-26	16-Dec-26	0	0	0	0	100%	0%
PRO-R25-SD-DL-130	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	64.00	30-Nov-26	08-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		352.00	30-Dec-26	18-Feb-27	0	0	0	0	0%	0%
PRO-R25-SD-DL-140	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	160.00	30-Dec-26	21-Jan-27	0	0	0	0	100%	0%
PRO-R25-SD-DL-150	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	112.00	03-Feb-27	18-Feb-27	0	0	0	0	42.86%	0%
Storm Drainage Ponds		112.00	11-Feb-27	27-Feb-27	0	0	0	0	0%	0%
PRO-DPO-CV-DL-10	Material Delivery & Site Inspection for Materials of Storm Drainage Ponds	112.00	11-Feb-27	27-Feb-27	0	0	0	0	0%	0%
Sewage Network		328.00	19-Oct-26	05-Dec-26	0	0	0	0	0%	0%
Issuance of Purchase Orders		168.00	19-Oct-26	11-Nov-26	0	0	0	0	0%	0%
Main Line Sections		112.00	19-Oct-26	03-Nov-26	0	0	0	0	0%	0%
PRO-SW-PO-100	Issuance of Purchase Order for Main Line Pipes of Sewage Network	56.00	19-Oct-26	26-Oct-26	0	0	0	0	100%	0%
PRO-SW-PO-110	Issuance of Purchase Order for Manhole of Sewage Network	56.00	27-Oct-26	03-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		56.00	04-Nov-26	11-Nov-26	0	0	0	0	0%	0%
PRO-SW-PO-120	Issuance of Purchase Order for Manhole Covers of Sewage Network	56.00	04-Nov-26	11-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		160.00	27-Oct-26	18-Nov-26	0	0	0	0	0%	0%
Main Line Sections		136.00	27-Oct-26	15-Nov-26	0	0	0	0	0%	0%

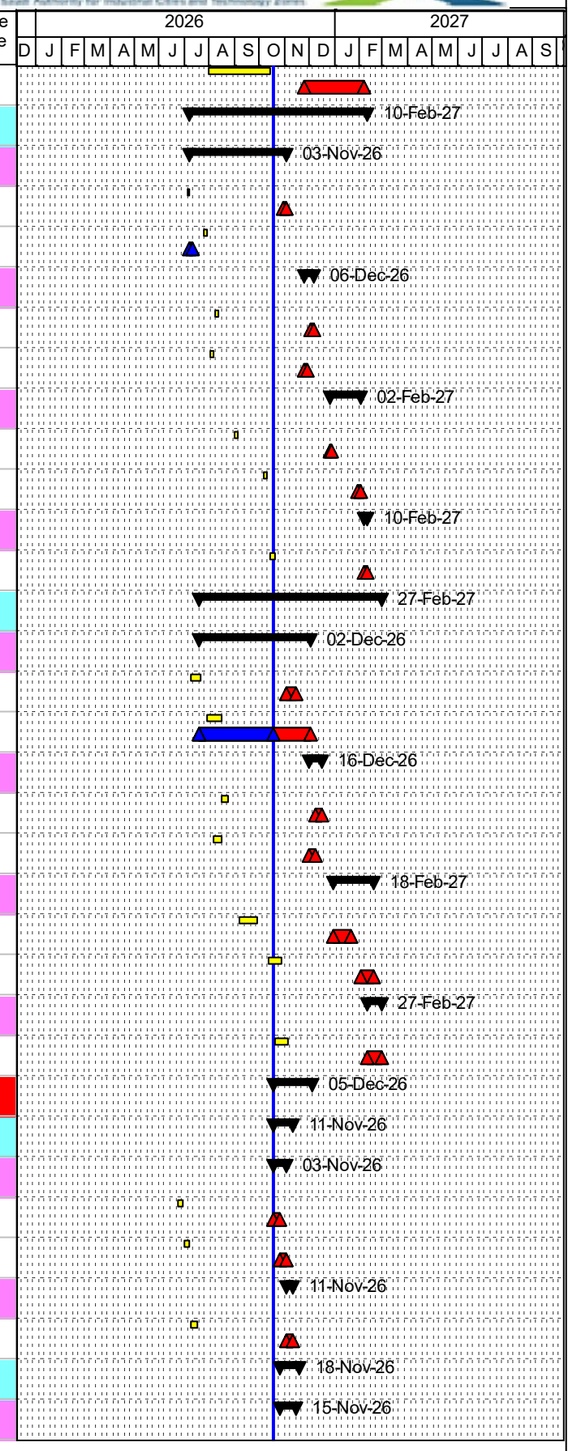

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-SW-MF-100	Manufacturing of Main Line Pipes for Sewage Network	80.00	27-Oct-26	07-Nov-26	0	0	0	0	100%	0%
PRO-SW-MF-110	Manufacturing of Manholes for Sewage Network	80.00	04-Nov-26	15-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		48.00	12-Nov-26	18-Nov-26	0	0	0	0	0%	0%
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	48.00	12-Nov-26	18-Nov-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		128.00	08-Nov-26	25-Nov-26	0	0	0	0	0%	0%
Main Line Sections		112.00	08-Nov-26	23-Nov-26	0	0	0	0	0%	0%
PRO-SW-1DL-100	1ST Material Delivery for Main Line Pipes of Sewage Network	32.00	08-Nov-26	11-Nov-26	0	0	0	0	100%	0%
PRO-SW-1DL-110	1ST Material Delivery for Manholes of Sewage Network	32.00	19-Nov-26	23-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		16.00	24-Nov-26	25-Nov-26	0	0	0	0	0%	0%
PRO-SW-1DL-120	1ST Material Delivery for Manholes Covers of Sewage Network	16.00	24-Nov-26	25-Nov-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		80.00	24-Nov-26	05-Dec-26	0	0	0	0	0%	0%
Main Line Sections		80.00	24-Nov-26	05-Dec-26	0	0	0	0	0%	0%
PRO-R25-SW-DL-100	Material Delivery & Site Inspection of Main Line Pipes for Sewage Network	32.00	01-Dec-26	05-Dec-26	0	0	0	0	100%	0%
PRO-R25-SW-DL-110	Material Delivery & Site Inspection of Manholes for Sewage Network	32.00	24-Nov-26	28-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		32.00	26-Nov-26	30-Nov-26	0	0	0	0	0%	0%
PRO-R25-SW-DL-120	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	32.00	26-Nov-26	30-Nov-26	0	0	0	0	100%	0%
Treated Sewage Effluent (Tse)		416.00	19-Oct-26	17-Dec-26	0	0	0	0	0%	0%
Issuance of Purchase Orders		56.00	19-Oct-26	26-Oct-26	0	0	0	0	0%	0%
PRO-TSE-PO-120	Issuance of Purchase Order for Materials of Treated Sewage Effluent (Tse)	56.00	19-Oct-26	26-Oct-26	0	0	0	0	100%	0%
Manufacturing of Material		192.00	27-Oct-26	23-Nov-26	0	0	0	0	0%	0%
PRO-TSE-MF-120	Manufacturing of Materials for Treated Sewage Effluent (Tse)	192.00	27-Oct-26	23-Nov-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		56.00	24-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-TSE-1DL-120	1ST Material Delivery for Materials of Treated Sewage Effluent (Tse)	56.00	24-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		112.00	02-Dec-26	17-Dec-26	0	0	0	0	0%	0%
PRO-R25-TSE-DL-120	Material Delivery & Site Inspection of Materials for Treated Sewage Effluent (Tse)	112.00	02-Dec-26	17-Dec-26	0	0	0	0	100%	0%
Potable Water Network		2200.00	02-May-26 A	27-Mar-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		1216.00	02-May-26 A	31-Oct-26	0	0	0	0	0%	0%
Main Line Sections		88.00	02-May-26 A	12-May-26 A	0	0	0	0	0%	0%
PRO-PW-PO-100	Issuance of Purchase Order for Main Line Pipes and Materials of Potable Water Network	88.00	02-May-26 A	12-May-26 A	0	0	0	0	100%	100%
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	88.00	02-May-26 A	12-May-26 A	0	0	0	0	100%	100%
Fire Hydrant		40.00	19-Oct-26	24-Oct-26	0	0	0	0	0%	0%
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	40.00	19-Oct-26	24-Oct-26	0	0	0	0	100%	0%
Testing and Finishes		48.00	25-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	48.00	25-Oct-26	31-Oct-26	0	0	0	0	100%	0%

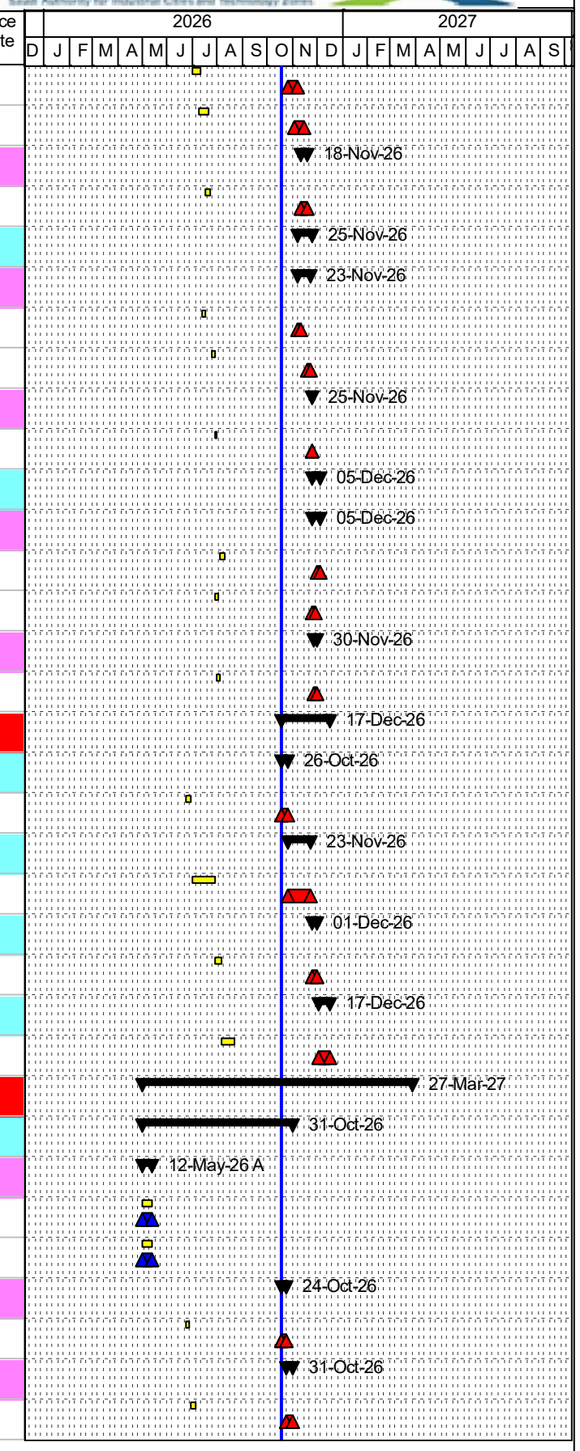


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Manufacturing of Material		632.00	05-Jul-26 A	28-Dec-26	0	0	0	0	0%	0%
Main Line Sections		336.00	05-Jul-26 A	15-Nov-26	0	0	0	0	0%	0%
PRO-PW-MF-100	Manufacturing of Main Line Pipes and Materials for Potable Water Network	272.00	05-Jul-26 A	07-Jul-26 A	0	0	0	0	100%	100%
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	192.00	19-Oct-26	15-Nov-26	0	0	0	0	100%	0%
Fire Hydrant		120.00	16-Nov-26	02-Dec-26	0	0	0	0	0%	0%
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	120.00	16-Nov-26	02-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		400.00	01-Nov-26	28-Dec-26	0	0	0	0	0%	0%
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	400.00	01-Nov-26	28-Dec-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		200.00	12-Jul-26 A	05-Jan-27	0	0	0	0	0%	0%
Main Line Sections		200.00	12-Jul-26 A	05-Jan-27	0	0	0	0	0%	0%
PRO-PW-1DL-100	1ST Material Delivery for Main Line Pipes and Materials of Potable Water Network	56.00	12-Jul-26 A	16-Jul-26 A	0	0	0	0	100%	100%
PRO-PW-1DL-110	1ST Material Delivery for Valves of Potable Water Network	56.00	29-Dec-26	05-Jan-27	0	0	0	0	100%	0%
Fire Hydrant		56.00	29-Dec-26	05-Jan-27	0	0	0	0	0%	0%
PRO-PW-1DL-120	1ST Material Delivery for Fire Hydrants of Potable Water Network	56.00	29-Dec-26	05-Jan-27	0	0	0	0	100%	0%
Testing and Finishes		56.00	29-Dec-26	05-Jan-27	0	0	0	0	0%	0%
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	56.00	29-Dec-26	05-Jan-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		672.00	10-Oct-26 A	27-Mar-27	0	0	0	0	0%	0%
Main Line Sections		312.00	10-Oct-26 A	30-Jan-27	0	0	0	0	0%	0%
PRO-R25-PW-DL-100	Material Delivery & Site Inspection of Main Line Pipes and Materials for Potable Water	168.00	10-Oct-26 A	09-Jan-27 A	0	0	0	0	100%	100%
PRO-R25-PW-DL-110	Material Delivery & Site Inspection of Valves for Potable Water Network	168.00	06-Jan-27	30-Jan-27	0	0	0	0	52.38%	0%
Fire Hydrant		48.00	06-Jan-27	12-Jan-27	0	0	0	0	0%	0%
PRO-R25-PW-DL-120	Material Delivery & Site Inspection of Fire Hydrants for Potable Water Network	48.00	06-Jan-27	12-Jan-27	0	0	0	0	100%	0%
Testing and Finishes		528.00	06-Jan-27	27-Mar-27	0	0	0	0	0%	0%
PRO-R25-PW-DL-130	Material Delivery & Site Inspection for Finishes of Potable Water Network	528.00	06-Jan-27	27-Mar-27	0	0	0	0	48.48%	0%
Irrigation Network		600.00	01-Nov-26	26-Jan-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		72.00	01-Nov-26	10-Nov-26	0	0	0	0	0%	0%
Main Line Pipes		72.00	01-Nov-26	10-Nov-26	0	0	0	0	0%	0%
PRO-IR-PO-100	Issuance of Purchase Order for Main Line Pipes of Irrigation Network	40.00	01-Nov-26	05-Nov-26	0	0	0	0	100%	0%
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	32.00	07-Nov-26	10-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		336.00	07-Nov-26	24-Dec-26	0	0	0	0	0%	0%
Main Line Pipes		336.00	07-Nov-26	24-Dec-26	0	0	0	0	0%	0%
PRO-IR-MF-100	Manufacturing of Main Line Pipes for Irrigation Network	168.00	07-Nov-26	30-Nov-26	0	0	0	0	100%	0%
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	168.00	01-Dec-26	24-Dec-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		224.00	01-Dec-26	02-Jan-27	0	0	0	0	0%	0%

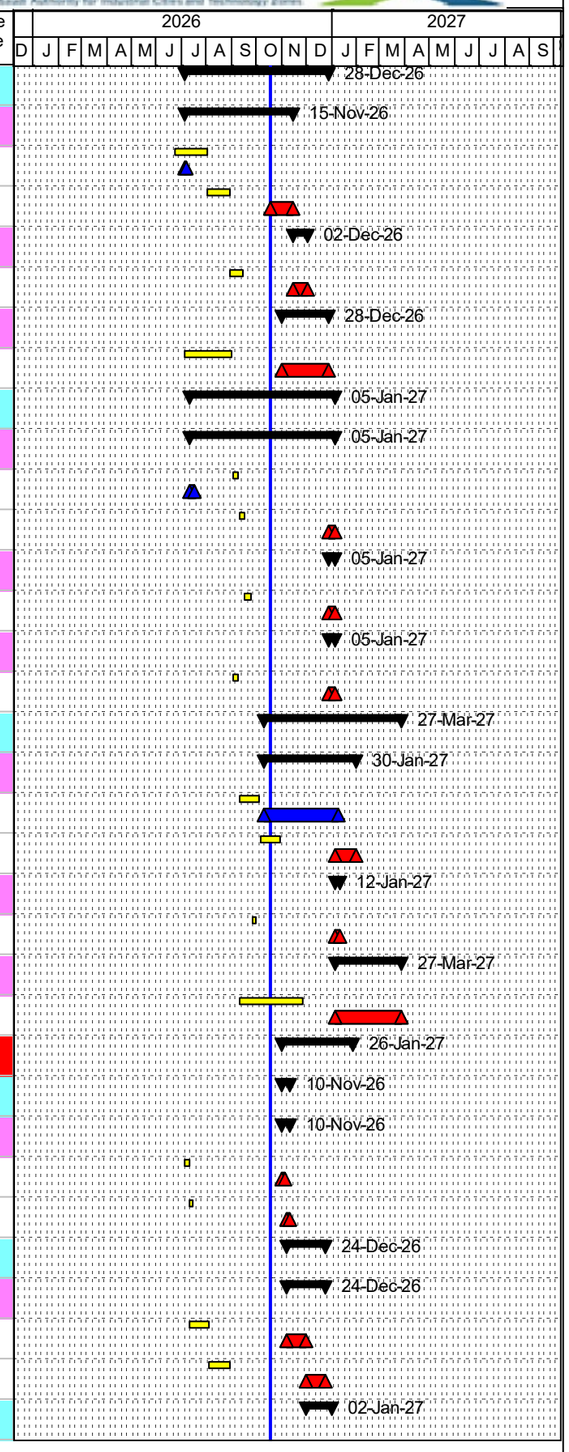


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Main Line Pipes		224.00	01-Dec-26	02-Jan-27	0	0	0	0	0%	0%
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	56.00	01-Dec-26	08-Dec-26	0	0	0	0	100%	0%
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	56.00	26-Dec-26	02-Jan-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		336.00	09-Dec-26	26-Jan-27	0	0	0	0	0%	0%
Main Line Pipes		336.00	09-Dec-26	26-Jan-27	0	0	0	0	0%	0%
PRO-R25-IR-DL-100	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	168.00	09-Dec-26	02-Jan-27	0	0	0	0	100%	0%
PRO-R25-IR-DL-110	Material Delivery & Site Inspection of Valves for Irrigation Network	168.00	03-Jan-27	26-Jan-27	0	0	0	0	100%	0%
Medium Voltage Network		528.00	11-Nov-26	26-Jan-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		48.00	11-Nov-26	17-Nov-26	0	0	0	0	0%	0%
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Materials of Medium Voltage Network	48.00	11-Nov-26	17-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		168.00	18-Nov-26	12-Dec-26	0	0	0	0	0%	0%
PRO-MV-MF-100	Manufacturing of Medium Voltage Materials for Medium Voltage Network	168.00	18-Nov-26	12-Dec-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		56.00	13-Dec-26	20-Dec-26	0	0	0	0	0%	0%
PRO-MV-1DL-100	1ST Material Delivery for Medium Voltage Materials of Medium Voltage Network	56.00	13-Dec-26	20-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		168.00	03-Jan-27	26-Jan-27	0	0	0	0	0%	0%
PRO-MV-DL-100	Material Delivery & Site Inspection of Medium Voltage Materials for Medium Voltage Network	168.00	03-Jan-27	26-Jan-27	0	0	0	0	100%	0%
Low Voltage Network		1088.00	19-Oct-26	29-Mar-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		224.00	19-Oct-26	19-Nov-26	0	0	0	0	0%	0%
Main Low Voltage Cables Works		56.00	19-Oct-26	26-Oct-26	0	0	0	0	0%	0%
PRO-LV-ML-PO-100	Issuance of Purchase Order for Main Low Voltage Cables of Low Voltage Network	56.00	19-Oct-26	26-Oct-26	0	0	0	0	100%	0%
Service Low Voltage Cables Works		56.00	19-Oct-26	26-Oct-26	0	0	0	0	0%	0%
PRO-LV-HC-PO-100	Issuance of Purchase Order for Service Low Voltage Cables of Low Voltage Network	56.00	19-Oct-26	26-Oct-26	0	0	0	0	100%	0%
Distribution Pillar Works		112.00	27-Oct-26	11-Nov-26	0	0	0	0	0%	0%
PRO-LV-DP-PO-100	Issuance of Purchase Order for Distribution Pillars of Low Voltage Network	56.00	27-Oct-26	03-Nov-26	0	0	0	0	100%	0%
PRO-LV-DP-PO-110	Issuance of Purchase Order for Low Voltage Earthing of Low Voltage Network	56.00	04-Nov-26	11-Nov-26	0	0	0	0	100%	0%
Termination and Testing Works		56.00	12-Nov-26	19-Nov-26	0	0	0	0	0%	0%
PRO-LV-TT-PO-100	Issuance of Purchase Order for Cable Lugs of Low Voltage Network	56.00	12-Nov-26	19-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		728.00	27-Oct-26	09-Feb-27	0	0	0	0	0%	0%
Main Low Voltage Cables Works		240.00	27-Oct-26	30-Nov-26	0	0	0	0	0%	0%
PRO-LV-ML-MF-100	Manufacturing of Main Low Voltage Cables for Low Voltage Network	240.00	27-Oct-26	30-Nov-26	0	0	0	0	100%	0%
Service Low Voltage Cables Works		240.00	27-Oct-26	30-Nov-26	0	0	0	0	0%	0%
PRO-LV-HC-MF-100	Manufacturing of Service Low Voltage Cables for Low Voltage Network	240.00	27-Oct-26	30-Nov-26	0	0	0	0	100%	0%
Distribution Pillar Works		376.00	04-Nov-26	28-Dec-26	0	0	0	0	0%	0%
PRO-LV-DP-MF-100	Manufacturing of Distribution Pillars for Low Voltage Network	320.00	04-Nov-26	20-Dec-26	0	0	0	0	100%	0%

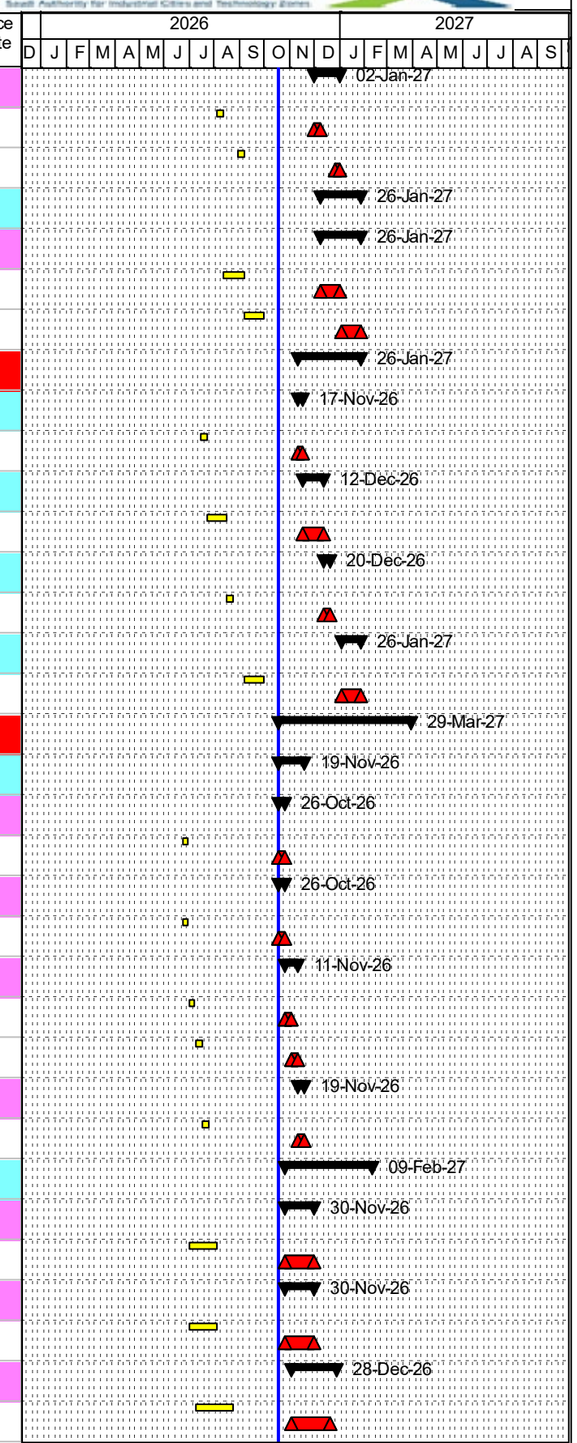

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-LV-DP-MF-110	Manufacturing of Low Voltage Earthing for Low Voltage Network	320.00	12-Nov-26	28-Dec-26	0	0	0	0	100%	0%
Termination and Testing Works		560.00	21-Nov-26	09-Feb-27	0	0	0	0	0%	0%
PRO-LV-TT-MF-100	Manufacturing of Cable Lugs for Low Voltage Network	560.00	21-Nov-26	09-Feb-27	0	0	0	0	100%	0%
1st Delivery of Material to Site		496.00	01-Dec-26	10-Feb-27	0	0	0	0	0%	0%
Main Low Voltage Cables Works		272.00	01-Dec-26	09-Jan-27	0	0	0	0	0%	0%
PRO-LV-ML-1DL-100	1ST Material Delivery for Main Low Voltage Cables of Low Voltage Network	272.00	01-Dec-26	09-Jan-27	0	0	0	0	100%	0%
Service Low Voltage Cables Works		56.00	10-Jan-27	17-Jan-27	0	0	0	0	0%	0%
PRO-LV-HC-1DL-100	1ST Material Delivery for Service Low Voltage Cables of Low Voltage Network	56.00	10-Jan-27	17-Jan-27	0	0	0	0	100%	0%
Distribution Pillar Works		112.00	18-Jan-27	02-Feb-27	0	0	0	0	0%	0%
PRO-LV-DP-1DL-100	1ST Material Delivery for Distribution Pillars of Low Voltage Network	56.00	18-Jan-27	25-Jan-27	0	0	0	0	100%	0%
PRO-LV-DP-1DL-110	1ST Material Delivery for Low Voltage Earthing of Low Voltage Network	56.00	26-Jan-27	02-Feb-27	0	0	0	0	100%	0%
Termination and Testing Works		56.00	03-Feb-27	10-Feb-27	0	0	0	0	0%	0%
PRO-LV-TT-1DL-100	1ST Material Delivery for Cable Lugs of Low Voltage Network	56.00	03-Feb-27	10-Feb-27	0	0	0	0	100%	0%
Delivery of Material to Site		520.00	10-Jan-27	29-Mar-27	0	0	0	0	0%	0%
Main Low Voltage Cables Works		56.00	10-Jan-27	17-Jan-27	0	0	0	0	0%	0%
PRO-LV-ML-DL-100	Material Delivery of Main Low Voltage Cables for Low Voltage Network	56.00	10-Jan-27	17-Jan-27	0	0	0	0	100%	0%
Service Low Voltage Cables Works		168.00	18-Jan-27	10-Feb-27	0	0	0	0	0%	0%
PRO-LV-HC-DL-100	Material Delivery of Service Low Voltage Cables for Low Voltage Network	168.00	18-Jan-27	10-Feb-27	0	0	0	0	100%	0%
Distribution Pillar Works		160.00	10-Feb-27	04-Mar-27	0	0	0	0	0%	0%
PRO-LV-DP-DL-100	Material Delivery of Distribution Pillars for Low Voltage Network	152.00	11-Feb-27	04-Mar-27	0	0	0	0	5.26%	0%
PRO-LV-DP-DL-120	Material Delivery of Low Voltage Earthing for Low Voltage Network	160.00	10-Feb-27	04-Mar-27	0	0	0	0	10%	0%
Termination and Testing Works		144.00	06-Mar-27	29-Mar-27	0	0	0	0	0%	0%
PRO-LV-TT-DL-100	Material Delivery of Cable Lugs for Low Voltage Network	144.00	06-Mar-27	29-Mar-27	0	0	0	0	0%	0%
Street Lighting Network		1040.00	12-Nov-26	15-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		136.00	12-Nov-26	01-Dec-26	0	0	0	0	0%	0%
Cabling Works		40.00	12-Nov-26	17-Nov-26	0	0	0	0	0%	0%
PRO-SL-PO-100	Issuance of Purchase Order for Lighting Cables of Street Lighting Network	40.00	12-Nov-26	17-Nov-26	0	0	0	0	100%	0%
Lighting Poles Works		40.00	12-Nov-26	17-Nov-26	0	0	0	0	0%	0%
PRO-SL-PO-110	Issuance of Purchase Order for Lighting Poles Foundations of Street Lighting Network	40.00	12-Nov-26	17-Nov-26	0	0	0	0	100%	0%
PRO-SL-PO-120	Issuance of Purchase Order for Lighting Poles of Street Lighting Network	40.00	12-Nov-26	17-Nov-26	0	0	0	0	100%	0%
PRO-SL-PO-140	Issuance of Purchase Order for Lighting Fixtures of Street Lighting Network	40.00	12-Nov-26	17-Nov-26	0	0	0	0	100%	0%
Distribution Panel Board		48.00	12-Nov-26	18-Nov-26	0	0	0	0	0%	0%
PRO-SL-PO-160	Issuance of Purchase Order for Distrubution Panel Boards of Street Lighting Network	48.00	12-Nov-26	18-Nov-26	0	0	0	0	100%	0%
Termination and Testing Works		56.00	18-Nov-26	25-Nov-26	0	0	0	0	0%	0%

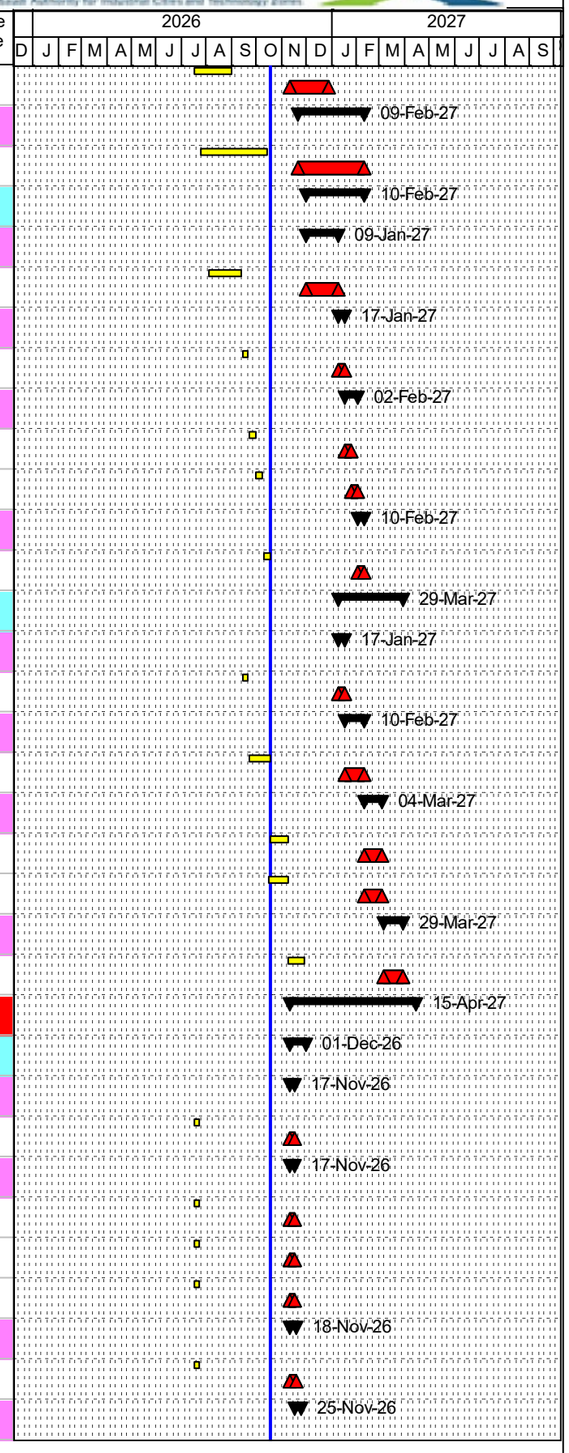


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-SL-PO-130	Issuance of Purchase Order for Fuse Boxes of Street Lighting Network	48.00	19-Nov-26	25-Nov-26	0	0	0	0	100%	0%
PRO-SL-PO-170	Issuance of Purchase Order for Cable Lugs of Street Lighting Network	48.00	18-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Earthing System Works		48.00	25-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-SL-PO-150	Issuance of Purchase Order for Lighting Earthing of Street Lighting Network	48.00	25-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		784.00	18-Nov-26	15-Mar-27	0	0	0	0	0%	0%
Cabling Works		160.00	18-Nov-26	10-Dec-26	0	0	0	0	0%	0%
PRO-SL-MF-100	Manufacturing of Lighting Cables for Street Lighting Network	160.00	18-Nov-26	10-Dec-26	0	0	0	0	100%	0%
Lighting Poles Works		168.00	12-Dec-26	04-Jan-27	0	0	0	0	0%	0%
PRO-SL-MF-110	Manufacturing of Lighting Poles Foundations for Street Lighting Network	168.00	12-Dec-26	04-Jan-27	0	0	0	0	100%	0%
PRO-SL-MF-120	Manufacturing of Lighting Poles for Street Lighting Network	168.00	12-Dec-26	04-Jan-27	0	0	0	0	100%	0%
PRO-SL-MF-140	Manufacturing of Lighting Fixtures for Street Lighting Network	168.00	12-Dec-26	04-Jan-27	0	0	0	0	100%	0%
Distribution Panel Board		240.00	05-Jan-27	08-Feb-27	0	0	0	0	0%	0%
PRO-SL-MF-160	Manufacturing of Distrubution Panel Boards for Street Lighting Network	240.00	05-Jan-27	08-Feb-27	0	0	0	0	100%	0%
Termination and Testing Works		728.00	26-Nov-26	15-Mar-27	0	0	0	0	0%	0%
PRO-SL-MF-130	Manufacturing of Fuse Boxes for Street Lighting Network	560.00	26-Nov-26	15-Feb-27	0	0	0	0	95.71%	0%
PRO-SL-MF-170	Manufacturing of Cable Lugs for Street Lighting Network	168.00	16-Feb-27	15-Mar-27	0	0	0	0	0%	0%
Earthing System Works		320.00	02-Dec-26	17-Jan-27	0	0	0	0	0%	0%
PRO-SL-MF-150	Manufacturing of Lighting Earthing for Street Lighting Network	320.00	02-Dec-26	17-Jan-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		720.00	12-Dec-26	29-Mar-27	0	0	0	0	0%	0%
Cabling Works		48.00	12-Dec-26	17-Dec-26	0	0	0	0	0%	0%
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	48.00	12-Dec-26	17-Dec-26	0	0	0	0	100%	0%
Lighting Poles Works		144.00	05-Jan-27	25-Jan-27	0	0	0	0	0%	0%
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	48.00	05-Jan-27	11-Jan-27	0	0	0	0	100%	0%
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	48.00	12-Jan-27	18-Jan-27	0	0	0	0	100%	0%
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	48.00	19-Jan-27	25-Jan-27	0	0	0	0	100%	0%
Distribution Panel Board		48.00	09-Feb-27	15-Feb-27	0	0	0	0	0%	0%
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	48.00	09-Feb-27	15-Feb-27	0	0	0	0	50%	0%
Termination and Testing Works		216.00	16-Feb-27	22-Mar-27	0	0	0	0	0%	0%
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	48.00	16-Feb-27	22-Feb-27	0	0	0	0	0%	0%
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	48.00	16-Mar-27	22-Mar-27	0	0	0	0	0%	0%
Earthing System Works		48.00	23-Mar-27	29-Mar-27	0	0	0	0	0%	0%
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	48.00	23-Mar-27	29-Mar-27	0	0	0	0	0%	0%
Material Delivery & Site Inspection		792.00	19-Dec-26	15-Apr-27	0	0	0	0	0%	0%
Cabling Works		168.00	19-Dec-26	11-Jan-27	0	0	0	0	0%	0%

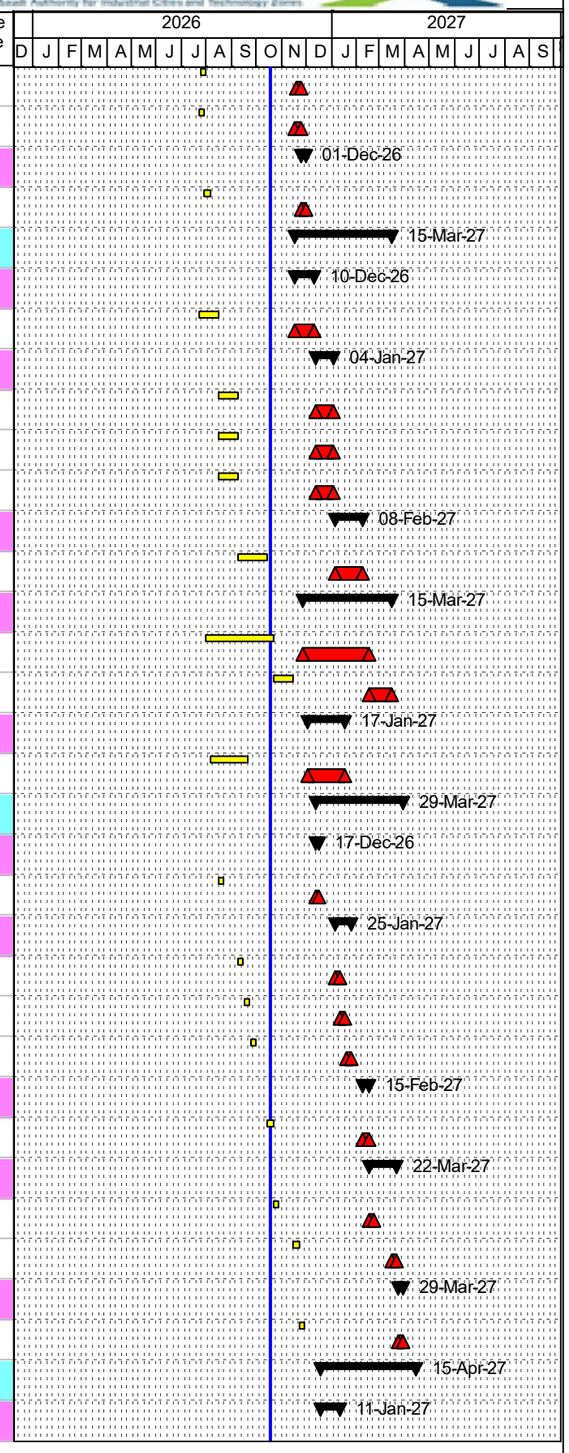


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-R25-SL-DL-100	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	168.00	19-Dec-26	11-Jan-27	0	0	0	0	100%	0%
Lighting Poles Works		336.00	05-Jan-27	22-Feb-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-110	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting Network	168.00	05-Jan-27	28-Jan-27	0	0	0	0	100%	0%
PRO-R25-SL-DL-120	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	168.00	30-Jan-27	22-Feb-27	0	0	0	0	57.14%	0%
PRO-R25-SL-DL-140	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	168.00	30-Jan-27	22-Feb-27	0	0	0	0	57.14%	0%
Distribution Panel Board		168.00	23-Feb-27	22-Mar-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-160	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting	168.00	23-Feb-27	22-Mar-27	0	0	0	0	0%	0%
Termination and Testing Works		168.00	23-Mar-27	15-Apr-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-130	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	168.00	23-Mar-27	15-Apr-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-170	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	168.00	23-Mar-27	15-Apr-27	0	0	0	0	0%	0%
Earthing System Works		168.00	23-Mar-27	15-Apr-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-150	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	168.00	23-Mar-27	15-Apr-27	0	0	0	0	0%	0%
Telecom and Light Current Network		744.00	25-Nov-26	16-Mar-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		160.00	25-Nov-26	17-Dec-26	0	0	0	0	0%	0%
Ducts Works		56.00	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	56.00	25-Nov-26	02-Dec-26	0	0	0	0	100%	0%
Manholes Works		56.00	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	56.00	25-Nov-26	02-Dec-26	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		160.00	25-Nov-26	17-Dec-26	0	0	0	0	0%	0%
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	160.00	25-Nov-26	17-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		560.00	03-Dec-26	22-Feb-27	0	0	0	0	0%	0%
Ducts Works		160.00	03-Dec-26	26-Dec-26	0	0	0	0	0%	0%
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	160.00	03-Dec-26	26-Dec-26	0	0	0	0	100%	0%
Manholes Works		160.00	27-Dec-26	18-Jan-27	0	0	0	0	0%	0%
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	160.00	27-Dec-26	18-Jan-27	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		240.00	19-Jan-27	22-Feb-27	0	0	0	0	0%	0%
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	240.00	19-Jan-27	22-Feb-27	0	0	0	0	70%	0%
1st Material Delivery & Site Inspection		448.00	27-Dec-26	01-Mar-27	0	0	0	0	0%	0%
Ducts Works		48.00	27-Dec-26	02-Jan-27	0	0	0	0	0%	0%
PRO-TE-1DL-100	1ST Material Delivery for Ducts of Telecom Network	48.00	27-Dec-26	02-Jan-27	0	0	0	0	100%	0%
Manholes Works		48.00	19-Jan-27	25-Jan-27	0	0	0	0	0%	0%
PRO-TE-1DL-110	1ST Material Delivery for Manholes of Telecom Network	48.00	19-Jan-27	25-Jan-27	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		48.00	23-Feb-27	01-Mar-27	0	0	0	0	0%	0%
PRO-CTV-1DL-100	1ST Material Delivery for Civil and Finishes Works of CCTV Complete System	48.00	23-Feb-27	01-Mar-27	0	0	0	0	0%	0%

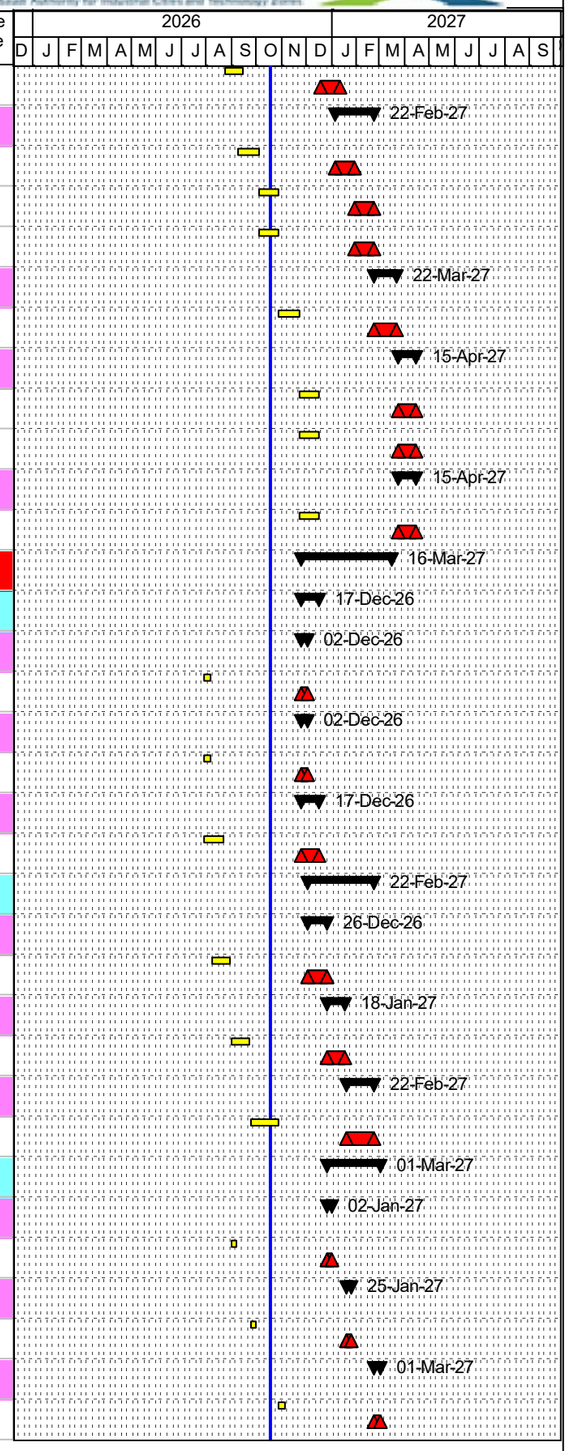


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Material Delivery & Site Inspection		480.00	03-Jan-27	16-Mar-27	0	0	0	0	0%	0%
Ducts Works		120.00	03-Jan-27	19-Jan-27	0	0	0	0	0%	0%
PRO-R25-TE-DL-100	Material Delivery & Site Inspection for Ducts of Telecom Network	120.00	03-Jan-27	19-Jan-27	0	0	0	0	100%	0%
Manholes Works		120.00	26-Jan-27	11-Feb-27	0	0	0	0	0%	0%
PRO-R25-TE-DL-110	Material Delivery & Site Inspection of Manholes for Telecom Network	120.00	26-Jan-27	11-Feb-27	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		80.00	02-Mar-27	16-Mar-27	0	0	0	0	0%	0%
PRO-R25-CTV-DL-100	Material Delivery & Site Inspection of for Civil and Finishes Works of CCTV Complete	80.00	02-Mar-27	16-Mar-27	0	0	0	0	0%	0%
Road Works		1272.00	19-Oct-26	25-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		336.00	19-Oct-26	06-Dec-26	0	0	0	0	0%	0%
Road Works		336.00	19-Oct-26	06-Dec-26	0	0	0	0	0%	0%
PRO-RD-PO-100	Issuance of Purchase Order for Subgrade of Road Works	56.00	19-Oct-26	26-Oct-26	0	0	0	0	100%	0%
PRO-RD-PO-110	Issuance of Purchase Order for Aggregate Base Course of Road Works	56.00	27-Oct-26	03-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-120	Issuance of Purchase Order for Prime Coat of Road Works	56.00	04-Nov-26	11-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-130	Issuance of Purchase Order for Asphaltic Base Course Laver of Road Works	56.00	12-Nov-26	19-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-180	Issuance of Purchase Order for Asphaltic Wearing Course Laver for Roads Network	56.00	21-Nov-26	28-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-190	Issuance of Purchase Order for Tack Coat Layer for Roads Network	56.00	29-Nov-26	06-Dec-26	0	0	0	0	100%	0%
Pavement Works		112.00	04-Nov-26	19-Nov-26	0	0	0	0	0%	0%
PRO-RD-PO-140	Issuance of Purchase Order for Interlock Tiles of Landscaping	56.00	04-Nov-26	11-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-150	Issuance of Purchase Order for Curbstones of Landscaping	56.00	12-Nov-26	19-Nov-26	0	0	0	0	100%	0%
Traffic Signs Boards and Roads Marking		112.00	21-Nov-26	06-Dec-26	0	0	0	0	0%	0%
PRO-RD-PO-160	Issuance of Purchase Order for Traffic Signs Boards of Road Works	56.00	21-Nov-26	28-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-170	Issuance of Purchase Order for Road Markings of Road Works	56.00	29-Nov-26	06-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		920.00	27-Oct-26	13-Mar-27	0	0	0	0	0%	0%
Road Works		720.00	27-Oct-26	08-Feb-27	0	0	0	0	0%	0%
PRO-RD-MF-100	Manufacturing of Subgrade for Road Works	80.00	27-Oct-26	07-Nov-26	0	0	0	0	100%	0%
PRO-RD-MF-110	Manufacturing of Aggregate Base Course for Road Works	160.00	08-Nov-26	30-Nov-26	0	0	0	0	100%	0%
PRO-RD-MF-120	Manufacturing of Prime Coat for Road Works	160.00	01-Dec-26	23-Dec-26	0	0	0	0	100%	0%
PRO-RD-MF-130	Manufacturing of Asphaltic Base Course Layer for Road Works	160.00	24-Dec-26	16-Jan-27	0	0	0	0	100%	0%
PRO-RD-MF-180	Manufacturing of Asphaltic Wearing Course Layer for Roads Network	160.00	17-Jan-27	08-Feb-27	0	0	0	0	100%	0%
PRO-RD-MF-190	Manufacturing of Tack Coat Layer for Roads Network	400.00	07-Dec-26	02-Feb-27	0	0	0	0	100%	0%
Pavement Works		168.00	03-Feb-27	27-Feb-27	0	0	0	0	0%	0%
PRO-RD-MF-140	Manufacturing of Interlock Tiles for Landscaping	168.00	03-Feb-27	27-Feb-27	0	0	0	0	38.1%	0%
PRO-RD-MF-150	Manufacturing of Curbstones for Landscaping	160.00	03-Feb-27	25-Feb-27	0	0	0	0	40%	0%
Traffic Signs Boards and Roads Marking		696.00	29-Nov-26	13-Mar-27	0	0	0	0	0%	0%

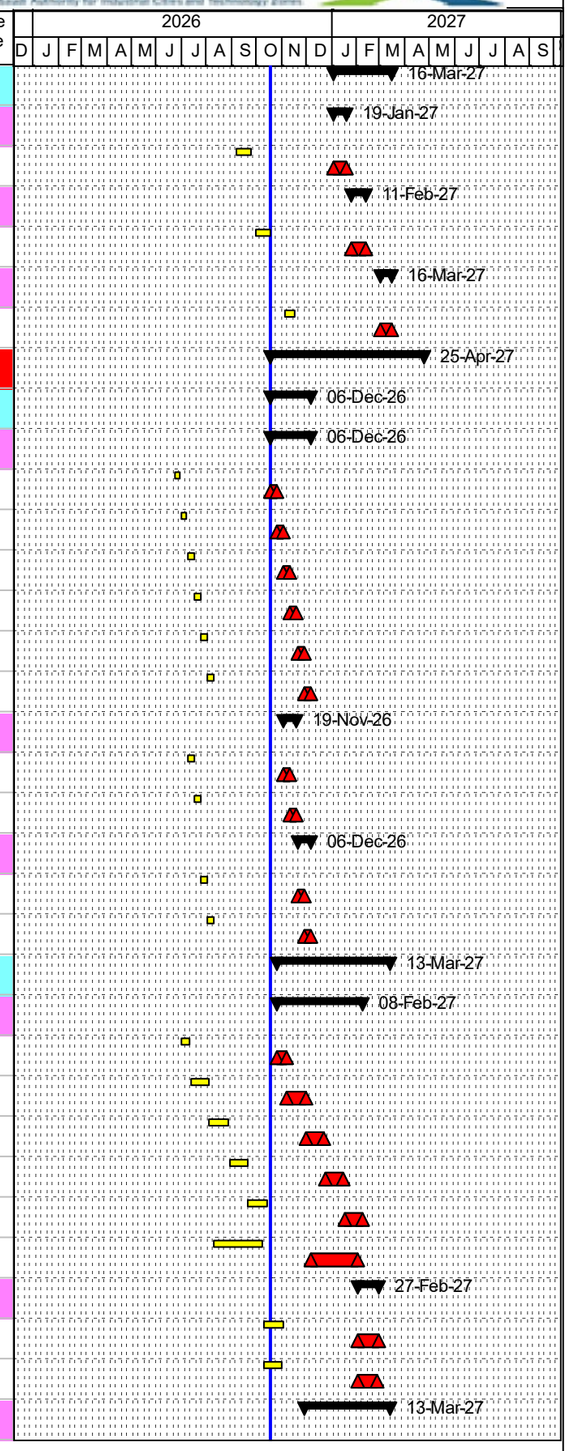

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-RD-MF-160	Manufacturing of Traffic Signs Boards for Road Works	640.00	29-Nov-26	01-Mar-27	0	0	0	0	81.25%	0%
PRO-RD-MF-170	Manufacturing of Road Markings for Road Works	640.00	07-Dec-26	13-Mar-27	0	0	0	0	72.5%	0%
1st Material Delivery & Site Inspection		992.00	08-Nov-26	04-Apr-27	0	0	0	0	0%	0%
Road Works		752.00	08-Nov-26	24-Feb-27	0	0	0	0	0%	0%
PRO-RD-1DL-100	1ST Material Delivery for Subgrade of Road Works	56.00	08-Nov-26	15-Nov-26	0	0	0	0	100%	0%
PRO-RD-1DL-110	1ST Material Delivery for Aggregate Base Course of Road Works	56.00	01-Dec-26	08-Dec-26	0	0	0	0	100%	0%
PRO-RD-1DL-120	1ST Material Delivery for Prime Coat of Road Works	120.00	24-Dec-26	10-Jan-27	0	0	0	0	100%	0%
PRO-RD-1DL-130	1ST Material Delivery for Asphaltic Base Course Layer of Road Works	56.00	17-Jan-27	24-Jan-27	0	0	0	0	100%	0%
PRO-RD-1DL-180	1ST Material Delivery for Asphaltic Wearing Course Layer for Roads Network	56.00	09-Feb-27	16-Feb-27	0	0	0	0	42.86%	0%
PRO-RD-1DL-190	1ST Material Delivery for Tack Coat Layer for Roads Network	56.00	17-Feb-27	24-Feb-27	0	0	0	0	0%	0%
Pavement Works		112.00	28-Feb-27	18-Mar-27	0	0	0	0	0%	0%
PRO-RD-1DL-140	1ST Material Delivery for Interlock Tiles of Landscaping	56.00	28-Feb-27	07-Mar-27	0	0	0	0	0%	0%
PRO-RD-1DL-150	1ST Material Delivery for Curbstones of Landscaping	56.00	08-Mar-27	18-Mar-27	0	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		112.00	20-Mar-27	04-Apr-27	0	0	0	0	0%	0%
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	56.00	28-Mar-27	04-Apr-27	0	0	0	0	0%	0%
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	56.00	20-Mar-27	27-Mar-27	0	0	0	0	0%	0%
Material Delivery & Site Inspection		1080.00	16-Nov-26	25-Apr-27	0	0	0	0	0%	0%
Pre-Bituminous Construction		336.00	16-Nov-26	03-Jan-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-100	Material Delivery & Site Inspection for Subgrade of Road Works	168.00	16-Nov-26	09-Dec-26	0	0	0	0	100%	0%
PRO-R25-RD-DL-110	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	168.00	10-Dec-26	03-Jan-27	0	0	0	0	100%	0%
Bituminous Construction		432.00	11-Jan-27	17-Mar-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-160	Material Delivery & Site Inspection for Prime Coat Layer of Road Works	88.00	11-Jan-27	23-Jan-27	0	0	0	0	100%	0%
PRO-R25-RD-DL-170	Material Delivery & Site Inspection for Asphaltic Base Course Layer of Road Works	88.00	25-Jan-27	06-Feb-27	0	0	0	0	100%	0%
PRO-RD-DL-200	Material Delivery for Asphaltic Wearing Course Layer for Roads Network	88.00	17-Feb-27	01-Mar-27	0	0	0	0	0%	0%
PRO-RD-DL-210	Material Delivery for Tack Coat Layer for Roads Network	88.00	02-Mar-27	17-Mar-27	0	0	0	0	0%	0%
Pavement Works		176.00	18-Mar-27	12-Apr-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-120	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	88.00	18-Mar-27	30-Mar-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-130	Material Delivery & Site Inspection of Curbstones for Landscaping	88.00	31-Mar-27	12-Apr-27	0	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		176.00	31-Mar-27	25-Apr-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-140	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	88.00	13-Apr-27	25-Apr-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-150	Material Delivery & Site Inspection of Road Markings For Road Works	88.00	31-Mar-27	12-Apr-27	0	0	0	0	0%	0%
Superstructure Works		424.00	19-Oct-26	19-Dec-26	0	0	0	0	0%	0%
Issuance of Purchase Orders		88.00	19-Oct-26	31-Oct-26	0	0	0	0	0%	0%
Water Pump Station		32.00	19-Oct-26	22-Oct-26	0	0	0	0	0%	0%

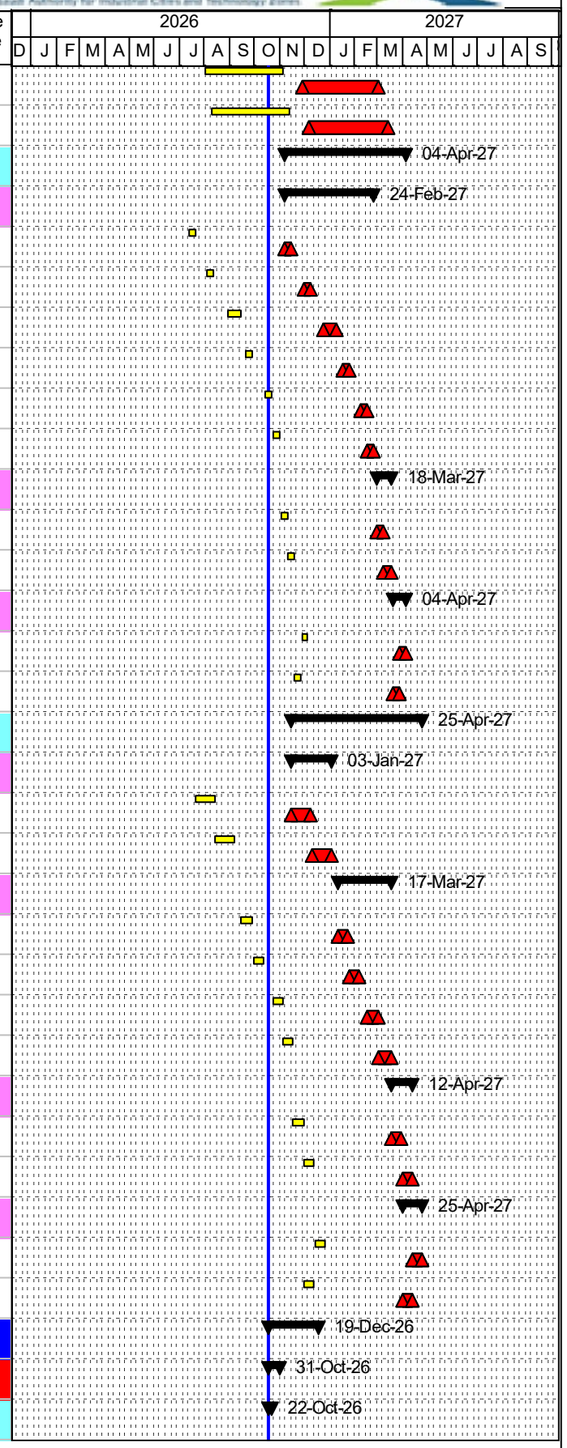

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-LS-CV-PO-20	Issuance of Purchase Order for Works for Water Pump Station	32.00	19-Oct-26	22-Oct-26	0	0	0	0	100%	0%
Storage Tank (TSE)		56.00	24-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Works for Storage Tank (TSE)	56.00	24-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Control Room		56.00	24-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-TSE-CV-PO-40	Issuance of Purchase Order for Works for Control Room	56.00	24-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Sewage Pump Stations		56.00	24-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-SPS-CV-PO-10	Issuance of Purchase Order for Works of Sewage Pump Station	56.00	24-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Gaurd Room		56.00	24-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-GR-CV-PO-40	Issuance of Purchase Order for Materials for Gaurd Room	56.00	24-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Boundary Fence		56.00	24-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-FE-CV-PO-50	Issuance of Purchase Order for Materials for Boundary Fence	56.00	24-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Manufacturing of Material		224.00	24-Oct-26	24-Nov-26	0	0	0	0	0%	0%
Water Pump Station		56.00	24-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-LS-CV-MF-30	Manufacturing of Works for Works for Water Pump Station	56.00	24-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Storage Tank (TSE)		112.00	01-Nov-26	16-Nov-26	0	0	0	0	0%	0%
PRO-TSE-CV-MF-40	Manufacturing of Works for Storage Tank (TSE)	112.00	01-Nov-26	16-Nov-26	0	0	0	0	100%	0%
Control Room		168.00	01-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-TSE-CV-MF-50	Manufacturing of Works for Control Room	168.00	01-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Sewage Pump Stations		168.00	01-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-SPS-CV-MF-10	Manufacturing of Works of Sewage Pump Station	168.00	01-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Gaurd Room		168.00	01-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-GR-CV-MF-50	Manufacturing of Materials for Gaurd Room	168.00	01-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Boundary Fence		168.00	01-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-FE-CV-MF-60	Manufacturing of Materials for Boundary Fence	168.00	01-Nov-26	24-Nov-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		280.00	24-Oct-26	02-Dec-26	0	0	0	0	0%	0%
Water Pump Station		48.00	24-Oct-26	29-Oct-26	0	0	0	0	0%	0%
PRO-LS-CV-1DL-40	1ST Material Delivery for Works of Water Pump Station	48.00	24-Oct-26	29-Oct-26	0	0	0	0	100%	0%
Storage Tank (TSE)		56.00	17-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-TSE-CV-1DL-50	1ST Material Delivery for Works for Storage Tank (TSE)	56.00	17-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Control Room		56.00	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-1DL-60	1ST Material Delivery for Works for Control Room	56.00	25-Nov-26	02-Dec-26	0	0	0	0	100%	0%
Sewage Pump Stations		56.00	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%
PRO-SPS-CV-1DL-10	1ST Material Delivery for Works of Sewage Pump Station	56.00	25-Nov-26	02-Dec-26	0	0	0	0	100%	0%
Gaurd Room		56.00	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%

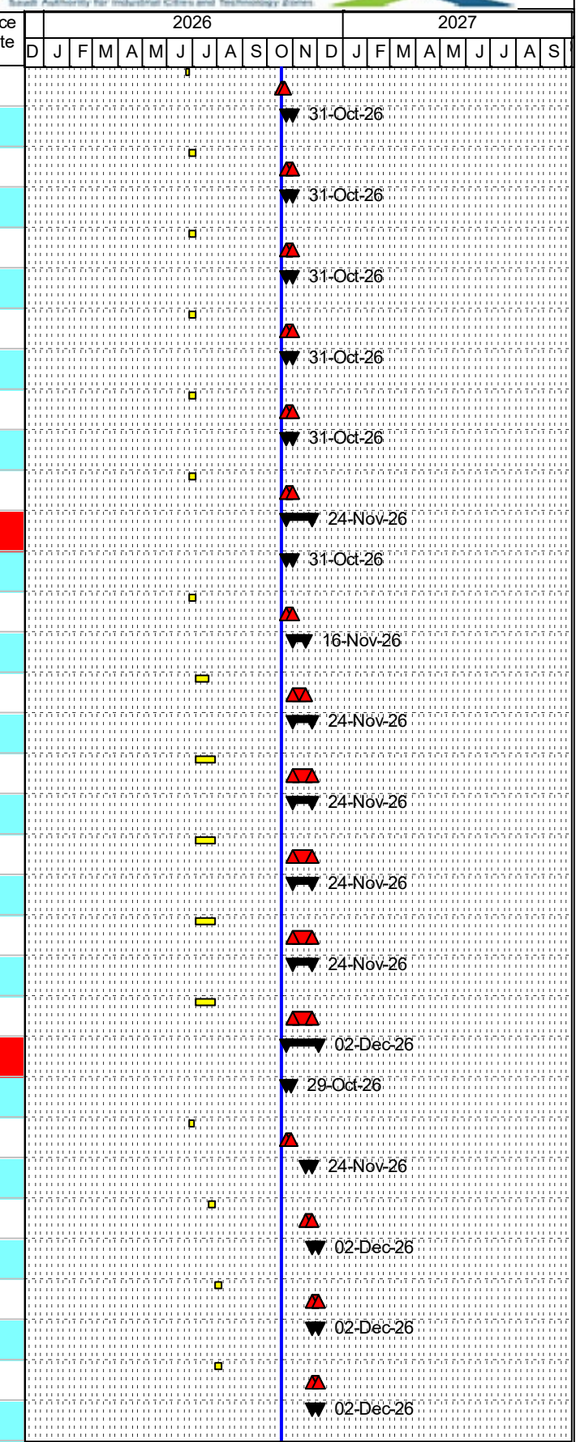

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-GR-CV-1DL-60	1ST Material Delivery for Materials for Gaurd Room	56.00	25-Nov-26	02-Dec-26	0	0	0	0	100%	0%
Boundary Fence		56.00	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%
PRO-FE-CV-1DL-70	1ST Material Delivery for Materials for Boundary Fence	56.00	25-Nov-26	02-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		392.00	24-Oct-26	19-Dec-26	0	0	0	0	0%	0%
Water Pump Station		80.00	24-Oct-26	03-Nov-26	0	0	0	0	0%	0%
PRO-LS-CV-DL-50	Material Delivery & Site Inspection for Works for Water Pump Station	80.00	24-Oct-26	03-Nov-26	0	0	0	0	100%	0%
Storage Tank (TSE)		216.00	04-Nov-26	05-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-DL-60	Material Delivery & Site Inspection for Works for Storage Tank (TSE)	216.00	04-Nov-26	05-Dec-26	0	0	0	0	100%	0%
Control Room		112.00	03-Dec-26	19-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-DL-70	Material Delivery & Site Inspection for Works for Control Room	112.00	03-Dec-26	19-Dec-26	0	0	0	0	100%	0%
Sewage Pump Stations		112.00	03-Dec-26	19-Dec-26	0	0	0	0	0%	0%
PRO-SPS-CV-DL-10	Material Delivery & Site Inspection for Works for Pump Station	112.00	03-Dec-26	19-Dec-26	0	0	0	0	100%	0%
Gaurd Room		112.00	03-Dec-26	19-Dec-26	0	0	0	0	0%	0%
PRO-GR-CV-DL-70	Material Delivery & Site Inspection for Materials for Gaurd Room	112.00	03-Dec-26	19-Dec-26	0	0	0	0	100%	0%
Boundary Fence		112.00	03-Dec-26	19-Dec-26	0	0	0	0	0%	0%
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Materials for Boundary Fence	112.00	03-Dec-26	19-Dec-26	0	0	0	0	100%	0%
Softscape and Planting Works		736.00	04-Nov-26	18-Feb-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		96.00	04-Nov-26	17-Nov-26	0	0	0	0	0%	0%
Main Line Pipes		96.00	04-Nov-26	17-Nov-26	0	0	0	0	0%	0%
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	48.00	04-Nov-26	10-Nov-26	0	0	0	0	100%	0%
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders	48.00	11-Nov-26	17-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		528.00	11-Nov-26	26-Jan-27	0	0	0	0	0%	0%
Main Line Pipes		528.00	11-Nov-26	26-Jan-27	0	0	0	0	0%	0%
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	480.00	11-Nov-26	19-Jan-27	0	0	0	0	100%	0%
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	480.00	18-Nov-26	26-Jan-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		96.00	20-Jan-27	02-Feb-27	0	0	0	0	0%	0%
Main Line Pipes		96.00	20-Jan-27	02-Feb-27	0	0	0	0	0%	0%
PRO-IR-1DL-140	1ST Material Delivery for Softscape and Planting Works	48.00	20-Jan-27	26-Jan-27	0	0	0	0	100%	0%
PRO-IR-1DL-150	1ST Material Delivery for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	48.00	27-Jan-27	02-Feb-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		160.00	27-Jan-27	18-Feb-27	0	0	0	0	0%	0%
Main Line Pipes		160.00	27-Jan-27	18-Feb-27	0	0	0	0	0%	0%
PRO-R25-IR-DL-140	Material Delivery & Site Inspection of Softscape and Planting Works	80.00	27-Jan-27	07-Feb-27	0	0	0	0	100%	0%
PRO-R25-IR-DL-150	Material Delivery & Site Inspection of Site Furnishings (Seating Bench,Stone Boulders	80.00	08-Feb-27	18-Feb-27	0	0	0	0	40%	0%
Long Lead Time Items		1456.00	04-Nov-26	13-Jun-27	0	0	0	0	0%	0%

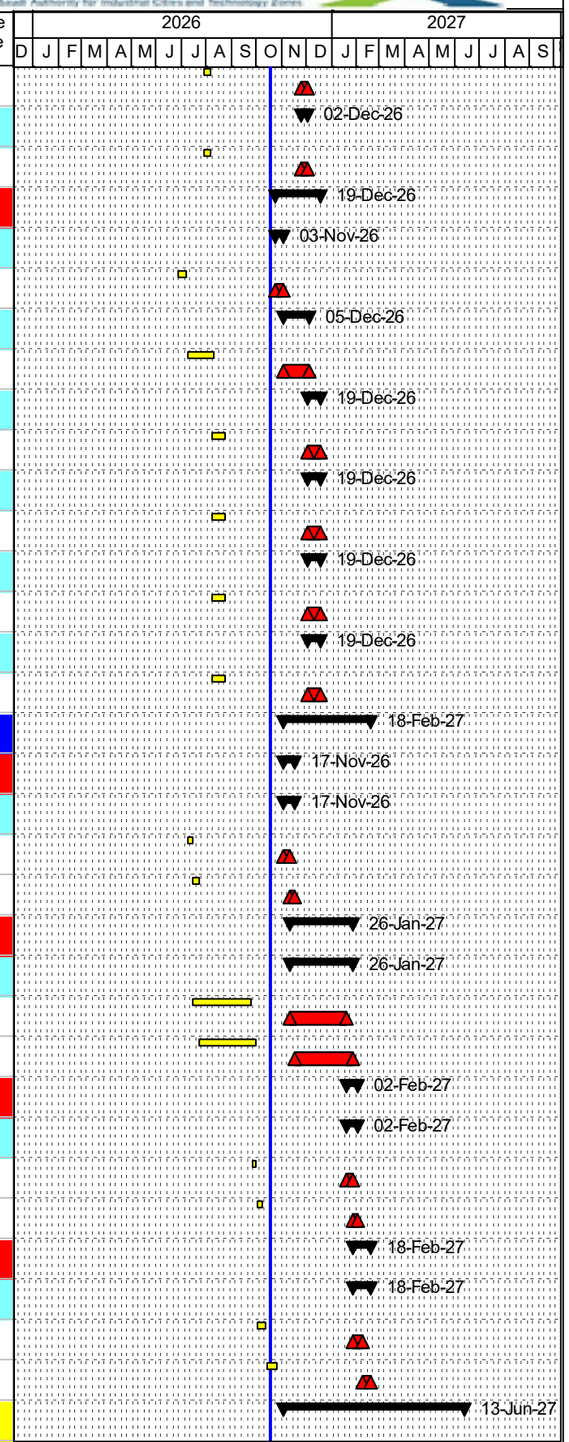

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Superstructure Works		1456.00	04-Nov-26	13-Jun-27	0	0	0	0	0%	0%
Sewage Pump Station		1192.00	04-Nov-26	29-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		48.00	04-Nov-26	10-Nov-26	0	0	0	0	0%	0%
PRO-SPS-LL-PO-10	Issuance of Purchase Order for Electromechanical Works for Pump Station	48.00	04-Nov-26	10-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		800.00	11-Nov-26	07-Mar-27	0	0	0	0	0%	0%
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Station	800.00	11-Nov-26	07-Mar-27	0	0	0	0	80%	0%
Material Shipping/Custom Clearance/Delivery		168.00	08-Mar-27	04-Apr-27	0	0	0	0	0%	0%
PRO-SPS-LL-SH/DL-10	Material Delivery for Electromechanical Works for Pump Station	168.00	08-Mar-27	04-Apr-27	0	0	0	0	0%	0%
Material Site Inspection		176.00	05-Apr-27	29-Apr-27	0	0	0	0	0%	0%
PRO-SPS-LL-MSI-10	Material Site Inspection for Electromechanical Works for Pump Station	176.00	05-Apr-27	29-Apr-27	0	0	0	0	0%	0%
Water Pump Station		952.00	11-Nov-26	01-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		56.00	11-Nov-26	18-Nov-26	0	0	0	0	0%	0%
PRO-LS-LL-PO-20	Issuance of Purchase Order for Electromechanical Works for Water Pump	56.00	11-Nov-26	18-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		560.00	19-Nov-26	08-Feb-27	0	0	0	0	0%	0%
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Water Pump Station	560.00	19-Nov-26	08-Feb-27	0	0	0	0	100%	0%
Material Shipping/Custom Clearance/Delivery		168.00	09-Feb-27	04-Mar-27	0	0	0	0	0%	0%
PRO-LS-LL-SH/DL-20	Material Delivery for Electromechanical Works for Water Pump Station	168.00	09-Feb-27	04-Mar-27	0	0	0	0	14.29%	0%
Material Site Inspection		168.00	06-Mar-27	01-Apr-27	0	0	0	0	0%	0%
PRO-LS-LL-MSI-20	Material Site Inspection for Electromechanical Works for Water Pump Station	168.00	06-Mar-27	01-Apr-27	0	0	0	0	0%	0%
Storage Tank (TSE)		1352.00	19-Nov-26	13-Jun-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		56.00	19-Nov-26	26-Nov-26	0	0	0	0	0%	0%
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank	56.00	19-Nov-26	26-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		960.00	28-Nov-26	19-Apr-27	0	0	0	0	0%	0%
PRO-TSE-LL-MF-30	Manufacturing of Electromechanical Works for Storage Tank (TSE)	960.00	28-Nov-26	19-Apr-27	0	0	0	0	55%	0%
Material Shipping/Custom Clearance/Delivery		168.00	20-Apr-27	13-May-27	0	0	0	0	0%	0%
PRO-TSE-LL-SH/DL-30	Material Delivery for Electromechanical Works for Storage Tank (TSE)	168.00	20-Apr-27	13-May-27	0	0	0	0	0%	0%
Material Site Inspection		168.00	20-May-27	13-Jun-27	0	0	0	0	0%	0%
PRO-TSE-LL-MSI-30	Material Site Inspection for Electromechanical Works for Storage Tank (TSE)	168.00	20-May-27	13-Jun-27	0	0	0	0	0%	0%
Construction Works		3054.00	10-Mar-26 A	16-Jun-27	93,061,973	34,795,176	23,121,817	22,765,905	37.26%	24.76%
Infrastructure Networks		3038.00	10-Mar-26 A	14-Jun-27	57,696,530	32,291,178	13,535,825	13,257,665	55.97%	23.46%
Internal		3038.00	10-Mar-26 A	14-Jun-27	32,508,953	16,641,136	3,055,456	3,055,656	51.19%	9.4%
Alignment-RD-01		2902.00	10-Mar-26 A	25-May-27	15,199,337	8,180,211	3,055,456	3,055,656	53.82%	20.1%
Earthworks		1774.00	10-Mar-26 A	30-Dec-26	4,697,995	4,697,995	3,055,456	3,055,656	100%	65.04%
Earthworks		1774.00	10-Mar-26 A	30-Dec-26	4,697,995	4,697,995	3,055,456	3,055,656	100%	65.04%

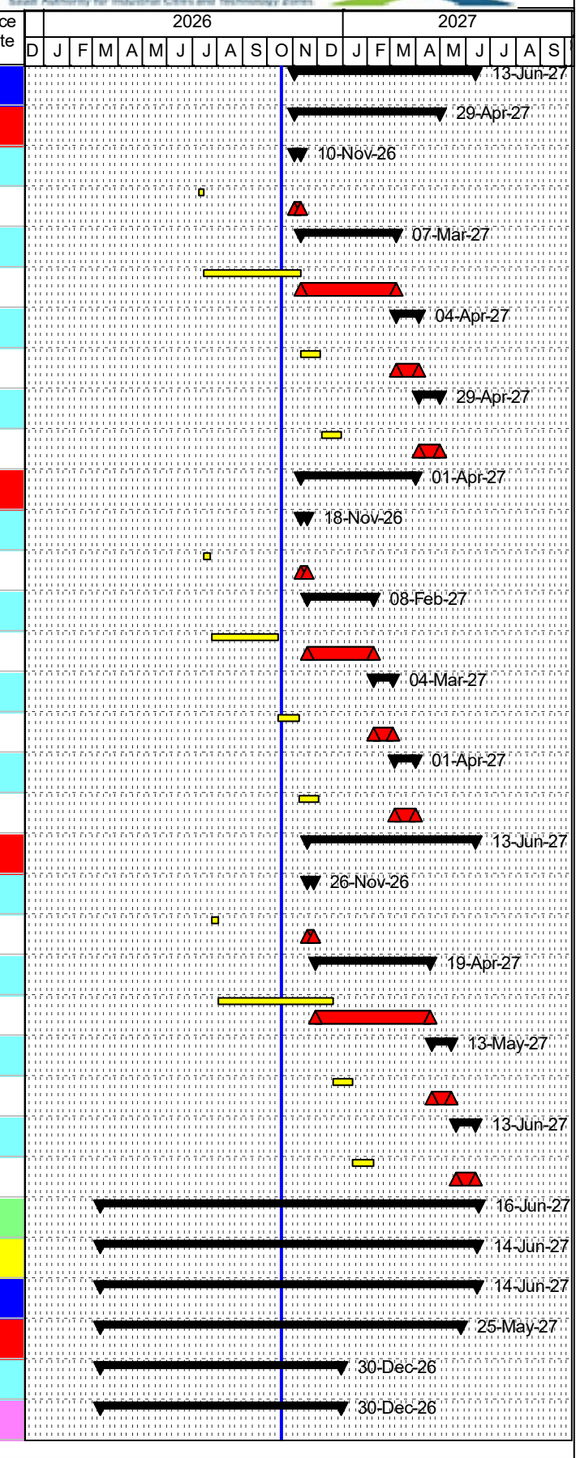

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-EW-210	Excavation and Backfilling Works Upto Design Level for Earthworks for	648.00	10-Mar-26 A	22-Jun-26 A	379,596	379,596	379,596	379,596	100%	100%
CO-EW-210_R	Excavation and Backfilling Works Upto Design Level for Earthworks for	160.00	01-Jul-26 A	15-Jul-26 A	1,772,616	1,772,616	1,772,616	1,772,616	100%	100%
CO-EW-210_R01	Excavation and Backfilling Works Upto Design Level for Earthworks for	160.00	31-Aug-26 A	30-Dec-26	2,545,782	2,545,782	903,244	903,443	100%	35.48%
Storm Drainage Network		488.00	19-Oct-26	28-Dec-26	2,292,989	2,292,989	0	0	100%	0%
Manholes		328.00	19-Oct-26	05-Dec-26	340,545	340,545	0	0	100%	0%
CO-SD-MH-230	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	96.00	19-Oct-26	01-Nov-26	22,703	22,703	0	0	100%	0%
CO-SD-MH-240	Install RC Footing Works for Manholes of Storm Drainage Network for Alignment-RD-01	72.00	05-Nov-26	15-Nov-26	113,515	113,515	0	0	100%	0%
CO-SD-MH-250	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	56.00	16-Nov-26	23-Nov-26	136,218	136,218	0	0	100%	0%
CO-SD-MH-260	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-01	80.00	24-Nov-26	05-Dec-26	68,109	68,109	0	0	100%	0%
Main Line Sections		184.00	16-Nov-26	12-Dec-26	1,523,566	1,523,566	0	0	100%	0%
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	64.00	16-Nov-26	24-Nov-26	209,385	209,385	0	0	100%	0%
CO-SD-ML-150	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-01	64.00	24-Nov-26	02-Dec-26	933,291	933,291	0	0	100%	0%
CO-SD-ML-160	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	64.00	03-Dec-26	12-Dec-26	380,890	380,890	0	0	100%	0%
Catch Basin Sections		176.00	03-Dec-26	28-Dec-26	428,877	428,877	0	0	100%	0%
CO-SD-CB-180	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network for	64.00	03-Dec-26	12-Dec-26	107,219	107,219	0	0	100%	0%
CO-SD-CB-190	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	56.00	13-Dec-26	20-Dec-26	250,178	250,178	0	0	100%	0%
CO-SD-CB-200	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network for	56.00	21-Dec-26	28-Dec-26	71,479	71,479	0	0	100%	0%
Sewage Network		480.00	13-Dec-26	20-Feb-27	801,144	631,685	0	0	78.85%	0%
Manholes		480.00	13-Dec-26	20-Feb-27	264,213	228,985	0	0	86.67%	0%
CO-SW-MH-210	Excavation Works for Main Line Manholes of Sewage Network for Alignment-RD-01	96.00	13-Dec-26	26-Dec-26	17,614	17,614	0	0	100%	0%
CO-SW-MH-220	Installation RC Footing Works for Main Line Manholes of Sewage Network for	96.00	27-Dec-26	09-Jan-27	88,071	88,071	0	0	100%	0%
CO-SW-MH-230	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96.00	10-Jan-27	23-Jan-27	52,843	52,843	0	0	100%	0%
CO-SW-MH-240	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96.00	24-Jan-27	06-Feb-27	52,843	52,843	0	0	100%	0%
CO-SW-MH-250	Backfilling Works for Main Line Manholes of Sewage Network for Alignment-RD-01	96.00	07-Feb-27	20-Feb-27	52,843	17,614	0	0	33.33%	0%
Main Line Sections		368.00	29-Dec-26	20-Feb-27	536,930	402,701	0	0	75%	0%
CO-SW-ML-140	Trench Excavation and Bedding Works for Main Lines of Sewage Network for	64.00	29-Dec-26	06-Jan-27	79,139	79,139	0	0	100%	0%
CO-SW-ML-150	Pipes Laying Works for Main Lines of Sewage Network for Alignment-RD-01	64.00	07-Jan-27	16-Jan-27	323,562	323,562	0	0	100%	0%
CO-SW-ML-160	Trench Backfilling and Compaction Works for Main Lines of Sewage Network for	48.00	14-Feb-27	20-Feb-27	134,230	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		336.00	06-Dec-26	23-Jan-27	94,795	94,795	0	0	100%	0%
CO-TSE-ML-200	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	56.00	06-Dec-26	13-Dec-26	11,940	11,940	0	0	100%	0%
CO-TSE-ML-210	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-01	136.00	19-Dec-26	06-Jan-27	59,156	59,156	0	0	100%	0%
CO-TSE-ML-230	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	112.00	07-Jan-27	23-Jan-27	23,699	23,699	0	0	100%	0%
Potable Water Network		256.00	06-Dec-26	11-Jan-27	373,599	373,599	0	0	100%	0%
Main Line Sections		256.00	06-Dec-26	11-Jan-27	248,155	248,155	0	0	100%	0%

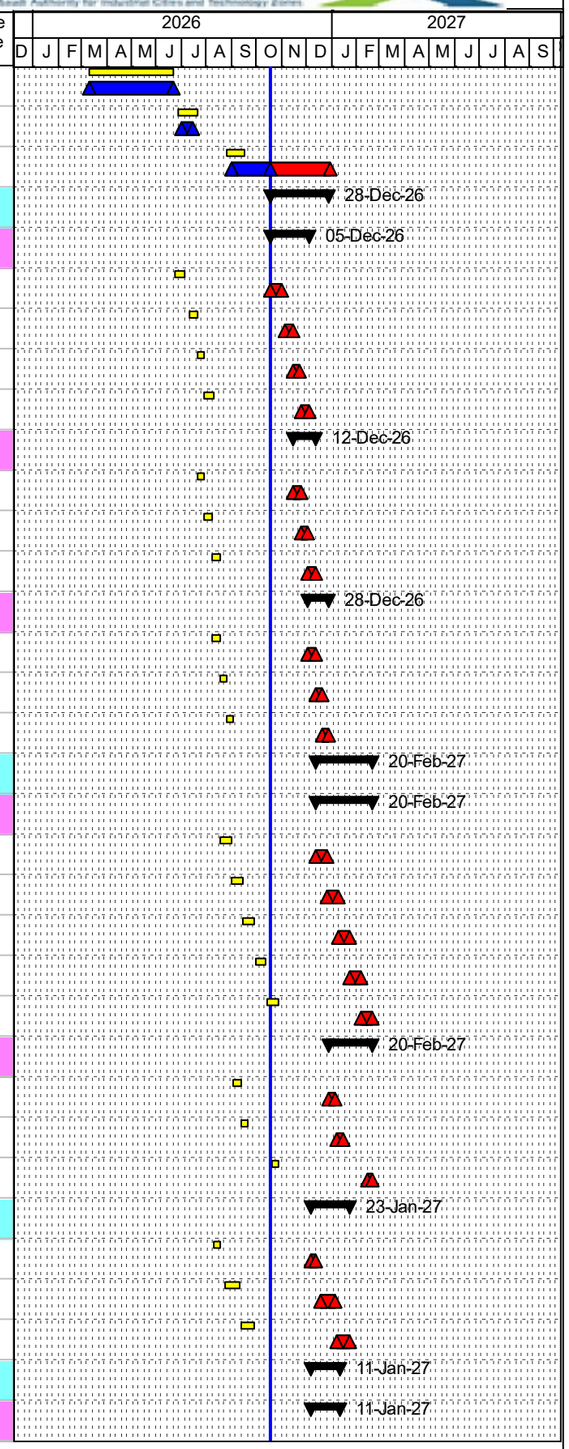


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-PW-ML-140	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	48.00	06-Dec-26	12-Dec-26	45,473	45,473	0	0	100%	0%
CO-PW-ML-150	Pipes Laying and accessories for Main Lines of Potable Water Network for	48.00	29-Dec-26	04-Jan-27	112,515	112,515	0	0	100%	0%
CO-PW-ML-160	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	48.00	05-Jan-27	11-Jan-27	90,167	90,167	0	0	100%	0%
Valve Chamber		240.00	08-Dec-26	11-Jan-27	62,485	62,485	0	0	100%	0%
CO-PW-VC-230	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	32.00	08-Dec-26	12-Dec-26	3,905	3,905	0	0	100%	0%
CO-PW-VC-240	Installation Works for Valves of Potable Water Network for Alignment-RD-01	32.00	17-Dec-26	21-Dec-26	10,154	10,154	0	0	100%	0%
CO-PW-VC-250	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	32.00	07-Jan-27	11-Jan-27	7,811	7,811	0	0	100%	0%
CO-PW-VC190	Installation of Valve Chambers of Potable Water Network for Alignment-RD-01	32.00	13-Dec-26	16-Dec-26	40,615	40,615	0	0	100%	0%
Fire Hydrant		208.00	13-Dec-26	11-Jan-27	62,959	62,959	0	0	100%	0%
CO-PW-FH-170	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-01	120.00	13-Dec-26	29-Dec-26	3,935	3,935	0	0	100%	0%
CO-PW-FH-180	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-01	24.00	05-Jan-27	07-Jan-27	51,154	51,154	0	0	100%	0%
CO-PW-FH-190	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	24.00	09-Jan-27	11-Jan-27	7,870	7,870	0	0	100%	0%
Irrigation Network		288.00	24-Jan-27	06-Mar-27	601,521	89,147	0	0	14.82%	0%
Main Line Pipes		288.00	24-Jan-27	06-Mar-27	601,521	89,147	0	0	14.82%	0%
CO-IR-ML-150	Trench Excavation and Bedding Works for Main Lines of Irrigation Network for	56.00	24-Jan-27	31-Jan-27	13,844	13,844	0	0	100%	0%
CO-IR-ML-160	Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-01	64.00	01-Feb-27	09-Feb-27	69,218	69,218	0	0	100%	0%
CO-IR-ML-170	Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-01	56.00	10-Feb-27	17-Feb-27	21,302	6,086	0	0	28.57%	0%
CO-IR-ML-180	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for	32.00	02-Mar-27	06-Mar-27	27,687	0	0	0	0%	0%
CO-IR-ML-190	Installation Works for Bulbblers And Sprinklers and Irrigation Control System of Irrigation	80.00	18-Feb-27	01-Mar-27	469,471	0	0	0	0%	0%
Medium Voltage Network		144.00	21-Feb-27	16-Mar-27	153,221	0	0	0	0%	0%
Cabling Works		144.00	21-Feb-27	16-Mar-27	153,221	0	0	0	0%	0%
CO-MV-ML-280	Trench Excavation and Bedding Works for Medium Voltage Network for Alignment-RD-01	48.00	21-Feb-27	27-Feb-27	29,351	0	0	0	0%	0%
CO-MV-ML-290	Duct Laying Works for Medium Voltage Network for Alignment-RD-01	48.00	28-Feb-27	06-Mar-27	85,162	0	0	0	0%	0%
CO-MV-ML-300	Trench Backfilling and Compaction Works for Medium Voltage Network for Alignment-RD-01	48.00	07-Mar-27	16-Mar-27	38,709	0	0	0	0%	0%
Low Voltage Network		200.00	17-Mar-27	14-Apr-27	158,103	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		144.00	17-Mar-27	06-Apr-27	81,711	0	0	0	0%	0%
CON-LV-ML-130	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	48.00	17-Mar-27	23-Mar-27	15,956	0	0	0	0%	0%
CON-LV-ML-140	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-01	48.00	24-Mar-27	30-Mar-27	45,209	0	0	0	0%	0%
CON-LV-ML-150	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	48.00	31-Mar-27	06-Apr-27	20,546	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		152.00	24-Mar-27	14-Apr-27	73,733	0	0	0	0%	0%
CON-LV-HC-130	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	48.00	24-Mar-27	30-Mar-27	7,978	0	0	0	0%	0%
CON-LV-HC-140	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-01	56.00	31-Mar-27	07-Apr-27	45,209	0	0	0	0%	0%
CON-LV-HC-150	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	48.00	08-Apr-27	14-Apr-27	20,546	0	0	0	0%	0%
Distribution Pillars Works		56.00	24-Mar-27	31-Mar-27	2,659	0	0	0	0%	0%

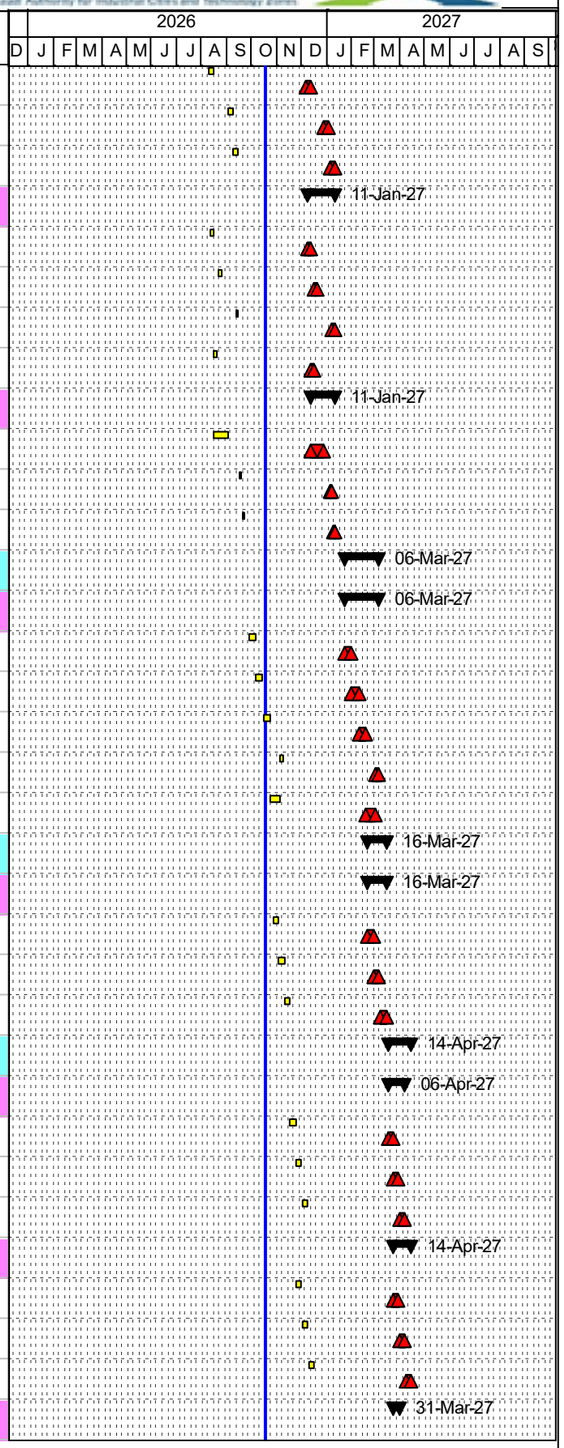

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CON-LV-DP-130	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	56.00	24-Mar-27	31-Mar-27	2,659	0	0	0	0%	0%
Street Lighting Network		184.00	28-Feb-27	29-Mar-27	80,615	0	0	0	0%	0%
Lighting Poles Works		152.00	28-Feb-27	24-Mar-27	33,194	0	0	0	0%	0%
CO-SL-LP-350	Installation Works for Lighting Poles Foundation of Street Lighting Network for	64.00	28-Feb-27	08-Mar-27	7,113	0	0	0	0%	0%
CO-SL-LP-360	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-01	40.00	13-Mar-27	17-Mar-27	23,710	0	0	0	0%	0%
CO-SL-LP-380	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-01	48.00	18-Mar-27	24-Mar-27	2,371	0	0	0	0%	0%
Cabling Works		80.00	18-Mar-27	29-Mar-27	47,420	0	0	0	0%	0%
CO-SL-CL-290	Cable Laying Works for Street Lighting Network for Alignment-RD-01	40.00	18-Mar-27	23-Mar-27	26,081	0	0	0	0%	0%
CO-SL-CL-300	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-01	40.00	24-Mar-27	29-Mar-27	21,339	0	0	0	0%	0%
Telecom and Light Current Network		168.00	30-Mar-27	22-Apr-27	1,517,343	0	0	0	0%	0%
Ducts Works		56.00	15-Apr-27	22-Apr-27	94,908	0	0	0	0%	0%
CO-TE-DW-150	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-01	32.00	15-Apr-27	19-Apr-27	65,249	0	0	0	0%	0%
CO-TE-DW-160	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	24.00	20-Apr-27	22-Apr-27	29,659	0	0	0	0%	0%
Manholes Works		64.00	30-Mar-27	07-Apr-27	36,239	0	0	0	0%	0%
CO-TE-MH-170	Excavation Works for Manholes of Telecom Network for Alignment-RD-01	32.00	30-Mar-27	03-Apr-27	2,416	0	0	0	0%	0%
CO-TE-MH-180	Installation Works for Manholes of Telecom Network for Alignment-RD-01	32.00	30-Mar-27	03-Apr-27	26,575	0	0	0	0%	0%
CO-TE-MH-190	Backfilling Works for Manholes of Telecom Network for Alignment-RD-01	32.00	04-Apr-27	07-Apr-27	7,248	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		64.00	08-Apr-27	17-Apr-27	1,386,196	0	0	0	0%	0%
CO-TE-CTV-150	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-01	64.00	08-Apr-27	17-Apr-27	1,386,196	0	0	0	0%	0%
Road Network		80.00	24-Apr-27	04-May-27	2,662,858	0	0	0	0%	0%
Pavement Works		80.00	24-Apr-27	04-May-27	2,607,263	0	0	0	0%	0%
CO-RD-PV-180	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-01	80.00	24-Apr-27	04-May-27	263,715	0	0	0	0%	0%
CO-RD-PV-190	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-01	80.00	24-Apr-27	04-May-27	2,343,548	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		64.00	24-Apr-27	02-May-27	55,595	0	0	0	0%	0%
CO-RD-F-RM-190	Application of Road Marking Works For Road Works for Alignment-RD-01	32.00	24-Apr-27	27-Apr-27	35,713	0	0	0	0%	0%
CO-RD-F-TS-130	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-01	32.00	28-Apr-27	02-May-27	19,882	0	0	0	0%	0%
Finishes for Infrastructure Networks		440.00	17-Mar-27	25-May-27	1,765,154	0	0	0	0%	0%
Storm Drainage Network		184.00	24-Apr-27	25-May-27	780,323	0	0	0	0%	0%
Testing and Finishes		184.00	24-Apr-27	25-May-27	780,323	0	0	0	0%	0%
CO-SD-CB-TF-170	Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-01	56.00	05-May-27	12-May-27	71,479	0	0	0	0%	0%
CO-SD-CB-TF-180	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network for	48.00	13-May-27	25-May-27	107,219	0	0	0	0%	0%
CO-SD-CB-TF-190	Catch Basin Internal Finishes (Benching) for Storm Drainage Network for Alignment-RD-01	48.00	24-Apr-27	29-Apr-27	107,219	0	0	0	0%	0%
CO-SD-MH-TF-230	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-01	16.00	03-May-27	04-May-27	113,515	0	0	0	0%	0%
CO-SD-ML-TF-110	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-01	16.00	01-May-27	02-May-27	380,890	0	0	0	0%	0%

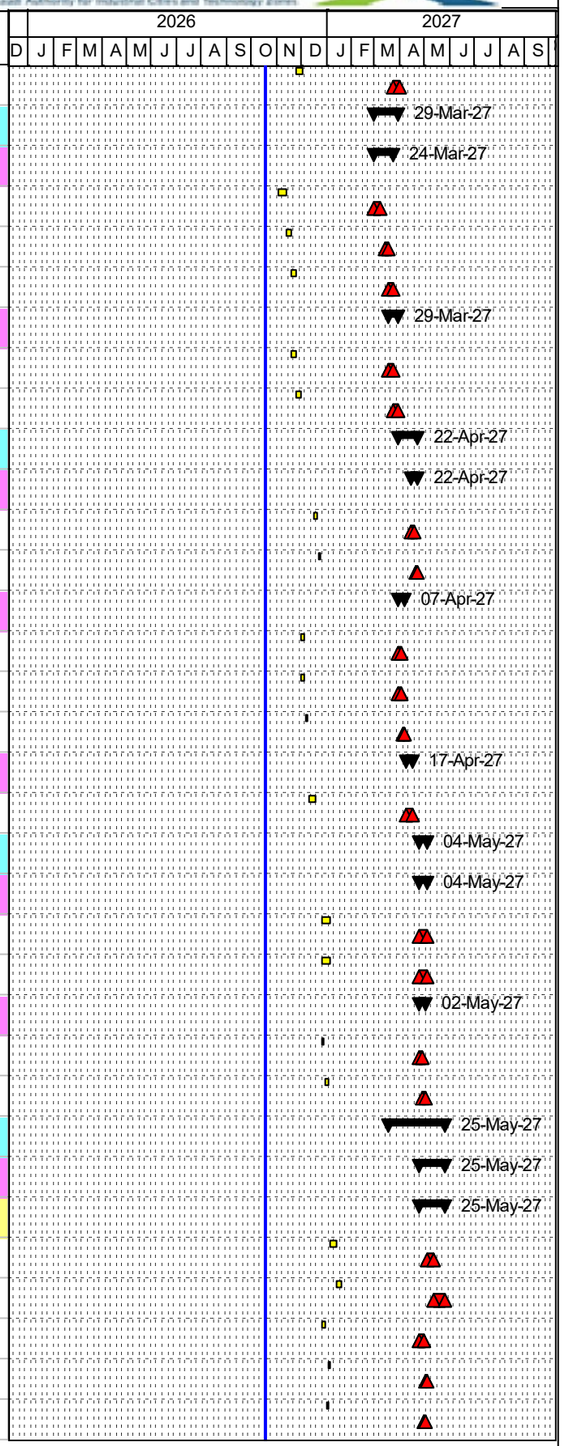

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Sewage Network		56.00	24-Apr-27	01-May-27	222,301	0	0	0	0%	0%
Testing and Finishes		56.00	24-Apr-27	01-May-27	222,301	0	0	0	0%	0%
CO-SW-TF-230	Final Testing For Main Line of Sewage Network for Alignment-RD-01	32.00	27-Apr-27	01-May-27	134,230	0	0	0	0%	0%
CO-SW-TF-250	Testing Works for Main Line Manholes of Sewage Network for Alignment-RD-01	24.00	24-Apr-27	26-Apr-27	88,071	0	0	0	0%	0%
Potable Water Network		64.00	24-Apr-27	02-May-27	234,043	0	0	0	0%	0%
Testing and Finishes		64.00	24-Apr-27	02-May-27	234,043	0	0	0	0%	0%
CO-PW-TF-140	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	32.00	24-Apr-27	27-Apr-27	15,740	0	0	0	0%	0%
CO-PW-TF-150	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-01	16.00	28-Apr-27	29-Apr-27	128,136	0	0	0	0%	0%
CO-PW-TF-220	Testing of Potable Water Network for Alignment-RD-01	16.00	01-May-27	02-May-27	90,167	0	0	0	0%	0%
Irrigation Network		16.00	03-May-27	04-May-27	27,687	0	0	0	0%	0%
Testing and Finishes		16.00	03-May-27	04-May-27	27,687	0	0	0	0%	0%
CO-IR-TF-170	Final Testing (pressure tests) of Irrigation Network for Alignment-RD-01	16.00	03-May-27	04-May-27	27,687	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		16.00	03-May-27	04-May-27	23,699	0	0	0	0%	0%
Testing and Finishes		16.00	03-May-27	04-May-27	23,699	0	0	0	0%	0%
CO-TSE-TF-210	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-01	16.00	03-May-27	04-May-27	23,699	0	0	0	0%	0%
Medium Voltage Network		16.00	17-Mar-27	18-Mar-27	30,971	0	0	0	0%	0%
Termination and Testing Works		16.00	17-Mar-27	18-Mar-27	30,971	0	0	0	0%	0%
CO-MV-TF-230	Testing and Termination Works of Medium Voltage Network for Alignment-RD-01	16.00	17-Mar-27	18-Mar-27	30,971	0	0	0	0%	0%
Low Voltage Network		32.00	15-Apr-27	19-Apr-27	32,877	0	0	0	0%	0%
Termination and Testing Works		32.00	15-Apr-27	19-Apr-27	32,877	0	0	0	0%	0%
CON-LV-TT-120	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	32.00	15-Apr-27	19-Apr-27	32,877	0	0	0	0%	0%
Street Lighting Network		184.00	30-Mar-27	25-Apr-27	30,897	0	0	0	0%	0%
Termination and Testing Works		184.00	30-Mar-27	25-Apr-27	27,118	0	0	0	0%	0%
CO-SL-LP-370	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48.00	30-Mar-27	05-Apr-27	12,892	0	0	0	0%	0%
CO-SL-TF-410	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-01	24.00	22-Apr-27	25-Apr-27	14,226	0	0	0	0%	0%
Earthing System Works		40.00	17-Apr-27	21-Apr-27	3,779	0	0	0	0%	0%
CO-SL-ES-240	Install Earthing System Works for Lighting Poles of Street Lighting Network for	24.00	17-Apr-27	19-Apr-27	1,890	0	0	0	0%	0%
CO-SL-ES-250	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	16.00	20-Apr-27	21-Apr-27	1,890	0	0	0	0%	0%
Telecom and Light Current Network		48.00	24-Apr-27	29-Apr-27	382,356	0	0	0	0%	0%
Testing and Finishes		48.00	24-Apr-27	29-Apr-27	382,356	0	0	0	0%	0%
CO-TE-CTV-TF-180	Testing and Interface modules with Telecom for Alignment-RD-01	24.00	24-Apr-27	26-Apr-27	35,807	0	0	0	0%	0%
CO-TE-CTV-TF-310	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	24.00	27-Apr-27	29-Apr-27	346,549	0	0	0	0%	0%
Alignment-RD-02		1392.00	15-Nov-26	14-Jun-27	7,655,882	3,874,904	0	0	50.61%	0%
Earthworks		96.00	15-Nov-26	28-Nov-26	2,314,449	2,314,449	0	0	100%	0%

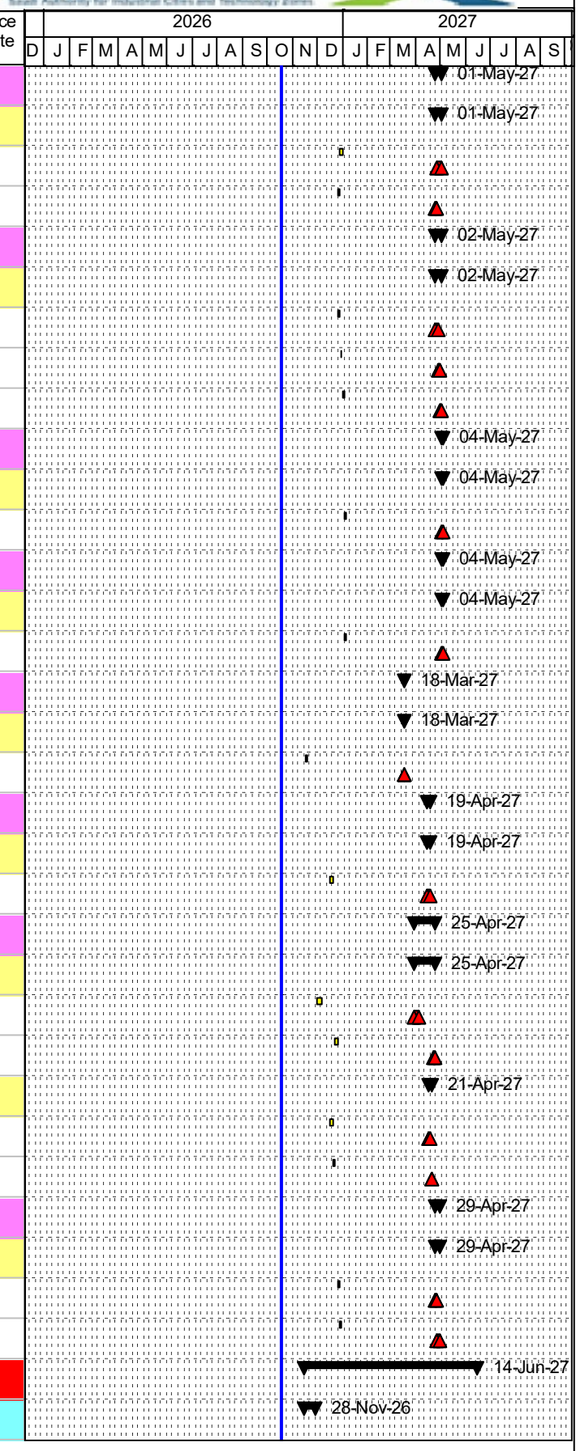


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Earthworks		96.00	15-Nov-26	28-Nov-26	2,314,449	2,314,449	0	0	100%	0%
CO-EW-220	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-02	96.00	15-Nov-26	28-Nov-26	2,314,449	2,314,449	0	0	100%	0%
Storm Drainage Network		744.00	29-Nov-26	20-Mar-27	1,062,822	1,028,976	0	0	96.82%	0%
Manholes		104.00	29-Nov-26	13-Dec-26	114,795	114,795	0	0	100%	0%
CO-SD-MH-270	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	32.00	29-Nov-26	02-Dec-26	7,653	7,653	0	0	100%	0%
CO-SD-MH-280	Install RC Footing Works for Manholes of Storm Drainage Network for Alignment-RD-02	24.00	03-Dec-26	06-Dec-26	38,265	38,265	0	0	100%	0%
CO-SD-MH-290	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	24.00	07-Dec-26	09-Dec-26	45,918	45,918	0	0	100%	0%
CO-SD-MH-300	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-02	24.00	10-Dec-26	13-Dec-26	22,959	22,959	0	0	100%	0%
Main Line Sections		72.00	10-Dec-26	20-Dec-26	744,950	744,950	0	0	100%	0%
CO-SD-ML-170	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	24.00	10-Dec-26	13-Dec-26	106,954	106,954	0	0	100%	0%
CO-SD-ML-180	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-02	24.00	14-Dec-26	16-Dec-26	451,755	451,755	0	0	100%	0%
CO-SD-ML-190	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	24.00	17-Dec-26	20-Dec-26	186,241	186,241	0	0	100%	0%
Catch Basin Sections		592.00	21-Dec-26	20-Mar-27	203,078	169,231	0	0	83.33%	0%
CO-SD-CB-210	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network for	144.00	21-Dec-26	10-Jan-27	50,769	50,769	0	0	100%	0%
CO-SD-CB-220	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	152.00	11-Jan-27	01-Feb-27	118,462	118,462	0	0	100%	0%
CO-SD-CB-230	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network for	40.00	15-Mar-27	20-Mar-27	33,846	0	0	0	0%	0%
Sewage Network		464.00	21-Dec-26	25-Feb-27	276,597	212,191	0	0	76.72%	0%
Manholes		464.00	21-Dec-26	25-Feb-27	94,811	75,849	0	0	80%	0%
CO-SW-MH-260	Excavation Works for Main Line Manholes of Sewage Network for Alignment-RD-02	88.00	21-Dec-26	02-Jan-27	6,321	6,321	0	0	100%	0%
CO-SW-MH-270	Installation RC Footing Works for Main Line Manholes of Sewage Network for	88.00	03-Jan-27	14-Jan-27	31,604	31,604	0	0	100%	0%
CO-SW-MH-280	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96.00	16-Jan-27	28-Jan-27	18,962	18,962	0	0	100%	0%
CO-SW-MH-290	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96.00	30-Jan-27	11-Feb-27	18,962	18,962	0	0	75%	0%
CO-SW-MH-300	Backfilling Works for Main Line Manholes of Sewage Network for Alignment-RD-02	96.00	13-Feb-27	25-Feb-27	18,962	0	0	0	0%	0%
Main Line Sections		464.00	21-Dec-26	25-Feb-27	181,786	136,343	0	0	75%	0%
CO-SW-ML-170	Trench Excavation and Bedding Works for Main Lines of Sewage Network for	88.00	21-Dec-26	02-Jan-27	28,571	28,571	0	0	100%	0%
CO-SW-ML-180	Pipes Laying Works for Main Lines of Sewage Network for Alignment-RD-02	88.00	03-Jan-27	14-Jan-27	107,771	107,771	0	0	100%	0%
CO-SW-ML-190	Trench Backfilling and Compaction Works for Main Lines of Sewage Network for	88.00	14-Feb-27	25-Feb-27	45,443	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		328.00	21-Dec-26	06-Feb-27	310,747	310,747	0	0	100%	0%
CO-TSE-ML-250	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	96.00	21-Dec-26	03-Jan-27	38,990	38,990	0	0	100%	0%
CO-TSE-ML-260	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-02	136.00	04-Jan-27	23-Jan-27	194,070	194,070	0	0	100%	0%
CO-TSE-ML-280	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	96.00	24-Jan-27	06-Feb-27	77,686	77,686	0	0	100%	0%
Potable Water Network		144.00	07-Feb-27	27-Feb-27	232,618	8,540	0	0	3.67%	0%
Main Line Sections		136.00	07-Feb-27	25-Feb-27	77,824	5,677	0	0	7.29%	0%
CO-PW-ML-170	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	40.00	07-Feb-27	11-Feb-27	14,191	5,677	0	0	40%	0%

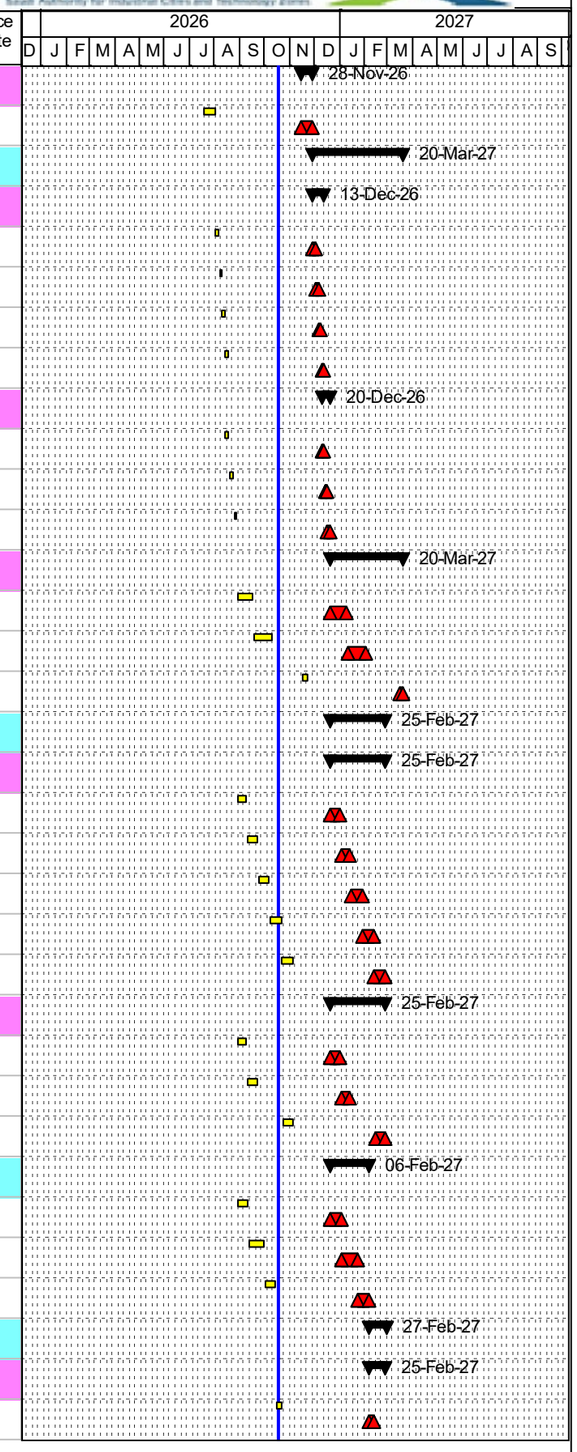

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-PW-ML-180	Pipes Laying and accessories for Main Lines of Potable Water Network for	56.00	13-Feb-27	20-Feb-27	35,342	0	0	0	0%	0%
CO-PW-ML-190	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	40.00	21-Feb-27	25-Feb-27	28,291	0	0	0	0%	0%
Valve Chamber		144.00	07-Feb-27	27-Feb-27	91,835	2,864	0	0	3.12%	0%
CO-PW-VC-260	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	40.00	07-Feb-27	11-Feb-27	5,740	2,864	0	0	40%	0%
CO-PW-VC-270	Installation Works for Valves of Potable Water Network for Alignment-RD-02	40.00	16-Feb-27	21-Feb-27	14,923	0	0	0	0%	0%
CO-PW-VC-280	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	40.00	22-Feb-27	27-Feb-27	11,479	0	0	0	0%	0%
CO-PW-VC200	Installation of Valve Chambers of Potable Water Network for Alignment-RD-02	24.00	13-Feb-27	15-Feb-27	59,693	0	0	0	0%	0%
Fire Hydrant		104.00	13-Feb-27	27-Feb-27	62,959	0	0	0	0%	0%
CO-PW-FH-200	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-02	24.00	13-Feb-27	15-Feb-27	3,935	0	0	0	0%	0%
CO-PW-FH-210	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-02	24.00	21-Feb-27	23-Feb-27	51,154	0	0	0	0%	0%
CO-PW-FH-220	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	24.00	24-Feb-27	27-Feb-27	7,870	0	0	0	0%	0%
Irrigation Network		144.00	14-Feb-27	06-Mar-27	267,506	0	0	0	0%	0%
Main Line Pipes		144.00	14-Feb-27	06-Mar-27	267,506	0	0	0	0%	0%
CO-IR-ML-200	Trench Excavation and Bedding Works for Main Lines of Irrigation Network for	24.00	14-Feb-27	16-Feb-27	6,922	0	0	0	0%	0%
CO-IR-ML-210	Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-02	24.00	21-Feb-27	23-Feb-27	34,609	0	0	0	0%	0%
CO-IR-ML-220	Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-02	24.00	24-Feb-27	27-Feb-27	9,941	0	0	0	0%	0%
CO-IR-ML-230	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for	24.00	03-Mar-27	06-Mar-27	13,844	0	0	0	0%	0%
CO-IR-ML-240	Installation Works for Bulbblers And Sprinkler and Irrigation Control System of Irrigation	24.00	28-Feb-27	02-Mar-27	202,191	0	0	0	0%	0%
Medium Voltage Network		96.00	21-Mar-27	03-Apr-27	28,138	0	0	0	0%	0%
Cabling Works		96.00	21-Mar-27	03-Apr-27	28,138	0	0	0	0%	0%
CO-MV-ML-310	Trench Excavation and Bedding Works for Medium Voltage Network for Alignment-RD-02	32.00	21-Mar-27	24-Mar-27	6,170	0	0	0	0%	0%
CO-MV-ML-320	Duct Laying Works for Medium Voltage Network for Alignment-RD-02	32.00	25-Mar-27	29-Mar-27	15,103	0	0	0	0%	0%
CO-MV-ML-330	Trench Backfilling and Compaction Works for Medium Voltage Network for Alignment-RD-02	32.00	30-Mar-27	03-Apr-27	6,865	0	0	0	0%	0%
Low Voltage Network		320.00	07-Mar-27	25-Apr-27	139,309	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		280.00	07-Mar-27	19-Apr-27	70,049	0	0	0	0%	0%
CON-LV-ML-160	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	40.00	04-Apr-27	08-Apr-27	13,675	0	0	0	0%	0%
CON-LV-ML-170	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-02	96.00	07-Mar-27	23-Mar-27	38,755	0	0	0	0%	0%
CON-LV-ML-180	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	72.00	10-Apr-27	19-Apr-27	17,619	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		112.00	10-Apr-27	25-Apr-27	63,213	0	0	0	0%	0%
CON-LV-HC-160	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	32.00	10-Apr-27	13-Apr-27	6,839	0	0	0	0%	0%
CON-LV-HC-170	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-02	48.00	14-Apr-27	20-Apr-27	38,755	0	0	0	0%	0%
CON-LV-HC-180	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	32.00	21-Apr-27	25-Apr-27	17,619	0	0	0	0%	0%
Distribution Pillars Works		112.00	04-Apr-27	19-Apr-27	6,047	0	0	0	0%	0%
CON-LV-DP-160	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	48.00	04-Apr-27	10-Apr-27	2,281	0	0	0	0%	0%

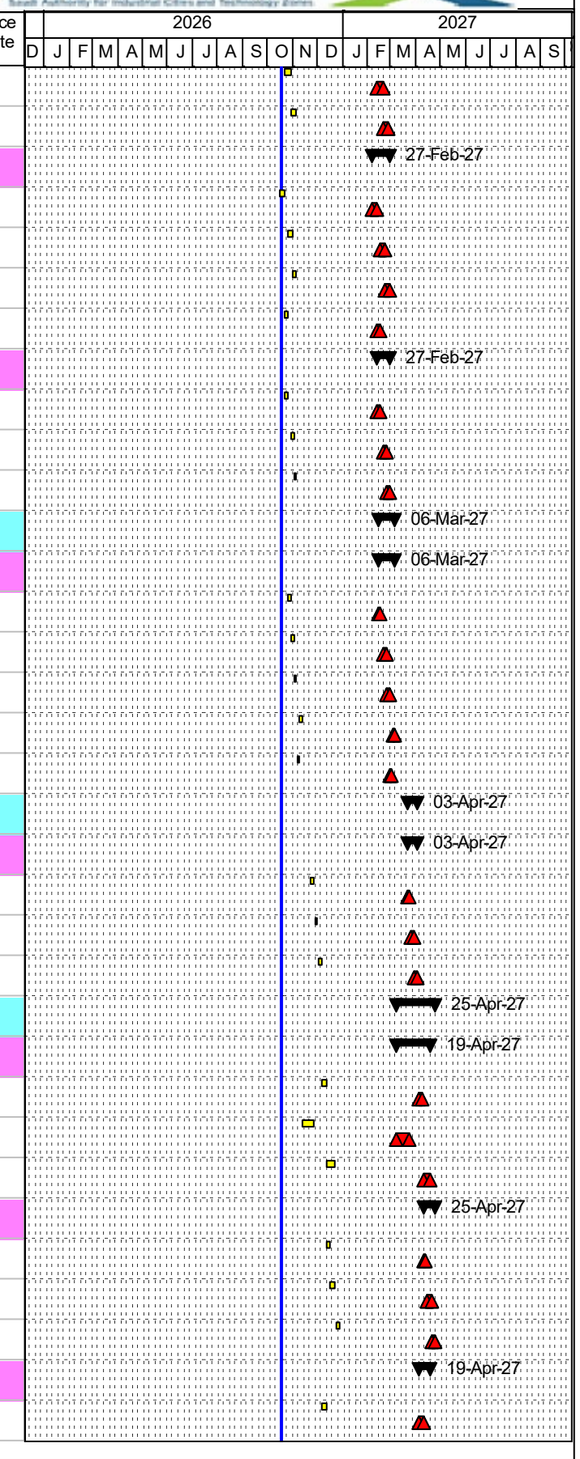

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CON-LV-DP-170	Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for	32.00	11-Apr-27	14-Apr-27	1,883	0	0	0	0%	0%
CON-LV-DP-180	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-02	32.00	15-Apr-27	19-Apr-27	1,883	0	0	0	0%	0%
Street Lighting Network		168.00	11-Apr-27	04-May-27	123,598	0	0	0	0%	0%
Lighting Poles Works		88.00	11-Apr-27	22-Apr-27	44,088	0	0	0	0%	0%
CO-SL-LP-400	Installation Works for Lighting Poles Foundation of Street Lighting Network for	32.00	11-Apr-27	14-Apr-27	9,458	0	0	0	0%	0%
CO-SL-LP-410	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-02	32.00	15-Apr-27	19-Apr-27	31,466	0	0	0	0%	0%
CO-SL-LP-430	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-02	24.00	20-Apr-27	22-Apr-27	3,165	0	0	0	0%	0%
Cabling Works		56.00	11-Apr-27	18-Apr-27	62,968	0	0	0	0%	0%
CO-SL-CL-320	Cable Laying Works for Street Lighting Network for Alignment-RD-02	32.00	11-Apr-27	14-Apr-27	34,631	0	0	0	0%	0%
CO-SL-CL-330	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-02	24.00	15-Apr-27	18-Apr-27	28,337	0	0	0	0%	0%
Distrubution Panel Boards		80.00	24-Apr-27	04-May-27	16,541	0	0	0	0%	0%
CO-SL-DB-330	Installation Works for Panel Board Concrete Foundations of Street Lighting Network for	24.00	24-Apr-27	26-Apr-27	3,545	0	0	0	0%	0%
CO-SL-DB-340	Installation Works for Lighting Panel Boards of Street Lighting Network for Alignment-RD-02	56.00	27-Apr-27	04-May-27	12,997	0	0	0	0%	0%
Telecom and Light Current Network		296.00	04-Apr-27	22-May-27	650,864	0	0	0	0%	0%
Ducts Works		80.00	05-May-27	22-May-27	116,180	0	0	0	0%	0%
CO-TE-DW-190	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-02	40.00	05-May-27	10-May-27	79,875	0	0	0	0%	0%
CO-TE-DW-200	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	40.00	11-May-27	22-May-27	36,306	0	0	0	0%	0%
Manholes Works		72.00	04-Apr-27	13-Apr-27	30,612	0	0	0	0%	0%
CO-TE-MH-200	Excavation Works for Manholes of Telecom Network for Alignment-RD-02	24.00	04-Apr-27	06-Apr-27	2,041	0	0	0	0%	0%
CO-TE-MH-210	Installation Works for Manholes of Telecom Network for Alignment-RD-02	24.00	07-Apr-27	10-Apr-27	22,449	0	0	0	0%	0%
CO-TE-MH-220	Backfilling Works for Manholes of Telecom Network for Alignment-RD-02	24.00	11-Apr-27	13-Apr-27	6,122	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		48.00	14-Apr-27	20-Apr-27	504,071	0	0	0	0%	0%
CO-TE-CTV-180	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-02	48.00	14-Apr-27	20-Apr-27	504,071	0	0	0	0%	0%
Road Works		208.00	26-Apr-27	31-May-27	1,365,735	0	0	0	0%	0%
Pavement Works		112.00	26-Apr-27	11-May-27	1,338,540	0	0	0	0%	0%
CO-RD-PV-200	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-02	40.00	26-Apr-27	01-May-27	131,137	0	0	0	0%	0%
CO-RD-PV-210	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-02	72.00	02-May-27	11-May-27	1,207,402	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		64.00	23-May-27	31-May-27	27,195	0	0	0	0%	0%
CO-RD-F-RM-200	Application of Road Marking Works For Road Works for Alignment-RD-02	32.00	23-May-27	26-May-27	17,728	0	0	0	0%	0%
CO-RD-F-TS-140	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-02	32.00	27-May-27	31-May-27	9,468	0	0	0	0%	0%
Finishes for Infrastructure Networks		456.00	04-Apr-27	14-Jun-27	883,500	0	0	0	0%	0%
Storm Drainage Network		240.00	05-May-27	14-Jun-27	359,891	0	0	0	0%	0%
Testing and Finishes		240.00	05-May-27	14-Jun-27	359,891	0	0	0	0%	0%
CO-SD-CB-TF-200	Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-02	48.00	30-May-27	05-Jun-27	33,846	0	0	0	0%	0%

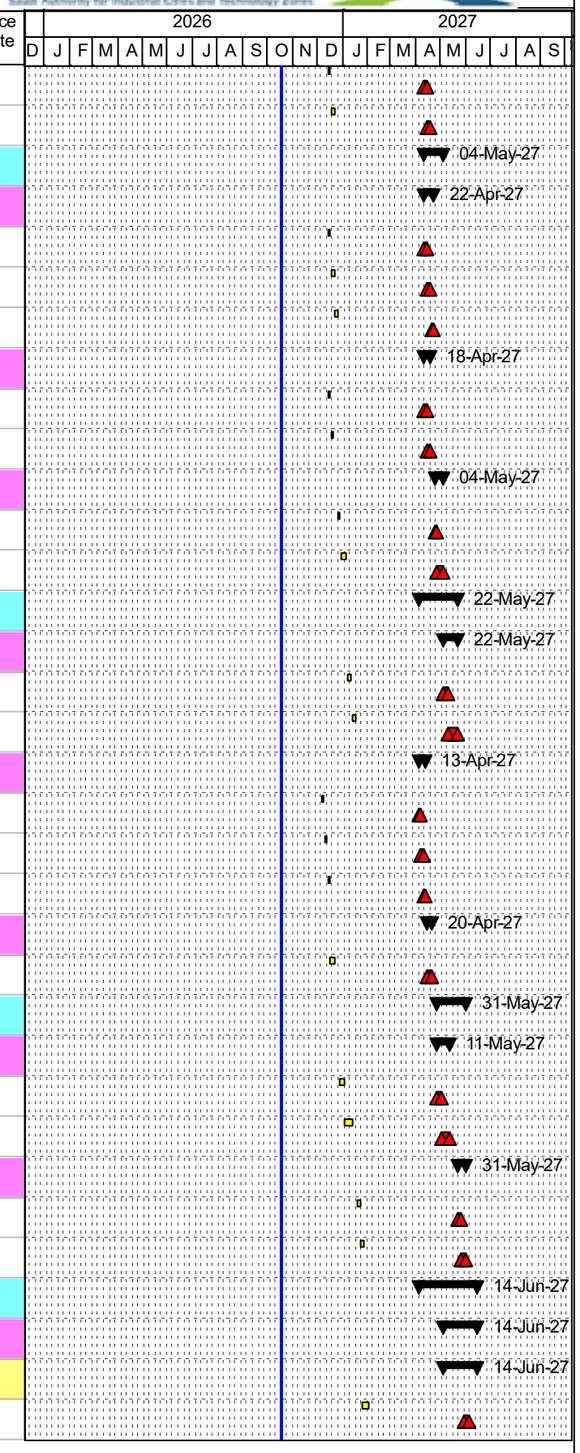

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SD-CB-TF-210	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network for	64.00	06-Jun-27	14-Jun-27	50,769	0	0	0	0%	0%
CO-SD-CB-TF-220	Catch Basin Internal Finishes (Benching) for Storm Drainage Network for Alignment-RD-02	48.00	23-May-27	29-May-27	50,769	0	0	0	0%	0%
CO-SD-MH-TF-250	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-02	48.00	23-May-27	29-May-27	38,265	0	0	0	0%	0%
CO-SD-ML-TF-120	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-02	48.00	05-May-27	11-May-27	186,241	0	0	0	0%	0%
Sewage Network		144.00	24-Apr-27	13-May-27	77,047	0	0	0	0%	0%
Testing and Finishes		144.00	24-Apr-27	13-May-27	77,047	0	0	0	0%	0%
CO-SW-TF-270	Final Testing For Main Line of Sewage Network for Alignment-RD-02	144.00	24-Apr-27	13-May-27	45,443	0	0	0	0%	0%
CO-SW-TF-290	Testing Works for Main Line Manholes of Sewage Network for Alignment-RD-02	144.00	24-Apr-27	13-May-27	31,604	0	0	0	0%	0%
Potable Water Network		240.00	20-Apr-27	30-May-27	102,331	0	0	0	0%	0%
Testing and Finishes		240.00	20-Apr-27	30-May-27	102,331	0	0	0	0%	0%
CO-PW-TF-160	Testing of Potable Water Network for Alignment-RD-02	64.00	22-May-27	30-May-27	28,291	0	0	0	0%	0%
CO-PW-TF-170	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	112.00	20-Apr-27	05-May-27	15,740	0	0	0	0%	0%
CO-PW-TF-180	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-02	64.00	06-May-27	20-May-27	58,301	0	0	0	0%	0%
Irrigation Network		32.00	02-May-27	05-May-27	13,844	0	0	0	0%	0%
Testing and Finishes		32.00	02-May-27	05-May-27	13,844	0	0	0	0%	0%
CO-IR-TF-180	Final Testing (pressure tests) of Irrigation Network for Alignment-RD-02	32.00	02-May-27	05-May-27	13,844	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		48.00	23-May-27	29-May-27	77,686	0	0	0	0%	0%
Testing and Finishes		48.00	23-May-27	29-May-27	77,686	0	0	0	0%	0%
CO-TSE-TF-190	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-02	48.00	23-May-27	29-May-27	77,686	0	0	0	0%	0%
Medium Voltage Network		48.00	04-Apr-27	10-Apr-27	5,492	0	0	0	0%	0%
Termination and Testing Works		48.00	04-Apr-27	10-Apr-27	5,492	0	0	0	0%	0%
CO-MV-TF-240	Testing and Termination Works of Medium Voltage Network for Alignment-RD-02	48.00	04-Apr-27	10-Apr-27	5,492	0	0	0	0%	0%
Low Voltage Network		64.00	25-Apr-27	03-May-27	29,795	0	0	0	0%	0%
Termination and Testing Works		64.00	25-Apr-27	03-May-27	29,257	0	0	0	0%	0%
CON-LV-TT-140	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	32.00	29-Apr-27	03-May-27	28,181	0	0	0	0%	0%
CON-LV-TT-150	Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for	32.00	25-Apr-27	28-Apr-27	1,076	0	0	0	0%	0%
Earthing System Works		16.00	29-Apr-27	01-May-27	538	0	0	0	0%	0%
CON-LV-ES-120	Earthing System Works for Distribution Pillars Units of Low Voltage Network for	16.00	29-Apr-27	01-May-27	538	0	0	0	0%	0%
Street Lighting Network		128.00	27-Apr-27	20-May-27	52,148	0	0	0	0%	0%
Termination and Testing Works		128.00	27-Apr-27	20-May-27	46,478	0	0	0	0%	0%
CO-SL-LP-420	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	16.00	27-Apr-27	28-Apr-27	20,510	0	0	0	0%	0%
CO-SL-TF-440	Termination Works For Panel Board Cables of Street Lighting Network for Alignment-RD-02	48.00	05-May-27	11-May-27	4,726	0	0	0	0%	0%
CO-SL-TF-450	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-02	16.00	13-May-27	20-May-27	18,880	0	0	0	0%	0%
CO-SL-TF-460	Testing Works For Panel Board Cables of Street Lighting Network for Alignment-RD-02	16.00	13-May-27	20-May-27	2,363	0	0	0	0%	0%

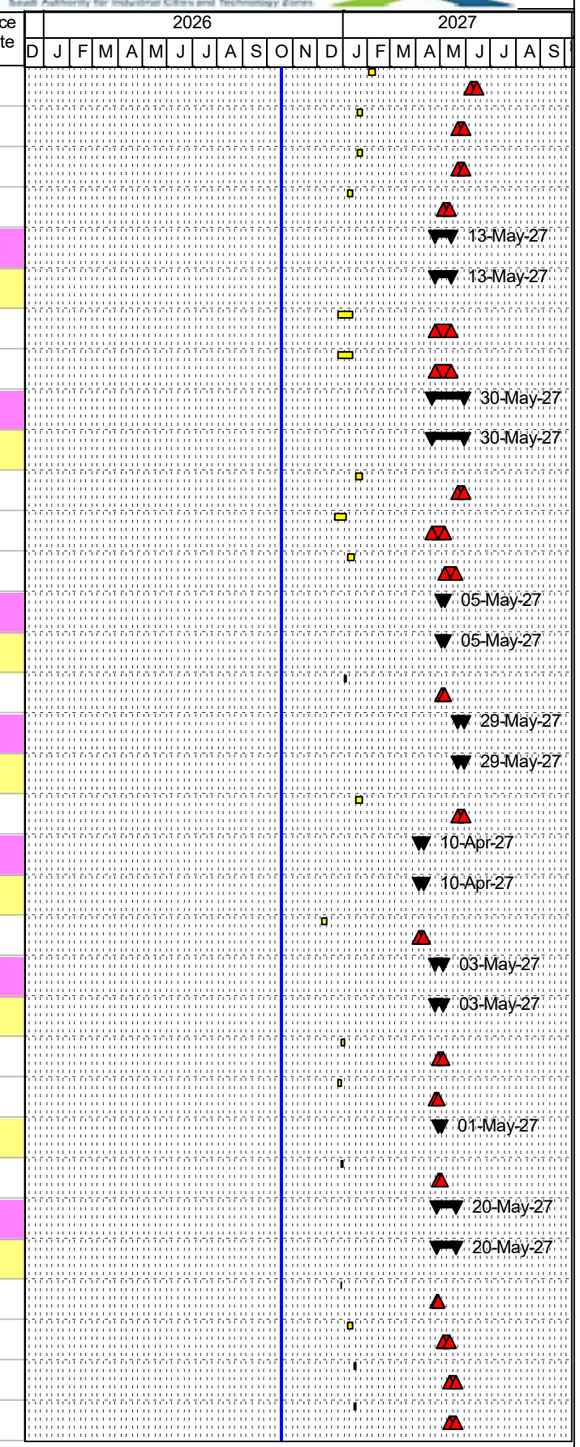

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Earthing System Works		96.00	29-Apr-27	12-May-27	5,669	0	0	0	0%	0%
CO-SL-ES-260	Install Earthing System Works for Lighting Poles of Street Lighting Network for	48.00	29-Apr-27	05-May-27	2,835	0	0	0	0%	0%
CO-SL-ES-270	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	48.00	06-May-27	12-May-27	2,835	0	0	0	0%	0%
Telecom and Light Current Network		48.00	29-Apr-27	05-May-27	165,267	0	0	0	0%	0%
Testing and Finishes		48.00	29-Apr-27	05-May-27	165,267	0	0	0	0%	0%
CO-TE-CTV-TF-220	Testing and Interface modules with Telecom for Alignment-RD-02	24.00	29-Apr-27	02-May-27	39,249	0	0	0	0%	0%
CO-TE-CTV-TF-350	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	24.00	03-May-27	05-May-27	126,018	0	0	0	0%	0%
Alignment-RD-03-1		1368.00	19-Oct-26	09-May-27	3,448,486	1,276,024	0	0	37%	0%
Earthworks		96.00	19-Oct-26	01-Nov-26	829,055	829,055	0	0	100%	0%
Earthworks		96.00	19-Oct-26	01-Nov-26	829,055	829,055	0	0	100%	0%
CO-EW-200	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-1	96.00	19-Oct-26	01-Nov-26	829,055	829,055	0	0	100%	0%
Storm Drainage Network		264.00	02-Nov-26	09-Dec-26	122,202	122,202	0	0	100%	0%
Manholes		264.00	02-Nov-26	09-Dec-26	48,644	48,644	0	0	100%	0%
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	80.00	02-Nov-26	12-Nov-26	3,243	3,243	0	0	100%	0%
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network for	24.00	14-Nov-26	16-Nov-26	16,215	16,215	0	0	100%	0%
CO-SD-MH-200	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	80.00	17-Nov-26	28-Nov-26	19,458	19,458	0	0	100%	0%
CO-SD-MH-220	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-03-1	80.00	29-Nov-26	09-Dec-26	9,729	9,729	0	0	100%	0%
Main Line Sections		80.00	29-Nov-26	09-Dec-26	73,558	73,558	0	0	100%	0%
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	24.00	29-Nov-26	01-Dec-26	9,196	9,196	0	0	100%	0%
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-1	24.00	02-Dec-26	05-Dec-26	45,975	45,975	0	0	100%	0%
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	32.00	06-Dec-26	09-Dec-26	18,387	18,387	0	0	100%	0%
Treated Sewage Effluent (Tse)		952.00	17-Dec-26	08-May-27	880,133	273,530	0	0	31.08%	0%
CO-TSE-ML-150	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	32.00	17-Dec-26	21-Dec-26	4,681	4,681	0	0	100%	0%
CO-TSE-ML-160	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-03-1	32.00	22-Dec-26	26-Dec-26	21,975	21,975	0	0	100%	0%
CO-TSE-ML-170	Installation Works for Main Line Valves of Treated Sewage Effluent (Tse) for	48.00	27-Dec-26	02-Jan-27	11,899	11,899	0	0	100%	0%
CO-TSE-ML-180	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	40.00	10-Jan-27	14-Jan-27	8,884	8,884	0	0	100%	0%
CO-TSE-ML-190	Installation Works for Valve and Washout Chambers of Treated Sewage Effluent (Tse)	48.00	03-Jan-27	09-Jan-27	226,089	226,089	0	0	100%	0%
Treated Sewage Effluent (Tse) Storage Tank		48.00	02-May-27	08-May-27	606,604	0	0	0	0%	0%
CO-TSE-TF-180	Installation of Storage Tank of Treated Sewage Effluent (Tse) for Alignment-RD-03-1	48.00	02-May-27	08-May-27	606,604	0	0	0	0%	0%
Potable Water Network		704.00	16-Jan-27	01-May-27	671,455	51,237	0	0	7.63%	0%
Main Line Sections		136.00	16-Jan-27	03-Feb-27	15,148	14,361	0	0	94.81%	0%
CO-PW-ML-100	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	40.00	16-Jan-27	20-Jan-27	2,765	2,765	0	0	100%	0%
CO-PW-ML-110	Pipes Laying and accessories for Main Lines of Potable Water Network for	40.00	21-Jan-27	26-Jan-27	6,878	6,878	0	0	100%	0%
CO-PW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	56.00	27-Jan-27	03-Feb-27	5,505	4,719	0	0	85.71%	0%

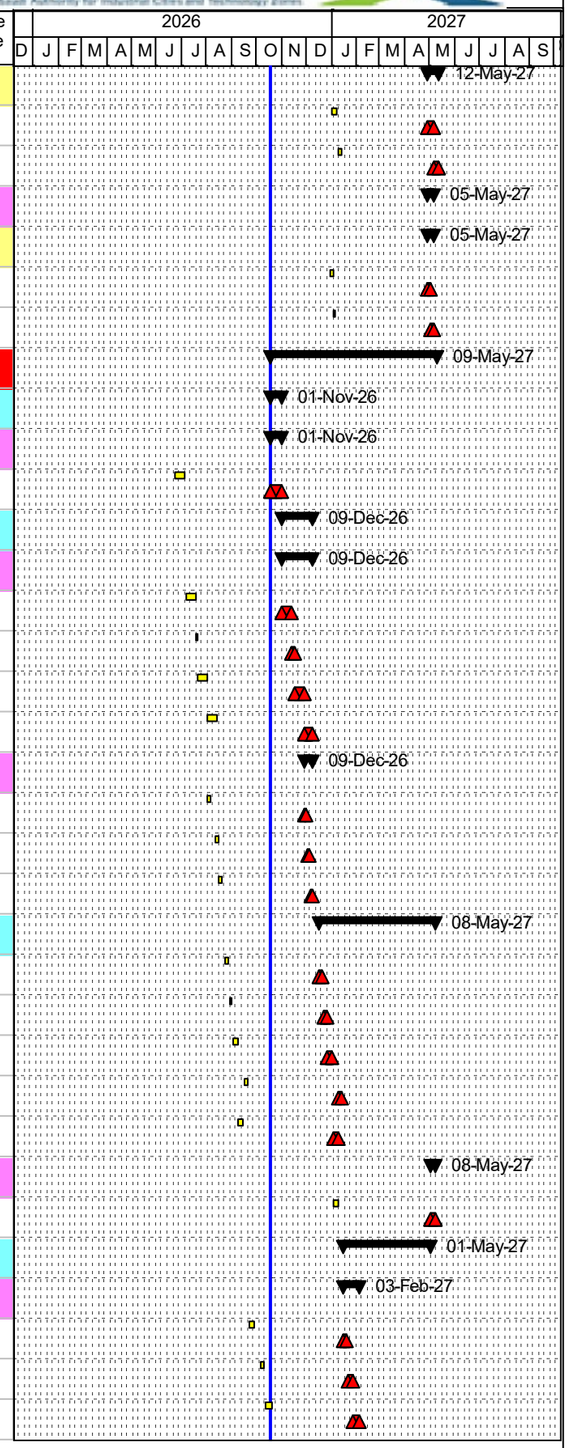

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Valve Chamber		136.00	18-Jan-27	06-Feb-27	40,710	29,006	0	0	71.25%	0%
CO-PW-VC-170	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	24.00	18-Jan-27	20-Jan-27	2,544	2,544	0	0	100%	0%
CO-PW-VC-190	Installation Works for Valves of Potable Water Network for Alignment-RD-03-1	24.00	31-Jan-27	02-Feb-27	6,615	0	0	0	0%	0%
CO-PW-VC-220	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	24.00	03-Feb-27	06-Feb-27	5,089	0	0	0	0%	0%
CO-PW-VC180	Installation of Valve Chambers of Potable Water Network for Alignment-RD-03-1	24.00	21-Jan-27	24-Jan-27	26,462	26,462	0	0	100%	0%
Fire Hydrant		112.00	21-Jan-27	06-Feb-27	8,994	7,870	0	0	87.5%	0%
CO-PW-FH-140	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-03-1	16.00	21-Jan-27	23-Jan-27	562	562	0	0	100%	0%
CO-PW-FH-150	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-03-1	16.00	27-Jan-27	28-Jan-27	7,308	7,308	0	0	100%	0%
CO-PW-FH-160	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	16.00	04-Feb-27	06-Feb-27	1,124	0	0	0	0%	0%
Potable Water Network Storage Tank		48.00	25-Apr-27	01-May-27	606,604	0	0	0	0%	0%
CO-PW-TF-130	Installation of Storage Tank of Potable Water Network for Alignment-RD-03-1	48.00	25-Apr-27	01-May-27	606,604	0	0	0	0%	0%
Low Voltage Network		376.00	04-Feb-27	03-Apr-27	38,649	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		152.00	04-Feb-27	25-Feb-27	18,678	0	0	0	0%	0%
CON-LV-ML-100	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	64.00	04-Feb-27	13-Feb-27	3,648	0	0	0	0%	0%
CON-LV-ML-110	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-1	56.00	14-Feb-27	21-Feb-27	10,333	0	0	0	0%	0%
CON-LV-ML-120	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	32.00	22-Feb-27	25-Feb-27	4,697	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		216.00	14-Feb-27	20-Mar-27	16,853	0	0	0	0%	0%
CON-LV-HC-100	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	32.00	14-Feb-27	17-Feb-27	1,823	0	0	0	0%	0%
CON-LV-HC-110	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-1	56.00	06-Mar-27	16-Mar-27	10,333	0	0	0	0%	0%
CON-LV-HC-120	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	24.00	17-Mar-27	20-Mar-27	4,697	0	0	0	0%	0%
Distribution Pillars Works		96.00	21-Mar-27	03-Apr-27	3,119	0	0	0	0%	0%
CON-LV-DP-100	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	32.00	21-Mar-27	24-Mar-27	608	0	0	0	0%	0%
CON-LV-DP-110	Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for	32.00	25-Mar-27	29-Mar-27	1,255	0	0	0	0%	0%
CON-LV-DP-120	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-1	32.00	30-Mar-27	03-Apr-27	1,255	0	0	0	0%	0%
Street Lighting Network		160.00	06-Mar-27	31-Mar-27	24,454	0	0	0	0%	0%
Lighting Poles Works		128.00	06-Mar-27	27-Mar-27	10,069	0	0	0	0%	0%
CO-SL-LP-550	Installation Works for Lighting Poles Foundation of Street Lighting Network for	40.00	06-Mar-27	14-Mar-27	2,158	0	0	0	0%	0%
CO-SL-LP-560	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1	40.00	15-Mar-27	20-Mar-27	7,192	0	0	0	0%	0%
CO-SL-LP-570	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1	48.00	21-Mar-27	27-Mar-27	719	0	0	0	0%	0%
Cabling Works		80.00	21-Mar-27	31-Mar-27	14,384	0	0	0	0%	0%
CO-SL-CL-410	Cable Laying Works for Street Lighting Network for Alignment-RD-03-1	40.00	21-Mar-27	25-Mar-27	7,911	0	0	0	0%	0%
CO-SL-CL-420	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-1	40.00	27-Mar-27	31-Mar-27	6,473	0	0	0	0%	0%
Telecom and Light Current Network		96.00	28-Mar-27	10-Apr-27	234,558	0	0	0	0%	0%
Ducts Works		64.00	01-Apr-27	10-Apr-27	30,845	0	0	0	0%	0%

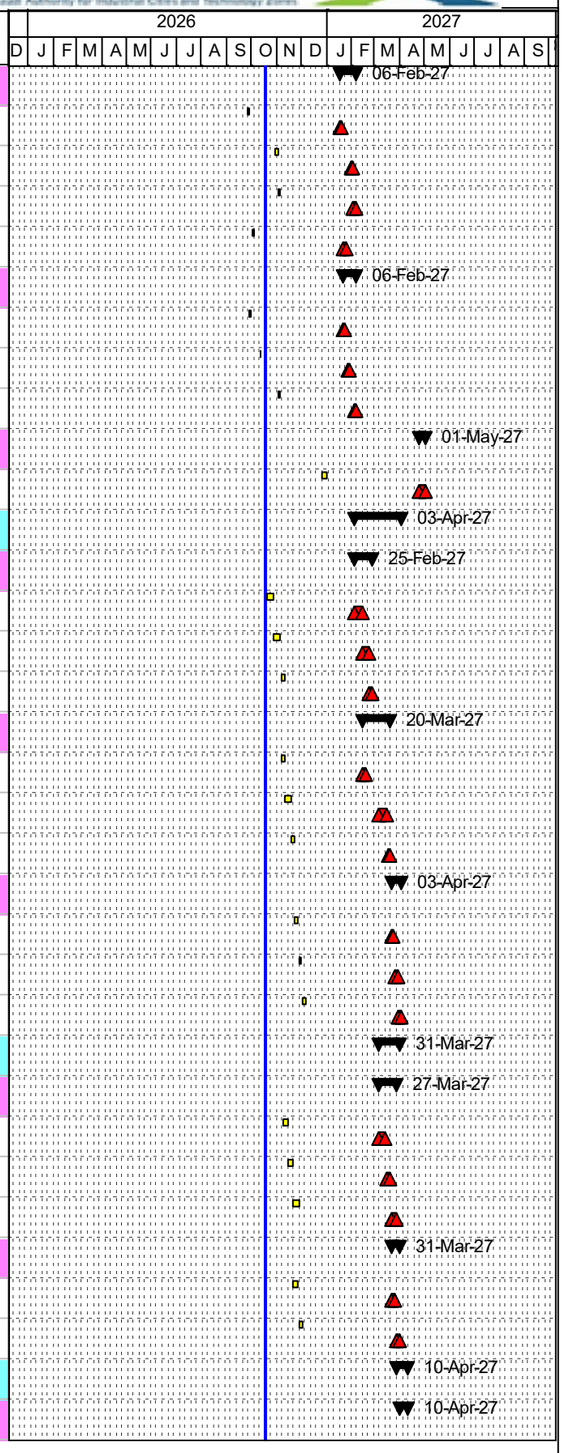

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-TE-DW-110	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-03-1	32.00	01-Apr-27	05-Apr-27	21,205	0	0	0	0%	0%
CO-TE-DW-130	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	32.00	06-Apr-27	10-Apr-27	9,640	0	0	0	0%	0%
Manholes Works		48.00	28-Mar-27	03-Apr-27	14,687	0	0	0	0%	0%
CO-TE-MH-140	Excavation Works for Manholes of Telecom Network for Alignment-RD-03-1	16.00	28-Mar-27	29-Mar-27	979	0	0	0	0%	0%
CO-TE-MH-150	Installation Works for Manholes of Telecom Network for Alignment-RD-03-1	16.00	30-Mar-27	31-Mar-27	10,770	0	0	0	0%	0%
CO-TE-MH-160	Backfilling Works for Manholes of Telecom Network for Alignment-RD-03-1	16.00	01-Apr-27	03-Apr-27	2,937	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		32.00	04-Apr-27	07-Apr-27	189,027	0	0	0	0%	0%
CO-TE-CTV-110	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-1	32.00	04-Apr-27	07-Apr-27	189,027	0	0	0	0%	0%
Road Works		176.00	11-Apr-27	05-May-27	499,484	0	0	0	0%	0%
Pre-Bituminous Construction		112.00	11-Apr-27	26-Apr-27	134,372	0	0	0	0%	0%
CO-RD-PB-140	Subgrade Layer for Road Works for Alignment-RD-03-1	56.00	11-Apr-27	18-Apr-27	65,548	0	0	0	0%	0%
CO-RD-PB-150	Aggregate Base Course Layer for Road Works for Alignment-RD-03-1	56.00	19-Apr-27	26-Apr-27	68,824	0	0	0	0%	0%
Bituminous Construction		56.00	19-Apr-27	26-Apr-27	278,096	0	0	0	0%	0%
CO-RD-B-160	Bituminous Base Courses Layers for Road Works for Alignment-RD-03-1	16.00	19-Apr-27	20-Apr-27	138,392	0	0	0	0%	0%
CON-RD-MR-150	Preparation of Asphaltic Wearing Course Layer for Roads Network for	16.00	25-Apr-27	26-Apr-27	139,704	0	0	0	0%	0%
Pavement Works		104.00	21-Apr-27	05-May-27	75,922	0	0	0	0%	0%
CO-RD-PV-160	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-1	40.00	21-Apr-27	26-Apr-27	46,267	0	0	0	0%	0%
CO-RD-PV-170	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-1	64.00	27-Apr-27	05-May-27	29,656	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		32.00	27-Apr-27	01-May-27	11,093	0	0	0	0%	0%
CO-RD-F-RM-180	Application of Road Marking Works For Road Works for Alignment-RD-03-1	16.00	27-Apr-27	28-Apr-27	6,360	0	0	0	0%	0%
CO-RD-F-TS-120	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-1	16.00	29-Apr-27	01-May-27	4,734	0	0	0	0%	0%
Finishes for Infrastructure Networks		248.00	04-Apr-27	09-May-27	148,496	0	0	0	0%	0%
Storm Drainage Network		48.00	24-Apr-27	29-Apr-27	34,602	0	0	0	0%	0%
Testing and Finishes		48.00	24-Apr-27	29-Apr-27	34,602	0	0	0	0%	0%
CO-SD-MH-TF-210	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-03-1	24.00	27-Apr-27	29-Apr-27	16,215	0	0	0	0%	0%
CO-SD-ML-TF-100	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-03-1	24.00	24-Apr-27	26-Apr-27	18,387	0	0	0	0%	0%
Potable Water Network		32.00	20-Apr-27	24-Apr-27	24,809	0	0	0	0%	0%
Testing and Finishes		32.00	20-Apr-27	24-Apr-27	24,809	0	0	0	0%	0%
CO-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-03-1	32.00	20-Apr-27	24-Apr-27	17,055	0	0	0	0%	0%
CO-PW-TF-110	Testing of Potable Water Network for Alignment-RD-03-1	16.00	20-Apr-27	21-Apr-27	5,505	0	0	0	0%	0%
CO-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	24.00	20-Apr-27	22-Apr-27	2,249	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		8.00	09-May-27	09-May-27	8,884	0	0	0	0%	0%
Testing and Finishes		8.00	09-May-27	09-May-27	8,884	0	0	0	0%	0%
CO-TSE-TF-170	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-03-1	8.00	09-May-27	09-May-27	8,884	0	0	0	0%	0%

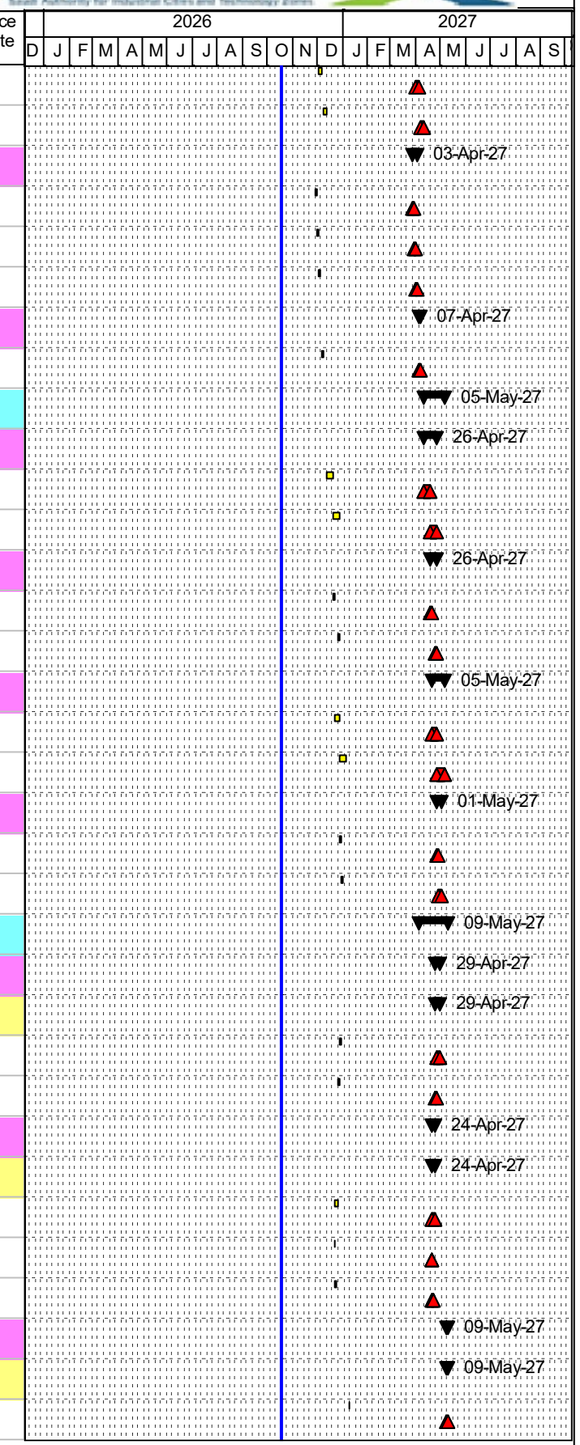

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Low Voltage Network		32.00	04-Apr-27	07-Apr-27	8,591	0	0	0	0%	0%
Termination and Testing Works		32.00	04-Apr-27	07-Apr-27	8,232	0	0	0	0%	0%
CON-LV-TT-100	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	16.00	06-Apr-27	07-Apr-27	7,515	0	0	0	0%	0%
CON-LV-TT-110	Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for	16.00	04-Apr-27	05-Apr-27	717	0	0	0	0%	0%
Earthing System Works		16.00	06-Apr-27	07-Apr-27	359	0	0	0	0%	0%
CON-LV-ES-100	Earthing System Works for Distribution Pillars Units of Low Voltage Network for	16.00	06-Apr-27	07-Apr-27	359	0	0	0	0%	0%
Street Lighting Network		136.00	13-Apr-27	02-May-27	10,034	0	0	0	0%	0%
Termination and Testing Works		136.00	13-Apr-27	02-May-27	9,003	0	0	0	0%	0%
CO-SL-LP-580	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48.00	13-Apr-27	19-Apr-27	4,688	0	0	0	0%	0%
CO-SL-TF-570	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1	48.00	26-Apr-27	02-May-27	4,315	0	0	0	0%	0%
Earthing System Works		40.00	20-Apr-27	25-Apr-27	1,031	0	0	0	0%	0%
CO-SL-ES-320	Install Earthing System Works for Lighting Poles of Street Lighting Network for	24.00	20-Apr-27	22-Apr-27	515	0	0	0	0%	0%
CO-SL-ES-330	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	16.00	24-Apr-27	25-Apr-27	515	0	0	0	0%	0%
Telecom and Light Current Network		48.00	08-Apr-27	14-Apr-27	61,576	0	0	0	0%	0%
Testing and Finishes		48.00	08-Apr-27	14-Apr-27	61,576	0	0	0	0%	0%
CO-TE-CTV-TF-140	Testing and Interface modules with Telecom for Alignment-RD-03-1	48.00	08-Apr-27	14-Apr-27	12,607	0	0	0	0%	0%
CO-TE-CTV-TF-330	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	48.00	08-Apr-27	14-Apr-27	48,969	0	0	0	0%	0%
Alignment-RD-03-2		1536.00	21-Oct-26	10-Jun-27	3,959,670	2,215,741	0	0	55.96%	0%
Earthworks		96.00	21-Oct-26	03-Nov-26	1,830,833	1,830,833	0	0	100%	0%
Earthworks		96.00	21-Oct-26	03-Nov-26	1,830,833	1,830,833	0	0	100%	0%
CO-EW-240	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-2	96.00	21-Oct-26	03-Nov-26	1,830,833	1,830,833	0	0	100%	0%
Storm Drainage Network		376.00	10-Dec-26	02-Feb-27	384,908	384,908	0	0	100%	0%
Manholes		288.00	10-Dec-26	20-Jan-27	163,658	163,658	0	0	100%	0%
CO-SD-MH-350	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	80.00	10-Dec-26	21-Dec-26	10,911	10,911	0	0	100%	0%
CO-SD-MH-360	Install RC Footing Works for Manholes of Storm Drainage Network for	72.00	22-Dec-26	31-Dec-26	54,553	54,553	0	0	100%	0%
CO-SD-MH-370	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	80.00	02-Jan-27	12-Jan-27	65,463	65,463	0	0	100%	0%
CO-SD-MH-380	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-03-2	56.00	13-Jan-27	20-Jan-27	32,732	32,732	0	0	100%	0%
Main Line Sections		144.00	13-Jan-27	02-Feb-27	221,251	221,251	0	0	100%	0%
CO-SD-ML-230	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	56.00	13-Jan-27	20-Jan-27	39,655	39,655	0	0	100%	0%
CO-SD-ML-240	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-2	40.00	21-Jan-27	26-Jan-27	126,283	126,283	0	0	100%	0%
CO-SD-ML-250	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	48.00	27-Jan-27	02-Feb-27	55,313	55,313	0	0	100%	0%
Medium Voltage Network		128.00	28-Feb-27	21-Mar-27	25,481	0	0	0	0%	0%
Cabling Works		128.00	28-Feb-27	21-Mar-27	25,481	0	0	0	0%	0%
CO-MV-ML-370	Trench Excavation and Bedding Works for Medium Voltage Network for	40.00	28-Feb-27	04-Mar-27	5,553	0	0	0	0%	0%

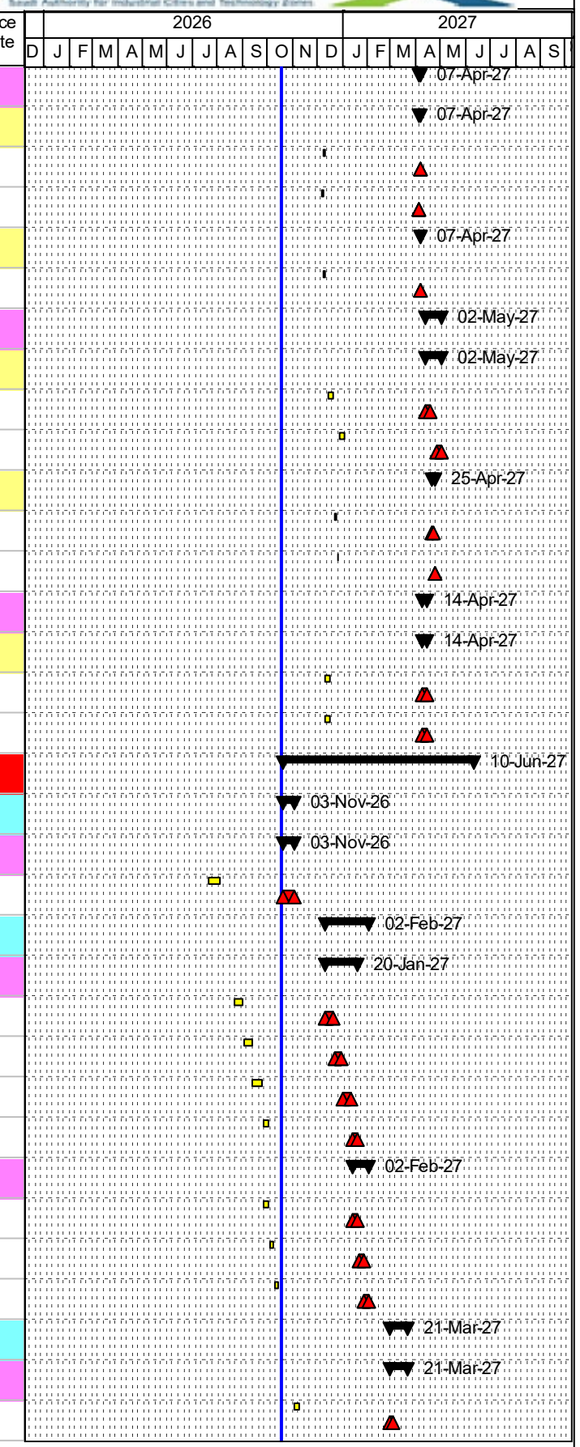

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-MV-ML-380	Duct Laying Works for Medium Voltage Network for Alignment-RD-03-2	40.00	07-Mar-27	15-Mar-27	13,701	0	0	0	0%	0%
CO-MV-ML-390	Trench Backfilling and Compaction Works for Medium Voltage Network for	32.00	17-Mar-27	21-Mar-27	6,228	0	0	0	0%	0%
Low Voltage Network		240.00	24-Mar-27	27-Apr-27	82,593	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		168.00	24-Mar-27	17-Apr-27	42,036	0	0	0	0%	0%
CON-LV-ML-220	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	48.00	24-Mar-27	30-Mar-27	8,206	0	0	0	0%	0%
CON-LV-ML-230	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-2	72.00	31-Mar-27	10-Apr-27	23,255	0	0	0	0%	0%
CON-LV-ML-240	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	48.00	11-Apr-27	17-Apr-27	10,574	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		192.00	31-Mar-27	27-Apr-27	37,933	0	0	0	0%	0%
CON-LV-HC-220	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	40.00	31-Mar-27	05-Apr-27	4,104	0	0	0	0%	0%
CON-LV-HC-230	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-2	72.00	11-Apr-27	20-Apr-27	23,255	0	0	0	0%	0%
CON-LV-HC-240	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	48.00	21-Apr-27	27-Apr-27	10,574	0	0	0	0%	0%
Distribution Pillars Works		88.00	01-Apr-27	13-Apr-27	2,624	0	0	0	0%	0%
CON-LV-DP-220	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	56.00	01-Apr-27	08-Apr-27	1,369	0	0	0	0%	0%
CON-LV-DP-230	Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for	16.00	10-Apr-27	11-Apr-27	628	0	0	0	0%	0%
CON-LV-DP-240	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-2	16.00	12-Apr-27	13-Apr-27	628	0	0	0	0%	0%
Street Lighting Network		168.00	06-Mar-27	01-Apr-27	55,021	0	0	0	0%	0%
Lighting Poles Works		128.00	06-Mar-27	27-Mar-27	22,656	0	0	0	0%	0%
CO-SL-LP-500	Installation Works for Lighting Poles Foundation of Street Lighting Network for	40.00	06-Mar-27	14-Mar-27	4,855	0	0	0	0%	0%
CO-SL-LP-510	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2	40.00	15-Mar-27	20-Mar-27	16,183	0	0	0	0%	0%
CO-SL-LP-520	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2	48.00	21-Mar-27	27-Mar-27	1,618	0	0	0	0%	0%
Cabling Works		80.00	22-Mar-27	01-Apr-27	32,365	0	0	0	0%	0%
CO-SL-CL-380	Cable Laying Works for Street Lighting Network for Alignment-RD-03-2	40.00	22-Mar-27	27-Mar-27	17,801	0	0	0	0%	0%
CO-SL-CL-390	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-2	40.00	28-Mar-27	01-Apr-27	14,564	0	0	0	0%	0%
Telecom and Light Current Network		24.00	28-Apr-27	01-May-27	252,036	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		24.00	28-Apr-27	01-May-27	252,036	0	0	0	0%	0%
CO-TE-CTV-240	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-2	24.00	28-Apr-27	01-May-27	252,036	0	0	0	0%	0%
Road Works		264.00	28-Apr-27	10-Jun-27	1,110,832	0	0	0	0%	0%
Pre-Bituminous Construction		80.00	28-Apr-27	09-May-27	299,699	0	0	0	0%	0%
CO-RD-PB-220	Subgrade Layer for Road Works for Alignment-RD-03-2	40.00	28-Apr-27	03-May-27	146,196	0	0	0	0%	0%
CO-RD-PB-230	Installation of Aggregate Base Course Layer and Interlock Works for Road Works for	40.00	04-May-27	09-May-27	153,503	0	0	0	0%	0%
Bituminous Construction		120.00	10-May-27	01-Jun-27	620,266	0	0	0	0%	0%
CO-RD-B-240	Bituminous Base Courses Layers for Road Works for Alignment-RD-03-2	24.00	10-May-27	12-May-27	308,669	0	0	0	0%	0%
CON-RD-MR-230	Preparation of Asphaltic Wearing Course Layer for Roads Network for	24.00	30-May-27	01-Jun-27	311,597	0	0	0	0%	0%
Pavement Works		112.00	13-May-27	03-Jun-27	169,336	0	0	0	0%	0%

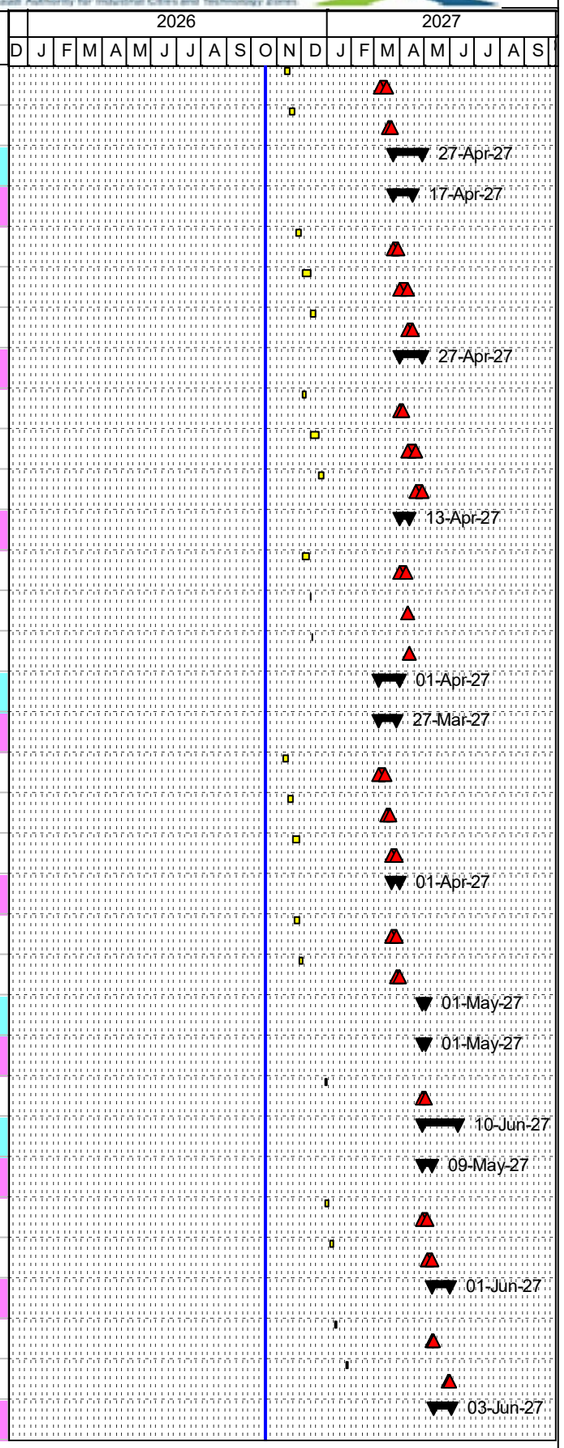

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-RD-PV-240	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-2	56.00	13-May-27	26-May-27	103,193	0	0	0	0%	0%
CO-RD-PV-250	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-2	56.00	27-May-27	03-Jun-27	66,143	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		48.00	05-Jun-27	10-Jun-27	21,532	0	0	0	0%	0%
CO-RD-F-RM-220	Application of Road Marking Works For Road Works for Alignment-RD-03-2	24.00	05-Jun-27	07-Jun-27	13,958	0	0	0	0%	0%
CO-RD-F-TS-160	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-2	24.00	08-Jun-27	10-Jun-27	7,574	0	0	0	0%	0%
Finishes for Infrastructure Networks		432.00	22-Mar-27	29-May-27	217,965	0	0	0	0%	0%
Storm Drainage Network		128.00	05-May-27	29-May-27	109,865	0	0	0	0%	0%
Testing and Finishes		128.00	05-May-27	29-May-27	109,865	0	0	0	0%	0%
CO-SD-CB-TF-260	Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-03-2	72.00	13-May-27	29-May-27	55,313	0	0	0	0%	0%
CO-SD-MH-TF-290	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-03-2	48.00	05-May-27	11-May-27	54,553	0	0	0	0%	0%
Medium Voltage Network		48.00	22-Mar-27	28-Mar-27	4,982	0	0	0	0%	0%
Termination and Testing Works		48.00	22-Mar-27	28-Mar-27	4,982	0	0	0	0%	0%
CO-MV-TF-260	Testing and Termination Works of Medium Voltage Network for Alignment-RD-03-2	48.00	22-Mar-27	28-Mar-27	4,982	0	0	0	0%	0%
Low Voltage Network		152.00	14-Apr-27	05-May-27	17,446	0	0	0	0%	0%
Termination and Testing Works		152.00	14-Apr-27	05-May-27	17,267	0	0	0	0%	0%
CON-LV-TT-180	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	56.00	28-Apr-27	05-May-27	16,908	0	0	0	0%	0%
CON-LV-TT-190	Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for	48.00	14-Apr-27	20-Apr-27	359	0	0	0	0%	0%
Earthing System Works		16.00	21-Apr-27	22-Apr-27	179	0	0	0	0%	0%
CON-LV-ES-140	Earthing System Works for Distribution Pillars Units of Low Voltage Network for	16.00	21-Apr-27	22-Apr-27	179	0	0	0	0%	0%
Street Lighting Network		120.00	06-Apr-27	22-Apr-27	22,662	0	0	0	0%	0%
Termination and Testing Works		120.00	06-Apr-27	22-Apr-27	20,257	0	0	0	0%	0%
CO-SL-LP-530	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48.00	06-Apr-27	12-Apr-27	10,548	0	0	0	0%	0%
CO-SL-TF-530	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2	48.00	17-Apr-27	22-Apr-27	9,710	0	0	0	0%	0%
Earthing System Works		40.00	17-Apr-27	21-Apr-27	2,405	0	0	0	0%	0%
CO-SL-ES-300	Install Earthing System Works for Lighting Poles of Street Lighting Network for	24.00	17-Apr-27	19-Apr-27	1,203	0	0	0	0%	0%
CO-SL-ES-310	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	16.00	20-Apr-27	21-Apr-27	1,203	0	0	0	0%	0%
Telecom and Light Current Network		32.00	02-May-27	05-May-27	63,009	0	0	0	0%	0%
Testing and Finishes		32.00	02-May-27	05-May-27	63,009	0	0	0	0%	0%
CO-TE-CTV-TF-320	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	32.00	02-May-27	05-May-27	63,009	0	0	0	0%	0%
Alignment-RD-03-3		1320.00	02-Nov-26	22-May-27	2,245,578	1,094,256	0	0	48.73%	0%
Earthworks		88.00	02-Nov-26	14-Nov-26	1,036,317	1,036,317	0	0	100%	0%
Earthworks		88.00	02-Nov-26	14-Nov-26	1,036,317	1,036,317	0	0	100%	0%
CO-EW-230	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-3	88.00	02-Nov-26	14-Nov-26	1,036,317	1,036,317	0	0	100%	0%
Storm Drainage Network		80.00	02-Dec-26	13-Dec-26	38,627	38,627	0	0	100%	0%

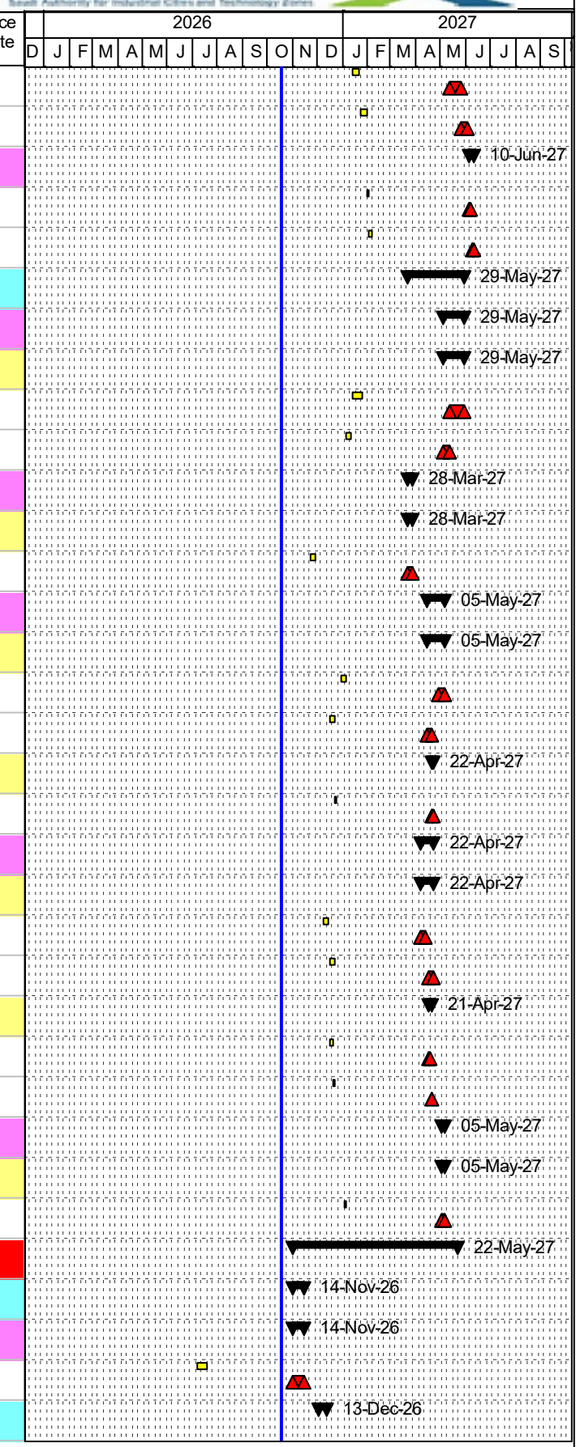


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Main Line Sections		80.00	02-Dec-26	13-Dec-26	38,627	38,627	0	0	100%	0%
CO-SD-ML-200	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	24.00	02-Dec-26	05-Dec-26	4,830	4,830	0	0	100%	0%
CO-SD-ML-210	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-3	24.00	06-Dec-26	08-Dec-26	24,141	24,141	0	0	100%	0%
CO-SD-ML-220	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	24.00	10-Dec-26	13-Dec-26	9,656	9,656	0	0	100%	0%
Treated Sewage Effluent (Tse)		264.00	14-Dec-26	20-Jan-27	6,040	6,040	0	0	100%	0%
CO-TSE-ML-300	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	88.00	14-Dec-26	26-Dec-26	755	755	0	0	100%	0%
CO-TSE-ML-310	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-03-3	88.00	27-Dec-26	07-Jan-27	3,775	3,775	0	0	100%	0%
CO-TSE-ML-330	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	88.00	09-Jan-27	20-Jan-27	1,510	1,510	0	0	100%	0%
Potable Water Network		256.00	21-Jan-27	27-Feb-27	53,061	12,581	0	0	23.71%	0%
Main Line Sections		240.00	21-Jan-27	24-Feb-27	17,558	5,586	0	0	31.81%	0%
CO-PW-ML-200	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	80.00	21-Jan-27	01-Feb-27	3,191	3,191	0	0	100%	0%
CO-PW-ML-210	Pipes Laying and accessories for Main Lines of Potable Water Network for	80.00	02-Feb-27	13-Feb-27	7,981	2,394	0	0	30%	0%
CO-PW-ML-220	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	80.00	14-Feb-27	24-Feb-27	6,386	0	0	0	0%	0%
Valve Chamber		256.00	21-Jan-27	27-Feb-27	26,509	6,826	0	0	25.75%	0%
CO-PW-VC-290	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	80.00	21-Jan-27	01-Feb-27	1,657	1,657	0	0	100%	0%
CO-PW-VC-300	Installation Works for Valves of Potable Water Network for Alignment-RD-03-3	72.00	14-Feb-27	23-Feb-27	4,308	0	0	0	0%	0%
CO-PW-VC-310	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	24.00	24-Feb-27	27-Feb-27	3,314	0	0	0	0%	0%
CO-PW-VC210	Installation of Valve Chambers of Potable Water Network for Alignment-RD-03-3	80.00	02-Feb-27	13-Feb-27	17,231	5,169	0	0	30%	0%
Fire Hydrant		176.00	02-Feb-27	27-Feb-27	8,994	169	0	0	1.88%	0%
CO-PW-FH-230	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-03-3	80.00	02-Feb-27	13-Feb-27	562	169	0	0	30%	0%
CO-PW-FH-240	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-03-3	80.00	14-Feb-27	24-Feb-27	7,308	0	0	0	0%	0%
CO-PW-FH-250	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	16.00	25-Feb-27	27-Feb-27	1,124	0	0	0	0%	0%
Irrigation Network		176.00	02-Feb-27	27-Feb-27	89,958	692	0	0	0.77%	0%
Main Line Pipes		176.00	02-Feb-27	27-Feb-27	89,958	692	0	0	0.77%	0%
CO-IR-ML-350	Trench Excavation and Bedding Works for Main Lines of Irrigation Network for	80.00	02-Feb-27	13-Feb-27	2,307	692	0	0	30%	0%
CO-IR-ML-360	Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-03-3	24.00	14-Feb-27	16-Feb-27	11,536	0	0	0	0%	0%
CO-IR-ML-370	Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-03-3	24.00	17-Feb-27	20-Feb-27	5,680	0	0	0	0%	0%
CO-IR-ML-380	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for	24.00	24-Feb-27	27-Feb-27	4,615	0	0	0	0%	0%
CO-IR-ML-390	Installation Works for Bulbblers And Sprinkler and Irrigation Control System of Irrigation	24.00	21-Feb-27	23-Feb-27	65,819	0	0	0	0%	0%
Medium Voltage Network		96.00	06-Mar-27	22-Mar-27	2,657	0	0	0	0%	0%
Cabling Works		96.00	06-Mar-27	22-Mar-27	2,657	0	0	0	0%	0%
CO-MV-ML-340	Trench Excavation and Bedding Works for Medium Voltage Network for	24.00	06-Mar-27	08-Mar-27	617	0	0	0	0%	0%
CO-MV-ML-350	Duct Laying Works for Medium Voltage Network for Alignment-RD-03-3	24.00	16-Mar-27	18-Mar-27	1,402	0	0	0	0%	0%
CO-MV-ML-360	Trench Backfilling and Compaction Works for Medium Voltage Network for	24.00	20-Mar-27	22-Mar-27	637	0	0	0	0%	0%

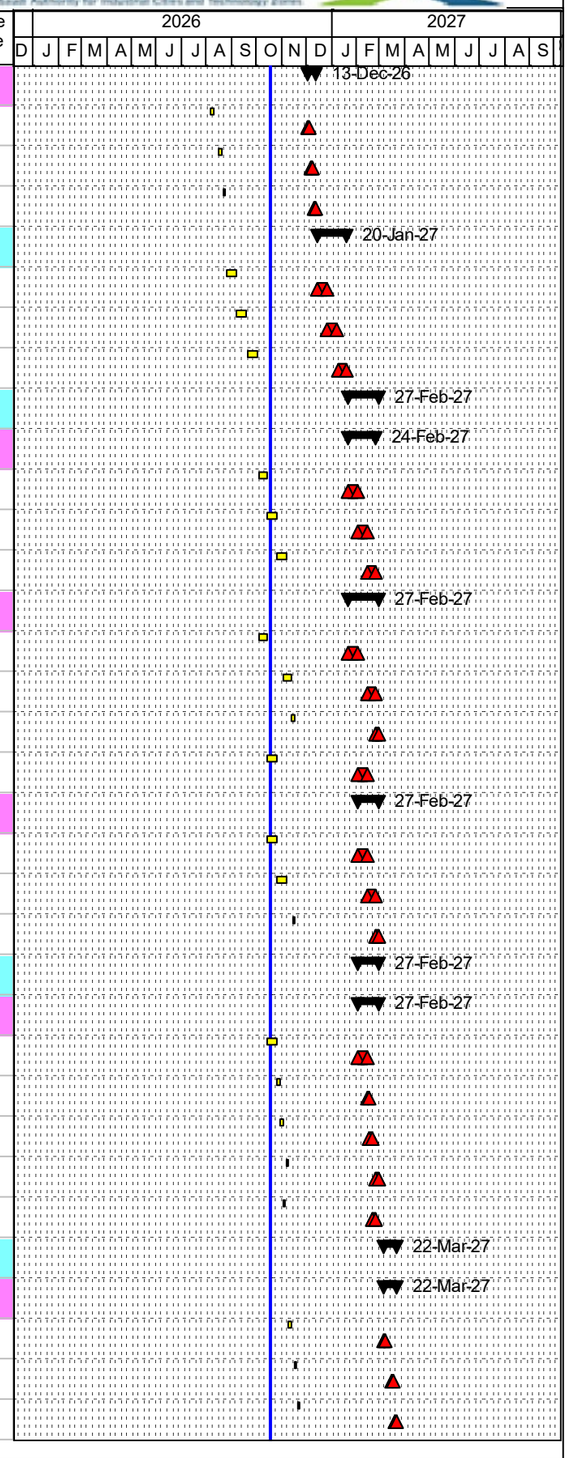

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Low Voltage Network		224.00	23-Mar-27	24-Apr-27	40,657	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		144.00	23-Mar-27	12-Apr-27	21,013	0	0	0	0%	0%
CON-LV-ML-190	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	56.00	23-Mar-27	30-Mar-27	4,104	0	0	0	0%	0%
CON-LV-ML-200	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-3	56.00	31-Mar-27	07-Apr-27	11,622	0	0	0	0%	0%
CON-LV-ML-210	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	32.00	08-Apr-27	12-Apr-27	5,287	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		136.00	31-Mar-27	19-Apr-27	18,960	0	0	0	0%	0%
CON-LV-HC-190	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	56.00	31-Mar-27	07-Apr-27	2,051	0	0	0	0%	0%
CON-LV-HC-200	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-3	56.00	08-Apr-27	15-Apr-27	11,622	0	0	0	0%	0%
CON-LV-HC-210	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	24.00	17-Apr-27	19-Apr-27	5,287	0	0	0	0%	0%
Distribution Pillars Works		32.00	20-Apr-27	24-Apr-27	684	0	0	0	0%	0%
CON-LV-DP-190	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-3	32.00	20-Apr-27	24-Apr-27	684	0	0	0	0%	0%
Street Lighting Network		144.00	23-Mar-27	12-Apr-27	30,567	0	0	0	0%	0%
Lighting Poles Works		144.00	23-Mar-27	12-Apr-27	12,586	0	0	0	0%	0%
CO-SL-LP-450	Installation Works for Lighting Poles Foundation of Street Lighting Network for	48.00	23-Mar-27	29-Mar-27	2,697	0	0	0	0%	0%
CO-SL-LP-460	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3	48.00	30-Mar-27	05-Apr-27	8,990	0	0	0	0%	0%
CO-SL-LP-480	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3	48.00	06-Apr-27	12-Apr-27	899	0	0	0	0%	0%
Cabling Works		48.00	06-Apr-27	12-Apr-27	17,981	0	0	0	0%	0%
CO-SL-CL-350	Cable Laying Works for Street Lighting Network for Alignment-RD-03-3	48.00	06-Apr-27	12-Apr-27	9,889	0	0	0	0%	0%
CO-SL-CL-360	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-3	48.00	06-Apr-27	12-Apr-27	8,091	0	0	0	0%	0%
Telecom and Light Current Network		208.00	01-Apr-27	01-May-27	232,186	0	0	0	0%	0%
Ducts Works		80.00	20-Apr-27	01-May-27	28,472	0	0	0	0%	0%
CO-TE-DW-230	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-03-3	48.00	20-Apr-27	26-Apr-27	19,575	0	0	0	0%	0%
CO-TE-DW-240	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	32.00	27-Apr-27	01-May-27	8,898	0	0	0	0%	0%
Manholes Works		64.00	01-Apr-27	10-Apr-27	14,687	0	0	0	0%	0%
CO-TE-MH-230	Excavation Works for Manholes of Telecom Network for Alignment-RD-03-3	16.00	01-Apr-27	03-Apr-27	979	0	0	0	0%	0%
CO-TE-MH-240	Installation Works for Manholes of Telecom Network for Alignment-RD-03-3	24.00	04-Apr-27	06-Apr-27	10,770	0	0	0	0%	0%
CO-TE-MH-250	Backfilling Works for Manholes of Telecom Network for Alignment-RD-03-3	24.00	07-Apr-27	10-Apr-27	2,937	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		24.00	11-Apr-27	13-Apr-27	189,027	0	0	0	0%	0%
CO-TE-CTV-210	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-3	24.00	11-Apr-27	13-Apr-27	189,027	0	0	0	0%	0%
Road Works		64.00	27-Apr-27	05-May-27	597,698	0	0	0	0%	0%
Pavement Works		32.00	27-Apr-27	01-May-27	585,170	0	0	0	0%	0%
CO-RD-PV-220	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-3	32.00	27-Apr-27	01-May-27	57,330	0	0	0	0%	0%
CO-RD-PV-230	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-3	32.00	27-Apr-27	01-May-27	527,840	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		64.00	27-Apr-27	05-May-27	12,528	0	0	0	0%	0%

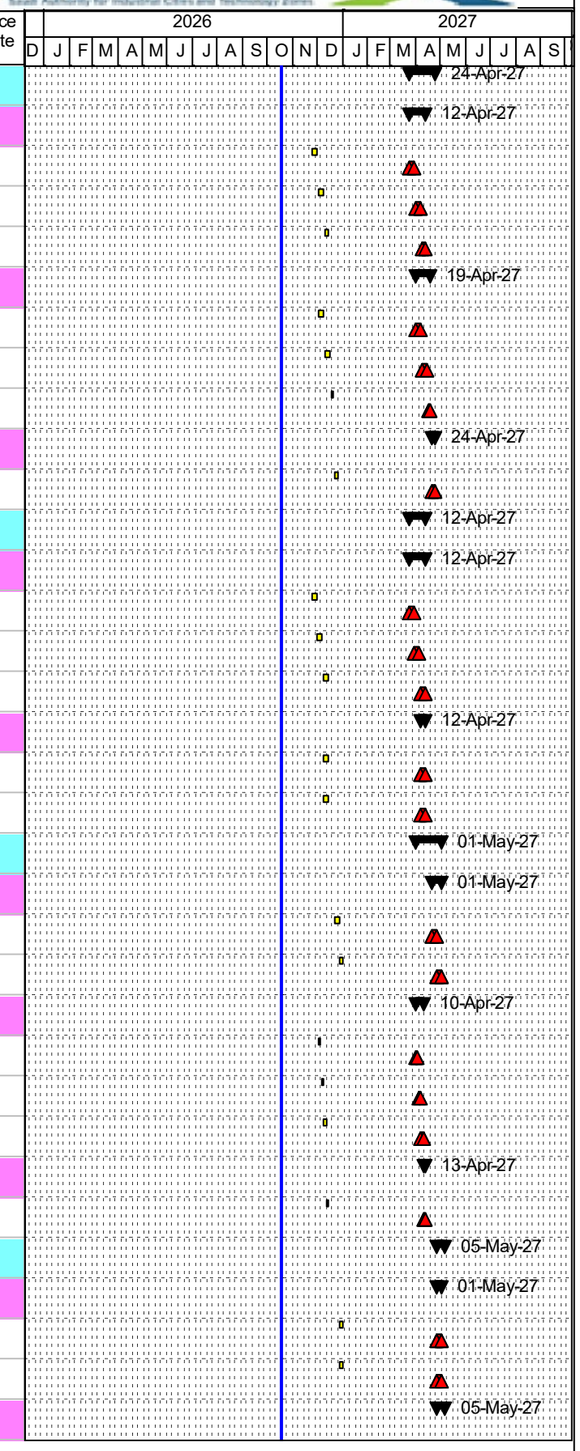

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-RD-F-RM-210	Application of Road Marking Works For Road Works for Alignment-RD-03-3	24.00	27-Apr-27	29-Apr-27	7,795	0	0	0	0%	0%
CO-RD-F-TS-150	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-3	32.00	02-May-27	05-May-27	4,734	0	0	0	0%	0%
Finishes for Infrastructure Networks		376.00	23-Mar-27	22-May-27	117,812	0	0	0	0%	0%
Storm Drainage Network		40.00	29-Apr-27	04-May-27	9,656	0	0	0	0%	0%
Testing and Finishes		40.00	29-Apr-27	04-May-27	9,656	0	0	0	0%	0%
CO-SD-ML-TF-130	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-03-3	40.00	29-Apr-27	04-May-27	9,656	0	0	0	0%	0%
Potable Water Network		56.00	20-Apr-27	27-Apr-27	23,243	0	0	0	0%	0%
Testing and Finishes		56.00	20-Apr-27	27-Apr-27	23,243	0	0	0	0%	0%
CO-PW-TF-190	Testing of Potable Water Network for Alignment-RD-03-3	24.00	24-Apr-27	26-Apr-27	6,386	0	0	0	0%	0%
CO-PW-TF-200	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	24.00	20-Apr-27	22-Apr-27	2,249	0	0	0	0%	0%
CO-PW-TF-210	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-03-3	32.00	24-Apr-27	27-Apr-27	14,609	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		48.00	10-May-27	22-May-27	1,510	0	0	0	0%	0%
Testing and Finishes		48.00	10-May-27	22-May-27	1,510	0	0	0	0%	0%
CO-TSE-TF-200	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-03-3	48.00	10-May-27	22-May-27	1,510	0	0	0	0%	0%
Irrigation Network		48.00	24-Apr-27	29-Apr-27	4,615	0	0	0	0%	0%
Testing and Finishes		48.00	24-Apr-27	29-Apr-27	4,615	0	0	0	0%	0%
CO-IR-TF-210	Final Testing (pressure tests) of Irrigation Network for Alignment-RD-03-3	48.00	24-Apr-27	29-Apr-27	4,615	0	0	0	0%	0%
Medium Voltage Network		48.00	23-Mar-27	29-Mar-27	510	0	0	0	0%	0%
Termination and Testing Works		48.00	23-Mar-27	29-Mar-27	510	0	0	0	0%	0%
CO-MV-TF-250	Testing and Termination Works of Medium Voltage Network for Alignment-RD-03-3	48.00	23-Mar-27	29-Mar-27	510	0	0	0	0%	0%
Low Voltage Network		48.00	25-Apr-27	01-May-27	8,454	0	0	0	0%	0%
Termination and Testing Works		48.00	25-Apr-27	01-May-27	8,454	0	0	0	0%	0%
CON-LV-TT-160	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	48.00	25-Apr-27	01-May-27	8,454	0	0	0	0%	0%
Street Lighting Network		136.00	20-Apr-27	09-May-27	12,457	0	0	0	0%	0%
Termination and Testing Works		136.00	20-Apr-27	09-May-27	11,254	0	0	0	0%	0%
CO-SL-LP-470	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48.00	20-Apr-27	26-Apr-27	5,860	0	0	0	0%	0%
CO-SL-TF-490	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3	48.00	03-May-27	09-May-27	5,394	0	0	0	0%	0%
Earthing System Works		88.00	20-Apr-27	02-May-27	1,203	0	0	0	0%	0%
CO-SL-ES-280	Install Earthing System Works for Lighting Poles of Street Lighting Network for	48.00	20-Apr-27	26-Apr-27	601	0	0	0	0%	0%
CO-SL-ES-290	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	48.00	26-Apr-27	02-May-27	601	0	0	0	0%	0%
Telecom and Light Current Network		96.00	15-Apr-27	28-Apr-27	57,368	0	0	0	0%	0%
Testing and Finishes		96.00	15-Apr-27	28-Apr-27	57,368	0	0	0	0%	0%
CO-TE-CTV-TF-260	Testing and Interface modules with Telecom for Alignment-RD-03-3	48.00	15-Apr-27	21-Apr-27	12,014	0	0	0	0%	0%
CO-TE-CTV-TF-340	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	48.00	22-Apr-27	28-Apr-27	45,355	0	0	0	0%	0%

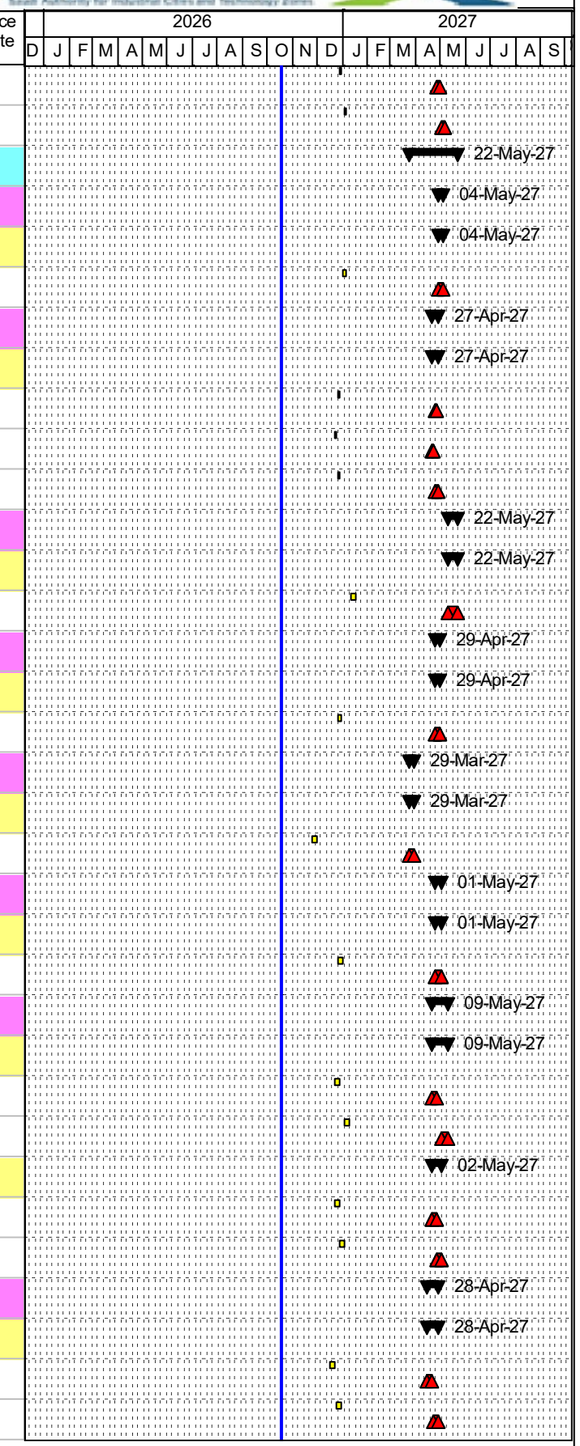

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
External		2672.00	01-Apr-26 A	04-May-27	25,187,577	15,650,043	10,480,369	10,202,009	62.13%	41.61%
External Road - 1 - 1		2664.00	01-Apr-26 A	03-May-27	5,221,714	3,247,135	2,608,226	2,608,226	62.19%	49.95%
Earthworks		1776.00	01-Apr-26 A	21-Dec-26	3,247,135	3,247,135	2,608,226	2,608,226	100%	80.32%
Earthworks		1776.00	01-Apr-26 A	21-Dec-26	3,247,135	3,247,135	2,608,226	2,608,226	100%	80.32%
CO-EW-250	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	536.00	01-Apr-26 A	22-Jun-26 A	2,608,226	2,608,226	2,608,226	2,608,226	100%	100%
CO-EW-250_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	64.00	13-Dec-26	21-Dec-26	638,908	638,908	0	0	100%	0%
Road Works		304.00	21-Mar-27	03-May-27	1,974,580	0	0	0	0%	0%
Road 01		304.00	21-Mar-27	03-May-27	1,974,580	0	0	0	0%	0%
Pre-Bituminous Construction		136.00	21-Mar-27	08-Apr-27	532,798	0	0	0	0%	0%
CO-RD-PB-240	Subgrade Layer for Road Works for External Road - 1 - 1	64.00	21-Mar-27	29-Mar-27	259,905	0	0	0	0%	0%
CO-RD-PB-250	Aggregate Base Course Layer for Road Works for External Road - 1 - 1	72.00	30-Mar-27	08-Apr-27	272,894	0	0	0	0%	0%
Bituminous Construction		64.00	10-Apr-27	18-Apr-27	1,102,685	0	0	0	0%	0%
CO-RD-B-260	Bituminous Base Courses Layers for Road Works for External Road - 1 - 1	32.00	10-Apr-27	13-Apr-27	548,740	0	0	0	0%	0%
CON-RD-MR-250	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 1	32.00	14-Apr-27	18-Apr-27	553,945	0	0	0	0%	0%
Pavement Works		112.00	14-Apr-27	29-Apr-27	301,042	0	0	0	0%	0%
CO-RD-PV-260	Fixing of Curbstone for Sidewalks Pavement for External Road - 1 - 1	64.00	14-Apr-27	22-Apr-27	183,454	0	0	0	0%	0%
CO-RD-PV-270	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 1 - 1	48.00	24-Apr-27	29-Apr-27	117,588	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		24.00	01-May-27	03-May-27	38,054	0	0	0	0%	0%
CO-RD-F-RM-230	Application of Road Marking Works For Road Works for External Road - 1 - 1	16.00	01-May-27	02-May-27	24,799	0	0	0	0%	0%
CO-RD-F-TS-170	Installation Works of Traffic Signs Boards For Road Works for External Road - 1 - 1	8.00	03-May-27	03-May-27	13,255	0	0	0	0%	0%
External Road - 1 - 2		2560.00	18-Apr-26 A	04-May-27	7,651,591	4,767,067	1,790,191	1,214,285	62.3%	23.4%
Earthworks		1560.00	18-Apr-26 A	11-Jan-27	4,767,067	4,767,067	1,790,191	1,214,285	100%	37.55%
Earthworks		1560.00	18-Apr-26 A	11-Jan-27	4,767,067	4,767,067	1,790,191	1,214,285	100%	37.55%
CO-EW-280	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	424.00	18-Apr-26 A	22-Jun-26 A	622,155	622,155	622,155	622,155	100%	100%
CO-EW-280_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	168.00	26-Sep-26 A	11-Jan-27	4,144,912	4,144,912	1,168,036	592,130	100%	28.18%
Road Works		312.00	21-Mar-27	04-May-27	2,884,524	0	0	0	0%	0%
Road 01		312.00	21-Mar-27	04-May-27	2,884,524	0	0	0	0%	0%
Pre-Bituminous Construction		96.00	21-Mar-27	03-Apr-27	778,172	0	0	0	0%	0%
CO-RD-PB-300	Subgrade Layer for Road Works for External Road - 1 - 2	48.00	21-Mar-27	27-Mar-27	379,600	0	0	0	0%	0%
CO-RD-PB-310	Aggregate Base Course Layer for Road Works for External Road - 1 - 2	48.00	28-Mar-27	03-Apr-27	398,572	0	0	0	0%	0%
Bituminous Construction		88.00	04-Apr-27	15-Apr-27	1,610,525	0	0	0	0%	0%
CO-RD-B-320	Bituminous Base Courses Layers for Road Works for External Road - 1 - 2	56.00	04-Apr-27	11-Apr-27	801,462	0	0	0	0%	0%
CON-RD-MR-310	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 1	32.00	12-Apr-27	15-Apr-27	809,064	0	0	0	0%	0%
Pavement Works		96.00	13-Apr-27	26-Apr-27	439,683	0	0	0	0%	0%

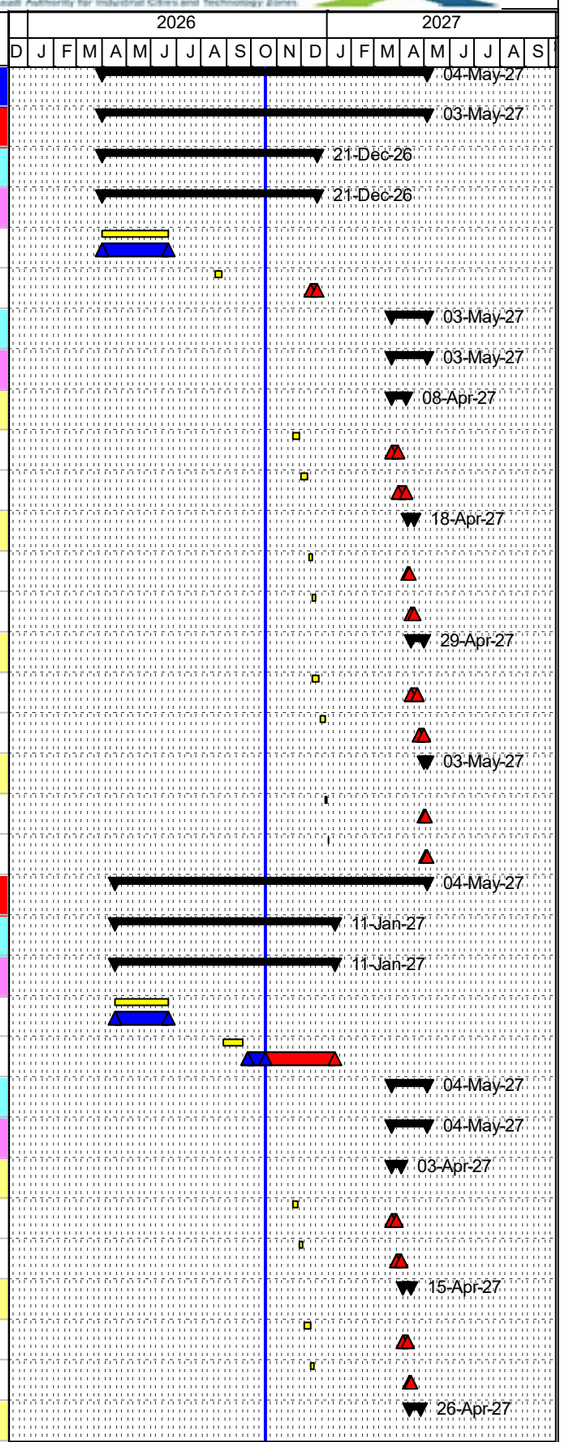

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-RD-PV-320	Fixing of Curbstone for Sidewalks Pavement for External Road - 1 - 2	48.00	13-Apr-27	19-Apr-27	267,941	0	0	0	0%	0%
CO-RD-PV-330	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 1 - 2	48.00	20-Apr-27	26-Apr-27	171,741	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		56.00	27-Apr-27	04-May-27	56,143	0	0	0	0%	0%
CO-RD-F-RM-260	Application of Road Marking Works For Road Works for External Road - 1 - 2	32.00	27-Apr-27	01-May-27	36,261	0	0	0	0%	0%
CO-RD-F-TS-200	Installation Works of Traffic Signs Boards For Road Works for External Road - 1 - 2	24.00	02-May-27	04-May-27	19,882	0	0	0	0%	0%
External Road - 2		2416.00	09-May-26 A	04-May-27	3,781,297	2,348,995	1,330,763	1,330,763	62.12%	35.19%
Earthworks		1832.00	09-May-26 A	04-Feb-27	2,348,995	2,348,995	1,330,763	1,330,763	100%	56.65%
Earthworks		1832.00	09-May-26 A	04-Feb-27	2,348,995	2,348,995	1,330,763	1,330,763	100%	56.65%
CO-EW-260	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	280.00	09-May-26 A	22-Jun-26 A	1,330,763	1,330,763	1,330,763	1,330,763	100%	100%
CO-EW-260_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	168.00	12-Jan-27	04-Feb-27	1,018,232	1,018,232	0	0	100%	0%
Road Works		360.00	14-Mar-27	04-May-27	1,432,302	0	0	0	0%	0%
Road 01		360.00	14-Mar-27	04-May-27	1,432,302	0	0	0	0%	0%
Pre-Bituminous Construction		56.00	14-Mar-27	21-Mar-27	386,518	0	0	0	0%	0%
CO-RD-PB-260	Subgrade Layer for Road Works for External Road - 2	56.00	14-Mar-27	21-Mar-27	188,547	0	0	0	0%	0%
CO-RD-PB-270	Aggregate Base Course Layer for Road Works for External Road - 2	32.00	17-Mar-27	21-Mar-27	197,971	0	0	0	0%	0%
Bituminous Construction		160.00	22-Mar-27	13-Apr-27	799,946	0	0	0	0%	0%
CO-RD-B-280	Bituminous Base Courses Layers for Road Works for External Road - 2	80.00	22-Mar-27	01-Apr-27	398,085	0	0	0	0%	0%
CON-RD-MR-270	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 2	80.00	03-Apr-27	13-Apr-27	401,861	0	0	0	0%	0%
Pavement Works		72.00	13-Apr-27	22-Apr-27	218,390	0	0	0	0%	0%
CO-RD-PV-280	Fixing of Curbstone for Sidewalks Pavement for External Road - 2	72.00	13-Apr-27	22-Apr-27	133,086	0	0	0	0%	0%
CO-RD-PV-290	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 2	72.00	13-Apr-27	22-Apr-27	85,304	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		80.00	24-Apr-27	04-May-27	27,448	0	0	0	0%	0%
CO-RD-F-RM-240	Application of Road Marking Works For Road Works for External Road - 2	80.00	24-Apr-27	04-May-27	17,980	0	0	0	0%	0%
CO-RD-F-TS-180	Installation Works of Traffic Signs Boards For Road Works for External Road - 2	16.00	26-Apr-27	27-Apr-27	9,468	0	0	0	0%	0%
External Road - 3		2416.00	09-May-26 A	04-May-27	8,532,974	5,286,846	4,751,189	5,048,735	61.96%	55.68%
Earthworks		1752.00	09-May-26 A	13-Feb-27	5,285,229	5,285,229	4,540,017	4,837,557	100%	85.9%
Earthworks		1752.00	09-May-26 A	13-Feb-27	5,285,229	5,285,229	4,540,017	4,837,557	100%	85.9%
CO-EW-270	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	280.00	09-May-26 A	22-Jun-26 A	2,968,746	2,968,746	2,968,746	2,968,746	100%	100%
CO-EW-270_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	168.00	23-Aug-26 A	13-Feb-27	2,316,484	2,316,484	1,571,271	1,868,812	9.52%	67.83%
Telecom and Light Current Network		344.00	26-Jan-27	20-Mar-27	38,794	1,616	0	0	4.17%	0%
Manholes Works		296.00	26-Jan-27	13-Mar-27	29,095	1,616	0	0	5.56%	0%
CO-TE-MH-290	Excavation Works for Manholes of Telecom Network for External Road - 3	144.00	26-Jan-27	15-Feb-27	1,940	1,616	0	0	83.33%	0%
CO-TE-MH-300	Installation Works for Manholes of Telecom Network for External Road - 3	152.00	16-Feb-27	13-Mar-27	21,337	0	0	0	0%	0%
CO-TE-MH-310	Backfilling Works for Manholes of Telecom Network for External Road - 3	48.00	03-Mar-27	13-Mar-27	5,819	0	0	0	0%	0%

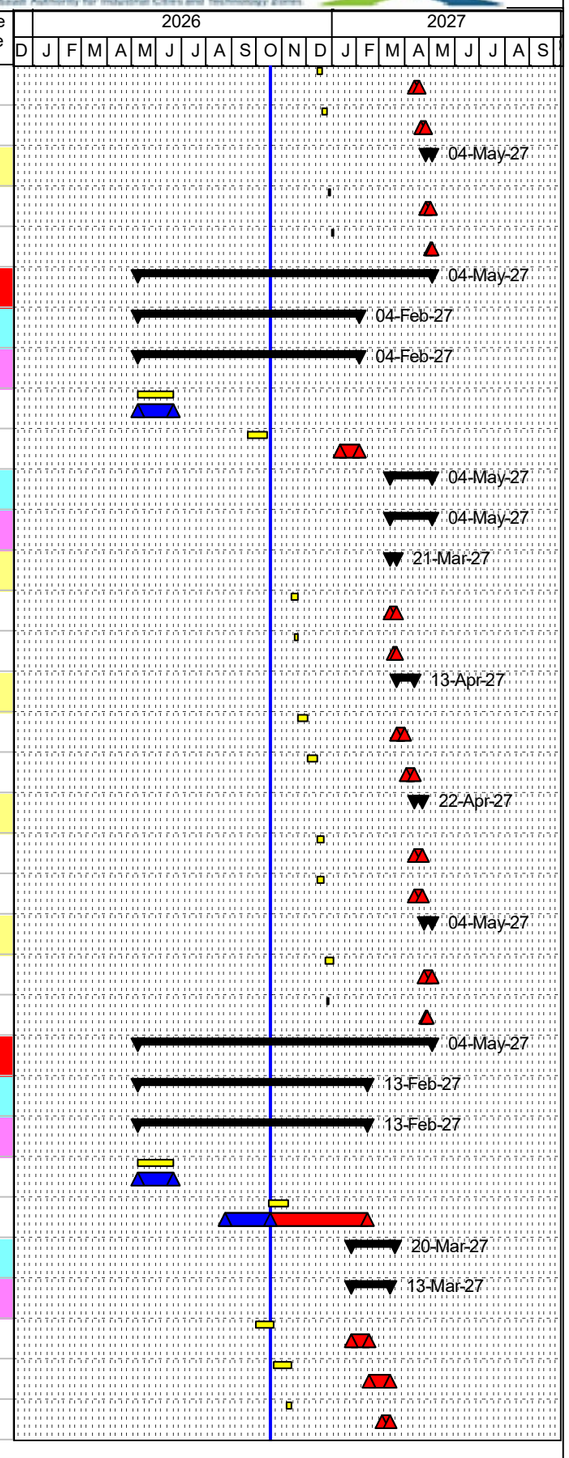

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Testing and Finishes		48.00	14-Mar-27	20-Mar-27	9,698	0	0	0	0%	0%
CO-TE-CTV-TF-360	Testing and Interface modules with Telecom for External Road - 3	48.00	14-Mar-27	20-Mar-27	9,698	0	0	0	0%	0%
Road Works		640.00	08-Sep-26 A	04-May-27	3,208,951	0	211,172	211,178	0%	6.58%
Road 01		640.00	08-Sep-26 A	04-May-27	3,208,951	0	211,172	211,178	0%	6.58%
Pre-Bituminous Construction		392.00	08-Sep-26 A	29-Mar-27	865,798	0	211,172	211,178	0%	24.39%
CO-RD-PB-280	Subgrade Layer for Road Works for External Road - 3	48.00	08-Sep-26 A	20-Mar-27	422,344	0	211,172	211,178	0%	50%
CO-RD-PB-290	Aggregate Base Course Layer for Road Works for External Road - 3	88.00	17-Mar-27	29-Mar-27	443,453	0	0	0	0%	0%
Bituminous Construction		184.00	03-Apr-27	28-Apr-27	1,791,868	0	0	0	0%	0%
CO-RD-B-300	Bituminous Base Courses Layers for Road Works for External Road - 3	96.00	03-Apr-27	15-Apr-27	891,705	0	0	0	0%	0%
CON-RD-MR-290	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 3	88.00	17-Apr-27	28-Apr-27	900,163	0	0	0	0%	0%
Pavement Works		24.00	24-Apr-27	26-Apr-27	489,192	0	0	0	0%	0%
CO-RD-PV-300	Fixing of Curbstone for Sidewalks Pavement for External Road - 3	24.00	24-Apr-27	26-Apr-27	298,112	0	0	0	0%	0%
CO-RD-PV-310	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 3	24.00	24-Apr-27	26-Apr-27	191,080	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		40.00	29-Apr-27	04-May-27	62,093	0	0	0	0%	0%
CO-RD-F-RM-250	Application of Road Marking Works For Road Works for External Road - 3	40.00	29-Apr-27	04-May-27	40,318	0	0	0	0%	0%
CO-RD-F-TS-190	Installation Works of Traffic Signs Boards For Road Works for External Road - 3	24.00	29-Apr-27	02-May-27	21,775	0	0	0	0%	0%
Superstructure Work		1760.00	01-Aug-26 A	16-Jun-27	35,365,443	2,503,998	9,585,992	9,508,240	7.02%	26.86%
Utility Buildings		1760.00	29-Aug-26 A	16-Jun-27	8,083,982	924,668	998,693	976,940	11.44%	12.35%
Water Pump Station		1760.00	15-Sep-26 A	16-Jun-27	3,313,461	539,240	346,091	346,091	16.27%	10.45%
Civil work		520.00	15-Sep-26 A	08-Dec-26	445,078	445,078	346,091	346,091	100%	77.76%
SubStructure		312.00	15-Sep-26 A	08-Nov-26	318,456	318,456	314,735	314,735	100%	98.83%
CO-UB-PS-100	Excavation Work for Water Pump station building	64.00	15-Sep-26 A	17-Sep-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-110	pouring P.C Conceret for Water Pump station building	16.00	19-Sep-26 A	20-Sep-26 A	296,132	296,132	296,132	296,132	100%	100%
CO-UB-PS-120	Formwork for Foundation for Water Pump station building	56.00	26-Sep-26 A	27-Sep-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-130	Steel fixing for Foundation for Water Pump station building	48.00	27-Sep-26 A	28-Sep-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-140	pouring for Foundation for Water Pump station building	8.00	01-Oct-26 A	03-Oct-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-150	curing and deshuttering formwork Pump station building	56.00	06-Oct-26 A	10-Oct-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-160	Backfilling and compaction work for pump station	32.00	04-Nov-26	08-Nov-26	3,721	3,721	0	0	100%	0%
Super structure		208.00	06-Oct-26 A	08-Dec-26	126,623	126,623	31,356	31,356	100%	24.76%
CO-UB-PS-170	Formwork for Wall and columns for Water Pump station building	40.00	06-Oct-26 A	08-Oct-26 A	10,452	10,452	10,452	10,452	100%	100%
CO-UB-PS-180	Steel fixing for Wall columns	32.00	08-Oct-26 A	10-Oct-26 A	10,452	10,452	10,452	10,452	100%	100%
CO-UB-PS-190	pouring for Wall columns	8.00	11-Oct-26 A	12-Oct-26 A	10,452	10,452	10,452	10,452	100%	100%
CO-UB-PS-200	curing and deshuttering formwork for Wall columns	56.00	09-Nov-26	16-Nov-26	10,452	10,452	0	0	100%	0%
CO-UB-PS-210	Waterproofing for Walls columns	16.00	17-Nov-26	18-Nov-26	10,452	10,452	0	0	100%	0%

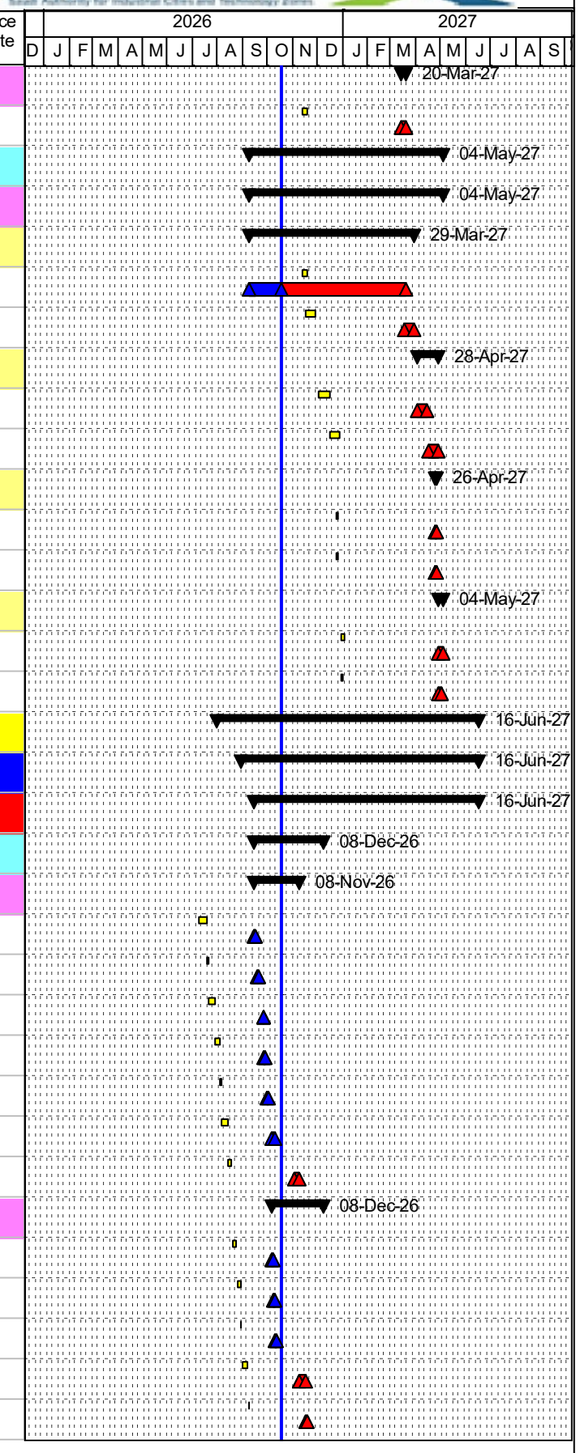

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-UB-PS-220	Formwork for pump roof	32.00	19-Nov-26	23-Nov-26	17,183	17,183	0	0	100%	0%
CO-UB-PS-230	Steel fixing for pump roof	32.00	24-Nov-26	28-Nov-26	17,183	17,183	0	0	100%	0%
CO-UB-PS-240	pouring for pump roof	16.00	29-Nov-26	30-Nov-26	17,183	17,183	0	0	100%	0%
CO-UB-PS-250	curing and deshuttering formwork for pump roof	56.00	01-Dec-26	08-Dec-26	22,812	22,812	0	0	100%	0%
Architectural work		240.00	09-Dec-26	12-Jan-27	152,986	94,161	0	0	61.55%	0%
CO-UB-PS-260	Executing Masonry Works for Water Pump station building	56.00	09-Dec-26	16-Dec-26	44,161	44,161	0	0	100%	0%
CO-UB-PS-270	Executing Plastering Works for Pump station building	56.00	17-Dec-26	24-Dec-26	43,051	43,051	0	0	100%	0%
CO-UB-PS-280	Executing Painting and Finishes Works for Pump station building	64.00	26-Dec-26	03-Jan-27	55,593	6,949	0	0	12.5%	0%
CO-UB-PS-320	Doors and windows Fixing &Stair Tiles	64.00	04-Jan-27	12-Jan-27	10,180	0	0	0	0%	0%
Mechanical work		288.00	01-May-27	16-Jun-27	2,715,397	0	0	0	0%	0%
CO-UB-PS-340	Executing HVAC System for Water Pump station building	80.00	01-May-27	11-May-27	88,142	0	0	0	0%	0%
CO-UB-PS-360	Executing Fire fighting institution works(piping and wire installation) for Water Pump station	80.00	12-May-27	29-May-27	19,869	0	0	0	0%	0%
CO-UB-PS-380	Executing Plummbing works for Water Pump station building	80.00	30-May-27	09-Jun-27	524,160	0	0	0	0%	0%
CO-UB-PS-390	Installation of pumps	48.00	10-Jun-27	16-Jun-27	2,083,226	0	0	0	0%	0%
Sewage Lift Station		480.00	29-Aug-26 A	21-Jan-27	564,483	0	372,559	350,805	0%	66%
Civil work		480.00	29-Aug-26 A	18-Jan-27	416,344	0	372,559	350,805	0%	89.48%
Sup Structure		384.00	29-Aug-26 A	10-Oct-26 A	228,618	0	228,618	228,618	0%	100%
CO-UB-LS-220	Excavation Work for Sewage Lift Station	72.00	29-Aug-26 A	31-Aug-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-230	pouring P.C Conceret for Sewage Lift Station	16.00	01-Sep-26 A	02-Sep-26 A	20,627	0	20,627	20,627	0%	100%
CO-UB-LS-240	Formwork for Foundation for Sewage Lift Station	96.00	03-Sep-26 A	03-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-250	Steel fixing for Foundation for Sewage Lift Station	80.00	03-Sep-26 A	06-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-260	pouring for Foundationfor Sewage Lift Station	16.00	03-Sep-26 A	08-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-270	curing and deshuttering formwork for Sewage Lift Station	56.00	03-Sep-26 A	10-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-280	Backfilling and compaction work for Sewage Lift Station	48.00	03-Sep-26 A	10-Oct-26 A	34,665	0	34,665	34,665	0%	100%
Super structure		352.00	30-Sep-26 A	18-Jan-27	187,726	0	143,941	122,187	0%	76.68%
CO-UB-LS-290	Formwork for Wall and columns for Sewage Lift Station	80.00	30-Sep-26 A	04-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-300	Steel fixing for Wall columns	72.00	05-Oct-26 A	06-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-310	pouring for Wall columns	8.00	07-Oct-26 A	08-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	56.00	11-Oct-26 A	12-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-330	Waterproofing for Walls columns	32.00	12-Oct-26 A	13-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-340	Formwork for pump roof	48.00	13-Oct-26 A	15-Oct-26 A	24,170	0	24,170	24,170	0%	100%
CO-UB-LS-350	Steel fixing for pump roof	48.00	17-Oct-26 A	18-Oct-26 A	24,170	0	24,170	24,170	0%	100%
CO-UB-LS-360	pouring for pump roof	8.00	18-Oct-26 A	04-Jan-27	24,170	0	21,753	0	0%	90%
CO-UB-LS-370	curing and deshuttering formwork for pump roof	96.00	05-Jan-27	18-Jan-27	41,368	0	0	0	0%	0%

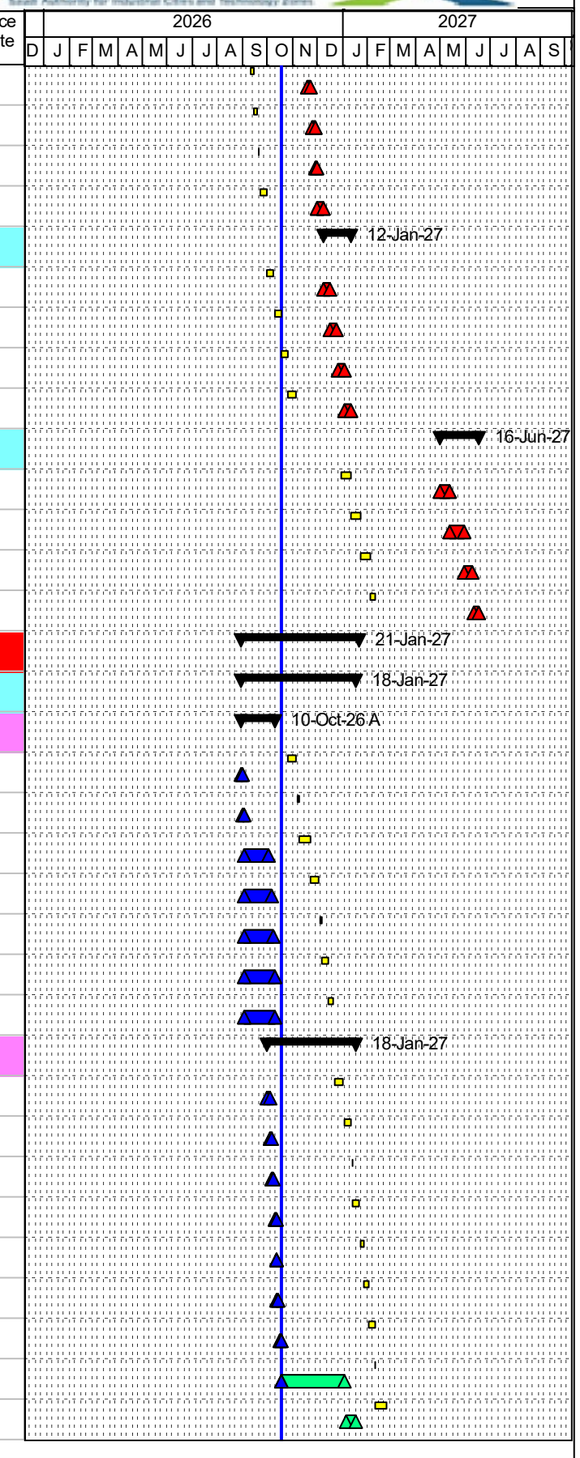

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Architectural work		24.00	19-Jan-27	21-Jan-27	148,139	0	0	0	0%	0%
CO-UB-LS-390	Executing Plastering and Finishes Works for Sewage Lift Station	24.00	19-Jan-27	21-Jan-27	148,139	0	0	0	0%	0%
Potable Water Tank		616.00	26-Dec-26	28-Mar-27	314,972	4,147	0	0	1.32%	0%
Eearth Work		176.00	26-Dec-26	19-Jan-27	99,522	4,147	0	0	4.17%	0%
CO-UB-PWT-100	Excavation work for tank foundation tank formation level for Potable Water Tank	96.00	26-Dec-26	07-Jan-27	49,761	4,147	0	0	8.33%	0%
CO-UB-PWT-110	Soil replacement Up to tank formation level for Potable Water Tank	80.00	09-Jan-27	19-Jan-27	49,761	0	0	0	0%	0%
Structural Work		328.00	20-Jan-27	08-Mar-27	168,191	0	0	0	0%	0%
CO-UB-PWT-120	Plain Concrete works for Potable Water Tank	56.00	20-Jan-27	27-Jan-27	18,908	0	0	0	0%	0%
CO-UB-PWT-130	Form work for Tank Foundation for Potable Water Tank	96.00	28-Jan-27	10-Feb-27	49,761	0	0	0	0%	0%
CO-UB-PWT-140	Steel Reinforcement work for Tank Foundation for Potable Water Tank	96.00	11-Feb-27	24-Feb-27	49,761	0	0	0	0%	0%
CO-UB-PWT-150	Casting concrete for Tank Foundation for Potable Water Tank	80.00	25-Feb-27	08-Mar-27	49,761	0	0	0	0%	0%
Tank Shell Erection&Roof Installation		112.00	13-Mar-27	28-Mar-27	47,259	0	0	0	0%	0%
CO-UB-PWT-170	shell erection for Potable Water Tank	112.00	13-Mar-27	28-Mar-27	47,259	0	0	0	0%	0%
IrrigationTank		512.00	09-Jan-27	27-Mar-27	314,972	0	0	0	0%	0%
Eearth Work		176.00	09-Jan-27	02-Feb-27	99,522	0	0	0	0%	0%
CO-UB-IRT-140	Excavation work for tank foundation tank formation level for Irrigation Tank	96.00	09-Jan-27	21-Jan-27	49,761	0	0	0	0%	0%
CO-UB-IRT-150	Soil replacement Up to tank formation level for Irrigation Tank	80.00	23-Jan-27	02-Feb-27	49,761	0	0	0	0%	0%
Structural Work		224.00	03-Feb-27	07-Mar-27	168,191	0	0	0	0%	0%
CO-UB-IRT-160	Plain Concrete works for Irrigation Tank	24.00	03-Feb-27	06-Feb-27	18,908	0	0	0	0%	0%
CO-UB-IRT-170	Form work for Tank Foundation for Irrigation Tank	80.00	07-Feb-27	17-Feb-27	49,761	0	0	0	0%	0%
CO-UB-IRT-180	Steel Reinforcement work for Tank Foundation for Irrigation Tank	88.00	18-Feb-27	02-Mar-27	49,761	0	0	0	0%	0%
CO-UB-IRT-190	Casting concrete for Tank Foundation for Irrigation Tank	32.00	03-Mar-27	07-Mar-27	49,761	0	0	0	0%	0%
Tank Shell Erection&Roof Installation		112.00	08-Mar-27	27-Mar-27	47,259	0	0	0	0%	0%
CO-UB-IRT-210	shell erection for Irrigation Tank	112.00	08-Mar-27	27-Mar-27	47,259	0	0	0	0%	0%
Control Room		984.00	03-Oct-26 A	08-May-27	3,576,093	381,282	280,043	280,043	10.66%	7.83%
Civil Work		224.00	03-Oct-26 A	13-Jan-27	472,675	381,282	280,043	280,043	80.66%	59.25%
CO-UB-CR-100	Excavation Work For Control Room Foundation	56.00	03-Oct-26 A	04-Oct-26 A	7,427	7,427	7,427	7,427	100%	100%
CO-UB-CR-110	Pouring for Plain Concrete	40.00	05-Oct-26 A	11-Oct-26 A	265,188	265,188	265,188	265,188	100%	100%
CO-UB-CR-120	Pouring R.C Footing For Control Room	168.00	13-Oct-26 A	17-Oct-26 A	7,427	7,427	7,427	7,427	100%	100%
CO-UB-CR-130	Pouring R.C Columns For Control Room	96.00	20-Dec-26	02-Jan-27	78,391	78,391	0	0	100%	0%
CO-UB-CR-140	Pouring Beams and Slab For Control Room	80.00	03-Jan-27	13-Jan-27	114,241	22,848	0	0	20%	0%
Finishing Work		760.00	14-Jan-27	08-May-27	3,103,418	0	0	0	0%	0%
Architictural work		336.00	14-Jan-27	03-Mar-27	362,218	0	0	0	0%	0%
CO-UB-CR-150	Brick Work For Control Room	80.00	14-Jan-27	25-Jan-27	99,292	0	0	0	0%	0%

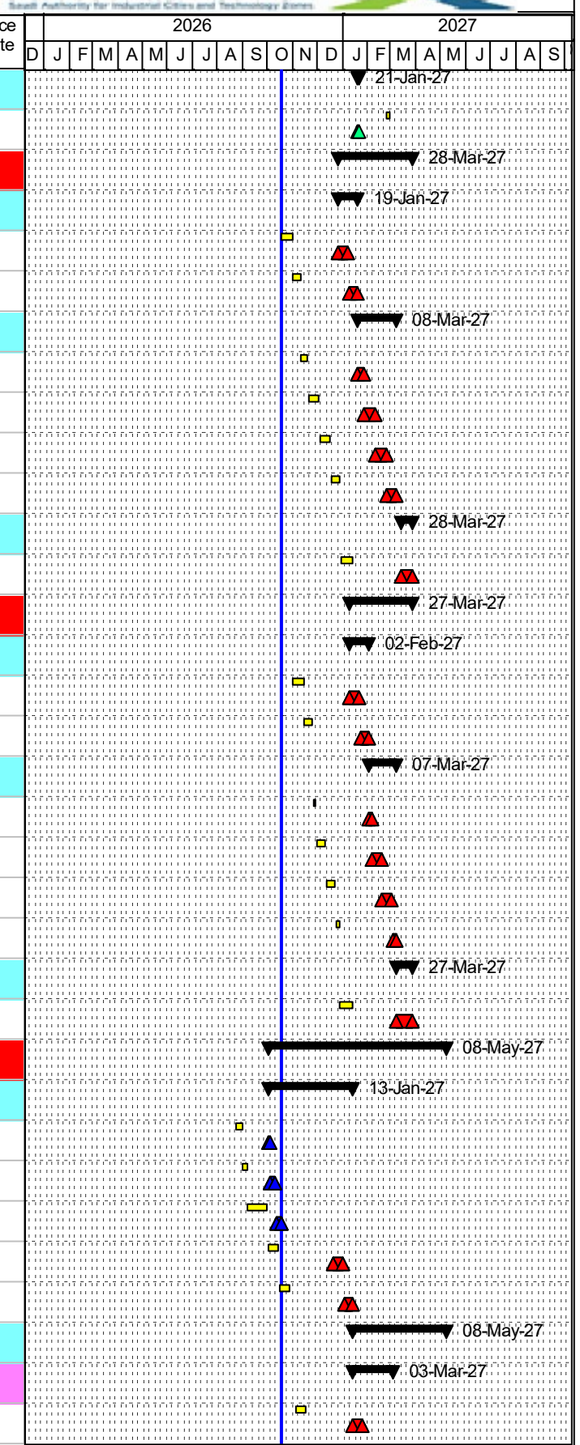


Primary Baseline · Remaining Work · Critical Remaining Work · Actual Work · Baseline Milestone · Milestone · Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-UB-CR-160	Thermal & Moisture Protection Work for Control Room	56.00	26-Jan-27	02-Feb-27	21,971	0	0	0	0%	0%
CO-UB-CR-200	Install For Curtian Wall and Windows and Doors	56.00	03-Feb-27	10-Feb-27	91,926	0	0	0	0%	0%
CO-UB-CR-240	External Finshing Work (Walls and Floor)	64.00	11-Feb-27	20-Feb-27	127,277	0	0	0	0%	0%
CO-UB-CR-250	Internal Finshing Work (Walls,Floor and Ceiling)	80.00	21-Feb-27	03-Mar-27	21,751	0	0	0	0%	0%
Mechanical Work		576.00	26-Jan-27	22-Apr-27	1,331,986	0	0	0	0%	0%
HVAC System		576.00	26-Jan-27	22-Apr-27	137,139	0	0	0	0%	0%
CO-UB-CR-170	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with supports,	168.00	26-Jan-27	18-Feb-27	68,570	0	0	0	0%	0%
CO-UB-CR-260	Install of Mini split actual and Ducted split	160.00	04-Mar-27	30-Mar-27	30,178	0	0	0	0%	0%
CO-UB-CR-310	Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm	160.00	31-Mar-27	22-Apr-27	38,392	0	0	0	0%	0%
Fire Fitting System		136.00	20-Feb-27	14-Mar-27	434,599	0	0	0	0%	0%
CO-UB-CR-180	Installation & Testing of 2 hours Fire rated system for closing the openings between	80.00	20-Feb-27	02-Mar-27	405,466	0	0	0	0%	0%
CO-UB-CR-270	Install Fire Extinguishers	48.00	04-Mar-27	14-Mar-27	29,133	0	0	0	0%	0%
Plumbing System		96.00	04-Mar-27	21-Mar-27	760,248	0	0	0	0%	0%
CO-UB-CR-370	Install of Sanitary Wares Including Relevant Pipes and Fittings	96.00	04-Mar-27	21-Mar-27	760,248	0	0	0	0%	0%
Electrical Work		376.00	04-Mar-27	01-May-27	965,706	0	0	0	0%	0%
LV Power		344.00	04-Mar-27	26-Apr-27	874,883	0	0	0	0%	0%
CO-UB-CR-190	Install of Distribution board For Control Room	80.00	04-Mar-27	18-Mar-27	87,096	0	0	0	0%	0%
CO-UB-CR-220	Install of Earting Cable for Control Room	112.00	20-Mar-27	04-Apr-27	190,403	0	0	0	0%	0%
CO-UB-CR-280	Install of Socket outlet and LED Lighting	152.00	05-Apr-27	26-Apr-27	597,384	0	0	0	0%	0%
Fire Detection And Alarm System		280.00	22-Mar-27	01-May-27	90,824	0	0	0	0%	0%
CO-UB-CR-210	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	32.00	22-Mar-27	25-Mar-27	35,785	0	0	0	0%	0%
CO-UB-CR-230	Install of Transmission Communication cable - Fiber Optics 12Core	32.00	27-Mar-27	30-Mar-27	17,975	0	0	0	0%	0%
CO-UB-CR-290	Install of power supply system for fire alarm control panel	32.00	31-Mar-27	04-Apr-27	11,246	0	0	0	0%	0%
CO-UB-CR-300	Install of Fire Alarm Control panel	48.00	05-Apr-27	11-Apr-27	16,024	0	0	0	0%	0%
CO-UB-CR-320	Installation of the addressable manual call point with operation safety glass breaking	24.00	12-Apr-27	14-Apr-27	243	0	0	0	0%	0%
CO-UB-CR-330	Install of the photoelectric heat & smoke detector	40.00	15-Apr-27	20-Apr-27	4,229	0	0	0	0%	0%
CO-UB-CR-340	Install of Sounder With Beacon	40.00	21-Apr-27	26-Apr-27	1,190	0	0	0	0%	0%
CO-UB-CR-350	Install of Addressable Control module	32.00	27-Apr-27	01-May-27	4,131	0	0	0	0%	0%
Furnitures work		48.00	02-May-27	08-May-27	443,507	0	0	0	0%	0%
CO-UB-CR-360	Office Chairs,Tables and Stand	48.00	02-May-27	08-May-27	443,507	0	0	0	0%	0%
Softscape and Planting Works		280.00	24-Apr-27	08-Jun-27	3,915,193	0	0	0	0%	0%
CO-LS-PL-160	Planting Works: Planting including plants, forming planting beds, suitable soil, supports,	120.00	24-Apr-27	10-May-27	2,361,373	0	0	0	0%	0%
CO-LS-SF-170	Site Furnishings (Seating Bench,Stone Boulders and Gravel)	160.00	11-May-27	08-Jun-27	1,553,820	0	0	0	0%	0%
Storm Drainage Ponds		440.00	01-Oct-26 A	28-Apr-27	8,820,044	0	3,969,020	3,969,053	0%	45%

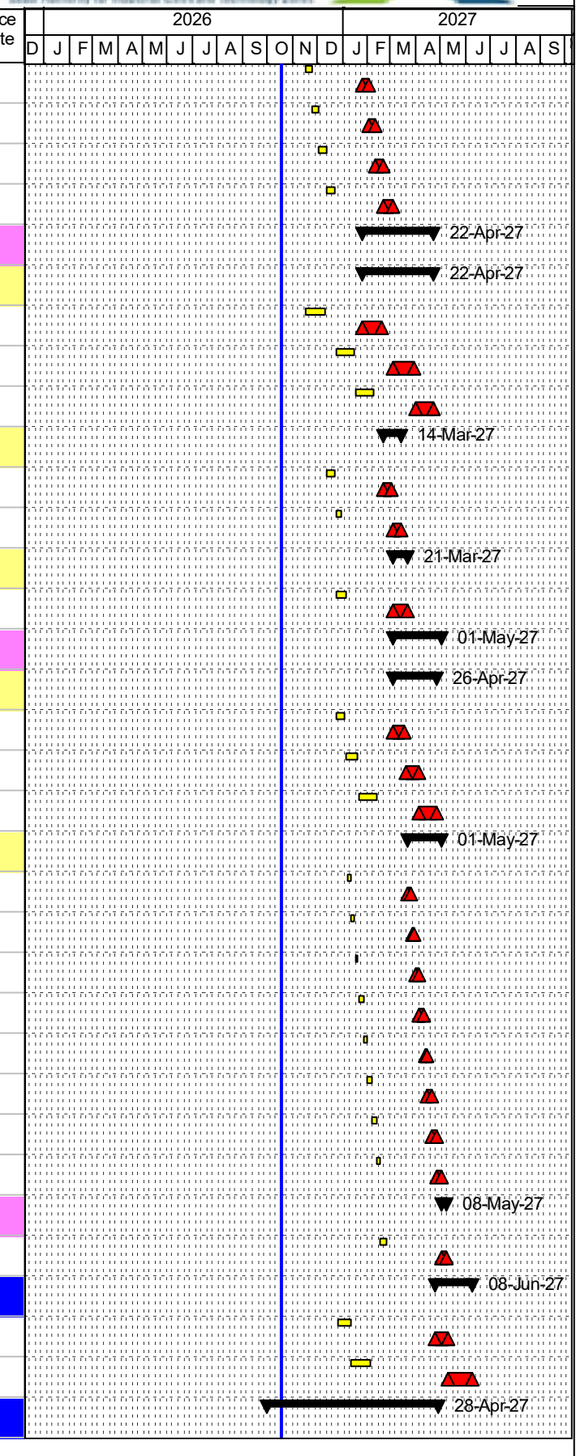


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SD-PO-100-P1	Excavation & Filling Works - PART 1 for Storm Drainage Ponds	56.00	01-Oct-26 A	07-Mar-27	4,093,463	0	3,684,116	3,684,116	0%	90%
CO-SD-PO-100-P2	Excavation & Filling Works - PART 2 for Storm Drainage Ponds	136.00	21-Mar-27	08-Apr-27	4,093,463	0	0	0	0%	0%
CO-SD-PO-110-P1	Finished Grouted Riprap - PART 1 for Storm Drainage Ponds	64.00	01-Mar-27 A	20-Mar-27	316,560	0	284,904	284,937	0%	90%
CO-SD-PO-110-P2	Finished Grouted Riprap - PART 2 for Storm Drainage Ponds	136.00	10-Apr-27	28-Apr-27	316,560	0	0	0	0%	0%
Boundary Fence and Gaurd Room		1488.00	01-Aug-26 A	06-Jun-27	14,546,224	1,579,329	4,618,279	4,562,248	10.62%	31.05%
Gaurd Room Work		352.00	11-Apr-27	06-Jun-27	1,497,270	0	0	0	0%	0%
Civil Work		120.00	11-Apr-27	27-Apr-27	67,559	0	0	0	0%	0%
A1000	Excavation Work For Guard Room Foundation	40.00	11-Apr-27	15-Apr-27	2,684	0	0	0	0%	0%
A1010	Pouring for Plain Concrete for Guard Room	8.00	17-Apr-27	17-Apr-27	2,684	0	0	0	0%	0%
A1020	Pouring R.C Footing for Guard Room	24.00	18-Apr-27	20-Apr-27	10,083	0	0	0	0%	0%
A1030	Pouring R.C Columns for Guard Room	24.00	21-Apr-27	24-Apr-27	3,675	0	0	0	0%	0%
A1040	Pouring Beams and Slab for Guard Room	24.00	25-Apr-27	27-Apr-27	48,433	0	0	0	0%	0%
Finishing Work		232.00	28-Apr-27	06-Jun-27	1,429,712	0	0	0	0%	0%
Architectural work		216.00	28-Apr-27	03-Jun-27	915,197	0	0	0	0%	0%
A1050	Brick Works for Architectural Works for Guard Rooms	48.00	28-Apr-27	04-May-27	21,591	0	0	0	0%	0%
A1060	Thermal & Moisture Protection Work for Architectural Works for Guard Rooms	40.00	05-May-27	10-May-27	12,891	0	0	0	0%	0%
A1070	Installation of Windows and Doors for Architectural Works for Guard Rooms	40.00	30-May-27	03-Jun-27	49,349	0	0	0	0%	0%
A1080	External Finshing Work (Walls and Floor) for Architectural Works for Guard Rooms	16.00	23-May-27	24-May-27	109,603	0	0	0	0%	0%
A1090	Internal Finshing Work (Walls,Floor and Ceiling) for Architectural Works for Guard	48.00	23-May-27	29-May-27	721,763	0	0	0	0%	0%
Mechanical Work		64.00	11-May-27	25-May-27	157,994	0	0	0	0%	0%
Drainage System		64.00	11-May-27	25-May-27	44,607	0	0	0	0%	0%
A1110	Installation of Sewage Piping System complete with joints, angles, reducer etc. for	32.00	11-May-27	20-May-27	33,221	0	0	0	0%	0%
A1120	Installation of all Sanitary Ware for Drainage System for Guard Rooms	32.00	22-May-27	25-May-27	11,386	0	0	0	0%	0%
Water Supply System		64.00	11-May-27	25-May-27	51,133	0	0	0	0%	0%
A1140	Installation of Water Piping System complete with joints, angles, reducer etc. for Water	24.00	11-May-27	13-May-27	13,381	0	0	0	0%	0%
A1180	Installation oF Water Supply Wares (Water Heater, Faucets, Etc..) for Water Supply	16.00	20-May-27	22-May-27	12,899	0	0	0	0%	0%
A1240	Installation of water tanks for Water Supply System for Guard Rooms	8.00	25-May-27	25-May-27	24,852	0	0	0	0%	0%
HVAC System		24.00	11-May-27	13-May-27	11,367	0	0	0	0%	0%
A1190	Installation of AC Units for HVAC System for Guard Rooms	8.00	13-May-27	13-May-27	4,142	0	0	0	0%	0%
A1200	Installation of AC Piping for HVAC System for Guard Rooms	16.00	11-May-27	12-May-27	7,225	0	0	0	0%	0%
Fire Fighting System		24.00	11-May-27	13-May-27	50,888	0	0	0	0%	0%
A1220	Installation & Testing of 2 hours Fire Fighting system for Fire Fighting System for Guard	16.00	11-May-27	12-May-27	29,586	0	0	0	0%	0%
A1230	Installation of Fire Extinguishers for Fire Fighting System for Guard Rooms	8.00	13-May-27	13-May-27	21,302	0	0	0	0%	0%
Electrical Work		88.00	11-May-27	29-May-27	335,219	0	0	0	0%	0%

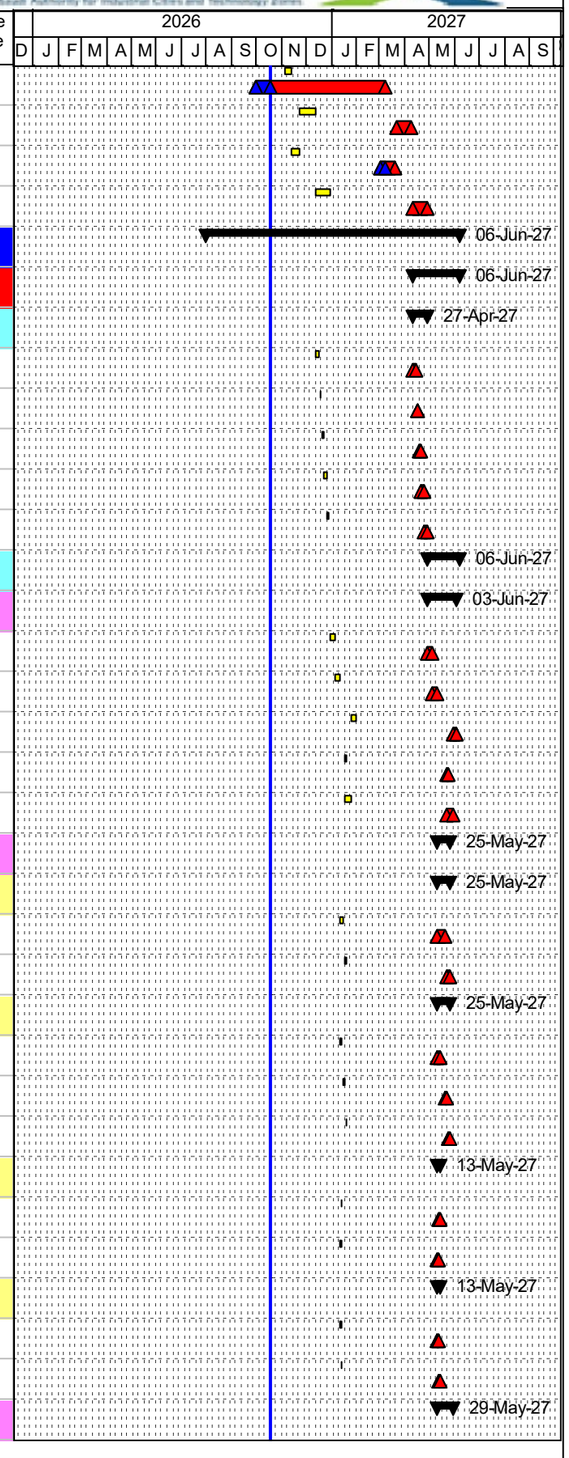


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
LV Power		72.00	11-May-27	26-May-27	107,021	0	0	0	0%	0%
A1250	Installation of Conduits and Cables for LV System for Gaurd Rooms	40.00	11-May-27	22-May-27	58,313	0	0	0	0%	0%
A1260	Install of Eletrical Finishes (DBs, Sockets and Lightings) and Termination for LV System for	32.00	23-May-27	26-May-27	48,708	0	0	0	0%	0%
Fire Detection And Alarm System		88.00	11-May-27	29-May-27	228,198	0	0	0	0%	0%
A1340	Installation of Conduits and Cables for Fire Alarm System for Gaurd Rooms	40.00	11-May-27	22-May-27	135,702	0	0	0	0%	0%
A1350	Installation of Fire Alarm Devices (AMCP, SD,HD, Sounder and Panels) for Fire Alarm	48.00	23-May-27	29-May-27	92,496	0	0	0	0%	0%
Furniture work		16.00	05-Jun-27	06-Jun-27	21,302	0	0	0	0%	0%
A1100	Office Chairs,Tables and Stand	16.00	05-Jun-27	06-Jun-27	21,302	0	0	0	0%	0%
Boundary Fence		1416.00	01-Aug-26 A	26-May-27	13,048,954	1,579,329	4,618,279	4,562,248	11.81%	34.53%
Boundary Fence - South		1104.00	01-Aug-26 A	05-Apr-27	3,343,920	947,307	548,551	973,654	28.33%	16.4%
Civil Work		488.00	01-Aug-26 A	02-Jan-27	1,036,327	947,307	492,560	917,633	91.41%	47.53%
CO-SU-FE-N-CI-100	Excavation Work For Boundary Fence South	128.00	01-Aug-26 A	03-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-110	Pouring for Plain Concrete For Boundary Fence South	112.00	08-Aug-26 A	13-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-120	Pouring R.C Footing For Boundary Fence South	96.00	15-Aug-26 A	22-Aug-26 A	312,570	312,570	312,570	312,570	100%	100%
CO-SU-FE-N-CI-130	Pouring R.C Columns For Boundary Fence South	128.00	26-Sep-26 A	20-Dec-26	472,304	472,304	47,230	472,304	100%	10%
CO-SU-FE-N-CI-140	Pouring Beams For Boundary Fence South	96.00	20-Dec-26	02-Jan-27	118,694	29,673	0	0	25%	0%
Finishing Work		664.00	13-Oct-26 A	05-Apr-27	2,307,593	0	55,991	56,021	0%	2.43%
Architictural work		496.00	13-Oct-26 A	08-Mar-27	1,666,313	0	55,991	56,021	0%	3.36%
CO-SU-FE-N-AR-100	Install Brick Work For Boundary Fence South	152.00	13-Oct-26 A	24-Jan-27	279,956	0	55,991	56,021	0%	20%
CO-SU-FE-N-AR-110	Insulation For Boundary Fence South	120.00	09-Feb-27	25-Feb-27	109,999	0	0	0	0%	0%
CO-SU-FE-N-AR-120	Install all the Relevant Cladding and Finishes For Boundary Fence South	72.00	27-Feb-27	08-Mar-27	1,276,358	0	0	0	0%	0%
Electrical Work		464.00	25-Jan-27	05-Apr-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-240	Installation of Conduits and Cables for Electricial Works For Boundary Fence South	104.00	25-Jan-27	08-Feb-27	154,292	0	0	0	0%	0%
CO-SU-FE-N-EL-250	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	168.00	13-Mar-27	05-Apr-27	486,987	0	0	0	0%	0%
Boundary Fence - West		1048.00	01-Aug-26 A	15-Apr-27	3,121,393	445,330	1,601,557	1,582,976	13.32%	47.89%
Civil Work		408.00	01-Aug-26 A	18-Oct-26 A	1,036,327	445,330	1,036,327	1,036,327	42.97%	100%
CO-SU-FE-N-CI-150	Excavation Work For Boundary Fence West	128.00	01-Aug-26 A	04-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-160	Pouring for Plain Concrete For Boundary Fence West	104.00	05-Aug-26 A	10-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-170	Pouring R.C Footing For Boundary Fence West	128.00	11-Aug-26 A	19-Aug-26 A	312,570	312,570	312,570	312,570	100%	100%
CO-SU-FE-N-CI-180	Pouring R.C Columns For Boundary Fence West	128.00	26-Sep-26 A	12-Oct-26 A	472,304	0	472,304	472,304	0%	100%
CO-SU-FE-N-CI-190	Pouring Beams For Boundary Fence West	96.00	12-Oct-26 A	18-Oct-26 A	118,694	0	118,694	118,694	0%	100%
Finishing Work		632.00	01-Oct-26 A	15-Apr-27	2,085,065	0	565,230	546,649	0%	24.49%
Architictural work		512.00	01-Oct-26 A	29-Mar-27	1,443,786	0	565,230	546,649	0%	33.92%
CO-SU-FE-N-AR-130	Install Brick Work For Boundary Fence West	128.00	01-Oct-26 A	04-Feb-27	279,956	0	265,958	265,919	0%	95%

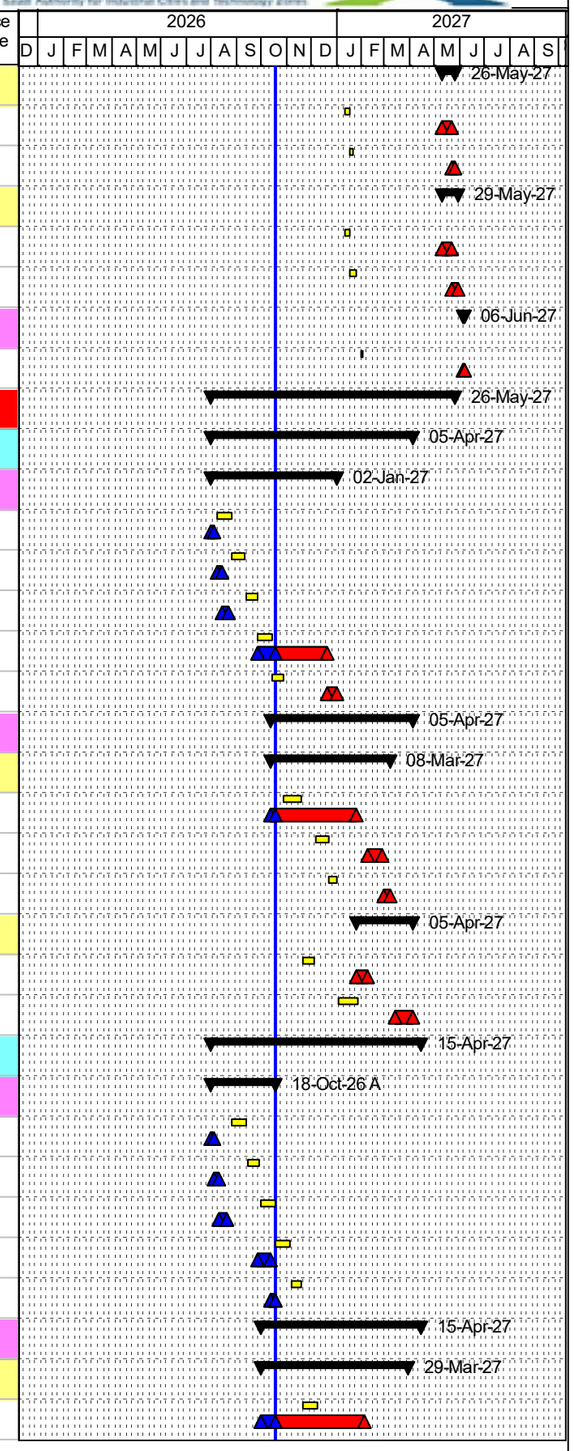


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SU-FE-N-AR-140	Insulation For Boundary Fence West	96.00	13-Oct-26 A	15-Mar-27	109,999	0	44,000	58,203	0%	40%
CO-SU-FE-N-AR-150	Install all the Relevant Cladding and Finishes For Boundary Fence West	96.00	16-Mar-27	29-Mar-27	1,053,831	0	255,272	222,527	0%	20%
Electrical Work		432.00	09-Feb-27	15-Apr-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-260	Installation of Conduits and Cables for Electricial Works For Boundary Fence West	64.00	09-Feb-27	17-Feb-27	154,292	0	0	0	0%	0%
CO-SU-FE-N-EL-270	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	72.00	06-Apr-27	15-Apr-27	486,987	0	0	0	0%	0%
Boundary Fence - North		896.00	01-Aug-26 A	12-Apr-27	3,239,721	132,759	1,493,863	1,338,341	3.97%	44.67%
Civil Work		360.00	01-Aug-26 A	16-Jan-27	1,036,327	132,759	917,633	917,633	12.81%	88.55%
CO-SU-FE-N-CI-200	Excavation Work For Boundary Fence North	128.00	01-Aug-26 A	04-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-210	Pouring for Plain Concrete For Boundary Fence North	104.00	05-Aug-26 A	11-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-220	Pouring R.C Footing For Boundary Fence North	128.00	11-Aug-26 A	02-Sep-26 A	312,570	0	312,570	312,570	0%	100%
CO-SU-FE-N-CI-230	Pouring R.C Columns For Boundary Fence North	128.00	26-Sep-26 A	12-Oct-26 A	472,304	0	472,304	472,304	0%	100%
CO-SU-FE-N-CI-240	Pouring Beams For Boundary Fence North	96.00	03-Jan-27	16-Jan-27	118,694	0	0	0	0%	0%
Finishing Work		480.00	01-Oct-26 A	12-Apr-27	2,203,394	0	576,229	420,708	0%	24.97%
Architictural work		384.00	01-Oct-26 A	05-Apr-27	1,562,115	0	576,229	420,708	0%	34.58%
CO-SU-FE-N-AR-160	Install Brick Work For Boundary Fence North	112.00	01-Oct-26 A	13-Feb-27	279,956	0	265,958	139,978	0%	95%
CO-SU-FE-N-AR-170	Insulation For Boundary Fence North	88.00	16-Mar-27	28-Mar-27	5,800	0	54,999	58,203	0%	50%
CO-SU-FE-N-AR-180	Install all the Relevant Cladding and Finishes For Boundary Fence North	48.00	11-Oct-26 A	05-Apr-27	1,276,358	0	255,272	222,527	0%	20%
Electrical Work		344.00	18-Feb-27	12-Apr-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-280	Installation of Conduits and Cables for Electricial Works For Boundary Fence North	56.00	18-Feb-27	25-Feb-27	154,292	0	0	0	0%	0%
CO-SU-FE-N-EL-290	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	48.00	06-Apr-27	12-Apr-27	486,987	0	0	0	0%	0%
Boundary Fence - East		1032.00	06-Sep-26 A	26-May-27	3,343,920	53,933	974,308	667,275	1.61%	29.14%
Civil Work		360.00	06-Sep-26 A	27-Jan-27	1,036,327	53,933	752,327	445,330	5.2%	72.6%
CO-SU-FE-N-CI-250	Excavation Work For Boundary Fence East	128.00	19-Dec-26 A	19-Dec-26 A	66,380	53,933	66,380	66,380	81.25%	100%
CO-SU-FE-N-CI-260	Pouring for Plain Concrete For Boundary Fence East	104.00	06-Sep-26 A	20-Sep-26 A	66,380	0	66,380	66,380	0%	100%
CO-SU-FE-N-CI-270	Pouring R.C Footing For Boundary Fence East	128.00	21-Sep-26 A	12-Oct-26 A	312,570	0	312,570	312,570	0%	100%
CO-SU-FE-N-CI-280	Pouring R.C Columns For Boundary Fence East	128.00	26-Sep-26 A	09-Jan-27	472,304	0	306,997	0	0%	65%
CO-SU-FE-N-CI-290	Pouring Beams For Boundary Fence East	80.00	17-Jan-27	27-Jan-27	118,694	0	0	0	0%	0%
Finishing Work		376.00	01-Oct-26 A	26-May-27	2,307,593	0	221,981	221,946	0%	9.62%
Architictural work		336.00	01-Oct-26 A	20-May-27	1,666,313	0	221,981	221,946	0%	13.32%
CO-SU-FE-N-AR-190	Install Brick Work For Boundary Fence East	88.00	08-Oct-26 A	22-Apr-27	279,956	0	111,983	111,947	0%	40%
CO-SU-FE-N-AR-200	Insulation For Boundary Fence East	64.00	01-Oct-26 A	12-Oct-26 A	109,999	0	109,999	109,999	0%	100%
CO-SU-FE-N-AR-210	Install all the Relevant Cladding and Finishes For Boundary Fence East	72.00	05-May-27	20-May-27	1,276,358	0	0	0	0%	0%
Electrical Work		192.00	24-Apr-27	26-May-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-300	Installation of Conduits and Cables for Electricial Works For Boundary Fence East	80.00	24-Apr-27	04-May-27	154,292	0	0	0	0%	0%

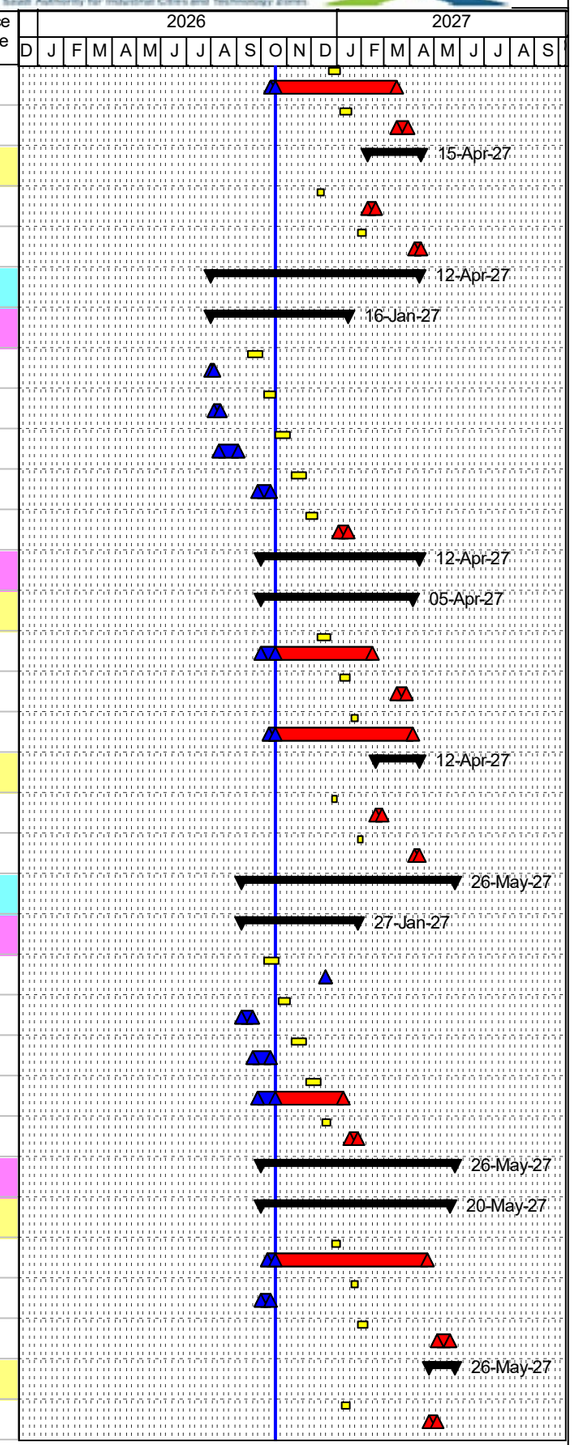

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SU-FE-N-EL-310	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	40.00	22-May-27	26-May-27	486,987	0	0	0	0%	0%
Testing and Comissioning		200.00	07-Jun-27	05-Jul-27	0	0	0	0	0%	0%
Infrastructure Networks		136.00	12-Jun-27	30-Jun-27	0	0	0	0	0%	0%
Low Voltage Network		96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
TC-LV-100	Testing and Commissioning of Low Voltage Network	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
Irrigation Network		96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
T/C-IR	Testing and Commissioning of Irrigation Network	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
TSE Network		96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
T/C-TSE-10	Testing and Commissioning of TSE Network	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
Potable Water Network		96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
T/C-PW	Testing and Commissioning of Potable Water Network	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
Sewage Network		96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
T/C-SW	Testing and Commissioning of Sewage Network	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
Storm Drainage Network		96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
T/C-SD	Testing and Commissioning of Storm Drainage Ponds and Storm Drainage Network	96.00	17-Jun-27	30-Jun-27	0	0	0	0	0%	0%
Street Lighting Network		96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
T/C-SL	Testing and Commissioning of Street Lighting Network	96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
Telecom and Light Current Network		96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
T/C-TE	Testing and Commissioning of Telecom and Light Current Networks	96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
Medium Voltage Network		96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
T/C-MV	Testing and Commissioning of Medium Voltage Network	96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
Road Works		96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
T/C-RD	Testing and Commissioning of Road Works	96.00	12-Jun-27	24-Jun-27	0	0	0	0	0%	0%
Utility Buildings		200.00	07-Jun-27	05-Jul-27	0	0	0	0	0%	0%
T/C-CTV	Testing and Commissioning of Guard Room and Boundary Fence	128.00	07-Jun-27	24-Jun-27	0	0	0	0	0%	0%
T/C-CTV10	Testing and Commissioning of Utility Buildings	128.00	17-Jun-27	05-Jul-27	0	0	0	0	0%	0%
T/C-CTV20	Testing and Commissioning of Softscape And Planting	128.00	09-Jun-27	27-Jun-27	0	0	0	0	0%	0%
Handing over and close out		192.00	12-Jun-27	08-Jul-27	0	0	0	0	0%	0%
As-Built		192.00	12-Jun-27	08-Jul-27	0	0	0	0	0%	0%
HO-100	Submission As-Built Drawing For Sewage Network	80.00	17-Jun-27	28-Jun-27	0	0	0	0	0%	0%
HO-130	Submission As-Built Drawing For Pond	80.00	17-Jun-27	28-Jun-27	0	0	0	0	0%	0%
HO-140	Submission As-Built Drawing For Roads Network	80.00	12-Jun-27	22-Jun-27	0	0	0	0	0%	0%
HO-150	Submission As-Built Drawing For Street Lighting Network	80.00	12-Jun-27	22-Jun-27	0	0	0	0	0%	0%

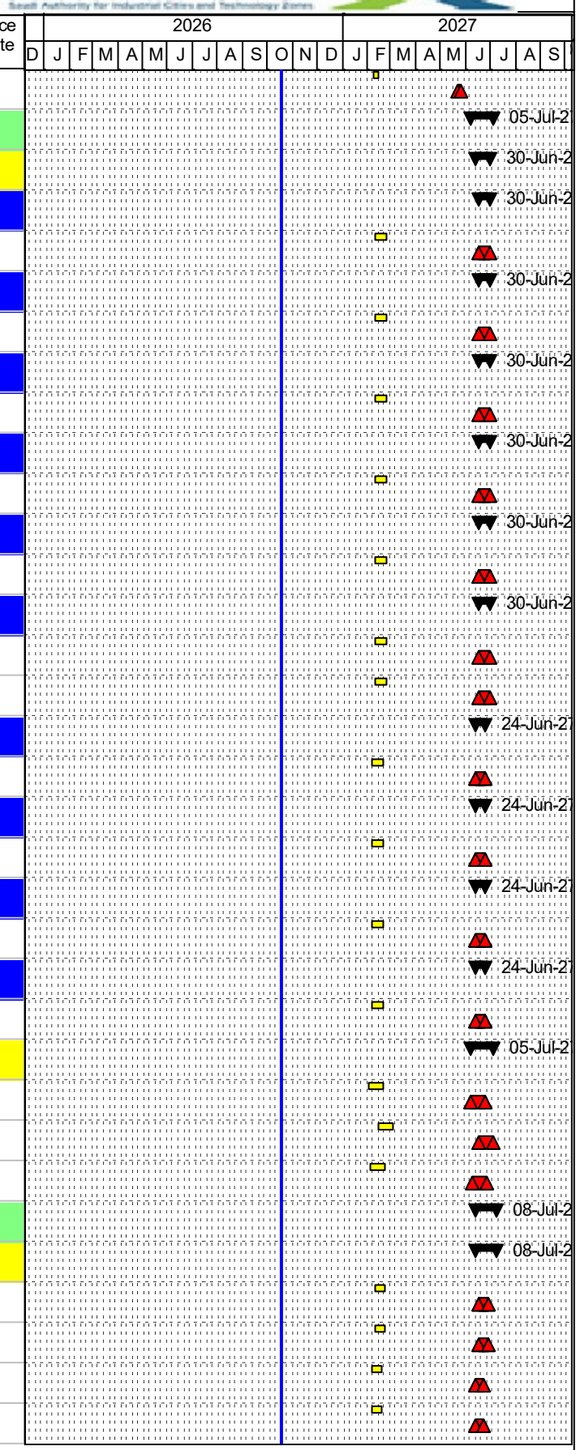


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 19-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
HO-160	Submission As-Built Drawing For Telecom and Light Current Networks	80.00	12-Jun-27	22-Jun-27	0	0	0	0	0%	0%
HO-170	Submission As-Built Drawing For Medium Voltage Network	56.00	01-Jul-27	08-Jul-27	0	0	0	0	0%	0%
HO-180	Submission As-Built Drawing For Irrigation Network	80.00	17-Jun-27	28-Jun-27	0	0	0	0	0%	0%
HO-190	As-Built Drawing For Potable Water Network	56.00	01-Jul-27	08-Jul-27	0	0	0	0	0%	0%
HO-200	Submission As-Built Drawing For Storm Network	80.00	17-Jun-27	28-Jun-27	0	0	0	0	0%	0%
HO-210	Submission As-Built Drawing For Utility Buildings	64.00	27-Jun-27	05-Jul-27	0	0	0	0	0%	0%
De-Mobilization Works		144.00	14-Jun-27	04-Jul-27	0	0	0	0	0%	0%
HO-120	Remove material stock & Storage area	64.00	26-Jun-27	04-Jul-27	0	0	0	0	0%	0%
HO-220	Removing Portable Caravan	56.00	17-Jun-27	24-Jun-27	0	0	0	0	0%	0%
HO-230	Remove Temporary Car Shades	80.00	14-Jun-27	24-Jun-27	0	0	0	0	0%	0%
Handing Over		160.00	16-Jun-27	08-Jul-27	0	0	0	0	0%	0%
HO-110	Final Testing Work	56.00	01-Jul-27	08-Jul-27	0	0	0	0	0%	0%
HO-240	Final Walkthrough and Inspection	64.00	16-Jun-27	24-Jun-27	0	0	0	0	0%	0%
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	64.00	16-Jun-27	24-Jun-27	0	0	0	0	0%	0%
HO-260	Review FIR Approval to ensure compliance with the actual status	64.00	16-Jun-27	24-Jun-27	0	0	0	0	0%	0%
HO-270	Review the sample drawing to ensure compliance with the actual status	64.00	16-Jun-27	24-Jun-27	0	0	0	0	0%	0%
HO-280	Punch List Completion	64.00	26-Jun-27	04-Jul-27	0	0	0	0	0%	0%

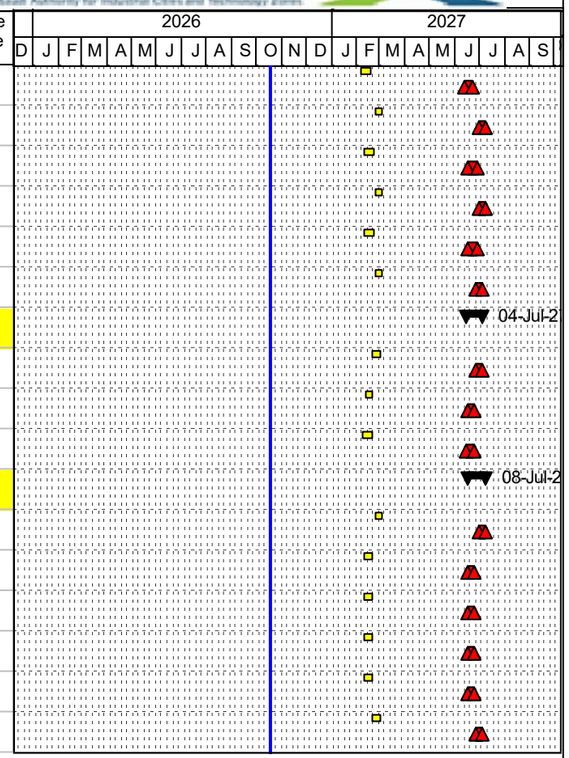

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
19-Oct-26	Third Industrial City		
