Completion of the Infrastructure Development of the First Phase, Third Industrial City, Jeddah

إستكمال شبكات البنية التحتية بالمدينة الصناعية الثالثة بجدة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	REVISED COMPLETION
MODON	Al-Rawaf Contracting	Egis	Shuaib A. Alshuaibi	29-Jul-2024	26-Sep-2026

Scope: sewage, storm water (with ponds and open channels), irrigation and potable water networks, 13.8 kV cable, street lighting, telecom ducts, and internal and external roads with asphalt and sidewalks.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 18-Oct-2026 the project is 98.96% complete against 99.93% planned, behind by 0.97% (SPI 0.99). Only 0.05% was gained this week (25 of 48,045 man-hours, in zones Z05, Z09 and Z10). The revised completion date of 26-Sep-2026 has passed.

PHYSICAL % COMPLETE

99.0% / 99.9% plan

▼ SPI 0.99 −0.97%

PROGRESS THIS WEEK

+0.05% / 0.00% plan

25 man-hours earned; the plan has no progress left for this week

CONTRACT TIME ELAPSED

103% · day 811 of 789

▼ P6 finish 08-Dec-2026

INVOICED TO DATE (GROSS)

78.3% · 250.2M SAR


24 invoices, last period ends 31-Aug-2026

The revised completion date has passed, and the forecasts finish the project 50 to 73 days late.

The contract completion was extended by two months to 26-Sep-2026 (CCO 2, approved 29-Jun-2026). The weekly report now forecasts completion on 15-Nov-2026, 50 days late. The P6 extract in the same workbook finishes the project on 08-Dec-2026 with −73 days of total float; the previous extract finished on 01-Dec-2026 with −66 days. The remaining work is in Main Roads (MR), zones Z02, Z04, Z05 and Z08, the new-scope items and close-out, and the testing and commissioning register shows 0% for every system.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet; the 18-Oct-2026 point is from the Progress sheet.

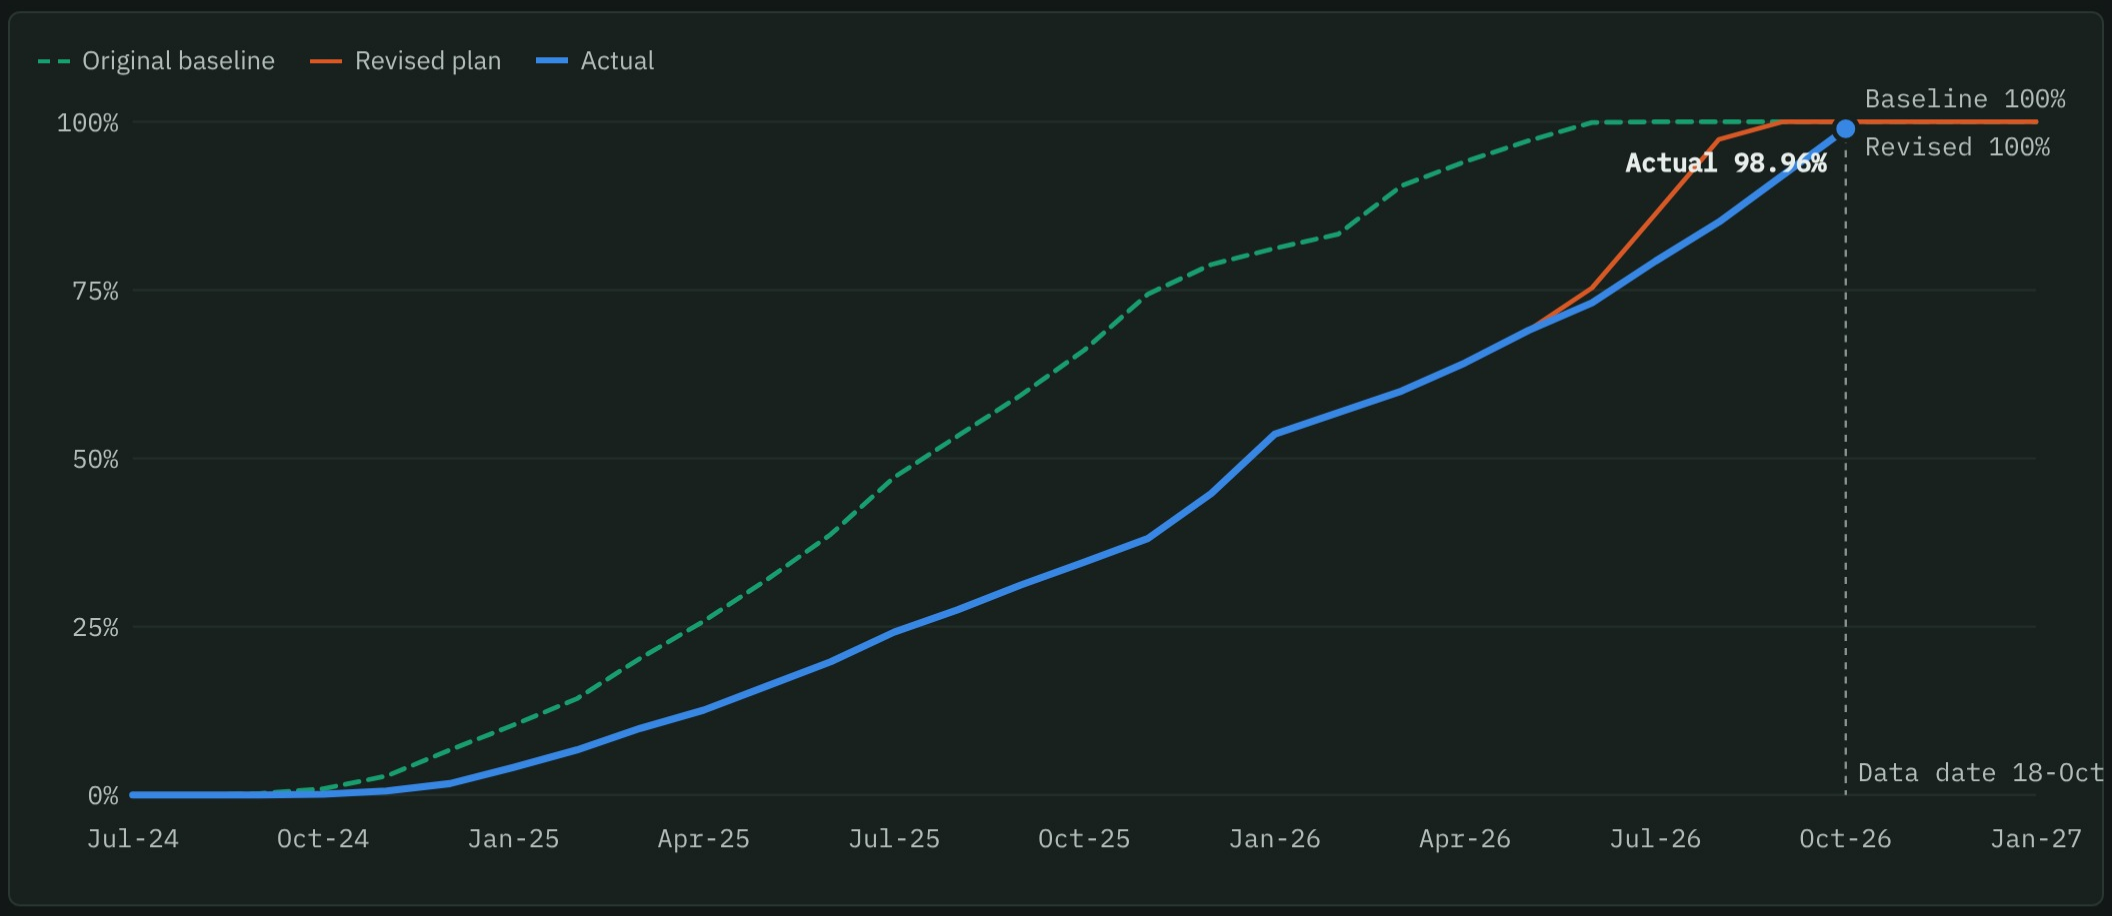

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
Previous P6 extract	99.93	98.91	-1.02	–	0.99
18-Oct-2026	**99.93**	**98.96**	**-0.97**	**+0.05**	**0.99**

Only the 18-Oct-2026 report was used. The first row is the earlier P6 extract kept in the same workbook (47,522 of 48,045 man-hours earned); the workbook does not give its date. Earlier weeks are not shown. The Physical-Chart Data sheet shows 100% actual at the end of September, which the Progress sheet contradicts, so that point is left out.

Progress by phase

Physical progress to date by construction work package, weighted by budgeted man-hours (48,045 in total). Engineering, procurement and close-out carry no man-hours; on the cost basis engineering and procurement are 100% earned and close-out is 95.2%.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
MR	36.5%	99.9%	99.4%	-0.6	0.99	▼ Behind
Pond and Swales	7.7%	100.0%	100.0%	0.0	1.00	✓ Complete
Z05	7.7%	100.0%	93.7%	-6.3	0.94	▼ Behind
Z02-2	6.4%	100.0%	100.0%	0.0	1.00	✓ Complete
Z06	6.3%	100.0%	99.6%	-0.4	1.00	▼ Behind
Z01	5.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Z02-1	5.6%	99.4%	100.0%	+0.6	1.01	✓ Complete
Z07	5.6%	100.0%	100.0%	0.0	1.00	✓ Complete
Z07-1	4.3%	100.0%	100.0%	0.0	1.00	✓ Complete
Z10	3.2%	100.0%	99.0%	-1.0	0.99	▼ Behind
High Mast	2.5%	100.0%	100.0%	0.0	1.00	✓ Complete
Z09	1.8%	99.8%	99.2%	-0.6	0.99	▼ Behind

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
New Scope	1.3%	100.0%	96.4%	-3.6	0.96	▼ Behind
Z13	1.1%	100.0%	100.0%	0.0	1.00	✓ Complete
Z02	1.0%	100.0%	94.4%	-5.6	0.94	▼ Behind
Z03	0.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Z08	0.7%	100.0%	87.3%	-12.7	0.87	▼ Behind
Z04	0.7%	100.0%	92.0%	-8.0	0.92	▼ Behind
Z11	0.7%	100.0%	99.7%	-0.3	1.00	▼ Behind
ELDREES	0.3%	100.0%	100.0%	0.0	1.00	✓ Complete
CCTV	0.0%	100.0%	100.0%	0.0	1.00	✓ Complete
Total	100%	**99.93%**	**98.96%**	**-0.97**	**0.99**	▼ Behind

The P6 schedule statistics (data date 18-Oct-2026) count 9,236 activities: 9,020 completed, 86 in progress and 130 not started, with 44 activities behind. The P6 extract finishes the project on 08-Dec-2026 with −73 days of total float.

Scope of work: quantities

Revised BOQ quantity and installed quantity for each network, from the Major Quantities sheet of the 18-Oct-2026 weekly report. The sheet has no previous-week column, so "This week" shows "–". Every listed item is reported as 100% installed.

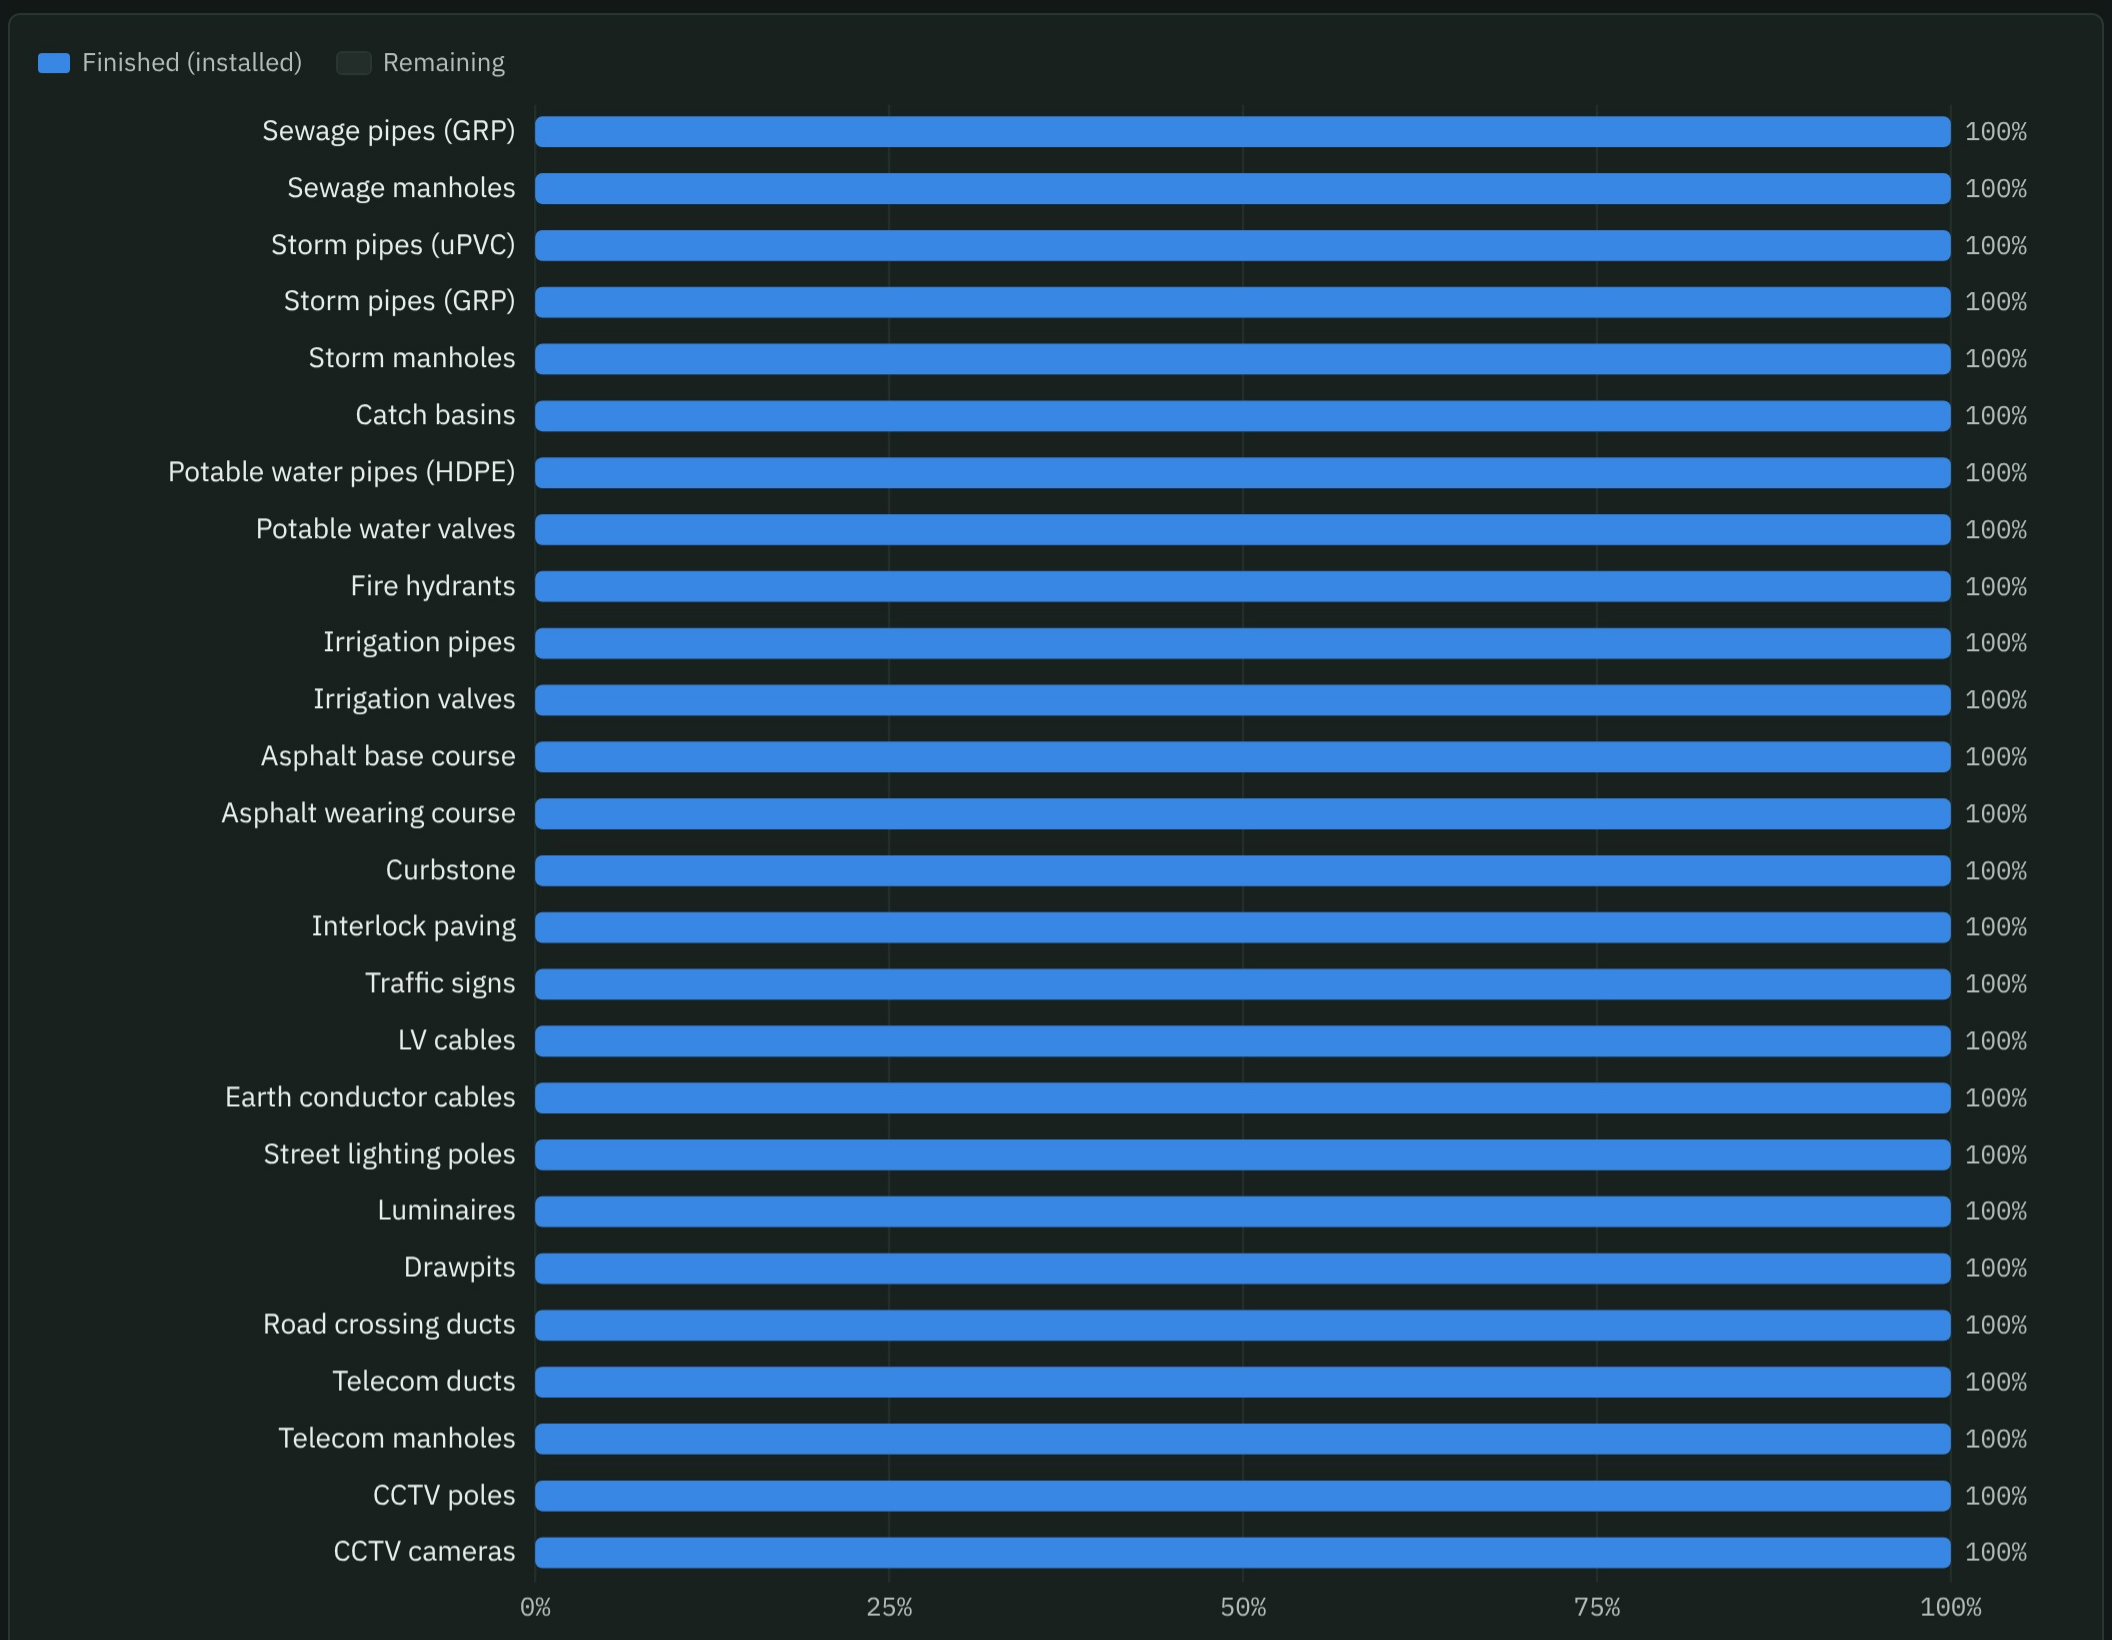

SCOPE ITEM	SIZE / TYPE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Sewage pipes (GRP)	DN 200	LM	21,379	21,379	–	0	100.0%	–
	DN 250	LM	4,579	4,579	–	0	100.0%	–
	DN 300	LM	204.6	204.6	–	0	100.0%	–
	DN 400	LM	531.9	531.9	–	0	100.0%	–
	Total	LM	**26,695**	**26,695**	–	**0**	**100.0%**	–
Sewage manholes	All sizes	EA	355	355	–	0	100.0%	–
Storm pipes (uPVC)	DN 300	LM	29,080	29,080	–	0	100.0%	–
Storm pipes (GRP)	DN 400	LM	11,758	11,758	–	0	100.0%	–
	DN 500	LM	4,240	4,240	–	0	100.0%	–
	DN 600	LM	5,966	5,966	–	0	100.0%	–
	DN 700	LM	5,347	5,347	–	0	100.0%	–
	DN 800	LM	6,312	6,312	–	0	100.0%	–

SCOPE ITEM	SIZE / TYPE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
	DN 900	LM	7,736	7,736	–	0	100.0%	–
	DN 1000	LM	2,856	2,856	–	0	100.0%	–
	DN 1100	LM	1,771	1,771	–	0	100.0%	–
	DN 1200	LM	8,972	8,972	–	0	100.0%	–
	DN 1400	LM	425.4	425.4	–	0	100.0%	–
	Total	LM	**55,383**	**55,383**	–	**0**	**100.0%**	–
Storm manholes	DN 1200	EA	203	203	–	0	100.0%	–
	DN 1500	EA	418	418	–	0	100.0%	–
	DN 2000	EA	219	219	–	0	100.0%	–
	Total	EA	**840**	**840**	–	**0**	**100.0%**	–
Catch basins	Single	EA	1,007	1,007	–	0	100.0%	–
	Double	EA	761	761	–	0	100.0%	–
	Total	EA	**1,768**	**1,768**	–	**0**	**100.0%**	–
Potable water pipes (HDPE)	DN 160	LM	8,045	8,045	–	0	100.0%	–
	DN 225	LM	2,000	2,000	–	0	100.0%	–
	DN 315	LM	215	215	–	0	100.0%	–
	DN 450	LM	1,890	1,890	–	0	100.0%	–
	Total	LM	**12,150**	**12,150**	–	**0**	**100.0%**	–
Potable water valves	Gate valves	EA	77	77	–	0	100.0%	–
	Butterfly valves	EA	2	2	–	0	100.0%	–
	Wash-out valves	EA	3	3	–	0	100.0%	–
	Air valves	EA	1	1	–	0	100.0%	–
	Total	EA	**83**	**83**	–	**0**	**100.0%**	–
Fire hydrants	ULFM 150	EA	193	193	–	0	100.0%	–
Irrigation pipes	HDPE DN 125	LM	24,479	24,479	–	0	100.0%	–
	HDPE DN 250	LM	28,362	28,362	–	0	100.0%	–
	HDPE DN 315	LM	7,061	7,061	–	0	100.0%	–
	HDPE DN 450	LM	8,870	8,870	–	0	100.0%	–
	HDPE DN 630	LM	2,221	2,221	–	0	100.0%	–
	GRP DN 800	LM	1,340	1,340	–	0	100.0%	–
	Total	LM	**72,333**	**72,333**	–	**0**	**100.0%**	–
Irrigation valves	Gate valves	EA	455	455	–	0	100.0%	–
	Butterfly valves	EA	61	61	–	0	100.0%	–
	Wash-out valves	EA	29	29	–	0	100.0%	–
	Air valves	EA	44	44	–	0	100.0%	–
	Total	EA	**589**	**589**	–	**0**	**100.0%**	–
Asphalt base course	Grading I	m^3	1,735	1,735	–	0	100.0%	–
Asphalt wearing course	Grading I	m^3	1,240	1,240	–	0	100.0%	–

SCOPE ITEM	SIZE / TYPE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Curbstone	Type K1-D	LM	15,100	15,100	–	0	100.0%	–
	Type L1	LM	1,972	1,972	–	0	100.0%	–
	Depressed K2	LM	750	750	–	0	100.0%	–
	Total	LM	**17,822**	**17,822**	–	**0**	**100.0%**	–
Interlock paving	All	m²	1,576	1,576	–	0	100.0%	–
Traffic signs	Single post	EA	31	31	–	0	100.0%	–
	Double post	EA	4	4	–	0	100.0%	–
	Total	EA	**35**	**35**	–	**0**	**100.0%**	–
LV cables	4C×6 mm²	LM	1,826	1,826	–	0	100.0%	–
	4C×10 mm²	LM	2,092	2,092	–	0	100.0%	–
	4C×16 mm²	LM	896	896	–	0	100.0%	–
	4C×25 mm²	LM	7,396	7,396	–	0	100.0%	–
	4C×35 mm²	LM	11,757	11,757	–	0	100.0%	–
	4C×50 mm²	LM	120	120	–	0	100.0%	–
	4C×150 mm²	LM	1,500	1,500	–	0	100.0%	–
	Total	LM	**25,587**	**25,587**	–	**0**	**100.0%**	–
Earth conductor cables	6 mm²	LM	4,208	4,208	–	0	100.0%	–
	16 mm²	LM	20,049	20,049	–	0	100.0%	–
	70 mm²	LM	2,700	2,700	–	0	100.0%	–
	Total	LM	**26,957**	**26,957**	–	**0**	**100.0%**	–
Street lighting poles	12 m, 2 arms	EA	10	10	–	0	100.0%	–
	12 m, 1 arm	EA	220	220	–	0	100.0%	–
	Total	EA	**230**	**230**	–	**0**	**100.0%**	–
Luminaires	LED 150 W	EA	240	240	–	0	100.0%	–
	LED 342 W	EA	88	88	–	0	100.0%	–
	LED 208 W	EA	102	102	–	0	100.0%	–
	Total	EA	**430**	**430**	–	**0**	**100.0%**	–
Drawpits	600×600	EA	783	783	–	0	100.0%	–
	900×900	EA	151	151	–	0	100.0%	–
	900×1800	EA	18	18	–	0	100.0%	–
	Total	EA	**952**	**952**	–	**0**	**100.0%**	–
Road crossing ducts	UPVC 160 mm	LM	1,116	1,116	–	0	100.0%	–
Telecom ducts	6-way, 50 mm	LM	8,100	8,100	–	0	100.0%	–
Telecom manholes	Type 1	EA	90	90	–	0	100.0%	–
CCTV poles	All	EA	18	18	–	0	100.0%	–
CCTV cameras	All	EA	82	82	–	0	100.0%	–

Revised quantities are far below the original BOQ for roads

The revised BOQ, still marked "under review", sets each total equal to the installed quantity. For road works it is a small part of the original BOQ: asphalt wearing course 1,240 of 63,689 m³, precast kerb K1-D 15,100 of 187,209 m, kerb L1 1,972 of 123,805 m and interlock 1,576 of 59,537 m².

Medium-voltage works revised to zero

The 13.8 kV cable (30,720 m in the original BOQ), its joints and terminations, the 950 m duct bank, the normally-open RMUs and the three street-lighting substations and RMUs all have a revised quantity of 0. They are left out of the table.

Milestones

Milestone dates from the Milestones sheet and finish dates from the P6 extract in the Progress sheet. The two give different completion forecasts, so both are shown.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	29-Jul-2024	29-Jul-2024 (actual)	–	–	✓ Done
Complete mobilisation	03-Sep-2024	26-Oct-2024 (actual)	–	–	✓ Done
Existing-condition survey and final reports	07-Sep-2025	23-Jul-2025 (actual)	–	–	✓ Done
Complete mechanical works	01-Oct-2025	27-Jun-2026	–	–	? Not updated
Complete steel structure erection	02-Jul-2026	25-Feb-2026	–	–	? Not updated
Complete earthworks	07-Jul-2026	02-Jul-2026	–	–	? Not updated
Complete all civil works	07-Jul-2026	02-Jul-2026	–	–	? Not updated
Complete demobilisation	23-Jul-2026	20-Jul-2026	–	–	? Not updated
All works complete, ready for initial handover	28-Jul-2026	28-Jul-2026	–	–	? Not updated
Construction (P6)	26-Sep-2026	–	10-Nov-2026	−45	▼ Late
Close-out (P6)	26-Sep-2026	–	08-Dec-2026	−63	▼ Late
Project completion	26-Sep-2026 (original 28-Jul-2026)	15-Nov-2026 (+50 d)	08-Dec-2026	−73	▼ Late

The two completion forecasts are 23 days apart, and the interim milestones have not been updated.

The weekly report forecasts completion on 15-Nov-2026; the P6 extract in the same workbook finishes on 08-Dec-2026. Six interim milestones still carry forecast dates between February and July 2026 that have already passed, with no actual dates recorded. The baseline for project completion is the revised date after the two-month extension (CCO 2).

Procurement of key materials

Delivered quantity against the revised BOQ quantity. Source: Major Quantities sheet, weekly report 18-Oct-2026.

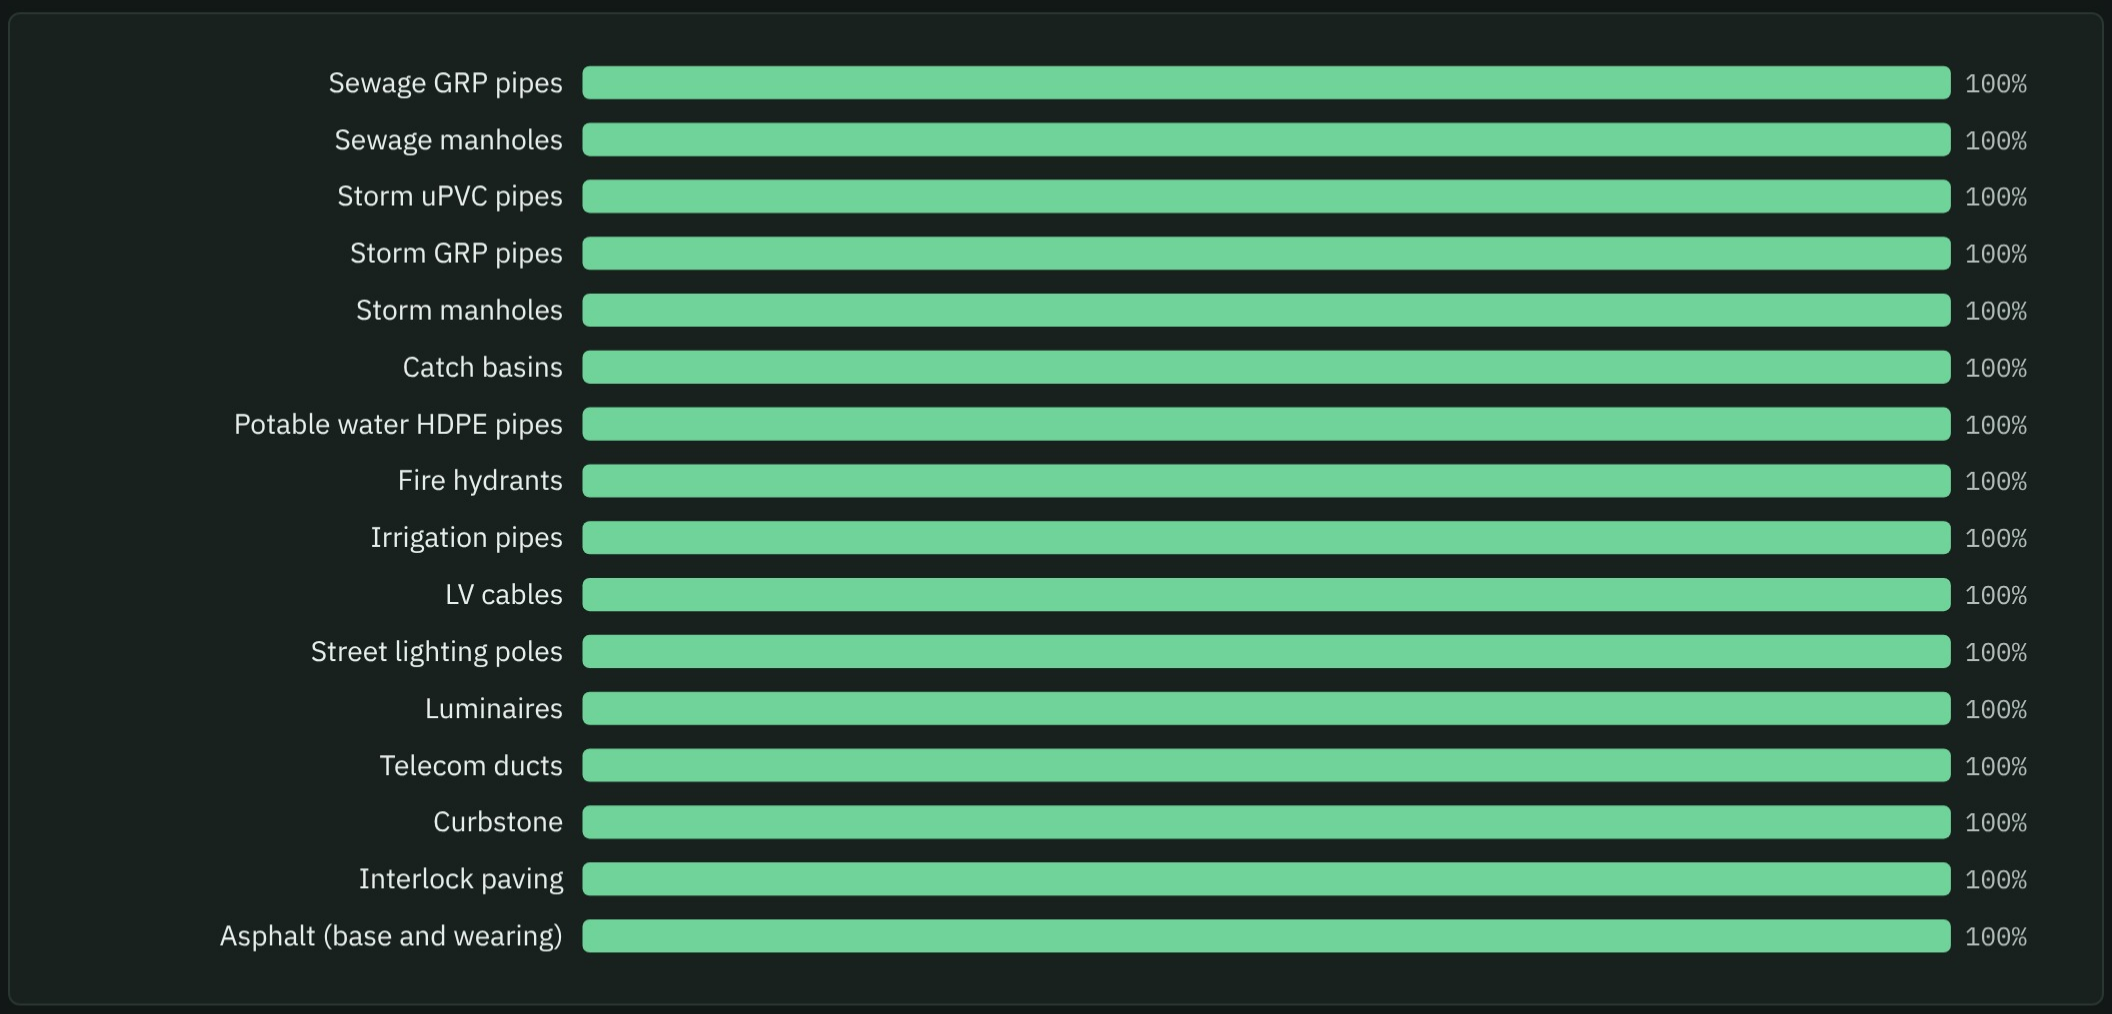

Deliveries complete against the revised quantities


Every material in the Major Quantities sheet is 100% delivered and installed against its revised quantity. The procurement summary still shows 12 of 20 purchase orders issued, 8 remaining and 10 materials on site.

The Procurement sheet is out of date

The detailed Procurement sheet, hidden in the workbook, still gives delivery rates from an earlier stage, for example kerbs 4.8%, interlock 6.9% and fire hydrants 79%. Nine of its 42 items are marked "to be descoped".

Manpower

Monthly manual head count, planned vs actual, August 2024 to January 2026, the last month with an actual figure. Source: Manpower sheet.

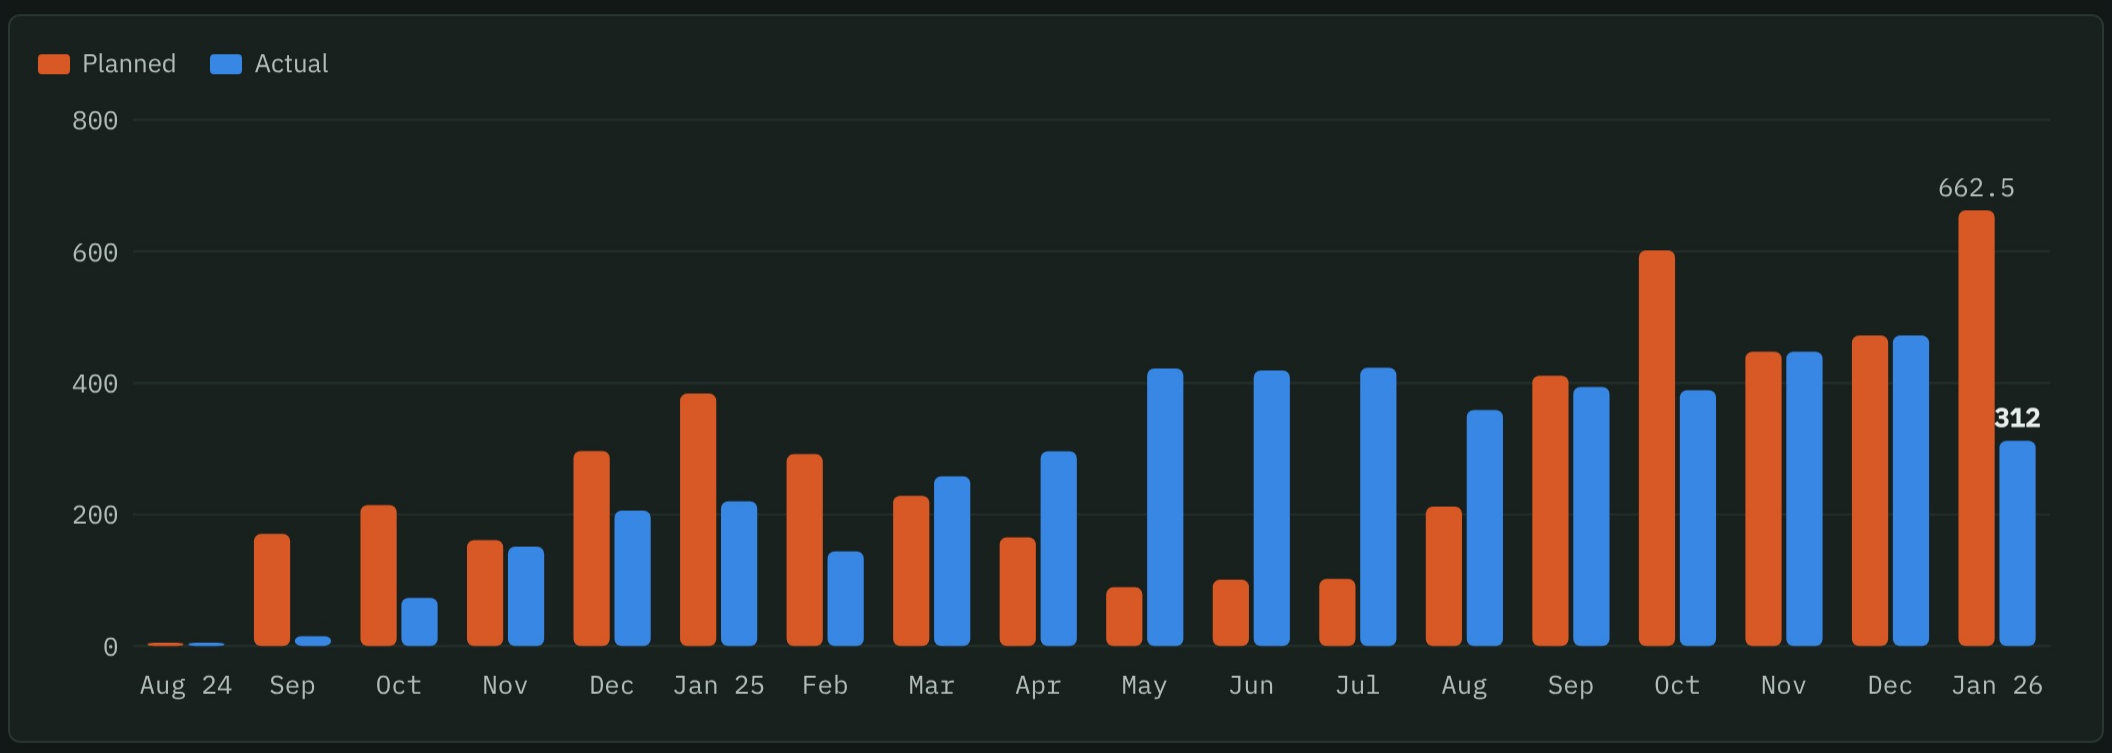

January 2026: 312 against 662.5 planned. The November and December 2025 actuals are identical to the planned values. For October 2026 the resources panel reports 1,092 manual and 92 non-manual staff (1,184) with no plan for the month, while the trade breakdown lists 389 workers against 602 planned. Equipment on site: 135 against 167 planned, 3 idle.

Cost and invoicing

Contract value

Storm water network	161,546,482
Roads, paving, markings and signage	67,012,837
TSE (irrigation) network	49,057,170
Industrial sewage network	19,706,041
Electrical works	13,120,144
Potable water network	9,302,202
BOQ total (excl. VAT)	**319,744,876**
Contract value incl. 15% VAT	367,706,607
Change orders	2 (no cost)

All values in SAR. CCO 1 (revised BOQ, approved 23-Jul-2025) and CCO 2 (two-month extension of time, approved 29-Jun-2026) do not change the contract value.

Invoices

Invoices submitted	24
Gross value	250,214,133
Advance payment recovery	25,021,413
Deductions and penalties	260,000
Retention	0
Net incl. VAT	258,711,628
PM-approved (23 invoices)	246,537,903
Paid (recorded)	0
Earned value to date	316,125,890
FIR value to date	278,116,807

Invoicing is 78.3% of the contract value against 98.96% physical progress. The log records no payments, and invoices #22 and #23 are marked "under review" although PM approval dates are entered.

Health, safety and quality

Safety Score 0.82

Safe man-hours (cumulative)	2,210,362
Man-hours this week	22,920
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses (cumulative)	11
Vehicle incidents (cumulative)	1
Inductions / toolbox talks	223 / 3,335

This week: 8 toolbox talks and 2 internal trainings. The latest HSE site inspection in the workbook is dated 26-Jul-2026.

Quality Score 0.91

NCRs issued / closed / open	129 / 96 / 33
Site instructions issued / open	187 / 1
MIRs issued / open	357 / 2
FIRs issued / pending	31,551 / 1,488
RFIs issued / open	238 / 0
Shop drawings submitted / total	2,520 / 2,539
Material submittals pending	35 of 78

QC inspection 18-Oct-2026. Average NCR closing time is 7 days.

Open issues and risks

ISSUE	OWNER	DETAIL
As-built drawings	MODON	The as-built drawings do not match site conditions, so connection areas need excavation to locate services.
Utility corridor cross-sections	MODON	The cross-section in the contract documents does not match the site; each road needs its own approved cross-section.
Factory inside the work area	MODON	A factory lies within the work area, so the networks on these roads must be re-routed. No official consultant response yet.
Existing lines change the scope	MODON	Existing lines found by the survey change the network layout and reduce the scope, as happened with the industrial sewage and water networks.
Existing MV lines	MODON	Existing MV lines change the scope, and MV as-built data has not been given to the contractor.
Box culvert, Zone 01	Contractor	More existing utilities than expected; the work continues slowly and carefully.
Box culvert, Zone 06	MODON	The excavation conflicts with a factory and its entrance.

All open items in the issue log were raised between September and December 2024 and are still marked Active; the log has no newer entries.

Data notes

- This report uses only the weekly report with data date 18-Oct-2026, the single file in this week's folder. Its Milestones sheet gives the contract week as 116, which is used as the report week; whole weeks from site handover would give 115.
- Site photos: the only photos in the upload are in the hidden Weekly Photos sheet, and their camera stamps date from 24 to 30 June 2025, so they are not shown as this week's photos.
- The Physical-Chart Data sheet shows 100% actual progress at 30-Sep-2026, while the Progress sheet gives 98.96% at 18-Oct-2026. The revised plan reaches 100% at 30-Sep-2026, but the Progress sheet gives 99.93% planned to date. The original baseline is built on 69,385 man-hours, the revised plan on 48,045.
- The Progress sheet holds two P6 extracts: one finishing 01-Dec-2026 (–66 days, 47,522 man-hours earned) and one finishing 08-Dec-2026 (–73 days, 47,547 man-hours). The second matches this week's figures and is used here. The weekly report forecast (15-Nov-2026) matches neither.

- Milestones 6 to 11 keep forecast dates from February to July 2026 that have passed without actual dates. "Complete steel structure erection for all blocks" does not fit an infrastructure project.
- Manpower: monthly actuals stop at January 2026, and the November and December 2025 actuals equal the planned values. The October 2026 head count (1,092 manual) does not match the trade breakdown (389).
- Major Quantities: the revised BOQ equals the installed quantity for every item. "Fire hydrant" (193) and "Fire hydrant ULFM 150" (193) look like the same item listed twice, and the 70 mm² earth conductor row appears twice; each is counted once here.
- The invoice summary shows 0 submitted invoices while the log lists 24. The FIR value sheet numbers its last entries as weekly reports 104 to 106 but dates them 04, 05 and 06-Oct-2026.
- The hidden Conclusion and SOURCE sheets still carry old figures (59.9% planned, 26.1% actual, Q2 2025 targets) and were not used. The Testing sheet shows 0% for all systems, with planned dates in 2025.

Compiled 28-Oct-2026 from the weekly report with data date 18-Oct-2026.
