Ready-Built Factories Program, Package 3: 20 Factories of 900 m² in Hail

برنامج المصانع الجاهزة و المنتجات الجديدة الحزمة الثالثة (المحفظة الاستثمارية) - حائل 20 مصنع 900 متر

CLIENT	WEEKLY REPORT	PROJECT START	CONTRACT COMPLETION	P6 FORECAST FINISH	SCHEDULE ACTIVITIES
MODON	No. 42	04-Dec-2025	03-Dec-2026	04-Nov-2026	1,827

Scope: 20 ready-built factories of 900 m² each in five blocks (A to E), with site works, networks, external works, roads and landscaping.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 26-Oct-2026 data date the project is 98.4% complete against 97.9% planned, 0.6% ahead. It gained 1.3% this week against 1.4% planned. Construction is at 98.2% and testing and commissioning at 99.0%, but project close-out has not started although 40.1% of it was planned by now.

PHYSICAL % COMPLETE
98.4% / 97.9% plan
▲ SPI 1.01 +0.6%

PROGRESS THIS WEEK
+1.3% / +1.4% plan
▼ 0.1% below the weekly plan

CONTRACT TIME ELAPSED
89.6% · day 326 of 364
▲ P6 finish 04-Nov-2026

SCHEDULE ACTIVITIES COMPLETED
96.3% · 1,759 of 1,827
18 in progress, 50 not started

The forecast finish slipped two days to 04-Nov-2026, still 29 days early, with zero float.

Last week's P6 update finished the project on 02-Nov-2026. Close-out has 0 of its 231 planned man-hours earned: as-built drawings and warranties due 26–28 Oct have not started and carry zero float. Fences and gates made no progress this week and stand at 67.1% against 100% planned.

Site photos this week

Four photos from the weekly report workbook No. 42. One carries a date stamp of 24-Oct-2026; the others have no date stamp. Asphalt and paving continue around the factories and the halls are being finished inside. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt compaction
Pneumatic roller on the new asphalt in front of the factory units.



Factory hall interior
Finished floor, air-conditioning ducts and lighting installed.



Road and paving works

Paving plant and rollers beside a factory, interlock being laid in front. Stamped 24-Oct-2026, 08:05, short address HAAA4119.



Internal wall panels

Insulated wall panels with the fire-fighting pipework in place.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (P6 labour units).
Source: P6 update report No. 42, data date 26-Oct-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	12.6%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	23.5%	100.1%	100.1%	0.0	1.00	✓ Complete
Construction	59.1%	97.7%	98.2%	+0.5	1.00	▲ On track
Testing & commissioning	3.4%	84.6%	99.0%	+14.3	1.17	▲ Ahead
Project close-out and demobilisation	0.5%	40.1%	0.0%	−40.1	0.00	▼ Not started
Total	100%	**97.9%**	**98.4%**	**+0.6**	**1.01**	▲ On track

Weights are each phase's share of the 116,740 budgeted man-hours. The schedule's own WBS labels give different weights (engineering 3%, procurement 27%, construction 60%, testing and commissioning 10%). Last week the project stood at 97.2% against 96.5% planned. The P6 update has 1,827 activities: 1,759 completed, 18 in progress and 50 not started.

Scope of work: factory blocks

Budgeted and earned man-hours for each factory block and for the site infrastructure, by discipline, from the P6 update report No. 42. No quantity tables were uploaded. "This week" is the man-hours earned since the 19-Oct-2026 P6 report.

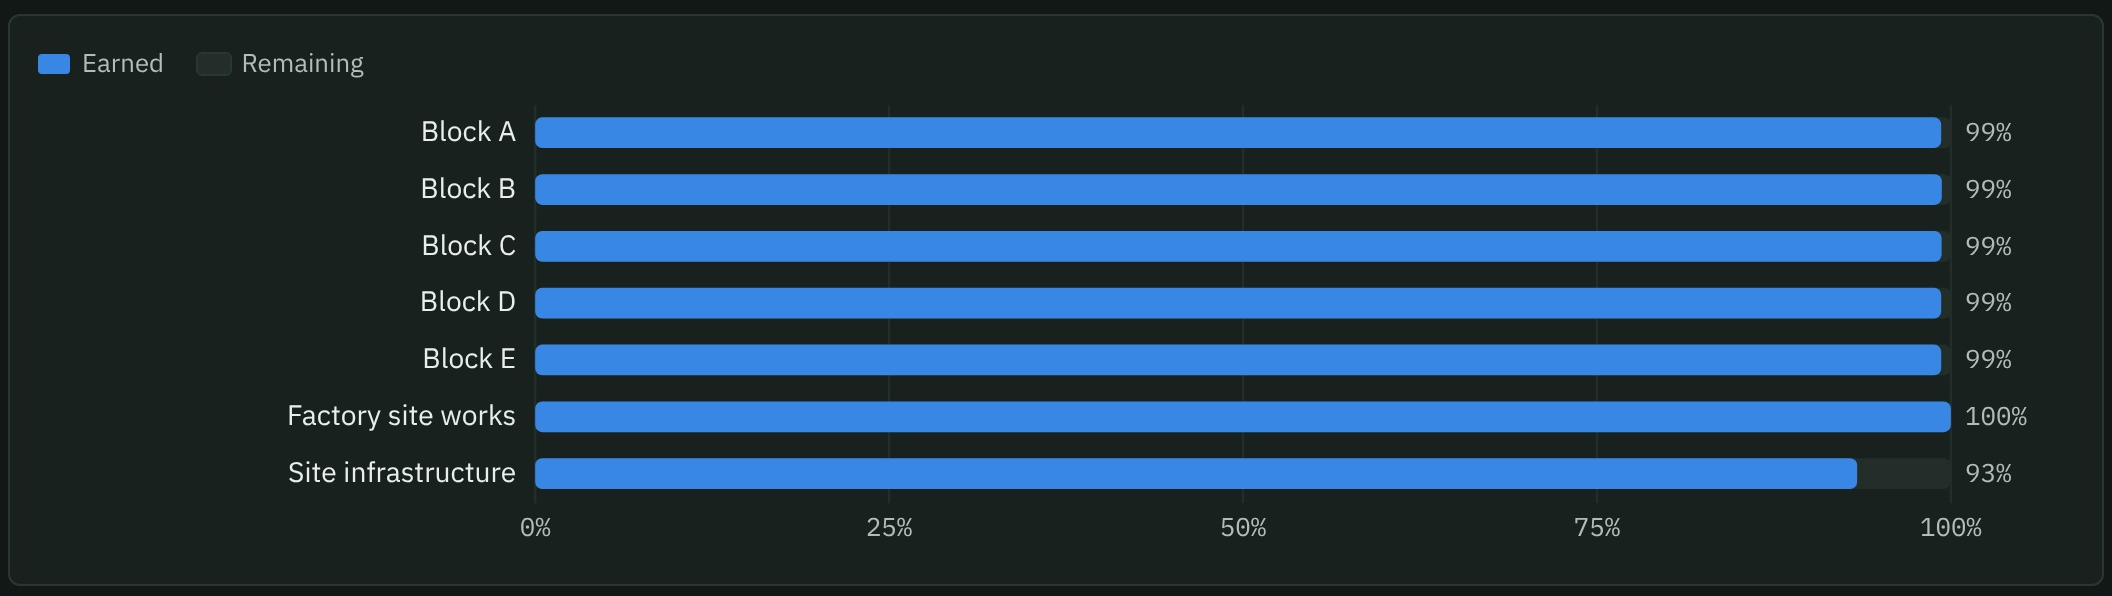

SCOPE ITEM	DISCIPLINE	UNIT	BUDGETED	EARNED	THIS WEEK	REMAINING	% COMPLETE
Block A	Structural	MH	3,008	3,008	0	0	100.0%
	Structural steel	MH	2,512	2,512	0	0	100.0%
	Architectural	MH	2,928	2,880	+171	48	98.4%
	Mechanical	MH	1,088	1,088	0	0	100.0%
	Electrical	MH	1,264	1,238	+33	26	97.9%
	Total	MH	**10,800**	**10,726**	**+204**	**74**	**99.3%**
Block B	Structural	MH	3,072	3,072	0	0	100.0%
	Structural steel	MH	2,512	2,512	0	0	100.0%
	Architectural	MH	2,992	2,944	+171	48	98.4%
	Mechanical	MH	1,088	1,088	0	0	100.0%
	Electrical	MH	1,248	1,226	+16	22	98.2%
	Total	MH	**10,912**	**10,842**	**+187**	**70**	**99.4%**
Block C	Structural	MH	2,960	2,960	0	0	100.0%
	Structural steel	MH	2,512	2,512	0	0	100.0%
	Architectural	MH	2,896	2,848	+171	48	98.3%
	Mechanical	MH	1,088	1,088	0	0	100.0%
	Electrical	MH	1,248	1,226	+13	22	98.2%
	Total	MH	**10,704**	**10,634**	**+184**	**70**	**99.3%**
Block D	Structural	MH	3,008	3,008	0	0	100.0%
	Structural steel	MH	2,512	2,512	0	0	100.0%
	Architectural	MH	2,928	2,880	+171	48	98.4%
	Mechanical	MH	1,088	1,088	0	0	100.0%
	Electrical	MH	1,264	1,238	+17	26	97.9%
	Total	MH	**10,800**	**10,726**	**+188**	**74**	**99.3%**
Block E	Structural	MH	3,040	3,040	0	0	100.0%
	Structural steel	MH	2,512	2,512	0	0	100.0%
	Architectural	MH	2,896	2,848	+171	48	98.3%

SCOPE ITEM	DISCIPLINE	UNIT	BUDGETED	EARNED	THIS WEEK	REMAINING	% COMPLETE
	Mechanical	MH	1,088	1,088	0	0	100.0%
	Electrical	MH	1,280	1,254	+34	26	98.0%
	Total	MH	**10,816**	**10,742**	**+205**	**74**	**99.3%**
Factory site works	All	MH	1,808	1,808	0	0	100.0%
Site infrastructure	Site works	MH	1,376	1,376	0	0	100.0%
	Networks	MH	4,960	4,960	0	0	100.0%
	External works: mechanical	MH	2,384	2,384	0	0	100.0%
	External works: electrical	MH	624	600	+16	24	96.2%
	External electrical works	MH	1,136	1,032	+24	104	90.8%
	Fences and gates	MH	1,360	912	0	448	67.1%
	Road works	MH	1,136	1,032	+250	104	90.8%
	Landscaping	MH	192	0	0	192	0.0%
	Total	MH	**13,168**	**12,296**	**+290**	**872**	**93.4%**

Blocks: 99.3–99.4% complete

Metal works and wall finishes are now complete in every block. Architectural works are at 98.3–98.4%: identification signs have not started in any block and specialties stand at 70–75%. Electrical works are at 97.9–98.2%, with access control at 80% and fire-alarm monitor modules at 70% in each block.

Site infrastructure: 93.4%

Road works gained 250 man-hours this week and reached 90.8%, ahead of the 77.3% planned; only traffic lines and wheel bumpers remain to start. Fences and gates made no progress (67.1% against 100% planned). Landscaping (trees and shrubs) has not started although 40.6% was planned.

Milestones

Baseline dates and P6 forecasts from the P6 update report No. 42, with total float from the P6 update (XER) file. The weekly report workbook has no text version, so its own forecasts could not be compared.

MILESTONE	BASELINE	P6 UPDATE FORECAST	CHANGE (DAYS)	P6 FLOAT (DAYS)	STATUS
Project start	04-Dec-2025	04-Dec-2025 (actual)	0	–	✓ Done
Construction start	24-Dec-2025	28-Dec-2025 (actual)	+4	–	✓ Done
Complete mobilisation	04-Jan-2026	05-Jan-2026 (actual)	+1	–	✓ Done
Site levelling, local roads and parking	07-Jan-2026	05-Jan-2026 (actual)	−2	–	✓ Done
Network start	03-Jun-2026	05-May-2026 (actual)	−29	–	✓ Done
Engineering and materials complete	09-Apr-2026	19-Oct-2026 (actual)	+193	–	✓ Done
Civil works complete	14-Jul-2026	26-Aug-2026 (actual)	+43	–	✓ Done
Environmental works complete	11-Oct-2026	19-Sep-2026 (actual)	−22	–	✓ Done
Mechanical works complete	01-Oct-2026	08-Oct-2026 (actual)	+7	–	✓ Done
Testing and commissioning complete	25-Oct-2026	27-Oct-2026	+2	7.5	▼ Late
Architectural works complete	04-Oct-2026	28-Oct-2026	+24	4.0	▼ Late
Electrical works complete	26-Nov-2026	28-Oct-2026	−29	4.0	● On time
Construction complete	09-Nov-2026	28-Oct-2026	−12	6.7	● On time
External works complete	09-Nov-2026	28-Oct-2026	−12	4.7	● On time

MILESTONE	BASELINE	P6 UPDATE FORECAST	CHANGE (DAYS)	P6 FLOAT (DAYS)	STATUS
Project completion	03-Dec-2026	04-Nov-2026	−29	0	Zero float

Construction is forecast to finish on 28-Oct-2026; the critical path now runs through close-out and handover.

Engineering and materials, civil, mechanical and environmental works are now closed with actual dates. Architectural works remain 24 days behind their baseline, and testing and commissioning 2 days. Project completion moved from 02-Nov-2026 to 04-Nov-2026 and has no float: as-built drawings, warranties, manuals, snag rectification and initial handover all sit on the critical path.

Procurement of key materials

Share of budgeted procurement man-hours earned for each material package. Source: P6 update report No. 42.



All material packages are delivered.

Every long-lead and short-lead package has an actual finish for delivery to site. The last packages, external works materials, finished on 15-Oct-2026. Short-lead mechanical materials show 8,272 earned man-hours against a budget of 8,236.

Open issues and risks

Drawn from the open activities in the P6 update. The weekly report's own issue log is in the workbook, which has no text version.

ISSUE	AREA	DETAIL
Close-out not started	Project close-out	0 of 576 man-hours earned against 231 planned (40.1%). As-built drawings (preparation and review) and warranties, due 26–28 Oct, have not started and have zero float. Training, manuals, snag rectification and initial handover follow from 29-Oct-2026 to 04-Nov-2026, also with 0 to 0.5 days of float.
Fences and gates stalled	Site infrastructure	No progress this week: 912 of 1,360 man-hours (67.1%) against 100% planned. Base plates, steel members, steel fence and gates have not started, with 1 day of float, and finish on 02-Nov-2026.
External electrical works	Site infrastructure	90.8% against 100% planned. Earthing is at 50% and the street-lighting feeder pillars and kWh meters at 0%, with 0.5 days of float.
Landscaping not started	Site infrastructure	Planting of trees and shrubs was due to start on 26-Oct-2026 (40.6% planned, 0% earned), with 1 day of float.
Building finishing	Blocks A to E	Identification signs have not started in any block. Access control (80%) and fire-alarm monitor modules (70%) are still in progress in every block, with 4 to 7 days of float.

Data notes

- The weekly report workbook (No. 42, dated 26-Oct-2026) has no text version in MD Files. Its figures for the S-curve, manpower, cost and invoicing, and health, safety and quality could not be used, so those sections are left out. Contractor, consultant and project manager are not named in any text file. Only its photos were used.
- Physical progress is P6 earned labour units divided by budgeted labour units, from the P6 update report: 116,740 budgeted, 114,247 planned and 114,925 earned man-hours. This week's gain compares it with the 19-Oct-2026 report (112,642 planned, 113,420 earned).
- The P6 update now records civil works complete on 26-Aug-2026 and mechanical works on 08-Oct-2026, although last week's update still forecast them for 19-Oct-2026 and 24-Oct-2026. The actual dates were entered after the fact.
- The file names use project code HAL1-05-009, while the P6 update file is coded HAL1-05-10.
- The P6 update file gives a planned start of 14-Mar-2023, while the project started on 04-Dec-2025. Its start and finish dates for completed activities are later than their actual dates (for example, project start 29-Dec-2025 against 04-Dec-2025 actual).
- Procurement earned and planned man-hours (27,496) exceed its budget (27,460), because the short-lead mechanical purchase orders show 2,480 earned against 2,444 budgeted.
- Asphalt wearing course and tack coat have shown 100% complete for two weeks but are still marked in progress, with no actual finish.
- Report week: the files state no contract week, so week 46 is the whole weeks from project start (04-Dec-2025) to the data date (326 days). "No. 42" is the weekly report's serial number, not the week.
- Only one photo carries a date stamp (24-Oct-2026, with a short address code); none has a GPS stamp.

Compiled 01-Nov-2026 from the W04 upload (P6 update and P6 reports for weekly report No. 42, data date 26-Oct-2026), compared with the 19-Oct-2026 P6 report.
