Infrastructure Network Development, Sudair City for Industry and Business

تطوير شبكات البنية التحتية بالمنطقة الصناعية بسدير المرحلة الثالثة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Technical Development Co. (TDC)	EGIS	Eng. Zyad Al Shabat	06-Jan-2026	05-Jul-2027

Scope: roads and paving, potable water, TSE, sewer, storm water, irrigation and landscaping, electrical (medium voltage, telecom, street lighting) and CCTV networks in Zones A and G, over 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 26-Oct-2026 the project is 46.4% complete against 42.2% planned, 4.3% ahead (SPI 1.10). This week it gained 0.99% against 1.49% planned, so the lead narrowed from 4.8% to 4.3%, the second weekly drop in a row. Road works and the storm and sewer networks are ahead; procurement, engineering, electrical works and CCTV are behind.

PHYSICAL % COMPLETE

46.4% / 42.2% plan

▲ SPI 1.10 +4.3%

PROGRESS THIS WEEK

+0.99% / +1.49% plan

▼ 0.50% below the weekly plan

CONTRACT TIME ELAPSED

53.8% · day 293 of 545

● P6 finish 05-Jul-2027

INVOICED TO DATE (GROSS)

14.6% · 24.6M SAR

4 invoices, last period ends 30-Sep-2026

Ahead overall, but the lead is shrinking and procurement is still behind.

This week's progress (0.99%) was again under the weekly plan (1.49%). Procurement is at 60.4% against 99.4% planned (SPI 0.61): MV cables (0 of 51,500 m), unit substations, street lighting poles and lighting panels are still not delivered, and the final substation location is still pending between the Client and SEC. The P6 update still finishes the project on the contract date, 05-Jul-2027, with zero float, but float on the MV and road-works milestones fell by 6 days this week.

Site photos this week

Six photos from the "Weekly Progress Photos" sheet of the 26-Oct-2026 weekly report; none carries a visible date stamp. Road works in Zone A dominate the week: asphalt base course on MC20, base course grading, compaction and prime coat on MC10, and subgrade grading on MCG0. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt base course, MC20 Zone A

First asphalt layer of the base course laid.




Asphalt compaction, MC20 Zone A

Rollers compacting the first asphalt layer of the base course.



Base course grading, MC10 Zone A

Base course layer being placed and graded on the arterial road.

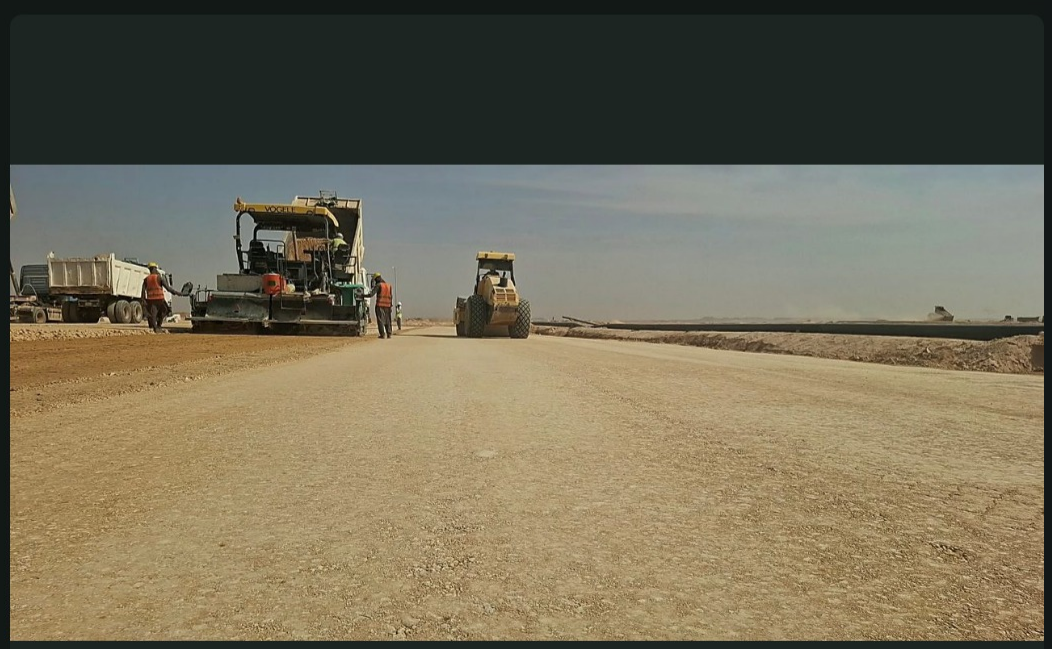


Base course compaction, MC10 Zone A

Compaction of the base course layer.



Prime coat (MC1), MC10 Zone A

MC1 sprayed on the base course layer.

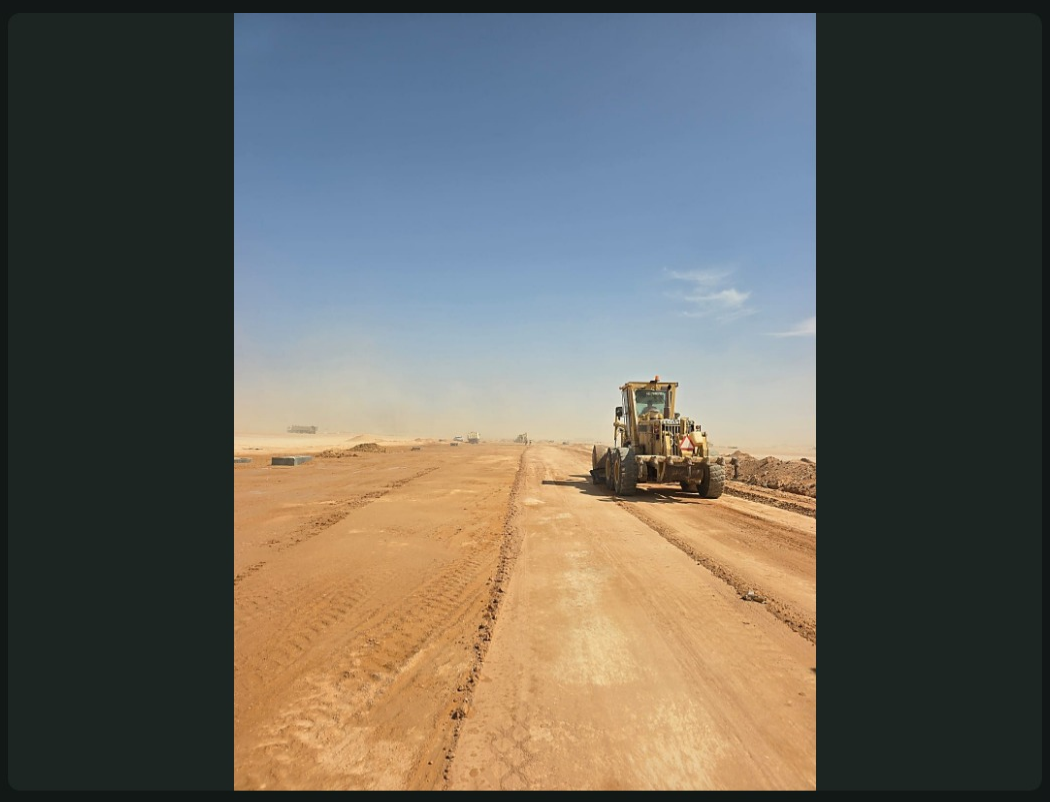


Subgrade grading, MCG0 Zone A

Grader levelling the subgrade layer.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly points dated the 6th of each month. Source: Physical-Chart Data sheet. There is no revised plan.

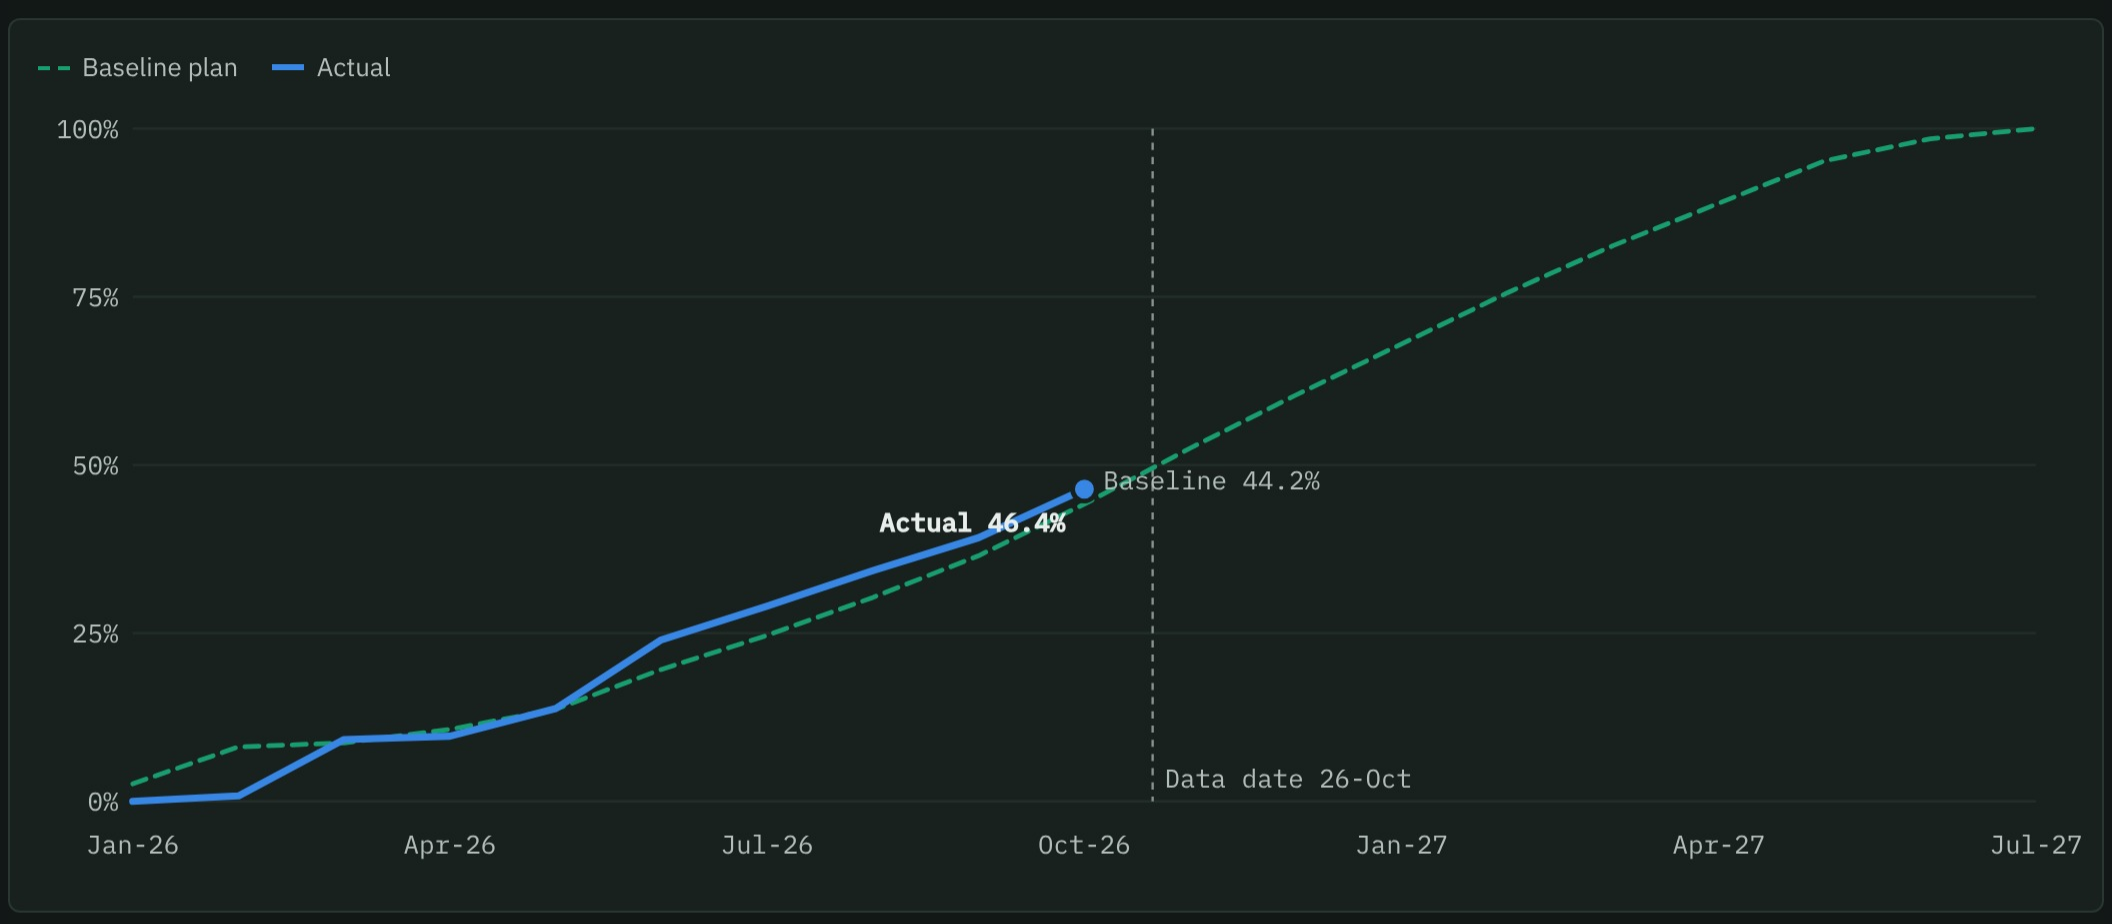

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	39.10	44.79	+5.69	–	1.15
19-Oct-2026	40.66	45.43	+4.77	+0.64	1.12
26-Oct-2026	**42.15**	**46.41**	**+4.26**	**+0.99**	**1.10**

Physical % complete from the 19-Oct and 26-Oct-2026 weekly reports. The 12-Oct-2026 row is the previous-week value in the 19-Oct report; its weekly gain is not stated. The chart's October point (44.2% planned) is dated 06-Oct, while the weekly report plans 42.2% to 26-Oct; see Data notes.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Network rows are part of Construction; their weights are shares of the whole project. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5%	100.0%	93.4%	−6.6%	0.93	▼ Behind
Procurement	13%	99.4%	60.4%	−39.0%	0.61	▼ Behind
Construction	75%	28.3%	41.2%	+12.9%	1.45	▲ Ahead
· Road works	16.4%	74.7%	81.7%	+6.9%	1.09	▲ Ahead
· Storm water drainage	16.5%	22.0%	46.4%	+24.4%	2.11	▲ Ahead
· Sewerage	5.5%	9.2%	72.7%	+63.5%	7.92	▲ Ahead
· TSE	7.7%	0.0%	6.6%	+6.6%	–	▲ Started early
· Potable water	12.3%	0.0%	15.0%	+15.0%	–	▲ Started early
· Electrical works	8.7%	50.9%	35.7%	−15.2%	0.70	▼ Behind
· Landscape & irrigation	6.8%	0.0%	4.7%	+4.7%	–	▲ Started early
· CCTV	1.2%	36.9%	12.2%	−24.7%	0.33	▼ Behind
Testing & commissioning	2%	0.0%	0.0%	0.0%	–	● Not yet due
Close-out	2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**42.2%**	**46.4%**	**+4.3%**	**1.10**	▲ Ahead

The P6 update (data date 26-Oct-2026) has 2,115 activities: 792 completed, 343 in progress and 980 not started. Its scheduled finish is 05-Jul-2027, the contract completion date.

Scope of work: quantities

Quantity executed on site for the major items, from the Major Quantities sheet of the 26-Oct-2026 weekly report. "This week" is the change since the 19-Oct-2026 report. The report gives no zone split. The scope table on the report's summary page shows 0 executed for every network and was not used.

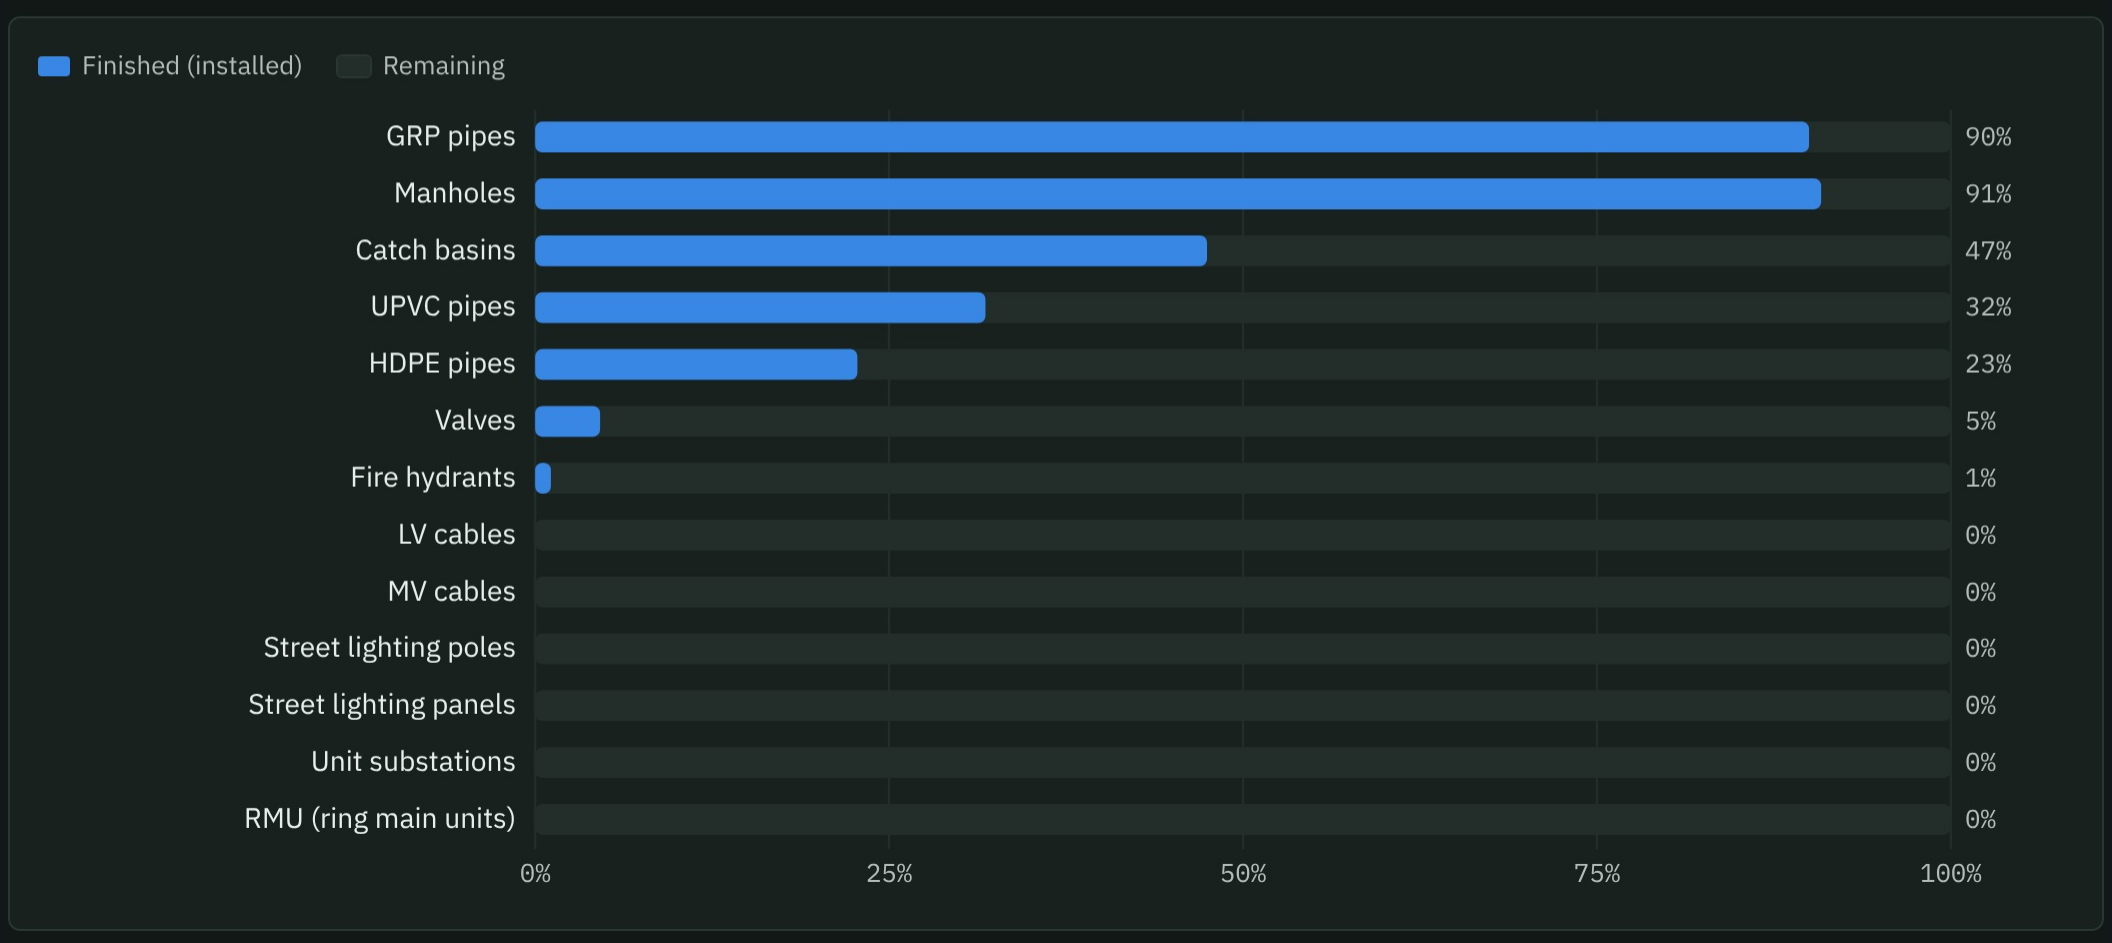

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
GRP pipes	All zones	m	18,337	16,500	0	1,837	90.0%	–
Manholes	All zones	EA	251	228	+3	23	90.8%	–
Catch basins	All zones	EA	295	140	+20	155	47.5%	–
UPVC pipes	All zones	m	4,716	1,500	+300	3,216	31.8%	–
HDPE pipes	All zones	m	28,557	6,500	+500	22,057	22.8%	–
Valves	All zones	EA	218	10	0	208	4.6%	–
Fire hydrants	All zones	EA	90	1	0	89	1.1%	–
LV cables	All zones	m	68,400	0	0	68,400	0.0%	–
MV cables	All zones	m	51,500	0	0	51,500	0.0%	–
Street lighting poles	All zones	EA	592	0	0	592	0.0%	–
Street lighting panels	All zones	EA	52	0	0	52	0.0%	–
Unit substations	All zones	EA	5	0	0	5	0.0%	–
RMU (ring main units)	All zones	EA	11	0	0	11	0.0%	–

Wet networks advanced; small gains this week

GRP pipes are 90% installed (16,500 of 18,337 m, unchanged this week) and manholes 91% (228 of 251, 3 this week). This week also added 20 catch basins (now 47%), 300 m of UPVC pipes (32%) and 500 m of HDPE pipes (23%).

Not yet started or barely started

Fire hydrants (1 of 90) and valves (10 of 218) have barely started. No LV or MV cable, street lighting pole, lighting panel, unit substation or RMU is installed yet.

Milestones

The weekly report and the P6 schedule update give different dates for several milestones. Both are shown so the difference can be resolved with the contractor. Baselines for the last four contractual milestones are from the approved baseline schedule uploaded with the previous week.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	06-Jan-2026	06-Jan-2026	06-Jan-2026 (actual)	–	✓ Done
Mobilisation finish	05-Feb-2026	05-Feb-2026	06-Apr-2026 (actual)	–	✓ Done
Baseline submission	05-Feb-2026	06-Apr-2026 (+60 d)	06-Apr-2026 (actual)	–	✓ Done
Quality lab	05-Feb-2026	16-Feb-2026 (+11 d)	–	–	✓ Done
RBF	05-Feb-2026	16-Feb-2026 (+11 d)	–	–	✓ Done
Technical submittals (plans and materials)	05-Mar-2026	16-Aug-2026 (+164 d)	25-Jul-2026 (actual)	–	✓ Done late
Engineering phase finish	05-Mar-2026	28-Sep-2026 (+207 d)	26-Oct-2026	77	▼ Late
Procurement phase finish	23-Jan-2027	17-Jan-2027	29-Dec-2026	30	● On track
Medium voltage works complete	21-Jan-2027	–	27-Feb-2027	21	▼ At risk
All network works complete	04-May-2027	–	21-Apr-2027	59	● On track
Road works complete	14-Apr-2027	–	24-Apr-2027	12	▼ At risk
Finishing works complete	05-Jul-2027	–	29-Jun-2027	5.7	● On track
Project finish (all works)	05-Jul-2027	05-Jul-2027	05-Jul-2027	0	● On time

The weekly report and the P6 update disagree on four milestone dates.

Mobilisation finished on 05-Feb-2026 in the weekly report but on 06-Apr-2026 in P6. Technical submittals finished on 16-Aug-2026 in the weekly report but on 25-Jul-2026 in P6. The weekly report forecasts the engineering phase to finish on 28-Sep-2026, while P6 still has it open on 26-Oct-2026. Procurement finishes on 17-Jan-2027 in the weekly report and 29-Dec-2026 in P6. In this week's P6 update the MV works moved 9 days later, to 37 days after their baseline (float 21 days, from 27), and road works moved 7 days later, to 10 days after their baseline (float 12 days, from 18). Project finish has no float left.

Procurement of key materials

Share of total quantity delivered to site. Source: Major Quantities sheet; asphalt, interlock and kerbstone from the completion rate in the Procurement sheet, weekly report 26-Oct-2026.



MV cables: nothing delivered


0 of 51,500 m. The Procurement sheet lists the material approval as not submitted, with the cables required on site by 31-May-2026. The risk register says the cables have been procured and that the final substation location is still pending between the Client and SEC.

Street lighting, substations and paving materials

Street lighting poles 1 of 592 delivered, lighting panels 0 of 52 and unit substations 0 of 5 (approval not submitted). This week kerbstone rose to 15% delivered (from 3.4%), interlock tiles to 15% (from 5.5%) and asphalt mix to 40% (from 30%), and the manhole, catch basin and valve box covers are now fully delivered.

Manpower

Monthly head count on site (manual plus non-manual), planned vs actual. Source: Manpower sheet.

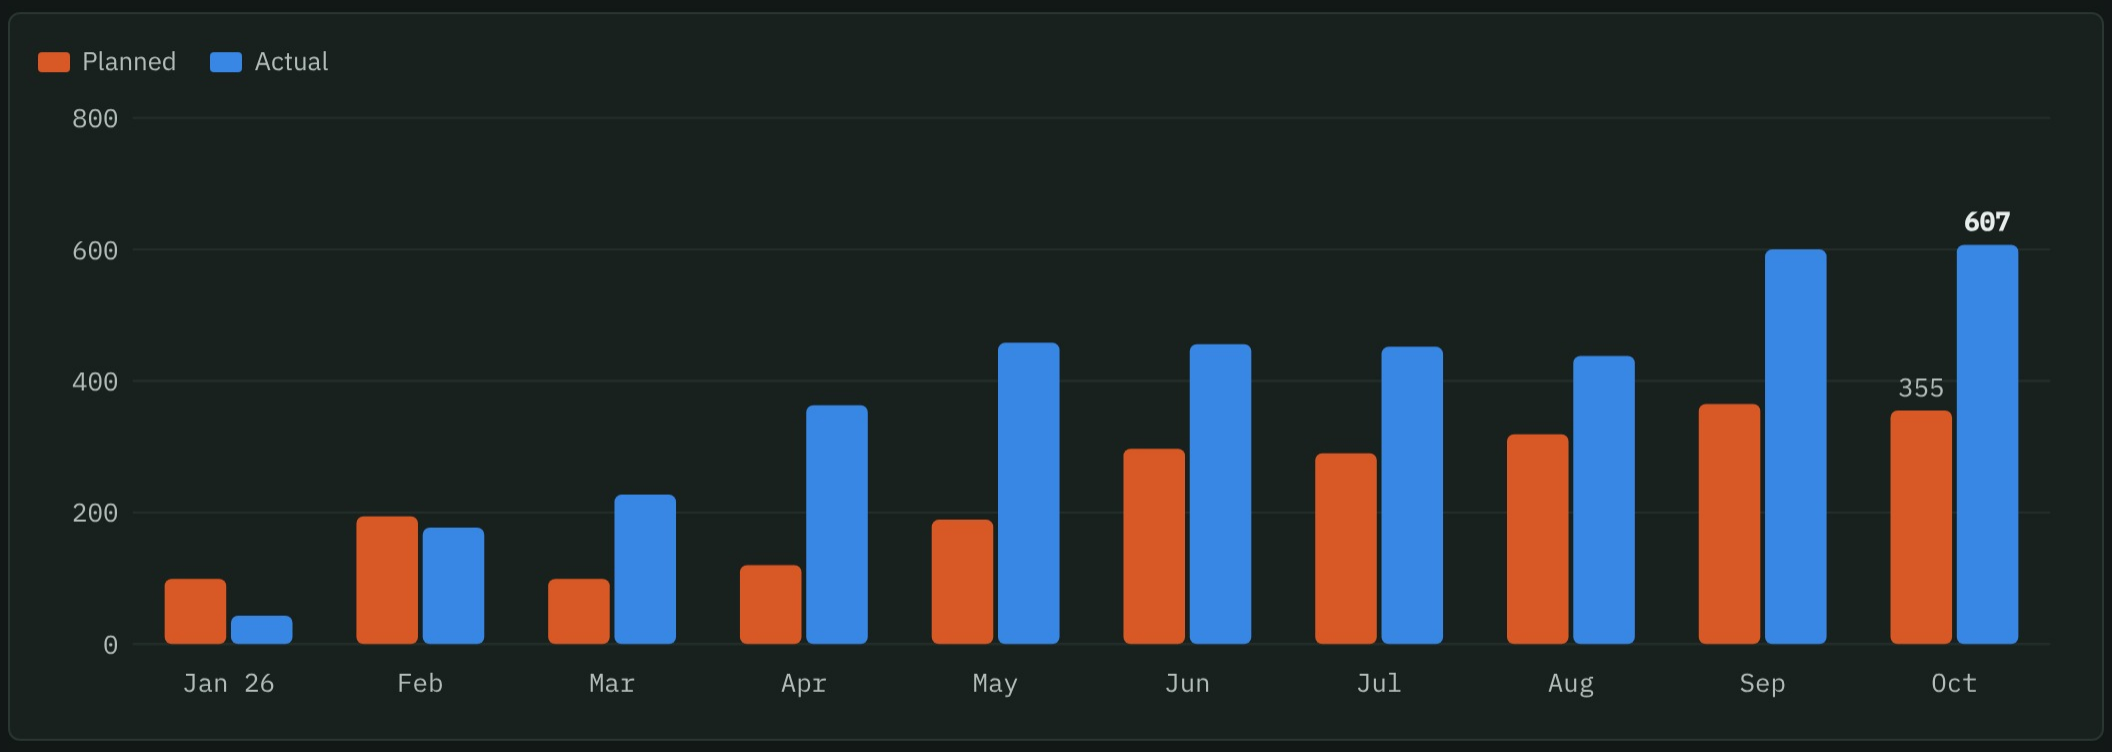

October head count is 607 (540 manual, 67 non-manual) against 355 planned (+71%); the 26-Oct report repeats the 19-Oct figures. Actual head count has been above plan every month since February. The site also has 332 pieces of equipment against 200 planned.

Cost and invoicing

Contract value

Road works	88,002,863
Storm water drainage network	25,405,198
Electrical works	20,082,302
CCTV works	9,305,708
Potable water network	7,779,405
Sewer network	7,071,027
Landscape & irrigation	6,835,461
TSE network	4,147,557
BOQ total (excl. VAT)	**168,629,520**
Contract value incl. 15% VAT	193,923,948
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. No change orders are registered.

Invoices

Invoices submitted	4
Gross value	24,575,402
Advance payment recovery (10%)	−2,457,540
Retention	0
Deductions and penalties	−34,000
VAT	3,317,679
Net incl. VAT	25,401,542
PM-approved / paid	0 / 0
Advance payment (10%)	16,862,952

Invoicing is 14.6% of the contract value against 45.4% physical progress. The invoice log shows none of the four invoices approved by the PM or paid yet; the first covers work up to 28-Jun-2026.

Health, safety and quality

Safety Score 81.8%

Safe man-hours (cumulative)	936,956
Man-hours this week	36,420
Man-hours this month	134,500
Internal trainings (cumulative)	56
Toolbox talks (cumulative)	42
Consultant safety inspection score	80.7%
Safety observations logged / closed	15 / 15

All man-hours are reported as safe. The report does not state incident counts clearly.

Quality Score 81.3%

NCRs issued / closed / open	22 / 17 / 5
Site instructions issued / open	7 / 1
MIRs issued / open	243 / 4
FIRs issued / open	4,008 / 68
Shop drawings submitted / processed	420 / 360
Shop drawings pending with consultant	0
Material submittals processed	62 of 65

Open issues and risks

ISSUE	OWNER	DETAIL
Substation location (MV)	Client / SEC	The final substation location is still pending confirmation between the Client and SEC. The MV cable size was settled by RFI (answered 09-Feb-2026) and the contractor is building MV road-crossing ducts at its own risk. Further delay may affect testing, energization and handover. Rated high (5 × 5).
Landscape proposal approval	Client	The landscape proposal (RFI-0036, 23-Aug-2026) awaits Client approval, which is needed to finalise the landscape shop drawings and procure the materials. Rated medium.
Procurement behind plan	Contractor	Procurement is at 60.4% against 99.4% planned. Approval of MV cables, unit substations, KWH meters, the fence for electrical works and road marking is still not submitted.
Float on MV and road works falling	Contractor	P6 moved MV works completion to 27-Feb-2027 (float 21 days, from 27) and road works completion to 24-Apr-2027 (float 12 days, from 18). Electrical works are at 35.7% against 50.9% planned and CCTV at 12.2% against 36.9%.
Engineering not closed	Contractor	Engineering is at 93.4% against 100% planned, unchanged this week, and P6 still has the engineering phase open. 5 NCRs remain open; no shop drawing is pending with the consultant.

All 15 safety observations in the issue log (08-Sep to 25-Oct-2026) and 18 of the 20 risks in the register are closed.

Data notes

- The uploaded files name the project "Phase Two – Part Two" (SUD1-02-011), while the repository folder and the project tracker call it Phase 3 (المرحلة الثالثة).
- The summary sheet labels cost-based progress as "Plan" and "Actual". This report uses physical progress (man-hour weighted) only: 42.15% planned and 46.41% actual.
- The Physical-Chart Data sheet plans 44.2% at its October point (06-Oct), more than the 42.15% planned to 26-Oct on the front sheet, and it shows the 26-Oct actual (46.41%) on the 06-Oct point.
- The front sheet leaves physical progress for electrical, landscape and CCTV works blank; the man-hours in the Progress sheet were used. Its BOQ values for CCTV Zone A and Zone G read 46,056 and 2 SAR instead of 6,513,996 and 2,791,854.
- The P6 update and the schedule panel of the weekly report now agree (792 completed, 343 in progress, 980 not started), but the front sheet still shows 144 in progress.
- The weekly report puts the procurement phase baseline at 23-Jan-2027; the approved baseline schedule (uploaded with the previous week) has 21-Nov-2026.
- The summary page's scope table shows 0 executed for every network, and its totals differ from the hidden Conclusion sheet (for example roads 15,234 m vs 18,252 m). Manholes are labelled "m" in the Major Quantities sheet but are counted in units.

- Procurement figures disagree: street lighting poles are 590 units and 10% complete in the Procurement sheet but 592 units with 1 delivered in Major Quantities; LV cables are 29,700 m vs 68,400 m. MV cables are "not submitted" in procurement, while the risk register says they have been procured.
- The manpower sheet repeats the 19-Oct figures. October planned head count is 355 in the monthly table (327 manual, 28 non-manual) but 335 in the head-count panel (300 manual, 35 non-manual).
- Several cells show #REF ! errors (EAC, risk scores, safety score in the status score). The substation risk carries a value of 6,835,460.61 SAR, which is the landscape BOQ value.
- Several sheets (Major Quantities, Milestones, Physical-Chart Data, Testing, CCO, Risk Register) still carry 19-Oct-2026 as their date, although the report's data date is 26-Oct-2026 and their contents were updated. This-week quantities are the change from the 19-Oct report. The report week is the contract week the report states (42 of 78); whole weeks since handover give 41.

Compiled 01-Nov-2026 from the weekly reports for the weeks ending 19 and 26 Oct 2026, with the P6 updates and the approved baseline schedule.
