
MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004 - Playground Initiative for Western Region (Asir - Jazan -		335	30.75%	30.81%	26-Mar-26	25-Jan-27	26-Mar-26 A	29-Apr-27	10,391,293.43	10,410,973.34	33,793,604.34	-77
KEY MILESTONES		335	0%	0%	26-Mar-26	25-Jan-27	26-Mar-26 A	29-Apr-27	0.00	0.00	0.00	-77
GENERAL MILESTONES		335	0%	0%	26-Mar-26	25-Jan-27	26-Mar-26 A	29-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-MS-1010	Project Commencement Date	0	100%	100%	26-Mar-26		26-Mar-26 A		0.00	0.00	0.00	0
MLTX-02-004-MS-1030	Project Completion	0	0%	0%		25-Jan-27		29-Apr-27	0.00	0.00	0.00	-77
CONTRACTUAL MILESTONE		305	0%	0%	29-Apr-26	25-Jan-27	29-Apr-26 A	29-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-MS-1050	Completion of Mobilization	0	100%	100%		02-Jun-26		02-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MS-1060	Baseline Programme Approval	0	100%	100%		29-Apr-26		29-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MS-1070	Completion of Testing & Commissioning	0	0%	0%		19-Jan-27		24-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-MS-1100	Completion of Engineering	0	100%	0%		22-Jul-26		22-Oct-26	0.00	0.00	0.00	-78
MLTX-02-004-MS-1120	Completion of Levelling Works	0	100%	0%		09-Aug-26		15-Oct-26	0.00	0.00	0.00	-58
MLTX-02-004-MS-1130	Completion of Toilet Building	0	0%	0%		30-Nov-26		25-Jan-27	0.00	0.00	0.00	-48
MLTX-02-004-MS-1140	Completion of Playground Area	0	0%	0%		16-Jan-27		20-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-MS-1150	Completion of Natural Landscape Works	0	0%	0%		13-Dec-26		04-Mar-27	0.00	0.00	0.00	-69
MLTX-02-004-MS-1160	Completion of Asir Works	0	0%	0%		19-Jan-27		31-Mar-27	0.00	0.00	0.00	-57
MLTX-02-004-MS-1170	Completion of Jazan Works	0	0%	0%		25-Jan-27		29-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-MS-1180	Completion of Jeddah Works	0	0%	0%		25-Jan-27		29-Mar-27	0.00	0.00	0.00	-50
JEDDAH		308	39.38%	36.72%	26-Mar-26	25-Jan-27	26-Mar-26 A	29-Mar-27	4,936,857.12	4,603,401.03	12,535,459.74	-50
MOBILIZATION		63	0%	0%	26-Mar-26	10-Jun-26	26-Mar-26 A	10-Jun-26 A	0.00	0.00	0.00	0
TOPOGRAPHIC SURVEY		4	0%	0%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2100	Site Survey Works	4	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
SITE FACILITIES & OFFICES		56	0%	0%	26-Mar-26	02-Jun-26	26-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1980	Manpower Mobalization	32	100%	100%	16-Apr-26	23-May-26	16-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1990	Equipment Mobalization	1	100%	100%	14-Apr-26	15-Apr-26	14-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2010	Site Layout Plan	4	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2020	Clear & Grub for Offices & Access Road	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2030	Construct Site Access Roads	2	100%	100%	11-Apr-26	12-Apr-26	10-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2040	Construct Temporary Fence	40	100%	100%	14-Apr-26	02-Jun-26	14-Apr-26 A	02-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2050	Construct Site Offices & Storage	23	100%	100%	15-Apr-26	12-May-26	15-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2060	Install Project Signs	5	100%	100%	26-Apr-26	30-Apr-26	26-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2070	Install Site Facilities	29	100%	100%	08-Apr-26	11-May-26	08-Apr-26 A	11-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2080	Electrical Works & Connections	23	100%	100%	15-Apr-26	12-May-26	15-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-2090	Construct Parking Sheds	6	100%	100%	12-Apr-26	18-Apr-26	12-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
PRELIMINARY SUBMITTALS		59	0%	0%	31-Mar-26	10-Jun-26	31-Mar-26 A	10-Jun-26 A	0.00	0.00	0.00	0
PREPARATIONS & SUBMITTAL BY CONTRACTORS		27	0%	0%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-200	Preparation and Submittal of Detailed Work Order	25	100%	100%	31-Mar-26	28-Apr-26	31-Mar-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-211	Preparation and Submittal of Project Execution Plan	27	100%	100%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-212	Submission of Contractor Project Quality Plan	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-213	Submission of Construction Safety & Environmental	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-214	Preparation and Submittal of Organization Chart	8	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-215	Preparation and Submittal of Communication Plan	8	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	0
APPROVALS BY EMPLOYERS		51	0%	0%	09-Apr-26	10-Jun-26	09-Apr-26 A	10-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-216	Approval of Detailed Work Order Programme (Baseline)	1	100%	100%	29-Apr-26	29-Apr-26	29-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-217	Approval of Project Execution Plan	1	100%	100%	13-May-26	13-May-26	13-May-26 A	13-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-218	Approval of Contractor Project Quality Plan	19	100%	100%	09-Apr-26	30-Apr-26	09-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-219	Approval of Construction Safety & Environmental	1	100%	100%	10-Jun-26	10-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-220	Approval of Organization Chart	10	100%	100%	09-Apr-26	20-Apr-26	09-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-221	Approval of Communication Plan	10	100%	100%	09-Apr-26	20-Apr-26	09-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
ENGINEERING		173	0%	0%	31-Mar-26	21-Jul-26	31-Mar-26 A	22-Oct-26	0.00	0.00	0.00	-79
SHOP DRAWINGS		144	0%	0%	31-Mar-26	21-Jul-26	31-Mar-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
SHOP DRAWINGS SUBMISSION		136	0%	0%	31-Mar-26	12-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-38
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		58	0%	0%	31-Mar-26	09-Jun-26	31-Mar-26 A	09-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Layout Plan	20	100%	100%	31-Mar-26	22-Apr-26	31-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Setting Out	22	100%	100%	31-Mar-26	25-Apr-26	31-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Grading Layout Plan	23	100%	100%	31-Mar-26	26-Apr-26	31-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Curb Setting Out Points	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Signing & Marking Layout Plan	1	100%	100%	09-Jun-26	09-Jun-26	09-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Standards Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		136	0%	0%	31-Mar-26	12-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-38
ARCHITECTURE WORKS		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Floor Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Elevations	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0

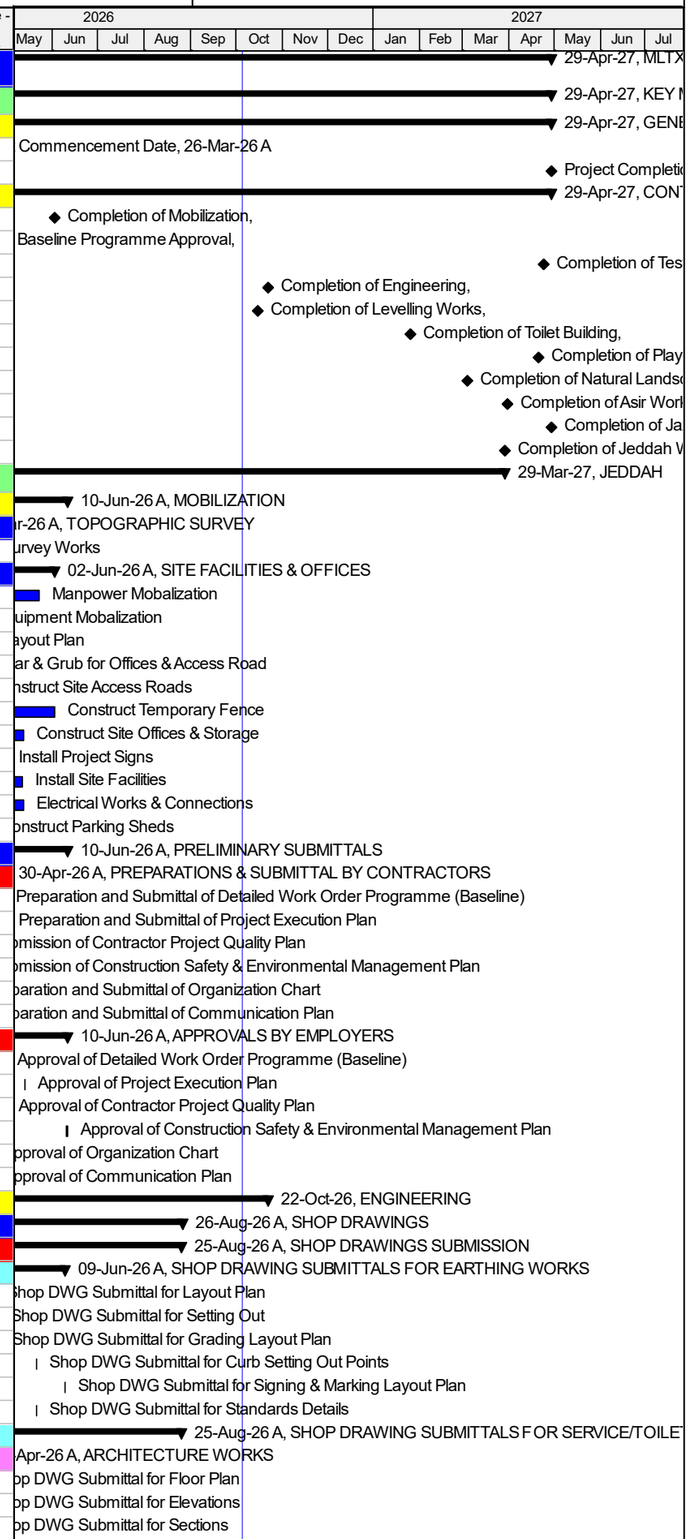

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Shop DWG Submittal for Ceiling Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Finishes Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Toilet Details	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Doors/Windows Schedule	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		9	0%	0%	08-Apr-26	18-Apr-26	08-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Foundation Plan	9	100%	100%	08-Apr-26	18-Apr-26	08-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Ground Floor Framing Plan	9	100%	100%	08-Apr-26	18-Apr-26	08-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Sections/Details	9	100%	100%	08-Apr-26	18-Apr-26	08-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		38	0%	0%	08-Apr-26	21-May-26	08-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for HVAC Plan	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Exhaust Air Plan	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for HVAC Equipment Schedule	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Fire Fighting Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Water Supply Layout	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Water Supply Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Drainage Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Drainage Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Dut Routing Layout	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Diffusers Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		129	0%	0%	08-Apr-26	12-Jul-26	08-Apr-26 A	25-Aug-26 A	0.00	0.00	0.00	-38
MLTX-02-004-EM	Shop DWG Submittal for Lighting Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Power Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Power Single Line Diagram	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Panel Board Schedules	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Lighting Installation Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Power Installation Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Cable Tray Installation Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Manhole & Ductbank Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Grounding Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Lightning Protection Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Fire Alarm Installation Details	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for CCTV Details	3	100%	100%	09-Jul-26	12-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-38
MLTX-02-004-EM	Shop DWG Submittal for Grounding Layout	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Lightning Protection System Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Fire Alarm Layout	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for CCTV Layout	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EM	Shop DWG Submittal for CCTV Riser Diagram	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EM	Shop DWG Submittal for Telephone & Data Layout	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Telephone & Data Riser Diagram	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		134	0%	0%	31-Mar-26	09-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
ARCHITECTURE WORKS		39	0%	0%	31-Mar-26	14-May-26	31-Mar-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Playground Plan/Layout	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Furniture & Marking	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Sections	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Interlock Pattern Plan	7	100%	100%	31-Mar-26	07-Apr-26	31-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Doors/Windows Schedule	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Dome Internal Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Air Dome System	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Foundation of Air Dome	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
AIR DOME SYSTEM		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Air Dome Structural Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Membrane Panel Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Cable Tension Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Airlock Door Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Emergency Exit Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
SPORTS EQUIPMENT		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Football Turf Installation	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Basketball Court Marking	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for Padel Court Structure	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		20	0%	0%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Submittal for HVAC Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0

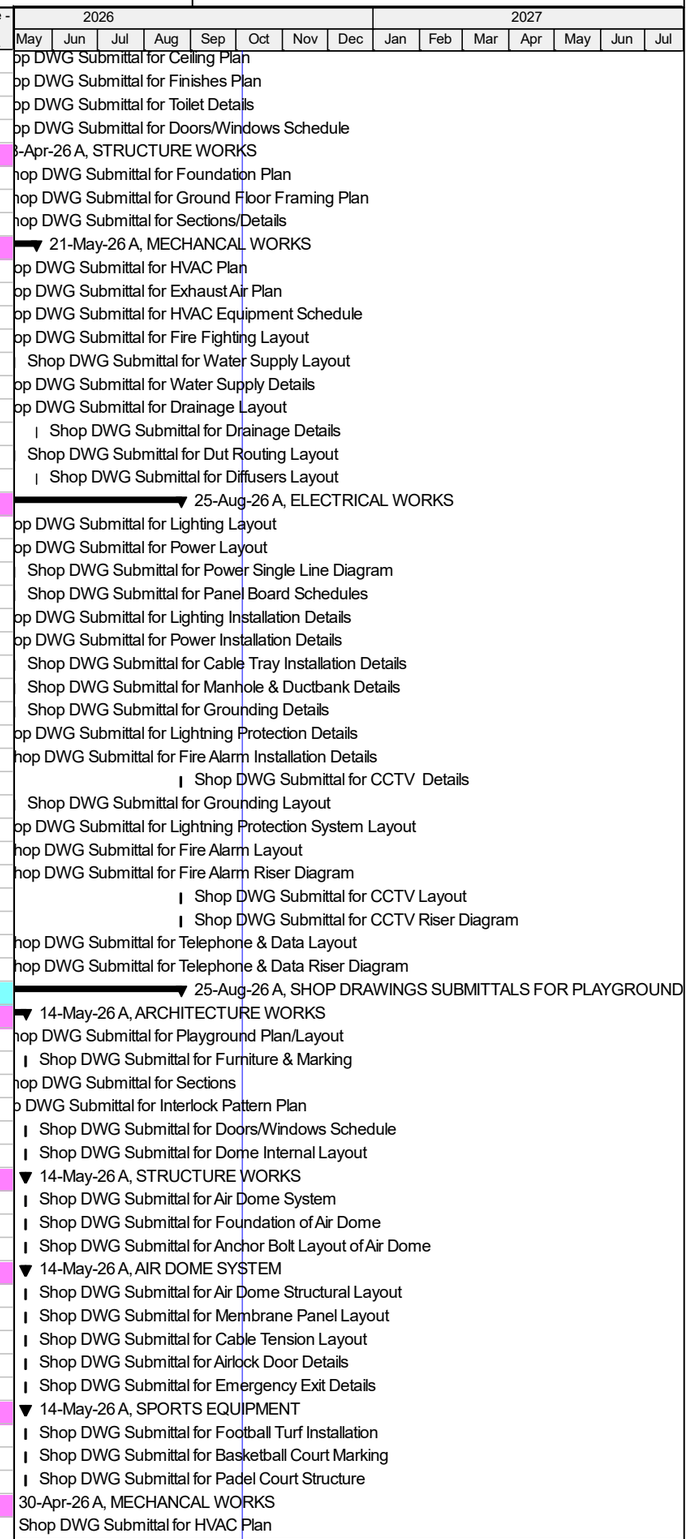


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Shop DWG Submittal for Exhaust Air Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		91	0%	0%	20-May-26	09-Jul-26	20-May-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for Lighting Layout	1	100%	100%	20-May-26	20-May-26	20-May-26 A	20-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Layout	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Single Line Diagram	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Panel Board Schedules	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Installation Details	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Details	4	100%	100%	05-Jul-26	08-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-41
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Layout	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for CCTV Riser Diagram	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		65	0%	0%	31-Mar-26	17-Jun-26	31-Mar-26 A	17-Jun-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		42	0%	0%	31-Mar-26	18-May-26	31-Mar-26 A	18-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Landscape Layout	20	100%	100%	31-Mar-26	22-Apr-26	31-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Hardscape Plan	5	100%	100%	13-May-26	18-May-26	13-May-26 A	18-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Planting Plan	5	100%	100%	13-May-26	18-May-26	13-May-26 A	18-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Landscape Details	5	100%	100%	13-May-26	18-May-26	13-May-26 A	18-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		1	0%	0%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Irrigation Details	1	100%	100%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Irrigation Layout	1	100%	100%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		1	0%	0%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting General Arrangement	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Network Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS APPROVALS		138	0%	0%	07-Apr-26	21-Jul-26	07-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
SHOP DRAWING APPROVAL FOR EARTHING WORKS		65	0%	0%	07-Apr-26	24-Jun-26	07-Apr-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Layout Plan	4	100%	100%	22-Apr-26	26-Apr-26	22-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Setting Out	17	100%	100%	07-Apr-26	26-Apr-26	07-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Grading Layout Plan	1	100%	100%	26-Apr-26	26-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Curb Setting Out Points	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Signing & Marking Layout Plan	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Standards Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		132	0%	0%	14-Apr-26	21-Jul-26	14-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
ARCHITECTURE WORKS		9	0%	0%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Floor Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Elevations	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Ceiling Plan	5	100%	100%	14-Apr-26	19-Apr-26	14-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Finishes Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Toilet Details	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Doors/Windows Schedule	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		6	0%	0%	18-Apr-26	23-Apr-26	18-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Foundation Plan	6	100%	100%	18-Apr-26	23-Apr-26	18-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Ground Floor Framing Plan	6	100%	100%	18-Apr-26	23-Apr-26	18-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections/Details	6	100%	100%	18-Apr-26	23-Apr-26	18-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for HVAC Plan	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Exhaust Air Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for HVAC Equipment Schedule	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Fire Fighting Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Water Supply Layout	0	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Water Supply Details	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Drainage Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Drainage Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Duct Routing Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Diffusers Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		131	0%	0%	15-Apr-26	21-Jul-26	15-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for Lighting Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Panel Board Schedules	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0

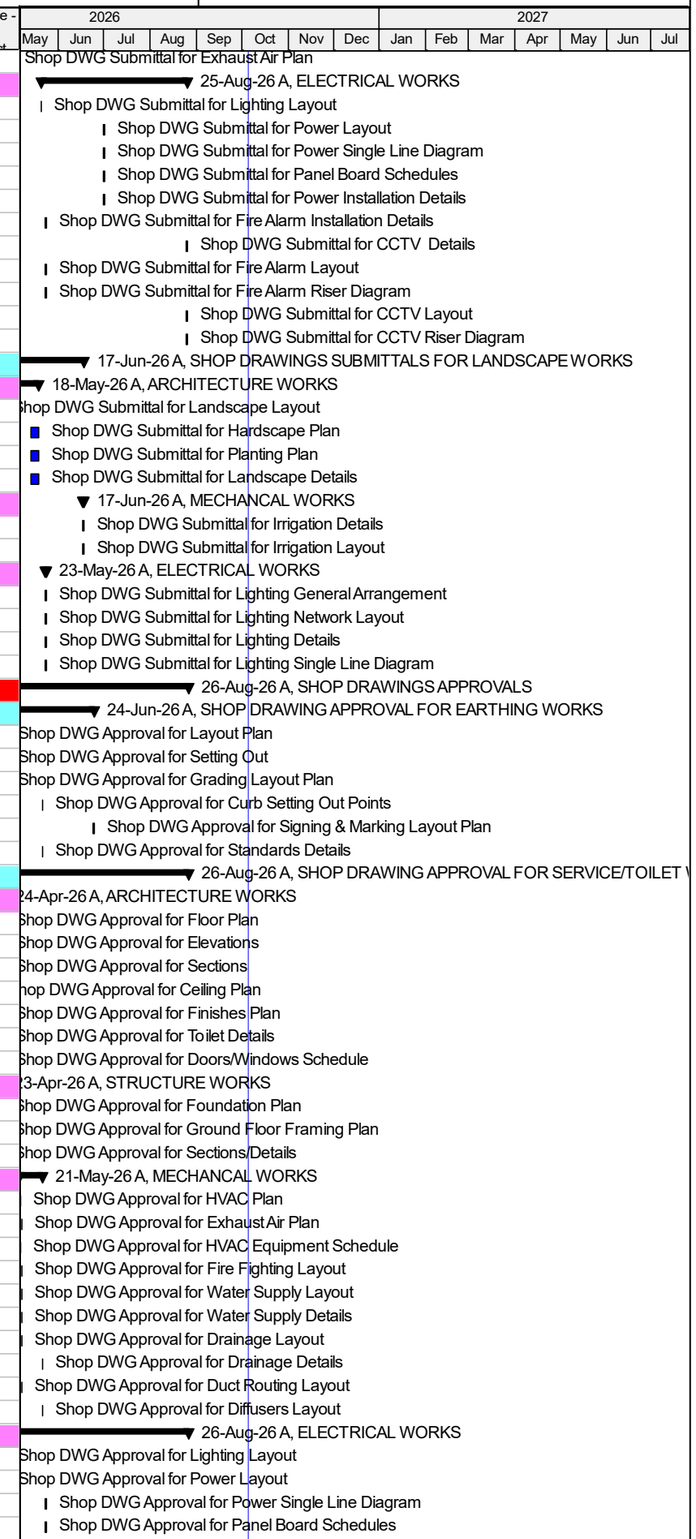


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Shop DWG Approval for Lighting Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Cable Tray Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Manhole & Ductbank Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Grounding Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lightning Protection Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Alarm Installation Details	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for CCTV Details	8	100%	100%	13-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EM	Shop DWG Approval for Grounding Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lightning Protection System Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Alarm Layout	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Alarm Riser Diagram	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for CCTV Layout	8	100%	100%	13-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EM	Shop DWG Approval for CCTV Riser Diagram	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EM	Shop DWG Approval for Telephone & Data Layout	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Telephone & Data Riser Diagram	7	100%	100%	20-Apr-26	27-Apr-26	20-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		137	0%	0%	08-Apr-26	21-Jul-26	08-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
ARCHITECTURE WORKS		54	0%	0%	08-Apr-26	13-Jun-26	08-Apr-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Playground Plan/Layout	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Furniture & Marking	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Sections	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Interlock Pattern Plan	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Doors/Windows Schedule	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Dome Internal Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		1	0%	0%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Air Dome System	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Foundation of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Foundation of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Anchor Bolt Layout of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
AIR DOME SYSTEM		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Air Dome Structural Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Membrane Panel Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Cable Tension Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Airlock Door Details	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Emergency Exit Details	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SPORTS EQUIPMENT		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Football Turf Installation	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Basketball Court Marking	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Padel Court Structure	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for HVAC Plan	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Exhaust Air Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		131	0%	0%	15-Apr-26	21-Jul-26	15-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EM	Shop DWG Approval for Lighting Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Single Line Diagram	6	100%	100%	05-Jul-26	11-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-EM	Shop DWG Approval for Panel Board Schedules	6	100%	100%	05-Jul-26	11-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-EM	Shop DWG Approval for Power Installation Details	6	100%	100%	05-Jul-26	11-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-EM	Shop DWG Approval for CCTV Details	10	100%	100%	09-Jul-26	20-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-32
MLTX-02-004-EM	Shop DWG Approval for CCTV Layout	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EM	Shop DWG Approval for CCTV Riser Diagram	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		87	0%	0%	11-Apr-26	11-Jul-26	11-Apr-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
ARCHITECTURE WORKS		20	0%	0%	22-Apr-26	14-May-26	22-Apr-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Landscape Layout	4	100%	100%	22-Apr-26	26-Apr-26	22-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Hardscape Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Planting Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Landscape Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		6	0%	0%	05-Jul-26	11-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-004-EM	Shop DWG Approval for Irrigation Details	6	100%	100%	05-Jul-26	11-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-004-EM	Shop DWG Approval for Irrigation Layout	6	100%	100%	05-Jul-26	11-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
ELECTRICAL WORKS		37	0%	0%	11-Apr-26	23-May-26	11-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lighting General Arrangement	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lighting Network Layout	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lighting Details	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0

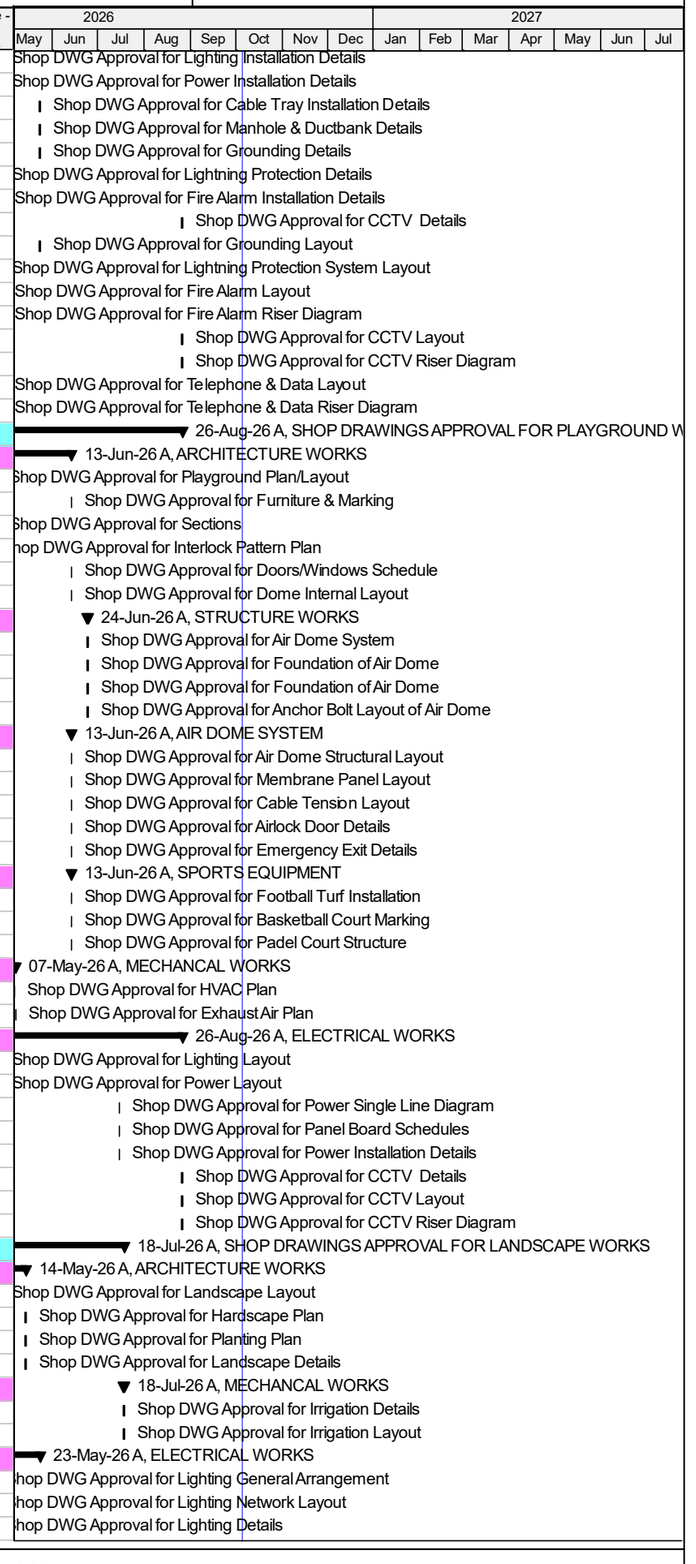

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule
D.D 05-10-2026

PROFAST شركة بروفاست المحدودة

egis

مدن MODON

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Shop DWG Approval for Lighting Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
METHOD STATEMENTS		173	0%	0%	31-Mar-26	21-Jul-26	31-Mar-26 A	22-Oct-26	0.00	0.00	0.00	-79
METHOD STATEMENT SUBMITTAL		163	0%	0%	31-Mar-26	21-Jul-26	31-Mar-26 A	11-Oct-26	0.00	0.00	0.00	-69
CIVIL WORKS		45	0%	0%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	17	100%	100%	31-Mar-26	19-Apr-26	31-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Concrete	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	22	100%	100%	31-Mar-26	25-Apr-26	31-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		114	0%	0%	31-May-26	11-Jul-26	31-May-26 A	11-Oct-26	0.00	0.00	0.00	-78
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Plastering	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Tilling	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Parking	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Soft	5	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Fence	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Air Dome	5	100%	100%	05-Jul-26	09-Jul-26	19-Aug-26 A	19-Aug-26 A	0.00	0.00	0.00	-35
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Metal	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Partitions	5	100%	100%	05-Jul-26	09-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	-5
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Gypsum	1	100%	100%	14-Jun-26	14-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	0
MECHANICAL WORKS		48	0%	0%	07-Apr-26	04-Jun-26	07-Apr-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Water	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Fire	7	100%	100%	07-Apr-26	14-Apr-26	07-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Irrigation	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for HVAC	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		49	0%	0%	13-Jun-26	21-Jul-26	13-Jun-26 A	22-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Electrical	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Lighting	1	100%	100%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	10	100%	100%	11-Jul-26	21-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	5
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for CCTV	10	100%	100%	11-Jul-26	21-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Lighting	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Preparation & Submission of Method Statement for Panel	9	100%	100%	05-Jul-26	14-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-3
METHOD STATEMENT APPROVAL		160	0%	0%	15-Apr-26	21-Jul-26	15-Apr-26 A	22-Oct-26	0.00	0.00	0.00	-79
CIVIL WORKS		6	0%	0%	21-May-26	31-May-26	21-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Earthwork	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Concrete Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Waterproofing	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		124	0%	0%	31-May-26	21-Jul-26	31-May-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-1	Approval of Method Statement for Plastering Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Masonary Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Tilling Works	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Seats/Benches Works	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Doors/Windows Works	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Interlock/Curbstone Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Parking Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Soft Scape Works	10	100%	100%	11-Jul-26	21-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	9
MLTX-02-004-EN-1	Approval of Method Statement for Fence Works	10	100%	0%	11-Jul-26	21-Jul-26	12-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-1	Approval of Method Statement for Air Dome Works	10	100%	100%	11-Jul-26	21-Jul-26	27-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	-32
MLTX-02-004-EN-1	Approval of Method Statement for Partitions Works	10	100%	100%	11-Jul-26	21-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	5
MLTX-02-004-EN-1	Approval of Method Statement for Gypsum Board Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MECHANICAL WORKS		47	0%	0%	15-Apr-26	11-Jun-26	15-Apr-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Sewage/Drainage System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Water Supply System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Fire Fighting System	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Irrigation System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for HVAC System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		21	0%	0%	05-Jul-26	21-Jul-26	11-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Approval of Method Statement for Electrical Conduits/Pulling	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Lighting Poles Installation	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-1	Approval of Method Statement for Telecommunication & Data	10	100%	100%	05-Jul-26	15-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for CCTV System	10	100%	100%	11-Jul-26	21-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-1

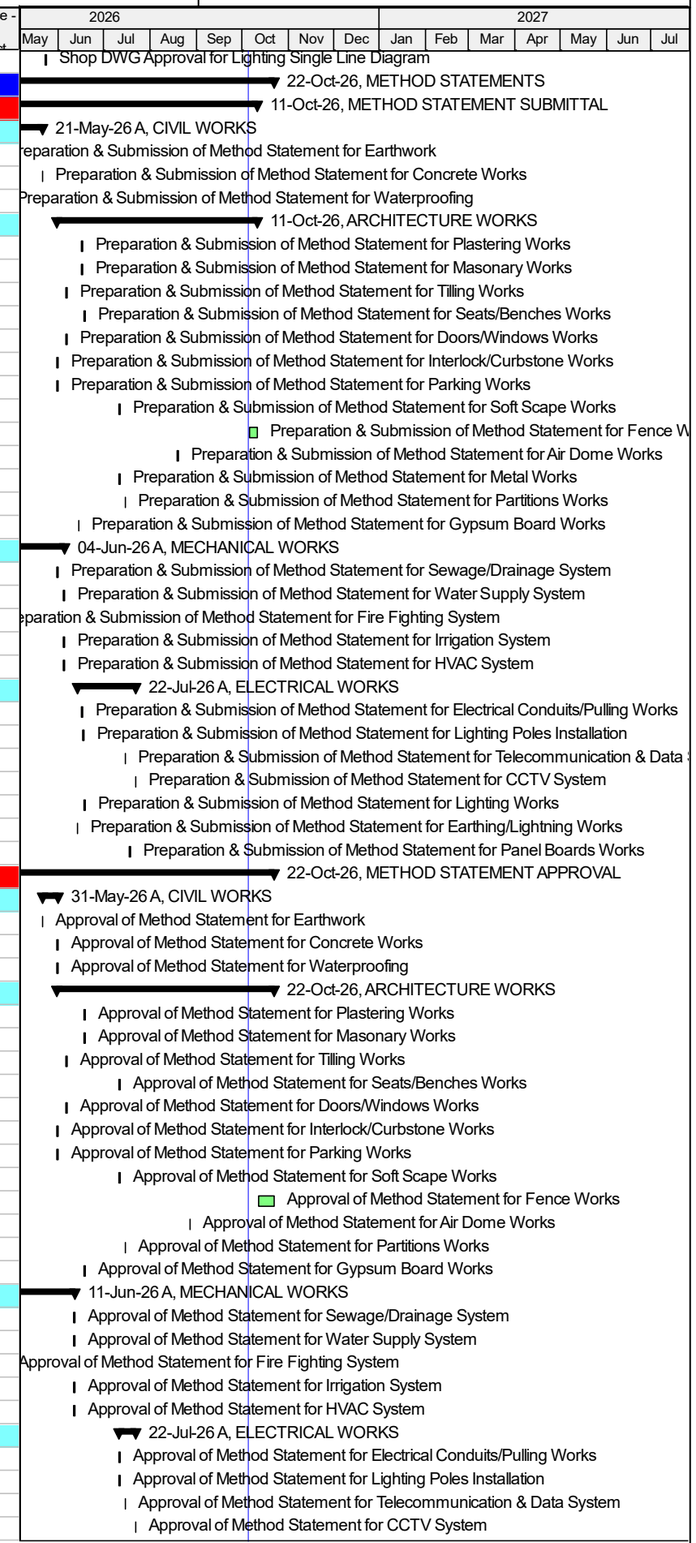

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN-1	Approval of Method Statement for Lighting Works	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-1	Approval of Method Statement for Earthing/Lightning Works	5	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Approval of Method Statement for Panel Boards Works	5	100%	100%	16-Jul-26	21-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	3
PRE-QUALIFICATION & MATERIAL		168	0%	0%	31-Mar-26	15-Jul-26	31-Mar-26 A	17-Oct-26	0.00	0.00	0.00	-79
PRE-QUALIFICATION		45	0%	0%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
TOILET/SERVICE WORKS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
STEEL REINFORCEMENT		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Steel Reinforcement	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Steel Reinforcement	2	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
READY MIX CONCRETE		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Ready Mixed Concrete	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval of Ready Mixed Concrete	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Concrete Blocks	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Concrete Blocks	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
WATER PROOFING		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Water Proofing	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Water Proofing	3	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
FLOOR/WALL TILES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Tilling Materials	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Tailling Material	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SUSPENDED CEILING		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Suspend Ceiling	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Suspend Ceiling	2	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
DOORS/WINDOWS		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Doors/Windows	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Doors/Windows	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
FURNITURES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Furnitures	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Furnitures	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Sanitary Fixtures	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Sanitary Fixtures	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
WATER SUPPLY PIPES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Water Supply Pipes	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Water Supply Pipes	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Package AC Units	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Package AC Units	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Air Diffusers/Grills	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Air Diffusers/Grills	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Galvanized Ducts	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Galvanized Ducts	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Exhaust Fans	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Exhaust Fans	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LIGHTING FIXTURES		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lighting Fixtures	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lighting Fixtures	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
SWITCHES/SOCKETS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Switches/Sockets	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Switches/Sockets	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EARTHING SYSTEM		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Earthing System	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Earthing System	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Distribution Panels	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Distribution Panels	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PLAYGROUND WORKS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0

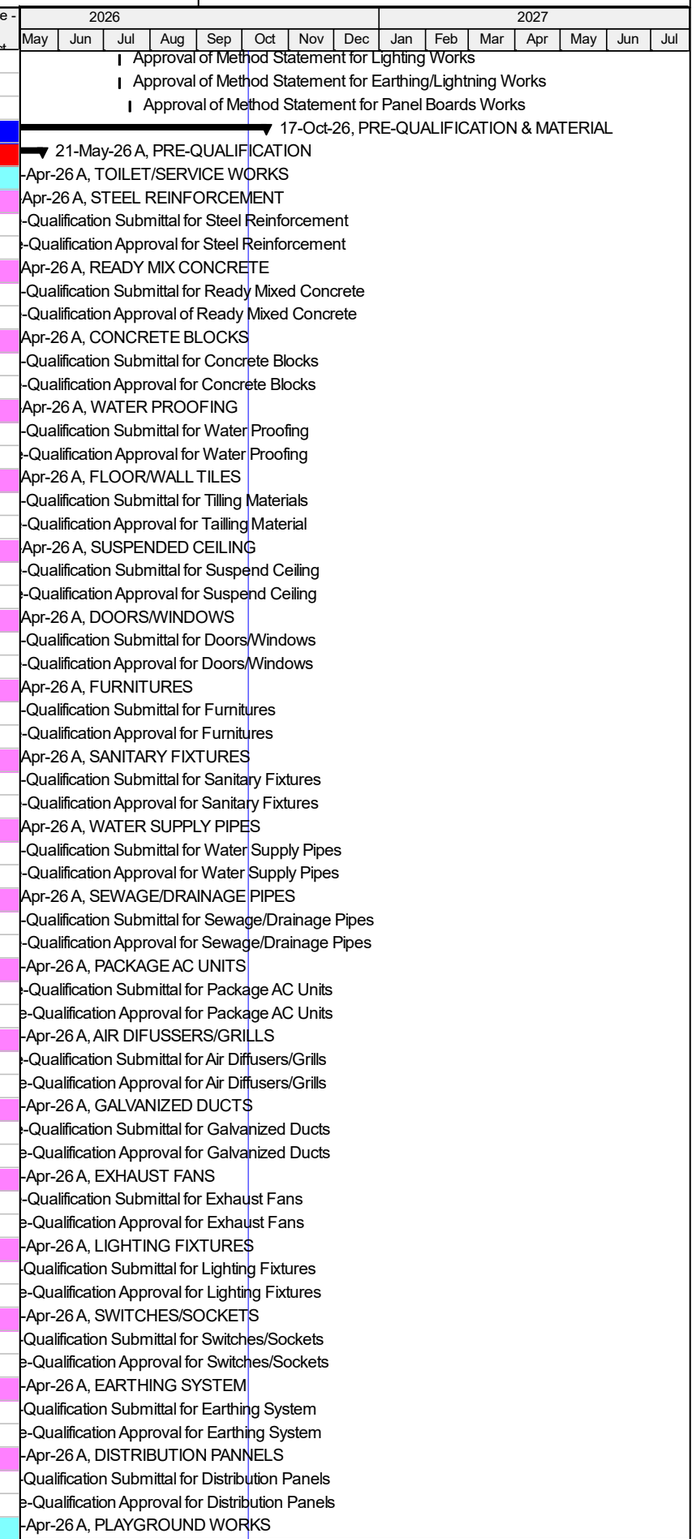

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PVC MEMBRANE		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for PVC Membrane	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for PVC Membrane	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
STEEL TENSION CABLES		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Steel Tension Cables	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Steel Tension Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EMERGENCY DOORS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Emergency Doors	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Emergency Doors	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PRESSURE UNITS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Pressure Units	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Pressure Units	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR LOCK DOORS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lock Doors	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lock Doors	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
ARTIFICIAL TURF		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Artificial TURF	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Artificial TURF	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Rubber Granules	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Rubber Granules	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PADEL GLASS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Padel Glass	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Padel Glass	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Wire Mesh/Steel Sets	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Wire Mesh/Steel Sets	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AGGREGATE BASE COURSE		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Aggregate Base Course	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Aggregate Base Course	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	07-Apr-26	14-Apr-26	07-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Bituminous Base & Wearing	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for the Site	3	100%	100%	12-Apr-26	14-Apr-26	12-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		2	0%	0%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Interlocking Block Pavers	1	100%	100%	11-Apr-26	11-Apr-26	11-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Interlocking Block Pavers	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MARKING PAINT		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Marking Paint	8	100%	100%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Marking Paint	1	100%	100%	12-Apr-26	12-Apr-26	12-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Package AC Units	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Package AC Units	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Air Difussers/Grills	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Air Difussers/Grills	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Galvanized Duct	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Galvanized Duct	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Exhaust Fans	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Exhaust Fans	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
DISTRIBUTION BOARDS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Distribution Boards	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Distribution Boards	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
POWER CABLES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Power Cables	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Power Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LIGHT FIXTURES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Light Fixtures	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Light Fixtures	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
CCTV MATERIALS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for CCTV	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for CCTV	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
POWER OUTLETS/SWITCHES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0

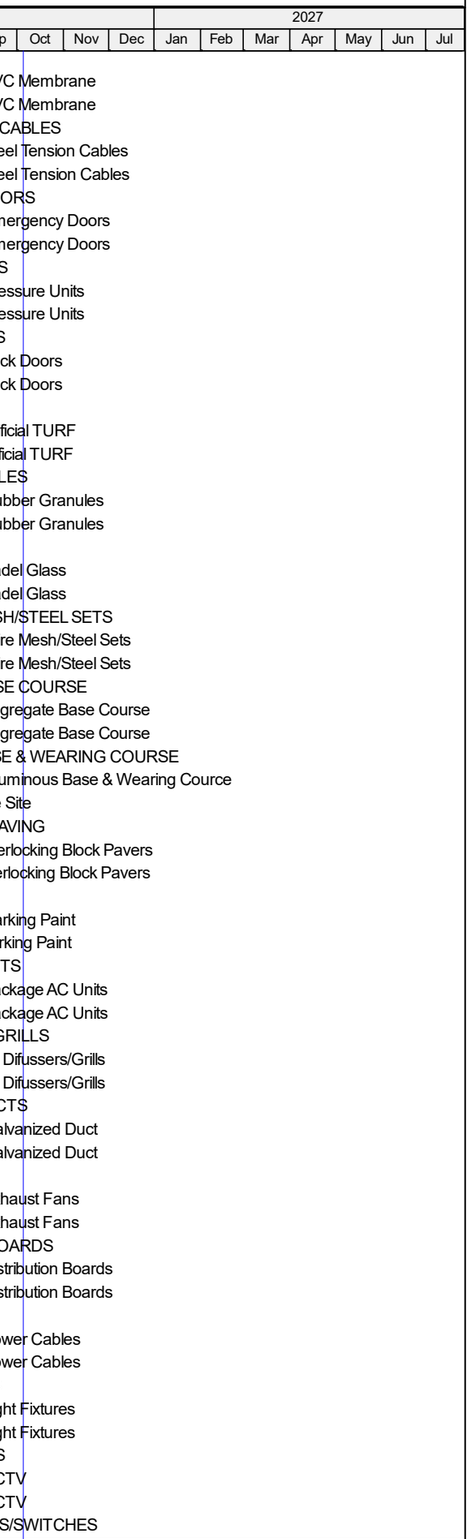


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Pre-Qualification Submittal for Power Outlets/Switches	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Power Outlets/Switches	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LANDSCAPE WORKS		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Interlocking Block Pavers	7	100%	100%	04-Apr-26	11-Apr-26	04-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Interlocking Block Pavers	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
CURBSTONE		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Curbstone	7	100%	100%	04-Apr-26	11-Apr-26	04-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Curbstone	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PAVEMENT MARKING		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Pavement Markings	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Pavement Markings	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
TRAFFIC SIGNS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Traffic Signs	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Traffic Signs	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
IRRIGATION PIPES/SPRINKLERS		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	20	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AGRICULTURE SOIL		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Agriculture Soil	20	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Agriculture Soil	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
TRACK SURFACE		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Track Surface	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Track Surface	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
GRASS/TREES		14	0%	0%	04-Apr-26	19-Apr-26	04-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Grass/Trees	10	100%	100%	04-Apr-26	14-Apr-26	04-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Grass/Trees	5	100%	100%	14-Apr-26	19-Apr-26	14-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
CABLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Cables	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Cables	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LIGHT POLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lighting poles	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lighting poles	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MATERIAL SUBMITTAL		159	0%	0%	11-Apr-26	15-Jul-26	11-Apr-26 A	17-Oct-26	0.00	0.00	0.00	-79
TOILET/SERVICE WORKS		91	0%	0%	11-Apr-26	11-Jul-26	11-Apr-26 A	22-Jul-26 A	0.00	0.00	0.00	-10
STEEL REINFORCEMENT		2	0%	0%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Steel Reinforcement	1	100%	100%	11-Apr-26	11-Apr-26	11-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Steel Reinforcement	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
READY MIX CONCRETE		2	0%	0%	14-Apr-26	15-Apr-26	14-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Ready Mixed Concrete	1	100%	100%	14-Apr-26	14-Apr-26	14-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval of Ready Mixed Concrete	2	100%	100%	14-Apr-26	15-Apr-26	14-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		3	0%	0%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Concrete Blocks	2	100%	100%	13-Apr-26	14-Apr-26	13-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Concrete Blocks	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
FLOOR/WALL TILES		87	0%	0%	15-Apr-26	11-Jul-26	15-Apr-26 A	22-Jul-26 A	0.00	0.00	0.00	-10
MLTX-02-004-EN	Material Submittal for Tilling Materials	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Tilling Material	6	100%	100%	05-Jul-26	11-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-10
SUSPENDED CEILING		5	0%	0%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Suspend Ceiling	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Suspend Ceiling	2	100%	100%	19-Apr-26	20-Apr-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
DOORS/WINDOWS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Doors/Windows	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Doors/Windows	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
FURNITURES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Furnitures	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Furnitures	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		14	0%	0%	15-Apr-26	30-Apr-26	15-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Sanitary Fixtures	6	100%	100%	15-Apr-26	21-Apr-26	15-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Sanitary Fixtures	11	100%	100%	19-Apr-26	30-Apr-26	19-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
WATER SUPPLY PIPES		2	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Water Supply Pipes	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Water Supply Pipes	2	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		2	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Sewage/Drainage Pipes	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0

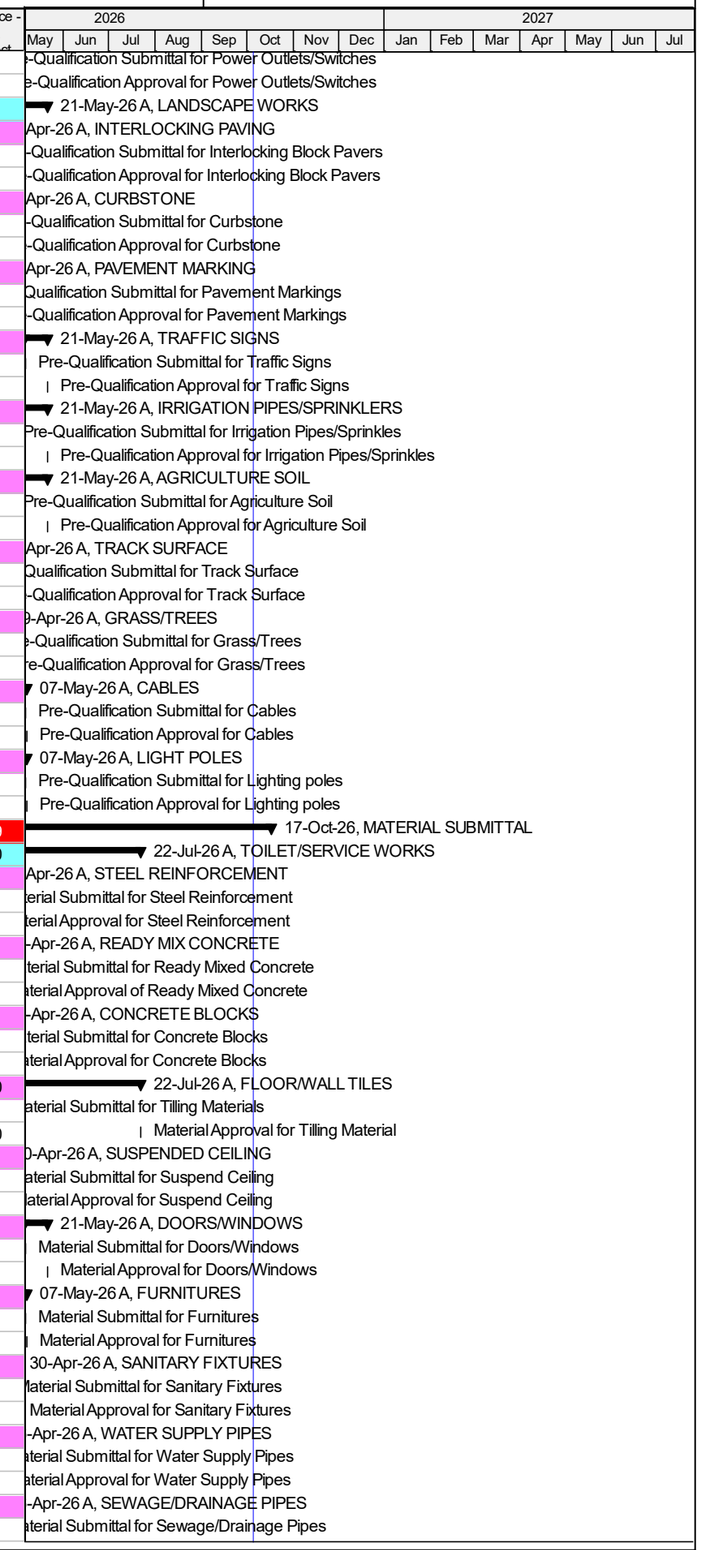


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Material Approval for Sewage/Drainage Pipes	2	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Package AC Units	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Package AC Units	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		19	0%	0%	16-Apr-26	07-May-26	16-Apr-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Air Diffusers/Grills	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Air Diffusers/Grills	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		6	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Galvanized Ducts	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Galvanized Ducts	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
EXHAUST FANS		18	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Exhaust Fans	2	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Exhaust Fans	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
LIGHTING FIXTURES		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Lighting Fixtures	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Lighting Fixtures	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
SWITCHES/SOCKETS		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Switches/Sockets	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Switches/Sockets	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
EARTHING SYSTEM		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Earthing System	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Earthing System	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Distribution Panels	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Distribution Panels	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
PLAYGROUND WORKS		158	0%	0%	12-Apr-26	15-Jul-26	12-Apr-26 A	17-Oct-26	0.00	0.00	0.00	-79
PVC MEMBRANE		77	0%	0%	06-May-26	15-Jul-26	06-May-26 A	27-Jul-26 A	0.00	0.00	0.00	-10
MLTX-02-004-EM	Material Submittal for PVC Membrane	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for PVC Membrane	10	100%	100%	05-Jul-26	15-Jul-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-10
STEEL TENSION CABLES		137	0%	0%	06-May-26	15-Jul-26	06-May-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Steel Tension Cables	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Steel Tension Cables	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
EMERGENCY DOORS		137	0%	0%	06-May-26	15-Jul-26	06-May-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Emergency Doors	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Emergency Doors	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
PRESSURE UNITS		137	0%	0%	06-May-26	15-Jul-26	06-May-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Pressure Units	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Pressure Units	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
AIR LOCK DOORS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Lock Doors	5	100%	100%	06-May-26	11-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Lock Doors	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
ARTIFICIAL TURF		17	0%	0%	12-Apr-26	30-Apr-26	12-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Artificial TURF	15	100%	100%	12-Apr-26	28-Apr-26	12-Apr-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Artificial TURF	3	100%	100%	28-Apr-26	30-Apr-26	28-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		73	0%	0%	06-May-26	15-Jul-26	06-May-26 A	22-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-004-EM	Material Submittal for Rubber Granules	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Rubber Granules	10	100%	100%	05-Jul-26	15-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-6
PADEL GLASS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Padel Glass	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Padel Glass	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		57	0%	0%	25-May-26	15-Jul-26	25-May-26 A	22-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-004-EM	Material Submittal for Wire Mesh/Steel Sets	1	100%	100%	25-May-26	25-May-26	25-May-26 A	25-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Wire Mesh/Steel Sets	10	100%	100%	05-Jul-26	15-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-6
AGGREGATE BASE COURSE		11	0%	0%	21-May-26	06-Jun-26	21-May-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Aggregate Base Course	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		2	0%	0%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Bituminous Base & Wearing Cource	2	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for the Site	1	100%	100%	18-Apr-26	18-Apr-26	18-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MARKING PAINT		6	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Marking Paint	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0

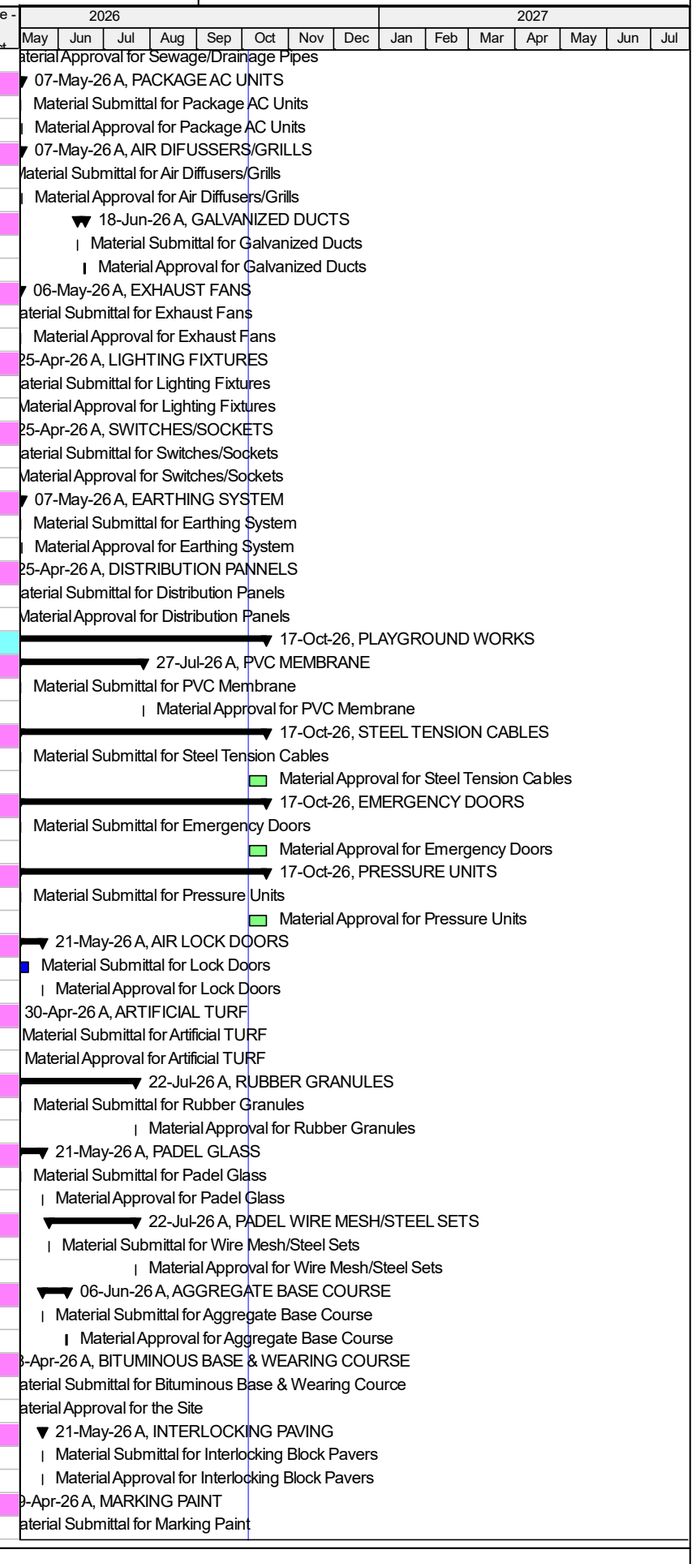

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Material Approval for Marking Paint	2	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Package AC Units	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Package AC Units	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Air Difussers/Grills	9	100%	100%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Air Difussers/Grills	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		6	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Galvanized Duct	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Galvanized Duct	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
EXHAUST FANS		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Exhaust Fans	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Exhaust Fans	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION BOARDS		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Distribution Boards	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Distribution Boards	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
POWER CABLES		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Power Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Power Cables	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
LIGHT FIXTURES		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Light Fixtures	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Light Fixtures	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
CCTV MATERIALS		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for CCTV	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for CCTV	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
POWER OUTLETS/SWITCHES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Power Outlets/Switches	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Power Outlets/Switches	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LANDSCAPE WORKS		44	0%	0%	13-Apr-26	06-Jun-26	13-Apr-26 A	06-Jun-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Interlocking Block Pavers	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Interlocking Block Pavers	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
CURBSTONE		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Curbstone	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Curbstone	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
PAVEMENT MARKING		6	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Pavement Markings	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Pavement Markings	2	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
TRAFFIC SIGNS		24	0%	0%	06-May-26	06-Jun-26	06-May-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Traffic Signs	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Traffic Signs	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
IRRIGATION PIPES/SPRINKLERS		34	0%	0%	13-Apr-26	21-May-26	13-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Irrigation Pipes/Sprinkles	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Irrigation Pipes/Sprinkles	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AGRICULTURE SOIL		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Agriculture Soil	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Agriculture Soil	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
TRACK SURFACE		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Track Surface	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Track Surface	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
GRASS/TREES		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Grass/Trees	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Grass/Trees	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
CABLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Cables	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Cables	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LIGHT POLES		22	0%	0%	13-Apr-26	07-May-26	13-Apr-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Lighting poles	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Lighting poles	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
PROCUREMENT		182	0%	0%	07-May-26	14-Sep-26	07-May-26 A	26-Nov-26	0.00	0.00	0.00	-62
SHORT LEAD ITEM		164	0%	0%	07-May-26	17-Aug-26	07-May-26 A	18-Nov-26	0.00	0.00	0.00	-79
TOILET/SERVICE WORKS		153	0%	0%	07-May-26	15-Aug-26	07-May-26 A	28-Oct-26	0.00	0.00	0.00	-63
STEEL REINFORCEMENT		58	0%	0%	13-May-26	09-Jul-26	13-May-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-PR-1	PO for Steel Reinforcement	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0

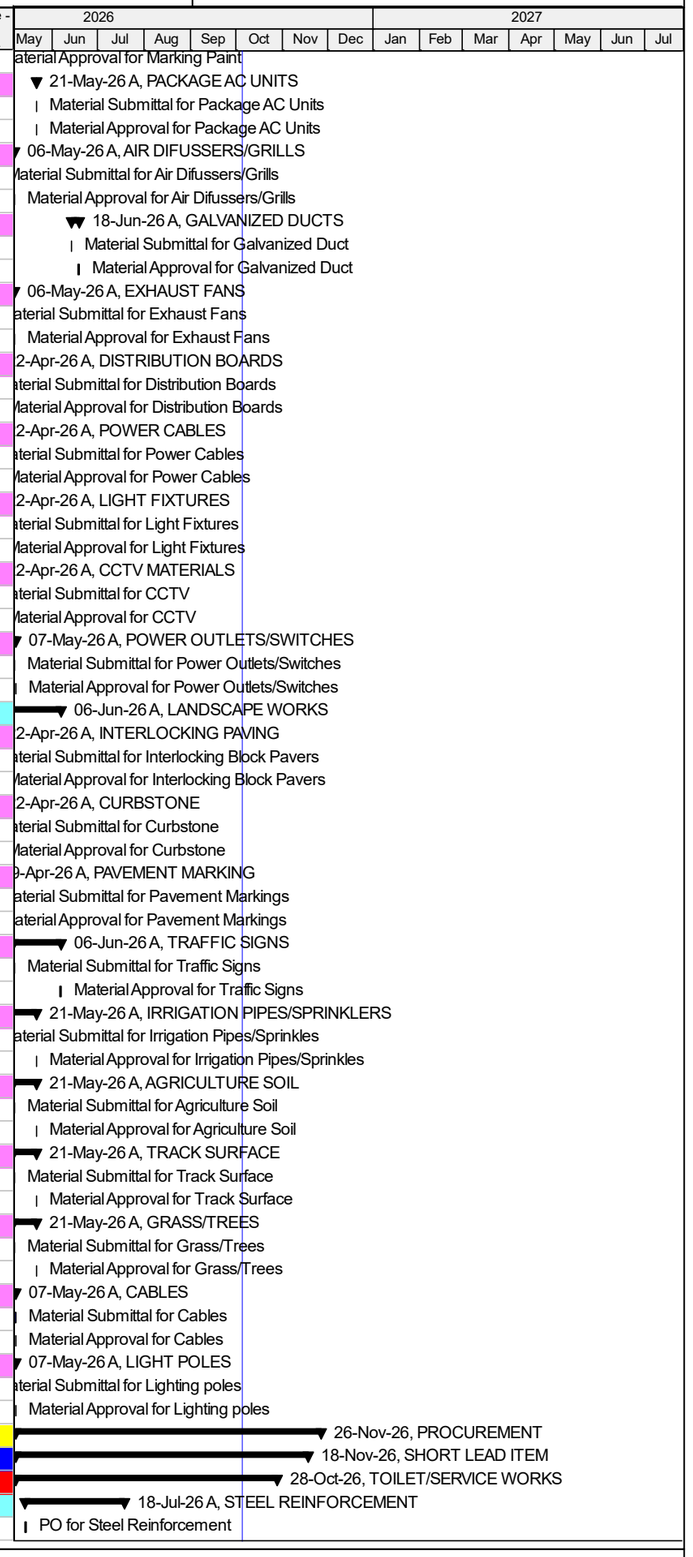


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-PR-1	Material Delivery of Steel Reinforcement	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
CONCRETE BLOCKS		74	0%	0%	07-May-26	13-Jul-26	07-May-26 A	27-Jul-26 A	0.00	0.00	0.00	-12
MLTX-02-004-PR-1	PO for Concrete Blocks	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery of Concrete Blocks	8	100%	100%	05-Jul-26	13-Jul-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-12
FLOOR/WALL TILES		91	0%	0%	05-Jul-26	15-Aug-26	22-Jul-26 A	27-Sep-26 A	0.00	0.00	0.00	-36
MLTX-02-004-PR-1	PO for Tilling Materials	5	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-11
MLTX-02-004-PR-1	Material Delivery of Tailling Material	13	100%	100%	01-Aug-26	15-Aug-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-36
SUSPENDED CEILING		37	0%	0%	24-Jun-26	19-Jul-26	24-Jun-26 A	22-Jul-26 A	0.00	0.00	0.00	-2
MLTX-02-004-PR-1	PO for Suspend Ceiling	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery of Suspend Ceiling	13	100%	100%	05-Jul-26	19-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-2
DOORS/WINDOWS		103	0%	0%	24-Jun-26	21-Jul-26	24-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Doors/Windows	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Doors/Windows	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
WATER SUPPLY PIPES		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Water Supply Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Water Supply Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Sewage/Drainage Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Sewage/Drainage Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		108	0%	0%	16-Jun-26	19-Jul-26	16-Jun-26 A	20-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Sanitary Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Sanitary Fixtures	13	100%	0%	05-Jul-26	19-Jul-26	06-Oct-26	20-Oct-26	0.00	0.00	0.00	-79
PACKAGE AC UNITS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Package AC Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Package AC Units	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
AIR DIFUSSERS/GRILLS		23	0%	0%	05-Jul-26	30-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-49
MLTX-02-004-PR-1	PO for Air Diffusers/Grills	8	100%	100%	05-Jul-26	13-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-63
MLTX-02-004-PR-1	Material Delivery for Air Diffusers/Grills	15	100%	100%	14-Jul-26	30-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-49
GALVANIZED DUCTS		23	0%	0%	05-Jul-26	30-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-49
MLTX-02-004-PR-1	PO for Galvanized Ducts	8	100%	100%	05-Jul-26	13-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-64
MLTX-02-004-PR-1	Material Delivery for Galvanized Ducts	15	100%	100%	14-Jul-26	30-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-49
EXHAUST FANS		97	0%	0%	18-Jun-26	15-Jul-26	18-Jun-26 A	27-Sep-26 A	0.00	0.00	0.00	-62
MLTX-02-004-PR-1	PO for Exhaust Fans	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Exhaust Fans	10	100%	100%	05-Jul-26	15-Jul-26	27-Sep-26 A	27-Sep-26 A	0.00	0.00	0.00	-62
LIGHTING FIXTURES		92	0%	0%	01-Jul-26	15-Jul-26	01-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Lighting Fixtures	2	100%	100%	01-Jul-26	02-Jul-26	01-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
SWITCHES/SOCKETS		95	0%	0%	24-Jun-26	12-Jul-26	24-Jun-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Switches/Sockets	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
EARTHING SYSTEM		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Earthing System	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Earthing System	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Distribution Panels	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Delivery for Distribution Panels	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
FURNITURES		115	0%	0%	16-Jun-26	27-Jul-26	16-Jun-26 A	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Furnitures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Furnitures	20	100%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
PLAYGROUND WORKS		164	0%	0%	07-May-26	17-Aug-26	07-May-26 A	18-Nov-26	0.00	0.00	0.00	-79
PVC MEMBRANE		115	0%	0%	16-Jun-26	27-Jul-26	16-Jun-26 A	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for PVC Membrane	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for PVC Membrane	20	100%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
ARTIFICIAL TURF		107	0%	0%	16-Jun-26	18-Jul-26	16-Jun-26 A	19-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Artificial TURF	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Artificial TURF	12	100%	0%	05-Jul-26	18-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-79
RUBBER GRANULES		107	0%	0%	16-Jun-26	18-Jul-26	16-Jun-26 A	19-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Rubber Granules	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Rubber Granules	12	100%	0%	05-Jul-26	18-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-79
PADEL GLASS		113	0%	0%	16-Jun-26	25-Jul-26	16-Jun-26 A	26-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Padel Glass	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Padel Glass	18	100%	0%	05-Jul-26	25-Jul-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-79
PADEL WIRE MESH/STEEL SETS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Wire Mesh/Steel Sets	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0

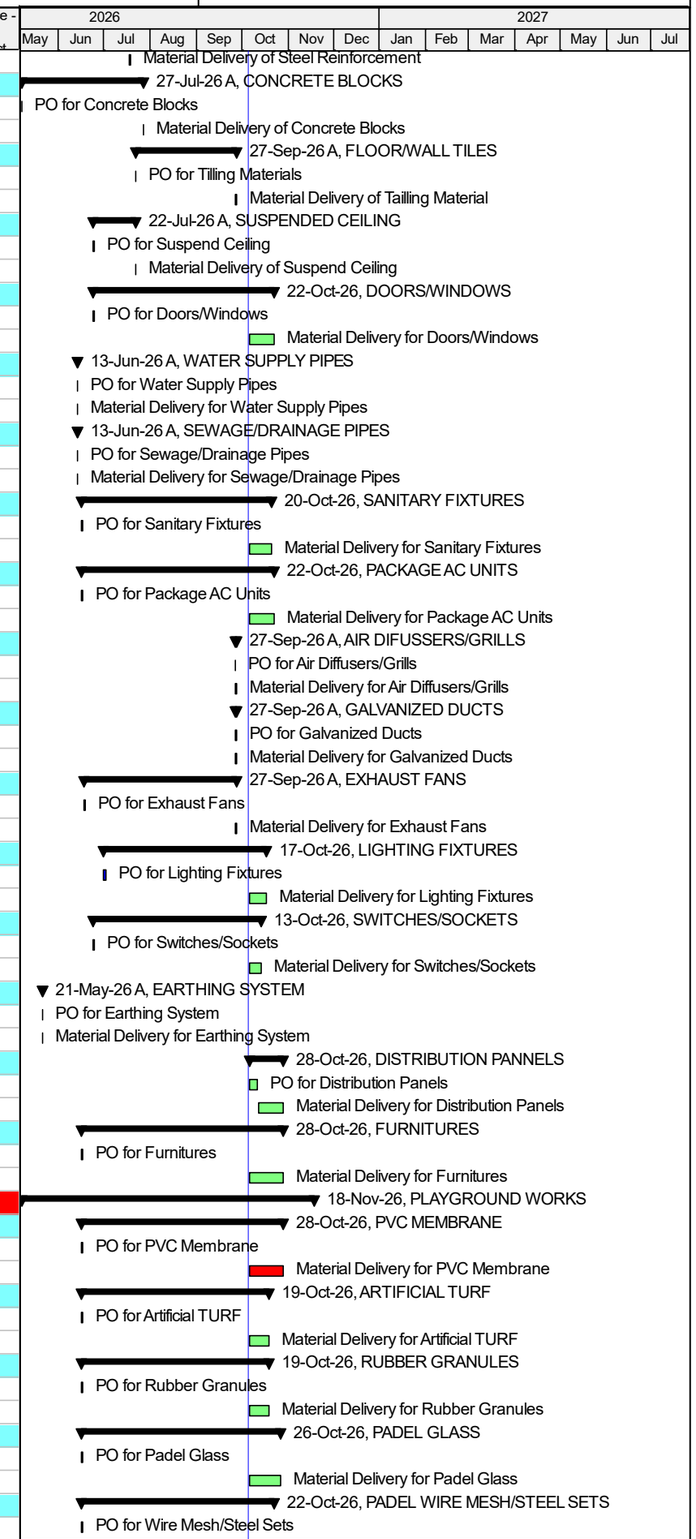

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
AGGREGATE BASE COURSE		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		15	0%	0%	16-Jun-26	02-Jul-26	16-Jun-26 A	02-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Bituminous Base & Wearing Course	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for the Site	1	100%	100%	02-Jul-26	02-Jul-26	02-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		134	0%	0%	07-May-26	13-Jul-26	07-May-26 A	14-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Interlocking Block Pavers	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Interlocking Block Pavers	8	100%	0%	05-Jul-26	13-Jul-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-79
MARKING PAINT		102	0%	0%	05-Jul-26	17-Aug-26	22-Jul-26 A	18-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Marking Paint	15	100%	100%	05-Jul-26	21-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-PR-1	Material Delivery for Marking Paint	17	100%	0%	29-Jul-26	17-Aug-26	31-Oct-26	18-Nov-26	0.00	0.00	0.00	-79
PACKAGE AC UNITS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Package AC Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Package AC Units	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
AIR DIFUSSERS/GRILLS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Air Difussers/Grills	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Galvanized Duct	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Exhaust Fans	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
DISTRIBUTION BOARDS		79	0%	0%	22-Jul-26	13-Aug-26	22-Jul-26 A	09-Nov-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Distribution Boards	5	100%	100%	22-Jul-26	27-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-PR-1	Material Delivery for Distribution Boards	15	100%	0%	28-Jul-26	13-Aug-26	24-Oct-26	09-Nov-26	0.00	0.00	0.00	-74
POWER CABLES		105	0%	0%	16-Jun-26	15-Jul-26	16-Jun-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Power Cables	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
LIGHT FIXTURES		111	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26 A	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Light Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Light Fixtures	16	100%	0%	05-Jul-26	22-Jul-26	06-Oct-26	24-Oct-26	0.00	0.00	0.00	-79
CCTV MATERIALS		21	0%	0%	05-Jul-26	28-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for CCTV	6	100%	0%	05-Jul-26	11-Jul-26	06-Oct-26	12-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Delivery for CCTV	15	100%	0%	12-Jul-26	28-Jul-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-79
POWER OUTLETS/SWITCHES		18	0%	0%	05-Jul-26	28-Jul-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-76
MLTX-02-004-PR-1	PO for Power Outlets/Switches	6	100%	0%	05-Jul-26	11-Jul-26	06-Oct-26	12-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Delivery for Power Outlets/Switches	6	100%	0%	22-Jul-26	28-Jul-26	20-Oct-26	26-Oct-26	0.00	0.00	0.00	-76
LANDSCAPE WORKS		153	0%	0%	07-May-26	10-Aug-26	07-May-26 A	05-Nov-26	0.00	0.00	0.00	-74
INTERLOCKING PAVING		138	0%	0%	07-May-26	18-Jul-26	07-May-26 A	19-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Interlocking Block Pavers	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Interlocking Block Pavers	12	100%	0%	05-Jul-26	18-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-79
CURBSTONE		127	0%	0%	07-May-26	18-Jul-26	07-May-26 A	14-Sep-26 A	0.00	0.00	0.00	-50
MLTX-02-004-PR-1	PO for Curbstone	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Curbstone	12	100%	100%	05-Jul-26	18-Jul-26	14-Sep-26 A	14-Sep-26 A	0.00	0.00	0.00	-50
PAVEMENT MARKING		78	0%	0%	05-Jul-26	21-Jul-26	18-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Pavement Markings	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-PR-1	Material Delivery for Pavement Markings	10	100%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
TRAFFIC SIGNS		74	0%	0%	05-Jul-26	21-Jul-26	22-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Traffic Signs	5	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-15
MLTX-02-004-PR-1	Material Delivery for Traffic Signs	10	100%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
IRRIGATION PIPES/SPRINKLERS		76	0%	0%	05-Jul-26	19-Jul-26	18-Jul-26 A	14-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	0%	11-Jul-26	19-Jul-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-74
AGRICULTURE SOIL		80	0%	0%	05-Jul-26	23-Jul-26	18-Jul-26 A	19-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Agriculture Soil	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-PR-1	Material Delivery for Agriculture Soil	12	100%	0%	11-Jul-26	23-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
TRACK SURFACE		98	0%	0%	24-Jun-26	15-Jul-26	24-Jun-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Track Surface	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Track Surface	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
GRASS/TREES		95	0%	0%	11-Jul-26	10-Aug-26	18-Jul-26 A	05-Nov-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Grass/Trees	5	100%	100%	11-Jul-26	15-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-2

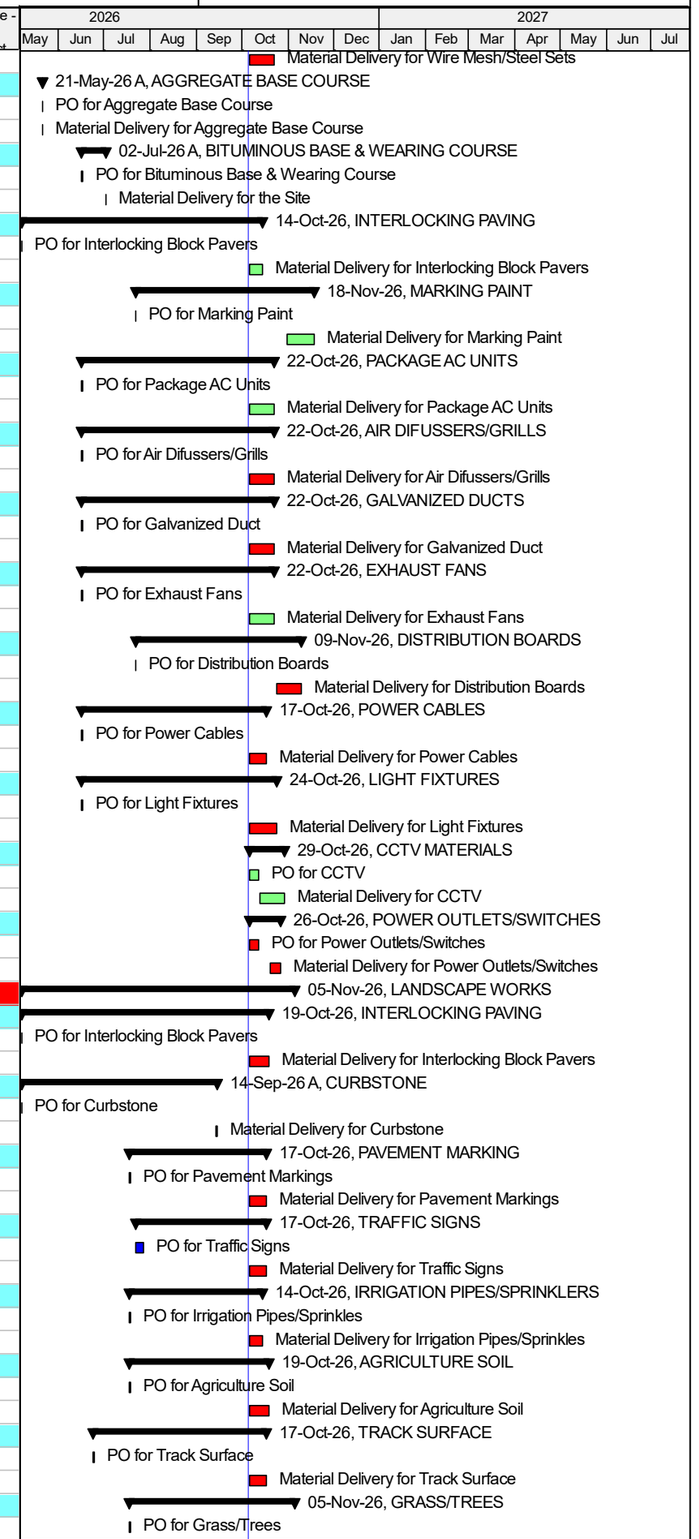

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-PR-1	Material Delivery for Grass/Trees	15	100%	0%	25-Jul-26	10-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-74
CABLES		70	0%	0%	11-Jul-26	02-Aug-26	18-Jul-26 A	17-Sep-26 A	0.00	0.00	0.00	-40
MLTX-02-004-PR-1	PO for Cables	5	100%	100%	11-Jul-26	15-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-2
MLTX-02-004-PR-1	Material Delivery for Cables	15	100%	100%	16-Jul-26	02-Aug-26	17-Sep-26 A	17-Sep-26 A	0.00	0.00	0.00	-40
LONG LEAD ITEM		151	0%	0%	16-Jun-26	14-Sep-26	16-Jun-26 A	26-Nov-26	0.00	0.00	0.00	-62
PLAYGROUND WORKS		140	0%	0%	16-Jun-26	25-Aug-26	16-Jun-26 A	26-Nov-26	0.00	0.00	0.00	-79
STEEL TENSION CABLES		129	0%	0%	16-Jun-26	18-Aug-26	16-Jun-26 A	14-Nov-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Steel Tension Cables	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	16-Jul-26	02-Aug-26	18-Oct-26	03-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Fabrication for Steel Tension Cables	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	7	100%	0%	11-Aug-26	18-Aug-26	07-Nov-26	14-Nov-26	0.00	0.00	0.00	-74
EMERGENCY DOORS		135	0%	0%	16-Jun-26	19-Aug-26	16-Jun-26 A	21-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Emergency Doors	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Emergency Doors	20	100%	0%	22-Jul-26	13-Aug-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Fabrication for Emergency Doors	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	5	100%	0%	15-Aug-26	19-Aug-26	16-Nov-26	21-Nov-26	0.00	0.00	0.00	-79
PRESSURE UNITS		140	0%	0%	16-Jun-26	25-Aug-26	16-Jun-26 A	26-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Pressure Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Pressure Units	20	100%	0%	22-Jul-26	13-Aug-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Fabrication for Pressure Units	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	5	100%	0%	20-Aug-26	25-Aug-26	22-Nov-26	26-Nov-26	0.00	0.00	0.00	-79
AIR LOCK DOORS		135	0%	0%	16-Jun-26	19-Aug-26	16-Jun-26 A	21-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Lock Doors	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Lock Doors	20	100%	0%	22-Jul-26	13-Aug-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Fabrication for Lock Doors	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	5	100%	0%	15-Aug-26	19-Aug-26	16-Nov-26	21-Nov-26	0.00	0.00	0.00	-79
LANDSCAPE WORKS		149	0%	0%	18-Jun-26	14-Sep-26	18-Jun-26 A	28-Sep-26 A	0.00	0.00	0.00	-11
LIGHT POLES		149	0%	0%	18-Jun-26	14-Sep-26	18-Jun-26 A	28-Sep-26 A	0.00	0.00	0.00	-11
MLTX-02-004-PR-1	PO for Lighting poles	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Fabrication for Lighting poles	25	100%	100%	19-Jul-26	16-Aug-26	27-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	-10
MLTX-02-004-PR-1	Material Delivery for Lighting poles	20	100%	100%	17-Aug-26	08-Sep-26	28-Sep-26 A	28-Sep-26 A	0.00	0.00	0.00	-16
MLTX-02-004-PR-1	Staging time	5	100%	100%	09-Sep-26	14-Sep-26	28-Sep-26 A	28-Sep-26 A	0.00	0.00	0.00	-11
CONSTRUCTION PHASE		283	39.38%	36.72%	25-Apr-26	25-Jan-27	25-Apr-26 A	29-Mar-27	4,936,857.12	4,603,401.03	12,535,459.74	-50
SITE WORKS		283	38.15%	37.13%	25-Apr-26	25-Jan-27	25-Apr-26 A	29-Mar-27	4,352,608.52	4,236,401.48	11,408,917.03	-50
EARTH WORKS		81	100%	100%	25-Apr-26	30-Jul-26	25-Apr-26 A	08-Aug-26 A	1,195,739.61	1,195,739.61	1,195,739.61	-7
MLTX-02-004-CN-133	Excavation (in all types of soil) including Compaction	15	100%	100%	25-Apr-26	11-May-26	25-Apr-26 A	11-May-26 A	211,926.00	211,926.00	211,926.00	0
MLTX-02-004-CN-133	Excavation (in all types of soil) including Compaction	15	100%	100%	27-Apr-26	14-May-26	27-Apr-26 A	14-May-26 A	10,773.75	10,773.75	10,773.75	0
MLTX-02-004-CN-133	Excavation (in all types of soil) including Compaction	13	100%	100%	25-Apr-26	10-May-26	25-Apr-26 A	10-May-26 A	130,541.73	130,541.73	130,541.73	0
MLTX-02-004-CN-133	Backfilling on Layers (Rockfill) including Compaction	44	100%	100%	10-May-26	02-Jul-26	10-May-26 A	02-Jul-26 A	290,941.90	290,941.90	290,941.90	0
MLTX-02-004-CN-133	Backfilling on Layers (Rockfill) including Compaction	39	100%	100%	16-May-26	02-Jul-26	16-May-26 A	02-Jul-26 A	51,187.50	51,187.50	51,187.50	0
MLTX-02-004-CN-133	Backfilling on Layers (Rockfill) including Compaction	44	100%	100%	10-May-26	02-Jul-26	10-May-26 A	02-Jul-26 A	238,875.00	238,875.00	238,875.00	0
MLTX-02-004-CN-138	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	05-Jul-26	13-Jul-26	05-Jul-26 A	19-Jul-26 A	27,300.00	27,300.00	27,300.00	-5
MLTX-02-004-CN-147	Backfilling on Layers (Selected Soil) including Compaction	15	100%	100%	14-Jul-26	30-Jul-26	09-Jul-26 A	05-Aug-26 A	131,824.88	131,824.88	131,824.88	-5
MLTX-02-004-CN-147	Backfilling on Layers (Selected Soil) including Compaction	10	100%	100%	14-Jul-26	25-Jul-26	18-Jul-26 A	08-Aug-26 A	102,368.86	102,368.86	102,368.86	-12
LANDSCAPE WORKS		190	31.21%	29.78%	05-Jul-26	25-Jan-27	11-Jul-26 A	29-Mar-27	3,156,868.91	3,012,874.37	10,115,678.40	-50
PLAYGROUND AREA		141	35.14%	55.46%	05-Jul-26	05-Jan-27	22-Aug-26 A	02-Feb-27	646,993.91	1,021,246.20	1,841,383.70	-24
FOOTBALL PLAYGROUND		129	66.67%	33.33%	05-Jul-26	21-Nov-26	22-Aug-26 A	19-Jan-27	230,100.00	115,050.00	345,150.00	-51
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Football Playground)	18	100%	100%	05-Jul-26	25-Jul-26	22-Aug-26 A	24-Aug-26 A	57,525.00	57,525.00	57,525.00	-26
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Football	11	100%	100%	26-Jul-26	06-Aug-26	29-Aug-26 A	15-Sep-26 A	57,525.00	57,525.00	57,525.00	-34
MLTX-02-004-CI	Finishing and Surface Finish Works (Football Playground)	15	80%	0%	21-Sep-26	08-Oct-26	29-Oct-26	15-Nov-26	115,050.00	0.00	143,812.50	-32
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	10	0%	0%	10-Nov-26	21-Nov-26	09-Jan-27	19-Jan-27	0.00	0.00	71,906.25	-51
MLTX-02-004-CI	Surface Marking and Painting (Football Playground)	10	0%	0%	27-Oct-26	07-Nov-26	03-Dec-26	14-Dec-26	0.00	0.00	14,381.25	-32
PADEL PLAYGROUND		111	75%	55%	26-Jul-26	21-Nov-26	22-Aug-26 A	19-Jan-27	160,875.00	117,975.00	214,500.00	-51
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Padel Playground)	11	100%	100%	26-Jul-26	06-Aug-26	22-Aug-26 A	24-Aug-26 A	75,075.00	75,075.00	75,075.00	-15
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Padel	10	100%	100%	08-Aug-26	18-Aug-26	29-Aug-26 A	15-Sep-26 A	42,900.00	42,900.00	42,900.00	-24
MLTX-02-004-CI	Finishing and Surface Finish Works (Padel Playground)	15	80%	0%	21-Sep-26	08-Oct-26	29-Oct-26	15-Nov-26	42,900.00	0.00	53,625.00	-32
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	10	0%	0%	10-Nov-26	21-Nov-26	09-Jan-27	19-Jan-27	0.00	0.00	32,175.00	-51
MLTX-02-004-CI	Surface Marking and Painting (Padel Playground)	10	0%	0%	10-Nov-26	21-Nov-26	09-Jan-27	19-Jan-27	0.00	0.00	10,725.00	-51
BASKETBALL PLAYGROUND		112	20%	20%	08-Aug-26	05-Dec-26	22-Aug-26 A	02-Feb-27	62,400.00	62,400.00	312,000.00	-51
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Basketball	10	100%	100%	08-Aug-26	18-Aug-26	22-Aug-26 A	24-Aug-26 A	31,200.00	31,200.00	31,200.00	-5
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Basketball	10	100%	100%	19-Aug-26	30-Aug-26	29-Aug-26 A	15-Sep-26 A	31,200.00	31,200.00	31,200.00	-14
MLTX-02-004-CI	Finishing and Surface Finish Works (Basketball Playground)	15	0%	0%	10-Oct-26	26-Oct-26	16-Nov-26	02-Dec-26	0.00	0.00	156,000.00	-32
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	22-Nov-26	02-Dec-26	20-Jan-27	31-Jan-27	0.00	0.00	78,000.00	-51
MLTX-02-004-CI	Surface Marking and Painting (Basketball Playground)	12	0%	0%	22-Nov-26	05-Dec-26	20-Jan-27	02-Feb-27	0.00	0.00	15,600.00	-51

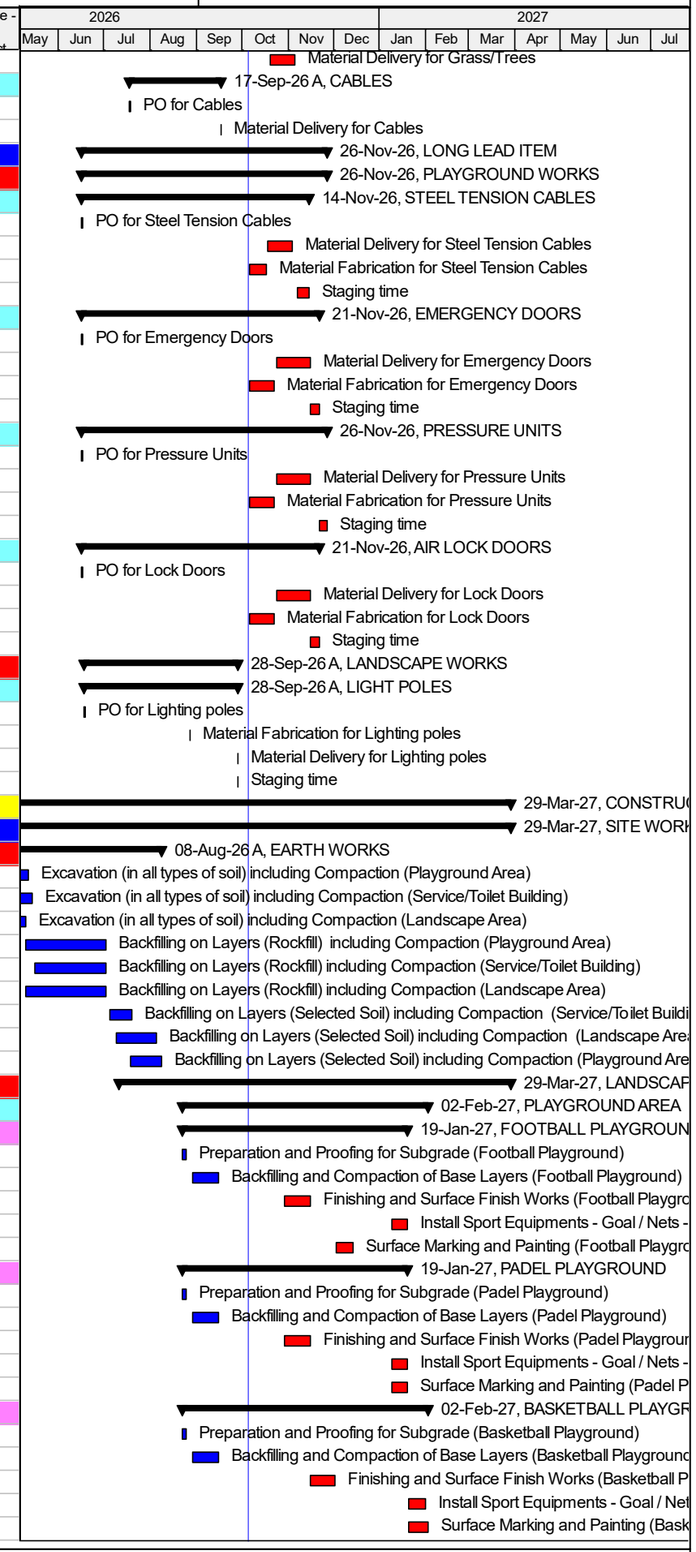

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PADEL FENCE		108	0%	30%	06-Dec-26	05-Jan-27	15-Sep-26 A	19-Nov-26	0.00	24,862.50	82,875.00	40
MLTX-02-004-CI	Excavation for Fence	5	0%	100%	06-Dec-26	10-Dec-26	15-Sep-26 A	15-Sep-26 A	0.00	8,287.50	8,287.50	73
MLTX-02-004-CI	Concrete Foundation for Fence including Posts Fixation	4	0%	100%	06-Dec-26	09-Dec-26	29-Sep-26 A	29-Sep-26 A	0.00	16,575.00	16,575.00	61
MLTX-02-004-CI	Backfilling and Reinstatement for Concrete Foundation	2	0%	0%	10-Dec-26	12-Dec-26	06-Oct-26	07-Oct-26	0.00	0.00	4,143.75	56
MLTX-02-004-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	13-Dec-26	23-Dec-26	27-Oct-26	07-Nov-26	0.00	0.00	33,150.00	40
MLTX-02-004-CI	Chain Link Fence Installation and Fixation	10	0%	0%	13-Dec-26	23-Dec-26	27-Oct-26	07-Nov-26	0.00	0.00	16,575.00	40
MLTX-02-004-CI	Install of Fence Gates	11	0%	0%	24-Dec-26	05-Jan-27	08-Nov-26	19-Nov-26	0.00	0.00	4,143.75	40
CURBSTOEN/INTERLOCK		43	21.83%	79.04%	29-Sep-26	05-Nov-26	20-Sep-26 A	05-Nov-26	193,618.91	700,958.70	886,858.70	0
MLTX-02-004-CI	Interlock Installation (Grey Scale) for LandScape (Including	15	0%	0%	20-Oct-26	05-Nov-26	20-Oct-26	05-Nov-26	0.00	0.00	185,900.00	0
MLTX-02-004-CI	Concrete Works Under Curbstone	8	75%	100%	29-Sep-26	07-Oct-26	20-Sep-26 A	22-Sep-26 A	193,618.91	258,158.55	258,158.55	13
MLTX-02-004-CI	Curbstone Installation	10	0%	100%	08-Oct-26	19-Oct-26	20-Sep-26 A	29-Sep-26 A	0.00	442,800.15	442,800.15	18
AIR DOME		168	44.77%	20.5%	31-Aug-26	04-Jan-27	11-Jul-26 A	28-Feb-27	2,509,875.00	1,149,281.25	5,606,250.00	-46
CIVIL WORKS		90	100%	48.81%	31-Aug-26	05-Oct-26	11-Jul-26 A	28-Nov-26	2,354,625.00	1,149,281.25	2,354,625.00	-46
MLTX-02-004-CI	Excavation for Foundation & Playground Area (Air Dome)	5	100%	100%	31-Aug-26	05-Sep-26	11-Jul-26 A	12-Aug-26 A	280,312.50	280,312.50	280,312.50	20
MLTX-02-004-CI	Concrete Works for Foundations including Anchor Bolts (Air	5	100%	100%	06-Sep-26	10-Sep-26	29-Jul-26 A	22-Sep-26 A	392,437.50	392,437.50	392,437.50	-10
MLTX-02-004-CI	Cable System Installation (Air Dome)	8	100%	85%	12-Sep-26	20-Sep-26	24-Sep-26 A	14-Oct-26	560,625.00	476,531.25	560,625.00	-20
MLTX-02-004-CI	Install of Membrane Covering System (Air Dome)	12	100%	0%	21-Sep-26	05-Oct-26	15-Nov-26	28-Nov-26	560,625.00	0.00	560,625.00	-46
MLTX-02-004-CI	Thermal Insulation Works (Air Dome)	6	100%	0%	21-Sep-26	28-Sep-26	15-Nov-26	21-Nov-26	560,625.00	0.00	560,625.00	-46
MECHANICAL WORKS		36	13.85%	0%	29-Sep-26	09-Nov-26	28-Nov-26	07-Jan-27	155,250.00	0.00	1,121,250.00	-51
MLTX-02-004-CI	Air Ducts and Grills Installation (Air Dome)	13	46.15%	0%	29-Sep-26	13-Oct-26	28-Nov-26	12-Dec-26	155,250.00	0.00	280,312.50	-51
MLTX-02-004-CI	Air Units Installation (Air Dome)	13	0%	0%	14-Oct-26	28-Oct-26	13-Dec-26	27-Dec-26	0.00	0.00	448,500.00	-51
MLTX-02-004-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	29-Oct-26	09-Nov-26	28-Dec-26	07-Jan-27	0.00	0.00	392,437.50	-51
ELECTRICAL WORKS		66	0%	0%	14-Oct-26	04-Jan-27	13-Dec-26	28-Feb-27	0.00	0.00	1,681,875.00	-46
MLTX-02-004-CI	Light Fixture Works (Air Dome)	15	0%	0%	14-Oct-26	31-Oct-26	13-Dec-26	29-Dec-26	0.00	0.00	280,312.50	-51
MLTX-02-004-CI	Distribution Board and Electrical Works (Air Dome)	15	0%	0%	07-Nov-26	23-Nov-26	30-Dec-26	16-Jan-27	0.00	0.00	280,312.50	-46
MLTX-02-004-CI	External Electrical Connection Works (Air Dome)	15	0%	0%	24-Nov-26	10-Dec-26	17-Jan-27	02-Feb-27	0.00	0.00	280,312.50	-46
MLTX-02-004-CI	Emergency Generator Installation (Air Dome)	11	0%	0%	12-Dec-26	23-Dec-26	03-Feb-27	15-Feb-27	0.00	0.00	560,625.00	-46
MLTX-02-004-CI	Control System Installation (Air Dome)	10	0%	0%	24-Dec-26	04-Jan-27	16-Feb-27	28-Feb-27	0.00	0.00	280,312.50	-46
FINISHES WORKS		28	0%	0%	24-Nov-26	26-Dec-26	17-Jan-27	17-Feb-27	0.00	0.00	448,500.00	-46
MLTX-02-004-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	24-Nov-26	10-Dec-26	17-Jan-27	02-Feb-27	0.00	0.00	224,250.00	-46
MLTX-02-004-CI	Logo and Signs Installation (Air Dome)	13	0%	0%	12-Dec-26	26-Dec-26	03-Feb-27	17-Feb-27	0.00	0.00	224,250.00	-46
IRRIGATION NETWORK		30	0%	79.29%	20-Oct-26	21-Nov-26	22-Aug-26 A	09-Nov-26	0.00	212,225.00	267,670.00	10
MLTX-02-004-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	12	0%	100%	20-Oct-26	02-Nov-26	22-Aug-26 A	31-Aug-26 A	0.00	80,795.00	80,795.00	53
MLTX-02-004-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	5	0%	100%	03-Nov-26	08-Nov-26	31-Aug-26 A	31-Aug-26 A	0.00	94,250.00	94,250.00	58
MLTX-02-004-CN-1	Installing of Valves and fittings for Irrigation Network	3	0%	80%	09-Nov-26	11-Nov-26	15-Sep-26 A	08-Oct-26	0.00	37,180.00	46,475.00	29
MLTX-02-004-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	18-Nov-26	21-Nov-26	07-Nov-26	09-Nov-26	0.00	0.00	46,150.00	10
NATURAL GROUND		5	0%	0%	12-Nov-26	17-Nov-26	10-Oct-26	14-Oct-26	0.00	0.00	117,000.00	29
MLTX-02-004-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	0%	12-Nov-26	17-Nov-26	10-Oct-26	14-Oct-26	0.00	0.00	117,000.00	29
PLANTING		18	0%	0%	22-Nov-26	12-Dec-26	10-Nov-26	30-Nov-26	0.00	0.00	884,633.75	10
MLTX-02-004-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	5	0%	0%	22-Nov-26	26-Nov-26	10-Nov-26	15-Nov-26	0.00	0.00	321,945.00	10
MLTX-02-004-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	05-Dec-26	12-Dec-26	23-Nov-26	30-Nov-26	0.00	0.00	175,175.00	10
MLTX-02-004-CN-1	Placement and Fixation of Trees	6	0%	0%	28-Nov-26	03-Dec-26	16-Nov-26	22-Nov-26	0.00	0.00	387,513.75	10
WALKING/BIKE PATHS		8	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26 A	14-Oct-26	0.00	276,412.50	552,825.01	58
MLTX-02-004-CN-1	Bike Path Preparation and Installation Works	8	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26 A	14-Oct-26	0.00	142,045.32	284,090.63	58
MLTX-02-004-CN-1	Walking Path Preparation and Installation Works	8	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26 A	14-Oct-26	0.00	134,367.19	268,734.38	58
GENERAL/FURNITURE		138	0%	41.81%	20-Oct-26	25-Jan-27	19-Sep-26 A	29-Mar-27	0.00	353,709.41	845,915.95	-50
MLTX-02-004-CN-1	Stamped Concrete Works for LandScape (Including	7	0%	0%	22-Dec-26	29-Dec-26	06-Mar-27	16-Mar-27	0.00	0.00	28,080.00	-62
MLTX-02-004-CN-1	Traffic Signs Posts and Poles Installation	5	0%	0%	13-Jan-27	18-Jan-27	07-Nov-26	11-Nov-26	0.00	0.00	9,750.00	58
MLTX-02-004-CN-1	Fixation and Installation of Steel Frame for Benches	10	0%	0%	22-Dec-26	02-Jan-27	15-Oct-26	26-Oct-26	0.00	0.00	17,276.03	58
MLTX-02-004-CN-1	Fixation and Installation of Benches	9	0%	0%	03-Jan-27	12-Jan-27	27-Oct-26	05-Nov-26	0.00	0.00	40,310.73	58
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Seats	9	0%	0%	03-Jan-27	12-Jan-27	27-Oct-26	05-Nov-26	0.00	0.00	43,680.00	58
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	9	0%	0%	03-Jan-27	12-Jan-27	27-Oct-26	05-Nov-26	0.00	0.00	17,160.00	58
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	13-Jan-27	25-Jan-27	17-Mar-27	29-Mar-27	0.00	0.00	14,625.00	-50
MLTX-02-004-CN-1	Preleminary Works for Site Light Poles Including Cable and	12	0%	100%	20-Oct-26	02-Nov-26	19-Sep-26 A	01-Oct-26 A	0.00	202,497.75	202,497.75	27
MLTX-02-004-CN-1	Installing of Site Light Poles	12	0%	32%	30-Dec-26	12-Jan-27	04-Oct-26 A	19-Oct-26	0.00	151,211.66	472,536.45	73
PARKING		89	0%	28.5%	30-Dec-26	12-Jan-27	11-Aug-26 A	19-Oct-26	0.00	27,787.50	97,499.02	73
MLTX-02-004-CN-13	Interlock Installation (8 Cm) for Parking Area (Including	8	0%	0%	04-Jan-27	12-Jan-27	11-Oct-26	19-Oct-26	0.00	0.00	68,249.02	73
MLTX-02-004-CN-13	Site Preparation & Compaction Under Interlock for Parking	4	0%	95%	30-Dec-26	03-Jan-27	11-Aug-26 A	10-Oct-26	0.00	27,787.50	29,250.00	73
TOILET/SERVICE BUILDING		118	51.86%	32.58%	14-Jul-26	30-Nov-26	19-Jul-26 A	05-Dec-26	584,248.60	366,999.56	1,126,542.71	-4
STRUCTURE WORKS		37	100%	100%	14-Jul-26	14-Sep-26	19-Jul-26 A	11-Aug-26 A	157,950.00	157,950.00	157,950.00	29
CONCRETE WORKS		37	100%	100%	15-Jul-26	14-Sep-26	19-Jul-26 A	03-Aug-26 A	113,782.50	113,782.50	113,782.50	36
SUB-STRUCTURE		5	100%	100%	15-Jul-26	23-Jul-26	19-Jul-26 A	25-Jul-26 A	33,345.00	33,345.00	33,345.00	-1
MLTX-02-004-CI	Plain Concrete Under Footing	3	100%	100%	15-Jul-26	18-Jul-26	19-Jul-26 A	19-Jul-26 A	1,170.00	1,170.00	1,170.00	-1
MLTX-02-004-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	19-Jul-26	23-Jul-26	20-Jul-26 A	25-Jul-26 A	32,175.00	32,175.00	32,175.00	-1



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SUPER-STRUCTURE		24	100%	100%	29-Jul-26	14-Sep-26	30-Jul-26 A	03-Aug-26 A	80,437.50	80,437.50	80,437.50	36
MLTX-02-004-CI	AAC Panels Works for Walls	18	100%	100%	29-Jul-26	18-Aug-26	30-Jul-26 A	01-Aug-26 A	48,262.50	48,262.50	48,262.50	15
MLTX-02-004-CI	Parpet Works and Lintels	8	100%	100%	06-Sep-26	14-Sep-26	01-Aug-26 A	02-Aug-26 A	16,087.50	16,087.50	16,087.50	37
MLTX-02-004-CI	AAC Panels Works for Slabs	15	100%	100%	19-Aug-26	05-Sep-26	02-Aug-26 A	03-Aug-26 A	16,087.50	16,087.50	16,087.50	28
UNDER GROUND SEPTIC TANK		11	100%	100%	15-Jul-26	12-Aug-26	23-Jul-26 A	27-Jul-26 A	33,930.00	33,930.00	33,930.00	14
MLTX-02-004-CN-1	Plain Concrete Under Footing	3	100%	100%	15-Jul-26	18-Jul-26	23-Jul-26 A	23-Jul-26 A	1,170.00	1,170.00	1,170.00	-5
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Slab Including	8	100%	100%	04-Aug-26	12-Aug-26	27-Jul-26 A	27-Jul-26 A	8,775.00	8,775.00	8,775.00	14
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Foundation Including	8	100%	100%	19-Jul-26	27-Jul-26	23-Jul-26 A	23-Jul-26 A	7,605.00	7,605.00	7,605.00	3
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	6	100%	100%	28-Jul-26	03-Aug-26	27-Jul-26 A	27-Jul-26 A	16,380.00	16,380.00	16,380.00	6
THERMAL & MOISTER PROTECTION		28	100%	100%	14-Jul-26	27-Aug-26	20-Jul-26 A	11-Aug-26 A	10,237.50	10,237.50	10,237.50	14
ANTI TERMIT CONTROL		10	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26 A	30-Jul-26 A	4,387.50	4,387.50	4,387.50	-14
MLTX-02-004-CI	Anti Termite Works Under Foundation	1	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26 A	20-Jul-26 A	1,755.00	1,755.00	1,755.00	-5
MLTX-02-004-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	14-Jul-26	14-Jul-26	30-Jul-26 A	30-Jul-26 A	2,632.50	2,632.50	2,632.50	-14
POLYETHYLENE SHEET		10	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26 A	30-Jul-26 A	2,193.75	2,193.75	2,193.75	-14
MLTX-02-004-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26 A	20-Jul-26 A	877.50	877.50	877.50	-5
MLTX-02-004-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	14-Jul-26	14-Jul-26	30-Jul-26 A	30-Jul-26 A	1,316.25	1,316.25	1,316.25	-14
EPOXY		10	100%	100%	13-Aug-26	27-Aug-26	09-Aug-26 A	11-Aug-26 A	3,656.25	3,656.25	3,656.25	14
MLTX-02-004-CI	Surface Preparation for Epoxy Coating	5	100%	100%	13-Aug-26	18-Aug-26	09-Aug-26 A	09-Aug-26 A	1,096.88	1,096.88	1,096.88	8
MLTX-02-004-CI	Epoxy Coating for Walls and Slab of Tank	8	100%	100%	19-Aug-26	27-Aug-26	11-Aug-26 A	11-Aug-26 A	2,559.38	2,559.38	2,559.38	14
MASONARY WORK		4	100%	100%	25-Jul-26	28-Jul-26	10-Aug-26 A	12-Aug-26 A	12,285.00	12,285.00	12,285.00	-13
MLTX-02-004-CN-14(	CMU Masonary Works Including all Accessories	4	100%	100%	25-Jul-26	28-Jul-26	10-Aug-26 A	12-Aug-26 A	12,285.00	12,285.00	12,285.00	-13
THERMAL & MOISTER PROTECTION		26	76.07%	85.64%	15-Sep-26	08-Oct-26	15-Sep-26 A	12-Oct-26	26,396.18	29,717.81	34,700.25	-3
MLTX-02-004-CN-14(	Preparing Surface and Preliminary Works for Toilets	4	100%	100%	15-Sep-26	19-Sep-26	15-Sep-26 A	15-Sep-26 A	2,106.00	2,106.00	2,106.00	3
MLTX-02-004-CN-14(	Finalize Water Proofing Works for Toilets	5	100%	100%	20-Sep-26	26-Sep-26	15-Sep-26 A	28-Sep-26 A	4,914.00	4,914.00	4,914.00	-2
MLTX-02-004-CN-14(	Preparing Surface and Preliminary Works for Roofing and	5	100%	100%	27-Sep-26	01-Oct-26	27-Sep-26 A	27-Sep-26 A	11,072.10	11,072.10	11,072.10	4
MLTX-02-004-CN-14(	Finalize Water Proofing Works for Roofing and Wet Areas	6	50%	70%	03-Oct-26	08-Oct-26	28-Sep-26 A	12-Oct-26	8,304.08	11,625.71	16,608.15	-3
MECHANICAL WORK		93	54.86%	7.37%	15-Sep-26	08-Nov-26	15-Aug-26 A	12-Nov-26	237,700.13	31,950.75	433,285.13	-4
HVAC SYSTEM		23	0%	47.55%	12-Oct-26	08-Nov-26	27-Sep-26 A	12-Nov-26	0.00	13,260.00	27,885.00	-4
MLTX-02-004-CN-1	Preliminary HVAC and Ventilation Works	3	0%	100%	12-Oct-26	14-Oct-26	27-Sep-26 A	27-Sep-26 A	0.00	9,360.00	9,360.00	15
MLTX-02-004-CN-1	Install and Finish HVAC and Ventilation Works Including Split	6	0%	0%	02-Nov-26	08-Nov-26	07-Nov-26	12-Nov-26	0.00	0.00	14,625.00	-4
MLTX-02-004-CN-1	Exhaust, Air Ducts Installation with all Accessories	7	0%	100%	15-Oct-26	22-Oct-26	27-Sep-26 A	27-Sep-26 A	0.00	3,900.00	3,900.00	22
WATER SUPPLY SYSTEM		64	46.77%	2.74%	17-Sep-26	18-Oct-26	15-Aug-26 A	01-Nov-26	118,072.50	6,922.50	252,427.50	-12
MLTX-02-004-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	17-Sep-26	20-Sep-26	15-Aug-26 A	15-Aug-26 A	6,922.50	6,922.50	6,922.50	31
MLTX-02-004-CN-1	Installing of HDPE Pipes and Valves for Water Supply	5	100%	0%	27-Sep-26	01-Oct-26	11-Oct-26	15-Oct-26	39,000.00	0.00	39,000.00	-12
MLTX-02-004-CN-1	Installing of Booster Pump Units Including fittings and	5	0%	0%	08-Oct-26	13-Oct-26	22-Oct-26	27-Oct-26	0.00	0.00	91,000.00	-12
MLTX-02-004-CN-1	Installing of GRP Tanks	5	60%	0%	03-Oct-26	07-Oct-26	17-Oct-26	21-Oct-26	62,400.00	0.00	104,000.00	-12
MLTX-02-004-CN-1	Installing of Valves and Fittings	4	100%	0%	21-Sep-26	26-Sep-26	06-Oct-26	10-Oct-26	9,750.00	0.00	9,750.00	-12
MLTX-02-004-CN-1	Installing of Water Heater	4	0%	0%	14-Oct-26	18-Oct-26	28-Oct-26	01-Nov-26	0.00	0.00	1,755.00	-12
SEWER/DRAINAGE SYSTEM		68	79.21%	7.79%	15-Sep-26	29-Oct-26	15-Aug-26 A	03-Nov-26	119,627.63	11,768.25	151,022.63	-4
MLTX-02-004-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	15-Sep-26	16-Sep-26	15-Aug-26 A	15-Aug-26 A	11,768.25	11,768.25	11,768.25	28
MLTX-02-004-CN-1	Installing of Plumping Fixtures and Accessories	4	100%	0%	29-Sep-26	03-Oct-26	17-Oct-26	20-Oct-26	10,359.38	0.00	10,359.38	-15
MLTX-02-004-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	24-Sep-26	28-Sep-26	12-Oct-26	15-Oct-26	85,312.50	0.00	85,312.50	-15
MLTX-02-004-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	0%	17-Sep-26	22-Sep-26	06-Oct-26	11-Oct-26	12,187.50	0.00	12,187.50	-15
MLTX-02-004-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	3	0%	0%	27-Oct-26	29-Oct-26	01-Nov-26	03-Nov-26	0.00	0.00	31,395.00	-4
FIRE PROTECTION		4	0%	0%	04-Nov-26	08-Nov-26	09-Nov-26	12-Nov-26	0.00	0.00	1,950.00	-4
MLTX-02-004-CN-1	Installing of Fire Fighting Extinguisher and accessories	4	0%	0%	04-Nov-26	08-Nov-26	09-Nov-26	12-Nov-26	0.00	0.00	1,950.00	-4
ELECTRICAL WORKS		83	33.66%	33.66%	15-Sep-26	16-Nov-26	16-Aug-26 A	21-Nov-26	72,832.50	72,832.50	216,401.38	-4
ROUGH-IN WORKS		24	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	72,832.50	72,832.50	72,832.50	23
MLTX-02-004-CN-1	Preleminary Works for Cable Works	9	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	10,700.04	10,700.04	10,700.04	23
MLTX-02-004-CN-1	Preleminary Works for Sockets and Power Points	9	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	9,230.91	9,230.91	9,230.91	23
MLTX-02-004-CN-1	Preleminary Works for Lightning Works	9	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	9,750.00	9,750.00	9,750.00	23
MLTX-02-004-CN-1	Preleminary Works for Data & Telecommunication System	9	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	12,285.00	12,285.00	12,285.00	23
MLTX-02-004-CN-1	Preleminary Works for Security and Access Control System	9	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	15,266.55	15,266.55	15,266.55	23
MLTX-02-004-CN-1	Preleminary Works for Earthing Works	9	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	15,600.00	15,600.00	15,600.00	23
FIXTURE WORKS		13	0%	0%	02-Nov-26	16-Nov-26	07-Nov-26	21-Nov-26	0.00	0.00	143,568.88	-4
MLTX-02-004-CN-1	Installing of Fire automation and Fire Alarm System	7	0%	0%	09-Nov-26	16-Nov-26	14-Nov-26	21-Nov-26	0.00	0.00	34,320.00	-4
MLTX-02-004-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	04-Nov-26	08-Nov-26	09-Nov-26	12-Nov-26	0.00	0.00	13,846.49	-4
MLTX-02-004-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	04-Nov-26	08-Nov-26	09-Nov-26	12-Nov-26	0.00	0.00	16,050.06	-4
MLTX-02-004-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	04-Nov-26	08-Nov-26	09-Nov-26	12-Nov-26	0.00	0.00	18,427.50	-4
MLTX-02-004-CN-1	Installing and Finalize Works of Security and Access Control	6	0%	0%	02-Nov-26	08-Nov-26	07-Nov-26	12-Nov-26	0.00	0.00	22,899.83	-4
MLTX-02-004-CN-1	Installing and Finalize Works of Earthing Works	6	0%	0%	02-Nov-26	08-Nov-26	07-Nov-26	12-Nov-26	0.00	0.00	23,400.00	-4
MLTX-02-004-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	02-Nov-26	08-Nov-26	07-Nov-26	12-Nov-26	0.00	0.00	14,625.00	-4
DOORS/WINDOWS		37	40%	0%	15-Sep-26	30-Nov-26	24-Oct-26	05-Dec-26	27,300.00	0.00	68,250.00	-4
MLTX-02-004-CN-14(	Preliminary Works For Doors	3	100%	0%	15-Sep-26	17-Sep-26	24-Oct-26	26-Oct-26	3,900.00	0.00	3,900.00	-32

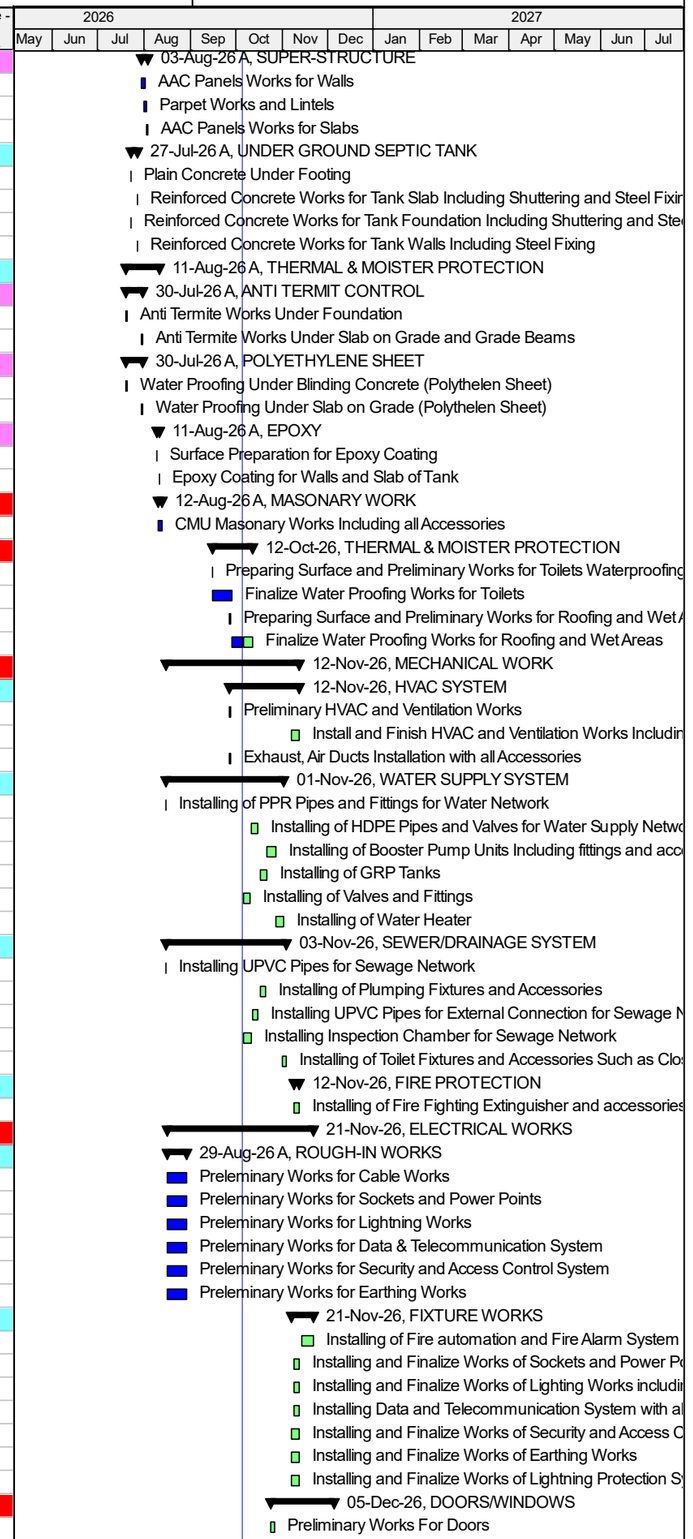

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-CN-141	Finalize Metal Doors for Toilets Building	12	0%	0%	17-Nov-26	30-Nov-26	22-Nov-26	05-Dec-26	0.00	0.00	5,850.00	-4
MLTX-02-004-CN-142	Finalize Glazzed Curtain Wall Works	4	0%	0%	02-Nov-26	05-Nov-26	07-Nov-26	10-Nov-26	0.00	0.00	35,100.00	-4
MLTX-02-004-CN-145	Preliminary Works For Windows/Curtain Wall	2	100%	0%	15-Sep-26	16-Sep-26	24-Oct-26	25-Oct-26	23,400.00	0.00	23,400.00	-32
METAL WORKS		9	0%	100%	12-Oct-26	29-Oct-26	16-Sep-26 A	27-Sep-26 A	0.00	9,750.00	9,750.00	28
MLTX-02-004-CN-140	Installation of Galvanized Steel Ladder	8	0%	100%	12-Oct-26	20-Oct-26	27-Sep-26 A	27-Sep-26 A	0.00	5,850.00	5,850.00	20
MLTX-02-004-CN-142	Installation of Galvanized Steel Roof Scupper	8	0%	100%	21-Oct-26	29-Oct-26	16-Sep-26 A	16-Sep-26 A	0.00	3,900.00	3,900.00	36
FINISHING WORKS		52	31.36%	38.78%	27-Sep-26	17-Nov-26	29-Aug-26 A	22-Nov-26	42,472.30	52,513.50	135,414.50	-4
FLOOR FINISHES		41	73.58%	69.32%	30-Sep-26	17-Nov-26	01-Oct-26 A	22-Nov-26	12,626.25	11,895.00	17,160.00	-4
MLTX-02-004-CN-1	Creamic Tiles Floor Finish Works	4	100%	100%	30-Sep-26	04-Oct-26	01-Oct-26 A	04-Oct-26 A	11,895.00	11,895.00	11,895.00	1
MLTX-02-004-CN-1	Granite Tiles Floor Finish Works	4	25%	0%	05-Oct-26	08-Oct-26	06-Oct-26	10-Oct-26	731.25	0.00	2,925.00	-1
MLTX-02-004-CN-1	Epoxy Coat on Concrete Floor	10	0%	0%	07-Nov-26	17-Nov-26	11-Nov-26	22-Nov-26	0.00	0.00	1,170.00	-4
MLTX-02-004-CN-1	Ceramic Skirting Tiles Finish Works	2	0%	0%	10-Oct-26	11-Oct-26	11-Oct-26	12-Oct-26	0.00	0.00	1,170.00	-1
WALL FINISHES		51	26.21%	38.66%	27-Sep-26	03-Nov-26	29-Aug-26 A	08-Nov-26	27,537.25	40,618.50	105,072.50	-4
MLTX-02-004-CN-1	Preliminary Works for Wall Finish Works including Plastering	3	100%	100%	27-Sep-26	29-Sep-26	29-Aug-26 A	09-Sep-26 A	18,369.00	18,369.00	18,369.00	16
MLTX-02-004-CN-1	Preliminary Works for Wall Finish Works (External)	8	100%	100%	27-Sep-26	05-Oct-26	09-Sep-26 A	10-Sep-26 A	6,552.00	6,552.00	6,552.00	20
MLTX-02-004-CN-1	Painting Finish Works for External Walls	3	0%	0%	06-Oct-26	08-Oct-26	17-Oct-26	19-Oct-26	0.00	0.00	10,478.00	-9
MLTX-02-004-CN-1	Ceramic Finish Works for Walls	6	16.67%	100%	05-Oct-26	11-Oct-26	28-Sep-26 A	29-Sep-26 A	2,616.25	15,697.50	15,697.50	11
MLTX-02-004-CN-1	Phenolic Partitions for Toilets	5	0%	0%	21-Oct-26	26-Oct-26	26-Oct-26	31-Oct-26	0.00	0.00	31,200.00	-4
MLTX-02-004-CN-1	Glass Partitions including all accessories and doors	5	0%	0%	27-Oct-26	01-Nov-26	01-Nov-26	05-Nov-26	0.00	0.00	12,285.00	-4
MLTX-02-004-CN-1	Granite Capping for Parpet	2	0%	0%	10-Oct-26	11-Oct-26	13-Oct-26	14-Oct-26	0.00	0.00	8,151.00	-3
MLTX-02-004-CN-1	Painting Finish Works for Internal Walls	2	0%	0%	02-Nov-26	03-Nov-26	07-Nov-26	08-Nov-26	0.00	0.00	2,340.00	-4
CELLING FINISHES		13	17.51%	0%	30-Sep-26	24-Oct-26	06-Oct-26	20-Oct-26	2,308.80	0.00	13,182.00	3
MLTX-02-004-CN-1	Painting Finish Works for Ceiling	3	0%	0%	21-Oct-26	24-Oct-26	18-Oct-26	20-Oct-26	0.00	0.00	1,638.00	3
MLTX-02-004-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	5	0%	0%	15-Oct-26	20-Oct-26	06-Oct-26	11-Oct-26	0.00	0.00	6,926.40	8
MLTX-02-004-CN-1	Preliminary Works for Ceiling Painting Works	10	50%	0%	30-Sep-26	11-Oct-26	06-Oct-26	17-Oct-26	2,308.80	0.00	4,617.60	-5
SPECIALTIES WORK		26	12.5%	0%	04-Oct-26	15-Nov-26	21-Oct-26	19-Nov-26	7,312.50	0.00	58,506.46	-4
MLTX-02-004-CN-141	Sanitary Fixtures and Accessories Works	4	50%	0%	04-Oct-26	07-Oct-26	21-Oct-26	25-Oct-26	7,312.50	0.00	14,625.00	-15
MLTX-02-004-CN-141	Installation of MODON Logo on the entrance	10	0%	0%	04-Nov-26	15-Nov-26	09-Nov-26	19-Nov-26	0.00	0.00	19,506.46	-4
MLTX-02-004-CN-145	Installation of Phenolic Locker	2	0%	0%	27-Oct-26	28-Oct-26	01-Nov-26	02-Nov-26	0.00	0.00	24,375.00	-4
TESTING & COMMISSIONING		104	0%	0%	01-Dec-26	18-Jan-27	08-Nov-26	09-Mar-27	0.00	0.00	0.00	-42
MLTX-02-004-TC-11920	Testing and Commissioning for MEP Works for Playground	8	0%	0%	05-Jan-27	13-Jan-27	01-Mar-27	09-Mar-27	0.00	0.00	0.00	-46
MLTX-02-004-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	15	0%	0%	01-Dec-26	17-Dec-26	06-Dec-26	22-Dec-26	0.00	0.00	0.00	-4
MLTX-02-004-TC-11940	Testing and Commissioning for MEP Works for Landscape	4	0%	0%	14-Jan-27	18-Jan-27	08-Nov-26	11-Nov-26	0.00	0.00	0.00	58
ASIR		319	21.55%	33.27%	26-Mar-26	24-Jan-27	26-Mar-26 A	11-Apr-27	2,279,478.29	3,519,653.97	10,578,073.08	-62
MOBILIZATION		63	0%	0%	26-Mar-26	10-Jun-26	26-Mar-26 A	10-Jun-26 A	0.00	0.00	0.00	0
TOPOGRAPHIC SURVEY		4	0%	0%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1320	Site Survey Works	4	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
SITE FACILITIES & OFFICES		50	0%	0%	26-Mar-26	23-May-26	26-Mar-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1340	Site Layout Plan	4	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1350	Clear & Grub for Offices & Access Road	3	100%	100%	31-Mar-26	02-Apr-26	31-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1360	Construct Site Access Roads	4	100%	100%	31-Mar-26	04-Apr-26	31-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1370	Construct Temporary Fence	32	100%	100%	15-Apr-26	21-May-26	15-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1380	Construct Site Offices & Storage	19	100%	100%	20-Apr-26	11-May-26	20-Apr-26 A	11-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1390	Install Project Signs	3	100%	100%	21-Apr-26	23-Apr-26	21-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1400	Install Site Facilities	24	100%	100%	12-Apr-26	09-May-26	12-Apr-26 A	09-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1410	Electrical Works & Connections	27	100%	100%	12-Apr-26	12-May-26	12-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1420	Construct Parking Sheds	27	100%	100%	12-Apr-26	12-May-26	12-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1430	Equipment Mobalization	24	100%	100%	14-Apr-26	12-May-26	14-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1440	Manpower Mobalization	32	100%	100%	16-Apr-26	23-May-26	16-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
PRELIMINARY SUBMITTALS		59	0%	0%	31-Mar-26	10-Jun-26	31-Mar-26 A	10-Jun-26 A	0.00	0.00	0.00	0
PREPARATIONS & SUBMITTAL BY CONTRACTORS		27	0%	0%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-154	Preparation and Submittal of Detailed Work Order	25	100%	100%	31-Mar-26	28-Apr-26	31-Mar-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-155	Preparation and Submittal of Project Execution Plan	27	100%	100%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-156	Submission of Contractor Project Quality Plan	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-157	Submission of Construction Safety & Environmental	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-158	Preparation and Submittal of Organization Chart	8	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-159	Preparation and Submittal of Communication Plan	8	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	0
APPROVALS BY EMPLOYERS		51	0%	0%	09-Apr-26	10-Jun-26	09-Apr-26 A	10-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-168	Approval of Detailed Work Order Programme (Baseline)	1	100%	100%	29-Apr-26	29-Apr-26	29-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-169	Approval of Project Execution Plan	1	100%	100%	13-May-26	13-May-26	13-May-26 A	13-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-170	Approval of Contractor Project Quality Plan	19	100%	100%	09-Apr-26	30-Apr-26	09-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-171	Approval of Construction Safety & Environmental	1	100%	100%	10-Jun-26	10-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-172	Approval of Organization Chart	18	100%	100%	09-Apr-26	29-Apr-26	09-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-173	Approval of Communication Plan	10	100%	100%	09-Apr-26	20-Apr-26	09-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0

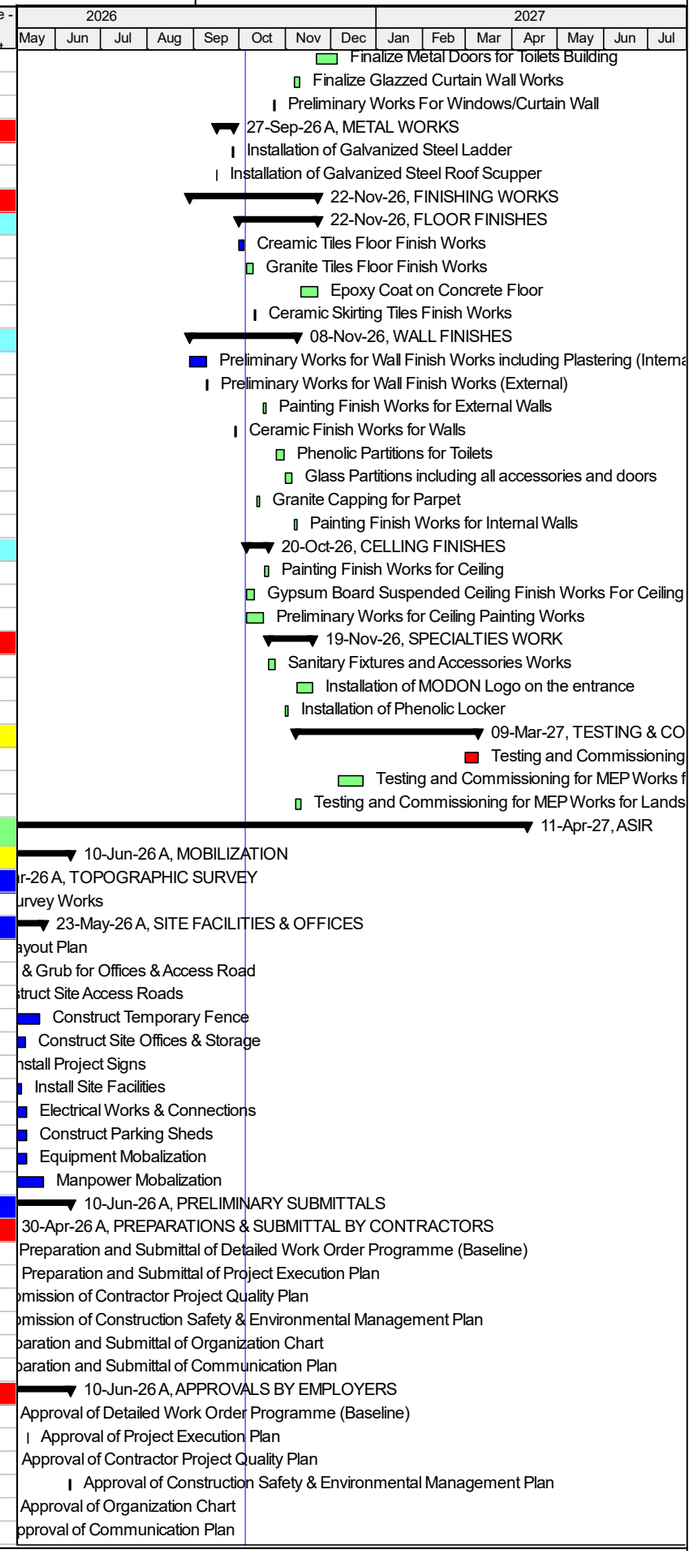

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
ENGINEERING		209	0%	0%	31-Mar-26	02-Sep-26	31-Mar-26 A	03-Dec-26	0.00	0.00	0.00	-78
SHOP DRAWINGS		141	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26 A	26-Aug-26 A	0.00	0.00	0.00	-34
SHOP DRAWINGS SUBMISSION		141	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		58	0%	0%	31-Mar-26	09-Jun-26	31-Mar-26 A	09-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Layout Plan	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Setting Out	44	100%	100%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Grading Layout Plan	25	100%	100%	31-Mar-26	28-Apr-26	31-Mar-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Curb Setting Out Points	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Signing & Marking Layout Plan	1	100%	100%	09-Jun-26	09-Jun-26	09-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Submittal for Standards Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		141	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
ARCHITECTURE WORKS		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Floor Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Elevations	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Ceiling Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Finishes Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Toilet Details	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Doors/Windows Schedule	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		20	0%	0%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Foundation Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Ground Floor Framing Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections/Details	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		38	0%	0%	08-Apr-26	21-May-26	08-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for HVAC Plan	7	100%	100%	08-Apr-26	15-Apr-26	08-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Exhaust Air Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for HVAC Equipment Schedule	7	100%	100%	08-Apr-26	15-Apr-26	08-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Drainage Layout	38	100%	100%	08-Apr-26	21-May-26	08-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Drainage Details	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Dut Routing Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Diffusers Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Fighting Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Water Supply Layout	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Water Supply Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		134	0%	0%	08-Apr-26	18-Jul-26	08-Apr-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
MLTX-02-004-EN	Shop DWG Submittal for Lighting Layout	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Layout	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Single Line Diagram	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Panel Board Schedules	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Installation Details	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Installation Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Cable Tray Installation Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Manhole & Ductbank Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Grounding Details	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Installation Details	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Layout	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lightning Protection Details	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lightning Protection System Layout	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Details	6	100%	100%	05-Jul-26	11-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-004-EN	Shop DWG Submittal for CCTV Layout	6	100%	100%	05-Jul-26	11-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-004-EN	Shop DWG Submittal for Telephone & Data Layout	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Grounding Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Riser Diagram	6	100%	100%	12-Jul-26	18-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
MLTX-02-004-EN	Shop DWG Submittal for Telephone & Data Riser Diagram	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		141	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
ARCHITECTURE WORKS		39	0%	0%	31-Mar-26	14-May-26	31-Mar-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Playground Plan/Layout	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Furniture & Marking	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Interlock Pattern Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Doors/Windows Schedule	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Dome Internal Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0

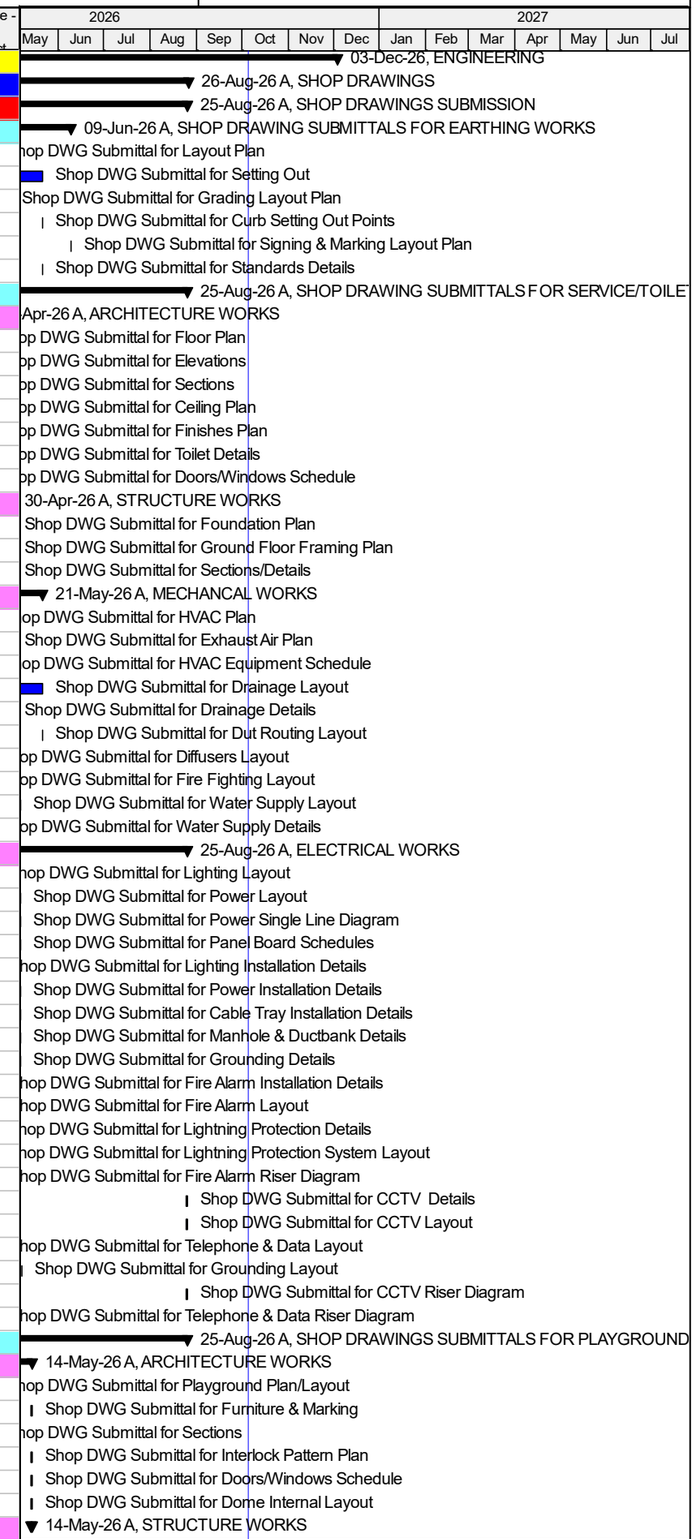

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Shop DWG Submittal for Air Dome System	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Foundation of Air Dome	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
AIR DOME SYSTEM		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Air Dome Structural Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Membrane Panel Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Cable Tension Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Airlock Door Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Emergency Exit Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
SPORTS EQUIPMENT		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Football Turf Installation	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Basketball Court Marking	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Padel Court Structure	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		20	0%	0%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for HVAC Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Exhaust Air Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		96	0%	0%	23-May-26	18-Jul-26	23-May-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
MLTX-02-004-EN	Shop DWG Submittal for Lighting Layout	1	100%	100%	25-May-26	25-May-26	25-May-26 A	25-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Layout	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Installation Details	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Single Line Diagram	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Panel Board Schedules	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Details	6	100%	100%	05-Jul-26	11-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-004-EN	Shop DWG Submittal for CCTV Layout	6	100%	100%	05-Jul-26	11-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-004-EN	Shop DWG Submittal for CCTV Riser Diagram	6	100%	100%	12-Jul-26	18-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-33
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		65	0%	0%	31-Mar-26	17-Jun-26	31-Mar-26 A	17-Jun-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		39	0%	0%	31-Mar-26	14-May-26	31-Mar-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Landscape Layout	6	100%	100%	31-Mar-26	06-Apr-26	31-Mar-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Hardscape Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Planting Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Landscape Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		1	0%	0%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Irrigation Details	1	100%	100%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Irrigation Layout	1	100%	100%	17-Jun-26	17-Jun-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		1	0%	0%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting General Arrangement	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Network Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS APPROVALS		129	0%	0%	07-Apr-26	11-Jul-26	07-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-40
SHOP DRAWING APPROVAL FOR EARTHING WORKS		52	0%	0%	07-Apr-26	09-Jun-26	07-Apr-26 A	09-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-2	Shop DWG Approval for Layout Plan	6	100%	100%	18-Apr-26	23-Apr-26	18-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-2	Shop DWG Approval for Setting Out	0	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-2	Shop DWG Approval for Grading Layout Plan	20	100%	100%	07-Apr-26	29-Apr-26	07-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-2	Shop DWG Approval for Curb Setting Out Points	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-2	Shop DWG Approval for Signing & Marking Layout Plan	1	100%	100%	09-Jun-26	09-Jun-26	09-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-2	Shop DWG Approval for Standards Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		111	0%	0%	14-Apr-26	11-Jul-26	14-Apr-26 A	12-Aug-26 A	0.00	0.00	0.00	-28
ARCHITECTURE WORKS		9	0%	0%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Floor Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Elevations	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Ceiling Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Finishes Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Toilet Details	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Doors/Windows Schedule	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Foundation Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Ground Floor Framing Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections/Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		13	0%	0%	07-May-26	21-May-26	07-May-26 A	21-May-26 A	0.00	0.00	0.00	0

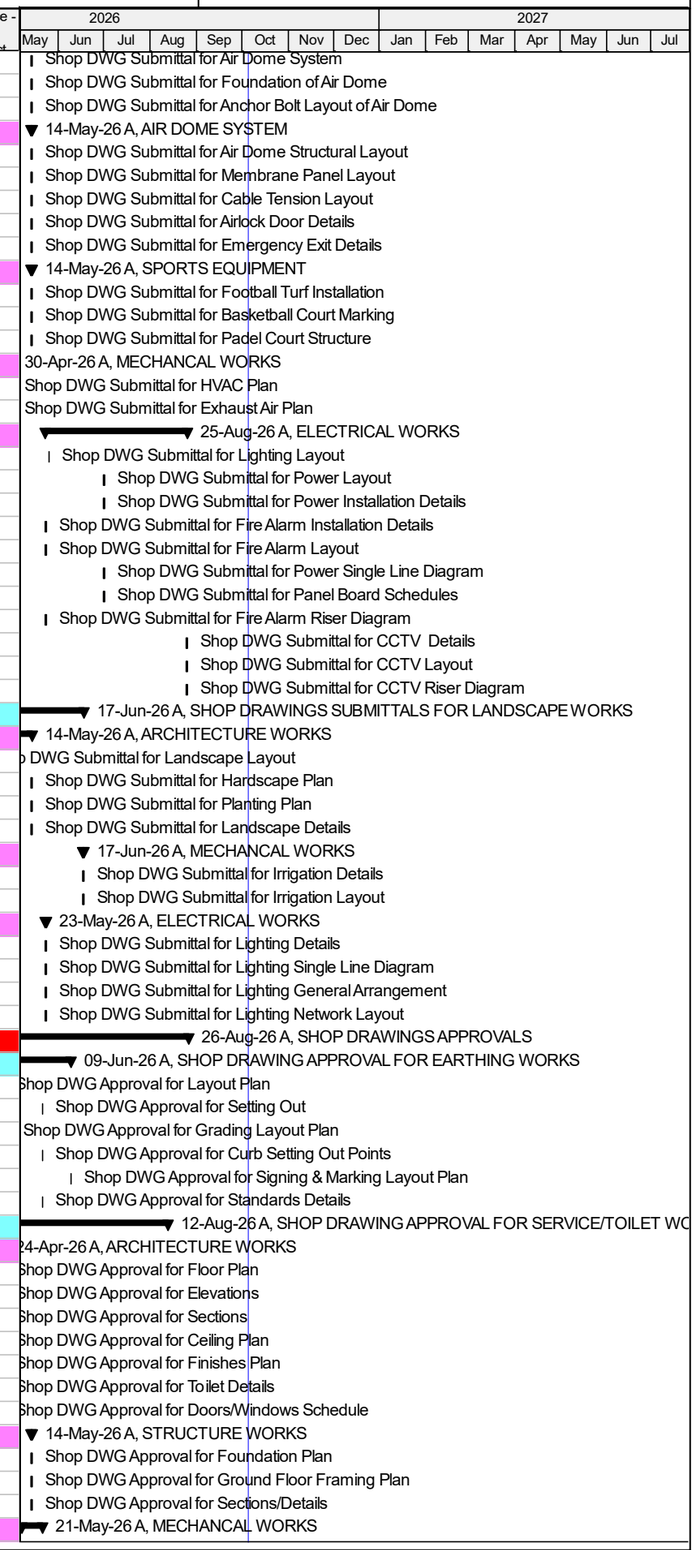

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Shop DWG Approval for HVAC Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Exhaust Air Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for HVAC Equipment Schedule	4	100%	100%	07-May-26	11-May-26	07-May-26 A	11-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Drainage Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Drainage Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Duct Routing Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Diffusers Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Fighting Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Water Supply Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Water Supply Details	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		110	0%	0%	15-Apr-26	11-Jul-26	15-Apr-26 A	12-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-004-EM	Shop DWG Approval for Lighting Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Panel Board Schedules	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lighting Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Cable Tray Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Manhole & Ductbank Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Grounding Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Alarm Installation Details	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Alarm Layout	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lightning Protection Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Lightning Protection System Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Fire Alarm Riser Diagram	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for CCTV Details	6	100%	100%	05-Jul-26	11-Jul-26	12-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-004-EM	Shop DWG Approval for CCTV Layout	6	100%	100%	05-Jul-26	11-Jul-26	12-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-004-EM	Shop DWG Approval for Telephone & Data Layout	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Grounding Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for CCTV Riser Diagram	6	100%	100%	05-Jul-26	11-Jul-26	12-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-004-EM	Shop DWG Approval for Telephone & Data Riser Diagram	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		122	0%	0%	15-Apr-26	11-Jul-26	15-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-40
ARCHITECTURE WORKS		45	0%	0%	19-Apr-26	13-Jun-26	19-Apr-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Playground Plan/Layout	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Furniture & Marking	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Sections	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Interlock Pattern Plan	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Doors/Windows Schedule	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Dome Internal Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		1	0%	0%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Air Dome System	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Foundation of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Foundation of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Anchor Bolt Layout of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
AIR DOME SYSTEM		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Air Dome Structural Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Membrane Panel Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Cable Tension Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Airlock Door Details	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Emergency Exit Details	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SPORTS EQUIPMENT		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Football Turf Installation	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Basketball Court Marking	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Padel Court Structure	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		1	0%	0%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for HVAC Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Exhaust Air Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		122	0%	0%	15-Apr-26	11-Jul-26	15-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EM	Shop DWG Approval for Lighting Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Power Single Line Diagram	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for Panel Board Schedules	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Shop DWG Approval for CCTV Details	6	100%	100%	05-Jul-26	11-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-40

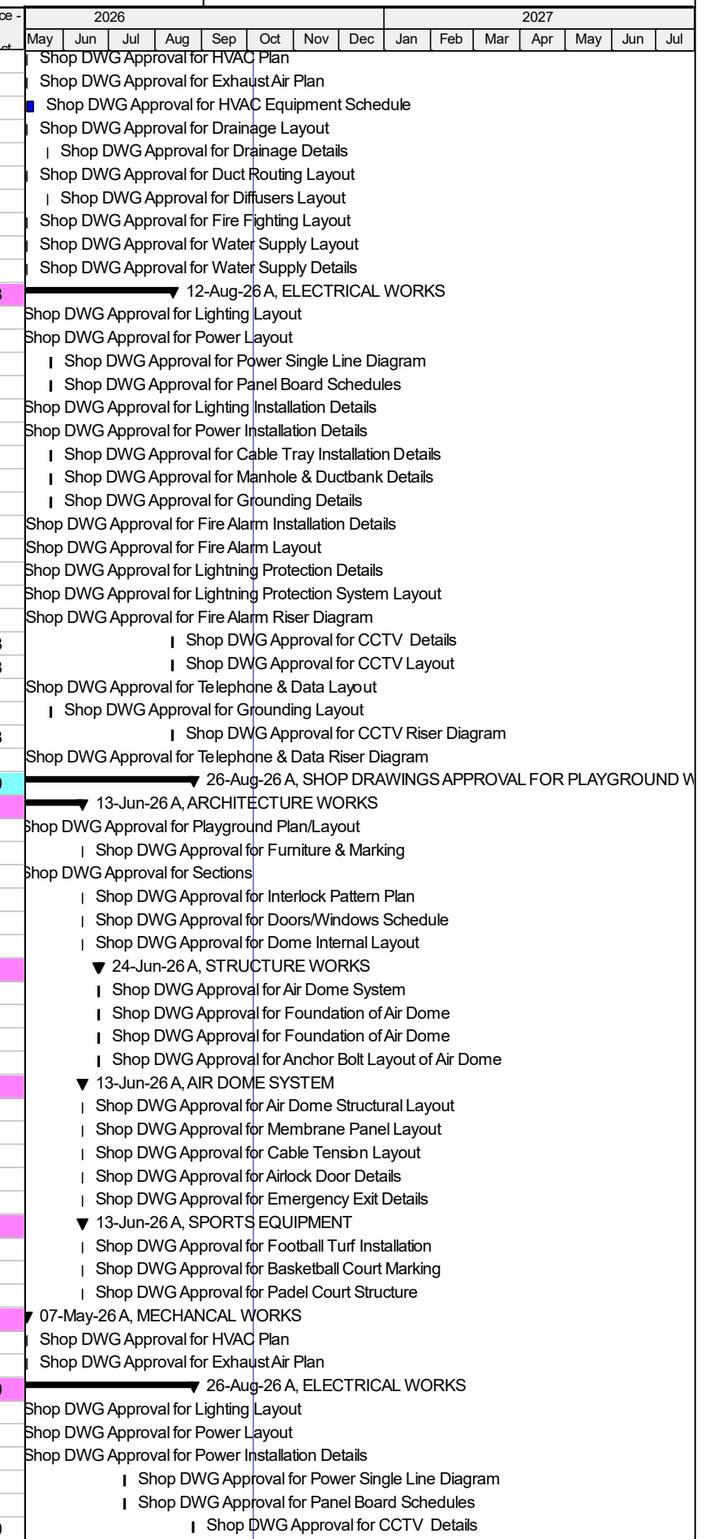

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Shop DWG Approval for CCTV Layout	6	100%	100%	05-Jul-26	11-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Approval for CCTV Riser Diagram	6	100%	100%	05-Jul-26	11-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-40
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		62	0%	0%	11-Apr-26	24-Jun-26	11-Apr-26 A	24-Jun-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		23	0%	0%	19-Apr-26	14-May-26	19-Apr-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Landscape Layout	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Hardscape Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Planting Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Landscape Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		1	0%	0%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Irrigation Details	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Irrigation Layout	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		37	0%	0%	11-Apr-26	23-May-26	11-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Details	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting General Arrangement	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Network Layout	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
METHOD STATEMENTS		174	0%	0%	31-Mar-26	03-Aug-26	31-Mar-26 A	24-Oct-26	0.00	0.00	0.00	-69
METHOD STATEMENT SUBMITTAL		164	0%	0%	31-Mar-26	19-Jul-26	31-Mar-26 A	12-Oct-26	0.00	0.00	0.00	-72
CIVIL WORKS		45	0%	0%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	17	100%	100%	31-Mar-26	19-Apr-26	31-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Concrete	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	22	100%	100%	31-Mar-26	25-Apr-26	31-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		115	0%	0%	31-May-26	11-Jul-26	31-May-26 A	12-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Plastering	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Tilling	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Parking	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Soft	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Parking	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Soft	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Fence	6	100%	0%	05-Jul-26	11-Jul-26	06-Oct-26	12-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Air Dome	6	100%	100%	05-Jul-26	11-Jul-26	17-Aug-26 A	17-Aug-26 A	0.00	0.00	0.00	-32
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Metal	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Partitions	6	100%	100%	05-Jul-26	11-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Gypsum	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MECHANICAL WORKS		48	0%	0%	07-Apr-26	04-Jun-26	07-Apr-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Water	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Fire	7	100%	100%	07-Apr-26	14-Apr-26	07-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Irrigation	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for HVAC	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		58	0%	0%	18-Jun-26	19-Jul-26	18-Jun-26 A	11-Aug-26 A	0.00	0.00	0.00	-20
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	7	100%	100%	12-Jul-26	19-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for CCTV	7	100%	100%	12-Jul-26	19-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-3
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Lighting	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Panel	6	100%	100%	05-Jul-26	11-Jul-26	11-Aug-26 A	11-Aug-26 A	0.00	0.00	0.00	-27
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Electrical	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Preparation & Submission of Method Statement for Lighting	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
METHOD STATEMENT APPROVAL		161	0%	0%	15-Apr-26	03-Aug-26	15-Apr-26 A	24-Oct-26	0.00	0.00	0.00	-69
CIVIL WORKS		1	0%	0%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Earthwork	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Concrete Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Waterproofing	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		125	0%	0%	31-May-26	22-Jul-26	31-May-26 A	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-4	Approval of Method Statement for Plastering Works	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Masonary Works	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Tilling Works	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Seats/Benches Works	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Doors/Windows Works	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Interlock/Curbstone Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Parking Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Soft Scape Works	10	100%	100%	12-Jul-26	22-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	10

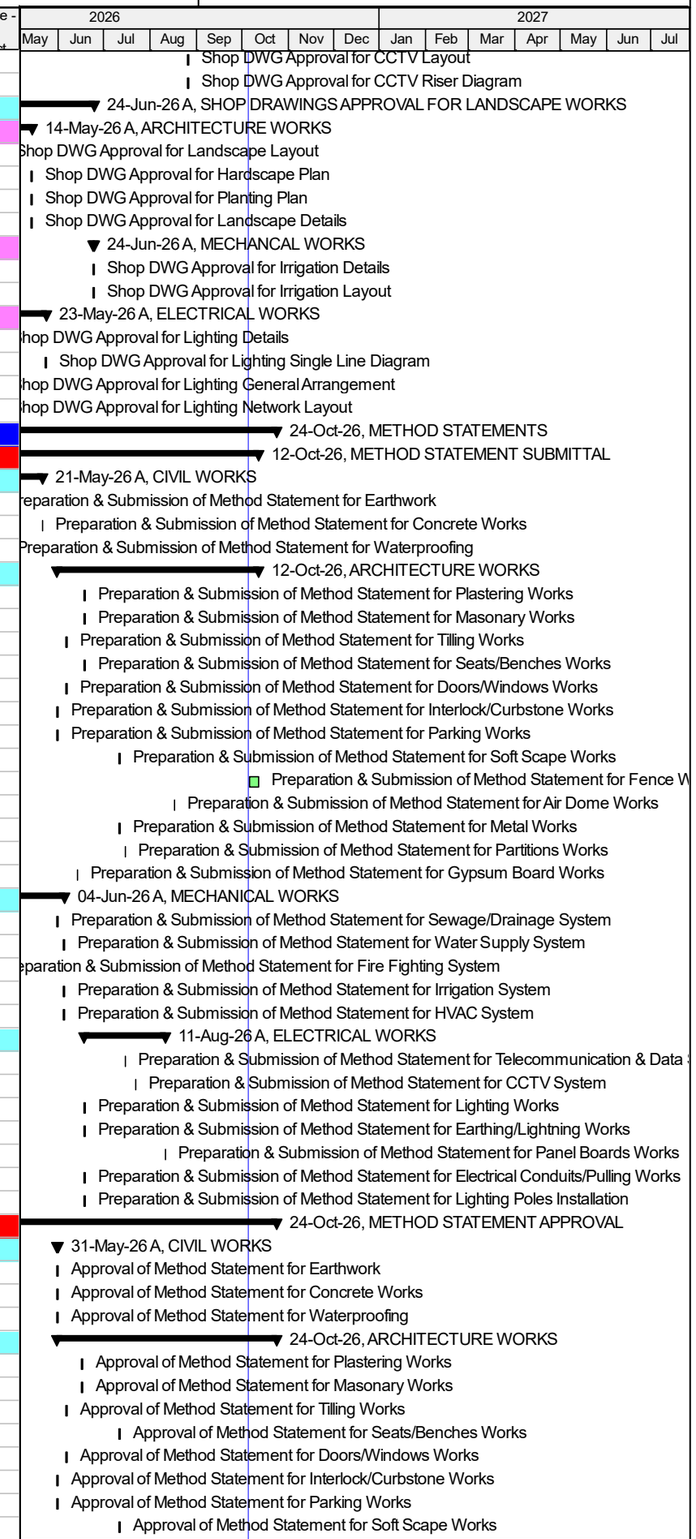


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN-4	Approval of Method Statement for Fence Works	10	100%	0%	12-Jul-26	22-Jul-26	13-Oct-26	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-4	Approval of Method Statement for Air Dome Works	10	100%	100%	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN-4	Approval of Method Statement for Partitions Works	10	100%	100%	12-Jul-26	22-Jul-26	27-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN-4	Approval of Method Statement for Gypsum Board Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MECHANICAL WORKS		47	0%	0%	15-Apr-26	11-Jun-26	15-Apr-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Sewage/Drainage System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Water Supply System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Fire Fighting System	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Irrigation System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for HVAC System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		70	0%	0%	16-Jun-26	03-Aug-26	16-Jun-26 A	12-Aug-26 A	0.00	0.00	0.00	-8
MLTX-02-004-EN-4	Approval of Method Statement for Electrical Conduits/Pulling	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-4	Approval of Method Statement for Lighting Poles Installation	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-4	Approval of Method Statement for Telecommunication & Data	10	100%	100%	23-Jul-26	03-Aug-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	16
MLTX-02-004-EN-4	Approval of Method Statement for CCTV System	10	100%	100%	23-Jul-26	03-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	10
MLTX-02-004-EN-4	Approval of Method Statement for Lighting Works	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-4	Approval of Method Statement for Earthing/Lightning Works	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-4	Approval of Method Statement for Panel Boards Works	10	100%	100%	12-Jul-26	22-Jul-26	12-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	-18
PRE-QUALIFICATION & MATERIAL		209	0%	0%	31-Mar-26	02-Sep-26	31-Mar-26 A	03-Dec-26	0.00	0.00	0.00	-78
PRE-QUALIFICATION		45	0%	0%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
TOILET/SERVICE WORKS		21	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26 A	23-Apr-26 A	0.00	0.00	0.00	0
STEEL REINFORCEMENT		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Steel Reinforcement	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Steel Reinforcement	2	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
READY MIX CONCRETE		21	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Ready Mixed Concrete	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Ready Mixed Concrete	11	100%	100%	12-Apr-26	23-Apr-26	12-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		21	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Concrete Blocks	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	07-Apr-26	23-Apr-26	07-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
WATER PROOFING		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Water Proofing	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Water Proofing	3	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
FLOOR/WALL TILES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Tilling Materials	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Tailling Material	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SUSPENDED CEILING		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Suspend Ceiling	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Suspend Ceiling	2	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
DOORS/WINDOWS		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Doors/Windows	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Doors/Windows	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
FURNITURES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Furnitures	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Furnitures	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Sanitary Fixtures	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Sanitary Fixtures	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
WATER SUPPLY PIPES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Water Supply Pipes	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Water Supply Pipes	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Package AC Units	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Package AC Units	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Air Diffusers/Grills	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Air Diffusers/Grills	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Galvanized Ducts	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Galvanized Ducts	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0

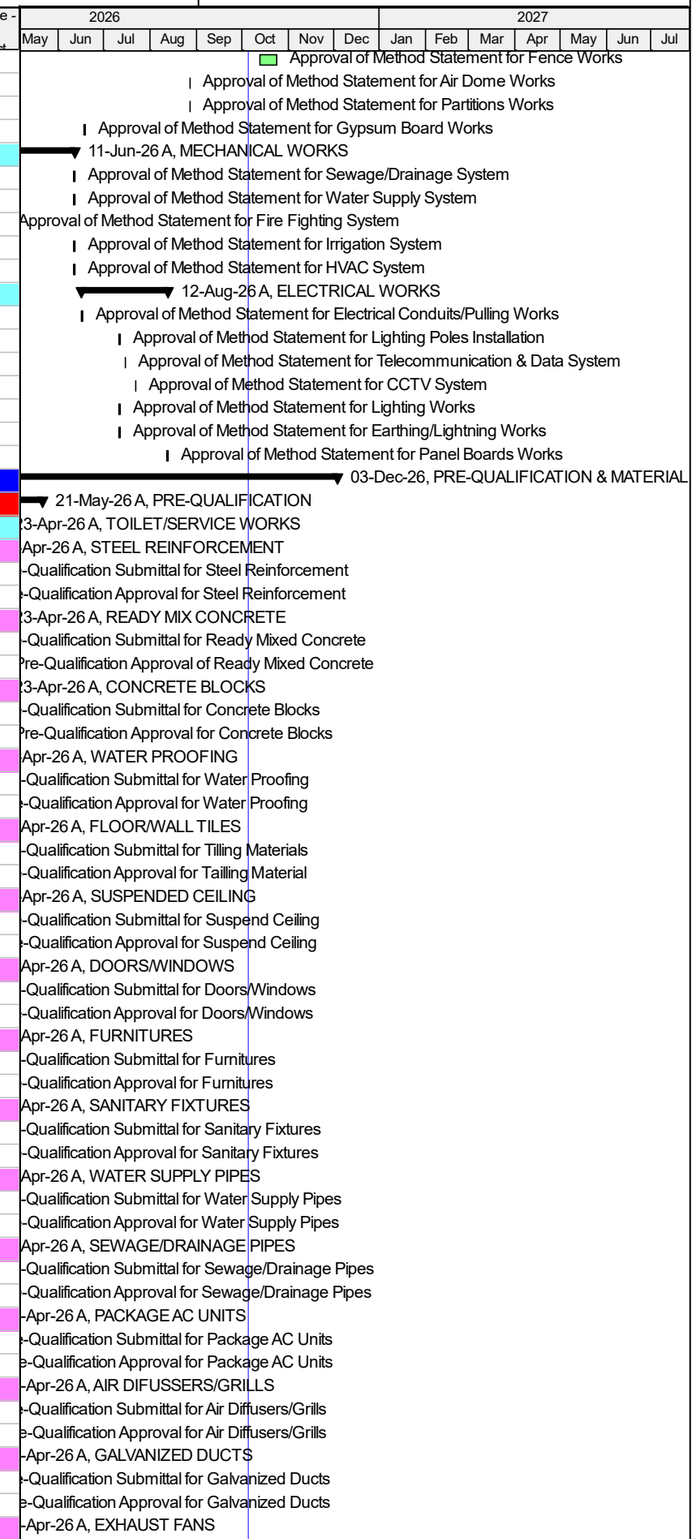

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Pre-Qualification Submittal for Exhaust Fans	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Exhaust Fans	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LIGHTING FIXTURES		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lighting Fixtures	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lighting Fixtures	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
SWITCHES/SOCKETS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Switches/Sockets	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Switches/Sockets	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EARTHING SYSTEM		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Earthing System	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Earthing System	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Distribution Panels	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Distribution Panels	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PLAYGROUND WORKS		21	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26 A	23-Apr-26 A	0.00	0.00	0.00	0
PVC MEMBRANE		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for PVC Membrane	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for PVC Membrane	4	100%	100%	12-Apr-26	15-Apr-26	12-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
STEEL TENSION CABLES		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Steel Tension Cables	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Steel Tension Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EMERGENCY DOORS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Emergency Doors	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Emergency Doors	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PRESSURE UNITS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Pressure Units	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Pressure Units	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR LOCK DOORS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lock Doors	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lock Doors	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
ARTIFICIAL TURF		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Artificial TURF	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Artificial TURF	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Rubber Granules	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Rubber Granules	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PADEL GLASS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Padel Glass	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Padel Glass	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Wire Mesh/Steel Sets	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Wire Mesh/Steel Sets	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AGGREGATE BASE COURSE		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Aggregate Base Course	14	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Aggregate Base Course	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	07-Apr-26	14-Apr-26	07-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Bituminous Base & Wearing	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for the Site	3	100%	100%	12-Apr-26	14-Apr-26	12-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		15	0%	0%	07-Apr-26	23-Apr-26	07-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Interlocking Block Pavers	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Interlocking Block Pavers	11	100%	100%	12-Apr-26	23-Apr-26	12-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MARKING PAINT		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Marking Paint	8	100%	100%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Marking Paint	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Package AC Units	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Package AC Units	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Air Difussers/Grills	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Air Difussers/Grills	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Galvanized Duct	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Galvanized Duct	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Pre-Qualification Submittal for Exhaust Fans	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Exhaust Fans	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
DISTRIBUTION BOARDS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Distribution Boards	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Distribution Boards	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
POWER CABLES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Power Cables	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Power Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LIGHT FIXTURES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Light Fixtures	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Light Fixtures	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
CCTV MATERIALS		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for CCTV	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for CCTV	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
POWER OUTLETS/SWITCHES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Power Outlets/Switches	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Power Outlets/Switches	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LANDSCAPE WORKS		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		18	0%	0%	04-Apr-26	23-Apr-26	04-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Interlocking Block Pavers	8	100%	100%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Interlocking Block Pavers	11	100%	100%	12-Apr-26	23-Apr-26	12-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
CURBSTONE		18	0%	0%	04-Apr-26	23-Apr-26	04-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Curbstone	8	100%	100%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Curbstone	11	100%	100%	12-Apr-26	23-Apr-26	12-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	0
PAVEMENT MARKING		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Pavement Markings	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Pavement Markings	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
TRAFFIC SIGNS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Traffic Signs	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Traffic Signs	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
IRRIGATION PIPES/SPRINKLERS		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	20	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AGRICULTURE SOIL		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Agriculture Soil	20	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Agriculture Soil	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
TRACK SURFACE		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Track Surface	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Track Surface	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
GRASS/TREES		14	0%	0%	04-Apr-26	19-Apr-26	04-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Grass/Trees	10	100%	100%	04-Apr-26	14-Apr-26	04-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Grass/Trees	5	100%	100%	14-Apr-26	19-Apr-26	14-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
CABLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Cables	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Cables	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LIGHT POLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lighting poles	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lighting poles	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MATERIAL SUBMITTAL & APPROVAL		200	0%	0%	11-Apr-26	02-Sep-26	11-Apr-26 A	03-Dec-26	0.00	0.00	0.00	-78
TOILET/SERVICE WORKS		92	0%	0%	11-Apr-26	12-Jul-26	11-Apr-26 A	22-Jul-26 A	0.00	0.00	0.00	-9
STEEL REINFORCEMENT		4	0%	0%	11-Apr-26	14-Apr-26	11-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Steel Reinforcement	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Steel Reinforcement	3	100%	100%	12-Apr-26	14-Apr-26	12-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
READY MIX CONCRETE		10	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Ready Mixed Concrete	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval of Ready Mixed Concrete	7	100%	100%	19-Apr-26	26-Apr-26	19-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		10	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Concrete Blocks	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Concrete Blocks	7	100%	100%	19-Apr-26	26-Apr-26	19-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
FLOOR/WALL TILES		88	0%	0%	15-Apr-26	12-Jul-26	15-Apr-26 A	22-Jul-26 A	0.00	0.00	0.00	-9
MLTX-02-004-EN	Material Submittal for Tilling Materials	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Tilling Material	7	100%	100%	05-Jul-26	12-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-9
SUSPENDED CEILING		5	0%	0%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Suspend Ceiling	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0

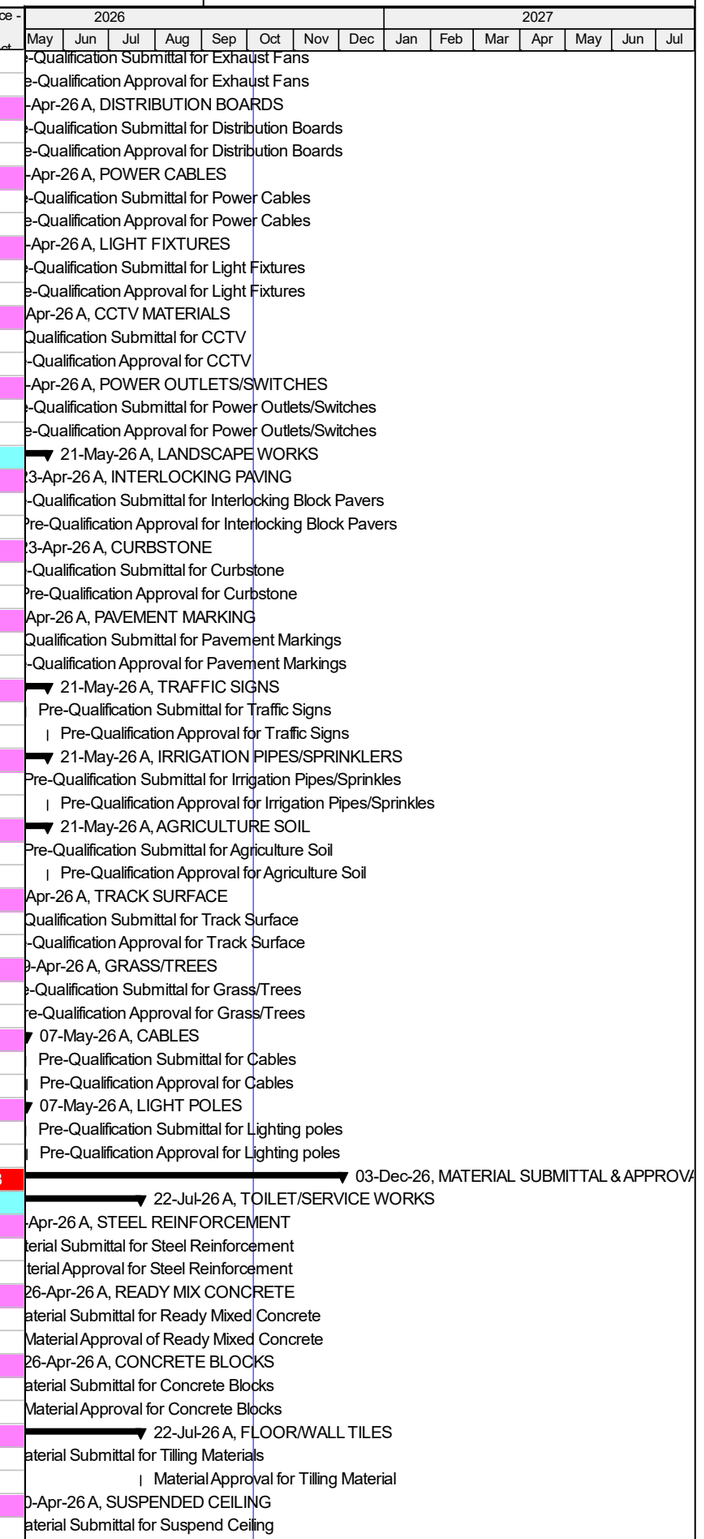

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Material Approval for Suspend Ceiling	2	100%	100%	19-Apr-26	20-Apr-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
DOORS/WINDOWS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Doors/Windows	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Doors/Windows	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
FURNITURES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Furnitures	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Furnitures	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		14	0%	0%	15-Apr-26	30-Apr-26	15-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Sanitary Fixtures	6	100%	100%	15-Apr-26	21-Apr-26	15-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Sanitary Fixtures	11	100%	100%	19-Apr-26	30-Apr-26	19-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
WATER SUPPLY PIPES		2	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Water Supply Pipes	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Water Supply Pipes	2	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		2	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Sewage/Drainage Pipes	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Sewage/Drainage Pipes	2	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Package AC Units	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Package AC Units	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		18	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Air Diffusers/Grills	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Air Diffusers/Grills	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		6	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Galvanized Ducts	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Galvanized Ducts	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
EXHAUST FANS		18	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Exhaust Fans	2	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Exhaust Fans	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
LIGHTING FIXTURES		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Lighting Fixtures	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Lighting Fixtures	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
SWITCHES/SOCKETS		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Switches/Sockets	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Switches/Sockets	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
EARTHING SYSTEM		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Earthing System	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Earthing System	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Distribution Panels	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Distribution Panels	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
PLAYGROUND WORKS		199	0%	0%	12-Apr-26	02-Sep-26	12-Apr-26 A	03-Dec-26	0.00	0.00	0.00	-78
PVC MEMBRANE		153	0%	0%	15-Apr-26	13-Jul-26	15-Apr-26 A	14-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for PVC Membrane	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for PVC Membrane	8	100%	0%	05-Jul-26	13-Jul-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-79
STEEL TENSION CABLES		144	0%	0%	06-May-26	23-Jul-26	06-May-26 A	25-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Steel Tension Cables	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Steel Tension Cables	9	100%	0%	14-Jul-26	23-Jul-26	15-Oct-26	25-Oct-26	0.00	0.00	0.00	-79
EMERGENCY DOORS		153	0%	0%	06-May-26	03-Aug-26	06-May-26 A	04-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Emergency Doors	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Emergency Doors	9	100%	0%	25-Jul-26	03-Aug-26	26-Oct-26	04-Nov-26	0.00	0.00	0.00	-79
PRESSURE UNITS		162	0%	0%	06-May-26	13-Aug-26	06-May-26 A	15-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Pressure Units	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Pressure Units	9	100%	0%	04-Aug-26	13-Aug-26	05-Nov-26	15-Nov-26	0.00	0.00	0.00	-79
AIR LOCK DOORS		170	0%	0%	06-May-26	24-Aug-26	06-May-26 A	24-Nov-26	0.00	0.00	0.00	-78
MLTX-02-004-EM	Material Submittal for Lock Doors	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Lock Doors	8	100%	0%	16-Aug-26	24-Aug-26	16-Nov-26	24-Nov-26	0.00	0.00	0.00	-78
ARTIFICIAL TURF		17	0%	0%	12-Apr-26	30-Apr-26	12-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Artificial TURF	15	100%	100%	12-Apr-26	28-Apr-26	12-Apr-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Artificial TURF	3	100%	100%	28-Apr-26	30-Apr-26	28-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Rubber Granules	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Rubber Granules	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
PADEL GLASS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Padel Glass	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0

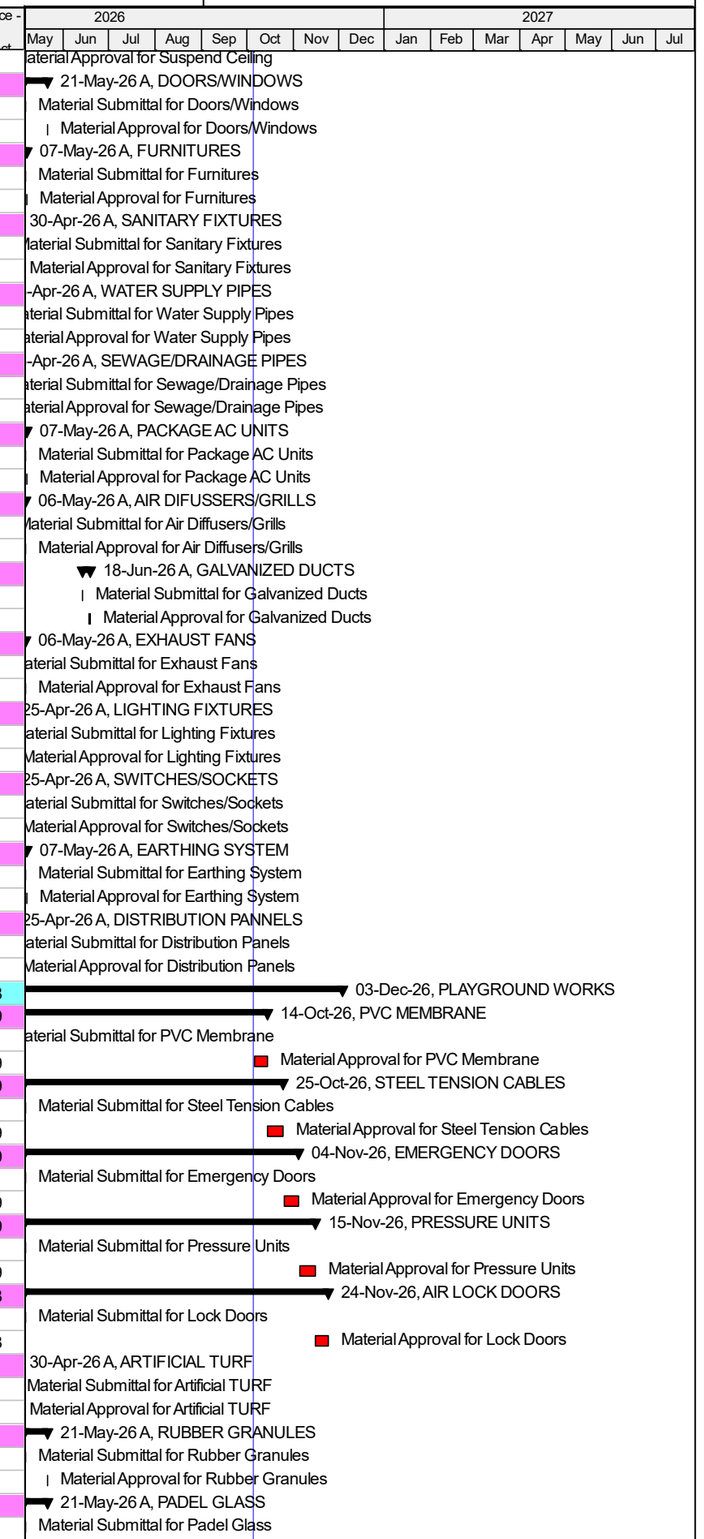

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Material Approval for Padel Glass	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		162	0%	0%	25-May-26	02-Sep-26	25-May-26 A	03-Dec-26	0.00	0.00	0.00	-78
MLTX-02-004-EM	Material Submittal for Wire Mesh/Steel Sets	1	100%	100%	25-May-26	25-May-26	25-May-26 A	25-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Wire Mesh/Steel Sets	8	100%	0%	25-Aug-26	02-Sep-26	25-Nov-26	03-Dec-26	0.00	0.00	0.00	-78
AGGREGATE BASE COURSE		22	0%	0%	21-May-26	18-Jun-26	21-May-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Aggregate Base Course	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		2	0%	0%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Bituminous Base & Wearing Cource	2	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for the Site	1	100%	100%	18-Apr-26	18-Apr-26	18-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MARKING PAINT		6	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Marking Paint	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Marking Paint	2	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Package AC Units	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Package AC Units	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Air Difussers/Grills	9	100%	100%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Air Difussers/Grills	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		6	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Galvanized Duct	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Galvanized Duct	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
EXHAUST FANS		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Exhaust Fans	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Exhaust Fans	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION BOARDS		11	0%	0%	13-Apr-26	25-Apr-26	13-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Distribution Boards	6	100%	100%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Distribution Boards	6	100%	100%	19-Apr-26	25-Apr-26	19-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
POWER CABLES		7	0%	0%	13-Apr-26	20-Apr-26	13-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Power Cables	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Power Cables	4	100%	100%	16-Apr-26	20-Apr-26	16-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
LIGHT FIXTURES		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Light Fixtures	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Light Fixtures	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
CCTV MATERIALS		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for CCTV	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for CCTV	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
POWER OUTLETS/SWITCHES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Power Outlets/Switches	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Power Outlets/Switches	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LANDSCAPE WORKS		93	0%	0%	13-Apr-26	11-Jul-26	13-Apr-26 A	27-Jul-26 A	0.00	0.00	0.00	-14
INTERLOCKING PAVING		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Interlocking Block Pavers	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Interlocking Block Pavers	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
CURBSTONE		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Curbstone	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Curbstone	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
PAVEMENT MARKING		6	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Pavement Markings	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Pavement Markings	2	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
TRAFFIC SIGNS		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Traffic Signs	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Traffic Signs	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
IRRIGATION PIPES/SPRINKLERS		93	0%	0%	13-Apr-26	11-Jul-26	13-Apr-26 A	27-Jul-26 A	0.00	0.00	0.00	-14
MLTX-02-004-EM	Material Submittal for Irrigation Pipes/Sprinkles	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Irrigation Pipes/Sprinkles	6	100%	100%	05-Jul-26	11-Jul-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-14
AGRICULTURE SOIL		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Agriculture Soil	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Agriculture Soil	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
TRACK SURFACE		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Track Surface	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0

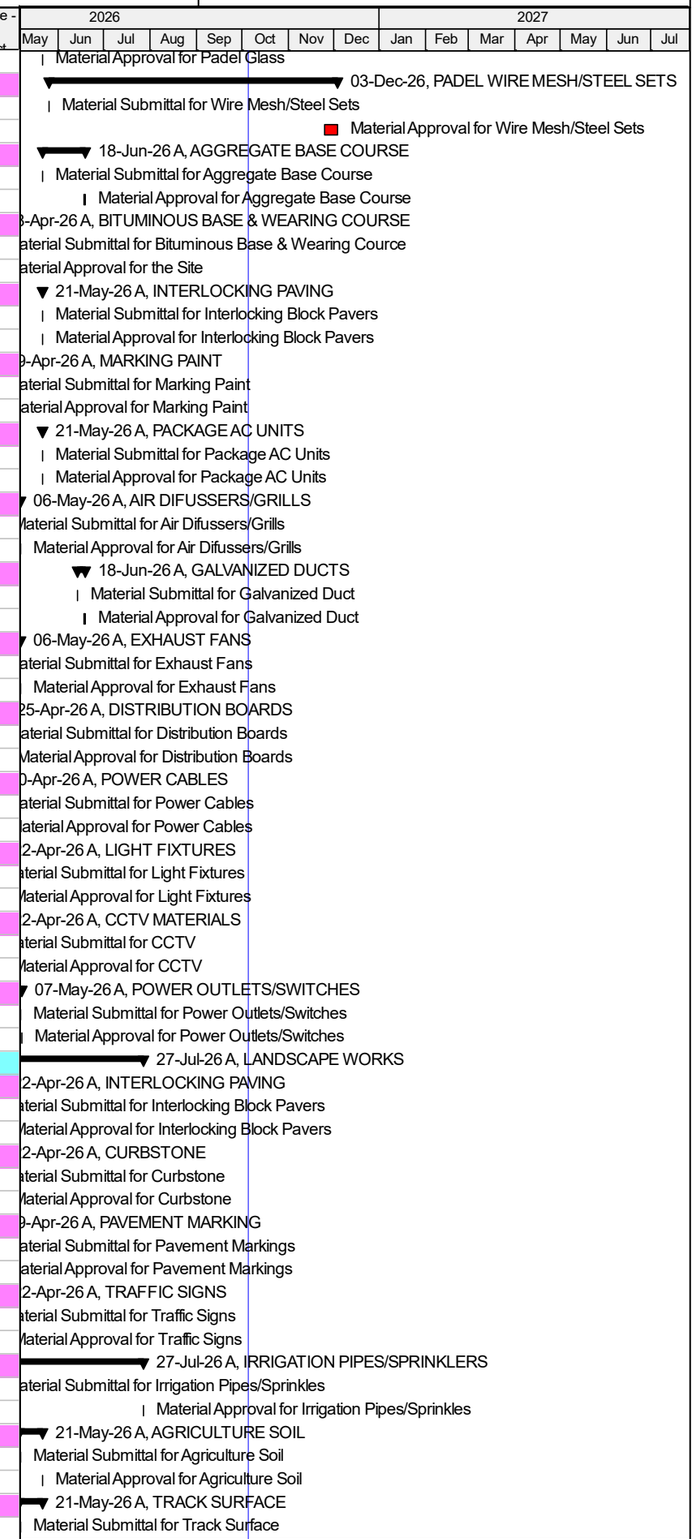

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Material Approval for Track Surface	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
GRASS/TREES		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Grass/Trees	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Grass/Trees	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
CABLES		7	0%	0%	13-Apr-26	20-Apr-26	13-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Cables	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Cables	4	100%	100%	16-Apr-26	20-Apr-26	16-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
LIGHT POLES		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Lighting poles	7	100%	100%	13-Apr-26	20-Apr-26	13-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Lighting poles	18	100%	100%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
PROCUREMENT		251	0%	0%	07-May-26	07-Dec-26	07-May-26 A	17-Jan-27	0.00	0.00	0.00	-35
SHORT LEAD ITEM		211	0%	0%	07-May-26	12-Oct-26	07-May-26 A	12-Jan-27	0.00	0.00	0.00	-79
TOILET/SERVICE WORKS		146	0%	0%	07-May-26	08-Aug-26	07-May-26 A	28-Oct-26	0.00	0.00	0.00	-69
STEEL REINFORCEMENT		24	0%	0%	13-May-26	13-Jun-26	13-May-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-7	PO for Steel Reinforcement	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-7	Material Delivery of Steel Reinforcement	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		70	0%	0%	07-May-26	08-Jul-26	07-May-26 A	27-Jul-26 A	0.00	0.00	0.00	-16
MLTX-02-004-PR-7	PO for Concrete Blocks	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-7	Material Delivery of Concrete Blocks	4	100%	100%	05-Jul-26	08-Jul-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-16
FLOOR/WALL TILES		71	0%	0%	13-Jul-26	02-Aug-26	22-Jul-26 A	12-Sep-26 A	0.00	0.00	0.00	-35
MLTX-02-004-PR-8	PO for Tilling Materials	5	100%	100%	13-Jul-26	18-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-PR-8	Material Delivery of Tailling Material	13	100%	100%	19-Jul-26	02-Aug-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-35
SUSPENDED CEILING		77	0%	0%	19-Jul-26	08-Aug-26	22-Jul-26 A	20-Oct-26	0.00	0.00	0.00	-62
MLTX-02-004-PR-8	PO for Suspend Ceiling	5	100%	100%	19-Jul-26	23-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-004-PR-8	Material Delivery of Suspend Ceiling	13	100%	0%	25-Jul-26	08-Aug-26	06-Oct-26	20-Oct-26	0.00	0.00	0.00	-62
DOORS/WINDOWS		103	0%	0%	24-Jun-26	21-Jul-26	24-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Doors/Windows	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Doors/Windows	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
WATER SUPPLY PIPES		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	PO for Water Supply Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Water Supply Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	PO for Sewage/Drainage Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Sewage/Drainage Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		108	0%	0%	16-Jun-26	19-Jul-26	16-Jun-26 A	20-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Sanitary Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Sanitary Fixtures	13	100%	0%	05-Jul-26	19-Jul-26	06-Oct-26	20-Oct-26	0.00	0.00	0.00	-79
PACKAGE AC UNITS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Package AC Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Package AC Units	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
AIR DIFUSSERS/GRILLS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Air Diffusers/Grills	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Air Diffusers/Grills	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Galvanized Ducts	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Galvanized Ducts	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		105	0%	0%	16-Jun-26	15-Jul-26	16-Jun-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Exhaust Fans	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Exhaust Fans	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
LIGHTING FIXTURES		105	0%	0%	16-Jun-26	15-Jul-26	16-Jun-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Lighting Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Lighting Fixtures	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
SWITCHES/SOCKETS		95	0%	0%	24-Jun-26	12-Jul-26	24-Jun-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Switches/Sockets	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Switches/Sockets	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
EARTHING SYSTEM		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	PO for Earthing System	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Earthing System	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		79	0%	0%	05-Jul-26	27-Jul-26	22-Jul-26 A	22-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-8	PO for Distribution Panels	5	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-11
MLTX-02-004-PR-8	Material Delivery for Distribution Panels	15	100%	0%	11-Jul-26	27-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-74
FURNITURES		115	0%	0%	16-Jun-26	27-Jul-26	16-Jun-26 A	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Furnitures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Furnitures	20	100%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79

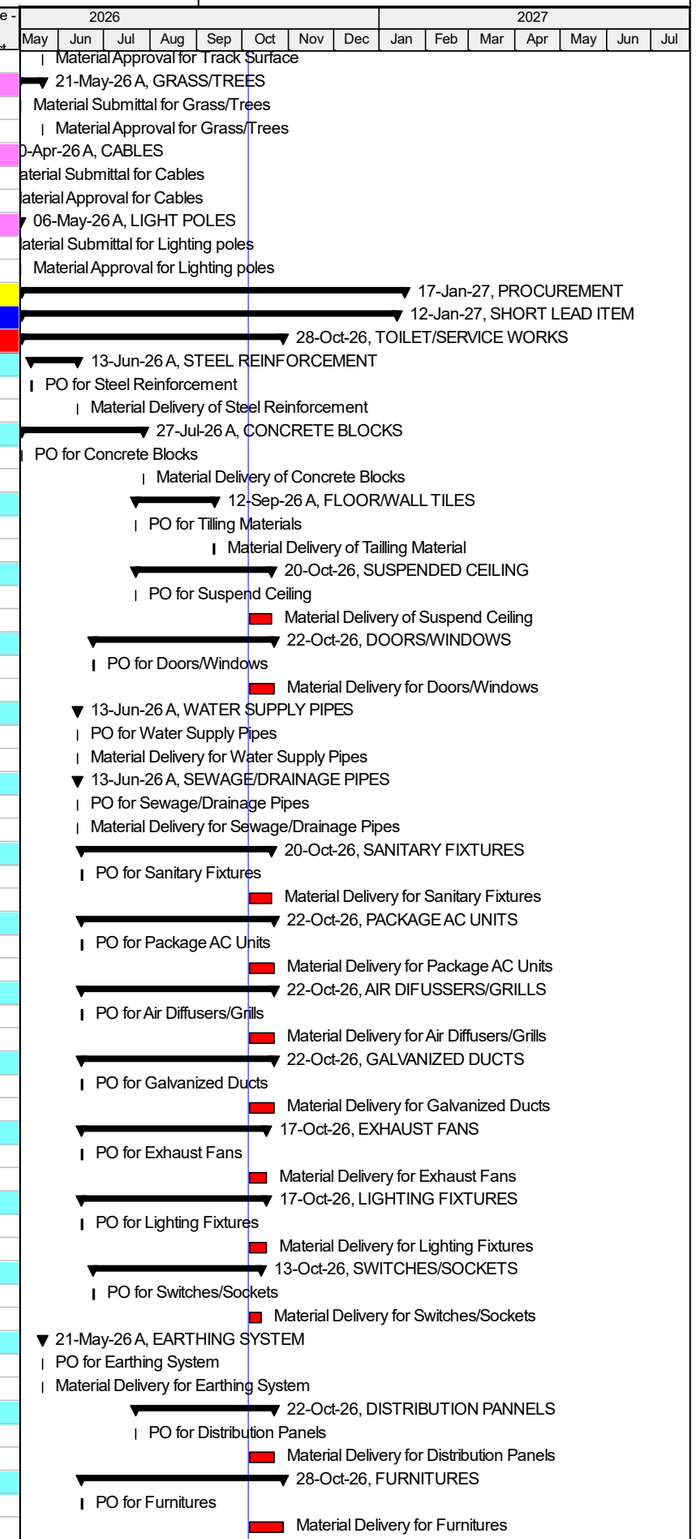

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PLAYGROUND WORKS		172	0%	0%	07-May-26	01-Sep-26	07-May-26 A	28-Nov-26	0.00	0.00	0.00	-74
PVC MEMBRANE		99	0%	0%	16-Jun-26	08-Jul-26	16-Jun-26 A	10-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for PVC Membrane	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for PVC Membrane	4	100%	0%	05-Jul-26	08-Jul-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-79
ARTIFICIAL TURF		111	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26 A	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Artificial TURF	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Artificial TURF	12	100%	0%	09-Jul-26	22-Jul-26	11-Oct-26	24-Oct-26	0.00	0.00	0.00	-79
RUBBER GRANULES		43	0%	0%	16-Jun-26	18-Jul-26	16-Jun-26 A	22-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-PR-8	PO for Rubber Granules	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Rubber Granules	12	100%	100%	05-Jul-26	18-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-4
PADEL GLASS		113	0%	0%	16-Jun-26	25-Jul-26	16-Jun-26 A	26-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Padel Glass	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Padel Glass	18	100%	0%	05-Jul-26	25-Jul-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-79
PADEL WIRE MESH/STEEL SETS		111	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26 A	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Wire Mesh/Steel Sets	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Wire Mesh/Steel Sets	16	100%	0%	05-Jul-26	22-Jul-26	06-Oct-26	24-Oct-26	0.00	0.00	0.00	-79
AGGREGATE BASE COURSE		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	PO for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		1	0%	0%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	PO for Bituminous Base & Wearing Course	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for the Site	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		133	0%	0%	07-May-26	12-Jul-26	07-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Interlocking Block Pavers	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Interlocking Block Pavers	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
MARKING PAINT		75	0%	0%	05-Jul-26	18-Jul-26	18-Jul-26 A	13-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-8	PO for Marking Paint	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-PR-8	Material Delivery for Marking Paint	7	100%	0%	11-Jul-26	18-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-74
PACKAGE AC UNITS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Package AC Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Package AC Units	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
AIR DIFUSSERS/GRILLS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Air Difussers/Grills	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Air Difussers/Grills	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Galvanized Duct	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Galvanized Duct	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		110	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Exhaust Fans	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Exhaust Fans	15	100%	0%	05-Jul-26	21-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
DISTRIBUTION BOARDS		79	0%	0%	23-Jul-26	15-Aug-26	22-Jul-26 A	10-Nov-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-8	PO for Distribution Boards	5	100%	100%	23-Jul-26	28-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	6
MLTX-02-004-PR-8	Material Delivery for Distribution Boards	15	100%	0%	29-Jul-26	15-Aug-26	25-Oct-26	10-Nov-26	0.00	0.00	0.00	-74
POWER CABLES		74	0%	0%	29-Jul-26	15-Aug-26	22-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-53
MLTX-02-004-PR-8	PO for Power Cables	5	100%	100%	29-Jul-26	03-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	10
MLTX-02-004-PR-8	Material Delivery for Power Cables	10	100%	0%	04-Aug-26	15-Aug-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-53
LIGHT FIXTURES		111	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26 A	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Light Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Light Fixtures	16	100%	0%	05-Jul-26	22-Jul-26	06-Oct-26	24-Oct-26	0.00	0.00	0.00	-79
CCTV MATERIALS		46	0%	0%	12-Jul-26	01-Sep-26	06-Oct-26	28-Nov-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-8	PO for CCTV	5	100%	0%	12-Jul-26	16-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-8	Material Delivery for CCTV	15	100%	0%	16-Aug-26	01-Sep-26	11-Nov-26	28-Nov-26	0.00	0.00	0.00	-74
POWER OUTLETS/SWITCHES		79	0%	0%	22-Jul-26	15-Aug-26	22-Jul-26 A	09-Nov-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-8	PO for Power Outlets/Switches	6	100%	100%	22-Jul-26	28-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	5
MLTX-02-004-PR-8	Material Delivery for Power Outlets/Switches	15	100%	0%	29-Jul-26	15-Aug-26	24-Oct-26	09-Nov-26	0.00	0.00	0.00	-73
LANDSCAPE WORKS		211	0%	0%	07-May-26	12-Oct-26	07-May-26 A	12-Jan-27	0.00	0.00	0.00	-79
INTERLOCKING PAVING		184	0%	0%	07-May-26	15-Sep-26	07-May-26 A	12-Dec-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-8	PO for Interlocking Block Pavers	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Interlocking Block Pavers	12	100%	0%	02-Sep-26	15-Sep-26	29-Nov-26	12-Dec-26	0.00	0.00	0.00	-74
CURBSTONE		113	0%	0%	07-May-26	05-Aug-26	07-May-26 A	12-Aug-26 A	0.00	0.00	0.00	-6
MLTX-02-004-PR-8	PO for Curbstone	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Delivery for Curbstone	12	100%	100%	23-Jul-26	05-Aug-26	12-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	-6
PAVEMENT MARKING		46	0%	0%	06-Aug-26	23-Aug-26	22-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-46
MLTX-02-004-PR-8	PO for Pavement Markings	5	100%	100%	06-Aug-26	11-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	17

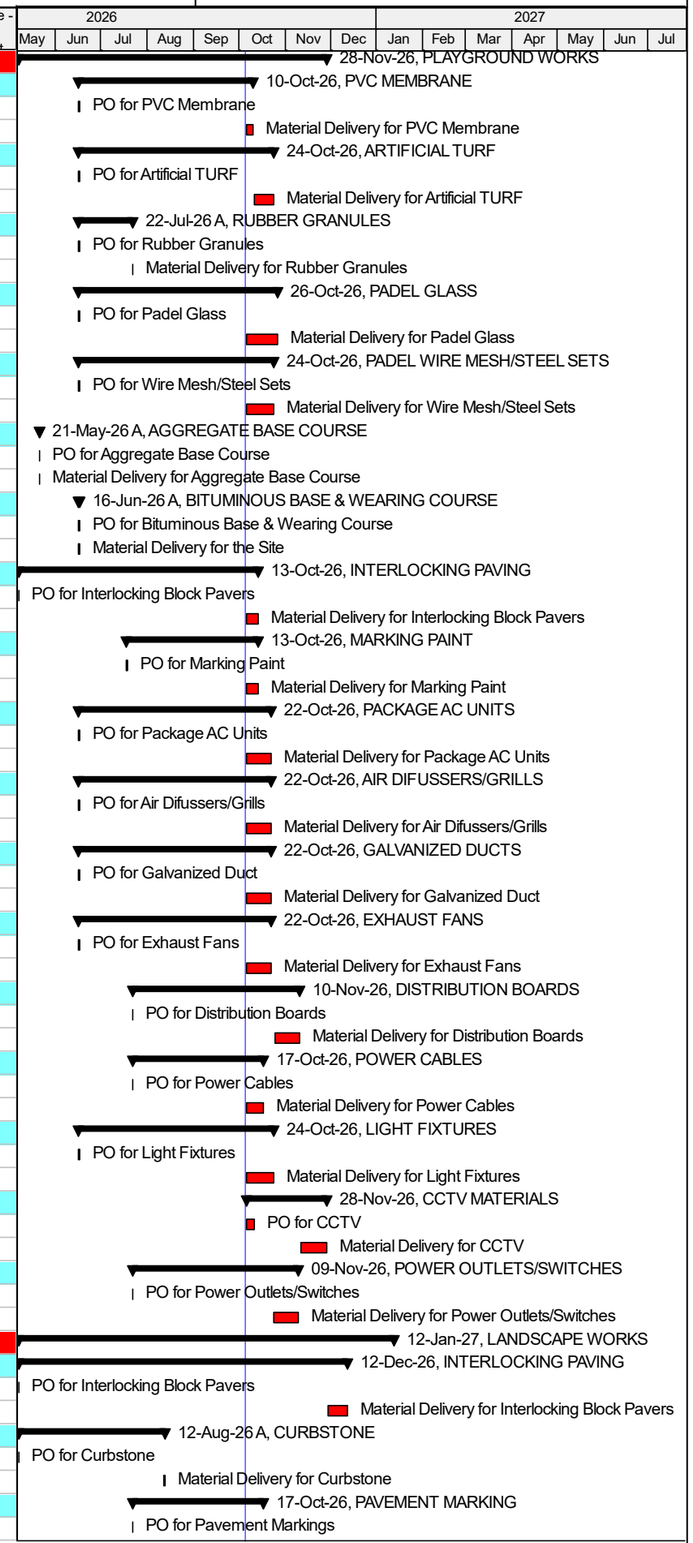

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-PR-9	Material Delivery for Pavement Markings	10	100%	0%	12-Aug-26	23-Aug-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-46
TRAFFIC SIGNS		14	0%	0%	16-Sep-26	03-Oct-26	19-Dec-26	03-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	PO for Traffic Signs	5	100%	0%	16-Sep-26	21-Sep-26	19-Dec-26	23-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Material Delivery for Traffic Signs	9	100%	0%	22-Sep-26	03-Oct-26	24-Dec-26	03-Jan-27	0.00	0.00	0.00	-79
IRRIGATION PIPES/SPRINKLERS		63	0%	0%	12-Aug-26	26-Aug-26	18-Jul-26 A	07-Nov-26	0.00	0.00	0.00	-61
MLTX-02-004-PR-9	PO for Irrigation Pipes/Sprinkles	5	100%	100%	12-Aug-26	17-Aug-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	26
MLTX-02-004-PR-9	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	0%	18-Aug-26	26-Aug-26	29-Oct-26	07-Nov-26	0.00	0.00	0.00	-61
AGRICULTURE SOIL		17	0%	0%	22-Sep-26	12-Oct-26	24-Dec-26	12-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	PO for Agriculture Soil	5	100%	0%	22-Sep-26	28-Sep-26	24-Dec-26	29-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Material Delivery for Agriculture Soil	12	50%	0%	29-Sep-26	12-Oct-26	30-Dec-26	12-Jan-27	0.00	0.00	0.00	-79
TRACK SURFACE		15	0%	0%	05-Sep-26	21-Sep-26	07-Dec-26	23-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	PO for Track Surface	5	100%	0%	05-Sep-26	09-Sep-26	07-Dec-26	12-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Material Delivery for Track Surface	10	100%	0%	10-Sep-26	21-Sep-26	13-Dec-26	23-Dec-26	0.00	0.00	0.00	-79
GRASS/TREES		20	0%	0%	10-Sep-26	04-Oct-26	13-Dec-26	04-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	PO for Grass/Trees	5	100%	0%	10-Sep-26	15-Sep-26	13-Dec-26	17-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Material Delivery for Grass/Trees	15	100%	0%	16-Sep-26	04-Oct-26	19-Dec-26	04-Jan-27	0.00	0.00	0.00	-79
CABLES		20	0%	0%	12-Aug-26	03-Sep-26	28-Sep-26 A	28-Sep-26 A	0.00	0.00	0.00	-20
MLTX-02-004-PR-9	PO for Cables	5	100%	100%	12-Aug-26	17-Aug-26	28-Sep-26 A	28-Sep-26 A	0.00	0.00	0.00	-35
MLTX-02-004-PR-9	Material Delivery for Cables	15	100%	100%	18-Aug-26	03-Sep-26	28-Sep-26 A	28-Sep-26 A	0.00	0.00	0.00	-20
LONG LEAD ITEM		220	0%	0%	16-Jun-26	07-Dec-26	16-Jun-26 A	17-Jan-27	0.00	0.00	0.00	-35
PLAYGROUND WORKS		184	0%	0%	16-Jun-26	17-Oct-26	16-Jun-26 A	17-Jan-27	0.00	0.00	0.00	-79
STEEL TENSION CABLES		184	0%	0%	16-Jun-26	17-Oct-26	16-Jun-26 A	17-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Steel Tension Cables	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Fabrication for Steel Tension Cables	20	100%	0%	29-Jul-26	20-Aug-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-58
MLTX-02-004-PR-8	Material Delivery for Steel Tension Cables	29	89.66%	0%	05-Sep-26	08-Oct-26	07-Dec-26	09-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Staging time	7	0%	0%	10-Oct-26	17-Oct-26	10-Jan-27	17-Jan-27	0.00	0.00	0.00	-79
EMERGENCY DOORS		148	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26 A	06-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Emergency Doors	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Fabrication for Emergency Doors	20	100%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	Material Delivery for Emergency Doors	25	100%	0%	28-Jul-26	25-Aug-26	29-Oct-26	26-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Staging time	8	100%	0%	26-Aug-26	03-Sep-26	28-Nov-26	06-Dec-26	0.00	0.00	0.00	-79
PRESSURE UNITS		148	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26 A	06-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Pressure Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Fabrication for Pressure Units	20	100%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	Material Delivery for Pressure Units	25	100%	0%	28-Jul-26	25-Aug-26	29-Oct-26	26-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Staging time	8	100%	0%	26-Aug-26	03-Sep-26	28-Nov-26	06-Dec-26	0.00	0.00	0.00	-79
AIR LOCK DOORS		148	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26 A	06-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	PO for Lock Doors	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-8	Material Fabrication for Lock Doors	20	100%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-8	Material Delivery for Lock Doors	25	100%	0%	28-Jul-26	25-Aug-26	29-Oct-26	26-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Staging time	8	100%	0%	26-Aug-26	03-Sep-26	28-Nov-26	06-Dec-26	0.00	0.00	0.00	-79
LANDSCAPE WORKS		218	0%	0%	18-Jun-26	07-Dec-26	18-Jun-26 A	29-Sep-26 A	0.00	0.00	0.00	59
LIGHT POLES		218	0%	0%	18-Jun-26	07-Dec-26	18-Jun-26 A	29-Sep-26 A	0.00	0.00	0.00	59
MLTX-02-004-PR-9	PO for Lighting poles	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-9	Material Fabrication for Lighting poles	30	53.33%	100%	16-Sep-26	21-Oct-26	29-Sep-26 A	29-Sep-26 A	0.00	0.00	0.00	19
MLTX-02-004-PR-9	Material Delivery for Lighting poles	25	0%	100%	22-Oct-26	19-Nov-26	29-Sep-26 A	29-Sep-26 A	0.00	0.00	0.00	44
MLTX-02-004-PR-9	Staging time	15	0%	100%	21-Nov-26	07-Dec-26	29-Sep-26 A	29-Sep-26 A	0.00	0.00	0.00	59
CONSTRUCTION PHASE		292	21.55%	33.27%	27-Apr-26	24-Jan-27	27-Apr-26 A	11-Apr-27	2,279,478.29	3,519,653.97	10,578,073.08	-62
SITE WORKS		292	15.16%	33.06%	27-Apr-26	24-Jan-27	27-Apr-26 A	11-Apr-27	1,416,801.21	3,090,247.75	9,346,371.54	-62
EARTH WORKS		89	100%	100%	27-Apr-26	09-Aug-26	27-Apr-26 A	12-Aug-26 A	487,645.71	487,645.71	487,645.71	-3
MLTX-02-004-CN-993	Excavation (in all types of soil) including Compaction	13	100%	100%	27-Apr-26	11-May-26	27-Apr-26 A	11-May-26 A	101,400.00	101,400.00	101,400.00	0
MLTX-02-004-CN-994	Excavation (in all types of soil) including Compaction	8	100%	100%	06-May-26	16-May-26	06-May-26 A	16-May-26 A	32,321.25	32,321.25	32,321.25	0
MLTX-02-004-CN-995	Excavation (in all types of soil) including Compaction	17	100%	100%	29-Apr-26	19-May-26	29-Apr-26 A	19-May-26 A	209,327.63	209,327.63	209,327.63	0
MLTX-02-004-CN-996	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	17-May-26	13-Jun-26	17-May-26 A	13-Jun-26 A	61,425.00	61,425.00	61,425.00	0
MLTX-02-004-CN-997	Backfilling on Layers (Selected Soil) including Compaction	18	100%	100%	17-May-26	09-Jun-26	17-May-26 A	09-Jun-26 A	17,062.50	17,062.50	17,062.50	0
MLTX-02-004-CN-998	Backfilling on Layers (Selected Soil) including Compaction	23	100%	100%	08-Jun-26	04-Jul-26	08-Jun-26 A	04-Jul-26 A	29,859.38	29,859.38	29,859.38	0
MLTX-02-004-CN-998	Backfilling on Layers (Selected Soil) including Compaction	30	100%	100%	05-Jul-26	09-Aug-26	04-Jul-26 A	12-Aug-26 A	36,249.96	36,249.96	36,249.96	-3
LANDSCAPE WORKS		270	10.49%	29.38%	23-May-26	24-Jan-27	23-May-26 A	11-Apr-27	929,155.50	2,602,602.04	8,858,725.83	-62
PLAYGROUND AREA		253	22.51%	46.41%	23-May-26	04-Jan-27	23-May-26 A	22-Mar-27	256,405.50	528,742.50	1,139,255.00	-62
FOOTBALL PLAYGROUND		234	20%	20%	23-May-26	13-Dec-26	23-May-26 A	24-Feb-27	57,525.00	57,525.00	287,625.00	-62
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Football Playground)	1	100%	100%	23-May-26	24-May-26	23-May-26 A	24-May-26 A	28,762.50	28,762.50	28,762.50	0
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Football	32	100%	100%	24-May-26	04-Jul-26	24-May-26 A	04-Jul-26 A	24,448.13	24,448.13	24,448.13	0
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Football	30	100%	100%	05-Jul-26	08-Aug-26	20-Jul-26 A	31-Aug-26 A	4,314.38	4,314.38	4,314.38	-20
MLTX-02-004-CI	Finishing and Surface Finish Works (Football Playground)	30	0%	0%	29-Oct-26	02-Dec-26	25-Oct-26	28-Nov-26	0.00	0.00	143,812.50	4

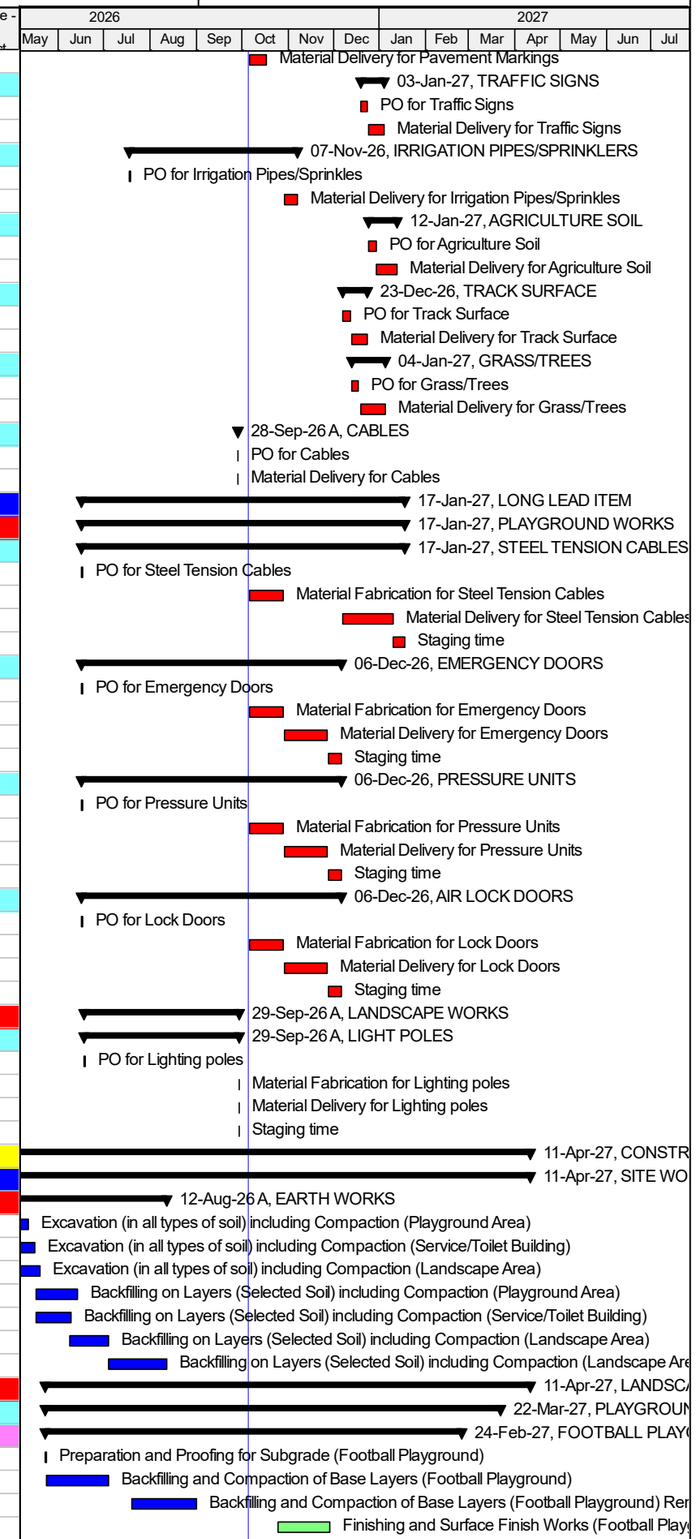

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	9	0%	0%	03-Dec-26	13-Dec-26	14-Feb-27	24-Feb-27	0.00	0.00	71,906.25	-62
MLTX-02-004-CI	Surface Marking and Painting (Football Playground)	8	0%	0%	03-Dec-26	12-Dec-26	14-Feb-27	23-Feb-27	0.00	0.00	14,381.25	-62
PADEL PLAYGROUND		235	55%	80%	23-May-26	14-Dec-26	23-May-26 A	25-Feb-27	117,975.00	171,600.00	214,500.00	-62
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Padel Playground)	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	75,075.00	75,075.00	75,075.00	0
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Padel	32	100%	100%	24-May-26	04-Jul-26	24-May-26 A	04-Jul-26 A	37,537.50	37,537.50	37,537.50	0
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Padel	30	100%	100%	09-Aug-26	12-Sep-26	20-Jul-26 A	09-Aug-26 A	5,362.50	5,362.50	5,362.50	30
MLTX-02-004-CI	Finishing and Surface Finish Works (Padel Playground)	30	0%	100%	29-Oct-26	02-Dec-26	15-Sep-26 A	16-Sep-26 A	0.00	53,625.00	53,625.00	66
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	10	0%	0%	03-Dec-26	14-Dec-26	14-Feb-27	25-Feb-27	0.00	0.00	32,175.00	-62
MLTX-02-004-CI	Surface Marking and Painting (Padel Playground)	8	0%	0%	03-Dec-26	12-Dec-26	14-Feb-27	23-Feb-27	0.00	0.00	10,725.00	-62
BASKETBALL PLAYGROUND		251	19.54%	69.98%	23-May-26	20-Dec-26	23-May-26 A	20-Mar-27	60,918.00	218,205.00	311,805.00	-73
MLTX-02-004-CI	Backfilling and Compaction Subgrade (Basketball	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	31,200.00	31,200.00	31,200.00	0
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Basketball	32	100%	100%	24-May-26	04-Jul-26	24-May-26 A	04-Jul-26 A	27,495.00	27,495.00	27,495.00	0
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Basketball	30	63.33%	100%	13-Sep-26	18-Oct-26	20-Jul-26 A	09-Aug-26 A	2,223.00	3,510.00	3,510.00	60
MLTX-02-004-CI	Finishing and Surface Finish Works (Basketball Playground)	30	0%	100%	29-Oct-26	02-Dec-26	15-Sep-26 A	16-Sep-26 A	0.00	156,000.00	156,000.00	65
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	03-Dec-26	20-Dec-26	14-Feb-27	03-Mar-27	0.00	0.00	78,000.00	-62
MLTX-02-004-CI	Surface Marking and Painting (Basketball Playground)	7	0%	0%	13-Dec-26	20-Dec-26	09-Mar-27	20-Mar-27	0.00	0.00	15,600.00	-73
PADEL FENCE		174	0%	30%	21-Dec-26	04-Jan-27	16-Aug-26 A	22-Mar-27	0.00	24,862.50	82,875.00	-62
MLTX-02-004-CI	Excavation for Fence	5	0%	100%	21-Dec-26	26-Dec-26	16-Aug-26 A	16-Aug-26 A	0.00	8,287.50	8,287.50	112
MLTX-02-004-CI	Concrete Foundation for Fence including Posts Fixation	5	0%	100%	21-Dec-26	26-Dec-26	25-Aug-26 A	01-Sep-26 A	0.00	16,575.00	16,575.00	98
MLTX-02-004-CI	Backfilling and Reinstatement for Concrete Foundation	4	0%	0%	27-Dec-26	30-Dec-26	04-Mar-27	08-Mar-27	0.00	0.00	4,143.75	-57
MLTX-02-004-CI	Tempered Glass Fenc Installation and Fixation	2	0%	0%	31-Dec-26	02-Jan-27	09-Mar-27	14-Mar-27	0.00	0.00	33,150.00	-57
MLTX-02-004-CI	Chain Link Fence Installation and Fixation	2	0%	0%	03-Jan-27	04-Jan-27	21-Mar-27	22-Mar-27	0.00	0.00	16,575.00	-62
MLTX-02-004-CI	Install of Fence Gates	2	0%	0%	03-Jan-27	04-Jan-27	21-Mar-27	22-Mar-27	0.00	0.00	4,143.75	-62
CURBSTOEN/INTERLOCK		100	8.24%	23.32%	23-Aug-26	22-Oct-26	10-Aug-26 A	23-Dec-26	19,987.50	56,550.00	242,450.00	-53
MLTX-02-004-CI	Interlock Installation (Grey Scale) for LandScape (Including	10	0%	0%	12-Oct-26	22-Oct-26	13-Dec-26	23-Dec-26	0.00	0.00	185,900.00	-53
MLTX-02-004-CI	Concrete Works Under Curbstone	15	100%	100%	23-Aug-26	08-Sep-26	10-Aug-26 A	10-Aug-26 A	19,987.50	19,987.50	19,987.50	26
MLTX-02-004-CI	Curbstone Installation	4	0%	100%	07-Oct-26	11-Oct-26	11-Aug-26 A	16-Aug-26 A	0.00	36,562.50	36,562.50	47
AIR DOME		232	12%	20.5%	16-Jun-26	31-Dec-26	16-Jun-26 A	18-Mar-27	672,750.00	1,149,281.25	5,606,250.00	-62
CIVIL WORKS		200	28.57%	48.81%	16-Jun-26	24-Nov-26	16-Jun-26 A	04-Feb-27	672,750.00	1,149,281.25	2,354,625.00	-62
MLTX-02-004-CI	Excavation for Foundation & Playground Area (Air Dome)	12	100%	100%	16-Jun-26	29-Jun-26	16-Jun-26 A	29-Jun-26 A	280,312.50	280,312.50	280,312.50	0
MLTX-02-004-CI	Concrete Works for Foundations including Anchor Bolts (Air	26	100%	100%	23-Jul-26	22-Aug-26	11-Jul-26 A	22-Sep-26 A	392,437.50	392,437.50	392,437.50	-26
MLTX-02-004-CI	Cable System Installation (Air Dome)	10	0%	85%	18-Oct-26	28-Oct-26	24-Sep-26 A	17-Oct-26	0.00	476,531.25	560,625.00	10
MLTX-02-004-CI	Install of Membrane Covering System (Air Dome)	14	0%	0%	09-Nov-26	24-Nov-26	20-Jan-27	04-Feb-27	0.00	0.00	560,625.00	-62
MLTX-02-004-CI	Thermal Insulation Works (Air Dome)	14	0%	0%	09-Nov-26	24-Nov-26	20-Jan-27	04-Feb-27	0.00	0.00	560,625.00	-62
MECHANICAL WORKS		13	0%	0%	25-Nov-26	09-Dec-26	06-Feb-27	20-Feb-27	0.00	0.00	1,121,250.00	-62
MLTX-02-004-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	25-Nov-26	06-Dec-26	06-Feb-27	16-Feb-27	0.00	0.00	280,312.50	-62
MLTX-02-004-CI	Air Units Installation (Air Dome)	13	0%	0%	25-Nov-26	09-Dec-26	06-Feb-27	20-Feb-27	0.00	0.00	448,500.00	-62
MLTX-02-004-CI	Exhaust Fans and Ducts Installation (Air Dome)	7	0%	0%	25-Nov-26	02-Dec-26	06-Feb-27	13-Feb-27	0.00	0.00	392,437.50	-62
ELECTRICAL WORKS		19	0%	0%	10-Dec-26	31-Dec-26	21-Feb-27	18-Mar-27	0.00	0.00	1,681,875.00	-62
MLTX-02-004-CI	Light Fixture Works (Air Dome)	4	0%	0%	10-Dec-26	14-Dec-26	21-Feb-27	25-Feb-27	0.00	0.00	280,312.50	-62
MLTX-02-004-CI	Distribution Board and Electrical Works (Air Dome)	3	0%	0%	15-Dec-26	17-Dec-26	27-Feb-27	01-Mar-27	0.00	0.00	280,312.50	-62
MLTX-02-004-CI	External Electrical Connection Works (Air Dome)	4	0%	0%	19-Dec-26	22-Dec-26	02-Mar-27	06-Mar-27	0.00	0.00	280,312.50	-62
MLTX-02-004-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	23-Dec-26	27-Dec-26	07-Mar-27	14-Mar-27	0.00	0.00	560,625.00	-62
MLTX-02-004-CI	Control System Installation (Air Dome)	4	0%	0%	28-Dec-26	31-Dec-26	15-Mar-27	18-Mar-27	0.00	0.00	280,312.50	-62
FINISHES WORKS		15	0%	0%	10-Dec-26	27-Dec-26	21-Feb-27	14-Mar-27	0.00	0.00	448,500.00	-62
MLTX-02-004-CI	Doors Installation Including Emergency, Entrance doors (Air	6	0%	0%	10-Dec-26	16-Dec-26	21-Feb-27	28-Feb-27	0.00	0.00	224,250.00	-62
MLTX-02-004-CI	Logo and Signs Installation (Air Dome)	9	0%	0%	17-Dec-26	27-Dec-26	01-Mar-27	14-Mar-27	0.00	0.00	224,250.00	-62
IRRIGATION NETWORK		98	0%	82.03%	12-Oct-26	04-Nov-26	20-Aug-26 A	16-Jan-27	0.00	253,142.50	308,587.50	-62
MLTX-02-004-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	4	0%	100%	12-Oct-26	15-Oct-26	20-Aug-26 A	29-Aug-26 A	0.00	107,250.00	107,250.00	40
MLTX-02-004-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	4	0%	100%	17-Oct-26	20-Oct-26	29-Aug-26 A	31-Aug-26 A	0.00	108,712.50	108,712.50	43
MLTX-02-004-CN-1	Installing of Valves and fittings for Irrigation Network	4	0%	80%	21-Oct-26	25-Oct-26	24-Sep-26 A	10-Oct-26	0.00	37,180.00	46,475.00	13
MLTX-02-004-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	02-Nov-26	04-Nov-26	13-Jan-27	16-Jan-27	0.00	0.00	46,150.00	-62
NATURAL GROUND		6	0%	0%	26-Oct-26	01-Nov-26	14-Dec-26	20-Dec-26	0.00	0.00	80,291.25	-42
MLTX-02-004-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	26-Oct-26	01-Nov-26	14-Dec-26	20-Dec-26	0.00	0.00	80,291.25	-42
PLANTING		33	0%	0%	05-Nov-26	13-Dec-26	17-Jan-27	24-Feb-27	0.00	0.00	597,837.50	-62
MLTX-02-004-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	0%	0%	05-Nov-26	08-Nov-26	17-Jan-27	19-Jan-27	0.00	0.00	186,420.00	-62
MLTX-02-004-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	10-Dec-26	13-Dec-26	21-Feb-27	24-Feb-27	0.00	0.00	175,175.00	-62
MLTX-02-004-CN-1	Placement and Fixation of Trees	3	0%	0%	07-Dec-26	09-Dec-26	17-Feb-27	20-Feb-27	0.00	0.00	236,242.50	-62
WALKING/BIKE PATHS		12	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	19-Oct-26	0.00	138,206.39	276,412.77	59
MLTX-02-004-CN-1	Bike Path Preparation and Installation Works	12	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	19-Oct-26	0.00	71,022.68	142,045.36	59
MLTX-02-004-CN-1	Walking Path Preparation and Installation Works	12	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	19-Oct-26	0.00	67,183.70	134,367.41	59
GENERAL/FURNITURE		145	0%	62.73%	12-Oct-26	24-Jan-27	29-Sep-26 A	11-Apr-27	0.00	533,229.40	850,091.81	-62
MLTX-02-004-CN-1	Stamped Concrete Works for LandScape (Including	9	0%	0%	28-Dec-26	06-Jan-27	06-Mar-27	18-Mar-27	0.00	0.00	42,068.52	-57
MLTX-02-004-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	28-Dec-26	04-Jan-27	20-Oct-26	27-Oct-26	0.00	0.00	17,276.03	59



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-CN-1	Fixation and Installation of Benches	7	0%	0%	05-Jan-27	12-Jan-27	23-Mar-27	30-Mar-27	0.00	0.00	40,310.73	-62
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	05-Jan-27	12-Jan-27	23-Mar-27	30-Mar-27	0.00	0.00	43,680.00	-62
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	05-Jan-27	13-Jan-27	23-Mar-27	31-Mar-27	0.00	0.00	17,160.00	-62
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Trash Bins	9	0%	0%	14-Jan-27	24-Jan-27	01-Apr-27	11-Apr-27	0.00	0.00	14,625.00	-62
MLTX-02-004-CN-1	Preleminary Works for Site Light Poles Including Cable and	12	0%	100%	12-Oct-26	25-Oct-26	29-Sep-26 A	01-Oct-26 A	0.00	202,497.75	202,497.75	20
MLTX-02-004-CN-1	Installing of Site Light Poles	11	0%	70%	07-Jan-27	19-Jan-27	01-Oct-26 A	18-Oct-26	0.00	330,731.65	472,473.79	80
TOILET/SERVICE BUILDING		170	70.04%	34.86%	06-Jun-26	02-Nov-26	06-Jun-26 A	21-Dec-26	862,677.07	429,406.22	1,231,701.54	-42
STRUCTURE WORKS		61	100%	100%	06-Jun-26	18-Aug-26	06-Jun-26 A	26-Jul-26 A	158,021.66	158,021.66	158,021.66	20
CONCRETE WORKS		54	100%	100%	14-Jun-26	18-Aug-26	14-Jun-26 A	26-Jul-26 A	113,782.50	113,782.50	113,782.50	20
SUB-STRUCTURE		8	100%	100%	14-Jun-26	23-Jun-26	14-Jun-26 A	23-Jun-26 A	33,345.00	33,345.00	33,345.00	0
MLTX-02-004-CI	Plain Concrete Under Footing	2	100%	100%	14-Jun-26	16-Jun-26	14-Jun-26 A	16-Jun-26 A	1,170.00	1,170.00	1,170.00	0
MLTX-02-004-CI	Reinforced Concrete Works for Slab on Grade Including	7	100%	100%	15-Jun-26	23-Jun-26	15-Jun-26 A	23-Jun-26 A	32,175.00	32,175.00	32,175.00	0
SUPER-STRUCTURE		19	100%	100%	15-Jul-26	18-Aug-26	22-Jul-26 A	26-Jul-26 A	80,437.50	80,437.50	80,437.50	20
MLTX-02-004-CI	AAC Panels Works for Walls	12	100%	100%	15-Jul-26	28-Jul-26	22-Jul-26 A	23-Jul-26 A	48,262.50	48,262.50	48,262.50	4
MLTX-02-004-CI	AAC Panels Works for Slabs	10	100%	100%	29-Jul-26	09-Aug-26	23-Jul-26 A	26-Jul-26 A	16,087.50	16,087.50	16,087.50	12
MLTX-02-004-CI	Parpet Works and Lintels	8	100%	100%	10-Aug-26	18-Aug-26	26-Jul-26 A	26-Jul-26 A	16,087.50	16,087.50	16,087.50	20
UNDER GROUND SEPTIC TANK		18	100%	100%	06-Jun-26	27-Jun-26	06-Jun-26 A	27-Jun-26 A	33,930.00	33,930.00	33,930.00	0
MLTX-02-004-CN-1	Plain Concrete Under Footing	4	100%	100%	06-Jun-26	10-Jun-26	06-Jun-26 A	10-Jun-26 A	1,170.00	1,170.00	1,170.00	0
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Foundation Including	9	100%	100%	10-Jun-26	20-Jun-26	10-Jun-26 A	20-Jun-26 A	7,605.00	7,605.00	7,605.00	0
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	4	100%	100%	17-Jun-26	21-Jun-26	17-Jun-26 A	21-Jun-26 A	16,380.00	16,380.00	16,380.00	0
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Slab Including	5	100%	100%	22-Jun-26	27-Jun-26	22-Jun-26 A	27-Jun-26 A	8,775.00	8,775.00	8,775.00	0
THERMAL & MOISTER PROTECTION		47	100%	100%	06-Jun-26	18-Jul-26	06-Jun-26 A	22-Jul-26 A	10,309.16	10,309.16	10,309.16	-3
ANTI TERMIT CONTROL		20	100%	100%	06-Jun-26	29-Jun-26	06-Jun-26 A	29-Jun-26 A	4,387.50	4,387.50	4,387.50	0
MLTX-02-004-CI	Anti Termite Works Under Foundation	7	100%	100%	06-Jun-26	14-Jun-26	06-Jun-26 A	14-Jun-26 A	1,755.00	1,755.00	1,755.00	0
MLTX-02-004-CI	Anti Termite Works Under Slab on Grade and Grade Beams	5	100%	100%	23-Jun-26	29-Jun-26	23-Jun-26 A	29-Jun-26 A	2,632.50	2,632.50	2,632.50	0
POLYETHYLENE SHEET		21	100%	100%	06-Jun-26	29-Jun-26	06-Jun-26 A	29-Jun-26 A	2,193.75	2,193.75	2,193.75	0
MLTX-02-004-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	7	100%	100%	06-Jun-26	14-Jun-26	06-Jun-26 A	14-Jun-26 A	877.50	877.50	877.50	0
MLTX-02-004-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	6	100%	100%	23-Jun-26	29-Jun-26	23-Jun-26 A	29-Jun-26 A	1,316.25	1,316.25	1,316.25	0
EPOXY		13	100%	100%	05-Jul-26	18-Jul-26	14-Jul-26 A	22-Jul-26 A	3,727.91	3,727.91	3,727.91	-3
MLTX-02-004-CI	Surface Preparation for Epoxy Coating	5	100%	100%	05-Jul-26	09-Jul-26	14-Jul-26 A	21-Jul-26 A	1,168.54	1,168.54	1,168.54	-10
MLTX-02-004-CI	Epoxy Coating for Walls and Slab of Tank	7	100%	100%	11-Jul-26	18-Jul-26	21-Jul-26 A	22-Jul-26 A	2,559.38	2,559.38	2,559.38	-3
MASONARY WORK		5	100%	100%	09-Jul-26	14-Jul-26	26-Jul-26 A	28-Jul-26 A	12,285.00	12,285.00	12,285.00	-12
MLTX-02-004-CN-11C	CMU Masonary Works Including all Accessories	5	100%	100%	09-Jul-26	14-Jul-26	26-Jul-26 A	28-Jul-26 A	12,285.00	12,285.00	12,285.00	-12
THERMAL & MOISTER PROTECTION		15	100%	65.41%	23-Aug-26	15-Sep-26	26-Sep-26 A	14-Oct-26	34,700.25	22,697.81	34,700.25	-24
MLTX-02-004-CN-11C	Preparing Surface and Preliminary Works for Toilets	2	100%	0%	23-Aug-26	24-Aug-26	06-Oct-26	07-Oct-26	2,106.00	0.00	2,106.00	-37
MLTX-02-004-CN-11C	Preparing Surface and Preliminary Works for Roofing and	5	100%	100%	01-Sep-26	06-Sep-26	26-Sep-26 A	26-Sep-26 A	11,072.10	11,072.10	11,072.10	-16
MLTX-02-004-CN-11C	Finalize Water Proofing Works for Toilets	6	100%	0%	25-Aug-26	31-Aug-26	08-Oct-26	14-Oct-26	4,914.00	0.00	4,914.00	-37
MLTX-02-004-CN-11C	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	70%	07-Sep-26	15-Sep-26	27-Sep-26 A	14-Oct-26	16,608.15	11,625.71	16,608.15	-24
MECHANICAL WORK		81	85.18%	7.29%	01-Sep-26	20-Oct-26	04-Jul-26 A	08-Dec-26	327,743.16	28,050.75	384,753.88	-42
HVAC SYSTEM		64	47.55%	33.57%	15-Sep-26	20-Oct-26	10-Aug-26 A	08-Dec-26	13,260.00	9,360.00	27,885.00	-42
MLTX-02-004-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	15-Sep-26	17-Sep-26	10-Aug-26 A	10-Aug-26 A	9,360.00	9,360.00	9,360.00	33
MLTX-02-004-CN-1	Exhaust, Air Ducts Installation with all Accessories	8	100%	0%	19-Sep-26	28-Sep-26	24-Oct-26	01-Nov-26	3,900.00	0.00	3,900.00	-29
MLTX-02-004-CN-1	Install and Finish HVAC and Ventilation Works Including Split	6	0%	0%	14-Oct-26	20-Oct-26	02-Dec-26	08-Dec-26	0.00	0.00	14,625.00	-42
WATER SUPPLY SYSTEM		70	95.74%	3.26%	03-Sep-26	10-Oct-26	04-Jul-26 A	28-Nov-26	203,386.79	6,922.50	212,427.50	-42
MLTX-02-004-CN-1	Installing of Valves and Fittings	2	100%	0%	07-Sep-26	08-Sep-26	06-Oct-26	07-Oct-26	9,750.00	0.00	9,750.00	-24
MLTX-02-004-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	0%	09-Sep-26	12-Sep-26	08-Oct-26	11-Oct-26	39,000.00	0.00	39,000.00	-24
MLTX-02-004-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	03-Sep-26	06-Sep-26	04-Jul-26 A	09-Aug-26 A	6,922.50	6,922.50	6,922.50	24
MLTX-02-004-CN-1	Installing of Booster Pump Units Including fittings and	7	85.71%	0%	29-Sep-26	06-Oct-26	02-Nov-26	09-Nov-26	43,714.29	0.00	51,000.00	-29
MLTX-02-004-CN-1	Installing of GRP Tanks	8	100%	0%	19-Sep-26	28-Sep-26	18-Oct-26	26-Oct-26	104,000.00	0.00	104,000.00	-24
MLTX-02-004-CN-1	Installing of Water Heater	4	0%	0%	06-Oct-26	10-Oct-26	24-Nov-26	28-Nov-26	0.00	0.00	1,755.00	-42
SEWER/DRAINAGE SYSTEM		77	77.97%	8.26%	01-Sep-26	15-Oct-26	04-Jul-26 A	03-Dec-26	111,096.38	11,768.25	142,491.38	-42
MLTX-02-004-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	14-Sep-26	17-Sep-26	26-Oct-26	29-Oct-26	76,781.25	0.00	76,781.25	-35
MLTX-02-004-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	01-Sep-26	02-Sep-26	04-Jul-26 A	09-Aug-26 A	11,768.25	11,768.25	11,768.25	21
MLTX-02-004-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	19-Sep-26	20-Sep-26	08-Nov-26	09-Nov-26	10,359.38	0.00	10,359.38	-42
MLTX-02-004-CN-1	Installing Inspection Chamber for Sewage Network	9	100%	0%	03-Sep-26	13-Sep-26	15-Oct-26	25-Oct-26	12,187.50	0.00	12,187.50	-35
MLTX-02-004-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	9	0%	0%	06-Oct-26	15-Oct-26	24-Nov-26	03-Dec-26	0.00	0.00	31,395.00	-42
FIRE PROTECTION		4	0%	0%	17-Oct-26	20-Oct-26	05-Dec-26	08-Dec-26	0.00	0.00	1,950.00	-42
MLTX-02-004-CN-1	Installing of Fire Fighting Extinguisher and accessories	4	0%	0%	17-Oct-26	20-Oct-26	05-Dec-26	08-Dec-26	0.00	0.00	1,950.00	-42
ELECTRICAL WORKS		115	39.54%	39.54%	19-Aug-26	25-Oct-26	30-Jul-26 A	13-Dec-26	148,882.50	148,882.50	376,526.25	-42
ROUGH-IN WORKS		36	100%	100%	19-Aug-26	30-Aug-26	30-Jul-26 A	26-Aug-26 A	148,882.50	148,882.50	148,882.50	3
MLTX-02-004-CN-1	Preleminary Works for Earthing Works	10	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	15,600.00	15,600.00	15,600.00	3
MLTX-02-004-CN-1	Preleminary Works for Panel Boards	10	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	76,050.00	76,050.00	76,050.00	3
MLTX-02-004-CN-1	Preleminary Works for Cable Works	10	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	10,700.04	10,700.04	10,700.04	3
MLTX-02-004-CN-1	Preleminary Works for Sockets and Power Points	10	100%	100%	19-Aug-26	30-Aug-26	30-Jul-26 A	30-Jul-26 A	9,230.91	9,230.91	9,230.91	26




© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-CN-1	Preleminary Works for Lightning Works	10	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	9,750.00	9,750.00	9,750.00	3
MLTX-02-004-CN-1	Preleminary Works for Data & Telecommunication System	10	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	12,285.00	12,285.00	12,285.00	3
MLTX-02-004-CN-1	Preleminary Works for Security and Access Control System	10	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	15,266.55	15,266.55	15,266.55	3
FIXTURE WORKS		10	0%	0%	14-Oct-26	25-Oct-26	02-Dec-26	13-Dec-26	0.00	0.00	227,643.75	-42
MLTX-02-004-CN-1	Installing and Finish Works of Panel Boards	10	0%	0%	14-Oct-26	25-Oct-26	02-Dec-26	13-Dec-26	0.00	0.00	84,075.00	-42
MLTX-02-004-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	17-Oct-26	20-Oct-26	05-Dec-26	08-Dec-26	0.00	0.00	18,427.50	-42
MLTX-02-004-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	17-Oct-26	20-Oct-26	05-Dec-26	08-Dec-26	0.00	0.00	13,846.37	-42
MLTX-02-004-CN-1	Installing and Finalize Works of Earthing Works	6	0%	0%	14-Oct-26	20-Oct-26	02-Dec-26	08-Dec-26	0.00	0.00	23,400.00	-42
MLTX-02-004-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	21-Oct-26	25-Oct-26	09-Dec-26	13-Dec-26	0.00	0.00	34,320.00	-42
MLTX-02-004-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	17-Oct-26	20-Oct-26	05-Dec-26	08-Dec-26	0.00	0.00	16,050.06	-42
MLTX-02-004-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	14-Oct-26	20-Oct-26	02-Dec-26	08-Dec-26	0.00	0.00	14,625.00	-42
MLTX-02-004-CN-1	Installing and Finalize Works of Security and Access Control	6	0%	0%	14-Oct-26	20-Oct-26	02-Dec-26	08-Dec-26	0.00	0.00	22,899.83	-42
DOORS/WINDOWS		51	40%	0%	19-Aug-26	02-Nov-26	24-Oct-26	21-Dec-26	27,300.00	0.00	68,250.00	-42
MLTX-02-004-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	19-Aug-26	20-Aug-26	24-Oct-26	25-Oct-26	23,400.00	0.00	23,400.00	-55
MLTX-02-004-CN-111	Preliminary Works For Doors	3	100%	0%	19-Aug-26	22-Aug-26	24-Oct-26	26-Oct-26	3,900.00	0.00	3,900.00	-55
MLTX-02-004-CN-111	Finalize Metal Doors for Toilets Building	7	0%	0%	18-Oct-26	25-Oct-26	02-Dec-26	09-Dec-26	0.00	0.00	5,850.00	-39
MLTX-02-004-CN-111	Finalize Glazzed Curtain Wall Works	7	0%	0%	26-Oct-26	02-Nov-26	14-Dec-26	21-Dec-26	0.00	0.00	35,100.00	-42
METAL WORKS		47	76.19%	71.43%	19-Jul-26	17-Oct-26	20-Sep-26 A	17-Oct-26	10,400.00	9,750.00	13,650.00	0
MLTX-02-004-CN-111	Installation of Galvanized Steel Ladder	12	100%	100%	19-Sep-26	03-Oct-26	21-Sep-26 A	03-Oct-26 A	5,850.00	5,850.00	5,850.00	0
MLTX-02-004-CN-111	Installation of DI Cover for Tank	10	100%	0%	19-Jul-26	29-Jul-26	06-Oct-26	17-Oct-26	3,900.00	0.00	3,900.00	-67
MLTX-02-004-CN-111	Installation of Galvanized Steel Roof Scupper	12	16.67%	100%	04-Oct-26	17-Oct-26	20-Sep-26 A	20-Sep-26 A	650.00	3,900.00	3,900.00	23
FINISHING WORKS		64	89.07%	34.4%	01-Sep-26	17-Oct-26	29-Aug-26 A	05-Dec-26	128,719.50	49,718.50	144,514.50	-42
FLOOR FINISHES		34	93.18%	0%	07-Sep-26	17-Oct-26	27-Oct-26	05-Dec-26	15,990.00	0.00	17,160.00	-42
MLTX-02-004-CN-1	Creamic Tiles Floor Finish Works	2	100%	0%	07-Sep-26	08-Sep-26	27-Oct-26	28-Oct-26	11,895.00	0.00	11,895.00	-42
MLTX-02-004-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	09-Sep-26	13-Sep-26	29-Oct-26	02-Nov-26	2,925.00	0.00	2,925.00	-42
MLTX-02-004-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	14-Oct-26	17-Oct-26	02-Dec-26	05-Dec-26	0.00	0.00	1,170.00	-42
MLTX-02-004-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	0%	14-Sep-26	17-Sep-26	03-Nov-26	07-Nov-26	1,170.00	0.00	1,170.00	-42
WALL FINISHES		63	87.19%	43.55%	01-Sep-26	15-Oct-26	29-Aug-26 A	03-Dec-26	99,547.50	49,718.50	114,172.50	-42
MLTX-02-004-CN-1	Stone Cladding Finish Works for External Walls	5	100%	100%	21-Sep-26	27-Sep-26	19-Sep-26 A	26-Sep-26 A	9,100.00	9,100.00	9,100.00	1
MLTX-02-004-CN-1	Glass Partitions including all accessories and doors	7	0%	0%	06-Oct-26	13-Oct-26	24-Nov-26	01-Dec-26	0.00	0.00	12,285.00	-42
MLTX-02-004-CN-1	Granite Capping for Parpet	2	100%	0%	16-Sep-26	17-Sep-26	15-Oct-26	17-Oct-26	8,151.00	0.00	8,151.00	-24
MLTX-02-004-CN-1	Preliminary Works for Wall Finish Works including Plastering	5	100%	100%	01-Sep-26	06-Sep-26	29-Aug-26 A	09-Sep-26 A	18,369.00	18,369.00	18,369.00	-3
MLTX-02-004-CN-1	Preliminary Works for Wall Finish Works (External)	10	100%	100%	01-Sep-26	12-Sep-26	10-Sep-26 A	12-Sep-26 A	6,552.00	6,552.00	6,552.00	0
MLTX-02-004-CN-1	Painting Finish Works for External Walls	7	100%	0%	13-Sep-26	20-Sep-26	12-Oct-26	19-Oct-26	10,478.00	0.00	10,478.00	-24
MLTX-02-004-CN-1	Ceramic Finish Works for Walls	5	100%	100%	09-Sep-26	14-Sep-26	12-Sep-26 A	14-Sep-26 A	15,697.50	15,697.50	15,697.50	0
MLTX-02-004-CN-1	Phenolic Partitions for Toilets	7	100%	0%	28-Sep-26	05-Oct-26	16-Nov-26	23-Nov-26	31,200.00	0.00	31,200.00	-42
MLTX-02-004-CN-1	Painting Finish Works for Internal Walls	2	0%	0%	14-Oct-26	15-Oct-26	02-Dec-26	03-Dec-26	0.00	0.00	2,340.00	-42
CELLING FINISHES		19	100%	0%	07-Sep-26	30-Sep-26	06-Oct-26	27-Oct-26	13,182.00	0.00	13,182.00	-23
MLTX-02-004-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	0%	07-Sep-26	09-Sep-26	21-Oct-26	24-Oct-26	4,617.60	0.00	4,617.60	-37
MLTX-02-004-CN-1	Painting Finish Works for Ceiling	3	100%	0%	28-Sep-26	30-Sep-26	25-Oct-26	27-Oct-26	1,638.00	0.00	1,638.00	-23
MLTX-02-004-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	0%	19-Sep-26	27-Sep-26	06-Oct-26	13-Oct-26	6,926.40	0.00	6,926.40	-14
SPECIALTIES WORK		15	37.5%	0%	21-Sep-26	08-Oct-26	10-Nov-26	26-Nov-26	14,625.00	0.00	39,000.00	-42
MLTX-02-004-CN-113	Installation of Phenolic Locker	3	0%	0%	06-Oct-26	08-Oct-26	24-Nov-26	26-Nov-26	0.00	0.00	24,375.00	-42
MLTX-02-004-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	21-Sep-26	27-Sep-26	10-Nov-26	15-Nov-26	14,625.00	0.00	14,625.00	-42
TESTING & COMMISSIONING		59	0%	0%	05-Nov-26	12-Jan-27	17-Jan-27	30-Mar-27	0.00	0.00	0.00	-62
MLTX-02-004-TC-11860	Testing and Commissioning for MEP Works for Playground	10	0%	0%	02-Jan-27	12-Jan-27	20-Mar-27	30-Mar-27	0.00	0.00	0.00	-62
MLTX-02-004-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	22	0%	0%	05-Nov-26	30-Nov-26	17-Jan-27	10-Feb-27	0.00	0.00	0.00	-62
MLTX-02-004-TC-11880	Testing and Commissioning for MEP Works for Landscape	22	0%	0%	01-Dec-26	26-Dec-26	11-Feb-27	09-Mar-27	0.00	0.00	0.00	-62
JAZAN		335	29.73%	21.42%	26-Mar-26	25-Jan-27	26-Mar-26 A	29-Apr-27	3,174,958.02	2,287,918.34	10,680,071.52	-77
MOBILIZATION		63	0%	0%	26-Mar-26	10-Jun-26	26-Mar-26 A	10-Jun-26 A	0.00	0.00	0.00	0
TOPOGRAPHIC SURVEY		4	0%	0%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1860	Site Survey Works	4	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
SITE FACILITIES & OFFICES		56	0%	0%	26-Mar-26	02-Jun-26	26-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1740	Manpower Mobalization	32	100%	100%	16-Apr-26	23-May-26	16-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1750	Equipment Mobalization	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1770	Site Layout Plan	4	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1780	Clear & Grub for Offices & Access Road	3	100%	100%	31-Mar-26	02-Apr-26	31-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1790	Construct Site Access Roads	4	100%	100%	31-Mar-26	04-Apr-26	31-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1800	Construct Temporary Fence	39	100%	100%	15-Apr-26	02-Jun-26	15-Apr-26 A	02-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1810	Construct Site Offices & Storage	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1820	Install Project Signs	18	100%	100%	20-Apr-26	10-May-26	20-Apr-26 A	10-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1830	Install Site Facilities	1	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1840	Electrical Works & Connections	1	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-1850	Construct Parking Sheds	1	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0

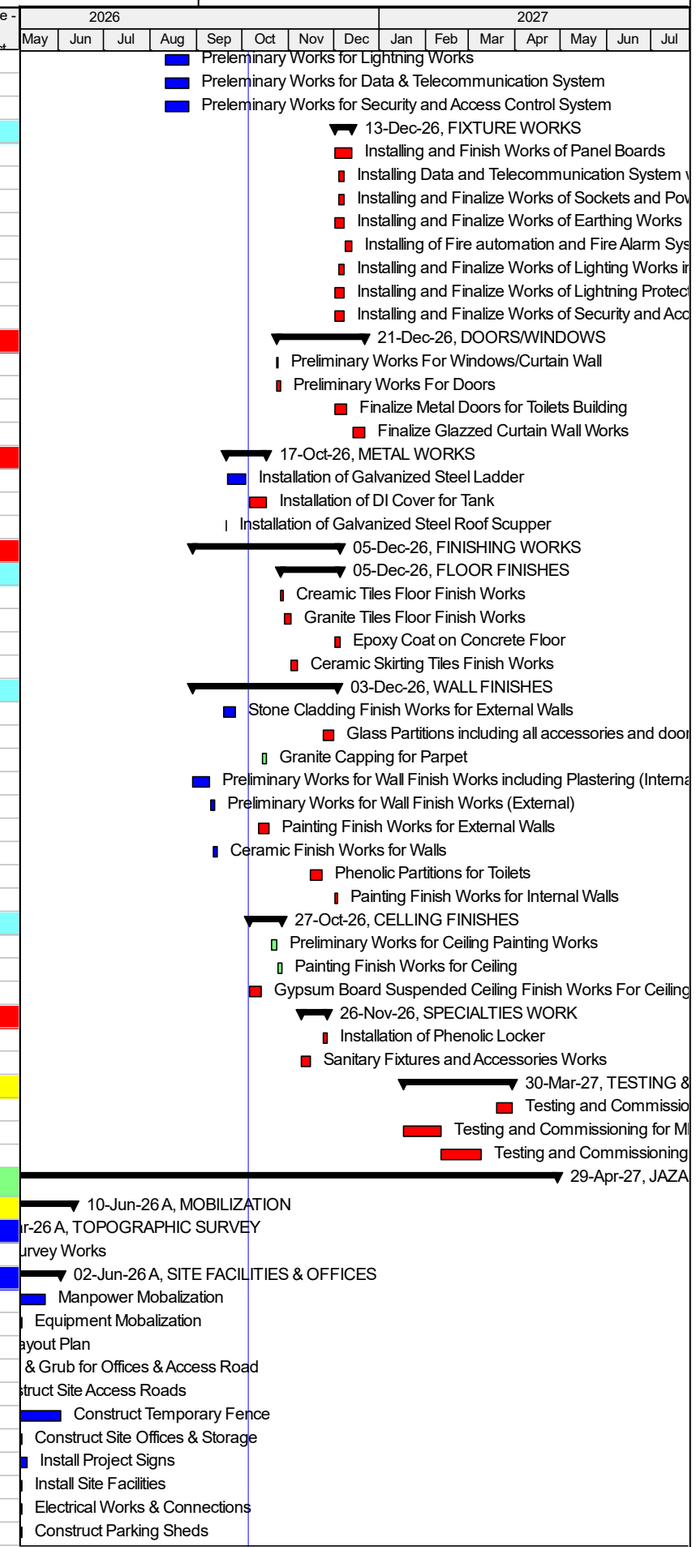

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PRELIMINARY SUBMITTALS		59	0%	0%	31-Mar-26	10-Jun-26	31-Mar-26 A	10-Jun-26 A	0.00	0.00	0.00	0
PREPARATIONS & SUBMITTAL BY CONTRACTORS		27	0%	0%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-176	Preparation and Submittal of Detailed Work Order	25	100%	100%	31-Mar-26	28-Apr-26	31-Mar-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-187	Preparation and Submittal of Project Execution Plan	27	100%	100%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-188	Submission of Contractor Project Quality Plan	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-189	Submission of Construction Safety & Environmental	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-190	Preparation and Submittal of Organization Chart	8	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-191	Preparation and Submittal of Communication Plan	8	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	0
APPROVALS BY EMPLOYERS		51	0%	0%	09-Apr-26	10-Jun-26	09-Apr-26 A	10-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-192	Approval of Detailed Work Order Programme (Baseline)	1	100%	100%	29-Apr-26	29-Apr-26	29-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-193	Approval of Project Execution Plan	1	100%	100%	13-May-26	13-May-26	13-May-26 A	13-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-194	Approval of Contractor Project Quality Plan	19	100%	100%	09-Apr-26	30-Apr-26	09-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-195	Approval of Construction Safety & Environmental	1	100%	100%	10-Jun-26	10-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-196	Approval of Organization Chart	10	100%	100%	09-Apr-26	20-Apr-26	09-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-MB-197	Approval of Communication Plan	10	100%	100%	09-Apr-26	20-Apr-26	09-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
ENGINEERING		173	0%	0%	31-Mar-26	02-Aug-26	31-Mar-26 A	22-Oct-26	0.00	0.00	0.00	-69
SHOP DRAWINGS		144	0%	0%	31-Mar-26	21-Jul-26	31-Mar-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
SHOP DRAWINGS SUBMISSION		134	0%	0%	31-Mar-26	09-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		68	0%	0%	31-Mar-26	21-Jun-26	31-Mar-26 A	21-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Shop DWG Submittal for Layout Plan	15	100%	100%	31-Mar-26	16-Apr-26	31-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Shop DWG Submittal for Setting Out	21	100%	100%	31-Mar-26	23-Apr-26	31-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Shop DWG Submittal for Grading Layout Plan	6	100%	100%	31-Mar-26	06-Apr-26	31-Mar-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Shop DWG Submittal for Curb Setting Out Points	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Shop DWG Submittal for Signing & Marking Layout Plan	1	100%	100%	21-Jun-26	21-Jun-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Shop DWG Submittal for Standards Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		134	0%	0%	31-Mar-26	09-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
ARCHITECTURE WORKS		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Floor Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Elevations	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Ceiling Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Finishes Plan	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Toilet Details	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Doors/Windows Schedule	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		20	0%	0%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Foundation Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Ground Floor Framing Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections/Details	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		38	0%	0%	08-Apr-26	21-May-26	08-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for HVAC Plan	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Exhaust Air Plan	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for HVAC Equipment Schedule	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Fighting Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Water Supply Layout	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Water Supply Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Drainage Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Drainage Details	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Dut Routing Layout	6	100%	100%	08-Apr-26	14-Apr-26	08-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Diffusers Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		127	0%	0%	08-Apr-26	09-Jul-26	08-Apr-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for Lighting Layout	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Layout	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Single Line Diagram	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Panel Board Schedules	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Installation Details	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Installation Details	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Cable Tray Installation Details	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Manhole & Ductbank Details	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Grounding Details	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lightning Protection Details	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Installation Details	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Details	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for Grounding Layout	2	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lightning Protection System Layout	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0

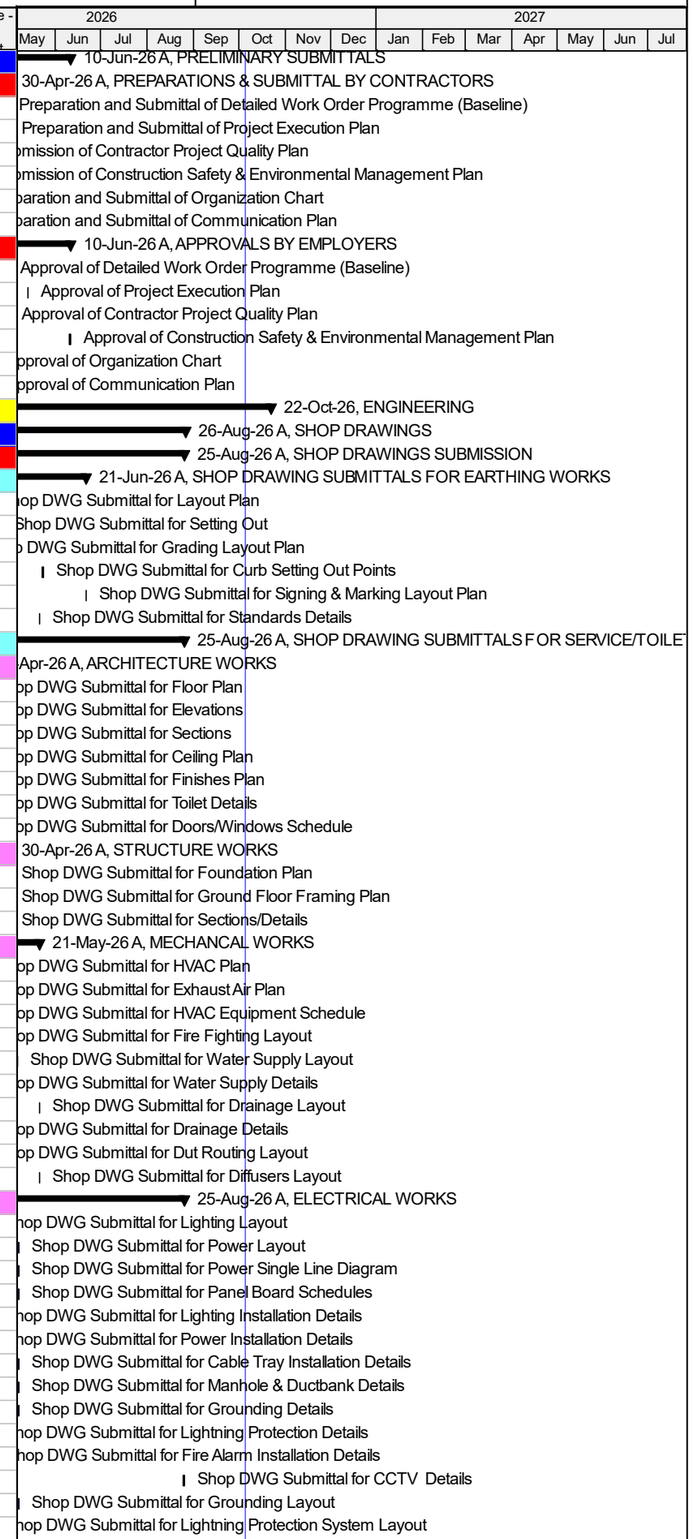

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Layout	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Layout	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for CCTV Riser Diagram	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for Telephone & Data Layout	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Telephone & Data Riser Diagram	11	100%	100%	08-Apr-26	20-Apr-26	08-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		134	0%	0%	31-Mar-26	09-Jul-26	31-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
ARCHITECTURE WORKS		39	0%	0%	31-Mar-26	14-May-26	31-Mar-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Playground Plan/Layout	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Furniture & Marking	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Sections	16	100%	100%	31-Mar-26	18-Apr-26	31-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Interlock Pattern Plan	7	100%	100%	31-Mar-26	07-Apr-26	31-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Doors/Windows Schedule	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Dome Internal Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Air Dome System	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Foundation of Air Dome	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
AIR DOME SYSTEM		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Air Dome Structural Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Membrane Panel Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Cable Tension Layout	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Airlock Door Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Emergency Exit Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
SPORTS EQUIPMENT		2	0%	0%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Football Turf Installation	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Basketball Court Marking	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Padel Court Structure	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		20	0%	0%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for HVAC Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Exhaust Air Plan	20	100%	100%	08-Apr-26	30-Apr-26	08-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		89	0%	0%	23-May-26	09-Jul-26	23-May-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for Lighting Layout	1	100%	100%	25-May-26	25-May-26	25-May-26 A	25-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Power Layout	5	100%	100%	05-Jul-26	09-Jul-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-004-EN	Shop DWG Submittal for Power Single Line Diagram	5	100%	100%	05-Jul-26	09-Jul-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-004-EN	Shop DWG Submittal for Panel Board Schedules	5	100%	100%	05-Jul-26	09-Jul-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-004-EN	Shop DWG Submittal for Power Installation Details	5	100%	100%	05-Jul-26	09-Jul-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Details	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for CCTV Layout	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-004-EN	Shop DWG Submittal for CCTV Riser Diagram	5	100%	100%	05-Jul-26	09-Jul-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-40
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		95	0%	0%	31-Mar-26	09-Jul-26	31-Mar-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
ARCHITECTURE WORKS		39	0%	0%	31-Mar-26	14-May-26	31-Mar-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Landscape Layout	15	100%	100%	31-Mar-26	16-Apr-26	31-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Hardscape Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Planting Plan	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Landscape Details	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		5	0%	0%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-EN	Shop DWG Submittal for Irrigation Details	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-EN	Shop DWG Submittal for Irrigation Layout	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
ELECTRICAL WORKS		1	0%	0%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting General Arrangement	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Network Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Submittal for Lighting Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS APPROVALS		138	0%	0%	07-Apr-26	21-Jul-26	07-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
SHOP DRAWING APPROVAL FOR EARTHING WORKS		71	0%	0%	07-Apr-26	01-Jul-26	07-Apr-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Layout Plan	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Setting Out	17	100%	100%	07-Apr-26	26-Apr-26	07-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Grading Layout Plan	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Curb Setting Out Points	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Shop DWG Approval for Signing & Marking Layout Plan	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0

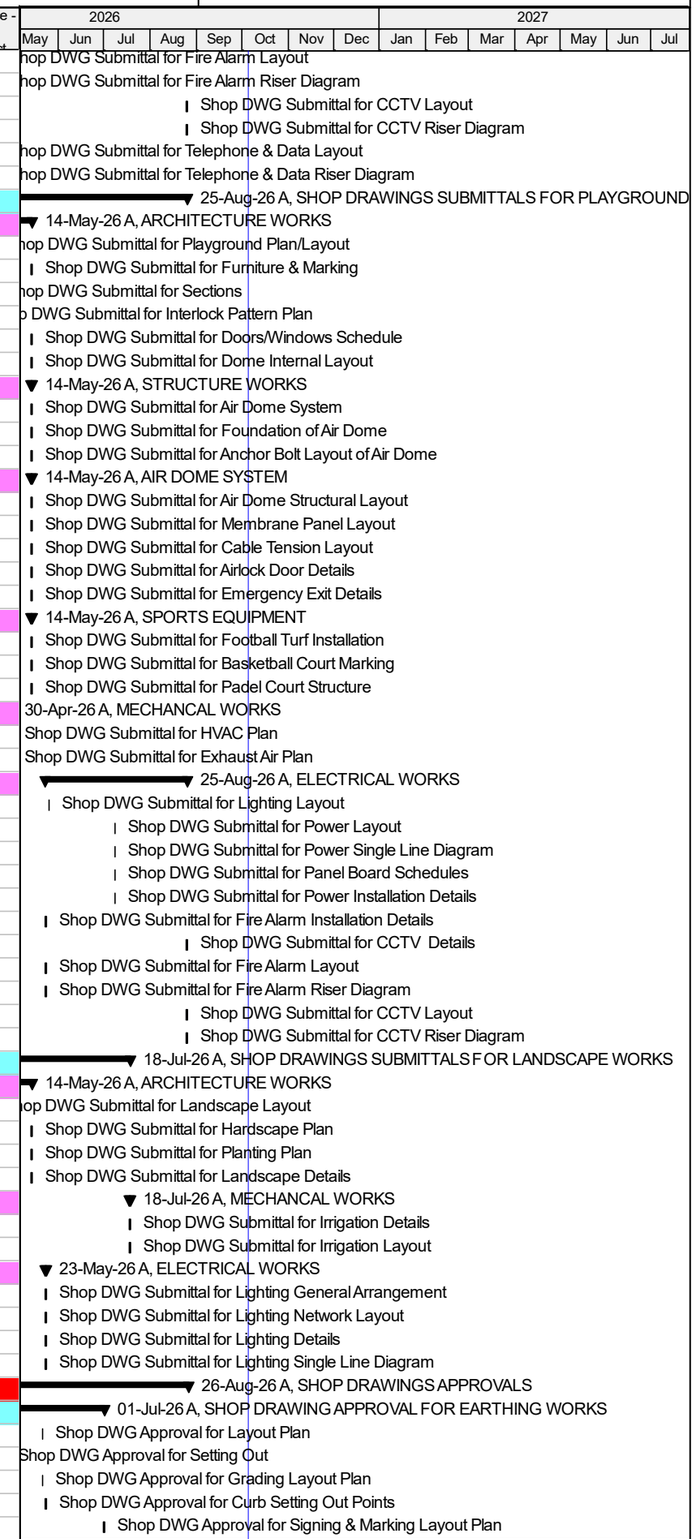


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN-1	Shop DWG Approval for Standards Details	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		132	0%	0%	14-Apr-26	21-Jul-26	14-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
ARCHITECTURE WORKS		9	0%	0%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Floor Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Elevations	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Ceiling Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Finishes Plan	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Toilet Details	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Doors/Windows Schedule	9	100%	100%	14-Apr-26	23-Apr-26	14-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		1	0%	0%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Foundation Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Ground Floor Framing Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections/Details	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		13	0%	0%	07-May-26	21-May-26	07-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for HVAC Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Exhaust Air Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for HVAC Equipment Schedule	4	100%	100%	07-May-26	11-May-26	07-May-26 A	11-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Fire Fighting Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Water Supply Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Water Supply Details	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Drainage Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Drainage Details	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Duct Routing Layout	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Diffusers Layout	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		131	0%	0%	15-Apr-26	21-Jul-26	15-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for Lighting Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Panel Board Schedules	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Cable Tray Installation Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Manhole & Ductbank Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Grounding Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lightning Protection Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Fire Alarm Installation Details	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for CCTV Details	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for Grounding Layout	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lightning Protection System Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Fire Alarm Layout	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Fire Alarm Riser Diagram	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for CCTV Layout	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for CCTV Riser Diagram	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for Telephone & Data Layout	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Telephone & Data Riser Diagram	6	100%	100%	21-Apr-26	27-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	0
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		137	0%	0%	08-Apr-26	21-Jul-26	08-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
ARCHITECTURE WORKS		59	0%	0%	08-Apr-26	18-Jun-26	08-Apr-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Playground Plan/Layout	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Furniture & Marking	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Sections	5	100%	100%	19-Apr-26	23-Apr-26	19-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Interlock Pattern Plan	10	100%	100%	08-Apr-26	19-Apr-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Doors/Windows Schedule	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Dome Internal Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
STRUCTURE WORKS		1	0%	0%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Air Dome System	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Foundation of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Foundation of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Anchor Bolt Layout of Air Dome	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
AIR DOME SYSTEM		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Air Dome Structural Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Membrane Panel Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Cable Tension Layout	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Airlock Door Details	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0

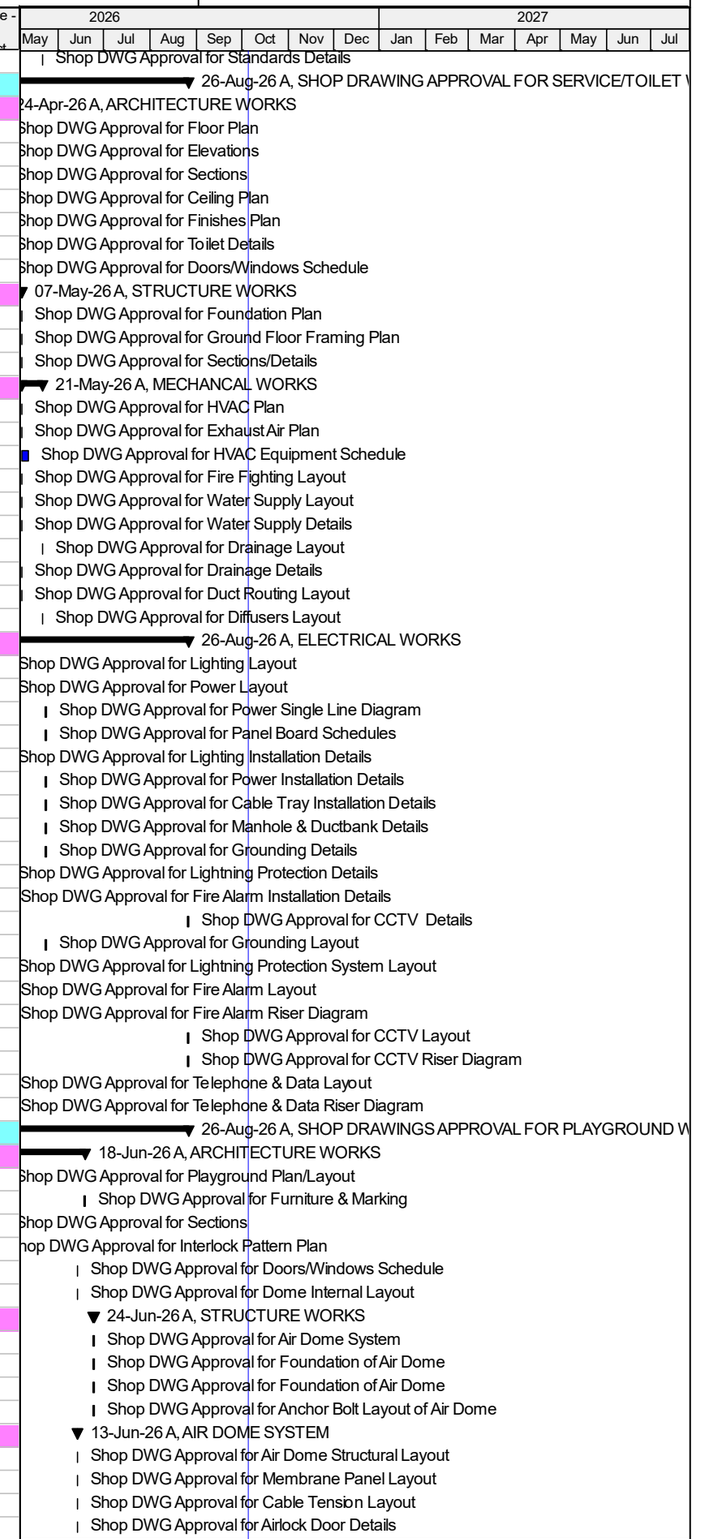

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Shop DWG Approval for Emergency Exit Details	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SPORTS EQUIPMENT		1	0%	0%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Football Turf Installation	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Basketball Court Marking	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Padel Court Structure	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		1	0%	0%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for HVAC Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Exhaust Air Plan	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		131	0%	0%	15-Apr-26	21-Jul-26	15-Apr-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for Lighting Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Layout	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Power Single Line Diagram	10	100%	100%	11-Jul-26	21-Jul-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	11
MLTX-02-004-EN	Shop DWG Approval for Panel Board Schedules	10	100%	100%	11-Jul-26	21-Jul-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	11
MLTX-02-004-EN	Shop DWG Approval for Power Installation Details	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for CCTV Details	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for CCTV Layout	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-004-EN	Shop DWG Approval for CCTV Riser Diagram	10	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-31
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		91	0%	0%	11-Apr-26	21-Jul-26	11-Apr-26 A	18-Jul-26 A	0.00	0.00	0.00	3
ARCHITECTURE WORKS		31	0%	0%	18-Apr-26	23-May-26	17-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Landscape Layout	6	100%	100%	18-Apr-26	23-Apr-26	17-Apr-26 A	24-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Hardscape Plan	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Planting Plan	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Landscape Details	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
MECHANCAL WORKS		10	0%	0%	11-Jul-26	21-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-004-EN	Shop DWG Approval for Irrigation Details	10	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-004-EN	Shop DWG Approval for Irrigation Layout	10	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	3
ELECTRICAL WORKS		37	0%	0%	11-Apr-26	23-May-26	11-Apr-26 A	23-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting General Arrangement	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Network Layout	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Details	10	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Shop DWG Approval for Lighting Single Line Diagram	1	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	0
METHOD STATEMENTS		173	0%	0%	31-Mar-26	02-Aug-26	31-Mar-26 A	22-Oct-26	0.00	0.00	0.00	-69
METHOD STATEMENT SUBMITTAL		163	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26 A	11-Oct-26	0.00	0.00	0.00	-72
CIVIL WORKS		45	0%	0%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for	17	100%	100%	31-Mar-26	19-Apr-26	31-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for Concrete	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for	22	100%	100%	31-Mar-26	25-Apr-26	31-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		114	0%	0%	31-May-26	11-Jul-26	31-May-26 A	11-Oct-26	0.00	0.00	0.00	-78
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for Plastering	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Tilling	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Parking	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Soft	5	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Fence	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Air Dome	5	100%	100%	05-Jul-26	09-Jul-26	17-Aug-26 A	17-Aug-26 A	0.00	0.00	0.00	-33
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Metal	6	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Partitions	5	100%	100%	05-Jul-26	09-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	-5
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Gypsum	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MECHANICAL WORKS		48	0%	0%	07-Apr-26	04-Jun-26	07-Apr-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Water	1	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Fire	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Irrigation	0	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for HVAC	0	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		58	0%	0%	18-Jun-26	18-Jul-26	18-Jun-26 A	12-Aug-26 A	0.00	0.00	0.00	-22
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for Electrical	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-7	Preparation & Submission of Method Statement for Lighting	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for	7	100%	100%	11-Jul-26	18-Jul-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	2
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for CCTV	7	100%	100%	11-Jul-26	18-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Lighting	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0

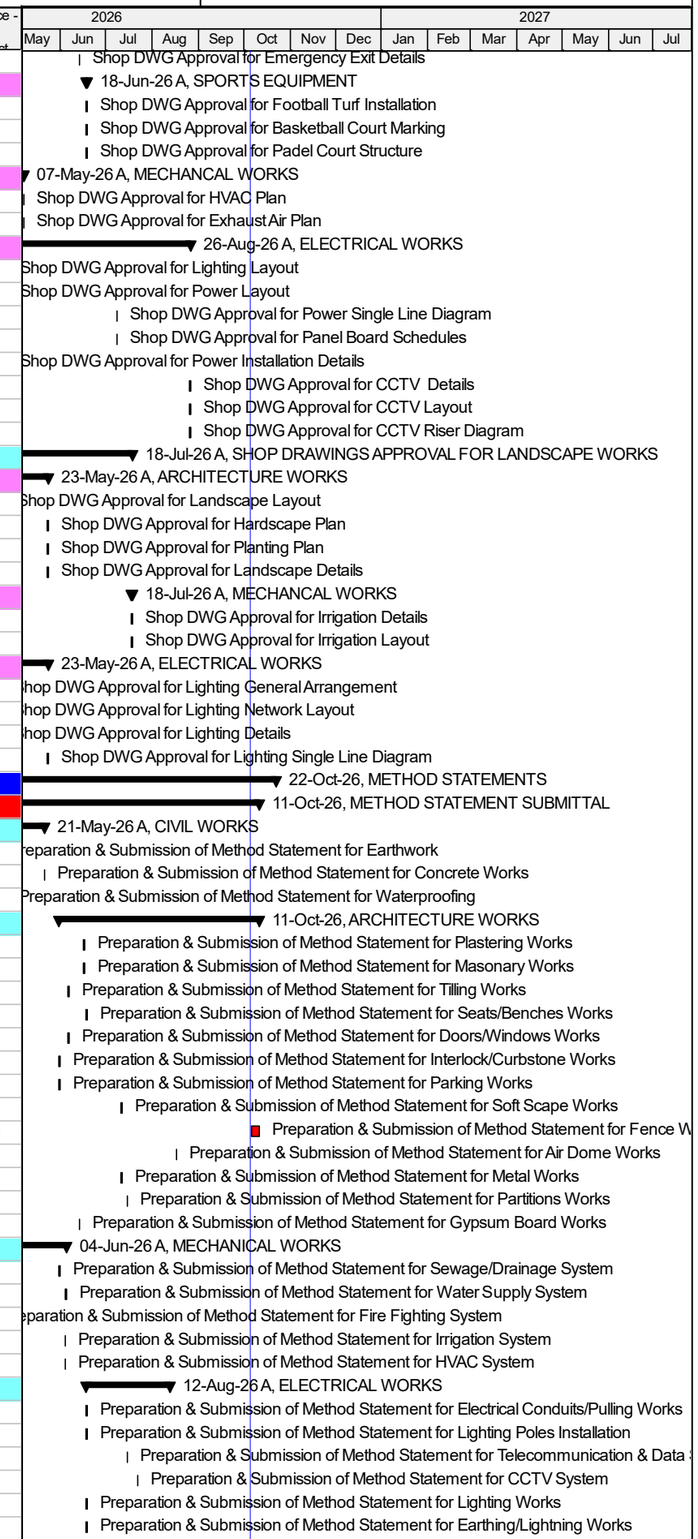

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN-8	Preparation & Submission of Method Statement for Panel	6	100%	100%	05-Jul-26	11-Jul-26	12-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	-28
METHOD STATEMENT APPROVAL		160	0%	0%	15-Apr-26	02-Aug-26	15-Apr-26 A	22-Oct-26	0.00	0.00	0.00	-69
CIVIL WORKS		1	0%	0%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Earthwork	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Concrete Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Waterproofing	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
ARCHITECTURE WORKS		124	0%	0%	31-May-26	21-Jul-26	31-May-26 A	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-1	Approval of Method Statement for Plastering Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Masonary Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Tilling Works	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Seats/Benches Works	5	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Approval of Method Statement for Doors/Windows Works	1	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Interlock/Curbstone Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Parking Works	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Soft Scape Works	10	100%	100%	11-Jul-26	21-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	9
MLTX-02-004-EN-1	Approval of Method Statement for Fence Works	10	100%	0%	11-Jul-26	21-Jul-26	12-Oct-26	22-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN-1	Approval of Method Statement for Air Dome Works	10	100%	100%	11-Jul-26	21-Jul-26	27-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	-32
MLTX-02-004-EN-1	Approval of Method Statement for Partitions Works	10	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-004-EN-1	Approval of Method Statement for Gypsum Board Works	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MECHANICAL WORKS		47	0%	0%	15-Apr-26	11-Jun-26	15-Apr-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Sewage/Drainage System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Water Supply System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Fire Fighting System	10	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for Irrigation System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN-1	Approval of Method Statement for HVAC System	1	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0
ELECTRICAL WORKS		49	0%	0%	05-Jul-26	02-Aug-26	11-Jul-26 A	15-Aug-26 A	0.00	0.00	0.00	-11
MLTX-02-004-EN-1	Approval of Method Statement for Electrical Conduits/Pulling	5	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-004-EN-1	Approval of Method Statement for Lighting Poles Installation	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-1	Approval of Method Statement for Telecommunication & Data	10	100%	100%	22-Jul-26	02-Aug-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	15
MLTX-02-004-EN-1	Approval of Method Statement for CCTV System	10	100%	100%	19-Jul-26	29-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	6
MLTX-02-004-EN-1	Approval of Method Statement for Lighting Works	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-1	Approval of Method Statement for Earthing/Lightning Works	10	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-EN-1	Approval of Method Statement for Panel Boards Works	10	100%	100%	12-Jul-26	22-Jul-26	15-Aug-26 A	15-Aug-26 A	0.00	0.00	0.00	-20
PRE-QUALIFICATION & MATERIAL		165	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26 A	13-Oct-26	0.00	0.00	0.00	-74
PRE-QUALIFICATION		45	0%	0%	31-Mar-26	21-May-26	31-Mar-26 A	21-May-26 A	0.00	0.00	0.00	0
TOILET/SERVICE WORKS		18	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26 A	20-Apr-26 A	0.00	0.00	0.00	0
STEEL REINFORCEMENT		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Steel Reinforcement	2	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Steel Reinforcement	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
READY MIX CONCRETE		18	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Ready Mixed Concrete	14	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval of Ready Mixed Concrete	5	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		18	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Concrete Blocks	14	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Concrete Blocks	5	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
WATER PROOFING		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Water Proofing	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Water Proofing	3	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
FLOOR/WALL TILES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Tilling Materials	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Tailling Material	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SUSPENDED CEILING		12	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Suspend Ceiling	11	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Suspend Ceiling	2	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
DOORS/WINDOWS		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Doors/Windows	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Doors/Windows	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
FURNITURES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Furnitures	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Furnitures	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Sanitary Fixtures	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Sanitary Fixtures	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
WATER SUPPLY PIPES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0

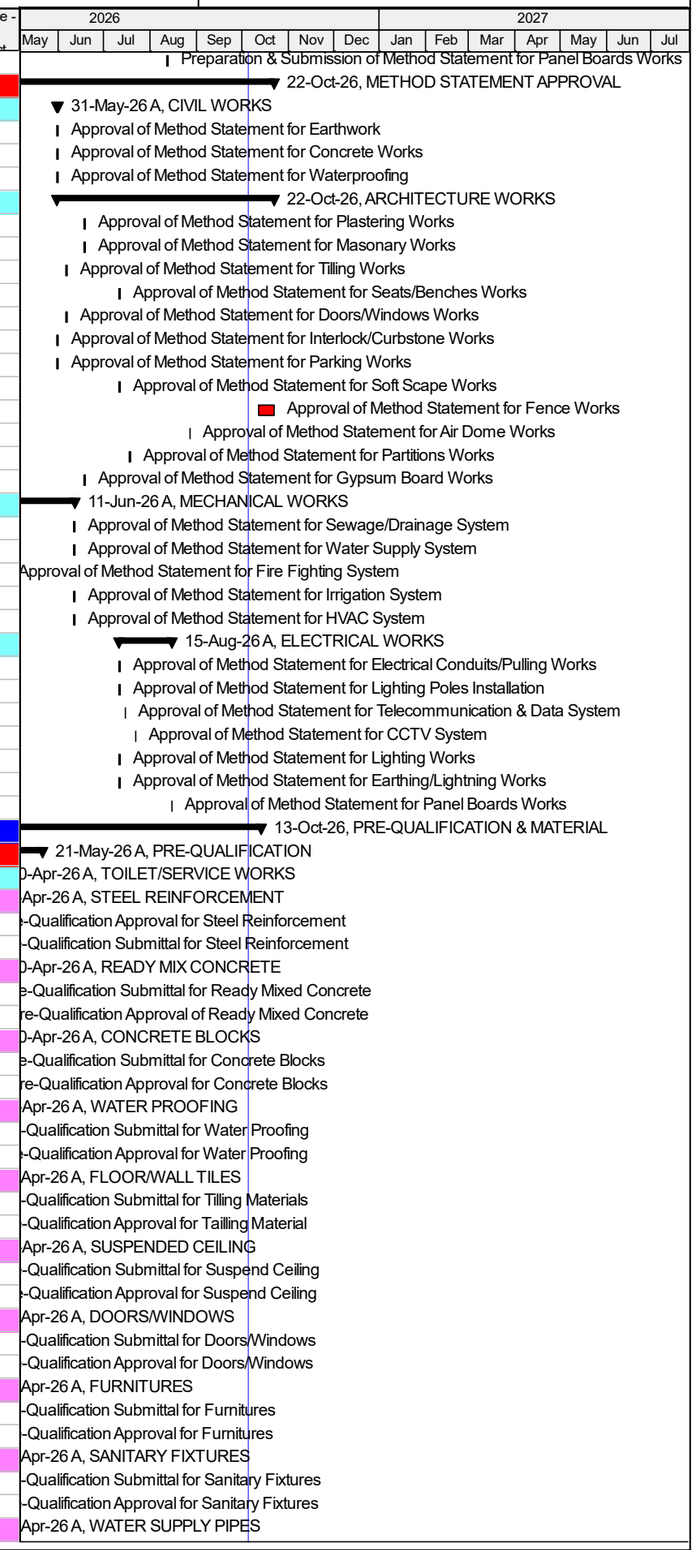


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Pre-Qualification Submittal for Water Supply Pipes	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Water Supply Pipes	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Package AC Units	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Package AC Units	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Air Diffusers/Grills	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Air Diffusers/Grills	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Galvanized Ducts	6	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Galvanized Ducts	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Exhaust Fans	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Exhaust Fans	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LIGHTING FIXTURES		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lighting Fixtures	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lighting Fixtures	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
SWITCHES/SOCKETS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Switches/Sockets	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Switches/Sockets	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EARTHING SYSTEM		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Earthing System	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Earthing System	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Distribution Panels	3	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Distribution Panels	5	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PLAYGROUND WORKS		18	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26 A	20-Apr-26 A	0.00	0.00	0.00	0
PVC MEMBRANE		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for PVC Membrane	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for PVC Membrane	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
STEEL TENSION CABLES		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Steel Tension Cables	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Steel Tension Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EMERGENCY DOORS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Emergency Doors	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Emergency Doors	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PRESSURE UNITS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Pressure Units	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Pressure Units	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR LOCK DOORS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lock Doors	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lock Doors	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
ARTIFICIAL TURF		11	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Artificial TURF	10	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Artificial TURF	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Rubber Granules	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Rubber Granules	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PADEL GLASS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Padel Glass	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Padel Glass	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		14	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Wire Mesh/Steel Sets	12	100%	100%	31-Mar-26	13-Apr-26	31-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Wire Mesh/Steel Sets	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AGGREGATE BASE COURSE		18	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Aggregate Base Course	18	100%	100%	31-Mar-26	20-Apr-26	31-Mar-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Aggregate Base Course	3	100%	100%	18-Apr-26	20-Apr-26	18-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	07-Apr-26	14-Apr-26	07-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Bituminous Base & Wearing	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for the Site	3	100%	100%	12-Apr-26	14-Apr-26	12-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		12	0%	0%	07-Apr-26	20-Apr-26	07-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0

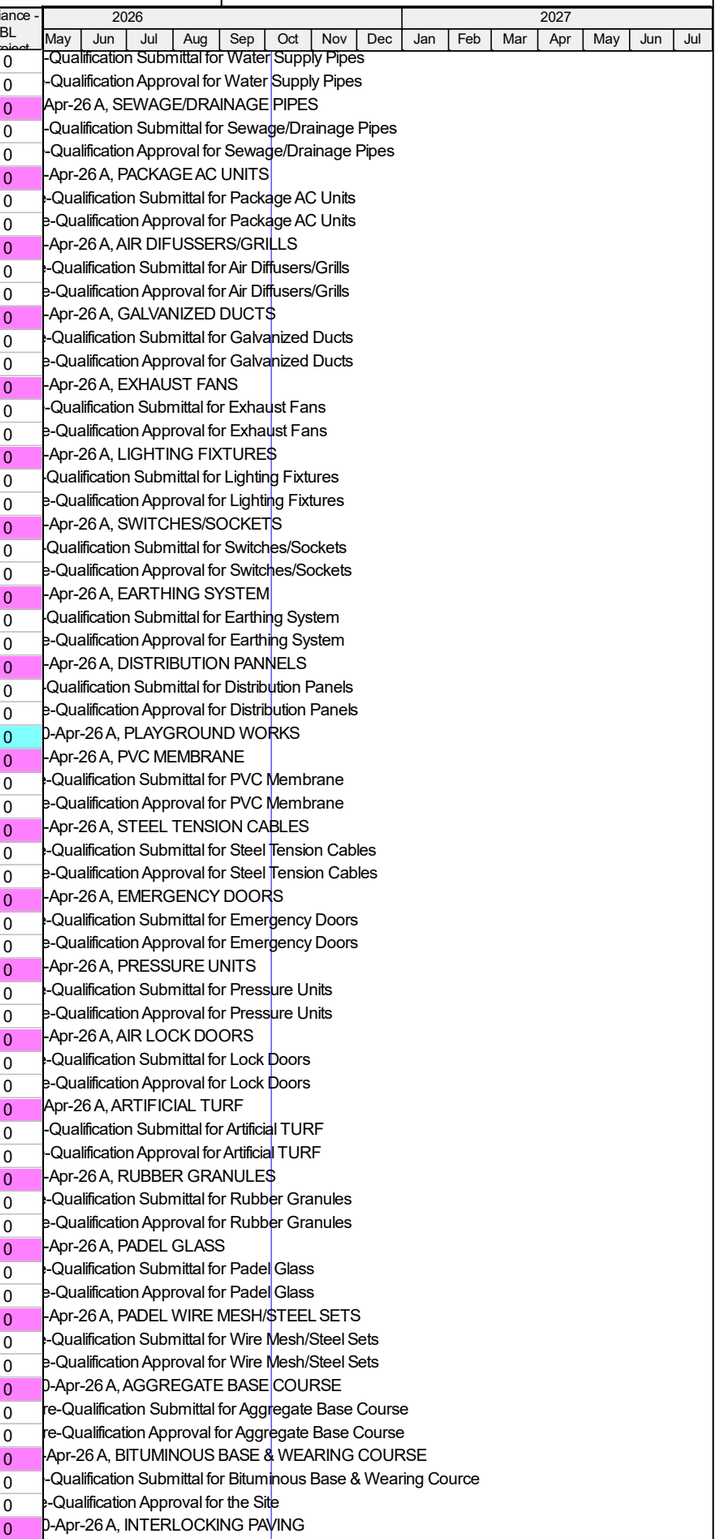

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Pre-Qualification Submittal for Interlocking Block Pavers	8	100%	100%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Interlocking Block Pavers	5	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MARKING PAINT		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Marking Paint	8	100%	100%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Marking Paint	1	100%	100%	12-Apr-26	12-Apr-26	12-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Package AC Units	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Package AC Units	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Air Difussers/Grills	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Air Difussers/Grills	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Galvanized Duct	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Galvanized Duct	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Exhaust Fans	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Exhaust Fans	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
DISTRIBUTION BOARDS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Distribution Boards	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Distribution Boards	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
POWER CABLES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Power Cables	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Power Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LIGHT FIXTURES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Light Fixtures	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Light Fixtures	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
CCTV MATERIALS		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for CCTV	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for CCTV	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
POWER OUTLETS/SWITCHES		11	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Power Outlets/Switches	9	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Power Outlets/Switches	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
LANDSCAPE WORKS		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		15	0%	0%	04-Apr-26	20-Apr-26	04-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Interlocking Block Pavers	11	100%	100%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Interlocking Block Pavers	5	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
CURBSTONE		15	0%	0%	04-Apr-26	20-Apr-26	04-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Curbstone	11	100%	100%	04-Apr-26	15-Apr-26	04-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Curbstone	5	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
PAVEMENT MARKING		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Pavement Markings	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Pavement Markings	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
TRAFFIC SIGNS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Traffic Signs	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Traffic Signs	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
IRRIGATION PIPES/SPRINKLERS		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	20	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AGRICULTURE SOIL		42	0%	0%	04-Apr-26	21-May-26	04-Apr-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Agriculture Soil	20	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Agriculture Soil	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
TRACK SURFACE		8	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Track Surface	3	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Track Surface	5	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
GRASS/TREES		14	0%	0%	04-Apr-26	19-Apr-26	04-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Grass/Trees	10	100%	100%	04-Apr-26	14-Apr-26	04-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Grass/Trees	5	100%	100%	14-Apr-26	19-Apr-26	14-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
CABLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Cables	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Cables	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LIGHT POLES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Submittal for Lighting poles	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Pre-Qualification Approval for Lighting poles	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MATERIAL SUBMITTAL		159	0%	0%	07-Apr-26	18-Jul-26	07-Apr-26 A	13-Oct-26	0.00	0.00	0.00	-74

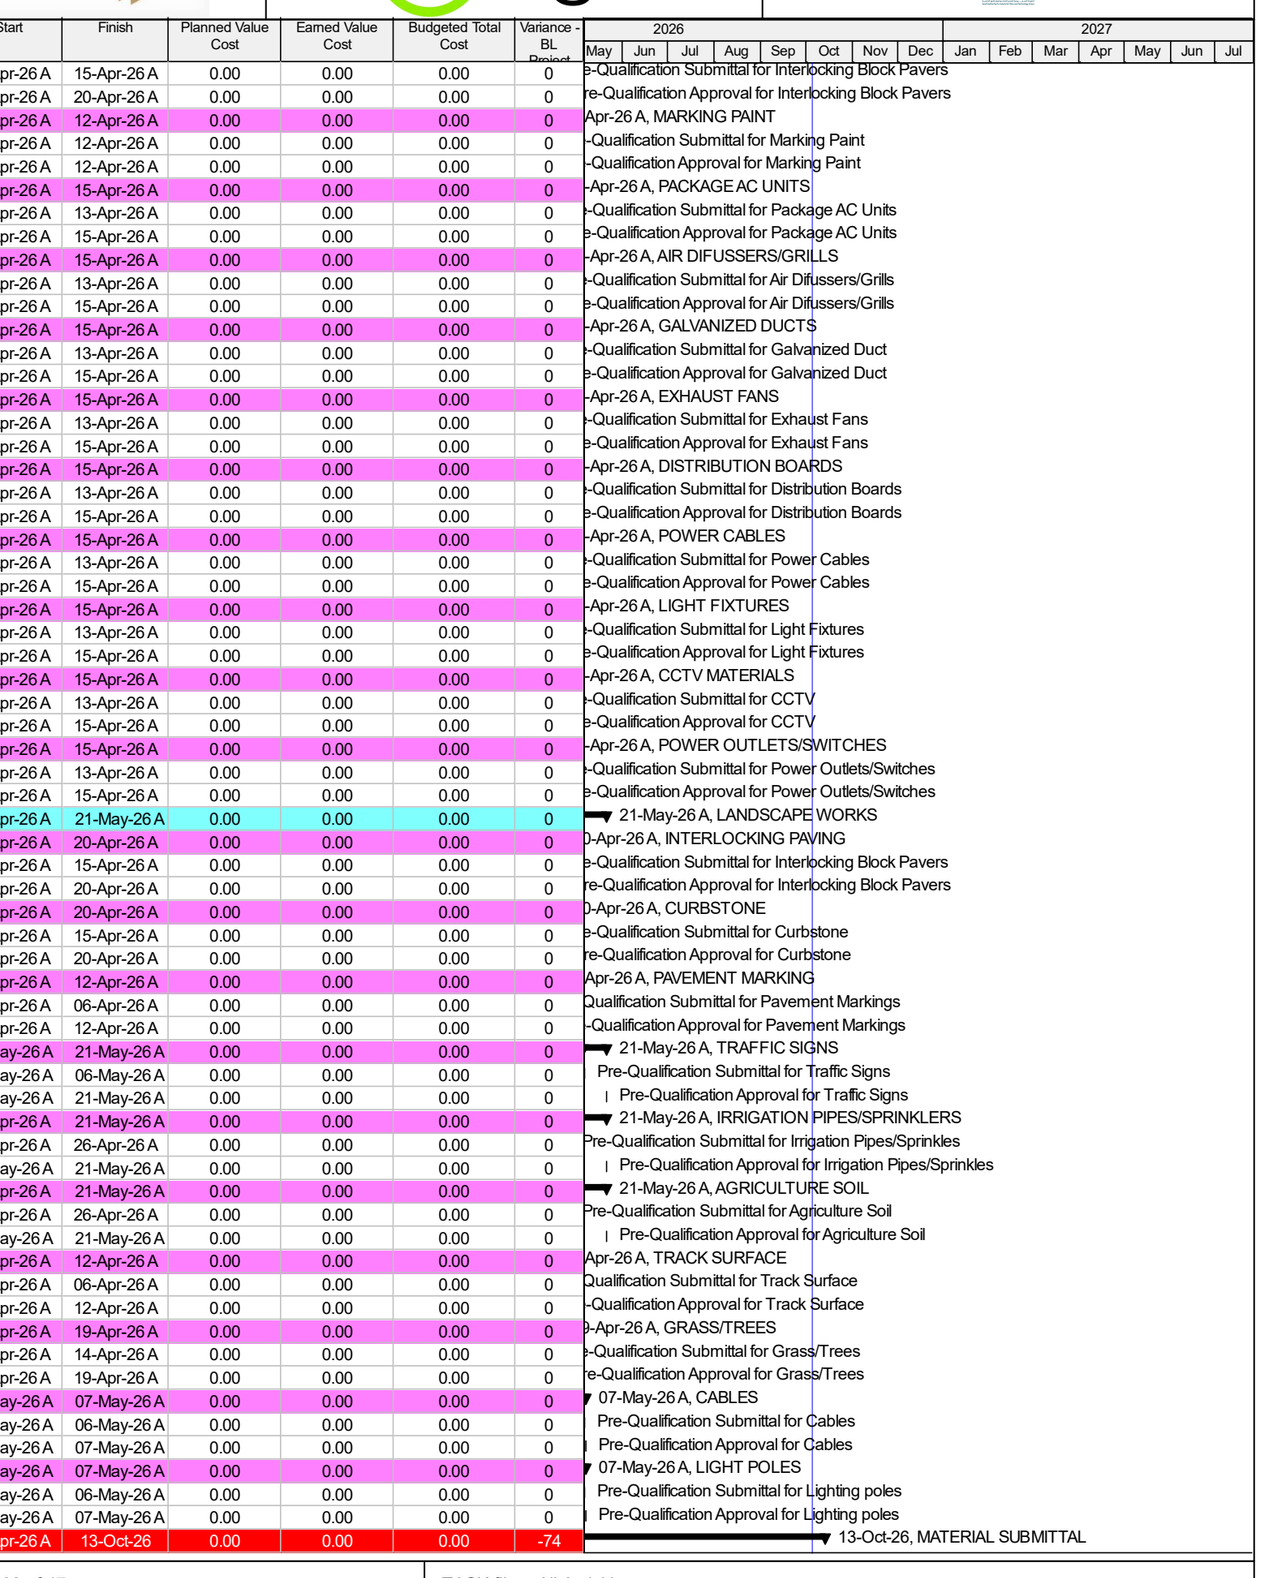


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
TOILET/SERVICE WORKS		155	0%	0%	11-Apr-26	12-Jul-26	11-Apr-26 A	12-Oct-26	0.00	0.00	0.00	-78
STEEL REINFORCEMENT		2	0%	0%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Steel Reinforcement	1	100%	100%	11-Apr-26	11-Apr-26	11-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Steel Reinforcement	2	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	0.00	0.00	0.00	0
READY MIX CONCRETE		10	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Ready Mixed Concrete	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval of Ready Mixed Concrete	7	100%	100%	19-Apr-26	26-Apr-26	19-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		10	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Concrete Blocks	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Concrete Blocks	7	100%	100%	19-Apr-26	26-Apr-26	19-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0
FLOOR/WALL TILES		88	0%	0%	15-Apr-26	12-Jul-26	15-Apr-26 A	22-Jul-26 A	0.00	0.00	0.00	-9
MLTX-02-004-EN	Material Submittal for Tilling Materials	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Tilling Material	7	100%	100%	05-Jul-26	12-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-9
SUSPENDED CEILING		5	0%	0%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Suspend Ceiling	3	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Suspend Ceiling	2	100%	100%	19-Apr-26	20-Apr-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	0
DOORS/WINDOWS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Doors/Windows	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Doors/Windows	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
FURNITURES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Furnitures	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Furnitures	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		14	0%	0%	15-Apr-26	30-Apr-26	15-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Sanitary Fixtures	6	100%	100%	15-Apr-26	21-Apr-26	15-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Sanitary Fixtures	11	100%	100%	19-Apr-26	30-Apr-26	19-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
WATER SUPPLY PIPES		2	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Water Supply Pipes	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Water Supply Pipes	2	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		2	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Sewage/Drainage Pipes	1	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Sewage/Drainage Pipes	2	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	0
PACKAGE AC UNITS		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Package AC Units	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Package AC Units	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		18	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Air Diffusers/Grills	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Air Diffusers/Grills	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		104	0%	0%	13-Jun-26	11-Jul-26	13-Jun-26 A	12-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN	Material Submittal for Galvanized Ducts	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Galvanized Ducts	6	100%	0%	05-Jul-26	11-Jul-26	06-Oct-26	12-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		18	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Exhaust Fans	2	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Exhaust Fans	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
LIGHTING FIXTURES		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Lighting Fixtures	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Lighting Fixtures	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
SWITCHES/SOCKETS		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Switches/Sockets	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Switches/Sockets	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
EARTHING SYSTEM		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Earthing System	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Earthing System	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		8	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Distribution Panels	3	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Distribution Panels	5	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	0.00	0.00	0.00	0
PLAYGROUND WORKS		155	0%	0%	12-Apr-26	12-Jul-26	12-Apr-26 A	13-Oct-26	0.00	0.00	0.00	-79
PVC MEMBRANE		134	0%	0%	06-May-26	12-Jul-26	06-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN	Material Submittal for PVC Membrane	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for PVC Membrane	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
STEEL TENSION CABLES		134	0%	0%	06-May-26	12-Jul-26	06-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN	Material Submittal for Steel Tension Cables	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Steel Tension Cables	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
EMERGENCY DOORS		134	0%	0%	06-May-26	12-Jul-26	06-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EN	Material Submittal for Emergency Doors	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0

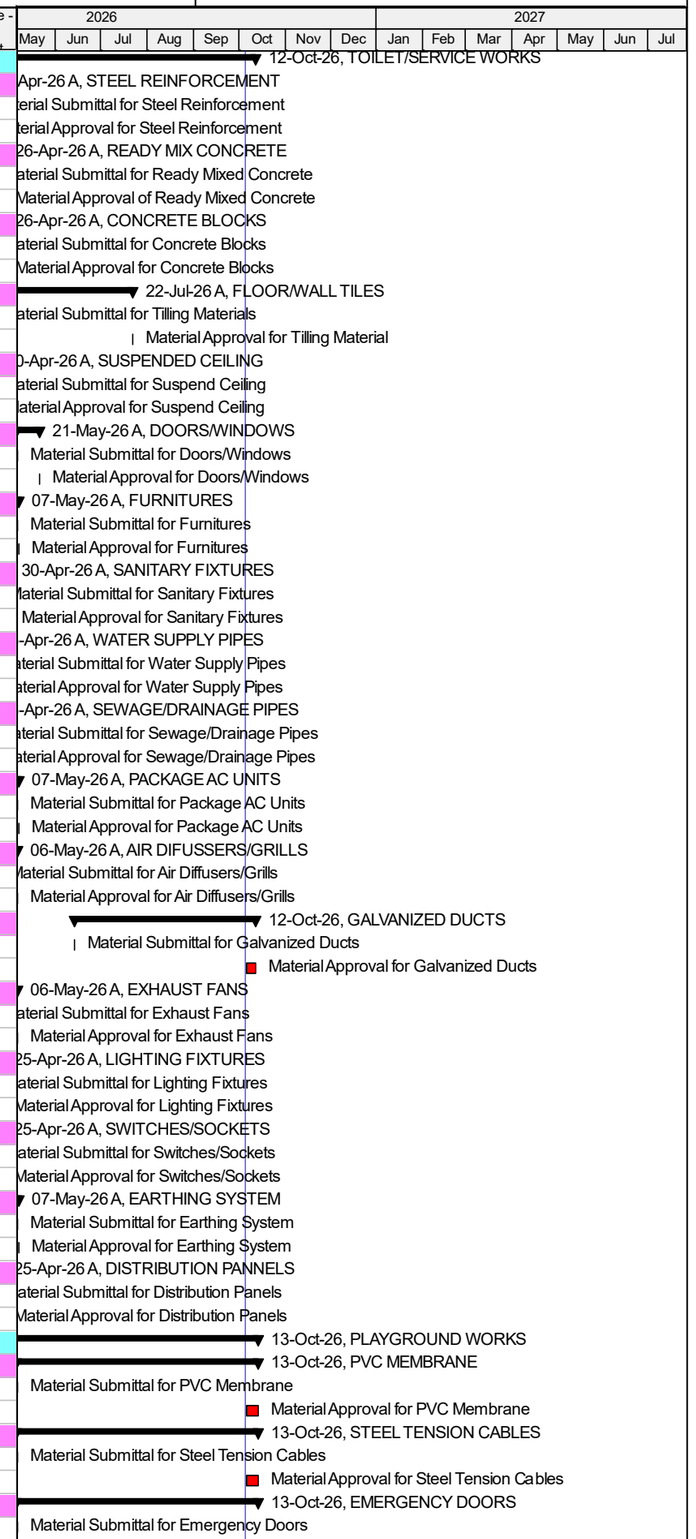

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EM	Material Approval for Emergency Doors	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
PRESSURE UNITS		134	0%	0%	06-May-26	12-Jul-26	06-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Pressure Units	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Pressure Units	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
AIR LOCK DOORS		134	0%	0%	06-May-26	12-Jul-26	06-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Lock Doors	5	100%	100%	06-May-26	11-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Lock Doors	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
ARTIFICIAL TURF		17	0%	0%	12-Apr-26	30-Apr-26	12-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Artificial TURF	15	100%	100%	12-Apr-26	28-Apr-26	12-Apr-26 A	28-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Artificial TURF	3	100%	100%	28-Apr-26	30-Apr-26	28-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Rubber Granules	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Rubber Granules	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
PADEL GLASS		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Padel Glass	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Padel Glass	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		118	0%	0%	25-May-26	12-Jul-26	25-May-26 A	13-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Wire Mesh/Steel Sets	1	100%	100%	25-May-26	25-May-26	25-May-26 A	25-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Wire Mesh/Steel Sets	7	100%	0%	05-Jul-26	12-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-79
PACKAGE AC UNITS		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Package AC Units	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Package AC Units	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
AIR DIFUSSERS/GRILLS		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Air Difussers/Grills	9	100%	100%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Air Difussers/Grills	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
AGGREGATE BASE COURSE		33	0%	0%	21-May-26	01-Jul-26	21-May-26 A	01-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Aggregate Base Course	1	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		2	0%	0%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Bituminous Base & Wearing Cource	2	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for the Site	1	100%	100%	18-Apr-26	18-Apr-26	18-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MARKING PAINT		6	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Marking Paint	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Marking Paint	2	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		104	0%	0%	13-Jun-26	11-Jul-26	13-Jun-26 A	12-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-EM	Material Submittal for Galvanized Duct	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Galvanized Duct	6	100%	0%	05-Jul-26	11-Jul-26	06-Oct-26	12-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		21	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Exhaust Fans	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Exhaust Fans	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION BOARDS		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Distribution Boards	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Distribution Boards	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
POWER CABLES		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Power Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Power Cables	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
LIGHT FIXTURES		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Light Fixtures	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Light Fixtures	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
CCTV MATERIALS		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for CCTV	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for CCTV	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
POWER OUTLETS/SWITCHES		2	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Power Outlets/Switches	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Power Outlets/Switches	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
LANDSCAPE WORKS		98	0%	0%	07-Apr-26	18-Jul-26	07-Apr-26 A	27-Jul-26 A	0.00	0.00	0.00	-8
INTERLOCKING PAVING		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Approval for Interlocking Block Pavers	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
CURBSTONE		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EM	Material Submittal for Curbstone	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0

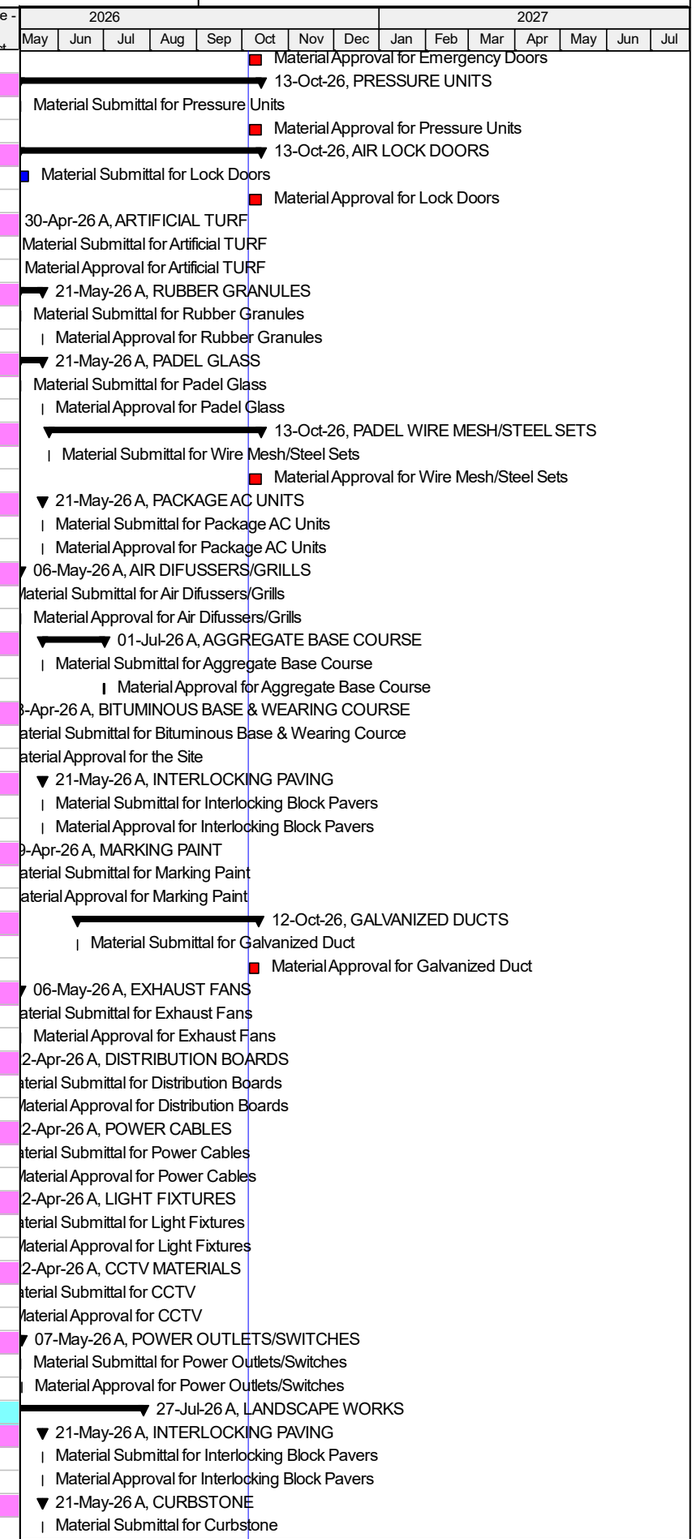


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-EN	Material Approval for Curbstone	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
PAVEMENT MARKING		6	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Pavement Markings	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Pavement Markings	2	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	0
TRAFFIC SIGNS		65	0%	0%	06-May-26	11-Jul-26	06-May-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-004-EN	Material Submittal for Traffic Signs	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Traffic Signs	6	100%	100%	05-Jul-26	11-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
IRRIGATION PIPES/SPRINKLERS		93	0%	0%	13-Apr-26	18-Jul-26	13-Apr-26 A	27-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-004-EN	Material Submittal for Irrigation Pipes/Sprinkles	5	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Irrigation Pipes/Sprinkles	6	100%	100%	12-Jul-26	18-Jul-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-8
AGRICULTURE SOIL		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Agriculture Soil	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Agriculture Soil	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
TRACK SURFACE		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Track Surface	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Track Surface	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
GRASS/TREES		14	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Grass/Trees	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Grass/Trees	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
CABLES		9	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Cables	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Cables	6	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	0.00	0.00	0.00	0
LIGHT POLES		8	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Submittal for Lighting poles	3	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-004-EN	Material Approval for Lighting poles	1	100%	100%	07-Apr-26	07-Apr-26	07-Apr-26 A	07-Apr-26 A	0.00	0.00	0.00	0
PROCUREMENT		234	0%	0%	06-May-26	07-Nov-26	06-May-26 A	07-Feb-27	0.00	0.00	0.00	-79
SHORT LEAD ITEM		214	0%	0%	06-May-26	21-Oct-26	06-May-26 A	14-Jan-27	0.00	0.00	0.00	-73
TOILET/SERVICE WORKS		197	0%	0%	06-May-26	24-Sep-26	06-May-26 A	26-Dec-26	0.00	0.00	0.00	-79
STEEL REINFORCEMENT		13	0%	0%	13-May-26	31-May-26	13-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery of Steel Reinforcement	1	100%	100%	31-May-26	31-May-26	31-May-26 A	31-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-9	PO for Steel Reinforcement	2	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26 A	0.00	0.00	0.00	0
CONCRETE BLOCKS		72	0%	0%	06-May-26	09-Jul-26	06-May-26 A	27-Jul-26 A	0.00	0.00	0.00	-15
MLTX-02-004-PR-1	PO for Concrete Blocks	1	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery of Concrete Blocks	5	100%	100%	05-Jul-26	09-Jul-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-15
FLOOR/WALL TILES		28	0%	0%	19-Jul-26	08-Aug-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-77
MLTX-02-004-PR-1	PO for Tilling Materials	5	100%	0%	19-Jul-26	23-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-67
MLTX-02-004-PR-1	Material Delivery of Tailling Material	13	100%	0%	25-Jul-26	08-Aug-26	24-Oct-26	07-Nov-26	0.00	0.00	0.00	-77
SUSPENDED CEILING		18	0%	0%	05-Jul-26	25-Jul-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Suspend Ceiling	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Delivery of Suspend Ceiling	13	100%	0%	11-Jul-26	25-Jul-26	12-Oct-26	26-Oct-26	0.00	0.00	0.00	-79
DOORS/WINDOWS		98	0%	0%	24-Jun-26	15-Jul-26	24-Jun-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Doors/Windows	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Doors/Windows	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
WATER SUPPLY PIPES		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Water Supply Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Water Supply Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SEWAGE/DRAINAGE PIPES		1	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Sewage/Drainage Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Sewage/Drainage Pipes	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		117	0%	0%	16-Jun-26	29-Jul-26	16-Jun-26 A	31-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Sanitary Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Sanitary Fixtures	12	100%	0%	16-Jul-26	29-Jul-26	18-Oct-26	31-Oct-26	0.00	0.00	0.00	-79
PACKAGE AC UNITS		127	0%	0%	16-Jun-26	10-Aug-26	16-Jun-26 A	11-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Package AC Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Package AC Units	10	100%	0%	30-Jul-26	10-Aug-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-79
AIR DIFUSSERS/GRILLS		137	0%	0%	16-Jun-26	22-Aug-26	16-Jun-26 A	23-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Air Diffusers/Grills	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Air Diffusers/Grills	10	100%	0%	11-Aug-26	22-Aug-26	12-Nov-26	23-Nov-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		108	0%	0%	16-Jun-26	19-Jul-26	16-Jun-26 A	20-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Galvanized Ducts	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Galvanized Ducts	13	100%	0%	05-Jul-26	19-Jul-26	06-Oct-26	20-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		123	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26 A	07-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Exhaust Fans	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	20-Jul-26	05-Aug-26	21-Oct-26	07-Nov-26	0.00	0.00	0.00	-79

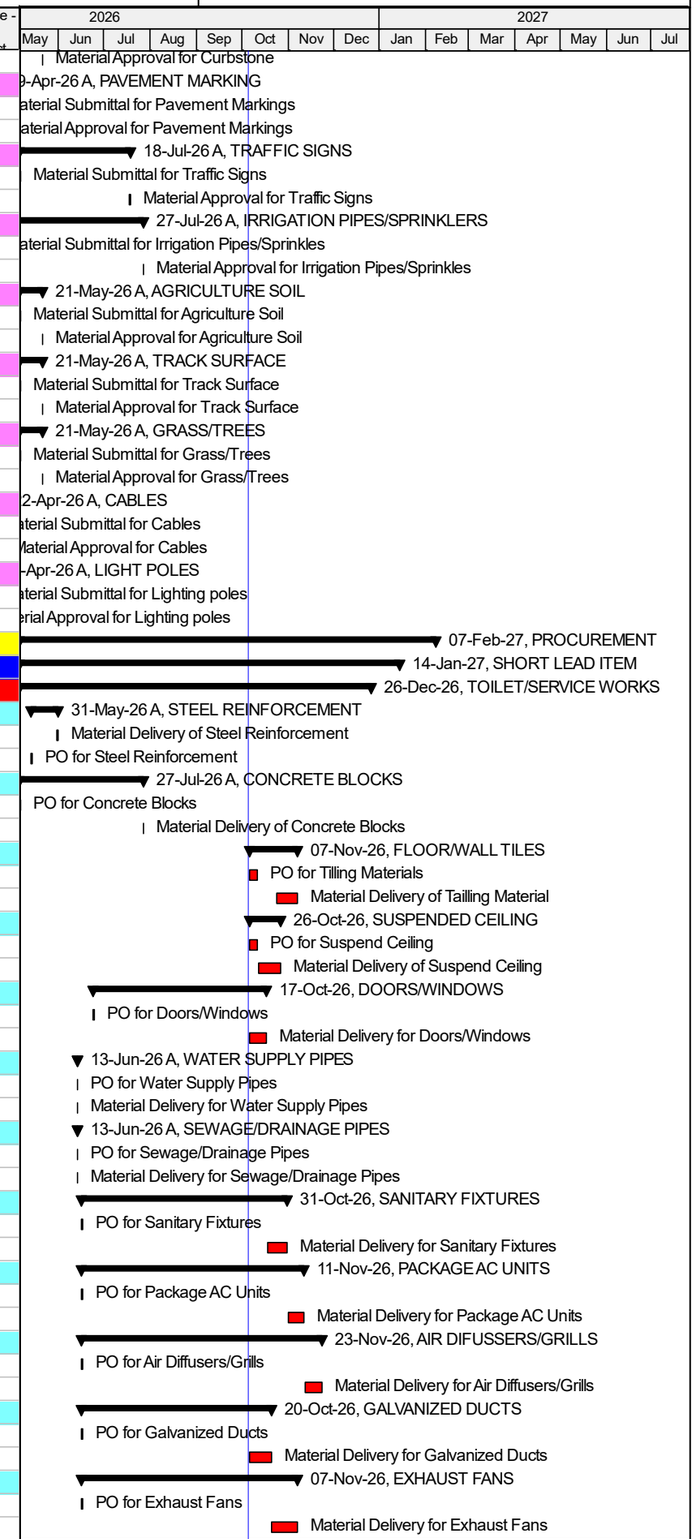

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
LIGHTING FIXTURES		138	0%	0%	16-Jun-26	23-Aug-26	16-Jun-26 A	24-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Lighting Fixtures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Lighting Fixtures	15	100%	0%	06-Aug-26	23-Aug-26	08-Nov-26	24-Nov-26	0.00	0.00	0.00	-79
SWITCHES/SOCKETS		138	0%	0%	24-Jun-26	31-Aug-26	24-Jun-26 A	02-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Switches/Sockets	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	24-Aug-26	31-Aug-26	25-Nov-26	02-Dec-26	0.00	0.00	0.00	-79
EARTHING SYSTEM		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Earthing System	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Earthing System	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		79	0%	0%	05-Jul-26	27-Jul-26	22-Jul-26 A	22-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Distribution Panels	5	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-11
MLTX-02-004-PR-1	Material Delivery for Distribution Panels	15	100%	0%	11-Jul-26	27-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-74
FURNITURES		165	0%	0%	16-Jun-26	24-Sep-26	16-Jun-26 A	26-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Furnitures	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Furnitures	20	100%	0%	01-Sep-26	24-Sep-26	03-Dec-26	26-Dec-26	0.00	0.00	0.00	-79
PLAYGROUND WORKS		213	0%	0%	07-May-26	21-Oct-26	07-May-26 A	14-Jan-27	0.00	0.00	0.00	-73
PVC MEMBRANE		99	0%	0%	16-Jun-26	08-Jul-26	16-Jun-26 A	10-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for PVC Membrane	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for PVC Membrane	4	100%	0%	05-Jul-26	08-Jul-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-79
ARTIFICIAL TURF		111	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26 A	24-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Artificial TURF	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Artificial TURF	12	100%	0%	09-Jul-26	22-Jul-26	11-Oct-26	24-Oct-26	0.00	0.00	0.00	-79
RUBBER GRANULES		123	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26 A	07-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Rubber Granules	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Rubber Granules	12	100%	0%	23-Jul-26	05-Aug-26	25-Oct-26	07-Nov-26	0.00	0.00	0.00	-79
PADEL GLASS		141	0%	0%	16-Jun-26	26-Aug-26	16-Jun-26 A	28-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Padel Glass	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Padel Glass	18	100%	0%	06-Aug-26	26-Aug-26	08-Nov-26	28-Nov-26	0.00	0.00	0.00	-79
PADEL WIRE MESH/STEEL SETS		156	0%	0%	16-Jun-26	13-Sep-26	16-Jun-26 A	15-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Wire Mesh/Steel Sets	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	27-Aug-26	13-Sep-26	29-Nov-26	15-Dec-26	0.00	0.00	0.00	-79
AGGREGATE BASE COURSE		1	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Aggregate Base Course	1	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	0
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	16-Jun-26	23-Jun-26	16-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	PO for Bituminous Base & Wearing Course	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for the Site	1	100%	100%	23-Jun-26	23-Jun-26	23-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	0
INTERLOCKING PAVING		194	0%	0%	07-May-26	21-Sep-26	07-May-26 A	23-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Interlocking Block Pavers	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Interlocking Block Pavers	7	100%	0%	14-Sep-26	21-Sep-26	16-Dec-26	23-Dec-26	0.00	0.00	0.00	-79
MARKING PAINT		75	0%	0%	05-Jul-26	19-Jul-26	18-Jul-26 A	13-Oct-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-1	PO for Marking Paint	6	100%	100%	05-Jul-26	11-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-004-PR-1	Material Delivery for Marking Paint	7	100%	0%	12-Jul-26	19-Jul-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-73
PACKAGE AC UNITS		117	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26 A	31-Oct-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-1	PO for Package AC Units	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Package AC Units	15	100%	0%	20-Jul-26	05-Aug-26	14-Oct-26	31-Oct-26	0.00	0.00	0.00	-73
AIR DIFUSSERS/GRILLS		132	0%	0%	16-Jun-26	23-Aug-26	16-Jun-26 A	17-Nov-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-1	PO for Air Difussers/Grills	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	06-Aug-26	23-Aug-26	01-Nov-26	17-Nov-26	0.00	0.00	0.00	-73
GALVANIZED DUCTS		147	0%	0%	16-Jun-26	09-Sep-26	16-Jun-26 A	05-Dec-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-1	PO for Galvanized Duct	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	24-Aug-26	09-Sep-26	18-Nov-26	05-Dec-26	0.00	0.00	0.00	-73
EXHAUST FANS		162	0%	0%	16-Jun-26	28-Sep-26	16-Jun-26 A	22-Dec-26	0.00	0.00	0.00	-73
MLTX-02-004-PR-1	PO for Exhaust Fans	1	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	06-Dec-26	22-Dec-26	0.00	0.00	0.00	-73
DISTRIBUTION BOARDS		79	0%	0%	05-Jul-26	27-Jul-26	22-Jul-26 A	22-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Distribution Boards	5	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-11
MLTX-02-004-PR-1	Material Delivery for Distribution Boards	15	100%	0%	11-Jul-26	27-Jul-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-74
POWER CABLES		74	0%	0%	28-Jul-26	13-Aug-26	22-Jul-26 A	03-Nov-26	0.00	0.00	0.00	-69
MLTX-02-004-PR-1	PO for Power Cables	5	100%	100%	28-Jul-26	02-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	9
MLTX-02-004-PR-1	Material Delivery for Power Cables	10	100%	0%	03-Aug-26	13-Aug-26	24-Oct-26	03-Nov-26	0.00	0.00	0.00	-69
LIGHT FIXTURES		21	0%	0%	15-Aug-26	07-Sep-26	08-Nov-26	01-Dec-26	0.00	0.00	0.00	-72
MLTX-02-004-PR-1	PO for Light Fixtures	5	100%	0%	15-Aug-26	19-Aug-26	08-Nov-26	12-Nov-26	0.00	0.00	0.00	-72
MLTX-02-004-PR-1	Material Delivery for Light Fixtures	16	100%	0%	20-Aug-26	07-Sep-26	14-Nov-26	01-Dec-26	0.00	0.00	0.00	-72

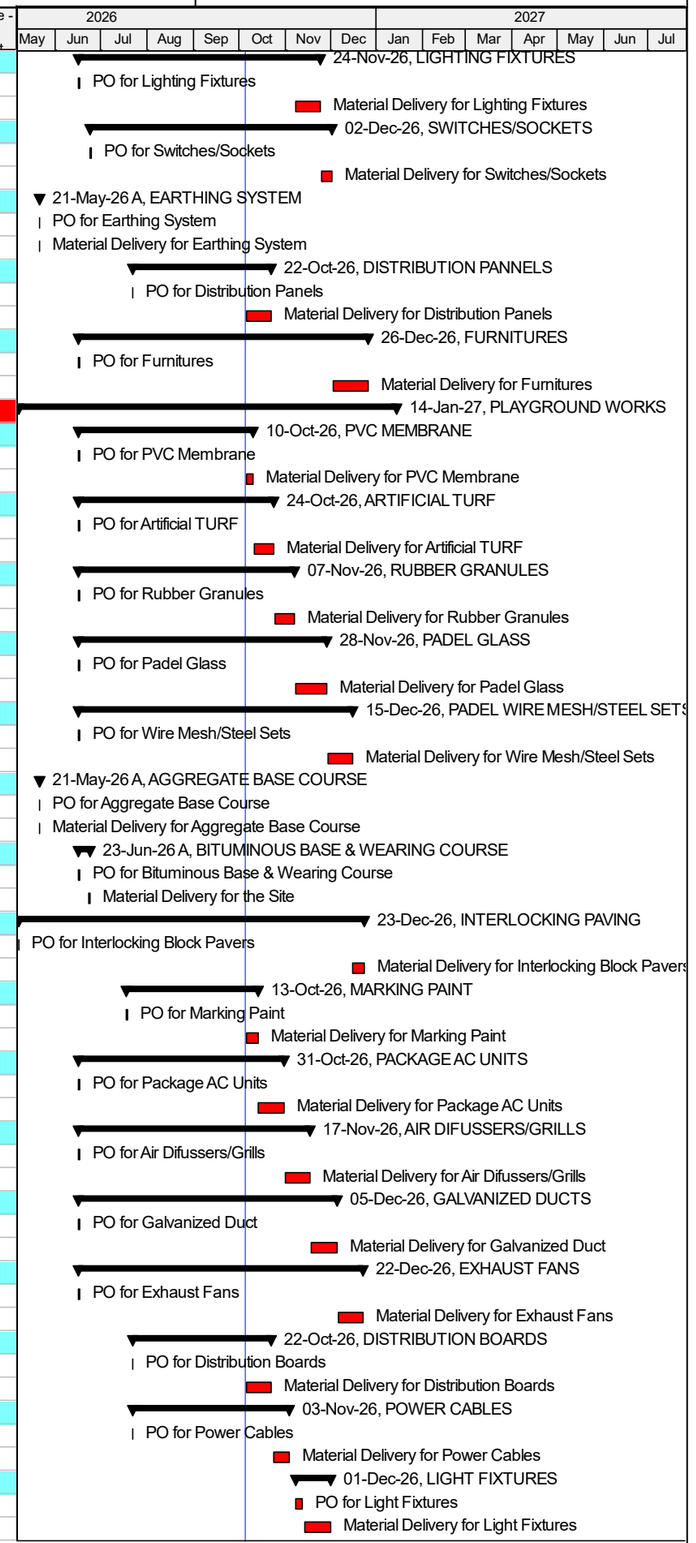

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CCTV MATERIALS		38	0%	0%	08-Sep-26	21-Oct-26	02-Dec-26	14-Jan-27	0.00	0.00	0.00	-73
MLTX-02-004-PR-1	PO for CCTV	10	100%	0%	08-Sep-26	19-Sep-26	02-Dec-26	13-Dec-26	0.00	0.00	0.00	-72
MLTX-02-004-PR-1	Material Delivery for CCTV	20	30%	0%	29-Sep-26	21-Oct-26	23-Dec-26	14-Jan-27	0.00	0.00	0.00	-73
POWER OUTLETS/SWITCHES		21	0%	0%	20-Sep-26	14-Oct-26	14-Dec-26	06-Jan-27	0.00	0.00	0.00	-72
MLTX-02-004-PR-1	PO for Power Outlets/Switches	6	100%	0%	20-Sep-26	27-Sep-26	14-Dec-26	20-Dec-26	0.00	0.00	0.00	-72
MLTX-02-004-PR-1	Material Delivery for Power Outlets/Switches	15	46.67%	0%	28-Sep-26	14-Oct-26	21-Dec-26	06-Jan-27	0.00	0.00	0.00	-72
LANDSCAPE WORKS		204	0%	0%	07-May-26	04-Oct-26	07-May-26 A	04-Jan-27	0.00	0.00	0.00	-79
INTERLOCKING PAVING		136	0%	0%	07-May-26	15-Jul-26	07-May-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Interlocking Block Pavers	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Interlocking Block Pavers	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
CURBSTONE		136	0%	0%	07-May-26	15-Jul-26	07-May-26 A	17-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Curbstone	1	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Curbstone	10	100%	0%	05-Jul-26	15-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-79
PAVEMENT MARKING		78	0%	0%	16-Jul-26	02-Aug-26	18-Jul-26 A	28-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Pavement Markings	5	100%	100%	16-Jul-26	21-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-004-PR-1	Material Delivery for Pavement Markings	10	100%	0%	22-Jul-26	02-Aug-26	18-Oct-26	28-Oct-26	0.00	0.00	0.00	-74
TRAFFIC SIGNS		87	0%	0%	03-Aug-26	18-Aug-26	18-Jul-26 A	08-Nov-26	0.00	0.00	0.00	-69
MLTX-02-004-PR-1	PO for Traffic Signs	5	100%	100%	03-Aug-26	08-Aug-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	18
MLTX-02-004-PR-1	Material Delivery for Traffic Signs	9	100%	0%	09-Aug-26	18-Aug-26	29-Oct-26	08-Nov-26	0.00	0.00	0.00	-69
IRRIGATION PIPES/SPRINKLERS		137	0%	0%	19-Aug-26	04-Oct-26	18-Jul-26 A	04-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	100%	19-Aug-26	24-Aug-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	32
MLTX-02-004-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	0%	26-Sep-26	04-Oct-26	27-Dec-26	04-Jan-27	0.00	0.00	0.00	-79
AGRICULTURE SOIL		80	0%	0%	05-Jul-26	23-Jul-26	18-Jul-26 A	19-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Agriculture Soil	5	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-7
MLTX-02-004-PR-1	Material Delivery for Agriculture Soil	12	100%	0%	11-Jul-26	23-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
TRACK SURFACE		110	0%	0%	24-Jun-26	04-Aug-26	24-Jun-26 A	31-Oct-26	0.00	0.00	0.00	-74
MLTX-02-004-PR-1	PO for Track Surface	1	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Track Surface	10	100%	0%	25-Jul-26	04-Aug-26	20-Oct-26	31-Oct-26	0.00	0.00	0.00	-74
GRASS/TREES		83	0%	0%	05-Aug-26	27-Aug-26	18-Jul-26 A	17-Nov-26	0.00	0.00	0.00	-69
MLTX-02-004-PR-1	PO for Grass/Trees	5	100%	100%	05-Aug-26	10-Aug-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	20
MLTX-02-004-PR-1	Material Delivery for Grass/Trees	15	100%	0%	11-Aug-26	27-Aug-26	01-Nov-26	17-Nov-26	0.00	0.00	0.00	-69
CABLES		116	0%	0%	22-Jul-26	14-Sep-26	22-Jul-26 A	05-Dec-26	0.00	0.00	0.00	-69
MLTX-02-004-PR-1	PO for Cables	5	100%	100%	22-Jul-26	27-Jul-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	4
MLTX-02-004-PR-1	Material Delivery for Cables	15	100%	0%	29-Aug-26	14-Sep-26	18-Nov-26	05-Dec-26	0.00	0.00	0.00	-69
LONG LEAD ITEM		205	0%	0%	13-Jun-26	07-Nov-26	13-Jun-26 A	07-Feb-27	0.00	0.00	0.00	-79
PLAYGROUND WORKS		175	0%	0%	13-Jun-26	06-Oct-26	13-Jun-26 A	03-Jan-27	0.00	0.00	0.00	-76
STEEL TENSION CABLES		152	0%	0%	13-Jun-26	05-Sep-26	13-Jun-26 A	07-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Steel Tension Cables	1	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	25-Jul-26	27-Aug-26	26-Oct-26	29-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Fabrication for Steel Tension Cables	10	100%	0%	13-Jul-26	23-Jul-26	14-Oct-26	25-Oct-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	7	100%	0%	29-Aug-26	05-Sep-26	30-Nov-26	07-Dec-26	0.00	0.00	0.00	-79
EMERGENCY DOORS		122	0%	0%	28-Jul-26	10-Sep-26	18-Jul-26 A	13-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Emergency Doors	5	100%	100%	28-Jul-26	02-Aug-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	13
MLTX-02-004-PR-1	Material Delivery for Emergency Doors	15	100%	0%	15-Aug-26	31-Aug-26	18-Oct-26	03-Nov-26	0.00	0.00	0.00	-54
MLTX-02-004-PR-1	Material Fabrication for Emergency Doors	10	100%	0%	03-Aug-26	13-Aug-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-54
MLTX-02-004-PR-1	Staging time	5	100%	0%	06-Sep-26	10-Sep-26	08-Dec-26	13-Dec-26	0.00	0.00	0.00	-79
PRESSURE UNITS		60	0%	0%	28-Jul-26	06-Oct-26	06-Oct-26	14-Dec-26	0.00	0.00	0.00	-59
MLTX-02-004-PR-1	PO for Pressure Units	10	100%	0%	28-Jul-26	08-Aug-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-59
MLTX-02-004-PR-1	Material Delivery for Pressure Units	25	100%	0%	01-Sep-26	30-Sep-26	10-Nov-26	08-Dec-26	0.00	0.00	0.00	-59
MLTX-02-004-PR-1	Material Fabrication for Pressure Units	20	100%	0%	09-Aug-26	31-Aug-26	18-Oct-26	09-Nov-26	0.00	0.00	0.00	-59
MLTX-02-004-PR-1	Staging time	5	80%	0%	01-Oct-26	06-Oct-26	09-Dec-26	14-Dec-26	0.00	0.00	0.00	-59
AIR LOCK DOORS		60	0%	0%	25-Jul-26	03-Oct-26	26-Oct-26	03-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	PO for Lock Doors	10	100%	0%	25-Jul-26	04-Aug-26	26-Oct-26	05-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Delivery for Lock Doors	25	100%	0%	29-Aug-26	27-Sep-26	30-Nov-26	28-Dec-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Material Fabrication for Lock Doors	20	100%	0%	05-Aug-26	27-Aug-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	5	100%	0%	28-Sep-26	03-Oct-26	29-Dec-26	03-Jan-27	0.00	0.00	0.00	-79
LANDSCAPE WORKS		200	0%	0%	18-Jun-26	07-Nov-26	18-Jun-26 A	07-Feb-27	0.00	0.00	0.00	-79
LIGHT POLES		200	0%	0%	18-Jun-26	07-Nov-26	18-Jun-26 A	07-Feb-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-1	Staging time	5	0%	0%	02-Nov-26	07-Nov-26	02-Feb-27	07-Feb-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	PO for Lighting poles	1	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	0
MLTX-02-004-PR-9	Material Fabrication for Lighting poles	30	100%	0%	29-Aug-26	03-Oct-26	30-Nov-26	03-Jan-27	0.00	0.00	0.00	-79
MLTX-02-004-PR-9	Material Delivery for Lighting poles	25	8%	0%	04-Oct-26	01-Nov-26	04-Jan-27	01-Feb-27	0.00	0.00	0.00	-79
CONSTRUCTION PHASE		304	29.73%	21.42%	02-May-26	25-Jan-27	02-May-26 A	29-Apr-27	3,174,958.02	2,287,918.34	10,680,071.52	-77
SITE WORKS		304	23.51%	19.72%	02-May-26	25-Jan-27	02-May-26 A	29-Apr-27	2,210,322.50	1,853,224.67	9,399,910.39	-77

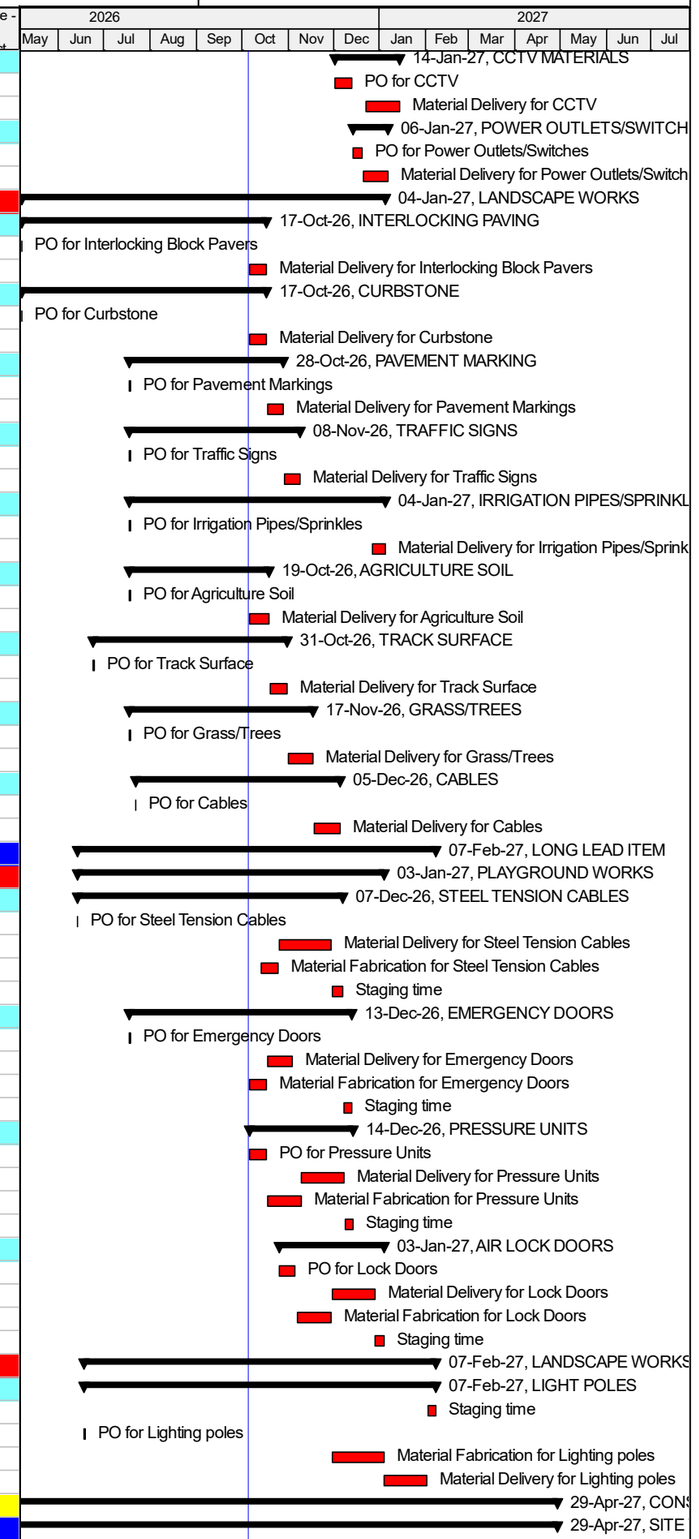

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
EARTH WORKS		109	100%	99.2%	02-May-26	23-Jul-26	02-May-26 A	15-Oct-26	542,446.88	538,095.94	542,446.88	-71
MLTX-02-004-CN-118	Excavation (in all types of soil) including Compaction	8	100%	100%	02-May-26	11-May-26	02-May-26 A	11-May-26 A	133,098.00	133,098.00	133,098.00	0
MLTX-02-004-CN-118	Excavation (in all types of soil) including Compaction	12	100%	100%	07-May-26	21-May-26	07-May-26 A	21-May-26 A	32,321.25	32,321.25	32,321.25	0
MLTX-02-004-CN-119	Excavation (in all types of soil) including Compaction	14	100%	100%	06-May-26	23-May-26	06-May-26 A	23-May-26 A	202,990.13	202,990.13	202,990.13	0
MLTX-02-004-CN-119	Backfilling on Layers (Selected Soil) including Compaction	32	100%	100%	25-May-26	04-Jul-26	25-May-26 A	04-Jul-26 A	22,181.25	22,181.25	22,181.25	0
MLTX-02-004-CN-119	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	15-Jul-26	23-Jul-26	05-Jul-26 A	22-Aug-26 A	56,647.50	56,647.50	56,647.50	-25
MLTX-02-004-CN-119	Backfilling on Layers (Selected Soil) including Compaction	14	100%	100%	25-May-26	14-Jun-26	25-May-26 A	14-Jun-26 A	8,190.00	8,190.00	8,190.00	0
MLTX-02-004-CN-119	Backfilling on Layers (Selected Soil) including Compaction	9	100%	95%	05-Jul-26	14-Jul-26	29-Aug-26 A	15-Oct-26	87,018.75	82,667.81	87,018.75	-79
LANDSCAPE WORKS		208	19.04%	15.01%	05-Jul-26	25-Jan-27	15-Jul-26 A	29-Apr-27	1,667,875.63	1,315,128.73	8,759,963.03	-77
PLAYGROUND AREA		165	35.89%	0%	05-Jul-26	16-Jan-27	06-Oct-26	20-Apr-27	434,500.63	0.00	1,210,722.50	-77
FOOTBALL PLAYGROUND		122	61.11%	0%	05-Jul-26	07-Dec-26	17-Oct-26	08-Mar-27	210,925.00	0.00	345,150.00	-77
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Football Playground)	17	100%	0%	05-Jul-26	23-Jul-26	17-Oct-26	04-Nov-26	57,525.00	0.00	57,525.00	-88
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Football	25	100%	0%	25-Jul-26	22-Aug-26	05-Nov-26	03-Dec-26	57,525.00	0.00	57,525.00	-88
MLTX-02-004-CI	Finishing and Surface Finish Works (Football Playground)	30	66.67%	0%	12-Sep-26	17-Oct-26	14-Dec-26	17-Jan-27	95,875.00	0.00	143,812.50	-79
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	8	0%	0%	29-Nov-26	07-Dec-26	28-Feb-27	08-Mar-27	0.00	0.00	71,906.25	-77
MLTX-02-004-CI	Surface Marking and Painting (Football Playground)	8	0%	0%	29-Nov-26	07-Dec-26	28-Feb-27	08-Mar-27	0.00	0.00	14,381.25	-77
PADEL PLAYGROUND		118	55%	0%	25-Jul-26	22-Dec-26	05-Nov-26	27-Mar-27	117,975.00	0.00	214,500.00	-77
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Padel Playground)	25	100%	0%	25-Jul-26	22-Aug-26	05-Nov-26	03-Dec-26	75,075.00	0.00	75,075.00	-88
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Padel	20	100%	0%	23-Aug-26	14-Sep-26	05-Dec-26	27-Dec-26	42,900.00	0.00	42,900.00	-88
MLTX-02-004-CI	Finishing and Surface Finish Works (Padel Playground)	30	0%	0%	18-Oct-26	21-Nov-26	18-Jan-27	21-Feb-27	0.00	0.00	53,625.00	-79
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	13	0%	0%	29-Nov-26	13-Dec-26	28-Feb-27	17-Mar-27	0.00	0.00	32,175.00	-77
MLTX-02-004-CI	Surface Marking and Painting (Padel Playground)	8	0%	0%	14-Dec-26	22-Dec-26	18-Mar-27	27-Mar-27	0.00	0.00	10,725.00	-77
BASKETBALL PLAYGROUND		93	15.67%	0%	23-Aug-26	22-Dec-26	05-Dec-26	27-Mar-27	48,880.00	0.00	312,000.00	-77
MLTX-02-004-CI	Preparation and Proofing for Subgrade (Padel Playground)	20	100%	0%	23-Aug-26	14-Sep-26	05-Dec-26	27-Dec-26	31,200.00	0.00	31,200.00	-88
MLTX-02-004-CI	Backfilling and Compaction of Base Layers (Basketball	30	56.67%	0%	15-Sep-26	20-Oct-26	28-Dec-26	31-Jan-27	17,680.00	0.00	31,200.00	-88
MLTX-02-004-CI	Finishing and Surface Finish Works (Basketball Playground)	30	0%	0%	21-Oct-26	24-Nov-26	01-Feb-27	08-Mar-27	0.00	0.00	156,000.00	-88
MLTX-02-004-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	08-Dec-26	19-Dec-26	09-Mar-27	23-Mar-27	0.00	0.00	78,000.00	-77
MLTX-02-004-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	14-Dec-26	22-Dec-26	18-Mar-27	27-Mar-27	0.00	0.00	15,600.00	-77
PADEL FENCE		21	0%	0%	23-Dec-26	16-Jan-27	28-Mar-27	20-Apr-27	0.00	0.00	82,875.00	-77
MLTX-02-004-CI	Excavation for Fence	3	0%	0%	23-Dec-26	26-Dec-26	28-Mar-27	30-Mar-27	0.00	0.00	8,287.50	-77
MLTX-02-004-CI	Concrete Foundation for Fence including Posts Fixation	4	0%	0%	27-Dec-26	30-Dec-26	31-Mar-27	04-Apr-27	0.00	0.00	16,575.00	-77
MLTX-02-004-CI	Backfilling and Reinstatement for Concrete Foundation	4	0%	0%	31-Dec-26	04-Jan-27	05-Apr-27	08-Apr-27	0.00	0.00	4,143.75	-77
MLTX-02-004-CI	Tempered Glass Fenc Installation and Fixation	5	0%	0%	05-Jan-27	10-Jan-27	10-Apr-27	14-Apr-27	0.00	0.00	33,150.00	-77
MLTX-02-004-CI	Chain Link Fence Installation and Fixation	5	0%	0%	05-Jan-27	10-Jan-27	10-Apr-27	14-Apr-27	0.00	0.00	16,575.00	-77
MLTX-02-004-CI	Install of Fence Gates	5	0%	0%	11-Jan-27	16-Jan-27	15-Apr-27	20-Apr-27	0.00	0.00	4,143.75	-77
CURBSTOEN/INTERLOCK		83	22.14%	0%	27-Sep-26	24-Oct-26	06-Oct-26	10-Jan-27	56,720.63	0.00	256,197.50	-67
MLTX-02-004-CI	Interlock Installation (Grey Scale) for LandScape (Including	15	0%	0%	07-Oct-26	24-Oct-26	24-Dec-26	10-Jan-27	0.00	0.00	185,900.00	-67
MLTX-02-004-CI	Concrete Works Under Curbstone	5	100%	0%	27-Sep-26	01-Oct-26	06-Oct-26	11-Oct-26	15,990.00	0.00	15,990.00	-8
MLTX-02-004-CI	Curbstone Installation	4	75%	0%	03-Oct-26	06-Oct-26	14-Dec-26	17-Dec-26	40,730.63	0.00	54,307.50	-62
AIR DOME		182	22%	20.5%	15-Sep-26	26-Dec-26	15-Jul-26 A	30-Mar-27	1,233,375.00	1,149,281.25	5,606,250.00	-77
CIVIL WORKS		147	52.38%	48.81%	15-Sep-26	15-Nov-26	15-Jul-26 A	13-Feb-27	1,233,375.00	1,149,281.25	2,354,625.00	-77
MLTX-02-004-CI	Excavation for Foundation & Playground Area (Air Dome)	5	100%	100%	15-Sep-26	20-Sep-26	15-Jul-26 A	15-Aug-26 A	280,312.50	280,312.50	280,312.50	32
MLTX-02-004-CI	Concrete Works for Foundations including Anchor Bolts (Air	4	100%	100%	21-Sep-26	26-Sep-26	29-Jul-26 A	22-Sep-26 A	392,437.50	392,437.50	392,437.50	2
MLTX-02-004-CI	Cable System Installation (Air Dome)	3	100%	85%	27-Sep-26	29-Sep-26	24-Sep-26 A	08-Oct-26	560,625.00	476,531.25	560,625.00	-8
MLTX-02-004-CI	Install of Membrane Covering System (Air Dome)	4	0%	0%	08-Nov-26	11-Nov-26	06-Feb-27	09-Feb-27	0.00	0.00	560,625.00	-77
MLTX-02-004-CI	Thermal Insulation Works (Air Dome)	3	0%	0%	12-Nov-26	15-Nov-26	10-Feb-27	13-Feb-27	0.00	0.00	560,625.00	-77
MECHANICAL WORKS		13	0%	0%	16-Nov-26	30-Nov-26	14-Feb-27	01-Mar-27	0.00	0.00	1,121,250.00	-77
MLTX-02-004-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	16-Nov-26	26-Nov-26	14-Feb-27	25-Feb-27	0.00	0.00	280,312.50	-77
MLTX-02-004-CI	Air Units Installation (Air Dome)	13	0%	0%	16-Nov-26	30-Nov-26	14-Feb-27	01-Mar-27	0.00	0.00	448,500.00	-77
MLTX-02-004-CI	Exhaust Fans and Ducts Installation (Air Dome)	11	0%	0%	16-Nov-26	28-Nov-26	14-Feb-27	27-Feb-27	0.00	0.00	392,437.50	-77
ELECTRICAL WORKS		22	0%	0%	01-Dec-26	26-Dec-26	02-Mar-27	30-Mar-27	0.00	0.00	1,681,875.00	-77
MLTX-02-004-CI	Light Fixture Works (Air Dome)	20	0%	0%	01-Dec-26	23-Dec-26	02-Mar-27	28-Mar-27	0.00	0.00	280,312.50	-77
MLTX-02-004-CI	Distribution Board and Electrical Works (Air Dome)	18	0%	0%	01-Dec-26	21-Dec-26	02-Mar-27	25-Mar-27	0.00	0.00	280,312.50	-77
MLTX-02-004-CI	External Electrical Connection Works (Air Dome)	20	0%	0%	01-Dec-26	23-Dec-26	02-Mar-27	28-Mar-27	0.00	0.00	280,312.50	-77
MLTX-02-004-CI	Emergency Generator Installation (Air Dome)	20	0%	0%	01-Dec-26	23-Dec-26	02-Mar-27	28-Mar-27	0.00	0.00	560,625.00	-77
MLTX-02-004-CI	Control System Installation (Air Dome)	22	0%	0%	01-Dec-26	26-Dec-26	02-Mar-27	30-Mar-27	0.00	0.00	280,312.50	-77
FINISHES WORKS		25	0%	0%	19-Nov-26	17-Dec-26	17-Feb-27	22-Mar-27	0.00	0.00	448,500.00	-77
MLTX-02-004-CI	Doors Installation Including Emergency, Entrance doors (Air	10	0%	0%	19-Nov-26	30-Nov-26	17-Feb-27	01-Mar-27	0.00	0.00	224,250.00	-77
MLTX-02-004-CI	Logo and Signs Installation (Air Dome)	15	0%	0%	01-Dec-26	17-Dec-26	02-Mar-27	22-Mar-27	0.00	0.00	224,250.00	-77
IRRIGATION NETWORK		22	0%	0%	07-Oct-26	01-Nov-26	05-Jan-27	30-Jan-27	0.00	0.00	267,670.00	-77
MLTX-02-004-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	5	0%	0%	07-Oct-26	12-Oct-26	05-Jan-27	10-Jan-27	0.00	0.00	80,795.00	-77
MLTX-02-004-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	5	0%	0%	13-Oct-26	18-Oct-26	11-Jan-27	16-Jan-27	0.00	0.00	94,250.00	-77
MLTX-02-004-CN-1	Installing of Valves and fittings for Irrigation Network	4	0%	0%	19-Oct-26	22-Oct-26	17-Jan-27	20-Jan-27	0.00	0.00	46,475.00	-77
MLTX-02-004-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	29-Oct-26	01-Nov-26	27-Jan-27	30-Jan-27	0.00	0.00	46,150.00	-77

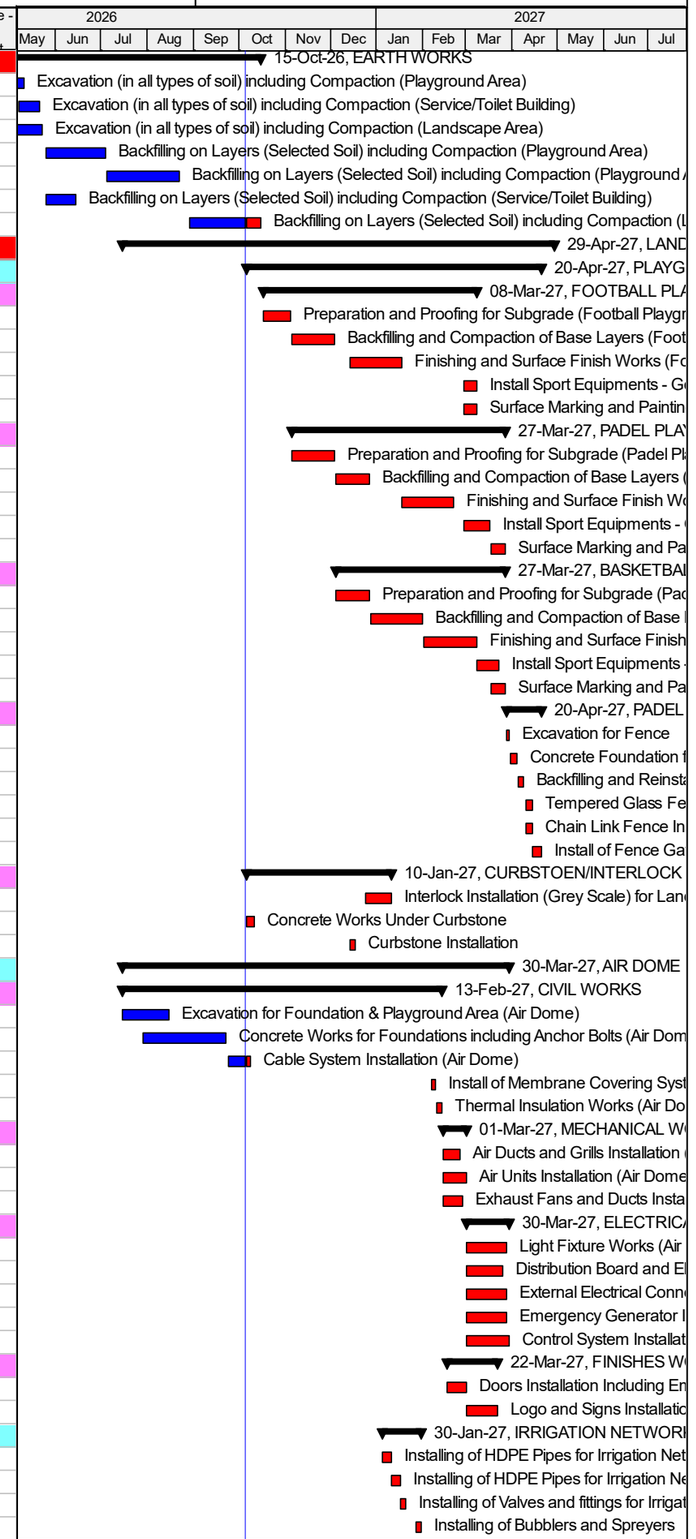

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
NATURAL GROUND		5	0%	0%	24-Oct-26	28-Oct-26	21-Jan-27	26-Jan-27	0.00	0.00	80,291.25	-77
MLTX-02-004-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	0%	24-Oct-26	28-Oct-26	21-Jan-27	26-Jan-27	0.00	0.00	80,291.25	-77
PLANTING		28	0%	0%	02-Nov-26	03-Dec-26	31-Jan-27	04-Mar-27	0.00	0.00	573,462.50	-77
MLTX-02-004-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	5	0%	0%	02-Nov-26	07-Nov-26	31-Jan-27	04-Feb-27	0.00	0.00	186,420.00	-77
MLTX-02-004-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	01-Dec-26	03-Dec-26	02-Mar-27	04-Mar-27	0.00	0.00	175,175.00	-77
MLTX-02-004-CN-1	Placement and Fixation of Trees	3	0%	0%	28-Nov-26	30-Nov-26	27-Feb-27	01-Mar-27	0.00	0.00	211,867.50	-77
WALKING/BIKE PATHS		8	0%	60%	05-Dec-26	13-Dec-26	19-Aug-26 A	14-Oct-26	0.00	165,847.48	276,412.47	51
MLTX-02-004-CN-1	Bike Path Preparation and Installation Works	8	0%	60%	05-Dec-26	13-Dec-26	19-Aug-26 A	14-Oct-26	0.00	85,227.17	142,045.28	51
MLTX-02-004-CN-1	Walking Path Preparation and Installation Works	8	0%	60%	05-Dec-26	13-Dec-26	19-Aug-26 A	14-Oct-26	0.00	80,620.31	134,367.19	51
GENERAL/FURNITURE		165	0%	0%	07-Oct-26	25-Jan-27	15-Oct-26	29-Apr-27	0.00	0.00	745,154.31	-77
MLTX-02-004-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	14-Dec-26	22-Dec-26	15-Oct-26	24-Oct-26	0.00	0.00	14,040.00	51
MLTX-02-004-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	06-Jan-27	13-Jan-27	11-Apr-27	18-Apr-27	0.00	0.00	9,750.00	-77
MLTX-02-004-CN-1	Fixation and Installation of Steel Frame for Benches	12	0%	0%	14-Dec-26	27-Dec-26	15-Oct-26	28-Oct-26	0.00	0.00	17,276.03	51
MLTX-02-004-CN-1	Fixation and Installation of Benches	8	0%	0%	28-Dec-26	05-Jan-27	29-Oct-26	07-Nov-26	0.00	0.00	40,310.73	51
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Seats	8	0%	0%	28-Dec-26	05-Jan-27	29-Oct-26	07-Nov-26	0.00	0.00	43,680.00	51
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	28-Dec-26	05-Jan-27	29-Oct-26	07-Nov-26	0.00	0.00	17,160.00	51
MLTX-02-004-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	17-Jan-27	25-Jan-27	21-Apr-27	29-Apr-27	0.00	0.00	14,625.00	-77
MLTX-02-004-CN-1	Preleminary Works for Site Light Poles Including Cable and	14	0%	0%	07-Oct-26	22-Oct-26	19-Dec-26	03-Jan-27	0.00	0.00	113,197.50	-62
MLTX-02-004-CN-1	Installing of Site Light Poles	11	0%	0%	24-Dec-26	05-Jan-27	29-Mar-27	10-Apr-27	0.00	0.00	475,115.06	-77
PARKING		12	0%	0%	23-Dec-26	05-Jan-27	25-Oct-26	07-Nov-26	0.00	0.00	97,500.48	51
MLTX-02-004-CN-119	Interlock Installation (8 Cm) for Parking Area (Including	7	0%	0%	29-Dec-26	05-Jan-27	31-Oct-26	07-Nov-26	0.00	0.00	68,249.02	51
MLTX-02-004-CN-119	Site Preparation & Compaction Under Interlock for Parking	5	0%	0%	23-Dec-26	28-Dec-26	25-Oct-26	29-Oct-26	0.00	0.00	29,251.46	51
TOILET/SERVICE BUILDING		193	75.35%	33.96%	14-Jun-26	16-Nov-26	14-Jun-26 A	25-Jan-27	964,635.52	434,693.68	1,280,161.13	-60
STRUCTURE WORKS		57	100%	100%	14-Jun-26	19-Aug-26	14-Jun-26 A	09-Aug-26 A	157,950.00	157,950.00	157,950.00	9
CONCRETE WORKS		51	100%	100%	14-Jun-26	19-Aug-26	14-Jun-26 A	23-Jul-26 A	113,782.50	113,782.50	113,782.50	23
SUB-STRUCTURE		16	100%	100%	14-Jun-26	02-Jul-26	14-Jun-26 A	02-Jul-26 A	33,345.00	33,345.00	33,345.00	0
MLTX-02-004-CI	Plain Concrete Under Footing	1	100%	100%	14-Jun-26	15-Jun-26	14-Jun-26 A	15-Jun-26 A	1,170.00	1,170.00	1,170.00	0
MLTX-02-004-CI	Reinforced Concrete Works for Slab on Grade Including	16	100%	100%	15-Jun-26	02-Jul-26	15-Jun-26 A	02-Jul-26 A	32,175.00	32,175.00	32,175.00	0
SUPER-STRUCTURE		19	100%	100%	16-Jul-26	19-Aug-26	18-Jul-26 A	23-Jul-26 A	80,437.50	80,437.50	80,437.50	23
MLTX-02-004-CI	AAC Panels Works for Walls	11	100%	100%	16-Jul-26	28-Jul-26	18-Jul-26 A	21-Jul-26 A	48,262.50	48,262.50	48,262.50	7
MLTX-02-004-CI	Parpet Works and Lintels	8	100%	100%	11-Aug-26	19-Aug-26	23-Jul-26 A	23-Jul-26 A	16,087.50	16,087.50	16,087.50	23
MLTX-02-004-CI	AAC Panels Works for Slabs	10	100%	100%	29-Jul-26	09-Aug-26	21-Jul-26 A	22-Jul-26 A	16,087.50	16,087.50	16,087.50	15
UNDER GROUND SEPTIC TANK		39	100%	100%	15-Jun-26	10-Aug-26	15-Jun-26 A	15-Jul-26 A	33,930.00	33,930.00	33,930.00	22
MLTX-02-004-CN-1	Plain Concrete Under Footing	1	100%	100%	15-Jun-26	16-Jun-26	15-Jun-26 A	16-Jun-26 A	1,170.00	1,170.00	1,170.00	0
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Slab Including	16	100%	100%	23-Jul-26	10-Aug-26	11-Jul-26 A	15-Jul-26 A	8,775.00	8,775.00	8,775.00	22
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Foundation Including	13	100%	100%	16-Jun-26	01-Jul-26	16-Jun-26 A	01-Jul-26 A	7,605.00	7,605.00	7,605.00	0
MLTX-02-004-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	16	100%	100%	05-Jul-26	22-Jul-26	05-Jul-26 A	07-Jul-26 A	16,380.00	16,380.00	16,380.00	13
THERMAL & MOISTER PROTECTION		57	100%	100%	14-Jun-26	19-Aug-26	14-Jun-26 A	09-Aug-26 A	10,237.50	10,237.50	10,237.50	9
ANTI TERMIT CONTROL		15	100%	100%	14-Jun-26	30-Jun-26	14-Jun-26 A	30-Jun-26 A	4,387.50	4,387.50	4,387.50	0
MLTX-02-004-CI	Anti Termite Works Under Foundation	1	100%	100%	14-Jun-26	15-Jun-26	14-Jun-26 A	15-Jun-26 A	1,755.00	1,755.00	1,755.00	0
MLTX-02-004-CI	Anti Termite Works Under Slab on Grade and Grade Beams	4	100%	100%	27-Jun-26	30-Jun-26	27-Jun-26 A	30-Jun-26 A	2,632.50	2,632.50	2,632.50	0
POLYETHYLENE SHEET		15	100%	100%	14-Jun-26	30-Jun-26	14-Jun-26 A	30-Jun-26 A	2,193.75	2,193.75	2,193.75	0
MLTX-02-004-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	14-Jun-26	15-Jun-26	14-Jun-26 A	15-Jun-26 A	877.50	877.50	877.50	0
MLTX-02-004-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	2	100%	100%	29-Jun-26	30-Jun-26	29-Jun-26 A	30-Jun-26 A	1,316.25	1,316.25	1,316.25	0
EPOXY		8	100%	100%	11-Aug-26	19-Aug-26	08-Aug-26 A	09-Aug-26 A	3,656.25	3,656.25	3,656.25	9
MLTX-02-004-CI	Surface Preparation for Epoxy Coating	3	100%	100%	11-Aug-26	13-Aug-26	08-Aug-26 A	08-Aug-26 A	1,096.88	1,096.88	1,096.88	5
MLTX-02-004-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	15-Aug-26	19-Aug-26	09-Aug-26 A	09-Aug-26 A	2,559.38	2,559.38	2,559.38	9
MASONARY WORK		5	100%	100%	11-Jul-26	15-Jul-26	26-Jul-26 A	05-Aug-26 A	12,285.00	12,285.00	12,285.00	-18
MLTX-02-004-CN-126	CMU Masonary Works Including all Accessories	5	100%	100%	11-Jul-26	15-Jul-26	26-Jul-26 A	05-Aug-26 A	12,285.00	12,285.00	12,285.00	-18
THERMAL & MOISTER PROTECTION		16	100%	55.84%	20-Aug-26	13-Sep-26	29-Sep-26 A	14-Oct-26	34,700.25	19,376.18	34,700.25	-26
MLTX-02-004-CN-126	Preparing Surface and Preliminary Works for Toilets	2	100%	0%	20-Aug-26	22-Aug-26	06-Oct-26	07-Oct-26	2,106.00	0.00	2,106.00	-39
MLTX-02-004-CN-126	Finalize Water Proofing Works for Toilets	5	100%	0%	23-Aug-26	27-Aug-26	08-Oct-26	13-Oct-26	4,914.00	0.00	4,914.00	-39
MLTX-02-004-CN-126	Preparing Surface and Preliminary Works for Roofing and	6	100%	100%	29-Aug-26	03-Sep-26	29-Sep-26 A	29-Sep-26 A	11,072.10	11,072.10	11,072.10	-21
MLTX-02-004-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	50%	05-Sep-26	13-Sep-26	29-Sep-26 A	14-Oct-26	16,608.15	8,304.08	16,608.15	-26
MECHANICAL WORK		101	91.11%	13.91%	29-Aug-26	18-Oct-26	04-Jul-26 A	27-Dec-26	394,777.27	60,290.75	433,285.13	-60
HVAC SYSTEM		29	47.55%	0%	12-Sep-26	18-Oct-26	24-Nov-26	27-Dec-26	13,260.00	0.00	27,885.00	-60
MLTX-02-004-CN-1	Preliminary HVAC and Ventilation Works	4	100%	0%	12-Sep-26	15-Sep-26	24-Nov-26	28-Nov-26	9,360.00	0.00	9,360.00	-62
MLTX-02-004-CN-1	Install and Finish HVAC and Ventilation Works Including Split	9	0%	0%	08-Oct-26	18-Oct-26	17-Dec-26	27-Dec-26	0.00	0.00	14,625.00	-60
MLTX-02-004-CN-1	Exhaust, Air Ducts Installation with all Accessories	8	100%	0%	16-Sep-26	26-Sep-26	29-Nov-26	07-Dec-26	3,900.00	0.00	3,900.00	-62
WATER SUPPLY SYSTEM		92	99.6%	19.22%	31-Aug-26	10-Oct-26	04-Aug-26 A	19-Dec-26	251,424.64	48,522.50	252,427.50	-60
MLTX-02-004-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	31-Aug-26	02-Sep-26	04-Aug-26 A	08-Aug-26 A	6,922.50	6,922.50	6,922.50	22
MLTX-02-004-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	0%	10-Sep-26	13-Sep-26	13-Oct-26	15-Oct-26	39,000.00	0.00	39,000.00	-27
MLTX-02-004-CN-1	Installing of Booster Pump Units Including fittings and	5	100%	0%	27-Sep-26	01-Oct-26	08-Dec-26	13-Dec-26	91,000.00	0.00	91,000.00	-62
MLTX-02-004-CN-1	Installing of GRP Tanks	8	100%	40%	16-Sep-26	26-Sep-26	15-Sep-26 A	14-Oct-26	104,000.00	41,600.00	104,000.00	-16

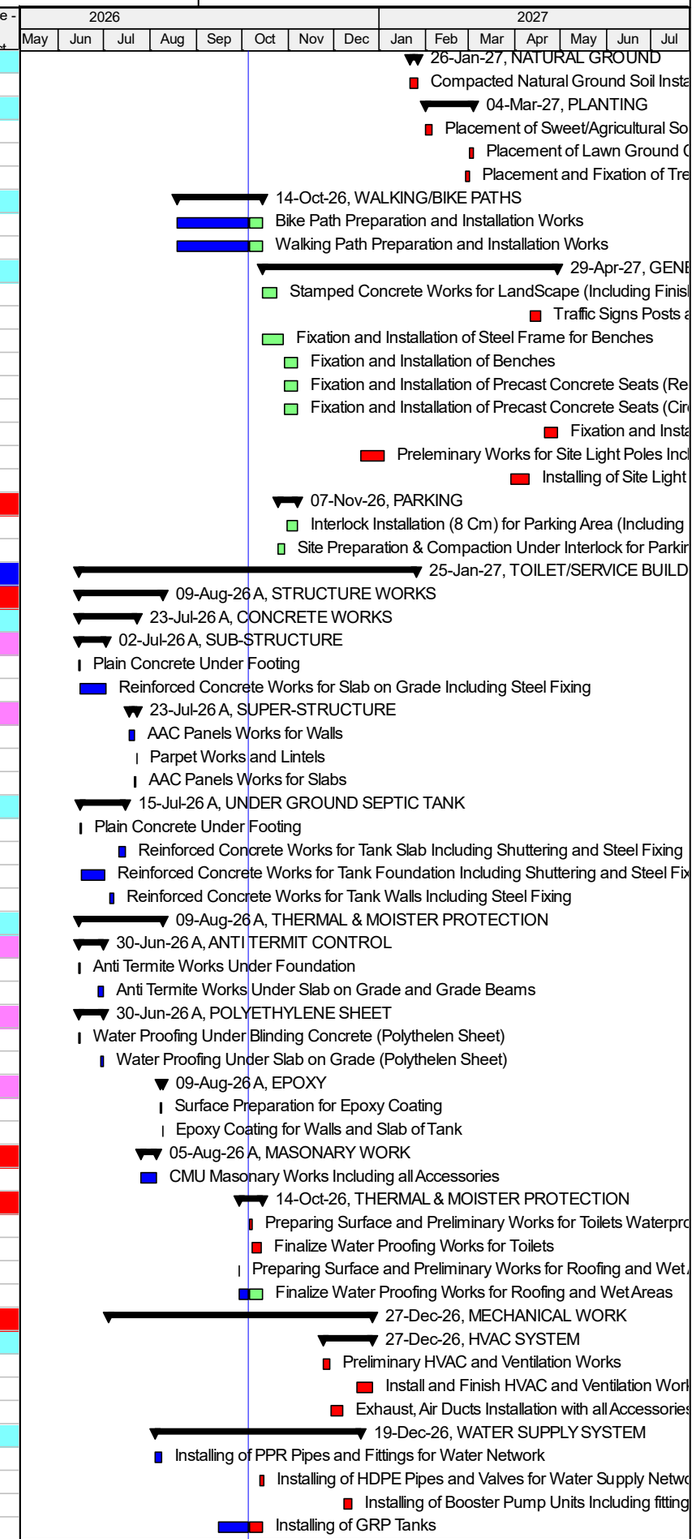

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004-CN-1	Installing of Valves and Fittings	6	100%	0%	03-Sep-26	09-Sep-26	06-Oct-26	12-Oct-26	9,750.00	0.00	9,750.00	-27
MLTX-02-004-CN-1	Installing of Water Heater	7	42.86%	0%	03-Oct-26	10-Oct-26	12-Dec-26	19-Dec-26	752.14	0.00	1,755.00	-60
SEWER/DRAINAGE SYSTEM		96	86.14%	7.79%	29-Aug-26	12-Oct-26	04-Jul-26 A	21-Dec-26	130,092.63	11,768.25	151,022.63	-60
MLTX-02-004-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	29-Aug-26	30-Aug-26	04-Jul-26 A	08-Aug-26 A	11,768.25	11,768.25	11,768.25	20
MLTX-02-004-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	17-Sep-26	19-Sep-26	22-Nov-26	23-Nov-26	10,359.38	0.00	10,359.38	-55
MLTX-02-004-CN-1	Installing UPVC Pipes for External Connection for Sewage	7	100%	0%	09-Sep-26	16-Sep-26	24-Oct-26	31-Oct-26	85,312.50	0.00	85,312.50	-37
MLTX-02-004-CN-1	Installing Inspection Chamber for Sewage Network	8	100%	0%	31-Aug-26	08-Sep-26	14-Oct-26	22-Oct-26	12,187.50	0.00	12,187.50	-37
MLTX-02-004-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	9	33.33%	0%	03-Oct-26	12-Oct-26	12-Dec-26	21-Dec-26	10,465.00	0.00	31,395.00	-60
FIRE PROTECTION		7	0%	0%	11-Oct-26	18-Oct-26	20-Dec-26	27-Dec-26	0.00	0.00	1,950.00	-60
MLTX-02-004-CN-1	Installing of Fire Fighting Extinguisher and accessories	7	0%	0%	11-Oct-26	18-Oct-26	20-Dec-26	27-Dec-26	0.00	0.00	1,950.00	-60
ELECTRICAL WORKS		122	39.54%	39.54%	20-Aug-26	24-Oct-26	11-Aug-26 A	02-Jan-27	148,882.50	148,882.50	376,526.25	-60
ROUGH-IN WORKS		25	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	148,882.50	148,882.50	148,882.50	3
MLTX-02-004-CN-1	Preleminary Works for Panel Boards	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	76,050.00	76,050.00	76,050.00	3
MLTX-02-004-CN-1	Preleminary Works for Cable Works	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	10,700.04	10,700.04	10,700.04	3
MLTX-02-004-CN-1	Preleminary Works for Sockets and Power Points	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	9,230.91	9,230.91	9,230.91	3
MLTX-02-004-CN-1	Preleminary Works for Lightning Works	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	9,750.00	9,750.00	9,750.00	3
MLTX-02-004-CN-1	Preleminary Works for Data & Telecommunication System	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	12,285.00	12,285.00	12,285.00	3
MLTX-02-004-CN-1	Preleminary Works for Security and Access Control System	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	15,266.55	15,266.55	15,266.55	3
MLTX-02-004-CN-1	Preleminary Works for Earthing Works	9	100%	100%	20-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26 A	15,600.00	15,600.00	15,600.00	3
FIXTURE WORKS		14	0%	0%	08-Oct-26	24-Oct-26	17-Dec-26	02-Jan-27	0.00	0.00	227,643.75	-60
MLTX-02-004-CN-1	Installing of Fire automation and Fire Alarm System	5	0%	0%	19-Oct-26	24-Oct-26	28-Dec-26	02-Jan-27	0.00	0.00	34,320.00	-60
MLTX-02-004-CN-1	Installing and Finish Works of Panel Boards	10	0%	0%	08-Oct-26	19-Oct-26	17-Dec-26	28-Dec-26	0.00	0.00	84,075.00	-60
MLTX-02-004-CN-1	Installing and Finalize Works of Sockets and Power Points	7	0%	0%	11-Oct-26	18-Oct-26	20-Dec-26	27-Dec-26	0.00	0.00	13,846.37	-60
MLTX-02-004-CN-1	Installing and Finalize Works of Lighting Works including Light	7	0%	0%	11-Oct-26	18-Oct-26	20-Dec-26	27-Dec-26	0.00	0.00	16,050.06	-60
MLTX-02-004-CN-1	Installing Data and Telecommunication System with all	7	0%	0%	11-Oct-26	18-Oct-26	20-Dec-26	27-Dec-26	0.00	0.00	18,427.50	-60
MLTX-02-004-CN-1	Installing and Finalize Works of Security and Access Control	9	0%	0%	08-Oct-26	18-Oct-26	17-Dec-26	27-Dec-26	0.00	0.00	22,899.83	-60
MLTX-02-004-CN-1	Installing and Finalize Works of Earthing Works	9	0%	0%	08-Oct-26	18-Oct-26	17-Dec-26	27-Dec-26	0.00	0.00	23,400.00	-60
MLTX-02-004-CN-1	Installing and Finalize Works of Lightning Protection System	9	0%	0%	08-Oct-26	18-Oct-26	17-Dec-26	27-Dec-26	0.00	0.00	14,625.00	-60
DOORS/WINDOWS		57	40%	0%	20-Aug-26	13-Oct-26	18-Oct-26	22-Dec-26	27,300.00	0.00	68,250.00	-60
MLTX-02-004-CN-12(	Preliminary Works For Doors	10	100%	0%	20-Aug-26	31-Aug-26	18-Oct-26	28-Oct-26	3,900.00	0.00	3,900.00	-49
MLTX-02-004-CN-12(	Finalize Metal Doors for Toilets Building	5	0%	0%	08-Oct-26	13-Oct-26	17-Dec-26	22-Dec-26	0.00	0.00	5,850.00	-60
MLTX-02-004-CN-13(	Finalize Glazzed Curtain Wall Works	5	0%	0%	08-Oct-26	13-Oct-26	17-Dec-26	22-Dec-26	0.00	0.00	35,100.00	-60
MLTX-02-004-CN-131	Preliminary Works For Windows/Curtain Wall	12	100%	0%	20-Aug-26	02-Sep-26	18-Oct-26	31-Oct-26	23,400.00	0.00	23,400.00	-49
METAL WORKS		25	100%	0%	20-Aug-26	04-Oct-26	06-Oct-26	03-Nov-26	13,650.00	0.00	13,650.00	-26
MLTX-02-004-CN-12(	Installation of Galvanized Steel Ladder	5	100%	0%	16-Sep-26	21-Sep-26	18-Oct-26	22-Oct-26	5,850.00	0.00	5,850.00	-26
MLTX-02-004-CN-12(	Installation of DI Cover for Tank	4	100%	0%	20-Aug-26	24-Aug-26	06-Oct-26	10-Oct-26	3,900.00	0.00	3,900.00	-39
MLTX-02-004-CN-12(	Installation of Galvanized Steel Roof Scupper	10	100%	0%	22-Sep-26	04-Oct-26	24-Oct-26	03-Nov-26	3,900.00	0.00	3,900.00	-26
FINISHING WORKS		114	94.17%	24.85%	29-Aug-26	16-Nov-26	05-Sep-26 A	25-Jan-27	136,090.50	35,909.25	144,514.50	-60
FLOOR FINISHES		68	93.18%	0%	03-Sep-26	16-Nov-26	08-Nov-26	25-Jan-27	15,990.00	0.00	17,160.00	-60
MLTX-02-004-CN-1	Creamic Tiles Floor Finish Works	2	100%	0%	03-Sep-26	05-Sep-26	08-Nov-26	09-Nov-26	11,895.00	0.00	11,895.00	-55
MLTX-02-004-CN-1	Granite Tiles Floor Finish Works	6	100%	0%	06-Sep-26	12-Sep-26	10-Nov-26	16-Nov-26	2,925.00	0.00	2,925.00	-55
MLTX-02-004-CN-1	Epoxy Coat on Concrete Floor	20	0%	0%	25-Oct-26	16-Nov-26	03-Jan-27	25-Jan-27	0.00	0.00	1,170.00	-60
MLTX-02-004-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	0%	13-Sep-26	16-Sep-26	17-Nov-26	21-Nov-26	1,170.00	0.00	1,170.00	-55
WALL FINISHES		82	93.65%	31.45%	29-Aug-26	10-Oct-26	05-Sep-26 A	19-Dec-26	106,918.50	35,909.25	114,172.50	-60
MLTX-02-004-CN-1	Preliminary Works for Wall Finish Works including Plastering	3	100%	100%	31-Aug-26	02-Sep-26	05-Sep-26 A	12-Sep-26 A	18,369.00	18,369.00	18,369.00	-8
MLTX-02-004-CN-1	Preliminary Works for Wall Finish Works (External)	14	100%	100%	29-Aug-26	13-Sep-26	20-Sep-26 A	30-Sep-26 A	6,552.00	6,552.00	6,552.00	-14
MLTX-02-004-CN-1	Painting Finish Works for External Walls	3	100%	0%	14-Sep-26	16-Sep-26	17-Oct-26	19-Oct-26	10,478.00	0.00	10,478.00	-27
MLTX-02-004-CN-1	Ceramic Finish Works for Walls	5	100%	70%	06-Sep-26	10-Sep-26	04-Oct-26 A	11-Oct-26	15,697.50	10,988.25	15,697.50	-25
MLTX-02-004-CN-1	Phenolic Partitions for Toilets	7	100%	0%	24-Sep-26	01-Oct-26	03-Dec-26	10-Dec-26	31,200.00	0.00	31,200.00	-60
MLTX-02-004-CN-1	Stone Cladding Finish Works for External Walls	5	100%	0%	17-Sep-26	22-Sep-26	20-Oct-26	25-Oct-26	9,100.00	0.00	9,100.00	-27
MLTX-02-004-CN-1	Glass Partitions including all accessories and doors	5	60%	0%	03-Oct-26	07-Oct-26	12-Dec-26	16-Dec-26	7,371.00	0.00	12,285.00	-60
MLTX-02-004-CN-1	Granite Capping for Parpet	2	100%	0%	14-Sep-26	15-Sep-26	15-Oct-26	17-Oct-26	8,151.00	0.00	8,151.00	-26
MLTX-02-004-CN-1	Painting Finish Works for Internal Walls	2	0%	0%	08-Oct-26	10-Oct-26	17-Dec-26	19-Dec-26	0.00	0.00	2,340.00	-60
CELLING FINISHES		41	100%	0%	03-Sep-26	01-Oct-26	27-Oct-26	13-Dec-26	13,182.00	0.00	13,182.00	-62
MLTX-02-004-CN-1	Painting Finish Works for Ceiling	9	100%	0%	21-Sep-26	01-Oct-26	03-Dec-26	13-Dec-26	1,638.00	0.00	1,638.00	-62
MLTX-02-004-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	4	100%	0%	16-Sep-26	20-Sep-26	29-Nov-26	02-Dec-26	6,926.40	0.00	6,926.40	-62
MLTX-02-004-CN-1	Preliminary Works for Ceiling Painting Works	15	100%	0%	03-Sep-26	20-Sep-26	27-Oct-26	12-Nov-26	4,617.60	0.00	4,617.60	-45
SPECIALTIES WORK		17	100%	0%	20-Sep-26	04-Oct-26	24-Nov-26	13-Dec-26	39,000.00	0.00	39,000.00	-60
MLTX-02-004-CN-127	Sanitary Fixtures and Accessories Works	3	100%	0%	20-Sep-26	22-Sep-26	24-Nov-26	26-Nov-26	14,625.00	0.00	14,625.00	-55
MLTX-02-004-CN-131	Installation of Phenolic Locker	2	100%	0%	03-Oct-26	04-Oct-26	12-Dec-26	13-Dec-26	24,375.00	0.00	24,375.00	-60
TESTING & COMMISSIONING		68	0%	0%	17-Nov-26	19-Jan-27	31-Jan-27	24-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-TC-11890	Testing and Commissioning for MEP Works for Playground	16	0%	0%	27-Dec-26	13-Jan-27	31-Mar-27	18-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	25	0%	0%	17-Nov-26	15-Dec-26	31-Jan-27	01-Mar-27	0.00	0.00	0.00	-64
MLTX-02-004-TC-11910	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	14-Jan-27	19-Jan-27	19-Apr-27	24-Apr-27	0.00	0.00	0.00	-77

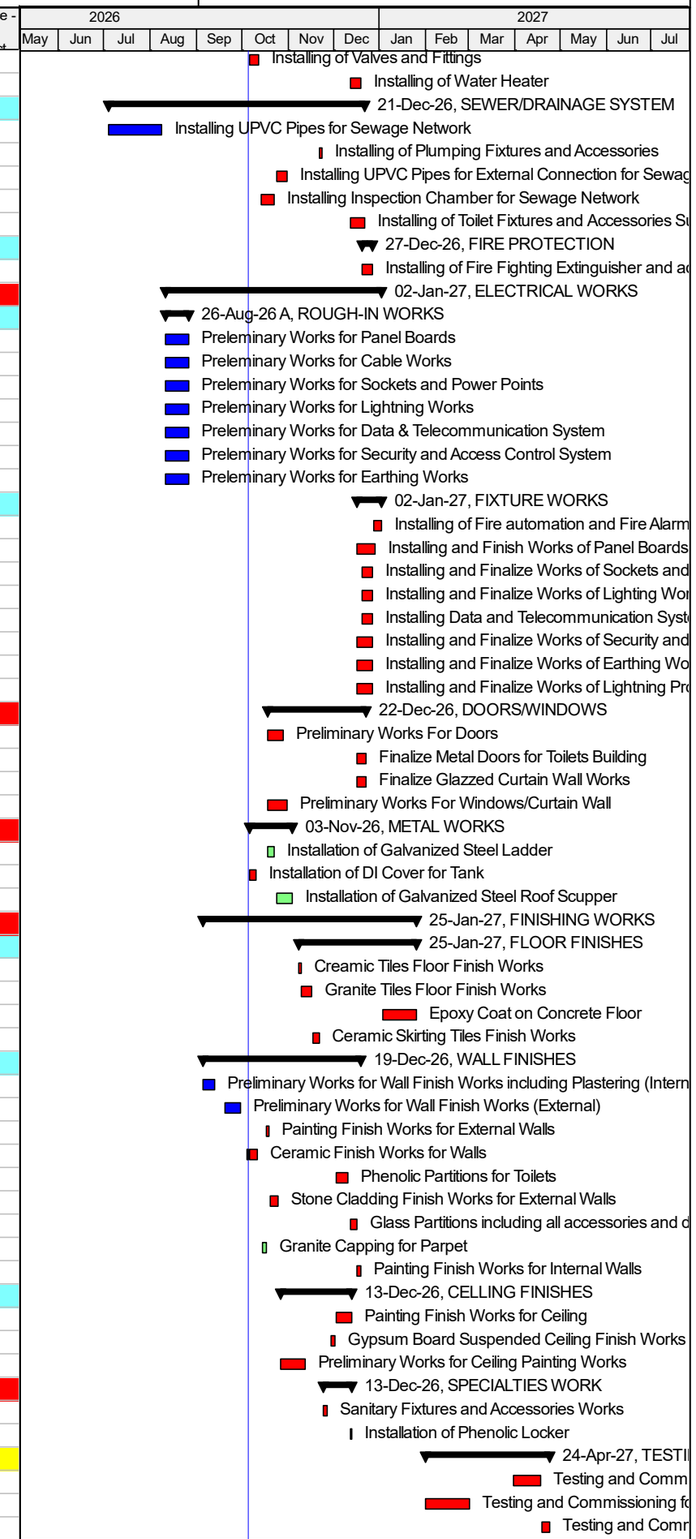

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PROJECT CLOSEOUT & DEMOBILIZATION		48	0%	0%	14-Jan-27	25-Jan-27	02-Mar-27	29-Apr-27	0.00	0.00	0.00	-77
As-Built DWGs		46	0%	0%	14-Jan-27	23-Jan-27	02-Mar-27	27-Apr-27	0.00	0.00	0.00	-77
As-Built DWGs Submittals		42	0%	0%	14-Jan-27	18-Jan-27	02-Mar-27	22-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-1200(	As-Built DWGs Submittal for Playground Area Works	4	0%	0%	14-Jan-27	18-Jan-27	19-Apr-27	22-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	4	0%	0%	14-Jan-27	18-Jan-27	02-Mar-27	06-Mar-27	0.00	0.00	0.00	-39
MLTX-02-004-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	14-Jan-27	18-Jan-27	19-Apr-27	22-Apr-27	0.00	0.00	0.00	-77
As-Built DWGs Approvals		42	0%	0%	19-Jan-27	23-Jan-27	07-Mar-27	27-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-1204(	As-Built DWGs Approval for Playground Area Works	4	0%	0%	19-Jan-27	23-Jan-27	24-Apr-27	27-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	4	0%	0%	19-Jan-27	23-Jan-27	07-Mar-27	14-Mar-27	0.00	0.00	0.00	-39
MLTX-02-004-CO-1206(	As-Built DWGs Approval for Landscape Works	4	0%	0%	19-Jan-27	23-Jan-27	24-Apr-27	27-Apr-27	0.00	0.00	0.00	-77
Demobilization		6	0%	0%	19-Jan-27	25-Jan-27	24-Apr-27	29-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-12080	Demobilization of Manpower	2	0%	0%	19-Jan-27	20-Jan-27	24-Apr-27	25-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-12090	Removal of Equipment from Site	2	0%	0%	19-Jan-27	20-Jan-27	24-Apr-27	25-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-12100	Site Clean Up	2	0%	0%	21-Jan-27	23-Jan-27	26-Apr-27	27-Apr-27	0.00	0.00	0.00	-77
MLTX-02-004-CO-12110	Restoration of Ground Surfaces	2	0%	0%	24-Jan-27	25-Jan-27	28-Apr-27	29-Apr-27	0.00	0.00	0.00	-77

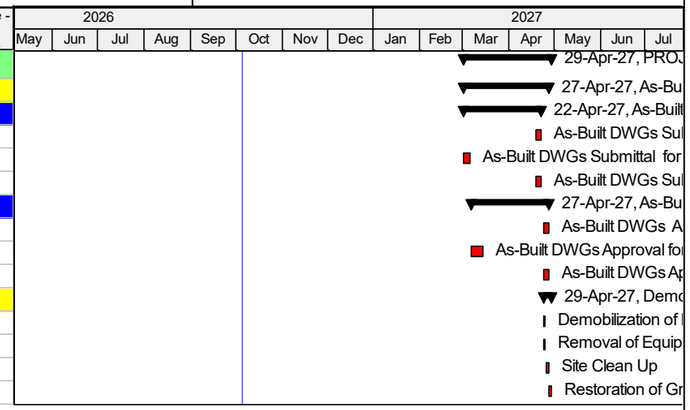

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
