MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


2 Weeks look ahead schedule
D.D 02-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R R	186	71.34%	56.15%	04-May-26	31-Dec-26	01-Jun-26 A	19-Dec-26	2,130,333.87	1,676,780.81	2,986,354.59	12
ARAR		108	78.03%	49.59%	27-Jun-26	28-Nov-26	11-Jun-26 A	19-Dec-26	856,207.18	544,155.48	1,097,279.58	-17
ENGINEERING		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
SHOP DRAWINGS		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
SHOP DRAWINGS SUBMISSION		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
ELECTRICAL WORKS		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
MLTX-02-005-EN-2580	Shop DWG Submittal for Power Layout	27	100%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
PROCUREMENT		40	0%	0%	27-Jun-26	28-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-17
SHORT LEAD ITEM		40	0%	0%	27-Jun-26	28-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-17
TOILET/SERVICE WORKS		40	0%	0%	27-Jun-26	28-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-17
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-8490	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-109
SWITCHES/SOCKETS		27	0%	0%	28-Oct-26	28-Nov-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-8530	Material Delivery for Switches/Sockets	27	15.19%	0%	28-Oct-26	28-Nov-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-4
FURNITURES		29	0%	0%	30-Aug-26	03-Oct-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	-54
MLTX-02-005-PR-8150	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	-54
PLAYGROUND WORKS		30	0%	0%	15-Jul-26	24-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-37
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-53
MLTX-02-005-PR-8970	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-53
MARKING PAINT		15	0%	0%	10-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-9090	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-44
CCTV MATERIALS		25	0%	0%	26-Sep-26	24-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-32
MLTX-02-005-PR-9410	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-32
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-9470	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-93
LANDSCAPE WORKS		25	0%	0%	15-Jul-26	17-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-11
PAVEMENT MARKING		5	0%	0%	15-Jul-26	20-Jul-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-9580	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-93
TRAFFIC SIGNS		10	0%	0%	13-Aug-26	16-Sep-26	02-Nov-26	14-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-9640	Material Delivery for Traffic Signs	10	100%	0%	13-Aug-26	16-Sep-26	02-Nov-26	14-Nov-26	0.00	0.00	0.00	-48
AGRICULTURE SOIL		22	0%	0%	18-Aug-26	12-Sep-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-9720	Material Delivery for Agriculture Soil	22	100%	0%	18-Aug-26	12-Sep-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	-64
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	14-Nov-26	25-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-9760	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	14-Nov-26	25-Nov-26	0.00	0.00	0.00	-48
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-9800	Material Delivery for Grass/Trees	25	44.4%	0%	20-Oct-26	17-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-11
LONG LEAD ITEM		25	0%	0%	27-Sep-26	23-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-6
PLAYGROUND WORKS		25	0%	0%	27-Sep-26	23-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-6
STEEL TENSION CABLES		15	0%	0%	27-Sep-26	13-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-8690	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-31
EMERGENCY DOORS		20	0%	0%	26-Oct-26	17-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-8730	Material Delivery for Emergency Doors	20	30.5%	0%	26-Oct-26	17-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-6
PRESSURE UNITS		25	0%	0%	26-Oct-26	23-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-8770	Material Delivery for Pressure Units	25	24.4%	0%	26-Oct-26	23-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-6
AIR LOCK DOORS		20	0%	0%	14-Oct-26	05-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-8800	Material Fabrication for Lock Doors	20	80.5%	0%	14-Oct-26	05-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-16
CONSTRUCTION PHASE		108	78.03%	49.59%	13-Sep-26	23-Nov-26	11-Jun-26 A	28-Nov-26	856,207.18	544,155.48	1,097,279.58	-3
SITE WORKS		90	75.57%	49.63%	17-Sep-26	23-Nov-26	11-Jun-26 A	28-Nov-26	745,562.84	489,653.93	986,635.24	-3
LANDSCAPE WORKS		90	75.57%	49.63%	17-Sep-26	23-Nov-26	11-Jun-26 A	28-Nov-26	745,562.84	489,653.93	986,635.24	-3
PLAYGROUND AREA		20	100%	0%	01-Oct-26	24-Oct-26	02-Nov-26	25-Nov-26	30,677.48	0.00	30,677.48	-27
PADEL FENCE		20	100%	0%	01-Oct-26	24-Oct-26	02-Nov-26	25-Nov-26	30,677.48	0.00	30,677.48	-27
MLTX-02-005-CN-1026(	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	02-Nov-26	25-Nov-26	30,677.48	0.00	30,677.48	-27
NATURAL GROUND		6	0%	80%	17-Nov-26	23-Nov-26	27-Oct-26 A	09-Nov-26	0.00	52,000.00	65,000.00	13
MLTX-02-005-CN-10550	Compacted Natural Ground Soil Installation Works for Landscape	6	0%	80%	17-Nov-26	23-Nov-26	27-Oct-26 A	09-Nov-26	0.00	52,000.00	65,000.00	13
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	28-Nov-26	347,251.46	104,175.44	347,251.46	-23
MLTX-02-005-CN-10570	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	6	100%	30%	17-Sep-26	24-Sep-26	31-Oct-26 A	28-Nov-26	104,175.44	31,252.63	104,175.44	-54
MLTX-02-005-CN-10580	Placement of Lawn Ground Cover (Rolling and Compaction)	4	100%	30%	27-Oct-26	31-Oct-26	31-Oct-26 A	25-Nov-26	141,732.50	42,519.75	141,732.50	-21
MLTX-02-005-CN-10590	Placement and Fixation of Trees	5	100%	30%	26-Sep-26	30-Sep-26	31-Oct-26 A	26-Nov-26	101,343.52	30,403.06	101,343.52	-48
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	28-Nov-26	367,633.90	183,816.95	367,633.90	-22
MLTX-02-005-CN-10510	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	28-Nov-26	187,554.12	93,777.06	187,554.12	-34
MLTX-02-005-CN-10520	Walking Path Preparation and Installation Works	12	100%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	28-Nov-26	180,079.78	90,039.89	180,079.78	-22
GENERAL/FURNITURE		13	0%	85%	08-Nov-26	22-Nov-26	18-Oct-26 A	17-Nov-26	0.00	149,661.54	176,072.40	5

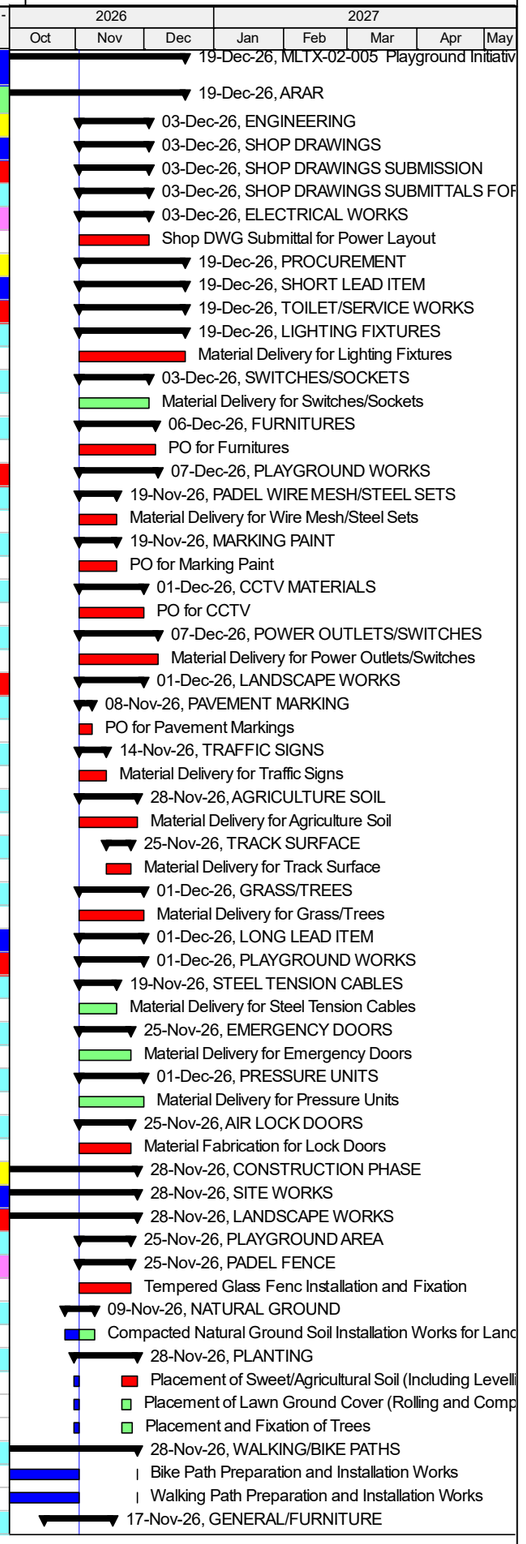

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-11800	Installing of Site Light Poles	13	0%	85%	08-Nov-26	22-Nov-26	18-Oct-26 A	17-Nov-26	0.00	149,661.54	176,072.40	5
TOILET/SERVICE BUILDING		58	100%	49.26%	13-Sep-26	22-Oct-26	03-Oct-26 A	21-Nov-26	110,644.34	54,501.55	110,644.34	-24
THERMAL & MOISTER PROTECTION		8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-42
MLTX-02-005-CN-11080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-42
MECHANICAL WORK		18	100%	19.89%	29-Sep-26	17-Oct-26	22-Oct-26 A	15-Nov-26	36,762.98	7,311.98	36,762.98	-24
SEWER/DRAINAGE SYSTEM		18	100%	19.89%	29-Sep-26	17-Oct-26	22-Oct-26 A	15-Nov-26	36,762.98	7,311.98	36,762.98	-24
MLTX-02-005-CN-11580	Installing UPVC Pipes for External Connection for Sewage Network	4	100%	0%	05-Oct-26	08-Oct-26	08-Nov-26	12-Nov-26	14,217.67	0.00	14,217.67	-29
MLTX-02-005-CN-11600	Installing of Plumping Fixtures and Accessories	2	100%	0%	15-Oct-26	17-Oct-26	12-Nov-26	15-Nov-26	10,358.68	0.00	10,358.68	-24
MLTX-02-005-CN-11850	Installing Inspection Chamber for Sewage Network	5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	08-Nov-26	12,186.63	7,311.98	12,186.63	-29
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	02-Nov-26	07-Nov-26	3,899.72	0.00	3,899.72	-41
MLTX-02-005-CN-11160	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	02-Nov-26	07-Nov-26	3,899.72	0.00	3,899.72	-41
FINISHING WORKS		14	100%	83.21%	06-Oct-26	13-Oct-26	20-Oct-26 A	10-Nov-26	38,750.40	32,243.02	38,750.40	-23
FLOOR FINISHES		4	100%	0%	06-Oct-26	10-Oct-26	02-Nov-26	07-Nov-26	2,924.82	0.00	2,924.82	-23
MLTX-02-005-CN-11210	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	02-Nov-26	07-Nov-26	2,924.82	0.00	2,924.82	-23
WALL FINISHES		7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	10-Nov-26	35,825.58	32,243.02	35,825.58	-23
MLTX-02-005-CN-11300	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	10-Nov-26	35,825.58	32,243.02	35,825.58	-23
SPECIALTIES WORK		5	100%	0%	18-Oct-26	22-Oct-26	15-Nov-26	21-Nov-26	14,623.96	0.00	14,623.96	-24
MLTX-02-005-CN-11390	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	15-Nov-26	21-Nov-26	14,623.96	0.00	14,623.96	-24
HASA OASIS		186	78.84%	72.32%	04-May-26	07-Dec-26	01-Jun-26 A	07-Dec-26	997,374.78	914,847.08	1,265,071.64	1
ENGINEERING		25	0%	0%	04-May-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
SHOP DRAWINGS		25	0%	0%	04-May-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
ELECTRICAL WORKS		25	0%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
MLTX-02-005-EN-8660	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
SHOP DRAWINGS APPROVALS		25	0%	0%	28-Oct-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		25	0%	0%	28-Oct-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
ELECTRICAL WORKS		25	0%	0%	28-Oct-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-EN-1184(	Shop DWG Approval for Power Installation Details	25	16.4%	0%	28-Oct-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
PROCUREMENT		30	0%	0%	16-Jun-26	10-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-22
SHORT LEAD ITEM		30	0%	0%	16-Jun-26	03-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-28
TOILET/SERVICE WORKS		20	0%	0%	16-Jun-26	19-Oct-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-31
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-10130	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-10140	Material Delivery for Distribution Panels	15	100%	0%	03-Oct-26	19-Oct-26	08-Nov-26	25-Nov-26	0.00	0.00	0.00	-31
FURNITURES		19	0%	0%	16-Jun-26	07-Jul-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	-118
MLTX-02-005-PR-10330	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	-118
PLAYGROUND WORKS		30	0%	0%	28-Jun-26	03-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-28
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-10780	Material Delivery for Artificial TURF	30	93.67%	0%	30-Sep-26	03-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-28
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-10800	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-36
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-10820	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-39
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-39
MARKING PAINT		15	0%	0%	28-Jun-26	14-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-10350	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-108
AIR DIFUSSERS/GRILLS		15	0%	0%	24-Sep-26	11-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-10470	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-33
GALVANIZED DUCTS		15	0%	0%	24-Sep-26	11-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-10490	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-33
EXHAUST FANS		15	0%	0%	10-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-10510	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-44
CCTV MATERIALS		15	0%	0%	04-Jul-26	20-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-10690	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-103
LANDSCAPE WORKS		25	0%	0%	21-Sep-26	26-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-30
TRAFFIC SIGNS		5	0%	0%	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-10080	Material Delivery for Traffic Signs	5	100%	0%	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-35
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-10920	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-30
LONG LEAD ITEM		25	0%	0%	15-Jul-26	10-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-17
PLAYGROUND WORKS		25	0%	0%	15-Jul-26	10-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-17
STEEL TENSION CABLES		16	0%	0%	21-Sep-26	10-Oct-26	02-Nov-26	21-Nov-26	0.00	0.00	0.00	-35

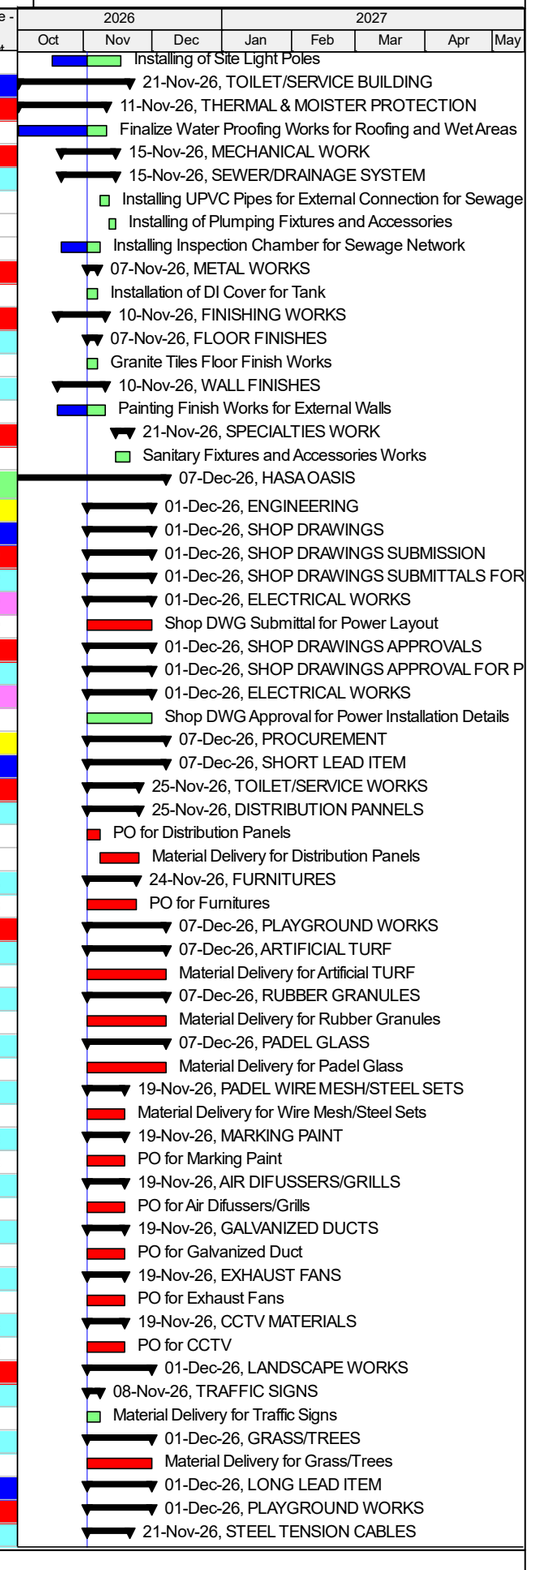

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-10560	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	02-Nov-26	21-Nov-26	0.00	0.00	0.00	-35
EMERGENCY DOORS		25	0%	0%	15-Jul-26	12-Aug-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-10580	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-93
PRESSURE UNITS		25	0%	0%	13-Oct-26	10-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-10600	Material Delivery for Pressure Units	25	68.4%	0%	13-Oct-26	10-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-17
AIR LOCK DOORS		25	0%	0%	03-Oct-26	31-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-10620	Material Delivery for Lock Doors	25	100%	0%	03-Oct-26	31-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-26
CONSTRUCTION PHASE		186	78.84%	72.32%	30-Jul-26	07-Dec-26	01-Jun-26 A	05-Dec-26	997,374.78	914,847.08	1,265,071.64	3
SITE WORKS		135	77.65%	71.45%	29-Sep-26	07-Dec-26	01-Jun-26 A	05-Dec-26	930,317.96	855,958.34	1,198,014.82	3
LANDSCAPE WORKS		135	77.65%	71.45%	29-Sep-26	07-Dec-26	01-Jun-26 A	05-Dec-26	930,317.96	855,958.34	1,198,014.82	3
PLAYGROUND AREA		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	05-Nov-26	180,520.67	144,416.54	180,520.67	-29
CURBSTOEN/INTERLOCK		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	05-Nov-26	180,520.67	144,416.54	180,520.67	-29
MLTX-02-005-CN-1196(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	05-Nov-26	180,520.67	144,416.54	180,520.67	-29
NATURAL GROUND		15	0%	70.17%	29-Nov-26	07-Dec-26	13-Oct-26 A	08-Nov-26	0.00	134,544.00	191,740.00	26
MLTX-02-005-CN-11980	Tartan Floor Installation Works for Landscape (Including Finishing Works)	3	0%	60%	05-Dec-26	07-Dec-26	14-Oct-26 A	05-Nov-26	0.00	76,044.00	126,740.00	28
MLTX-02-005-CN-11990	Compacted Natural Ground Soil Installation Works for Landscape	5	0%	90%	29-Nov-26	03-Dec-26	13-Oct-26 A	08-Nov-26	0.00	58,500.00	65,000.00	23
PLANTING		101	87.76%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	05-Nov-26	304,731.71	240,773.38	347,251.46	-2
MLTX-02-005-CN-12050	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	3	100%	95%	24-Oct-26	26-Oct-26	03-Oct-26 A	05-Nov-26	104,175.44	98,966.67	104,175.44	-8
MLTX-02-005-CN-12060	Placement of Lawn Ground Cover (Rolling and Compaction)	3	70%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	05-Nov-26	99,212.75	70,866.25	141,732.50	-2
MLTX-02-005-CN-12070	Placement and Fixation of Trees	3	100%	70%	27-Oct-26	29-Oct-26	14-Oct-26 A	05-Nov-26	101,343.52	70,940.46	101,343.52	-5
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	02-Nov-26	367,633.90	294,107.12	367,633.90	-13
MLTX-02-005-CN-12000	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	02-Nov-26	187,554.12	150,043.30	187,554.12	-21
MLTX-02-005-CN-12010	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	02-Nov-26	180,079.78	144,063.82	180,079.78	-13
GENERAL/FURNITURE		42	69.84%	37.99%	15-Oct-26	16-Nov-26	14-Oct-26 A	05-Dec-26	77,431.68	42,117.30	110,868.79	-15
MLTX-02-005-CN-11970	Stamped Concrete Works for LandScape (Including Finishing Works)	18	72.78%	45%	18-Oct-26	07-Nov-26	14-Oct-26 A	23-Nov-26	68,115.63	42,117.30	93,594.00	-13
MLTX-02-005-CN-12440	Fixation and Installation of Steel Frame for Benches	28	53.93%	0%	15-Oct-26	16-Nov-26	02-Nov-26	05-Dec-26	9,316.05	0.00	17,274.79	-15
TOILET/SERVICE BUILDING		70	100%	87.82%	30-Jul-26	20-Oct-26	20-Sep-26 A	23-Nov-26	67,056.82	58,888.74	67,056.82	-28
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	23-Nov-26	16,607.28	14,946.55	16,607.28	-80
MLTX-02-005-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	23-Nov-26	16,607.28	14,946.55	16,607.28	-80
FINISHING WORKS		3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	05-Nov-26	35,825.58	32,243.02	35,825.58	-13
WALL FINISHES		3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	05-Nov-26	35,825.58	32,243.02	35,825.58	-13
MLTX-02-005-CN-13010	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	05-Nov-26	35,825.58	32,243.02	35,825.58	-13
SPECIALTIES WORK		3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	05-Nov-26	14,623.96	11,699.17	14,623.96	-31
MLTX-02-005-CN-12700	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	05-Nov-26	14,623.96	11,699.17	14,623.96	-31
DAMMAM		167	44.35%	34.9%	21-May-26	31-Dec-26	06-Sep-26 A	17-Dec-26	276,751.91	217,778.25	624,003.37	13
ENGINEERING		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
SHOP DRAWINGS		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
SHOP DRAWINGS SUBMISSION		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
MLTX-02-005-EN-1293(	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-134
MLTX-02-005-EN-1296(	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
PROCUREMENT		84	0%	0%	21-May-26	08-Dec-26	25-Oct-26 A	06-Dec-26	0.00	0.00	0.00	3
SHORT LEAD ITEM		84	0%	0%	21-May-26	08-Dec-26	25-Oct-26 A	06-Dec-26	0.00	0.00	0.00	3
TOILET/SERVICE WORKS		29	0%	0%	17-Jun-26	29-Oct-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	-31
DISTRIBUTION PANNELS		15	0%	0%	13-Oct-26	29-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-11210	PO for Distribution Panels	15	100%	0%	13-Oct-26	29-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-17
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	-117
MLTX-02-005-PR-11410	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-PR-11420	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	12-Nov-26	06-Dec-26	0.00	0.00	0.00	-117
PLAYGROUND WORKS		28	0%	0%	21-May-26	02-Dec-26	02-Nov-26	05-Dec-26	0.00	0.00	0.00	-1
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	02-Nov-26	26-Nov-26	0.00	0.00	0.00	-137
MLTX-02-005-PR-11620	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	02-Nov-26	26-Nov-26	0.00	0.00	0.00	-137
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	-132
MLTX-02-005-PR-11880	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	-132
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	02-Nov-26	05-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-11900	Material Delivery for Padel Glass	28	43.21%	0%	19-Oct-26	19-Nov-26	02-Nov-26	05-Dec-26	0.00	0.00	0.00	-12
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-127
MLTX-02-005-PR-11920	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-127
BITUMINOUS BASE & WEARING COURSE		15	0%	0%	15-Jun-26	01-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-119
MLTX-02-005-PR-11080	PO for Bituminous Base & Wearing Course	15	100%	0%	15-Jun-26	01-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-119
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-11730	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-11740	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	08-Nov-26	19-Nov-26	0.00	0.00	0.00	-107

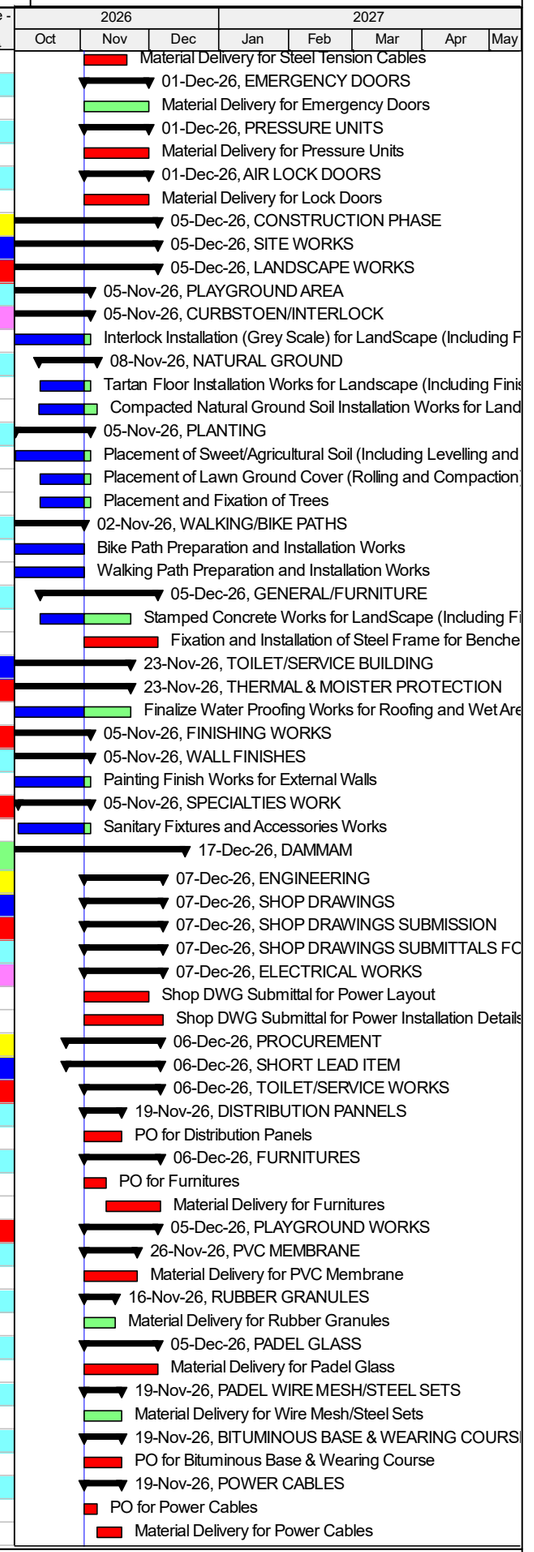

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


2 Weeks look ahead schedule
D.D 02-11-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	08-Nov-26	01-Dec-26	0.00	0.00	0.00	2
MLTX-02-005-PR-11760	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	08-Nov-26	01-Dec-26	0.00	0.00	0.00	2
CCTV MATERIALS		5	0%	0%	30-Jul-26	04-Aug-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-11770	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-80
LANDSCAPE WORKS		15	0%	0%	22-Nov-26	08-Dec-26	25-Oct-26 A	02-Nov-26	0.00	0.00	0.00	32
GRASS/TREES		15	0%	0%	22-Nov-26	08-Dec-26	25-Oct-26 A	02-Nov-26	0.00	0.00	0.00	32
MLTX-02-005-PR-12000	Material Delivery for Grass/Trees	15	0%	50%	22-Nov-26	08-Dec-26	25-Oct-26 A	02-Nov-26	0.00	0.00	0.00	32
LONG LEAD ITEM		22	0%	0%	07-Sep-26	30-Nov-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	3
PLAYGROUND WORKS		22	0%	0%	07-Sep-26	30-Nov-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	3
STEEL TENSION CABLES		15	0%	0%	07-Sep-26	24-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-47
MLTX-02-005-PR-11640	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-47
EMERGENCY DOORS		15	0%	0%	04-Nov-26	21-Nov-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	2
MLTX-02-005-PR-11660	Material Delivery for Emergency Doors	15	0%	0%	04-Nov-26	21-Nov-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	2
PRESSURE UNITS		22	0%	0%	05-Nov-26	30-Nov-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	3
MLTX-02-005-PR-11680	Material Delivery for Pressure Units	10	0%	0%	05-Nov-26	16-Nov-26	02-Nov-26	14-Nov-26	0.00	0.00	0.00	3
MLTX-02-005-PR-12070	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	16-Nov-26	28-Nov-26	0.00	0.00	0.00	3
AIR LOCK DOORS		12	0%	0%	05-Nov-26	18-Nov-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	3
MLTX-02-005-PR-11700	Material Delivery for Lock Doors	12	0%	0%	05-Nov-26	18-Nov-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	3
CONSTRUCTION PHASE		167	44.35%	34.9%	18-Aug-26	31-Dec-26	06-Sep-26 A	17-Dec-26	276,751.91	217,778.25	624,003.37	13
SITE WORKS		113	41.42%	32.24%	15-Sep-26	31-Dec-26	20-Oct-26 A	19-Nov-26	245,520.67	191,132.53	592,772.13	37
LANDSCAPE WORKS		113	41.42%	32.24%	15-Sep-26	31-Dec-26	20-Oct-26 A	19-Nov-26	245,520.67	191,132.53	592,772.13	37
PLAYGROUND AREA		6	100%	35%	15-Sep-26	21-Sep-26	21-Oct-26 A	09-Nov-26	180,520.67	63,182.23	180,520.67	-40
CURBSTOEN/INTERLOCK		6	100%	35%	15-Sep-26	21-Sep-26	21-Oct-26 A	09-Nov-26	180,520.67	63,182.23	180,520.67	-40
MLTX-02-005-CN-1339(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	6	100%	35%	15-Sep-26	21-Sep-26	21-Oct-26 A	09-Nov-26	180,520.67	63,182.23	180,520.67	-40
NATURAL GROUND		15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	19-Nov-26	65,000.00	58,500.00	65,000.00	-20
MLTX-02-005-CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	19-Nov-26	65,000.00	58,500.00	65,000.00	-20
PLANTING		27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	14-Nov-26	0.00	69,450.29	347,251.46	42
MLTX-02-005-CN-13480	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	09-Nov-26	0.00	20,835.09	104,175.44	29
MLTX-02-005-CN-13490	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	20%	24-Dec-26	31-Dec-26	01-Nov-26 A	10-Nov-26	0.00	28,346.50	141,732.50	45
MLTX-02-005-CN-13500	Placement and Fixation of Trees	10	0%	20%	13-Dec-26	23-Dec-26	01-Nov-26 A	14-Nov-26	0.00	20,268.70	101,343.52	35
TOILET/SERVICE BUILDING		130	100%	85.32%	18-Aug-26	31-Oct-26	06-Sep-26 A	17-Dec-26	31,231.24	26,645.72	31,231.24	-40
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-64
MLTX-02-005-CN-14080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-64
SPECIALTIES WORK		4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	17-Dec-26	14,623.96	11,699.17	14,623.96	-40
MLTX-02-005-CN-14130	Sanitary Fixtures and Accessories Works	4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	17-Dec-26	14,623.96	11,699.17	14,623.96	-40

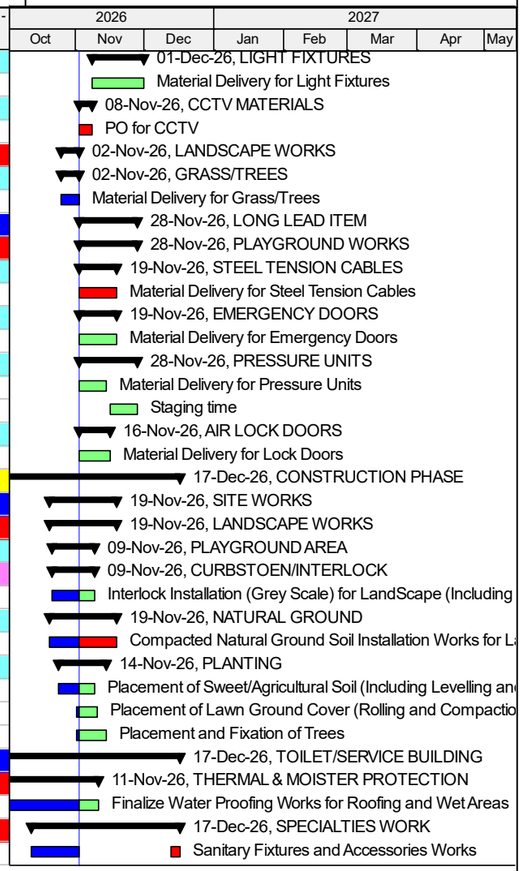

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation
