
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oa	314	42.16%	42.35%	03-Mar-26	02-Jan-27	03-Mar-26 A	27-Feb-27	12,647,106.88	12,704,269.70	29,997,851.67	-46
KEY MILESTONES		301	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	27-Feb-27	0.00	0.00	0.00	-46
GENERAL MILESTONES		301	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	27-Feb-27	0.00	0.00	0.00	-46
CONTRACTUAL MILESTONE		270	0%	0%	11-Apr-26	02-Jan-27	02-Apr-26 A	27-Feb-27	0.00	0.00	0.00	-46
ARAR		314	41%	38.99%	03-Mar-26	02-Jan-27	04-Mar-26 A	13-Feb-27	4,192,992.00	3,986,992.40	10,226,640.03	-35
MOBILIZATION		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	9
ENGINEERING		252	0%	0%	07-Mar-26	13-Dec-26	07-Mar-26 A	03-Jan-27	0.00	0.00	0.00	-17
PROCUREMENT		204	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	03-Feb-27	0.00	0.00	0.00	-42
CONSTRUCTION PHASE		280	41%	38.99%	15-Apr-26	31-Dec-26	04-Apr-26 A	11-Feb-27	4,192,992.00	3,986,992.40	10,226,640.03	-35
SITE WORKS		255	37.47%	35.64%	15-Apr-26	30-Dec-26	04-Apr-26 A	11-Feb-27	3,394,051.13	3,228,794.22	9,058,565.25	-36
EARTH WORKS		68	100%	100%	15-Apr-26	06-Jul-26	04-Apr-26 A	05-Aug-26 A	494,887.02	494,887.02	494,887.02	-25
LANDSCAPE WORKS		222	34.01%	31.46%	24-May-26	30-Dec-26	17-May-26 A	11-Feb-27	2,892,729.84	2,675,413.87	8,505,184.90	-36
PLAYGROUND AREA		222	48.26%	49.89%	24-May-26	27-Dec-26	19-May-26 A	11-Feb-27	661,090.90	683,464.16	1,369,978.66	-39
FOOTBALL PLAYGROUND		209	35%	35%	24-May-26	13-Dec-26	19-May-26 A	27-Jan-27	110,897.50	110,897.50	316,849.99	-38
PADEL PLAYGROUND		189	45%	70%	20-Jun-26	19-Dec-26	19-May-26 A	27-Jan-27	105,292.80	163,788.80	233,984.00	-33
BASKETBALL PLAYGROUND		172	69.52%	69.52%	14-Jul-26	23-Dec-26	19-May-26 A	01-Feb-27	221,133.58	221,133.58	318,089.68	-33
PADEL FENCE		92	30.26%	4.22%	01-Sep-26	16-Nov-26	08-Aug-26 A	19-Dec-26	41,982.68	5,859.94	138,749.98	-27
CURBSTOEN/INTERLOCK		110	50.17%	50.17%	06-Oct-26	27-Dec-26	15-Aug-26 A	11-Feb-27	181,784.34	181,784.34	362,305.01	-39
AIR DOME		115	23.18%	23.18%	26-Sep-26	21-Dec-26	17-May-26 A	07-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-40
CIVIL WORKS		101	48.29%	48.29%	26-Sep-26	07-Dec-26	17-May-26 A	21-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-38
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	1,233,296.81	-37
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	25-Jan-27	06-Feb-27	0.00	0.00	1,513,591.54	-40
FINISHES WORKS		9	0%	0%	15-Dec-26	21-Dec-26	27-Jan-27	07-Feb-27	0.00	0.00	168,176.84	-40
IRRIGATION NETWORK		139	83.53%	83.53%	28-Jun-26	30-Nov-26	18-Aug-26 A	08-Dec-26	127,308.67	127,308.67	152,414.87	-6
NATURAL GROUND		26	0%	27.12%	17-Nov-26	30-Nov-26	27-Oct-26 A	08-Dec-26	0.00	52,000.00	191,740.00	-6
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	28-Nov-26	347,251.46	104,175.44	347,251.46	-23
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	28-Nov-26	367,633.90	183,816.95	367,633.90	-22
GENERAL/FURNITURE		78	19.12%	47.87%	19-Oct-26	30-Dec-26	03-Oct-26 A	13-Jan-27	89,917.40	225,121.14	470,271.40	-11
PARKING		24	11%	100%	01-Nov-26	28-Nov-26	16-May-26 A	12-Oct-26 A	6,434.27	58,493.33	58,493.33	40
TOILET/SERVICE BUILDING		216	68.4%	64.91%	02-Jul-26	31-Dec-26	21-May-26 A	30-Jan-27	798,940.88	758,198.17	1,168,074.78	-24
STRUCTURE WORKS		58	100%	100%	02-Jul-26	07-Sep-26	21-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	31
MASONARY WORK		5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
THERMAL & MOISTER PROTECTION		54	100%	95.21%	29-Aug-26	21-Sep-26	26-Sep-26 A	11-Nov-26	34,698.32	33,037.59	34,698.32	-42
MECHANICAL WORK		167	62.8%	52.33%	16-Jul-26	19-Dec-26	18-Jul-26 A	24-Dec-26	166,205.09	138,508.96	264,673.10	-4
ELECTRICAL WORKS		118	53.29%	53.29%	13-Sep-26	19-Dec-26	19-Jul-26 A	30-Jan-27	206,217.32	206,217.32	386,998.59	-35
DOORS/WINDOWS		120	88.57%	100%	17-Sep-26	31-Dec-26	20-Oct-26 A	02-Nov-26 A	60,445.68	68,245.12	68,245.12	52
METAL WORKS		75	57.14%	71.43%	14-Sep-26	23-Nov-26	16-Sep-26 A	07-Nov-26	7,799.44	9,749.30	13,649.02	15
FINISHING WORKS		102	80.52%	76.6%	22-Sep-26	12-Dec-26	10-Aug-26 A	07-Jan-27	133,767.24	127,256.05	166,130.97	-22
SPECIALTIES WORK		64	25%	0%	18-Oct-26	17-Dec-26	15-Nov-26	28-Jan-27	14,623.96	0.00	58,495.83	-35
TESTING & COMMISSIONING		31	0%	0%	20-Dec-26	02-Jan-27	07-Jan-27	13-Feb-27	0.00	0.00	0.00	-35
HASA OASIS		312	43.38%	46.83%	03-Mar-26	02-Jan-27	04-Mar-26 A	24-Feb-27	4,319,245.64	4,662,792.85	9,955,979.43	-44
MOBILIZATION		32	0%	0%	03-Mar-26	12-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
ENGINEERING		248	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	30-Dec-26	0.00	0.00	0.00	-10
PROCUREMENT		220	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	24-Jan-27	0.00	0.00	0.00	-45
CONSTRUCTION PHASE		293	43.38%	46.83%	29-Mar-26	31-Dec-26	04-Apr-26 A	15-Feb-27	4,319,245.64	4,662,792.85	9,955,979.43	-38
SITE WORKS		292	39.19%	42.59%	29-Mar-26	31-Dec-26	04-Apr-26 A	15-Feb-27	3,444,696.75	3,744,045.05	8,789,975.14	-38
EARTH WORKS		43	100%	100%	29-Mar-26	17-May-26	04-Apr-26 A	08-Aug-26 A	294,826.31	294,826.31	294,826.31	-67
LANDSCAPE WORKS		251	37.34%	40.19%	16-May-26	31-Dec-26	16-May-26 A	15-Feb-27	3,149,870.44	3,390,725.41	8,436,655.50	-38
PLAYGROUND AREA		251	74.11%	76.9%	16-May-26	31-Dec-26	18-May-26 A	15-Feb-27	964,448.14	1,000,815.42	1,301,449.27	-38
FOOTBALL PLAYGROUND		194	82.64%	85%	16-May-26	09-Dec-26	18-May-26 A	02-Jan-27	261,853.88	269,322.49	316,849.99	-19
PADEL PLAYGROUND		192	45%	70%	11-Jun-26	31-Dec-26	18-May-26 A	23-Jan-27	105,292.80	163,788.80	233,984.00	-18
BASKETBALL PLAYGROUND		170	70.49%	70.92%	07-Jul-26	31-Dec-26	18-May-26 A	23-Jan-27	234,996.44	236,425.54	333,381.64	-18
PADEL FENCE		87	0%	9.24%	28-Nov-26	31-Dec-26	06-Aug-26 A	15-Feb-27	0.00	5,077.72	54,928.63	-38
CURBSTOEN/INTERLOCK		19	100%	90.03%	09-Sep-26	01-Oct-26	12-Aug-26 A	05-Nov-26	362,305.01	326,200.88	362,305.01	-29
AIR DOME		159	23.18%	23.18%	30-Jul-26	10-Dec-26	16-May-26 A	02-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-45
CIVIL WORKS		149	48.29%	48.29%	30-Jul-26	07-Dec-26	16-May-26 A	21-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-38
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	29-Dec-26	16-Jan-27	0.00	0.00	1,233,296.81	-33
ELECTRICAL WORKS		14	0%	0%	02-Dec-26	10-Dec-26	17-Jan-27	02-Feb-27	0.00	0.00	1,513,591.54	-45
FINISHES WORKS		30	0%	0%	15-Nov-26	10-Dec-26	29-Dec-26	02-Feb-27	0.00	0.00	168,176.84	-45
IRRIGATION NETWORK		105	39.78%	83.53%	03-Sep-26	07-Dec-26	18-Jul-26 A	05-Jan-27	60,637.90	127,308.67	152,414.87	-24
NATURAL GROUND		15	0%	70.17%	29-Nov-26	07-Dec-26	13-Oct-26 A	08-Nov-26	0.00	134,544.00	191,740.00	26
PLANTING		101	87.76%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	05-Nov-26	304,731.71	240,773.38	347,251.46	-2
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	02-Nov-26	367,633.90	294,107.12	367,633.90	-13

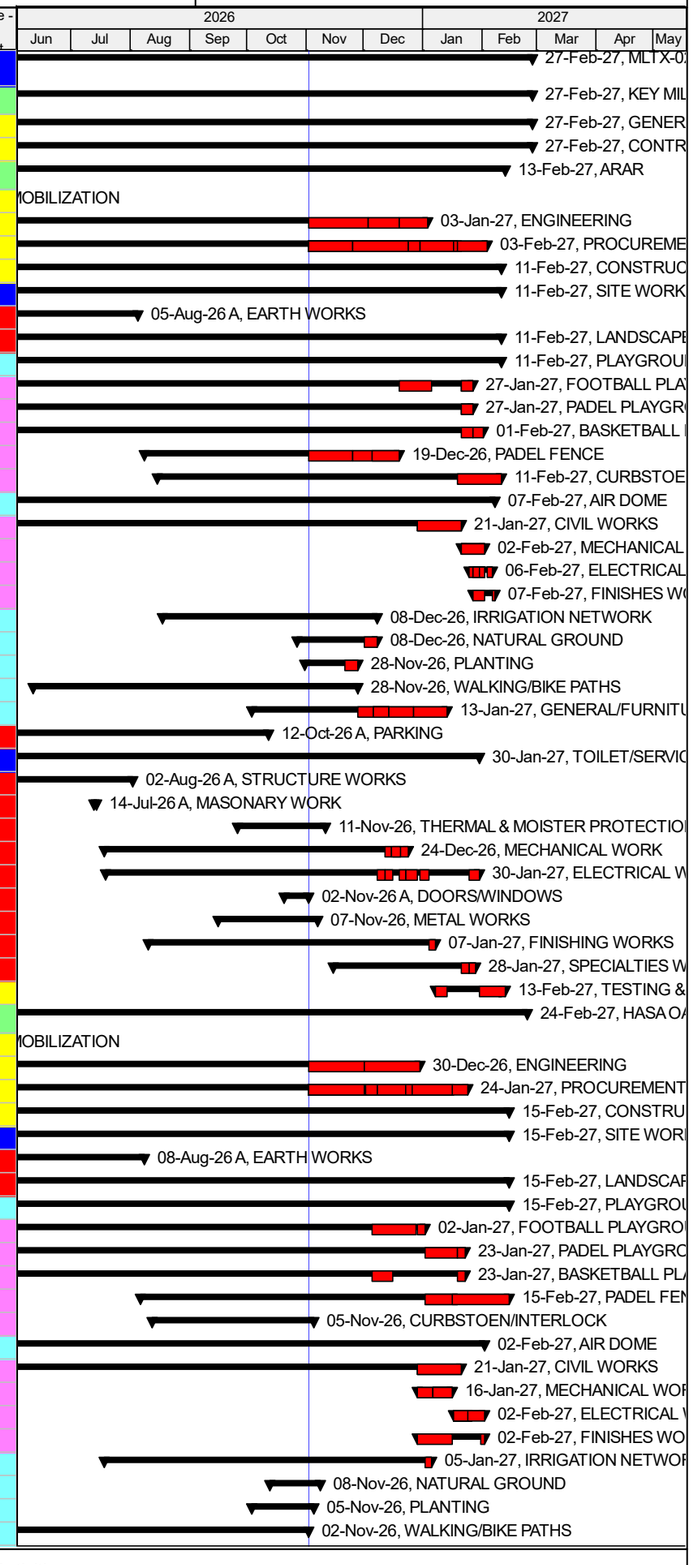

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	97	32.51%	62.44%	06-Oct-26	24-Dec-26	03-Sep-26 A	27-Jan-27	152,891.28	293,649.30	470,271.40	-28
	PARKING	12	0%	100%	24-Nov-26	07-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	68
	TOILET/SERVICE BUILDING	258	75%	78.79%	09-May-26	23-Dec-26	24-May-26 A	28-Jan-27	874,548.89	918,747.80	1,166,004.29	-30
	STRUCTURE WORKS	45	100%	100%	09-May-26	02-Jul-26	24-May-26 A	10-Aug-26 A	162,899.73	162,899.73	162,899.73	-33
	MASONARY WORK	5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
	THERMAL & MOISTER PROTECTION	41	100%	95.21%	04-Jul-26	19-Aug-26	10-Sep-26 A	23-Nov-26	34,698.32	33,037.59	34,698.32	-80
	MECHANICAL WORK	121	99.26%	99.26%	24-Aug-26	21-Dec-26	12-Jul-26 A	13-Jan-27	262,723.23	262,723.23	264,673.10	-19
	ELECTRICAL WORKS	122	53.29%	59.43%	03-Sep-26	21-Dec-26	14-Jul-26 A	25-Jan-27	206,217.58	229,999.44	386,998.85	-29
	DOORS/WINDOWS	213	14.29%	100%	04-Jul-26	16-Dec-26	28-Sep-26 A	28-Oct-26 A	9,749.30	68,245.12	68,245.12	43
	METAL WORKS	59	100%	71.43%	03-Sep-26	20-Oct-26	06-Sep-26 A	12-Dec-26	13,649.02	9,749.30	13,649.02	-44
	FINISHING WORKS	115	96.13%	78.09%	20-Aug-26	16-Dec-26	17-Aug-26 A	28-Jan-27	157,703.65	128,110.12	164,060.22	-36
	SPECIALTIES WORK	97	25%	20%	27-Sep-26	23-Dec-26	04-Oct-26 A	18-Jan-27	14,623.96	11,699.17	58,495.83	-21
	TESTING & COMMISSIONING	28	0%	0%	08-Dec-26	02-Jan-27	21-Jan-27	24-Feb-27	0.00	0.00	0.00	-44
	DAMMAM	305	42.13%	41.31%	03-Mar-26	02-Jan-27	04-Mar-26 A	27-Feb-27	4,134,869.23	4,054,484.46	9,815,232.20	-46
	MOBILIZATION	33	0%	0%	03-Mar-26	13-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
	ENGINEERING	250	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	30-Dec-26	0.00	0.00	0.00	-15
	PROCUREMENT	251	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	03-Feb-27	0.00	0.00	0.00	-37
	CONSTRUCTION PHASE	270	42.13%	41.31%	16-Apr-26	31-Dec-26	04-Apr-26 A	27-Feb-27	4,134,869.23	4,054,484.46	9,815,232.20	-47
	SITE WORKS	270	37.51%	36.39%	16-Apr-26	31-Dec-26	04-Apr-26 A	27-Feb-27	3,244,214.37	3,147,680.96	8,649,227.95	-47
	EARTH WORKS	44	100%	100%	16-Apr-26	09-Jun-26	04-Apr-26 A	13-Aug-26 A	263,237.78	263,237.78	263,237.78	-55
	LANDSCAPE WORKS	248	35.09%	33.94%	12-May-26	31-Dec-26	19-May-26 A	27-Feb-27	2,922,483.27	2,825,949.85	8,327,496.85	-47
	PLAYGROUND AREA	239	78.58%	57.99%	12-May-26	31-Dec-26	19-May-26 A	10-Feb-27	1,010,607.86	745,864.17	1,286,157.31	-34
	FOOTBALL PLAYGROUND	221	85%	35%	12-May-26	15-Dec-26	19-May-26 A	30-Jan-27	269,322.49	110,897.50	316,849.99	-38
	PADEL PLAYGROUND	219	70%	70%	24-May-26	24-Dec-26	19-May-26 A	08-Feb-27	163,788.80	163,788.80	233,984.00	-38
	BASKETBALL PLAYGROUND	170	67.65%	69.52%	26-Jul-26	31-Dec-26	19-May-26 A	10-Feb-27	215,191.56	221,133.58	318,089.68	-34
	PADEL FENCE	56	0%	9.24%	25-Nov-26	24-Dec-26	08-Aug-26 A	30-Jan-27	0.00	5,077.72	54,928.63	-30
	CURBSTOEN/INTERLOCK	150	100%	67.61%	27-Aug-26	21-Sep-26	10-Aug-26 A	09-Nov-26	362,305.01	244,966.57	362,305.01	-40
	AIR DOME	195	23.18%	23.18%	18-Jun-26	24-Dec-26	14-Jul-26 A	02-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-33
	CIVIL WORKS	185	48.29%	48.29%	18-Jun-26	07-Dec-26	14-Jul-26 A	21-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-38
	MECHANICAL WORKS	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	1,233,296.81	-38
	ELECTRICAL WORKS	10	0%	0%	08-Dec-26	24-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	1,513,591.54	-33
	FINISHES WORKS	4	0%	0%	12-Dec-26	15-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	168,176.84	-38
	IRRIGATION NETWORK	127	83.53%	83.53%	10-Sep-26	02-Dec-26	24-Aug-26 A	07-Feb-27	127,308.67	127,308.67	152,414.87	-56
	NATURAL GROUND	40	56.37%	30.51%	10-Oct-26	12-Nov-26	20-Oct-26 A	07-Dec-26	108,091.60	58,500.00	191,740.00	-20
	PLANTING	27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	14-Nov-26	0.00	69,450.29	347,251.46	42
	WALKING/BIKE PATHS	31	100%	100%	22-Sep-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	273,767.20	273,767.20	273,767.20	35
	GENERAL/FURNITURE	133	21.94%	53.49%	22-Sep-26	31-Dec-26	20-Sep-26 A	27-Feb-27	103,180.43	251,532.00	470,271.40	-47
	PARKING	15	100%	100%	14-Oct-26	31-Oct-26	18-Jul-26 A	19-Sep-26 A	58,493.33	58,493.33	58,493.33	35
	TOILET/SERVICE BUILDING	213	76.39%	77.77%	01-Jun-26	29-Dec-26	23-May-26 A	06-Feb-27	890,654.86	906,803.50	1,166,004.25	-32
	STRUCTURE WORKS	54	100%	100%	01-Jun-26	02-Aug-26	23-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	0
	MASONARY WORK	5	100%	100%	06-Jul-26	11-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	2
	THERMAL & MOISTER PROTECTION	21	100%	95.21%	03-Aug-26	26-Aug-26	25-Aug-26 A	11-Nov-26	34,698.32	33,037.59	34,698.32	-64
	MECHANICAL WORK	109	99.26%	99.26%	09-Sep-26	26-Dec-26	12-Jul-26 A	16-Jan-27	262,723.23	262,723.23	264,673.10	-17
	ELECTRICAL WORKS	118	53.29%	55.12%	12-Sep-26	29-Dec-26	14-Jul-26 A	28-Jan-27	206,217.55	213,302.65	386,998.82	-25
	DOORS/WINDOWS	118	91.43%	100%	19-Sep-26	27-Dec-26	17-Sep-26 A	26-Oct-26 A	62,395.54	68,245.12	68,245.12	53
	METAL WORKS	71	100%	71.43%	10-Sep-26	26-Oct-26	05-Sep-26 A	17-Dec-26	13,649.02	9,749.30	13,649.02	-44
	FINISHING WORKS	106	73.85%	80.98%	27-Aug-26	21-Dec-26	17-Aug-26 A	30-Dec-26	121,163.41	132,862.61	164,060.21	-7
	SPECIALTIES WORK	32	25%	20%	27-Oct-26	23-Dec-26	12-Oct-26 A	06-Feb-27	14,623.96	11,699.17	58,495.83	-37
	TESTING & COMMISSIONING	8	0%	0%	24-Dec-26	02-Jan-27	16-Feb-27	27-Feb-27	0.00	0.00	0.00	-46
	PROJECT CLOSEOUT & DEMOBILIZATION	29	0%	0%	08-Dec-26	02-Jan-27	21-Jan-27	25-Feb-27	0.00	0.00	0.00	-45
	As-Built DWGs	27	0%	0%	08-Dec-26	31-Dec-26	21-Jan-27	23-Feb-27	0.00	0.00	0.00	-44
	Demobilization	6	0%	0%	28-Dec-26	02-Jan-27	17-Feb-27	25-Feb-27	0.00	0.00	0.00	-45

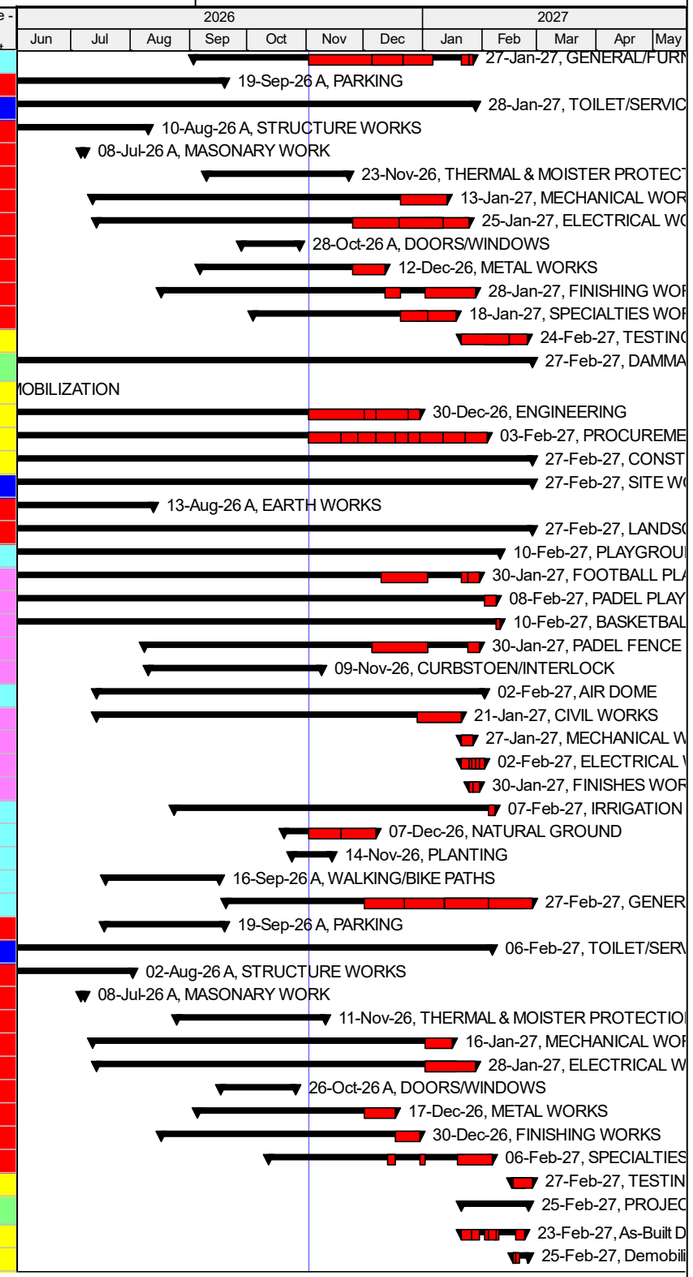

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
