
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oa		186	12.93%	8.84%	04-May-26	02-Jan-27	01-Jun-26 A	27-Feb-27	2,452,788.75	1,676,780.81	18,970,362.77	-46
KEY MILESTONES		46	0%	0%	17-Dec-26	02-Jan-27	03-Jan-27	27-Feb-27	0.00	0.00	0.00	-46
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	27-Feb-27	27-Feb-27	0.00	0.00	0.00	-46
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		27-Feb-27	0.00	0.00	0.00	-46
CONTRACTUAL MILESTONE		46	0%	0%	17-Dec-26	02-Jan-27	03-Jan-27	27-Feb-27	0.00	0.00	0.00	-46
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		02-Jan-27		27-Feb-27	0.00	0.00	0.00	-46
MLTX-02-005-MS-1100	Completion of Engineering	0	0%	0%		17-Dec-26		03-Jan-27	0.00	0.00	0.00	-13
MLTX-02-005-MS-1130	Completion of Toilet Building	0	0%	0%		31-Dec-26		15-Feb-27	0.00	0.00	0.00	-38
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		31-Dec-26		15-Feb-27	0.00	0.00	0.00	-38
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		31-Dec-26		27-Feb-27	0.00	0.00	0.00	-47
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		31-Dec-26		11-Feb-27	0.00	0.00	0.00	-35
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		31-Dec-26		15-Feb-27	0.00	0.00	0.00	-38
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		31-Dec-26		27-Feb-27	0.00	0.00	0.00	-47
ARAR		130	13.37%	8.02%	27-Jun-26	02-Jan-27	11-Jun-26 A	13-Feb-27	907,307.84	544,155.48	6,783,803.11	-35
ENGINEERING		53	0%	0%	19-Sep-26	08-Dec-26	02-Nov-26	03-Jan-27	0.00	0.00	0.00	-21
SHOP DRAWINGS		53	0%	0%	19-Sep-26	08-Dec-26	02-Nov-26	03-Jan-27	0.00	0.00	0.00	-21
SHOP DRAWINGS SUBMISSION		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
ELECTRICAL WORKS		27	0%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	27	100%	0%	19-Sep-26	20-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-37
SHOP DRAWINGS APPROVALS		26	0%	0%	09-Nov-26	08-Dec-26	03-Dec-26	03-Jan-27	0.00	0.00	0.00	-21
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		26	0%	0%	09-Nov-26	08-Dec-26	03-Dec-26	03-Jan-27	0.00	0.00	0.00	-21
ELECTRICAL WORKS		26	0%	0%	09-Nov-26	08-Dec-26	03-Dec-26	03-Jan-27	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Approval for Power Layout	13	0%	0%	09-Nov-26	23-Nov-26	03-Dec-26	19-Dec-26	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	13	0%	0%	24-Nov-26	08-Dec-26	19-Dec-26	03-Jan-27	0.00	0.00	0.00	-21
PROCUREMENT		80	0%	0%	27-Jun-26	15-Dec-26	02-Nov-26	03-Feb-27	0.00	0.00	0.00	-42
SHORT LEAD ITEM		80	0%	0%	27-Jun-26	15-Dec-26	02-Nov-26	03-Feb-27	0.00	0.00	0.00	-42
TOILET/SERVICE WORKS		69	0%	0%	27-Jun-26	28-Nov-26	02-Nov-26	21-Jan-27	0.00	0.00	0.00	-46
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-E	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-109
SWITCHES/SOCKETS		27	0%	0%	28-Oct-26	28-Nov-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-4
MLTX-02-005-PR-E	Material Delivery for Switches/Sockets	27	15.19%	0%	28-Oct-26	28-Nov-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-4
DISTRIBUTION PANNELS		15	0%	0%	04-Oct-26	20-Oct-26	06-Dec-26	23-Dec-26	0.00	0.00	0.00	-54
MLTX-02-005-PR-E	Material Delivery for Distribution Panels	15	100%	0%	04-Oct-26	20-Oct-26	06-Dec-26	23-Dec-26	0.00	0.00	0.00	-54
FURNITURES		69	0%	0%	30-Aug-26	19-Nov-26	02-Nov-26	21-Jan-27	0.00	0.00	0.00	-53
MLTX-02-005-PR-E	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	-54
MLTX-02-005-PR-E	Material Delivery for Furnitures	40	60.25%	0%	05-Oct-26	19-Nov-26	06-Dec-26	21-Jan-27	0.00	0.00	0.00	-53
PLAYGROUND WORKS		80	0%	0%	15-Jul-26	15-Dec-26	02-Nov-26	03-Feb-27	0.00	0.00	0.00	-42
PVC MEMBRANE		21	0%	0%	29-Sep-26	22-Oct-26	19-Nov-26	14-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-E	Material Delivery for PVC Membrane	21	100%	0%	29-Sep-26	22-Oct-26	19-Nov-26	14-Dec-26	0.00	0.00	0.00	-44
ARTIFICIAL TURF		12	0%	0%	26-Oct-26	08-Nov-26	15-Dec-26	29-Dec-26	0.00	0.00	0.00	-43
MLTX-02-005-PR-E	Material Delivery for Artificial TURF	12	50.83%	0%	26-Oct-26	08-Nov-26	15-Dec-26	29-Dec-26	0.00	0.00	0.00	-43
RUBBER GRANULES		32	0%	0%	10-Oct-26	15-Nov-26	19-Nov-26	27-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-E	Material Delivery for Rubber Granules	32	62.81%	0%	10-Oct-26	15-Nov-26	19-Nov-26	27-Dec-26	0.00	0.00	0.00	-35
PADEL GLASS		18	0%	0%	16-Nov-26	06-Dec-26	29-Dec-26	19-Jan-27	0.00	0.00	0.00	-37
MLTX-02-005-PR-E	Material Delivery for Padel Glass	18	0%	0%	16-Nov-26	06-Dec-26	29-Dec-26	19-Jan-27	0.00	0.00	0.00	-37
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-53
MLTX-02-005-PR-E	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-53
BITUMINOUS BASE & WEARING COURSE		27	0%	0%	29-Sep-26	29-Oct-26	19-Nov-26	21-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-S	Material Delivery for the Site	27	100%	0%	29-Sep-26	29-Oct-26	19-Nov-26	21-Dec-26	0.00	0.00	0.00	-44
INTERLOCKING PAVING		17	0%	0%	11-Nov-26	30-Nov-26	30-Dec-26	19-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-S	Material Delivery for Interlocking Block Pavers	17	0%	0%	11-Nov-26	30-Nov-26	30-Dec-26	19-Jan-27	0.00	0.00	0.00	-42
MARKING PAINT		37	0%	0%	10-Sep-26	19-Oct-26	02-Nov-26	15-Dec-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-S	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-S	Material Delivery for Marking Paint	17	100%	0%	30-Sep-26	19-Oct-26	25-Nov-26	15-Dec-26	0.00	0.00	0.00	-48
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Sep-26	21-Oct-26	19-Nov-26	13-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-S	PO for Air Difussers/Grills	5	100%	0%	29-Sep-26	04-Oct-26	19-Nov-26	25-Nov-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-S	Material Delivery for Air Difussers/Grills	15	100%	0%	05-Oct-26	21-Oct-26	25-Nov-26	13-Dec-26	0.00	0.00	0.00	-44
DISTRIBUTION BOARDS		20	0%	0%	29-Sep-26	21-Oct-26	19-Nov-26	13-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-S	PO for Distribution Boards	5	100%	0%	29-Sep-26	04-Oct-26	19-Nov-26	25-Nov-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-S	Material Delivery for Distribution Boards	15	100%	0%	05-Oct-26	21-Oct-26	25-Nov-26	13-Dec-26	0.00	0.00	0.00	-44
POWER CABLES		60	0%	0%	05-Oct-26	15-Dec-26	25-Nov-26	03-Feb-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-S	PO for Power Cables	5	100%	0%	05-Oct-26	10-Oct-26	25-Nov-26	01-Dec-26	0.00	0.00	0.00	-44

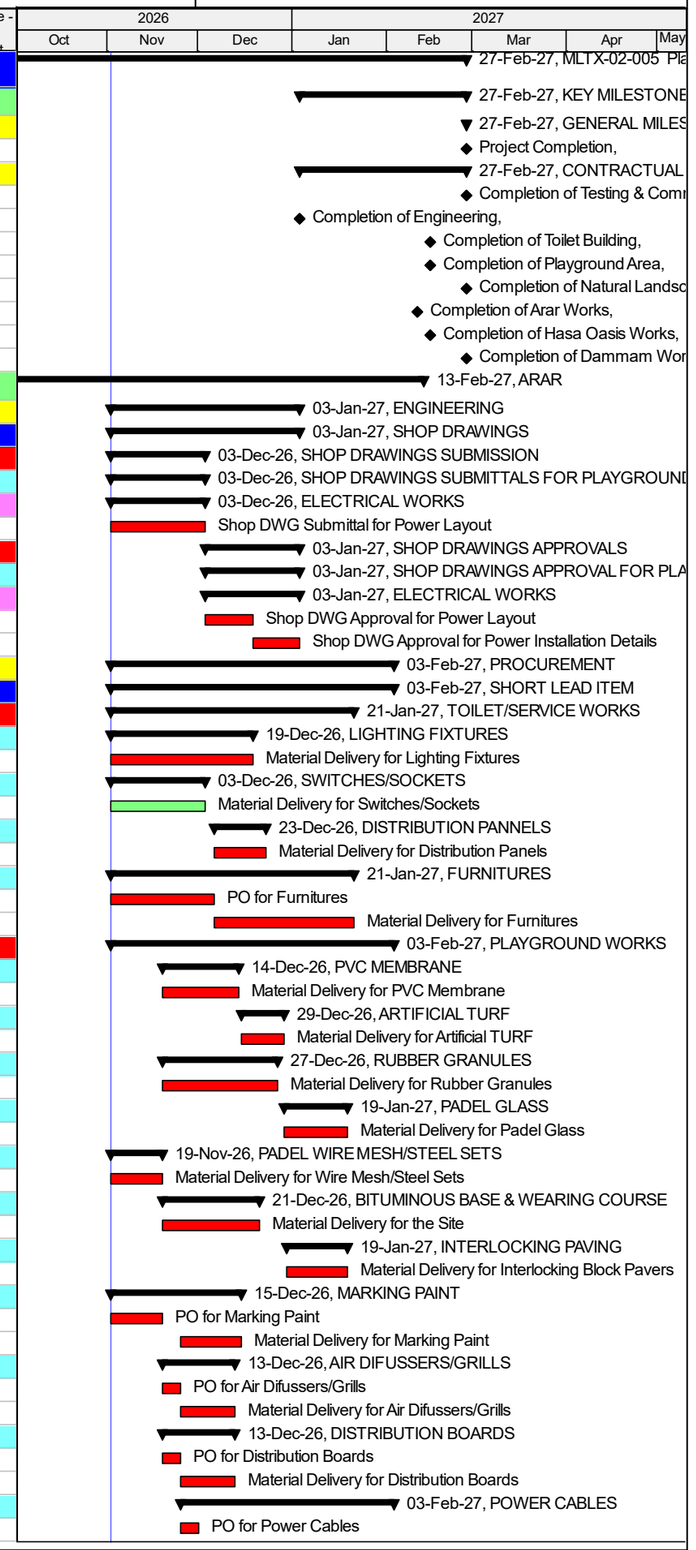

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for Power Cables	30	0%	0%	11-Nov-26	15-Dec-26	30-Dec-26	03-Feb-27	0.00	0.00	0.00	-42
LIGHT FIXTURES		10	0%	0%	11-Oct-26	21-Oct-26	01-Dec-26	13-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	100%	0%	11-Oct-26	21-Oct-26	01-Dec-26	13-Dec-26	0.00	0.00	0.00	-44
CCTV MATERIALS		50	0%	0%	26-Sep-26	10-Nov-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-9	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-32
MLTX-02-005-PR-9	Material Delivery for CCTV	15	47.33%	0%	25-Oct-26	10-Nov-26	13-Dec-26	30-Dec-26	0.00	0.00	0.00	-42
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-93
LANDSCAPE WORKS		67	0%	0%	15-Jul-26	23-Nov-26	02-Nov-26	19-Jan-27	0.00	0.00	0.00	-48
PAVEMENT MARKING		67	0%	0%	15-Jul-26	23-Nov-26	02-Nov-26	19-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	30	37%	0%	20-Oct-26	23-Nov-26	15-Dec-26	19-Jan-27	0.00	0.00	0.00	-48
TRAFFIC SIGNS		10	0%	0%	13-Aug-26	16-Sep-26	02-Nov-26	14-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-9	Material Delivery for Traffic Signs	10	100%	0%	13-Aug-26	16-Sep-26	02-Nov-26	14-Nov-26	0.00	0.00	0.00	-48
AGRICULTURE SOIL		22	0%	0%	18-Aug-26	12-Sep-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-9	Material Delivery for Agriculture Soil	22	100%	0%	18-Aug-26	12-Sep-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	-64
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	14-Nov-26	25-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	14-Nov-26	25-Nov-26	0.00	0.00	0.00	-48
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	25	44.4%	0%	20-Oct-26	17-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-11
LONG LEAD ITEM		65	0%	0%	27-Sep-26	10-Dec-26	02-Nov-26	17-Jan-27	0.00	0.00	0.00	-31
PLAYGROUND WORKS		65	0%	0%	27-Sep-26	10-Dec-26	02-Nov-26	17-Jan-27	0.00	0.00	0.00	-31
STEEL TENSION CABLES		27	0%	0%	27-Sep-26	27-Oct-26	02-Nov-26	03-Dec-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-9	Staging time	12	100%	0%	14-Oct-26	27-Oct-26	19-Nov-26	03-Dec-26	0.00	0.00	0.00	-31
EMERGENCY DOORS		65	0%	0%	26-Oct-26	05-Dec-26	02-Nov-26	17-Jan-27	0.00	0.00	0.00	-36
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	20	30.5%	0%	26-Oct-26	17-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-9	Staging time	15	0%	0%	18-Nov-26	05-Dec-26	30-Dec-26	17-Jan-27	0.00	0.00	0.00	-36
PRESSURE UNITS		30	0%	0%	26-Oct-26	29-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	24.4%	0%	26-Oct-26	23-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-9	Staging time	5	0%	0%	24-Nov-26	29-Nov-26	01-Dec-26	07-Dec-26	0.00	0.00	0.00	-6
AIR LOCK DOORS		50	0%	0%	14-Oct-26	10-Dec-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	80.5%	0%	14-Oct-26	05-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	0%	0%	07-Nov-26	05-Dec-26	25-Nov-26	24-Dec-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-9	Staging time	5	0%	0%	06-Dec-26	10-Dec-26	24-Dec-26	30-Dec-26	0.00	0.00	0.00	-16
CONSTRUCTION PHASE		129	13.37%	8.02%	13-Sep-26	30-Dec-26	11-Jun-26 A	11-Feb-27	907,307.84	544,155.48	6,783,803.11	-36
SITE WORKS		111	12.11%	7.75%	17-Sep-26	30-Dec-26	11-Jun-26 A	11-Feb-27	765,465.90	489,653.93	6,319,424.95	-36
LANDSCAPE WORKS		111	12.11%	7.75%	17-Sep-26	30-Dec-26	11-Jun-26 A	11-Feb-27	765,465.90	489,653.93	6,319,424.95	-36
PLAYGROUND AREA		87	5.26%	0%	01-Oct-26	27-Dec-26	02-Nov-26	11-Feb-27	36,122.74	0.00	686,514.50	-39
FOOTBALL PLAYGROUND		34	0%	0%	17-Nov-26	13-Dec-26	19-Dec-26	27-Jan-27	0.00	0.00	205,952.49	-38
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	15	0%	0%	17-Nov-26	03-Dec-26	19-Dec-26	05-Jan-27	0.00	0.00	158,424.99	-27
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	31,685.00	-38
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	15,842.50	-38
PADEL PLAYGROUND		5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	70,195.20	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	58,496.00	-33
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	11,699.20	-33
BASKETBALL PLAYGROUND		9	0%	0%	14-Dec-26	23-Dec-26	21-Jan-27	01-Feb-27	0.00	0.00	96,956.10	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	80,796.75	-33
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	4	0%	0%	20-Dec-26	23-Dec-26	27-Jan-27	01-Feb-27	0.00	0.00	16,159.35	-33
PADEL FENCE		40	27.18%	0%	01-Oct-26	16-Nov-26	02-Nov-26	19-Dec-26	36,122.74	0.00	132,890.04	-27
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	02-Nov-26	25-Nov-26	30,677.48	0.00	30,677.48	-27
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	20	35.5%	0%	25-Oct-26	16-Nov-26	25-Nov-26	19-Dec-26	5,445.25	0.00	15,338.75	-27
MLTX-02-005-CI	Install of Fence Gates	12	0%	0%	03-Nov-26	16-Nov-26	05-Dec-26	19-Dec-26	0.00	0.00	86,873.81	-27
CURBSTOEN/INTERLOCK		20	0%	0%	05-Dec-26	27-Dec-26	19-Jan-27	11-Feb-27	0.00	0.00	180,520.67	-39
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	05-Dec-26	27-Dec-26	19-Jan-27	11-Feb-27	0.00	0.00	180,520.67	-39
AIR DOME		34	0%	0%	15-Nov-26	21-Dec-26	29-Dec-26	07-Feb-27	0.00	0.00	4,306,367.09	-40
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	1,391,301.90	-38
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	942,830.33	-38
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	448,471.57	-38
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	1,233,296.81	-37
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	728,766.30	-37
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	336,353.67	-37
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-37
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	25-Jan-27	06-Feb-27	0.00	0.00	1,513,591.54	-40

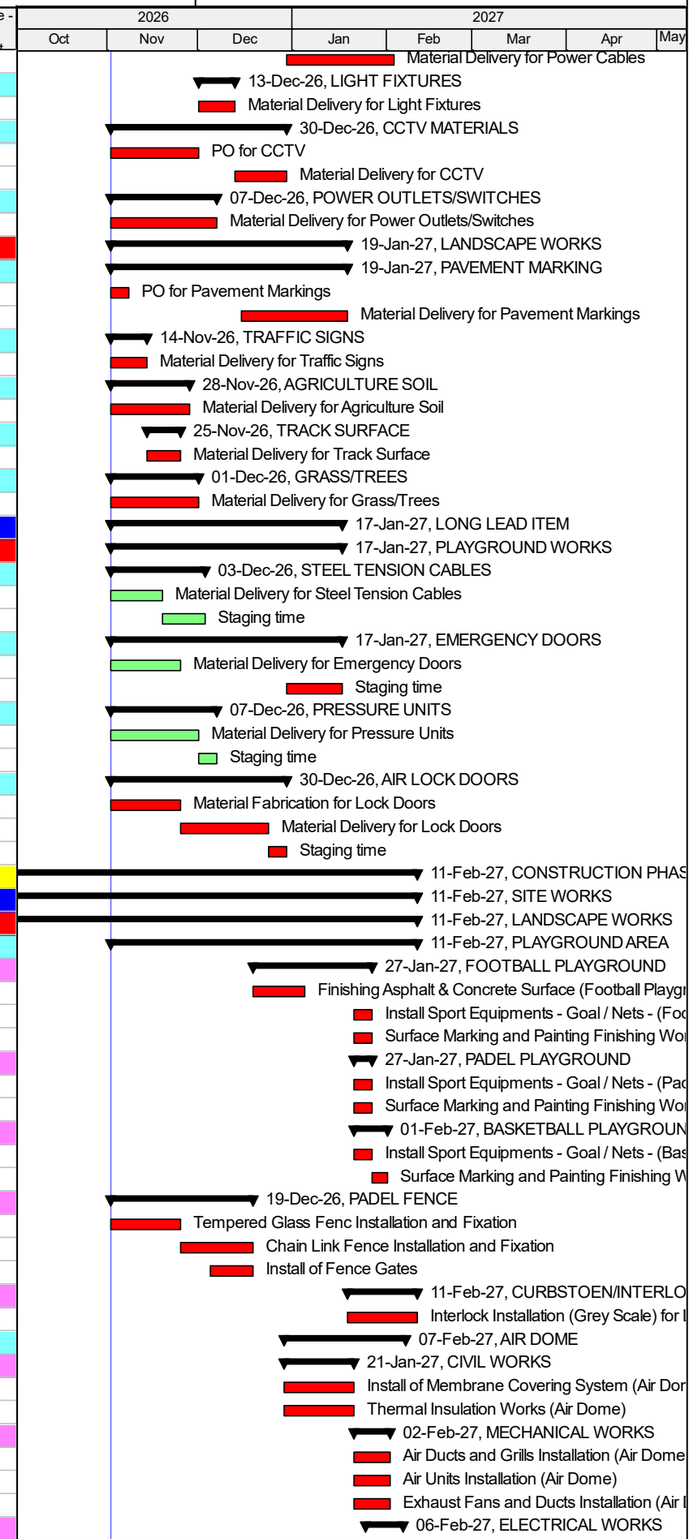

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Light Fixture Works (Air Dome)	7	0%	0%	13-Dec-26	20-Dec-26	25-Jan-27	02-Feb-27	0.00	0.00	224,235.78	-37
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	27-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-37
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	27-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-37
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	3	0%	0%	17-Dec-26	20-Dec-26	30-Jan-27	02-Feb-27	0.00	0.00	504,530.51	-37
MLTX-02-005-CI	Control System Installation (Air Dome)	2	0%	0%	19-Dec-26	20-Dec-26	03-Feb-27	06-Feb-27	0.00	0.00	448,471.57	-40
FINISHES WORKS		9	0%	0%	15-Dec-26	21-Dec-26	27-Jan-27	07-Feb-27	0.00	0.00	168,176.84	-40
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	5	0%	0%	15-Dec-26	20-Dec-26	27-Jan-27	02-Feb-27	0.00	0.00	112,117.89	-37
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	1	0%	0%	21-Dec-26	21-Dec-26	06-Feb-27	07-Feb-27	0.00	0.00	56,058.95	-40
IRRIGATION NETWORK		3	0%	0%	28-Nov-26	30-Nov-26	05-Dec-26	08-Dec-26	0.00	0.00	25,106.20	-6
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	28-Nov-26	30-Nov-26	05-Dec-26	08-Dec-26	0.00	0.00	25,106.20	-6
NATURAL GROUND		26	0%	27.12%	17-Nov-26	30-Nov-26	27-Oct-26 A	08-Dec-26	0.00	52,000.00	191,740.00	-6
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	6	0%	0%	24-Nov-26	30-Nov-26	01-Dec-26	08-Dec-26	0.00	0.00	126,740.00	-6
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	80%	17-Nov-26	23-Nov-26	27-Oct-26 A	09-Nov-26	0.00	52,000.00	65,000.00	13
PLANTING		15	100%	30%	17-Sep-26	31-Oct-26	31-Oct-26 A	28-Nov-26	347,251.46	104,175.44	347,251.46	-23
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	100%	30%	17-Sep-26	24-Sep-26	31-Oct-26 A	28-Nov-26	104,175.44	31,252.63	104,175.44	-54
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	4	100%	30%	27-Oct-26	31-Oct-26	31-Oct-26 A	25-Nov-26	141,732.50	42,519.75	141,732.50	-21
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	100%	30%	26-Sep-26	30-Sep-26	31-Oct-26 A	26-Nov-26	101,343.52	30,403.06	101,343.52	-48
WALKING/BIKE PATHS		24	100%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	28-Nov-26	367,633.90	183,816.95	367,633.90	-22
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	28-Nov-26	187,554.12	93,777.06	187,554.12	-34
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	100%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	28-Nov-26	180,079.78	90,039.89	180,079.78	-22
GENERAL/FURNITURE		44	3.66%	37.91%	27-Oct-26	30-Dec-26	18-Oct-26 A	13-Jan-27	14,457.80	149,661.54	394,811.80	-11
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	2%	0%	02-Nov-26	07-Nov-26	28-Nov-26	03-Dec-26	1,871.88	0.00	93,594.00	-22
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	14-Dec-26	30-Dec-26	27-Dec-26	13-Jan-27	0.00	0.00	9,749.30	-11
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	72.86%	0%	27-Oct-26	03-Nov-26	28-Nov-26	06-Dec-26	12,585.92	0.00	17,274.79	-27
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	23-Nov-26	30-Nov-26	06-Dec-26	14-Dec-26	0.00	0.00	40,307.84	-11
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	23-Nov-26	30-Nov-26	06-Dec-26	14-Dec-26	0.00	0.00	32,757.76	-11
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	23-Nov-26	30-Nov-26	06-Dec-26	14-Dec-26	0.00	0.00	12,869.04	-11
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	01-Dec-26	13-Dec-26	14-Dec-26	27-Dec-26	0.00	0.00	12,186.67	-11
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	85%	08-Nov-26	22-Nov-26	18-Oct-26 A	17-Nov-26	0.00	149,661.54	176,072.40	5
TOILET/SERVICE BUILDING		118	30.54%	11.74%	13-Sep-26	19-Dec-26	03-Oct-26 A	30-Jan-27	141,841.94	54,501.55	464,378.16	-35
THERMAL & MOISTER PROTECTION		8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-42
MLTX-02-005-CN-110	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-42
MECHANICAL WORK		52	27.54%	5.48%	29-Sep-26	19-Dec-26	22-Oct-26 A	24-Dec-26	36,762.98	7,311.98	133,476.12	-4
HVAC SYSTEM		3	0%	0%	05-Dec-26	07-Dec-26	12-Dec-26	15-Dec-26	0.00	0.00	14,623.96	-6
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	0%	0%	05-Dec-26	07-Dec-26	12-Dec-26	15-Dec-26	0.00	0.00	14,623.96	-6
WATER SUPPLY SYSTEM		7	0%	0%	12-Dec-26	19-Dec-26	16-Dec-26	24-Dec-26	0.00	0.00	48,746.52	-4
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	0%	0%	12-Dec-26	19-Dec-26	16-Dec-26	24-Dec-26	0.00	0.00	48,746.52	-4
SEWER/DRAINAGE SYSTEM		48	53.94%	10.73%	29-Sep-26	12-Dec-26	22-Oct-26 A	20-Dec-26	36,762.98	7,311.98	68,155.77	-6
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	05-Oct-26	08-Oct-26	08-Nov-26	12-Nov-26	14,217.67	0.00	14,217.67	-29
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	15-Oct-26	17-Oct-26	12-Nov-26	15-Nov-26	10,358.68	0.00	10,358.68	-24
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	60%	29-Sep-26	04-Oct-26	22-Oct-26 A	08-Nov-26	12,186.63	7,311.98	12,186.63	-29
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	0%	0%	08-Dec-26	12-Dec-26	15-Dec-26	20-Dec-26	0.00	0.00	31,392.79	-6
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	15-Dec-26	17-Dec-26	0.00	0.00	1,949.87	-1
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	0%	0%	14-Dec-26	15-Dec-26	15-Dec-26	17-Dec-26	0.00	0.00	1,949.87	-1
ELECTRICAL WORKS		45	0%	0%	09-Nov-26	19-Dec-26	08-Dec-26	30-Jan-27	0.00	0.00	180,781.27	-35
FIXTURE WORKS		45	0%	0%	09-Nov-26	19-Dec-26	08-Dec-26	30-Jan-27	0.00	0.00	180,781.27	-35
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	0%	0%	09-Nov-26	14-Nov-26	23-Dec-26	29-Dec-26	0.00	0.00	102,367.69	-38
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	13-Dec-26	16-Dec-26	12-Dec-26	16-Dec-26	0.00	0.00	6,239.59	1
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	07-Dec-26	10-Dec-26	12-Dec-26	16-Dec-26	0.00	0.00	7,085.10	-4
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	0%	0%	01-Dec-26	03-Dec-26	08-Dec-26	12-Dec-26	0.00	0.00	6,824.51	-6
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	15-Dec-26	19-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	34,317.53	-35
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	07-Dec-26	10-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	14,259.43	-10
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	05-Dec-26	10-Dec-26	12-Dec-26	19-Dec-26	0.00	0.00	2,437.33	-6
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	0%	0%	05-Dec-26	08-Dec-26	30-Dec-26	04-Jan-27	0.00	0.00	7,250.09	-22
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	02-Nov-26	07-Nov-26	3,899.72	0.00	3,899.72	-41
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	02-Nov-26	07-Nov-26	3,899.72	0.00	3,899.72	-41
FINISHING WORKS		67	98.35%	45.34%	06-Oct-26	12-Dec-26	20-Oct-26 A	07-Jan-27	69,948.00	32,243.02	71,117.94	-22
FLOOR FINISHES		57	71.43%	0%	06-Oct-26	12-Dec-26	02-Nov-26	07-Jan-27	2,924.82	0.00	4,094.76	-22
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	02-Nov-26	07-Nov-26	2,924.82	0.00	2,924.82	-23
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	09-Dec-26	12-Dec-26	04-Jan-27	07-Jan-27	0.00	0.00	1,169.94	-22
WALL FINISHES		33	100%	48.11%	06-Oct-26	31-Oct-26	20-Oct-26 A	29-Nov-26	67,023.18	32,243.02	67,023.18	-24
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	10-Nov-26	35,825.58	32,243.02	35,825.58	-23
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	24-Oct-26	31-Oct-26	21-Nov-26	29-Nov-26	31,197.60	0.00	31,197.60	-24
SPECIALTIES WORK		64	25%	0%	18-Oct-26	17-Dec-26	15-Nov-26	28-Jan-27	14,623.96	0.00	58,495.83	-35

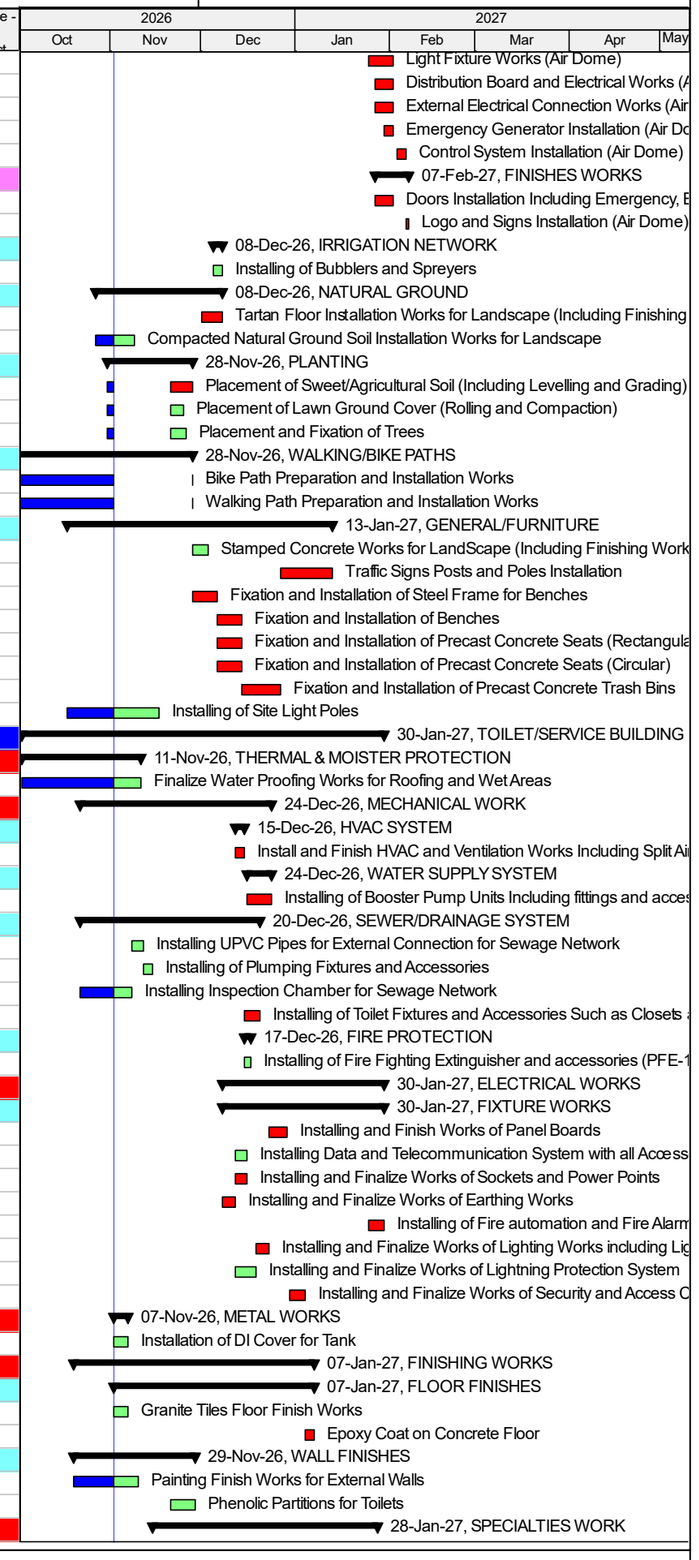

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	0%	0%	15-Dec-26	17-Dec-26	25-Jan-27	28-Jan-27	0.00	0.00	24,373.26	-35
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	15-Nov-26	21-Nov-26	14,623.96	0.00	14,623.96	-24
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	0%	0%	12-Dec-26	14-Dec-26	21-Jan-27	25-Jan-27	0.00	0.00	19,498.61	-35
TESTING & COMMISSIONING		31	0%	0%	20-Dec-26	02-Jan-27	07-Jan-27	13-Feb-27	0.00	0.00	0.00	-35
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	2	0%	0%	30-Dec-26	31-Dec-26	09-Feb-27	11-Feb-27	0.00	0.00	0.00	-35
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	12	0%	0%	20-Dec-26	02-Jan-27	30-Jan-27	13-Feb-27	0.00	0.00	0.00	-35
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	27-Dec-26	31-Dec-26	07-Jan-27	13-Jan-27	0.00	0.00	0.00	-10
HASA OASIS		186	16.63%	14.74%	04-May-26	02-Jan-27	01-Jun-26 A	24-Feb-27	1,032,472.10	914,847.08	6,208,033.66	-44
ENGINEERING		50	0%	0%	04-May-26	25-Nov-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-29
SHOP DRAWINGS		50	0%	0%	04-May-26	25-Nov-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-29
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
ELECTRICAL WORKS		25	0%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-152
SHOP DRAWINGS APPROVALS		50	0%	0%	06-Jun-26	25-Nov-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-29
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		50	0%	0%	06-Jun-26	25-Nov-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-29
ELECTRICAL WORKS		50	0%	0%	06-Jun-26	25-Nov-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-29
MLTX-02-005-EI	Shop DWG Approval for Power Layout	25	100%	0%	06-Jun-26	04-Jul-26	01-Dec-26	30-Dec-26	0.00	0.00	0.00	-152
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	25	16.4%	0%	28-Oct-26	25-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-4
PROCUREMENT		71	0%	0%	16-Jun-26	01-Dec-26	02-Nov-26	24-Jan-27	0.00	0.00	0.00	-45
SHORT LEAD ITEM		71	0%	0%	16-Jun-26	01-Dec-26	02-Nov-26	24-Jan-27	0.00	0.00	0.00	-45
TOILET/SERVICE WORKS		49	0%	0%	16-Jun-26	19-Oct-26	02-Nov-26	29-Dec-26	0.00	0.00	0.00	-60
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	03-Oct-26	19-Oct-26	08-Nov-26	25-Nov-26	0.00	0.00	0.00	-31
FURNITURES		49	0%	0%	16-Jun-26	11-Aug-26	02-Nov-26	29-Dec-26	0.00	0.00	0.00	-118
MLTX-02-005-PR-1	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	-118
MLTX-02-005-PR-1	Material Delivery for Furnitures	30	100%	0%	08-Jul-26	11-Aug-26	24-Nov-26	29-Dec-26	0.00	0.00	0.00	-118
PLAYGROUND WORKS		71	0%	0%	28-Jun-26	01-Dec-26	02-Nov-26	24-Jan-27	0.00	0.00	0.00	-45
PVC MEMBRANE		30	0%	0%	29-Sep-26	02-Nov-26	19-Nov-26	24-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	30	97%	0%	29-Sep-26	02-Nov-26	19-Nov-26	24-Dec-26	0.00	0.00	0.00	-44
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	30	93.67%	0%	30-Sep-26	03-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-28
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-36
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-39
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-39
MARKING PAINT		32	0%	0%	28-Jun-26	03-Aug-26	02-Nov-26	09-Dec-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	15-Jul-26	03-Aug-26	19-Nov-26	09-Dec-26	0.00	0.00	0.00	-108
AIR DIFUSSERS/GRILLS		40	0%	0%	24-Sep-26	09-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	72.4%	0%	12-Oct-26	09-Nov-26	19-Nov-26	19-Dec-26	0.00	0.00	0.00	-33
GALVANIZED DUCTS		40	0%	0%	24-Sep-26	09-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	72.4%	0%	12-Oct-26	09-Nov-26	19-Nov-26	19-Dec-26	0.00	0.00	0.00	-33
EXHAUST FANS		40	0%	0%	10-Sep-26	02-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	96.4%	0%	05-Oct-26	02-Nov-26	19-Nov-26	19-Dec-26	0.00	0.00	0.00	-39
DISTRIBUTION BOARDS		20	0%	0%	10-Oct-26	01-Nov-26	19-Nov-26	13-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	10-Oct-26	14-Oct-26	19-Nov-26	25-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	15-Oct-26	01-Nov-26	25-Nov-26	13-Dec-26	0.00	0.00	0.00	-35
POWER CABLES		35	0%	0%	22-Oct-26	01-Dec-26	07-Dec-26	17-Jan-27	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Power Cables	15	60.67%	0%	22-Oct-26	08-Nov-26	07-Dec-26	24-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Power Cables	20	0%	0%	09-Nov-26	01-Dec-26	24-Dec-26	17-Jan-27	0.00	0.00	0.00	-39
LIGHT FIXTURES		20	0%	0%	09-Nov-26	01-Dec-26	24-Dec-26	17-Jan-27	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	09-Nov-26	01-Dec-26	24-Dec-26	17-Jan-27	0.00	0.00	0.00	-39
CCTV MATERIALS		71	0%	0%	04-Jul-26	29-Nov-26	02-Nov-26	24-Jan-27	0.00	0.00	0.00	-47
MLTX-02-005-PR-1	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	12-Nov-26	29-Nov-26	06-Jan-27	24-Jan-27	0.00	0.00	0.00	-47
POWER OUTLETS/SWITCHES		41	0%	0%	23-Jul-26	10-Nov-26	19-Nov-26	06-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-1	PO for Power Outlets/Switches	16	100%	0%	23-Jul-26	10-Aug-26	19-Nov-26	08-Dec-26	0.00	0.00	0.00	-101

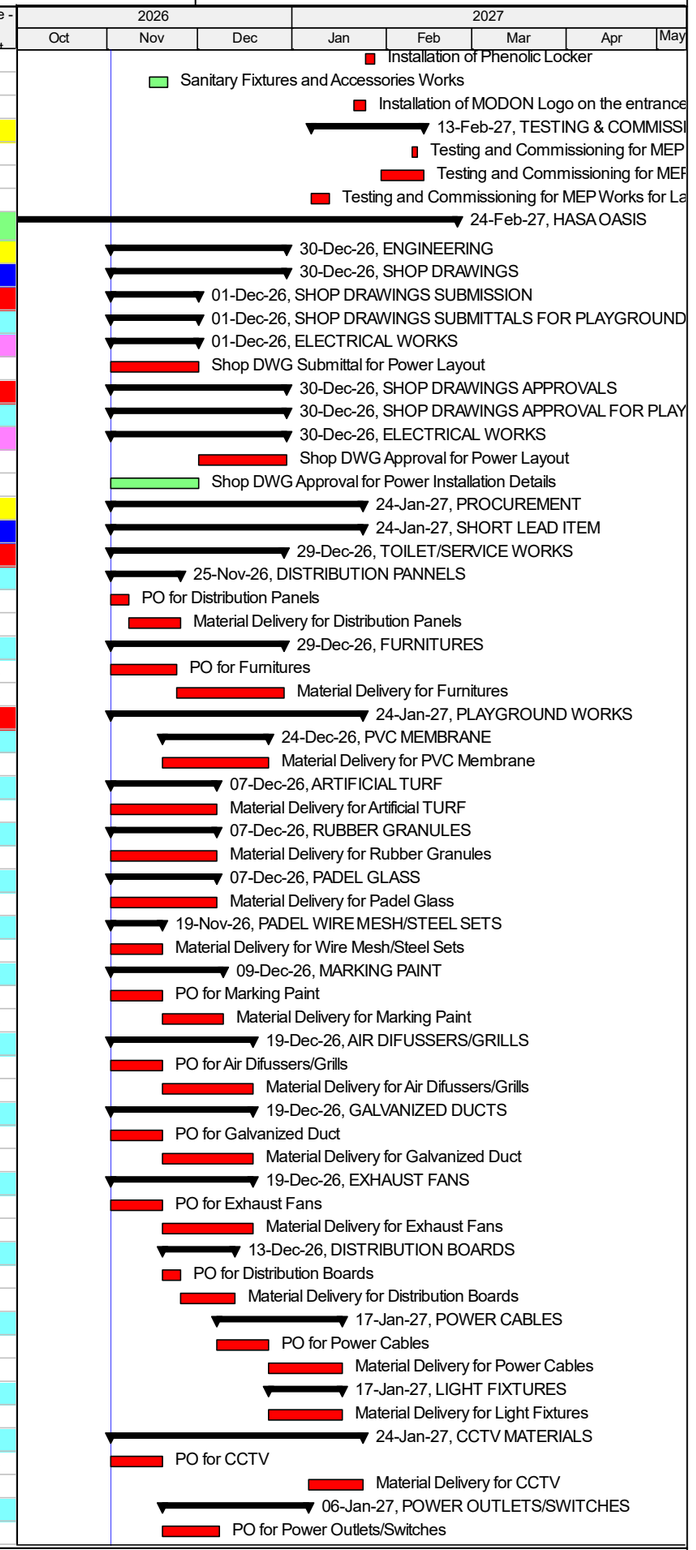

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	68.4%	0%	13-Oct-26	10-Nov-26	08-Dec-26	06-Jan-27	0.00	0.00	0.00	-48
LANDSCAPE WORKS		64	0%	0%	11-Aug-26	04-Nov-26	02-Nov-26	16-Jan-27	0.00	0.00	0.00	-61
PAVEMENT MARKING		33	0%	0%	11-Aug-26	04-Nov-26	08-Dec-26	16-Jan-27	0.00	0.00	0.00	-61
MLTX-02-005-PR-1	PO for Pavement Markings	13	100%	0%	11-Aug-26	25-Aug-26	08-Dec-26	23-Dec-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	20	85.5%	0%	13-Oct-26	04-Nov-26	23-Dec-26	16-Jan-27	0.00	0.00	0.00	-61
TRAFFIC SIGNS		5	0%	0%	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	5	100%	0%	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-35
TRACK SURFACE		2	0%	0%	29-Aug-26	30-Aug-26	23-Dec-26	26-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Track Surface	2	100%	0%	29-Aug-26	30-Aug-26	23-Dec-26	26-Dec-26	0.00	0.00	0.00	-99
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-30
LONG LEAD ITEM		31	0%	0%	15-Jul-26	16-Nov-26	02-Nov-26	08-Dec-26	0.00	0.00	0.00	-18
PLAYGROUND WORKS		31	0%	0%	15-Jul-26	16-Nov-26	02-Nov-26	08-Dec-26	0.00	0.00	0.00	-18
STEEL TENSION CABLES		26	0%	0%	21-Sep-26	21-Oct-26	02-Nov-26	02-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	02-Nov-26	21-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	Staging time	10	100%	0%	11-Oct-26	21-Oct-26	21-Nov-26	02-Dec-26	0.00	0.00	0.00	-35
EMERGENCY DOORS		30	0%	0%	15-Jul-26	18-Aug-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Staging time	5	100%	0%	13-Aug-26	18-Aug-26	01-Dec-26	07-Dec-26	0.00	0.00	0.00	-93
PRESSURE UNITS		30	0%	0%	13-Oct-26	16-Nov-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	68.4%	0%	13-Oct-26	10-Nov-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-1	Staging time	5	0%	0%	11-Nov-26	16-Nov-26	01-Dec-26	07-Dec-26	0.00	0.00	0.00	-17
AIR LOCK DOORS		31	0%	0%	03-Oct-26	05-Nov-26	02-Nov-26	08-Dec-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	03-Oct-26	31-Oct-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	Staging time	5	22%	0%	01-Nov-26	05-Nov-26	02-Dec-26	08-Dec-26	0.00	0.00	0.00	-27
CONSTRUCTION PHASE		186	16.63%	14.74%	30-Jul-26	31-Dec-26	01-Jun-26 A	15-Feb-27	1,032,472.10	914,847.08	6,208,033.66	-38
SITE WORKS		135	15.76%	14.5%	29-Sep-26	31-Dec-26	01-Jun-26 A	15-Feb-27	930,317.96	855,958.34	5,901,888.43	-38
LANDSCAPE WORKS		135	15.76%	14.5%	29-Sep-26	31-Dec-26	01-Jun-26 A	15-Feb-27	930,317.96	855,958.34	5,901,888.43	-38
PLAYGROUND AREA		119	40.56%	32.45%	29-Sep-26	31-Dec-26	21-Sep-26 A	15-Feb-27	180,520.67	144,416.54	445,050.38	-38
FOOTBALL PLAYGROUND		24	0%	0%	17-Nov-26	09-Dec-26	05-Dec-26	02-Jan-27	0.00	0.00	47,527.50	-19
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	0%	0%	17-Nov-26	09-Dec-26	05-Dec-26	28-Dec-26	0.00	0.00	31,685.00	-15
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	3	0%	0%	17-Nov-26	19-Nov-26	29-Dec-26	02-Jan-27	0.00	0.00	15,842.50	-36
PADEL PLAYGROUND		18	0%	0%	12-Dec-26	31-Dec-26	02-Jan-27	23-Jan-27	0.00	0.00	70,195.20	-18
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	12-Dec-26	28-Dec-26	02-Jan-27	19-Jan-27	0.00	0.00	58,496.00	-18
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	3	0%	0%	29-Dec-26	31-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	11,699.20	-18
BASKETBALL PLAYGROUND		42	0%	0%	17-Nov-26	31-Dec-26	05-Dec-26	23-Jan-27	0.00	0.00	96,956.10	-18
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	17-Nov-26	28-Nov-26	05-Dec-26	16-Dec-26	0.00	0.00	80,796.75	-15
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	3	0%	0%	29-Dec-26	31-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	16,159.35	-18
PADEL FENCE		38	0%	0%	02-Dec-26	31-Dec-26	02-Jan-27	15-Feb-27	0.00	0.00	49,850.91	-38
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	02-Jan-27	19-Jan-27	0.00	0.00	30,677.48	-26
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	02-Jan-27	19-Jan-27	0.00	0.00	15,338.75	-26
MLTX-02-005-CI	Install of Fence Gates	26	0%	0%	02-Dec-26	31-Dec-26	16-Jan-27	15-Feb-27	0.00	0.00	3,834.68	-38
CURBSTOEN/INTERLOCK		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	05-Nov-26	180,520.67	144,416.54	180,520.67	-29
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	05-Nov-26	180,520.67	144,416.54	180,520.67	-29
AIR DOME		30	0%	0%	15-Nov-26	10-Dec-26	29-Dec-26	02-Feb-27	0.00	0.00	4,306,367.09	-45
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	1,391,301.90	-38
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	942,830.33	-38
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	448,471.57	-38
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	29-Dec-26	16-Jan-27	0.00	0.00	1,233,296.81	-33
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	15	0%	0%	21-Nov-26	07-Dec-26	29-Dec-26	16-Jan-27	0.00	0.00	728,766.30	-33
MLTX-02-005-CI	Air Units Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	06-Jan-27	16-Jan-27	0.00	0.00	336,353.67	-33
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	06-Jan-27	16-Jan-27	0.00	0.00	168,176.84	-33
ELECTRICAL WORKS		14	0%	0%	02-Dec-26	10-Dec-26	17-Jan-27	02-Feb-27	0.00	0.00	1,513,591.54	-45
MLTX-02-005-CI	Light Fixture Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	17-Jan-27	26-Jan-27	0.00	0.00	224,235.78	-39
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	17-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-39
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	17-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-39
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	17-Jan-27	26-Jan-27	0.00	0.00	504,530.51	-39
MLTX-02-005-CI	Control System Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	24-Jan-27	02-Feb-27	0.00	0.00	448,471.57	-45
FINISHES WORKS		30	0%	0%	15-Nov-26	10-Dec-26	29-Dec-26	02-Feb-27	0.00	0.00	168,176.84	-45
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	15-Nov-26	01-Dec-26	29-Dec-26	16-Jan-27	0.00	0.00	112,117.89	-38
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	09-Dec-26	10-Dec-26	31-Jan-27	02-Feb-27	0.00	0.00	56,058.95	-45
IRRIGATION NETWORK		3	0%	0%	05-Dec-26	07-Dec-26	02-Jan-27	05-Jan-27	0.00	0.00	25,106.20	-24
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	05-Dec-26	07-Dec-26	02-Jan-27	05-Jan-27	0.00	0.00	25,106.20	-24
NATURAL GROUND		15	0%	70.17%	29-Nov-26	07-Dec-26	13-Oct-26 A	08-Nov-26	0.00	134,544.00	191,740.00	26

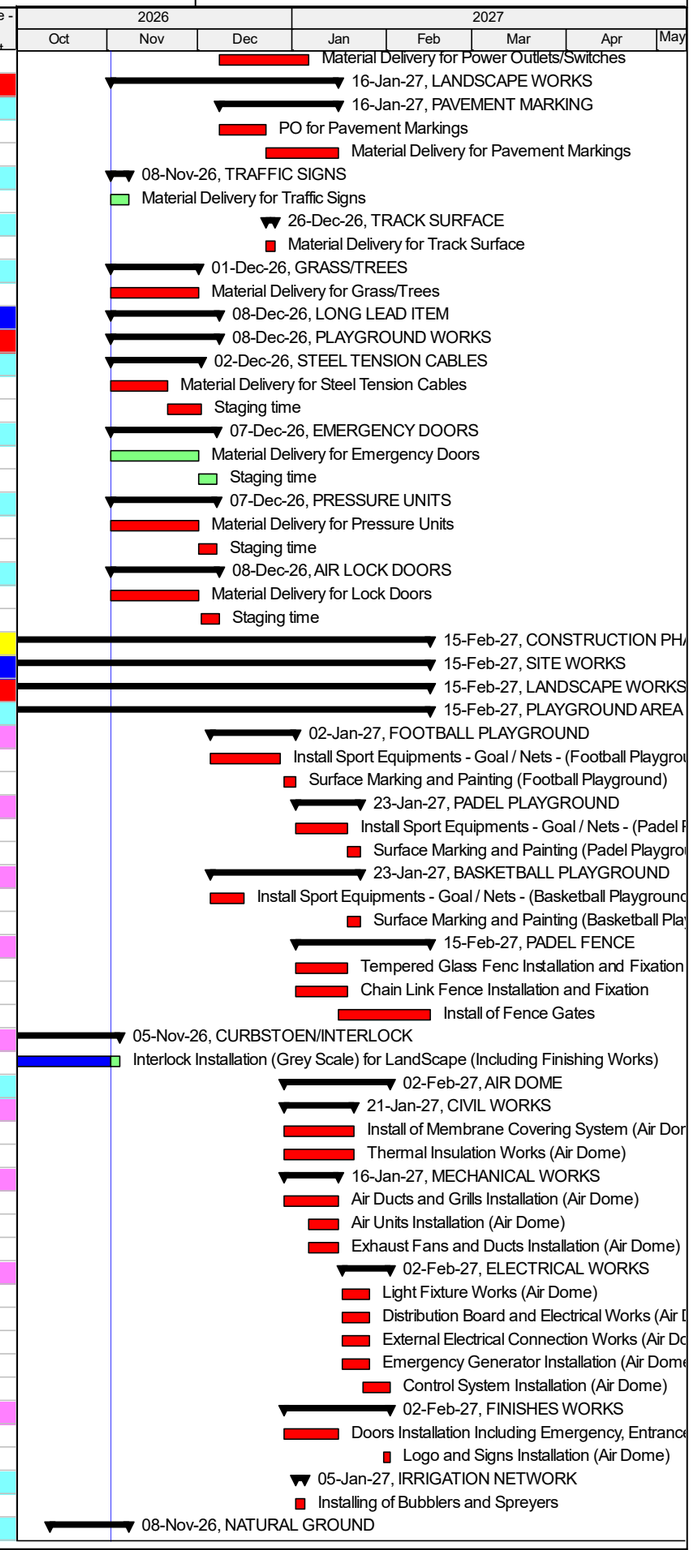

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	60%	05-Dec-26	07-Dec-26	14-Oct-26 A	05-Nov-26	0.00	76,044.00	126,740.00	28
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	90%	29-Nov-26	03-Dec-26	13-Oct-26 A	08-Nov-26	0.00	58,500.00	65,000.00	23
PLANTING		101	87.76%	69.34%	24-Oct-26	02-Nov-26	03-Oct-26 A	05-Nov-26	304,731.71	240,773.38	347,251.46	-2
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	100%	95%	24-Oct-26	26-Oct-26	03-Oct-26 A	05-Nov-26	104,175.44	98,966.67	104,175.44	-8
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	70%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	05-Nov-26	99,212.75	70,866.25	141,732.50	-2
MLTX-02-005-CN-1	Placement and Fixation of Trees	3	100%	70%	27-Oct-26	29-Oct-26	14-Oct-26 A	05-Nov-26	101,343.52	70,940.46	101,343.52	-5
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	02-Nov-26	367,633.90	294,107.12	367,633.90	-13
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	02-Nov-26	187,554.12	150,043.30	187,554.12	-21
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	02-Nov-26	180,079.78	144,063.82	180,079.78	-13
GENERAL/FURNITURE		88	35.4%	19.25%	15-Oct-26	24-Dec-26	14-Oct-26 A	27-Jan-27	77,431.68	42,117.30	218,739.40	-28
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	72.78%	45%	18-Oct-26	07-Nov-26	14-Oct-26 A	23-Nov-26	68,115.63	42,117.30	93,594.00	-13
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	3	0%	0%	20-Dec-26	22-Dec-26	21-Jan-27	25-Jan-27	0.00	0.00	9,749.30	-28
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	28	53.93%	0%	15-Oct-26	16-Nov-26	02-Nov-26	05-Dec-26	9,316.05	0.00	17,274.79	-15
MLTX-02-005-CN-1	Fixation and Installation of Benches	14	0%	0%	17-Nov-26	02-Dec-26	05-Dec-26	21-Dec-26	0.00	0.00	40,307.84	-15
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	14	0%	0%	03-Dec-26	19-Dec-26	05-Dec-26	21-Dec-26	0.00	0.00	32,757.76	-1
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	14	0%	0%	03-Dec-26	19-Dec-26	21-Dec-26	06-Jan-27	0.00	0.00	12,869.04	-15
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	2	0%	0%	23-Dec-26	24-Dec-26	25-Jan-27	27-Jan-27	0.00	0.00	12,186.67	-28
TOILET/SERVICE BUILDING		155	33.37%	19.24%	30-Jul-26	23-Dec-26	20-Sep-26 A	28-Jan-27	102,154.14	58,888.74	306,145.23	-30
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	23-Nov-26	16,607.28	14,946.55	16,607.28	-80
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	23-Nov-26	16,607.28	14,946.55	16,607.28	-80
MECHANICAL WORK		21	0%	0%	28-Nov-26	21-Dec-26	20-Dec-26	13-Jan-27	0.00	0.00	1,949.87	-19
FIRE PROTECTION		21	0%	0%	28-Nov-26	21-Dec-26	20-Dec-26	13-Jan-27	0.00	0.00	1,949.87	-19
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	0%	0%	28-Nov-26	21-Dec-26	20-Dec-26	13-Jan-27	0.00	0.00	1,949.87	-19
ELECTRICAL WORKS		52	0%	0%	04-Nov-26	20-Dec-26	25-Nov-26	25-Jan-27	0.00	0.00	156,999.41	-30
FIXTURE WORKS		52	0%	0%	04-Nov-26	20-Dec-26	25-Nov-26	25-Jan-27	0.00	0.00	156,999.41	-30
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	18	0%	0%	28-Nov-26	17-Dec-26	20-Dec-26	10-Jan-27	0.00	0.00	34,317.53	-19
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	0%	0%	04-Nov-26	26-Nov-26	25-Nov-26	19-Dec-26	0.00	0.00	102,367.69	-18
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	28-Nov-26	20-Dec-26	20-Dec-26	12-Jan-27	0.00	0.00	6,239.59	-19
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	0%	0%	21-Nov-26	13-Dec-26	02-Jan-27	25-Jan-27	0.00	0.00	7,250.09	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	0%	0%	28-Nov-26	20-Dec-26	19-Dec-26	11-Jan-27	0.00	0.00	6,824.51	-18
METAL WORKS		14	100%	0%	05-Oct-26	20-Oct-26	25-Nov-26	12-Dec-26	3,899.72	0.00	3,899.72	-44
MLTX-02-005-CN-129	Installation of DI Cover for Tank	14	100%	0%	05-Oct-26	20-Oct-26	25-Nov-26	12-Dec-26	3,899.72	0.00	3,899.72	-44
FINISHING WORKS		88	98.28%	47.28%	18-Oct-26	16-Dec-26	27-Sep-26 A	28-Jan-27	67,023.18	32,243.02	68,193.12	-36
FLOOR FINISHES		23	0%	0%	21-Nov-26	16-Dec-26	02-Jan-27	28-Jan-27	0.00	0.00	1,169.94	-36
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	23	0%	0%	21-Nov-26	16-Dec-26	02-Jan-27	28-Jan-27	0.00	0.00	1,169.94	-36
WALL FINISHES		54	100%	48.11%	18-Oct-26	28-Oct-26	27-Sep-26 A	20-Dec-26	67,023.18	32,243.02	67,023.18	-44
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	05-Nov-26	35,825.58	32,243.02	35,825.58	-13
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	21-Oct-26	28-Oct-26	12-Dec-26	20-Dec-26	31,197.60	0.00	31,197.60	-44
SPECIALTIES WORK		97	25%	20%	27-Sep-26	23-Dec-26	04-Oct-26 A	18-Jan-27	14,623.96	11,699.17	58,495.83	-21
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	05-Nov-26	14,623.96	11,699.17	14,623.96	-31
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	17	0%	0%	05-Dec-26	23-Dec-26	29-Dec-26	18-Jan-27	0.00	0.00	19,498.61	-21
MLTX-02-005-CN-131	Installation of Phenolic Locker	12	0%	0%	28-Nov-26	10-Dec-26	20-Dec-26	03-Jan-27	0.00	0.00	24,373.26	-19
TESTING & COMMISSIONING		28	0%	0%	08-Dec-26	02-Jan-27	21-Jan-27	24-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	18	0%	0%	12-Dec-26	31-Dec-26	02-Feb-27	24-Feb-27	0.00	0.00	0.00	-45
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	7	0%	0%	26-Dec-26	02-Jan-27	07-Feb-27	15-Feb-27	0.00	0.00	0.00	-37
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	21	0%	0%	08-Dec-26	31-Dec-26	21-Jan-27	15-Feb-27	0.00	0.00	0.00	-38
DAMMAM		167	8.58%	3.64%	21-May-26	02-Jan-27	06-Sep-26 A	27-Feb-27	513,008.81	217,778.25	5,978,525.99	-46
ENGINEERING		50	0%	0%	25-May-26	02-Aug-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-127
SHOP DRAWINGS		50	0%	0%	25-May-26	02-Aug-26	02-Nov-26	30-Dec-26	0.00	0.00	0.00	-127
SHOP DRAWINGS SUBMISSION		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	02-Nov-26	01-Dec-26	0.00	0.00	0.00	-134
MLTX-02-005-EI	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	02-Nov-26	07-Dec-26	0.00	0.00	0.00	-134
SHOP DRAWINGS APPROVALS		25	0%	0%	02-Jul-26	02-Aug-26	01-Dec-26	30-Dec-26	0.00	0.00	0.00	-127
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		25	0%	0%	02-Jul-26	02-Aug-26	01-Dec-26	30-Dec-26	0.00	0.00	0.00	-127
ELECTRICAL WORKS		25	0%	0%	02-Jul-26	02-Aug-26	01-Dec-26	30-Dec-26	0.00	0.00	0.00	-127
MLTX-02-005-EI	Shop DWG Approval for Power Layout	25	100%	0%	02-Jul-26	30-Jul-26	01-Dec-26	30-Dec-26	0.00	0.00	0.00	-129
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	15	100%	0%	16-Jul-26	02-Aug-26	07-Dec-26	24-Dec-26	0.00	0.00	0.00	-122
PROCUREMENT		84	0%	0%	21-May-26	21-Dec-26	25-Oct-26 A	03-Feb-27	0.00	0.00	0.00	-37
SHORT LEAD ITEM		84	0%	0%	21-May-26	21-Dec-26	25-Oct-26 A	03-Feb-27	0.00	0.00	0.00	-37
TOILET/SERVICE WORKS		40	0%	0%	17-Jun-26	28-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-17
LIGHTING FIXTURES		10	0%	0%	22-Jul-26	02-Aug-26	06-Dec-26	17-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	06-Dec-26	17-Dec-26	0.00	0.00	0.00	-116

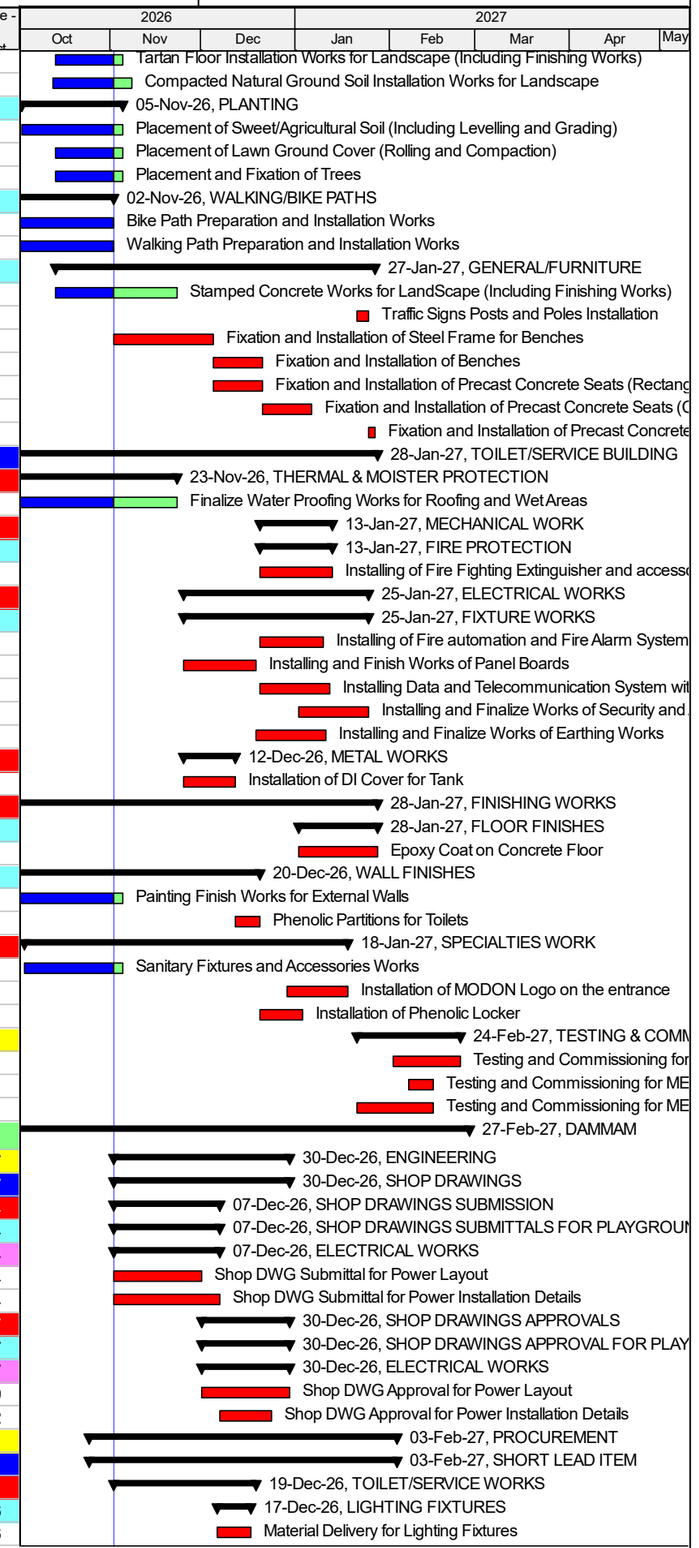

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
DISTRIBUTION PANNELS		40	0%	0%	13-Oct-26	28-Nov-26	02-Nov-26	19-Dec-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-1	PO for Distribution Panels	15	100%	0%	13-Oct-26	29-Oct-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	25	8.4%	0%	31-Oct-26	28-Nov-26	19-Nov-26	19-Dec-26	0.00	0.00	0.00	-17
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	-117
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	12-Nov-26	06-Dec-26	0.00	0.00	0.00	-117
PLAYGROUND WORKS		70	0%	0%	21-May-26	21-Dec-26	02-Nov-26	23-Jan-27	0.00	0.00	0.00	-27
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	02-Nov-26	26-Nov-26	0.00	0.00	0.00	-137
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	02-Nov-26	26-Nov-26	0.00	0.00	0.00	-137
ARTIFICIAL TURF		12	0%	0%	18-Jun-26	01-Jul-26	26-Nov-26	10-Dec-26	0.00	0.00	0.00	-137
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	18-Jun-26	01-Jul-26	26-Nov-26	10-Dec-26	0.00	0.00	0.00	-137
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	-132
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	-132
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	02-Nov-26	05-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	Material Delivery for Padel Glass	28	43.21%	0%	19-Oct-26	19-Nov-26	02-Nov-26	05-Dec-26	0.00	0.00	0.00	-12
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-127
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-127
BITUMINOUS BASE & WEARING COURSE		32	0%	0%	15-Jun-26	21-Jul-26	02-Nov-26	09-Dec-26	0.00	0.00	0.00	-119
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	15	100%	0%	15-Jun-26	01-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-119
MLTX-02-005-PR-1	Material Delivery for the Site	17	100%	0%	02-Jul-26	21-Jul-26	19-Nov-26	09-Dec-26	0.00	0.00	0.00	-119
MARKING PAINT		32	0%	0%	02-Jul-26	08-Aug-26	19-Nov-26	27-Dec-26	0.00	0.00	0.00	-119
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	19-Nov-26	07-Dec-26	0.00	0.00	0.00	-119
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	20-Jul-26	08-Aug-26	07-Dec-26	27-Dec-26	0.00	0.00	0.00	-119
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	08-Nov-26	19-Nov-26	0.00	0.00	0.00	-107
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	08-Nov-26	01-Dec-26	0.00	0.00	0.00	2
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	08-Nov-26	01-Dec-26	0.00	0.00	0.00	2
CCTV MATERIALS		62	0%	0%	30-Jul-26	21-Dec-26	02-Nov-26	13-Jan-27	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	02-Nov-26	08-Nov-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	05-Dec-26	21-Dec-26	27-Dec-26	13-Jan-27	0.00	0.00	0.00	-19
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	17-Dec-26	23-Jan-27	0.00	0.00	0.00	-38
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	17-Dec-26	24-Dec-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	24-Dec-26	23-Jan-27	0.00	0.00	0.00	-38
LANDSCAPE WORKS		55	0%	0%	15-Aug-26	13-Dec-26	25-Oct-26 A	03-Feb-27	0.00	0.00	0.00	-44
PAVEMENT MARKING		15	0%	0%	15-Aug-26	31-Aug-26	24-Dec-26	11-Jan-27	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	24-Dec-26	30-Dec-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	20-Aug-26	31-Aug-26	30-Dec-26	11-Jan-27	0.00	0.00	0.00	-112
TRAFFIC SIGNS		10	0%	0%	22-Nov-26	13-Dec-26	23-Jan-27	03-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	10	0%	0%	22-Nov-26	13-Dec-26	23-Jan-27	03-Feb-27	0.00	0.00	0.00	-44
IRRIGATION PIPES/SPRINKLERS		8	0%	0%	22-Nov-26	30-Nov-26	06-Dec-26	15-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	0%	0%	22-Nov-26	30-Nov-26	06-Dec-26	15-Dec-26	0.00	0.00	0.00	-12
TRACK SURFACE		10	0%	0%	10-Nov-26	21-Nov-26	11-Jan-27	23-Jan-27	0.00	0.00	0.00	-53
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	0%	0%	10-Nov-26	21-Nov-26	11-Jan-27	23-Jan-27	0.00	0.00	0.00	-53
GRASS/TREES		15	0%	0%	22-Nov-26	08-Dec-26	25-Oct-26 A	02-Nov-26	0.00	0.00	0.00	32
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	50%	22-Nov-26	08-Dec-26	25-Oct-26 A	02-Nov-26	0.00	0.00	0.00	32
LONG LEAD ITEM		22	0%	0%	07-Sep-26	30-Nov-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	3
PLAYGROUND WORKS		22	0%	0%	07-Sep-26	30-Nov-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	3
STEEL TENSION CABLES		22	0%	0%	07-Sep-26	19-Oct-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	-47
MLTX-02-005-PR-1	Staging time	7	100%	0%	12-Oct-26	19-Oct-26	19-Nov-26	28-Nov-26	0.00	0.00	0.00	-33
EMERGENCY DOORS		18	0%	0%	04-Nov-26	24-Nov-26	02-Nov-26	23-Nov-26	0.00	0.00	0.00	2
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	15	0%	0%	04-Nov-26	21-Nov-26	02-Nov-26	19-Nov-26	0.00	0.00	0.00	2
MLTX-02-005-PR-1	Staging time	3	0%	0%	22-Nov-26	24-Nov-26	19-Nov-26	23-Nov-26	0.00	0.00	0.00	2
PRESSURE UNITS		22	0%	0%	05-Nov-26	30-Nov-26	02-Nov-26	28-Nov-26	0.00	0.00	0.00	3
MLTX-02-005-PR-1	Material Delivery for Pressure Units	10	0%	0%	05-Nov-26	16-Nov-26	02-Nov-26	14-Nov-26	0.00	0.00	0.00	3
MLTX-02-005-PR-1	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	16-Nov-26	28-Nov-26	0.00	0.00	0.00	3
AIR LOCK DOORS		20	0%	0%	05-Nov-26	26-Nov-26	02-Nov-26	25-Nov-26	0.00	0.00	0.00	2
MLTX-02-005-PR-1	Material Delivery for Lock Doors	12	0%	0%	05-Nov-26	18-Nov-26	02-Nov-26	16-Nov-26	0.00	0.00	0.00	3
MLTX-02-005-PR-1	Staging time	5	0%	0%	22-Nov-26	26-Nov-26	19-Nov-26	25-Nov-26	0.00	0.00	0.00	2
CONSTRUCTION PHASE		167	8.58%	3.64%	02-Jul-26	31-Dec-26	06-Sep-26 A	27-Feb-27	513,008.81	217,778.25	5,978,525.99	-47
SITE WORKS		113	8.34%	3.36%	02-Jul-26	31-Dec-26	20-Oct-26 A	27-Feb-27	474,758.09	191,132.53	5,692,679.52	-47
LANDSCAPE WORKS		113	8.34%	3.36%	02-Jul-26	31-Dec-26	20-Oct-26 A	27-Feb-27	474,758.09	191,132.53	5,692,679.52	-47
PLAYGROUND AREA		66	56.17%	10.47%	02-Jul-26	31-Dec-26	21-Oct-26 A	10-Feb-27	338,945.66	63,182.23	603,475.37	-34

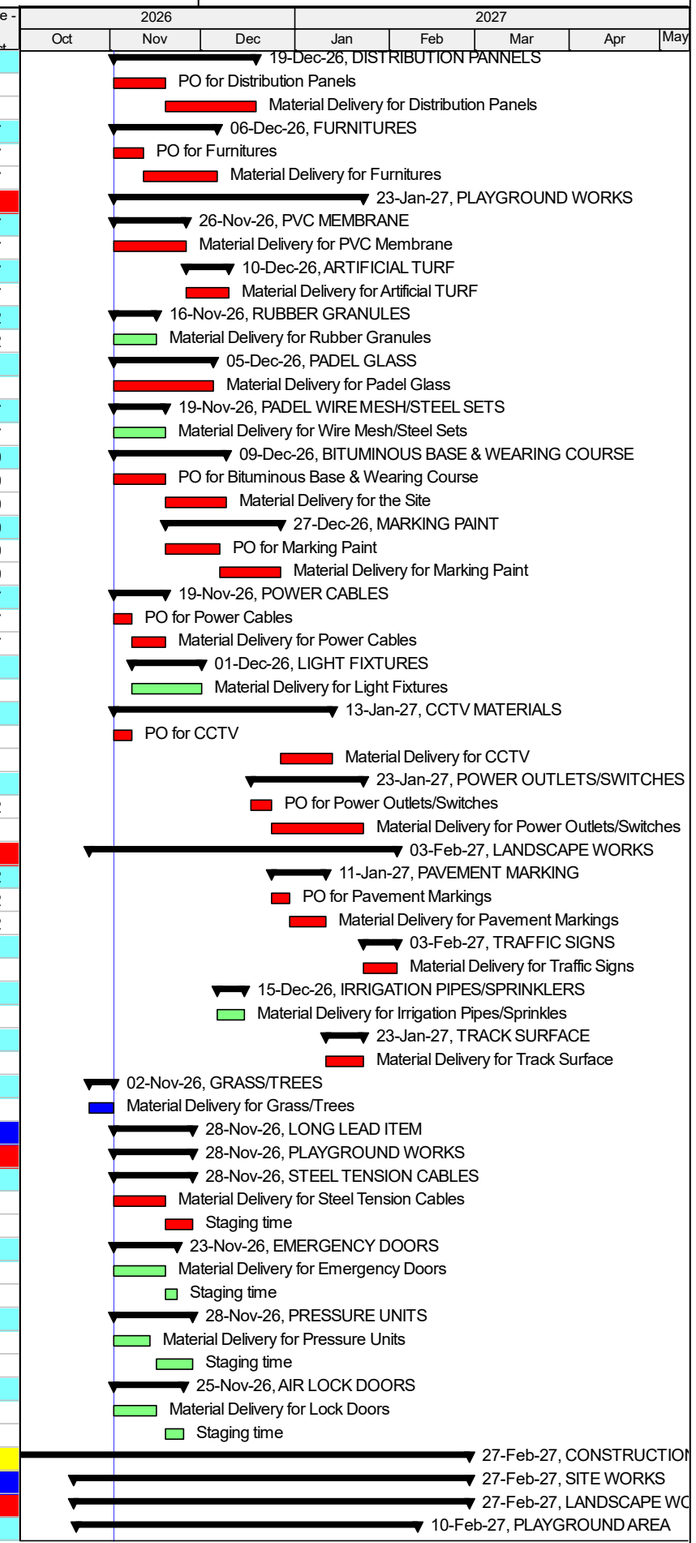

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
FOOTBALL PLAYGROUND		43	76.92%	0%	02-Jul-26	15-Dec-26	10-Dec-26	30-Jan-27	158,424.99	0.00	205,952.49	-38
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	02-Jul-26	25-Jul-26	10-Dec-26	03-Jan-27	158,424.99	0.00	158,424.99	-137
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	10-Dec-26	15-Dec-26	24-Jan-27	30-Jan-27	0.00	0.00	31,685.00	-38
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	2	0%	0%	08-Dec-26	09-Dec-26	21-Jan-27	24-Jan-27	0.00	0.00	15,842.50	-38
PADEL PLAYGROUND		5	0%	0%	20-Dec-26	24-Dec-26	02-Feb-27	08-Feb-27	0.00	0.00	70,195.20	-38
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	02-Feb-27	08-Feb-27	0.00	0.00	58,496.00	-38
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	02-Feb-27	08-Feb-27	0.00	0.00	11,699.20	-38
BASKETBALL PLAYGROUND		2	0%	0%	30-Dec-26	31-Dec-26	08-Feb-27	10-Feb-27	0.00	0.00	96,956.10	-34
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	2	0%	0%	30-Dec-26	31-Dec-26	08-Feb-27	10-Feb-27	0.00	0.00	80,796.75	-34
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	2	0%	0%	30-Dec-26	31-Dec-26	08-Feb-27	10-Feb-27	0.00	0.00	16,159.35	-34
PADEL FENCE		48	0%	0%	26-Nov-26	24-Dec-26	05-Dec-26	30-Jan-27	0.00	0.00	49,850.91	-30
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	05-Dec-26	03-Jan-27	0.00	0.00	30,677.48	-7
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	05-Dec-26	03-Jan-27	0.00	0.00	15,338.75	-7
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	20-Dec-26	24-Dec-26	24-Jan-27	30-Jan-27	0.00	0.00	3,834.68	-30
CURBSTOEN/INTERLOCK		6	100%	35%	15-Sep-26	21-Sep-26	21-Oct-26 A	09-Nov-26	180,520.67	63,182.23	180,520.67	-40
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	6	100%	35%	15-Sep-26	21-Sep-26	21-Oct-26 A	09-Nov-26	180,520.67	63,182.23	180,520.67	-40
AIR DOME		30	0%	0%	15-Nov-26	24-Dec-26	29-Dec-26	02-Feb-27	0.00	0.00	4,306,367.09	-33
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	1,391,301.90	-38
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	942,830.33	-38
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	21-Jan-27	0.00	0.00	448,471.57	-38
MECHANICAL WORKS		5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	1,233,296.81	-38
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	4	0%	0%	08-Dec-26	12-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	728,766.30	-38
MLTX-02-005-CI	Air Units Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	336,353.67	-38
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	27-Jan-27	0.00	0.00	168,176.84	-38
ELECTRICAL WORKS		10	0%	0%	08-Dec-26	24-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	1,513,591.54	-33
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	08-Dec-26	19-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	224,235.78	-38
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	12-Dec-26	19-Dec-26	25-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-38
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	13-Dec-26	19-Dec-26	26-Jan-27	02-Feb-27	0.00	0.00	168,176.84	-38
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	15-Dec-26	19-Dec-26	28-Jan-27	02-Feb-27	0.00	0.00	504,530.51	-38
MLTX-02-005-CI	Control System Installation (Air Dome)	3	0%	0%	22-Dec-26	24-Dec-26	30-Jan-27	02-Feb-27	0.00	0.00	448,471.57	-33
FINISHES WORKS		4	0%	0%	12-Dec-26	15-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	168,176.84	-38
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	2	0%	0%	12-Dec-26	13-Dec-26	25-Jan-27	27-Jan-27	0.00	0.00	112,117.89	-38
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	14-Dec-26	15-Dec-26	27-Jan-27	30-Jan-27	0.00	0.00	56,058.95	-38
IRRIGATION NETWORK		2	0%	0%	01-Dec-26	02-Dec-26	04-Feb-27	07-Feb-27	0.00	0.00	25,106.20	-56
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	01-Dec-26	02-Dec-26	04-Feb-27	07-Feb-27	0.00	0.00	25,106.20	-56
NATURAL GROUND		40	56.37%	30.51%	10-Oct-26	12-Nov-26	20-Oct-26 A	07-Dec-26	108,091.60	58,500.00	191,740.00	-20
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	34%	0%	27-Oct-26	12-Nov-26	19-Nov-26	07-Dec-26	43,091.60	0.00	126,740.00	-20
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	100%	90%	10-Oct-26	26-Oct-26	20-Oct-26 A	19-Nov-26	65,000.00	58,500.00	65,000.00	-20
PLANTING		27	0%	20%	06-Dec-26	31-Dec-26	24-Oct-26 A	14-Nov-26	0.00	69,450.29	347,251.46	42
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	09-Nov-26	0.00	20,835.09	104,175.44	29
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	20%	24-Dec-26	31-Dec-26	01-Nov-26 A	10-Nov-26	0.00	28,346.50	141,732.50	45
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	20%	13-Dec-26	23-Dec-26	01-Nov-26 A	14-Nov-26	0.00	20,268.70	101,343.52	35
GENERAL/FURNITURE		74	12.67%	0%	11-Oct-26	31-Dec-26	01-Dec-26	27-Feb-27	27,720.83	0.00	218,739.40	-47
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	6.11%	0%	01-Nov-26	21-Nov-26	22-Dec-26	12-Jan-27	5,719.63	0.00	93,594.00	-44
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	15-Dec-26	31-Dec-26	04-Feb-27	23-Feb-27	0.00	0.00	9,749.30	-44
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	18	100%	0%	11-Oct-26	31-Oct-26	01-Dec-26	22-Dec-26	17,274.79	0.00	17,274.79	-44
MLTX-02-005-CN-1	Fixation and Installation of Benches	20	5.5%	0%	01-Nov-26	23-Nov-26	12-Jan-27	04-Feb-27	2,216.93	0.00	40,307.84	-62
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	20	5.5%	0%	01-Nov-26	23-Nov-26	12-Jan-27	04-Feb-27	1,801.68	0.00	32,757.76	-62
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	20	5.5%	0%	01-Nov-26	23-Nov-26	12-Jan-27	04-Feb-27	707.80	0.00	12,869.04	-62
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	18	0%	0%	24-Nov-26	14-Dec-26	04-Feb-27	27-Feb-27	0.00	0.00	12,186.67	-62
TOILET/SERVICE BUILDING		146	13.38%	9.32%	18-Aug-26	29-Dec-26	06-Sep-26 A	06-Feb-27	38,250.72	26,645.72	285,846.47	-32
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-64
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	11-Nov-26	16,607.28	14,946.55	16,607.28	-64
MECHANICAL WORK		12	0%	0%	13-Dec-26	26-Dec-26	02-Jan-27	16-Jan-27	0.00	0.00	1,949.87	-17
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	02-Jan-27	16-Jan-27	0.00	0.00	1,949.87	-17
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	12	0%	0%	13-Dec-26	26-Dec-26	02-Jan-27	16-Jan-27	0.00	0.00	1,949.87	-17
ELECTRICAL WORKS		57	0%	0%	23-Nov-26	29-Dec-26	23-Nov-26	28-Jan-27	0.00	0.00	173,696.17	-25
FIXTURE WORKS		57	0%	0%	23-Nov-26	29-Dec-26	23-Nov-26	28-Jan-27	0.00	0.00	173,696.17	-25
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	15	0%	0%	12-Dec-26	28-Dec-26	02-Jan-27	19-Jan-27	0.00	0.00	34,317.53	-18
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	0%	0%	06-Dec-26	29-Dec-26	02-Jan-27	26-Jan-27	0.00	0.00	102,367.69	-23
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	14	0%	0%	12-Dec-26	27-Dec-26	02-Jan-27	18-Jan-27	0.00	0.00	14,259.43	-18
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	14	0%	0%	12-Dec-26	27-Dec-26	02-Jan-27	18-Jan-27	0.00	0.00	6,239.59	-18
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	14	0%	0%	25-Nov-26	10-Dec-26	23-Nov-26	09-Dec-26	0.00	0.00	7,250.09	2
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	02-Jan-27	28-Jan-27	0.00	0.00	6,824.51	-34

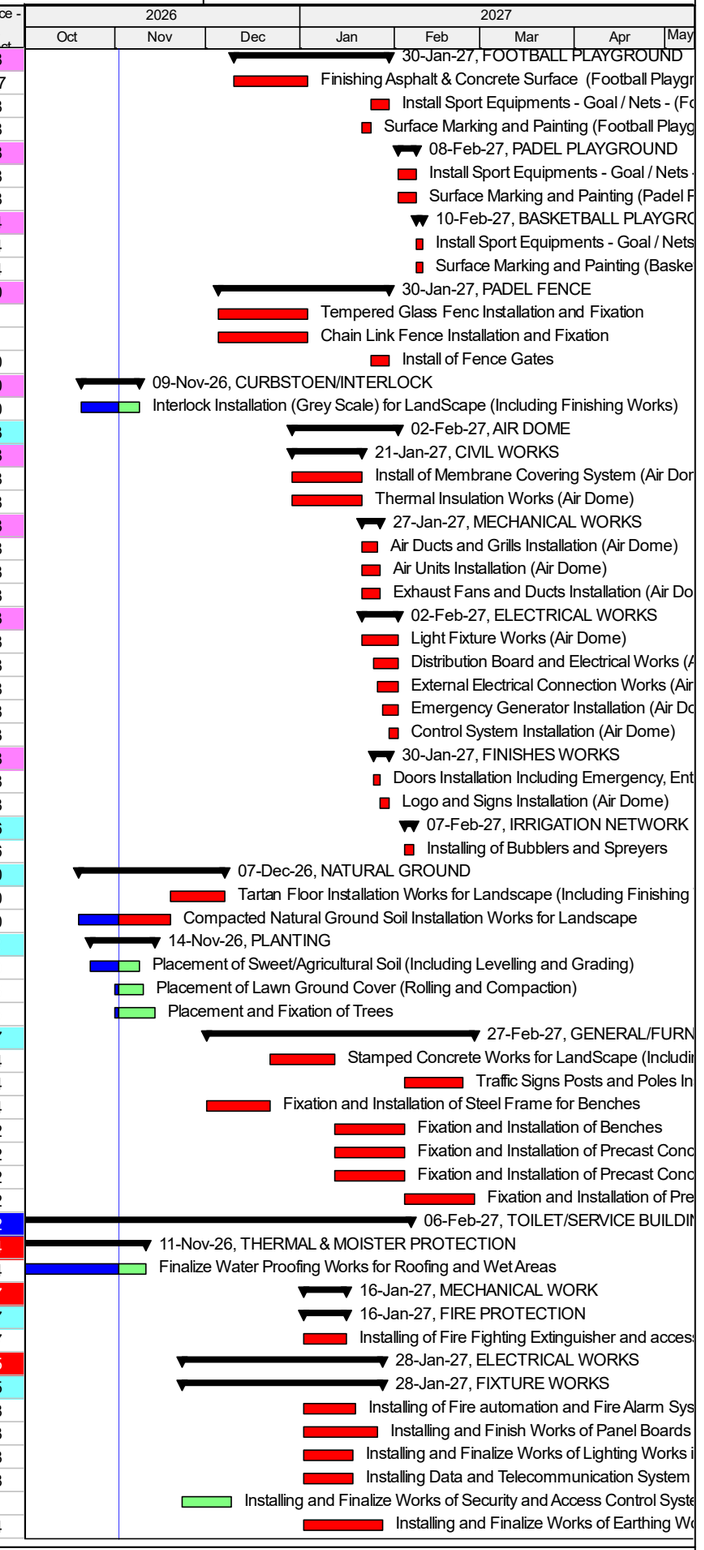

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 02-11-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	15	0%	0%	13-Dec-26	29-Dec-26	09-Dec-26	27-Dec-26	0.00	0.00	2,437.33	3
METAL WORKS		14	100%	0%	11-Oct-26	26-Oct-26	01-Dec-26	17-Dec-26	3,899.72	0.00	3,899.72	-44
MLTX-02-005-CN-144	Installation of DI Cover for Tank	14	100%	0%	11-Oct-26	26-Oct-26	01-Dec-26	17-Dec-26	3,899.72	0.00	3,899.72	-44
FINISHING WORKS		11	10%	0%	01-Nov-26	12-Nov-26	17-Dec-26	30-Dec-26	3,119.76	0.00	31,197.60	-40
WALL FINISHES		11	10%	0%	01-Nov-26	12-Nov-26	17-Dec-26	30-Dec-26	3,119.76	0.00	31,197.60	-40
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	10%	0%	01-Nov-26	12-Nov-26	17-Dec-26	30-Dec-26	3,119.76	0.00	31,197.60	-40
SPECIALTIES WORK		32	25%	20%	27-Oct-26	23-Dec-26	12-Oct-26 A	06-Feb-27	14,623.96	11,699.17	58,495.83	-37
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	100%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	17-Dec-26	14,623.96	11,699.17	14,623.96	-40
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	15	0%	0%	07-Dec-26	23-Dec-26	19-Jan-27	06-Feb-27	0.00	0.00	19,498.61	-37
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	0%	0%	14-Nov-26	15-Nov-26	30-Dec-26	02-Jan-27	0.00	0.00	24,373.26	-40
TESTING & COMMISSIONING		8	0%	0%	24-Dec-26	02-Jan-27	16-Feb-27	27-Feb-27	0.00	0.00	0.00	-46
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	27-Dec-26	31-Dec-26	16-Feb-27	23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	3	0%	0%	30-Dec-26	02-Jan-27	18-Feb-27	23-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	7	0%	0%	24-Dec-26	31-Dec-26	17-Feb-27	27-Feb-27	0.00	0.00	0.00	-47
PROJECT CLOSEOUT & DEMOBILIZATION		29	0%	0%	08-Dec-26	02-Jan-27	21-Jan-27	25-Feb-27	0.00	0.00	0.00	-45
As-Built DWGs		27	0%	0%	08-Dec-26	31-Dec-26	21-Jan-27	23-Feb-27	0.00	0.00	0.00	-44
As-Built DWGs Submittals		16	0%	0%	08-Dec-26	27-Dec-26	21-Jan-27	09-Feb-27	0.00	0.00	0.00	-37
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	12-Dec-26	13-Dec-26	02-Feb-27	04-Feb-27	0.00	0.00	0.00	-45
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	26-Dec-26	27-Dec-26	07-Feb-27	09-Feb-27	0.00	0.00	0.00	-37
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	08-Dec-26	12-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	0.00	-38
As-Built DWGs Approvals		23	0%	0%	15-Dec-26	31-Dec-26	26-Jan-27	23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	19-Dec-26	21-Dec-26	04-Feb-27	08-Feb-27	0.00	0.00	0.00	-41
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	29-Dec-26	31-Dec-26	18-Feb-27	23-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	15-Dec-26	17-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	0.00	-36
Demobilization		6	0%	0%	28-Dec-26	02-Jan-27	17-Feb-27	25-Feb-27	0.00	0.00	0.00	-45
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	28-Dec-26	28-Dec-26	17-Feb-27	18-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	28-Dec-26	28-Dec-26	17-Feb-27	18-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	18-Feb-27	20-Feb-27	0.00	0.00	0.00	-42
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	24-Feb-27	25-Feb-27	0.00	0.00	0.00	-45

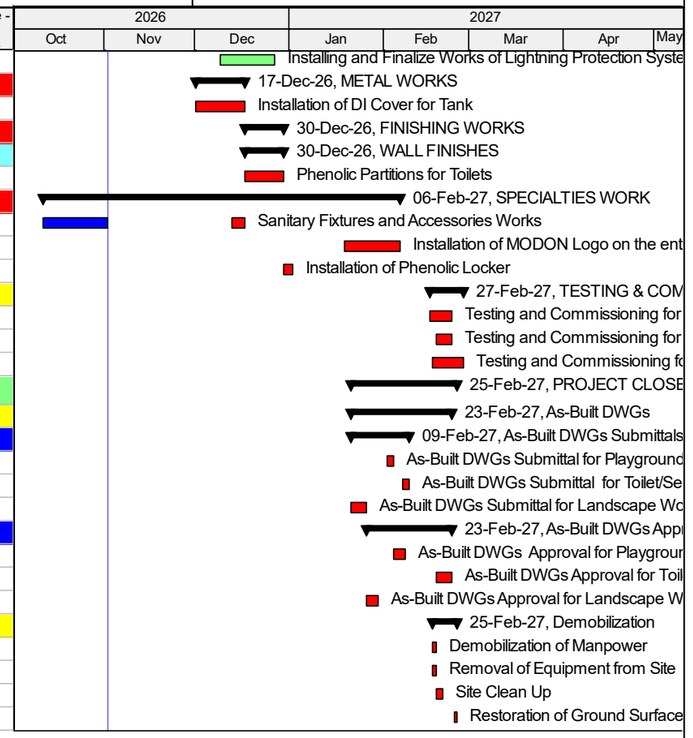

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation
