Developing Infrastructure Networks in Riyadh's Fourth Industrial City

مشروع تطوير شبكات البنية التحتية بالرياض الرابعة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Rawaf Contracting	EGIS Saudi Engineering Consultancy	Shuaib A. Alshuaibi	30-Nov-2025	30-May-2028

Scope: infrastructure over about 6.5 km² of the Fourth Industrial City in Riyadh: roads and tunnels, electrical, telecom, ICT and security networks, potable water and fire-fighting, irrigation, sewage and stormwater networks, and sewage and stormwater pumping stations.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 23.6% against 29.4% planned, the project is behind by 5.8% (SPI 0.80). It gained 3.1% this week. Earthworks are far ahead of plan, but procurement, the zone network works and the tunnels are behind.

PHYSICAL % COMPLETE
23.6% / 29.4% plan
▼ SPI 0.80 −5.8%

PROGRESS THIS WEEK
+3.1% / −1.5% plan
? The weekly plan figure is negative

CONTRACT TIME ELAPSED
35.4% · day 323 of 912
▼ Forecast finish 06-Feb-2029

INVOICED TO DATE (GROSS)
16.0% · 71.0M SAR
8 invoices, last period ends 30-Sep-2026

The weekly report forecasts completion about eight months late.

The weekly report forecasts completion on 06-Feb-2029, 252 days after the contract completion date of 30-May-2028. The P6 extract in the same workbook gives 13-Feb-2029 with −259 days of total float. The "Complete MV and road works" milestone (30-Sep-2026) has passed with asphalt at 8.0% and the MV network at 0.3% installed.

Site photos this week

Six photos from the 19-Oct-2026 weekly upload, all GPS-stamped 13-Oct-2026. Base course, asphalt and prime coat on road RD-A-1 in Zones 04 and 05, and ground improvement and backfilling on block BL-23. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt work, RD-A-1, Zone 05

Paver laying the bituminous base course. GPS-stamped 13-Oct-2026, 07:24.



Prime coat (MC1), RD-A-1, Zone 05

Distributor spraying the MC1 prime coat. GPS-stamped 13-Oct-2026, 16:09.



Aggregate base course, RD-A-1, Zone 05

Pavers and tippers placing the base course. GPS-stamped 13-Oct-2026, 08:25.



Aggregate base course, RD-A-1, Zone 04

Roller compacting behind the paver. GPS-stamped 13-Oct-2026, 08:04.



Rapid impact compaction, BL-23, Zone 07

RIC rig compacting the block platform. GPS-stamped 13-Oct-2026, 08:59.



Backfilling, BL-23, Zone 09

Dozer spreading fill as a tipper unloads. GPS-stamped 13-Oct-2026, 08:59.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet, 19-Oct-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	2.0%	100.0%	80.9%	−19.1%	0.81	▼ Behind
Procurement	8.2%	100.0%	5.1%	−94.9%	0.05	▼ Behind
Construction	78.7%	24.5%	27.5%	+3.0%	1.12	▲ Ahead
↳ Earthworks	21.9%	23.7%	71.6%	+47.9%	3.02	▲ Ahead
↳ Zone works (Z1–Z9)	50.7%	22.2%	8.0%	−14.3%	0.36	▼ Behind
↳ Tunnels	3.0%	93.8%	62.3%	−31.5%	0.66	▼ Behind
↳ Stations, open channels, demolition	3.1%	0.0%	0.1%	+0.1%	–	● Not yet due
Testing & commissioning	11.2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**29.4%**	**23.6%**	**−5.8%**	**0.80**	▼ Behind

Within the zone works, SPI ranges from 0.01 (Zone 2) to 0.52 (Zone 6), and Zone 1 has not started. Preliminaries and permits carry less than 0.01% of the weight.

Scope of work: quantities

Total scope, quantity executed and quantity remaining for each item, from the BOQ breakdown slide of the 19-Oct-2026 progress presentation (the same figures as the workbook's Major Quantities sheet). Quantities are given for the whole project, not by zone. The latest report does not give last week's quantities, so the "This week" column is blank.

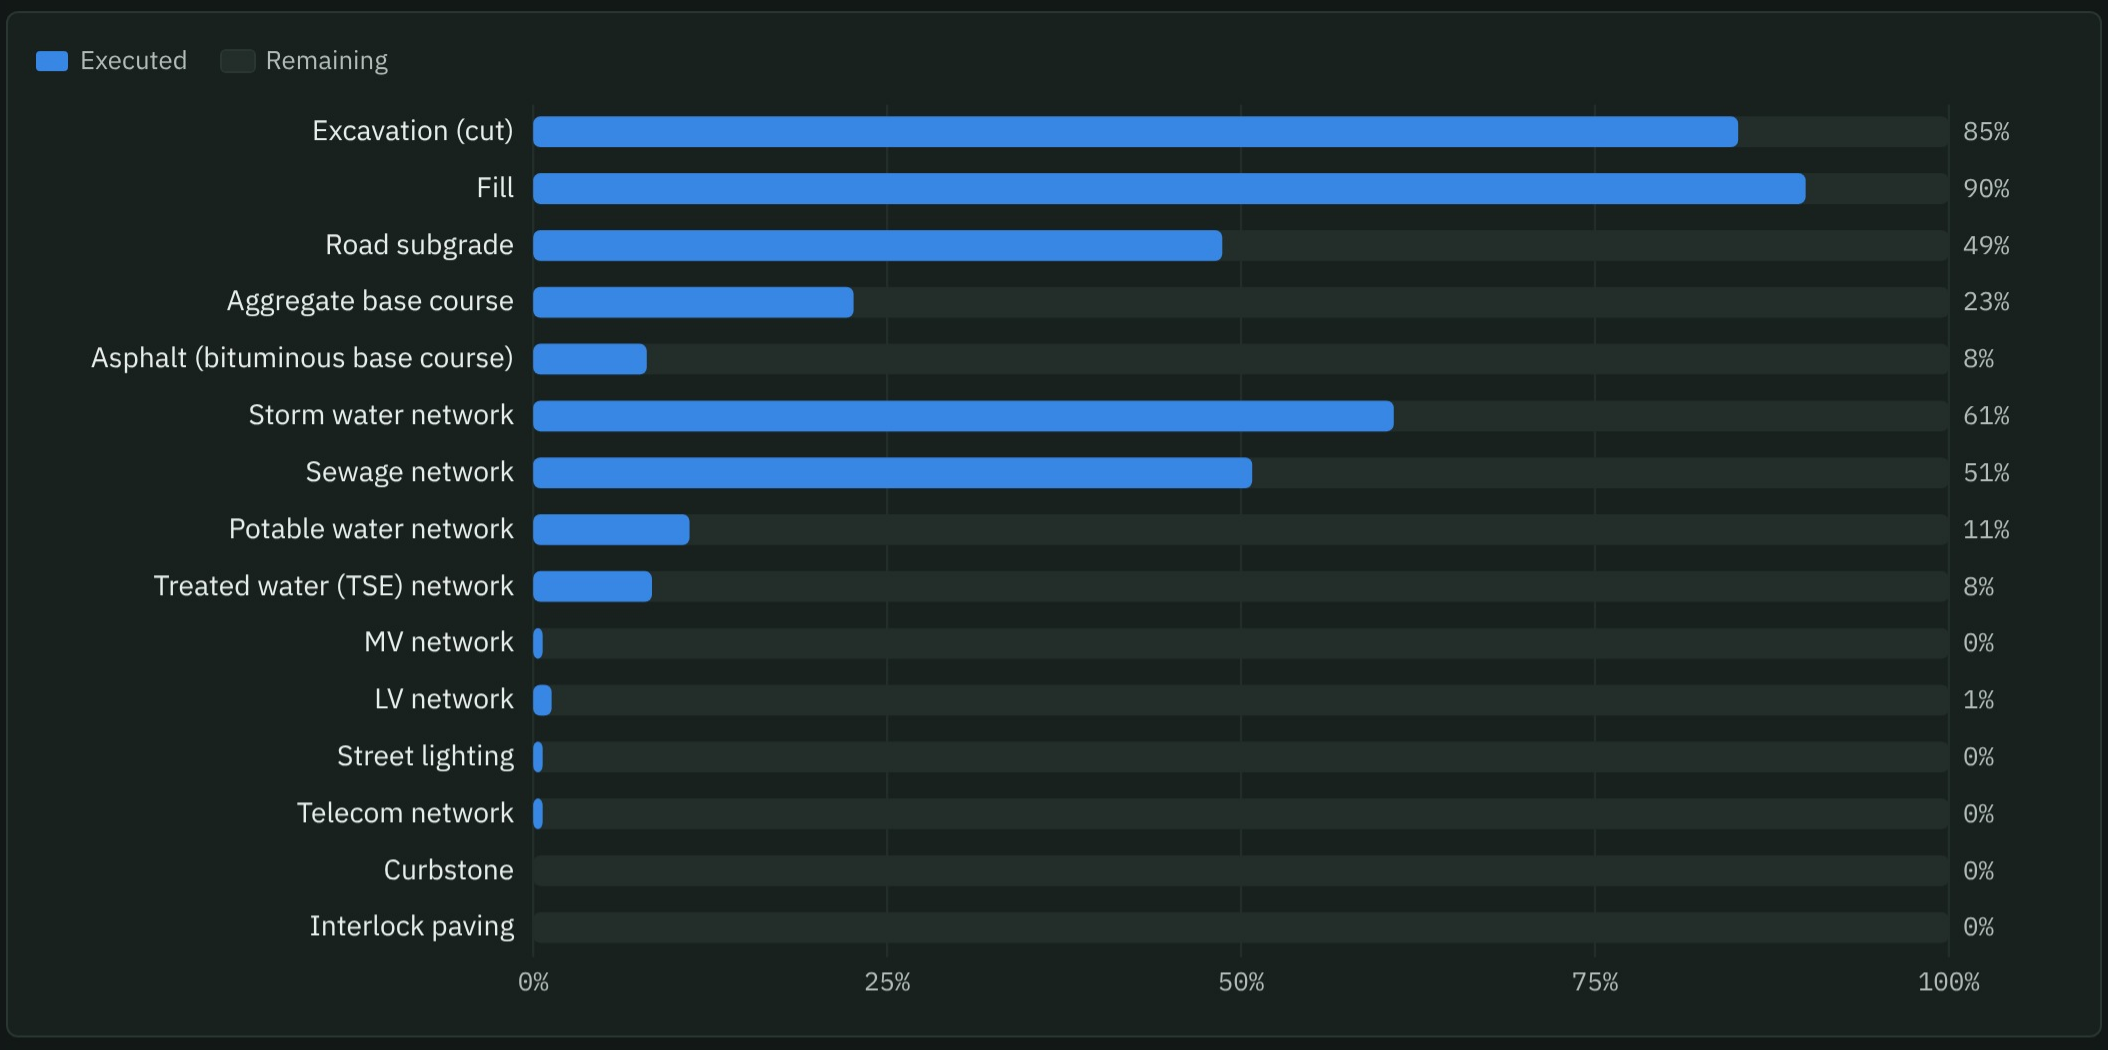

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation (cut)	All	m³	4,319,104	3,676,360	–	642,744	85.1%	–
Fill	All	m³	3,811,986	3,426,403	–	385,583	89.9%	–
Road subgrade	All	m³	232,143	113,000	–	119,143	48.7%	–
Aggregate base course	All	m³	145,809	33,000	–	112,809	22.6%	–
Asphalt (bituminous base course)	All	m³	86,559	6,946	–	79,613	8.0%	–
Storm water network	All	LM	50,642	30,786	–	19,856	60.8%	–
Sewage network	All	LM	22,579	11,468	–	11,111	50.8%	–
Potable water network	All	LM	31,687	3,500	–	28,187	11.0%	–
Treated water (TSE) network	All	LM	35,746	3,000	–	32,746	8.4%	–
MV network	All	LM	131,104	350	–	130,754	0.3%	–
LV network	All	LM	24,579	320	–	24,259	1.3%	–
Street lighting	All	LM	67,945	180	–	67,765	0.3%	–
Telecom network	All	LM	53,637	201	–	53,436	0.4%	–
Curbstone	All	LM	130,589	0	–	130,589	0.0%	–
Interlock paving	All	m²	42,347	0	–	42,347	0.0%	–

Earthworks well advanced

Cut is 85.1% and fill 89.9% complete. Subgrade is at 48.7%, aggregate base course 22.6% and asphalt 8.0%. Of the wet networks, the storm network is 60.8% and sewage 50.8% installed.

Networks barely started

The MV network is at 0.3% (350 of 131,104 m), street lighting 0.3%, telecom 0.4% and LV 1.3%. Potable water is at 11.1% and treated water (TSE) at 8.4%. Curbstone and interlock have not started.

Milestones

Contract milestones from the Milestones sheet of the weekly report, with the status given in the progress presentation. No P6 milestone dates were provided in readable form.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	DAYS CHANGE	PRESENTATION	STATUS
Contract award	09-Nov-2025	09-Nov-2025	0	–	✓ Done
Contract signing	22-Nov-2025	22-Nov-2025	0	–	✓ Done
Site handover	30-Nov-2025	30-Nov-2025	0	–	✓ Done
Complete mobilisation	29-Dec-2025	30-Mar-2026	−91	Finished	✓ Done, late
Drawings and materials submitted and approved	28-Jan-2026	30-Apr-2026	−92	Ongoing, completion 30-Jun-2026	▼ Late
All materials delivered to site	28-Feb-2026	–	–	Ongoing	▼ Late
Complete MV and road works	30-Sep-2026	30-Sep-2026	0	Ongoing	▼ Late
Complete deep networks	30-May-2027	30-May-2027	0	Not started	▼ At risk
Complete all networks	30-Nov-2027	30-Nov-2027	0	Not started	▼ At risk
All works complete, ready for initial handover	30-May-2028	30-May-2028	0	Not started	? Conflicts with forecast 06-Feb-2029
Demobilisation and PAC	30-May-2028	30-May-2028	0	Not started	▼ At risk

The weekly report gives three different completion dates.

The Milestones sheet keeps 30-May-2028 with no change, the General Information sheet forecasts 06-Feb-2029 (−252 days), and the P6 extract on the Progress sheet finishes the project on 13-Feb-2029 with −259 days of total float. The "Complete MV and road works" milestone still shows 30-Sep-2026 with no delay, although the date has passed and the presentation reports it as ongoing.

Procurement of key materials

Share of total quantity delivered to site. Source: procurement status slide, progress presentation 19-Oct-2026.

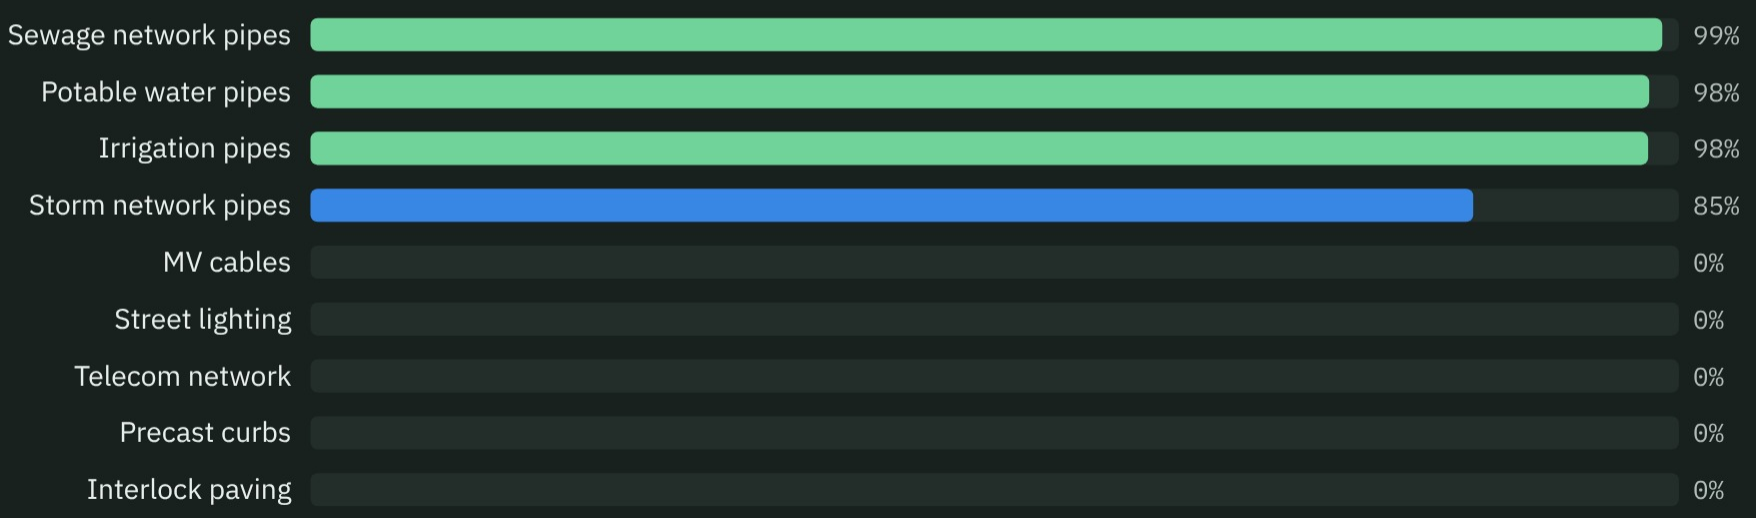

Electrical, telecom, curbs and interlock: nothing delivered


MV (131,104 LM), street lighting (67,945 LM), telecom (53,637 LM), precast curbs (130,589 LM) and interlock (42,347 m²) are all at 0% delivered. The MV and street-lighting suppliers have no approved material submittal in the presentation.

Pipes for the wet networks mostly on site

Sewage 99%, potable water 98% and irrigation 98% of pipe length is delivered. The storm network is at 85% (43,030 of 50,642 LM). Delivery of manhole rings and covers, GRP and UPVC pipes is continuing.

Manpower

Monthly manual head count on site, planned vs actual. Source: Manpower sheet, weekly report 19-Oct-2026.

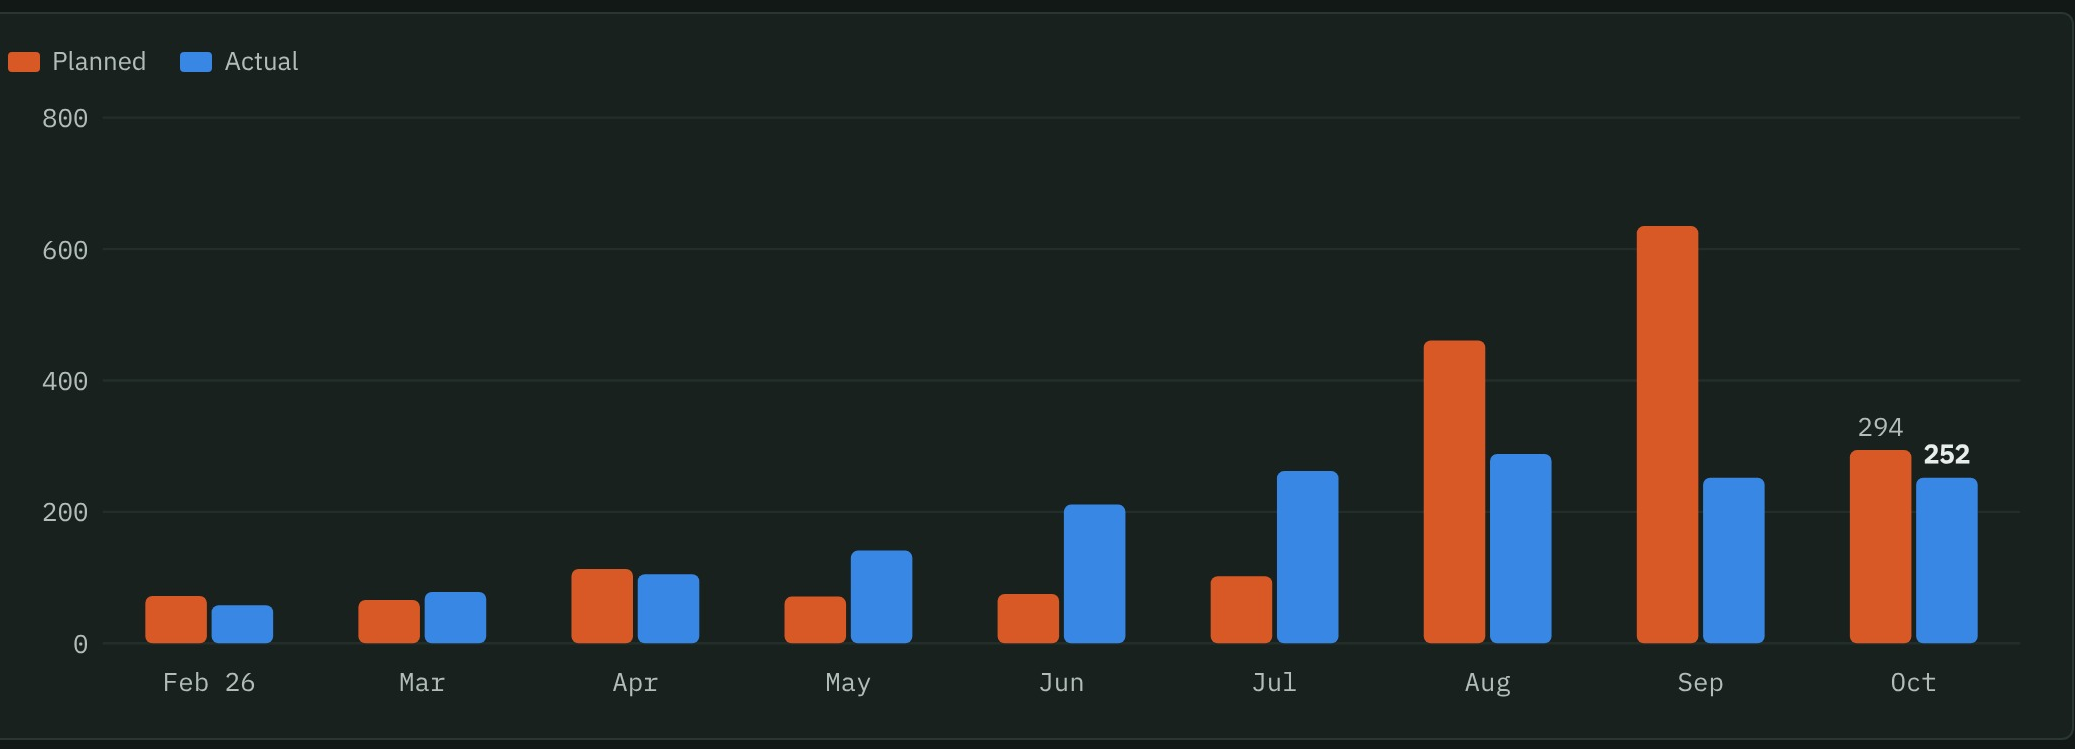

October manual head count is 252 against 294 planned (–14%), plus 47 non-manual staff, for 299 in total. October repeats September's figure of 252. The plan rises to 1,033 in March 2027. On site: 208 items of major equipment, including 56 excavators.

Cost and invoicing

Contract value

Bill 1: road and site works	214,146,361
Bill 2: electrical works	56,351,312
Bills 2.1–2.3: telecom, ICT and security	26,333,019
Bills 3–6: water, irrigation, sewage, storm	98,702,595
Bill 7: buildings, utilities and tunnels	49,466,713
Contract value	**445,000,000**
Revised BOQ (excl. VAT)	374,123,662
Change orders	0

All values in SAR. The bills add up to the 445,000,000 contract value. No change orders are registered.

Invoices

Invoices submitted	8
Gross value	71,001,361
Deductions and penalties	380,000
Net incl. VAT	81,271,566
Approved by the consultant	8
Approved by MODON PM / paid	0 / 0

Invoicing is 16.0% of the contract value against 23.6% physical progress. The presentation gives different totals: 54,980,525 invoiced and 41,804,647 paid.

Health, safety and quality

Safety Score 0.55

Safe man-hours (cumulative)	458,560
Man-hours this week	18,000
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	1
Property damage	0
Inductions / toolbox talks	348 / 409

The safety score comes from the MODON HSE site inspection dated 09-Jul-2026.

Quality Score 0.81

Inspection requests issued / closed	720 / 700
MIRs issued / closed	101 / 100
NCRs issued / closed	34 / 33
Site instructions	0
Shop drawings submitted (code A / B)	1,453 (7 / 1,446)
Material submittals	111

Cumulative counts from the Quality-Stat sheet.

Open issues and risks

ISSUE	OWNER	DETAIL
Clash with SEC high-voltage cables	Contractor / SEC	High-voltage cables of the Saudi Electricity transmission company clash with Road C2. A technical solution was submitted and is awaiting SEC's reply. Rated critical; target 30-Oct-2026.
Clash with SEC medium-voltage cables	Contractor / SEC	MV cables clash with Road C8. SEC's contractor (Pillar) has visited the site and a start-of-work record was signed. Rated critical.
Clash with Green Riyadh services	Contractor / Green Riyadh	An air vent and cathodic protection on Road C8 clash with the works. Coordination with Green Riyadh's contractor is ongoing to get drawings and price the diversion. Rated critical.
Clash with ARAMCO gas lines	Contractor / ARAMCO	Wet and dry networks on Roads C8 and RD-L10 clash with two ARAMCO gas lines. ARAMCO approved the technical solutions for telecom, sewage, MV, ICT and LV; coordination continues for the remaining networks. Rated high.
Procurement delays	Contractor	Purchase orders had to be revised after the design changes, and material prices rose. Orders are now issued and supply is under way. Rated high.
Progress behind plan	Contractor	Progress lags the schedule because of the master plan change (Wadi Al-Sulai) and the equipment shortage at the start. Most shop drawings are done and equipment and network crews were increased. Rated critical.

Delay reasons stated in the report: the master layout changed after the Wadi Al-Sulai redesign, which changed the design of all networks; and equipment was short at the start of the project.

Data notes

This report uses only the files uploaded for 19-Oct-2026, and every progress percentage in it is physical % complete, weighted by budgeted man-hours. Earlier weeks were not used, so there is no S-curve section: the workbook's Physical-Chart Data sheet is empty.

- The workbook and the presentation also give a cost-based progress figure, labelled as actual progress in places. This report does not use it.
- The weekly planned progress is negative (−3,650 man-hours, −1.55%), which suggests the plan changed this week. Procurement achieved man-hours also fell by 2,055.
- Three completion dates appear in the workbook: 30-May-2028 (Milestones sheet), 06-Feb-2029 (General Information) and 13-Feb-2029 (P6 extract, −259 days float). The P6 extract labelled "last week" gives 17-Dec-2029.
- Procurement: the presentation shows 85–99% of pipes delivered, but the workbook's Major Quantities sheet shows storm 576 m (1.1%), sewage 720 m (3.2%) and potable water 0 delivered. Procurement man-hour progress is only 5.1%.

- Invoices: the workbook lists 8 invoices, 71,001,361 SAR gross and none paid; the presentation shows 54,980,525 SAR invoiced and 41,804,647 SAR paid.
- The contract value of 445,000,000 SAR is called "including VAT" on the Conclusion sheet, but the bill breakdown gives the same total as "excluding VAT".
- Scope totals differ between sheets: MV 131,104 m (presentation) vs 171,170 m (Major sheet); interlock 42,347 m² vs 46,105 m². The Conclusion sheet also lists a second fill row (3,947,936 m³, 2.9%) that looks like an error.
- Several summary panels show `#REF!` or `#DIV/0!` errors (top issues, safety and quality scores in Codes, chart data). Inspection requests show 720 issued, 700 closed and only 1 pending.
- The October manual head count (252) repeats September's.
- Photos are stamped 13-Oct-2026, while the presentation's highlights cover 6–12 Oct. Block BL-23 appears under Zone 07 in one file name and Zone 09 in another. A seventh photo (tunnel interior, 20-Oct-2026) has no stamp and was not used.
- The P6 update (XER archive) was not converted to readable text, so P6 activity counts and milestone floats are not shown.

Compiled 28-Oct-2026 from the weekly report and progress presentation uploaded for 19-Oct-2026.
