Developing Infrastructure Networks in Riyadh's Fourth Industrial City

مشروع تطوير شبكات البنية التحتية بالرياض الرابعة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Rawaf Contracting	EGIS Saudi Engineering Consultancy	Shuaib A. Alshuaibi	30-Nov-2025	30-May-2028

Scope: infrastructure over about 6.5 km² of the Fourth Industrial City in Riyadh: roads and tunnels, electrical, telecom, ICT and security networks, potable water and fire-fighting, irrigation, sewage and stormwater networks, and sewage and stormwater pumping stations.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 25.2% against 30.1% planned, the project is behind by 4.9% (SPI 0.84). It gained 1.6% this week against 0.8% planned, so the gap narrowed from 5.8% last week. Earthworks remain far ahead of plan, but procurement, the zone network works and the tunnels are behind.

PHYSICAL % COMPLETE

25.2% / 30.1% plan

▼ SPI 0.84 −4.9%

PROGRESS THIS WEEK

+1.6% / +0.8% plan

▲ 0.9% above the weekly plan

CONTRACT TIME ELAPSED

36.2% · day 330 of 912

▼ P6 finish 01-Feb-2029

INVOICED TO DATE (GROSS)

16.0% · 71.0M SAR

8 invoices, last period ends 30-Sep-2026

The schedule still finishes the project about eight months late.

The P6 extract in this week's report finishes the project on 01-Feb-2029, 247 days after the contract completion date of 30-May-2028 (last week: 13-Feb-2029, −259 days). The report's General Information sheet still gives 06-Feb-2029. The "Complete MV and road works" milestone (30-Sep-2026) has passed with asphalt at 11.0% and the MV network at 0.3% installed.

Site photos this week

Six photos from the 26-Oct-2026 weekly upload. Five are GPS-stamped 24-Oct-2026: asphalt and base course on roads RD-A-1 and RD-L-7, and excavation and ground improvement on blocks BL-31 and BL-33. The sixth shows storm pipe laying. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt work, RD-A-1, Zone 04

Paver laying the bituminous base course. GPS-stamped 24-Oct-2026, 07:43.




Aggregate base course, RD-A-1, Zone 08

Paver placing the base course from a tipper. GPS-stamped 24-Oct-2026, 07:54.



Aggregate base course, RD-L-7, Zone 05

Paver and tipper on the road formation. GPS-stamped 24-Oct-2026, 08:53.

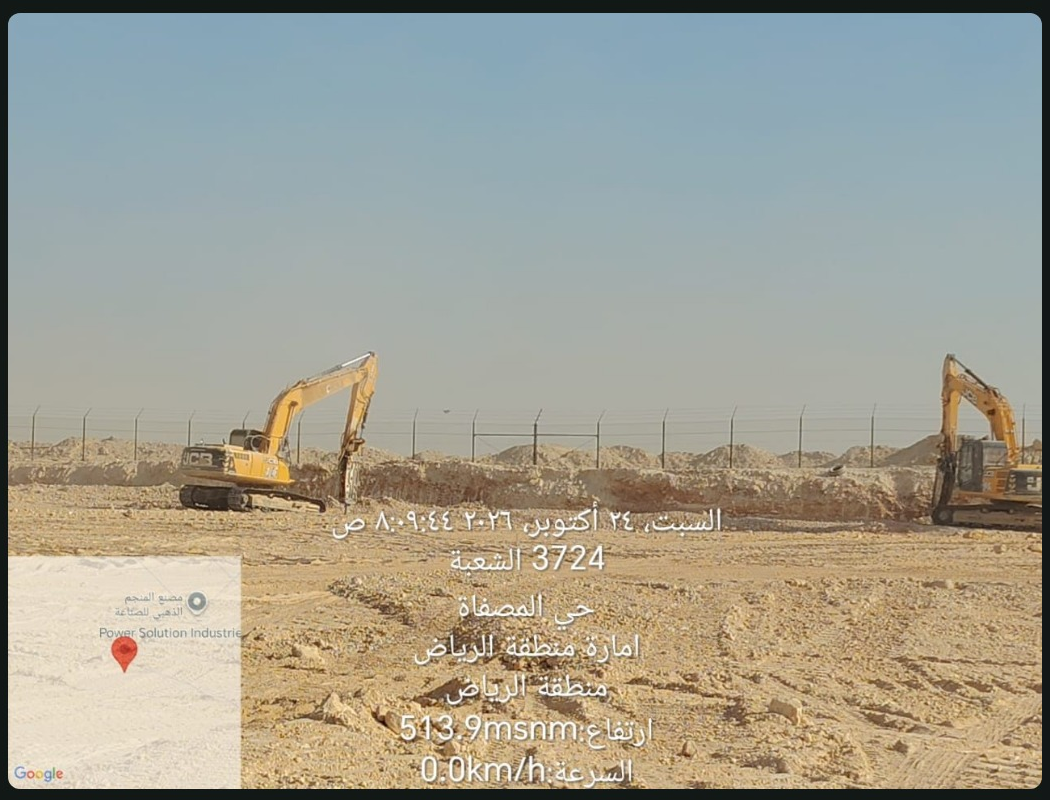

Cutting works, BL-31, Zone 09

Excavators cutting the block platform. GPS-stamped 24-Oct-2026, 08:09.



Rapid impact compaction, BL-33, Zone 09

RIC rig compacting the block platform. GPS-stamped 24-Oct-2026, 08:21.



Storm pipe installation

Pipe laid in an open trench. No stamp; file dated 24-Oct-2026.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet, 26-Oct-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	2.0%	100.0%	82.3%	−17.7%	0.82	▼ Behind
Procurement	8.2%	100.0%	6.6%	−93.4%	0.07	▼ Behind
Construction	78.7%	25.4%	29.3%	+3.9%	1.15	▲ Ahead
↳ Earthworks	21.9%	23.7%	74.0%	+50.3%	3.13	▲ Ahead
↳ Zone works (Z1–Z9)	50.7%	23.5%	9.2%	−14.3%	0.39	▼ Behind
↳ Tunnels	3.0%	97.5%	72.1%	−25.4%	0.74	▼ Behind
↳ Stations, open channels, demolition	3.1%	0.0%	1.4%	+1.4%	–	● Not yet due
Testing & commissioning	11.2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**30.1%**	**25.2%**	**−4.9%**	**0.84**	▼ Behind

Within the zone works, SPI ranges from 0.02 (Zones 1 and 2) to 0.54 (Zone 6); Zone 1 started this week. Stations recorded their first progress this week. Preliminaries and permits carry less than 0.01% of the weight.

Scope of work: quantities

Total scope, quantity executed and quantity remaining for each item, from the scope table on the Conclusion sheet of the 26-Oct-2026 weekly report (the same figures as its Major Quantities sheet). Quantities are for the whole project, not by zone. "This week" is this report's quantity minus the 19-Oct-2026 report's.

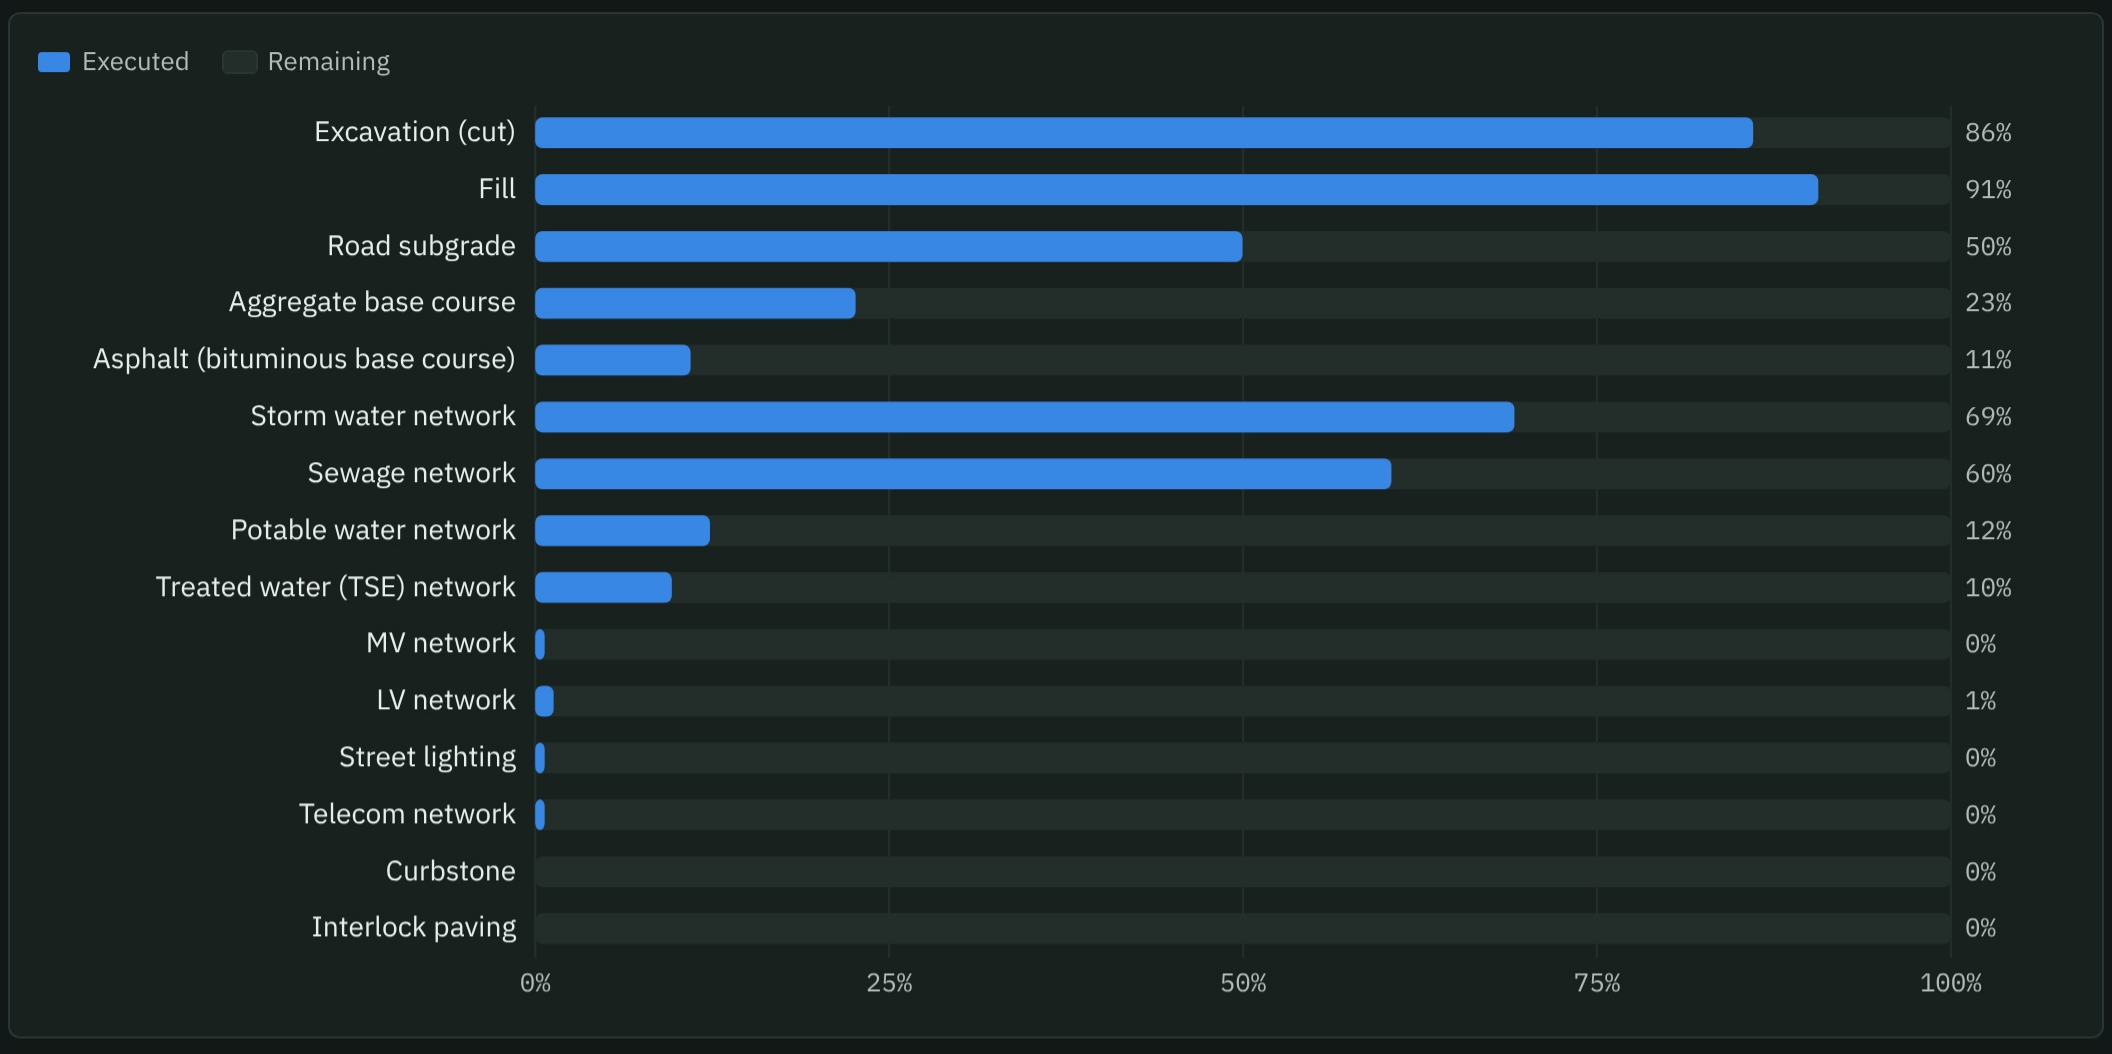

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation (cut)	All	m³	4,319,104	3,716,000	+39,640	603,104	86.0%	–
Fill	All	m³	3,811,986	3,455,205	+28,802	356,781	90.6%	–
Road subgrade	All	m³	232,143	116,000	+3,000	116,143	50.0%	–
Aggregate base course	All	m³	145,809	33,000	0	112,809	22.6%	–
Asphalt (bituminous base course)	All	m³	86,559	9,501	+2,555	77,058	11.0%	–
Storm water network	All	LM	50,642	35,030	+4,244	15,612	69.2%	–
Sewage network	All	LM	22,579	13,656	+2,188	8,923	60.5%	–
Potable water network	All	LM	31,687	3,912	+412	27,775	12.3%	–
Treated water (TSE) network	All	LM	35,746	3,450	+450	32,296	9.7%	–
MV network	All	LM	131,104	350	0	130,754	0.3%	–
LV network	All	LM	24,579	320	0	24,259	1.3%	–
Street lighting	All	LM	67,945	180	0	67,765	0.3%	–
Telecom network	All	LM	53,637	201	0	53,436	0.4%	–
Curbstone	All	LM	130,589	0	0	130,589	0.0%	–
Interlock paving	All	m²	42,347	0	0	42,347	0.0%	–

Earthworks and wet networks moving

Cut is 86.0% and fill 90.6% complete. Subgrade reached 50.0% and asphalt 11.0% (+2,555 m³ this week); aggregate base course stayed at 22.6%. The storm network rose to 69.2% (+4,244 m) and sewage to 60.5% (+2,188 m).

Electrical and telecom networks not moving

The MV network is still at 0.3% (350 of 131,104 m), street lighting 0.3%, telecom 0.4% and LV 1.3%, with no change this week. Potable water is at 12.3% and treated water (TSE) at 9.7%. Curbstone and interlock have not started.

Milestones

Contract milestones from the Milestones sheet of the weekly report. No P6 milestone dates were provided in readable form.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	DAYS CHANGE	STATUS
Contract award	09-Nov-2025	09-Nov-2025	0	✓ Done
Contract signing	22-Nov-2025	22-Nov-2025	0	✓ Done
Site handover	30-Nov-2025	30-Nov-2025	0	✓ Done
Complete mobilisation	29-Dec-2025	30-Mar-2026	−91	✓ Done, late
Drawings and materials submitted and approved	28-Jan-2026	30-Apr-2026	−92	▼ Late
All materials delivered to site	28-Feb-2026	–	–	▼ Late
Complete MV and road works	30-Sep-2026	30-Sep-2026	0	▼ Late
Complete deep networks	30-May-2027	30-May-2027	0	▼ At risk
Complete all networks	30-Nov-2027	30-Nov-2027	0	▼ At risk
All works complete, ready for initial handover	30-May-2028	30-May-2028	0	? Conflicts with P6 finish 01-Feb-2029
Demobilisation and PAC	30-May-2028	30-May-2028	0	▼ At risk

The weekly report still gives three different completion dates.

The Milestones sheet keeps 30-May-2028 with no change, the General Information sheet forecasts 06-Feb-2029 (−252 days, unchanged from last week), and the P6 extract on the Progress sheet finishes the project on 01-Feb-2029 with −247 days of total float. The "Complete MV and road works" milestone still shows 30-Sep-2026 with no delay, although the date has passed and the work is not finished.

Procurement of key materials

Share of total quantity delivered to site. Source: material delivery table on the Conclusion sheet and the Major Quantities sheet, weekly report 26-Oct-2026.



Electrical, telecom, curbs and interlock: nothing delivered


MV (131,104 LM), street lighting (67,945 LM), telecom (53,637 LM), precast curbs (130,589 LM) and interlock (42,347 m²) are all still at 0% delivered.

Wet-network materials mostly on site

Sewage 99%, potable water 98% and irrigation 98% of pipe length is delivered. The storm network is at 87% (44,030 of 50,642 LM), up 1,000 LM on last week. Inlet manholes are at 96% (480 of 501) and catch basins at 91% (906 of 998).

Manpower

Monthly manual head count on site, planned vs actual. Source: Manpower sheet, weekly report 26-Oct-2026.

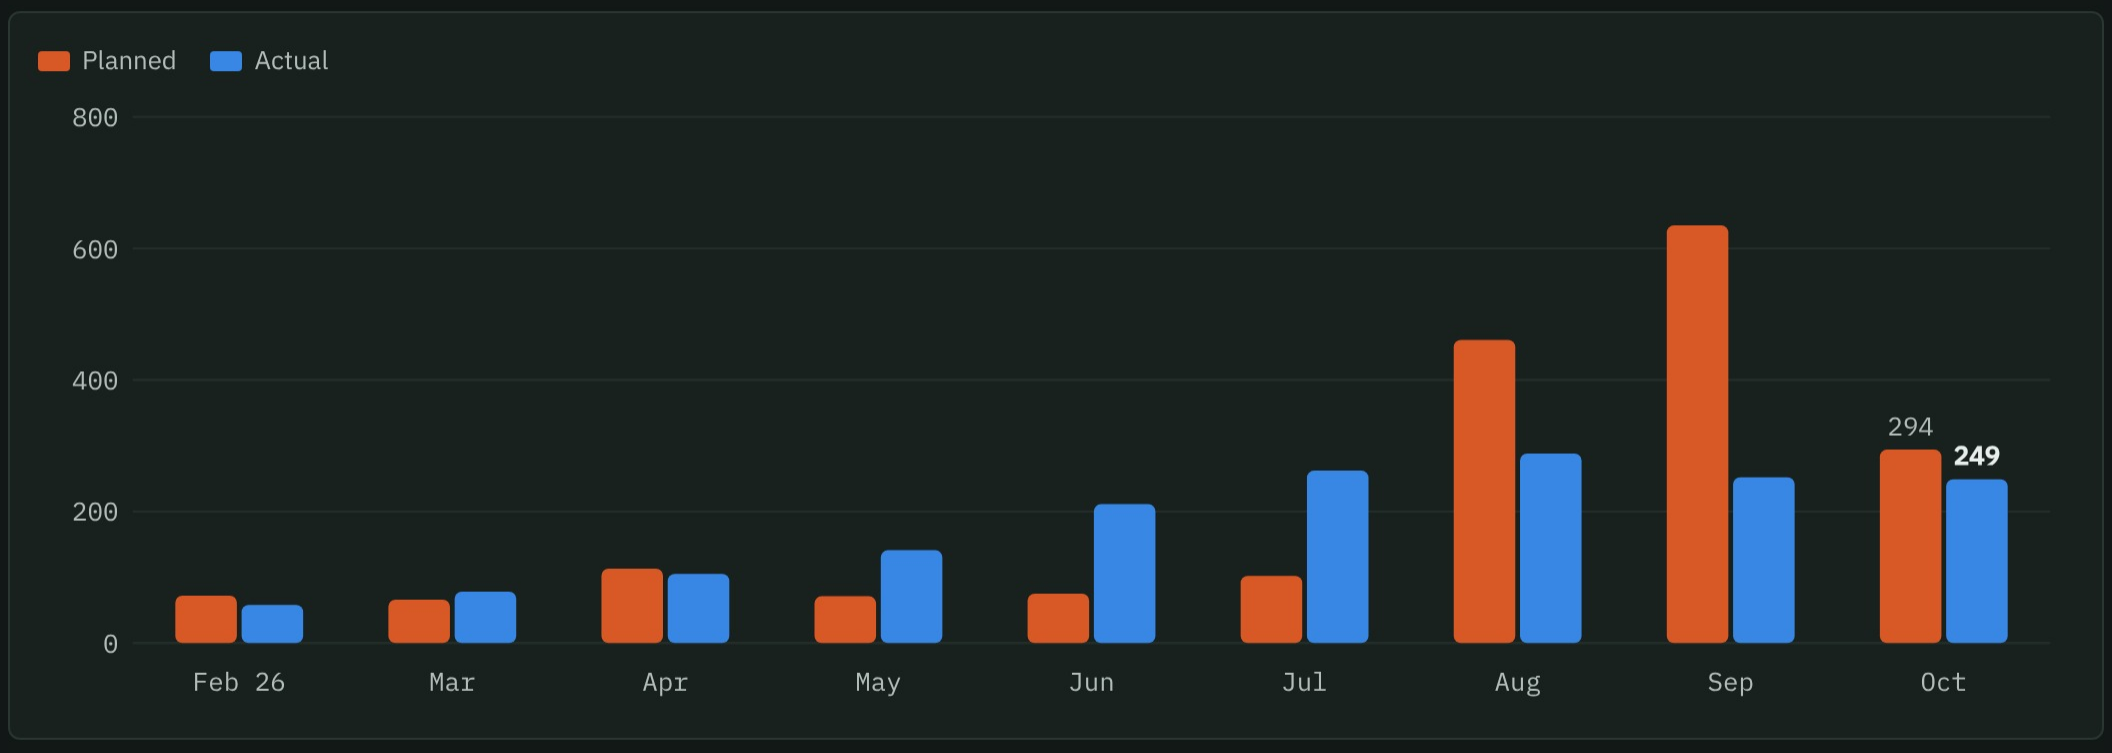

October manual head count is 249 against 294 planned (−15%), plus 47 non-manual staff, for 296 in total. Last week's report gave 252 for October. The plan rises to 1,033 in March 2027. On site: 208 items of major equipment, including 56 excavators.

Cost and invoicing

Contract value

Bill 1: road and site works	214,146,361
Bill 2: electrical works	56,351,312
Bills 2.1–2.3: telecom, ICT and security	26,333,019
Bills 3–6: water, irrigation, sewage, storm	98,702,595
Bill 7: buildings, utilities and tunnels	49,466,713
Contract value	**445,000,000**
Revised BOQ (excl. VAT)	352,632,896
Change orders	0

All values in SAR. The bills add up to the 445,000,000 contract value. The revised BOQ total fell from 374,123,662 last week. No change orders are registered.

Invoices

Invoices submitted	8
Gross value	71,001,361
Deductions and penalties	380,000
Net incl. VAT	81,271,566
Approved by the consultant	8
Approved by MODON PM / paid	0 / 0

Invoicing is 16.0% of the contract value against 25.2% physical progress. No new invoice was submitted this week.

Health, safety and quality

Safety Score 0.55

Safe man-hours (cumulative)	458,560
Man-hours this week	18,000
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	1
Property damage	0
Inductions / toolbox talks	348 / 409

All safety figures are identical to last week's report. The safety score comes from the MODON HSE site inspection dated 09-Jul-2026.

Quality Score 0.81

Inspection requests issued / closed	720 / 700
MIRs issued / closed	101 / 100
NCRs issued / closed	34 / 33
Site instructions	0
Shop drawings submitted (code A / B)	1,453 (7 / 1,446)
Material submittals	111

Cumulative counts from the Quality-Stat sheet, unchanged from last week.

Open issues and risks

ISSUE	OWNER	DETAIL
Clash with SEC high-voltage cables	Contractor / SEC	High-voltage cables of the Saudi Electricity transmission company clash with Road C2. A technical solution was submitted and is awaiting SEC's reply. Rated critical; target 30-Oct-2026.
Clash with SEC medium-voltage cables	Contractor / SEC	MV cables clash with Road C8. SEC's contractor (Pillar) has visited the site and a start-of-work record was signed. Rated critical.
Clash with Green Riyadh services	Contractor / Green Riyadh	An air vent and cathodic protection on Road C8 clash with the works. Coordination with Green Riyadh's contractor is ongoing to get drawings and price the diversion. Rated critical.
Clash with ARAMCO gas lines	Contractor / ARAMCO	Wet and dry networks on Roads C8 and RD-L10 clash with two ARAMCO gas lines. Technical solutions were submitted and await ARAMCO's reply; solutions for telecom, sewage, MV, ICT and LV are already approved. Rated high.
Procurement delays	Contractor	Purchase orders had to be revised after the design changes, and material prices rose. Orders are now issued and supply is under way. Rated high.
Progress behind plan	Contractor	Progress lags the schedule because of the master plan change (Wadi Al-Sulai) and the equipment shortage at the start. Most shop drawings are done and equipment and network crews were increased. Rated critical.

Delay reasons stated in the report: the master layout changed after the Wadi Al-Sulai redesign, which changed the design of all networks; and equipment was short at the start of the project.

Data notes

This report uses the weekly report uploaded for 26-Oct-2026 and, for this-week values, the 19-Oct-2026 report. Every progress percentage is physical % complete, weighted by budgeted man-hours. There is no S-curve section: the workbook's Physical-Chart Data sheet is empty.

- The week number, 47, is the contract week stated on the Milestones sheet ("Current Contract Weeks: 47 of 130").
- The workbook also gives a cost-based progress figure, labelled as actual progress in places. This report does not use it.
- Three completion dates appear in the workbook: 30-May-2028 (Milestones sheet), 06-Feb-2029 (General Information, not updated since last week) and 01-Feb-2029 (P6 extract, −247 days float; last week 13-Feb-2029).
- Procurement man-hour progress is only 6.6%, although 87–99% of the wet-network pipes are delivered. This week the Major Quantities sheet was updated to show the deliveries; last week it showed 1–3%.
- The safety statistics (18,000 man-hours this week, 458,560 cumulative) and the quality counts are identical to last week's report, so they appear not to have been updated.
- The October manual head count was changed from 252 (last week's report) to 249.
- The revised BOQ total changed from 374,123,662 to 352,632,896 SAR with no explanation.
- Invoices: the workbook lists 8 invoices, 71,001,361 SAR gross and none paid; last week's presentation showed 54,980,525 SAR invoiced and 41,804,647 SAR paid. The contract value of 445,000,000 SAR is called "including VAT" on the Conclusion sheet but "excluding VAT" in the bill breakdown.
- Scope totals differ between sheets: MV 131,104 m vs 171,170 m (Major sheet); interlock 42,347 m² vs 46,105 m². Several summary panels still show `#REF!` or `#DIV/0!` errors.
- No progress presentation or P6 update (XER) was uploaded this week. Milestone status therefore comes from the workbook only, and P6 milestone floats are not shown.
- Photos: five are stamped 24-Oct-2026; the storm pipe photo has no stamp. A tunnel wing-wall photo dated 28-Oct-2026 (after the data date) and a second BL-31 backfilling photo were not used.

Compiled 01-Nov-2026 from the weekly report uploaded for 26-Oct-2026, with this-week values from the 19-Oct-2026 report.
