New Infrastructure Development of the Second Phase, Third Industrial City, Jeddah

تطوير البنية التحتية بالمدينة الصناعية الثالثة بجدة

CLIENT	CONTRACTOR	MODON PM	CONTRACT START	CONTRACT COMPLETION
MODON	Alrawaf Contracting	Ahmed Kutbi	16-Mar-2025	15-Mar-2028

Scope: infrastructure networks (roads, sewage, storm water, potable water, TSE, irrigation, electrical, street lighting and telecom), the potable water and TSE pump stations, three lift stations, a mosque, the CMZ to Jeddah-Jazan linking road and the added scope of revised BOQ No. 03 (Zone 5). Contract value SAR 560 million excluding VAT.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (the labour units in the P6 schedule update). The weekly report archive uploaded this week holds only the P6 update, so the figures below were computed from it: 52.75% actual against 52.76% planned under the revised baseline, SPI 1.00. The total hides a split: the infrastructure networks are 10.3% behind their plan, offset by the pump stations and the Zone 5 added scope, which are ahead of it.

PHYSICAL % COMPLETE

52.75% / 52.76%

plan

SPI 1.00 −0.02%

PROGRESS THIS WEEK

—

No earlier week uploaded to compare with

CONTRACT TIME ELAPSED

53.8% · day 589 of 1,095

▼ P6 finish 19-Mar-2028

INVOICED (AS OF 15-JUN-2026)

48.7% · 272.6M SAR

Tracker Info sheet, not updated since June

The P6 update finishes the project 4 days after the contract date, and the works may be stopped.

Project finish is scheduled on 19-Mar-2028 against the contract completion date of 15-Mar-2028, driven by the TSE pump station: 134 open activities have zero float, 93 of them in the TSE pump station and 40 in the networks. The TSE, sewage and storm network finish milestones (baseline 11, 17 and 25 October 2026) are now forecast for November 2026. The risk log, in an entry dated 26-Oct-2026, records that works on the project have not resumed pending completion of safety and security requirements, and the P6 update records no activity started or finished after 19-Oct-2026.

Site photos this week

Six of the eight photos uploaded for this week. The time-stamped ones are dated 17-Oct-2026, in the previous week. They show asphalt base course paving in the Logistic Area and on road R66-04, the Mobco road formation and cable protection tiles on the electrical works. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt base course, Logistic Area

Pneumatic roller on the new layer. Stamped 17-Oct-2026, 09:16.




Asphalt paving, Logistic Area

Paver laying the base course. Stamped 17-Oct-2026, 09:16.




Asphalt base course, road R66-04

Paver and roller at sunrise. Stamped 17-Oct-2026, 06:47.

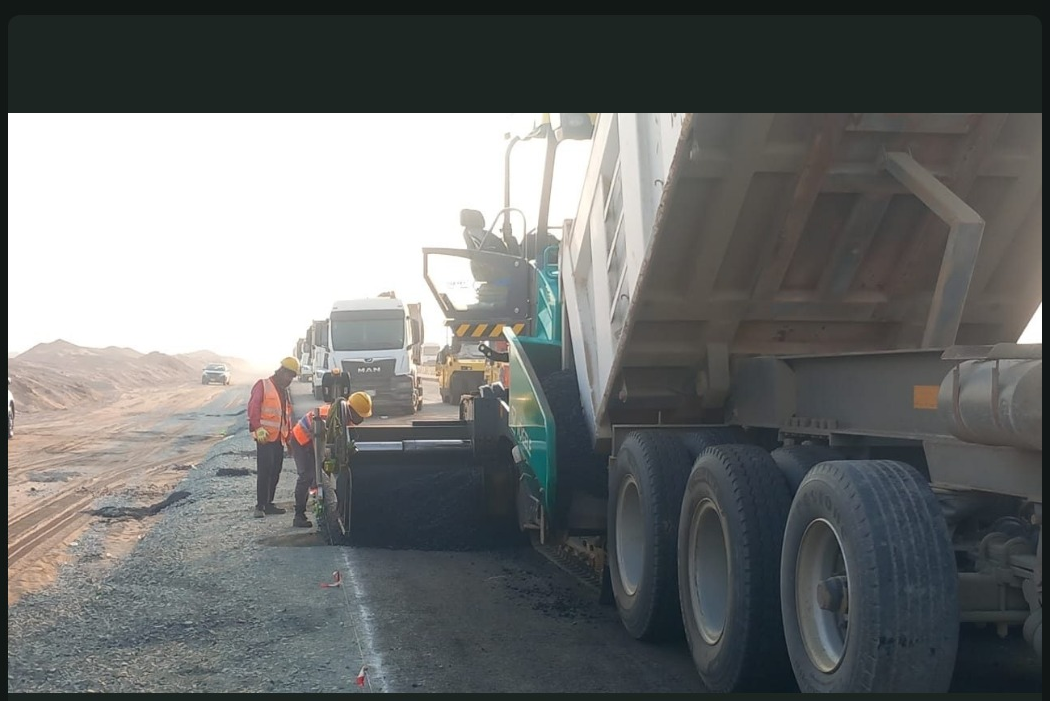

Asphalt paving, road R66-04

Tipper feeding the paver, crew alongside.

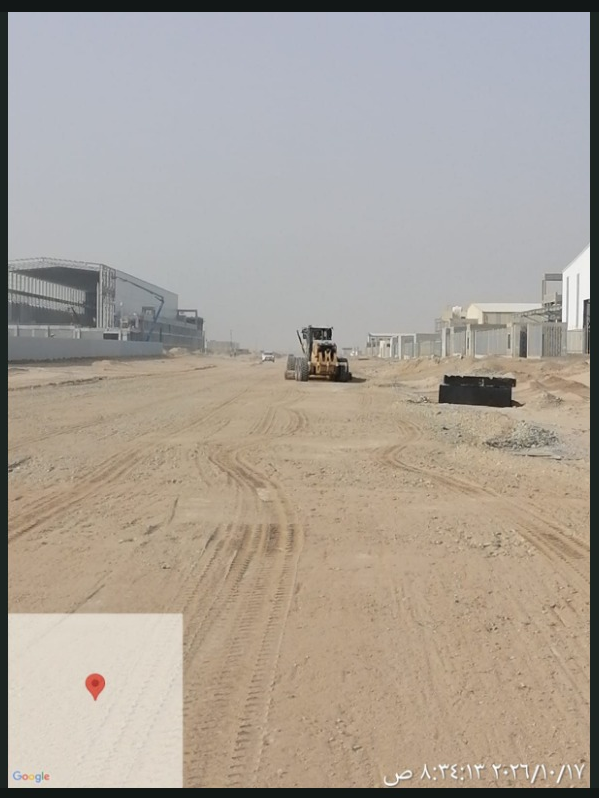

Mobco road works

Grader on the road formation beside the factories. Stamped 17-Oct-2026, 08:34.




Electrical works

Cable protection tiles laid in the trench. GPS 21.15281N 39.3528E.

Progress S-curve

Cumulative physical progress (man-hour weighted) at each month end. Source: P6 update 009-wpr78-26-10-2026 and revised baseline 009-RVSD03-REV02-1.

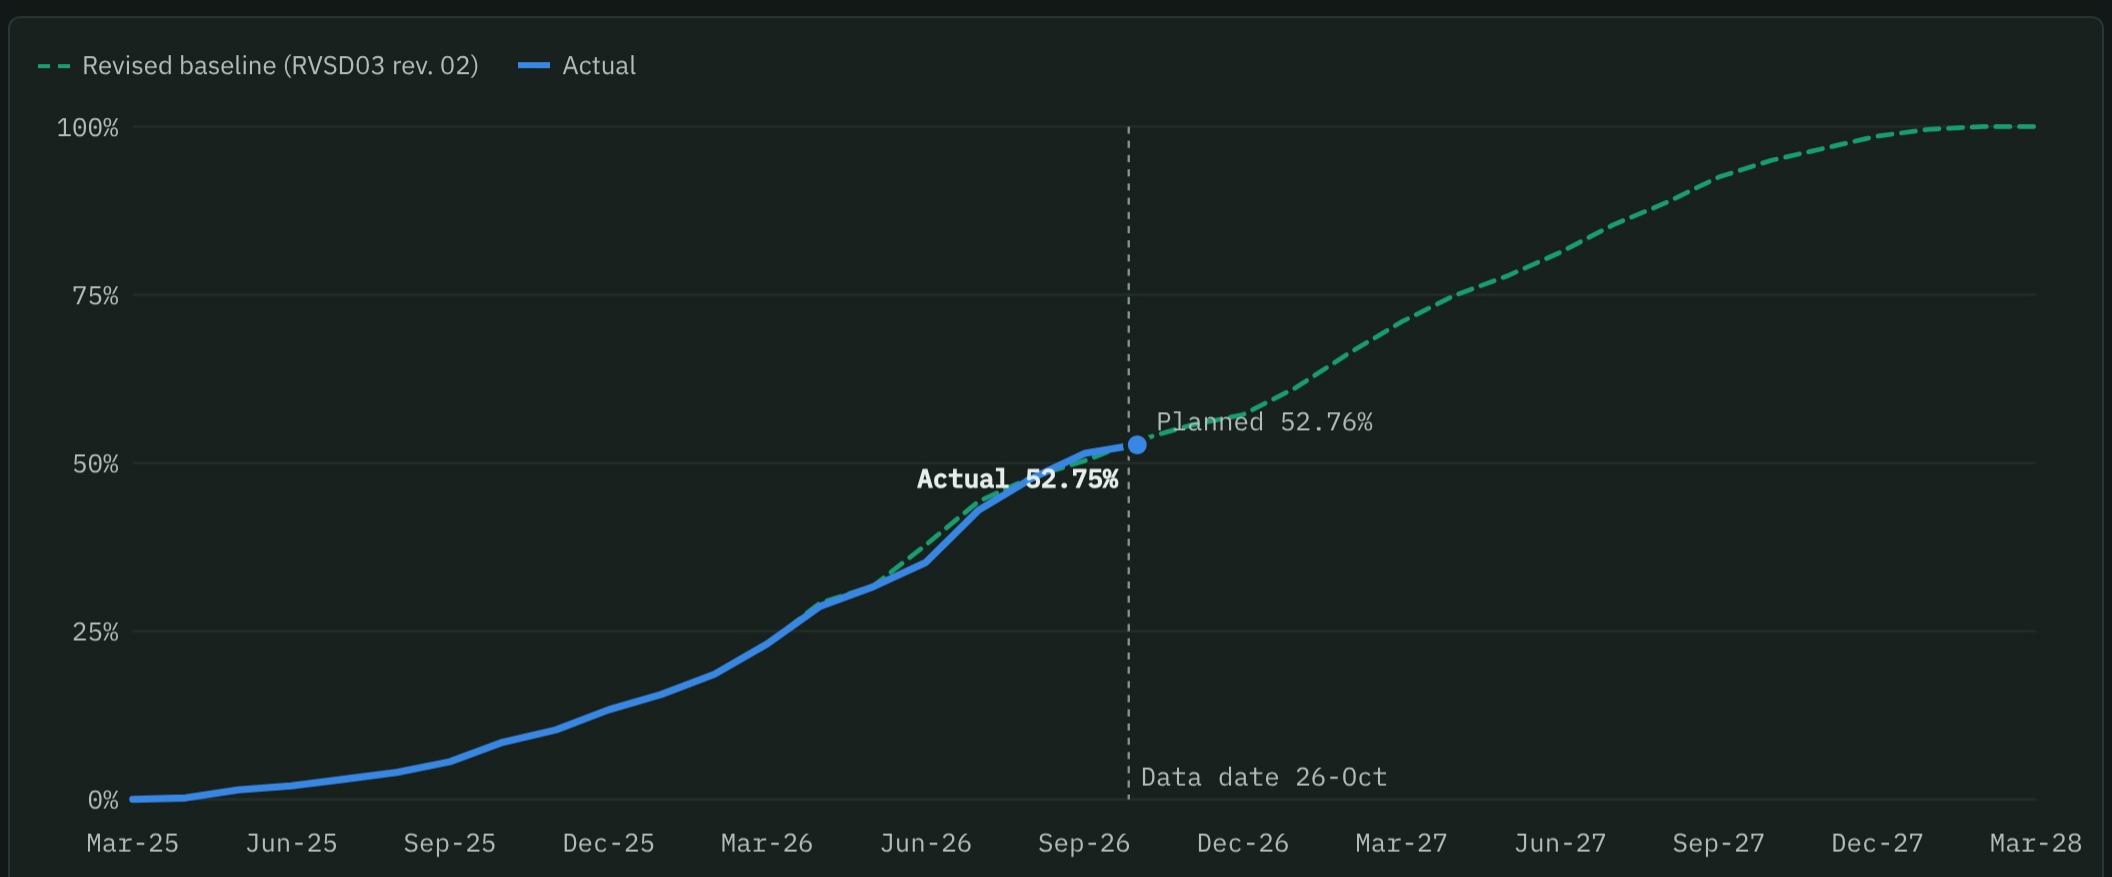

DATA DATE	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
26-Oct-2026	**52.76**	**52.75**	**-0.02%**	**—**	**1.00**

Method: each activity is weighted by its budgeted labour units in the P6 update. Planned progress spreads those units evenly between the activity's start and finish dates in the revised baseline; actual progress uses each activity's physical % complete. Monthly actuals before the data date spread completed work evenly between actual start and finish, so they are approximate. Engineering, procurement and close-out activities carry no labour units, so the measure covers the construction works. No earlier week was uploaded, so the gain this week cannot be computed.

Progress by phase

Physical progress to date by top-level WBS, measured by budgeted man-hours. SPI is not shown where less than 5% was planned.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Infrastructure networks	54.8%	75.8%	65.5%	−10.3%	0.86	▼ Behind
Potable water pump station	16.7%	21.3%	40.9%	+19.6%	1.92	▲ Ahead
Added scope, R.BOQ No. 03 (Zone 5, CMZ link, Pond 5)	10.8%	1.9%	26.1%	+24.2%	–	▲ Ahead
TSE pump station	5.3%	2.4%	14.3%	+11.9%	–	▲ Ahead, on critical path
New roads	3.9%	87.3%	59.0%	−28.3%	0.68	▼ Behind
CMZ to Jeddah-Jazan linking road	2.4%	100.0%	77.1%	−22.9%	0.77	▼ Behind
Lift station 02	1.5%	13.7%	30.6%	+16.9%	2.23	▲ Ahead
Lift station 01	1.4%	0.3%	27.4%	+27.1%	–	▲ Ahead
Mosque	1.2%	53.6%	68.2%	+14.6%	1.27	▲ Ahead
Al-Khorayef factory road	1.1%	62.8%	59.6%	−3.2%	0.95	▼ Slightly behind
Lift station 03	1.0%	1.2%	0.8%	−0.4%	–	▼ Slightly behind
Total	100%	**52.76%**	**52.75%**	**−0.02%**	**1.00**	● On plan

The P6 update (009-wpr78-26-10-2026, data date 26-Oct-2026) has 16,623 activities: 9,117 completed, 364 in progress and 7,142 not started. Its scheduled finish is 19-Mar-2028, 4 days after the contract date.

Milestones

Revised baseline (RVSD03 rev. 02) against the P6 update of 26-Oct-2026. No weekly report with its own milestone forecast was uploaded.

MILESTONE	BASELINE	P6 UPDATE FORECAST	VARIANCE (DAYS)	P6 FLOAT (DAYS)	STATUS
Project start	16-Mar-2025	16-Mar-2025 (actual)	0	–	✓ Done
Complete mobilisation	08-May-2025	08-May-2025 (actual)	0	–	✓ Done
Shop drawings and material submittals	29-Jun-2025	29-Jun-2025 (actual)	0	–	✓ Done
Finish of TSE network	11-Oct-2026	21-Nov-2026	+41	401	▼ Late
Finish of sewage network	17-Oct-2026	12-Nov-2026	+26	408	▼ Late
Finish of storm network	25-Oct-2026	08-Nov-2026	+14	412	▼ Late
Finish of CMZ road	14-Nov-2026	10-Feb-2027	+88	331	▼ Late
Finishing MV network (contractual)	19-Apr-2027	17-Dec-2026	−123	378	▲ Early
Finishing all networks (contractual)	15-Jun-2027	14-Feb-2027	−121	328	▲ Early
Finish of new roads	18-Feb-2027	20-Mar-2027	+30	365	▼ Late
Finishing road works (contractual)	20-Apr-2027	18-Jul-2027	+89	204	▼ Late
Finishing the deepest networks (contractual)	17-Aug-2027	12-Jun-2027	−66	235	▲ Early
Finish of Zone 5	13-Mar-2028	17-Nov-2027	−117	100	▲ Early
Finish of potable water pump station	08-Mar-2028	02-Mar-2028	−6	14	● Little float
Finish of TSE pump station	15-Mar-2028	19-Mar-2028	+4	0	▼ Late
Project finish	15-Mar-2028	19-Mar-2028	+4	0	▼ Late

Late milestones still show large float, because only the project finish drives float.

The TSE, sewage and storm networks were due by 25-Oct-2026 in the baseline and are now forecast for November 2026, and the contractual road works milestone moves from 20-Apr-2027 to 18-Jul-2027, yet P6 shows 200 to 400 days of float on them. The network milestone "Finish of Road Works" is scheduled on 27-Mar-2027, which does not match the contractual road works milestone of 18-Jul-2027.

Procurement of key materials

Share of the revised BOQ quantity delivered to site. Source: Procurement sheet of the procurement tracker dated 27-Oct-2026 (data date 26-Oct-2026).



Interlock and curbstone: barely delivered

Interlock: 0 of 166,014 m² delivered, PO issued. Curbstone: 29,512 m delivered across four curbstone types; the tracker repeats 160,860 m as the quantity of each type, so the total needed is unclear.

Stations and Zone 5

Of 1,464 tracked lines, 753 are delivered, 44 partly delivered, 8 marked available, 530 have a PO issued, 29 a PR issued and 100 no action yet, mostly fire alarm, CCTV and access control items for the station buildings. Station pumps: 3 of 7 delivered; station panels: 12 of 44; overhead cranes still at PR stage. Zone 5 lighting poles and luminaires (191 each) have POs issued, none delivered.

Cost and invoicing

Contract value

Contract value (excl. VAT)	560,000,000
Contract value incl. 15% VAT	644,000,000

All values in SAR, from the Info sheet of the procurement tracker. The risk and issue log gives the same contract value. No variation orders are recorded in the uploaded files.

Invoices

Invoiced to date	272,564,241
Share of contract value	48.67%

The Info sheet is dated 15-Jun-2026 and has not been updated since, so invoicing after mid-June is not known. The number of invoices and the paid amounts are not given.

Health, safety and quality

No safety statistics (man-hours, incidents) or inspection counts were uploaded this week. The approval logs below have a cut-off date of 26-Oct-2026; the open HSE and quality issues are listed under Open issues and risks.

Shop drawings

Drawings logged	3,502
Approved, code A	1,178
Approved as noted, code B	2,281
Revise and resubmit, code C	15
Under review	24
Remaining (potable water pump station)	4

Material submittals

Planned to date	120
Submitted	110
Late, not yet submitted	10
Approved, code A / code B	16 / 94
Pre-qualifications submitted	240
Pre-qualifications A / B / C / D	17 / 193 / 19 / 9

The 10 late submittals are 4 civil, 1 electrical, 5 architectural (also counted under infrastructure and stations).

Open issues and risks

ISSUE	OWNER	DETAIL
Works not resumed	Contractor	Risk log entry dated 26-Oct-2026: not resuming the works may delay the project beyond its contract duration. Mitigation: complete the safety and security requirements and resume works.
Weak HSE and security measures (critical)	Contractor	Safety violations. Action: raise HSE and security measures on the works.
Low manpower and equipment	Contractor	Low productivity, especially in the contractor's own crews. Action: increase manpower and productivity.
Repeated NCRs	Contractor	Rework caused by quality problems. Action: improve work quality and close the observations.
Repeated HSE observations	Contractor	Safety violations. Action: improve safety on the works and close the observations.
Changing scope (high risk)	MODON	The city's priorities and needs are changing: quantities reduced and new scope added. Mitigation: study the city's needs to fix the final scope.
Procurement delays (high risk)	Contractor	Late purchase orders and late delivery of long-lead materials; procurement also depends on cash flow (medium risk). Mitigation: follow up PO and delivery status.

Source: Risk - Issue Log workbook. Also in the risk register: harsh weather on site (heat, sand, heavy rain), rated medium.

Data notes

- The weekly report archive 009-wpr78-26-10-2026.rar contains only the P6 update (XER). No weekly report workbook, progress presentation, quantity, manpower or HSE sheets were uploaded, so the scope-quantities and manpower sections are left out.
- Physical % complete was computed from the P6 update by the method under the S-curve. The tracker's Info sheet and the 3-week look-ahead report cost-based (planned and earned value) progress, which is not used here.
- No earlier week was uploaded for this project, so this-week and gained-this-week values are shown as "—".
- The P6 update has a data date of 26-Oct-2026, but no activity has an actual start or finish after 19-Oct-2026, nor between 06 and 12-Oct-2026. The update may not reflect the last week of work.
- The time-stamped site photos are dated 17-Oct-2026, in the previous week.
- The Info sheet of the procurement tracker (contract dates, value, invoicing, MODON PM) is dated 15-Jun-2026 and has not been updated.

- Several pivot sheets of the procurement tracker (Zone 5 PO, Long Lead %, PV QTY) show #REF! errors. Some delivered quantities exceed the revised BOQ quantity, e.g. GRP pipes 86,378 m against 85,790 m and light-pole concrete bases 1,158 against 1,063.
- The curbstone lines repeat the same quantity (160,860 m) for four types; the total needed should be confirmed.
- Issue ID#04 in the issue log is filed under contract JDH3-02-010 with this project's name. Risk and issue scores do not follow the log's own rule (score = probability × impact); for example risk ID#02 is 4 × 4 but scored 4.
- Milestone float in P6 is measured to project finish only, so late interim milestones still show hundreds of days of float. No consultant is named in the uploaded files.

Compiled 01-Nov-2026 from the files uploaded for week W04 (22-Oct-2026): P6 update 009-wpr78-26-10-2026, procurement tracker 27-Oct-2026, shop drawing and material submittal logs, risk and issue log and site photos.
