


Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
Completion of the Infrastructure development of the 1st phase in the 3rd industrial city in Jeddah		28-Jun-26	26-Sep-26	30-Jun-26 A	15-Dec-26	4,148,786.46	7,327,652.64
JDH3-02-008-Milestones - MI		28-Jun-26	26-Sep-26	25-Oct-26	15-Dec-26	0.00	0.00
JDH3-02-008-Contractual Milestones		28-Jun-26	26-Sep-26	25-Oct-26	15-Dec-26	0.00	0.00
JDH3-02-008RMI102	Complete all Works including Testing & Commissioning, Cleanup, Closeout Documentation and Ready for Initial Hand		26-Sep-26		17-Nov-26	0.00	0.00
JDH3-02-008RMI112	Complete Demobilization		28-Jun-26		25-Oct-26	0.00	0.00
JDH3-02-008RMI22	Complete existing condition survey, submission of Final Reports		28-Jun-26		25-Oct-26	0.00	0.00
JDH3-02-008RMI42	Complete Earthworks		26-Sep-26		28-Oct-26	0.00	0.00
JDH3-02-008RMI52	Complete steel structure Erection for all blocks		28-Jun-26		25-Oct-26	0.00	0.00
JDH3-02-008RMI72	Complete all Civil Works		26-Sep-26		28-Oct-26	0.00	0.00
JDH3-02-008RMI8	Project Finish - MI		26-Sep-26		15-Dec-26	0.00	0.00
JDH3-02-008RMI82	Complete Mechanical Works		26-Sep-26		29-Oct-26	0.00	0.00
JDH3-02-008-Control Milestones		28-Jun-26	26-Sep-26	25-Oct-26	17-Nov-26	0.00	0.00
JDH3-02-008RMI5	Finishing Sewage, Storm and Electrical Networks - MI		26-Sep-26		17-Nov-26	0.00	0.00
JDH3-02-008RMI6	Finishing Water Network (Potable - TSE) - MI		12-Sep-26		26-Oct-26	0.00	0.00
JDH3-02-008RMI7	Finishing Road Kerbing and Pavement - MI		28-Jun-26		25-Oct-26	0.00	0.00
JDH3-02-008-Network Milestones		30-Jul-26	26-Sep-26	25-Oct-26	04-Nov-26	0.00	0.00
JDH3-02-008RELMI19	Finish of ELECTRICAL Network - MI - EL - SL - TC		30-Jul-26		25-Oct-26	0.00	0.00
JDH3-02-008RRDMI25	Finish for Road Works - RD - MI - RD		24-Sep-26		04-Nov-26	0.00	0.00
JDH3-02-008RSSMI11	Finish for Sewage Network - SS - MI - SS		17-Aug-26		25-Oct-26	0.00	0.00
JDH3-02-008RSTMI13	Finish for Storm Network - ST - MI - ST		26-Sep-26		29-Oct-26	0.00	0.00
JDH3-02-008RTSEMI17	Finish for TSE Network - TSE - MI - TSE		09-Sep-26		28-Oct-26	0.00	0.00
JDH3-02-008RWTMI15	Finish for Potable Water Network - WT - MI - WT		12-Sep-26		26-Oct-26	0.00	0.00
JDH3-02-008-Zones Millestones		29-Jul-26	26-Sep-26	25-Oct-26	17-Nov-26	0.00	0.00
JDH3-02-008DRSMI110	Finish of Al-Drees Fuel Station - MI - DRS		29-Jul-26		25-Oct-26	0.00	0.00
JDH3-02-008RMRMI28	Finish for Main Roads - MI - MR		26-Sep-26		29-Oct-26	0.00	0.00
JDH3-02-008RZ01MI30	Finish for Zone 01 - MI - Z01		17-Sep-26		25-Oct-26	0.00	0.00
JDH3-02-008RZ02-1MI34	Finish for Zone 02 - 1 - MI - Z02 - 1		03-Sep-26		02-Nov-26	0.00	0.00
JDH3-02-008RZ02-2MI36	Finish for Zone 02 - 2 - MI - Z02 - 2		03-Sep-26		25-Oct-26	0.00	0.00
JDH3-02-008RZ02MI32	Finish for Zone 02 - MI - Z02		26-Aug-26		31-Oct-26	0.00	0.00
JDH3-02-008RZ03MI38	Finish for Zone 03 - MI - Z03		23-Aug-26		25-Oct-26	0.00	0.00
JDH3-02-008RZ04MI40	Finish for Zone 04 - MI - Z04		23-Aug-26		10-Nov-26	0.00	0.00
JDH3-02-008RZ05MI42	Finish for Zone 05 - MI - Z05		07-Sep-26		11-Nov-26	0.00	0.00
JDH3-02-008RZ06MI44	Finish for Zone 06 - MI - Z06		16-Sep-26		25-Oct-26	0.00	0.00
JDH3-02-008RZ07-1MI48	Finish for Zone 07 - 1 - MI - Z07 - 1		29-Aug-26		25-Oct-26	0.00	0.00
JDH3-02-008RZ07MI46	Finish for Zone 07 - MI - Z07		12-Sep-26		26-Oct-26	0.00	0.00
JDH3-02-008RZ08MI50	Finish for Zone 08 - MI - Z08		21-Sep-26		17-Nov-26	0.00	0.00
JDH3-02-008RZ09MI76	Finish for Zone 09 - MI - Z09		07-Sep-26		26-Oct-26	0.00	0.00
JDH3-02-008RZ10MI96	Finish for Zone 10 - MI - Z10		21-Sep-26		26-Oct-26	0.00	0.00
JDH3-02-008RZ11MI56	Finish for Zone 11 - MI - Z11		21-Sep-26		09-Nov-26	0.00	0.00
JDH3-02-008RZ13MI60	Finish for Zone 13 - MI - Z13		05-Sep-26		25-Oct-26	0.00	0.00
JDH3-02-008-Engineering		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008-Shop Drawings - SD		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008-Shop Drawing Submittals		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008-Shop Drawing Submittals-New Scope		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
Road Works		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008RSD926	Prepare and Submit Drawing for Curbstone Works (New Scope)	28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008-Shop Drawing Approvals		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008-Shop Drawing Approvals-New Scope		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
Road Works		28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008RSD936	Review and Approval Drawing for Curbstone (New Scope)	28-Jun-26	04-Jul-26	26-Oct-26	01-Nov-26	0.00	0.00
JDH3-02-008-Construction		28-Jun-26	26-Sep-26	30-Jun-26 A	17-Nov-26	1,851,185.65	3,781,878.32

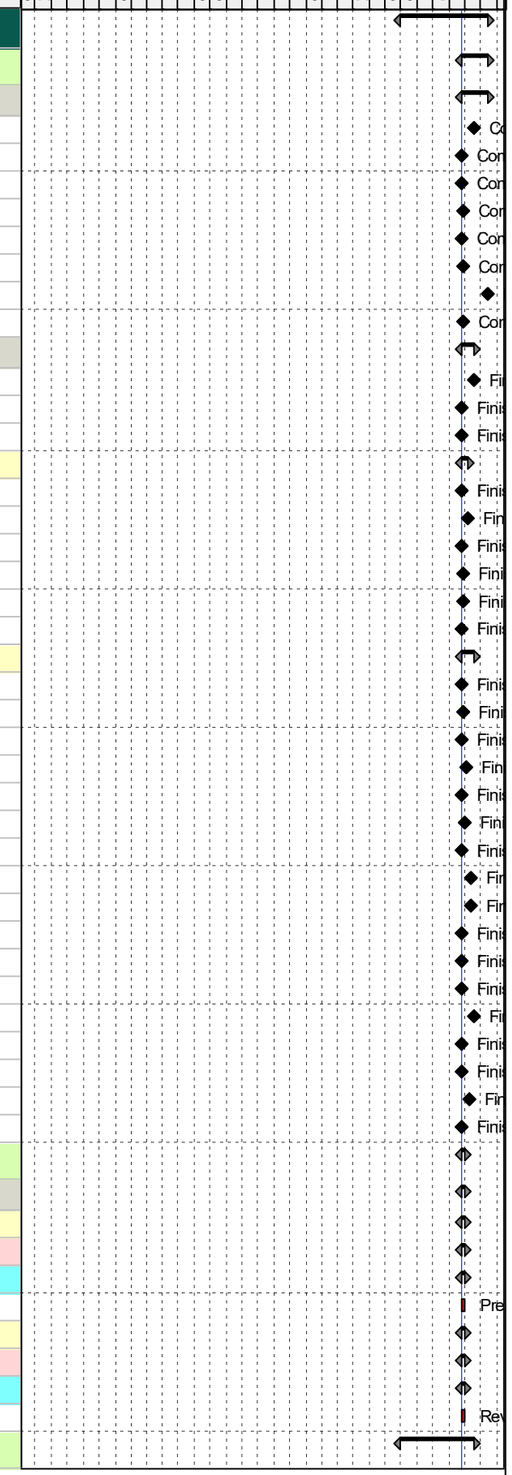


Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
High Mast		29-Jul-26	29-Jul-26	25-Oct-26	25-Oct-26	0.00	0.00
A3390	Finish of Electrical Network HM MI - EL		29-Jul-26		25-Oct-26	0.00	0.00
MR		28-Jun-26	09-Sep-26	30-Jun-26 A	31-Oct-26	559,032.45	859,615.30
A1070	Finish of Sewage network MR MI - SS		07-Sep-26		25-Oct-26	0.00	0.00
A1450	Finish of TSE Network MR MI - TSE		09-Sep-26		28-Oct-26	0.00	0.00
A1590	Finish of PT - WT Network MR MI - WT		26-Aug-26		25-Oct-26	0.00	0.00
L-17		28-Jun-26	28-Jul-26	30-Jun-26 A	31-Oct-26	323,332.64	473,922.63
JDH3-02-008-L-17-Storm Network - ST		28-Jun-26	28-Jul-26	30-Jun-26 A	31-Oct-26	323,332.64	473,922.63
JDH3-02-008-L-17-(ST)-Network		28-Jun-26	28-Jul-26	30-Jun-26 A	31-Oct-26	323,332.64	473,922.63
JDH3-02-008-L-17-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		28-Jun-26	28-Jul-26	30-Jun-26 A	31-Oct-26	323,332.64	473,922.63
JD3RMRL17ST60768-R	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L-17 - ST(R)	28-Jun-26	30-Jun-26	08-Aug-26 A	28-Oct-26	73,039.79	91,299.74
JD3RMRL17ST60769-R	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MI	16-Jul-26	18-Jul-26	08-Aug-26 A	28-Oct-26	18,259.95	22,824.93
JD3RMRL17ST60770-R	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L-17 - ST(R)	19-Jul-26	23-Jul-26	22-Aug-26 A	31-Oct-26	182,468.72	260,669.60
JD3RMRL17ST60771-R	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L-17 - ST(R)	25-Jul-26	26-Jul-26	22-Aug-26 A	31-Oct-26	23,697.24	47,394.47
JD3RMRL17ST60772	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L-17 - ST	27-Jul-26	28-Jul-26	30-Jun-26 A	31-Oct-26	25,866.94	51,733.89
L-51		28-Jun-26	13-Jul-26	30-Jun-26 A	29-Oct-26	137,840.85	211,790.79
JDH3-02-008-L-51-Storm Network - ST		28-Jun-26	13-Jul-26	30-Jun-26 A	29-Oct-26	137,840.85	211,790.79
JDH3-02-008-L-51-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		28-Jun-26	13-Jul-26	30-Jun-26 A	29-Oct-26	137,840.85	211,790.79
JD3RMRL51ST63620-R	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 51 - ST(R)	28-Jun-26	01-Jul-26	30-Jun-26 A	29-Oct-26	33,630.51	40,036.32
JD3RMRL51ST63621-R	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MI	02-Jul-26	06-Jul-26	30-Jun-26 A	29-Oct-26	7,606.90	10,009.08
JD3RMRL51ST63622-R	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 51 - ST(R)	07-Jul-26	08-Jul-26	22-Aug-26 A	29-Oct-26	79,134.13	106,938.01
JD3RMRL51ST63623-R	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 51 - ST(R)	09-Jul-26	11-Jul-26	22-Aug-26 A	29-Oct-26	1,555.46	19,443.27
JD3RMRL51ST63624-R	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 51 - ST(R)	12-Jul-26	13-Jul-26	30-Jun-26 A	29-Oct-26	15,913.85	35,364.10
L-58		04-Aug-26	17-Aug-26	30-Jun-26 A	29-Oct-26	97,858.96	173,901.88
JDH3-02-008-L-58-Storm Network - ST		04-Aug-26	17-Aug-26	30-Jun-26 A	29-Oct-26	97,858.96	173,901.88
JDH3-02-008-L-58-(ST)-NetWork		04-Aug-26	17-Aug-26	30-Jun-26 A	29-Oct-26	97,858.96	173,901.88
JDH3-02-008-L-58-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		04-Aug-26	17-Aug-26	30-Jun-26 A	29-Oct-26	97,858.96	173,901.88
JD3RMRL58ST64333-R	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 58 - ST(R)	04-Aug-26	05-Aug-26	15-Aug-26 A	27-Oct-26	22,566.71	30,495.56
JD3RMRL58ST64334-R	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MI	06-Aug-26	08-Aug-26	30-Jun-26 A	27-Oct-26	6,391.27	8,409.57
JD3RMRL58ST64335-R	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 58 - ST(R)	09-Aug-26	10-Aug-26	19-Jul-26 A	27-Oct-26	65,678.72	92,505.24
JD3RMRL58ST64336-R	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 58 - ST(R)	11-Aug-26	12-Aug-26	25-Jul-26 A	27-Oct-26	1,681.91	16,819.13
JD3RMRL58ST64337-R	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - MR - L - 58 - ST(R)	13-Aug-26	17-Aug-26	22-Aug-26 A	29-Oct-26	1,540.34	25,672.38
Z01		31-Aug-26	17-Sep-26	25-Oct-26	25-Oct-26	0.00	0.00
A1090	Finish of Storm Network Z01 MI - ST		17-Sep-26		25-Oct-26	0.00	0.00
A1230	Finish of TSE Network Z01 MI - TSE		01-Sep-26		25-Oct-26	0.00	0.00
A3450	Finish of PT - WT Network Z01 MI - WT		31-Aug-26		25-Oct-26	0.00	0.00
Z02		29-Jul-26	26-Aug-26	19-Jul-26 A	31-Oct-26	259,534.74	370,763.91
A1250	Finish of TSE Network Z02 MI - TSE		06-Aug-26		25-Oct-26	0.00	0.00
A3660	Finish of Storm Network Z02 MI - ST		26-Aug-26		31-Oct-26	0.00	0.00
RCB-Z02		29-Jul-26	18-Aug-26	19-Jul-26 A	31-Oct-26	259,534.74	370,763.91
JDH3-02-008-RCB-Z02-Storm Network - ST		29-Jul-26	18-Aug-26	19-Jul-26 A	31-Oct-26	259,534.74	370,763.91
JDH3-02-008-RCB-Z02-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		29-Jul-26	18-Aug-26	19-Jul-26 A	31-Oct-26	259,534.74	370,763.91
JD3RZ02RCBST21200-R	Excavation Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z02 - RCB - ST(R)	29-Jul-26	02-Aug-26	03-Aug-26 A	29-Oct-26	48,669.31	69,527.59
JD3RZ02RCBST21201-R	Soil Replacement and Bedding Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z	03-Aug-26	04-Aug-26	19-Jul-26 A	29-Oct-26	12,498.44	17,854.91
JD3RZ02RCBST21202-R	Installing for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z02 - RCB - ST(R)	05-Aug-26	10-Aug-26	03-Aug-26 A	31-Oct-26	141,401.25	202,001.79
JD3RZ02RCBST21203-R	Primary Test for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z02 - RCB - ST(R)	11-Aug-26	13-Aug-26	08-Aug-26 A	31-Oct-26	25,945.43	37,064.90
JD3RZ02RCBST21204	Backfilling Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z02 - RCB - ST	15-Aug-26	18-Aug-26	22-Aug-26 A	31-Oct-26	31,020.31	44,314.73
Z02-1		28-Jun-26	03-Sep-26	25-Oct-26	02-Nov-26	0.00	0.00
A1010	Finish of Sewage network Z02 - 1 MI - SS		17-Aug-26		25-Oct-26	0.00	0.00
A1100	Start of Storm Network Z02 - 1 MI - ST	28-Jun-26		26-Oct-26		0.00	0.00
A1110	Finish of Storm Network Z02 - 1 MI - ST		09-Aug-26		26-Oct-26	0.00	0.00
A1270	Finish of TSE Network Z02 - 1 MI - TSE		03-Sep-26		25-Oct-26	0.00	0.00

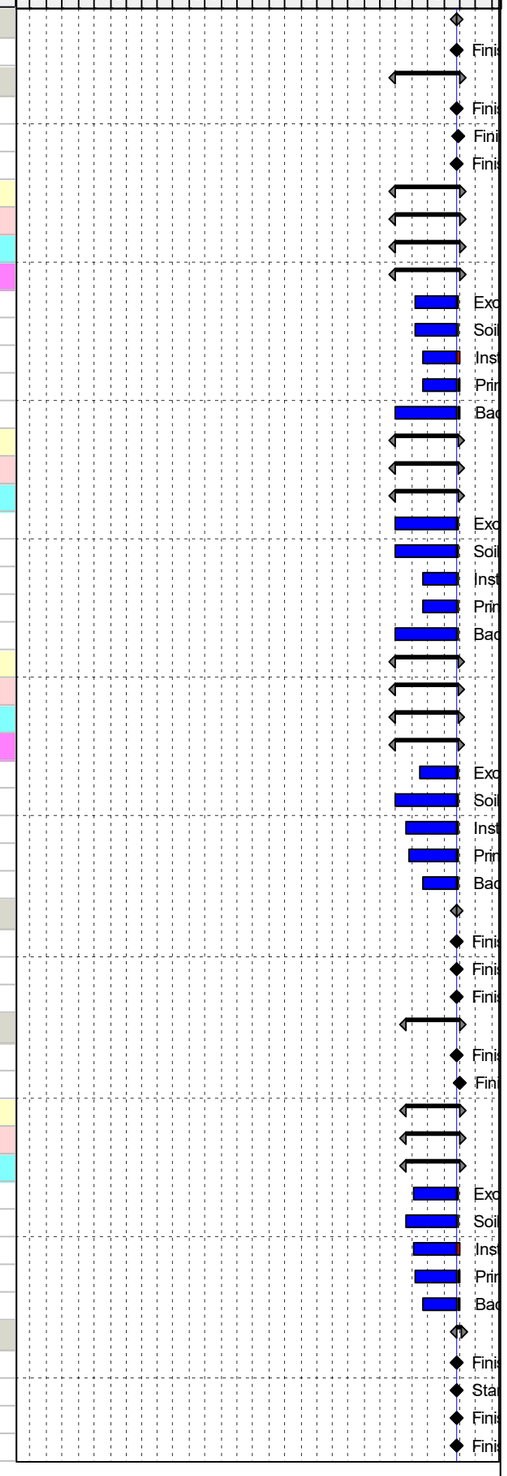


Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
A1470	Finish of PT - WT Network Z02 - 1 MI - WT		19-Aug-26		25-Oct-26	0.00	0.00
A3680	Finish of ELECTRICAL Network Z02 - 1 MI - EL - SL - TC		06-Aug-26		02-Nov-26	0.00	0.00
Z02-2		19-Jul-26	12-Sep-26	25-Oct-26	25-Oct-26	0.00	0.00
A1030	Finish of Sewage network Z02 - 2 MI - SS		19-Jul-26		25-Oct-26	0.00	0.00
A1130	Finish of Storm Network Z02 - 2 MI - ST		30-Jul-26		25-Oct-26	0.00	0.00
A1290	Finish of TSE Network Z02 - 2 MI - TSE		03-Sep-26		25-Oct-26	0.00	0.00
A1490	Finish of PT - WT Network Z02 - 2 MI - WT		12-Sep-26		25-Oct-26	0.00	0.00
Z03		23-Aug-26	23-Aug-26	25-Oct-26	25-Oct-26	0.00	0.00
A1310	Finish of TSE Network Z03 MI - TSE		23-Aug-26		25-Oct-26	0.00	0.00
Z04		14-Jul-26	02-Aug-26	26-Oct-26	10-Nov-26	0.00	208,867.59
A1850	Finish of Storm Network Z04 MI - ST		02-Aug-26		10-Nov-26	0.00	0.00
RCB-Z04		14-Jul-26	02-Aug-26	26-Oct-26	10-Nov-26	0.00	208,867.59
JDH3-02-008-RCB-Z04-Storm Network - ST		14-Jul-26	02-Aug-26		10-Nov-26	0.00	208,867.59
JDH3-02-008-RCB-Z04-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		14-Jul-26	26-Jul-26	26-Oct-26	07-Nov-26	0.00	143,181.84
JD3RZ04RCBST21878	Excavation Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z04 - RCB - ST	14-Jul-26	15-Jul-26	26-Oct-26	27-Oct-26	0.00	28,636.37
JD3RZ04RCBST21879	Soil Replacement and Bedding Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z	16-Jul-26	18-Jul-26	28-Oct-26	29-Oct-26	0.00	7,159.09
JD3RZ04RCBST21880	Installing for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z04 - RCB - ST	19-Jul-26	21-Jul-26	31-Oct-26	02-Nov-26	0.00	78,750.01
JD3RZ04RCBST21881	Primary Test for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z04 - RCB - ST	22-Jul-26	23-Jul-26	03-Nov-26	04-Nov-26	0.00	14,318.18
JD3RZ04RCBST21882	Backfilling Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z04 - RCB - ST	25-Jul-26	26-Jul-26	05-Nov-26	07-Nov-26	0.00	14,318.18
JDH3-02-008-RCB-Z04-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 1.51 to 2.50 m		16-Jul-26	28-Jul-26	28-Oct-26	09-Nov-26	0.00	24,192.15
JD3RZ04RCBST21888	Excavation Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z04 - RCB - ST	16-Jul-26	18-Jul-26	28-Oct-26	29-Oct-26	0.00	4,838.43
JD3RZ04RCBST21889	Soil Replacement and Bedding Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z0	19-Jul-26	20-Jul-26	31-Oct-26	01-Nov-26	0.00	1,209.61
JD3RZ04RCBST21890	Installing for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z04 - RCB - ST	21-Jul-26	22-Jul-26	02-Nov-26	03-Nov-26	0.00	13,305.68
JD3RZ04RCBST21891	Primary Test for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z04 - RCB - ST	23-Jul-26	25-Jul-26	04-Nov-26	05-Nov-26	0.00	2,419.21
JD3RZ04RCBST21892	Backfilling Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z04 - RCB - ST	27-Jul-26	28-Jul-26	08-Nov-26	09-Nov-26	0.00	2,419.21
JDH3-02-008-RCB-Z04-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 0.00 to 1.50 m		19-Jul-26	02-Aug-26	31-Oct-26	10-Nov-26	0.00	41,493.60
JD3RZ02RCBST2000	Excavation Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	19-Jul-26	20-Jul-26	31-Oct-26	01-Nov-26	0.00	8,298.72
JD3RZ02RCBST2001	Soil Replacement and Bedding Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02	21-Jul-26	22-Jul-26	02-Nov-26	03-Nov-26	0.00	2,074.68
JD3RZ02RCBST2002	Installing for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	23-Jul-26	25-Jul-26	04-Nov-26	05-Nov-26	0.00	22,821.48
JD3RZ02RCBST2003	Primary Test for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	26-Jul-26	27-Jul-26	07-Nov-26	08-Nov-26	0.00	4,149.36
JD3RZ02RCBST2004	Backfilling Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	01-Aug-26	02-Aug-26	09-Nov-26	10-Nov-26	0.00	4,149.36
Z05		28-Jun-26	07-Sep-26	06-Jul-26 A	11-Nov-26	442,484.54	1,150,789.27
A1350	Finish of TSE Network Z05 MI - TSE		19-Aug-26		25-Oct-26	0.00	0.00
A1870	Finish Storm Network Z05 MI - ST		07-Sep-26		11-Nov-26	0.00	0.00
RCB-Z05		29-Jul-26	27-Aug-26	06-Jul-26 A	11-Nov-26	442,484.54	906,436.37
JDH3-02-008-RCB-Z05-Storm Network - ST		29-Jul-26	27-Aug-26	06-Jul-26 A	11-Nov-26	442,484.54	906,436.37
JDH3-02-008-RCB-Z05-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		29-Jul-26	27-Aug-26	06-Jul-26 A	01-Nov-26	292,926.46	680,189.23
JD3RZ05RCBST20974-R	Excavation Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z05 - RCB - ST(R)	29-Jul-26	03-Aug-26	06-Jul-26 A	31-Oct-26	89,699.52	137,999.26
JD3RZ05RCBST20975-R	Soil Replacement and Bedding Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z	04-Aug-26	09-Aug-26	06-Jul-26 A	31-Oct-26	13,799.93	34,499.82
JD3RZ05RCBST20976-R	Installing for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z05 - RCB - ST(R)	10-Aug-26	15-Aug-26	04-Oct-26 A	31-Oct-26	148,479.87	371,199.67
JD3RZ05RCBST20977-R	Primary Test for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z05 - RCB - ST(R)	16-Aug-26	20-Aug-26	25-Sep-26 A	31-Oct-26	20,247.25	67,490.85
JD3RZ05RCBST20978	Backfilling Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z05 - RCB - ST	22-Aug-26	27-Aug-26	25-Sep-26 A	01-Nov-26	20,699.89	68,999.63
JDH3-02-008-RCB-Z05-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 1.51 to 2.50 m		04-Aug-26	15-Aug-26	01-Nov-26	11-Nov-26	0.00	12,592.74
JD3RZ05RCBST20984	Excavation Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z05 - RCB - ST	04-Aug-26	05-Aug-26	01-Nov-26	02-Nov-26	0.00	2,518.55
JD3RZ05RCBST20985	Soil Replacement and Bedding Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z0	06-Aug-26	08-Aug-26	03-Nov-26	04-Nov-26	0.00	629.64
JD3RZ05RCBST20986	Installing for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z05 - RCB - ST	09-Aug-26	10-Aug-26	05-Nov-26	07-Nov-26	0.00	6,926.01
JD3RZ05RCBST20987	Primary Test for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z05 - RCB - ST	11-Aug-26	12-Aug-26	08-Nov-26	09-Nov-26	0.00	1,259.27
JD3RZ05RCBST20988	Backfilling Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z05 - RCB - ST	13-Aug-26	15-Aug-26	10-Nov-26	11-Nov-26	0.00	1,259.27
JDH3-02-008-RCB-Z05-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 0.00 to 1.50 m		06-Aug-26	17-Aug-26	31-Aug-26 A	02-Nov-26	149,558.07	213,654.39
JD3RZ02RCBST3000	Excavation Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	06-Aug-26	08-Aug-26	31-Aug-26 A	02-Nov-26	29,911.61	42,730.88
JD3RZ02RCBST3001	Soil Replacement and Bedding Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02	09-Aug-26	10-Aug-26	31-Aug-26 A	02-Nov-26	7,477.90	10,682.72
JD3RZ02RCBST3002	Installing for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	11-Aug-26	12-Aug-26	31-Aug-26 A	02-Nov-26	82,256.94	117,509.92

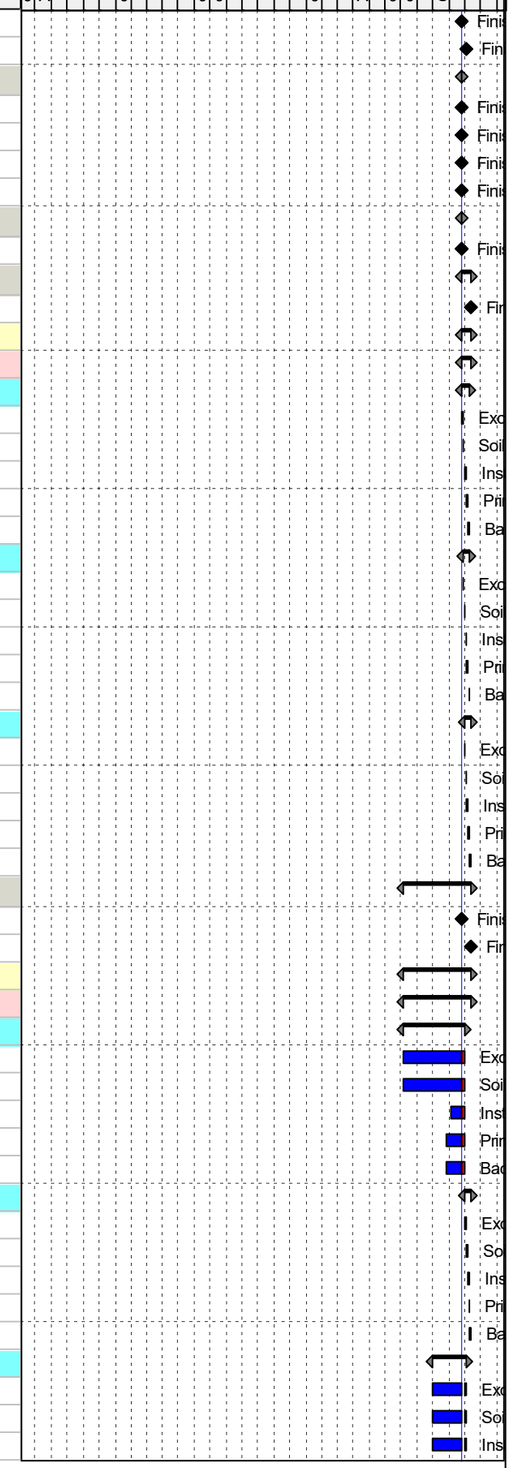


Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
JD3RZ02RCBST3003	Primary Test for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	13-Aug-26	15-Aug-26	12-Oct-26 A	02-Nov-26	14,955.81	21,365.44
JD3RZ02RCBST3004	Backfilling Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	16-Aug-26	17-Aug-26	12-Oct-26 A	02-Nov-26	14,955.81	21,365.44
TSE-Ro		28-Jun-26	07-Jul-26	26-Oct-26	04-Nov-26	0.00	244,352.90
JDH3-02-008-TSE-Ro-Road Works - RD		28-Jun-26	07-Jul-26	26-Oct-26	04-Nov-26	0.00	244,352.90
JDH3-02-008-TSE-Ro-(RD)-Bituminous base course (Grading I - Class A), including Prime Coat (MC1)		28-Jun-26	07-Jul-26	26-Oct-26	04-Nov-26	0.00	244,352.90
JD3RZ05TSERoRD11423-R	Supply and spreading of Prime coat MC1for ROADS - B1.32 11 26.01 - Z05 - TSE-Ro - RD(R)	28-Jun-26	01-Jul-26	26-Oct-26	29-Oct-26	0.00	24,435.29
JD3RZ05TSERoRD11424-R	Supply, lay and compaction Asphaltic base coursefor ROADS - B1.32 11 26.01 - Z05 - TSE-Ro - RD(R)	02-Jul-26	07-Jul-26	31-Oct-26	04-Nov-26	0.00	219,917.61
Z06		06-Aug-26	26-Sep-26	28-Sep-26 A	29-Oct-26	74,126.48	138,372.35
A1150	Finish of Storm Network Z06 MI - ST		16-Sep-26		25-Oct-26	0.00	0.00
A1370	Finish of TSE Network Z06 MI - TSE		07-Sep-26		25-Oct-26	0.00	0.00
A1550	Finish of PT - WT Network Z06 MI - WT		09-Sep-26		25-Oct-26	0.00	0.00
L-56		06-Aug-26	15-Aug-26	28-Sep-26 A	28-Oct-26	61,496.39	87,851.99
JDH3-02-008-L-56-Storm Network - ST		06-Aug-26	15-Aug-26	28-Sep-26 A	28-Oct-26	61,496.39	87,851.99
JDH3-02-008-L-56-(ST)-NetWork		06-Aug-26	15-Aug-26	28-Sep-26 A	28-Oct-26	61,496.39	87,851.99
JDH3-02-008-L-56-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		06-Aug-26	15-Aug-26	28-Sep-26 A	28-Oct-26	61,496.39	87,851.99
JD3RZ06L56ST24408-R	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z06 - L - 56 - ST(R)	06-Aug-26	09-Aug-26	28-Sep-26 A	28-Oct-26	24,267.04	34,667.20
JD3RZ06L56ST24409-R	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z06 - L - 56 - ST(R)	12-Aug-26	15-Aug-26	01-Oct-26 A	28-Oct-26	37,229.35	53,184.79
L-57		17-Sep-26	26-Sep-26	05-Oct-26 A	29-Oct-26	12,630.09	50,520.37
JDH3-02-008-L-57-Storm Network - ST		17-Sep-26	26-Sep-26	05-Oct-26 A	29-Oct-26	12,630.09	50,520.37
JDH3-02-008-L-57-(ST)-NetWork		17-Sep-26	26-Sep-26	05-Oct-26 A	29-Oct-26	12,630.09	50,520.37
JDH3-02-008-L-57-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		17-Sep-26	26-Sep-26	05-Oct-26 A	29-Oct-26	12,630.09	50,520.37
JD3RZ06L57ST25121	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z06 - L - 57 - ST	17-Sep-26	21-Sep-26	05-Oct-26 A	29-Oct-26	6,315.05	25,260.18
JD3RZ06L57ST25122	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z06 - L - 57 - ST	22-Sep-26	26-Sep-26	10-Oct-26 A	29-Oct-26	6,315.05	25,260.18
Z07-1		15-Jul-26	29-Aug-26	25-Oct-26	25-Oct-26	0.00	0.00
A1190	Finish of Storm Network Z07 - 1 MI - ST		15-Jul-26		25-Oct-26	0.00	0.00
A1410	Finish of TSE Network Z07 - 1 MI - TSE		26-Jul-26		25-Oct-26	0.00	0.00
A1510	Finish of PT - WT Network Z07 - 1 MI - WT		29-Aug-26		25-Oct-26	0.00	0.00
Z08		19-Aug-26	21-Sep-26	25-Sep-26 A	17-Nov-26	37,741.93	363,440.65
A1430	Finish of TSE Network Z08 MI - TSE		25-Aug-26		25-Oct-26	0.00	0.00
A3520	Finish of Storm Network Z08 MI - ST		21-Sep-26		17-Nov-26	0.00	0.00
RCB-Z08		19-Aug-26	10-Sep-26	25-Sep-26 A	17-Nov-26	37,741.93	363,440.65
JDH3-02-008-RCB-Z08-Storm Network - ST		19-Aug-26	10-Sep-26	25-Sep-26 A	17-Nov-26	37,741.93	363,440.65
JDH3-02-008-RCB-Z08-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		19-Aug-26	10-Sep-26	26-Oct-26	17-Nov-26	0.00	259,003.80
JD3RZ08RCBST21652	Excavation Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z08 - RCB - ST	19-Aug-26	22-Aug-26	26-Oct-26	28-Oct-26	0.00	51,800.76
JD3RZ08RCBST21653	Soil Replacement and Bedding Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z	23-Aug-26	26-Aug-26	29-Oct-26	02-Nov-26	0.00	12,950.19
JD3RZ08RCBST21654	Installing for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z08 - RCB - ST	27-Aug-26	01-Sep-26	03-Nov-26	08-Nov-26	0.00	142,452.09
JD3RZ08RCBST21655	Primary Test for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z08 - RCB - ST	02-Sep-26	06-Sep-26	09-Nov-26	12-Nov-26	0.00	25,900.38
JD3RZ08RCBST21656	Backfilling Works for UPVC Pipe Line - B6.33 14 11.01 - 300 mm - depth from 0.00 to 1.50 m - Z08 - RCB - ST	07-Sep-26	10-Sep-26	14-Nov-26	17-Nov-26	0.00	25,900.38
JDH3-02-008-RCB-Z08-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 1.51 to 2.50 m		23-Aug-26	02-Sep-26	29-Oct-26	09-Nov-26	0.00	10,082.02
JD3RZ08RCBST21662	Excavation Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z08 - RCB - ST	23-Aug-26	24-Aug-26	29-Oct-26	31-Oct-26	0.00	2,016.40
JD3RZ08RCBST21663	Soil Replacement and Bedding Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z0	25-Aug-26	26-Aug-26	01-Nov-26	02-Nov-26	0.00	504.10
JD3RZ08RCBST21664	Installing for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z08 - RCB - ST	27-Aug-26	29-Aug-26	03-Nov-26	04-Nov-26	0.00	5,545.11
JD3RZ08RCBST21665	Primary Test for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z08 - RCB - ST	30-Aug-26	31-Aug-26	05-Nov-26	07-Nov-26	0.00	1,008.20
JD3RZ08RCBST21666	Backfilling Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z08 - RCB - ST	01-Sep-26	02-Sep-26	08-Nov-26	09-Nov-26	0.00	1,008.20
JDH3-02-008-RCB-Z08-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 0.00 to 1.50 m		25-Aug-26	07-Sep-26	25-Sep-26 A	04-Nov-26	37,741.93	94,354.84
JD3RZ02RCBST60773	Excavation Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	25-Aug-26	26-Aug-26	04-Oct-26 A	31-Oct-26	9,435.48	18,870.97
JD3RZ02RCBST60774	Soil Replacement and Bedding Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02	27-Aug-26	29-Aug-26	25-Sep-26 A	31-Oct-26	2,358.87	4,717.74
JD3RZ02RCBST60775	Installing for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	30-Aug-26	31-Aug-26	25-Sep-26 A	31-Oct-26	25,947.58	51,895.16
JD3RZ02RCBST60776	Primary Test for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	01-Sep-26	02-Sep-26	01-Nov-26	02-Nov-26	0.00	9,435.48
JDH3-02-008-Final Testing and	Backfilling Works for GRP Pipe Line 400 mm - depth from 0.00 to 1.50 m - B6.33 42 11.01 - Z02 - RCB - ST	06-Sep-26	07-Sep-26	03-Nov-26	04-Nov-26	0.00	9,435.48
Z09		28-Jun-26	06-Aug-26	25-Jul-26 A	29-Oct-26	102,108.81	145,869.73
A3830	Finish of Sewage network MR MI - SS		02-Aug-26		25-Oct-26	0.00	0.00

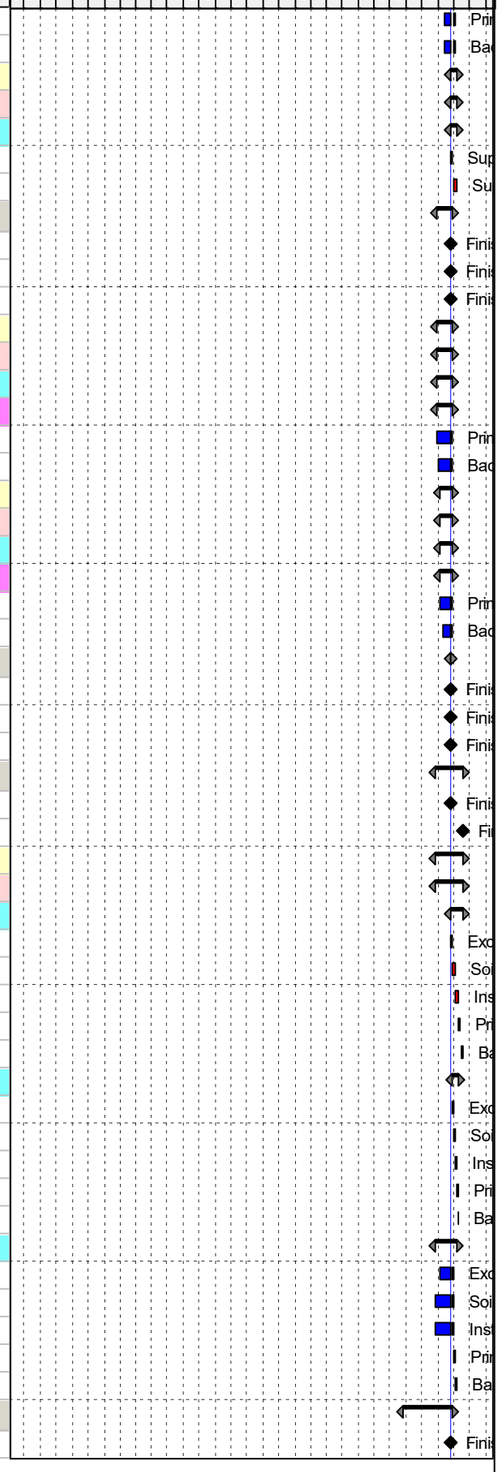


Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
L-19		28-Jun-26	11-Jul-26	07-Sep-26 A	28-Oct-26	69,717.26	99,596.09
JDH3-02-008-L-19-Storm Network - ST		28-Jun-26	11-Jul-26	07-Sep-26 A	28-Oct-26	69,717.26	99,596.09
JDH3-02-008-L-19-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		28-Jun-26	11-Jul-26	07-Sep-26 A	28-Oct-26	69,717.26	99,596.09
JD3RZ09L19ST60768-R	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19 - ST(R)	28-Jun-26	30-Jun-26	07-Sep-26 A	28-Oct-26	13,943.45	19,919.22
JD3RZ09L19ST60769-R	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z0	01-Jul-26	02-Jul-26	07-Sep-26 A	27-Oct-26	3,485.86	4,979.80
JDH3-02-008-Final Testing and	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19 - ST(R)	04-Jul-26	06-Jul-26	07-Sep-26 A	28-Oct-26	38,344.49	54,777.85
JD3RZ09L19ST60771-R	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19 - ST(R)	07-Jul-26	08-Jul-26	15-Oct-26 A	28-Oct-26	6,971.73	9,959.61
JD3RZ09L19ST60772-R	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19 - ST(R)	09-Jul-26	11-Jul-26	18-Oct-26 A	28-Oct-26	6,971.73	9,959.61
L-19-1		20-Jul-26	23-Jul-26	25-Jul-26 A	27-Oct-26	9,420.74	13,458.20
JDH3-02-008-L-19-1-Storm Network - ST		20-Jul-26	23-Jul-26	25-Jul-26 A	27-Oct-26	9,420.74	13,458.20
JDH3-02-008-L-19-1-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		20-Jul-26	23-Jul-26	25-Jul-26 A	27-Oct-26	9,420.74	13,458.20
JD3RZ09L191ST60771-R	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19-1 - ST(R)	20-Jul-26	21-Jul-26	12-Oct-26 A	27-Oct-26	3,261.25	4,658.92
JD3RZ09L191ST60772	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19-1 - ST	22-Jul-26	23-Jul-26	25-Jul-26 A	27-Oct-26	6,159.49	8,799.28
L-19-2		25-Jul-26	06-Aug-26	12-Oct-26 A	29-Oct-26	22,970.81	32,815.44
JDH3-02-008-L-19-2-Storm Network - ST		25-Jul-26	06-Aug-26	12-Oct-26 A	29-Oct-26	22,970.81	32,815.44
JDH3-02-008-L-19-2-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		25-Jul-26	06-Aug-26	12-Oct-26 A	29-Oct-26	22,970.81	32,815.44
JD3RZ09L192ST60768	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19-2 - ST	25-Jul-26	28-Jul-26	14-Oct-26 A	29-Oct-26	4,594.16	6,563.09
JD3RZ09L192ST60769	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z0	29-Jul-26	30-Jul-26	12-Oct-26 A	29-Oct-26	1,148.54	1,640.77
JD3RZ09L192ST60770	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19-2 - ST	01-Aug-26	02-Aug-26	12-Oct-26 A	29-Oct-26	12,633.94	18,048.49
JD3RZ09L192ST60771	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19-2 - ST	03-Aug-26	04-Aug-26	12-Oct-26 A	29-Oct-26	2,297.08	3,281.54
JD3RZ09L192ST60772	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z09 - L-19-2 - ST	05-Aug-26	06-Aug-26	12-Oct-26 A	29-Oct-26	2,297.08	3,281.54
Z10		08-Aug-26	03-Sep-26	22-Aug-26 A	11-Nov-26	243,032.13	361,982.72
A3850	Finish of Sewage network Z10 MI - SS		03-Sep-26		25-Oct-26	0.00	0.00
L-25		17-Aug-26	29-Aug-26	22-Aug-26 A	11-Nov-26	124,081.55	124,081.55
JDH3-02-008-L-25-Storm Network - ST		17-Aug-26	29-Aug-26	22-Aug-26 A	11-Nov-26	124,081.55	124,081.55
JDH3-02-008-L-25-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		17-Aug-26	29-Aug-26	22-Aug-26 A	11-Nov-26	124,081.55	124,081.55
JD3RZ10L25ST60768	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-25 - ST	17-Aug-26	18-Aug-26	22-Aug-26 A	05-Nov-26	24,816.31	24,816.31
JD3RZ10L25ST60769	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z1	19-Aug-26	20-Aug-26	22-Aug-26 A	05-Nov-26	6,204.08	6,204.08
JD3RZ10L25ST60770	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-25 - ST	22-Aug-26	24-Aug-26	31-Aug-26 A	11-Nov-26	68,244.85	68,244.85
JD3RZ10L25ST60771	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-25 - ST	25-Aug-26	26-Aug-26	01-Oct-26 A	11-Nov-26	12,408.15	12,408.15
JD3RZ10L25ST60772	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-25 - ST	27-Aug-26	29-Aug-26	04-Oct-26 A	11-Nov-26	12,408.15	12,408.15
L-26		08-Aug-26	23-Aug-26	31-Aug-26 A	28-Oct-26	118,950.59	237,901.18
JDH3-02-008-L-26-Storm Network - ST		08-Aug-26	23-Aug-26	31-Aug-26 A	28-Oct-26	118,950.59	237,901.18
JDH3-02-008-L-26-(ST)- Supply and install UPVC pipe Diameter 300 mm depth from 0.00 to 1.50 m		08-Aug-26	23-Aug-26	31-Aug-26 A	28-Oct-26	118,950.59	237,901.18
JD3RZ10L26ST60768	Excavation Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-26 - ST	08-Aug-26	09-Aug-26	31-Aug-26 A	27-Oct-26	23,790.12	47,580.24
JD3RZ10L26ST60769	Soil Replacement and Bedding Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z1	10-Aug-26	12-Aug-26	31-Aug-26 A	28-Oct-26	5,947.53	11,895.06
JD3RZ10L26ST60770	Installing for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-26 - ST	13-Aug-26	16-Aug-26	31-Aug-26 A	28-Oct-26	65,422.82	130,845.65
JD3RZ10L26ST60771	Primary Test for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-26 - ST	17-Aug-26	19-Aug-26	01-Oct-26 A	28-Oct-26	11,895.06	23,790.12
JD3RZ10L26ST60772	Backfilling Works for UPVC Pipe Line 300 mm - depth from 0.00 to 1.50 m - B6.33 14 11.01 - Z10 - L-26 - ST	20-Aug-26	23-Aug-26	25-Sep-26 A	28-Oct-26	11,895.06	23,790.12
Z11		30-Aug-26	21-Sep-26	26-Oct-26	09-Nov-26	0.00	9,683.12
A3540	Finish of Storm Network Z11 MI - ST		21-Sep-26		09-Nov-26	0.00	0.00
RCB-Z11		30-Aug-26	13-Sep-26	26-Oct-26	09-Nov-26	0.00	9,683.12
JDH3-02-008-RCB-Z11-Storm Network - ST		30-Aug-26	13-Sep-26	26-Oct-26	09-Nov-26	0.00	9,683.12
JDH3-02-008-RCB-Z11-(ST)- Supply and install GRP pipe Diameter 400 mm depth from 1.51 to 2.50 m		30-Aug-26	13-Sep-26	26-Oct-26	09-Nov-26	0.00	9,683.12
JD3RZ11RCBST22114	Excavation Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z11 - RCB - ST	30-Aug-26	01-Sep-26	26-Oct-26	28-Oct-26	0.00	1,936.62
JD3RZ11RCBST22115	Soil Replacement and Bedding Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z1	02-Sep-26	05-Sep-26	29-Oct-26	01-Nov-26	0.00	484.16
JD3RZ11RCBST22116	Installing for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z11 - RCB - ST	06-Sep-26	08-Sep-26	02-Nov-26	04-Nov-26	0.00	5,325.71
JD3RZ11RCBST22117	Primary Test for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z11 - RCB - ST	09-Sep-26	10-Sep-26	05-Nov-26	07-Nov-26	0.00	968.31
JD3RZ11RCBST22118	Backfilling Works for GRP Pipe Line - B6.33 42 11.02 - 400 mm - depth from 1.51 to 2.50 m - Z11 - RCB - ST	12-Sep-26	13-Sep-26	08-Nov-26	09-Nov-26	0.00	968.31
Z13		06-Jul-26	05-Sep-26	25-Oct-26	25-Oct-26	0.00	0.00
A3610	Finish of Storm Network Z13 MI - ST		06-Jul-26		25-Oct-26	0.00	0.00
A3740	Finish of PT - WT Network Z13 MI - WT		05-Sep-26		25-Oct-26	0.00	0.00

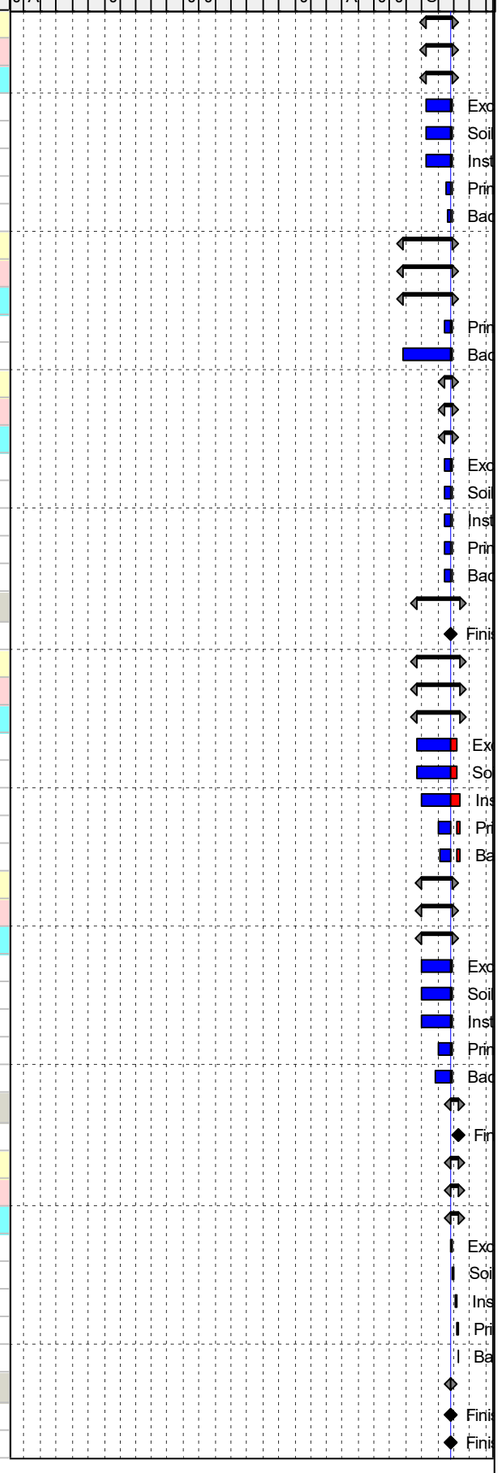

Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
A3750	Finish of TSE Network Z13 MI - TSE		01-Sep-26		25-Oct-26	0.00	0.00
New Scope		06-Aug-26	24-Sep-26	21-Sep-26 A	30-Oct-26	133,124.57	172,493.67
JDH3-02-008-New Scope-Road Works - RD		06-Aug-26	24-Sep-26	21-Sep-26 A	30-Oct-26	133,124.57	172,493.67
JDH3-02-008-New Scope-(RD)-Precast Concrete Curb		06-Aug-26	10-Aug-26	21-Sep-26 A	30-Oct-26	122,486.98	151,218.49
JD3RNSRD22700	Supply and installation Precast Concrete Kerb, Type K1 - D for ROADS - B1.32 14 13.01 - L-58 - RD	06-Aug-26	10-Aug-26	21-Sep-26 A	30-Oct-26	122,486.98	151,218.49
JDH3-02-008-New Scope-(RD)-Pavement Marking		31-Aug-26	24-Sep-26	21-Sep-26 A	30-Oct-26	10,637.59	21,275.18
JD3RNSRD24800	Supply and installation Retroreflective Thermoplastic White Traffic lines for ROADS- B1.32 17 23.01 - R1 -RD	31-Aug-26	04-Sep-26	21-Sep-26 A	30-Oct-26	7,008.31	14,016.61
JD3RNSRD24900	Supply and installation Retroreflective Thermoplastic Yellow Traffic lines for ROADS- B1.32 17 23.02 - R1 -RD	05-Sep-26	09-Sep-26	21-Sep-26 A	30-Oct-26	3,120.89	6,241.77
JD3RNSRD25000	Supply and install Straight Arrow for ROADS - B1.32 17 23.04 - R1 - RD	10-Sep-26	14-Sep-26	21-Sep-26 A	30-Oct-26	254.20	508.40
JD3RNSRD25100	Supply and install (Right/left) Arrowfor ROADS - B1.32 17 23.04 - R1 - RD	15-Sep-26	19-Sep-26	21-Sep-26 A	30-Oct-26	127.10	254.20
JD3RNSRD25200	Supply and install Straight - Right Arrowfor ROADS - B1.32 17 23.06 - R1 - RD	20-Sep-26	24-Sep-26	21-Sep-26 A	30-Oct-26	127.10	254.20
JDH3-02-008-Close Out		30-Jul-26	26-Sep-26	28-Aug-26 A	15-Dec-26	2,297,600.80	3,545,774.32
JDH3-02-008-Final Testing and Commissioning - FT		08-Aug-26	26-Sep-26	28-Aug-26 A	17-Nov-26	919,458.31	1,572,757.65
A3730	Finish All works of Testing And Commissioning - MI		26-Sep-26		17-Nov-26	0.00	0.00
JDH3-02-008-Final Testing and Commissioning - FT-MR		31-Aug-26	12-Sep-26	21-Sep-26 A	28-Oct-26	326,649.67	362,944.08
JDH3-02-008RMRFT1409	Final Testing And Commissioning for TSE (IRRIGATION) Network - FT - MR - TSE	10-Sep-26	12-Sep-26	03-Oct-26 A	28-Oct-26	145,177.63	181,472.04
JDH3-02-008RMRFT1413	Final Testing And Commissioning for Road Network - FT - MR - RD	31-Aug-26	03-Sep-26	21-Sep-26 A	26-Oct-26	181,472.04	181,472.04
JDH3-02-008-Final Testing and Commissioning - FT-Z02-1		08-Aug-26	01-Sep-26	28-Aug-26 A	02-Nov-26	302,453.38	302,453.38
JDH3-02-008RZ02-1FT1344	Final Testing And Commissioning for Street Lighting Network - FT - Z02 - 1 - SL	08-Aug-26	15-Aug-26	28-Aug-26 A	02-Nov-26	151,226.69	151,226.69
JDH3-02-008RZ02-1FT1345	Final Testing And Commissioning for Telecommunications Network - FT - Z02 - 1 - TC	26-Aug-26	01-Sep-26	28-Aug-26 A	01-Nov-26	151,226.69	151,226.69
JDH3-02-008-Final Testing and Commissioning - FT-Z02-2		02-Sep-26	08-Sep-26	28-Aug-26 A	01-Nov-26	181,472.04	181,472.04
JDH3-02-008RZ02-2FT1354	Final Testing And Commissioning for Telecommunications Network - FT - Z02 - 2 - TC	02-Sep-26	08-Sep-26	28-Aug-26 A	01-Nov-26	181,472.04	181,472.04
JDH3-02-008-Final Testing and Commissioning - FT-Z04		17-Sep-26	21-Sep-26	14-Oct-26 A	10-Nov-26	27,220.81	181,472.04
JDH3-02-008RZ04FT1361	Final Testing And Commissioning for Storm Network - FT - Z04 - ST	17-Sep-26	21-Sep-26	14-Oct-26 A	10-Nov-26	27,220.81	181,472.04
JDH3-02-008-Final Testing and Commissioning - FT-Z05		08-Sep-26	12-Sep-26	14-Oct-26 A	11-Nov-26	27,220.81	181,472.04
JDH3-02-008RZ05FT1364	Final Testing And Commissioning for Storm Network - FT - Z05 - ST	08-Sep-26	12-Sep-26	14-Oct-26 A	11-Nov-26	27,220.81	181,472.04
JDH3-02-008-Final Testing and Commissioning - FT-Z08		22-Sep-26	26-Sep-26	14-Oct-26 A	17-Nov-26	27,220.81	181,472.04
JDH3-02-008RZ08FT139	Final Testing And Commissioning for Storm Network - FT - Z08 - ST	22-Sep-26	26-Sep-26	14-Oct-26 A	17-Nov-26	27,220.81	181,472.04
JDH3-02-008-Final Testing and Commissioning - FT-Z11		22-Sep-26	26-Sep-26	14-Oct-26 A	09-Nov-26	27,220.81	181,472.04
JDH3-02-008RZ11FT140	Final Testing And Commissioning for Storm Network - FT - Z11 - ST	22-Sep-26	26-Sep-26	14-Oct-26 A	09-Nov-26	27,220.81	181,472.04
JDH3-02-008-Engineering		30-Jul-26	26-Sep-26	28-Aug-26 A	07-Nov-26	1,378,142.49	1,973,016.66
JDH3-02-008-As Built Drawings		26-Aug-26	26-Sep-26	28-Aug-26 A	01-Nov-26	1,378,142.49	1,973,016.66
A3722	Finish Approval of all asbuilt dwg - MI		26-Sep-26		01-Nov-26	0.00	0.00
JDH3-02-008-As Built Drawing Submittals		26-Aug-26	20-Sep-26	28-Aug-26 A	01-Nov-26	735,072.44	809,431.71
JDH3-02-008-As Built Drawing Submittals-MR		26-Aug-26	01-Sep-26	28-Aug-26 A	01-Nov-26	185,898.18	185,898.18
JDH3-02-008RMRAS430	Prepare and Submit Drawing for Telecommunications Network for - MR - AS	26-Aug-26	01-Sep-26	28-Aug-26 A	01-Nov-26	185,898.18	185,898.18
JDH3-02-008-As Built Drawing Submittals-Z02-1		02-Sep-26	08-Sep-26	28-Aug-26 A	01-Nov-26	185,898.18	185,898.18
JDH3-02-008RZ02-1AS345	Prepare and Submit Drawing for Telecommunications Network for - Z02 - 1 - AS	02-Sep-26	08-Sep-26	28-Aug-26 A	01-Nov-26	185,898.18	185,898.18
JDH3-02-008-As Built Drawing Submittals-Z04		12-Sep-26	17-Sep-26	21-Sep-26 A	01-Nov-26	148,718.54	185,898.18
JDH3-02-008-Final Testing and	Prepare and Submit Drawing for TSE (IRRIGATION) Network for - Z04 - AS - TSE	12-Sep-26	17-Sep-26	21-Sep-26 A	01-Nov-26	148,718.54	185,898.18
JDH3-02-008-As Built Drawing Submittals-Z05		05-Sep-26	10-Sep-26	21-Sep-26 A	01-Nov-26	148,718.54	185,898.18
JDH3-02-008RZ05AS367	Prepare and Submit Drawing for TSE (IRRIGATION) Network for - Z05 - AS - TSE	05-Sep-26	10-Sep-26	21-Sep-26 A	01-Nov-26	148,718.54	185,898.18
JDH3-02-008-As Built Drawing Submittals-Z09		13-Sep-26	14-Sep-26	28-Aug-26 A	27-Oct-26	11,618.65	11,618.65
JDH3-02-008RZ09AS11-R	Prepare and Submit Drawing for Sewage Network for - Z09 - AS - SS(R)	13-Sep-26	14-Sep-26	28-Aug-26 A	27-Oct-26	11,618.65	11,618.65
JDH3-02-008-As Built Drawing Submittals-Z10		15-Sep-26	20-Sep-26	28-Aug-26 A	31-Oct-26	54,220.35	54,220.35
JDH3-02-008RZ10AS11-R	Prepare and Submit Drawing for Sewage Network for - Z10 - AS - SS(R)	15-Sep-26	20-Sep-26	28-Aug-26 A	31-Oct-26	54,220.35	54,220.35
JDH3-02-008-As Built Drawing Approvals		02-Sep-26	26-Sep-26	28-Aug-26 A	01-Nov-26	643,070.05	1,163,584.95
JDH3-02-008RAS446	Review and Approval Drawing for Genral layout - AS	19-Sep-26	24-Sep-26	26-Oct-26	01-Nov-26	0.00	185,898.18
JDH3-02-008-As Built Drawing Approvals-MR		02-Sep-26	08-Sep-26	28-Aug-26 A	01-Nov-26	185,898.18	185,898.18
JDH3-02-008RMRAS627	Review and Approval Drawing for Telecommunications Network for - MR - AS	02-Sep-26	08-Sep-26	28-Aug-26 A	01-Nov-26	185,898.18	185,898.18
JDH3-02-008-As Built Drawing Approvals-Z02		20-Sep-26	26-Sep-26	12-Oct-26 A	01-Nov-26	74,359.27	185,898.18
JDH3-02-008RZ02AS470	Review and Approval Drawing for Storm Water Network for - Z02 - AS - ST	20-Sep-26	26-Sep-26	12-Oct-26 A	01-Nov-26	74,359.27	185,898.18

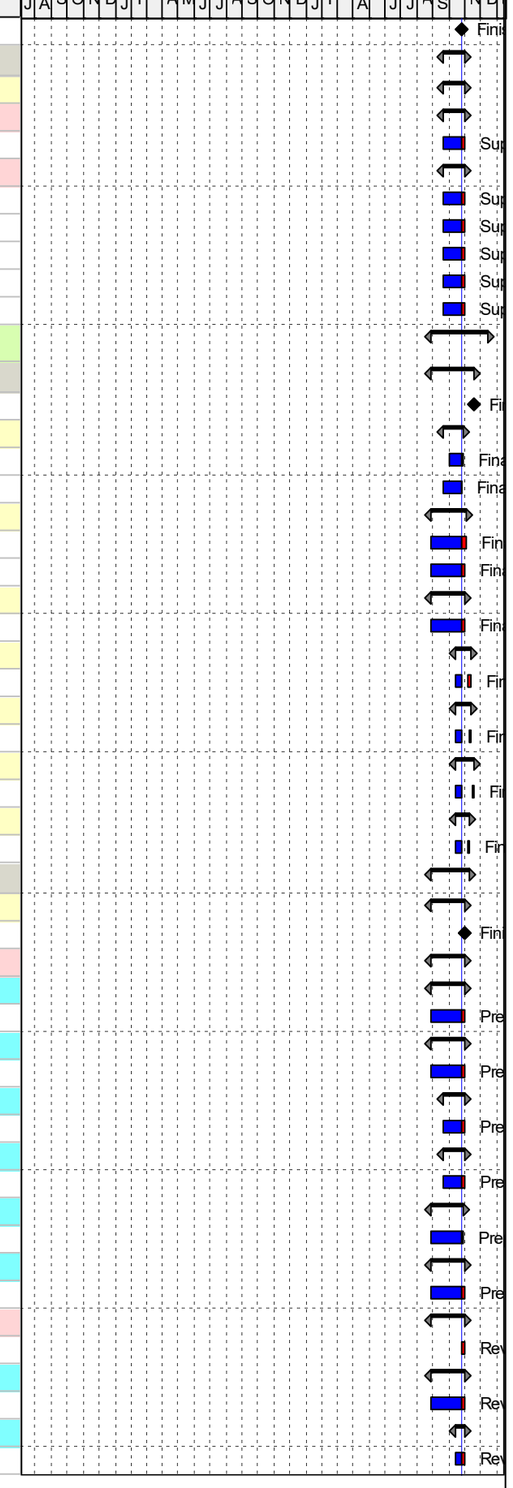

Activity ID	Activity Name	BL Project Start	BL Project Finish	Start	Finish	Earned Value Cost	Budgeted Total Cost
JDH3-02-008-As Built Drawing Approvals-Z05		20-Sep-26	26-Sep-26	26-Oct-26	01-Nov-26	0.00	185,898.18
JDH3-02-008RZ05AS502	Review and Approval Drawing for Storm Water Network for - Z05 - AS - ST	20-Sep-26	26-Sep-26	26-Oct-26	01-Nov-26	0.00	185,898.18
JDH3-02-008-As Built Drawing Approvals-Z08		17-Sep-26	23-Sep-26	21-Sep-26 A	01-Nov-26	148,718.54	185,898.18
JDH3-02-008RZ08AS528	Review and Approval Drawing for TSE (IRRIGATION) Network for - Z08 - AS - TSE	17-Sep-26	23-Sep-26	21-Sep-26 A	01-Nov-26	148,718.54	185,898.18
JDH3-02-008-As Built Drawing Approvals-Z09		15-Sep-26	19-Sep-26	28-Aug-26 A	29-Oct-26	117,047.03	117,047.03
JDH3-02-008RZ09AS1-R	Review and Approval Drawing for Sewage Network for - Z09 - AS - SS(R)	15-Sep-26	19-Sep-26	28-Aug-26 A	29-Oct-26	117,047.03	117,047.03
JDH3-02-008-As Built Drawing Approvals-Z10		21-Sep-26	26-Sep-26	28-Aug-26 A	31-Oct-26	117,047.03	117,047.03
JDH3-02-008RZ10AS1-R	Review and Approval Drawing for Sewage Network for - Z10 - AS - SS(R)	21-Sep-26	26-Sep-26	28-Aug-26 A	31-Oct-26	117,047.03	117,047.03
JDH3-02-008-Operational Spares		30-Jul-26	04-Aug-26	26-Oct-26	31-Oct-26	0.00	0.00
A3310	Supply Operational Spares	30-Jul-26	04-Aug-26	26-Oct-26	31-Oct-26	0.00	0.00
JDH3-02-008-Warranties and Guarantees		05-Aug-26	11-Aug-26	01-Nov-26	07-Nov-26	0.00	0.00
A3300	Warranties and Guarantess	05-Aug-26	11-Aug-26	01-Nov-26	07-Nov-26	0.00	0.00
JDH3-02-008-Training and Manuals		12-Aug-26	25-Aug-26	08-Nov-26	21-Nov-26	0.00	0.00
JDH3-02-008-Training		12-Aug-26	18-Aug-26	08-Nov-26	14-Nov-26	0.00	0.00
A3320	Training	12-Aug-26	18-Aug-26	08-Nov-26	14-Nov-26	0.00	0.00
JDH3-02-008-Manuals		19-Aug-26	25-Aug-26	15-Nov-26	21-Nov-26	0.00	0.00
A3330	Manual	19-Aug-26	25-Aug-26	15-Nov-26	21-Nov-26	0.00	0.00
JDH3-02-008-Demobilization		26-Aug-26	19-Sep-26	22-Nov-26	15-Dec-26	0.00	0.00
JDH3-02-008-Demobilization of Manpoer		26-Aug-26	29-Aug-26	22-Nov-26	24-Nov-26	0.00	0.00
A2100	Demobilize Manpower	26-Aug-26	29-Aug-26	22-Nov-26	24-Nov-26	0.00	0.00
JDH3-02-008-Removal of Euipment from the Site		30-Aug-26	02-Sep-26	25-Nov-26	29-Nov-26	0.00	0.00
A2110	Removal Equipments from The site	30-Aug-26	02-Sep-26	25-Nov-26	29-Nov-26	0.00	0.00
JDH3-02-008-Site Clean - up		03-Sep-26	07-Sep-26	30-Nov-26	03-Dec-26	0.00	0.00
A2120	Site Clean Up	03-Sep-26	07-Sep-26	30-Nov-26	03-Dec-26	0.00	0.00
JDH3-02-008-Removal of Site Offices and Structure		08-Sep-26	13-Sep-26	05-Dec-26	09-Dec-26	0.00	0.00
A2130	Removal of Site Offices and Structures	08-Sep-26	13-Sep-26	05-Dec-26	09-Dec-26	0.00	0.00
JDH3-02-008-Restoration of Ground Surfaces		14-Sep-26	19-Sep-26	10-Dec-26	15-Dec-26	0.00	0.00
A3290	Restoration of Ground Surface	14-Sep-26	19-Sep-26	10-Dec-26	15-Dec-26	0.00	0.00

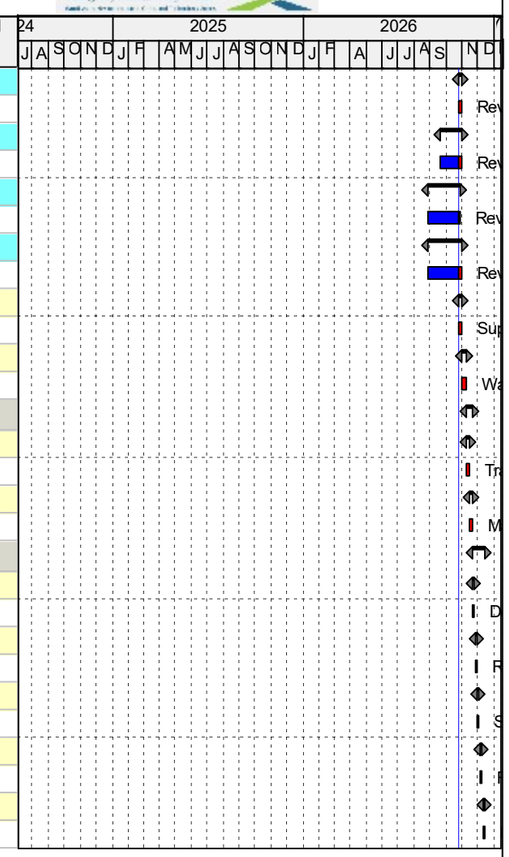

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Weekly Report

Date	Revision	Checked	Approved
25-Oct-26	Weekly Report		
