

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - F		606	01-Jun-25 A	08-Nov-27	19-Mar-25	11-Jan-27	32.47%	45,461,860.39	44,730,388.58
Key Milestones		332	06-Oct-26	08-Nov-27	14-Feb-26	11-Jan-27	0%	0.00	0.00
Contractual Milestones		160	28-Apr-27	08-Nov-27	01-Sep-26	11-Jan-27	0%	0.00	0.00
MS-CF-TE	Completion of Construction Works for Telecom Network	0		28-Apr-27*		01-Sep-26	0%	0.00	0.00
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		13-Jul-27*		28-Oct-26	0%	0.00	0.00
MS-CF-SW	Completion of Construction Works for Sewage Network	0		03-Aug-27*		08-Nov-26	0%	0.00	0.00
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		21-Aug-27*		28-Oct-26	0%	0.00	0.00
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		23-Aug-27*		12-Dec-26	0%	0.00	0.00
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		30-Aug-27*		18-Nov-26	0%	0.00	0.00
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		11-Sep-27*		15-Oct-26	0%	0.00	0.00
MS-CF-RD	Completion of Construction Works for Road Works	0		25-Oct-27		28-Dec-26	0%	0.00	0.00
MS-CF-PF	Project Completion Date	0		08-Nov-27		11-Jan-27	0%	0.00	0.00
Control Milestones		0	06-Oct-26	06-Oct-26	14-Feb-26	14-Feb-26	0%	0.00	0.00
MS-CS-MV	The Employer Approval NOC for Medium Voltage Network	0	06-Oct-26		14-Feb-26		0%	0.00	0.00
Intermediate Milestones		78	25-Jul-27	25-Oct-27	24-Aug-26	28-Dec-26	0%	0.00	0.00
MS-MO-10	Completion of Sewage Pump Stations	0		25-Jul-27		01-Dec-26	0%	0.00	0.00
MS-MO-20	Completion of Storm Drainage Ponds	0		04-Aug-27		24-Aug-26	0%	0.00	0.00
MS-MO-30	Completion of Tie In To Existing Networks	0		25-Oct-27		28-Dec-26	0%	0.00	0.00
Procurement Cycle		494	01-Jun-25 A	22-Jul-27	03-May-25	05-Oct-26	36.14%	4,081,387.49	4,081,387.49
Short Lead Time Items		494	29-Oct-25 A	22-Jul-27	03-May-25	05-Oct-26	38.23%	3,045,483.49	3,045,483.49
Infrastructure Networks		484	13-Dec-25 A	22-Jul-27	03-May-25	05-Oct-26	24.42%	2,451,809.89	2,451,809.89
Road Works		240	06-Oct-26	22-Jul-27	20-Jul-25	05-Oct-26	0%	1,332,031.52	1,332,031.52
1st Material Delivery & Site Inspection		6	06-Oct-26	12-Oct-26	20-Jul-25	18-Aug-25	0%	0.00	0.00
Pavement Works		6	06-Oct-26	12-Oct-26	20-Jul-25	26-Jul-25	0%	0.00	0.00
PRO-RD-1DL-140	1ST Material Delivery for Interlock Tiles of Landscaping	6	06-Oct-26	12-Oct-26	20-Jul-25	26-Jul-25	0%	0.00	0.00
PRO-RD-1DL-150	1ST Material Delivery for Curbstones of Landscaping	6	06-Oct-26	12-Oct-26	20-Jul-25	26-Jul-25	0%	0.00	0.00
Traffic Signs Boards and Roads Marking		6	06-Oct-26	12-Oct-26	12-Aug-25	18-Aug-25	0%	0.00	0.00
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	6	06-Oct-26	12-Oct-26	12-Aug-25	18-Aug-25	0%	0.00	0.00
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	6	06-Oct-26	12-Oct-26	12-Aug-25	18-Aug-25	0%	0.00	0.00
Material Delivery & Site Inspection		234	13-Oct-26	22-Jul-27	28-Dec-25	05-Oct-26	0%	1,332,031.52	1,332,031.52
Road 18 Local 1 (479 LM)		52	13-Oct-26	12-Dec-26	28-Dec-25	25-Feb-26	0%	6,299.98	6,299.98
Traffic Signs Boards and Roads Marking		52	13-Oct-26	12-Dec-26	28-Dec-25	25-Feb-26	0%	6,299.98	6,299.98
PRO-R18-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	13-Oct-26	11-Nov-26	28-Dec-25	26-Jan-26	0%	1,971.20	1,971.20
PRO-R18-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	12-Nov-26	12-Dec-26	27-Jan-26	25-Feb-26	0%	4,328.78	4,328.78
Road 17 Local 1 (500 LM)		52	12-Nov-26	11-Jan-27	27-Jan-26	31-Mar-26	0%	5,981.11	5,981.11
Traffic Signs Boards and Roads Marking		52	12-Nov-26	11-Jan-27	27-Jan-26	31-Mar-26	0%	5,981.11	5,981.11
PRO-R17-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	12-Nov-26	12-Dec-26	27-Jan-26	25-Feb-26	0%	1,504.80	1,504.80
PRO-R17-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	13-Dec-26	11-Jan-27	26-Feb-26	31-Mar-26	0%	4,476.31	4,476.31
Road 16 Local 1 (527 LM)		52	13-Dec-26	10-Feb-27	26-Feb-26	30-Apr-26	0%	6,736.31	6,736.31
Traffic Signs Boards and Roads Marking		52	13-Dec-26	10-Feb-27	26-Feb-26	30-Apr-26	0%	6,736.31	6,736.31
PRO-R16-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	13-Dec-26	11-Jan-27	26-Feb-26	31-Mar-26	0%	2,028.40	2,028.40
PRO-R16-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	12-Jan-27	10-Feb-27	01-Apr-26	30-Apr-26	0%	4,707.91	4,707.91
Road 15 Local 1 (556 LM)		52	12-Jan-27	17-Mar-27	01-Apr-26	04-Jun-26	0%	7,172.73	7,172.73
Traffic Signs Boards and Roads Marking		52	12-Jan-27	17-Mar-27	01-Apr-26	04-Jun-26	0%	7,172.73	7,172.73
PRO-R15-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	12-Jan-27	10-Feb-27	01-Apr-26	30-Apr-26	0%	2,233.00	2,233.00
PRO-R15-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	11-Feb-27	17-Mar-27	02-May-26	04-Jun-26	0%	4,939.73	4,939.73
Road 10 Local 2 (2352 LM)		156	13-Oct-26	17-Apr-27	26-Feb-26	05-Jul-26	0%	643,853.45	643,853.45
Bituminous Construction		26	13-Oct-26	11-Nov-26	26-Feb-26	30-Apr-26	0%	616,208.82	616,208.82
PRO-R10-RD-DL-	Material Delivery & Site Inspection for Prime Coat of Road Works	26	13-Oct-26	11-Nov-26	26-Feb-26	31-Mar-26	0%	123,242.68	123,242.68
PRO-R10-RD-DL-1	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	26	13-Oct-26	11-Nov-26	01-Apr-26	30-Apr-26	0%	492,966.14	492,966.14

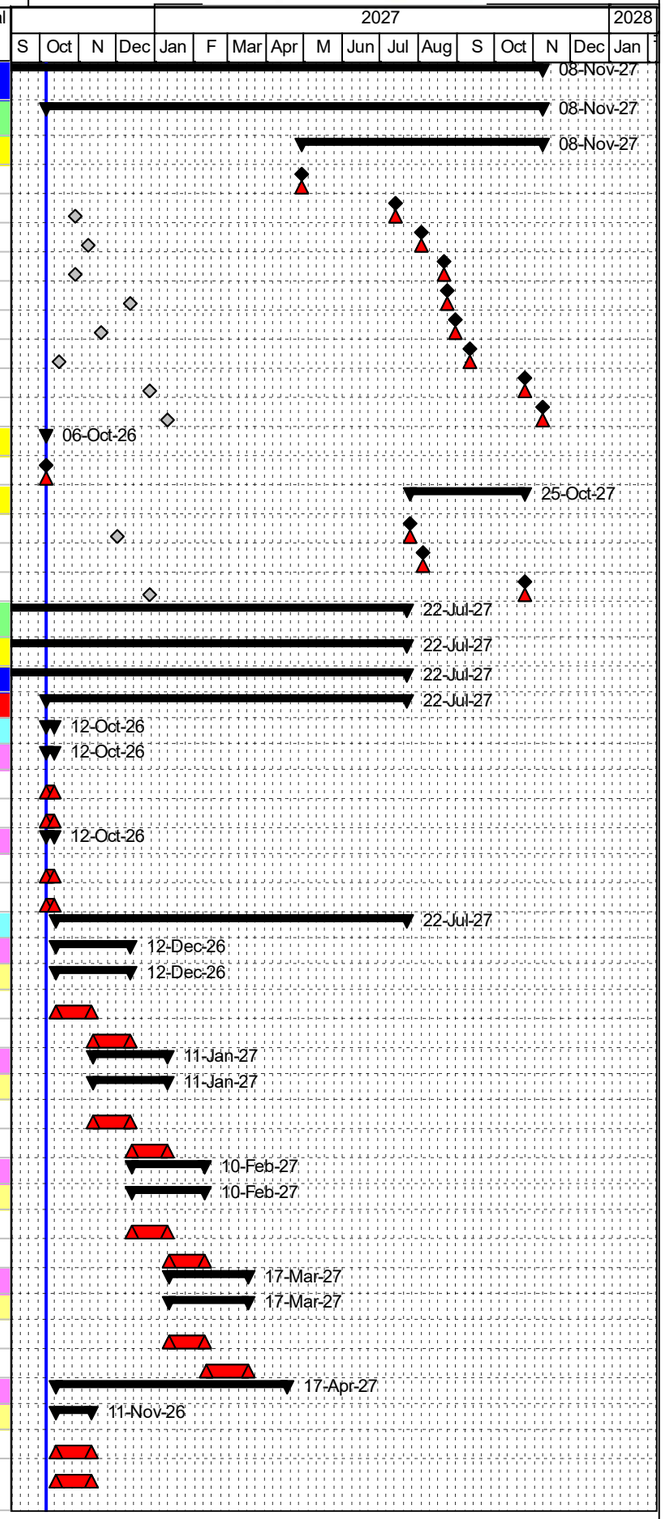

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Traffic Signs Boards and Roads Marking		52	11-Feb-27	17-Apr-27	02-May-26	05-Jul-26	0%	27,644.63	27,644.63
PRO-R10-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	11-Feb-27	17-Mar-27	02-May-26	04-Jun-26	0%	7,532.80	7,532.80
PRO-R10-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	18-Mar-27	17-Apr-27	06-Jun-26	05-Jul-26	0%	20,111.83	20,111.83
Road 14 Local 1 (584 LM)		52	18-Mar-27	23-May-27	06-Jun-26	04-Aug-26	0%	12,022.34	12,022.34
Traffic Signs Boards and Roads Marking		52	18-Mar-27	23-May-27	06-Jun-26	04-Aug-26	0%	12,022.34	12,022.34
PRO-R14-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	18-Mar-27	17-Apr-27	06-Jun-26	05-Jul-26	0%	3,361.60	3,361.60
PRO-R14-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	18-Apr-27	23-May-27	06-Jul-26	04-Aug-26	0%	8,660.74	8,660.74
Road 09 Local 2 (2278 LM)		182	12-Nov-26	22-Jun-27	02-May-26	03-Sep-26	0%	642,011.23	642,011.23
Bituminous Construction		26	12-Nov-26	12-Dec-26	02-May-26	05-Jul-26	0%	614,480.10	614,480.10
PRO-R09-RD-DL-	Material Delivery & Site Inspection for Prime Coat of Road Works	26	12-Nov-26	12-Dec-26	02-May-26	04-Jun-26	0%	122,896.26	122,896.26
PRO-R09-RD-DL-1	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	26	12-Nov-26	12-Dec-26	06-Jun-26	05-Jul-26	0%	491,583.84	491,583.84
Traffic Signs Boards and Roads Marking		52	18-Apr-27	22-Jun-27	06-Jul-26	03-Sep-26	0%	27,531.13	27,531.13
PRO-R09-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	18-Apr-27	23-May-27	06-Jul-26	04-Aug-26	0%	7,475.60	7,475.60
PRO-R09-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	24-May-27	22-Jun-27	05-Aug-26	03-Sep-26	0%	20,055.53	20,055.53
Road 11 Local 1 (670 LM)		52	24-May-27	22-Jul-27	05-Aug-26	05-Oct-26	0%	7,954.37	7,954.37
Traffic Signs Boards and Roads Marking		52	24-May-27	22-Jul-27	05-Aug-26	05-Oct-26	0%	7,954.37	7,954.37
PRO-R11-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	24-May-27	22-Jun-27	05-Aug-26	03-Sep-26	0%	2,085.60	2,085.60
PRO-R11-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	23-Jun-27	22-Jul-27	05-Sep-26	05-Oct-26	0%	5,868.77	5,868.77
Sewage Network		156	06-Oct-26	10-Apr-27	26-Jul-25	29-Mar-26	0%	0.00	0.00
Material Delivery & Site Inspection		156	06-Oct-26	10-Apr-27	26-Jul-25	29-Mar-26	0%	0.00	0.00
Road 17 Local 1 (500 LM)		26	06-Oct-26	04-Nov-26	25-Aug-25	25-Oct-25	0%	0.00	0.00
Testing and Finishes		26	06-Oct-26	04-Nov-26	25-Aug-25	25-Oct-25	0%	0.00	0.00
PRO-R17-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	06-Oct-26	04-Nov-26	25-Aug-25	24-Sep-25	0%	0.00	0.00
PRO-R17-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	06-Oct-26	04-Nov-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
Road 16 Local 1 (527 LM)		26	05-Nov-26	05-Dec-26	25-Sep-25	24-Nov-25	0%	0.00	0.00
Testing and Finishes		26	05-Nov-26	05-Dec-26	25-Sep-25	24-Nov-25	0%	0.00	0.00
PRO-R16-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	05-Nov-26	05-Dec-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
PRO-R16-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	05-Nov-26	05-Dec-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
Road 15 Local 1 (556 LM)		26	06-Dec-26	04-Jan-27	26-Oct-25	24-Dec-25	0%	0.00	0.00
Testing and Finishes		26	06-Dec-26	04-Jan-27	26-Oct-25	24-Dec-25	0%	0.00	0.00
PRO-R15-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	06-Dec-26	04-Jan-27	26-Oct-25	24-Nov-25	0%	0.00	0.00
PRO-R15-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	06-Dec-26	04-Jan-27	25-Nov-25	24-Dec-25	0%	0.00	0.00
Road 10 Local 2 (2352 LM)		26	05-Jan-27	03-Feb-27	25-Nov-25	24-Jan-26	0%	0.00	0.00
Testing and Finishes		26	05-Jan-27	03-Feb-27	25-Nov-25	24-Jan-26	0%	0.00	0.00
PRO-R10-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	05-Jan-27	03-Feb-27	25-Nov-25	24-Dec-25	0%	0.00	0.00
PRO-R10-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	05-Jan-27	03-Feb-27	25-Dec-25	24-Jan-26	0%	0.00	0.00
Road 14 Local 1 (584 LM)		26	04-Feb-27	07-Mar-27	25-Dec-25	23-Feb-26	0%	0.00	0.00
Testing and Finishes		26	04-Feb-27	07-Mar-27	25-Dec-25	23-Feb-26	0%	0.00	0.00
PRO-R14-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	04-Feb-27	07-Mar-27	25-Dec-25	24-Jan-26	0%	0.00	0.00
PRO-R14-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	04-Feb-27	07-Mar-27	25-Jan-26	23-Feb-26	0%	0.00	0.00
Road 09 Local 2 (2278 LM)		38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0%	0.00	0.00
Testing and Finishes		38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0%	0.00	0.00
PRO-R09-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Rising Main Networl	38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0%	0.00	0.00
PRO-R09-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Rising Main Network	38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0%	0.00	0.00
Road 11 Local 1 (670 LM)		26	08-Mar-27	10-Apr-27	25-Jan-26	29-Mar-26	0%	0.00	0.00
Testing and Finishes		26	08-Mar-27	10-Apr-27	25-Jan-26	29-Mar-26	0%	0.00	0.00
PRO-R11-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	08-Mar-27	10-Apr-27	24-Feb-26	29-Mar-26	0%	0.00	0.00
PRO-R11-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	08-Mar-27	10-Apr-27	25-Jan-26	23-Feb-26	0%	0.00	0.00
Storm Drainage Network		165	20-Jun-26 A	16-Jan-27	26-Jul-25	29-Mar-26	0%	0.00	0.00
Material Delivery & Site Inspection		165	20-Jun-26 A	16-Jan-27	26-Jul-25	29-Mar-26	0%	0.00	0.00
Road 18 Local 1 (479 LM)		26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0%	0.00	0.00
Testing and Finishes		26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0%	0.00	0.00

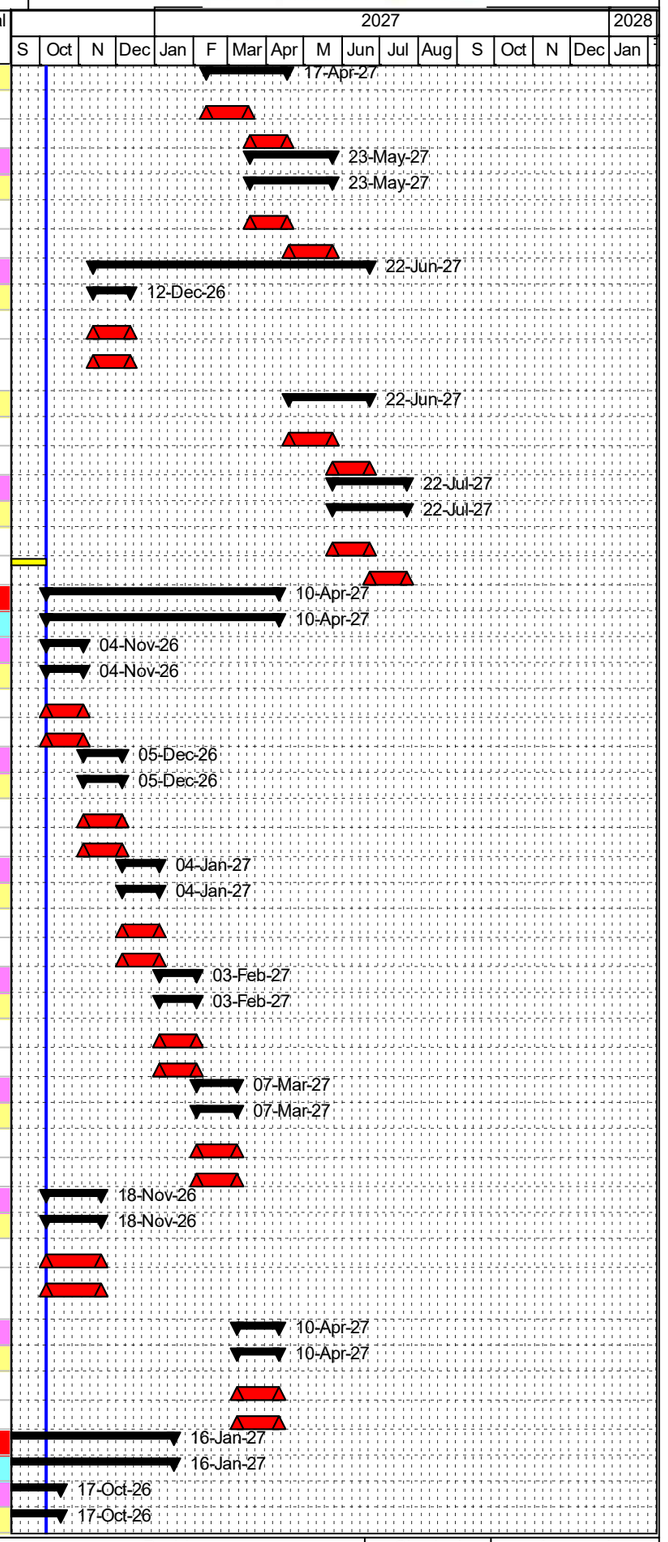

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R18-SD-DL-19	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0%	0.00	0.00
PRO-R18-SD-DL-21	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0%	0.00	0.00
PRO-R18-SD-DL-23	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0%	0.00	0.00
Road 17 Local 1 (500 LM)		26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0%	0.00	0.00
Testing and Finishes		26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0%	0.00	0.00
PRO-R17-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0%	0.00	0.00
PRO-R17-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0%	0.00	0.00
PRO-R17-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0%	0.00	0.00
Road 16 Local 1 (527 LM)		26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
PRO-R16-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
PRO-R16-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
PRO-R16-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0%	0.00	0.00
Road 15 Local 1 (556 LM)		26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
PRO-R15-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
PRO-R15-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
PRO-R15-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
Road 10 Local 2 (2352 LM)		26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0%	0.00	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0%	0.00	0.00
PRO-R10-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0%	0.00	0.00
PRO-R10-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0%	0.00	0.00
PRO-R10-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0%	0.00	0.00
Road 14 Local 1 (584 LM)		26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0%	0.00	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0%	0.00	0.00
PRO-R14-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0%	0.00	0.00
PRO-R14-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0%	0.00	0.00
PRO-R14-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0%	0.00	0.00
Road 09 Local 2 (2278 LM)		26	17-Nov-26	16-Dec-26	25-Jan-26	23-Feb-26	0%	0.00	0.00
Testing and Finishes		26	17-Nov-26	16-Dec-26	25-Jan-26	23-Feb-26	0%	0.00	0.00
PRO-R09-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	17-Nov-26	16-Dec-26	25-Jan-26	23-Feb-26	0%	0.00	0.00
PRO-R09-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	17-Nov-26	16-Dec-26	25-Jan-26	23-Feb-26	0%	0.00	0.00
PRO-R09-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	17-Nov-26	16-Dec-26	25-Jan-26	23-Feb-26	0%	0.00	0.00
Road 11 Local 1 (670 LM)		26	17-Dec-26	16-Jan-27	24-Feb-26	29-Mar-26	0%	0.00	0.00
Testing and Finishes		26	17-Dec-26	16-Jan-27	24-Feb-26	29-Mar-26	0%	0.00	0.00

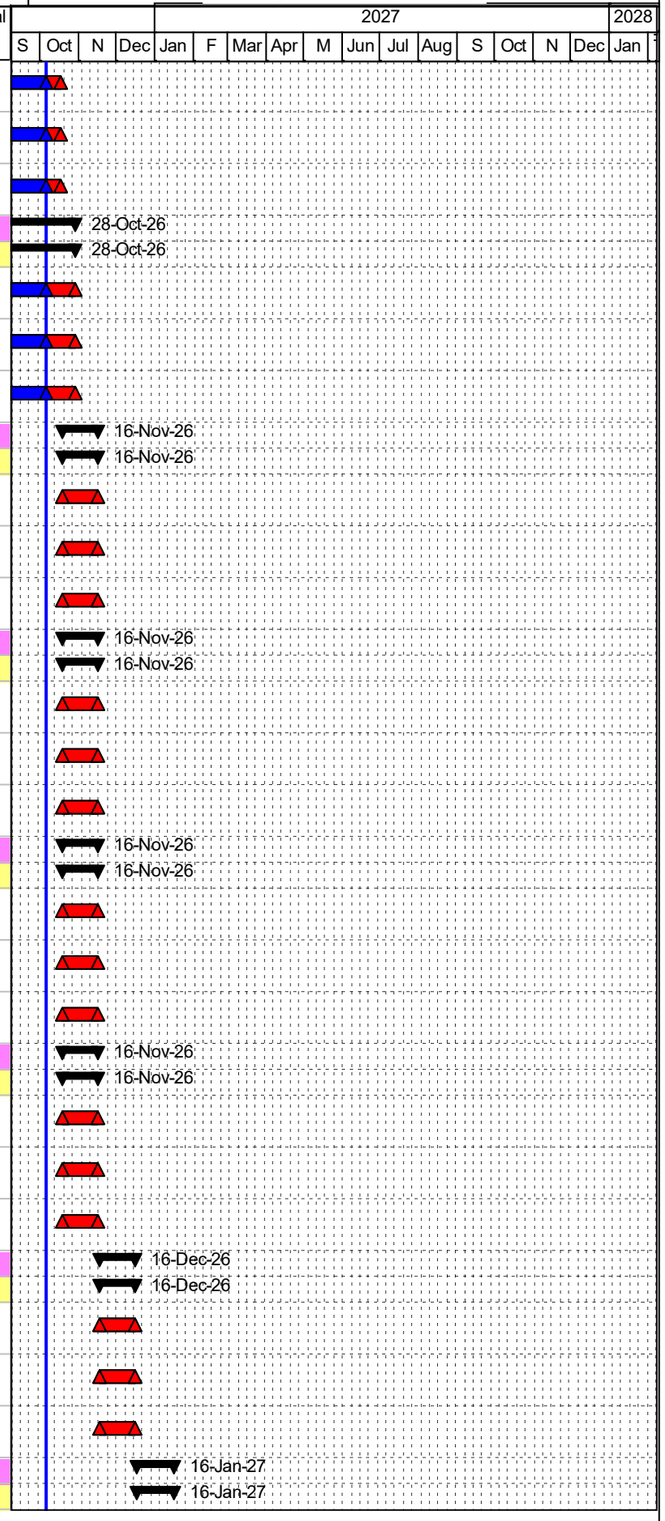

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R11-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	17-Dec-26	16-Jan-27	24-Feb-26	29-Mar-26	0%	0.00	0.00
PRO-R11-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	17-Dec-26	16-Jan-27	24-Feb-26	29-Mar-26	0%	0.00	0.00
PRO-R11-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	17-Dec-26	16-Jan-27	24-Feb-26	29-Mar-26	0%	0.00	0.00
Potable Water Network		406	13-Dec-25 A	23-May-27	31-May-25	09-Feb-26	36.91%	467,138.80	467,138.80
1st Material Delivery & Site Inspection		6	06-Oct-26	12-Oct-26	31-May-25	10-Jun-25	0%	0.00	0.00
Testing and Finishes		6	06-Oct-26	12-Oct-26	31-May-25	10-Jun-25	0%	0.00	0.00
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	6	06-Oct-26	12-Oct-26	31-May-25	10-Jun-25	0%	0.00	0.00
Material Delivery & Site Inspection		406	13-Dec-25 A	23-May-27	11-Jun-25	09-Feb-26	36.91%	467,138.80	467,138.80
Road 18 Local 1 (479 LM)		26	13-Oct-26	11-Nov-26	11-Jun-25	10-Jul-25	0%	0.00	0.00
Testing and Finishes		26	13-Oct-26	11-Nov-26	11-Jun-25	10-Jul-25	0%	0.00	0.00
PRO-R18-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	13-Oct-26	11-Nov-26	11-Jun-25	10-Jul-25	0%	0.00	0.00
Road 17 Local 1 (500 LM)		58	06-Oct-26	12-Dec-26	16-Jun-25	10-Aug-25	0%	5,532.80	5,532.80
Main Line Sections		26	06-Oct-26	04-Nov-26	16-Jun-25	15-Jul-25	0%	5,532.80	5,532.80
PRO-R17-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Oct-26	04-Nov-26	16-Jun-25	15-Jul-25	0%	5,532.80	5,532.80
Testing and Finishes		26	12-Nov-26	12-Dec-26	12-Jul-25	10-Aug-25	0%	0.00	0.00
PRO-R17-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	12-Nov-26	12-Dec-26	12-Jul-25	10-Aug-25	0%	0.00	0.00
Road 16 Local 1 (527 LM)		84	06-Oct-26	11-Jan-27	16-Jul-25	09-Sep-25	0%	3,952.00	3,952.00
Main Line Sections		26	06-Oct-26	04-Nov-26	16-Jul-25	14-Aug-25	0%	3,952.00	3,952.00
PRO-R16-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Oct-26	04-Nov-26	16-Jul-25	14-Aug-25	0%	3,952.00	3,952.00
Testing and Finishes		26	13-Dec-26	11-Jan-27	11-Aug-25	09-Sep-25	0%	0.00	0.00
PRO-R16-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	13-Dec-26	11-Jan-27	11-Aug-25	09-Sep-25	0%	0.00	0.00
Road 15 Local 1 (556 LM)		110	06-Oct-26	10-Feb-27	16-Aug-25	11-Oct-25	0%	4,742.40	4,742.40
Main Line Sections		26	06-Oct-26	04-Nov-26	16-Aug-25	14-Sep-25	0%	4,742.40	4,742.40
PRO-R15-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Oct-26	04-Nov-26	16-Aug-25	14-Sep-25	0%	4,742.40	4,742.40
Testing and Finishes		26	12-Jan-27	10-Feb-27	10-Sep-25	11-Oct-25	0%	0.00	0.00
PRO-R15-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	12-Jan-27	10-Feb-27	10-Sep-25	11-Oct-25	0%	0.00	0.00
Road 10 Local 2 (2352 LM)		354	13-Dec-25 A	17-Mar-27	15-Sep-25	10-Nov-25	60.95%	282,851.00	282,851.00
Main Line Sections		26	13-Dec-25 A	05-Dec-26	15-Sep-25	15-Oct-25	80%	215,514.40	215,514.40
PRO-R10-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Dec-25 A	05-Dec-26	15-Sep-25	15-Oct-25	80%	215,514.40	215,514.40
Testing and Finishes		26	11-Feb-27	17-Mar-27	12-Oct-25	10-Nov-25	0%	67,336.60	67,336.60
PRO-R10-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	11-Feb-27	17-Mar-27	12-Oct-25	10-Nov-25	0%	67,336.60	67,336.60
Road 14 Local 1 (584 LM)		26	05-Nov-26	05-Dec-26	16-Oct-25	15-Nov-25	0%	146,233.00	146,233.00
Main Line Sections		26	05-Nov-26	05-Dec-26	16-Oct-25	15-Nov-25	0%	146,233.00	146,233.00
PRO-R14-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	05-Nov-26	05-Dec-26	16-Oct-25	15-Nov-25	0%	146,233.00	146,233.00
Road 09 Local 2 (2278 LM)		110	06-Dec-26	17-Apr-27	16-Nov-25	10-Jan-26	0%	19,085.20	19,085.20
Main Line Sections		26	06-Dec-26	04-Jan-27	16-Nov-25	15-Dec-25	0%	19,085.20	19,085.20
PRO-R09-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Dec-26	04-Jan-27	16-Nov-25	15-Dec-25	0%	19,085.20	19,085.20
Testing and Finishes		26	18-Mar-27	17-Apr-27	11-Dec-25	10-Jan-26	0%	0.00	0.00
PRO-R09-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	18-Mar-27	17-Apr-27	11-Dec-25	10-Jan-26	0%	0.00	0.00
Road 11 Local 1 (670 LM)		110	05-Jan-27	23-May-27	16-Dec-25	09-Feb-26	0%	4,742.40	4,742.40
Main Line Sections		26	05-Jan-27	03-Feb-27	16-Dec-25	14-Jan-26	0%	4,742.40	4,742.40
PRO-R11-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	05-Jan-27	03-Feb-27	16-Dec-25	14-Jan-26	0%	4,742.40	4,742.40
Testing and Finishes		26	18-Apr-27	23-May-27	11-Jan-26	09-Feb-26	0%	0.00	0.00
PRO-R11-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	18-Apr-27	23-May-27	11-Jan-26	09-Feb-26	0%	0.00	0.00
Irrigation Network		20	06-Oct-26	28-Oct-26	17-Jul-25	07-Oct-25	0%	24,471.80	24,471.80
1st Material Delivery & Site Inspection		6	06-Oct-26	12-Oct-26	17-Jul-25	23-Jul-25	0%	0.00	0.00
Main Line Pipes		6	06-Oct-26	12-Oct-26	17-Jul-25	23-Jul-25	0%	0.00	0.00
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	06-Oct-26	12-Oct-26	17-Jul-25	23-Jul-25	0%	0.00	0.00
Material Delivery & Site Inspection		20	06-Oct-26	28-Oct-26	24-Jul-25	07-Oct-25	0%	24,471.80	24,471.80
Road 18 Local 1 (479 LM)		7	06-Oct-26	13-Oct-26	24-Jul-25	11-Aug-25	0%	4,631.80	4,631.80
Main Line Pipes		7	06-Oct-26	13-Oct-26	24-Jul-25	11-Aug-25	0%	4,631.80	4,631.80

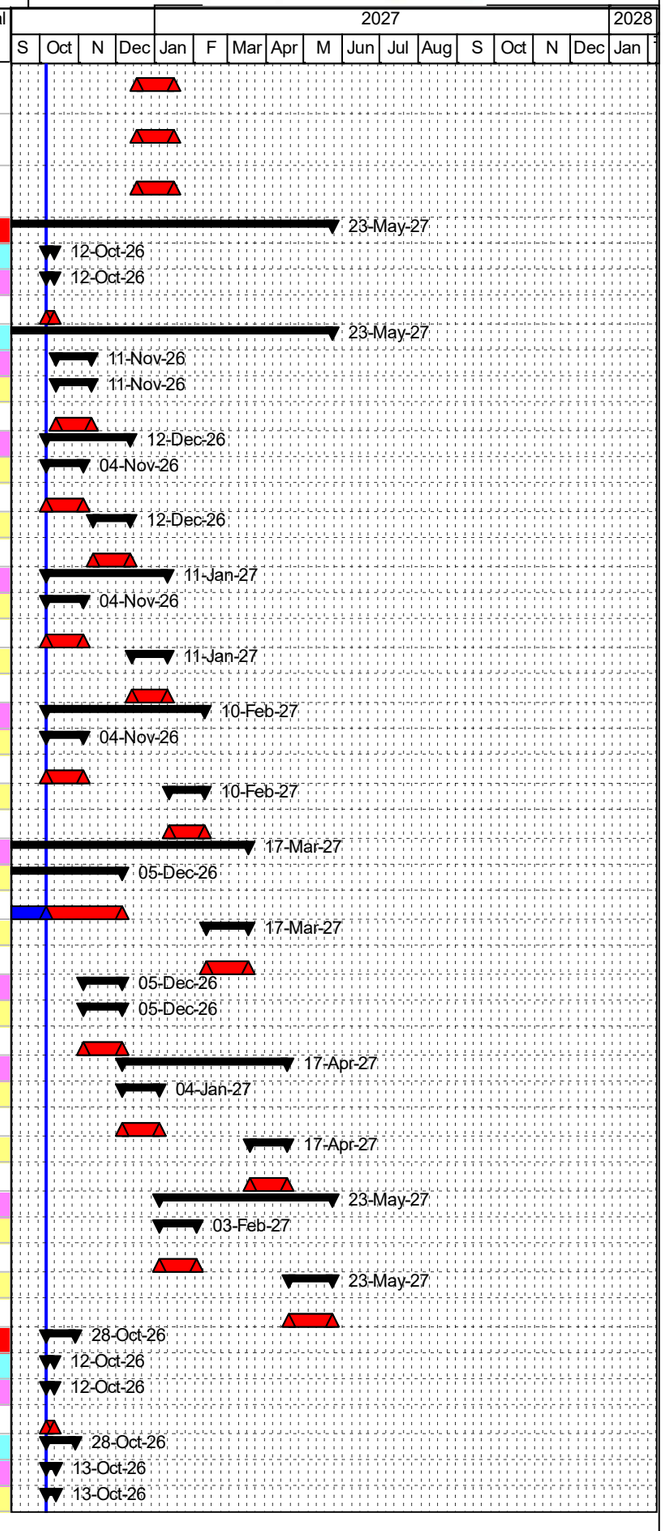

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R18-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	7	06-Oct-26	13-Oct-26	24-Jul-25	11-Aug-25	0%	4,631.80	4,631.80
Road 17 Local 1 (500 LM)		7	14-Oct-26	21-Oct-26	12-Aug-25	30-Aug-25	0%	10,795.40	10,795.40
Main Line Pipes		7	14-Oct-26	21-Oct-26	12-Aug-25	30-Aug-25	0%	10,795.40	10,795.40
PRO-R17-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	7	14-Oct-26	21-Oct-26	12-Aug-25	30-Aug-25	0%	10,795.40	10,795.40
Road 16 Local 1 (527 LM)		7	14-Oct-26	21-Oct-26	31-Aug-25	17-Sep-25	0%	5,474.60	5,474.60
Main Line Pipes		7	14-Oct-26	21-Oct-26	31-Aug-25	17-Sep-25	0%	5,474.60	5,474.60
PRO-R16-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	7	14-Oct-26	21-Oct-26	31-Aug-25	17-Sep-25	0%	5,474.60	5,474.60
Road 15 Local 1 (556 LM)		6	22-Oct-26	28-Oct-26	18-Sep-25	07-Oct-25	0%	3,570.00	3,570.00
Main Line Pipes		6	22-Oct-26	28-Oct-26	18-Sep-25	07-Oct-25	0%	3,570.00	3,570.00
PRO-R15-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	6	22-Oct-26	28-Oct-26	18-Sep-25	07-Oct-25	0%	3,570.00	3,570.00
Medium Voltage Network		478	13-Dec-25 A	15-Jul-27	03-May-25	04-Mar-26	87.4%	370,009.77	370,009.77
1st Material Delivery & Site Inspection		52	06-Oct-26	05-Dec-26	03-May-25	10-Nov-25	0%	0.00	0.00
RMU Concrete Works		52	06-Oct-26	05-Dec-26	10-Sep-25	10-Nov-25	0%	0.00	0.00
PRO-MV-1DL-110	1ST Material Delivery for RMU Concrete Foundations of Medium Voltage Network	52	06-Oct-26	05-Dec-26	10-Sep-25	10-Nov-25	0%	0.00	0.00
Termination and Testing Works		26	06-Oct-26	04-Nov-26	03-May-25	01-Jun-25	0%	0.00	0.00
PRO-MV-1DL-120	1ST Material Delivery for Termination and Joints Kits of Medium Voltage Network	26	06-Oct-26	04-Nov-26	03-May-25	01-Jun-25	0%	0.00	0.00
Material Delivery & Site Inspection		478	13-Dec-25 A	15-Jul-27	21-Jun-25	04-Mar-26	87.4%	370,009.77	370,009.77
Road 18 Local 1 (479 LM)		26	05-Nov-26	05-Dec-26	21-Jun-25	20-Jul-25	0%	1,067.20	1,067.20
Termination and Testing Works		26	05-Nov-26	05-Dec-26	21-Jun-25	20-Jul-25	0%	1,067.20	1,067.20
PRO-R18-MV-DL-13	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	05-Nov-26	05-Dec-26	21-Jun-25	20-Jul-25	0%	1,067.20	1,067.20
Road 17 Local 1 (500 LM)		64	06-Dec-26	17-Feb-27	21-Jul-25	04-Mar-26	0%	533.60	533.60
RMU Concrete Works		38	05-Jan-27	17-Feb-27	20-Jan-26	04-Mar-26	0%	0.00	0.00
PRO-R17-MV-DL-12	Material Delivery & Site Inspection of RMU Concrete Foundations for Medium Voltage Network	38	05-Jan-27	17-Feb-27	20-Jan-26	04-Mar-26	0%	0.00	0.00
Termination and Testing Works		26	06-Dec-26	04-Jan-27	21-Jul-25	19-Aug-25	0%	533.60	533.60
PRO-R17-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	06-Dec-26	04-Jan-27	21-Jul-25	19-Aug-25	0%	533.60	533.60
Road 16 Local 1 (527 LM)		26	05-Jan-27	03-Feb-27	20-Aug-25	18-Sep-25	0%	1,067.20	1,067.20
Termination and Testing Works		26	05-Jan-27	03-Feb-27	20-Aug-25	18-Sep-25	0%	1,067.20	1,067.20
PRO-R16-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	05-Jan-27	03-Feb-27	20-Aug-25	18-Sep-25	0%	1,067.20	1,067.20
Road 15 Local 1 (556 LM)		26	04-Feb-27	07-Mar-27	20-Sep-25	20-Oct-25	0%	533.60	533.60
Termination and Testing Works		26	04-Feb-27	07-Mar-27	20-Sep-25	20-Oct-25	0%	533.60	533.60
PRO-R15-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	04-Feb-27	07-Mar-27	20-Sep-25	20-Oct-25	0%	533.60	533.60
Road 10 Local 2 (2352 LM)		104	06-Dec-26	10-Apr-27	21-Oct-25	19-Jan-26	0%	2,134.40	2,134.40
RMU Concrete Works		26	06-Dec-26	04-Jan-27	21-Dec-25	19-Jan-26	0%	0.00	0.00
PRO-R10-MV-DL-12	Material Delivery & Site Inspection of RMU Concrete Foundations for Medium Voltage Network	26	06-Dec-26	04-Jan-27	21-Dec-25	19-Jan-26	0%	0.00	0.00
Termination and Testing Works		26	08-Mar-27	10-Apr-27	21-Oct-25	19-Nov-25	0%	2,134.40	2,134.40
PRO-R10-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	08-Mar-27	10-Apr-27	21-Oct-25	19-Nov-25	0%	2,134.40	2,134.40
Road 14 Local 1 (584 LM)		26	11-Apr-27	10-May-27	20-Nov-25	20-Dec-25	0%	1,067.20	1,067.20
Termination and Testing Works		26	11-Apr-27	10-May-27	20-Nov-25	20-Dec-25	0%	1,067.20	1,067.20
PRO-R14-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	11-Apr-27	10-May-27	20-Nov-25	20-Dec-25	0%	1,067.20	1,067.20
Road 09 Local 2 (2278 LM)		452	13-Dec-25 A	15-Jun-27	20-Nov-25	19-Jan-26	89.21%	362,539.37	362,539.37
Cabling Works		26	13-Dec-25 A	04-Nov-26	20-Nov-25	20-Dec-25	90%	359,337.77	359,337.77
PRO-R09-MV-DL-10	Material Delivery & Site Inspection of Medium Voltage Cables for Medium Voltage Network	26	13-Dec-25 A	04-Nov-26	20-Nov-25	20-Dec-25	90%	359,337.77	359,337.77
Termination and Testing Works		26	11-May-27	15-Jun-27	21-Dec-25	19-Jan-26	0%	3,201.60	3,201.60
PRO-R09-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	11-May-27	15-Jun-27	21-Dec-25	19-Jan-26	0%	3,201.60	3,201.60

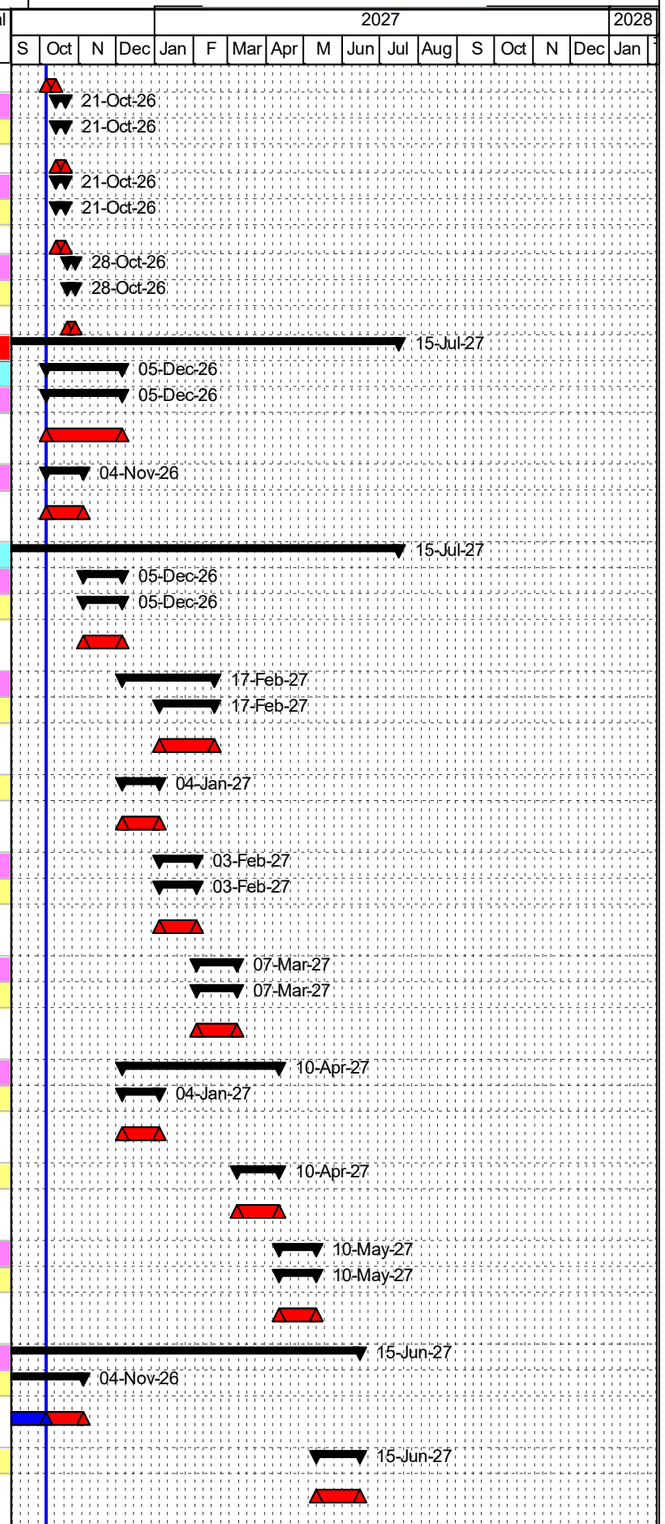

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Road 11 Local 1 (670 LM)		26	16-Jun-27	15-Jul-27	20-Jan-26	18-Feb-26	0%	1,067.20	1,067.20
Termination and Testing Works		26	16-Jun-27	15-Jul-27	20-Jan-26	18-Feb-26	0%	1,067.20	1,067.20
PRO-R11-MV-DL-11	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	16-Jun-27	15-Jul-27	20-Jan-26	18-Feb-26	0%	1,067.20	1,067.20
Street Lighting Network		233	21-Sep-26 A	08-Jul-27	26-Jul-25	23-Jun-26	39.9%	258,158.00	258,158.00
1st Material Delivery & Site Inspection		15	06-Oct-26	22-Oct-26	26-Jul-25	11-Aug-25	0%	0.00	0.00
Lighting Poles Works		6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0%	0.00	0.00
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0%	0.00	0.00
Distribution Panel Board		6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0%	0.00	0.00
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0%	0.00	0.00
Termination and Testing Works		15	06-Oct-26	22-Oct-26	26-Jul-25	11-Aug-25	0%	0.00	0.00
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	11-Aug-25	0%	0.00	0.00
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	06-Oct-26	22-Oct-26	26-Jul-25	11-Aug-25	0%	0.00	0.00
Earthing System Works		6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0%	0.00	0.00
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0%	0.00	0.00
Material Delivery & Site Inspection		233	21-Sep-26 A	08-Jul-27	02-Aug-25	23-Jun-26	39.9%	258,158.00	258,158.00
Road 18 Local 1 (479 LM)		40	13-Oct-26	28-Nov-26	16-Aug-25	15-Nov-25	0%	8,511.96	8,511.96
Lighting Poles Works		10	13-Oct-26	24-Oct-26	16-Aug-25	14-Sep-25	0%	3,754.80	3,754.80
PRO-R18-SL-DL-22	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	10	13-Oct-26	24-Oct-26	16-Aug-25	14-Sep-25	0%	3,754.80	3,754.80
Termination and Testing Works		40	13-Oct-26	28-Nov-26	15-Sep-25	15-Nov-25	0%	4,757.16	4,757.16
PRO-R18-SL-DL-2	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	14	13-Oct-26	28-Oct-26	15-Sep-25	15-Oct-25	0%	4,757.16	4,757.16
PRO-R18-SL-DL-2	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	29-Oct-26	28-Nov-26	16-Oct-25	15-Nov-25	0%	0.00	0.00
Road 17 Local 1 (500 LM)		66	13-Oct-26	28-Dec-26	15-Sep-25	15-Dec-25	0%	8,014.22	8,014.22
Lighting Poles Works		26	25-Oct-26	23-Nov-26	15-Sep-25	15-Oct-25	0%	3,933.60	3,933.60
PRO-R17-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	25-Oct-26	23-Nov-26	15-Sep-25	15-Oct-25	0%	3,933.60	3,933.60
Termination and Testing Works		66	13-Oct-26	28-Dec-26	16-Oct-25	15-Dec-25	0%	4,080.62	4,080.62
PRO-R17-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	13-Oct-26	11-Nov-26	16-Oct-25	15-Nov-25	0%	4,080.62	4,080.62
PRO-R17-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	29-Nov-26	28-Dec-26	16-Nov-25	15-Dec-25	0%	0.00	0.00
Road 16 Local 1 (527 LM)		92	13-Oct-26	27-Jan-27	16-Oct-25	14-Jan-26	0%	8,262.58	8,262.58
Lighting Poles Works		26	24-Nov-26	23-Dec-26	16-Oct-25	15-Nov-25	0%	4,112.40	4,112.40
PRO-R16-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	24-Nov-26	23-Dec-26	16-Oct-25	15-Nov-25	0%	4,112.40	4,112.40
Termination and Testing Works		92	13-Oct-26	27-Jan-27	16-Nov-25	14-Jan-26	0%	4,150.18	4,150.18
PRO-R16-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	13-Oct-26	11-Nov-26	16-Nov-25	15-Dec-25	0%	4,150.18	4,150.18
PRO-R16-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	29-Dec-26	27-Jan-27	16-Dec-25	14-Jan-26	0%	0.00	0.00
Road 15 Local 1 (556 LM)		92	12-Nov-26	28-Feb-27	16-Nov-25	14-Feb-26	0%	9,492.51	9,492.51
Lighting Poles Works		26	24-Nov-26	23-Dec-26	16-Nov-25	15-Dec-25	0%	4,470.00	4,470.00
PRO-R15-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	24-Nov-26	23-Dec-26	16-Nov-25	15-Dec-25	0%	4,470.00	4,470.00
Termination and Testing Works		92	12-Nov-26	28-Feb-27	16-Dec-25	14-Feb-26	0%	5,022.51	5,022.51
PRO-R15-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	12-Nov-26	12-Dec-26	16-Dec-25	14-Jan-26	0%	5,022.51	5,022.51
PRO-R15-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	28-Jan-27	28-Feb-27	15-Jan-26	14-Feb-26	0%	0.00	0.00
Road 10 Local 2 (2352 LM)		144	21-Sep-26 A	03-Apr-27	02-Aug-25	16-Mar-26	68.93%	149,437.50	149,437.50
Lighting Poles Works		26	24-Dec-26	23-Jan-27	16-Dec-25	14-Jan-26	0%	17,164.80	17,164.80
PRO-R10-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	24-Dec-26	23-Jan-27	16-Dec-25	14-Jan-26	0%	17,164.80	17,164.80
Distribution Panel Board		26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	80%	103,537.20	103,537.20
PRO-R10-SL-DL-16	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting Network	26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	80%	103,537.20	103,537.20
Termination and Testing Works		92	21-Sep-26 A	03-Apr-27	15-Jan-26	16-Mar-26	80%	25,217.50	25,217.50
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	21-Sep-26 A	11-Jan-27	15-Jan-26	14-Feb-26	80%	25,217.50	25,217.50
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	21-Sep-26 A	03-Apr-27	15-Feb-26	16-Mar-26	80%	0.00	0.00

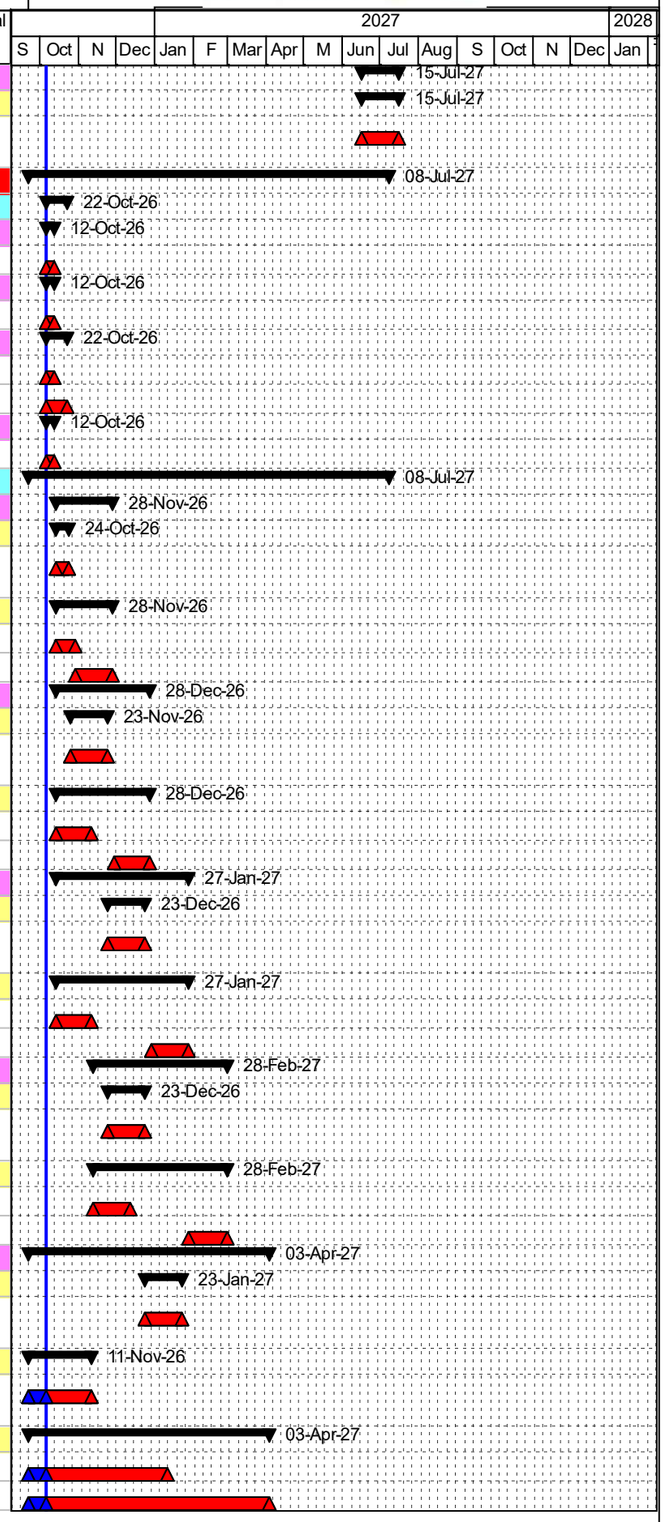

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Earthing System Works		26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	0%	3,518.00	3,518.00
PRO-R10-SL-DL-15	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	0%	3,518.00	3,518.00
Road 14 Local 1 (584 LM)		92	12-Jan-27	03-May-27	15-Jan-26	19-Apr-26	0%	17,817.51	17,817.51
Lighting Poles Works		26	24-Jan-27	23-Feb-27	15-Jan-26	14-Feb-26	0%	9,812.00	9,812.00
PRO-R14-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	24-Jan-27	23-Feb-27	15-Jan-26	14-Feb-26	0%	9,812.00	9,812.00
Termination and Testing Works		92	12-Jan-27	03-May-27	15-Feb-26	19-Apr-26	0%	8,005.51	8,005.51
PRO-R14-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	12-Jan-27	10-Feb-27	15-Feb-26	16-Mar-26	0%	8,005.51	8,005.51
PRO-R14-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	04-Apr-27	03-May-27	17-Mar-26	19-Apr-26	0%	0.00	0.00
Road 09 Local 2 (2278 LM)		196	13-Oct-26	08-Jun-27	02-Aug-25	19-May-26	0%	46,239.00	46,239.00
Lighting Poles Works		26	24-Feb-27	29-Mar-27	15-Feb-26	16-Mar-26	0%	17,522.40	17,522.40
PRO-R09-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	24-Feb-27	29-Mar-27	15-Feb-26	16-Mar-26	0%	17,522.40	17,522.40
Termination and Testing Works		92	11-Feb-27	08-Jun-27	17-Mar-26	19-May-26	0%	25,198.60	25,198.60
PRO-R09-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	11-Feb-27	17-Mar-27	17-Mar-26	19-Apr-26	0%	25,198.60	25,198.60
PRO-R09-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	04-May-27	08-Jun-27	20-Apr-26	19-May-26	0%	0.00	0.00
Earthing System Works		26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	0%	3,518.00	3,518.00
PRO-R09-SL-DL-15	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	0%	3,518.00	3,518.00
Road 11 Local 1 (670 LM)		92	18-Mar-27	08-Jul-27	17-Mar-26	23-Jun-26	0%	10,382.72	10,382.72
Lighting Poles Works		26	30-Mar-27	28-Apr-27	17-Mar-26	19-Apr-26	0%	5,006.40	5,006.40
PRO-R11-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	30-Mar-27	28-Apr-27	17-Mar-26	19-Apr-26	0%	5,006.40	5,006.40
Termination and Testing Works		92	18-Mar-27	08-Jul-27	20-Apr-26	23-Jun-26	0%	5,376.32	5,376.32
PRO-R11-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	18-Mar-27	17-Apr-27	20-Apr-26	19-May-26	0%	5,376.32	5,376.32
PRO-R11-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	09-Jun-27	08-Jul-27	20-May-26	23-Jun-26	0%	0.00	0.00
Superstructure Works		379	29-Oct-25 A	17-Mar-27	13-Aug-25	14-Feb-26	95.27%	593,673.60	593,673.60
Manufacturing of Material		40	06-Oct-26	21-Nov-26	16-Aug-25	25-Oct-25	0%	0.00	0.00
Storm Drainage Ponds (PO-J1 , PO-J2)		40	06-Oct-26	21-Nov-26	16-Aug-25	25-Oct-25	0%	0.00	0.00
PRO-DPO-CV-MF-2(	Manufacturing of Civil Works for Storm Drainage Ponds (PO-J2)	40	06-Oct-26	21-Nov-26	16-Aug-25	25-Oct-25	0%	0.00	0.00
1st Material Delivery & Site Inspection		66	06-Oct-26	21-Dec-26	13-Aug-25	24-Nov-25	0%	0.00	0.00
Sewage Pump Stations (PS 06)		40	06-Oct-26	21-Nov-26	13-Aug-25	29-Sep-25	0%	0.00	0.00
PRO-SPS-CV-1DL-1	1ST Material Delivery for Civil Works for Sewage Pump Stations (PS 06)	40	06-Oct-26	21-Nov-26	13-Aug-25	29-Sep-25	0%	0.00	0.00
Storm Drainage Ponds (PO-J1 , PO-J2)		26	22-Nov-26	21-Dec-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
PRO-DPO-CV-1DL-	1ST Material Delivery for Civil Works for Storm Drainage Ponds (PO-J2)	26	22-Nov-26	21-Dec-26	26-Oct-25	24-Nov-25	0%	0.00	0.00
Material Delivery & Site Inspection		379	29-Oct-25 A	17-Mar-27	15-Sep-25	14-Feb-26	95.27%	593,673.60	593,673.60
Storm Drainage Ponds (PO-J1 , PO-J2)		379	29-Oct-25 A	17-Mar-27	15-Sep-25	14-Feb-26	95.27%	593,673.60	593,673.60
PRO-DPO-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J1)	70	29-Oct-25 A	26-Dec-26	15-Sep-25	06-Dec-25	97%	508,118.00	508,118.00
PRO-DPO-CV-DL-20	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J2)	70	09-Sep-26 A	17-Mar-27	25-Nov-25	14-Feb-26	85%	85,555.60	85,555.60
Long Lead Time Items		298	01-Jun-25 A	08-May-27	29-Nov-25	31-Aug-26	30%	1,035,904.00	1,035,904.00
Superstructure Works		298	01-Jun-25 A	08-May-27	29-Nov-25	31-Aug-26	30%	1,035,904.00	1,035,904.00
Sewage Pump Stations (PS 06)		298	01-Jun-25 A	08-May-27	29-Nov-25	31-Aug-26	30%	1,035,904.00	1,035,904.00
Manufacturing of Material		100	01-Jun-25 A	02-Dec-26	29-Nov-25	28-Mar-26	0%	0.00	0.00
PRO-SPS7-LL-MF-10	Manufacturing of Electromechanical Works for Sewage Pump Stations (PS 06)	100	01-Jun-25 A	02-Dec-26	29-Nov-25	28-Mar-26	50%	0.00	0.00
Material Shipping/Custom Clearance/Delivery		80	03-Dec-26	07-Mar-27	29-Mar-26	04-Jul-26	0%	0.00	0.00
PRO-SPS7-LL-SH/DL	Material Delivery for Electromechanical Works for Sewage Pump Stations (PS 06)	80	03-Dec-26	07-Mar-27	29-Mar-26	04-Jul-26	0%	0.00	0.00
Material Site Inspection		50	15-Sep-26 A	08-May-27	05-Jul-26	31-Aug-26	30%	1,035,904.00	1,035,904.00
PRO-SPS7-LL-MSI-10	Material Site Inspection for Electromechanical Works for Sewage Pump Stations (PS06)	50	15-Sep-26 A	08-May-27	05-Jul-26	31-Aug-26	30%	1,035,904.00	1,035,904.00
Construction Works		594	10-Nov-25 A	25-Oct-27	19-Mar-25	28-Dec-26	20.87%	29,984,886.48	29,253,414.67

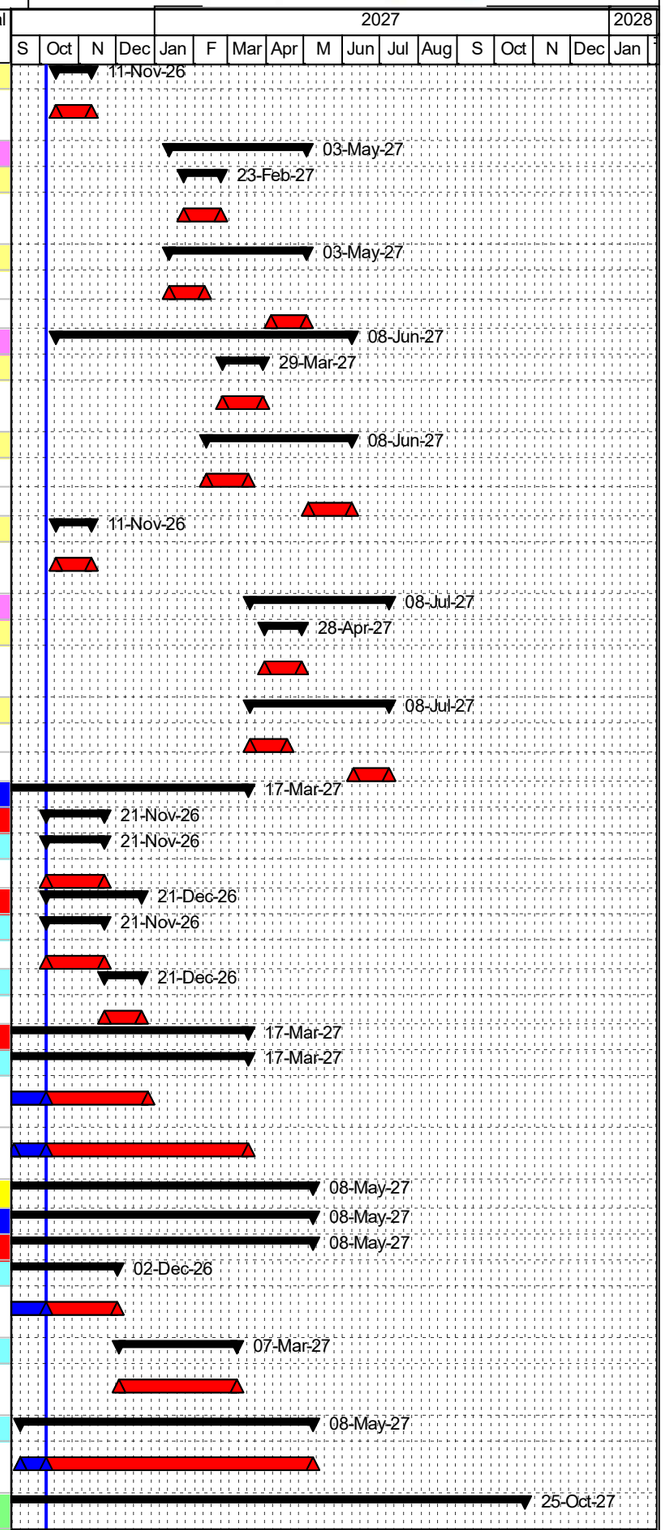

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Infrastructure Networks		594	10-Nov-25 A	25-Oct-27	19-Mar-25	28-Dec-26	24.75%	25,289,331.70	24,557,859.89
Phase 2 Block "J"		531	10-Nov-25 A	06-Sep-27	19-Mar-25	19-Nov-26	30.2%	15,892,758.35	15,263,243.95
Rising Main Network		240	17-Jan-26 A	14-Dec-26	27-Sep-25	13-Nov-25	68.16%	2,786,828.18	2,397,373.70
Main Line Sections		226	25-Feb-26 A	14-Dec-26	27-Sep-25	13-Nov-25	87.75%	1,336,085.86	1,336,085.86
CO-RM-SW-300	Pipes Laying Works for Main Lines of Rising Main Network	21	25-Feb-26 A	19-Nov-26	27-Sep-25	20-Oct-25	96%	1,169,075.13	1,169,075.13
CO-RM-SW-310	Trench Backfilling and Compaction Works for Main Lines of Rising Main Network	21	01-Sep-26 A	14-Dec-26	21-Oct-25	13-Nov-25	30%	167,010.73	167,010.73
Manholes		233	17-Jan-26 A	16-Nov-26	28-Sep-25	18-Oct-25	70.76%	835,053.66	835,053.66
CO-RM-SW-330	Installation RC Footing Works for Main Line Manholes of Rising Main Network	3	17-Jan-26 A	29-Oct-26	28-Sep-25	30-Sep-25	97%	66,804.29	66,804.29
CO-RM-SW-340	Install Grp Liner Wall Works for Main Line Manholes of Rising Main Network	6	17-Jan-26 A	05-Nov-26	01-Oct-25	07-Oct-25	98%	501,032.20	501,032.20
CO-RM-SW-350	Pouring Grp Liner Wall Works for Main Line Manholes of Rising Main Network	3	18-Sep-26 A	09-Nov-26	08-Oct-25	11-Oct-25	30%	66,804.29	66,804.29
CO-RM-SW-360	Backfilling Works for Main Line Manholes of Rising Main Network	5	21-Sep-26 A	15-Nov-26	12-Oct-25	16-Oct-25	15%	100,206.44	100,206.44
CO-RM-SW-370	Testing Works for Main Line Manholes of Rising Main Network	1	16-Nov-26	16-Nov-26	18-Oct-25	18-Oct-25	0%	100,206.44	100,206.44
Valves Chamber		121	14-May-26 A	15-Nov-26	05-Oct-25	01-Nov-25	22.14%	615,688.66	226,234.18
CO-RM-SW-400	RC Wall Works for Valve Chambers and Washout chamber of Rising Main Network	7	14-May-26 A	27-Oct-26	05-Oct-25	12-Oct-25	35%	389,454.48	0.00
CO-RM-SW-410	RC Slab Works for Valve Chambers and Washout chamber of Rising Main Network	7	27-Oct-26	03-Nov-26	13-Oct-25	20-Oct-25	0%	43,272.72	43,272.72
CO-RM-SW-420	Insulation Works for Valve Chambers and Washout chamber of Rising Main Network	2	04-Nov-26	05-Nov-26	21-Oct-25	22-Oct-25	0%	43,272.72	43,272.72
CO-RM-SW-430	Backfilling Works for Valve Chambers and Washout chamber of Rising Main Network	5	07-Nov-26	11-Nov-26	23-Oct-25	28-Oct-25	0%	53,143.29	53,143.29
CO-RM-SW-440	Testing and Covering Works for Valve Chambers and Washout chamber of Rising Main Network	3	12-Nov-26	15-Nov-26	29-Oct-25	01-Nov-25	0%	86,545.44	86,545.44
Road 09 Local 2 (2278 LM)		495	10-Nov-25 A	07-Aug-27	21-Jul-25	01-Oct-26	24.47%	6,117,624.88	5,983,278.97
SW_1		293	02-May-26 A	31-Jul-27	11-Aug-25	24-Sep-26	20.95%	3,211,612.03	3,211,612.03
Sewage Network		1	06-Oct-26	06-Oct-26	11-Aug-25	11-Aug-25	0%	35,494.42	35,494.42
Manholes		1	06-Oct-26	06-Oct-26	11-Aug-25	11-Aug-25	0%	35,494.42	35,494.42
CO-R09.S01-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09] -[SW-1]	1	06-Oct-26	06-Oct-26	11-Aug-25	11-Aug-25	0%	35,494.42	35,494.42
Storm Drainage Network		97	27-Jun-26 A	12-Nov-26	05-Oct-25	18-Nov-25	69.33%	287,863.46	287,863.46
Manholes		2	07-Oct-26	08-Oct-26	05-Oct-25	06-Oct-25	0%	38,388.86	38,388.86
CO-R09.S01-SD-	Testing Works for Manholes of Storm Drainage Network-[Road 09] -[SW-1]	2	07-Oct-26	08-Oct-26	05-Oct-25	06-Oct-25	0%	38,388.86	38,388.86
Catch Basin Sections		97	27-Jun-26 A	12-Nov-26	15-Oct-25	18-Nov-25	80%	249,474.61	249,474.61
CO-R09.S01-SD-14	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	6	27-Jun-26 A	15-Oct-26	15-Oct-25	21-Oct-25	90%	41,579.10	41,579.10
CO-R09.S01-SD-15	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	29-Jun-26 A	24-Oct-26	22-Oct-25	29-Oct-25	90%	124,737.30	124,737.30
CO-R09.S01-SD-17	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	10	03-Aug-26 A	12-Nov-26	08-Nov-25	18-Nov-25	90%	55,438.80	55,438.80
CO-R09.S01-SD-16	Testing Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	25-Oct-26	01-Nov-26	30-Oct-25	06-Nov-25	0%	27,719.40	27,719.40
Irrigation Network		129	02-May-26 A	02-Dec-26	09-Dec-25	28-Dec-25	16.96%	140,090.67	140,090.67
Main Line Pipes		129	02-May-26 A	02-Dec-26	09-Dec-25	28-Dec-25	16.96%	140,090.67	140,090.67
CO-R09.S01-IR-120	Installation Works for Main Line Valves of Irrigation Network-[Road 09] -[SW-1]	7	02-May-26 A	21-Nov-26	09-Dec-25	16-Dec-25	20%	118,783.66	118,783.66
CO-R09.S01-IR-140	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 09] -[SW-1]	10	22-Nov-26	02-Dec-26	17-Dec-25	28-Dec-25	0%	21,307.01	21,307.01
Street Lighting Network		162	03-Dec-26	20-Jun-27	29-Dec-25	13-Aug-26	0%	273,720.46	273,720.46
Lighting Poles Works		68	03-Dec-26	20-Feb-27	29-Dec-25	30-Apr-26	0%	140,446.74	140,446.74
CO-R09.S01-SL-10(	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	10	03-Dec-26	14-Dec-26	29-Dec-25	08-Jan-26	0%	4,663.50	4,663.50
CO-R09.S01-SL-11(	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 09] -[SW-1]	12	15-Dec-26	28-Dec-26	10-Jan-26	22-Jan-26	0%	17,826.69	17,826.69
CO-R09.S01-SL-12(	Installation Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	11	19-Jan-27	31-Jan-27	14-Feb-26	25-Feb-26	0%	51,298.52	51,298.52

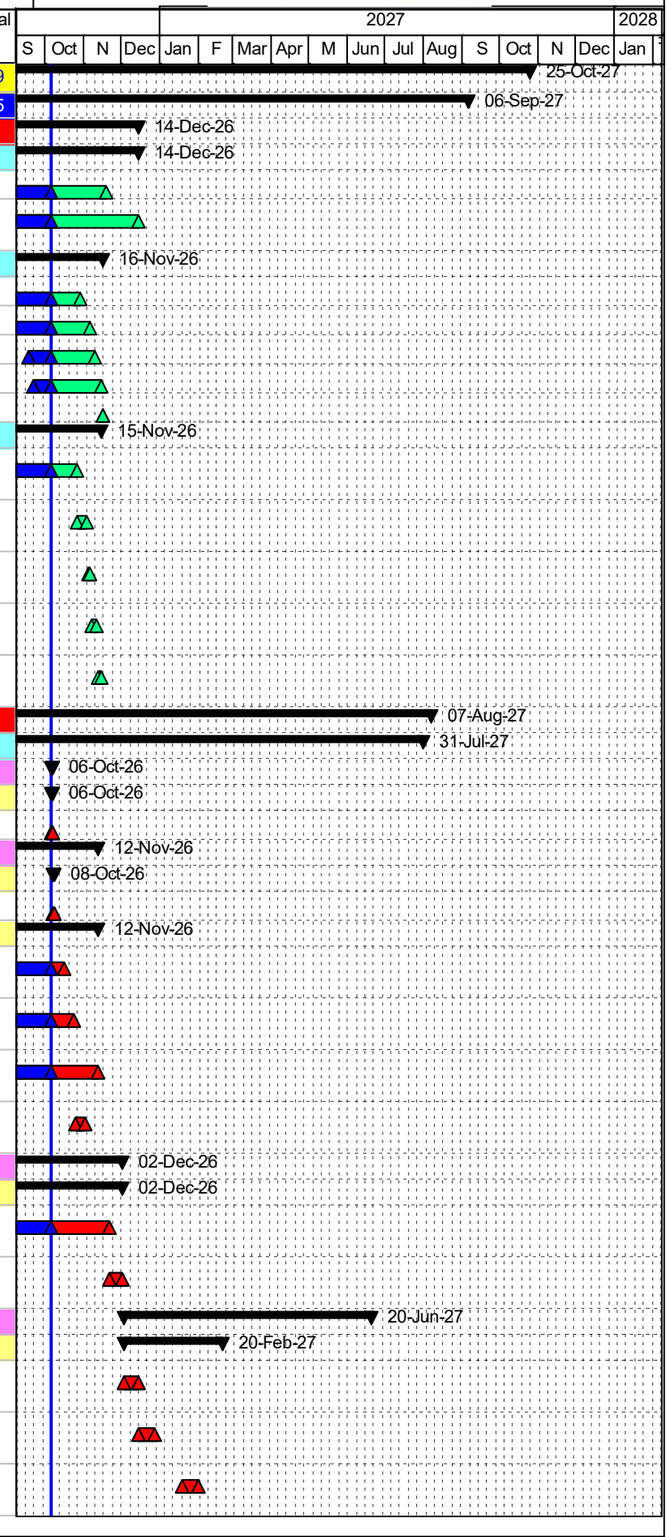

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09.S01-SL-21(	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	12	01-Feb-27	14-Feb-27	12-Apr-26	25-Apr-26	0%	18,654.01	18,654.01
CO-R09.S01-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 09] -[SW-1]	12	07-Feb-27	20-Feb-27	18-Apr-26	30-Apr-26	0%	29,350.02	29,350.02
CO-R09.S01-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	5	15-Feb-27	20-Feb-27	26-Apr-26	30-Apr-26	0%	18,654.01	18,654.01
Cabling Works		30	15-Dec-26	18-Jan-27	10-Jan-26	12-Feb-26	0%	94,451.91	94,451.91
CO-R09.S01-SL-14(	Trench Excavation and Bedding Works for Street Lighting Network-[Road 09] -[SW-1]	10	15-Dec-26	26-Dec-26	10-Jan-26	20-Jan-26	0%	0.00	0.00
CO-R09.S01-SL-1	Cable Laying Works for Street Lighting Network-[Road 09] -[SW-1]	10	27-Dec-26	06-Jan-27	21-Jan-26	01-Feb-26	0%	87,705.35	87,705.35
CO-R09.S01-SL-16(	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 09] -[SW-1]	10	07-Jan-27	18-Jan-27	02-Feb-26	12-Feb-26	0%	6,746.57	6,746.57
Distrubution Panel Boards		39	01-May-27	20-Jun-27	30-Jun-26	13-Aug-26	0%	38,821.81	38,821.81
CO-R09.S01-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 09] -[SW-1]	15	01-May-27	23-May-27	30-Jun-26	16-Jul-26	0%	0.00	0.00
CO-R09.S01-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 09] -[SW-1]	12	24-May-27	06-Jun-27	18-Jul-26	30-Jul-26	0%	0.00	0.00
CO-R09.S01-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 09] -[SW-1]	12	07-Jun-27	20-Jun-27	01-Aug-26	13-Aug-26	0%	38,821.81	38,821.81
CO-R09.S01-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 09] -[SW-1]	12	07-Jun-27	20-Jun-27	01-Aug-26	13-Aug-26	0%	0.00	0.00
Medium Voltage Network		23	30-Sep-26 A	06-Feb-27	14-Feb-26	03-Mar-26	2.3%	1,203,791.39	1,203,791.39
Cabling Works		23	30-Sep-26 A	06-Feb-27	14-Feb-26	03-Mar-26	2.3%	1,203,791.39	1,203,791.39
CO-R09.S01-MV-10	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 09] -[SW-1]	4	30-Sep-26 A	23-Jan-27	14-Feb-26	17-Feb-26	20%	138,631.25	138,631.25
CO-R09.S01-MV-1	Cable Laying Works for Medium Voltage Network-[Road 09] -[SW-1]	5	24-Jan-27	28-Jan-27	18-Feb-26	23-Feb-26	0%	745,612.10	745,612.10
CO-R09.S01-MV-12	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 09] -[SW-1]	7	30-Jan-27	06-Feb-27	24-Feb-26	03-Mar-26	0%	319,548.04	319,548.04
Telecom Network		38	07-Feb-27	27-Mar-27	03-May-26	20-Jun-26	0%	166,584.78	166,584.78
Ducts Works		12	07-Feb-27	20-Feb-27	03-May-26	16-May-26	0%	132,124.00	132,124.00
CO-R09.S01-TE-10(	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 09] -[SW-1]	2	07-Feb-27	08-Feb-27	03-May-26	04-May-26	0%	13,266.00	13,266.00
CO-R09.S01-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 09] -[SW-1]	4	09-Feb-27	13-Feb-27	05-May-26	09-May-26	0%	79,227.50	79,227.50
CO-R09.S01-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 09] -[SW-1]	2	14-Feb-27	15-Feb-27	10-May-26	11-May-26	0%	13,266.00	13,266.00
CO-R09.S01-TE-13(	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 09] -[SW-1]	4	16-Feb-27	20-Feb-27	12-May-26	16-May-26	0%	26,364.50	26,364.50
Manholes Works		36	09-Feb-27	27-Mar-27	05-May-26	20-Jun-26	0%	34,460.78	34,460.78
CO-R09.S01-TE-1	Excavation Works for Manholes of Telecom Network-[Road 09] -[SW-1]	12	09-Feb-27	23-Feb-27	05-May-26	18-May-26	0%	7,515.39	7,515.39
CO-R09.S01-TE-1	Installation Works for Manholes of Telecom Network-[Road 09] -[SW-1]	12	24-Feb-27	13-Mar-27	19-May-26	06-Jun-26	0%	19,430.00	19,430.00
CO-R09.S01-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 09] -[SW-1]	12	14-Mar-27	27-Mar-27	07-Jun-26	20-Jun-26	0%	7,515.39	7,515.39
Road Works		153	10-Jun-26 A	31-Jul-27	21-Jun-26	24-Sep-26	38.2%	1,104,066.86	1,104,066.86
Pre-Bituminous Construction		107	10-Jun-26 A	24-Apr-27	21-Jun-26	18-Jul-26	35.37%	890,287.34	890,287.34
CO-R09.S01-RD-I	Capping and Subgrade Layer for Road Works-[Road 09] -[SW-1]	21	10-Jun-26 A	20-Apr-27	21-Jun-26	14-Jul-26	60%	524,763.79	524,763.79
CO-R09.S01-RD-I	Aggregate Base Course Layer for Road Works-[Road 09] -[SW-1]	21	31-Mar-27	24-Apr-27	24-Jun-26	18-Jul-26	0%	365,523.55	365,523.55
Pavement Works		12	25-Aug-26 A	31-Jul-27	09-Sep-26	24-Sep-26	50%	213,779.51	213,779.51
CO-R09.S01-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09] -[SW-1]	12	25-Aug-26 A	31-Jul-27	09-Sep-26	24-Sep-26	50%	213,779.51	213,779.51
SW_2		495	10-Nov-25 A	07-Aug-27	21-Jul-25	01-Oct-26	28.36%	2,906,012.84	2,771,666.94
Sewage Network		279	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	92.79%	289,558.47	155,212.57
Main Line Sections		175	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	94.44%	284,501.38	150,155.47
CO-R09.S02-SW-10	Trench Excavation and Bedding Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	10-Nov-25 A	10-Oct-26	21-Jul-25	03-Aug-25	95%	63,214.65	21,071.55
CO-R09.S02-SW-	Pipes Laying Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	15-Feb-26 A	18-Oct-26	04-Aug-25	17-Aug-25	95%	189,643.95	110,625.64
CO-R09.S02-SW-13	Trench Backfilling and Compaction Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	02-May-26 A	26-Oct-26	18-Aug-25	31-Aug-25	90%	31,642.78	18,458.29
Manholes		1	11-Oct-26	11-Oct-26	25-Aug-25	25-Aug-25	0%	5,057.09	5,057.09
CO-R09.S02-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09]-[SW-2]	1	11-Oct-26	11-Oct-26	25-Aug-25	25-Aug-25	0%	5,057.09	5,057.09

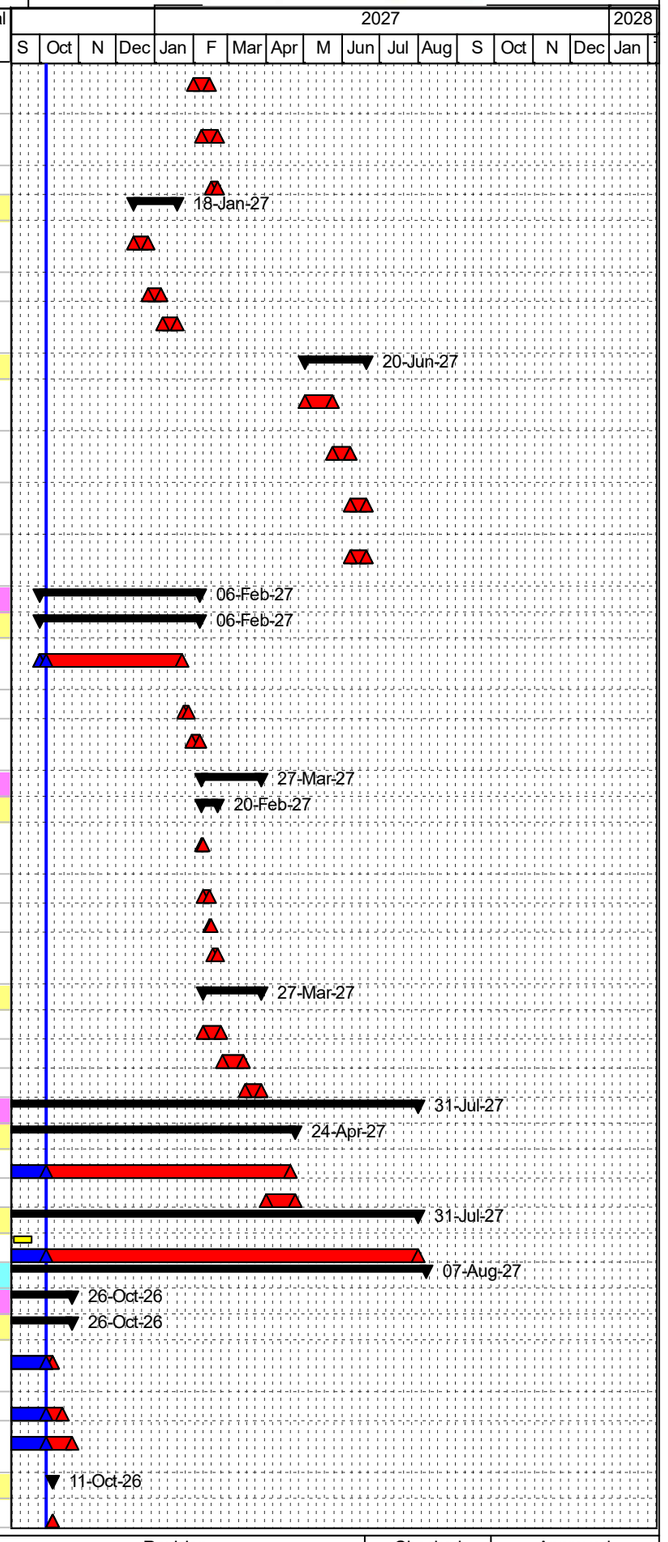

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Storm Drainage Network		86	22-Jan-26 A	29-Nov-26	16-Oct-25	20-Dec-25	65.95%	339,564.90	339,564.90
Main Line Sections		15	22-Jan-26 A	16-Nov-26	16-Oct-25	02-Nov-25	90%	51,701.44	51,701.44
CO-R09.S02-SD-13	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network-[Road 09]-[SW-2]	15	22-Jan-26 A	16-Nov-26	16-Oct-25	02-Nov-25	90%	51,701.44	51,701.44
Manholes		2	31-Oct-26	01-Nov-26	23-Oct-25	25-Oct-25	0%	38,388.86	38,388.86
CO-R09.S02-SD-2	Testing Works for Manholes of Storm Drainage Network-[Road 09]-[SW-2]	2	31-Oct-26	01-Nov-26	23-Oct-25	25-Oct-25	0%	38,388.86	38,388.86
Catch Basin Sections		84	24-Jun-26 A	29-Nov-26	03-Nov-25	20-Dec-25	71.11%	249,474.61	249,474.61
CO-R09.S02-SD-14	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	6	24-Jun-26 A	08-Nov-26	03-Nov-25	09-Nov-25	80%	41,579.10	41,579.10
CO-R09.S02-SD-15	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	7	25-Jun-26 A	16-Nov-26	30-Nov-25	07-Dec-25	80%	124,737.30	124,737.30
CO-R09.S02-SD-17	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	7	28-Jun-26 A	29-Nov-26	13-Dec-25	20-Dec-25	80%	55,438.80	55,438.80
CO-R09.S02-SD-1	Testing Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	4	17-Nov-26	21-Nov-26	08-Dec-25	11-Dec-25	0%	27,719.40	27,719.40
Potable Water Network		100	27-Jun-26 A	17-Jan-27	03-Nov-25	29-Dec-25	51.92%	432,458.35	432,458.35
Main Line Sections		53	27-Jun-26 A	17-Jan-27	03-Nov-25	29-Dec-25	88.08%	254,907.68	254,907.68
CO-R09.S02-PW-10	Trench Excavation and Bedding Works for Main Lines of Potable Water Network-[Road 09]-[SW-2]	7	27-Jun-26 A	24-Nov-26	03-Nov-25	10-Nov-25	95%	78,463.98	78,463.98
CO-R09.S02-PW-11	Pipes Laying and accessories for Main Lines of Potable Water Network-[Road 09]-[SW-2]	8	30-Jun-26 A	07-Jan-27	10-Dec-25	18-Dec-25	85%	96,160.67	96,160.67
CO-R09.S02-PW-13	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network-[Road 09]-[SW-2]	8	01-Jul-26 A	17-Jan-27	21-Dec-25	29-Dec-25	85%	80,283.03	80,283.03
Valve Chamber		6	25-Nov-26	01-Dec-26	11-Nov-25	17-Nov-25	0%	63,935.42	63,935.42
CO-R09.S02-PW-21	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 09]-[SW-2]	6	25-Nov-26	01-Dec-26	11-Nov-25	17-Nov-25	0%	63,935.42	63,935.42
Fire Hydrant		16	25-Nov-26	13-Dec-26	11-Nov-25	29-Dec-25	0%	113,615.25	113,615.25
CO-R09.S02-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	25-Nov-26	30-Nov-26	11-Nov-25	16-Nov-25	0%	17,042.29	17,042.29
CO-R09.S02-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 09]-[SW-2]	6	01-Dec-26	07-Dec-26	17-Dec-25	23-Dec-25	0%	73,849.91	73,849.91
CO-R09.S02-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	08-Dec-26	13-Dec-26	24-Dec-25	29-Dec-25	0%	22,723.05	22,723.05
Street Lighting Network		132	18-Jan-27	01-Jul-27	30-Dec-25	25-Aug-26	0%	573,622.71	573,622.71
Lighting Poles Works		60	18-Jan-27	01-Apr-27	30-Dec-25	01-Jun-26	0%	140,446.74	140,446.74
CO-R09.S02-SL-10	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	9	18-Jan-27	27-Jan-27	30-Dec-25	08-Jan-26	0%	4,663.50	4,663.50
CO-R09.S02-SL-11	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 09]-[SW-2]	9	28-Jan-27	07-Feb-27	10-Jan-26	19-Jan-26	0%	17,826.69	17,826.69
CO-R09.S02-SL-12	Installation Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	9	08-Feb-27	17-Feb-27	08-Feb-26	17-Feb-26	0%	51,298.52	51,298.52
CO-R09.S02-SL-21	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	20	18-Feb-27	17-Mar-27	26-Apr-26	18-May-26	0%	18,654.01	18,654.01
CO-R09.S02-SL-13	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 09]-[SW-2]	17	14-Mar-27	01-Apr-27	09-May-26	01-Jun-26	0%	29,350.02	29,350.02
CO-R09.S02-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	8	18-Mar-27	27-Mar-27	19-May-26	01-Jun-26	0%	18,654.01	18,654.01
Cabling Works		30	18-Feb-27	29-Mar-27	18-Feb-26	28-Mar-26	0%	94,451.91	94,451.91
CO-R09.S02-SL-14	Trench Excavation and Bedding Works for Street Lighting Network-[Road 09]-[SW-2]	10	18-Feb-27	02-Mar-27	18-Feb-26	01-Mar-26	0%	0.00	0.00
CO-R09.S02-SL-1	Cable Laying Works for Street Lighting Network-[Road 09]-[SW-2]	10	03-Mar-27	17-Mar-27	02-Mar-26	12-Mar-26	0%	87,705.35	87,705.35
CO-R09.S02-SL-16	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 09]-[SW-2]	10	18-Mar-27	29-Mar-27	14-Mar-26	28-Mar-26	0%	6,746.57	6,746.57
Distrubution Panel Boards		48	01-May-27	01-Jul-27	30-Jun-26	25-Aug-26	0%	338,724.06	338,724.06
CO-R09.S02-SL-17	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 09]-[SW-2]	10	01-May-27	11-May-27	30-Jun-26	11-Jul-26	0%	43,293.39	43,293.39
CO-R09.S02-SL-18	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 09]-[SW-2]	10	12-May-27	29-May-27	12-Jul-26	22-Jul-26	0%	48,506.22	48,506.22

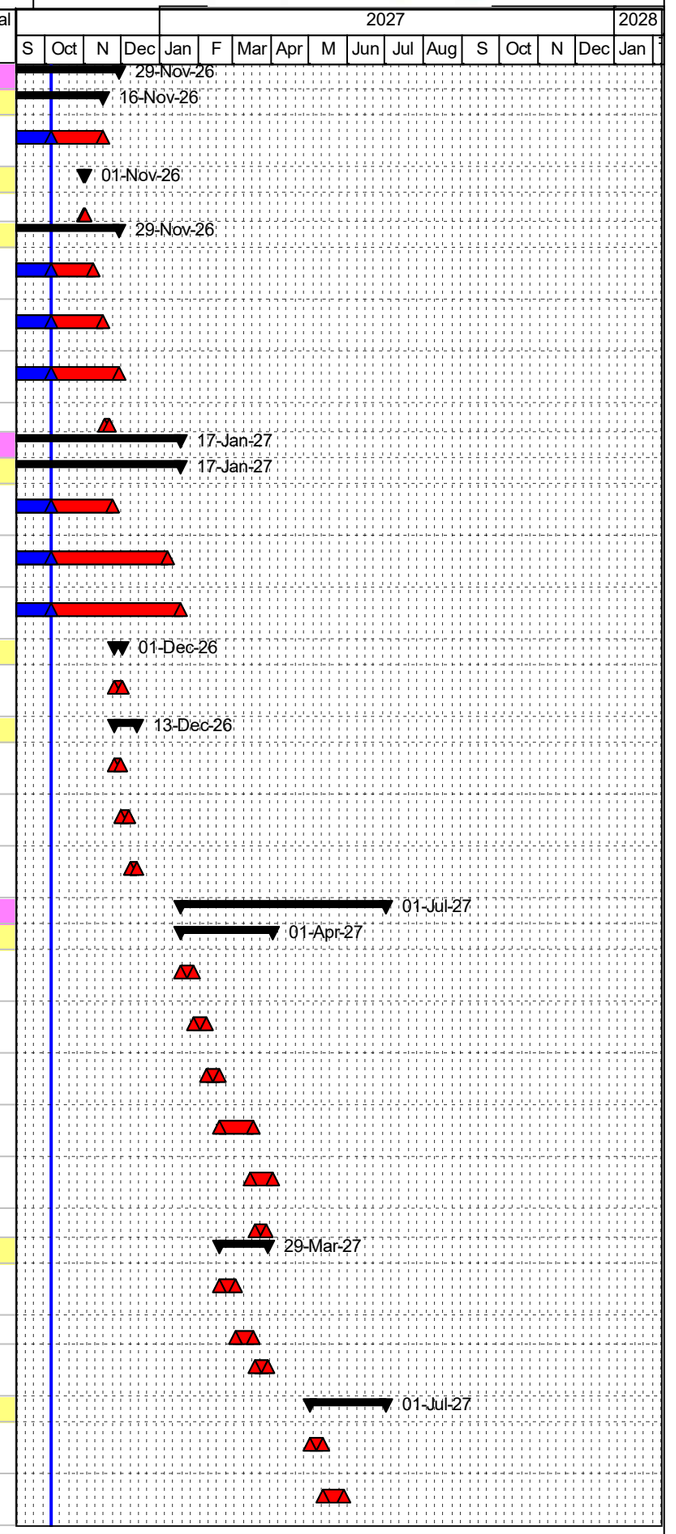

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09.S02-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 09]-[SW-2]	10	30-May-27	09-Jun-27	23-Jul-26	03-Aug-26	0%	177,856.16	177,856.16
CO-R09.S02-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 09]-[SW-2]	18	10-Jun-27	01-Jul-27	04-Aug-26	25-Aug-26	0%	69,068.29	69,068.29
Telecom Network		47	21-Feb-27	20-Apr-27	17-May-26	14-Jul-26	0%	166,741.56	166,741.56
Ducts Works		24	21-Feb-27	24-Mar-27	17-May-26	17-Jun-26	0%	132,124.00	132,124.00
CO-R09.S02-TE-10(	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 09]-[SW-2]	3	21-Feb-27	24-Feb-27	17-May-26	19-May-26	0%	13,266.00	13,266.00
CO-R09.S02-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 09]-[SW-2]	7	25-Feb-27	04-Mar-27	20-May-26	01-Jun-26	0%	79,227.50	79,227.50
CO-R09.S02-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 09]-[SW-2]	7	06-Mar-27	16-Mar-27	02-Jun-26	09-Jun-26	0%	13,266.00	13,266.00
CO-R09.S02-TE-13(	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 09]-[SW-2]	7	17-Mar-27	24-Mar-27	10-Jun-26	17-Jun-26	0%	26,364.50	26,364.50
Manholes Works		21	28-Mar-27	20-Apr-27	21-Jun-26	14-Jul-26	0%	34,617.56	34,617.56
CO-R09.S02-TE-1	Excavation Works for Manholes of Telecom Network-[Road 09]-[SW-2]	7	28-Mar-27	04-Apr-27	21-Jun-26	28-Jun-26	0%	6,300.28	6,300.28
CO-R09.S02-TE-1	Installation Works for Manholes of Telecom Network-[Road 09]-[SW-2]	7	05-Apr-27	12-Apr-27	29-Jun-26	06-Jul-26	0%	22,017.00	22,017.00
CO-R09.S02-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 09]-[SW-2]	7	13-Apr-27	20-Apr-27	07-Jul-26	14-Jul-26	0%	6,300.28	6,300.28
Road Works		55	25-Aug-26 A	07-Aug-27	15-Jul-26	01-Oct-26	9.68%	1,104,066.86	1,104,066.86
Pre-Bituminous Construction		21	21-Apr-27	20-May-27	15-Jul-26	08-Aug-26	0%	890,287.34	890,287.34
CO-R09.S02-RD-I	Capping and Subgrade Layer for Road Works-[Road 09]-[SW-2]	12	21-Apr-27	04-May-27	15-Jul-26	28-Jul-26	0%	524,763.79	524,763.79
CO-R09.S02-RD-I	Aggregate Base Course Layer for Road Works-[Road 09]-[SW-2]	18	25-Apr-27	20-May-27	19-Jul-26	08-Aug-26	0%	365,523.55	365,523.55
Pavement Works		18	25-Aug-26 A	07-Aug-27	09-Sep-26	01-Oct-26	50%	213,779.51	213,779.51
CO-R09.S02-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09]-[SW-2]	18	25-Aug-26 A	07-Aug-27	09-Sep-26	01-Oct-26	50%	213,779.51	213,779.51
Road 10 Local 2 (2352 LM)		256	17-Jun-26 A	21-Jun-27	23-Jul-25	01-Oct-26	19.22%	5,311,545.72	5,243,242.80
SW-3		195	25-Aug-26 A	19-Jun-27	09-Sep-25	29-Sep-26	17.73%	2,595,766.80	2,595,766.80
SW_3-East		195	25-Aug-26 A	19-Jun-27	09-Sep-25	29-Sep-26	17.44%	1,407,276.22	1,407,276.22
Storm Drainage Network		10	15-Sep-26 A	17-Oct-26	09-Sep-25	15-Oct-25	90%	34,250.86	34,250.86
Manholes		1	15-Sep-26 A	06-Oct-26	09-Sep-25	09-Sep-25	90%	20,352.09	20,352.09
CO-R10.S03-ES-	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-3]	1	15-Sep-26 A	06-Oct-26	09-Sep-25	09-Sep-25	90%	20,352.09	20,352.09
Catch Basin Sections		10	15-Sep-26 A	17-Oct-26	05-Oct-25	15-Oct-25	90%	13,898.77	13,898.77
CO-R10.S03-ES-	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-3]	10	15-Sep-26 A	17-Oct-26	05-Oct-25	15-Oct-25	90%	13,898.77	13,898.77
Potable Water Network		42	06-Oct-26	23-Nov-26	15-Oct-25	04-Nov-25	0%	138,828.57	138,828.57
Valve Chamber		16	05-Nov-26	23-Nov-26	15-Oct-25	02-Nov-25	0%	82,020.94	82,020.94
CO-R10.S03-ES-P	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	05-Nov-26	05-Nov-26	15-Oct-25	15-Oct-25	0%	1,160.87	1,160.87
CO-R10.S03-ES-P	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	07-Nov-26	09-Nov-26	16-Oct-25	19-Oct-25	0%	6,528.67	6,528.67
CO-R10.S03-ES-P	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	6	10-Nov-26	16-Nov-26	20-Oct-25	26-Oct-25	0%	15,233.56	15,233.56
CO-R10.S03-ES-P	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	2	17-Nov-26	18-Nov-26	27-Oct-25	28-Oct-25	0%	8,704.89	8,704.89
CO-R10.S03-ES-P	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	19-Nov-26	19-Nov-26	29-Oct-25	29-Oct-25	0%	41,688.07	41,688.07
CO-R10.S03-ES-P	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	21-Nov-26	23-Nov-26	30-Oct-25	02-Nov-25	0%	8,704.89	8,704.89
Fire Hydrant		15	06-Oct-26	22-Oct-26	19-Oct-25	04-Nov-25	0%	56,807.63	56,807.63
CO-R10.S03-ES-P	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	06-Oct-26	12-Oct-26	19-Oct-25	25-Oct-25	0%	8,521.14	8,521.14
CO-R10.S03-ES-P	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	26-Oct-25	01-Nov-25	0%	36,924.96	36,924.96
CO-R10.S03-ES-P	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	17-Oct-26	22-Oct-26	29-Oct-25	04-Nov-25	0%	11,361.53	11,361.53
Street Lighting Network		120	06-Oct-26	23-Feb-27	02-Dec-25	29-Jun-26	0%	398,748.28	398,748.28
Lighting Poles Works		33	06-Oct-26	12-Nov-26	02-Dec-25	16-Feb-26	0%	68,790.24	68,790.24
CO-R10.S03-ES-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	06-Oct-26	19-Oct-26	02-Dec-25	15-Dec-25	0%	2,284.16	2,284.16

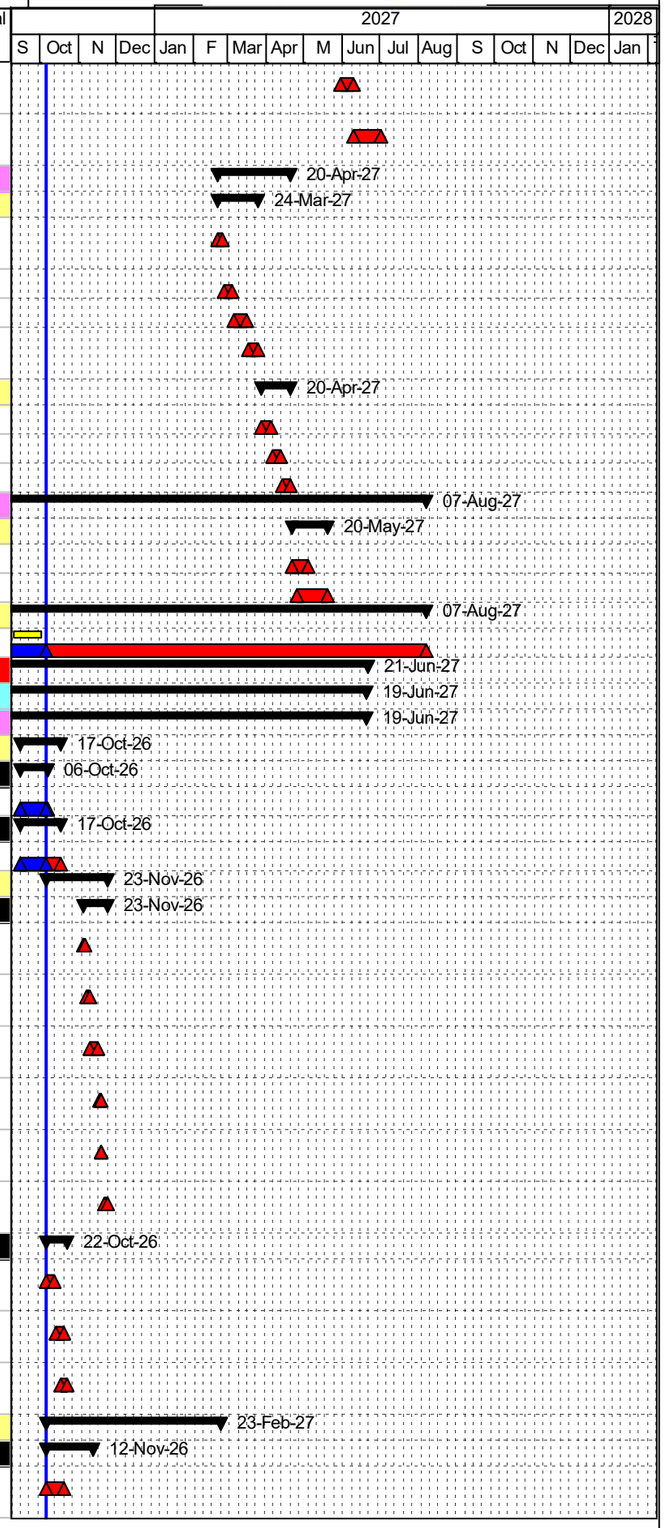

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S03-ES-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-3]	12	12-Oct-26	25-Oct-26	08-Dec-25	21-Dec-25	0%	8,731.44	8,731.44
CO-R10.S03-ES-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	18-Oct-26	07-Nov-26	14-Dec-25	03-Jan-26	0%	25,125.80	25,125.80
CO-R10.S03-ES-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-3]	18	24-Oct-26	12-Nov-26	26-Jan-26	16-Feb-26	0%	14,375.52	14,375.52
CO-R10.S03-ES-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	25-Oct-26	07-Nov-26	27-Jan-26	10-Feb-26	0%	9,136.66	9,136.66
CO-R10.S03-ES-	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	5	08-Nov-26	12-Nov-26	10-Feb-26	16-Feb-26	0%	9,136.66	9,136.66
Cabling Works		30	08-Nov-26	12-Dec-26	04-Jan-26	07-Feb-26	0%	47,398.36	47,398.36
CO-R10.S03-ES-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-3]	10	08-Nov-26	18-Nov-26	04-Jan-26	14-Jan-26	0%	0.00	0.00
CO-R10.S03-ES-	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-3]	10	19-Nov-26	30-Nov-26	15-Jan-26	26-Jan-26	0%	44,012.74	44,012.74
CO-R10.S03-ES-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-3]	10	01-Dec-26	12-Dec-26	27-Jan-26	07-Feb-26	0%	3,385.62	3,385.62
Distrubution Panel Boards		21	30-Jan-27	23-Feb-27	06-Jun-26	29-Jun-26	0%	282,559.68	282,559.68
CO-R10.S03-ES-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	30-Jan-27	11-Feb-27	06-Jun-26	18-Jun-26	0%	21,646.70	21,646.70
CO-R10.S03-ES-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-3]	12	06-Feb-27	18-Feb-27	13-Jun-26	25-Jun-26	0%	34,550.61	34,550.61
CO-R10.S03-ES-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-3]	12	06-Feb-27	18-Feb-27	13-Jun-26	25-Jun-26	0%	48,506.22	48,506.22
CO-R10.S03-ES-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	09-Feb-27	23-Feb-27	16-Jun-26	29-Jun-26	0%	177,856.16	177,856.16
Telecom Network		28	01-Dec-26	02-Jan-27	27-Jan-26	28-Feb-26	0%	80,544.72	80,544.72
Ducts Works		28	01-Dec-26	02-Jan-27	27-Jan-26	28-Feb-26	0%	66,430.50	66,430.50
CO-R10.S03-ES-TI	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	01-Dec-26	08-Dec-26	27-Jan-26	03-Feb-26	0%	6,700.00	6,700.00
CO-R10.S03-ES-	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	09-Dec-26	16-Dec-26	04-Feb-26	11-Feb-26	0%	39,764.50	39,764.50
CO-R10.S03-ES-	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-3]	7	17-Dec-26	24-Dec-26	12-Feb-26	19-Feb-26	0%	6,700.00	6,700.00
CO-R10.S03-ES-TI	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	26-Dec-26	02-Jan-27	21-Feb-26	28-Feb-26	0%	13,266.00	13,266.00
Manholes Works		21	09-Dec-26	02-Jan-27	04-Feb-26	28-Feb-26	0%	14,114.22	14,114.22
CO-R10.S03-ES-	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	09-Dec-26	16-Dec-26	04-Feb-26	11-Feb-26	0%	2,199.61	2,199.61
CO-R10.S03-ES-	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	17-Dec-26	24-Dec-26	12-Feb-26	19-Feb-26	0%	9,715.00	9,715.00
CO-R10.S03-ES-	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	26-Dec-26	02-Jan-27	21-Feb-26	28-Feb-26	0%	2,199.61	2,199.61
Medium Voltage Network		24	09-Sep-26 A	25-Jan-27	24-Feb-26	26-Mar-26	80%	201,322.52	201,322.52
Cabling Works		24	09-Sep-26 A	25-Jan-27	24-Feb-26	26-Mar-26	80%	201,322.52	201,322.52
CO-R10.S03-ES-M	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 10]-[SW-3]	18	09-Sep-26 A	18-Jan-27	24-Feb-26	16-Mar-26	80%	23,183.87	23,183.87
CO-R10.S03-ES-	Cable Laying Works for Medium Voltage Network-[Road 10]-[SW-3]	18	13-Sep-26 A	21-Jan-27	28-Feb-26	19-Mar-26	80%	124,697.05	124,697.05
CO-R10.S03-ES-M	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 10]-[SW-3]	18	16-Sep-26 A	25-Jan-27	03-Mar-26	26-Mar-26	80%	53,441.59	53,441.59
Road Works		97	25-Aug-26 A	19-Jun-27	07-Mar-26	29-Sep-26	9.68%	553,581.27	553,581.27
Pre-Bituminous Construction		21	09-Jan-27	01-Feb-27	07-Mar-26	02-Apr-26	0%	446,397.22	446,397.22
CO-R10.S03-ES-	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-3]	18	09-Jan-27	28-Jan-27	07-Mar-26	30-Mar-26	0%	263,120.65	263,120.65
CO-R10.S03-ES-	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-3]	18	12-Jan-27	01-Feb-27	10-Mar-26	02-Apr-26	0%	183,276.57	183,276.57
Pavement Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	50%	107,184.05	107,184.05
CO-R10.S03-ES-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	50%	107,184.05	107,184.05
SW_3-West		178	25-Aug-26 A	19-Jun-27	07-Dec-25	29-Sep-26	18.06%	1,188,490.57	1,188,490.57
Storm Drainage Network		10	06-Oct-26	17-Oct-26	07-Dec-25	11-Jan-26	0%	38,636.01	38,636.01
Manholes		1	06-Oct-26	06-Oct-26	07-Dec-25	07-Dec-25	0%	24,737.24	24,737.24
CO-R10.S03-WE	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-3]	1	06-Oct-26	06-Oct-26	07-Dec-25	07-Dec-25	0%	24,737.24	24,737.24
Catch Basin Sections		10	06-Oct-26	17-Oct-26	31-Dec-25	11-Jan-26	0%	13,898.77	13,898.77
CO-R10.S03-WE	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-3]	10	06-Oct-26	17-Oct-26	31-Dec-25	11-Jan-26	0%	13,898.77	13,898.77

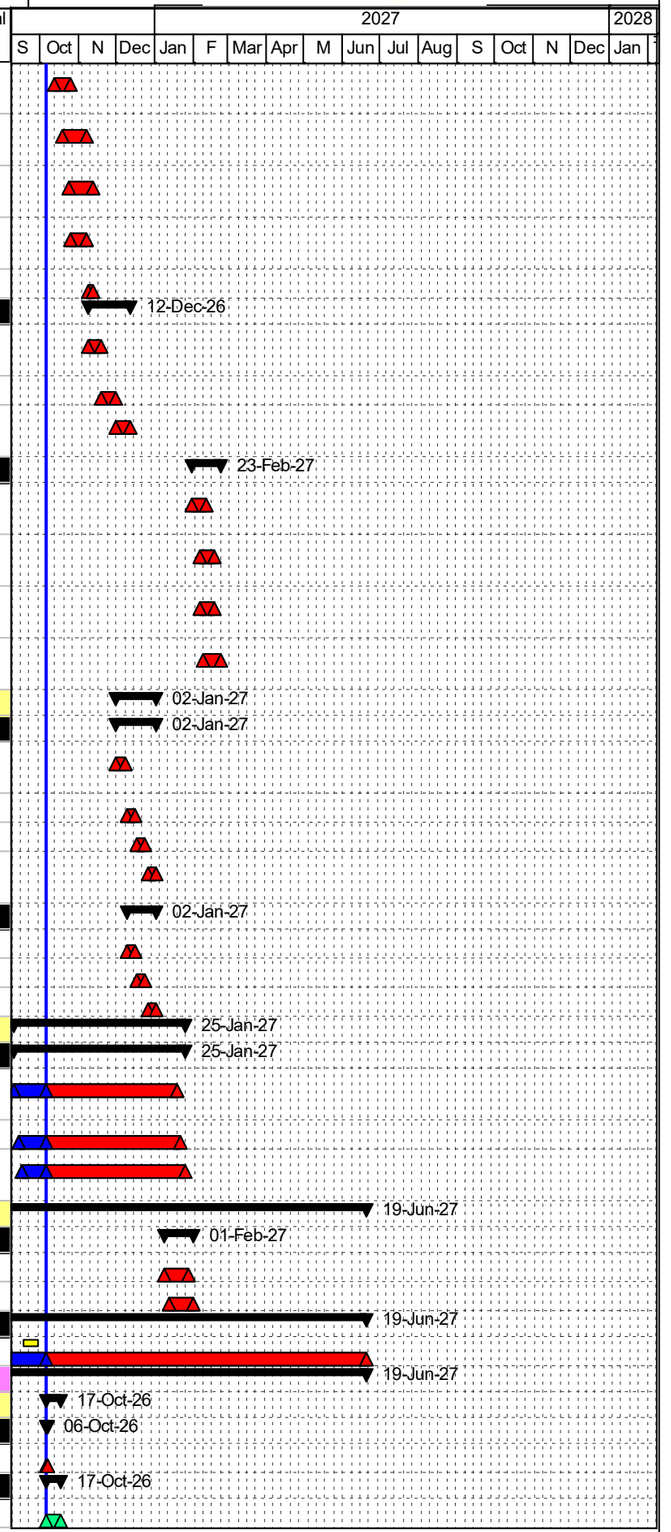

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Potable Water Network		16	06-Oct-26	24-Oct-26	05-Jan-26	25-Jan-26	0%	142,020.14	142,020.14
Valve Chamber		16	06-Oct-26	24-Oct-26	05-Jan-26	22-Jan-26	0%	85,212.52	85,212.52
CO-R10.S03-WE-F	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	06-Oct-26	06-Oct-26	05-Jan-26	05-Jan-26	0%	4,352.45	4,352.45
CO-R10.S03-WE-F	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	07-Oct-26	10-Oct-26	06-Jan-26	08-Jan-26	0%	6,528.67	6,528.67
CO-R10.S03-WE-F	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	6	11-Oct-26	17-Oct-26	10-Jan-26	15-Jan-26	0%	15,233.56	15,233.56
CO-R10.S03-WE-F	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	2	18-Oct-26	19-Oct-26	17-Jan-26	18-Jan-26	0%	8,704.89	8,704.89
CO-R10.S03-WE-F	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	20-Oct-26	20-Oct-26	19-Jan-26	19-Jan-26	0%	41,688.07	41,688.07
CO-R10.S03-WE-F	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	21-Oct-26	24-Oct-26	20-Jan-26	22-Jan-26	0%	8,704.89	8,704.89
Fire Hydrant		15	06-Oct-26	22-Oct-26	08-Jan-26	25-Jan-26	0%	56,807.63	56,807.63
CO-R10.S03-WE-F	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	06-Oct-26	12-Oct-26	08-Jan-26	14-Jan-26	0%	8,521.14	8,521.14
CO-R10.S03-WE-F	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	15-Jan-26	21-Jan-26	0%	36,924.96	36,924.96
CO-R10.S03-WE-F	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	17-Oct-26	22-Oct-26	19-Jan-26	25-Jan-26	0%	11,361.53	11,361.53
Street Lighting Network		120	06-Oct-26	23-Feb-27	22-Feb-26	29-Jun-26	0%	172,385.90	172,385.90
Lighting Poles Works		33	06-Oct-26	12-Nov-26	22-Feb-26	04-Apr-26	0%	68,790.24	68,790.24
CO-R10.S03-WE-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	06-Oct-26	19-Oct-26	22-Feb-26	07-Mar-26	0%	2,284.16	2,284.16
CO-R10.S03-WE-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-3]	12	12-Oct-26	25-Oct-26	28-Feb-26	12-Mar-26	0%	8,731.44	8,731.44
CO-R10.S03-WE-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	18-Oct-26	07-Nov-26	05-Mar-26	29-Mar-26	0%	25,125.80	25,125.80
CO-R10.S03-WE-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-3]	18	24-Oct-26	12-Nov-26	11-Mar-26	04-Apr-26	0%	14,375.52	14,375.52
CO-R10.S03-WE-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	25-Oct-26	07-Nov-26	12-Mar-26	29-Mar-26	0%	9,136.66	9,136.66
CO-R10.S03-WE	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	5	08-Nov-26	12-Nov-26	30-Mar-26	04-Apr-26	0%	9,136.66	9,136.66
Cabling Works		30	08-Nov-26	12-Dec-26	30-Mar-26	03-May-26	0%	47,398.36	47,398.36
CO-R10.S03-WE-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-3]	10	08-Nov-26	18-Nov-26	30-Mar-26	09-Apr-26	0%	0.00	0.00
CO-R10.S03-WE	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-3]	10	19-Nov-26	30-Nov-26	11-Apr-26	21-Apr-26	0%	44,012.74	44,012.74
CO-R10.S03-WE-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-3]	10	01-Dec-26	12-Dec-26	22-Apr-26	03-May-26	0%	3,385.62	3,385.62
Distrubution Panel Boards		21	30-Jan-27	23-Feb-27	06-Jun-26	29-Jun-26	0%	56,197.30	56,197.30
CO-R10.S03-WE-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	30-Jan-27	11-Feb-27	06-Jun-26	18-Jun-26	0%	21,646.70	21,646.70
CO-R10.S03-WE-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-3]	12	06-Feb-27	18-Feb-27	13-Jun-26	25-Jun-26	0%	0.00	0.00
CO-R10.S03-WE-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-3]	12	06-Feb-27	18-Feb-27	13-Jun-26	25-Jun-26	0%	34,550.61	34,550.61
CO-R10.S03-WE-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	09-Feb-27	23-Feb-27	16-Jun-26	29-Jun-26	0%	0.00	0.00
Telecom Network		24	04-Mar-27	04-Apr-27	17-Jun-26	14-Jul-26	0%	80,544.72	80,544.72
Ducts Works		24	04-Mar-27	04-Apr-27	17-Jun-26	14-Jul-26	0%	66,430.50	66,430.50
CO-R10.S03-WE-T	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-3]	3	04-Mar-27	07-Mar-27	17-Jun-26	20-Jun-26	0%	6,700.00	6,700.00
CO-R10.S03-WE	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	08-Mar-27	18-Mar-27	21-Jun-26	28-Jun-26	0%	39,764.50	39,764.50
CO-R10.S03-WE	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-3]	7	20-Mar-27	27-Mar-27	29-Jun-26	06-Jul-26	0%	6,700.00	6,700.00

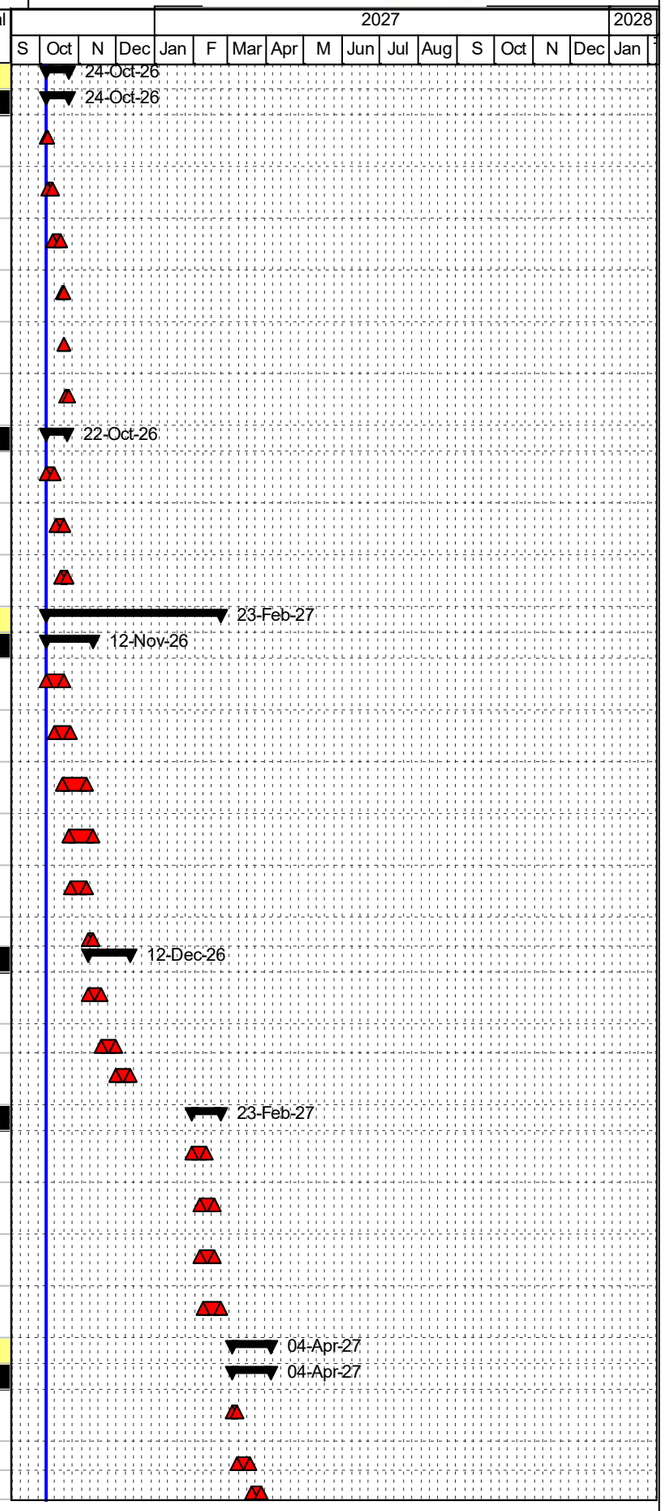

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S03-WE-T	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	13,266.00	13,266.00
Manholes Works		21	08-Mar-27	04-Apr-27	21-Jun-26	14-Jul-26	0%	14,114.22	14,114.22
CO-R10.S03-WE	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	08-Mar-27	18-Mar-27	21-Jun-26	28-Jun-26	0%	2,199.61	2,199.61
CO-R10.S03-WE	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	20-Mar-27	27-Mar-27	29-Jun-26	06-Jul-26	0%	9,715.00	9,715.00
CO-R10.S03-WE	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	2,199.61	2,199.61
Medium Voltage Network		16	22-Sep-26 A	18-Apr-27	11-Jul-26	28-Jul-26	80%	201,322.52	201,322.52
Cabling Works		16	22-Sep-26 A	18-Apr-27	11-Jul-26	28-Jul-26	80%	201,322.52	201,322.52
CO-R10.S03-WE-M	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 10]-[SW-3]	10	22-Sep-26 A	11-Apr-27	11-Jul-26	21-Jul-26	80%	23,183.87	23,183.87
CO-R10.S03-WE	Cable Laying Works for Medium Voltage Network-[Road 10]-[SW-3]	10	22-Sep-26 A	14-Apr-27	14-Jul-26	25-Jul-26	80%	124,697.05	124,697.05
CO-R10.S03-WE-M	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 10]-[SW-3]	10	22-Sep-26 A	18-Apr-27	18-Jul-26	28-Jul-26	80%	53,441.59	53,441.59
Road Works		24	25-Aug-26 A	19-Jun-27	21-Jul-26	29-Sep-26	9.68%	553,581.27	553,581.27
Pre-Bituminous Construction		21	08-Apr-27	02-May-27	21-Jul-26	13-Aug-26	0%	446,397.22	446,397.22
CO-R10.S03-WE	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-3]	12	08-Apr-27	21-Apr-27	21-Jul-26	03-Aug-26	0%	263,120.65	263,120.65
CO-R10.S03-WE	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-3]	18	12-Apr-27	02-May-27	25-Jul-26	13-Aug-26	0%	183,276.57	183,276.57
Pavement Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	50%	107,184.05	107,184.05
CO-R10.S03-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	50%	107,184.05	107,184.05
SW-4		256	17-Jun-26 A	21-Jun-27	23-Jul-25	01-Oct-26	20.64%	2,715,778.92	2,647,476.00
SW_4-East		243	21-Jun-26 A	19-Jun-27	23-Jul-25	29-Sep-26	19.39%	1,264,470.53	1,264,470.53
Sewage Network		1	06-Oct-26	06-Oct-26	23-Jul-25	23-Jul-25	0%	8,813.28	8,813.28
Manholes		1	06-Oct-26	06-Oct-26	23-Jul-25	23-Jul-25	0%	8,813.28	8,813.28
CO-R10.S04-ES-	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	23-Jul-25	23-Jul-25	0%	8,813.28	8,813.28
Storm Drainage Network		10	06-Oct-26	17-Oct-26	18-Dec-25	22-Jan-26	0%	34,250.86	34,250.86
Manholes		1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	0%	20,352.09	20,352.09
CO-R10.S04-ES-	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	0%	20,352.09	20,352.09
Catch Basin Sections		10	06-Oct-26	17-Oct-26	12-Jan-26	22-Jan-26	0%	13,898.77	13,898.77
CO-R10.S04-ES-	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	06-Oct-26	17-Oct-26	12-Jan-26	22-Jan-26	0%	13,898.77	13,898.77
Potable Water Network		141	21-Jun-26 A	02-Jan-27	15-Jan-26	11-Feb-26	42.42%	451,664.43	451,664.43
Valve Chamber		81	21-Jun-26 A	24-Oct-26	15-Jan-26	02-Feb-26	42.42%	451,664.43	451,664.43
CO-R10.S04-ES-P	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	21-Jun-26 A	20-Oct-26	29-Jan-26	29-Jan-26	60%	319,298.55	319,298.55
CO-R10.S04-ES-P	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	15-Jan-26	15-Jan-26	0%	16,109.01	16,109.01
CO-R10.S04-ES-P	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	07-Oct-26	10-Oct-26	17-Jan-26	19-Jan-26	0%	19,376.15	19,376.15
CO-R10.S04-ES-P	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	6	11-Oct-26	17-Oct-26	20-Jan-26	26-Jan-26	0%	45,211.01	45,211.01
CO-R10.S04-ES-P	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	2	18-Oct-26	19-Oct-26	27-Jan-26	28-Jan-26	0%	25,834.86	25,834.86
CO-R10.S04-ES-P	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	21-Oct-26	24-Oct-26	31-Jan-26	02-Feb-26	0%	25,834.86	25,834.86
Fire Hydrant		21	09-Dec-26	02-Jan-27	19-Jan-26	11-Feb-26	0%	0.00	0.00
CO-R10.S04-ES-P	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	09-Dec-26	16-Dec-26	19-Jan-26	26-Jan-26	0%	0.00	0.00
CO-R10.S04-ES-P	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	17-Dec-26	24-Dec-26	27-Jan-26	03-Feb-26	0%	0.00	0.00
CO-R10.S04-ES-P	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	26-Dec-26	02-Jan-27	04-Feb-26	11-Feb-26	0%	0.00	0.00
Street Lighting Network		77	29-Oct-26	26-Jan-27	10-Mar-26	15-Jun-26	0%	135,615.97	135,615.97
Lighting Poles Works		77	29-Oct-26	26-Jan-27	10-Mar-26	20-Apr-26	0%	68,790.24	68,790.24
CO-R10.S04-ES-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	29-Oct-26	05-Nov-26	10-Mar-26	17-Mar-26	0%	2,284.16	2,284.16

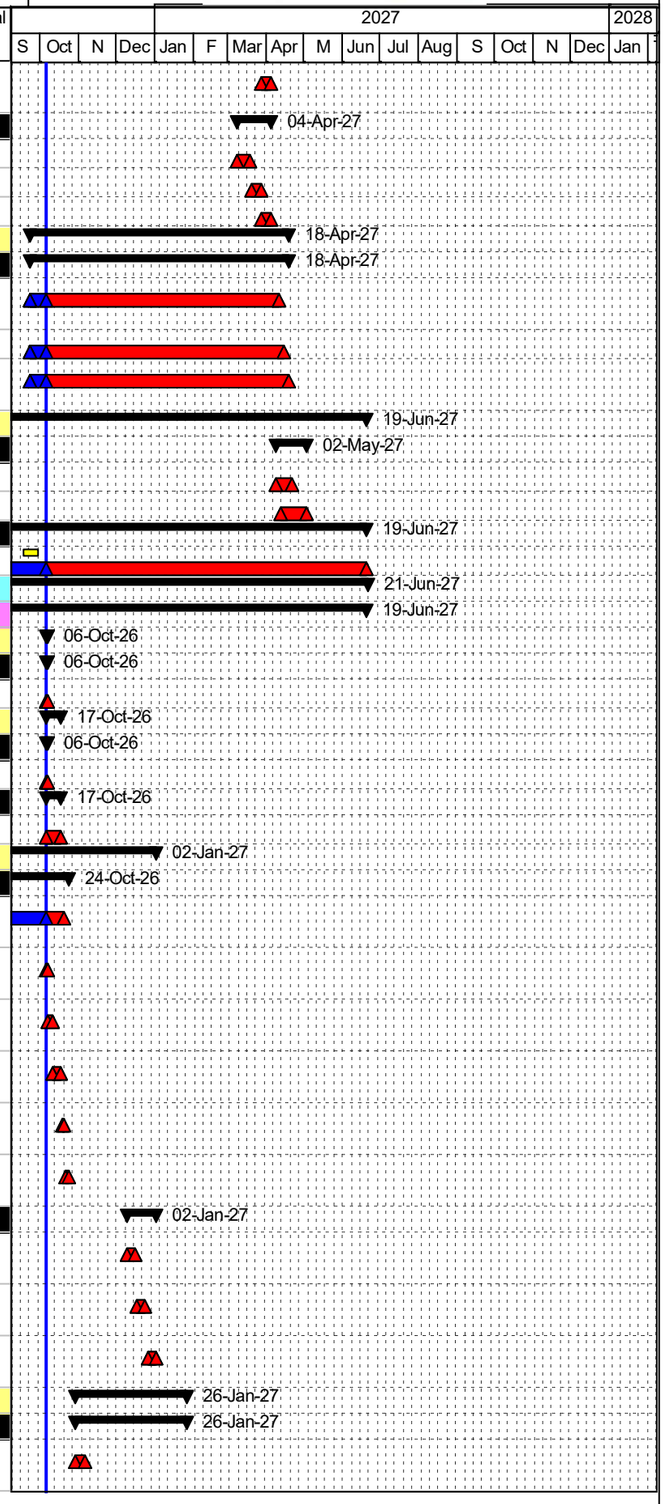

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S04-ES-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-4]	7	04-Nov-26	11-Nov-26	16-Mar-26	26-Mar-26	0%	8,731.44	8,731.44
CO-R10.S04-ES-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	10-Nov-26	17-Nov-26	25-Mar-26	01-Apr-26	0%	25,125.80	25,125.80
CO-R10.S04-ES-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	15	10-Nov-26	26-Nov-26	25-Mar-26	11-Apr-26	0%	9,136.66	9,136.66
CO-R10.S04-ES-	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	28-Nov-26	05-Dec-26	12-Apr-26	19-Apr-26	0%	9,136.66	9,136.66
CO-R10.S04-ES-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-4]	18	06-Jan-27	26-Jan-27	31-Mar-26	20-Apr-26	0%	14,375.52	14,375.52
Cabling Works		21	18-Nov-26	12-Dec-26	02-Apr-26	26-Apr-26	0%	47,398.36	47,398.36
CO-R10.S04-ES-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-4]	7	18-Nov-26	25-Nov-26	02-Apr-26	09-Apr-26	0%	0.00	0.00
CO-R10.S04-ES-	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-4]	7	26-Nov-26	03-Dec-26	11-Apr-26	18-Apr-26	0%	44,012.74	44,012.74
CO-R10.S04-ES-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-4]	7	05-Dec-26	12-Dec-26	19-Apr-26	26-Apr-26	0%	3,385.62	3,385.62
Distrubution Panel Boards		39	13-Dec-26	26-Jan-27	27-Apr-26	15-Jun-26	0%	19,427.37	19,427.37
CO-R10.S04-ES-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	18	13-Dec-26	02-Jan-27	27-Apr-26	17-May-26	0%	0.00	0.00
CO-R10.S04-ES-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-4]	12	23-Dec-26	05-Jan-27	07-May-26	20-May-26	0%	0.00	0.00
CO-R10.S04-ES-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	12	06-Jan-27	19-Jan-27	21-May-26	08-Jun-26	0%	0.00	0.00
CO-R10.S04-ES-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-4]	18	06-Jan-27	26-Jan-27	21-May-26	15-Jun-26	0%	19,427.37	19,427.37
Telecom Network		102	10-Dec-26	12-Apr-27	25-Apr-26	22-Jul-26	0%	80,544.72	80,544.72
Ducts Works		28	10-Dec-26	11-Jan-27	25-Apr-26	31-May-26	0%	66,430.50	66,430.50
CO-R10.S04-ES-TI	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	10-Dec-26	17-Dec-26	25-Apr-26	02-May-26	0%	6,700.00	6,700.00
CO-R10.S04-ES-	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	19-Dec-26	26-Dec-26	03-May-26	10-May-26	0%	39,764.50	39,764.50
CO-R10.S04-ES-	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-4]	7	27-Dec-26	03-Jan-27	11-May-26	18-May-26	0%	6,700.00	6,700.00
CO-R10.S04-ES-TI	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	04-Jan-27	11-Jan-27	19-May-26	31-May-26	0%	13,266.00	13,266.00
Manholes Works		21	20-Mar-27	12-Apr-27	29-Jun-26	22-Jul-26	0%	14,114.22	14,114.22
CO-R10.S04-ES-	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	20-Mar-27	27-Mar-27	29-Jun-26	06-Jul-26	0%	2,199.61	2,199.61
CO-R10.S04-ES-	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	9,715.00	9,715.00
CO-R10.S04-ES-	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	2,199.61	2,199.61
Road Works		20	25-Aug-26 A	19-Jun-27	23-Jul-26	29-Sep-26	9.68%	553,581.27	553,581.27
Pre-Bituminous Construction		17	13-Apr-27	02-May-27	23-Jul-26	11-Aug-26	0%	446,397.22	446,397.22
CO-R10.S04-ES-	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-4]	14	13-Apr-27	28-Apr-27	23-Jul-26	08-Aug-26	0%	263,120.65	263,120.65
CO-R10.S04-ES-	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-4]	12	19-Apr-27	02-May-27	29-Jul-26	11-Aug-26	0%	183,276.57	183,276.57
Pavement Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	50%	107,184.05	107,184.05
CO-R10.S04-ES-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	50%	107,184.05	107,184.05
SW_4-West		256	17-Jun-26 A	21-Jun-27	11-Nov-25	01-Oct-26	21.73%	1,451,308.39	1,383,005.47
Sewage Network		1	06-Oct-26	06-Oct-26	11-Nov-25	11-Nov-25	0%	10,264.33	10,264.33
Manholes		1	06-Oct-26	06-Oct-26	11-Nov-25	11-Nov-25	0%	10,264.33	10,264.33
CO-R10.S04-WE	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	11-Nov-25	11-Nov-25	0%	10,264.33	10,264.33
Storm Drainage Network		88	17-Jun-26 A	19-Oct-26	18-Dec-25	26-Jan-26	47.71%	147,127.45	78,824.53
Manholes		1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	0%	22,037.94	22,037.94
CO-R10.S04-WE	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	0%	22,037.94	22,037.94
Catch Basin Sections		88	17-Jun-26 A	19-Oct-26	28-Dec-25	26-Jan-26	56.11%	125,089.51	56,786.59
CO-R10.S04-WE-S	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	6	17-Jun-26 A	08-Oct-26	28-Dec-25	03-Jan-26	80%	20,848.43	6,949.48
CO-R10.S04-WE-S	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	7	20-Jun-26 A	11-Oct-26	04-Jan-26	11-Jan-26	70%	62,544.75	17,869.93
CO-R10.S04-WE	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	23-Jun-26 A	14-Oct-26	12-Jan-26	22-Jan-26	70%	13,898.77	4,169.63

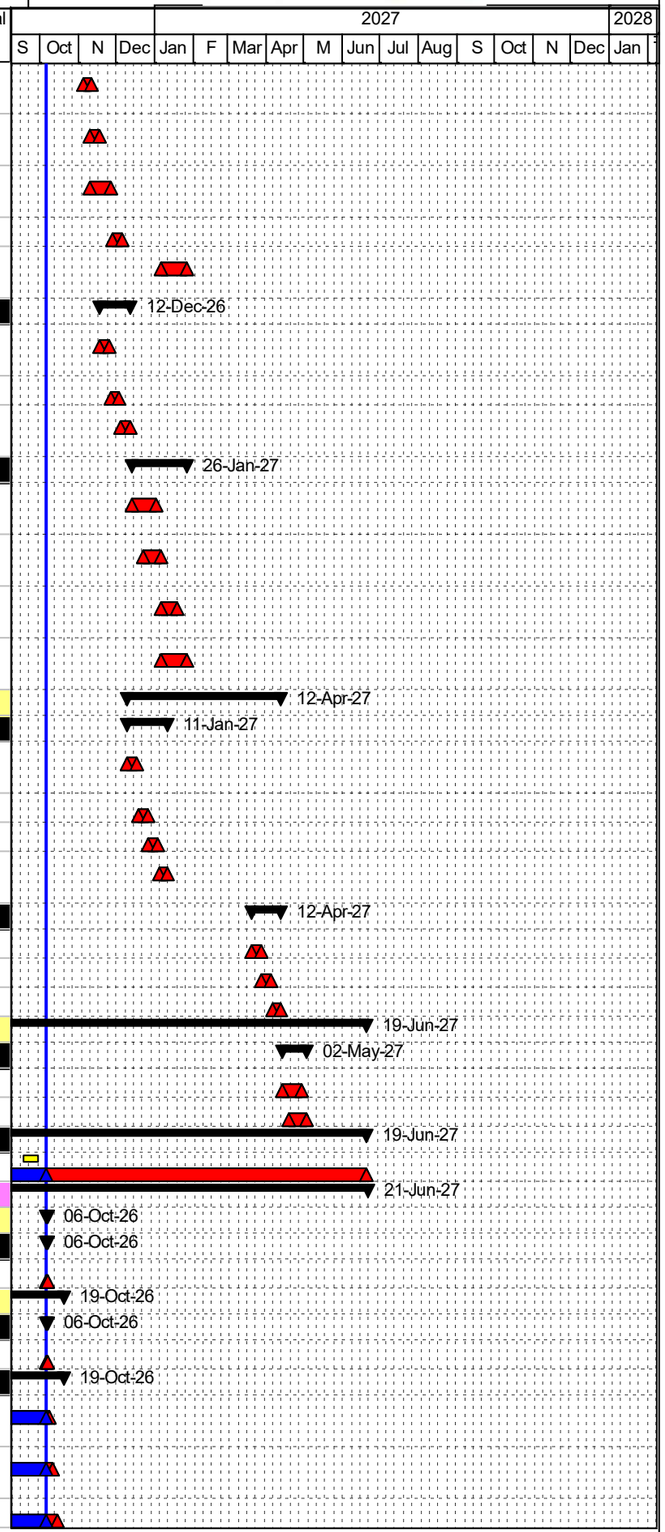

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S04-WE-S	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	7	12-Oct-26	19-Oct-26	19-Jan-26	26-Jan-26	0%	27,797.55	27,797.55
Potable Water Network		141	21-Jun-26 A	02-Jan-27	15-Jan-26	11-Feb-26	47.18%	406,090.05	406,090.05
Valve Chamber		81	21-Jun-26 A	24-Oct-26	15-Jan-26	02-Feb-26	47.18%	406,090.05	406,090.05
CO-R10.S04-WE-F	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	21-Jun-26 A	20-Oct-26	29-Jan-26	29-Jan-26	60%	319,298.55	319,298.55
CO-R10.S04-WE-F	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	15-Jan-26	15-Jan-26	0%	8,679.15	8,679.15
CO-R10.S04-WE-F	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	07-Oct-26	10-Oct-26	17-Jan-26	19-Jan-26	0%	13,018.73	13,018.73
CO-R10.S04-WE-F	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	6	11-Oct-26	17-Oct-26	20-Jan-26	26-Jan-26	0%	30,377.03	30,377.03
CO-R10.S04-WE-F	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	2	18-Oct-26	19-Oct-26	27-Jan-26	28-Jan-26	0%	17,358.30	17,358.30
CO-R10.S04-WE-F	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	21-Oct-26	24-Oct-26	31-Jan-26	02-Feb-26	0%	17,358.30	17,358.30
Fire Hydrant		21	09-Dec-26	02-Jan-27	19-Jan-26	11-Feb-26	0%	0.00	0.00
CO-R10.S04-WE-F	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	09-Dec-26	16-Dec-26	19-Jan-26	26-Jan-26	0%	0.00	0.00
CO-R10.S04-WE-F	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	17-Dec-26	24-Dec-26	27-Jan-26	03-Feb-26	0%	0.00	0.00
CO-R10.S04-WE-F	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	26-Dec-26	02-Jan-27	04-Feb-26	11-Feb-26	0%	0.00	0.00
Irrigation Network		25	06-Oct-26	03-Nov-26	12-Feb-26	08-Mar-26	0%	118,084.60	118,084.60
Main Line Pipes		25	06-Oct-26	03-Nov-26	12-Feb-26	08-Mar-26	0%	118,084.60	118,084.60
CO-R10.S04-WE-I	Trench Excavation and Bedding Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	6	06-Oct-26	12-Oct-26	12-Feb-26	18-Feb-26	0%	21,371.93	21,371.93
CO-R10.S04-WE	Pipes Laying Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	7	13-Oct-26	20-Oct-26	19-Feb-26	26-Feb-26	0%	64,103.07	64,103.07
CO-R10.S04-WE	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-4]	3	26-Oct-26	28-Oct-26	28-Feb-26	02-Mar-26	0%	21,925.75	21,925.75
CO-R10.S04-WE-I	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	5	29-Oct-26	03-Nov-26	03-Mar-26	08-Mar-26	0%	10,683.85	10,683.85
Street Lighting Network		97	04-Nov-26	25-Feb-27	09-Mar-26	07-Jul-26	0%	135,615.97	135,615.97
Lighting Poles Works		72	04-Nov-26	26-Jan-27	09-Mar-26	23-Apr-26	0%	68,790.24	68,790.24
CO-R10.S04-WE-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	10	04-Nov-26	15-Nov-26	09-Mar-26	19-Mar-26	0%	2,284.16	2,284.16
CO-R10.S04-WE-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-4]	10	10-Nov-26	21-Nov-26	15-Mar-26	29-Mar-26	0%	8,731.44	8,731.44
CO-R10.S04-WE-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	18	16-Nov-26	06-Dec-26	24-Mar-26	13-Apr-26	0%	25,125.80	25,125.80
CO-R10.S04-WE-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	15	19-Nov-26	06-Dec-26	30-Mar-26	15-Apr-26	0%	9,136.66	9,136.66
CO-R10.S04-WE	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	07-Dec-26	14-Dec-26	16-Apr-26	23-Apr-26	0%	9,136.66	9,136.66
CO-R10.S04-WE-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-4]	18	06-Jan-27	26-Jan-27	04-Apr-26	23-Apr-26	0%	14,375.52	14,375.52
Cabling Works		30	07-Dec-26	10-Jan-27	14-Apr-26	18-May-26	0%	47,398.36	47,398.36
CO-R10.S04-WE-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-4]	10	07-Dec-26	17-Dec-26	14-Apr-26	25-Apr-26	0%	0.00	0.00
CO-R10.S04-WE	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-4]	10	19-Dec-26	29-Dec-26	26-Apr-26	06-May-26	0%	44,012.74	44,012.74
CO-R10.S04-WE-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-4]	10	30-Dec-26	10-Jan-27	07-May-26	18-May-26	0%	3,385.62	3,385.62
Distrubution Panel Boards		39	11-Jan-27	25-Feb-27	19-May-26	07-Jul-26	0%	19,427.37	19,427.37
CO-R10.S04-WE-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	18	11-Jan-27	31-Jan-27	19-May-26	13-Jun-26	0%	0.00	0.00
CO-R10.S04-WE-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-4]	12	21-Jan-27	03-Feb-27	03-Jun-26	16-Jun-26	0%	0.00	0.00

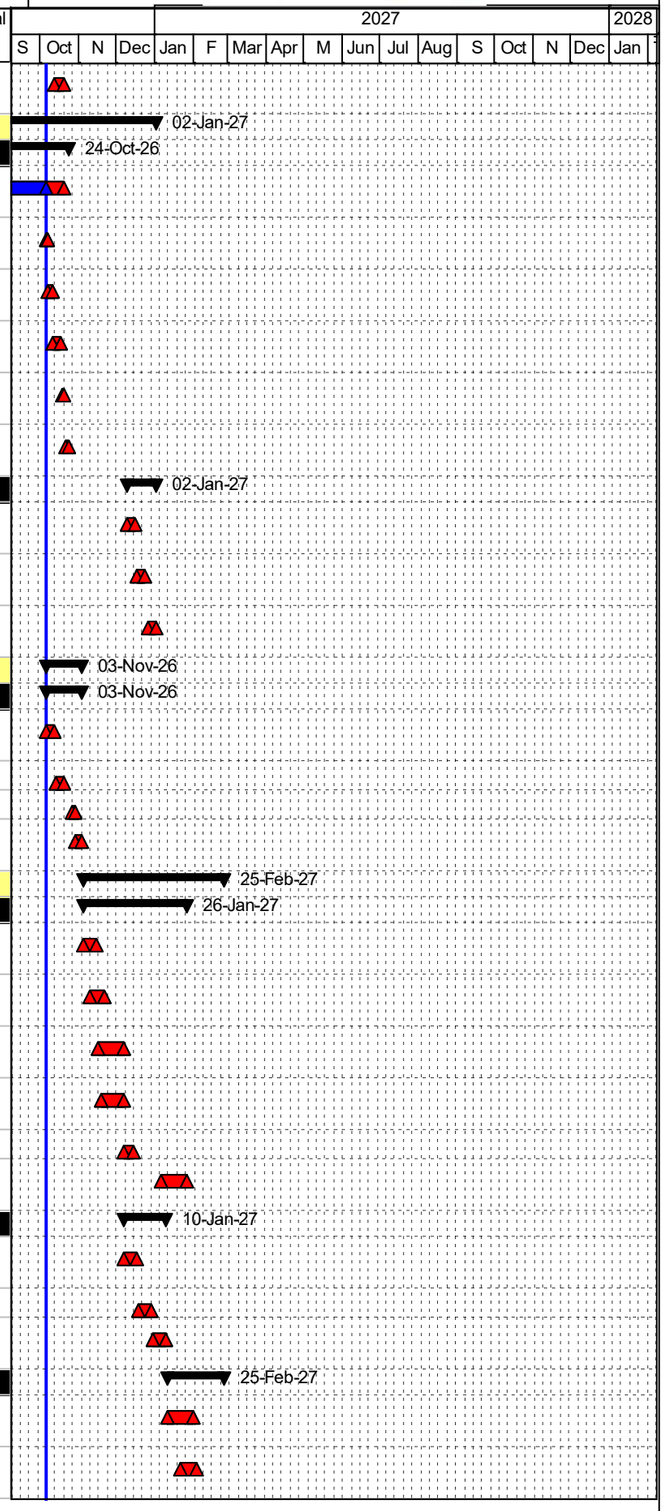

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S04-WE-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	12	04-Feb-27	17-Feb-27	17-Jun-26	30-Jun-26	0%	0.00	0.00
CO-R10.S04-WE-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-4]	18	04-Feb-27	25-Feb-27	17-Jun-26	07-Jul-26	0%	19,427.37	19,427.37
Telecom Network		28	08-Mar-27	12-Apr-27	21-Jun-26	22-Jul-26	0%	80,544.72	80,544.72
Ducts Works		28	08-Mar-27	12-Apr-27	21-Jun-26	22-Jul-26	0%	66,430.50	66,430.50
CO-R10.S04-WE-T	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	08-Mar-27	18-Mar-27	21-Jun-26	28-Jun-26	0%	6,700.00	6,700.00
CO-R10.S04-WE	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	20-Mar-27	27-Mar-27	29-Jun-26	06-Jul-26	0%	39,764.50	39,764.50
CO-R10.S04-WE	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-4]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	6,700.00	6,700.00
CO-R10.S04-WE-T	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	13,266.00	13,266.00
Manholes Works		21	20-Mar-27	12-Apr-27	29-Jun-26	22-Jul-26	0%	14,114.22	14,114.22
CO-R10.S04-WE	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	20-Mar-27	27-Mar-27	29-Jun-26	06-Jul-26	0%	2,199.61	2,199.61
CO-R10.S04-WE	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	9,715.00	9,715.00
CO-R10.S04-WE	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	2,199.61	2,199.61
Road Works		22	25-Aug-26 A	21-Jun-27	23-Jul-26	01-Oct-26	9.68%	553,581.27	553,581.27
Pre-Bituminous Construction		15	13-Apr-27	29-Apr-27	23-Jul-26	09-Aug-26	0%	446,397.22	446,397.22
CO-R10.S04-WE	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-4]	12	13-Apr-27	26-Apr-27	23-Jul-26	05-Aug-26	0%	263,120.65	263,120.65
CO-R10.S04-WE	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-4]	12	17-Apr-27	29-Apr-27	27-Jul-26	09-Aug-26	0%	183,276.57	183,276.57
Pavement Works		12	25-Aug-26 A	21-Jun-27	17-Sep-26	01-Oct-26	50%	107,184.05	107,184.05
CO-R10.S04-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	12	25-Aug-26 A	21-Jun-27	17-Sep-26	01-Oct-26	50%	107,184.05	107,184.05
Road 11 Local 1 (670 LM)		361	02-Apr-26 A	31-Jul-27	04-Oct-25	13-Oct-26	29.37%	425,005.95	387,594.87
SW_5		273	25-Apr-26 A	31-Jul-27	03-Jan-26	11-Oct-26	36.37%	157,859.16	120,448.08
Irrigation Network		93	25-Apr-26 A	19-Nov-26	03-Jan-26	21-Jan-26	30.45%	85,996.44	48,585.35
Main Line Pipes		93	25-Apr-26 A	19-Nov-26	03-Jan-26	21-Jan-26	30.45%	85,996.44	48,585.35
CO-R11.S05-IR-1	Pipes Laying Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	25-Apr-26 A	09-Nov-26	03-Jan-26	10-Jan-26	70%	37,411.08	0.00
CO-R11.S05-IR-1	Installation Works for Main Line Valves of Irrigation Network-[Road 11]-[SW-5]	3	09-Nov-26	11-Nov-26	11-Jan-26	13-Jan-26	0%	42,350.17	42,350.17
CO-R11.S05-IR-130	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	12-Nov-26	19-Nov-26	14-Jan-26	21-Jan-26	0%	6,235.18	6,235.18
Telecom Network		21	20-Mar-27	12-Apr-27	29-Jun-26	22-Jul-26	0%	9,400.77	9,400.77
Manholes Works		21	20-Mar-27	12-Apr-27	29-Jun-26	22-Jul-26	0%	9,400.77	9,400.77
CO-R11.S05-TE-1	Excavation Works for Manholes of Telecom Network-[Road 11]-[SW-5]	7	20-Mar-27	27-Mar-27	29-Jun-26	06-Jul-26	0%	1,256.92	1,256.92
CO-R11.S05-TE-1	Installation Works for Manholes of Telecom Network-[Road 11]-[SW-5]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	6,886.93	6,886.93
CO-R11.S05-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 11]-[SW-5]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	1,256.92	1,256.92
Road Works		10	25-Aug-26 A	31-Jul-27	30-Sep-26	11-Oct-26	50%	62,461.96	62,461.96
Pavement Works		10	25-Aug-26 A	31-Jul-27	30-Sep-26	11-Oct-26	50%	62,461.96	62,461.96
CO-R11.S05-RD-F	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-5]	10	25-Aug-26 A	31-Jul-27	30-Sep-26	11-Oct-26	50%	62,461.96	62,461.96
SW_6		317	02-Apr-26 A	31-Jul-27	04-Oct-25	13-Oct-26	25.24%	267,146.79	267,146.79
Sewage Network		147	02-Apr-26 A	11-Oct-26	04-Oct-25	14-Oct-25	44.44%	81,435.45	81,435.45
Manholes		147	02-Apr-26 A	11-Oct-26	04-Oct-25	14-Oct-25	44.44%	81,435.45	81,435.45
CO-R11.S06-SW-18	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network-[Road 11]-[SW-6]	4	02-Apr-26 A	10-Oct-26	04-Oct-25	07-Oct-25	50%	72,387.07	72,387.07
CO-R11.S06-SW-1	Testing Works for Main Line Manholes of Sewage Network-[Road 11]-[SW-6]	1	11-Oct-26	11-Oct-26	14-Oct-25	14-Oct-25	0%	9,048.38	9,048.38
Potable Water Network		110	06-Oct-26	10-Feb-27	28-Jan-26	28-Feb-26	0%	53,758.79	53,758.79
Valve Chamber		6	04-Feb-27	10-Feb-27	28-Jan-26	03-Feb-26	0%	15,887.04	15,887.04
CO-R11.S06-PW-21	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 11]-[SW-6]	6	04-Feb-27	10-Feb-27	28-Jan-26	03-Feb-26	0%	15,887.04	15,887.04
Fire Hydrant		21	06-Oct-26	29-Oct-26	04-Feb-26	28-Feb-26	0%	37,871.75	37,871.75
CO-R11.S06-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	06-Oct-26	13-Oct-26	04-Feb-26	11-Feb-26	0%	5,680.76	5,680.76
CO-R11.S06-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 11]-[SW-6]	7	14-Oct-26	21-Oct-26	12-Feb-26	19-Feb-26	0%	24,616.64	24,616.64

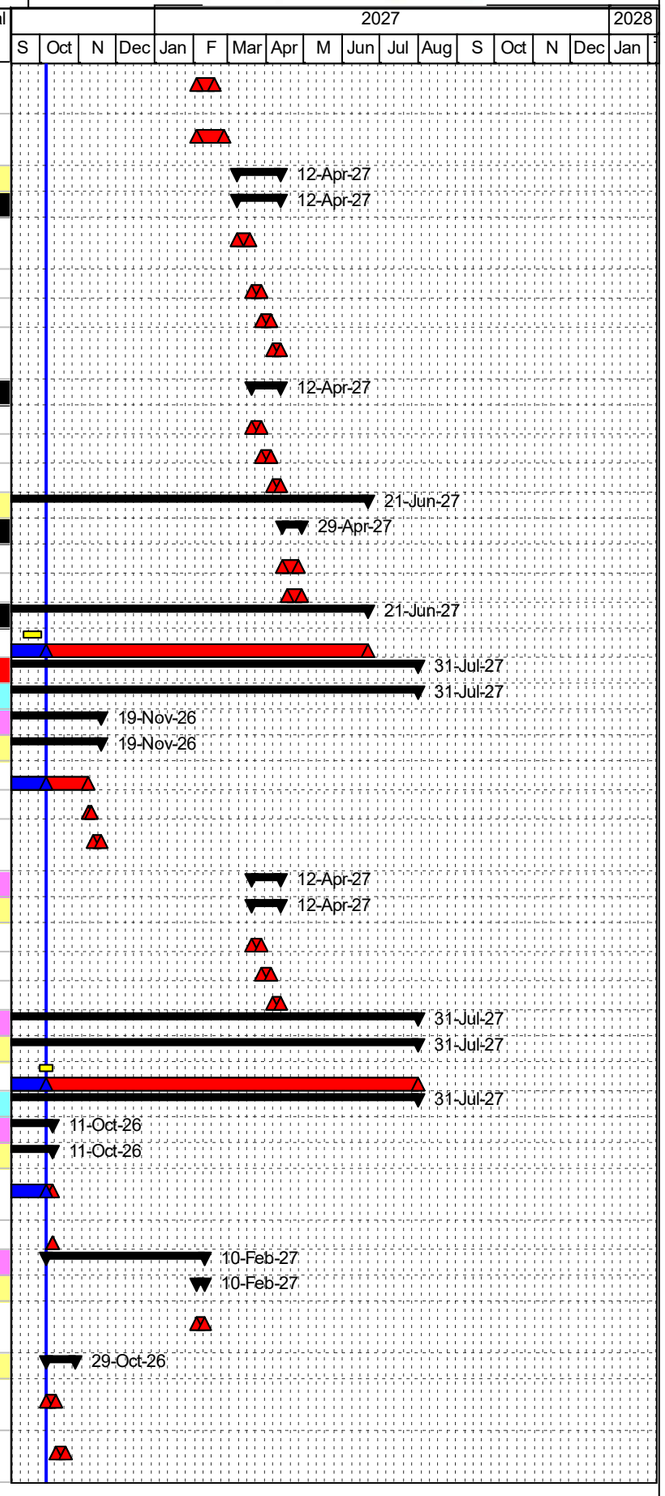

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R11.S06-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	22-Oct-26	29-Oct-26	21-Feb-26	28-Feb-26	0%	7,574.35	7,574.35
Street Lighting Network		135	22-Nov-26	02-May-27	19-May-26	25-Jul-26	0%	60,089.82	60,089.82
Lighting Poles Works		27	01-Apr-27	02-May-27	24-Jun-26	19-Jul-26	0%	38,090.30	38,090.30
CO-R11.S06-SL-21(	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	15	01-Apr-27	18-Apr-27	24-Jun-26	11-Jul-26	0%	10,659.43	10,659.43
CO-R11.S06-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 11]-[SW-6]	18	12-Apr-27	02-May-27	29-Jun-26	19-Jul-26	0%	16,771.44	16,771.44
CO-R11.S06-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	7	19-Apr-27	26-Apr-27	12-Jul-26	19-Jul-26	0%	10,659.43	10,659.43
Cabling Works		10	22-Nov-26	02-Dec-26	19-May-26	03-Jun-26	0%	3,988.85	3,988.85
CO-R11.S06-SL-16(	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 11]-[SW-6]	10	22-Nov-26	02-Dec-26	19-May-26	03-Jun-26	0%	3,988.85	3,988.85
Distrubution Panel Boards		36	01-Feb-27	18-Mar-27	14-Jun-26	25-Jul-26	0%	18,010.67	18,010.67
CO-R11.S06-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 11]-[SW-6]	12	01-Feb-27	14-Feb-27	14-Jun-26	27-Jun-26	0%	0.00	0.00
CO-R11.S06-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 11]-[SW-6]	12	15-Feb-27	01-Mar-27	28-Jun-26	11-Jul-26	0%	0.00	0.00
CO-R11.S06-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 11]-[SW-6]	12	02-Mar-27	18-Mar-27	12-Jul-26	25-Jul-26	0%	0.00	0.00
CO-R11.S06-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 11]-[SW-6]	12	02-Mar-27	18-Mar-27	12-Jul-26	25-Jul-26	0%	18,010.67	18,010.67
Telecom Network		21	28-Mar-27	20-Apr-27	07-Jul-26	30-Jul-26	0%	9,400.77	9,400.77
Manholes Works		21	28-Mar-27	20-Apr-27	07-Jul-26	30-Jul-26	0%	9,400.77	9,400.77
CO-R11.S06-TE-1	Excavation Works for Manholes of Telecom Network-[Road 11]-[SW-6]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	1,256.92	1,256.92
CO-R11.S06-TE-1	Installation Works for Manholes of Telecom Network-[Road 11]-[SW-6]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	6,886.93	6,886.93
CO-R11.S06-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 11]-[SW-6]	7	13-Apr-27	20-Apr-27	23-Jul-26	30-Jul-26	0%	1,256.92	1,256.92
Road Works		10	25-Aug-26 A	31-Jul-27	03-Oct-26	13-Oct-26	50%	62,461.96	62,461.96
Pavement Works		10	25-Aug-26 A	31-Jul-27	03-Oct-26	13-Oct-26	50%	62,461.96	62,461.96
CO-R11.S06-RD-F	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-6]	10	25-Aug-26 A	31-Jul-27	03-Oct-26	13-Oct-26	50%	62,461.96	62,461.96
Road 14 Local 1 (584 LM)		233	25-Aug-26 A	14-Aug-27	05-Aug-25	27-Oct-26	11.75%	786,844.48	786,844.48
SW_7		233	25-Aug-26 A	14-Aug-27	05-Aug-25	25-Oct-26	13.45%	343,716.86	343,716.86
Sewage Network		1	06-Oct-26	06-Oct-26	01-Sep-25	01-Sep-25	0%	6,319.37	6,319.37
Manholes		1	06-Oct-26	06-Oct-26	01-Sep-25	01-Sep-25	0%	6,319.37	6,319.37
CO-R14.S07-SW-:	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-7]	1	06-Oct-26	06-Oct-26	01-Sep-25	01-Sep-25	0%	6,319.37	6,319.37
Street Lighting Network		153	06-Oct-26	06-Apr-27	05-Aug-25	11-Jun-26	0%	17,596.88	17,596.88
Lighting Poles Works		124	09-Nov-26	06-Apr-27	20-Jan-26	11-Jun-26	0%	17,596.88	17,596.88
CO-R14.S07-SL-10(	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	12	09-Nov-26	22-Nov-26	20-Jan-26	02-Feb-26	0%	421.43	421.43
CO-R14.S07-SL-11(	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 14]-[SW-7]	12	23-Nov-26	06-Dec-26	03-Feb-26	16-Feb-26	0%	3,140.96	3,140.96
CO-R14.S07-SL-12(	Installation Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	18	07-Dec-26	27-Dec-26	17-Feb-26	09-Mar-26	0%	3,792.87	3,792.87
CO-R14.S07-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 14]-[SW-7]	18	17-Mar-27	06-Apr-27	18-May-26	11-Jun-26	0%	7,713.04	7,713.04
CO-R14.S07-SL-21(	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	12	18-Mar-27	31-Mar-27	19-May-26	06-Jun-26	0%	842.86	842.86
CO-R14.S07-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	5	01-Apr-27	06-Apr-27	07-Jun-26	11-Jun-26	0%	1,685.72	1,685.72
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	05-Aug-25	28-Aug-25	0%	0.00	0.00
salman	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14]-[SW-7]	18	06-Oct-26	26-Oct-26			0%	0.00	0.00
CO-R14.S07-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 14]-[SW-7]	18	10-Oct-26	29-Oct-26	05-Aug-25	25-Aug-25	0%	0.00	0.00
CO-R14.S07-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 14]-[SW-7]	18	10-Oct-26	29-Oct-26	05-Aug-25	25-Aug-25	0%	0.00	0.00

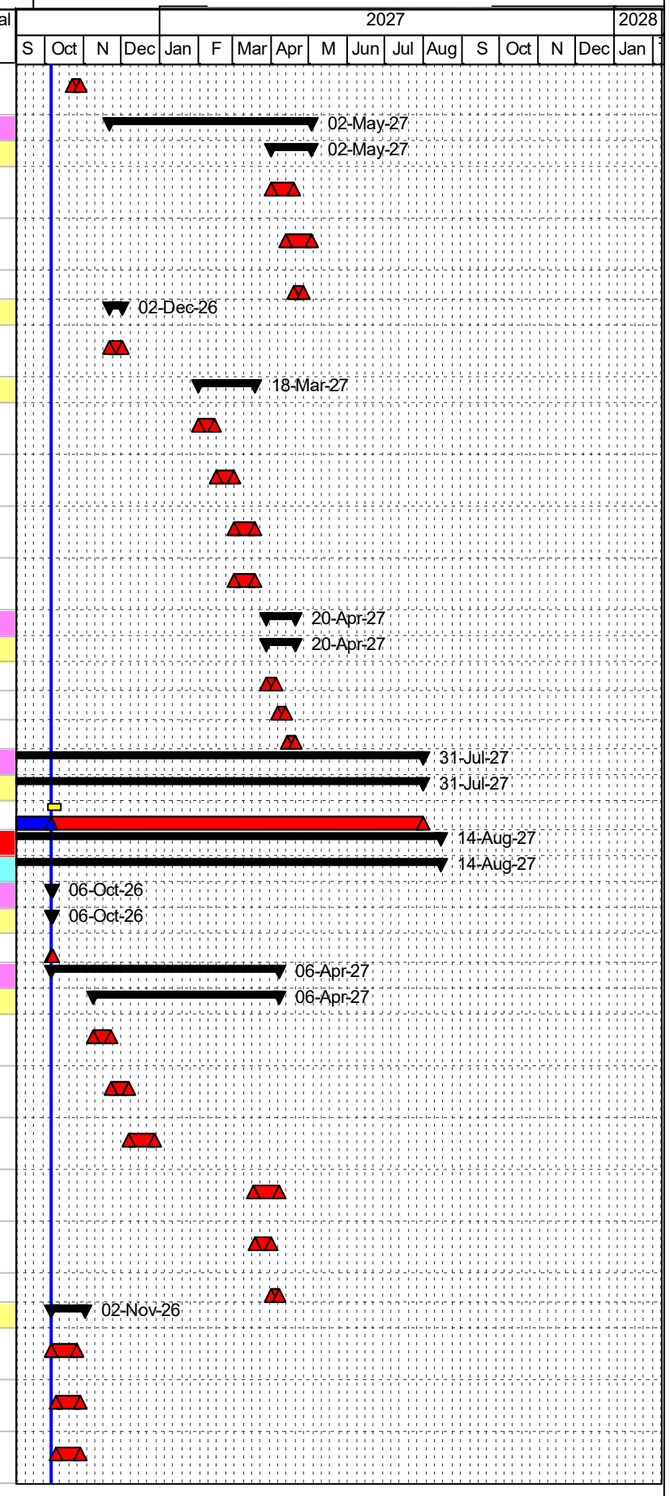

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R14.S07-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[SW-7]	18	13-Oct-26	02-Nov-26	09-Aug-25	28-Aug-25	0%	0.00	0.00
Telecom Network		44	25-Feb-27	20-Apr-27	20-May-26	30-Jul-26	0%	69,526.57	69,526.57
Ducts Works		37	25-Feb-27	12-Apr-27	20-May-26	30-Jul-26	0%	56,983.50	56,983.50
CO-R14.S07-TE-10(	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 14]-[SW-7]	3	25-Feb-27	28-Feb-27	20-May-26	23-May-26	0%	5,594.50	5,594.50
CO-R14.S07-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 14]-[SW-7]	7	20-Mar-27	27-Mar-27	07-Jul-26	14-Jul-26	0%	34,304.00	34,304.00
CO-R14.S07-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 14]-[SW-7]	7	28-Mar-27	04-Apr-27	15-Jul-26	22-Jul-26	0%	5,594.50	5,594.50
CO-R14.S07-TE-13(	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 14]-[SW-7]	7	05-Apr-27	12-Apr-27	23-Jul-26	30-Jul-26	0%	11,490.50	11,490.50
Manholes Works		21	28-Mar-27	20-Apr-27	07-Jul-26	30-Jul-26	0%	12,543.07	12,543.07
CO-R14.S07-TE-1	Excavation Works for Manholes of Telecom Network-[Road 14]-[SW-7]	7	28-Mar-27	04-Apr-27	07-Jul-26	14-Jul-26	0%	1,885.38	1,885.38
CO-R14.S07-TE-1	Installation Works for Manholes of Telecom Network-[Road 14]-[SW-7]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	8,772.31	8,772.31
CO-R14.S07-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 14]-[SW-7]	7	13-Apr-27	20-Apr-27	23-Jul-26	30-Jul-26	0%	1,885.38	1,885.38
Road Works		58	25-Aug-26 A	14-Aug-27	05-Sep-26	25-Oct-26	18.47%	250,274.04	250,274.04
Pre-Bituminous Construction		18	03-May-27	29-May-27	05-Sep-26	26-Sep-26	0%	157,846.53	157,846.53
CO-R14.S07-RD-I	Aggregate Base Course Layer for Road Works-[Road 14]-[SW-7]	18	03-May-27	29-May-27	05-Sep-26	26-Sep-26	0%	157,846.53	157,846.53
Pavement Works		12	25-Aug-26 A	14-Aug-27	12-Oct-26	25-Oct-26	50%	92,427.51	92,427.51
CO-R14.S07-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-7]	12	25-Aug-26 A	14-Aug-27	12-Oct-26	25-Oct-26	50%	92,427.51	92,427.51
SW_8		233	25-Aug-26 A	14-Aug-27	15-Sep-25	27-Oct-26	10.43%	443,127.62	443,127.62
Sewage Network		1	06-Oct-26	06-Oct-26	15-Sep-25	15-Sep-25	0%	2,341.78	2,341.78
Manholes		1	06-Oct-26	06-Oct-26	15-Sep-25	15-Sep-25	0%	2,341.78	2,341.78
CO-R14.S08-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-8]	1	06-Oct-26	06-Oct-26	15-Sep-25	15-Sep-25	0%	2,341.78	2,341.78
Potable Water Network		21	06-Oct-26	29-Oct-26	26-Feb-26	25-Mar-26	0%	53,020.45	53,020.45
Fire Hydrant		21	06-Oct-26	29-Oct-26	26-Feb-26	25-Mar-26	0%	53,020.45	53,020.45
CO-R14.S08-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	06-Oct-26	13-Oct-26	26-Feb-26	05-Mar-26	0%	7,953.07	7,953.07
CO-R14.S08-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 14]-[SW-8]	7	14-Oct-26	21-Oct-26	07-Mar-26	14-Mar-26	0%	34,463.29	34,463.29
CO-R14.S08-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	22-Oct-26	29-Oct-26	15-Mar-26	25-Mar-26	0%	10,604.09	10,604.09
Street Lighting Network		80	15-Feb-27	29-May-27	24-Jun-26	15-Aug-26	0%	67,964.77	67,964.77
Lighting Poles Works		45	01-Apr-27	29-May-27	24-Jun-26	09-Aug-26	0%	41,146.31	41,146.31
CO-R14.S08-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-8]	7	01-Apr-27	08-Apr-27	24-Jun-26	01-Jul-26	0%	15,989.15	15,989.15
CO-R14.S08-SL-85(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 14]-[SW-8]	18	03-May-27	29-May-27	20-Jul-26	09-Aug-26	0%	25,157.16	25,157.16
Distrubution Panel Boards		42	15-Feb-27	08-Apr-27	28-Jun-26	15-Aug-26	0%	26,818.47	26,818.47
CO-R14.S08-SL-DB	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14]-[SW-8]	18	15-Feb-27	08-Mar-27	28-Jun-26	18-Jul-26	0%	0.00	0.00
CO-R14.S08-SL-DB	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 14]-[SW-8]	18	02-Mar-27	25-Mar-27	12-Jul-26	01-Aug-26	0%	0.00	0.00
CO-R14.S08-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 14]-[SW-8]	25	02-Mar-27	03-Apr-27	12-Jul-26	09-Aug-26	0%	26,818.47	26,818.47
CO-R14.S08-SL-DB	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[SW-8]	18	20-Mar-27	08-Apr-27	26-Jul-26	15-Aug-26	0%	0.00	0.00
Telecom Network		48	01-Mar-27	28-Apr-27	07-Jun-26	08-Aug-26	0%	69,526.57	69,526.57
Ducts Works		41	01-Mar-27	20-Apr-27	07-Jun-26	08-Aug-26	0%	56,983.50	56,983.50
CO-R14.S08-TE-10(	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 14]-[SW-8]	3	01-Mar-27	03-Mar-27	07-Jun-26	09-Jun-26	0%	5,594.50	5,594.50
CO-R14.S08-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 14]-[SW-8]	7	28-Mar-27	04-Apr-27	15-Jul-26	22-Jul-26	0%	34,304.00	34,304.00
CO-R14.S08-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 14]-[SW-8]	7	05-Apr-27	12-Apr-27	23-Jul-26	30-Jul-26	0%	5,594.50	5,594.50
CO-R14.S08-TE-13(	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 14]-[SW-8]	7	13-Apr-27	20-Apr-27	01-Aug-26	08-Aug-26	0%	11,490.50	11,490.50
Manholes Works		21	05-Apr-27	28-Apr-27	15-Jul-26	08-Aug-26	0%	12,543.07	12,543.07
CO-R14.S08-TE-1	Excavation Works for Manholes of Telecom Network-[Road 14]-[SW-8]	7	05-Apr-27	12-Apr-27	15-Jul-26	22-Jul-26	0%	1,885.38	1,885.38

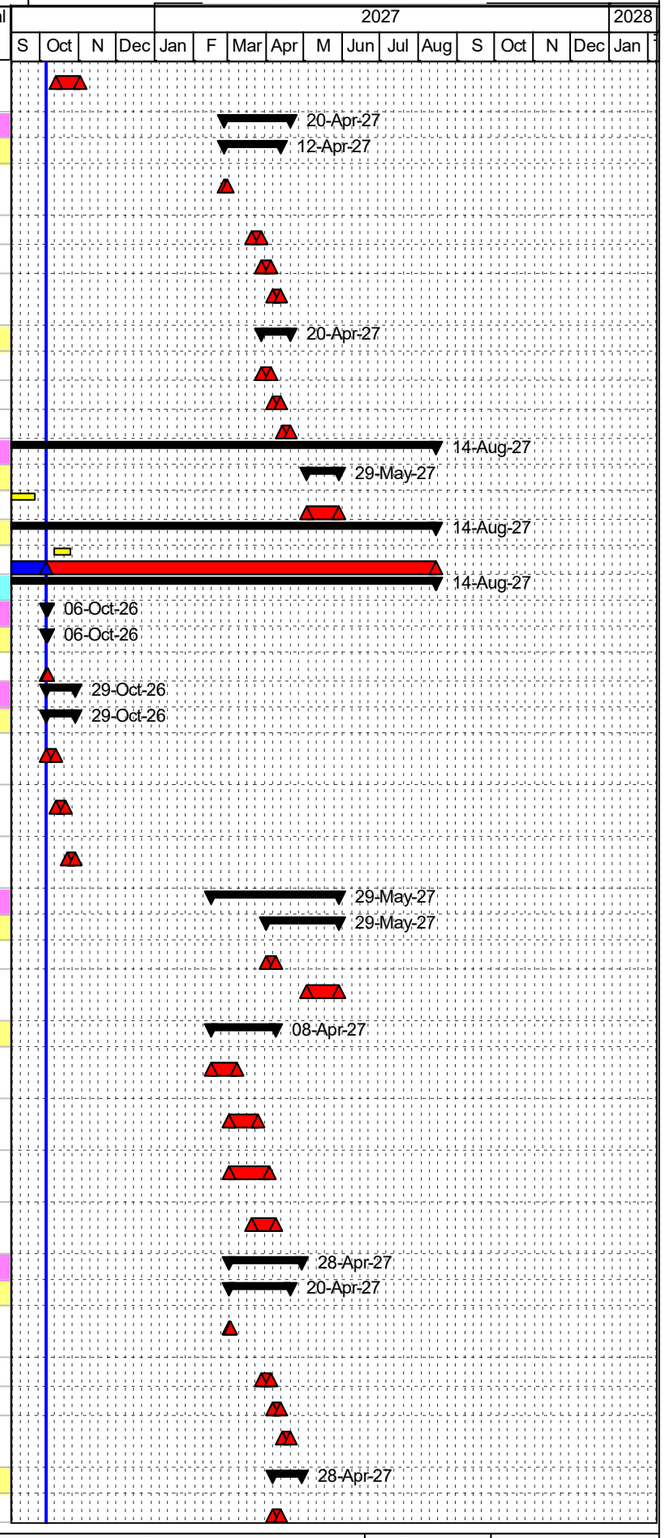


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part 2 Update 06/10/2026

Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R14.S08-TE-1	Installation Works for Manholes of Telecom Network-[Road 14]-[SW-8]	7	13-Apr-27	20-Apr-27	23-Jul-26	30-Jul-26	0%	8,772.31	8,772.31
CO-R14.S08-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 14]-[SW-8]	7	21-Apr-27	28-Apr-27	01-Aug-26	08-Aug-26	0%	1,885.38	1,885.38
Road Works		58	25-Aug-26 A	14-Aug-27	02-Sep-26	27-Oct-26	18.47%	250,274.04	250,274.04
Pre-Bituminous Construction		18	03-May-27	29-May-27	02-Sep-26	22-Sep-26	0%	157,846.53	157,846.53
CO-R14.S08-RD-I	Aggregate Base Course Layer for Road Works-[Road 14]-[SW-8]	18	03-May-27	29-May-27	02-Sep-26	22-Sep-26	0%	157,846.53	157,846.53
Pavement Works		12	25-Aug-26 A	14-Aug-27	14-Oct-26	27-Oct-26	50%	92,427.51	92,427.51
CO-R14.S08-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-8]	12	25-Aug-26 A	14-Aug-27	14-Oct-26	27-Oct-26	50%	92,427.51	92,427.51
Road 15 Local 1 (556 LM)		247	25-Aug-26 A	28-Aug-27	02-Jun-25	08-Nov-26	41.04%	180,060.06	180,060.06
SW_9		12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	90%	52,781.33	52,781.33
Road Works		12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	90%	52,781.33	52,781.33
Pavement Works		12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	90%	52,781.33	52,781.33
CO-R15.S09-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-9]	12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	90%	52,781.33	52,781.33
SW_10		245	25-Aug-26 A	25-Aug-27	02-Jun-25	08-Nov-26	20.73%	127,278.73	127,278.73
Sewage Network		1	06-Oct-26	06-Oct-26	05-Jul-25	06-Jul-25	0%	2,882.74	2,882.74
Manholes		1	06-Oct-26	06-Oct-26	05-Jul-25	06-Jul-25	0%	2,882.74	2,882.74
CO-R15.S10-SW-21	Testing Works for Main Line Manholes of Sewage Network-[Road 15]-[SW-10]	1	06-Oct-26	06-Oct-26	05-Jul-25	06-Jul-25	0%	2,882.74	2,882.74
Street Lighting Network		71	06-Oct-26	27-Dec-26	02-Jun-25	02-Feb-26	0%	41,317.27	41,317.27
Lighting Poles Works		71	06-Oct-26	27-Dec-26	13-Jan-26	02-Feb-26	0%	24,491.85	24,491.85
CO-R15.S10-SL-20(	Testing Works for Lighting Poles of Street Lighting Network-[Road 15]-[SW-10]	5	06-Oct-26	11-Oct-26	27-Jan-26	02-Feb-26	0%	9,517.35	9,517.35
CO-R15.S10-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 15]-[SW-10]	18	07-Dec-26	27-Dec-26	13-Jan-26	02-Feb-26	0%	14,974.50	14,974.50
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	02-Jun-25	03-Jul-25	0%	16,825.42	16,825.42
CO-R15.S10-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 15]-[SW-10]	18	06-Oct-26	26-Oct-26	02-Jun-25	26-Jun-25	0%	0.00	0.00
CO-R15.S10-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 15]-[SW-10]	18	10-Oct-26	29-Oct-26	10-Jun-25	30-Jun-25	0%	0.00	0.00
CO-R15.S10-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 15]-[SW-10]	18	10-Oct-26	29-Oct-26	10-Jun-25	30-Jun-25	0%	16,825.42	16,825.42
CO-R15.S10-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 15]-[SW-10]	18	13-Oct-26	02-Nov-26	14-Jun-25	03-Jul-25	0%	0.00	0.00
Potable Water Network		18	06-Oct-26	26-Oct-26	08-Mar-26	31-Mar-26	0%	30,297.40	30,297.40
Fire Hydrant		18	06-Oct-26	26-Oct-26	08-Mar-26	31-Mar-26	0%	30,297.40	30,297.40
CO-R15.S10-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	06-Oct-26	12-Oct-26	08-Mar-26	14-Mar-26	0%	4,544.61	4,544.61
CO-R15.S10-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 15]-[SW-10]	6	13-Oct-26	19-Oct-26	15-Mar-26	24-Mar-26	0%	19,693.31	19,693.31
CO-R15.S10-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	20-Oct-26	26-Oct-26	25-Mar-26	31-Mar-26	0%	6,059.48	6,059.48
Road Works		10	25-Aug-26 A	25-Aug-27	28-Oct-26	08-Nov-26	50%	52,781.33	52,781.33
Pavement Works		10	25-Aug-26 A	25-Aug-27	28-Oct-26	08-Nov-26	50%	52,781.33	52,781.33
CO-R15.S10-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-10]	10	25-Aug-26 A	25-Aug-27	28-Oct-26	08-Nov-26	50%	52,781.33	52,781.33
Road 16 Local 1 (527 LM)		257	25-Aug-26 A	06-Sep-27	29-Mar-26	19-Nov-26	69.19%	131,033.11	131,033.11
SW_11		10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	90%	50,367.85	50,367.85
Road Works		10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	90%	50,367.85	50,367.85
Pavement Works		10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	90%	50,367.85	50,367.85
CO-R16.S11-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-11]	10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	90%	50,367.85	50,367.85
SW_12		257	25-Aug-26 A	06-Sep-27	29-Mar-26	19-Nov-26	56.2%	80,665.25	80,665.25
Potable Water Network		24	06-Oct-26	02-Nov-26	29-Mar-26	18-Apr-26	0%	30,297.40	30,297.40
Fire Hydrant		24	06-Oct-26	02-Nov-26	29-Mar-26	18-Apr-26	0%	30,297.40	30,297.40
CO-R16.S12-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	06-Oct-26	12-Oct-26	29-Mar-26	04-Apr-26	0%	4,544.61	4,544.61
CO-R16.S12-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 16]-[SW-12]	6	20-Oct-26	26-Oct-26	05-Apr-26	11-Apr-26	0%	19,693.31	19,693.31

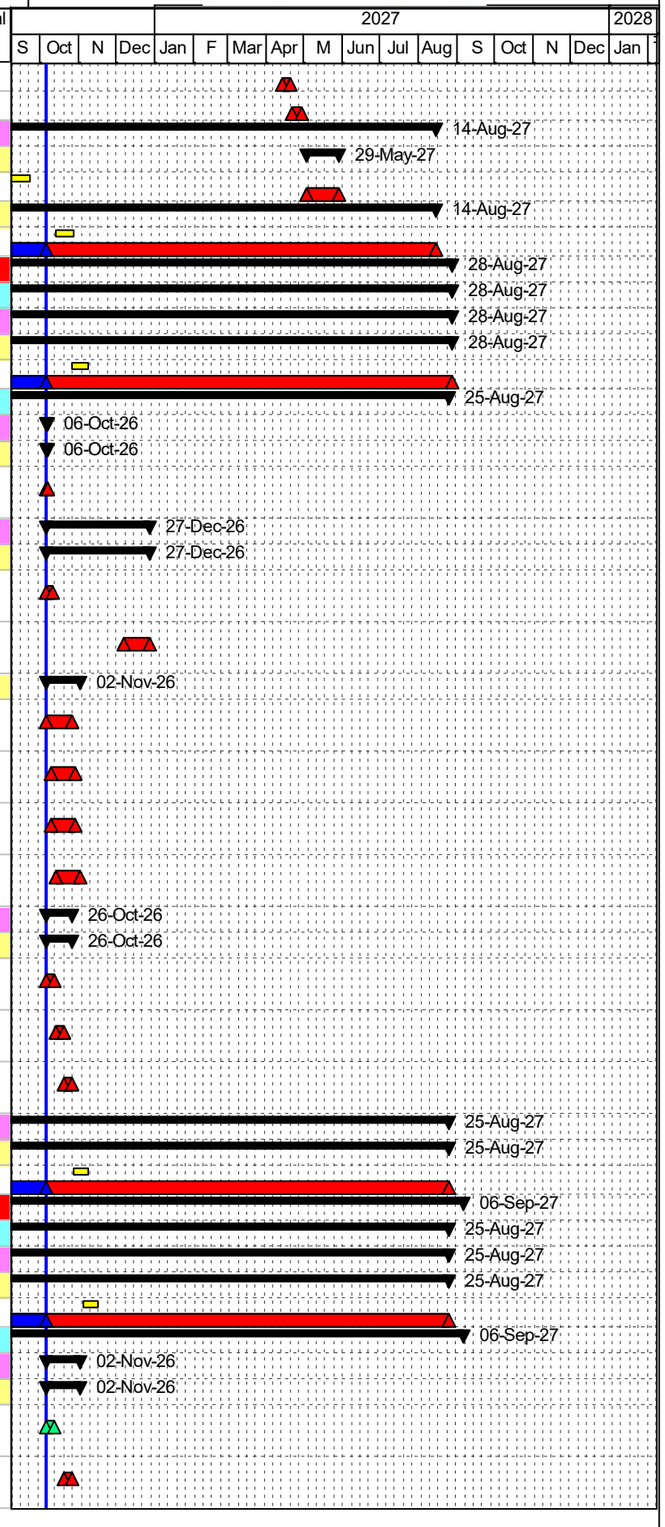

Primary Baseline | Actual Work | Summary | Remaining Work | Baseline Milestone | Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R16.S12-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	27-Oct-26	02-Nov-26	12-Apr-26	18-Apr-26	0%	6,059.48	6,059.48
Road Works		10	25-Aug-26 A	06-Sep-27	09-Nov-26	19-Nov-26	90%	50,367.85	50,367.85
Pavement Works		10	25-Aug-26 A	06-Sep-27	09-Nov-26	19-Nov-26	90%	50,367.85	50,367.85
CO-R16.S12-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-12]	10	25-Aug-26 A	06-Sep-27	09-Nov-26	19-Nov-26	90%	50,367.85	50,367.85
Road 17 Local 1 (500 LM)		45	06-Oct-26	26-Nov-26	16-Apr-25	01-Sep-26	0%	102,157.65	102,157.65
SW_14		45	06-Oct-26	26-Nov-26	16-Apr-25	01-Sep-26	0%	102,157.65	102,157.65
Sewage Network		1	06-Oct-26	06-Oct-26	21-May-25	21-May-25	0%	1,517.62	1,517.62
Manholes		1	06-Oct-26	06-Oct-26	21-May-25	21-May-25	0%	1,517.62	1,517.62
CO-R17.S14-SW-21	Testing Works for Main Line Manholes of Sewage Network-[Road 17]-[SW-14]	1	06-Oct-26	06-Oct-26	21-May-25	21-May-25	0%	1,517.62	1,517.62
Street Lighting Network		45	06-Oct-26	26-Nov-26	16-Apr-25	14-Dec-25	0%	71,658.51	71,658.51
Lighting Poles Works		45	06-Oct-26	26-Nov-26	24-Nov-25	14-Dec-25	0%	44,085.33	44,085.33
CO-R17.S14-SL-20(	Testing Works for Lighting Poles of Street Lighting Network-[Road 17]-[SW-14]	5	06-Oct-26	11-Oct-26	08-Dec-25	14-Dec-25	0%	17,131.23	17,131.23
CO-R17.S14-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 17]-[SW-14]	18	07-Nov-26	26-Nov-26	24-Nov-25	14-Dec-25	0%	26,954.10	26,954.10
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	16-Apr-25	13-May-25	0%	27,573.18	27,573.18
CO-R17.S14-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 17]-[SW-14]	18	06-Oct-26	26-Oct-26	16-Apr-25	06-May-25	0%	0.00	0.00
CO-R17.S14-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 17]-[SW-14]	18	10-Oct-26	29-Oct-26	20-Apr-25	10-May-25	0%	0.00	0.00
CO-R17.S14-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 17]-[SW-14]	18	10-Oct-26	29-Oct-26	20-Apr-25	10-May-25	0%	27,573.18	27,573.18
CO-R17.S14-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 17]-[SW-14]	18	13-Oct-26	02-Nov-26	23-Apr-25	13-May-25	0%	0.00	0.00
Potable Water Network		30	06-Oct-26	09-Nov-26	21-Apr-26	11-May-26	0%	22,723.05	22,723.05
Fire Hydrant		30	06-Oct-26	09-Nov-26	21-Apr-26	11-May-26	0%	22,723.05	22,723.05
CO-R17.S14-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	06-Oct-26	12-Oct-26	21-Apr-26	27-Apr-26	0%	3,408.46	3,408.46
CO-R17.S14-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 17]-[SW-14]	6	27-Oct-26	02-Nov-26	28-Apr-26	04-May-26	0%	14,769.98	14,769.98
CO-R17.S14-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	03-Nov-26	09-Nov-26	05-May-26	11-May-26	0%	4,544.61	4,544.61
Telecom Network		21	06-Oct-26	29-Oct-26	09-Aug-26	01-Sep-26	0%	6,258.47	6,258.47
Manholes Works		21	06-Oct-26	29-Oct-26	09-Aug-26	01-Sep-26	0%	6,258.47	6,258.47
CO-R17.S14-TE-1	Excavation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	06-Oct-26	13-Oct-26	09-Aug-26	16-Aug-26	0%	628.46	628.46
CO-R17.S14-TE-1	Installation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	14-Oct-26	21-Oct-26	17-Aug-26	24-Aug-26	0%	5,001.55	5,001.55
CO-R17.S14-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	22-Oct-26	29-Oct-26	25-Aug-26	01-Sep-26	0%	628.46	628.46
Road 18 Local 1 (479 LM)		24	06-Oct-26	02-Nov-26	19-Mar-25	27-Nov-25	0%	51,658.33	51,658.33
SW_16		24	06-Oct-26	02-Nov-26	19-Mar-25	27-Nov-25	0%	51,658.33	51,658.33
Street Lighting Network		24	06-Oct-26	02-Nov-26	19-Mar-25	27-Nov-25	0%	36,509.63	36,509.63
Lighting Poles Works		19	06-Oct-26	27-Oct-26	08-Nov-25	27-Nov-25	0%	20,573.15	20,573.15
CO-R18.S16-SL-20(	Testing Works for Lighting Poles of Street Lighting Network-[Road 18]-[SW-16]	5	06-Oct-26	11-Oct-26	22-Nov-25	27-Nov-25	0%	7,994.57	7,994.57
CO-R18.S16-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 18]-[SW-16]	18	07-Oct-26	27-Oct-26	08-Nov-25	27-Nov-25	0%	12,578.58	12,578.58
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	19-Mar-25	20-Apr-25	0%	15,936.47	15,936.47
CO-R18.S16-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 18]-[SW-16]	18	06-Oct-26	26-Oct-26	19-Mar-25	13-Apr-25	0%	0.00	0.00
CO-R18.S16-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 18]-[SW-16]	18	10-Oct-26	29-Oct-26	23-Mar-25	16-Apr-25	0%	0.00	0.00
CO-R18.S16-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 18]-[SW-16]	18	10-Oct-26	29-Oct-26	23-Mar-25	16-Apr-25	0%	15,936.47	15,936.47
CO-R18.S16-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 18]-[SW-16]	18	13-Oct-26	02-Nov-26	26-Mar-25	20-Apr-25	0%	0.00	0.00

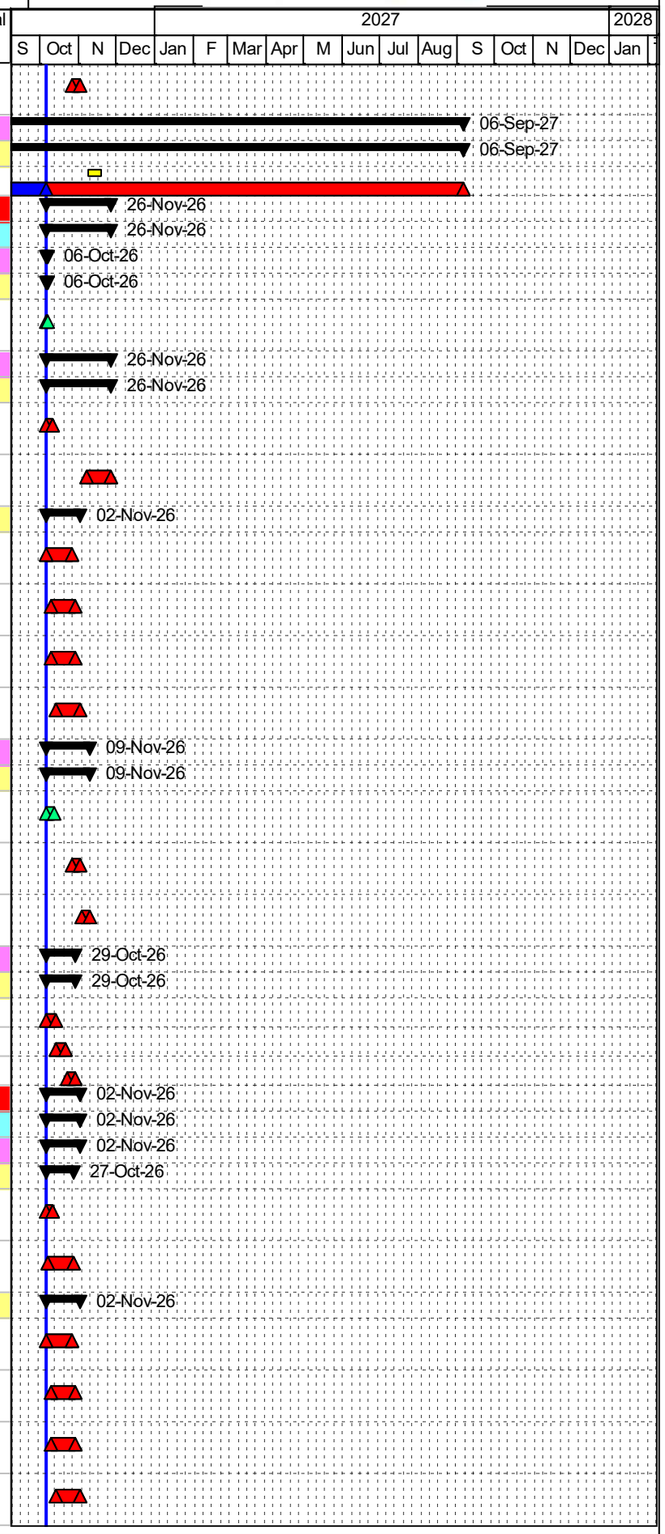

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Potable Water Network		18	06-Oct-26	26-Oct-26	23-Aug-25	11-Sep-25	0%	15,148.70	15,148.70
Fire Hydrant		18	06-Oct-26	26-Oct-26	23-Aug-25	11-Sep-25	0%	15,148.70	15,148.70
CO-R18.S16-PW-25	Excavation Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	06-Oct-26	12-Oct-26	23-Aug-25	28-Aug-25	0%	2,272.30	2,272.30
CO-R18.S16-PW-26	Installation Works for Fire Hydrant of Potable Water Network-[Road 18]-[SW-16]	6	13-Oct-26	19-Oct-26	30-Aug-25	04-Sep-25	0%	9,846.66	9,846.66
CO-R18.S16-PW-27	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	20-Oct-26	26-Oct-26	06-Sep-25	11-Sep-25	0%	3,029.74	3,029.74
Finishes for Infrastructure Networks		281	01-Jun-26 A	25-Oct-27	04-May-26	28-Dec-26	15.53%	9,396,573.36	9,294,615.93
Phase 2 Block "J"		281	01-Jun-26 A	25-Oct-27	04-May-26	28-Dec-26	15.53%	9,396,573.36	9,294,615.93
Road 09 Local 2 (2278 LM)		213	01-Jun-26 A	06-Oct-27	02-Jun-26	30-Nov-26	23.1%	3,449,609.39	3,347,651.96
Sewage Network		104	01-Jun-26 A	31-May-27	19-Jul-26	18-Aug-26	68.42%	289,897.37	289,897.37
Testing and Finishes		104	01-Jun-26 A	31-May-27	19-Jul-26	18-Aug-26	68.42%	289,897.37	289,897.37
CO-R09-SW-TF-10	Final Testing For Main Line of Sewage Network-[Road 09]	12	01-Jun-26 A	08-May-27	19-Jul-26	01-Aug-26	95%	208,794.34	208,794.34
CO-R09-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 09]	12	09-May-27	27-May-27	02-Aug-26	15-Aug-26	0%	40,551.52	40,551.52
CO-R09-SW-TF-120	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 09]	12	12-May-27	31-May-27	05-Aug-26	18-Aug-26	0%	40,551.52	40,551.52
Storm Drainage Network		33	17-Jun-26 A	15-Jun-27	15-Jul-26	02-Sep-26	78.91%	758,678.88	656,721.46
Testing and Finishes		33	17-Jun-26 A	15-Jun-27	15-Jul-26	02-Sep-26	78.91%	758,678.88	656,721.46
CO-R09-SD-TF-10	Testing Work for Pipes of Storm Drainage Network-[Road 09]	12	17-Jun-26 A	09-May-27	19-Jul-26	01-Aug-26	75%	101,957.42	0.00
CO-R09-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 09]	16	20-Jun-26 A	09-May-27	15-Jul-26	02-Aug-26	20%	27,719.40	27,719.40
CO-R09-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 09]	16	21-Jun-26 A	15-Jun-27	16-Aug-26	02-Sep-26	85%	601,282.66	601,282.66
CO-R09-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 09]	16	22-Jun-26 A	15-Jun-27	16-Aug-26	02-Sep-26	20%	27,719.40	27,719.40
Potable Water Network		33	09-May-27	21-Jun-27	02-Aug-26	08-Sep-26	0%	39,231.99	39,231.99
Testing and Finishes		33	09-May-27	21-Jun-27	02-Aug-26	08-Sep-26	0%	39,231.99	39,231.99
CO-R09-PW-TF-11	Testing Work for Main Line of Potable Water Network-[Road 09]	9	09-May-27	24-May-27	02-Aug-26	11-Aug-26	0%	39,231.99	39,231.99
CO-R09-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 09]	12	25-May-27	07-Jun-27	12-Aug-26	25-Aug-26	0%	0.00	0.00
CO-R09-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 09]	12	08-Jun-27	21-Jun-27	26-Aug-26	08-Sep-26	0%	0.00	0.00
Irrigation Network		16	05-May-27	29-May-27	29-Jul-26	16-Aug-26	0%	21,307.01	21,307.01
Testing and Finishes		16	05-May-27	29-May-27	29-Jul-26	16-Aug-26	0%	21,307.01	21,307.01
CO-R09-IR-TF-10(	Final Testing (pressure tests) of Irrigation Network-[Road 09]	16	05-May-27	29-May-27	29-Jul-26	16-Aug-26	0%	21,307.01	21,307.01
Street Lighting Network		86	03-Apr-27	17-Jul-27	02-Jun-26	09-Sep-26	0%	189,756.53	189,756.53
Termination and Testing Works		84	03-Apr-27	14-Jul-27	02-Jun-26	07-Sep-26	0%	177,971.23	177,971.23
CO-R09-SL-TF-100	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 09]	12	03-Apr-27	15-Apr-27	02-Jun-26	15-Jun-26	0%	80,958.78	80,958.78
CO-R09-SL-TF-110	Termination Works For Panel Board Cables of Street Lighting Network-[Road 09]	11	21-Jun-27	03-Jul-27	15-Aug-26	26-Aug-26	0%	64,674.97	64,674.97
CO-R09-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 09]	10	03-Jul-27	14-Jul-27	26-Aug-26	07-Sep-26	0%	32,337.48	32,337.48
Earthing System Works		74	17-Apr-27	17-Jul-27	16-Jun-26	09-Sep-26	0%	11,785.30	11,785.30
CO-R09-SL-ES-100	Install Earthing System Works for Lighting Poles of Street Lighting Network-[Road 09]	12	17-Apr-27	29-Apr-27	16-Jun-26	29-Jun-26	0%	6,125.14	6,125.14
CO-R09-SL-ES-110	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network-[Road 09]	12	03-Jul-27	17-Jul-27	26-Aug-26	09-Sep-26	0%	5,660.16	5,660.16
Medium Voltage Network		16	01-Jun-27	19-Jun-27	21-Jun-26	08-Jul-26	0%	0.00	0.00
Termination and Testing Works		16	01-Jun-27	19-Jun-27	21-Jun-26	08-Jul-26	0%	0.00	0.00
CO-R09-MV-TF-10	Termination Works of Medium Voltage Network-[Road 09]	16	01-Jun-27	19-Jun-27	21-Jun-26	08-Jul-26	0%	0.00	0.00
Road Works		57	31-Jul-27	06-Oct-27	24-Sep-26	30-Nov-26	0%	2,150,737.61	2,150,737.61
Bituminous Construction		27	31-Jul-27	31-Aug-27	24-Sep-26	26-Oct-26	0%	2,058,508.34	2,058,508.34
CO-R09-S1-RD-F-	Application of Prime Coat Layer for Road Works - S.W 01-[Road 09]	12	31-Jul-27	14-Aug-27	24-Sep-26	08-Oct-26	0%	576,151.93	576,151.93

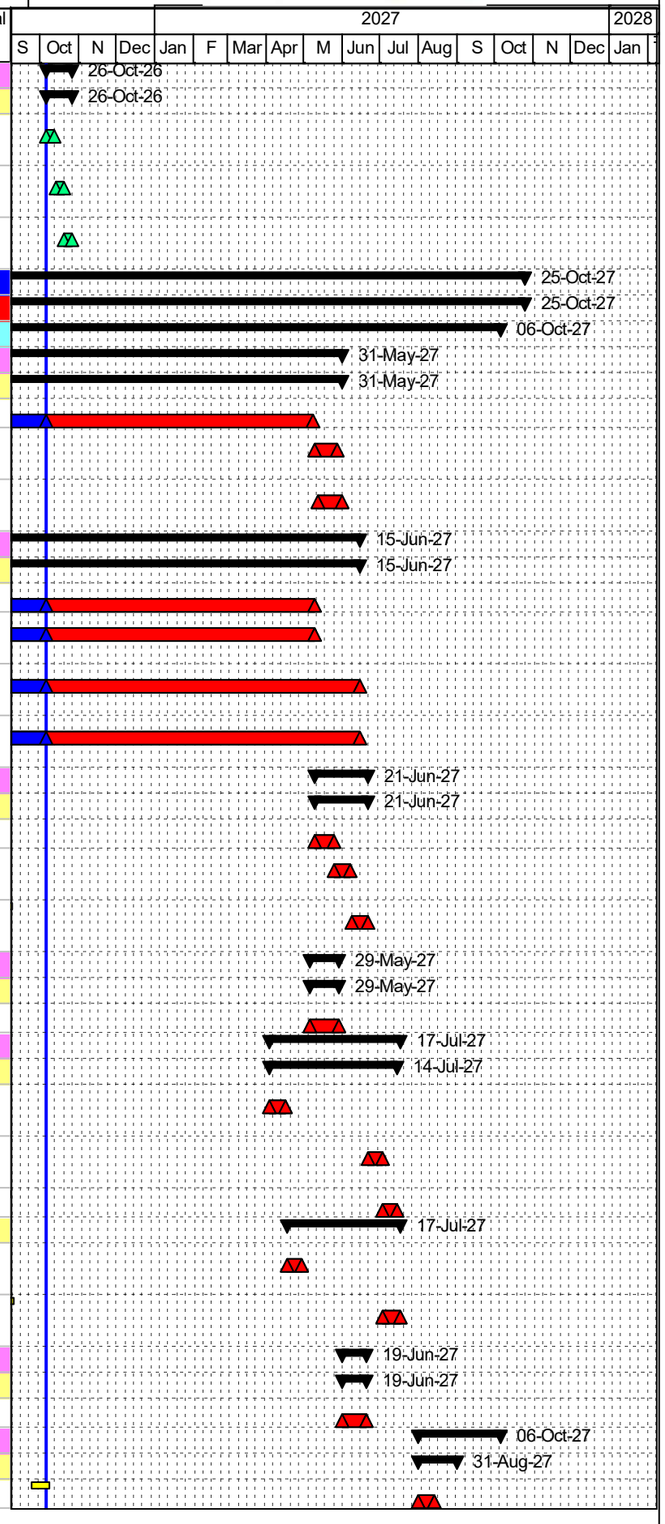

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09-S1-RD-F-1	Bituminous Base & Wearing Courses Layers for Road Works- S.W 01-[Road 09]	12	03-Aug-27	17-Aug-27	28-Sep-26	12-Oct-26	0%	453,102.24	453,102.24
CO-R09-S2-RD-F-	Application of Prime Coat Layer for Road Works- S.W 02-[Road 09]	18	07-Aug-27	28-Aug-27	01-Oct-26	22-Oct-26	0%	576,151.93	576,151.93
CO-R09-S2-RD-F-1	Bituminous Base & Wearing Courses Layers for Road Works- S.W 02-[Road 09]	18	10-Aug-27	31-Aug-27	05-Oct-26	26-Oct-26	0%	453,102.24	453,102.24
Traffic Signs Boards and Roads Marking		42	17-Aug-27	06-Oct-27	12-Oct-26	30-Nov-26	0%	92,229.28	92,229.28
CO-R09-S1-RD-F-	Application of Road Marking Works For Road Works- S.W 01-[Road 09]	12	17-Aug-27	31-Aug-27	12-Oct-26	26-Oct-26	0%	33,593.01	33,593.01
CO-R09-S2-RD-F-	Application of Road Marking Works For Road Works- S.W 02-[Road 09]	15	31-Aug-27	18-Sep-27	26-Oct-26	12-Nov-26	0%	33,593.01	33,593.01
CO-R09-S1-RD-F-	Installation Works of Traffic Signs Boards For Road Works- S.W 01-[Road 09]	12	31-Aug-27	14-Sep-27	26-Oct-26	09-Nov-26	0%	12,521.63	12,521.63
CO-R09-S2-RD-F-	Installation Works of Traffic Signs Boards For Road Works- S.W 02-[Road 09]	15	18-Sep-27	06-Oct-27	12-Nov-26	30-Nov-26	0%	12,521.63	12,521.63
Road 10 Local 2 (2352 LM)		163	17-Jun-26 A	20-Jul-27	04-May-26	31-Oct-26	12.79%	3,459,715.65	3,459,715.65
Sewage Network		27	19-Apr-27	25-May-27	29-Jul-26	29-Aug-26	0%	153,798.13	153,798.13
Testing and Finishes		27	19-Apr-27	25-May-27	29-Jul-26	29-Aug-26	0%	153,798.13	153,798.13
CO-R10-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 10]	12	19-Apr-27	02-May-27	29-Jul-26	11-Aug-26	0%	115,642.91	115,642.91
CO-R10-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 10]	12	03-May-27	22-May-27	12-Aug-26	25-Aug-26	0%	19,077.61	19,077.61
CO-R10-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 10]	12	06-May-27	25-May-27	16-Aug-26	29-Aug-26	0%	19,077.61	19,077.61
Storm Drainage Network		35	17-Jun-26 A	09-Jun-27	04-Aug-26	13-Sep-26	79.27%	558,232.55	558,232.55
Testing and Finishes		35	17-Jun-26 A	09-Jun-27	04-Aug-26	13-Sep-26	79.27%	558,232.55	558,232.55
CO-R10-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 10]	16	17-Jun-26 A	10-May-27	04-Aug-26	22-Aug-26	20%	27,795.73	27,795.73
CO-R10-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 10]	12	18-Jun-26 A	05-Jun-27	26-Aug-26	08-Sep-26	85%	502,641.74	502,641.74
CO-R10-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 10]	16	22-Jun-26 A	09-Jun-27	26-Aug-26	13-Sep-26	35%	27,795.08	27,795.08
Potable Water Network		32	26-Apr-27	07-Jun-27	08-Aug-26	03-Sep-26	0%	299,945.22	299,945.22
Testing and Finishes		32	26-Apr-27	07-Jun-27	08-Aug-26	03-Sep-26	0%	299,945.22	299,945.22
CO-R10-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 10]	12	26-Apr-27	09-May-27	08-Aug-26	20-Aug-26	0%	0.00	0.00
CO-R10-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 10]	12	10-May-27	29-May-27	22-Aug-26	03-Sep-26	0%	0.00	0.00
CO-R10-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 10]	12	25-May-27	07-Jun-27	12-Aug-26	25-Aug-26	0%	299,945.22	299,945.22
Irrigation Network		10	29-Apr-27	10-May-27	09-Aug-26	19-Aug-26	0%	100,762.62	100,762.62
Testing and Finishes		10	29-Apr-27	10-May-27	09-Aug-26	19-Aug-26	0%	100,762.62	100,762.62
CO-R10-IR-TF-12(	Final Testing (pressure tests) of Irrigation Network-[Road 10]	10	29-Apr-27	10-May-27	09-Aug-26	19-Aug-26	0%	100,762.62	100,762.62
Street Lighting Network		80	02-Jan-27	08-Apr-27	04-May-26	23-Jul-26	0%	190,052.00	190,052.00
Termination and Testing Works		80	02-Jan-27	08-Apr-27	04-May-26	23-Jul-26	0%	178,266.70	178,266.70
CO-R10-SL-TF-140	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 10]	12	02-Jan-27	14-Jan-27	04-May-26	17-May-26	0%	81,254.25	81,254.25
CO-R10-SL-TF-150	Termination Works For Panel Board Cables of Street Lighting Network-[Road 10]	12	24-Mar-27	06-Apr-27	08-Jul-26	21-Jul-26	0%	64,674.97	64,674.97
CO-R10-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 10]	2	07-Apr-27	08-Apr-27	22-Jul-26	23-Jul-26	0%	32,337.48	32,337.48
Earthing System Works		27	16-Jan-27	15-Feb-27	18-May-26	22-Jun-26	0%	11,785.30	11,785.30
CO-R10-SL-ES-140	Install Earthing System Works for Lighting Poles of Street Lighting Network-[Road 10]	12	16-Jan-27	28-Jan-27	18-May-26	04-Jun-26	0%	6,125.14	6,125.14
CO-R10-SL-ES-150	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network-[Road 10]	12	02-Feb-27	15-Feb-27	09-Jun-26	22-Jun-26	0%	5,660.16	5,660.16
Medium Voltage Network		7	19-Apr-27	26-Apr-27	09-Sep-26	16-Sep-26	0%	0.00	0.00
Termination and Testing Works		7	19-Apr-27	26-Apr-27	09-Sep-26	16-Sep-26	0%	0.00	0.00
CO-R10-MV-TF-14	Termination Works of Medium Voltage Network-[Road 10]	7	19-Apr-27	26-Apr-27	09-Sep-26	16-Sep-26	0%	0.00	0.00
Road Works		27	20-Jun-27	20-Jul-27	30-Sep-26	31-Oct-26	0%	2,156,925.13	2,156,925.13
Bituminous Construction		15	20-Jun-27	06-Jul-27	30-Sep-26	17-Oct-26	0%	2,064,314.89	2,064,314.89
CO-R10-S03-RD-I	Application of Prime Coat Layer for Road Works- S.W 05-[Road 10]	10	20-Jun-27	30-Jun-27	30-Sep-26	11-Oct-26	0%	577,776.85	577,776.85
CO-R10-S04-RD-I	Application of Prime Coat Layer for Road Works- S.W 06-[Road 10]	10	22-Jun-27	03-Jul-27	03-Oct-26	13-Oct-26	0%	577,776.85	577,776.85

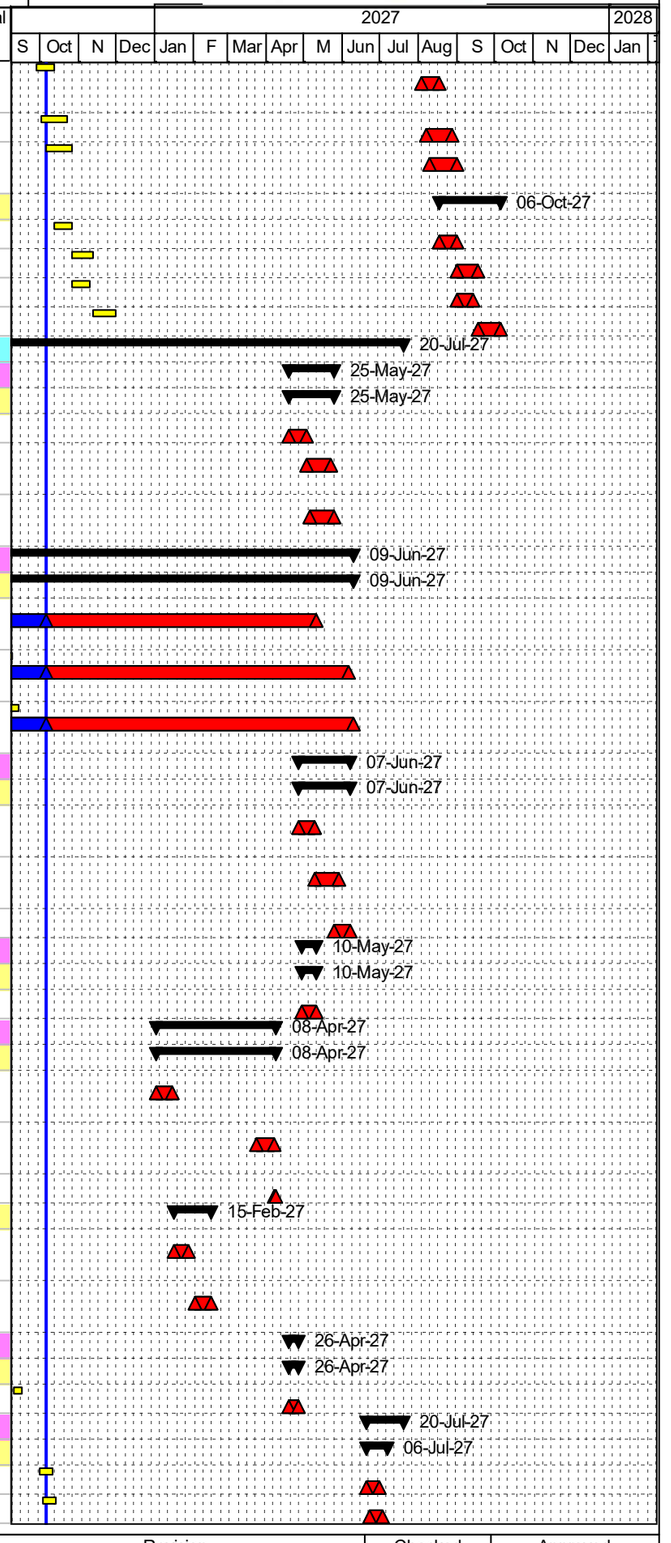

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10-S03-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 05-[Road 10]	10	23-Jun-27	04-Jul-27	04-Oct-26	14-Oct-26	0%	454,380.60	454,380.60
CO-R10-S04-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 06-[Road 10]	10	26-Jun-27	06-Jul-27	06-Oct-26	17-Oct-26	0%	454,380.60	454,380.60
Traffic Signs Boards and Roads Marking		14	05-Jul-27	20-Jul-27	15-Oct-26	31-Oct-26	0%	92,610.24	92,610.24
CO-R10-S03-RD-I	Application of Road Marking Works For Road Works- S.W 05-[Road 10]	12	05-Jul-27	18-Jul-27	15-Oct-26	28-Oct-26	0%	33,687.68	33,687.68
CO-R10-S03-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 05-[Road 10]	12	05-Jul-27	18-Jul-27	15-Oct-26	28-Oct-26	0%	12,617.44	12,617.44
CO-R10-S04-RD-I	Application of Road Marking Works For Road Works- S.W 06-[Road 10]	12	07-Jul-27	20-Jul-27	18-Oct-26	31-Oct-26	0%	33,687.68	33,687.68
CO-R10-S04-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 06-[Road 10]	10	10-Jul-27	20-Jul-27	20-Oct-26	31-Oct-26	0%	12,617.44	12,617.44
Road 11 Local 1 (670 LM)		145	22-Jun-26 A	30-Aug-27	18-May-26	11-Nov-26	26.99%	815,107.49	815,107.49
Sewage Network		27	03-May-27	08-Jun-27	12-Aug-26	12-Sep-26	0%	210,240.04	210,240.04
Testing and Finishes		27	03-May-27	08-Jun-27	12-Aug-26	12-Sep-26	0%	210,240.04	210,240.04
CO-R11-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 11]	12	03-May-27	22-May-27	12-Aug-26	25-Aug-26	0%	181,390.91	181,390.91
CO-R11-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 11]	12	23-May-27	05-Jun-27	26-Aug-26	08-Sep-26	0%	14,424.56	14,424.56
CO-R11-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 11]	12	26-May-27	08-Jun-27	30-Aug-26	12-Sep-26	0%	14,424.56	14,424.56
Storm Drainage Network		28	22-Jun-26 A	28-Jun-27	23-Aug-26	03-Oct-26	81.11%	271,250.20	271,250.20
Testing and Finishes		28	22-Jun-26 A	28-Jun-27	23-Aug-26	03-Oct-26	81.11%	271,250.20	271,250.20
CO-R11-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 11]	16	22-Jun-26 A	28-Jun-27	14-Sep-26	03-Oct-26	20%	8,111.50	8,111.50
CO-R11-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 11]	12	23-Jun-26 A	19-Jun-27	09-Sep-26	22-Sep-26	85%	255,027.20	255,027.20
CO-R11-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 11]	12	27-Jun-26 A	30-May-27	23-Aug-26	05-Sep-26	20%	8,111.50	8,111.50
Potable Water Network		32	10-May-27	21-Jun-27	26-Aug-26	22-Sep-26	0%	11,618.55	11,618.55
Testing and Finishes		32	10-May-27	21-Jun-27	26-Aug-26	22-Sep-26	0%	11,618.55	11,618.55
CO-R11-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 11]	12	10-May-27	29-May-27	26-Aug-26	08-Sep-26	0%	0.00	0.00
CO-R11-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 11]	12	30-May-27	12-Jun-27	09-Sep-26	22-Sep-26	0%	0.00	0.00
CO-R11-PW-TF-11	Testing Work for Main Line of Potable Water Network-[Road 11]	12	08-Jun-27	21-Jun-27	26-Aug-26	08-Sep-26	0%	11,618.55	11,618.55
Irrigation Network		10	11-May-27	27-May-27	23-Aug-26	02-Sep-26	0%	6,235.18	6,235.18
Testing and Finishes		10	11-May-27	27-May-27	23-Aug-26	02-Sep-26	0%	6,235.18	6,235.18
CO-R11-IR-TF-13(	Final Testing (pressure tests) of Irrigation Network-[Road 11]	10	11-May-27	27-May-27	23-Aug-26	02-Sep-26	0%	6,235.18	6,235.18
Street Lighting Network		80	07-Apr-27	14-Jul-27	18-May-26	10-Aug-26	0%	23,933.07	23,933.07
Termination and Testing Works		80	07-Apr-27	14-Jul-27	18-May-26	10-Aug-26	0%	23,933.07	23,933.07
CO-R11-SL-TF-160	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 11]	12	07-Apr-27	20-Apr-27	18-May-26	04-Jun-26	0%	23,933.07	23,933.07
CO-R11-SL-TF-170	Termination Works For Panel Board Cables of Street Lighting Network-[Road 11]	12	29-Jun-27	12-Jul-27	26-Jul-26	08-Aug-26	0%	0.00	0.00
CO-R11-SL-TF-38(	Testing Works For Panel Board Cables of Street Lighting Network-[Road 11]	2	13-Jul-27	14-Jul-27	09-Aug-26	10-Aug-26	0%	0.00	0.00
Medium Voltage Network		7	12-Jul-27	19-Jul-27	17-Sep-26	26-Sep-26	0%	0.00	0.00
Termination and Testing Works		7	12-Jul-27	19-Jul-27	17-Sep-26	26-Sep-26	0%	0.00	0.00
CO-R11-MV-TF-1(	Termination Works of Medium Voltage Network-[Road 11]	7	12-Jul-27	19-Jul-27	17-Sep-26	26-Sep-26	0%	0.00	0.00
Road Works		22	05-Aug-27	30-Aug-27	15-Oct-26	11-Nov-26	0%	291,830.45	291,830.45
Bituminous Construction		12	05-Aug-27	18-Aug-27	15-Oct-26	31-Oct-26	0%	265,183.32	265,183.32
CO-R11-S06-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 08-[Road 11]	12	05-Aug-27	18-Aug-27	18-Oct-26	31-Oct-26	0%	132,591.66	132,591.66
CO-R11-S05-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 07-[Road 11]	12	05-Aug-27	18-Aug-27	15-Oct-26	28-Oct-26	0%	132,591.66	132,591.66
Traffic Signs Boards and Roads Marking		10	19-Aug-27	30-Aug-27	29-Oct-26	11-Nov-26	0%	26,647.13	26,647.13
CO-R11-S06-RD-I	Application of Road Marking Works For Road Works- S.W 08-[Road 11]	10	19-Aug-27	30-Aug-27	01-Nov-26	11-Nov-26	0%	9,830.19	9,830.19
CO-R11-S06-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 08-[Road 11]	10	19-Aug-27	30-Aug-27	01-Nov-26	11-Nov-26	0%	3,493.38	3,493.38
CO-R11-S05-RD-I	Application of Road Marking Works For Road Works- S.W 07-[Road 11]	10	19-Aug-27	30-Aug-27	29-Oct-26	09-Nov-26	0%	9,830.19	9,830.19

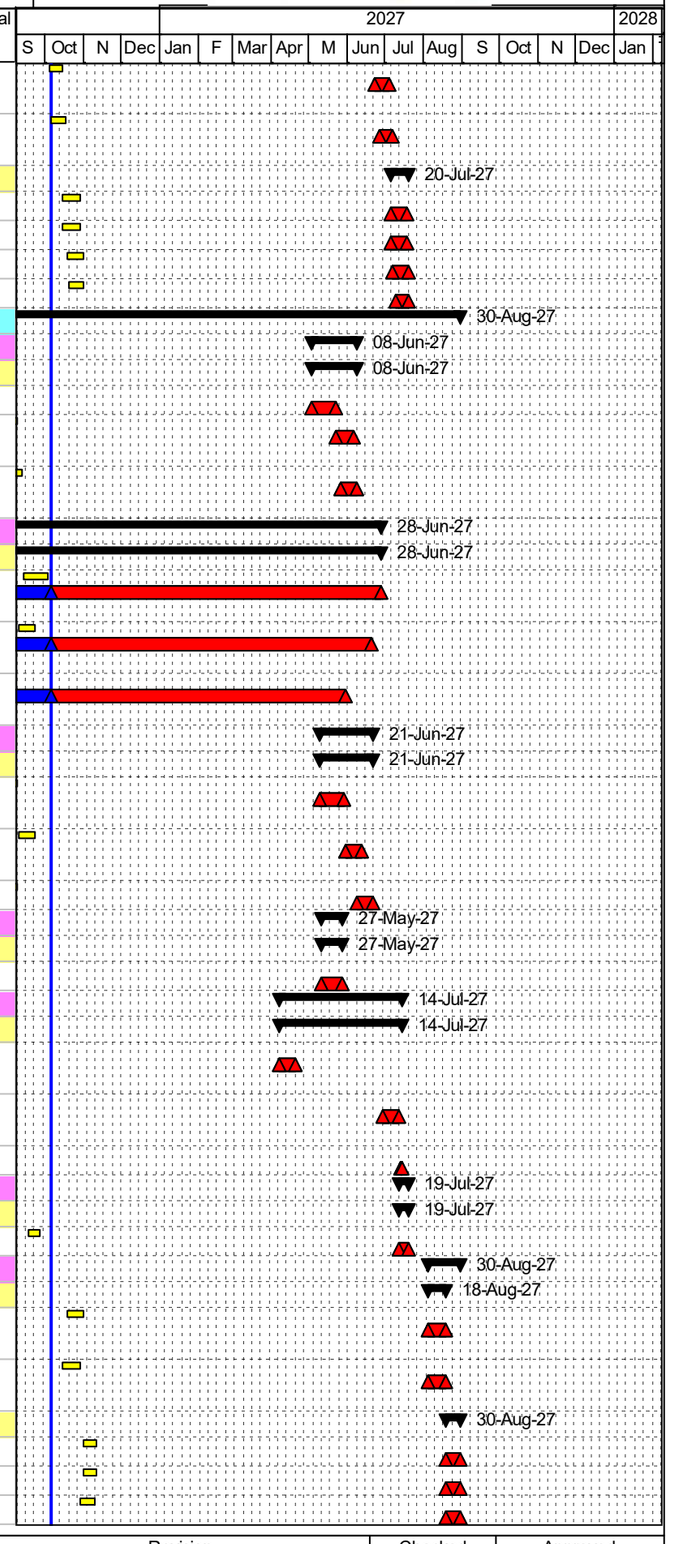

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R11-S05-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 07-[Road 11]	10	19-Aug-27	30-Aug-27	29-Oct-26	09-Nov-26	0%	3,493.38	3,493.38
Road 14 Local 1 (584 LM)		120	21-Apr-27	13-Sep-27	13-Jun-26	23-Nov-26	0%	1,081,359.15	1,081,359.15
Sewage Network		27	23-May-27	22-Jun-27	26-Aug-26	27-Sep-26	0%	48,450.33	48,450.33
Testing and Finishes		27	23-May-27	22-Jun-27	26-Aug-26	27-Sep-26	0%	48,450.33	48,450.33
CO-R14-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 14]	12	23-May-27	05-Jun-27	26-Aug-26	08-Sep-26	0%	31,128.01	31,128.01
CO-R14-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 14]	12	06-Jun-27	19-Jun-27	09-Sep-26	22-Sep-26	0%	8,661.16	8,661.16
CO-R14-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 14]	12	09-Jun-27	22-Jun-27	13-Sep-26	27-Sep-26	0%	8,661.16	8,661.16
Potable Water Network		32	30-May-27	05-Jul-27	09-Sep-26	07-Oct-26	0%	44,447.80	44,447.80
Testing and Finishes		32	30-May-27	05-Jul-27	09-Sep-26	07-Oct-26	0%	44,447.80	44,447.80
CO-R14-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 14]	12	30-May-27	12-Jun-27	09-Sep-26	22-Sep-26	0%	0.00	0.00
CO-R14-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 14]	12	13-Jun-27	26-Jun-27	24-Sep-26	07-Oct-26	0%	0.00	0.00
CO-R14-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 14]	12	22-Jun-27	05-Jul-27	09-Sep-26	22-Sep-26	0%	44,447.80	44,447.80
Irrigation Network		10	29-May-27	08-Jun-27	03-Sep-26	14-Sep-26	0%	24,385.30	24,385.30
Testing and Finishes		10	29-May-27	08-Jun-27	03-Sep-26	14-Sep-26	0%	24,385.30	24,385.30
CO-R11-IR-TF-14(	Final Testing (pressure tests) of Irrigation Network-[Road 14]	10	29-May-27	08-Jun-27	03-Sep-26	14-Sep-26	0%	24,385.30	24,385.30
Street Lighting Network		80	21-Apr-27	28-Jul-27	13-Jun-26	31-Aug-26	0%	34,865.46	34,865.46
Termination and Testing Works		80	21-Apr-27	28-Jul-27	13-Jun-26	31-Aug-26	0%	34,865.46	34,865.46
CO-R11-SL-TF-180	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 14]	12	21-Apr-27	04-May-27	13-Jun-26	25-Jun-26	0%	34,865.46	34,865.46
CO-R11-SL-TF-190	Termination Works For Panel Board Cables of Street Lighting Network-[Road 14]	12	13-Jul-27	26-Jul-27	16-Aug-26	29-Aug-26	0%	0.00	0.00
CO-R14-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 14]	2	27-Jul-27	28-Jul-27	30-Aug-26	31-Aug-26	0%	0.00	0.00
Medium Voltage Network		7	20-Jul-27	27-Jul-27	27-Sep-26	04-Oct-26	0%	0.00	0.00
Termination and Testing Works		7	20-Jul-27	27-Jul-27	27-Sep-26	04-Oct-26	0%	0.00	0.00
CO-R11-MV-TF-18	Termination Works of Medium Voltage Network-[Road 14]	7	20-Jul-27	27-Jul-27	27-Sep-26	04-Oct-26	0%	0.00	0.00
Road Works		26	15-Aug-27	13-Sep-27	26-Oct-26	23-Nov-26	0%	929,210.26	929,210.26
Bituminous Construction		15	15-Aug-27	31-Aug-27	26-Oct-26	11-Nov-26	0%	888,935.43	888,935.43
CO-R11-S07-RD-F	Application of Prime Coat Layer for Road Works- S.W 09-[Road 14]	12	15-Aug-27	28-Aug-27	26-Oct-26	08-Nov-26	0%	248,802.26	248,802.26
CO-R11-S08-RD-F	Application of Prime Coat Layer for Road Works- S.W 10-[Road 14]	10	15-Aug-27	25-Aug-27	28-Oct-26	08-Nov-26	0%	248,802.26	248,802.26
CO-R11-S07-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 09-[Road 14]	10	21-Aug-27	31-Aug-27	01-Nov-26	11-Nov-26	0%	195,665.46	195,665.46
CO-R11-S08-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 10-[Road 14]	10	21-Aug-27	31-Aug-27	01-Nov-26	11-Nov-26	0%	195,665.46	195,665.46
Traffic Signs Boards and Roads Marking		12	31-Aug-27	13-Sep-27	10-Nov-26	23-Nov-26	0%	40,274.83	40,274.83
CO-R11-S07-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 09-[Road 14]	12	31-Aug-27	13-Sep-27	10-Nov-26	23-Nov-26	0%	5,630.68	5,630.68
CO-R11-S07-RD-F	Application of Road Marking Works For Road Works- S.W 09-[Road 14]	10	01-Sep-27	12-Sep-27	12-Nov-26	23-Nov-26	0%	14,506.73	14,506.73
CO-R11-S08-RD-F	Application of Road Marking Works For Road Works- S.W 10-[Road 14]	10	01-Sep-27	12-Sep-27	12-Nov-26	23-Nov-26	0%	14,506.73	14,506.73
CO-R11-S08-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 10-[Road 14]	10	01-Sep-27	12-Sep-27	12-Nov-26	23-Nov-26	0%	5,630.68	5,630.68
Road 15 Local 1 (556 LM)		119	05-May-27	27-Sep-27	27-Jun-26	07-Dec-26	0%	117,781.16	117,781.16
Sewage Network		27	06-Jun-27	06-Jul-27	09-Sep-26	11-Oct-26	0%	44,914.62	44,914.62
Testing and Finishes		27	06-Jun-27	06-Jul-27	09-Sep-26	11-Oct-26	0%	44,914.62	44,914.62
CO-R15-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 15]	12	06-Jun-27	19-Jun-27	09-Sep-26	22-Sep-26	0%	20,768.02	20,768.02
CO-R15-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 15]	12	20-Jun-27	03-Jul-27	24-Sep-26	07-Oct-26	0%	12,073.30	12,073.30
CO-R15-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 15]	12	23-Jun-27	06-Jul-27	28-Sep-26	11-Oct-26	0%	12,073.30	12,073.30
Storm Drainage Network		45	31-May-27	21-Jul-27	20-Sep-26	09-Nov-26	0%	13,654.68	13,654.68
Testing and Finishes		45	31-May-27	21-Jul-27	20-Sep-26	09-Nov-26	0%	13,654.68	13,654.68
CO-R15-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 15]	12	31-May-27	13-Jun-27	20-Sep-26	04-Oct-26	0%	6,827.34	6,827.34

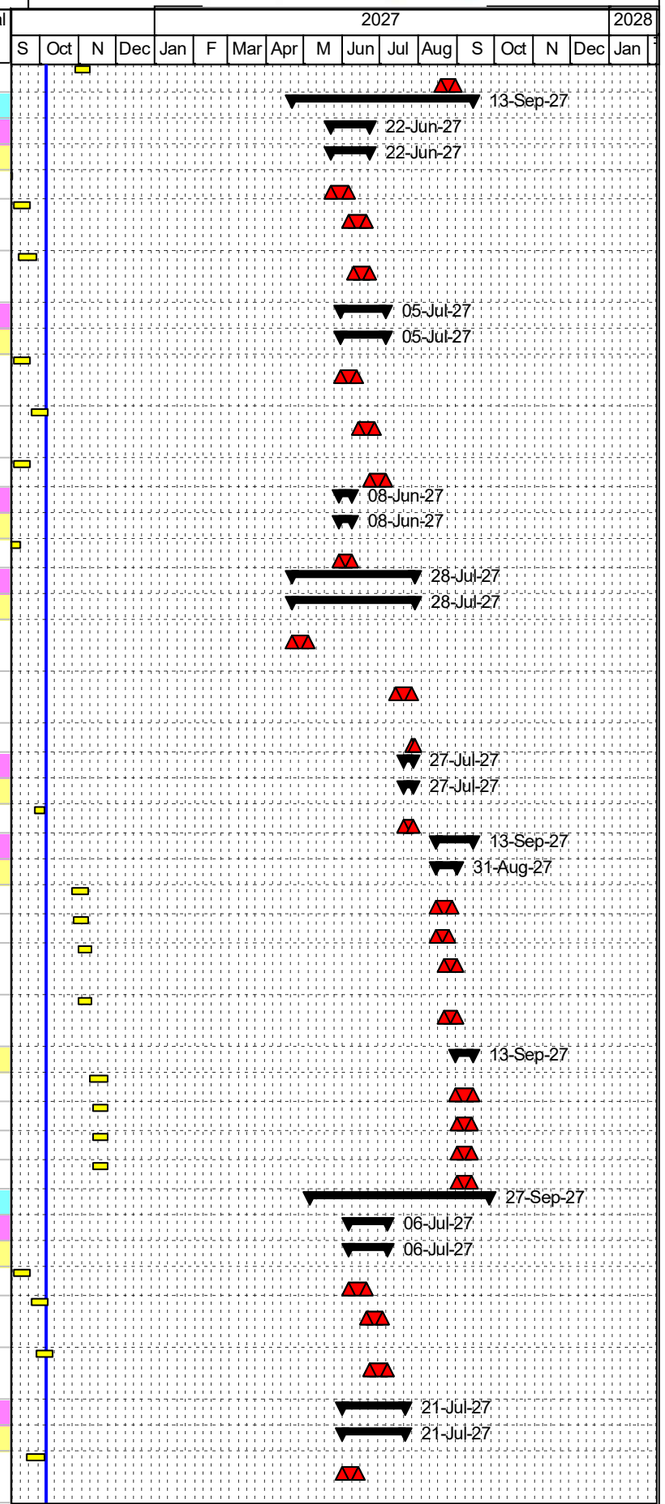

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R15-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 15]	16	04-Jul-27	21-Jul-27	22-Oct-26	09-Nov-26	0%	6,827.34	6,827.34
Potable Water Network		32	13-Jun-27	19-Jul-27	24-Sep-26	21-Oct-26	0%	9,843.19	9,843.19
Testing and Finishes		32	13-Jun-27	19-Jul-27	24-Sep-26	21-Oct-26	0%	9,843.19	9,843.19
CO-R15-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 15]	12	13-Jun-27	26-Jun-27	24-Sep-26	07-Oct-26	0%	0.00	0.00
CO-R15-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 15]	12	27-Jun-27	10-Jul-27	08-Oct-26	21-Oct-26	0%	0.00	0.00
CO-R15-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 15]	12	06-Jul-27	19-Jul-27	24-Sep-26	07-Oct-26	0%	9,843.19	9,843.19
Irrigation Network		10	09-Jun-27	20-Jun-27	15-Sep-26	27-Sep-26	0%	5,248.07	5,248.07
Testing and Finishes		10	09-Jun-27	20-Jun-27	15-Sep-26	27-Sep-26	0%	5,248.07	5,248.07
CO-R15-IR-TF-15(	Final Testing (pressure tests) of Irrigation Network-[Road 15]	10	09-Jun-27	20-Jun-27	15-Sep-26	27-Sep-26	0%	5,248.07	5,248.07
Street Lighting Network		96	05-May-27	30-Aug-27	27-Jun-26	04-Oct-26	0%	20,091.96	20,091.96
Termination and Testing Works		96	05-May-27	30-Aug-27	27-Jun-26	04-Oct-26	0%	20,091.96	20,091.96
CO-R15-SL-TF-200	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 15]	12	05-May-27	24-May-27	27-Jun-26	09-Jul-26	0%	20,091.96	20,091.96
CO-R15-SL-TF-210	Termination Works For Panel Board Cables of Street Lighting Network-[Road 15]	12	29-Jul-27	11-Aug-27	01-Sep-26	14-Sep-26	0%	0.00	0.00
CO-R15-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 15]	16	12-Aug-27	30-Aug-27	15-Sep-26	04-Oct-26	0%	0.00	0.00
Medium Voltage Network		7	28-Jul-27	04-Aug-27	05-Oct-26	12-Oct-26	0%	0.00	0.00
Termination and Testing Works		7	28-Jul-27	04-Aug-27	05-Oct-26	12-Oct-26	0%	0.00	0.00
CO-R15-MV-TF-2(	Termination Works of Medium Voltage Network-[Road 15]	7	28-Jul-27	04-Aug-27	05-Oct-26	12-Oct-26	0%	0.00	0.00
Road Works		12	13-Sep-27	27-Sep-27	24-Nov-26	07-Dec-26	0%	24,028.64	24,028.64
Traffic Signs Boards and Roads Marking		12	13-Sep-27	27-Sep-27	24-Nov-26	07-Dec-26	0%	24,028.64	24,028.64
CO-R15-S09-RD-I	Application of Road Marking Works For Road Works- S.W 11-[Road 15]	10	13-Sep-27	25-Sep-27	24-Nov-26	05-Dec-26	0%	8,274.04	8,274.04
CO-R15-S10-RD-I	Application of Road Marking Works For Road Works- S.W 12-[Road 15]	10	13-Sep-27	25-Sep-27	24-Nov-26	05-Dec-26	0%	8,274.04	8,274.04
CO-R15-S10-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 12-[Road 15]	12	13-Sep-27	27-Sep-27	24-Nov-26	07-Dec-26	0%	4,178.79	4,178.79
CO-R15-S09-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 11-[Road 15]	10	14-Sep-27	26-Sep-27	24-Nov-26	05-Dec-26	0%	3,301.76	3,301.76
Road 16 Local 1 (527 LM)		267	21-Nov-26	09-Oct-27	11-Jul-26	19-Dec-26	0%	163,353.98	163,353.98
Sewage Network		27	20-Jun-27	20-Jul-27	24-Sep-26	25-Oct-26	0%	28,932.88	28,932.88
Testing and Finishes		27	20-Jun-27	20-Jul-27	24-Sep-26	25-Oct-26	0%	28,932.88	28,932.88
CO-R16-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 16]	12	20-Jun-27	03-Jul-27	24-Sep-26	07-Oct-26	0%	14,883.24	14,883.24
CO-R16-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 16]	12	04-Jul-27	17-Jul-27	08-Oct-26	21-Oct-26	0%	7,024.82	7,024.82
CO-R16-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 16]	12	07-Jul-27	20-Jul-27	12-Oct-26	25-Oct-26	0%	7,024.82	7,024.82
Storm Drainage Network		216	21-Nov-26	09-Aug-27	10-Sep-26	28-Nov-26	0%	78,485.95	78,485.95
Testing and Finishes		216	21-Nov-26	09-Aug-27	10-Sep-26	28-Nov-26	0%	78,485.95	78,485.95
CO-R16-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 16]	16	21-Nov-26	08-Dec-26	10-Sep-26	29-Sep-26	0%	65,471.79	65,471.79
CO-R16-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 16]	12	14-Jun-27	27-Jun-27	05-Oct-26	18-Oct-26	0%	6,507.08	6,507.08
CO-R16-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 16]	16	22-Jul-27	09-Aug-27	10-Nov-26	28-Nov-26	0%	6,507.08	6,507.08
Potable Water Network		32	27-Jun-27	02-Aug-27	08-Oct-26	04-Nov-26	0%	9,456.46	9,456.46
Testing and Finishes		32	27-Jun-27	02-Aug-27	08-Oct-26	04-Nov-26	0%	9,456.46	9,456.46
CO-R16-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 16]	12	27-Jun-27	10-Jul-27	08-Oct-26	21-Oct-26	0%	0.00	0.00
CO-R16-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 16]	12	11-Jul-27	24-Jul-27	22-Oct-26	04-Nov-26	0%	0.00	0.00
CO-R16-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 16]	12	20-Jul-27	02-Aug-27	08-Oct-26	21-Oct-26	0%	9,456.46	9,456.46
Irrigation Network		10	21-Jun-27	01-Jul-27	28-Sep-26	08-Oct-26	0%	5,001.98	5,001.98
Testing and Finishes		10	21-Jun-27	01-Jul-27	28-Sep-26	08-Oct-26	0%	5,001.98	5,001.98
CO-R16-IR-TF-16(	Final Testing (pressure tests) of Irrigation Network-[Road 16]	10	21-Jun-27	01-Jul-27	28-Sep-26	08-Oct-26	0%	5,001.98	5,001.98
Street Lighting Network		86	25-May-27	01-Sep-27	11-Jul-26	06-Oct-26	0%	18,910.08	18,910.08
Termination and Testing Works		86	25-May-27	01-Sep-27	11-Jul-26	06-Oct-26	0%	18,910.08	18,910.08

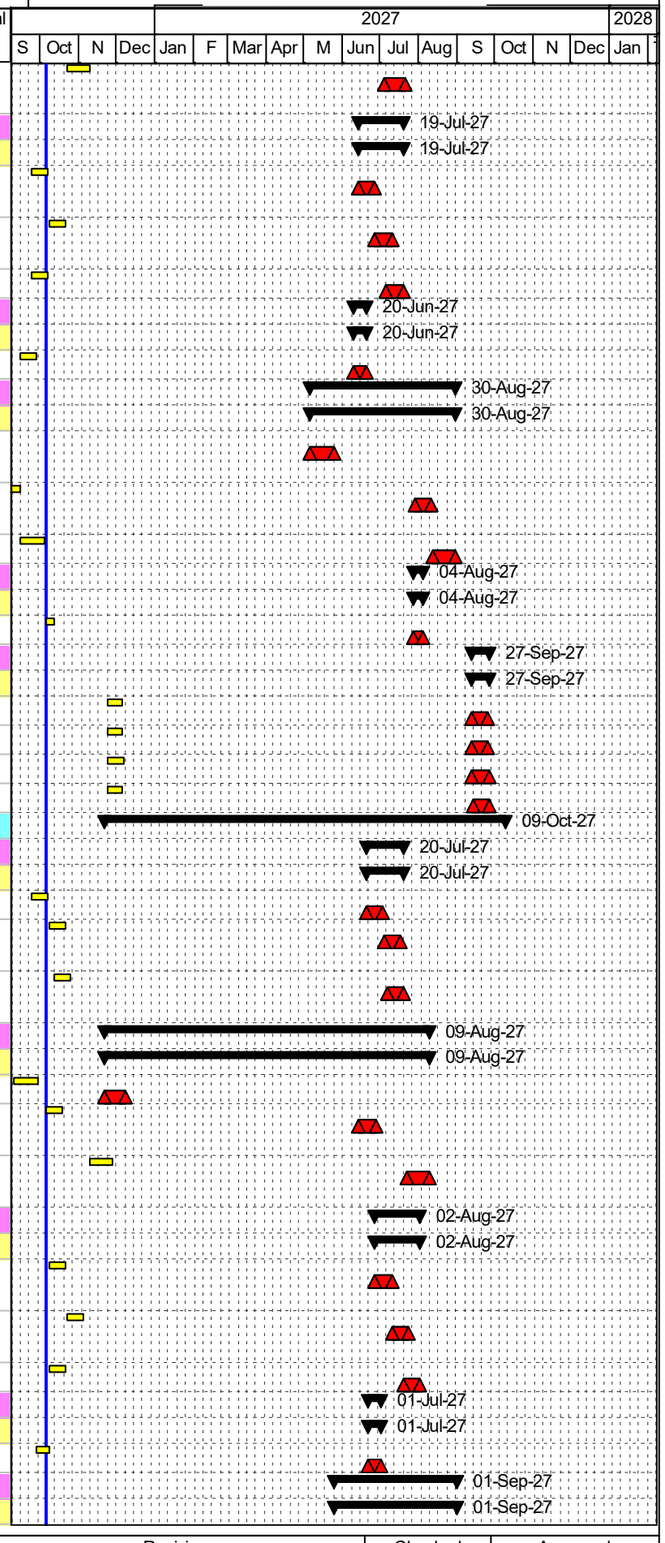

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R16-SL-TF-220	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 16]	12	25-May-27	07-Jun-27	11-Jul-26	23-Jul-26	0%	18,910.08	18,910.08
CO-R16-SL-TF-230	Termination Works For Panel Board Cables of Street Lighting Network-[Road 16]	12	12-Aug-27	25-Aug-27	15-Sep-26	29-Sep-26	0%	0.00	0.00
CO-R16-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 16]	2	31-Aug-27	01-Sep-27	05-Oct-26	06-Oct-26	0%	0.00	0.00
Medium Voltage Network		7	05-Aug-27	12-Aug-27	13-Oct-26	20-Oct-26	0%	0.00	0.00
Termination and Testing Works		7	05-Aug-27	12-Aug-27	13-Oct-26	20-Oct-26	0%	0.00	0.00
CO-R16-MV-TF-22	Termination Works of Medium Voltage Network-[Road 16]	7	05-Aug-27	12-Aug-27	13-Oct-26	20-Oct-26	0%	0.00	0.00
Road Works		12	26-Sep-27	09-Oct-27	06-Dec-26	19-Dec-26	0%	22,566.65	22,566.65
Traffic Signs Boards and Roads Marking		12	26-Sep-27	09-Oct-27	06-Dec-26	19-Dec-26	0%	22,566.65	22,566.65
CO-R16-S11-RD-F	Application of Road Marking Works For Road Works- S.W 13-[Road 16]	10	26-Sep-27	06-Oct-27	06-Dec-26	16-Dec-26	0%	7,885.75	7,885.75
CO-R16-S12-RD-I	Application of Road Marking Works For Road Works- S.W 14-[Road 16]	10	26-Sep-27	06-Oct-27	06-Dec-26	16-Dec-26	0%	7,885.75	7,885.75
CO-R16-S11-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 13-[Road 16]	10	27-Sep-27	07-Oct-27	06-Dec-26	16-Dec-26	0%	3,397.57	3,397.57
CO-R16-S12-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 14-[Road 16]	10	28-Sep-27	09-Oct-27	08-Dec-26	19-Dec-26	0%	3,397.57	3,397.57
Road 17 Local 1 (500 LM)		260	09-Dec-26	19-Oct-27	25-Jul-26	28-Dec-26	0%	145,258.19	145,258.19
Sewage Network		27	04-Jul-27	03-Aug-27	08-Oct-26	08-Nov-26	0%	28,783.37	28,783.37
Testing and Finishes		27	04-Jul-27	03-Aug-27	08-Oct-26	08-Nov-26	0%	28,783.37	28,783.37
CO-R17-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 17]	12	04-Jul-27	17-Jul-27	08-Oct-26	21-Oct-26	0%	15,594.88	15,594.88
CO-R17-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 17]	12	18-Jul-27	31-Jul-27	22-Oct-26	04-Nov-26	0%	6,594.24	6,594.24
CO-R17-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 17]	12	21-Jul-27	03-Aug-27	26-Oct-26	08-Nov-26	0%	6,594.24	6,594.24
Storm Drainage Network		212	09-Dec-26	23-Aug-27	04-Oct-26	12-Dec-26	0%	64,596.19	64,596.19
Testing and Finishes		212	09-Dec-26	23-Aug-27	04-Oct-26	12-Dec-26	0%	64,596.19	64,596.19
CO-R17-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 17]	16	09-Dec-26	27-Dec-26	04-Oct-26	21-Oct-26	0%	52,222.09	52,222.09
CO-R17-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 17]	12	28-Jun-27	11-Jul-27	19-Oct-26	01-Nov-26	0%	6,187.05	6,187.05
CO-R17-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 17]	12	10-Aug-27	23-Aug-27	29-Nov-26	12-Dec-26	0%	6,187.05	6,187.05
Potable Water Network		32	11-Jul-27	16-Aug-27	22-Oct-26	18-Nov-26	0%	9,062.59	9,062.59
Testing and Finishes		32	11-Jul-27	16-Aug-27	22-Oct-26	18-Nov-26	0%	9,062.59	9,062.59
CO-R17-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 17]	12	11-Jul-27	24-Jul-27	22-Oct-26	04-Nov-26	0%	0.00	0.00
CO-R17-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 17]	12	25-Jul-27	07-Aug-27	05-Nov-26	18-Nov-26	0%	0.00	0.00
CO-R17-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 17]	12	03-Aug-27	16-Aug-27	22-Oct-26	04-Nov-26	0%	9,062.59	9,062.59
Irrigation Network		10	03-Jul-27	13-Jul-27	18-Oct-26	28-Oct-26	0%	4,755.81	4,755.81
Testing and Finishes		10	03-Jul-27	13-Jul-27	18-Oct-26	28-Oct-26	0%	4,755.81	4,755.81
CO-R17-IR-TF-17(	Final Testing (pressure tests) of Irrigation Network-[Road 17]	10	03-Jul-27	13-Jul-27	18-Oct-26	28-Oct-26	0%	4,755.81	4,755.81
Street Lighting Network		82	08-Jun-27	11-Sep-27	25-Jul-26	15-Oct-26	0%	18,023.67	18,023.67
Termination and Testing Works		82	08-Jun-27	11-Sep-27	25-Jul-26	15-Oct-26	0%	18,023.67	18,023.67
CO-R17-SL-TF-240	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 17]	12	08-Jun-27	21-Jun-27	25-Jul-26	06-Aug-26	0%	18,023.67	18,023.67
CO-R17-SL-TF-250	Termination Works For Panel Board Cables of Street Lighting Network-[Road 17]	12	26-Aug-27	08-Sep-27	30-Sep-26	13-Oct-26	0%	0.00	0.00
CO-R17-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 17]	2	09-Sep-27	11-Sep-27	14-Oct-26	15-Oct-26	0%	0.00	0.00
Medium Voltage Network		7	14-Aug-27	21-Aug-27	21-Oct-26	28-Oct-26	0%	0.00	0.00
Termination and Testing Works		7	14-Aug-27	21-Aug-27	21-Oct-26	28-Oct-26	0%	0.00	0.00
CO-R17-MV-TF-24	Termination Works of Medium Voltage Network-[Road 17]	7	14-Aug-27	21-Aug-27	21-Oct-26	28-Oct-26	0%	0.00	0.00
Road Works		11	07-Oct-27	19-Oct-27	17-Dec-26	28-Dec-26	0%	20,036.56	20,036.56
Traffic Signs Boards and Roads Marking		11	07-Oct-27	19-Oct-27	17-Dec-26	28-Dec-26	0%	20,036.56	20,036.56
CO-R17-S13-RD-I	Application of Road Marking Works For Road Works- S.W 15-[Road 17]	10	07-Oct-27	18-Oct-27	17-Dec-26	28-Dec-26	0%	7,497.74	7,497.74
CO-R17-S14-RD-I	Application of Road Marking Works For Road Works- S.W 16-[Road 17]	10	07-Oct-27	18-Oct-27	17-Dec-26	28-Dec-26	0%	7,497.74	7,497.74
CO-R17-S13-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 15-[Road 17]	10	09-Oct-27	19-Oct-27	17-Dec-26	28-Dec-26	0%	2,520.54	2,520.54

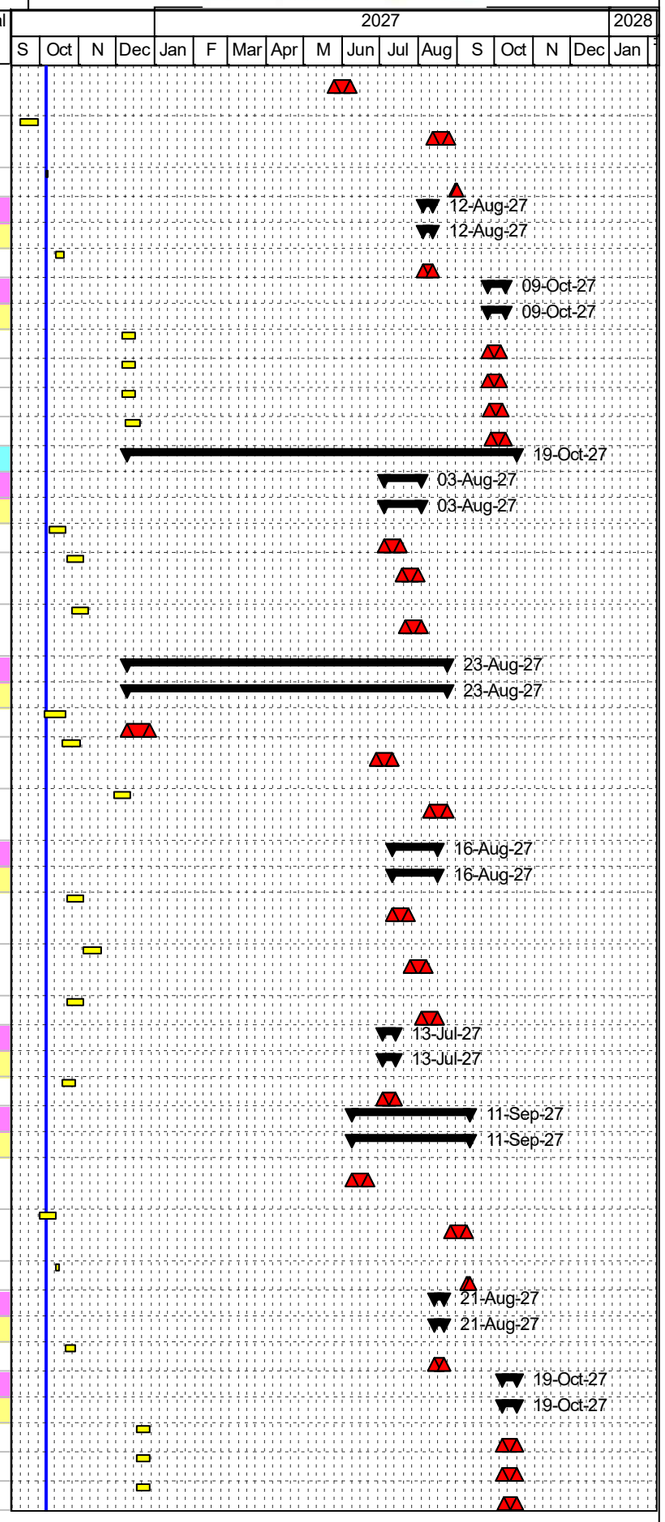

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R17-S14-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 16-[Road 17]	7	11-Oct-27	18-Oct-27	21-Dec-26	28-Dec-26	0%	2,520.54	2,520.54
Road 18 Local 1 (479 LM)		159	17-Apr-27	25-Oct-27	16-Jun-26	19-Dec-26	0%	164,388.34	164,388.34
Sewage Network		27	09-May-27	14-Jun-27	20-Aug-26	16-Sep-26	0%	29,758.61	29,758.61
Testing and Finishes		27	09-May-27	14-Jun-27	20-Aug-26	16-Sep-26	0%	29,758.61	29,758.61
CO-R18-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 18]	12	09-May-27	27-May-27	20-Aug-26	02-Sep-26	0%	12,906.70	12,906.70
CO-R18-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 18]	12	29-May-27	10-Jun-27	03-Sep-26	16-Sep-26	0%	8,425.95	8,425.95
CO-R18-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 18]	12	01-Jun-27	14-Jun-27	03-Sep-26	16-Sep-26	0%	8,425.95	8,425.95
Storm Drainage Network		44	09-May-27	04-Jul-27	03-Aug-26	09-Nov-26	0%	81,227.40	81,227.40
Testing and Finishes		44	09-May-27	04-Jul-27	03-Aug-26	09-Nov-26	0%	81,227.40	81,227.40
CO-R18-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 18]	16	09-May-27	01-Jun-27	04-Oct-26	21-Oct-26	0%	69,261.98	69,261.98
CO-R18-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 18]	16	10-May-27	02-Jun-27	03-Aug-26	20-Aug-26	0%	5,982.71	5,982.71
CO-R18-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 18]	16	16-Jun-27	04-Jul-27	22-Oct-26	09-Nov-26	0%	5,982.71	5,982.71
Potable Water Network		72	08-Jun-27	30-Aug-27	26-Aug-26	18-Nov-26	0%	10,265.70	10,265.70
Testing and Finishes		72	08-Jun-27	30-Aug-27	26-Aug-26	18-Nov-26	0%	10,265.70	10,265.70
CO-R18-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 18]	12	08-Jun-27	21-Jun-27	26-Aug-26	08-Sep-26	0%	0.00	0.00
CO-R18-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 18]	12	22-Jun-27	05-Jul-27	09-Sep-26	22-Sep-26	0%	0.00	0.00
CO-R18-PW-TF-1'	Testing Work for Main Line of Potable Water Network-[Road 18]	12	17-Aug-27	30-Aug-27	05-Nov-26	18-Nov-26	0%	10,265.70	10,265.70
Irrigation Network		16	30-May-27	16-Jun-27	17-Aug-26	03-Sep-26	0%	4,598.97	4,598.97
Testing and Finishes		16	30-May-27	16-Jun-27	17-Aug-26	03-Sep-26	0%	4,598.97	4,598.97
CO-R18-IR-TF-11(	Final Testing (pressure tests) of Irrigation Network-[Road 18]	16	30-May-27	16-Jun-27	17-Aug-26	03-Sep-26	0%	4,598.97	4,598.97
Street Lighting Network		76	17-Apr-27	19-Jul-27	16-Jun-26	12-Sep-26	0%	17,432.73	17,432.73
Termination and Testing Works		76	17-Apr-27	19-Jul-27	16-Jun-26	12-Sep-26	0%	17,432.73	17,432.73
CO-R18-SL-TF-120	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 18]	12	17-Apr-27	01-May-27	16-Jun-26	30-Jun-26	0%	17,432.73	17,432.73
CO-R18-SL-TF-130	Termination Works For Panel Board Cables of Street Lighting Network-[Road 18]	12	03-Jul-27	17-Jul-27	26-Aug-26	09-Sep-26	0%	0.00	0.00
CO-R18-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 18]	2	17-Jul-27	19-Jul-27	09-Sep-26	12-Sep-26	0%	0.00	0.00
Medium Voltage Network		16	20-Jun-27	07-Jul-27	09-Jul-26	27-Jul-26	0%	0.00	0.00
Termination and Testing Works		16	20-Jun-27	07-Jul-27	09-Jul-26	27-Jul-26	0%	0.00	0.00
CO-R18-MV-TF-12	Termination Works of Medium Voltage Network-[Road 18]	16	20-Jun-27	07-Jul-27	09-Jul-26	27-Jul-26	0%	0.00	0.00
Road Works		34	14-Sep-27	25-Oct-27	09-Nov-26	19-Dec-26	0%	21,104.95	21,104.95
Traffic Signs Boards and Roads Marking		34	14-Sep-27	25-Oct-27	09-Nov-26	19-Dec-26	0%	21,104.95	21,104.95
CO-R18-S15-RD-I	Application of Road Marking Works For Road Works- S.W 03-[Road 18]	12	14-Sep-27	29-Sep-27	09-Nov-26	23-Nov-26	0%	7,250.71	7,250.71
CO-R18-S15-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 03-[Road 18]	12	29-Sep-27	13-Oct-27	23-Nov-26	07-Dec-26	0%	3,301.76	3,301.76
CO-R18-S16-RD-I	Application of Road Marking Works For Road Works- S.W 04-[Road 18]	15	06-Oct-27	24-Oct-27	30-Nov-26	17-Dec-26	0%	7,250.71	7,250.71
CO-R18-S16-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 04-[Road 18]	10	13-Oct-27	25-Oct-27	07-Dec-26	19-Dec-26	0%	3,301.76	3,301.76
Independent Works		320	16-Sep-26 A	25-Oct-27	15-Feb-26	28-Dec-26	0%	4,695,554.78	4,695,554.78
Tie In To Existing Networks		148	29-Apr-27	25-Oct-27	02-Sep-26	28-Dec-26	0%	0.00	0.00
Phase 2 Block "J"		148	29-Apr-27	25-Oct-27	02-Sep-26	28-Dec-26	0%	0.00	0.00
Road 09 Local 2 (2278 LM)		69	14-Jul-27	03-Oct-27	17-Oct-26	20-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R09	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R09	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R09	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R09	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00

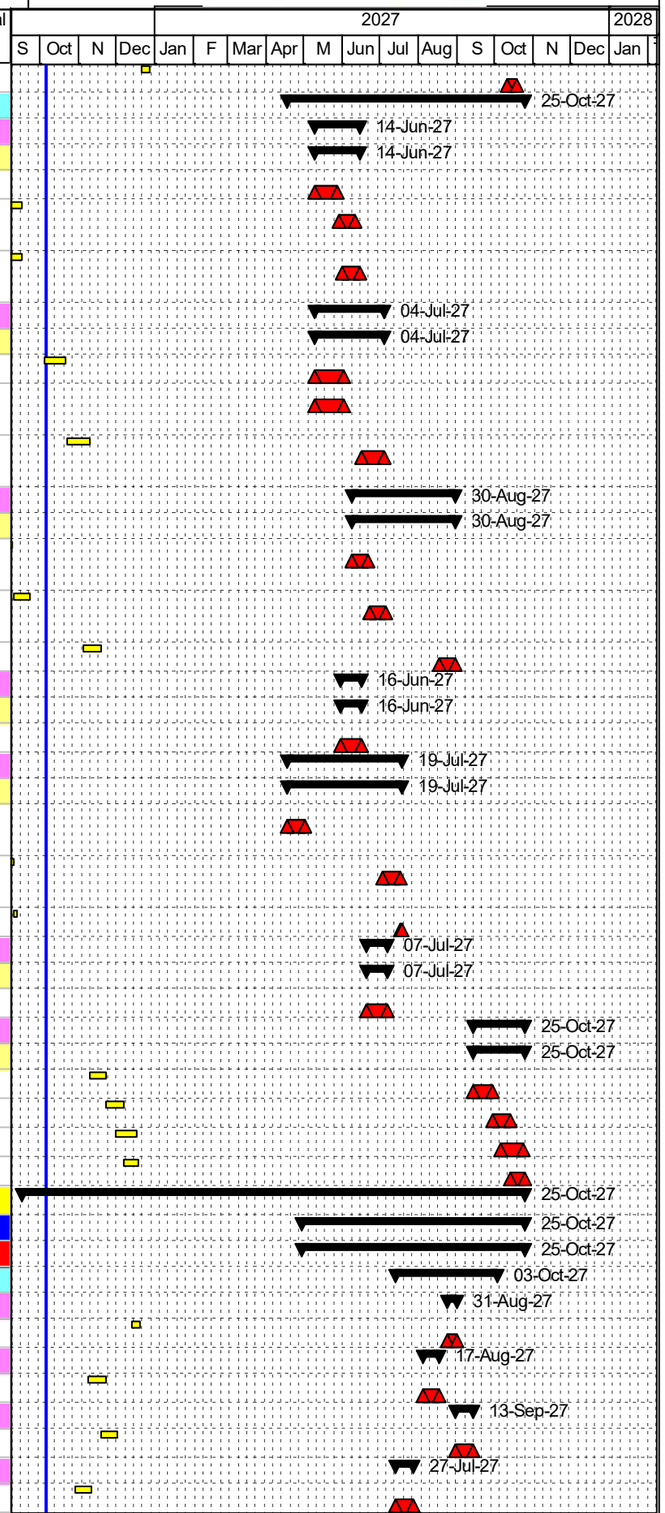

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R09-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R09-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R09-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road 10 Local 2 (2352 LM)		88	14-Jul-27	25-Oct-27	17-Oct-26	28-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R10	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R10	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R10	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R10	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R10-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R10-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R10-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road Works		5	19-Oct-27	25-Oct-27	23-Dec-26	28-Dec-26	0%	0.00	0.00
TIE-R10-RD	TIE IN Existing Network For Road Works	5	19-Oct-27	25-Oct-27	23-Dec-26	28-Dec-26	0%	0.00	0.00
Road 11 Local 1 (670 LM)		88	14-Jul-27	25-Oct-27	17-Oct-26	28-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R11	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R11	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R11	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R11	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R11-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R11-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R11-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road Works		5	19-Oct-27	25-Oct-27	23-Dec-26	28-Dec-26	0%	0.00	0.00
TIE-R11-RD	TIE IN Existing Network For Road Works	5	19-Oct-27	25-Oct-27	23-Dec-26	28-Dec-26	0%	0.00	0.00
Road 14 Local 1 (584 LM)		88	14-Jul-27	25-Oct-27	17-Oct-26	28-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R14	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R14	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R14	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R14	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R14-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R14-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00

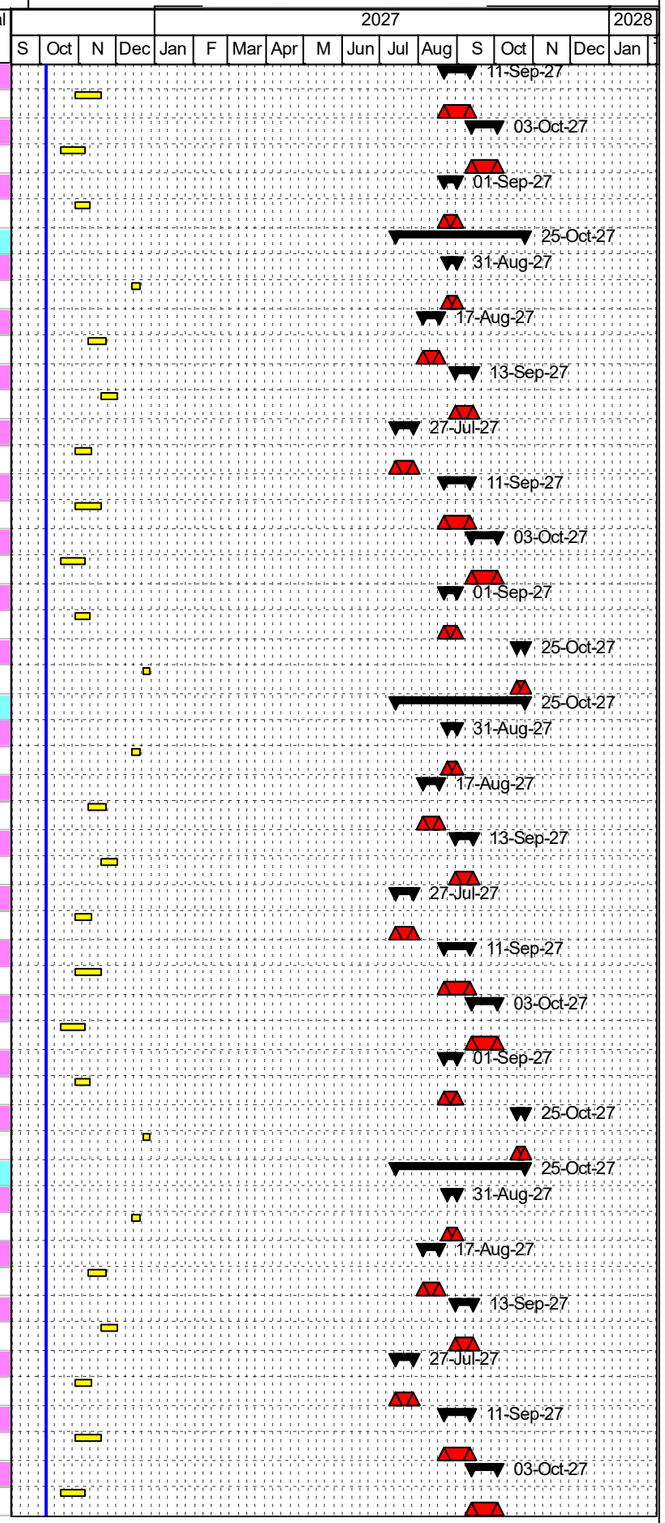

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R14-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road Works		5	19-Oct-27	25-Oct-27	23-Dec-26	28-Dec-26	0%	0.00	0.00
TIE-R14-RD	TIE IN Existing Network For Road Works	5	19-Oct-27	25-Oct-27	23-Dec-26	28-Dec-26	0%	0.00	0.00
Road 15 Local 1 (556 LM)		69	14-Jul-27	03-Oct-27	17-Oct-26	20-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R15	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R15	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R15	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R15	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R15-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R15-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R15-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road 16 Local 1 (527 LM)		69	14-Jul-27	03-Oct-27	17-Oct-26	20-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R16	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R16	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R16	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R16	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R16-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R16-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R16-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road 17 Local 1 (500 LM)		69	14-Jul-27	03-Oct-27	17-Oct-26	20-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R17	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
TIE-SW-R17	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R17	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R17	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R17-MV	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R17-SL	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
TIE-R17-TE	TIE IN Existing Network For Telecom Network	10	22-Aug-27	01-Sep-27	29-Oct-26	09-Nov-26	0%	0.00	0.00
Road 18 Local 1 (479 LM)		129	29-Apr-27	03-Oct-27	02-Sep-26	20-Dec-26	0%	0.00	0.00
Storm Drainage Network		7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
TIE-SD-R18	TIE IN Existing Network For Storm Drainage Network	7	24-Aug-27	31-Aug-27	13-Dec-26	20-Dec-26	0%	0.00	0.00
Sewage Network		12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00

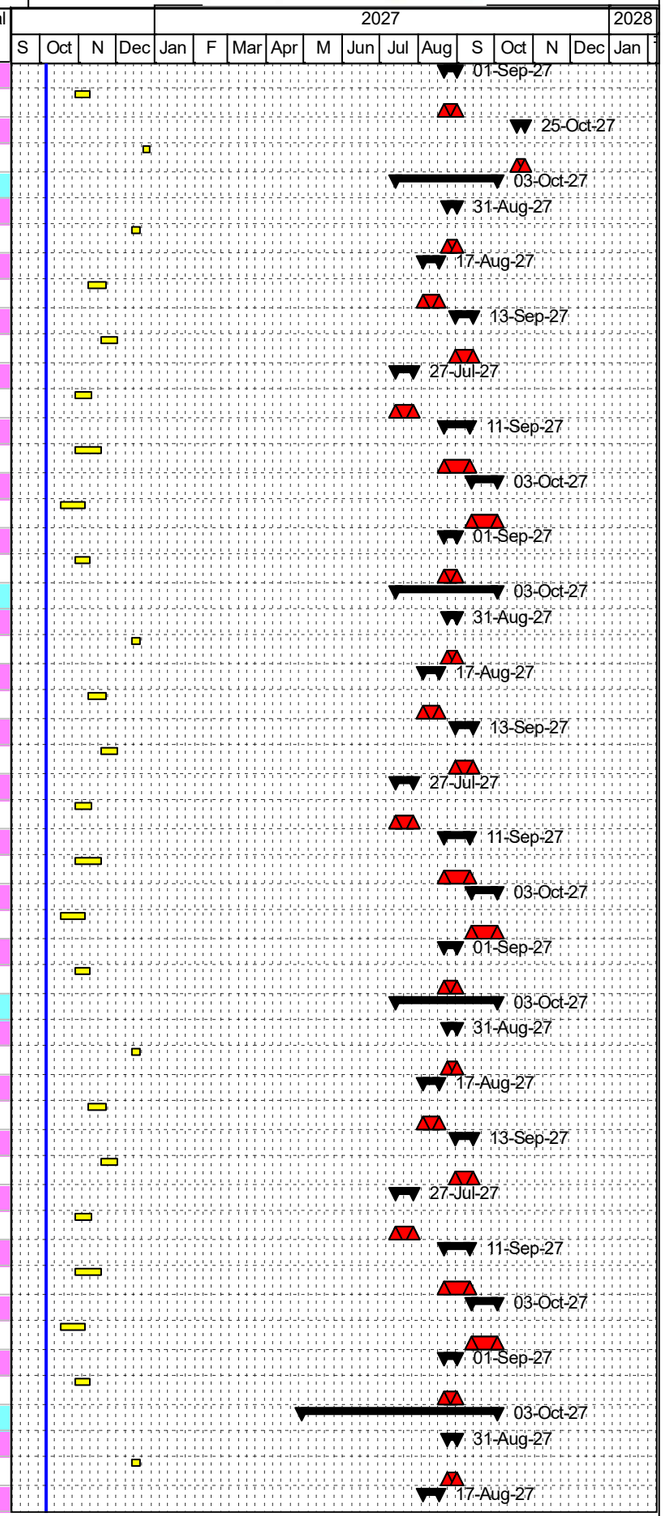


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
TIE-SW-R18	TIE IN Existing Network For Sewage Network	12	04-Aug-27	17-Aug-27	09-Nov-26	22-Nov-26	0%	0.00	0.00
Potable Water Network		12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
TIE-PW-R18	TIE IN Existing Network For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
Irrigation Network		12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
TIE-IR-R18	TIE IN Existing Network For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
Meduim Voltage Network		18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
TIE-R18-MV10	TIE IN Existing Network For Medium Voltage Network	18	22-Aug-27	11-Sep-27	29-Oct-26	18-Nov-26	0%	0.00	0.00
Street Lighting Network		18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
TIE-R18-SL10	TIE IN Existing Network For Street Lighting Network	18	12-Sep-27	03-Oct-27	17-Oct-26	05-Nov-26	0%	0.00	0.00
Telecom Network		12	29-Apr-27	12-May-27	02-Sep-26	15-Sep-26	0%	0.00	0.00
TIE-R18-TE10	TIE IN Existing Network For Telecom Network	12	29-Apr-27	12-May-27	02-Sep-26	15-Sep-26	0%	0.00	0.00
Sewage Pump Stations		219	16-Sep-26 A	25-Jul-27	05-Apr-26	01-Dec-26	0%	4,380,240.72	4,380,240.72
Sewage Pump Station (PS 06)		219	16-Sep-26 A	25-Jul-27	05-Apr-26	01-Dec-26	0%	4,380,240.72	4,380,240.72
Pump Station Main Building		187	16-Sep-26 A	17-Jun-27	05-Apr-26	06-Oct-26	0%	1,517,233.09	1,517,233.09
CO-SW-PS7-MB-11(	Concrete Works of Superstrucure	30	16-Sep-26 A	26-Dec-26	05-Apr-26	09-May-26	0%	66,973.20	66,973.20
CO-SW-PS7-MB-12(	Internal Finishes Works of Superstrucure	30	27-Dec-26	30-Jan-27	10-May-26	17-Jun-26	0%	19,135.20	19,135.20
CO-SW-PS7-MB-13(	Internal Electrical Works	30	31-Jan-27	07-Mar-27	18-Jun-26	22-Jul-26	0%	697,563.13	697,563.13
CO-SW-PS7-MB-14(	Internal Mechanical Works	30	08-Mar-27	14-Apr-27	23-Jul-26	26-Aug-26	0%	572,620.86	572,620.86
CO-SW-PS7-MB-15(	Electromechanical Main Works	30	09-May-27	17-Jun-27	01-Sep-26	06-Oct-26	0%	160,940.70	160,940.70
Generator With Umbrella Tank		75	31-Jan-27	02-May-27	18-Jun-26	13-Sep-26	0%	215,256.93	215,256.93
CO-SW-PS7-GN-10(	Concrete Works of Base	12	31-Jan-27	13-Feb-27	18-Jun-26	01-Jul-26	0%	43,051.39	43,051.39
CO-SW-PS7-GN-11(	Install Manually Operated Fuel Pump	21	14-Feb-27	14-Mar-27	02-Jul-26	26-Jul-26	0%	107,628.47	107,628.47
CO-SW-PS7-GN-12(	Install Ground Fuel Tank	21	15-Mar-27	07-Apr-27	27-Jul-26	19-Aug-26	0%	43,051.39	43,051.39
CO-SW-PS7-GN-13(	Fix Steel Structure for Umbrella	21	08-Apr-27	02-May-27	20-Aug-26	13-Sep-26	0%	21,525.69	21,525.69
Motor Control Centre Building		131	27-Dec-26	07-Jun-27	10-May-26	03-Oct-26	0%	1,971,444.87	1,971,444.87
CO-SW-PS7-MCC-1	Excavation Main Bulding	16	27-Dec-26	13-Jan-27	10-May-26	01-Jun-26	0%	96.48	96.48
CO-SW-PS7-MCC-1	Concrete Works of Superstrucure	21	14-Jan-27	07-Feb-27	02-Jun-26	25-Jun-26	0%	108,089.67	108,089.67
CO-SW-PS7-MCC-1	Internal Finishes Works of Superstrucure	21	08-Feb-27	04-Mar-27	27-Jun-26	20-Jul-26	0%	65,710.36	65,710.36
CO-SW-PS7-MCC-1	Internal Electrical Works	21	06-Mar-27	01-Apr-27	21-Jul-26	13-Aug-26	0%	298,746.30	298,746.30
CO-SW-PS7-MCC-1	Internal Mechanical Works	21	03-Apr-27	26-Apr-27	15-Aug-26	07-Sep-26	0%	75,272.49	75,272.49
CO-SW-PS7-MCC-1	Electromechanical Main Works	21	09-May-27	07-Jun-27	08-Sep-26	03-Oct-26	0%	1,423,529.57	1,423,529.57
Simple Building Works		50	03-May-27	05-Jul-27	14-Sep-26	11-Nov-26	0%	468,575.93	468,575.93
CO-SW-PS7-SBL-1(	Perimeter Fencing	23	03-May-27	03-Jun-27	14-Sep-26	11-Oct-26	0%	73,149.30	73,149.30
CO-SW-PS7-SBL-11	Outside Lighting	27	05-Jun-27	05-Jul-27	12-Oct-26	11-Nov-26	0%	16,425.72	16,425.72
CO-SW-PS7-SBL-12	Outside Duct Works	23	05-Jun-27	30-Jun-27	12-Oct-26	07-Nov-26	0%	9,922.70	9,922.70
CO-SW-PS7-SBL-13	Rectangular Wet Wells	27	05-Jun-27	05-Jul-27	12-Oct-26	11-Nov-26	0%	147,819.42	147,819.42
CO-SW-PS7-SBL-14	Round Wet Well Structure for basket screen	27	05-Jun-27	05-Jul-27	12-Oct-26	11-Nov-26	0%	67,770.50	67,770.50
CO-SW-PS7-SBL-15	Motorized basket screen	27	05-Jun-27	05-Jul-27	12-Oct-26	11-Nov-26	0%	153,488.29	153,488.29
Site Work and Service Road		21	01-Jul-27	25-Jul-27	08-Nov-26	01-Dec-26	0%	207,729.90	207,729.90
CO-SW-PS7-SWS-1	Outside Strom Drainage System	6	01-Jul-27	07-Jul-27	08-Nov-26	14-Nov-26	0%	40,230.00	40,230.00
CO-SW-PS7-SWS-1	Bituminous Works	15	08-Jul-27	25-Jul-27	15-Nov-26	01-Dec-26	0%	167,499.90	167,499.90
Storm Drainage Ponds		251	06-Oct-26	04-Aug-27	15-Feb-26	24-Aug-26	0%	315,314.06	315,314.06
Storm Drainage Pond (PO-J1)		136	06-Oct-26	17-Mar-27	15-Feb-26	30-Jul-26	0%	28,702.80	28,702.80
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 1	21	06-Oct-26	29-Oct-26	15-Feb-26	10-Mar-26	0%	5,740.56	5,740.56
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 2	21	31-Oct-26	23-Nov-26	11-Mar-26	07-Apr-26	0%	5,740.56	5,740.56
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 3	21	24-Nov-26	17-Dec-26	08-Apr-26	02-May-26	0%	5,740.56	5,740.56
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 4	21	19-Dec-26	11-Jan-27	03-May-26	31-May-26	0%	5,740.56	5,740.56
CO-SD-PO-K1-120	Outfall structure	26	12-Jan-27	10-Feb-27	01-Jun-26	30-Jun-26	0%	2,870.28	2,870.28
CO-SD-PO-K1-130	Acess Entrace Ramp	26	11-Feb-27	17-Mar-27	01-Jul-26	30-Jul-26	0%	2,870.28	2,870.28
Storm Drainage Pond (PO-J2)		185	22-Dec-26	04-Aug-27	15-Feb-26	24-Aug-26	0%	286,611.26	286,611.26
CO-SD-PO-K2-100-P	Excavation & Filling Works - PART 1	21	22-Dec-26	14-Jan-27	15-Feb-26	10-Mar-26	0%	68,423.75	68,423.75
CO-SD-PO-K2-110-P	Finished Grouted Riprap - PART 1	21	16-Jan-27	08-Feb-27	11-Mar-26	07-Apr-26	0%	2,583.25	2,583.25

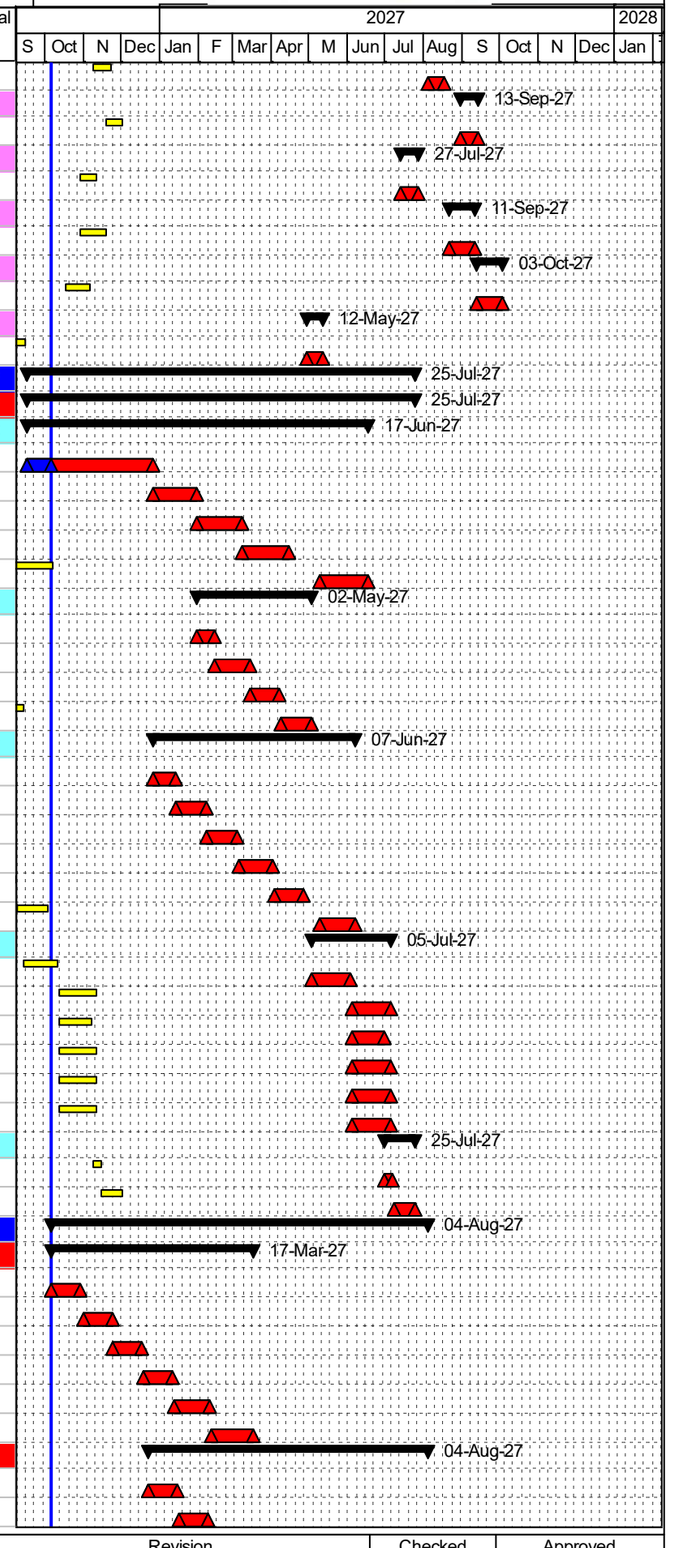

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SD-PO-K2-100-P:	Excavation & Filling Works - PART 2	21	16-Jan-27	08-Feb-27	11-Mar-26	07-Apr-26	0%	68,423.75	68,423.75
CO-SD-PO-K2-110-P:	Finished Grouted Riprap - PART 2	21	09-Feb-27	06-Mar-27	08-Apr-26	02-May-26	0%	2,583.25	2,583.25
CO-SD-PO-K2-100-P:	Excavation & Filling Works - PART 3	21	18-Mar-27	11-Apr-27	08-Apr-26	02-May-26	0%	68,423.75	68,423.75
CO-SD-PO-K2-110-P:	Finished Grouted Riprap - PART 3	21	12-Apr-27	05-May-27	03-May-26	31-May-26	0%	2,583.25	2,583.25
CO-SD-PO-K2-100-P:	Excavation & Filling Works - PART 4	21	12-Apr-27	05-May-27	03-May-26	31-May-26	0%	68,423.75	68,423.75
CO-SD-PO-K2-110-P:	Finished Grouted Riprap - PART 4	21	06-May-27	05-Jun-27	01-Jun-26	24-Jun-26	0%	2,583.25	2,583.25
CO-SD-PO-K2-120	Outfall structure	26	06-Jun-27	05-Jul-27	25-Jun-26	25-Jul-26	0%	1,291.63	1,291.63
CO-SD-PO-K2-130	Acess Entrace Ramp	26	06-Jul-27	04-Aug-27	26-Jul-26	24-Aug-26	0%	1,291.63	1,291.63
Testing and Comissioning		130	01-Jun-26 A	31-Oct-27	25-Aug-26	03-Jan-27	61.66%	11,395,586.42	11,395,586.42
Infrastructure Networks		118	01-Jun-26 A	31-Oct-27	07-Nov-26	03-Jan-27	63.44%	11,075,668.52	11,075,668.52
Irrigation Network		12	05-Jun-26 A	10-Aug-27	12-Nov-26	25-Nov-26	25%	624,273.76	624,273.76
T/C-IR	Testing and Commissioning of Irrigation Network	12	05-Jun-26 A	10-Aug-27	12-Nov-26	25-Nov-26	25%	624,273.76	624,273.76
Potable Water Network		12	01-Jul-26 A	28-Sep-27	03-Dec-26	16-Dec-26	55%	1,022,094.20	1,022,094.20
T/C-PW	Testing and Commissioning of Potable Water Network	12	01-Jul-26 A	28-Sep-27	03-Dec-26	16-Dec-26	55%	1,022,094.20	1,022,094.20
Sewage Network		12	01-Jun-26 A	10-Oct-27	19-Dec-26	31-Dec-26	80%	2,308,897.10	2,308,897.10
T/C-SW	Testing and Commissioning of Sewage Network	12	01-Jun-26 A	10-Oct-27	19-Dec-26	31-Dec-26	80%	2,308,897.10	2,308,897.10
Storm Drainage Network		10	10-Jun-26 A	12-Sep-27	21-Dec-26	31-Dec-26	80%	2,866,651.20	2,866,651.20
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	10-Jun-26 A	12-Sep-27	21-Dec-26	31-Dec-26	80%	2,866,651.20	2,866,651.20
Street Lighting Network		18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	32%	462,378.20	462,378.20
T/C-SL	Testing and Commissioning of Street Lighting Network	18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	32%	462,378.20	462,378.20
Telecom Network		10	05-Sep-26 A	20-Sep-27	10-Nov-26	21-Nov-26	32%	181,657.10	181,657.10
T/C-TE	Testing and Commissioning of Telecom Network	10	05-Sep-26 A	20-Sep-27	10-Nov-26	21-Nov-26	32%	181,657.10	181,657.10
Medium Voltage Network		10	05-Sep-26 A	03-Oct-27	22-Nov-26	02-Dec-26	50%	478,905.06	478,905.06
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	05-Sep-26 A	03-Oct-27	22-Nov-26	02-Dec-26	50%	478,905.06	478,905.06
Road Works		5	16-Aug-26 A	31-Oct-27	29-Dec-26	03-Jan-27	55%	3,130,811.90	3,130,811.90
T/C-RD	Testing and Commissioning of Road Works	5	16-Aug-26 A	31-Oct-27	29-Dec-26	03-Jan-27	55%	3,130,811.90	3,130,811.90
Independent Works		56	05-Aug-27	10-Oct-27	25-Aug-26	31-Dec-26	0%	319,917.90	319,917.90
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	30	05-Aug-27	08-Sep-27	25-Aug-26	29-Sep-26	0%	296,836.80	296,836.80
T/C-SPS	Testing and Commissioning of Sewage Pump Stations	26	09-Sep-27	10-Oct-27	02-Dec-26	31-Dec-26	0%	23,081.10	23,081.10
Handing over and close out		100	14-Jul-27	08-Nov-27	17-Oct-26	11-Jan-27	0%	0.00	0.00
As-Built		95	14-Jul-27	02-Nov-27	17-Oct-26	05-Jan-27	0%	0.00	0.00
HO-180	Submission As-Built Drawing For Irrigation Network	12	14-Jul-27	27-Jul-27	29-Oct-26	11-Nov-26	0%	0.00	0.00
HO-210	Submission As-Built Drawing For Pump station	12	26-Jul-27	08-Aug-27	02-Dec-26	15-Dec-26	0%	0.00	0.00
HO-160	Submission As-Built Drawing For Telecom Network	12	28-Jul-27	10-Aug-27	12-Nov-26	25-Nov-26	0%	0.00	0.00
HO-130	Submission As-Built Drawing For Pond	12	05-Aug-27	18-Aug-27	12-Nov-26	25-Nov-26	0%	0.00	0.00
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	22-Aug-27	04-Sep-27	12-Nov-26	25-Nov-26	0%	0.00	0.00
HO-200	Submission As-Built Drawing For Storm Network	12	24-Aug-27	06-Sep-27	13-Dec-26	26-Dec-26	0%	0.00	0.00
HO-190	As-Built Drawing For Potable Water Network	12	31-Aug-27	13-Sep-27	19-Nov-26	02-Dec-26	0%	0.00	0.00
HO-150	Submission As-Built Drawing For Street Lighting Network	12	12-Sep-27	26-Sep-27	17-Oct-26	29-Oct-26	0%	0.00	0.00
HO-140	Submission As-Built Drawing For Roads Network	5	25-Oct-27	31-Oct-27	29-Dec-26	03-Jan-27	0%	0.00	0.00
HO-100	Submission As-Built Drawing For Sewage Network	7	25-Oct-27	02-Nov-27	29-Dec-26	05-Jan-27	0%	0.00	0.00
De-Mobilization Works		5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
HO-220	Removing Portable Caravan	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
HO-230	Remove Temporary Car Shades	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
HO-120	Remove material stock & Storage area	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
Handing Over		7	31-Oct-27	08-Nov-27	04-Jan-27	11-Jan-27	0%	0.00	0.00
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
HO-260	Review FIR Approval to ensure compliance with the actual status	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
HO-270	Review the sample drawing to ensure compliance with the actual status	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00
HO-110	Final Testing Work	5	31-Oct-27	06-Nov-27	04-Jan-27	09-Jan-27	0%	0.00	0.00

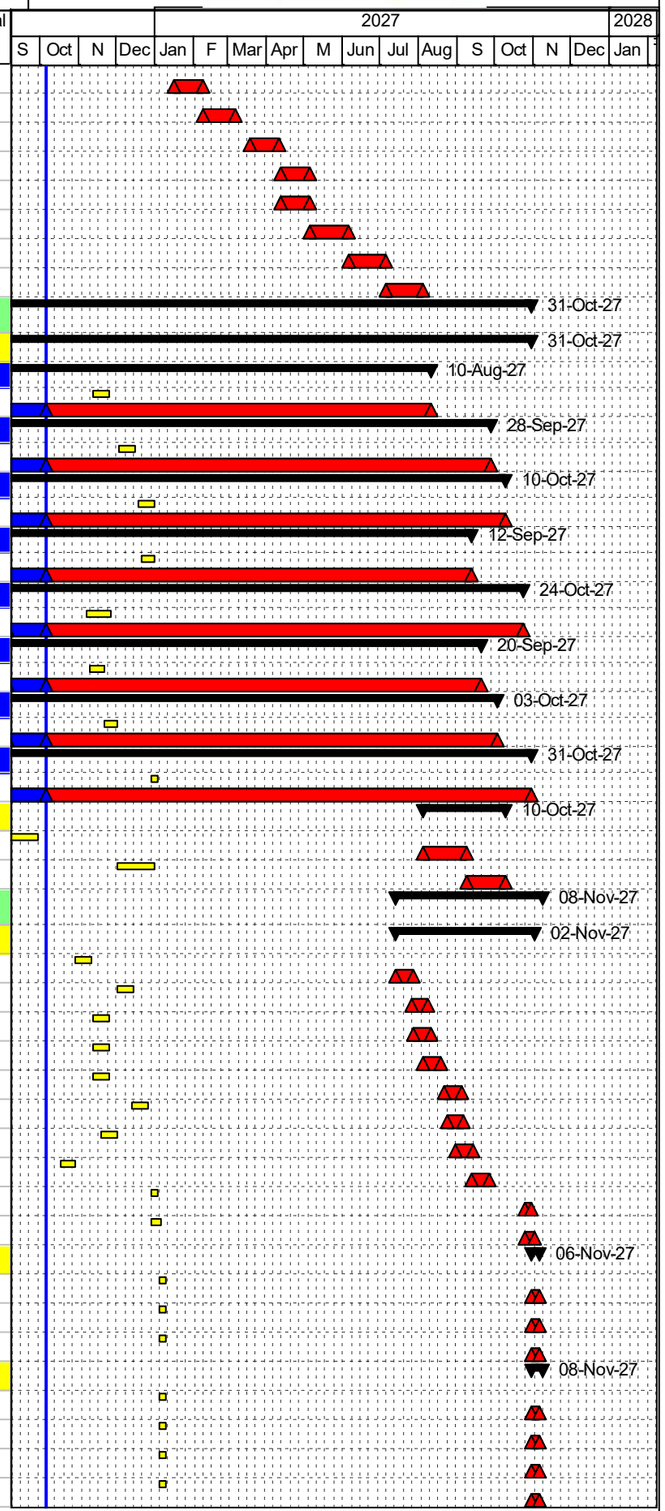


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part 2 Update 06/10/2026

Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
HO-240	Final Walkthrough and Inspection	2	06-Nov-27	08-Nov-27	10-Jan-27	11-Jan-27	0%	0.00	0.00
HO-280	Punch List Completion	2	06-Nov-27	08-Nov-27	10-Jan-27	11-Jan-27	0%	0.00	0.00



Primary Baseline | Actual Work | Summary

Remaining Work | Baseline Milestone

Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
