Development of Infrastructure Networks, 3rd Industrial City in Dammam, Phase 2 Part 2, Zone J

تطوير شبكات البنية التحتية للمدينة الصناعية الثالثة بالدمام المرحلة الثانية الجزء الثاني - المنطقة J

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ANSAB General Contracting	EGIS	Eng. Mohammed Al-Aissa	12-Jan-2025	11-Jan-2027

Scope: collector and local roads, potable water, sewerage, storm drainage, irrigation, medium-voltage, street lighting and telecom networks, a sewage pump station and storm drainage ponds for Block J. Contract value 117.4M SAR excluding VAT, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 27-Oct-2026 data date the project is 55.0% complete against 89.4% planned, behind by 34.4% (SPI 0.62). Only 0.17% was gained since the previous report against 4.07% planned, so the gap widened by 3.9%.

PHYSICAL % COMPLETE

55.0% / 89.4% plan

▼ SPI 0.62 −34.4%

PROGRESS THIS WEEK

+0.17% / +4.07% plan

▼ 3.9% below the weekly plan

CONTRACT TIME ELAPSED

89.6% · day 653 of 729

▼ Forecast finish 07-Sep-2027

INVOICED TO DATE (GROSS)

43.1% · 50.6M SAR

20 invoices, last period ends 30-Sep-2026

The project is forecast to finish almost eight months late, and progress has nearly stopped.

The weekly report and the P6 update (data date 27-Oct-2026) both forecast completion on 07-Sep-2027, 239 days after the contract completion date of 11-Jan-2027 and 7 days later than in report 92. The P6 completion milestone has −195.5 days of float. With 89.6% of the contract time used, 45.0% of the physical work remains, and every network completion milestone is between 134 and 212 days negative in P6.

Site photos this week

The six new photos uploaded with report 94; they carry no visible date stamp. They show road formation compaction, waterproofing on the concrete walls of the lift station and fill handling. Select a photo to view it larger, then use the arrows to move between photos.



Road formation

Compacted formation, with a roller working further along.



Road formation compaction

Rollers working along the compacted formation.



Lift station wall waterproofing

Protection membrane fixed to the cast wall, with starter bars above.



Lift station walls

Waterproofed wall section with reinforcement for the next pour.



Pipe sleeve in the wall

GRP pipe sleeve cast into the waterproofed wall.




Fill handling

Wheel loader moving fill material.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

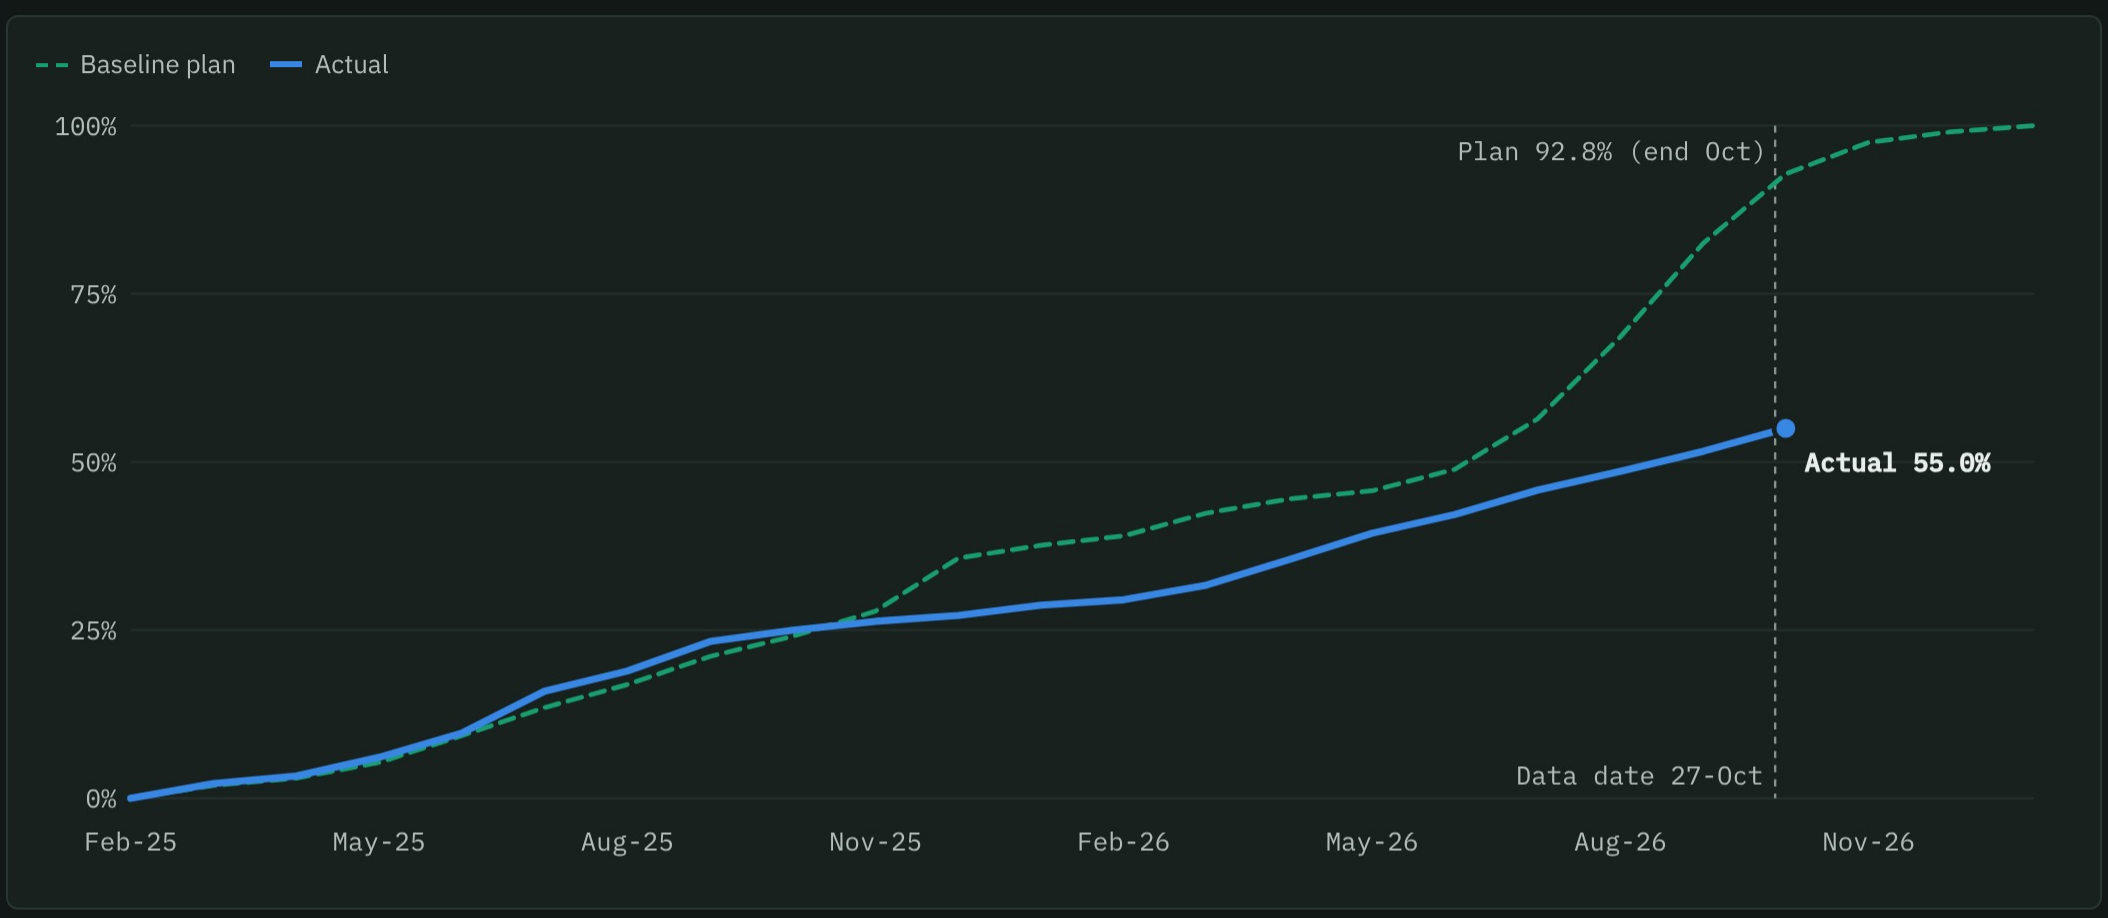

PERIOD ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED IN PERIOD	SPI
Jun-2026	48.9	42.3	−6.6	+2.9	0.86
Jul-2026	56.4	45.8	−10.6	+3.6	0.81
Aug-2026	68.6	48.6	−20.0	+2.8	0.71
Sep-2026	82.5	51.6	−30.9	+3.0	0.63
13-Oct-2026	85.3*	54.8	−30.5	+3.2	0.64
27-Oct-2026	**89.4***	**55.0**	**−34.4**	**+0.2**	**0.62**

Month-end values from the Physical-Chart Data sheet, then the data dates of report 92 (previous upload) and report 94. No report 93 was uploaded. * Planned value at the data date from the report cover; the plan for the end of October is 92.8%. Progress averaged about 3% a month from June to mid-October, then almost stopped: 0.2% in the last 14 days against 4.1% planned.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Earthworks network	8.3%	100.0%	100.0%	0.0	1.00	✓ Complete
Irrigation network	3.5%	98.7%	21.4%	−77.3	0.22	▼ Behind
Potable water network	4.1%	92.2%	33.8%	−58.4	0.37	▼ Behind
Medium-voltage network	3.6%	98.7%	76.8%	−21.9	0.78	▼ Behind
Street lighting network	12.5%	100.0%	26.3%	−73.7	0.26	▼ Behind
Telecom network	2.2%	100.0%	54.6%	−45.4	0.55	▼ Behind
Roads network	33.2%	77.0%	53.7%	−23.3	0.70	▼ Behind
Sewage network	17.6%	90.4%	54.9%	−35.5	0.61	▼ Behind
Storm drainage network	15.1%	94.3%	65.3%	−29.0	0.69	▼ Behind
Total	100%	**89.4%**	**55.0%**	**−34.4**	**0.62**	▼ Behind

Engineering, procurement and testing carry no man-hours in the physical measure and are not listed. In the last 14 days only roads (72 man-hours), storm drainage (2) and medium voltage (1) earned any progress, against 1,772 man-hours planned. The P6 update (data date 27-Oct-2026) has 1,921 activities: 1,227 completed, 64 in progress and 630 not started. Its scheduled finish is 07-Sep-2027, 239 days after the contract date.

Scope of work: quantities

Total, executed and remaining length of each network, from the execution summary in the Arabic progress summary sheet. "This week" is the change since the same sheet in the previous upload (report 92, 13-Oct-2026), so it covers 14 days.

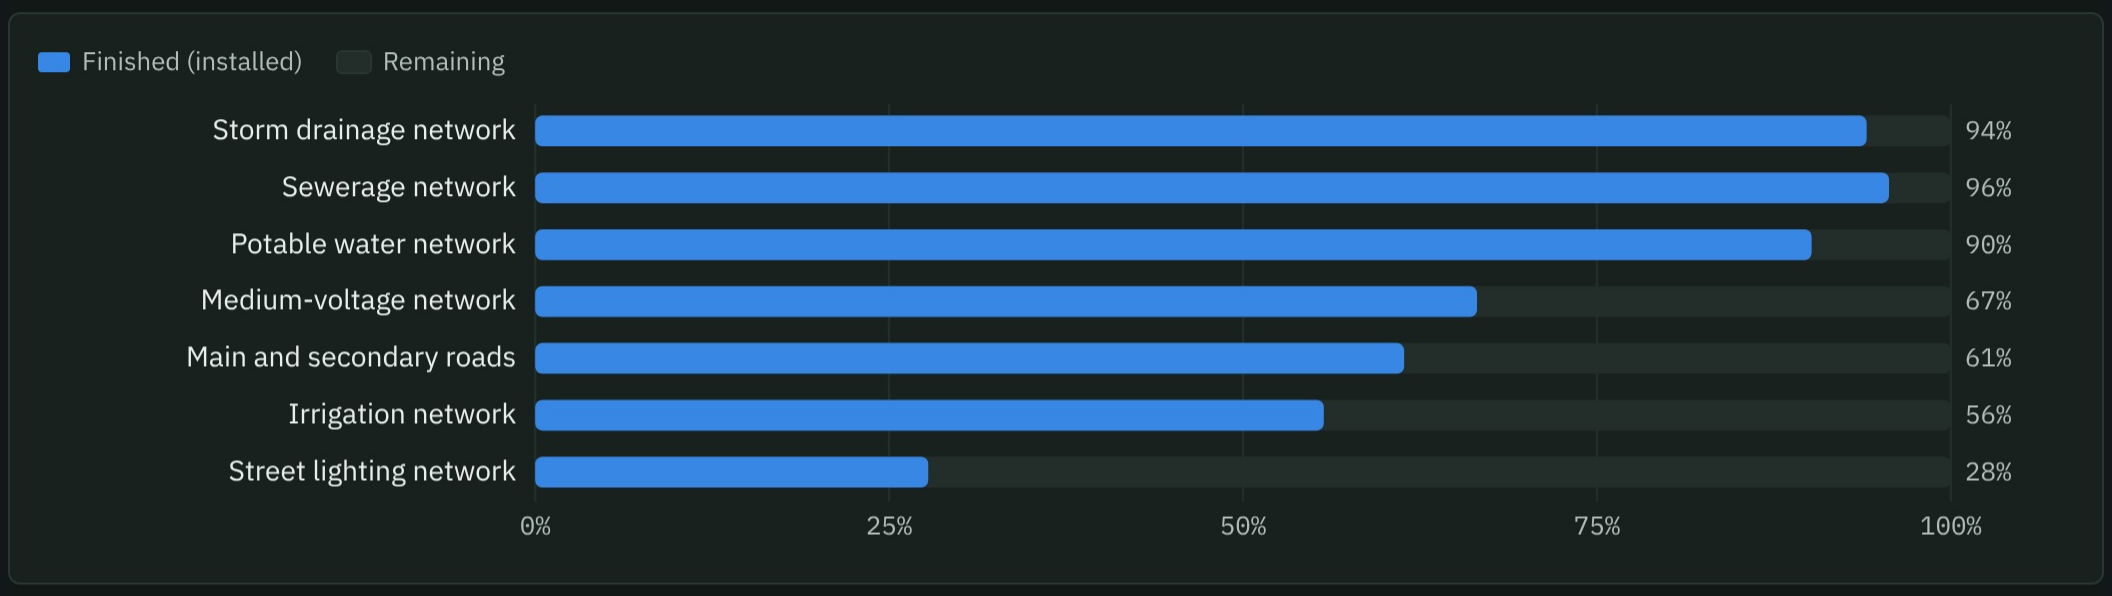

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Storm drainage network	Block J	LM	18,554	17,450	0	1,104	94.0%	–
Sewerage network	Block J	LM	9,152	8,752	0	400	95.6%	–
Potable water network	Block J	LM	12,200	11,000	+200	1,200	90.2%	–
Medium-voltage network	Block J	LM	17,328	11,528	+200	5,800	66.5%	–
Main and secondary roads	Block J	LM	8,146	5,000	0	3,146	61.4%	–
Irrigation network	Block J	LM	14,494	8,074	0	6,420	55.7%	–
Street lighting network	Block J	LM	12,786	3,550	0	9,236	27.8%	–

Work executed this week

NETWORK	ACTIVITY	UNIT	THIS WEEK	SOURCE
Potable water	Network executed (10,800 → 11,000)	LM	200	Summary sheet
Medium voltage	Network executed (11,328 → 11,528)	LM	200	Summary sheet
Roads	Physical progress earned	Man-hours	72	Progress sheet
Storm drainage	Physical progress earned	Man-hours	2	Progress sheet
Medium voltage	Physical progress earned	Man-hours	1	Progress sheet
Sewage pump station	Wall pouring	–	–	Weekly activities sheet

The weekly activities sheet repeats the activity list of report 92 and its quantity table is empty this time. Planned next: complete the 630 mm water line, the 500 mm irrigation line and the 800 mm line, about 1,000 m of MV cable on street 9, road works on street 10 and asphalt on road 14.

Furthest behind

Street lighting is 27.8% executed (3,550 of 12,786 LM): no LED luminaires, earthing, road-crossing ducts or draw pits have been installed. Irrigation is 55.7% and roads 61.4%. Traffic markings, signs and fire hydrants (0 of 55) have not started.

Close to finished

Sewerage is 95.6% and storm drainage 94.1% executed by length, and potable water 90.2%. The storm box conduit (2,051 m) is complete. Catch basins remain at 207 of 505 and the storm drainage ponds and sewage pump station are still under construction.

Milestones

Baseline and forecast dates from the weekly report's milestone table, against the P6 update of 27-Oct-2026. Days in brackets are the delay the weekly report gives against the baseline.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	12-Jan-2025	12-Jan-2025	12-Jan-2025 (actual)	–	✓ Done
Complete mobilisation	12-Mar-2025	12-Mar-2025	09-Mar-2025 (actual)	–	✓ Done
Shop drawings and materials approved	10-Feb-2025	11-Feb-2025	24-May-2025 (actual)	–	✓ Done
Earthworks network	24-May-2026	31-May-2025	–	–	✓ Done
Telecom network	28-Sep-2026	19-Apr-2027 (+203 d)	18-Mar-2027	−165	▼ Late
Irrigation network	23-Aug-2026	11-May-2027 (+261 d)	11-May-2027	−163	▼ Late
Potable water network	05-Oct-2026	11-Jul-2027 (+279 d)	27-Jun-2027	−180	▼ Late
Sewage network	06-Oct-2026	05-Jul-2027 (+272 d)	21-Jun-2027	−184	▼ Late
Medium-voltage network	17-Oct-2026	28-Apr-2027 (+193 d)	07-Apr-2027	−134	▼ Late
Road works	21-Oct-2026	24-Aug-2027 (+307 d)	24-Aug-2027	−195.5	▼ Late
Street lighting network	20-Dec-2026	21-Jul-2027 (+213 d)	30-Jun-2027	−212	▼ Late
Storm drainage network	–	19-Jul-2027	11-Jul-2027	−172	▼ Late
Storm drainage ponds	–	–	02-May-2027	−110	▼ Late
Sewage pump station	–	–	30-May-2027	−129	▼ Late
Tie-in to existing networks	–	–	24-Aug-2027	−192.5	▼ Late
Project completion	11-Jan-2027	07-Sep-2027 (+239 d)	07-Sep-2027	−195.5	▼ Late

The two forecasts agree on completion but not on the network milestones.

Both give 07-Sep-2027 for project completion and the same dates for irrigation and road works. For telecom, potable water, sewage, medium voltage, street lighting and storm drainage the P6 update is 8 to 32 days earlier than the weekly report. Every forecast slipped by 6 to 12 days since report 92. The Employer's NOC for the medium-voltage network is the only control milestone not yet achieved; P6 now schedules it for 22-Dec-2026 with −46 days of float.

Procurement of key materials

Share of the required quantity delivered to site. Source: Procurement sheet, weekly report 27-Oct-2026, unchanged since report 92. All listed materials are approved.

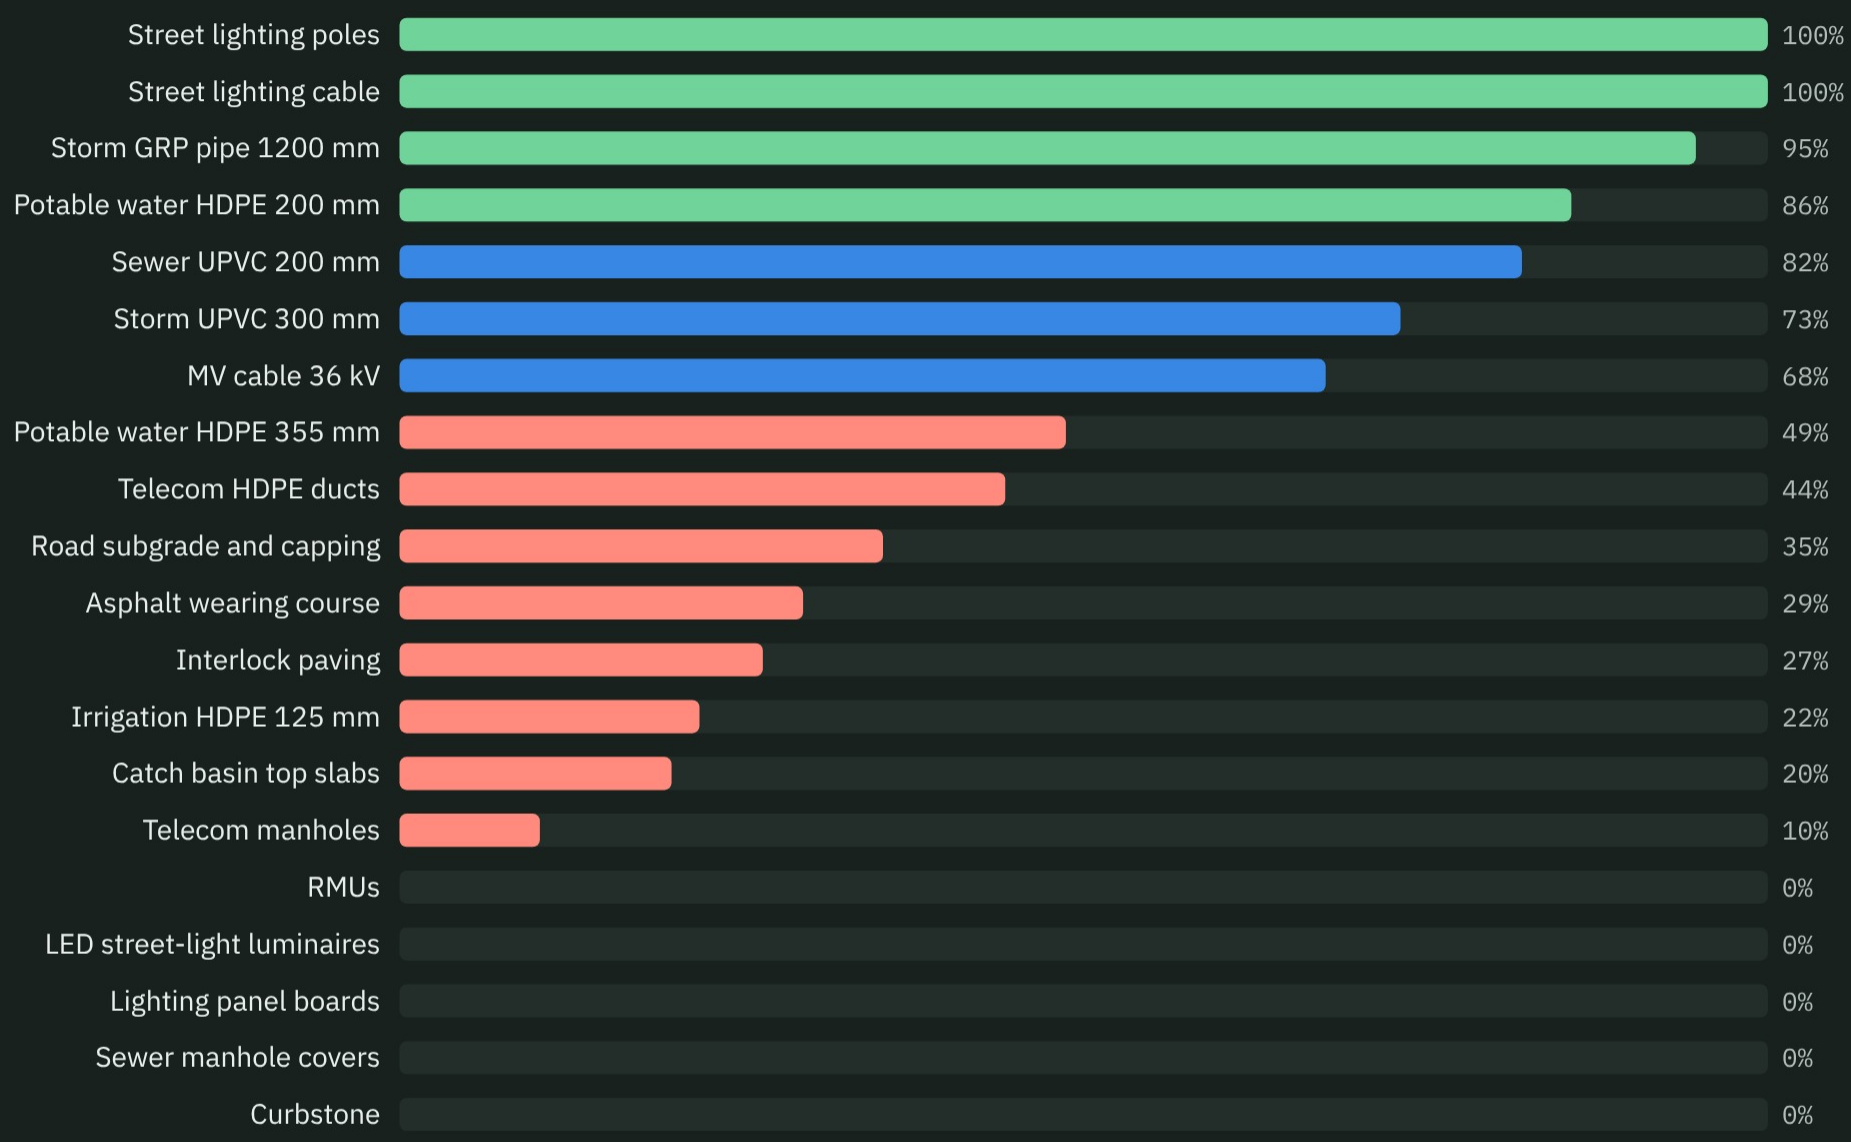

Nothing delivered yet for several items on the critical networks


RMUs (0 of 9), LED street-light luminaires (0 of 363), lighting panel boards (0 of 6), curbstone (0 of 42,552 pieces), sewer manhole covers (0 of 129) and storm covers and gratings. The register rates delay in long-lead materials as a high risk.

Telecom, irrigation and road layers lag

Telecom ducts are 44% delivered and telecom manholes 8 of 78. Irrigation 125 mm pipe is 22% delivered, catch-basin top slabs 20%, and road-layer materials (capping, subgrade, base course, asphalt, interlock) 17–35%. MV cable is at 8,378 of 12,378 m.

Manpower

Head count on site this month by trade, planned vs actual. Source: Manpower sheet. The report has no monthly history.

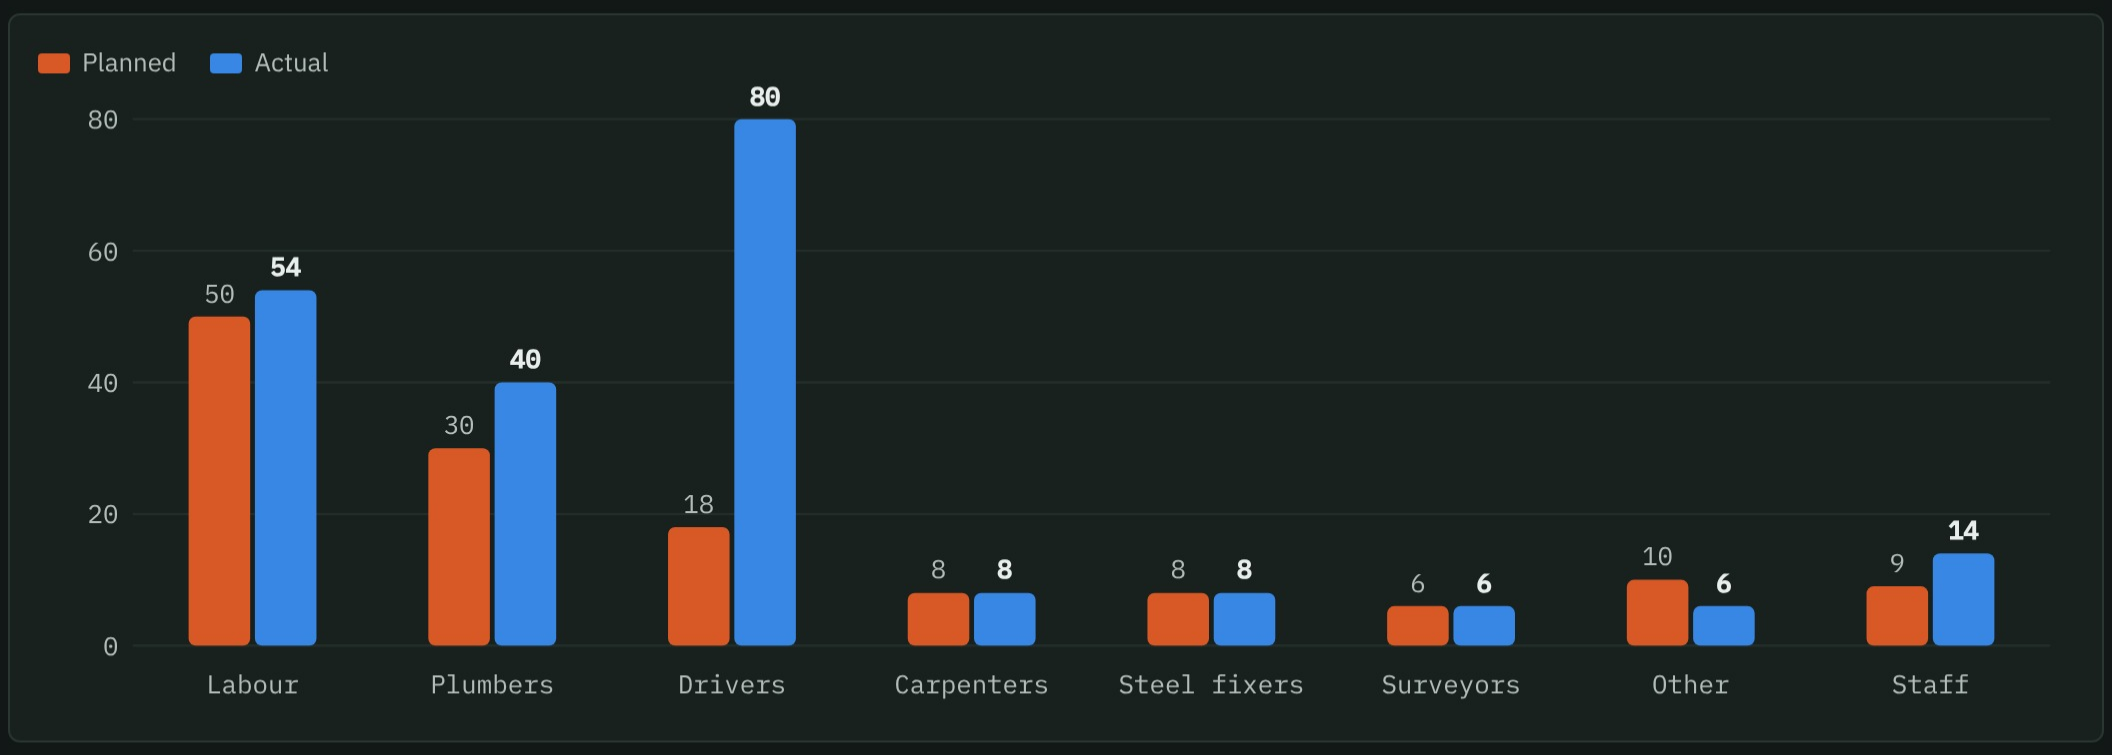

Total head count is 214 against 139 planned: 200 manual workers against 130 and 14 staff against 9. Carpenters and steel fixers now match a reduced plan (8 each, down from 18 and 15 in report 92), and drivers and operators are far above it (80 against 18). Equipment on site is 100 units against 11 planned. Despite this, almost no physical progress was earned.

Cost and invoicing

Contract value

Roads and paving	31,308,119
Storm water drainage	33,717,595
Sewerage and lift stations	24,177,287
Potable water	10,220,942
Irrigation	6,738,491
Street lighting and telecom	6,440,353
Medium voltage	4,788,987
BOQ total (excl. VAT)	**117,391,774**
Contract value incl. 15% VAT	135,000,540
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. The change order log is empty; the report lists one potential change.

Invoices

Advance payment (10%)	11,739,177
Progress invoices submitted	20
Gross value	50,649,221
Advance payment recovered	5,064,922
Retention / penalties	0 / 0
Approved by MODON PM	50,649,221
Paid (18 invoices)	40,094,952

Invoicing is 43.1% of the contract value against 55.0% physical progress. Invoice 20 (01-Sep to 30-Sep-2026, 7,234,753 SAR gross) was added this week. Invoices 19 and 20 are approved and awaiting payment.

Health, safety and quality

Safety Score 0.82

Safe man-hours (cumulative)	398,698
Man-hours this week	9,600
Lost-time injuries	0
Fatalities	0
First-aid cases	5
Near misses	1
Property damage	0
Inductions / toolbox talks	96 / 320

Cumulative figures. This week: 2 inductions and 6 toolbox talks.

Quality Score 0.90

FIRs issued (cumulative)	1,881
FIRs closed	1,791
FIRs pending (0–10 days)	90
NCRs issued / closed	21 / 21
Site instructions issued / closed	13 / 12
MIRs issued	0
Shop drawings submitted (all code B)	23
Material submittals (A / B / C / D)	1 / 72 / 2 / 1

NCRs close in 7 days on average. 7 material submittals are still to be approved.

Open issues and risks

ISSUE	OWNER	DETAIL
Schedule delay	Contractor	Forecast completion 07-Sep-2027, 239 days late. Only 0.17% was gained in 14 days against 4.07% planned. The report shows 418 failed-start activities (406 in report 92) and 674 critical-path activities (669). No recovery schedule approval is recorded.
Long-lead materials	Contractor	Risk 05, rated high and open: delays in long-lead materials could stop work. Mitigation: chase suppliers and get MODON approval for alternative sources. Target 20-Nov-2026.
Tie-in to existing networks	Contractor / MODON	Risk 01, rated low and open: existing infrastructure may not be ready for the tie-ins, delaying commissioning and handover. P6 tie-in milestone 24-Aug-2027, –192.5 days of float.
Testing and commissioning	Contractor	Testing was planned to start on 12-Oct-2026 (telecom), 18-Oct-2026 (irrigation) and 26-Oct-2026 (street lighting and medium voltage). None has started; the forecast starts run from 12-Nov-2026 to 04-Jan-2027.
MV network NOC	Contractor	The Employer's NOC for the medium-voltage network is still outstanding (P6: 22-Dec-2026, –46 days).

Closed in the registers: groundwater and dewatering (high), delayed or failed testing, and the two logged issues (irrigation connection point, pump-station force main). The BOQ re-measurement saving is recorded as a realised opportunity.

Data notes

Built from the W04 upload (report 94); the previous upload (report 92) was used only for this-week changes.

- Report 93 was not uploaded. The previous upload holds report 92 (13-Oct-2026), so the "this week" figures (0.17% physical, 200 m of water and MV) cover 14 days. The cover still labels them weekly.
- Week 93 is the contract week stated in the report's milestone sheet ("93 of 104"), and matches 12-Jan-2025 to 27-Oct-2026 = 653 days. The workbook itself is numbered report 94.
- On the report cover the physical progress by WBS is still shifted by one row (Earthworks shows Irrigation's man-hours, and so on). The figures were taken from the Progress sheet.
- The Arabic summary sheet labels cost-based figures as planned and actual "progress". This report uses physical progress (man-hour weighted) only: 89.38% planned and 54.98% actual.
- In the Physical-Chart Data sheet the October earned figure is now 75 man-hours (it was 1,493 in report 92), so the month value was overwritten with the latest period. The cumulative actual (54.98%) is consistent.
- The physical forecast in the chart data still reaches 100% in January 2027, which contradicts the forecast completion of 07-Sep-2027. The "Last week vs this week" sheet is still based on P6 updates of April 2026.

- The summary sheet shows 200 m more potable water and MV network, but the Major Quantities sheet and the procurement log are identical to report 92. Network totals in the summary still do not match the Major Quantities sheet (for example potable water 12,200 LM against 9,720 m of pipe).
- The weekly activities sheet repeats report 92's activity list word for word, and its this-week quantity table is empty.
- Manpower: the manual plan fell from 165 to 130 while the actual rose from 152 to 200. The trade table totals 202 and the cover's trade total 122 (without drivers and operators). The next-month manual forecast is still 1,148.
- HSE: the statistics advanced by one week only (9,600 hours) across the 14 days since report 92, and the inspection sheet still covers 26-Aug to 01-Sep-2026.
- The summary sheet gives site handover as 12-Feb-2025 (12-Jan-2025 in the weekly report), and its milestone dates differ from the weekly report baseline.
- The procurement log still has deliveries above the required quantity (sewer GRP 400 mm SN5000 1,060 of 261 m, irrigation 110 mm couplings 322 of 58) and unit typos ("m132", "m133").
- The P6 file's project ID is MOD3-J-1 (MOD3-J-2 in the 20-Oct-2026 update). The failed-start list is still named 20-10-2026 although its content changed.
- Storm drainage is 33,717,565 SAR in the summary sheet and 33,717,595 SAR in the invoice; the earthworks milestone baseline (24-May-2026) is later than its actual finish (31-May-2025); the look-ahead sheet is unchanged and still gives 22-Feb-2026 as the expected finish.
- Several cover fields show #REF ! (EAC, top issues), and the invoice log still has stray values of 21,100,000 and 20,900,000.
- Photos: the ten photos from report 92 were uploaded again and are not reused; the six new photos have no visible date stamp.

Compiled 01-Nov-2026 from the W04 upload: weekly report 94 and the P6 update, both with data date 27-Oct-2026.
