Additional Development and Network Completion, Tabuk Industrial City

تطوير اضافي و استكمال شبكات في تبوك

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ASAS for Developing & Operating Industrial Cities	EGIS	Eng. Yazeed Alragabah	04-Sep-2025	03-Sep-2027

Scope: roads, the Pond A storm-water outfall, storm, sewerage, potable water and fire-fighting, TSE irrigation, road lighting, telecom and CCTV networks in three zones of Tabuk Industrial City. Contract value 140.5M SAR excl. VAT.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 51.9% against 36.7% planned under the revised plan, 15.2% ahead (SPI 1.42). This week it gained 1.2% against 1.5% planned, so the lead narrowed slightly.

PHYSICAL % COMPLETE
51.9% / 36.7% plan
▲ SPI 1.42 +15.2%

PROGRESS THIS WEEK
+1.2% / +1.5% plan
▼ 0.3% below the weekly plan

CONTRACT TIME ELAPSED
57.2% · day 417 of 729
▼ Forecast finish 07-Oct-2027

INVOICED TO DATE (GROSS)
32.9% · 46.2M SAR
14 invoices, last period ends 15-Oct-2026

Well ahead of the revised plan, but the forecast finish is still about five weeks after the contract date.

The P6 update (data date 26-Oct-2026) finishes the project on 07-Oct-2027, 34 days after the contract completion date of 03-Sep-2027, with −29.5 days of float; the weekly report forecasts handover on 06-Oct-2027 (33 days late). Open activities with negative float rose from 220 to 228, mostly in electrical (82), CCTV (70) and telecom (43) works. Against the original baseline, which called for 64.2% by the end of October, the project is behind.

Site photos this week

The two site photos in the 26-Oct-2026 weekly report that are large enough to show. Select a photo to view it larger, then use the arrows to move between photos.



Road subgrade

Grader and roller on the subgrade layer. No date stamp; weekly report 26-Oct-2026.




Pipeline pressure test

Test pump and gauge at a test point. Consultant photo stamped 19-Oct-2026, 13:37.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet, weekly report 26-Oct-2026.

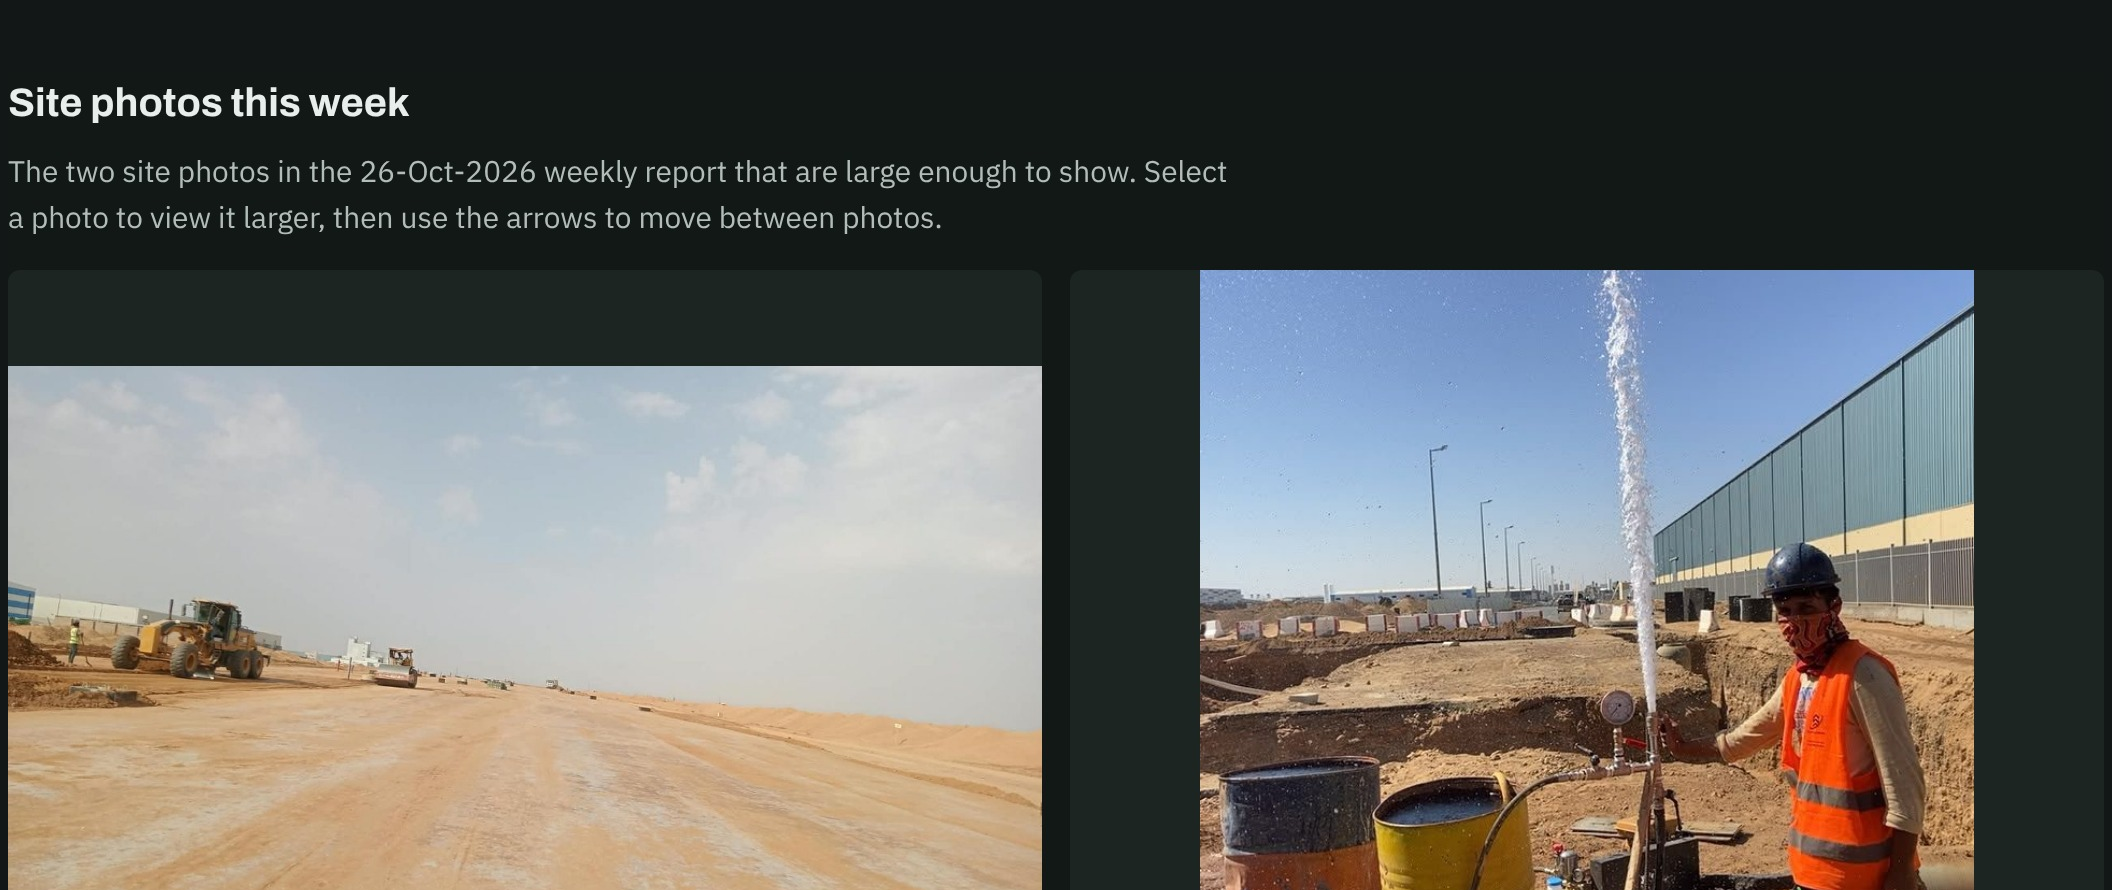

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	34.6	49.9	+15.3	–	1.44
19-Oct-2026	35.2	50.7	+15.5	+0.8	1.44
26-Oct-2026	**36.7**	**51.9**	**+15.2**	**+1.2**	**1.42**

From the Progress sheets of the 19-Oct and 26-Oct weekly reports (the 12-Oct row is the "last week" column of the 19-Oct report); earlier weeks are not available. The weekly table uses 354,339 budgeted man-hours; the S-curve sheet uses 373,967 and shows 49.2% actual at the same date.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.5%	100.0%	100.0%	0.0	1.00	✓ Complete
Construction works	98.0%	37.0%	52.5%	+15.5	1.42	▲ Ahead
Zone 1	21.1%	41.4%	60.2%	+18.7	1.45	▲ Ahead
Zone 2	25.3%	48.9%	72.7%	+23.8	1.49	▲ Ahead
Zone 3	51.6%	29.3%	39.5%	+10.2	1.35	▲ Ahead
Close-out	1.6%	0.0%	0.0%	0.0	–	● Not yet due
Total	100%	**36.7%**	**51.9%**	**+15.2**	**1.42**	▲ Ahead

Engineering and procurement carry no man-hours in this measure, so they are not shown. The P6 update has 1,492 activities: 601 completed, 203 in progress and 688 not started.

Scope of work: quantities

Total, finished and remaining quantity for the main items, from the Major Quantities sheet of the 26-Oct-2026 weekly report. "This week" is the change from the 19-Oct-2026 report. The sheet gives project totals only, with no split by zone and no backfill figures.

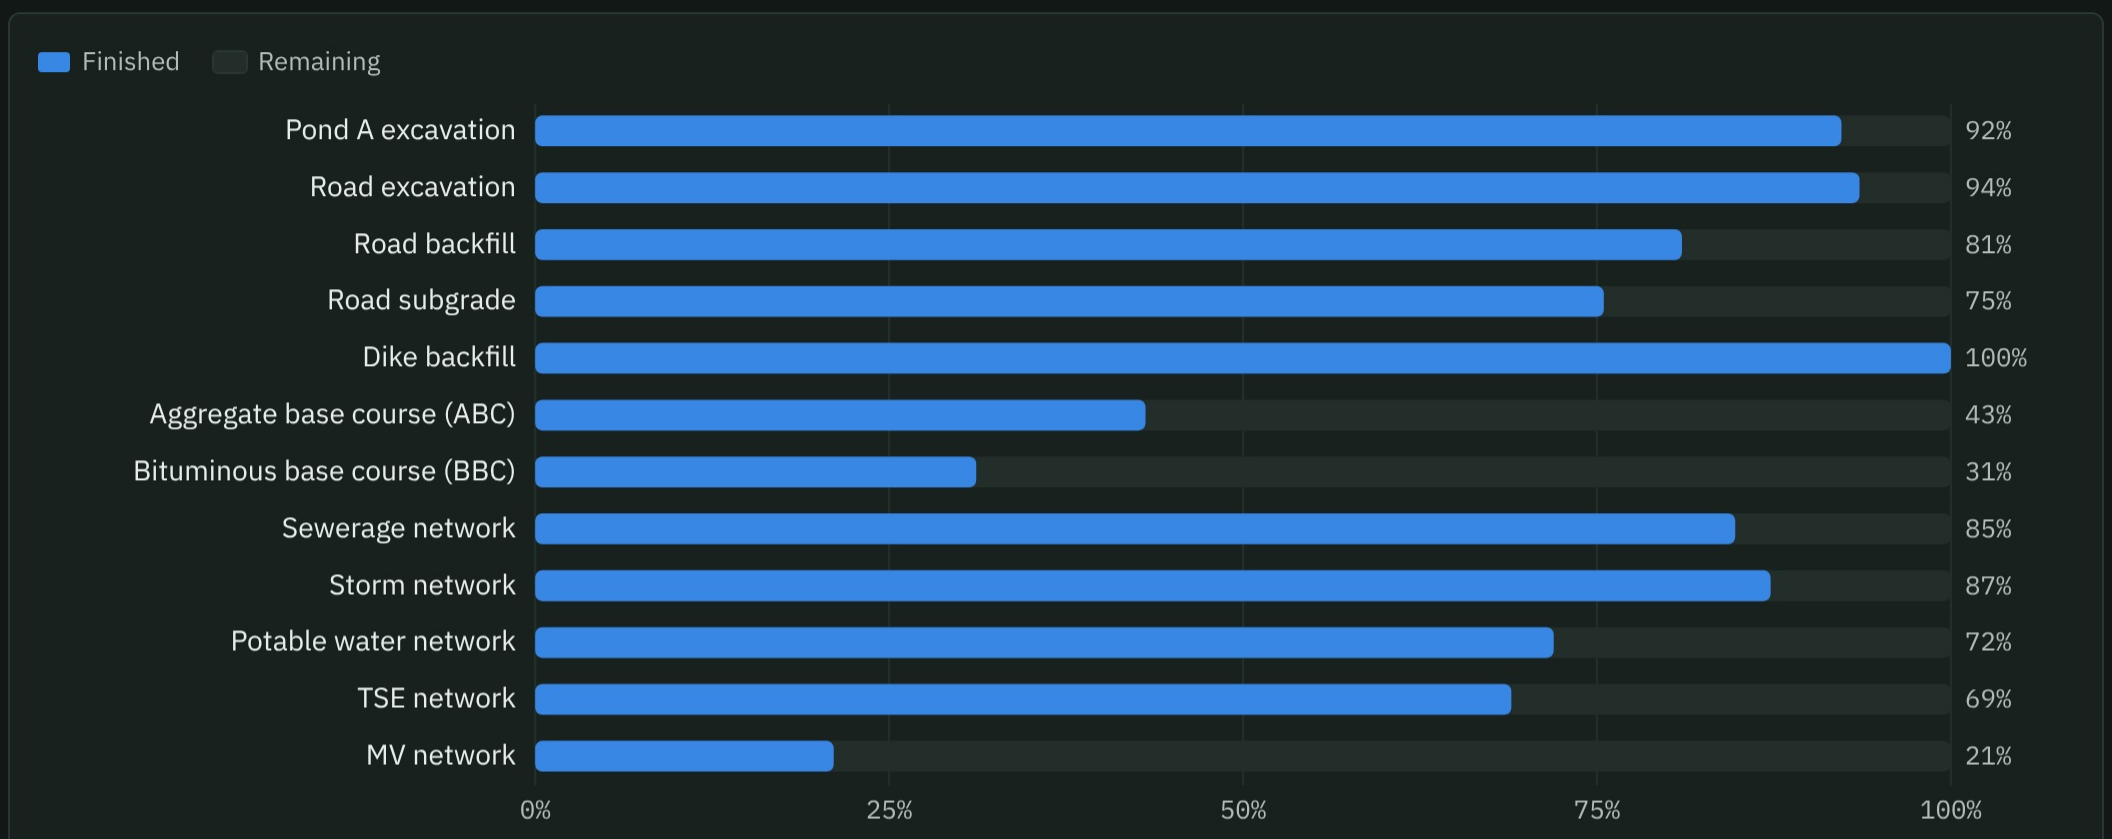

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Pond A excavation	All zones	m³	321,070	296,255	0	24,815	92.3%	–
Road excavation	All zones	m³	99,925	93,475	0	6,450	93.5%	–
Road backfill	All zones	m³	107,100	86,755	+5,155	20,345	81.0%	–
Road subgrade	All zones	m³	72,730	54,900	+1,000	17,830	75.5%	–
Dike backfill	All zones	m³	3,865	3,865	0	0	100.0%	–
Aggregate base course (ABC)	All zones	m³	48,485	20,903	+1,317	27,582	43.1%	–
Bituminous base course (BBC)	All zones	m³	27,310	8,508	0	18,802	31.2%	–
Sewerage network	All zones	LM	8,370	7,095	+40	1,275	84.8%	–
Storm network	All zones	LM	15,638	13,647	+329	1,991	87.3%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Potable water network	All zones	LM	13,221	9,512	+70	3,709	71.9%	–
TSE network	All zones	LM	12,223	8,428	+250	3,795	69.0%	–
MV network	All zones	LM	23,700	4,998	0	18,702	21.1%	–

Wet networks well advanced

Sewerage is 85% laid, storm 87%, potable water 72% and TSE 69%. This week added 329 m of storm, 250 m of TSE, 70 m of potable water and 40 m of sewer pipe.

Road layers and MV behind

Aggregate base course is at 43% (+1,317 m³ this week) and bituminous base course at 31%, unchanged. The MV network is still at 21%, with no progress this week; its connection to the substation is an open issue.

Milestones

Baseline and forecast from the Milestones sheet of the weekly report; P6 forecast and total float from the P6 update (data date 26-Oct-2026). For the network finishes the baseline is the P6 baseline from the progress tracker, and the weekly report gives no forecast.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	04-Sep-2025	04-Sep-2025	04-Sep-2025 (actual)	–	✓ Done
Complete preliminary submittals	06-Dec-2025	24-Nov-2026 (+353 d)	–	–	▼ Late
Complete Zone 1	09-Feb-2027	04-Oct-2027 (+237 d)	24-Jun-2027	+61.2	? Conflicts with P6
Complete Zone 2	02-Aug-2027	05-Sep-2027 (+34 d)	18-Jul-2027	+16.1	? Conflicts with P6
Complete Zone 3	02-Aug-2027	29-Sep-2027 (+58 d)	12-Jun-2027	+72.0	? Conflicts with P6
Sewerage network	14-Aug-2027	–	21-Mar-2027	+143.4	● Float available
Potable water network	21-Aug-2027	–	17-Jun-2027	+67.0	● Float available
TSE network	21-Jul-2027	–	23-Jun-2027	+62.6	● Float available
Storm network	14-Aug-2027	–	29-Jul-2027	+31.8	● Float available
Telecom network	16-Aug-2027	–	12-Sep-2027	−7.6	▼ At risk
CCTV network	03-Sep-2027	–	25-Sep-2027	−18.6	▼ Late
Road works	02-Sep-2027	–	07-Oct-2027	−29.5	▼ Late
Electrical works	03-Sep-2027	–	04-Oct-2027	−26.2	▼ Late
Complete delivery of all materials	03-Aug-2027	07-Oct-2027 (+65 d)	–	–	▼ Late
All works complete, ready for initial handover	10-Aug-2027	25-Sep-2027 (+46 d)	–	–	▼ Late
Project handover	03-Sep-2027	06-Oct-2027 (+33 d)	06-Oct-2027	−28.7	▼ Late

The weekly report and P6 disagree on the zone completion dates.

The weekly report forecasts Zones 1, 2 and 3 to finish between 05-Sep-2027 and 04-Oct-2027, while the P6 update finishes them between 12-Jun-2027 and 18-Jul-2027 with positive float. Both put final handover on 06-Oct-2027; the P6 project finish is 07-Oct-2027. The late items in P6 are road works, electrical, CCTV and telecom.

Procurement of key materials

Completion rate of delivery per material. Source: Procurement sheet, weekly report 26-Oct-2026.

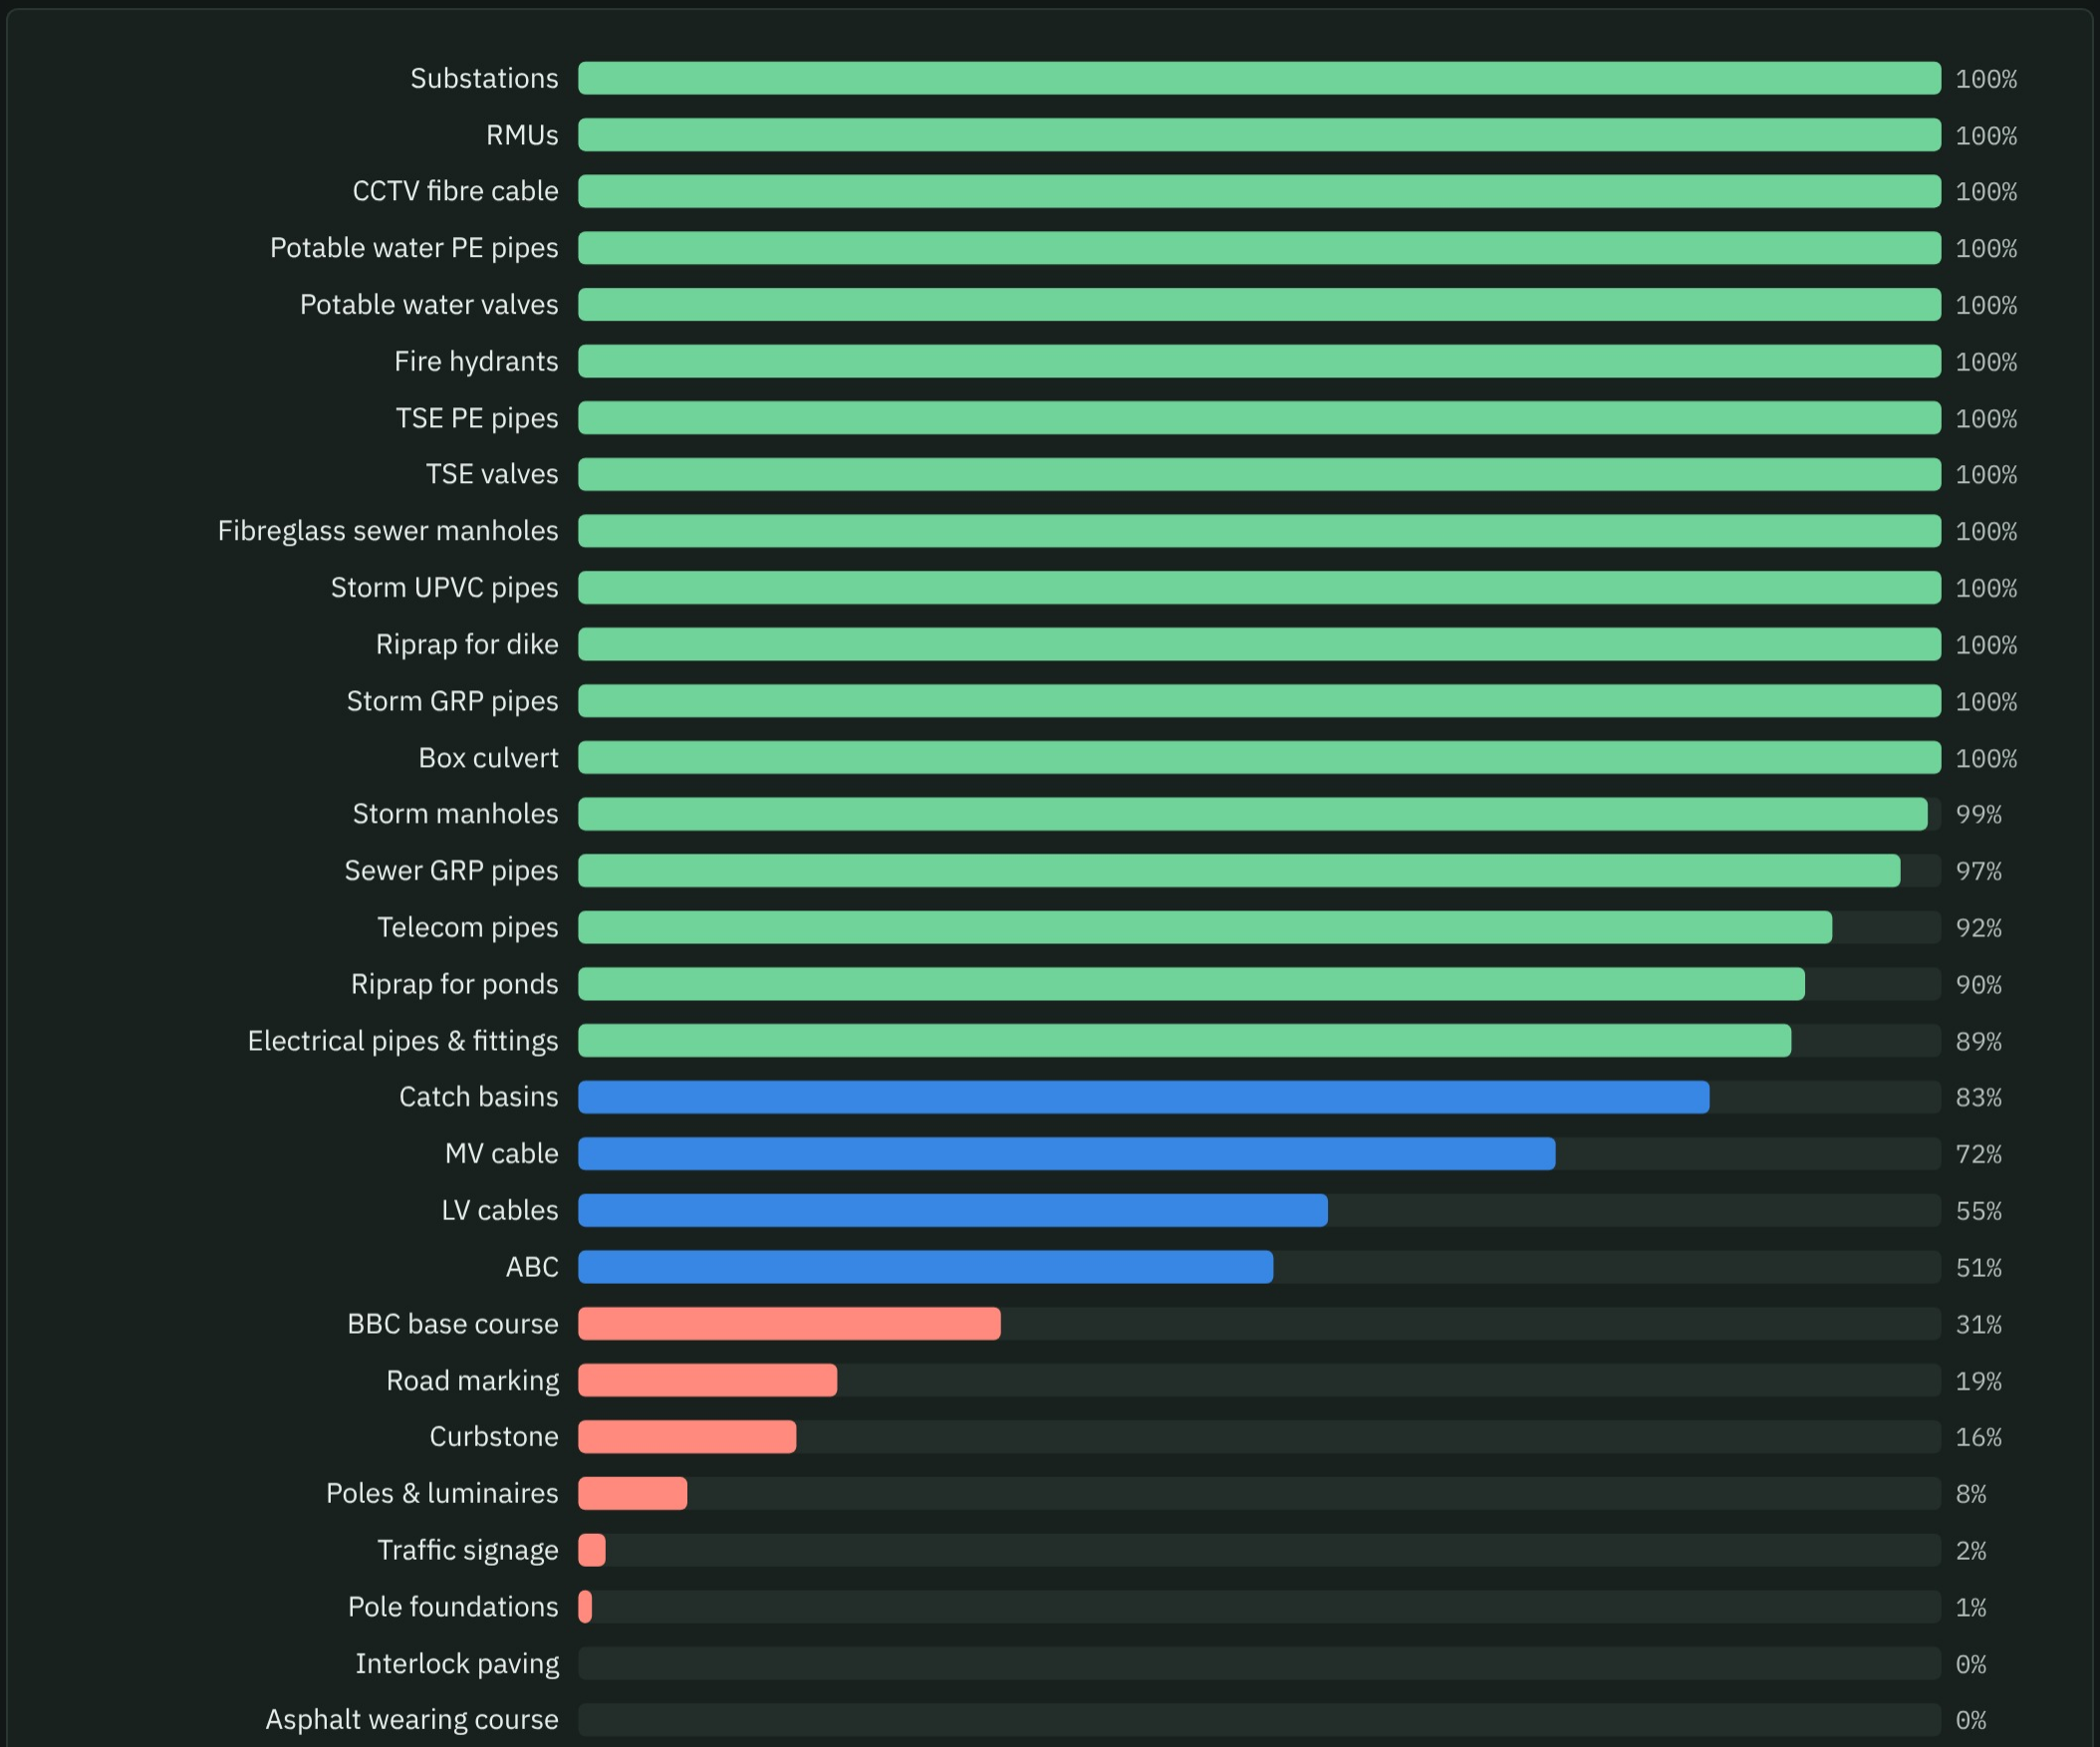

Street lighting has only just started arriving; interlock and wearing course not yet


Poles and luminaires started arriving on 21-Oct-2026 (8% of 957) and pole foundations on 24-Oct-2026 (1%). Interlock (62,075 m²) and the asphalt wearing course have purchase orders but no delivery. Curbstone is at 16% and traffic signage at 2%.

Electrical cables part-delivered

MV cable is at 72% of 115,400 m and LV cables at 55%. Substations and RMUs are fully delivered. Storm GRP pipes and box culverts were completed this week; the other wet-network materials are complete or nearly so.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

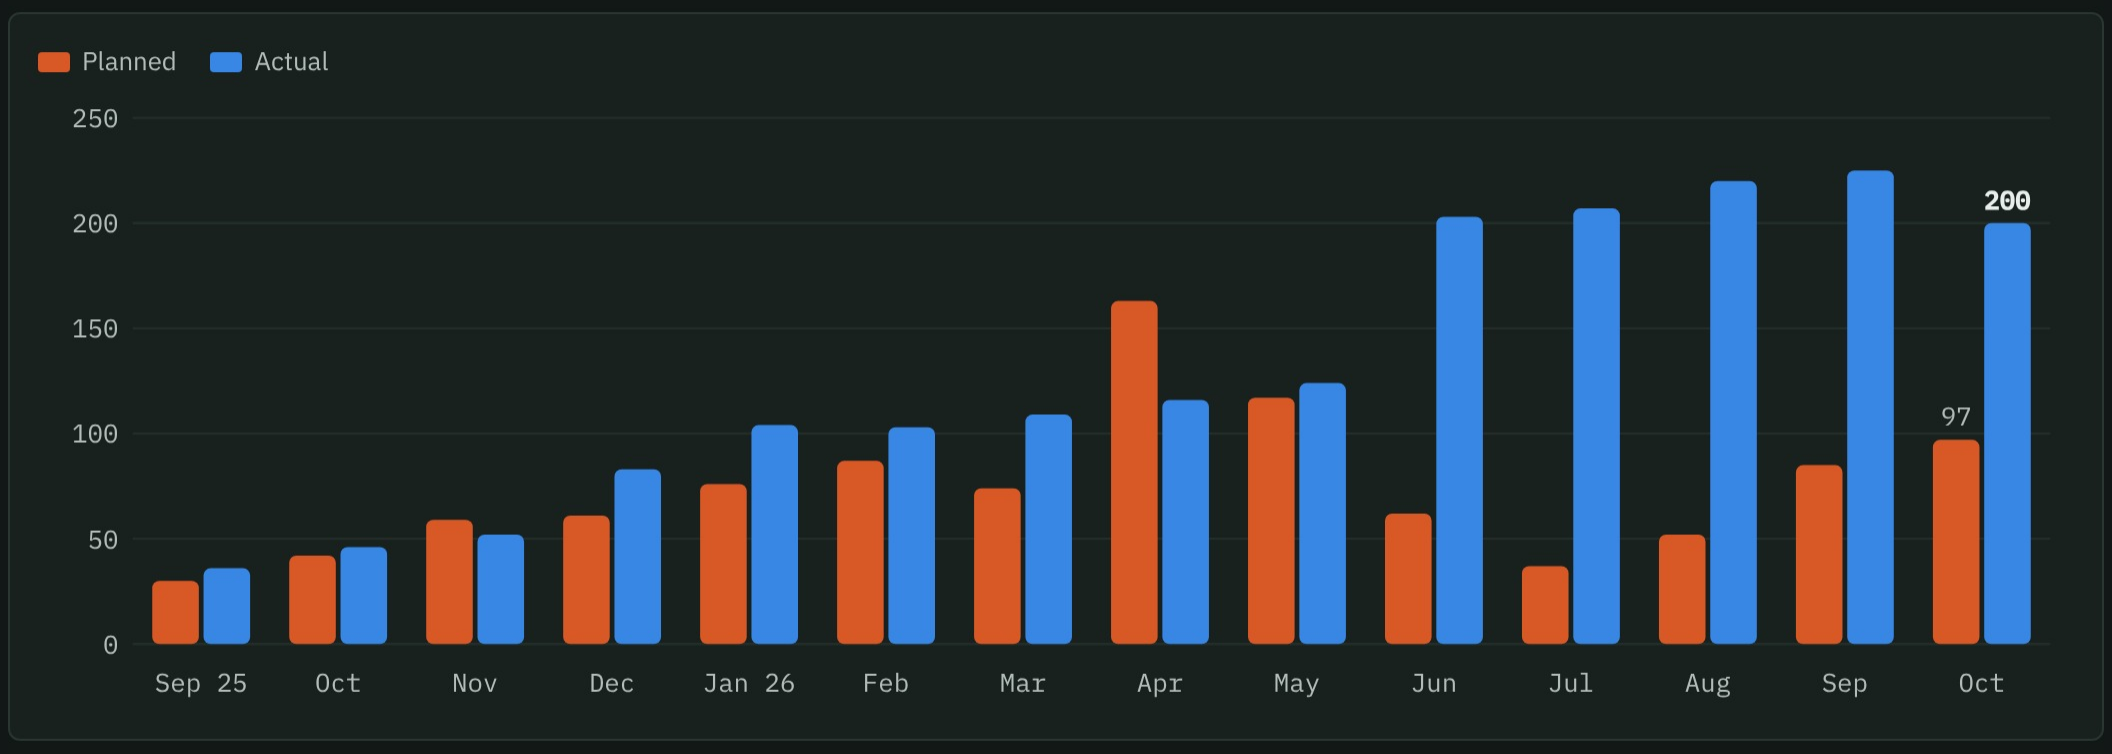

October head count is 200 (35 non-manual, 165 manual) against 97 planned, down from 225 in September. The plan rises to a peak of 229 in March 2027. Equipment on site in October: 62 against 32 planned.

Cost and invoicing

Contract value

Roads	55,700,828
Storm water network	42,542,241
Electrical	21,956,853
Potable water network	7,176,559
TSE network	6,656,378
Sewerage network	6,435,003
Contract value (excl. VAT)	**140,467,862**
Change orders	0

All values in SAR, from the BOQ summary in the weekly report. The parts add up to the contract value. No change orders are registered.

Invoices

Invoices in the log	14
Gross value submitted	46,212,660
PM-approved (13 invoices)	43,497,867
Paid incl. VAT (13 invoices)	50,080,548
Deductions and penalties	76,000
Advance payment (10%)	14,046,786
Retention	0
FIR value to date	55,119,520

Invoicing is 32.9% of the contract value against 51.9% physical progress. No new invoice this week; invoice 14 (1–15 Oct 2026) is still waiting for PM approval.

Health, safety and quality

Safety Score 0.95

Safe man-hours (cumulative)	381,284
Man-hours this week	9,660
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	8 / 36

Quality Score 0.93

FIRs issued / pending	7,260 / 149
MIRs issued / pending	245 / 1
NCRs issued / closed	11 / 11
Site instructions issued / closed	20 / 20
Shop drawing submittals	428
Material submittals approved	48 / 52

Cumulative to 26-Oct-2026. The consultant's weekly audit on 24-Oct-2026 scored quality 0.99 and safety 0.95.

Open issues and risks

ISSUE	OWNER	DETAIL
MV connection to the substation	MODON	Open since 15-Jun-2026. The start of the MV network connection to the station is waiting for the station's response; target moved from 30-Oct to 03-Nov-2026.
Shop drawings to Code A	Contractor	Open since 29-Jun-2026. Drawings are being submitted for upgrade to Code A; target 30-Oct-2026.
Fence blocking electrical works	MODON	Open since 06-Jul-2026. A Shinko fence obstructs the electrical works; referred to the consultant, target moved from 26-Oct to 03-Nov-2026.
More telecom manholes	Contractor	Open since 05-Oct-2026. The number of telecom manholes has increased; waiting for the shop drawing, target moved from 26-Oct to 03-Nov-2026.
Deep excavation	Contractor	Open safety risk: collapse of excavation sides. Barriers and warning signs are in place and equipment is kept away from the edges.

The project challenges named in this week's MODON summary are still the Code A drawing approval and the MV connection to the substation.

Data notes

- Physical progress appears with two values. The weekly report's summary and Progress sheet give 51.91% (183,924 of 354,339 budgeted man-hours), while the Physical-Chart Data sheet gives 49.18% (of 373,967). The headline uses the report's own summary figure.
- The MODON weekly summary file and the P6 progress tracker label cost-weighted progress as "actual" and "planned". This report uses physical % complete (man-hour weighted) only.
- The project ID differs between files: TAB1-02-003 in the weekly report, TAB1-01-009 in the MODON summary file and the older procurement sheet, and TAB1-02-005 to TAB1-02-008 in the risk register.
- Report week: the Milestones sheet states contract week 60 of 109, and the consultant's audits label 24-Oct-2026 as Week-60. Counting whole weeks from site handover gives 59. The report uses the stated week 60. The contract length in weeks changed from 108 to 109.
- Forecast finish: the weekly report gives 06-Oct-2027 (33 days late), and the P6 update gives a project finish of 07-Oct-2027 (34 days late, float −29.5 days) with final handover on 06-Oct-2027.
- Zone milestones disagree three ways: the weekly report's baseline (Zone 1 09-Feb-2027), the P6 baseline in the progress tracker (Zone 1 05-Jun-2027), and the forecasts in the weekly report and P6; see Milestones. The "Complete mobilization" milestone has a baseline of 10-Aug-2027, which looks wrong.
- The HSE statistics repeat last week's figures (9,660 man-hours this week, 381,284 cumulative), so cumulative safe man-hours did not increase.
- The "Resources at site" panel (28/32 non-manual, 57/192 manual) still shows the September figures, not October's (28/35 and 69/165). Cumulative actual equipment has stayed at 269 since March 2026.
- The workbook has two procurement sheets. "Procurement (2)" is an older version with lower rates (for example ABC 32% against 51%); the report uses "Procurement". Some items have no quantity or delivery rate.
- All 14 risk register entries are marked "Open", although 10 of them have their treatment closed. Three open issues had their target dates moved to 03-Nov-2026 without a change in the action taken.
- Scope quantities have no zone split and no backfill values. Only two photos in the report are large enough to use; the other two are 382 and 410 px wide.

Compiled 01-Nov-2026 from the weekly report for the week ending 26-Oct-2026, with the 19-Oct-2026 report for this-week values.
