
Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Development of Phase One – Part Two – Third Industrial City in Dammam - 13-C		773	19-May-25	18-May-27	19-May-25 A	03-Jun-27	),260,141.66
Milestones		0	16-Jul-25	16-Jul-25	15-Oct-26	15-Oct-26	0.00
MIL-0004	Submission and Approval of Drawings and Specifications	0		16-Jul-25		15-Oct-26*	0.00
Mobilization		469	19-May-25	02-Aug-25	19-May-25 A	17-Dec-26	0.00
Deliverables		469	19-May-25	02-Aug-25	19-May-25 A	17-Dec-26	0.00
Submittals		469	19-May-25	02-Aug-25	19-May-25 A	17-Dec-26	0.00
S100015	Prepare & Submit Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover	60	19-May-25	02-Aug-25	10-Oct-26	17-Dec-26	0.00
S10002	Prepare & Submit Method of Statement	20	19-May-25	16-Jun-25	19-May-25 A	13-Oct-26	0.00
Approvals		10	17-Jun-25	28-Jun-25	17-Jul-25 A	19-Oct-26	0.00
S100106	Approval of Method of Statement	10	17-Jun-25	28-Jun-25	17-Jul-25 A	19-Oct-26	0.00
Engineering		265	03-Jul-25	03-Mar-26	20-Jul-25 A	21-Oct-26	433,169.77
Shop Drawing		10	03-Jul-25	16-Jul-25	01-Mar-26 A	15-Oct-26	0.00
Approvals		10	03-Jul-25	16-Jul-25	01-Mar-26 A	15-Oct-26	0.00
A1630	Landscape details approval	10	03-Jul-25	16-Jul-25	01-Mar-26 A	15-Oct-26	0.00
Material Submittal & Approval		265	03-Jul-25	03-Mar-26	20-Jul-25 A	21-Oct-26	433,169.77
Long Lead Items		128	03-Jul-25	30-Jul-25	20-Jul-25 A	14-Oct-26	311,534.63
Generators & Fuel Tanks - PS & Control Bldg backup power		128	03-Jul-25	30-Jul-25	20-Jul-25 A	14-Oct-26	311,534.63
A102930	Material Submittal for Generators & Fuel Tanks - PS & Control Bldg backup power	13	03-Jul-25	21-Jul-25	20-Jul-25 A	13-Oct-26	186,920.78
A102940	Material Approval for Generators & Fuel Tanks - PS & Control Bldg backup power	7	22-Jul-25	30-Jul-25	15-Dec-25 A	14-Oct-26	124,613.85
Short Lead Items		48	18-Feb-26	03-Mar-26	21-Feb-26 A	21-Oct-26	121,635.14
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		7	18-Feb-26	03-Mar-26	21-Feb-26 A	20-Oct-26	16,354.74
A103180	Material Approval for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	7	18-Feb-26	03-Mar-26	21-Feb-26 A	20-Oct-26	16,354.74
Landscaping Materials (Soil, Plants) - Final works, softscape		7	18-Feb-26	03-Mar-26	01-Apr-26 A	21-Oct-26	105,280.40
A103200	Material Approval for Landscaping Materials (Soil, Plants) - Final works, softscape	7	18-Feb-26	03-Mar-26	01-Apr-26 A	21-Oct-26	105,280.40
Procurement		367	05-Aug-25	25-Jan-27	13-Aug-25 A	16-Jan-27	,476,564.74
Prequalification		105	19-Jan-26	29-Jan-26	13-Aug-25 A	14-Oct-26	0.00
Short Lead Items		105	19-Jan-26	29-Jan-26	13-Aug-25 A	14-Oct-26	0.00
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		10	19-Jan-26	29-Jan-26	02-May-26 A	14-Oct-26	0.00
A103560	Prequalification Approval for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	10	19-Jan-26	29-Jan-26	02-May-26 A	14-Oct-26	0.00
Landscaping Materials (Soil, Plants) - Final works, softscape		10	19-Jan-26	29-Jan-26	13-Aug-25 A	14-Oct-26	0.00
A103580	Prequalification Approval for Landscaping Materials (Soil, Plants) - Final works, softscape	10	19-Jan-26	29-Jan-26	13-Aug-25 A	14-Oct-26	0.00
Long Lead Items		181	05-Aug-25	17-Dec-25	08-Dec-25 A	05-Nov-26	,196,886.87
Control & Instrumentation Devices - Flow meters, pressure sensors		65	04-Oct-25	17-Dec-25	13-Apr-26 A	05-Nov-26	285,073.41
A102620	Staging Time for Control & Instrumentation Devices - Flow meters, pressure sensors	30	13-Nov-25	17-Dec-25	16-Apr-26 A	05-Nov-26	0.00
A1570	Delivery for Control & Instrumentation Devices - Flow meters, pressure sensors	35	04-Oct-25	12-Nov-25	13-Apr-26 A	13-Oct-26	285,073.41
Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations		30	12-Nov-25	16-Dec-25	20-Jan-26 A	14-Oct-26	0.00
A102640	Staging Time for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	30	12-Nov-25	16-Dec-25	20-Jan-26 A	14-Oct-26	0.00
Generators & Fuel Tanks - PS & Control Bldg backup power		181	05-Aug-25	13-Dec-25	08-Dec-25 A	02-Nov-26	,911,813.46
A102230	Manufacturing for Generators & Fuel Tanks - PS & Control Bldg backup power	55	05-Aug-25	08-Oct-25	08-Dec-25 A	18-Oct-26	0.00
A102250	Delivery for Generators & Fuel Tanks - PS & Control Bldg backup power	21	15-Oct-25	08-Nov-25	10-Dec-25 A	19-Oct-26	,911,813.46
A102670	Custom Clearance for Generators & Fuel Tanks - PS & Control Bldg backup power	5	09-Oct-25	14-Oct-25	01-Jan-26 A	18-Oct-26	0.00
A102680	Staging Time for Generators & Fuel Tanks - PS & Control Bldg backup power	30	09-Nov-25	13-Dec-25	04-Jul-26 A	02-Nov-26	0.00
Short Lead Items		271	03-Mar-26	25-Jan-27	24-Nov-25 A	16-Jan-27	,279,677.87
Asphalt		63	12-Nov-26	25-Jan-27	01-Dec-25 A	08-Dec-26	635,735.66
A102730	Delivery for Asphalt Phase 1	21	12-Nov-26	07-Dec-26	01-Dec-25 A	08-Dec-26	211,911.89
A103740	Delivery for Asphalt Phase 2	21	07-Dec-26	31-Dec-26	08-Dec-25 A	08-Dec-26	211,911.89
A103750	Delivery for Asphalt Phase 3	21	31-Dec-26	25-Jan-27	14-Dec-25 A	08-Dec-26	211,911.89
Communication Ducts & Manholes - Telecom systems		30	28-Oct-26	02-Dec-26	24-Nov-25 A	16-Jan-27 A	393,029.41
A102050	Delivery for Communication Ducts & Manholes - Telecom systems	30	28-Oct-26	02-Dec-26	24-Nov-25 A	16-Jan-27 A	393,029.41

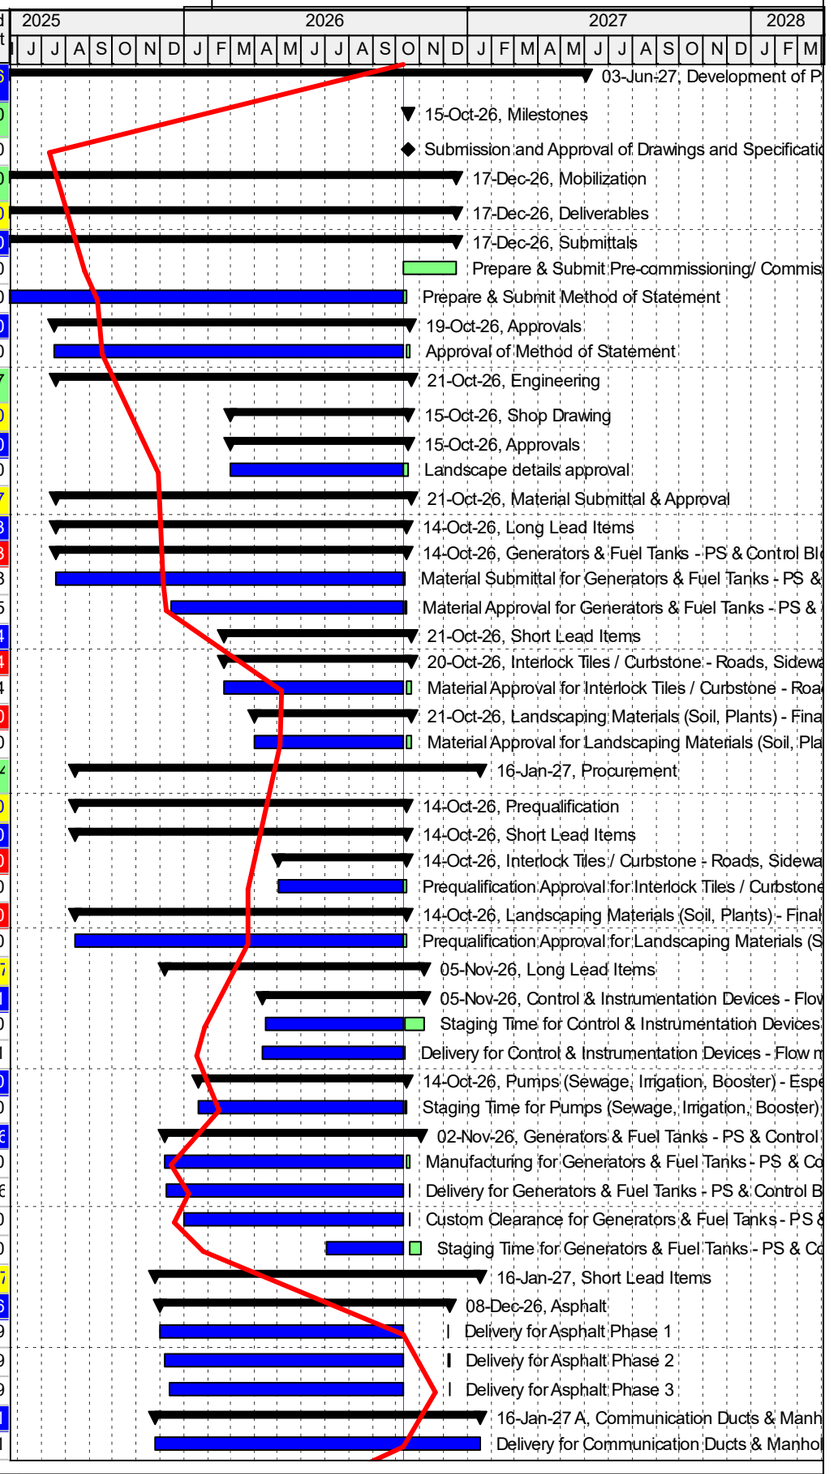


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		90	11-Mar-26	07-Jul-26	01-Jan-26 A	09-Nov-26	250,912.80
A102380	Manufacturing for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	11-Mar-26	23-Apr-26	01-Jan-26 A	20-Oct-26	0.00
A102400	Delivery for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	23-Apr-26	02-Jun-26	01-Apr-26 A	21-Oct-26	250,912.80
A102820	Staging Time for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	02-Jun-26	07-Jul-26	04-Jul-26 A	09-Nov-26	0.00
Landscaping Materials (Soil, Plants) - Final works, softscape		64	03-Mar-26	02-Jun-26	21-Oct-26	04-Jan-27	0.00
A102350	Issue PO for Landscaping Materials (Soil, Plants) - Final works, softscape	4	03-Mar-26	10-Mar-26	21-Oct-26	26-Oct-26	0.00
A102360	Manufacturing for Landscaping Materials (Soil, Plants) - Final works, softscape	60	11-Mar-26	02-Jun-26	26-Oct-26	04-Jan-27	0.00
Construction		544	19-Oct-25	25-Apr-27	03-Sep-25 A	03-Jun-27	9,006,953.2
Zone 3		328	19-Oct-25	10-Oct-26	04-Oct-25 A	24-Apr-27	8,792,446.8
Sewerage Network Zone 3		168	19-Oct-25	25-Jun-26	13-Jan-26 A	24-Apr-27	1,479,546.2
Pipework: Supply, Installation, and Testing		154	29-Dec-25	27-Jan-26	01-Mar-26 A	02-Nov-26	20,836.71
HDPE Pressure Pipes Installation (250mm–630mm)		154	29-Dec-25	27-Jan-26	01-Mar-26 A	02-Nov-26	20,836.71
MOD-SWN-	Backfilling & Warning Tape HDPE for Sewerage Network Zone 3	15	13-Jan-26	27-Jan-26	19-Oct-26	02-Nov-26	10,418.36
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 3	15	29-Dec-25	12-Jan-26	01-Mar-26 A	18-Oct-26	10,418.36
Fittings and Valves		24	14-Dec-25	10-Jan-26	10-Oct-26	05-Nov-26	27,640.08
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 3	6	14-Dec-25	20-Dec-25	10-Oct-26	15-Oct-26	6,826.21
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 3	4	21-Dec-25	24-Dec-25	17-Oct-26	20-Oct-26	4,830.30
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 3	4	25-Dec-25	29-Dec-25	21-Oct-26	25-Oct-26	4,392.82
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 3	10	30-Dec-25	10-Jan-26	26-Oct-26	05-Nov-26	11,590.74
Valve & Flow Meter Chambers		55	19-Oct-25	06-Jan-26	08-Jun-26 A	16-Nov-26	33,389.88
Valve Chambers Construction		48	19-Oct-25	20-Dec-25	08-Jun-26 A	08-Nov-26	5,515.25
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	08-Jun-26 A	18-Oct-26	1,034.11
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	22-Jul-26 A	28-Oct-26	689.41
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 3	15	06-Dec-25	20-Dec-25	04-Aug-26 A	08-Nov-26	689.41
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 3	6	30-Nov-25	05-Dec-25	31-Jul-26 A	31-Oct-26	3,102.33
Water Drain Chambers Construction		42	19-Oct-25	24-Dec-25	16-Jun-26 A	10-Nov-26	15,675.99
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	16-Jun-26 A	16-Oct-26	3,359.14
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	23-Jun-26 A	24-Oct-26	2,239.43
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone 3	19	06-Dec-25	24-Dec-25	01-Jul-26 A	10-Nov-26	10,077.42
Discharge Chambers Construction		55	19-Oct-25	06-Jan-26	01-Jul-26 A	16-Nov-26	10,950.53
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	01-Jul-26 A	18-Oct-26	2,346.54
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	15-Jul-26 A	28-Oct-26	1,564.36
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 3	13	25-Dec-25	06-Jan-26	01-Aug-26 A	16-Nov-26	7,039.63
Flow Meter Chambers Construction		42	19-Oct-25	29-Nov-25	14-Jul-26 A	30-Oct-26	1,248.11
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	14-Jul-26 A	18-Oct-26	748.87
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	29-Jul-26 A	30-Oct-26	499.24
Manholes		128	09-Nov-25	27-Jan-26	24-Feb-26 A	08-Nov-26	271,787.00
1500mm GRP Manholes (Standard & Backdrop)		128	09-Nov-25	25-Jan-26	10-Mar-26 A	08-Nov-26	260,172.16
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	21-Dec-25	10-Jan-26	18-Mar-26 A	24-Oct-26	180,119.19
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	10-Mar-26 A	18-Oct-26	40,026.49
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 3	15	11-Jan-26	25-Jan-26	24-Oct-26	08-Nov-26	40,026.49
1800mm GRP Manholes (Standard & Backdrop)		59	09-Nov-25	27-Jan-26	24-Feb-26 A	29-Oct-26	10,982.49
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	11-Jan-26	27-Jan-26	04-Mar-26 A	29-Oct-26	8,985.68
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	24-Feb-26 A	18-Oct-26	1,996.82
2000mm GRP Manholes (Standard & Backdrop)		21	09-Nov-25	29-Nov-25	04-Mar-26 A	18-Oct-26	632.35
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	04-Mar-26 A	18-Oct-26	632.35
Pumping Stations		40	01-Dec-25	25-Jun-26	13-Jan-26 A	24-Apr-27	1,125,892.53
In-Line Booster Stations		21	01-Dec-25	24-Dec-25	10-Oct-26	02-Nov-26	656,073.36
MOD-SWN-	In-Line Booster Stations - Civil Works for Sewerage Network Zone 3	21	01-Dec-25	24-Dec-25	10-Oct-26	02-Nov-26	656,073.36
Engine/Motor Control Center Buildings		7	01-Dec-25	08-Dec-25	11-Oct-26	18-Oct-26	42,052.73

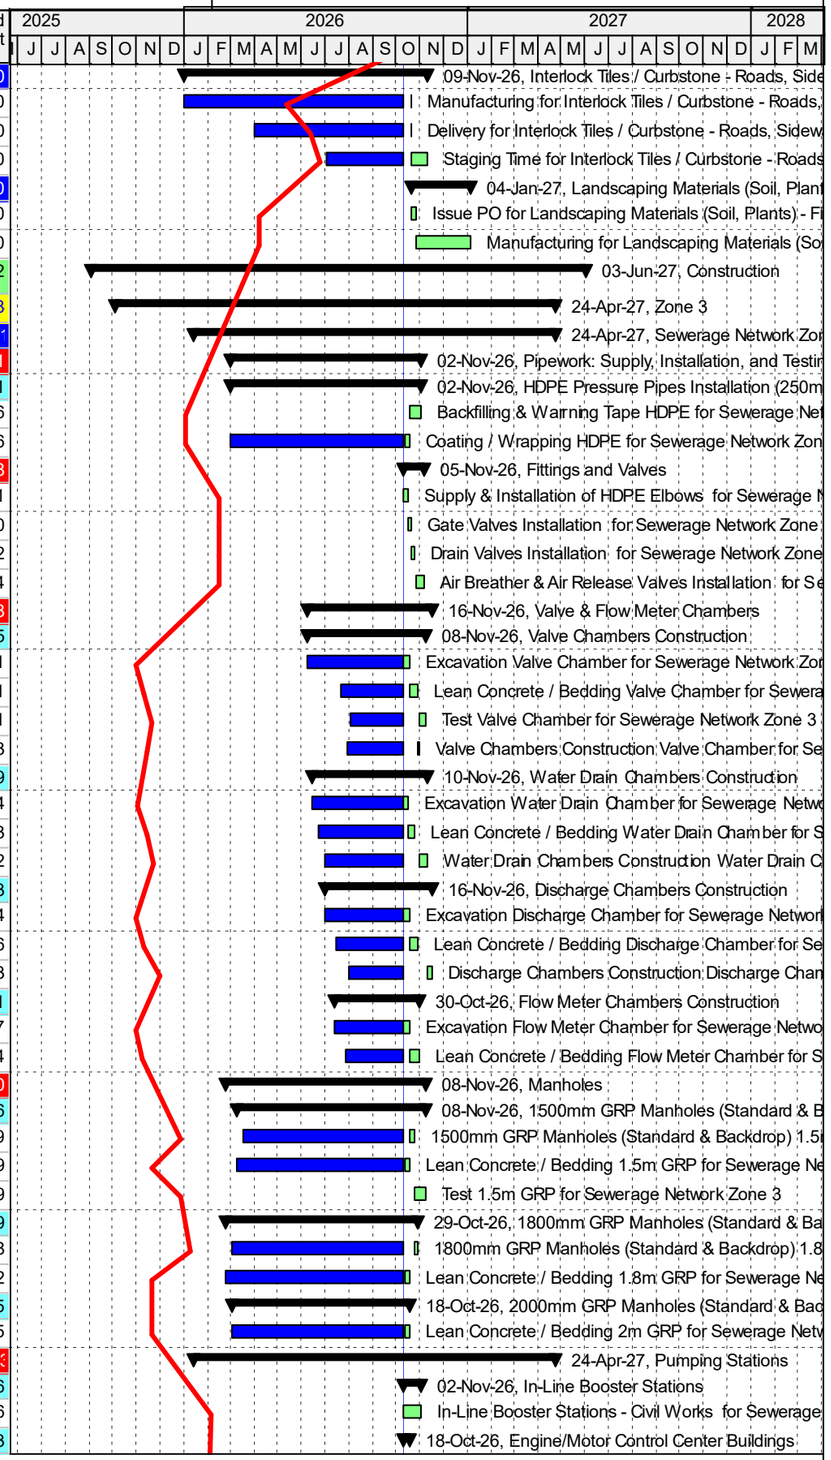


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-SWN-	MCC Building – PS4 for Sewerage Network Zone 3	7	01-Dec-25	08-Dec-25	11-Oct-26	18-Oct-26	42,052.73
Valves and Fittings (General Supply & Installation)		8	18-Dec-25	27-Dec-25	30-Aug-26 A	12-Nov-26	43,723.31
MOD-SWN-	Valves, fittings, flow meters – PS3 for Sewerage Network Zone 3	2	18-Dec-25	20-Dec-25	30-Aug-26 A	07-Nov-26	11,924.59
MOD-SWN-	Valves, fittings, flow meters – PS4 for Sewerage Network Zone 3	3	21-Dec-25	23-Dec-25	01-Sep-26 A	10-Nov-26	14,516.89
MOD-SWN-	35mm SS 316 mesh network – PS4 for Sewerage Network Zone 3	3	24-Dec-25	27-Dec-25	08-Sep-26 A	12-Nov-26	17,281.83
Lighting Works		13	10-Jun-26	25-Jun-26	13-Jan-26 A	24-Apr-27	384,043.12
MOD-SWN-	250W Flood Light installation – PS3 & PS4 for Sewerage Network Zone 3	13	10-Jun-26	25-Jun-26	13-Jan-26 A	24-Apr-27	384,043.12
Rainwater Drainage Network Zone 3		222	15-Nov-25	18-Jan-26	05-Jan-26 A	07-Nov-26	3,861,084.25
Pipe Laying Works		221	03-Dec-25	18-Jan-26	05-Jan-26 A	06-Nov-26	154,441.32
Supply & Installation of uPVC Pipes (250–300mm dia)		82	06-Dec-25	13-Dec-25	23-Feb-26 A	16-Oct-26	75,388.93
MOD-RWN-	Coating / Wrapping UPVC for Rainwater Drainage Network Zone 3	2	06-Dec-25	07-Dec-25	23-Feb-26 A	13-Oct-26	37,694.46
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 3	8	06-Dec-25	13-Dec-25	21-Jun-26 A	16-Oct-26	37,694.46
Supply & Installation of GRP Pipes (350–800mm dia)		42	08-Dec-25	18-Jan-26	01-Jun-26 A	30-Oct-26	51,668.82
MOD-RWN-	Test (Pressure-slope) GRP for Rainwater Drainage Network Zone 3	11	08-Dec-25	18-Dec-25	01-Jun-26 A	15-Oct-26	17,222.94
MOD-RWN-	Coating / Wrapping GRP for Rainwater Drainage Network Zone 3	21	19-Dec-25	08-Jan-26	01-Jul-26 A	25-Oct-26	17,222.94
MOD-RWN-	Backfilling & compaction GRP for Rainwater Drainage Network Zone 3	10	09-Jan-26	18-Jan-26	01-Aug-26 A	30-Oct-26	17,222.94
uPVC Connection Pipes (150mm dia)		221	03-Dec-25	03-Jan-26	05-Jan-26 A	06-Nov-26	27,383.57
MOD-RWN-	Lay & connect UPVC Con. for Rainwater Drainage Network Zone 3	8	03-Dec-25	10-Dec-25	05-Jan-26 A	13-Oct-26	18,957.86
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 3	3	11-Dec-25	13-Dec-25	13-Oct-26	16-Oct-26	4,212.86
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 3	21	14-Dec-25	03-Jan-26	16-Oct-26	06-Nov-26	4,212.86
Precast Concrete Box Culverts		51	15-Nov-25	18-Dec-25	05-Sep-26 A	03-Nov-26	609,520.19
Box Culverts (500x500mm to 3500x800mm)		51	15-Nov-25	18-Dec-25	05-Sep-26 A	03-Nov-26	609,520.19
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 3	10	15-Nov-25	02-Dec-25	05-Sep-26 A	18-Oct-26	212,007.02
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	4	02-Dec-25	07-Dec-25	18-Oct-26	22-Oct-26	79,502.63
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 3	10	07-Dec-25	18-Dec-25	22-Oct-26	03-Nov-26	318,010.53
Manholes		7	07-Dec-25	15-Dec-25	22-Oct-26	31-Oct-26	27,301.33
Circular GRP Manholes (1200–1800mm dia)		7	07-Dec-25	15-Dec-25	22-Oct-26	31-Oct-26	8,004.81
MOD-RWN-	Excavate to full manhole depth Circular Manhole for Rainwater Drainage Network Zone 3	7	07-Dec-25	15-Dec-25	22-Oct-26	31-Oct-26	8,004.81
Concrete Manholes for 1500x1500 Box Pipes		6	07-Dec-25	14-Dec-25	22-Oct-26	29-Oct-26	12,407.65
MOD-RWN-	Excavation Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	22-Oct-26	29-Oct-26	12,407.65
Concrete Manholes for 1000x1000 Box Pipes		6	07-Dec-25	14-Dec-25	22-Oct-26	29-Oct-26	6,888.88
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	22-Oct-26	29-Oct-26	6,888.88
Chambers and Catch Basins		120	29-Dec-25	17-Jan-26	16-Mar-26 A	28-Oct-26	74,226.71
Gully Outfalls		33	29-Dec-25	05-Jan-26	16-Mar-26 A	24-Oct-26	31,336.47
MOD-RWN-	Provide slope protection (riprap) Gully Outfall for Rainwater Drainage Network Zone 3	4	29-Dec-25	03-Jan-26	16-Mar-26 A	22-Oct-26	13,429.92
MOD-RWN-	Compact and shape terrain Gully Outfall for Rainwater Drainage Network Zone 3	2	03-Jan-26	05-Jan-26	23-Jun-26 A	24-Oct-26	17,906.55
Rainwater Catch Basins		2	07-Jan-26	10-Jan-26	01-Jul-26 A	22-Oct-26	26,080.25
MOD-RWN-	Backfill and surface finish Catch Basin for Rainwater Drainage Network Zone 3	2	07-Jan-26	10-Jan-26	01-Jul-26 A	22-Oct-26	26,080.25
Precast Chambers for Absorption Pits		5	11-Jan-26	17-Jan-26	22-Oct-26	28-Oct-26	16,809.98
MOD-RWN-	Backfill and compact Absorption Pit for Rainwater Drainage Network Zone 3	5	11-Jan-26	17-Jan-26	22-Oct-26	28-Oct-26	16,809.98
Gully Outfalls to Swales		142	28-Dec-25	17-Jan-26	09-Feb-26 A	07-Nov-26	150,363.53
Gully Outfalls to Swales		133	31-Dec-25	17-Jan-26	09-Feb-26 A	27-Oct-26	127,366.76
MOD-RWN-	Excavate outfall channel Gully Outfall to Swales for Rainwater Drainage Network Zone 3	4	31-Dec-25	05-Jan-26	09-Feb-26 A	22-Oct-26	28,303.72
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	5	05-Jan-26	11-Jan-26	01-Mar-26 A	24-Oct-26	63,683.38
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	3	11-Jan-26	14-Jan-26	04-Mar-26 A	25-Oct-26	21,227.79
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	14-Jan-26	17-Jan-26	25-Oct-26	27-Oct-26	14,151.86
Riprap Works & Protection		13	28-Dec-25	12-Jan-26	22-Oct-26	07-Nov-26	22,996.78
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 3	3	28-Dec-25	31-Dec-25	22-Oct-26	26-Oct-26	3,537.97
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 3	10	31-Dec-25	12-Jan-26	26-Oct-26	07-Nov-26	19,458.81
Backfilling & Bedding		126	03-Dec-25	18-Jan-26	29-Mar-26 A	02-Nov-26	535,371.75
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		126	03-Dec-25	18-Jan-26	29-Mar-26 A	02-Nov-26	535,371.75

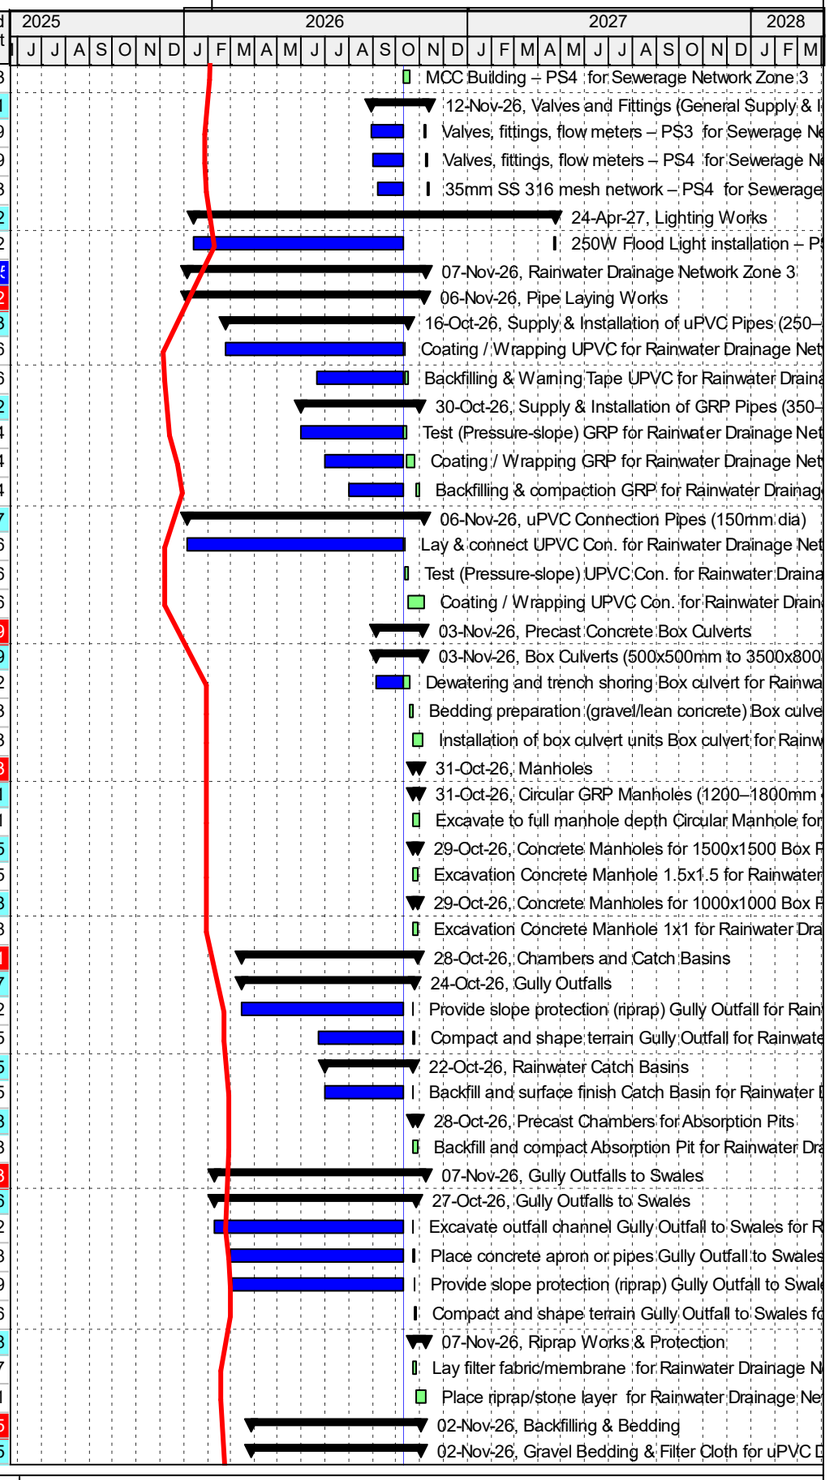


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 3	21	03-Dec-25	28-Dec-25	29-Mar-26 A	13-Oct-26	344,167.55
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 3	6	28-Dec-25	04-Jan-26	01-Jul-26 A	19-Oct-26	114,722.52
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 3	12	04-Jan-26	18-Jan-26	19-Oct-26	02-Nov-26	76,481.68
Deep Basin for Groundwater Collection (2.5–3.0m)		142	30-Nov-25	18-Jan-26	16-Feb-26 A	02-Nov-26	2,309,859.43
MOD-RWN-DB	Pipe connections for inflow for Rainwater Drainage Network Zone 3	12	30-Nov-25	14-Dec-25	16-Feb-26 A	13-Oct-26	513,302.09
MOD-RWN-DB	Cover slab and access shaft for Rainwater Drainage Network Zone 3	13	14-Dec-25	29-Dec-25	24-Feb-26 A	17-Oct-26	769,953.14
MOD-RWN-DB	Waterproofing & sealant for Rainwater Drainage Network Zone 3	10	29-Dec-25	10-Jan-26	04-Jul-26 A	25-Oct-26	898,278.67
MOD-RWN-DB	Backfill in controlled layers for Rainwater Drainage Network Zone 3	7	10-Jan-26	18-Jan-26	25-Oct-26	02-Nov-26	128,325.52
Potable Water Network Zone 3		303	19-Oct-25	18-Jan-26	13-Oct-25 A	29-Dec-26	5,600,555.40
Pipe Installation Works		68	13-Nov-25	14-Dec-25	16-Jan-26 A	20-Oct-26	751,774.60
MOD-PWN-PI-	HDPE Pipe Laying (200 mm to 710 mm) for Potable Water Network Zone 3	10	13-Nov-25	03-Dec-25	16-Jan-26 A	15-Oct-26	451,064.76
MOD-PWN-PI-	Test (Pressure-slope) for Potable Water Network Zone 3	3	04-Dec-25	06-Dec-25	01-Feb-26 A	16-Oct-26	100,236.61
MOD-PWN-PI-	Coating / Wrapping for Potable Water Network Zone 3	5	07-Dec-25	11-Dec-25	09-Feb-26 A	18-Oct-26	100,236.61
MOD-PWN-PI-	Backfilling & Warning Tape for Potable Water Network Zone 3	3	12-Dec-25	14-Dec-25	23-Feb-26 A	20-Oct-26	100,236.61
Valve Installation & Chambers		20	27-Dec-25	18-Jan-26	10-Oct-26	02-Nov-26	47,445.51
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 3	14	27-Dec-25	11-Jan-26	10-Oct-26	26-Oct-26	31,630.34
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	26-Oct-26	02-Nov-26	15,815.17
Flow Meter Installation		63	30-Nov-25	07-Jan-26	05-Sep-26 A	17-Nov-26	39,998.50
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 3	8	30-Nov-25	08-Dec-25	05-Sep-26 A	14-Oct-26	9,230.42
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 3	10	18-Dec-25	29-Dec-25	08-Sep-26 A	11-Nov-26	21,537.66
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 3	8	30-Dec-25	07-Jan-26	15-Sep-26 A	17-Nov-26	9,230.42
Washout & Air Valve Chambers		26	22-Dec-25	03-Jan-26	16-Aug-26 A	15-Oct-26	84,011.28
MOD-PWN-WA	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 3	6	22-Dec-25	28-Dec-25	16-Aug-26 A	13-Oct-26	45,075.10
MOD-PWN-WA	Covers, Ladders & Tags for Potable Water Network Zone 3	3	29-Dec-25	31-Dec-25	15-Sep-26 A	13-Oct-26	19,468.09
MOD-PWN-WA	Backfilling & Final Finishing for Potable Water Network Zone 3	2	01-Jan-26	03-Jan-26	13-Oct-26	15-Oct-26	19,468.09
Pumping Station (Structure & Civil Works)		18	19-Oct-25	09-Nov-25	10-Oct-26	29-Oct-26	157,715.02
MOD-PWN-PS	Excavation & Blinding for Potable Water Network Zone 3	10	19-Oct-25	30-Oct-25	10-Oct-26	20-Oct-26	78,857.51
MOD-PWN-PS	Reinforced Concrete/GRP Shell Construction for Potable Water Network Zone 3	8	30-Oct-25	09-Nov-25	21-Oct-26	29-Oct-26	78,857.51
Water Storage System		11	05-Jan-26	18-Jan-26	13-Oct-25 A	29-Dec-26	5,159,570.07
MOD-PWN-WS	Structural tanks for supply or pressure equalization for Potable Water Network Zone 3	11	05-Jan-26	18-Jan-26	13-Oct-25 A	29-Dec-26	5,159,570.07
Street Lighting		16	22-Dec-25	11-Jan-26	13-Dec-25 A	06-Dec-26	360,040.43
MOD-PWN-SL-	Conduits, Cabling, Backfilling for Potable Water Network Zone 3	12	22-Dec-25	05-Jan-26	15-Dec-25 A	06-Dec-26	72,008.09
MOD-PWN-SL-	Pole & Fixture Installation for Potable Water Network Zone 3	16	24-Dec-25	11-Jan-26	13-Dec-25 A	06-Dec-26	288,032.34
Irrigation Network Zone 3		183	18-Nov-25	06-Jan-26	07-Apr-26 A	10-Nov-26	441,083.59
Excavation, Pipe Laying & Backfilling		128	18-Nov-25	14-Dec-25	07-Apr-26 A	16-Oct-26	409,713.37
MOD-IRN-EB-1	HDPE Pipe Laying (125 mm to 630 mm) for Irrigation Network Zone 3	21	18-Nov-25	08-Dec-25	07-Apr-26 A	15-Oct-26	245,828.02
MOD-IRN-EB-1	Test (Pressure-slope) for Irrigation Network Zone 3	2	09-Dec-25	10-Dec-25	01-May-26 A	15-Oct-26	54,628.45
MOD-IRN-EB-1	Coating / Wrapping for Irrigation Network Zone 3	2	11-Dec-25	12-Dec-25	01-Jun-26 A	15-Oct-26	54,628.45
MOD-IRN-EB-1	Backfilling & Warning Tape for Irrigation Network Zone 3	2	13-Dec-25	14-Dec-25	13-Jul-26 A	16-Oct-26	54,628.45
Valves and Appurtenances		2	27-Dec-25	28-Dec-25	07-Jul-26 A	13-Oct-26	2,225.96
MOD-IRN-VA-9	Support Brackets/Anchor Blocks for Irrigation Network Zone 3	2	27-Dec-25	28-Dec-25	07-Jul-26 A	13-Oct-26	2,225.96
Flow Meter Chambers		77	18-Dec-25	06-Jan-26	01-Jul-26 A	10-Nov-26	29,144.25
MOD-IRN-FC-1	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 3	6	31-Dec-25	06-Jan-26	21-Jul-26 A	10-Nov-26	6,725.60
MOD-IRN-FC-8	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	6	18-Dec-25	24-Dec-25	01-Jul-26 A	07-Nov-26	15,693.06
MOD-IRN-FC-9	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 3	5	25-Dec-25	30-Dec-25	02-Jul-26 A	08-Nov-26	6,725.60
Rainwater Collection Ponds Zone 3		206	22-Jan-26	10-Oct-26	04-Oct-25 A	16-Jan-27	6,019,252.8
Excavation for Rainwater Drainage Pond		186	22-Jan-26	10-Mar-26	04-Oct-25 A	06-Jan-27	374,909.60
Deep excavation, backfill, disposal for pond formation		186	22-Jan-26	10-Mar-26	04-Oct-25 A	06-Jan-27	374,909.60
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 3	6	11-Feb-26	19-Feb-26	01-Jul-26 A	04-Jan-27	29,598.13
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone 3	7	19-Feb-26	05-Mar-26	10-Aug-26 A	06-Jan-27	98,660.42

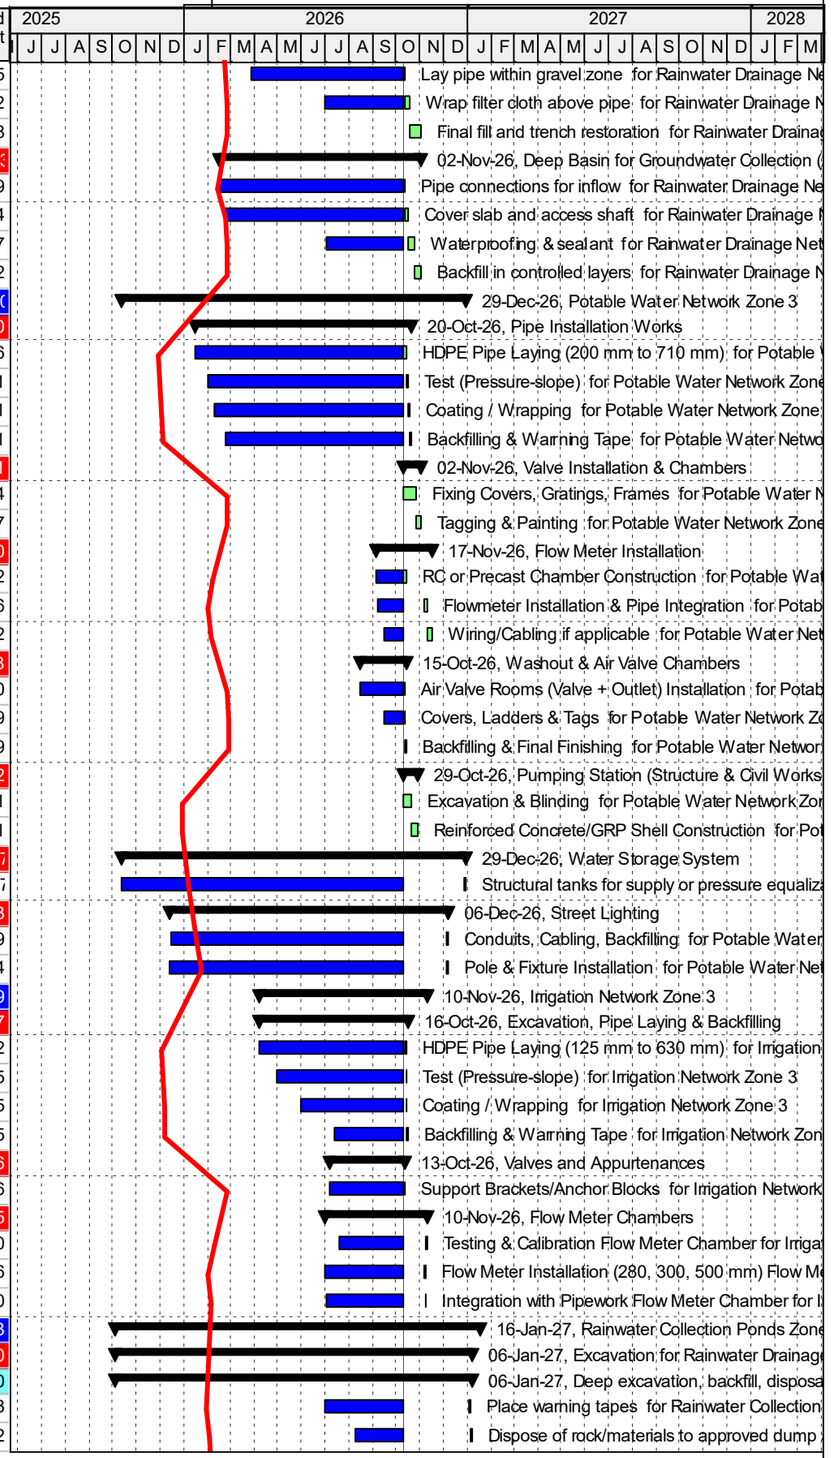


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 3	2	07-Mar-26	10-Mar-26	01-Sep-26 A	06-Jan-27	7,892.83
MOD-RCP-E	Excavate in layers to final depth for Rainwater Collection Ponds Zone 3	12	22-Jan-26	04-Feb-26	04-Oct-25 A	02-Jan-27	120,365.71
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 3	5	05-Feb-26	10-Feb-26	01-Mar-26 A	03-Jan-27	118,392.51
General Site Preparation		39	16-Mar-26	10-May-26	12-Oct-25 A	05-Jan-27	4,165,976.4
MOD-RCP-GS-	Earthwork excavation (other than topsoil or rock) - Zone 3 (3 Ponds) for Rainwater Collec	21	16-Mar-26	15-Apr-26	12-Oct-25 A	03-Jan-27	7,689,673.8
MOD-RCP-GS-	Transport and disposal to approved locations - Zone 3 (3 Ponds) for Rainwater Collectio	21	15-Apr-26	10-May-26	06-Dec-25 A	05-Jan-27	3,476,302.5
Backfilling Works		146	10-May-26	23-Jul-26	18-Nov-25 A	16-Jan-27	802,306.77
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	10-May-26	01-Jun-26	11-Dec-25 A	07-Jan-27	168,906.69
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 3	21	01-Jun-26	25-Jun-26	29-Nov-25 A	10-Jan-27	295,586.71
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 3	20	25-Jun-26	19-Jul-26	18-Nov-25 A	14-Jan-27	211,133.36
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 3	4	19-Jul-26	23-Jul-26	01-Aug-26 A	16-Jan-27	126,680.02
Geotextile & Bedding		28	01-Jun-26	04-Jul-26	12-Jan-26 A	16-Jan-27	644,822.98
Installation of geotextile lining and coarse sand bedding		28	01-Jun-26	04-Jul-26	12-Jan-26 A	16-Jan-27	644,822.98
MOD-RCP-C	Trim subgrade to required level for Rainwater Collection Ponds Zone 3	7	01-Jun-26	09-Jun-26	12-Jan-26 A	09-Jan-27	143,293.99
MOD-RCP-C	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	09-Jun-26	04-Jul-26	29-Jan-26 A	16-Jan-27	501,528.98
Concrete Structures		7	01-Oct-26	10-Oct-26	16-May-26 A	26-Nov-26 A	22,907.54
Construction of pond slab, walls, vertical structures		7	01-Oct-26	10-Oct-26	16-May-26 A	26-Nov-26 A	22,907.54
MOD-RCP-C	Apply waterproofing, bitumen, screed, perimeter lining for Rainwater Collection Ponds Z	7	01-Oct-26	10-Oct-26	16-May-26 A	26-Nov-26 A	22,907.54
Energy Dissipation & Siphon Structures		3	26-Sep-26	29-Sep-26	18-Nov-25 A	01-Dec-26 A	8,329.52
Siphon pipes, energy dissipators, and associated civil works		3	26-Sep-26	29-Sep-26	18-Nov-25 A	01-Dec-26 A	8,329.52
MOD-RCP-E	Excavate for low-level areas for Rainwater Collection Ponds Zone 3	3	26-Sep-26	29-Sep-26	18-Nov-25 A	01-Dec-26 A	8,329.52
Road Crossing Zone 3		24	12-Feb-26	07-May-26	01-Apr-26 A	16-Jan-27	390,924.54
uPVC Road Crossing Pipes		24	12-Feb-26	07-May-26	01-Apr-26 A	16-Jan-27	390,924.54
Installation of uPVC pipes of various diameters crossing roadways		24	12-Feb-26	07-May-26	01-Apr-26 A	16-Jan-27	390,924.54
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 3	10	12-Feb-26	26-Mar-26	09-Jun-26 A	05-Jan-27	90,213.36
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 3	10	26-Mar-26	13-Apr-26	01-Apr-26 A	10-Jan-27	60,142.24
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 3	10	13-Apr-26	07-May-26	01-May-26 A	16-Jan-27	240,568.95
Zone 2		338	19-Oct-25	27-Sep-26	17-Nov-25 A	01-Apr-27	3,465,464.58
Sewerage Network Zone 2		306	19-Oct-25	17-Feb-26	11-Jan-26 A	17-Nov-26	1,358,251.57
Pipework: Supply, Installation, and Testing		157	19-Oct-25	19-Jan-26	11-Jan-26 A	17-Nov-26	187,530.42
HDPE Pressure Pipes Installation (250mm–630mm)		157	19-Oct-25	19-Jan-26	11-Jan-26 A	17-Nov-26	187,530.42
MOD-SWN-	HDPE Pressure Pipes Installation (250mm–630mm) HDPE for Sewerage Network Zone 2	21	30-Nov-25	20-Dec-25	09-Feb-26 A	02-Nov-26	93,765.21
MOD-SWN-	Excavation and Trenching HDPE for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	11-Jan-26 A	14-Oct-26	41,673.43
MOD-SWN-	Lean Concrete / Bedding HDPE for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	15-Jan-26 A	22-Oct-26	10,418.36
MOD-SWN-	Test (Pressure - Slope) HDPE for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	16-Mar-26 A	09-Nov-26	20,836.71
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 2	15	05-Jan-26	19-Jan-26	21-Mar-26 A	17-Nov-26	20,836.71
Valve & Flow Meter Chambers		134	19-Oct-25	06-Jan-26	01-Jul-26 A	10-Nov-26	66,779.77
Valve Chambers Construction		119	19-Oct-25	20-Dec-25	01-Jul-26 A	09-Nov-26	11,030.50
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	01-Jul-26 A	14-Oct-26	2,068.22
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	14-Jul-26 A	22-Oct-26	1,378.81
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 2	15	06-Dec-25	20-Dec-25	25-Oct-26	09-Nov-26	1,378.81
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 2	6	30-Nov-25	05-Dec-25	28-Jul-26 A	25-Oct-26	6,204.65
Water Drain Chambers Construction		67	19-Oct-25	24-Dec-25	28-Jul-26 A	04-Nov-26	31,351.99
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	28-Jul-26 A	14-Oct-26	6,718.28
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	01-Aug-26 A	22-Oct-26	4,478.86
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone 2	19	06-Dec-25	24-Dec-25	18-Aug-26 A	04-Nov-26	20,154.85
Discharge Chambers Construction		45	19-Oct-25	06-Jan-26	14-Jul-26 A	10-Nov-26	21,901.06
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	14-Jul-26 A	18-Oct-26	4,693.08
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	17-Aug-26 A	28-Oct-26	3,128.72
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 2	13	25-Dec-25	06-Jan-26	18-Aug-26 A	10-Nov-26	14,079.25

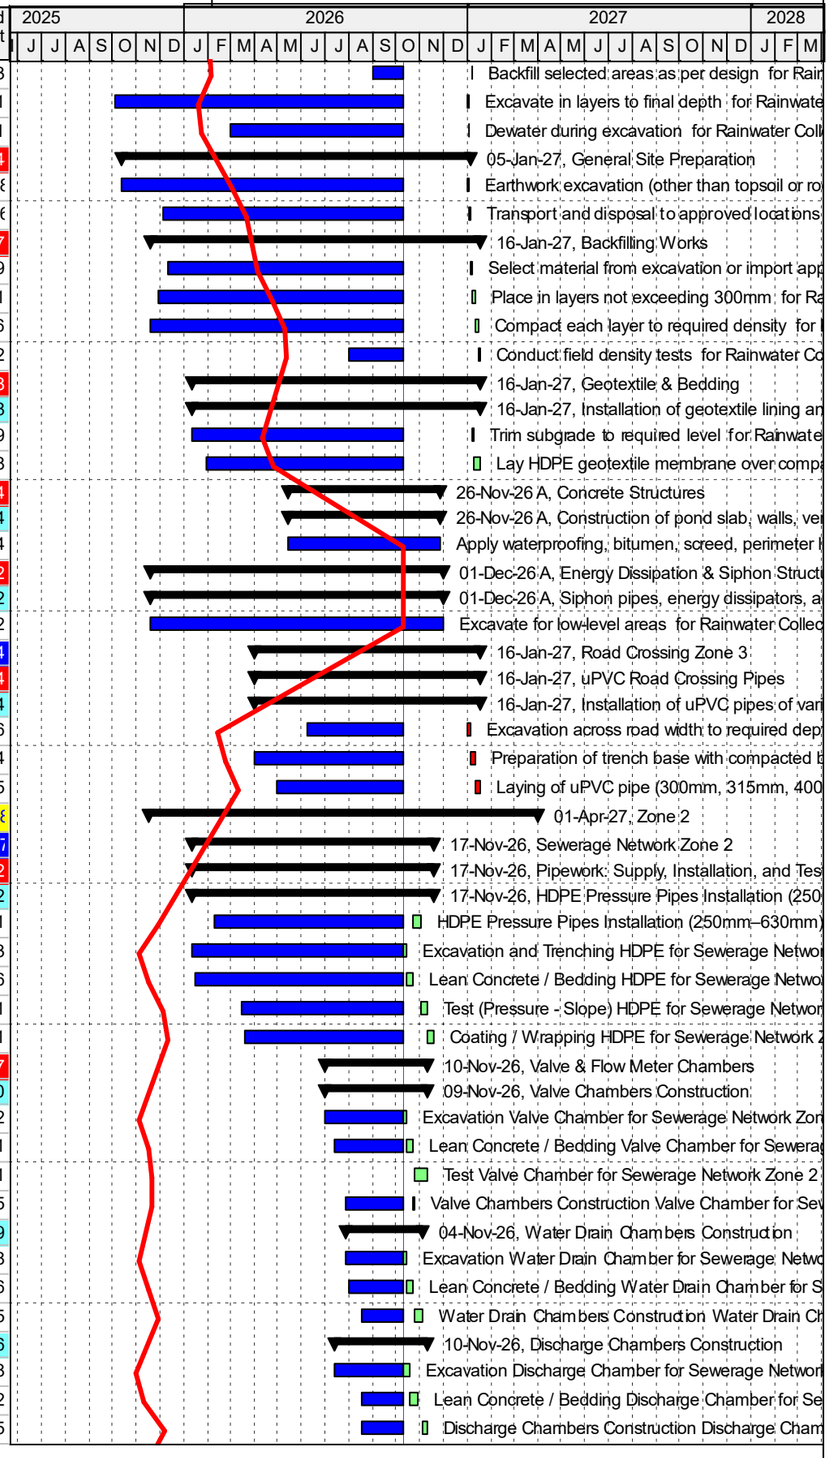


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Flow Meter Chambers Construction		42	19-Oct-25	29-Nov-25	19-Aug-26 A	30-Oct-26	2,496.22
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	19-Aug-26 A	18-Oct-26	1,497.73
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	26-Aug-26 A	30-Oct-26	998.49
Manholes		237	09-Nov-25	17-Feb-26	07-Feb-26 A	06-Nov-26	1,103,941.36
1200mm GRP Manholes with Backdrop		231	09-Nov-25	04-Jan-26	07-Feb-26 A	31-Oct-26	549,417.87
MOD-SWN-	1200mm GRP Manholes with Backdrop 1.2m GRP for Sewerage Network Zone 2	21	30-Nov-25	20-Dec-25	14-Feb-26 A	16-Oct-26	380,366.22
MOD-SWN-	Lean Concrete / Bedding 1.2m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	07-Feb-26 A	13-Oct-26	84,525.83
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	16-Oct-26	31-Oct-26	84,525.83
1500mm GRP Manholes (Standard & Backdrop)		234	09-Nov-25	25-Jan-26	14-Feb-26 A	03-Nov-26	520,344.32
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	21-Dec-25	10-Jan-26	25-Feb-26 A	19-Oct-26	360,238.37
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	14-Feb-26 A	14-Oct-26	80,052.97
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 2	15	11-Jan-26	25-Jan-26	19-Oct-26	03-Nov-26	80,052.97
1800mm GRP Manholes (Standard & Backdrop)		236	09-Nov-25	11-Feb-26	16-Feb-26 A	05-Nov-26	25,958.62
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	11-Jan-26	27-Jan-26	28-Feb-26 A	21-Oct-26	17,971.35
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	16-Feb-26 A	13-Oct-26	3,993.63
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 2	15	28-Jan-26	11-Feb-26	21-Oct-26	05-Nov-26	3,993.63
2000mm GRP Manholes (Standard & Backdrop)		237	09-Nov-25	17-Feb-26	16-Mar-26 A	06-Nov-26	8,220.58
MOD-SWN-	2000mm GRP Manholes (Standard & Backdrop) 2m GRP for Sewerage Network Zone 2	6	28-Jan-26	02-Feb-26	22-Mar-26 A	22-Oct-26	5,691.17
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	16-Mar-26 A	13-Oct-26	1,264.70
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 2	15	03-Feb-26	17-Feb-26	22-Oct-26	06-Nov-26	1,264.70
Rainwater Drainage Network Zone 2		259	27-Nov-25	18-Jan-26	01-Dec-25 A	31-Oct-26	1,091,562.45
Pipe Laying Works		21	14-Dec-25	05-Jan-26	04-Jan-26 A	14-Oct-26	16,851.43
uPVC Connection Pipes (150mm dia)		21	14-Dec-25	05-Jan-26	04-Jan-26 A	14-Oct-26	16,851.43
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 2	2	04-Jan-26	05-Jan-26	04-Jan-26 A	14-Oct-26	8,425.71
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 2	21	14-Dec-25	03-Jan-26	12-Jan-26 A	14-Oct-26	8,425.71
Precast Concrete Box Culverts		135	27-Nov-25	08-Jan-26	18-Apr-26 A	31-Oct-26	1,329,047.71
Box Culverts (500x500mm to 3500x800mm)		132	27-Nov-25	30-Dec-25	27-Apr-26 A	27-Oct-26	1,293,242.83
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 2	7	27-Nov-25	06-Dec-25	27-Apr-26 A	13-Oct-26	424,014.04
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	6	06-Dec-25	13-Dec-25	30-Apr-26 A	17-Oct-26	159,005.27
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 2	5	13-Dec-25	25-Dec-25	17-Oct-26	22-Oct-26	636,021.07
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 2	4	25-Dec-25	30-Dec-25	22-Oct-26	27-Oct-26	74,202.46
Tube Culverts at Road Intersections		11	30-Nov-25	13-Dec-25	18-Apr-26 A	17-Oct-26	25,056.68
MOD-RWN-	Trench excavation under road Tube culvert for Rainwater Drainage Network Zone 2	11	30-Nov-25	13-Dec-25	18-Apr-26 A	17-Oct-26	25,056.68
Box Culverts at Road Intersections		17	20-Dec-25	08-Jan-26	12-Oct-26	31-Oct-26	10,748.19
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 2	4	20-Dec-25	24-Dec-25	12-Oct-26	15-Oct-26	9,377.62
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 2	1	24-Dec-25	25-Dec-25	17-Oct-26	17-Oct-26	1,082.03
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 2	12	25-Dec-25	08-Jan-26	18-Oct-26	31-Oct-26	288.54
Manholes		179	13-Dec-25	15-Jan-26	05-Jan-26 A	28-Oct-26	1,360,040.89
Circular GRP Manholes (1200–1800mm dia)		177	17-Dec-25	15-Jan-26	05-Jan-26 A	26-Oct-26	434,546.64
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 2	7	17-Dec-25	25-Dec-25	05-Jan-26 A	18-Oct-26	139,512.34
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 2	5	25-Dec-25	31-Dec-25	06-Jan-26 A	19-Oct-26	137,225.25
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	8	31-Dec-25	10-Jan-26	07-Jan-26 A	21-Oct-26	114,354.38
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 2	3	10-Jan-26	13-Jan-26	06-Jul-26 A	24-Oct-26	34,306.31
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 2	2	13-Jan-26	15-Jan-26	24-Oct-26	26-Oct-26	9,148.35
Concrete Manholes for 1500x1500 Box Pipes		115	18-Dec-25	07-Jan-26	16-Feb-26 A	28-Oct-26	673,558.16
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	4	18-Dec-25	23-Dec-25	16-Feb-26 A	18-Oct-26	216,247.62
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	6	23-Dec-25	30-Dec-25	01-Mar-26 A	21-Oct-26	212,702.58
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	3	30-Dec-25	03-Jan-26	05-Jul-26 A	24-Oct-26	177,252.15
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	2	03-Jan-26	05-Jan-26	24-Oct-26	26-Oct-26	53,175.64
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	2	05-Jan-26	07-Jan-26	26-Oct-26	28-Oct-26	14,180.17

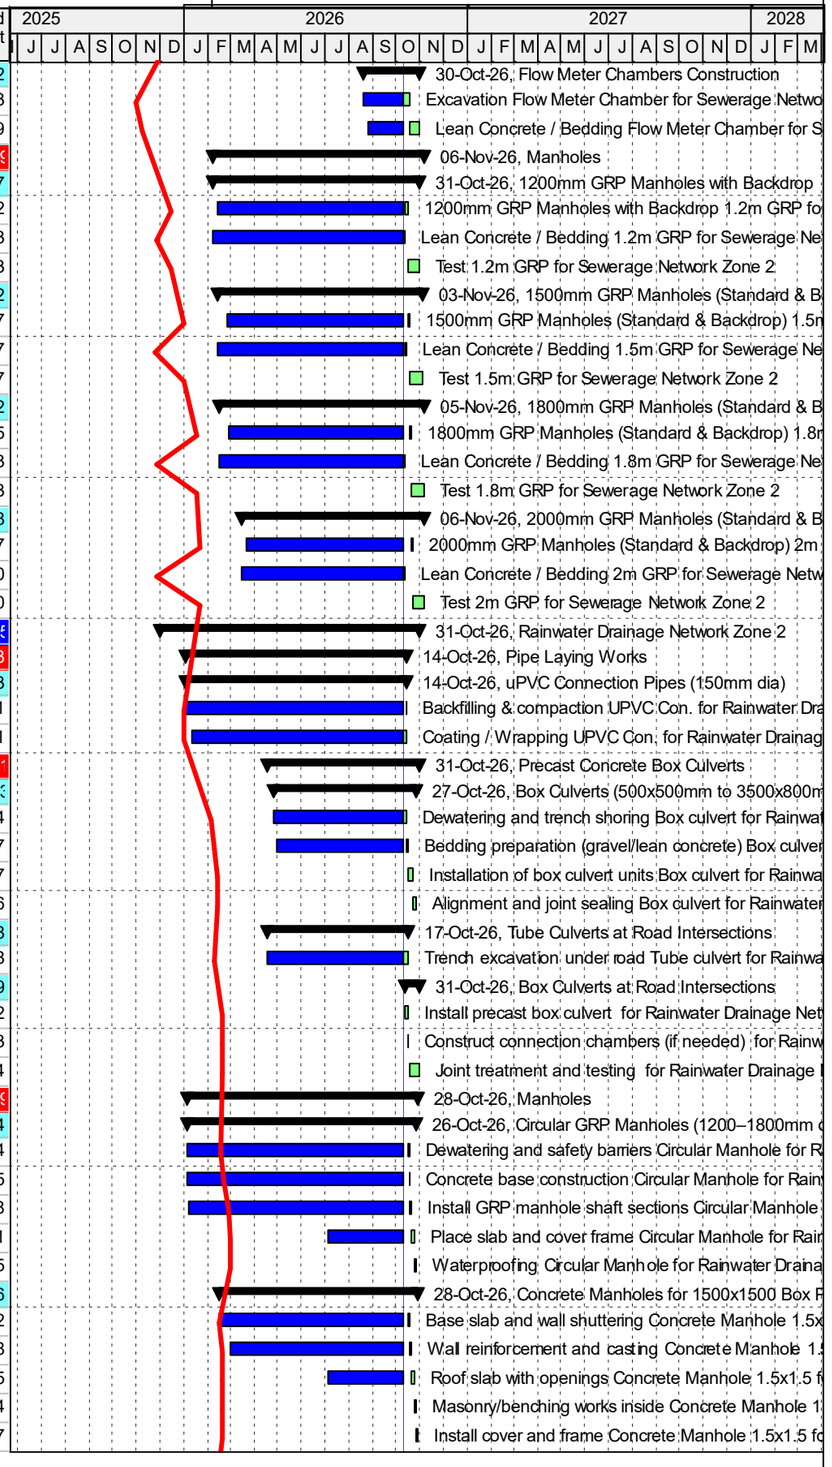


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Concrete Manholes for 1000x1000 Box Pipes		118	13-Dec-25	25-Dec-25	02-Mar-26 A	27-Oct-26	251,936.10
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	2	17-Dec-25	20-Dec-25	19-Oct-26	21-Oct-26	120,063.30
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	5	20-Dec-25	25-Dec-25	21-Oct-26	27-Oct-26	118,095.04
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	4	13-Dec-25	17-Dec-25	02-Mar-26 A	19-Oct-26	13,777.76
Gully Outfalls to Swales		199	24-Dec-25	18-Jan-26	01-Feb-26 A	28-Oct-26	314,878.93
Gully Outfalls to Swales		193	28-Dec-25	18-Jan-26	07-Feb-26 A	21-Oct-26	254,733.51
MOD-RWN-	Excavate outfall channel Gully Outfall to Swales for Rainwater Drainage Network Zone 2	5	28-Dec-25	03-Jan-26	07-Feb-26 A	17-Oct-26	56,607.45
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zo	7	03-Jan-26	11-Jan-26	15-Feb-26 A	18-Oct-26	127,366.76
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	4	11-Jan-26	15-Jan-26	20-Feb-26 A	18-Oct-26	42,455.59
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	17-Jan-26	18-Jan-26	19-Oct-26	21-Oct-26	28,303.72
Riprap Works & Protection		131	24-Dec-25	11-Jan-26	01-Feb-26 A	28-Oct-26	60,145.41
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 2	3	24-Dec-25	28-Dec-25	01-Feb-26 A	18-Oct-26	7,075.93
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 2	7	28-Dec-25	05-Jan-26	17-Feb-26 A	22-Oct-26	38,917.62
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 2	5	05-Jan-26	11-Jan-26	22-Oct-26	28-Oct-26	14,151.86
Backfilling & Bedding		31	09-Dec-25	06-Jan-26	01-Dec-25 A	19-Oct-26	1,070,743.50
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		31	09-Dec-25	06-Jan-26	01-Dec-25 A	19-Oct-26	1,070,743.50
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 2	8	28-Dec-25	06-Jan-26	01-Dec-25 A	19-Oct-26	152,963.36
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 2	9	09-Dec-25	20-Dec-25	03-Jan-26 A	14-Oct-26	688,335.11
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 2	7	20-Dec-25	28-Dec-25	03-Jan-26 A	17-Oct-26	229,445.04
Potable Water Network Zone 2		57	02-Dec-25	07-Jan-26	11-Aug-26 A	12-Nov-26	324,449.74
Valve Installation & Chambers		10	21-Dec-25	31-Dec-25	10-Oct-26	21-Oct-26	94,891.03
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 2	6	21-Dec-25	27-Dec-25	10-Oct-26	17-Oct-26	63,260.68
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 2	4	28-Dec-25	31-Dec-25	17-Oct-26	21-Oct-26	31,630.34
Flow Meter Installation		57	02-Dec-25	31-Dec-25	01-Sep-26 A	12-Nov-26	61,536.16
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 2	7	02-Dec-25	09-Dec-25	01-Sep-26 A	13-Oct-26	18,460.85
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 2	12	18-Dec-25	31-Dec-25	06-Sep-26 A	12-Nov-26	43,075.31
Washout & Air Valve Chambers		24	27-Dec-25	07-Jan-26	11-Aug-26 A	17-Oct-26	168,022.55
MOD-PWN-WA	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 2	5	27-Dec-25	31-Dec-25	11-Aug-26 A	13-Oct-26	90,150.20
MOD-PWN-WA	Covers, Ladders & Tags for Potable Water Network Zone 2	4	01-Jan-26	05-Jan-26	17-Sep-26 A	14-Oct-26	38,936.18
MOD-PWN-WA	Backfilling & Final Finishing for Potable Water Network Zone 2	2	06-Jan-26	07-Jan-26	14-Oct-26	17-Oct-26	38,936.18
Irrigation Network Zone 2		72	03-Jan-26	14-Jan-26	01-Jul-26 A	09-Nov-26	58,288.51
Flow Meter Chambers		72	03-Jan-26	14-Jan-26	01-Jul-26 A	09-Nov-26	58,288.51
MOD-IRN-FC-2	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	5	03-Jan-26	07-Jan-26	01-Jul-26 A	05-Nov-26	31,386.12
MOD-IRN-FC-3	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 2	2	08-Jan-26	10-Jan-26	02-Jul-26 A	07-Nov-26	13,451.19
MOD-IRN-FC-4	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 2	4	11-Jan-26	14-Jan-26	22-Jul-26 A	09-Nov-26	13,451.19
Rainwater Collection Ponds Zone 2		154	22-Jan-26	27-Sep-26	17-Nov-25 A	01-Apr-27	632,912.32
Excavation for Rainwater Drainage Pond		23	22-Jan-26	05-Mar-26	08-Jun-26 A	04-Jan-27	104,861.93
Deep excavation, backfill, disposal for pond formation		23	22-Jan-26	05-Mar-26	08-Jun-26 A	04-Jan-27	104,861.93
MOD-RCP-E	Excavate in layers to final depth for Rainwater Collection Ponds Zone 2	12	22-Jan-26	04-Feb-26	08-Jun-26 A	02-Jan-27	34,390.20
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 2	5	05-Feb-26	10-Feb-26	07-Jul-26 A	03-Jan-27	33,826.43
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 2	6	11-Feb-26	19-Feb-26	21-Jul-26 A	03-Jan-27	8,456.61
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone 2	7	19-Feb-26	05-Mar-26	01-Aug-26 A	04-Jan-27	28,188.69
Backfilling Works		142	08-Jun-26	17-Aug-26	17-Nov-25 A	16-Jan-27	229,230.51
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 2	21	25-Jun-26	20-Jul-26	17-Nov-25 A	10-Jan-27	84,453.34
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 2	20	20-Jul-26	12-Aug-26	25-Nov-25 A	14-Jan-27	60,323.82
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 2	4	12-Aug-26	17-Aug-26	01-Aug-26 A	16-Jan-27	36,194.29
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	08-Jun-26	25-Jun-26	18-Nov-25 A	05-Jan-27	48,259.05
Geotextile & Bedding		42	04-Jul-26	22-Aug-26	17-Jan-26 A	17-Feb-27	266,117.42
Installation of geotextile lining and coarse sand bedding		42	04-Jul-26	22-Aug-26	17-Jan-26 A	17-Feb-27	266,117.42
MOD-RCP-C	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	04-Jul-26	28-Jul-26	17-Jan-26 A	19-Jan-27	143,293.99

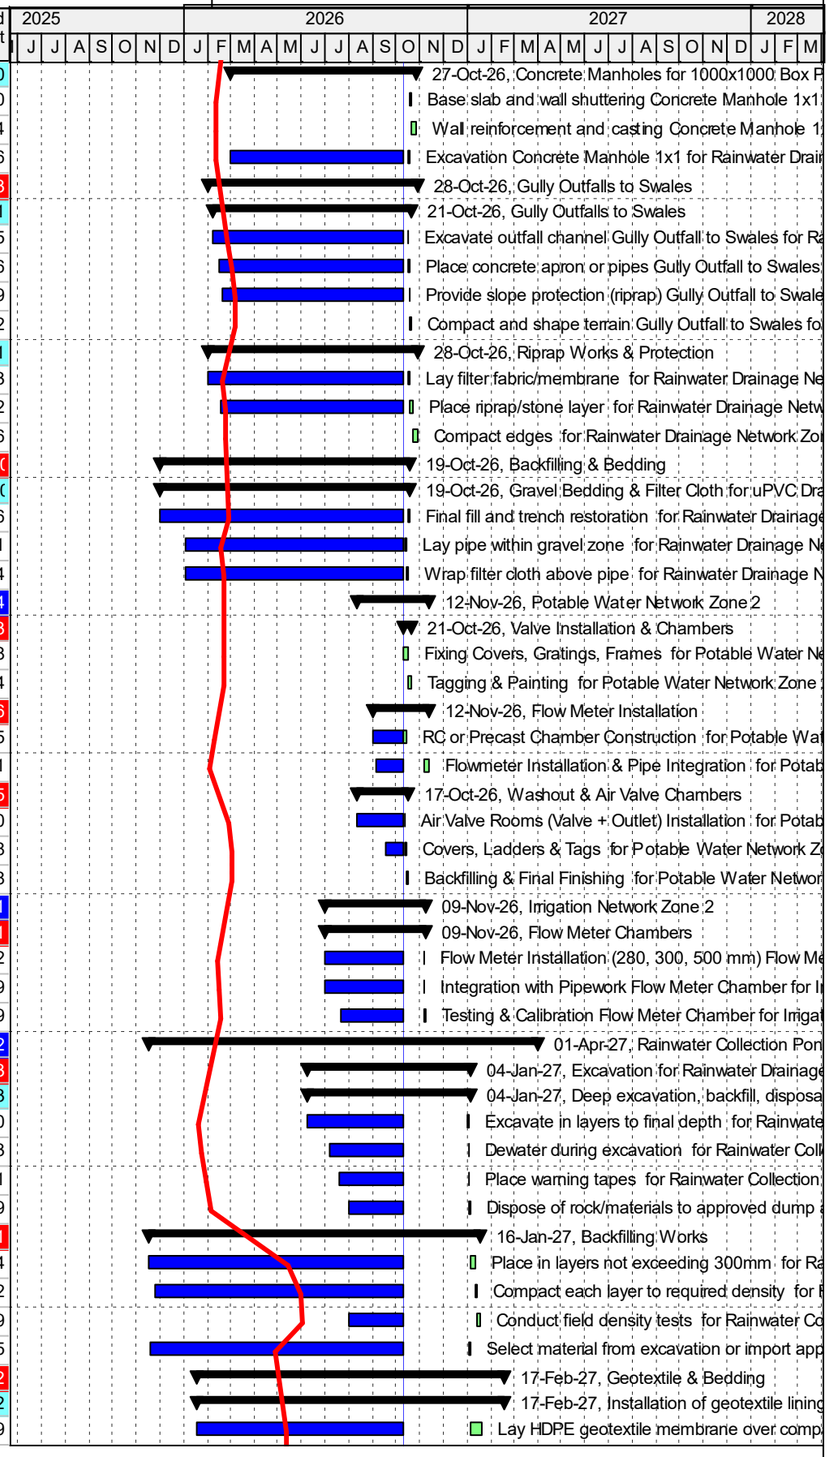

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RCP-(	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 2	21	28-Jul-26	22-Aug-26	22-Jul-26 A	17-Feb-27	122,823.42
Concrete Structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	32,702.46
Construction of pond slab, walls, vertical structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	32,702.46
MOD-RCP-(	Install formwork and reinforcement for Rainwater Collection Ponds Zone 2	8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	32,702.46
Zone 1		340	19-Oct-25	11-Oct-26	03-Sep-25 A	04-Feb-27	5,482,943.1
Sewerage Network Zone 1		287	19-Oct-25	03-Feb-26	11-Dec-25 A	24-Nov-26	1,382,533.62
Pipework: Supply, Installation, and Testing		58	05-Jan-26	03-Feb-26	11-Dec-25 A	17-Oct-26	41,673.43
HDPE Pressure Pipes Installation (250mm–630mm)		58	05-Jan-26	03-Feb-26	11-Dec-25 A	17-Oct-26	41,673.43
MOD-SWN-	Backfilling & Warning Tape HDPE for Sewerage Network Zone 1	15	20-Jan-26	03-Feb-26	05-Feb-26 A	17-Oct-26	20,836.71
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 1	15	05-Jan-26	19-Jan-26	11-Dec-25 A	13-Oct-26	20,836.71
Fittings and Valves		14	21-Dec-25	05-Jan-26	12-Oct-26	28-Oct-26	32,098.68
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 1	6	21-Dec-25	27-Dec-25	12-Oct-26	19-Oct-26	13,652.43
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 1	4	28-Dec-25	31-Dec-25	19-Oct-26	24-Oct-26	9,660.60
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 1	4	01-Jan-26	05-Jan-26	24-Oct-26	28-Oct-26	8,785.65
Valve & Flow Meter Chambers		134	19-Oct-25	11-Jan-26	01-Jun-26 A	24-Nov-26	74,373.00
Valve Chambers Construction		48	19-Oct-25	05-Dec-25	01-Jun-26 A	06-Nov-26	9,651.69
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	01-Jun-26 A	20-Oct-26	2,068.22
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	09-Jun-26 A	02-Nov-26	1,378.81
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 1	6	30-Nov-25	05-Dec-25	23-Jun-26 A	06-Nov-26	6,204.65
Water Drain Chambers Construction		130	19-Oct-25	08-Jan-26	11-Jul-26 A	19-Nov-26	35,830.84
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	11-Jul-26 A	16-Oct-26	6,718.28
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	22-Jul-26 A	24-Oct-26	4,478.86
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	01-Aug-26 A	19-Nov-26	4,478.86
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone	19	06-Dec-25	24-Dec-25	29-Jul-26 A	13-Nov-26	20,154.85
Discharge Chambers Construction		71	19-Oct-25	06-Jan-26	13-Jul-26 A	22-Nov-26	21,901.06
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	13-Jul-26 A	20-Oct-26	4,693.08
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	14-Jul-26 A	02-Nov-26	3,128.72
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 1	13	25-Dec-25	06-Jan-26	29-Jul-26 A	22-Nov-26	14,079.25
Flow Meter Chambers Construction		39	19-Oct-25	11-Jan-26	11-Jul-26 A	24-Nov-26	6,989.41
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	11-Jul-26 A	17-Oct-26	1,497.73
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	28-Jul-26 A	26-Oct-26	998.49
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 1	5	07-Jan-26	11-Jan-26	01-Aug-26 A	24-Nov-26	4,493.20
Manholes		20	05-Dec-25	08-Jan-26	11-Oct-26	31-Oct-26	509,511.41
1200mm GRP Manholes with Backdrop		20	05-Dec-25	24-Dec-25	11-Oct-26	31-Oct-26	253,577.48
MOD-SWN-	Backfilling 1.2m GRP for Sewerage Network Zone 1	15	10-Dec-25	24-Dec-25	16-Oct-26	31-Oct-26	169,051.65
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 1	5	05-Dec-25	09-Dec-25	11-Oct-26	16-Oct-26	84,525.83
1500mm GRP Manholes (Standard & Backdrop)		20	10-Dec-25	29-Dec-25	11-Oct-26	31-Oct-26	240,158.92
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 1	15	15-Dec-25	29-Dec-25	16-Oct-26	31-Oct-26	160,105.94
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 1	5	10-Dec-25	14-Dec-25	11-Oct-26	16-Oct-26	80,052.97
1800mm GRP Manholes (Standard & Backdrop)		20	11-Dec-25	30-Dec-25	11-Oct-26	31-Oct-26	11,980.90
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 1	15	16-Dec-25	30-Dec-25	16-Oct-26	31-Oct-26	7,987.27
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 1	5	11-Dec-25	15-Dec-25	11-Oct-26	16-Oct-26	3,993.63
2000mm GRP Manholes (Standard & Backdrop)		20	20-Dec-25	08-Jan-26	11-Oct-26	31-Oct-26	3,794.11
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	16-Oct-26	31-Oct-26	2,529.41
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 1	5	20-Dec-25	24-Dec-25	11-Oct-26	16-Oct-26	1,264.70
Pumping Stations		151	19-Nov-25	27-Dec-25	01-Jan-26 A	10-Nov-26	724,877.10
Perimeter Walls & Gates		10	01-Dec-25	11-Dec-25	30-Jul-26 A	14-Oct-26	27,650.44
MOD-SWN-	Main entrance gates – Each PS for Sewerage Network Zone 1	10	01-Dec-25	11-Dec-25	30-Jul-26 A	14-Oct-26	27,650.44
Engine/Motor Control Center Buildings		7	01-Dec-25	08-Dec-25	11-Oct-26	18-Oct-26	42,052.73
MOD-SWN-	MCC Building – PS2 for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	11-Oct-26	18-Oct-26	42,052.73
Pump Well and Valve Chambers		27	19-Nov-25	20-Dec-25	11-Oct-26	10-Nov-26	197,138.61

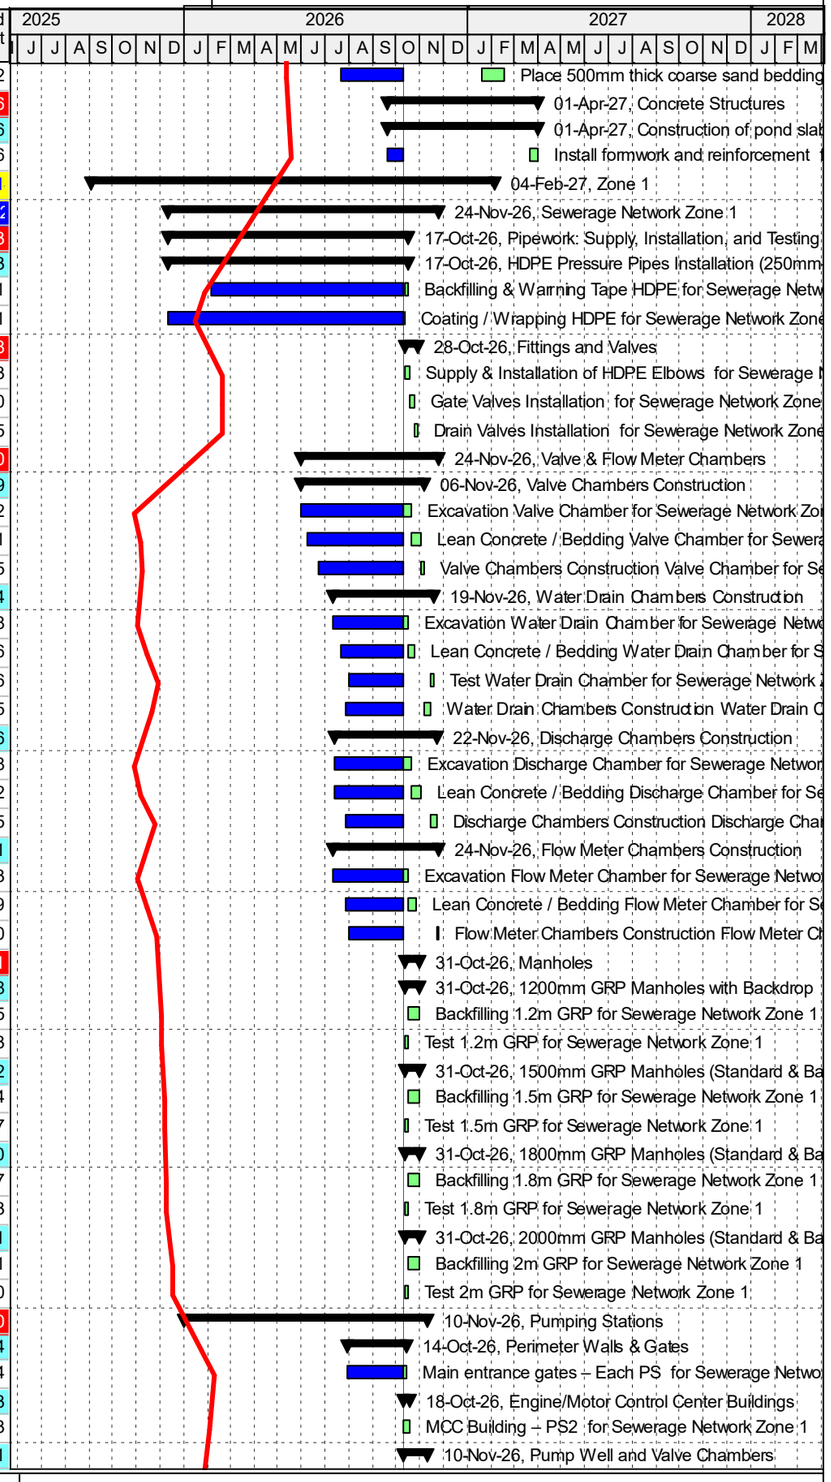


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-SWN-	Pump well & valve chamber structure – PS1 (2 wells, 12m deep) for Sewerage Network	13	19-Nov-25	03-Dec-25	11-Oct-26	25-Oct-26	74,197.09
MOD-SWN-	Concrete wall (5x5x1m) inside PS1 well for Sewerage Network Zone 1	7	04-Dec-25	11-Dec-25	26-Oct-26	02-Nov-26	41,284.68
MOD-SWN-	Pump well & valve chamber structure – PS2 (2 wells, 3m each, 9m depth) for Sewerage	14	04-Dec-25	20-Dec-25	26-Oct-26	10-Nov-26	81,656.84
Lighting Works		13	13-Dec-25	27-Dec-25	01-Jan-26 A	05-Nov-26	384,043.12
MOD-SWN-	250W Flood Light installation – Each PS for Sewerage Network Zone 1	13	13-Dec-25	27-Dec-25	01-Jan-26 A	05-Nov-26	384,043.12
Duct Works		1	04-Dec-25	04-Dec-25	26-Oct-26	26-Oct-26	2,760.41
MOD-SWN-	uPVC duct Track 1 – All PSs for Sewerage Network Zone 1	1	04-Dec-25	04-Dec-25	26-Oct-26	26-Oct-26	2,760.41
Landscaping / Interlocking Tiles		17	06-Dec-25	24-Dec-25	12-Oct-26	31-Oct-26	50,952.81
MOD-SWN-	Building perimeter interlock tiles for Sewerage Network Zone 1	17	06-Dec-25	24-Dec-25	12-Oct-26	31-Oct-26	50,952.81
Pumping Station Internal Drainage Network		7	01-Dec-25	08-Dec-25	10-Oct-26	17-Oct-26	20,278.98
MOD-SWN-	Internal surface drainage channels for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	10-Oct-26	17-Oct-26	20,278.98
Rainwater Drainage Network Zone 1		301	24-Nov-25	18-Jan-26	01-Jan-26 A	01-Nov-26	3,416,198.45
Pipe Laying Works		49	06-Dec-25	05-Jan-26	08-Jan-26 A	18-Oct-26	100,666.07
Supply & Installation of uPVC Pipes (250–300mm dia)		8	06-Dec-25	13-Dec-25	10-Jan-26 A	13-Oct-26	75,388.93
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 1	8	06-Dec-25	13-Dec-25	10-Jan-26 A	13-Oct-26	75,388.93
uPVC Connection Pipes (150mm dia)		23	11-Dec-25	05-Jan-26	08-Jan-26 A	18-Oct-26	25,277.14
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 1	3	11-Dec-25	13-Dec-25	08-Jan-26 A	13-Oct-26	8,425.71
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 1	2	04-Jan-26	05-Jan-26	11-Jan-26 A	18-Oct-26	8,425.71
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 1	21	14-Dec-25	03-Jan-26	10-Jan-26 A	17-Oct-26	8,425.71
Precast Concrete Box Culverts		127	24-Nov-25	04-Jan-26	28-Apr-26 A	31-Oct-26	1,050,622.86
Box Culverts (500x500mm to 3500x800mm)		127	25-Nov-25	03-Jan-26	28-Apr-26 A	31-Oct-26	890,429.49
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 1	8	25-Nov-25	11-Dec-25	28-Apr-26 A	17-Oct-26	636,021.07
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 1	4	13-Dec-25	16-Dec-25	05-May-26 A	19-Oct-26	74,202.46
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Zo	5	17-Dec-25	25-Dec-25	19-Oct-26	25-Oct-26	106,003.51
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 1	5	27-Dec-25	03-Jan-26	25-Oct-26	31-Oct-26	74,202.46
Tube Culverts at Road Intersections		120	24-Nov-25	04-Jan-26	12-May-26 A	28-Oct-26	149,445.20
MOD-RWN-	Pipe bedding and twin pipe alignment Tube culvert for Rainwater Drainage Network Zone	6	24-Nov-25	01-Dec-25	12-May-26 A	13-Oct-26	13,423.22
MOD-RWN-	Pipe laying and jointing Tube culvert for Rainwater Drainage Network Zone 1	10	01-Dec-25	25-Dec-25	24-May-26 A	19-Oct-26	118,124.35
MOD-RWN-	Backfilling and road reinstatement Tube culvert for Rainwater Drainage Network Zone 1	8	25-Dec-25	04-Jan-26	19-Oct-26	28-Oct-26	17,897.63
Box Culverts at Road Intersections		15	02-Dec-25	22-Dec-25	11-Oct-26	28-Oct-26	10,748.19
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 1	4	02-Dec-25	07-Dec-25	11-Oct-26	15-Oct-26	9,377.62
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 1	1	07-Dec-25	08-Dec-25	15-Oct-26	17-Oct-26	1,082.03
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 1	10	08-Dec-25	22-Dec-25	17-Oct-26	28-Oct-26	288.54
Manholes		143	25-Nov-25	18-Jan-26	01-Jan-26 A	01-Nov-26	1,494,838.45
Circular GRP Manholes (1200–1800mm dia)		43	01-Dec-25	18-Jan-26	01-Jan-26 A	31-Oct-26	441,407.90
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 1	10	01-Dec-25	11-Dec-25	01-Jan-26 A	15-Oct-26	139,512.34
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 1	5	13-Dec-25	17-Dec-25	03-Jan-26 A	17-Oct-26	137,225.25
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	13	18-Dec-25	01-Jan-26	06-Jan-26 A	22-Oct-26	114,354.38
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 1	6	03-Jan-26	08-Jan-26	11-Jan-26 A	25-Oct-26	34,306.31
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 1	5	10-Jan-26	14-Jan-26	12-Jan-26 A	28-Oct-26	9,148.35
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 1	3	15-Jan-26	18-Jan-26	13-Jan-26 A	31-Oct-26	6,861.26
Concrete Manholes for 1500x1500 Box Pipes		112	01-Dec-25	11-Jan-26	03-Jan-26 A	27-Oct-26	673,558.16
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Network	7	01-Dec-25	08-Dec-25	03-Jan-26 A	15-Oct-26	216,247.62
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netwo	8	09-Dec-25	17-Dec-25	15-Feb-26 A	18-Oct-26	212,702.58
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	5	18-Dec-25	23-Dec-25	17-Feb-26 A	19-Oct-26	177,252.15
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	4	24-Dec-25	28-Dec-25	21-Feb-26 A	21-Oct-26	53,175.64
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	6	05-Jan-26	11-Jan-26	24-Feb-26 A	27-Oct-26	14,180.17
Concrete Manholes for 1000x1000 Box Pipes		105	25-Nov-25	04-Jan-26	01-Jan-26 A	01-Nov-26	379,872.39
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	6	25-Nov-25	01-Dec-25	01-Jan-26 A	15-Oct-26	13,777.76
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	4	02-Dec-25	06-Dec-25	01-Feb-26 A	17-Oct-26	120,063.30

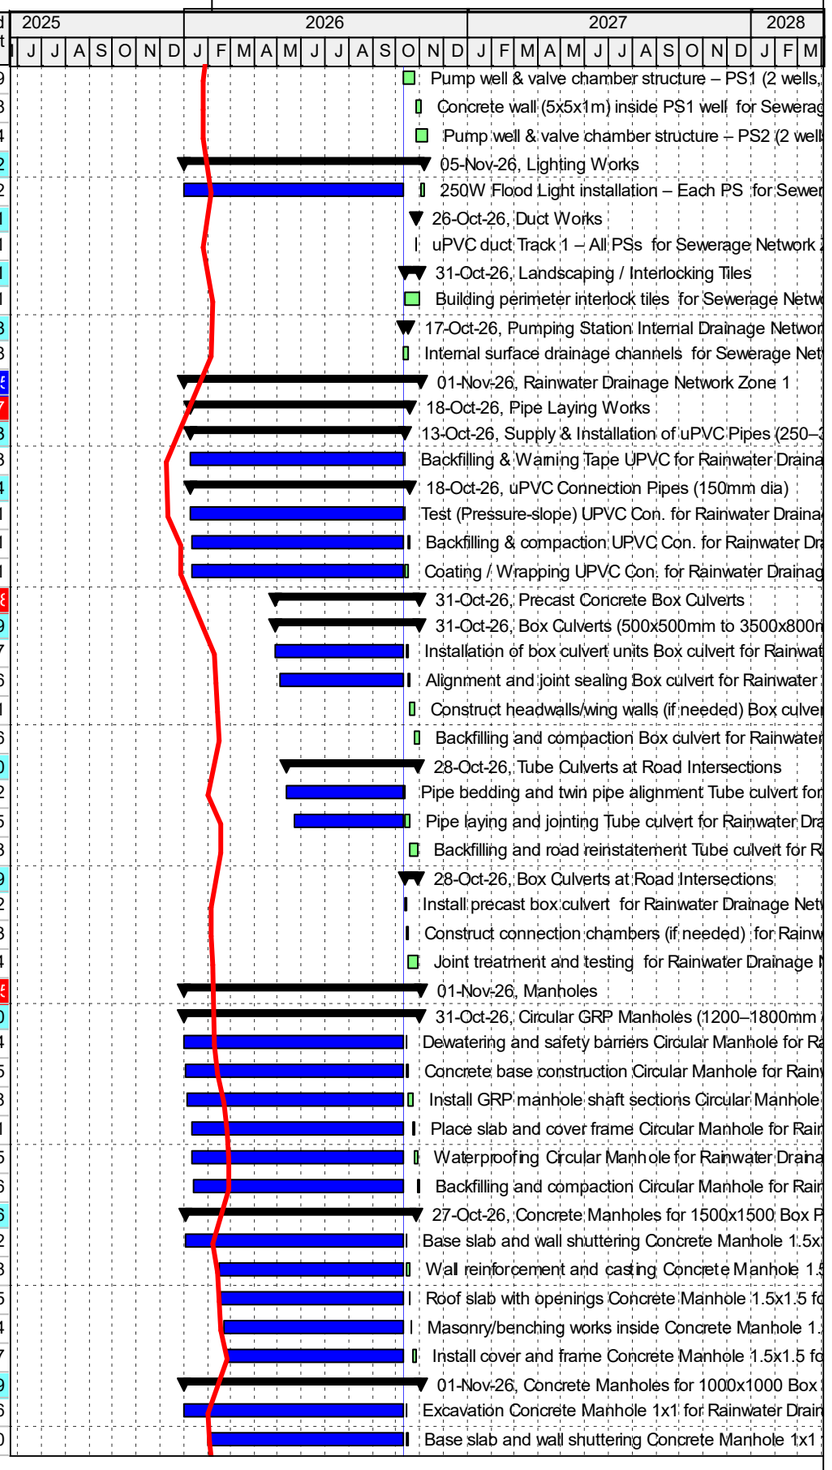


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	7	07-Dec-25	14-Dec-25	01-Apr-26 A	20-Oct-26	118,095.04
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	8	15-Dec-25	23-Dec-25	06-Apr-26 A	25-Oct-26	98,412.54
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	10	24-Dec-25	04-Jan-26	21-Apr-26 A	01-Nov-26	29,523.76
Chambers and Catch Basins		2	13-Jan-26	14-Jan-26	02-May-26 A	17-Oct-26	52,160.51
Rainwater Catch Basins		2	13-Jan-26	14-Jan-26	02-May-26 A	17-Oct-26	52,160.51
MOD-RWN-	Backfill and surface finish Catch Basin for Rainwater Drainage Network Zone 1	2	13-Jan-26	14-Jan-26	02-May-26 A	17-Oct-26	52,160.51
Gully Outfalls to Swales		67	27-Dec-25	15-Jan-26	07-Jan-26 A	20-Oct-26	258,271.48
Gully Outfalls to Swales		66	27-Dec-25	07-Jan-26	07-Jan-26 A	18-Oct-26	198,126.07
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	5	27-Dec-25	31-Dec-25	07-Jan-26 A	17-Oct-26	127,366.76
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	4	01-Jan-26	05-Jan-26	01-Feb-26 A	17-Oct-26	42,455.59
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	06-Jan-26	07-Jan-26	02-Apr-26 A	18-Oct-26	28,303.72
Riprap Works & Protection		27	03-Jan-26	15-Jan-26	01-Feb-26 A	20-Oct-26	60,145.41
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 1	2	03-Jan-26	04-Jan-26	01-Feb-26 A	17-Oct-26	7,075.93
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 1	7	05-Jan-26	12-Jan-26	28-Feb-26 A	19-Oct-26	38,917.62
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 1	3	13-Jan-26	15-Jan-26	01-Apr-26 A	20-Oct-26	14,151.86
Backfilling & Bedding		12	05-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	459,639.06
Backfilling Materials (Type A – 201–700mm Pipes)		6	12-Jan-26	18-Jan-26	13-Oct-26	20-Oct-26	306,675.71
MOD-RWN-	Final fill to subgrade level for Rainwater Drainage Network Zone 1	6	12-Jan-26	18-Jan-26	13-Oct-26	20-Oct-26	306,675.71
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		12	05-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	152,963.36
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 1	12	05-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	152,963.36
Potable Water Network Zone 1		135	25-Nov-25	06-Jan-26	07-May-26 A	14-Nov-26	261,189.05
Valve Installation & Chambers		2	25-Dec-25	27-Dec-25	11-Oct-26	13-Oct-26	31,630.34
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 1	2	25-Dec-25	27-Dec-25	11-Oct-26	13-Oct-26	31,630.34
Flow Meter Installation		135	25-Nov-25	04-Jan-26	07-May-26 A	14-Nov-26	61,536.16
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 1	8	25-Nov-25	03-Dec-25	07-May-26 A	13-Oct-26	18,460.85
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 1	15	18-Dec-25	04-Jan-26	01-Jul-26 A	14-Nov-26	43,075.31
Washout & Air Valve Chambers		29	22-Dec-25	06-Jan-26	16-Aug-26 A	18-Oct-26	168,022.55
MOD-PWN-W/	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 1	7	22-Dec-25	29-Dec-25	16-Aug-26 A	14-Oct-26	90,150.20
MOD-PWN-W/	Covers, Ladders & Tags for Potable Water Network Zone 1	4	30-Dec-25	03-Jan-26	14-Sep-26 A	14-Oct-26	38,936.18
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 1	3	04-Jan-26	06-Jan-26	15-Oct-26	18-Oct-26	38,936.18
Irrigation Network Zone 1		32	06-Jan-26	18-Jan-26	01-Jul-26 A	08-Nov-26	68,896.53
Valve Rooms		3	15-Jan-26	18-Jan-26	11-Jul-26 A	13-Oct-26	24,059.21
MOD-IRN-VR-0	Fixing Frame & Cover Valve Chamber for Irrigation Network Zone 1	2	15-Jan-26	17-Jan-26	11-Jul-26 A	13-Oct-26	18,044.41
MOD-IRN-VR-0	Backfilling and Finishing Valve Chamber for Irrigation Network Zone 1	1	18-Jan-26	18-Jan-26	13-Jul-26 A	13-Oct-26	6,014.80
Flow Meter Chambers		6	06-Jan-26	14-Jan-26	01-Jul-26 A	08-Nov-26	44,837.31
MOD-IRN-FC-0	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	6	06-Jan-26	12-Jan-26	01-Jul-26 A	08-Nov-26	31,386.12
MOD-IRN-FC-0	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 1	2	13-Jan-26	14-Jan-26	02-Jul-26 A	08-Nov-26	13,451.19
Rainwater Collection Ponds Zone 1		180	05-Feb-26	11-Oct-26	03-Sep-25 A	04-Feb-27	0,354,125.4
Excavation for Rainwater Drainage Pond		18	05-Feb-26	05-Mar-26	30-Nov-25 A	04-Jan-27	105,707.59
Deep excavation, backfill, disposal for pond formation		18	05-Feb-26	05-Mar-26	30-Nov-25 A	04-Jan-27	105,707.59
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 1	5	05-Feb-26	10-Feb-26	30-Nov-25 A	02-Jan-27	50,739.65
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 1	6	11-Feb-26	19-Feb-26	10-Dec-25 A	03-Jan-27	12,684.91
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone	7	19-Feb-26	05-Mar-26	17-Dec-25 A	04-Jan-27	42,283.04
General Site Preparation		42	02-Jul-26	20-Aug-26	08-Dec-25 A	16-Jan-27	),443,984.29
MOD-RCP-GS-	Earthwork excavation (other than topsoil or rock) - Zone 1 (2 Ponds) - P3	21	02-Jul-26	27-Jul-26	10-Dec-25 A	09-Jan-27	5,126,449.25
MOD-RCP-GS-	Transport and disposal to approved locations - Zone 1 (2 Ponds) - P3	21	27-Jul-26	20-Aug-26	08-Dec-25 A	16-Jan-27	1,317,535.04
Backfilling Works		97	27-Jul-26	06-Oct-26	03-Sep-25 A	23-Jan-27	343,845.76
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	27-Jul-26	13-Aug-26	03-Sep-25 A	11-Jan-27	72,388.58
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 1	21	13-Aug-26	07-Sep-26	03-Sep-25 A	16-Jan-27	126,680.02
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 1	20	07-Sep-26	01-Oct-26	16-Nov-25 A	20-Jan-27	90,485.73
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 1	4	01-Oct-26	06-Oct-26	01-Aug-26 A	23-Jan-27	54,291.44

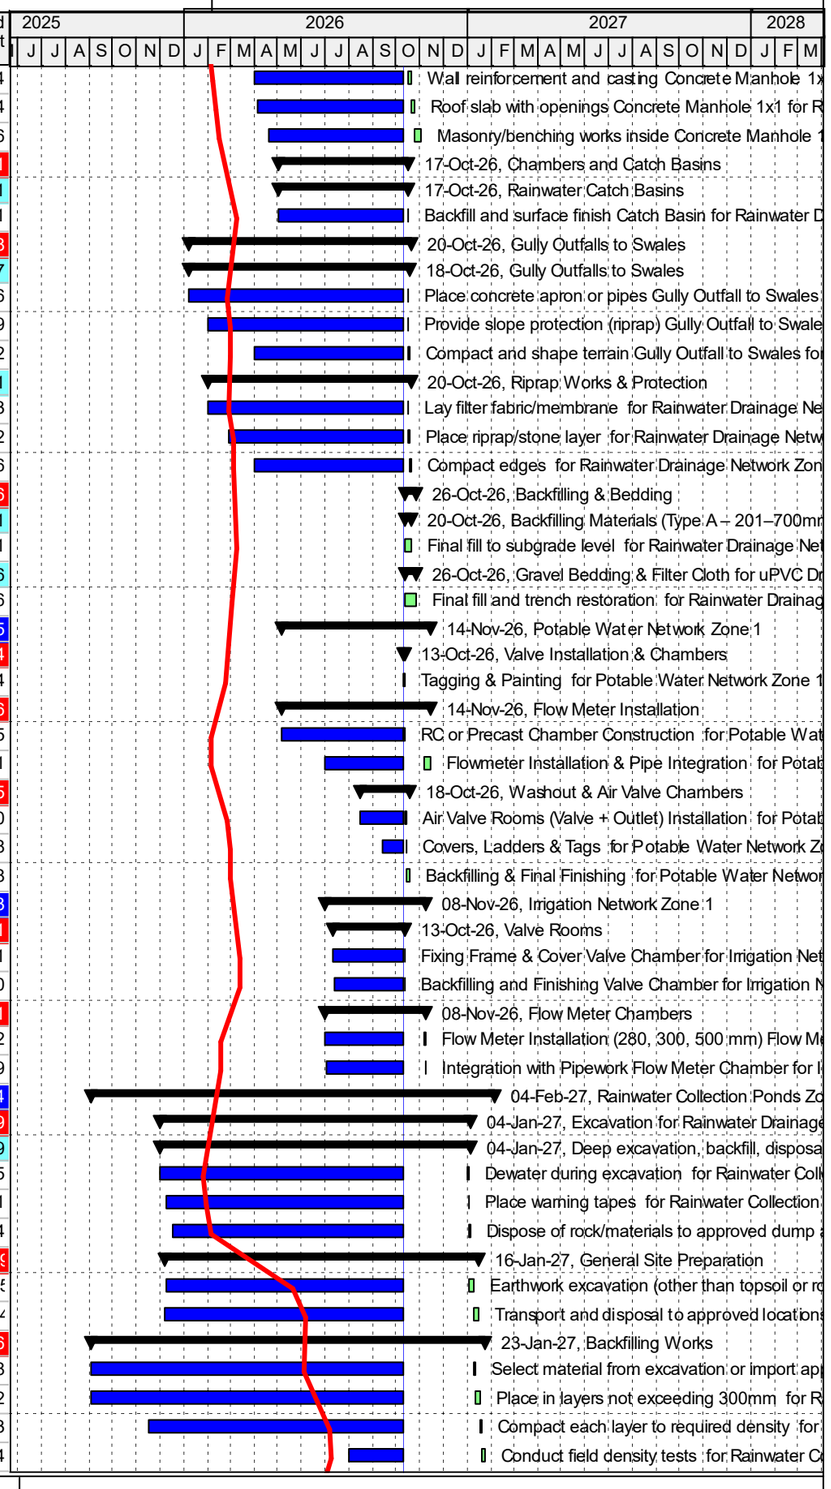


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Geotextile & Bedding		49	13-Aug-26	11-Oct-26	07-Jan-26 A	04-Feb-27	460,587.84
Installation of geotextile lining and coarse sand bedding		49	13-Aug-26	11-Oct-26	07-Jan-26 A	04-Feb-27	460,587.84
MOD-RCP-(	Trim subgrade to required level for Rainwater Collection Ponds Zone 1	7	13-Aug-26	22-Aug-26	07-Jan-26 A	14-Jan-27	61,411.71
MOD-RCP-(	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	22-Aug-26	15-Sep-26	15-Jan-26 A	25-Jan-27	214,940.99
MOD-RCP-(	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 1	21	15-Sep-26	11-Oct-26	22-Jan-26 A	04-Feb-27	184,235.14
General		219	10-May-26	25-Apr-27	04-Nov-25 A	03-Jun-27	3,266,098.7(
Local Roads		44	27-Dec-26	24-Feb-27	01-Aug-26 A	03-Jun-27	8,878.15
Precast Curbs (Type K1-D)		44	27-Dec-26	24-Feb-27	01-Aug-26 A	03-Jun-27	8,878.15
MOD-LOR-PC-(	Excavation & Subgrade Preparation for Local Roads	8	27-Dec-26	05-Jan-27	01-Aug-26 A	09-May-27	1,566.73
MOD-LOR-PC-(	Pour concrete base & hunching for Local Roads	8	05-Jan-27	14-Jan-27	11-Aug-26 A	18-May-27	1,566.73
MOD-LOR-PC-(	Install precast curbs for Local Roads	20	14-Jan-27	08-Feb-27	18-Aug-26 A	30-May-27	4,177.95
MOD-LOR-PC-(	Backfill & compact for Local Roads	8	08-Feb-27	24-Feb-27	01-Sep-26 A	03-Jun-27	1,566.73
Arterial Roads		37	10-May-26	01-Aug-26	27-Jun-26 A	08-Mar-27	324,466.66
Precast Curbs (Type K1-D)		37	10-May-26	01-Aug-26	27-Jun-26 A	08-Mar-27	324,466.66
MOD-ARR-PC-(	Excavation & Subgrade Prep for Arterial Roads	8	10-May-26	19-May-26	27-Jun-26 A	25-Jan-27	46,352.38
MOD-ARR-PC-(	Concrete Base & Hunching for Arterial Roads	8	19-May-26	02-Jun-26	29-Jun-26 A	02-Feb-27	46,352.38
MOD-ARR-PC-(	Curb Installation for Arterial Roads	21	07-Jul-26	01-Aug-26	01-Jul-26 A	08-Mar-27	231,761.90
Communications		219	22-Jun-26	25-Apr-27	04-Nov-25 A	18-Apr-27	7,932,753.8(
Ductworks		167	22-Jun-26	14-Feb-27	04-Nov-25 A	18-Apr-27	3,135,306.2(
Concrete-Protected Service Culverts (50mm, 8 Outlets)		53	22-Jun-26	23-Aug-26	04-Nov-25 A	04-Mar-27	5,247,104.1(
MOD-COC-[	Trench Excavation for Communications	10	22-Jun-26	08-Jul-26	04-Nov-25 A	24-Feb-27	1,749,034.7(
MOD-COC-[	Culvert Installation & Concrete Protection for Communications	18	08-Jul-26	29-Jul-26	08-Nov-25 A	28-Feb-27	2,915,057.8(
MOD-COC-[	Backfilling & Compaction for Communications	21	29-Jul-26	23-Aug-26	10-Nov-25 A	04-Mar-27	583,011.57
Road Crossing Ducts (Exit 8)		121	16-Sep-26	14-Feb-27	01-Dec-25 A	18-Apr-27	888,202.07
MOD-COC-[	Horizontal Directional Drilling (HDD) for Communications	21	16-Sep-26	12-Oct-26	01-Dec-25 A	07-Apr-27	355,280.83
MOD-COC-[	Duct Installation & Joint Sealing for Communications	15	06-Jan-27	24-Jan-27	09-Dec-25 A	10-Apr-27	355,280.83
MOD-COC-[	Asphalt/Paving Restoration for Communications	15	24-Jan-27	14-Feb-27	01-Apr-26 A	18-Apr-27	177,640.41
Manholes (Telecom, 2000x1000x1001mm)		31	20-Mar-27	25-Apr-27	16-Dec-25 A	18-Apr-27	1,797,447.6(
MOD-COC-MH-	Concrete Works - Foundation - Wall - Roof for Communications	10	20-Mar-27	31-Mar-27	16-Dec-25 A	18-Apr-27	1,198,298.45
MOD-COC-MH-	Frame/Cover Installation for Communications	21	31-Mar-27	25-Apr-27	17-Dec-25 A	18-Apr-27	599,149.23
Testing & Commissioning & Closeout		157	12-Jan-26	18-May-27	14-Jan-26 A	08-May-27	7,343,453.8
Testing & Commissioning		157	12-Jan-26	18-May-27	14-Jan-26 A	08-May-27	7,343,453.8
Zone 3		77	12-Jan-26	09-Apr-26	20-Jan-26 A	24-Dec-26	2,891,237.2(
A102060	Testing and Commissioning for Sewerage Network Zone 3	21	05-Mar-26	09-Apr-26	05-Mar-26 A	24-Dec-26	350,278.50
A103590	Testing and Commissioning for Rain Water Drainage Network Zone 3	21	19-Jan-26	11-Feb-26	29-Jan-26 A	07-Dec-26	1,789,001.67
A103600	Testing and Commissioning for Potable Water Network Zone 3	21	19-Jan-26	11-Feb-26	31-Jan-26 A	23-Nov-26	454,067.96
A103610	Testing and Commissioning for Irrigation Network Zone 3	21	12-Jan-26	04-Feb-26	20-Jan-26 A	12-Dec-26	297,889.13
Zone 2		84	14-Jan-26	09-Apr-26	14-Jan-26 A	22-Dec-26	5,782,474.4(
A103640	Testing and Commissioning for Sewerage Network Zone 2	21	05-Mar-26	09-Apr-26	05-Mar-26 A	22-Dec-26	700,557.00
A103650	Testing and Commissioning for Rain Water Drainage Network Zone 2	21	19-Jan-26	11-Feb-26	11-Apr-26 A	24-Nov-26	3,578,003.32
A103660	Testing and Commissioning for Potable Water Network Zone 2	21	14-Jan-26	07-Feb-26	14-Jan-26 A	02-Dec-26	908,135.90
A103670	Testing and Commissioning for Irrigation Network Zone 2	21	19-Jan-26	11-Feb-26	10-Feb-26 A	19-Nov-26	595,778.27
Zone 1		86	18-Jan-26	25-Mar-26	18-Jan-26 A	02-Jan-27	5,782,474.4(
A103690	Testing and Commissioning for Sewerage Network Zone 1	21	11-Feb-26	25-Mar-26	11-Feb-26 A	02-Jan-27	700,557.00
A103700	Testing and Commissioning for Rain Water Drainage Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	16-Nov-26	3,578,003.32
A103710	Testing and Commissioning for Potable Water Network Zone 1	21	18-Jan-26	10-Feb-26	18-Jan-26 A	01-Dec-26	908,135.90
A103720	Testing and Commissioning for Irrigation Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	18-Nov-26	595,778.27
General		21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6(
A103630	Testing and Commissioning for Communication	21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6(

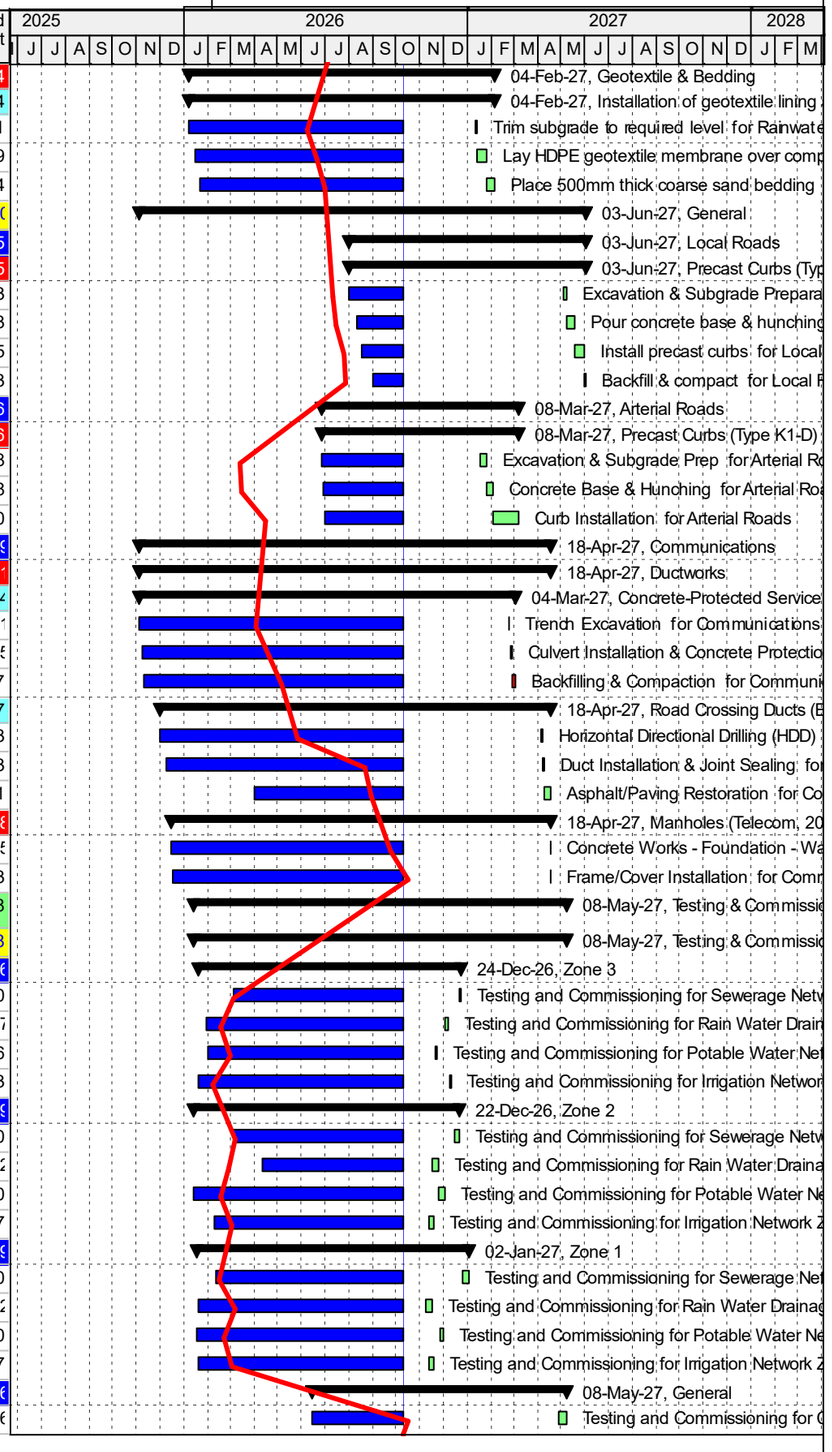

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation
