Development of Phase One – Part Two, Third Industrial City in Dammam

مشروع تطوير المرحلة الأولى الجزء الثاني بالمدينة الصناعية الثالثة بالدمام

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Mofarreh Alharbi and Partners	EGIS	Ihab Mohammed Attia	19-May-2025	18-May-2027

Scope: arterial and local roads, potable water, sewage, storm drainage, irrigation, street lighting and telecom networks, sewage pump stations and storm drainage ponds for Phase 1, Part 2 of the 3rd Industrial City in Dammam.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 27-Oct-2026 data date the project is 77.4% complete against 96.5% planned, 19.1% behind plan, and gained only 0.07% this week against 0.34% planned.

PHYSICAL % COMPLETE
77.4% / 96.5% plan
▼ SPI 0.80 –19.1%

PROGRESS THIS WEEK
+0.07% / +0.34% plan
▼ 0.27% below the weekly plan

CONTRACT TIME ELAPSED
72.2% · day 527 of 730
▼ P6 finish 12-Jun-2027

INVOICED TO DATE (GROSS)
15.9% · 37.3M SAR
12 progress invoices, last period ends 15-Jul-2026

The project is 19.1% behind plan and the current pace cannot close the gap.

22.6% of the work remains with 29 whole weeks left to the contract completion date of 18-May-2027, which needs about 0.78% a week; this week achieved 0.07%. The P6 update (data date 24-Oct-2026) finishes the project on 12-Jun-2027, 25 days late with –24 days of float, while the weekly report still forecasts 18-May-2027. The weakest areas are the Zone 3 networks (66.7% against 98.1% planned), sewage networks in Zones 1 and 3, and the road crossings.

Site photos this week

Six photos uploaded with this week's report, stamped 19 to 21 October 2026 where the stamp is visible. Work this week centred on potable water and irrigation pipes, valves and fire hydrants, telecom trenches and the pump stations. Select a photo to view it larger, then use the arrows to move between photos.



Trench excavation

Excavator opening a network trench. Stamped 19-Oct-2026, 06:36, 25.92121°N 49.96035°E.



HDPE pipe welding

Butt-fusion welding of an HDPE line in the trench. Stamped 20-Oct-2026, 14:17.



Pipe jointing

Crew jointing HDPE pipe and fittings in an open trench.



Valve installation

Gate valve set on the line and checked for level. Stamped 21-Oct-2026, 08:12.



Fire hydrant installation

Fire hydrant installed in its pit. Stamped 21-Oct-2026, 08:39.




Pump station pipework

Pipework and valves being installed at a pump station. Stamped 20-Oct-2026, 15:06.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet; October actual from the weekly report.

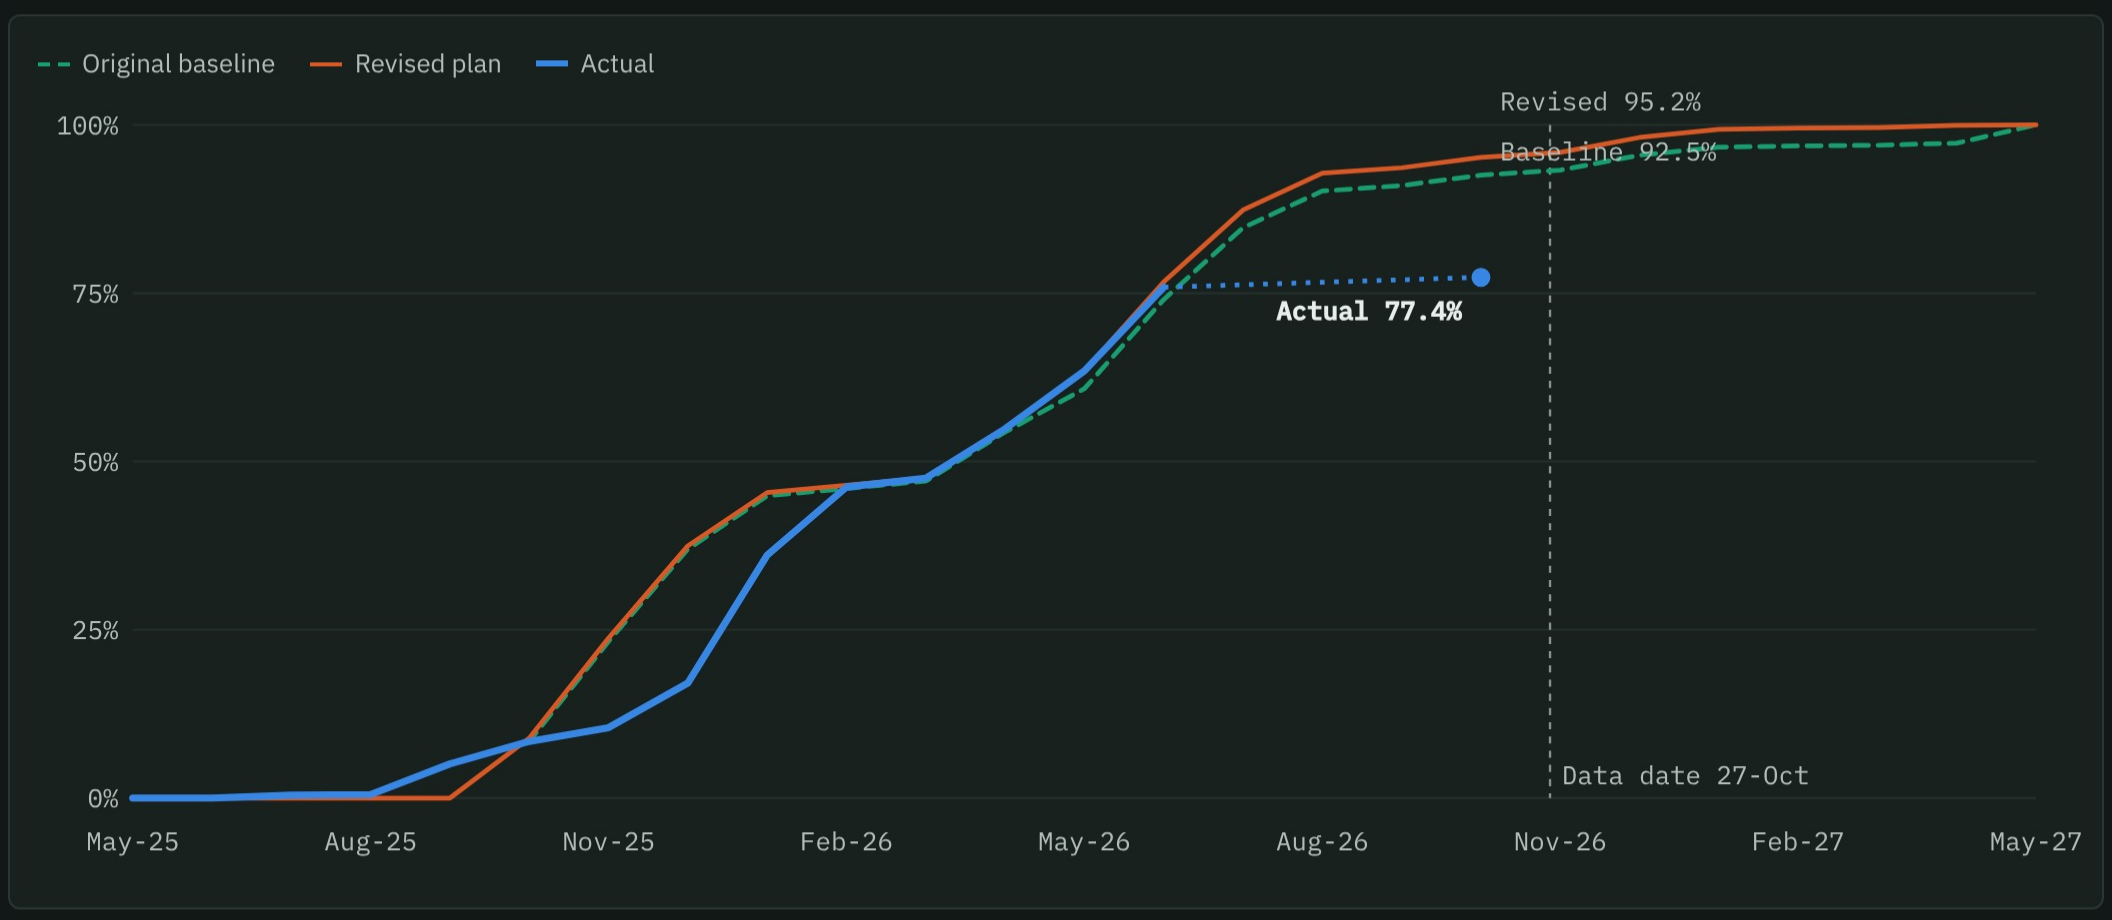

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
27-Oct-2026	**96.5**	**77.4**	**−19.1%**	**+0.07%**	**0.80**

Only this week's report has been uploaded, so earlier weeks cannot be shown. The chart sheet records monthly actuals only up to June 2026 (75.9%); the dotted line joins it to this week's 77.4%. The weekly report's planned 96.5% is higher than both the baseline (92.5%) and the revised plan (95.2%) for October.

Progress by phase


Physical progress to date by zone and network, weighted by budgeted man-hours. Engineering and procurement carry no man-hours, so they have no physical measure.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Zone 1	42.1%	**95.8%**	**81.7%**	**-14.1%**	**0.85**	▼ Behind
Sewage network	7.0%	91.5%	58.0%	-33.5%	0.63	▼ Late
Storm drainage network	4.4%	100.0%	81.4%	-18.6%	0.81	▼ Late
Potable water network	3.1%	100.0%	94.7%	-5.3%	0.95	▼ Behind
Irrigation network	2.1%	100.0%	96.7%	-3.3%	0.97	▲ On track
Storm water collection ponds	24.3%	96.2%	89.9%	-6.3%	0.93	▼ Behind
Road crossings	1.3%	78.9%	0.0%	-78.9%	0.00	▼ Not started
Zone 2	20.0%	**99.8%**	**83.7%**	**-16.1%**	**0.84**	▼ Late
Sewage network	3.9%	100.0%	81.4%	-18.6%	0.81	▼ Late
Storm drainage network	4.4%	100.0%	77.6%	-22.4%	0.78	▼ Late
Potable water network	0.8%	100.0%	87.7%	-12.3%	0.88	▼ Behind
Irrigation network	2.7%	100.0%	96.3%	-3.7%	0.96	▲ On track
Storm water collection ponds	6.9%	99.4%	98.9%	-0.4%	1.00	▲ On track
Road crossings	1.3%	100.0%	0.0%	-100.0%	0.00	▼ Not started
Zone 3	31.5%	**98.1%**	**66.7%**	**-31.4%**	**0.68**	▼ Late
Sewage network	7.6%	93.0%	49.2%	-43.8%	0.53	▼ Late
Storm drainage network	5.3%	100.0%	70.4%	-29.6%	0.70	▼ Late
Potable water network	6.1%	100.0%	45.0%	-55.0%	0.45	▼ Late
Irrigation network	0.8%	100.0%	90.1%	-9.9%	0.90	▼ Behind
Storm water collection ponds	11.0%	99.4%	89.3%	-10.1%	0.90	▼ Behind
Road crossings	0.6%	100.0%	31.8%	-68.2%	0.32	▼ Late
General	6.4%	**61.8%**	**57.6%**	**-4.1%**	**0.93**	▼ Behind
Local roads *	0.4%	6.9%	33.1%	+26.3%	4.83	▲ Ahead
Arterial roads *	0.4%	100.0%	12.0%	-88.0%	0.12	▼ Late
Telecom *	3.8%	82.1%	92.9%	+10.8%	1.13	▲ Ahead
Landscape	1.9%	24.5%	0.0%	-24.5%	0.00	▼ Not started
Total	100%	**96.5%**	**77.4%**	**-19.1%**	**0.80**	▼ Late

Planned and actual from the Weekly Progress Report sheet. * Zone 3, local roads, arterial roads and telecom use the cumulative actual man-hours of the P6 export in the Progress sheet, because the summary rows for them are inconsistent (see Data notes). The P6 update (data date 24-Oct-2026) has 136 activities: 11 completed, 68 in progress and 57 not started.

Scope of work: quantities

Quantities in the Alharbi (MG) scope, from the 27-Oct-2026 weekly presentation: network pipes from the network quantities slide, and manholes, valves, hydrants and lighting from the progress scope slide. "This week" cannot be calculated because no earlier week has been uploaded.

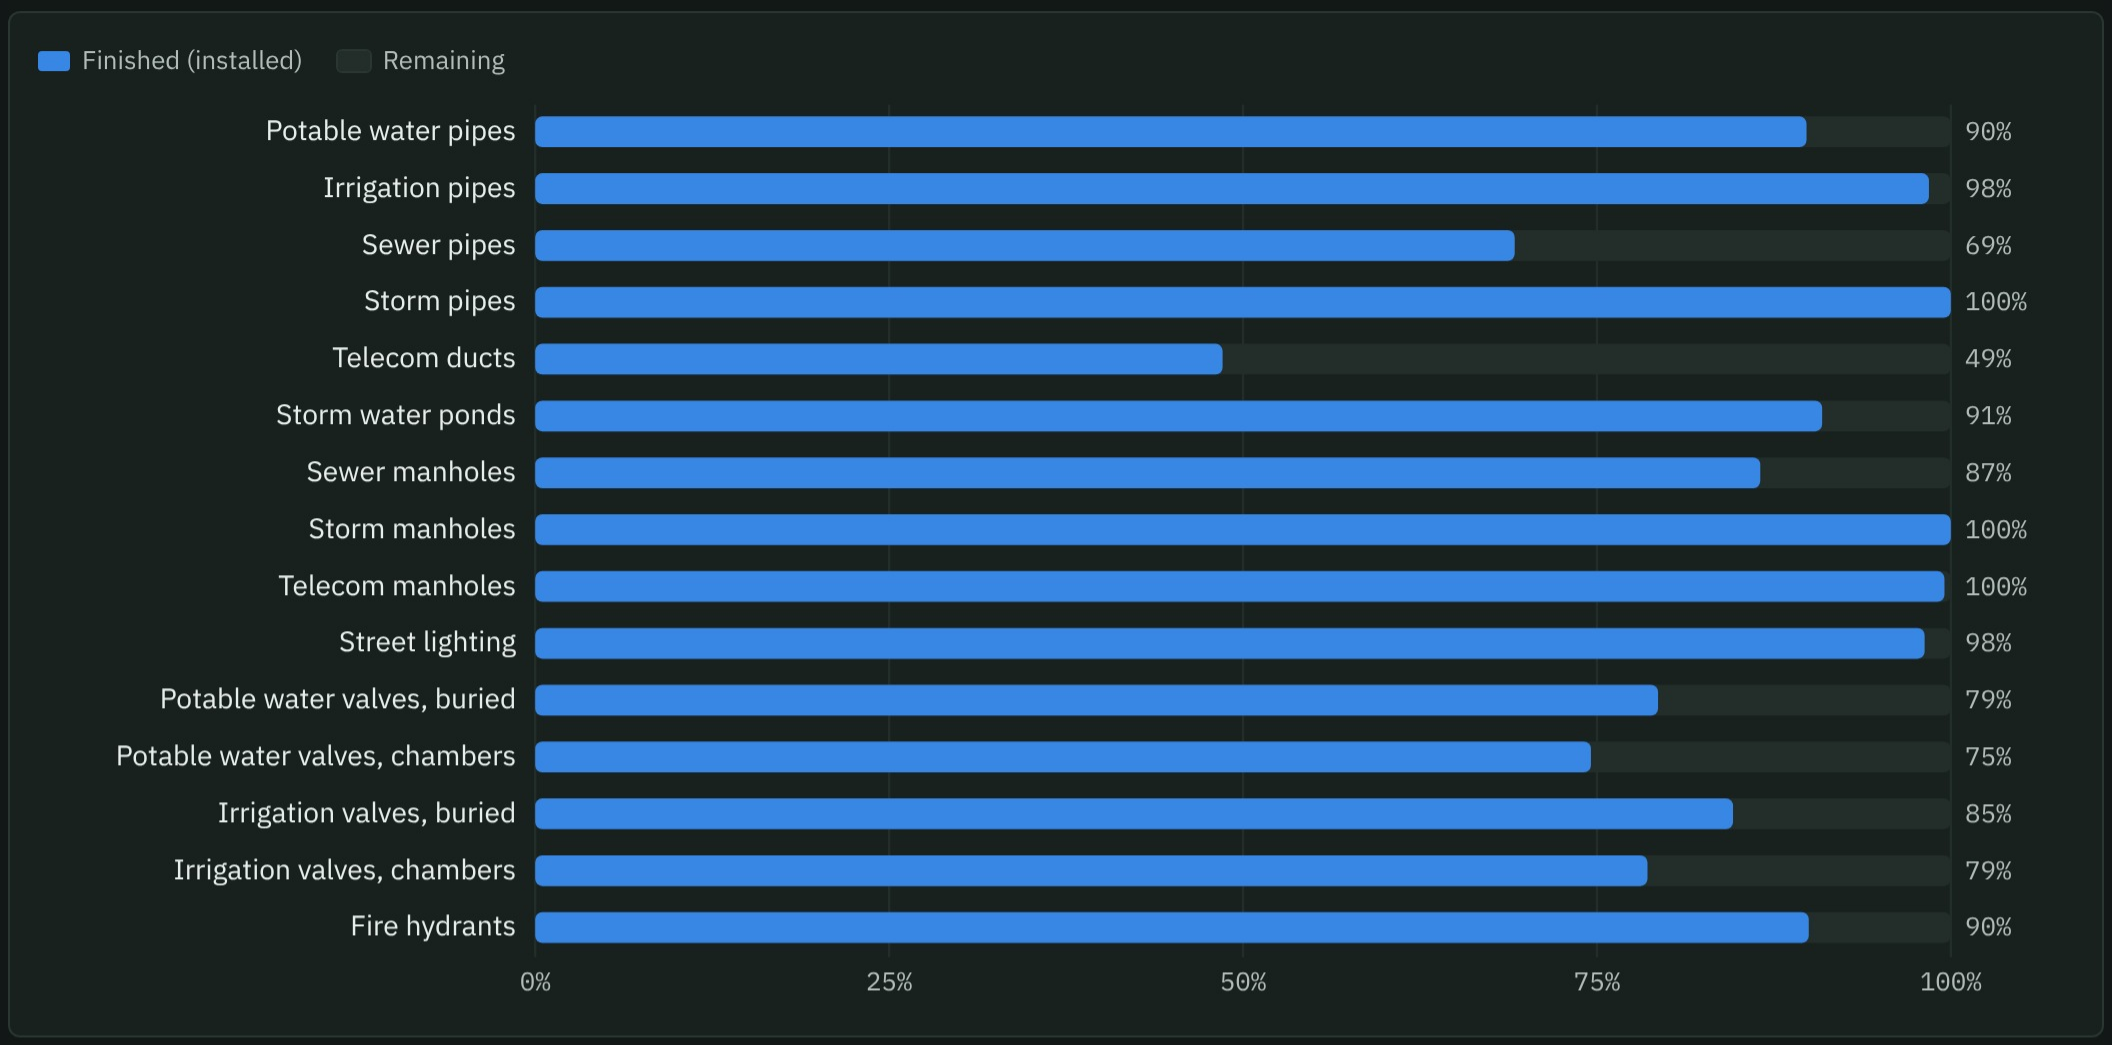

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Potable water pipes	All zones	m	2,992	2,687	–	305	89.8%	–
Irrigation pipes	All zones	m	4,911	4,835	–	76	98.5%	–
Sewer pipes	All zones	m	396	274	–	122	69.2%	–
Storm pipes	All zones	m	42,616	42,616	–	0	100.0%	–
Telecom ducts	All zones	m	64,321	31,233	–	33,088	48.6%	–
Storm water ponds	All zones	nos	11	10	–	1	90.9%	–
Sewer manholes	All zones	nos	104	90	–	14	86.5%	–
Storm manholes	All zones	nos	13	13	–	0	100.0%	–
Telecom manholes	All zones	nos	444	442	–	2	99.5%	–
Street lighting	All zones	unit not stated	54	53	–	1	98.1%	–
Potable water valves, buried	All zones	nos	440	349	–	91	79.3%	–
Potable water valves, chambers	All zones	nos	59	44	–	15	74.6%	–
Irrigation valves, buried	All zones	nos	884	748	–	136	84.6%	–
Irrigation valves, chambers	All zones	nos	70	55	–	15	78.6%	–
Fire hydrants	All zones	nos	279	251	–	28	90.0%	–

Telecom and sewage are the largest open quantities

Telecom ducts are 49% installed (31,233 of 64,321 m) and sewer pipes 69% (274 of 396 m). Of the installed network, 2,184 m of potable water, 2,998 m of irrigation and 6,705 m of telecom have been tested and handed to the consultant; no sewer or storm lengths have been handed over yet.

Previous contractor's networks

Alharbi has re-tested 74,073 m of water, 77,912 m of irrigation and 38,914 m of sewer from the previous contractor's scope, but only 8,588 m, 3,442 m and 9,343 m have been handed to the consultant. 31,676 m of storm network and 5,516 m of telecom remain to be tested.

Milestones

The weekly report keeps every forecast on the baseline date, while the P6 schedules show the interim network milestones and completion late. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	19-May-2025	19-May-2025	19-May-2025 (actual)	–	✓ Done
Site preparations	18-Jun-2025	18-Jun-2025	17-Jun-2025 (actual)	–	✓ Done
Drawings and specifications approved	18-Jul-2025	18-Jul-2025	11-Nov-2025	–	✓ Done
Report, work plan and schedule submitted	18-Jul-2025	18-Jul-2025	13-Sep-2025	–	✓ Done
Water networks and tanks complete	18-Jan-2026	18-Jan-2026	23-May-2026	–	▼ Late
Rainwater drainage works complete	18-Jan-2026	18-Jan-2026	08-Apr-2026	–	▼ Late
Testing and commissioning finish	–	18-May-2027	24-Apr-2027	−41	▼ At risk
Revised scope finish	–	–	06-May-2027	−82	▼ At risk
Completion of all project services	18-May-2027	18-May-2027	11-Jul-2027	–	▼ Late
Project finish / final handover	18-May-2027	18-May-2027	12-Jun-2027	−24	▼ Late

Three P6 sources give three different finish dates, and none matches the weekly report.

The uploaded P6 update (data date 24-Oct-2026) finishes the project on 12-Jun-2027 (+25 days). The P6 milestone table in the weekly report workbook shows final handover on 11-Jul-2027 (+54 days), and the P6 export in its Progress sheet shows 24-Oct-2027 (+159 days). The weekly report forecasts 18-May-2027 with no delay. The water and rainwater milestones of 18-Jan-2026 have passed; the presentation puts the potable water network at 80% and the storm network at 68%.

Procurement of key materials

Share of total quantity delivered to site for the long-lead items. Source: weekly presentation 27-Oct-2026, long-lead items slide.



Pumps: 3 of 15 delivered


Grundfos pump accessories are being installed at the stations, but only 3 pumps have arrived because of global shipping problems. The pump station control panels (IGEC, 1 set) and sewage station panels (WAMCO, 4 sets) are not expected in full until January 2027.

Generators and surge vessels

The two generators (Kohler – Abunayyan) are in the Kingdom and wait for the factory acceptance test before delivery to site. Surge vessels (7) were due to start arriving around 15-Oct-2026; none is delivered. The water pump maintenance order (SPP) is waiting for parts.

Manpower

Monthly head count on site (staff and labour), planned vs actual. Source: Manpower sheet.

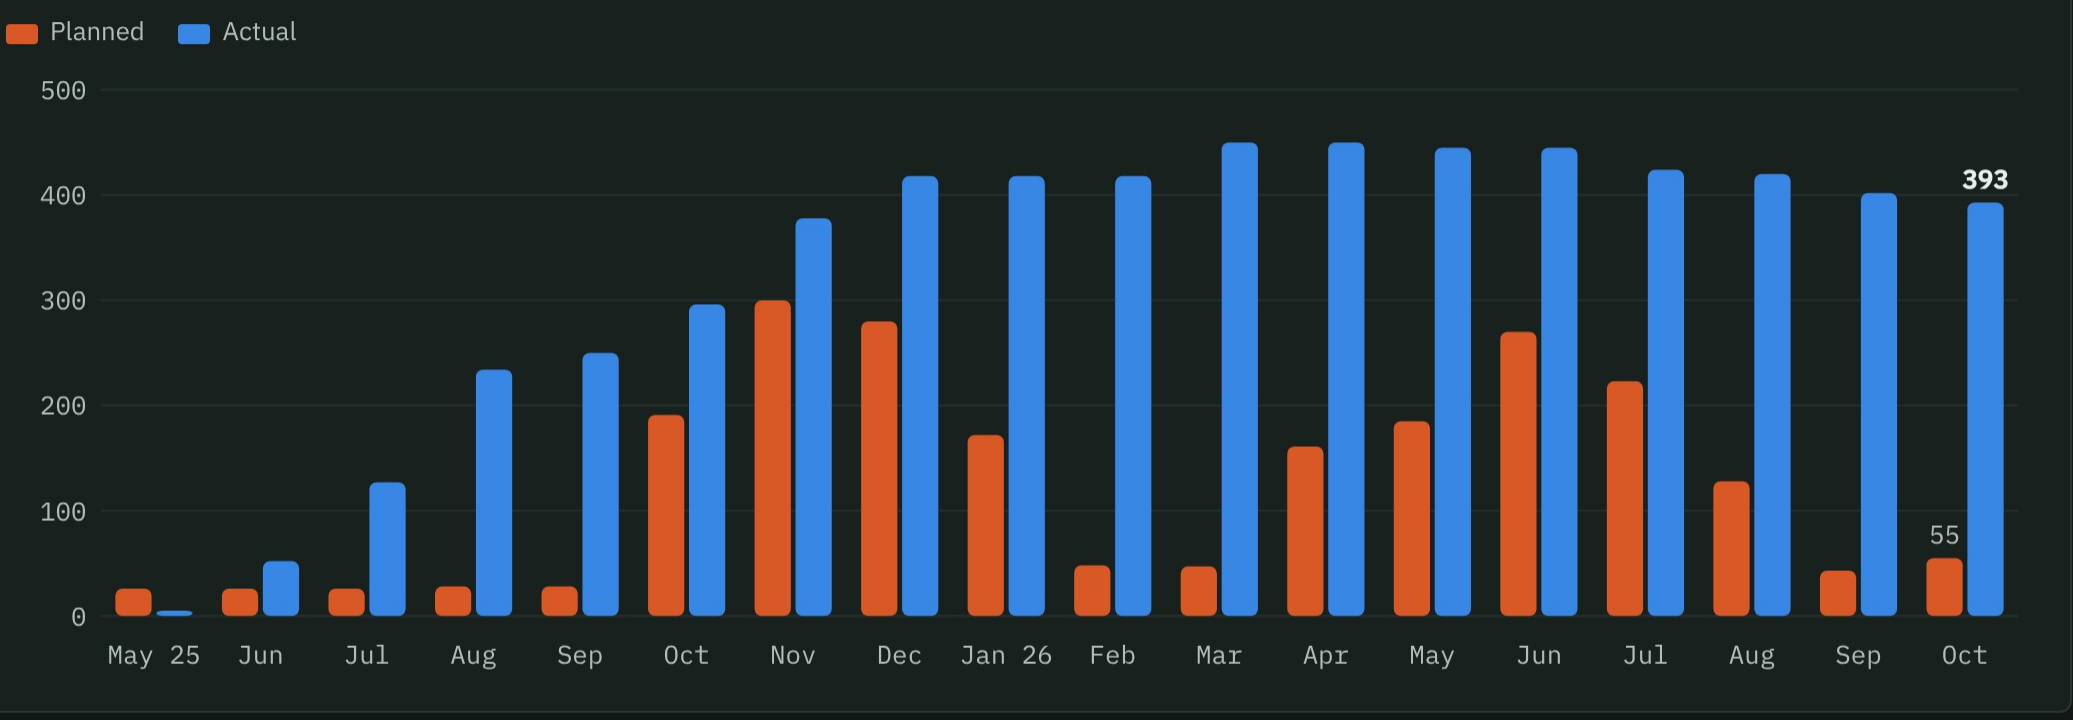

October head count is 393 (59 staff and 334 labour) against 55 planned. The plan comes from the resource-loaded P6 schedule and is far below the numbers actually on site, so it is not a useful benchmark. Actual labour has fallen from 397 in March–April to 334 in October; the issue log names low manpower and productivity as a cause of delay.

Cost and invoicing

Contract value

Original contract value (weekly report)	233,776,077
Contract value (presentation, excl. VAT)	233,575,734
Current project value after scope saving	164,170,171
Current saving	69,405,562
Change orders	0

All values in SAR. The two contract values differ by 200,343 SAR. The presentation records a scope reduction to 164.2M SAR; no change order is registered for it.

Invoices

Progress invoices submitted / approved	12 / 12
Gross value submitted	37,272,238
Advance payment (10%)	23,377,608
Retention (10%)	6,064,985
Invoices paid	4 · 15,540,346
Total disbursed to invoice 14 (presentation)	65,141,130
Executed but not yet paid (presentation)	13,244,299

The weekly report counts invoices to the period ending 15-Jul-2026; the presentation counts disbursements to invoice 14 (September 2026), 27.9% of the contract value. Invoicing stays well below the 77.4% physical progress.

Health, safety and quality

Safety Score 0.83

Safe man-hours (cumulative)	1,547,996
Man-hours this week	25,560
Lost-time injuries	0
Fatalities	0
First-aid cases	13
Near misses	1
Property damage	8
Inductions / toolbox talks	1,329 / 107

HSE inspection week: 21–27 Oct 2026. The issue log rates weak HSE procedures as critical.

Quality Score 0.91

FIRs issued / closed / open	6,340 / 6,279 / 61
NCRs issued / closed	53 / 53
Site instructions issued / open	89 / 2
MIRs issued / open	113 / 1
Shop drawings submitted (of 1,698)	1,687
Shop drawings approved A / B	306 / 1,368
Material submittals approved A / B	7 / 100

Quality inspection day: 27-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Pond 4	Contractor	MODON approved the proposal, but execution is weak. Work starts after the sewer network at the junction of Road 25 and Road 9. Target date 30-Sep-2026 has passed.
Road 25 crossings	Contractor	Asphalt cutting on Road 25 for the buried networks: the junction with Road 2 is done and the junction with Road 9 is in progress (target 31-Oct-2026). Permits for Road 25 have been stopped.
Pump station equipment	Contractor	The water station control system (target 31-Aug-2026, passed), generators, surge vessels and pumps are paid and being manufactured. Water pump maintenance has a purchase order and takes two weeks once parts arrive.
Network testing	Contractor	Testing is needed so complete networks can be handed over. The test plan has been submitted; marked urgent.
Third-party interfaces	Not assigned	Slab settlement caused by Watco and Al-Issa works; the Al-Issa office gate conflicts with a lighting pole foundation; work in Block F is stopped until the power line to the Chinese factory is extended.
Manpower and productivity	Contractor	Low manpower and equipment and low productivity of the contractor's own crews (MODON issue log, high priority).
Manual excavation	Contractor	Excavation is done by hand because there are no records of the existing services; trial pits are dug before excavation.
Drawings and existing network	Contractor	IFC drawings do not match site conditions. The BOQ for repairing the existing network is unclear, and the consultant and owner rejected replacing all damaged pipes from manhole to manhole.

Open risks in the MODON register: change in the industrial city's priorities reducing the scope (high), delays in purchases because of regional shipping problems (high), frequent work stoppages lowering daily output (medium), and differences between the signed contract value and the work on site (medium).

Data notes

- This is the first week uploaded for the project (W01–W03 are empty), so there are no previous-week values: scope quantities have no "This week" figure and the S-curve table has a single row. The weekly progress (+0.07%) is the figure stated in the weekly report.
- The report week is the contract week stated in the Milestones sheet ("Current Contract Weeks: 75 of 104"), which matches (27-Oct-2026 – 19-May-2025) ÷ 7. The workbook calls itself report #63 and the file names say WPR 56; neither is the week number.
- Data dates differ between files: weekly report 27-Oct-2026, P6 update 24-Oct-2026, P6 export in the Progress sheet labelled 20-Oct-26, procurement log 20-Oct-2026.
- Several physical-progress rows in the Weekly Progress Report sheet are wrong: Construction shows 189.8% planned and 206.6% earned; Zone 3 shows 354,449 earned man-hours (the whole project's total) against a 147,160 budget; local roads show 997%; telecom shows 0% and arterial roads 0% although the P6 export records 16,489 and 199 actual man-hours. The P6 export values were used for these rows. The project totals (96.5% planned, 77.4% actual) are consistent with the P6 actual units.
- The man-hour budget is 458,486 in the total row but 467,288 as the sum of the zones (467,280 in the S-curve sheet).
- The planned 96.5% to date does not match either curve in the Physical-Chart Data sheet (baseline 92.5%, revised plan 95.2% for October). The chart sheet's monthly actuals stop at June 2026, and the March–May 2026 actuals are identical to the revised plan values.
- Completion forecasts disagree: weekly report 18-May-2027, P6 update 12-Jun-2027, P6 milestone table 11-Jul-2027, P6 export 24-Oct-2027. Interim milestones 3 to 6 are still marked "F" (forecast) in the weekly report with 2025–2026 dates.
- The Target schedule sheet and presentation slides 3, 4 and 10 report value-weighted (cost-based) progress labelled as actual or achieved; those figures are not used in this report.
- Contract value is 233,776,077 SAR in the weekly report and 233,575,734 SAR in the presentation. Invoices: the weekly report shows 37.3M SAR (12 invoices), the invoice log totals 60.6M SAR including the advance payment, and the presentation shows 65.1M SAR disbursed to invoice 14. The invoice log has payment dates for invoices 6–8 that fall before their periods.

- Manpower: the summary panel shows 388 labour and 57 staff (445), while the monthly table and the presentation show 334 labour and 59 staff (393) for October.
- Scope quantities: the progress scope slide is labelled "15 September update" and gives telecom as 11,800 of 21,318 and potable water as 2,687 of 2,839, against 31,233 of 64,321 m and 2,687 of 2,992 m on the network quantities slide. The street lighting quantity (53 of 54) has no unit.
- Procurement: the 20-Oct procurement log shows 2 pumps delivered against 3 in the 27-Oct presentation, labels the Kohler – Abunayyan order as the fuel system (generators in the presentation), and labels the VEGA order as generators (no name in the presentation). The workbook's Procurement sheet has no quantities.
- The "Modon PM" field in the weekly report is blank; the PM name is taken from the MODON risk and issue log. The Major Quantities sheet shows "Final BOQ submitted and under review" for every network.

Compiled 01-Nov-2026 from the weekly report uploaded for week 75 (data date 27-Oct-2026).
