
Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		366	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	95,996,525.00	65,605,417.65	65,630,825.45	68.34%	68.37%
PROJECT MILESTONES		353	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	0.00	0.00	0.00	0%	0%
MOBILIZATION		35	07-Jan-26	16-Feb-26	07-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
ENGINEERING (3%)		159	22-Jan-26	17-May-26	15-Jan-26 A	05-Jul-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%
PROCUREMENT (20%)		258	04-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	19,199,305.00	18,012,864.10	19,199,305.00	93.82%	100%
CONSTRUCTION (67%)		321	27-Jan-26	21-Feb-27	14-Jan-26 A	28-Feb-27	64,317,671.75	37,523,725.44	36,378,528.97	58.34%	56.56%
RBF 900 SQM FACTORIES		321	27-Jan-26	16-Feb-27	14-Jan-26 A	28-Feb-27	55,841,646.40	35,883,887.59	33,844,973.57	64.26%	60.61%
SITE WORKS		16	27-Jan-26	25-Feb-26	14-Jan-26 A	31-Jan-26 A	10,892.39	10,892.39	10,892.39	100%	100%
BLOCK B6		270	10-Feb-26	23-Nov-26	15-Feb-26 A	24-Jan-27	5,075,523.09	3,607,961.04	2,621,371.68	71.09%	51.65%
BLOCK B5		248	19-Feb-26	23-Nov-26	16-Feb-26 A	05-Jan-27	5,075,523.09	4,617,286.04	3,108,847.38	90.97%	61.25%
BLOCK B4		243	25-Feb-26	01-Dec-26	17-Feb-26 A	04-Jan-27	5,075,523.09	4,290,448.70	3,245,831.89	84.53%	63.95%
BLOCK B3		303	03-Mar-26	28-Dec-26	17-Feb-26 A	20-Feb-27	5,075,523.09	3,476,170.36	2,720,525.80	68.49%	53.6%
BLOCK B2		274	08-Mar-26	02-Jan-27	17-Feb-26 A	16-Feb-27	5,075,523.09	3,106,737.04	2,687,295.06	61.21%	52.95%
BLOCK B1		278	12-Mar-26	03-Jan-27	17-Mar-26 A	23-Feb-27	5,075,523.09	3,291,210.87	2,667,226.41	64.84%	52.55%
BLOCK B7		273	10-Feb-26	06-Jan-27	16-Feb-26 A	04-Jan-27	5,075,523.09	3,278,936.91	3,759,151.29	64.6%	74.06%
BLOCK B8		292	19-Feb-26	14-Jan-27	17-Feb-26 A	28-Feb-27	5,075,523.09	2,687,335.31	3,320,936.13	52.95%	65.43%
BLOCK B9		287	25-Feb-26	31-Jan-27	17-Feb-26 A	13-Feb-27	5,075,523.09	2,666,759.17	3,339,986.43	52.54%	65.81%
BLOCK B10		293	03-Mar-26	08-Feb-27	18-Feb-26 A	18-Feb-27	5,075,523.09	2,496,308.73	3,221,399.98	49.18%	63.47%
BLOCK B11		288	08-Mar-26	16-Feb-27	18-Feb-26 A	24-Feb-27	5,075,523.09	2,353,841.04	3,141,509.13	46.38%	61.9%
SITE INFRASTRUCTURE		290	10-Feb-26	21-Feb-27	19-Jan-26 A	27-Feb-27	8,476,025.35	1,639,837.85	2,533,555.40	19.35%	29.89%
SITE WORKS		23	10-Feb-26	10-Mar-26	19-Jan-26 A	28-Feb-26 A	197,690.88	197,690.88	197,690.88	100%	100%
NETWORKS		90	07-Sep-26	23-Dec-26	01-Aug-26 A	01-Feb-27	1,901,944.63	670,749.27	1,180,962.82	35.27%	62.09%
EXTERNAL WORKS		83	15-Sep-26	25-Jan-27	01-Jul-26 A	27-Feb-27	3,338,525.71	771,397.70	1,154,901.70	23.11%	34.59%
ROAD WORKS		34	23-Nov-26	21-Feb-27	16-Jan-27	25-Feb-27	2,873,764.57	0.00	0.00	0%	0%
LANDSCAPING		12	02-Feb-27	15-Feb-27	09-Feb-27	24-Feb-27	164,099.55	0.00	0.00	0%	0%
TESTING AND COMMISSIONING (10%)		185	24-May-26	18-Feb-27	17-Jun-26 A	27-Feb-27	9,599,652.50	7,188,932.37	7,173,095.73	74.89%	74.72%
PREOJECT CLOSEOUT		21	02-Feb-27	06-Mar-27	09-Feb-27	06-Mar-27	0.00	0.00	0.00	0%	0%

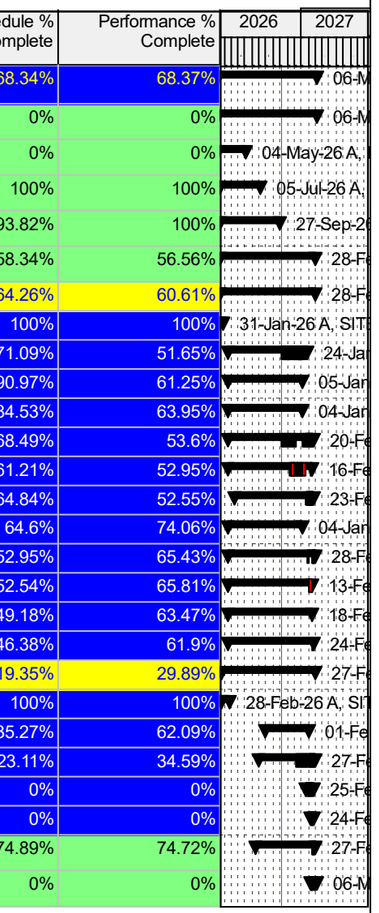

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
29-Sep-26	Weekly Report		
