
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Performance % Complete	Performance % Complete - Labor Units	Budget At Completion
DAM3-02-3	44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3	366	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	70.38%	75%	95,996,525.00
DAM3-02-3.1	PROJECT MILESTONES	353	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	0%	0%	0.00
DAM3-02-3.1.1	CONTRACTUAL MILESTONES	353	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	0%	0%	0.00
DAM3-02-3.1.3	DISCIPLINE MILESTONES	294	27-Jan-26	21-Feb-27	15-Feb-26 A	25-Feb-27	0%	0%	0.00
DAM3-02-3.2	MOBILIZATION	35	07-Jan-26	16-Feb-26	07-Jan-26 A	04-May-26 A	0%	100%	0.00
DAM3-02-3.2.3	SITE FACILITIES AND OFFICES	27	07-Jan-26	07-Feb-26	07-Jan-26 A	23-Feb-26 A	0%	100%	0.00
DAM3-02-3.2.2	PRELIMINARY SUBMITTALS	31	22-Jan-26	16-Feb-26	14-Jan-26 A	04-May-26 A	0%	100%	0.00
DAM3-02-3.3	ENGINEERING (3%)	159	22-Jan-26	17-May-26	15-Jan-26 A	05-Jul-26 A	100%	100%	2,879,895.75
DAM3-02-3.3.1	SHOP DRAWINGS	138	27-Jan-26	17-May-26	20-Jan-26 A	05-Jul-26 A	0%	100%	0.00
DAM3-02-3.3.4	PRE QUALIFACTION FOR MATERIALS	138	22-Jan-26	12-Apr-26	15-Jan-26 A	11-Jun-26 A	0%	100%	0.00
DAM3-02-3.3.2	MATERIAL SUBMITTAL	108	27-Jan-26	20-Apr-26	15-Jan-26 A	14-Jun-26 A	100%	100%	2,879,895.75
DAM3-02-3.3.3	METHOD STATEMENTS	125	29-Jan-26	23-Apr-26	07-Feb-26 A	23-Jun-26 A	0%	100%	0.00
DAM3-02-3.4	PROCUREMENT (20%)	258	04-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	100%	100%	19,199,305.00
DAM3-02-3.4.2	LONG LEAD MATERIALS	245	09-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	100%	100%	9,350,010.31
DAM3-02-3.4.1	SHORT LEAD MATERIALS	258	04-Feb-26	14-Oct-26	14-Jan-26 A	21-Sep-26 A	100%	100%	9,849,294.69
DAM3-02-3.5	CONSTRUCTION (67%)	321	27-Jan-26	21-Feb-27	14-Jan-26 A	27-Feb-27	59.54%	67.5%	64,317,671.75
DAM3-02-3.5.1	RBF 900 SQM FACTORIES	321	27-Jan-26	16-Feb-27	14-Jan-26 A	23-Feb-27	63.86%	70.34%	55,841,646.40
DAM3-02-3.5.2	SITE INFRASTRUCTURE	290	10-Feb-26	21-Feb-27	19-Jan-26 A	27-Feb-27	31.04%	37.88%	8,476,025.35
DAM3-02-3.6	TESTING AND COMMISSIONING (10%)	183	24-May-26	18-Feb-27	17-Jun-26 A	24-Feb-27	74.89%	17.97%	9,599,652.50
DAM3-02-3.6.3	TESTING AND COMMISSIONING 900 Sq.m-2	183	24-May-26	18-Feb-27	28-Jun-26 A	24-Feb-27	3.26%	2.25%	1,943,587.85
DAM3-02-3.6.4	TESTING AND COMMISSIONING SITE INFRASTRUCTURE	85	06-Oct-26	06-Feb-27	13-Oct-26 A	18-Feb-27	23.73%	30.07%	530,478.84
DAM3-02-3.6.1	SNAGG WORKS	79	10-Jun-26	16-Jul-26	17-Jun-26 A	21-Oct-26	98.24%	0%	7,125,585.81
DAM3-02-3.7	PREOJECT CLOSEOUT	20	02-Feb-27	06-Mar-27	09-Feb-27	06-Mar-27	0%	0%	0.00
DAM3-02-3.7.1	ENGINEERING	8	02-Feb-27	10-Feb-27	09-Feb-27	18-Feb-27	0%	0%	0.00
DAM3-02-3.7.2	TRAINING AND MANUALS	10	11-Feb-27	23-Feb-27	18-Feb-27	03-Mar-27	0%	0%	0.00
DAM3-02-3.7.4	DEMOBILIZATION	13	09-Feb-27	24-Feb-27	16-Feb-27	04-Mar-27	0%	0%	0.00
DAM3-02-3.7.5	FINAL HANDOVER	6	23-Feb-27	06-Mar-27	27-Feb-27	06-Mar-27	0%	0%	0.00

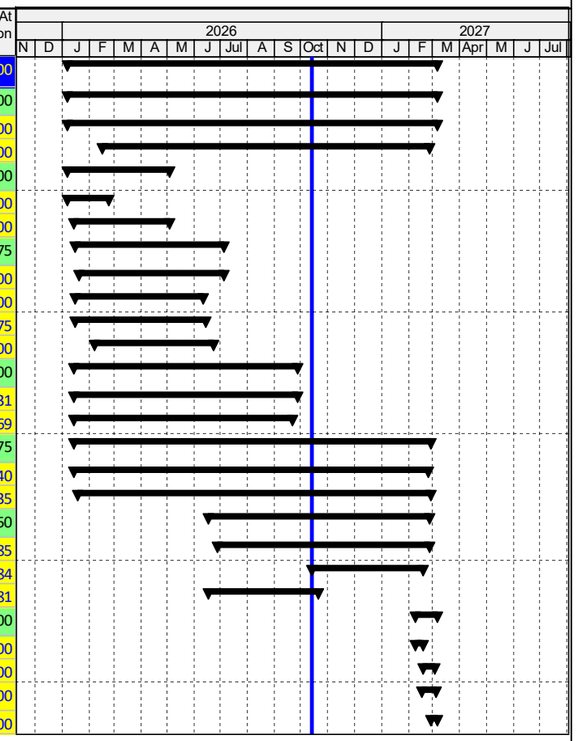

◆ ◆ Milestone
summary

TASK filter: All Activities

© Oracle Corporation
