
# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| **44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3** | | 366 | 95,996,525.00 | 07-Jan-26 | 06-Mar-27 | 07-Jan-26 | | 69,925,401.98 | 70,141,305.82 | 1.00 |
| **PROJECT MILESTONES** | | 350 | 0.00 | 07-Jan-26 | 06-Mar-27 | 07-Jan-26 | | 0.00 | 0.00 | 0.00 |
| **CONTRACTUAL MILESTONES** | | 350 | 0.00 | 07-Jan-26 | 06-Mar-27 | 07-Jan-26 | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0010 | Project Start Date | 0 | 0.00 | 07-Jan-26 | | 07-Jan-26 | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0040 | Completion of Time Schedule submission | 0 | 0.00 | | 28-Jan-26 | | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0050 | Completion of Plans (PEP,PQP,HSE, Procurement Plan) | 0 | 0.00 | | 04-Feb-26 | | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0020 | Completion of Mobilization Works | 0 | 0.00 | | 07-Feb-26 | | 18-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0030 | Completion of Site Suvey Works | 0 | 0.00 | | 09-Feb-26 | | 12-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0070 | Completion of Site levelling, local roads & parkings | 0 | 0.00 | | 12-Feb-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0060 | Completion of Engineering and Materials | 0 | 0.00 | | 07-May-26 | | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0080 | Network start | 0 | 0.00 | 07-Sep-26 | | 01-Aug-26 | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0110 | Competion of Testing and Commissioning | 0 | 0.00 | | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0090 | Completion of Construction | 0 | 0.00 | | 21-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-MMS-0100 | Project Completion Date | 0 | 0.00 | | 06-Mar-27 | | | 0.00 | 0.00 | 0.00 |
| **DISCIPLINE MILESTONES** | | 286 | 0.00 | 27-Jan-26 | 21-Feb-27 | 15-Feb-26 | | 0.00 | 0.00 | 0.00 |
| **900 SQM FACTORIES** | | 286 | 0.00 | 27-Jan-26 | 21-Feb-27 | 15-Feb-26 | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2360 | Construction Start | 0 | 0.00 | 27-Jan-26 | | 15-Feb-26 | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2310 | Completion of Civil works | 0 | 0.00 | | 01-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2330 | Completion of Mechanical works | 0 | 0.00 | | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2320 | Completion of Electrical works | 0 | 0.00 | | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2340 | Completion of Architectural works | 0 | 0.00 | | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2370 | Construction Finish | 0 | 0.00 | | 21-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **SITE INFRASTRUCTURE** | | 18 | 0.00 | 22-Dec-26 | 21-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2460 | Completion of Environmentall works | 0 | 0.00 | | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-PMS-DMS-2450 | Completion of External works | 0 | 0.00 | | 21-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **MOBILIZATION** | | 35 | 0.00 | 07-Jan-26 | 16-Feb-26 | 07-Jan-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| **SITE FACILITIES AND OFFICES** | | 27 | 0.00 | 07-Jan-26 | 07-Feb-26 | 07-Jan-26 | 23-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0010 | Site Survey | 2 | 0.00 | 07-Jan-26 | 08-Jan-26 | 12-Feb-26 | 12-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0011 | Site Layout Plan Prep | 2 | 0.00 | 10-Jan-26 | 11-Jan-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0012 | Site Layout Plan Submittal | 2 | 0.00 | 12-Jan-26 | 13-Jan-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0013 | Site Layout Plan Owner Approval | 2 | 0.00 | 14-Jan-26 | 15-Jan-26 | 04-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0014 | Clear and Grub for Offices and Access Roads | 2 | 0.00 | 15-Jan-26 | 17-Jan-26 | 11-Jan-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0015 | Construct Site Offices | 4 | 0.00 | 18-Jan-26 | 21-Jan-26 | 19-Jan-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0016 | Electrical Works and Connections | 4 | 0.00 | 22-Jan-26 | 26-Jan-26 | 09-Feb-26 | 23-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0017 | Site Utilities | 4 | 0.00 | 27-Jan-26 | 31-Jan-26 | 11-Feb-26 | 23-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0018 | Install Project Signs | 4 | 0.00 | 01-Feb-26 | 04-Feb-26 | 03-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0019 | Mobilization of Manpower | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 07-Jan-26 | 23-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-MOB-SO.0020 | Mobilization of Equipment | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 25-Jan-26 | 23-Feb-26 | 0.00 | 0.00 | 0.00 |
| **PRELIMINARY SUBMITTALS** | | 31 | 0.00 | 22-Jan-26 | 16-Feb-26 | 14-Jan-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| **PREPARATION AND SUBMITTALS** | | 21 | 0.00 | 22-Jan-26 | 04-Feb-26 | 14-Jan-26 | 21-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-0010 | Project Execution Plan | 2 | 0.00 | 22-Jan-26 | 24-Jan-26 | 21-Feb-26 | 21-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-0011 | Health & Safety Plan | 2 | 0.00 | 25-Jan-26 | 26-Jan-26 | 26-Jan-26 | 26-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-0012 | Baseline Schedule | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 14-Jan-26 | 14-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-0013 | Risk Management plan | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 28-Jan-26 | 28-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-0014 | Communication Plan | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 21-Feb-26 | 21-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-0015 | Quality Control Plan | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 28-Jan-26 | 28-Jan-26 | 0.00 | 0.00 | 0.00 |
| **REVIEW AND APPROVALS** | | 29 | 0.00 | 25-Jan-26 | 16-Feb-26 | 14-Jan-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-1010 | Project Execution Plan | 10 | 0.00 | 25-Jan-26 | 04-Feb-26 | 21-Feb-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-1011 | Health & Safety Plan | 10 | 0.00 | 27-Jan-26 | 07-Feb-26 | 26-Jan-26 | 28-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-1012 | Risk Management plan | 10 | 0.00 | 01-Feb-26 | 11-Feb-26 | 28-Jan-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-1013 | Communication Plan | 10 | 0.00 | 03-Feb-26 | 14-Feb-26 | 21-Feb-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-1014 | Quality Control Plan | 10 | 0.00 | 05-Feb-26 | 16-Feb-26 | 28-Jan-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-PRE-SUB-1015 | Baseline Schedule | 10 | 0.00 | 05-Feb-26 | 16-Feb-26 | 14-Jan-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| **ENGINEERING (3%)** | | 159 | 2,879,895.75 | 22-Jan-26 | 17-May-26 | 15-Jan-26 | 05-Jul-26 | 2,879,895.75 | 2,879,895.75 | 1.00 |
| **SHOP DRAWINGS** | | 138 | 0.00 | 27-Jan-26 | 17-May-26 | 20-Jan-26 | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| **PREPARATION AND SUBMITTAL** | | 136 | 0.00 | 27-Jan-26 | 07-May-26 | 20-Jan-26 | 01-Jul-26 | 0.00 | 0.00 | 0.00 |
| **STRUCTURAL** | | 87 | 0.00 | 10-Feb-26 | 22-Mar-26 | 03-Feb-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-750 | FOUNDATION LAYOUT | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 18-Feb-26 | 18-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-760 | GRADE BEAM / SLAB ON GRADE LAYOUT | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-770 | BASE PLATE LAYOUT | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |




Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

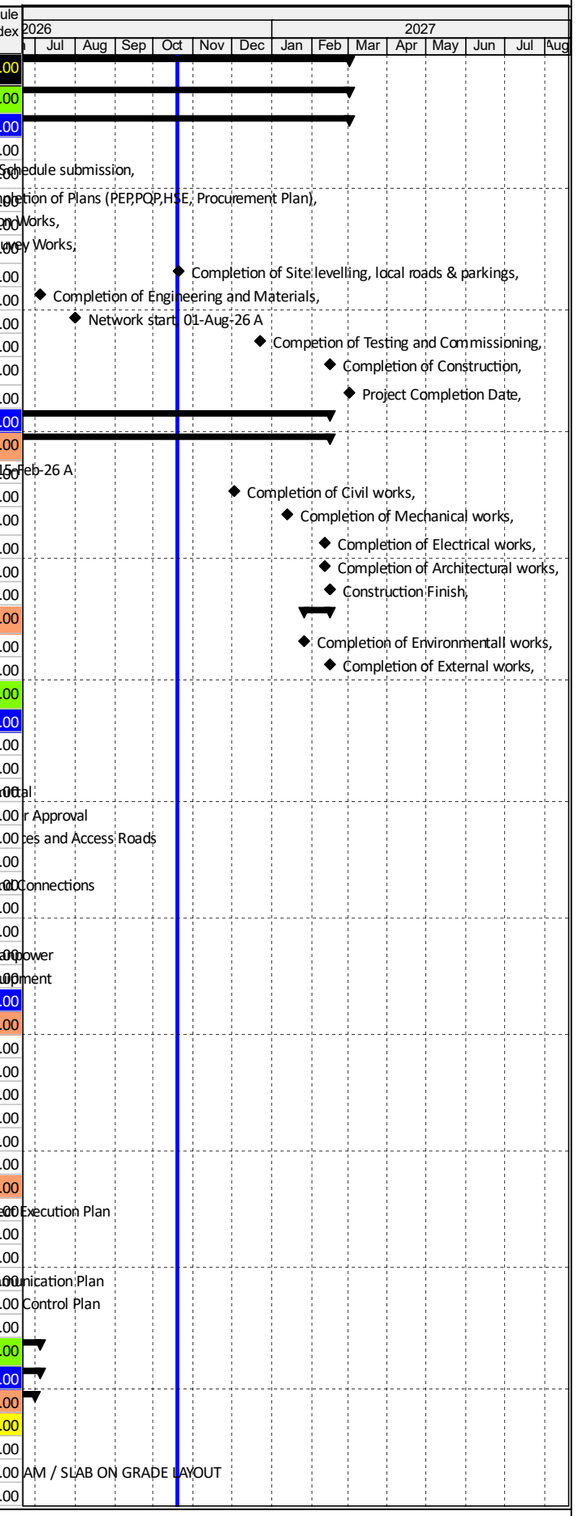


TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-SS-C-780 | TIE BEAM @ 4500mm EL. | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-790 | ROOF FRAMING LAYOUT | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-800 | PURLINS FRAMING LAYOUT | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-810 | ROOF SHEETING LAYOUT | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-820 | COLUMNS AND AXIS LAYOUT | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-830 | SECTIONS | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-840 | EXTERNAL WALL SECTION DETAILS | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-850 | BASE PLATE DETAILS | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-860 | TYPICAL STRUCTURAL SECTION DETAILS | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-870 | STRUCTURAL SCHEDULE | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 02-Jun-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-880 | PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2) | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-C-890 | PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2) | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 75 | 0.00 | 25-Feb-26 | 04-Apr-26 | 03-Feb-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-830 | GROUND FLOOR LAYOUT PLAN | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-840 | GROUND FLOOR ENLARGED LAYOUT PLAN | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-850 | SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 02-Jun-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-860 | ELEVATIONS (SHEET 01 0F 02) | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-1170 | ELEVATIONS (SHEET 01 0F 02) | 5 | 0.00 | 05-Mar-26 | 10-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-870 | BUILDING SECTIONS | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-880 | WALL SECTIONS | 2 | 0.00 | 11-Mar-26 | 12-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-890 | CEILING LAYOUT PLAN | 2 | 0.00 | 14-Mar-26 | 15-Mar-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-900 | FINISHING LAYOUT PLAN | 2 | 0.00 | 16-Mar-26 | 21-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-910 | TOILET DETAILS | 2 | 0.00 | 22-Mar-26 | 23-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-920 | DOORS & WINDOWS SCHEDULE | 2 | 0.00 | 24-Mar-26 | 25-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-930 | MISCELLANEOUS DETAILS - 01 | 2 | 0.00 | 26-Mar-26 | 28-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-940 | MISCELLANEOUS DETAILS - 02 | 2 | 0.00 | 29-Mar-26 | 30-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-950 | SIGNAGE LOCATION PLAN | 2 | 0.00 | 31-Mar-26 | 01-Apr-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-A-960 | SIGNAGE DESIGN DETAILS | 2 | 0.00 | 02-Apr-26 | 04-Apr-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 47 | 0.00 | 03-Mar-26 | 23-Apr-26 | 04-Feb-26 | 16-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-600 | TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 17-Mar-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-610 | TOILETS DETAILS PLUMBING-DRAINAGE | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 11-Mar-26 | 11-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-620 | TYPICAL ROOF PLUMBING PLAN | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-630 | GROUND FLOOR WATER SUPPLY PLAN | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 17-Mar-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-640 | TOILET DETAILS PLUMBING-WATER | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 11-Mar-26 | 11-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-650 | SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-660 | SCHEMATIC RISER DIAGRAM PLUMBING-WATER | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-670 | GENERAL MISELLANEOUS DETAILS PLUMBING | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-680 | GENERAL MISELLANEOUS DETAILS PLUMBING | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-690 | SCHEDULE- PLUMBING | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 17-Mar-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-700 | PUMP ROOM LAYOUT | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 16-Apr-26 | 16-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-710 | PUMP ROOM 3D & SECTIONS VIEW | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 16-Apr-26 | 16-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-720 | SCHEDULES | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 17-Mar-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-730 | GROUND FLOOR PLAN-HVAC SYSTEM | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 26-Mar-26 | 26-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-740 | TYPICAL ROOF HVAC PLAN | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 26-Mar-26 | 26-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-750 | GENERAL-INSTRUMENTATION & CONTROL | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-760 | GENERAL MISCELLANEOUS DETAILS - HVAC | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-770 | TYPICAL GROUND FLOOR PLAN FIREFIGHTING | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 14-Mar-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-780 | SCHEMATIC RISER DIAGRAM FIREFIGHTING | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-790 | GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING | 2 | 0.00 | 20-Apr-26 | 21-Apr-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-M-800 | MISCELLANEOUS DETAILS | 2 | 0.00 | 22-Apr-26 | 23-Apr-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 133 | 0.00 | 05-Mar-26 | 05-May-26 | 09-Feb-26 | 25-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-940 | GROUND FLOOR POWER PLAN | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-950 | GROUND FLOOR POWER FOR MECHANICAL | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-960 | ROOF FLOOR POWER FOR MECHANICAL | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-970 | ROOF FLOOR POWER | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 08-Apr-26 | 09-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-980 | PV SYSTEM CALCULATION | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 25-Jun-26 | 25-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-990 | GROUND FLOOR LIGHTING PLAN | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1000 | ROOF FLOOR LIGHTING PLAN | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1010 | GOUND FLOOR ACCESS CONTROL | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1020 | GROUND FLOOR FIRE ALARM PLAN | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1030 | GROUND FLOOR CCTV PLAN | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1040 | GROUND FLOOR DATA & TELECOM PLAN | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |

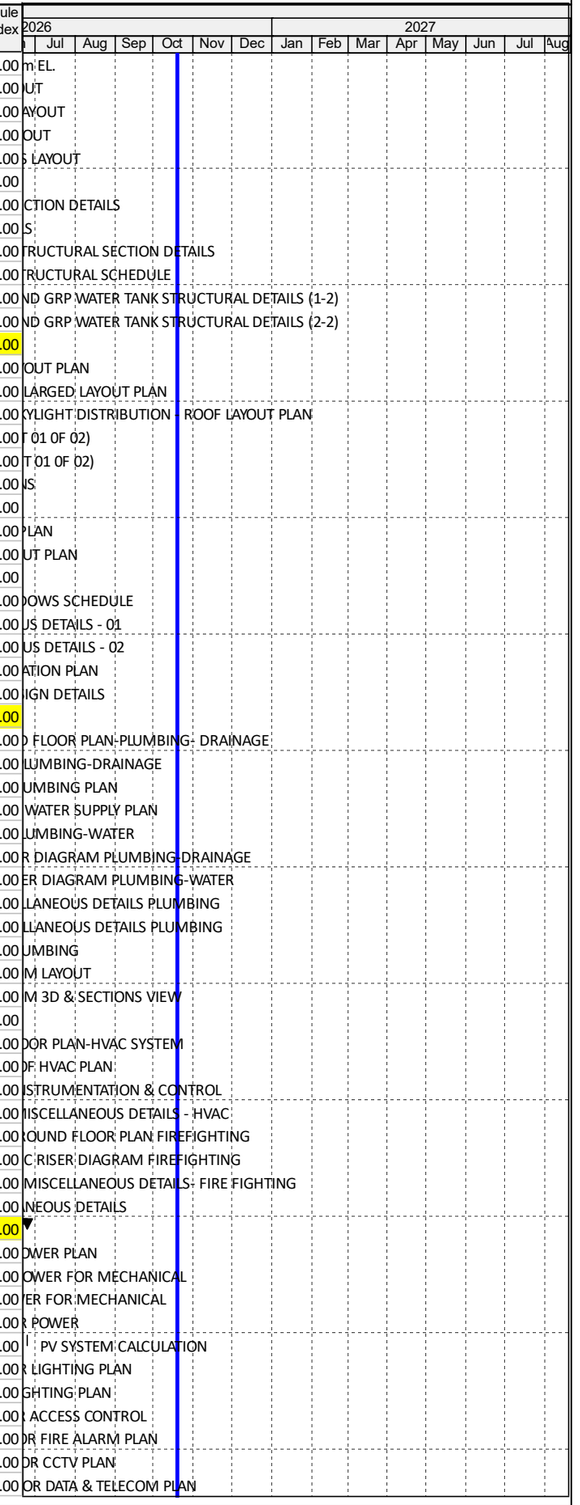





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-SS-E-1050 | GROUND FLOOR GROUNDING PLAN | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1060 | ROOF FLOOR LIGHTENING PLAN | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1070 | POWER RISER DIAGRAM | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1080 | FIRE ALARM RISER DIAGRAM | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1090 | DATA & TELECOME RISER DIAGRAM | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1100 | ACCESS CONTROL RISER DIAGRAM | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1110 | SCHEDULES | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1120 | ELECTRICAL DETAILS | 2 | 0.00 | 20-Apr-26 | 21-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1130 | GROUND FLOOR POWER PLAN | 1 | 0.00 | 22-Apr-26 | 23-Apr-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1140 | POWER FOR MECHANICAL | 2 | 0.00 | 25-Apr-26 | 26-Apr-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1150 | GROUND FLOOR LIGHTING PLAN | 2 | 0.00 | 27-Apr-26 | 28-Apr-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1160 | GROUND FLOOR GROUNDING PLAN | 2 | 0.00 | 29-Apr-26 | 30-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1170 | RISER DIAGRAM | 2 | 0.00 | 02-May-26 | 03-May-26 | 27-Apr-26 | 27-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-E-1180 | ELECTRICAL DETAILS | 2 | 0.00 | 04-May-26 | 05-May-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| **ROAD DRAWINGS** | | 117 | 0.00 | 27-Jan-26 | 29-Mar-26 | 20-Jan-26 | 01-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-730 | GRADING LAYOUT PLAN | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-740 | ROAD LAYOUT PLAN | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-750 | TYPICAL CROSS SECTIONS - KEY PLAN | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-760 | TYPICAL CROSS SECTIONS | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-770 | ROAD PROFILES | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-780 | TOPOGRAPHIC SURVEY-CONTOURS MAP | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 20-Jan-26 | 20-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-790 | ALIGNMENT & CURB SETTING OUT | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-800 | ALIGNMENT & CURB SETTING OUT TABLES | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-810 | ALIGNMNET GEOMETRIC DATA | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-820 | SWEPT PATH LAYOUT PLAN | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-830 | SIGNING & MARKING LAYOUT PLAN | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-840 | ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-850 | ROAD STANDARD DETAILS-TYPICAL CURB DETAILS | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-860 | ROAD STANDARD DETAILS-ROAD SIGN DETAILS | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-870 | ROAD STANDARD DETAILS-ROAD MARKING DETAILS | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-880 | GENERAL SITE PLAN - OVERALL | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 08-Mar-26 | 08-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-890 | SITE SETTING-OUT PLAN - OVERALL | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 08-Mar-26 | 08-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-900 | GENERAL LANDSCAPE LAYOUT | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 08-Mar-26 | 08-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-910 | GENERAL HARDSCAPE LAYOUT | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 08-Mar-26 | 08-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-920 | GENERAL SOFTSCAPE LAYOUT | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 08-Mar-26 | 08-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-930 | PUMP ROOM DETAILS | 1 | 0.00 | 21-Mar-26 | 22-Mar-26 | 14-Mar-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-940 | GENERAL DETAILS | 1 | 0.00 | 23-Mar-26 | 24-Mar-26 | 18-Mar-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-950 | LANDSCAPE DETAILS | 1 | 0.00 | 25-Mar-26 | 26-Mar-26 | 01-Jul-26 | 01-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-R-960 | LANDSCAPE SCHEDULES | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 08-Mar-26 | 08-Mar-26 | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 74 | 0.00 | 01-Mar-26 | 07-May-26 | 10-Feb-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-690 | POTABLE WATER NETWORK | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 11-May-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-700 | FIRE FIGHTING WATER NETWORK | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 11-May-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-710 | POTABLE WATER NETWORK PROFILES | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 11-May-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-720 | FIRE FIGHTING NETWORK PROFILE | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 11-May-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-730 | PIPE TRENCH DETAILS | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-740 | BURIED GATE VALVE DETAILS | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-750 | SINGLE VALVE CHAMBER DETAILS | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-760 | DOUBLE VALVE CHAMBER DETAILS | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-770 | WASHOUT CHAMBER DETAILS | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-780 | AIR RELEASE VALVE CHAMBER DETAILS | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-790 | FLOW METER DETAILS | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 02-Jun-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-800 | FLOW METER REINFORCEMENT DETAILS | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 02-Jun-26 | 02-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-810 | THRUST BLOCK DETAILS (SHEET 1 OF 4) | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-820 | THRUST BLOCK DETAILS (SHEET 2 OF 4) | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-830 | THRUST BLOCK DETAILS (SHEET 3 OF 4) | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-840 | THRUST BLOCK DETAILS (SHEET 4 OF 4) | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-850 | SEWAGE NETWORK | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 14-May-26 | 14-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-860 | SEWAGE NETWORK PROFILES | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 14-May-26 | 14-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-870 | GENERAL NOTES | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-880 | PIPE TRENCHES DETAILS (1) | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-890 | PIPE TRENCHES DETAILS (2) | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-900 | CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A) | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |

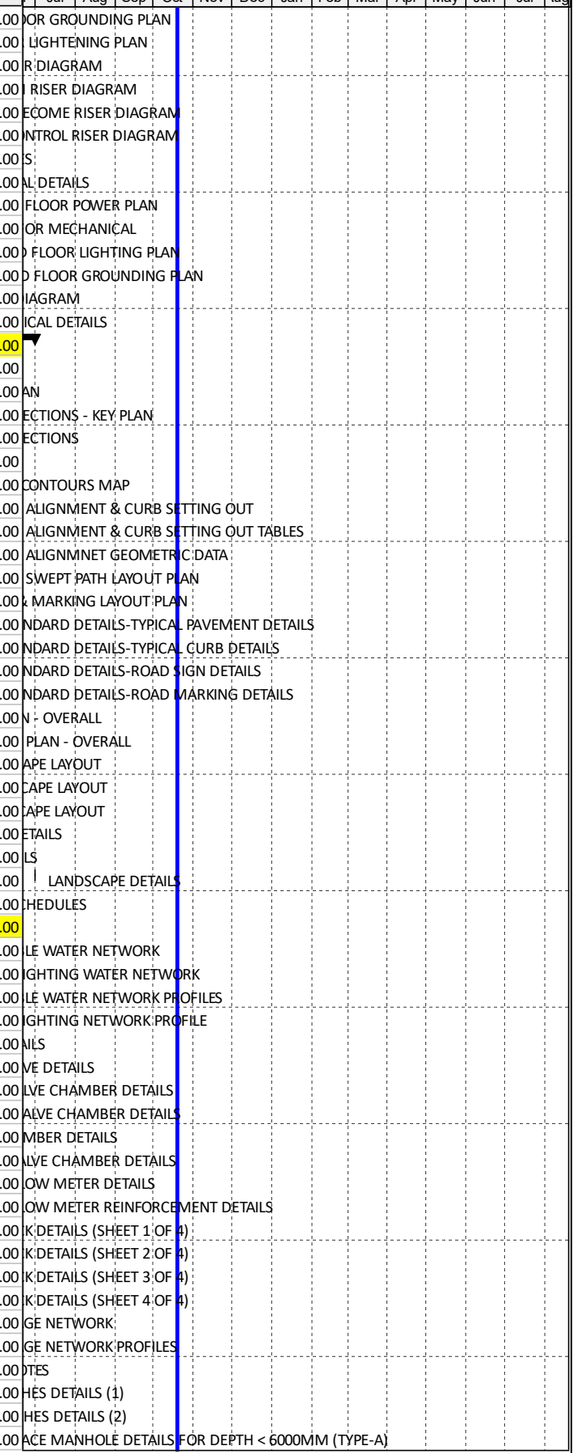





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-SS-EX-910 | CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B) | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 12-Feb-26 | 12-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-920 | BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-930 | BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-940 | PRECAST MANHOLE DETAILS | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 15-Apr-26 | 15-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-950 | IRRIGATION NETWORK LAYOUT SHEET 1 OF 1 | 2 | 0.00 | 20-Apr-26 | 21-Apr-26 | 12-May-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-960 | PIPE TRENCH DETAILS | 2 | 0.00 | 22-Apr-26 | 23-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-970 | BURIED GATE VALVE DETAILS | 2 | 0.00 | 25-Apr-26 | 26-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-980 | SINGLE VALVE CHAMBER DETAILS | 2 | 0.00 | 27-Apr-26 | 28-Apr-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-990 | DOUBLE VALVE CHAMBER DETAILS | 2 | 0.00 | 29-Apr-26 | 30-Apr-26 | 21-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-1000 | WASHOUT CHAMBER DETAILS | 2 | 0.00 | 02-May-26 | 03-May-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-1010 | AIR RELEASE VALVE CHAMBER DETAILS | 2 | 0.00 | 04-May-26 | 05-May-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-1020 | THRUST BLOCK DETAILS (SHEET 1 OF 4) | 2 | 0.00 | 06-May-26 | 07-May-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-1030 | THRUST BLOCK DETAILS (SHEET 2 OF 4) | 2 | 0.00 | 06-May-26 | 07-May-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-1040 | THRUST BLOCK DETAILS (SHEET 3 OF 4) | 2 | 0.00 | 06-May-26 | 07-May-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SS-EX-1050 | THRUST BLOCK DETAILS (SHEET 4 OF 4) | 2 | 0.00 | 06-May-26 | 07-May-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| **REVIEW AND APPROVAL** | | 117 | 0.00 | 29-Jan-26 | 17-May-26 | 20-Jan-26 | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| **STRUCTURAL** | | 87 | 0.00 | 12-Feb-26 | 24-Mar-26 | 03-Feb-26 | 03-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-750 | FOUNDATION LAYOUT | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 18-Feb-26 | 07-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-760 | GRADE BEAM / SLAB ON GRADE LAYOUT | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 21-Apr-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-770 | BASE PLATE LAYOUT | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 07-Feb-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-780 | TIE BEAM @ 4500mm EL. | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 01-Mar-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-790 | ROOF FRAMING LAYOUT | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 07-Feb-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-800 | PURLINS FRAMING LAYOUT | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 07-Feb-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-810 | ROOF SHEETING LAYOUT | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 07-Feb-26 | 17-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-820 | COLUMNS AND AXIS LAYOUT | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 07-Feb-26 | 07-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-830 | SECTIONS | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-840 | EXTERNAL WALL SECTION DETAILS | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-850 | BASE PLATE DETAILS | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-860 | TYPICAL STRUCTURAL SECTION DETAILS | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 21-Apr-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-870 | STRUCTURAL SCHEDULE | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 02-Jun-26 | 03-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-880 | PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2) | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 29-Mar-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-C-890 | PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2) | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 29-Mar-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 75 | 0.00 | 01-Mar-26 | 06-Apr-26 | 03-Feb-26 | 03-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-830 | GROUND FLOOR LAYOUT PLAN | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 03-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-840 | GROUND FLOOR ENLARGED LAYOUT PLAN | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 03-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-850 | SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 02-Jun-26 | 03-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-860 | ELEVATIONS (SHEET 01 0F 02) | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-870 | ELEVATIONS (SHEET 01 0F 02) | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-1170 | BUILDING SECTIONS | 5 | 0.00 | 12-Mar-26 | 21-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-880 | WALL SECTIONS | 2 | 0.00 | 14-Mar-26 | 15-Mar-26 | 03-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-890 | CEILING LAYOUT PLAN | 2 | 0.00 | 16-Mar-26 | 21-Mar-26 | 05-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-900 | FINISHING LAYOUT PLAN | 2 | 0.00 | 22-Mar-26 | 23-Mar-26 | 09-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-910 | TOILET DETAILS | 2 | 0.00 | 24-Mar-26 | 25-Mar-26 | 11-Feb-26 | 25-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-920 | DOORS & WINDOWS SCHEDULE | 2 | 0.00 | 26-Mar-26 | 28-Mar-26 | 11-Feb-26 | 25-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-930 | MISCELLANEOUS DETAILS - 01 | 2 | 0.00 | 29-Mar-26 | 30-Mar-26 | 11-Feb-26 | 25-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-940 | MISCELLANEOUS DETAILS - 02 | 2 | 0.00 | 31-Mar-26 | 01-Apr-26 | 11-Feb-26 | 25-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-950 | SIGNAGE LOCATION PLAN | 2 | 0.00 | 02-Apr-26 | 04-Apr-26 | 11-Feb-26 | 25-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-A-960 | SIGNAGE DESIGN DETAILS | 2 | 0.00 | 05-Apr-26 | 06-Apr-26 | 11-Feb-26 | 25-Feb-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 51 | 0.00 | 05-Mar-26 | 26-Apr-26 | 04-Feb-26 | 09-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-600 | TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 17-Mar-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-610 | TOILETS DETAILS PLUMBING-DRAINAGE | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 11-Mar-26 | 10-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-620 | TYPICAL ROOF PLUMBING PLAN | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 16-Mar-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-630 | GROUND FLOOR WATER SUPPLY PLAN | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 17-Mar-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-640 | TOILET DETAILS PLUMBING-WATER | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 11-Mar-26 | 10-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-650 | SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 04-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-660 | SCHEMATIC RISER DIAGRAM PLUMBING-WATER | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 04-Feb-26 | 13-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-670 | GENERAL MISELLANEOUS DETAILS PLUMBING | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 04-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-680 | GENERAL MISELLANEOUS DETAILS PLUMBING | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 04-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-690 | SCHEDULE- PLUMBING | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 17-Mar-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-700 | PUMP ROOM LAYOUT | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 16-Apr-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-710 | PUMP ROOM 3D & SECTIONS VIEW | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 21-Apr-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-720 | SCHEDULES | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 17-Mar-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |

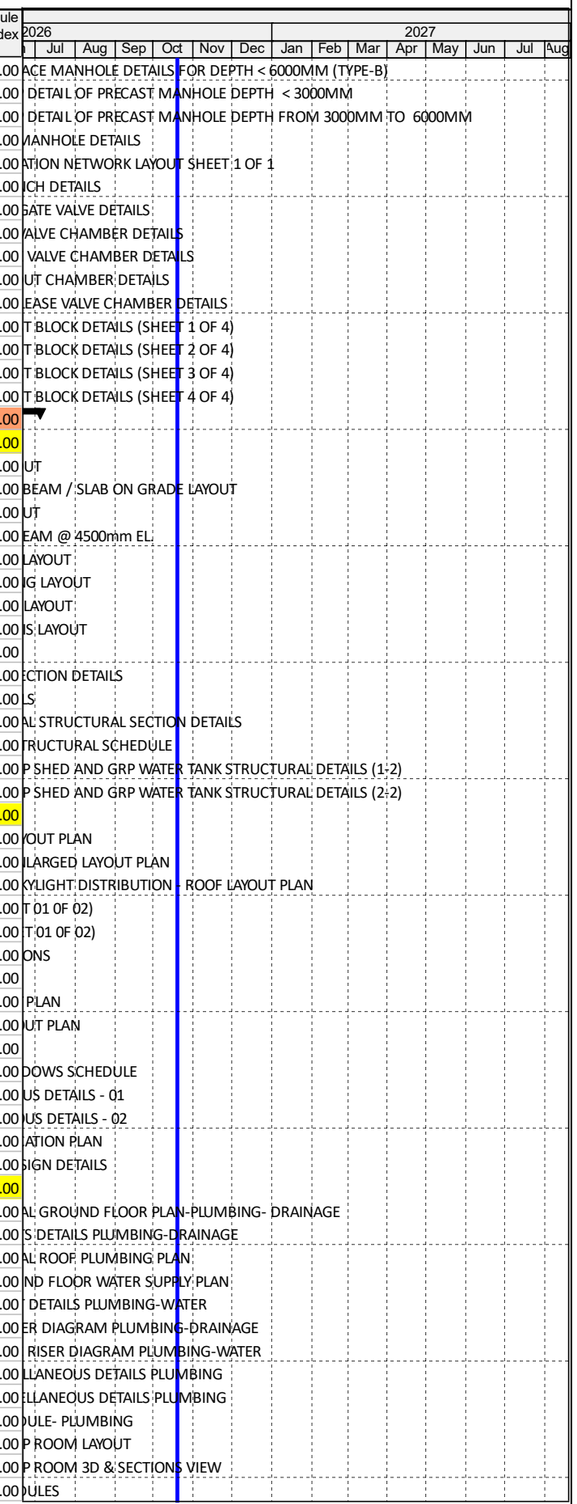




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-SA-M-730 | GROUND FLOOR PLAN-HVAC SYSTEM | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 26-Mar-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-740 | TYPICAL ROOF HVAC PLAN | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 26-Mar-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-750 | GENERAL-INSTRUMENTATION & CONTROL | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 04-Feb-26 | 09-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-760 | GENERAL MISCELLANEOUS DETAILS - HVAC | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 05-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-770 | TYPICAL GROUND FLOOR PLAN FIREFIGHTING | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 14-Mar-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-780 | SCHEMATIC RISER DIAGRAM FIREFIGHTING | 2 | 0.00 | 20-Apr-26 | 21-Apr-26 | 04-Feb-26 | 09-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-790 | GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING | 2 | 0.00 | 22-Apr-26 | 23-Apr-26 | 04-Feb-26 | 09-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-M-800 | MISCELLANEOUS DETAILS | 2 | 0.00 | 25-Apr-26 | 26-Apr-26 | 04-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 99 | 0.00 | 08-Mar-26 | 07-May-26 | 09-Feb-26 | 28-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-940 | GROUND FLOOR POWER PLAN | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 09-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-950 | GROUND FLOOR POWER FOR MECHANICAL | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 09-Feb-26 | 18-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-960 | ROOF FLOOR POWER FOR MECHANICAL | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 09-Feb-26 | 15-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-970 | ROOF FLOOR POWER | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 08-Apr-26 | 09-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-980 | PV SYSTEM CALCULATION | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 25-Jun-26 | 28-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-990 | GROUND FLOOR LIGHTING PLAN | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 09-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1000 | ROOF FLOOR LIGHTING PLAN | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 09-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1010 | GOUND FLOOR ACCESS CONTROL | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 29-Mar-26 | 18-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1020 | GROUND FLOOR FIRE ALARM PLAN | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 29-Mar-26 | 15-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1030 | GROUND FLOOR CCTV PLAN | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 01-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1040 | GROUND FLOOR DATA & TELECOM PLAN | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 01-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1050 | GROUND FLOOR GROUNDING PLAN | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 01-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1060 | ROOF FLOOR LIGHTENING PLAN | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 09-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1070 | POWER RISER DIAGRAM | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 29-Mar-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1080 | FIRE ALARM RISER DIAGRAM | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 29-Mar-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1090 | DATA & TELECOME RISER DIAGRAM | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 29-Mar-26 | 30-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1100 | ACCESS CONTROL RISER DIAGRAM | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 29-Mar-26 | 30-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1110 | SCHEDULES | 2 | 0.00 | 20-Apr-26 | 21-Apr-26 | 29-Mar-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1120 | ELECTRICAL DETAILS | 2 | 0.00 | 22-Apr-26 | 23-Apr-26 | 01-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1130 | GROUND FLOOR POWER PLAN | 2 | 0.00 | 25-Apr-26 | 26-Apr-26 | 09-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1140 | POWER FOR MECHANICAL | 2 | 0.00 | 27-Apr-26 | 28-Apr-26 | 09-Feb-26 | 18-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1150 | GROUND FLOOR LIGHTING PLAN | 2 | 0.00 | 29-Apr-26 | 30-Apr-26 | 09-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1160 | GROUND FLOOR GROUNDING PLAN | 2 | 0.00 | 02-May-26 | 03-May-26 | 01-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1170 | RISER DIAGRAM | 2 | 0.00 | 04-May-26 | 05-May-26 | 27-Apr-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-E-1180 | ELECTRICAL DETAILS | 2 | 0.00 | 06-May-26 | 07-May-26 | 01-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| **ROAD DRAWINGS** | | 117 | 0.00 | 29-Jan-26 | 31-Mar-26 | 20-Jan-26 | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-730 | GRADING LAYOUT PLAN | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 03-Feb-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-740 | ROAD LAYOUT PLAN | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 16-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-750 | TYPICAL CROSS SECTIONS - KEY PLAN | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 16-Mar-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-760 | TYPICAL CROSS SECTIONS | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 16-Mar-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-770 | ROAD PROFILES | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 16-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-780 | TOPOGRAPHIC SURVEY-CONTOURS MAP | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 20-Jan-26 | 22-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-790 | ALIGNMENT & CURB SETTING OUT | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-800 | ALIGNMENT & CURB SETTING OUT TABLES | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-810 | ALIGNMINET GEOMETRIC DATA | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-820 | SWEPT PATH LAYOUT PLAN | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 14-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-830 | SIGNING & MARKING LAYOUT PLAN | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 21-Apr-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-840 | ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 21-Apr-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-850 | ROAD STANDARD DETAILS-TYPICAL CURB DETAILS | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 21-Apr-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-860 | ROAD STANDARD DETAILS-ROAD SIGN DETAILS | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 21-Apr-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-870 | ROAD STANDARD DETAILS-ROAD MARKING DETAILS | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 21-Apr-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-880 | GENERAL SITE PLAN - OVERALL | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 08-Mar-26 | 20-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-890 | SITE SETTING-OUT PLAN - OVERALL | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 08-Mar-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-900 | GENERAL LANDSCAPE LAYOUT | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 08-Mar-26 | 06-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-910 | GENERAL HARDSCAPE LAYOUT | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 08-Mar-26 | 07-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-920 | GENERAL SOFTSCAPE LAYOUT | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 08-Mar-26 | 09-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-930 | PUMP ROOM DETAILS | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 14-Mar-26 | 06-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-940 | GENERAL DETAILS | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 18-Mar-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-950 | LANDSCAPE DETAILS | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 01-Jul-26 | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-R-960 | LANDSCAPE SCHEDULES | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 08-Mar-26 | 06-May-26 | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 78 | 0.00 | 03-Mar-26 | 17-May-26 | 10-Feb-26 | 08-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-690 | POTABLE WATER NETWORK | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 11-May-26 | 01-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-700 | FIRE FIGHTING WATER NETWORK | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 11-May-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |

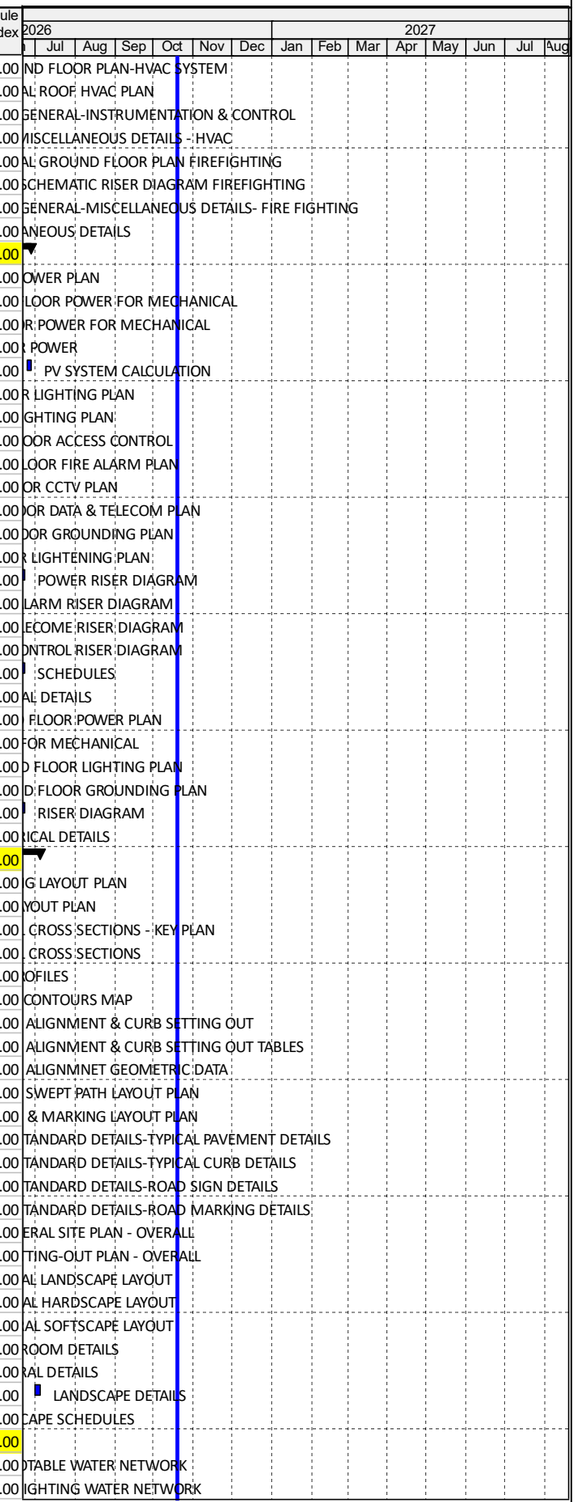





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-SA-EX-710 | POTABLE WATER NETWORK PROFILES | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 11-May-26 | 25-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-720 | FIRE FIGHTING NETWORK PROFILE | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 11-May-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-730 | PIPE TRENCH DETAILS | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 10-Feb-26 | 10-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-740 | BURIED GATE VALVE DETAILS | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 10-Feb-26 | 31-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-750 | SINGLE VALVE CHAMBER DETAILS | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 21-Apr-26 | 27-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-760 | DOUBLE VALVE CHAMBER DETAILS | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 21-Apr-26 | 27-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-770 | WASHOUT CHAMBER DETAILS | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 10-Feb-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-780 | AIR RELEASE VALVE CHAMBER DETAILS | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 10-Feb-26 | 25-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-790 | FLOW METER DETAILS | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 02-Jun-26 | 03-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-800 | FLOW METER REINFORCEMENT DETAILS | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 02-Jun-26 | 03-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-830 | THRUST BLOCK DETAILS (SHEET 3 OF 4) | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-840 | THRUST BLOCK DETAILS (SHEET 4 OF 4) | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-810 | THRUST BLOCK DETAILS (SHEET 1 OF 4) | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-850 | SEWAGE NETWORK | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 14-May-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-820 | THRUST BLOCK DETAILS (SHEET 2 OF 4) | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-860 | SEWAGE NETWORK PROFILES | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 14-May-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-870 | GENERAL NOTES | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-880 | PIPE TRENCHES DETAILS (1) | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-890 | PIPE TRENCHES DETAILS (2) | 2 | 0.00 | 15-Apr-26 | 16-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-900 | CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A) | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 10-Feb-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-910 | CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B) | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 12-Feb-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-920 | BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 10-Feb-26 | 19-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-930 | BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM | 2 | 0.00 | 18-Apr-26 | 19-Apr-26 | 10-Feb-26 | 19-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-940 | PRECAST MANHOLE DETAILS | 2 | 0.00 | 20-Apr-26 | 21-Apr-26 | 15-Apr-26 | 08-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-950 | IRRIGATION NETWORK LAYOUT SHEET 1 OF 1 | 2 | 0.00 | 22-Apr-26 | 23-Apr-26 | 12-May-26 | 17-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-960 | PIPE TRENCH DETAILS | 2 | 0.00 | 25-Apr-26 | 26-Apr-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-970 | BURIED GATE VALVE DETAILS | 2 | 0.00 | 27-Apr-26 | 28-Apr-26 | 10-Feb-26 | 31-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-980 | SINGLE VALVE CHAMBER DETAILS | 2 | 0.00 | 29-Apr-26 | 30-Apr-26 | 21-Apr-26 | 27-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-990 | DOUBLE VALVE CHAMBER DETAILS | 2 | 0.00 | 02-May-26 | 03-May-26 | 21-Apr-26 | 27-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-1000 | WASHOUT CHAMBER DETAILS | 2 | 0.00 | 04-May-26 | 05-May-26 | 10-Feb-26 | 11-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-1010 | AIR RELEASE VALVE CHAMBER DETAILS | 2 | 0.00 | 06-May-26 | 07-May-26 | 10-Feb-26 | 25-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-1020 | THRUST BLOCK DETAILS (SHEET 1 OF 4) | 2 | 0.00 | 09-May-26 | 10-May-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-1030 | THRUST BLOCK DETAILS (SHEET 2 OF 4) | 2 | 0.00 | 11-May-26 | 12-May-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-1040 | THRUST BLOCK DETAILS (SHEET 3 OF 4) | 2 | 0.00 | 13-May-26 | 14-May-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-SA-EX-1050 | THRUST BLOCK DETAILS (SHEET 4 OF 4) | 2 | 0.00 | 16-May-26 | 17-May-26 | 10-Feb-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| **PRE QUALIFACTION FOR MATERIALS** | | 138 | 0.00 | 22-Jan-26 | 12-Apr-26 | 15-Jan-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| **PREPARATION AND SUBMITTAL** | | 108 | 0.00 | 22-Jan-26 | 09-Apr-26 | 15-Jan-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| **STRUCTURAL** | | 10 | 0.00 | 22-Jan-26 | 02-Feb-26 | 15-Jan-26 | 19-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-C-0010 | Anti termite | 2 | 0.00 | 22-Jan-26 | 24-Jan-26 | 15-Jan-26 | 15-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-C-0020 | Concrete mix | 2 | 0.00 | 25-Jan-26 | 26-Jan-26 | 15-Jan-26 | 15-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-C-0030 | Polyethylene sheet | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 19-Jan-26 | 19-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-C-0040 | Bitumen paint | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 15-Jan-26 | 15-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-C-0050 | Rebar | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 15-Jan-26 | 15-Jan-26 | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 100 | 0.00 | 25-Jan-26 | 02-Mar-26 | 08-Feb-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0020 | PES -Steel Structure | 2 | 0.00 | 25-Jan-26 | 26-Jan-26 | 19-Feb-26 | 23-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0040 | Concrete masonry unit (CMU) | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0050 | Steel ladder | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 25-Feb-26 | 28-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0060 | Steel gratings | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 19-May-26 | 19-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0070 | Steel rails | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0120 | Doors | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0130 | Windows | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0140 | Ceramic tiles | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 25-Mar-26 | 25-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0150 | Granite strip | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 03-May-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0170 | Epoxy paint | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 20-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0180 | Internl paint | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 25-Mar-26 | 25-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0190 | Gypsum board | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 24-Feb-26 | 24-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0200 | Aluminum Composite Panel | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0230 | Steel fence and gates | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 20-May-26 | 20-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-A-0240 | Identification sign; ID01 & ID02 | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 98 | 0.00 | 27-Jan-26 | 09-Apr-26 | 24-Jan-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0010 | Seamless black steel or ERW pipes | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0030 | PPR pipes | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |

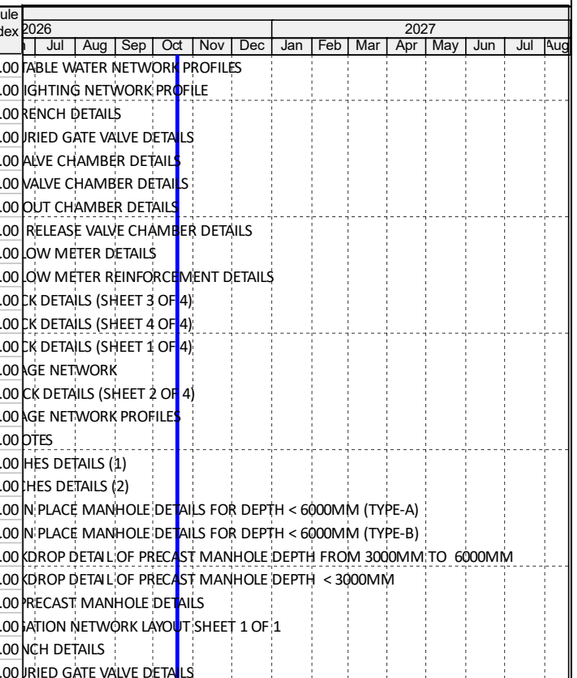





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-PS-M-0040 | HVAC duct | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0050 | Flexible duct | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0060 | Exhaust diffuser | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 27-May-26 | 27-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0070 | U/G HDPE pipes | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0080 | Warning tapes | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 14-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0090 | Fire hose cabinet | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0100 | Automatic air release valve | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0110 | OS & Y gate valve | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0120 | Fire alarm check valve | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0140 | Ball valve | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 11-Feb-26 | 12-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0150 | Capped connection | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0160 | UPVC pipes | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 04-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0170 | Roof vent caps | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0180 | Floor drain | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0190 | Gully trap | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0200 | Electric water heater | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0210 | Western water closet | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0220 | Bib tap | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 04-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0230 | Toilet Fittings | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0240 | Lavatory / wash basin | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0250 | Inline exhaust fans | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 02-Feb-26 | 02-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0260 | Wall propeller type exhaust fans | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 02-Feb-26 | 02-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0270 | Fire pumps | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0280 | Fire fighting valves | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 02-Feb-26 | 02-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0320 | Booster pump | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 03-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0330 | GRP tank | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 24-Jan-26 | 28-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0340 | Water supply valves | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 02-Feb-26 | 02-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-M-0350 | Water tap | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 85 | 0.00 | 29-Jan-26 | 05-Apr-26 | 07-Feb-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0010 | PVC conduits | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0020 | Wires | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 14-Mar-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0030 | Cable Tray | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0040 | Grounding system | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 14-Mar-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0050 | Wiring devices | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0060 | HDPE ducts | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 20-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0070 | Low Voltage cables | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 14-Mar-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0080 | Main distribution board (MDB) | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 19-Apr-26 | 19-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0090 | Lighting panel board | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 19-Apr-26 | 19-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0100 | PP-AC panel | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 19-Apr-26 | 19-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0110 | Disconnect switches | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 25-Mar-26 | 25-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0120 | Suspended High Bay LED lights | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0130 | Flood lights | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0140 | Recessed mounted LED downlight | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0150 | LED Emergency Lights wall mounted | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0160 | LED Emergency Exit Light | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0170 | Wall mounted, duplex, telephone and data outlet | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0180 | Fire alarm system | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0200 | Street Lighting poles | 1 | 0.00 | 15-Mar-26 | 16-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0210 | Distribution board for pump room | 1 | 0.00 | 21-Mar-26 | 22-Mar-26 | 19-Apr-26 | 19-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0220 | Surface mounted lights | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0230 | CCTV System | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0240 | Access control system | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0250 | Solar system | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 24-Feb-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0260 | Main program system & controller | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 20-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-E-0270 | PLC controller | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 20-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 14 | 0.00 | 25-Mar-26 | 09-Apr-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EX-0010 | Asphalt works | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EX-0020 | Concrete parking bumper | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EX-0030 | Road markings | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EX-0040 | Road signs | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EX-0060 | Interlock tiles | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EX-0070 | Curbstones | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |

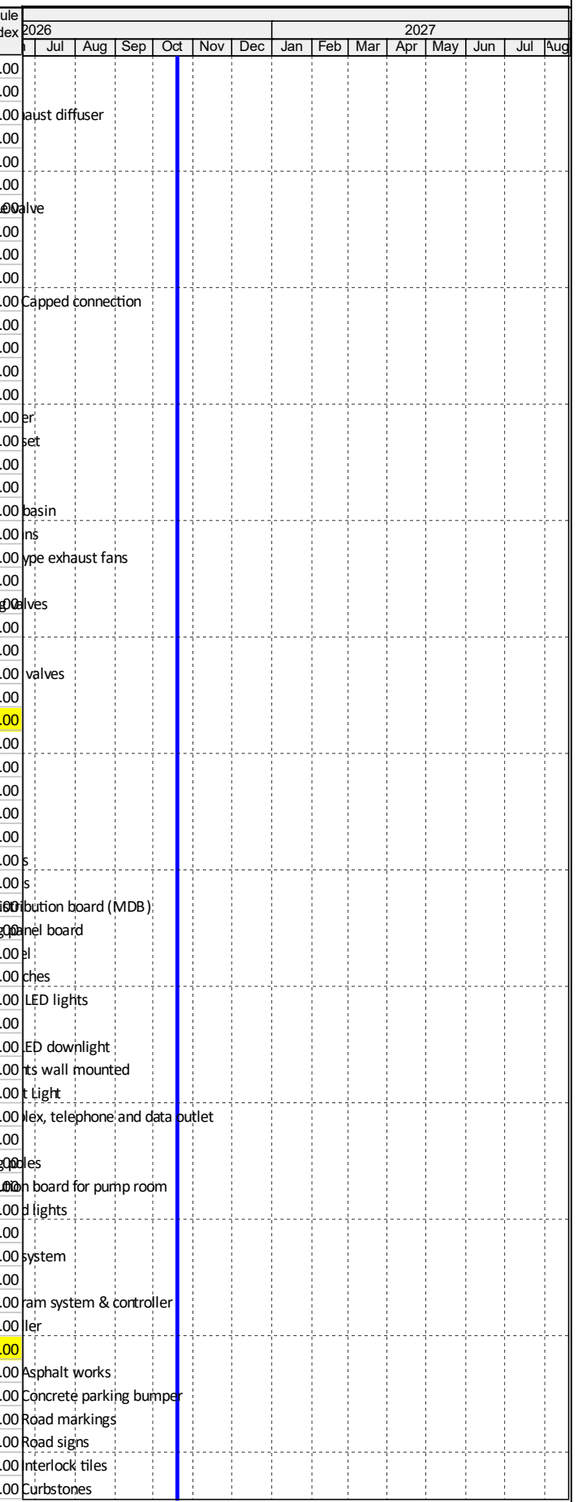




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-PS-EX-0080 | Gravel bedding | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 10-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| **ENVIRONMETAL** | | 75 | 0.00 | 29-Jan-26 | 16-Feb-26 | 03-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0010 | HDPE pipes for fire system | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0020 | Directly buried gate valve for fire system | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 14-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0030 | HDPE pipes for water supply system | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0040 | Directly buried gate valve for water system | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 14-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0050 | Air valve | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0060 | Washout valve | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0070 | Gate valve | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PS-EN-0080 | UPVC pipes | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 03-Feb-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| **REVIEW AND APPROVAL** | | 138 | 0.00 | 25-Jan-26 | 12-Apr-26 | 15-Jan-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| **STRUCTURAL** | | 34 | 0.00 | 25-Jan-26 | 04-Feb-26 | 15-Jan-26 | 21-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-C-0010 | Anti termite | 2 | 0.00 | 25-Jan-26 | 26-Jan-26 | 15-Jan-26 | 20-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-C-0020 | Concrete mix | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 15-Jan-26 | 20-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-C-0030 | Polyethylene sheet | 5 | 0.00 | 29-Jan-26 | 31-Jan-26 | 19-Jan-26 | 21-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-C-0040 | Bitumen paint | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 15-Jan-26 | 20-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-C-0050 | Rebar | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 15-Jan-26 | 20-Jan-26 | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 104 | 0.00 | 27-Jan-26 | 04-Mar-26 | 08-Feb-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0020 | PES -Steel Structure | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 17-Feb-26 | 19-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0040 | Concrete masonry unit (CMU) | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 08-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0050 | Steel ladder | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 17-Feb-26 | 19-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0060 | Steel gratings | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 19-May-26 | 20-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0070 | Steel rails | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 10-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0120 | Doors | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 16-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0130 | Windows | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 08-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0140 | Ceramic tiles | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 25-Mar-26 | 26-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0150 | Granite strip | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 03-May-26 | 04-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0170 | Epoxy paint | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 20-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0180 | Internl paint | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 25-Mar-26 | 26-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0190 | Gypsum board | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 24-Feb-26 | 12-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0200 | Aluminum Composite Panel | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 09-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0230 | Steel fence and gates | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 20-May-26 | 21-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-A-0240 | Identification sign; ID01 & ID02 | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 10-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 98 | 0.00 | 29-Jan-26 | 12-Apr-26 | 24-Jan-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0010 | Seamless black steel or ERW pipes | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 08-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0030 | PPR pipes | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 03-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0040 | HVAC duct | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 09-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0050 | Flexible duct | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 09-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0060 | Exhaust diffuser | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 27-May-26 | 28-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0070 | U/G HDPE pipes | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 04-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0080 | Warning tapes | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 14-Feb-26 | 15-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0090 | Fire hose cabinet | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 04-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0100 | Automatic air release valve | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 08-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0110 | OS & Y gate valve | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 08-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0120 | Fire alarm check valve | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 08-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0140 | Ball valve | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0150 | Capped connection | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 10-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0160 | UPVC pipes | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 04-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0170 | Roof vent caps | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 16-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0180 | Floor drain | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 16-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0190 | Gully trap | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 07-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0200 | Electric water heater | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 05-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0210 | Western water closet | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 05-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0220 | Bib tap | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 06-Apr-26 | 07-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0230 | Toilet Fittings | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 07-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0240 | Lavatory / wash basin | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 05-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0250 | Inline exhaust fans | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 02-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0260 | Wall propeller type exhaust fans | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 02-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0270 | Fire pumps | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 03-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0280 | Fire fighting valves | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 02-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0330 | Booster pump | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 03-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0340 | GRP tank | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 24-Jan-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |

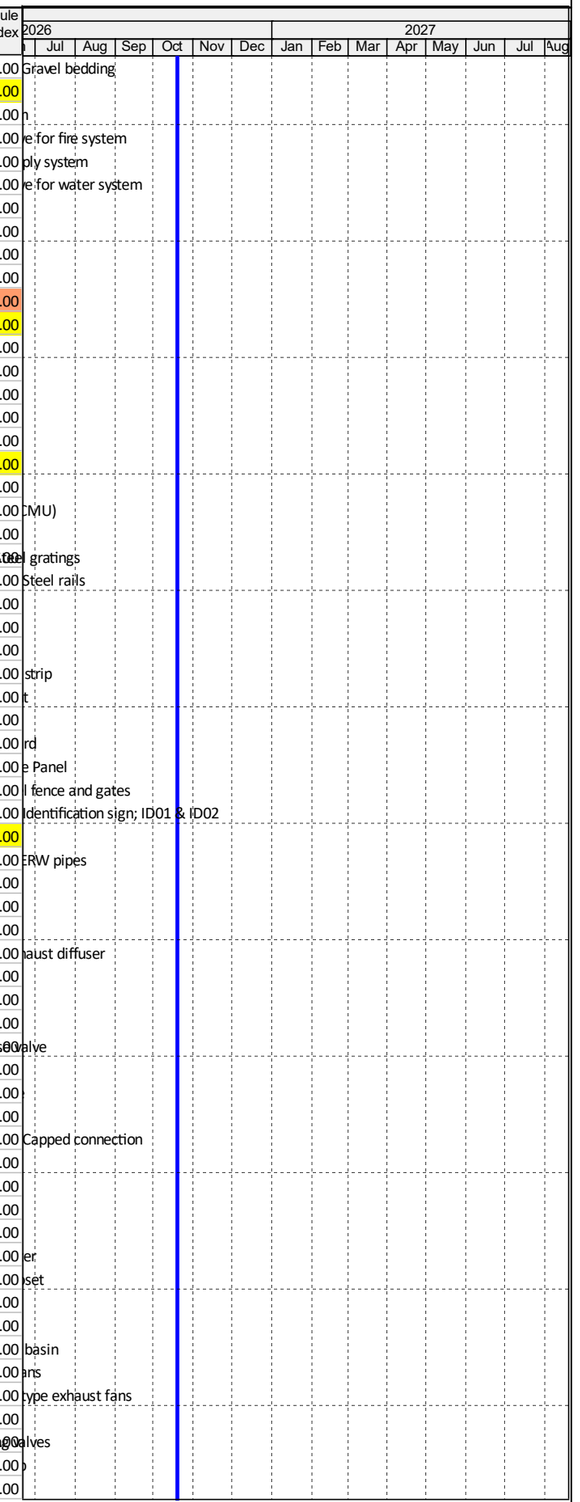




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-PA-M-0350 | Water supply valves | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 02-Feb-26 | 03-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-M-0320 | Water tap | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 11-Feb-26 | 12-Feb-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 85 | 0.00 | 01-Feb-26 | 07-Apr-26 | 07-Feb-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0010 | PVC conduits | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 07-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0020 | Wires | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 14-Mar-26 | 15-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0030 | Cable Tray | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 03-Mar-26 | 04-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0040 | Grounding system | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 14-Mar-26 | 15-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0050 | Wiring devices | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 03-Mar-26 | 04-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0060 | HDPE ducts | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 20-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0070 | Low Voltage cables | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 14-Mar-26 | 15-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0080 | Main distribution board (MDB) | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 19-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0090 | Lighting panel board | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 19-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0100 | PP-AC panel | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 19-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0110 | Disconnect switches | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 25-Mar-26 | 26-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0120 | Suspended High Bay LED lights | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0130 | Flood lights | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0140 | Recessed mounted LED downlight | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0150 | LED Emergency Lights wall mounted | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0160 | LED Emergency Exit Light | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0170 | Wall mounted, duplex, telephone and data outlet | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 11-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0180 | Fire alarm system | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 09-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0200 | Street Lighting poles | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0210 | Distribution board for pump room | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 19-Apr-26 | 20-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0220 | Surface mounted lights | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 01-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0230 | CCTV System | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 11-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0240 | Access control system | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 09-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0250 | Solar system | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 24-Feb-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0260 | Main program system & controller | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 20-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-E-0270 | PLC controller | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 20-Apr-26 | 21-Apr-26 | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 14 | 0.00 | 28-Mar-26 | 12-Apr-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0010 | Asphalt works | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0020 | Concrete parking bumper | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0030 | Road markings | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0040 | Road signs | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0060 | Interlock tiles | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0070 | Curbstones | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EX-0080 | Gravel bedding | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 09-Jun-26 | 10-Jun-26 | 0.00 | 0.00 | 0.00 |
| **ENVIRONMETAL** | | 73 | 0.00 | 01-Feb-26 | 19-Feb-26 | 03-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0010 | HDPE pipes for fire system | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 05-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0020 | Directly buried gate valve for fire system | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 14-Feb-26 | 15-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0030 | HDPE pipes for water supply system | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 05-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0040 | Directly buried gate valve for water system | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 14-Feb-26 | 15-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0050 | Air valve | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 16-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0060 | Washout valve | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 16-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0070 | Gate valve | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 16-Feb-26 | 17-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PA-EN-0080 | UPVC pipes | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 03-Feb-26 | 04-Feb-26 | 0.00 | 0.00 | 0.00 |
| **MATERIAL SUBMITTAL** | | 108 | 2,879,895.75 | 27-Jan-26 | 20-Apr-26 | 15-Jan-26 | 14-Jun-26 | 2,879,895.75 | 2,879,895.75 | 1.00 |
| **PREPARATION AND SUBMITTAL** | | 108 | 0.00 | 27-Jan-26 | 14-Apr-26 | 15-Jan-26 | 13-Jun-26 | 0.00 | 0.00 | 0.00 |
| **STRUCTURAL** | | 10 | 0.00 | 27-Jan-26 | 07-Feb-26 | 15-Jan-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-C-0010 | Anti termite | 2 | 0.00 | 27-Jan-26 | 28-Jan-26 | 14-Mar-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-C-0020 | Concrete mix | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 15-Jan-26 | 15-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-C-0030 | Polyethylene sheet | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 22-Jan-26 | 22-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-C-0040 | Bitumen paint | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 22-Jan-26 | 22-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-C-0050 | Rebar | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 22-Jan-26 | 22-Jan-26 | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 100 | 0.00 | 29-Jan-26 | 07-Mar-26 | 07-Feb-26 | 13-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-1700 | PES -Steel Structure | 2 | 0.00 | 29-Jan-26 | 31-Jan-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0020 | Concrete masonry unit (CMU) | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0030 | Steel ladder | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0040 | Steel gratings | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 21-May-26 | 21-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0050 | Steel rails | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 13-Jun-26 | 13-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0100 | Doors | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 19-Feb-26 | 19-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0110 | Windows | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 19-Feb-26 | 19-Feb-26 | 0.00 | 0.00 | 0.00 |

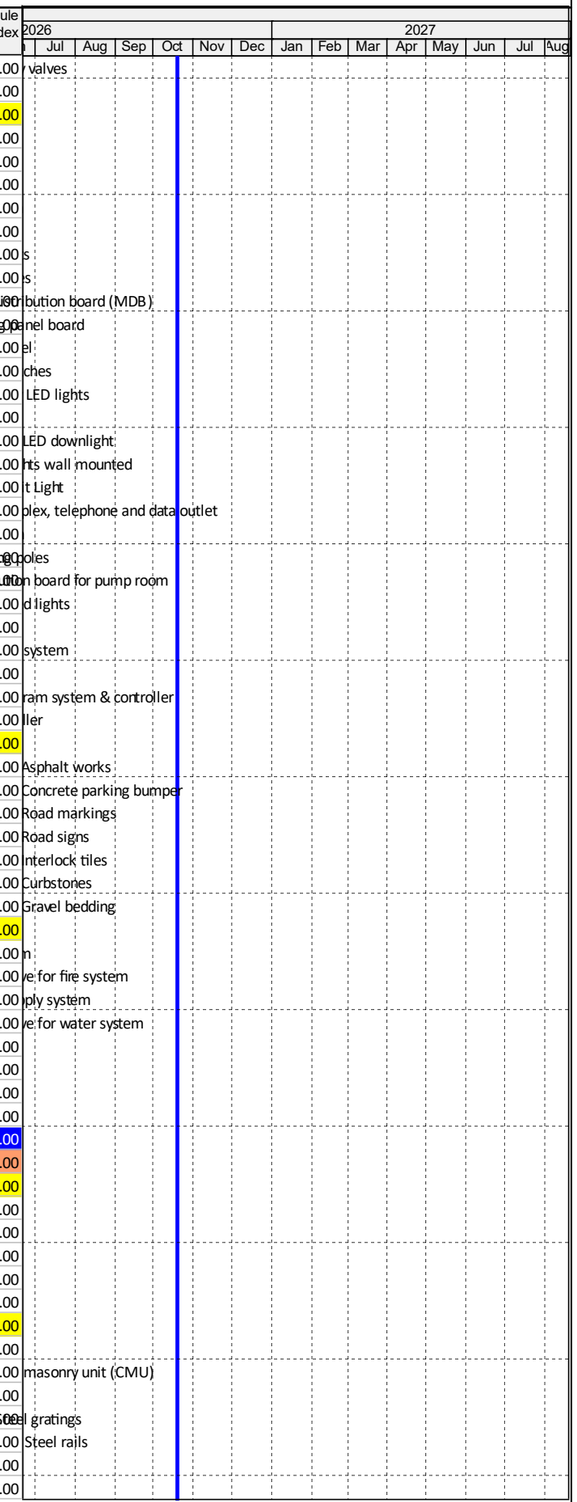





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-MS-A-0120 | Ceramic tiles | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 30-Mar-26 | 30-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0130 | Granite strip | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 09-May-26 | 09-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0150 | Epoxy paint | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 29-Apr-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0160 | Internl paint | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-0170 | Gypsum board | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 19-Apr-26 | 19-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-1720 | Aluminum Composite Panel | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 19-Feb-26 | 19-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-1750 | Steel fence and gates | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 23-May-26 | 23-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-A-1760 | Identification sign; ID01 & ID02 | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 13-Jun-26 | 13-Jun-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 98 | 0.00 | 01-Feb-26 | 14-Apr-26 | 05-Feb-26 | 13-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0020 | Seamless black steel or ERW pipes | 2 | 0.00 | 01-Feb-26 | 02-Feb-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0080 | PPR pipes | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0220 | HVAC duct | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 04-Mar-26 | 04-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0230 | Flexible duct | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 04-Mar-26 | 04-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0240 | Exhaust diffuser | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 01-Jun-26 | 01-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0010 | U/G HDPE pipes | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0340 | Warning tapes | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0030 | Fire hose cabinet | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0040 | Automatic air release valve | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0050 | OS & Y gate valve | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0060 | Fire alarm check valve | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0090 | Ball valve | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 14-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0100 | Capped connection | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 13-Jun-26 | 13-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0110 | UPVC pipes | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 07-Feb-26 | 07-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0120 | Roof vent caps | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0130 | Floor drain | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0140 | Gully trap | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0150 | Electric water heater | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0160 | Western water closet | 2 | 0.00 | 15-Mar-26 | 16-Mar-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0170 | Bib tap | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 14-Feb-26 | 14-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0180 | Toilet Fittings | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0190 | Lavatory / wash basin | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0200 | Inline exhaust fans | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 18-Mar-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0210 | Wall propeller type exhaust fans | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 18-Mar-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0250 | Fire pumps | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0270 | Fire fighting valves | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0310 | Booster pump | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 05-Feb-26 | 05-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0320 | GRP tank | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 02-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-0330 | Water supply valves | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 10-Feb-26 | 10-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-M-3410 | Water tap | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 14-Feb-26 | 14-Feb-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 69 | 0.00 | 03-Feb-26 | 09-Apr-26 | 09-Feb-26 | 30-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0040 | PVC conduits | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 09-Feb-26 | 09-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0050 | Wires | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-210 | Cable Tray | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 07-Mar-26 | 07-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0120 | Grounding system | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0140 | Wiring devices | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 07-Mar-26 | 07-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0160 | HDPE ducts | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 30-Apr-26 | 30-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0010 | Low Voltage cables | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 16-Mar-26 | 16-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0020 | Main distribution board (MDB) | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-190 | Lighting panel board | 2 | 0.00 | 23-Feb-26 | 25-Feb-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-200 | PP-AC panel | 2 | 0.00 | 25-Feb-26 | 28-Feb-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0030 | Disconnect switches | 2 | 0.00 | 01-Mar-26 | 02-Mar-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0060 | Suspended High Bay LED lights | 2 | 0.00 | 03-Mar-26 | 04-Mar-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0070 | Flood lights | 2 | 0.00 | 05-Mar-26 | 07-Mar-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0080 | Recessed mounted LED downlight | 2 | 0.00 | 08-Mar-26 | 09-Mar-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0090 | LED Emergency Lights wall mounted | 2 | 0.00 | 10-Mar-26 | 11-Mar-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0100 | LED Emergency Exit Light | 2 | 0.00 | 12-Mar-26 | 14-Mar-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0110 | Wall mounted, duplex, telephone and data outlet | 1 | 0.00 | 15-Mar-26 | 16-Mar-26 | 29-Mar-26 | 29-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0130 | Fire alarm system | 2 | 0.00 | 21-Mar-26 | 22-Mar-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0170 | Street Lighting poles | 2 | 0.00 | 23-Mar-26 | 24-Mar-26 | 04-Mar-26 | 04-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0180 | Distribution board for pump room | 2 | 0.00 | 25-Mar-26 | 26-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0190 | Surface mounted lights | 2 | 0.00 | 28-Mar-26 | 29-Mar-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0230 | CCTV System | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 28-Mar-26 | 28-Mar-26 | 0.00 | 0.00 | 0.00 |

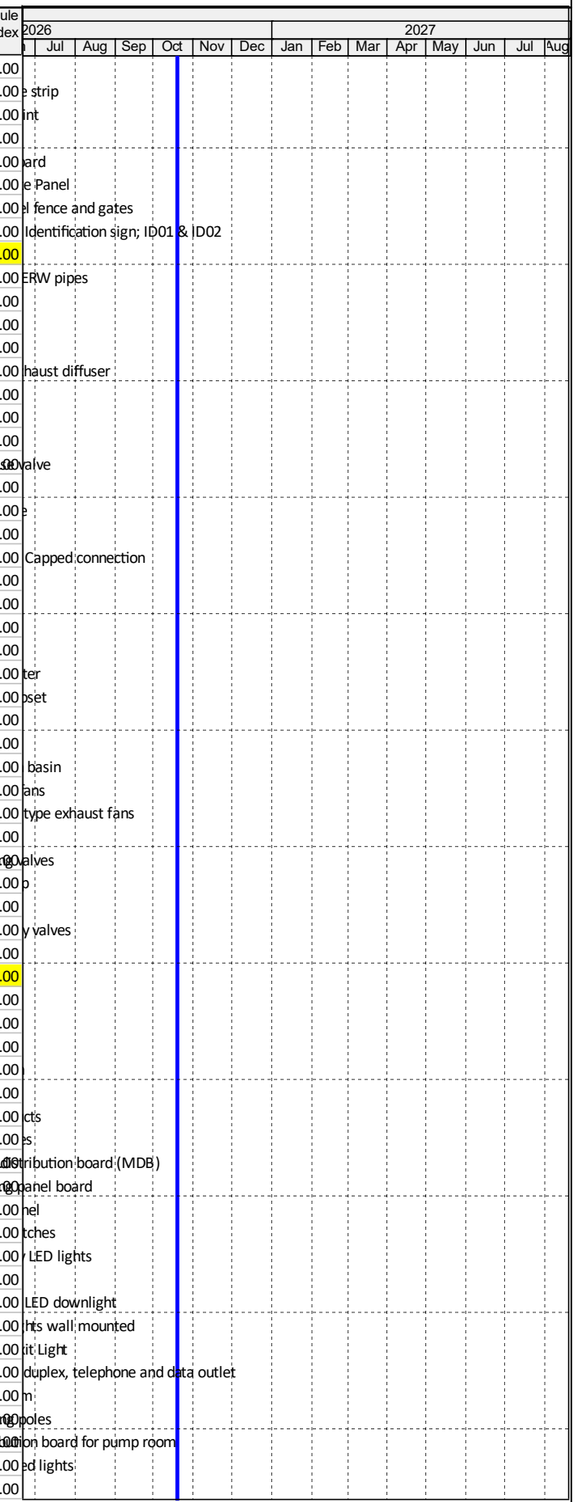





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-MS-E-0240 | Access control system | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 11-Feb-26 | 11-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0250 | Solar system | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 03-Mar-26 | 03-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0260 | Main program system & controller | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 30-Apr-26 | 30-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-E-0270 | PLC controller | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 30-Apr-26 | 30-Apr-26 | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 14 | 0.00 | 30-Mar-26 | 14-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0010 | Asphalt works | 2 | 0.00 | 30-Mar-26 | 31-Mar-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0020 | Concrete parking bumper | 2 | 0.00 | 01-Apr-26 | 02-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0030 | Road markings | 2 | 0.00 | 04-Apr-26 | 05-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0040 | Road signs | 2 | 0.00 | 06-Apr-26 | 07-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0060 | Interlock tiles | 2 | 0.00 | 08-Apr-26 | 09-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0070 | Curbstones | 2 | 0.00 | 11-Apr-26 | 12-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EX-0080 | Gravel bedding | 2 | 0.00 | 13-Apr-26 | 14-Apr-26 | 11-Jun-26 | 11-Jun-26 | 0.00 | 0.00 | 0.00 |
| **ENVIRONMETAL** | | 55 | 0.00 | 03-Feb-26 | 23-Feb-26 | 08-Feb-26 | 18-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0010 | HDPE pipes for fire system | 2 | 0.00 | 03-Feb-26 | 04-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0020 | Directly buried gate valve for fire system | 2 | 0.00 | 05-Feb-26 | 07-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0030 | HDPE pipes for water supply system | 2 | 0.00 | 08-Feb-26 | 09-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0040 | Directly buried gate valve for water system | 2 | 0.00 | 10-Feb-26 | 11-Feb-26 | 16-Feb-26 | 16-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0050 | Air valve | 2 | 0.00 | 12-Feb-26 | 14-Feb-26 | 18-Feb-26 | 18-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0060 | Washout valve | 2 | 0.00 | 15-Feb-26 | 16-Feb-26 | 18-Feb-26 | 18-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0070 | Gate valve | 2 | 0.00 | 17-Feb-26 | 19-Feb-26 | 18-Feb-26 | 18-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MS-EN-0080 | UPVC pipes | 2 | 0.00 | 19-Feb-26 | 23-Feb-26 | 08-Feb-26 | 08-Feb-26 | 0.00 | 0.00 | 0.00 |
| **REVIEW AND APPROVAL** | | 104 | 2,879,895.75 | 29-Jan-26 | 20-Apr-26 | 20-Jan-26 | 14-Jun-26 | 2,879,895.75 | 2,879,895.75 | 1.00 |
| **STRUCTURAL** | | 20 | 481,112.68 | 29-Jan-26 | 12-Feb-26 | 20-Jan-26 | 07-Apr-26 | 481,112.68 | 481,112.68 | 1.00 |
| DAM3-E-MA-C-0010 | Anti termite | 5 | 19,546.44 | 29-Jan-26 | 03-Feb-26 | 14-Mar-26 | 07-Apr-26 | 19,546.44 | 19,546.44 | 1.00 |
| DAM3-E-MA-C-0020 | Concrete mix | 5 | 251,751.70 | 01-Feb-26 | 05-Feb-26 | 20-Jan-26 | 20-Jan-26 | 251,751.70 | 251,751.70 | 1.00 |
| DAM3-E-MA-C-0030 | Polyethylene sheet | 5 | 13,035.98 | 03-Feb-26 | 08-Feb-26 | 22-Jan-26 | 29-Jan-26 | 13,035.98 | 13,035.98 | 1.00 |
| DAM3-E-MA-C-0040 | Bitumen paint | 5 | 28,944.10 | 05-Feb-26 | 10-Feb-26 | 22-Jan-26 | 29-Jan-26 | 28,944.10 | 28,944.10 | 1.00 |
| DAM3-E-MA-C-0050 | Rebar | 5 | 167,834.46 | 08-Feb-26 | 12-Feb-26 | 22-Jan-26 | 29-Jan-26 | 167,834.46 | 167,834.46 | 1.00 |
| **ARCHITECTURAL** | | 93 | 1,232,403.28 | 03-Feb-26 | 12-Mar-26 | 07-Feb-26 | 14-Jun-26 | 1,232,403.28 | 1,232,403.28 | 1.00 |
| DAM3-E-MA-A-0020 | Concrete masonry unit (CMU) | 5 | 62,820.36 | 03-Feb-26 | 08-Feb-26 | 26-Apr-26 | 29-Apr-26 | 62,820.36 | 62,820.36 | 1.00 |
| DAM3-E-MA-A-0030 | Steel ladder | 5 | 4,846.16 | 05-Feb-26 | 10-Feb-26 | 07-Feb-26 | 10-Feb-26 | 4,846.16 | 4,846.16 | 1.00 |
| DAM3-E-MA-A-0040 | Steel gratings | 5 | 3,179.40 | 08-Feb-26 | 12-Feb-26 | 21-May-26 | 24-May-26 | 3,179.40 | 3,179.40 | 1.00 |
| DAM3-E-MA-A-0050 | Steel rails | 5 | 755.54 | 10-Feb-26 | 15-Feb-26 | 13-Jun-26 | 14-Jun-26 | 755.54 | 755.54 | 1.00 |
| DAM3-E-MA-A-0100 | Doors | 5 | 75,386.56 | 12-Feb-26 | 17-Feb-26 | 19-Feb-26 | 25-Feb-26 | 75,386.56 | 75,386.56 | 1.00 |
| DAM3-E-MA-A-1700 | PES -Steel Structure | 5 | 799,834.94 | 12-Feb-26 | 17-Feb-26 | 07-Feb-26 | 17-Mar-26 | 799,834.94 | 799,834.94 | 1.00 |
| DAM3-E-MA-A-0110 | Windows | 5 | 52,525.19 | 15-Feb-26 | 21-Feb-26 | 19-Feb-26 | 25-Feb-26 | 52,525.19 | 52,525.19 | 1.00 |
| DAM3-E-MA-A-0120 | Ceramic tiles | 5 | 36,151.26 | 17-Feb-26 | 24-Feb-26 | 30-Mar-26 | 04-May-26 | 36,151.26 | 36,151.26 | 1.00 |
| DAM3-E-MA-A-0130 | Granite strip | 5 | 330.55 | 19-Feb-26 | 26-Feb-26 | 09-May-26 | 17-May-26 | 330.55 | 330.55 | 1.00 |
| DAM3-E-MA-A-0150 | Epoxy paint | 5 | 56,848.54 | 23-Feb-26 | 01-Mar-26 | 21-Apr-26 | 26-Apr-26 | 56,848.54 | 56,848.54 | 1.00 |
| DAM3-E-MA-A-0160 | Internl paint | 5 | 21,754.04 | 25-Feb-26 | 03-Mar-26 | 29-Mar-26 | 03-May-26 | 21,754.04 | 21,754.04 | 1.00 |
| DAM3-E-MA-A-0170 | Gypsum board | 5 | 23,046.95 | 01-Mar-26 | 05-Mar-26 | 19-Apr-26 | 14-Jun-26 | 23,046.95 | 23,046.95 | 1.00 |
| DAM3-E-MA-A-1720 | Aluminum Composite Panel | 5 | 86,631.78 | 03-Mar-26 | 08-Mar-26 | 21-Apr-26 | 26-Apr-26 | 86,631.78 | 86,631.78 | 1.00 |
| DAM3-E-MA-A-1750 | Steel fence and gates | 5 | 3,548.60 | 05-Mar-26 | 10-Mar-26 | 23-May-26 | 25-May-26 | 3,548.60 | 3,548.60 | 1.00 |
| DAM3-E-MA-A-1760 | Identification sign; ID01 & ID02 | 5 | 4,743.41 | 08-Mar-26 | 12-Mar-26 | 08-Jun-26 | 13-Jun-26 | 4,743.41 | 4,743.41 | 1.00 |
| **MECHANICAL** | | 101 | 303,435.06 | 03-Feb-26 | 20-Apr-26 | 05-Feb-26 | 14-Jun-26 | 303,435.06 | 303,435.06 | 1.00 |
| DAM3-E-MA-M-0020 | Seamless black steel or ERW pipes | 5 | 35,657.12 | 03-Feb-26 | 08-Feb-26 | 10-Feb-26 | 26-Feb-26 | 35,657.12 | 35,657.12 | 1.00 |
| DAM3-E-MA-M-0080 | PPR pipes | 5 | 11,485.19 | 05-Feb-26 | 10-Feb-26 | 05-Feb-26 | 11-May-26 | 11,485.19 | 11,485.19 | 1.00 |
| DAM3-E-MA-M-0220 | HVAC duct | 5 | 73,629.07 | 08-Feb-26 | 12-Feb-26 | 04-Mar-26 | 12-May-26 | 73,629.07 | 73,629.07 | 1.00 |
| DAM3-E-MA-M-0230 | Flexible duct | 5 | 10,444.45 | 10-Feb-26 | 15-Feb-26 | 04-Mar-26 | 12-May-26 | 10,444.45 | 10,444.45 | 1.00 |
| DAM3-E-MA-M-0240 | Exhaust diffuser | 5 | 1,056.00 | 12-Feb-26 | 17-Feb-26 | 01-Jun-26 | 04-Jun-26 | 1,056.00 | 1,056.00 | 1.00 |
| DAM3-E-MA-M-0010 | U/G HDPE pipes | 5 | 7,495.73 | 15-Feb-26 | 21-Feb-26 | 07-Feb-26 | 08-Mar-26 | 7,495.73 | 7,495.73 | 1.00 |
| DAM3-E-MA-M-0340 | Warning tapes | 5 | 2,111.55 | 15-Feb-26 | 21-Feb-26 | 16-Feb-26 | 03-Mar-26 | 2,111.55 | 2,111.55 | 1.00 |
| DAM3-E-MA-M-0030 | Fire hose cabinet | 5 | 7,466.16 | 17-Feb-26 | 24-Feb-26 | 07-Feb-26 | 01-Mar-26 | 7,466.16 | 7,466.16 | 1.00 |
| DAM3-E-MA-M-0040 | Automatic air release valve | 5 | 265.43 | 19-Feb-26 | 26-Feb-26 | 10-Feb-26 | 26-Feb-26 | 265.43 | 265.43 | 1.00 |
| DAM3-E-MA-M-0050 | OS & Y gate valve | 5 | 1,744.73 | 23-Feb-26 | 01-Mar-26 | 10-Feb-26 | 26-Feb-26 | 1,744.73 | 1,744.73 | 1.00 |
| DAM3-E-MA-M-0060 | Fire alarm check valve | 5 | 3,998.51 | 25-Feb-26 | 03-Mar-26 | 10-Feb-26 | 26-Feb-26 | 3,998.51 | 3,998.51 | 1.00 |
| DAM3-E-MA-M-0090 | Ball valve | 5 | 2,134.82 | 01-Mar-26 | 05-Mar-26 | 14-Feb-26 | 16-Apr-26 | 2,134.82 | 2,134.82 | 1.00 |
| DAM3-E-MA-M-0100 | Capped connection | 5 | 136.99 | 03-Mar-26 | 08-Mar-26 | 13-Jun-26 | 14-Jun-26 | 136.99 | 136.99 | 1.00 |
| DAM3-E-MA-M-0110 | UPVC pipes | 5 | 19,003.97 | 05-Mar-26 | 10-Mar-26 | 07-Feb-26 | 12-Apr-26 | 19,003.97 | 19,003.97 | 1.00 |
| DAM3-E-MA-M-0120 | Roof vent caps | 5 | 456.64 | 08-Mar-26 | 12-Mar-26 | 16-Feb-26 | 14-Jun-26 | 456.64 | 456.64 | 1.00 |
| DAM3-E-MA-M-0130 | Floor drain | 5 | 11,113.99 | 10-Mar-26 | 15-Mar-26 | 16-Feb-26 | 04-Jun-26 | 11,113.99 | 11,113.99 | 1.00 |
| DAM3-E-MA-M-0140 | Gully trap | 5 | 2,397.38 | 12-Mar-26 | 21-Mar-26 | 09-Feb-26 | 26-Feb-26 | 2,397.38 | 2,397.38 | 1.00 |

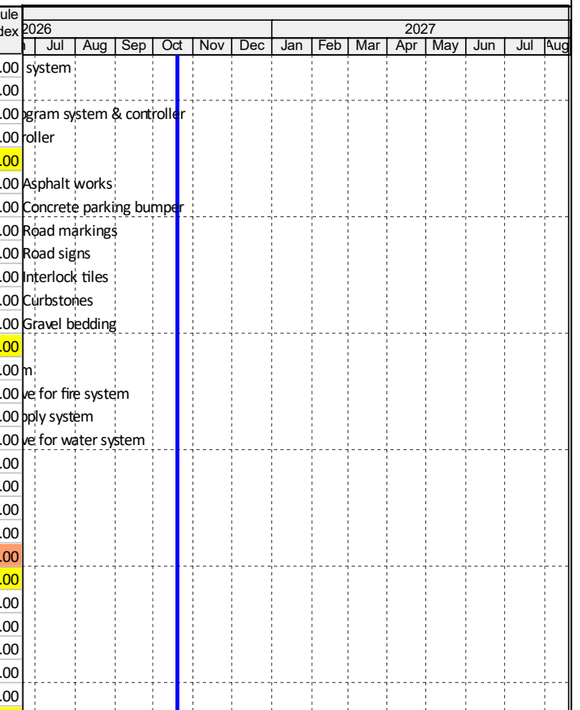




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-MA-M-0150 | Electric water heater | 5 | 896.17 | 15-Mar-26 | 23-Mar-26 | 08-Feb-26 | 01-Mar-26 | 896.17 | 896.17 | 1.00 |
| DAM3-E-MA-M-0160 | Western water closet | 5 | 9,812.19 | 21-Mar-26 | 25-Mar-26 | 08-Feb-26 | 17-May-26 | 9,812.19 | 9,812.19 | 1.00 |
| DAM3-E-MA-M-0170 | Bib tap | 5 | 936.14 | 23-Mar-26 | 28-Mar-26 | 14-Feb-26 | 16-Apr-26 | 936.14 | 936.14 | 1.00 |
| DAM3-E-MA-M-0180 | Toilet Fittings | 5 | 11,319.13 | 25-Mar-26 | 30-Mar-26 | 09-Feb-26 | 01-Jun-26 | 11,319.13 | 11,319.13 | 1.00 |
| DAM3-E-MA-M-0190 | Lavatory / wash basin | 5 | 10,548.52 | 28-Mar-26 | 01-Apr-26 | 08-Feb-26 | 17-May-26 | 10,548.52 | 10,548.52 | 1.00 |
| DAM3-E-MA-M-0200 | Inline exhaust fans | 5 | 4,121.24 | 30-Mar-26 | 04-Apr-26 | 18-Mar-26 | 19-Apr-26 | 4,121.24 | 4,121.24 | 1.00 |
| DAM3-E-MA-M-0210 | Wall propeller type exhaust fans | 5 | 23,066.33 | 01-Apr-26 | 06-Apr-26 | 18-Mar-26 | 19-Apr-26 | 23,066.33 | 23,066.33 | 1.00 |
| DAM3-E-MA-M-0250 | Fire pumps | 5 | 15,505.34 | 04-Apr-26 | 08-Apr-26 | 05-Feb-26 | 24-Feb-26 | 15,505.34 | 15,505.34 | 1.00 |
| DAM3-E-MA-M-0270 | Fire fighting valves | 5 | 1,332.84 | 06-Apr-26 | 11-Apr-26 | 10-Feb-26 | 26-Mar-26 | 1,332.84 | 1,332.84 | 1.00 |
| DAM3-E-MA-M-0310 | Booster pump | 5 | 1,938.67 | 08-Apr-26 | 13-Apr-26 | 05-Feb-26 | 11-Feb-26 | 1,938.67 | 1,938.67 | 1.00 |
| DAM3-E-MA-M-0320 | GRP tank | 5 | 31,477.96 | 11-Apr-26 | 15-Apr-26 | 02-Mar-26 | 07-Apr-26 | 31,477.96 | 31,477.96 | 1.00 |
| DAM3-E-MA-M-0330 | Water supply valves | 5 | 467.18 | 13-Apr-26 | 18-Apr-26 | 10-Feb-26 | 26-Mar-26 | 467.18 | 467.18 | 1.00 |
| DAM3-E-MA-M-3410 | Water tap | 5 | 1,415.62 | 15-Apr-26 | 20-Apr-26 | 14-Feb-26 | 16-Apr-26 | 1,415.62 | 1,415.62 | 1.00 |
| **ELECTRICAL** | | 74 | 472,829.48 | 05-Feb-26 | 15-Apr-26 | 09-Feb-26 | 14-Jun-26 | 472,829.48 | 472,829.48 | 1.00 |
| DAM3-E-MA-E-0040 | PVC conduits | 5 | 2,360.80 | 05-Feb-26 | 10-Feb-26 | 09-Feb-26 | 01-Mar-26 | 2,360.80 | 2,360.80 | 1.00 |
| DAM3-E-MA-E-0050 | Wires | 5 | 1,106.91 | 08-Feb-26 | 12-Feb-26 | 16-Mar-26 | 29-Mar-26 | 1,106.91 | 1,106.91 | 1.00 |
| DAM3-E-MA-E-210 | Cable Tray | 5 | 159.57 | 10-Feb-26 | 15-Feb-26 | 07-Mar-26 | 08-Mar-26 | 159.57 | 159.57 | 1.00 |
| DAM3-E-MA-E-0120 | Grounding system | 5 | 9,771.19 | 12-Feb-26 | 17-Feb-26 | 16-Mar-26 | 29-Mar-26 | 9,771.19 | 9,771.19 | 1.00 |
| DAM3-E-MA-E-0140 | Wiring devices | 5 | 9,962.15 | 15-Feb-26 | 21-Feb-26 | 07-Mar-26 | 08-Mar-26 | 9,962.15 | 9,962.15 | 1.00 |
| DAM3-E-MA-E-0160 | HDPE ducts | 5 | 26,402.96 | 17-Feb-26 | 24-Feb-26 | 30-Apr-26 | 03-May-26 | 26,402.96 | 26,402.96 | 1.00 |
| DAM3-E-MA-E-0010 | Low Voltage cables | 5 | 44,855.17 | 19-Feb-26 | 26-Feb-26 | 16-Mar-26 | 29-Mar-26 | 44,855.17 | 44,855.17 | 1.00 |
| DAM3-E-MA-E-0020 | Main distribution board (MDB) | 5 | 15,994.03 | 23-Feb-26 | 01-Mar-26 | 26-Apr-26 | 12-May-26 | 15,994.03 | 15,994.03 | 1.00 |
| DAM3-E-MA-E-190 | Lighting panel board | 5 | 9,064.43 | 25-Feb-26 | 03-Mar-26 | 26-Apr-26 | 12-May-26 | 9,064.43 | 9,064.43 | 1.00 |
| DAM3-E-MA-E-200 | PP-AC panel | 5 | 10,662.68 | 01-Mar-26 | 05-Mar-26 | 26-Apr-26 | 12-May-26 | 10,662.68 | 10,662.68 | 1.00 |
| DAM3-E-MA-E-0030 | Disconnect switches | 5 | 15,086.41 | 03-Mar-26 | 08-Mar-26 | 29-Mar-26 | 14-Jun-26 | 15,086.41 | 15,086.41 | 1.00 |
| DAM3-E-MA-E-0060 | Suspended High Bay LED lights | 5 | 14,938.02 | 05-Mar-26 | 10-Mar-26 | 03-Mar-26 | 07-Mar-26 | 14,938.02 | 14,938.02 | 1.00 |
| DAM3-E-MA-E-0070 | Flood lights | 5 | 2,268.18 | 08-Mar-26 | 12-Mar-26 | 03-Mar-26 | 07-Mar-26 | 2,268.18 | 2,268.18 | 1.00 |
| DAM3-E-MA-E-0080 | Recessed mounted LED downlight | 5 | 20,081.13 | 10-Mar-26 | 15-Mar-26 | 03-Mar-26 | 07-Mar-26 | 20,081.13 | 20,081.13 | 1.00 |
| DAM3-E-MA-E-0090 | LED Emergency Lights wall mounted | 5 | 4,144.06 | 12-Mar-26 | 21-Mar-26 | 03-Mar-26 | 07-Mar-26 | 4,144.06 | 4,144.06 | 1.00 |
| DAM3-E-MA-E-0100 | LED Emergency Exit Light | 5 | 1,145.13 | 15-Mar-26 | 23-Mar-26 | 03-Mar-26 | 07-Mar-26 | 1,145.13 | 1,145.13 | 1.00 |
| DAM3-E-MA-E-0110 | Wall mounted, duplex, telephone and data outlet | 4 | 13,294.12 | 21-Mar-26 | 25-Mar-26 | 29-Mar-26 | 13-Apr-26 | 13,294.12 | 13,294.12 | 1.00 |
| DAM3-E-MA-E-0130 | Fire alarm system | 5 | 41,920.11 | 23-Mar-26 | 28-Mar-26 | 11-Feb-26 | 30-Mar-26 | 41,920.11 | 41,920.11 | 1.00 |
| DAM3-E-MA-E-0170 | Street Lighting poles | 4 | 10,525.31 | 25-Mar-26 | 30-Mar-26 | 04-Mar-26 | 20-May-26 | 10,525.31 | 10,525.31 | 1.00 |
| DAM3-E-MA-E-0180 | Distribution board for pump room | 4 | 11,002.71 | 28-Mar-26 | 01-Apr-26 | 26-Apr-26 | 12-May-26 | 11,002.71 | 11,002.71 | 1.00 |
| DAM3-E-MA-E-0190 | Surface mounted lights | 5 | 11,068.82 | 30-Mar-26 | 04-Apr-26 | 03-Mar-26 | 07-Mar-26 | 11,068.82 | 11,068.82 | 1.00 |
| DAM3-E-MA-E-0230 | CCTV System | 4 | 37,604.85 | 01-Apr-26 | 06-Apr-26 | 28-Mar-26 | 13-Apr-26 | 37,604.85 | 37,604.85 | 1.00 |
| DAM3-E-MA-E-0240 | Access control system | 5 | 13,602.34 | 04-Apr-26 | 08-Apr-26 | 11-Feb-26 | 07-Mar-26 | 13,602.34 | 13,602.34 | 1.00 |
| DAM3-E-MA-E-0250 | Solar system | 4 | 124,744.29 | 06-Apr-26 | 11-Apr-26 | 03-Mar-26 | 25-Apr-26 | 124,744.29 | 124,744.29 | 1.00 |
| DAM3-E-MA-E-0260 | Main program system & controller | 5 | 12,578.11 | 08-Apr-26 | 13-Apr-26 | 30-Apr-26 | 12-May-26 | 12,578.11 | 12,578.11 | 1.00 |
| DAM3-E-MA-E-0270 | PLC controller | 5 | 8,486.00 | 11-Apr-26 | 15-Apr-26 | 30-Apr-26 | 12-May-26 | 8,486.00 | 8,486.00 | 1.00 |
| **EXTERNAL** | | 29 | 332,383.67 | 01-Apr-26 | 20-Apr-26 | 11-Jun-26 | 13-Jun-26 | 332,383.67 | 332,383.67 | 1.00 |
| DAM3-E-MA-EX-0010 | Asphalt works | 5 | 280,347.76 | 01-Apr-26 | 06-Apr-26 | 11-Jun-26 | 13-Jun-26 | 280,347.76 | 280,347.76 | 1.00 |
| DAM3-E-MA-EX-0020 | Concrete parking bumper | 5 | 1,433.72 | 04-Apr-26 | 08-Apr-26 | 11-Jun-26 | 13-Jun-26 | 1,433.72 | 1,433.72 | 1.00 |
| DAM3-E-MA-EX-0030 | Road markings | 5 | 1,696.34 | 06-Apr-26 | 11-Apr-26 | 11-Jun-26 | 13-Jun-26 | 1,696.34 | 1,696.34 | 1.00 |
| DAM3-E-MA-EX-0040 | Road signs | 5 | 4,654.29 | 08-Apr-26 | 13-Apr-26 | 11-Jun-26 | 13-Jun-26 | 4,654.29 | 4,654.29 | 1.00 |
| DAM3-E-MA-EX-0060 | Interlock tiles | 5 | 21,297.02 | 11-Apr-26 | 15-Apr-26 | 11-Jun-26 | 13-Jun-26 | 21,297.02 | 21,297.02 | 1.00 |
| DAM3-E-MA-EX-0070 | Curbstones | 5 | 13,036.86 | 13-Apr-26 | 18-Apr-26 | 11-Jun-26 | 13-Jun-26 | 13,036.86 | 13,036.86 | 1.00 |
| DAM3-E-MA-EX-0080 | Gravel bedding | 5 | 9,917.68 | 15-Apr-26 | 20-Apr-26 | 11-Jun-26 | 13-Jun-26 | 9,917.68 | 9,917.68 | 1.00 |
| **ENVIRONMETAL** | | 59 | 57,731.58 | 05-Feb-26 | 01-Mar-26 | 08-Feb-26 | 14-Jun-26 | 57,731.58 | 57,731.58 | 1.00 |
| DAM3-E-MA-EN-0010 | HDPE pipes for fire system | 5 | 21,745.93 | 05-Feb-26 | 10-Feb-26 | 08-Feb-26 | 26-Feb-26 | 21,745.93 | 21,745.93 | 1.00 |
| DAM3-E-MA-EN-0020 | Directly buried gate valve for fire system | 5 | 1,090.50 | 08-Feb-26 | 12-Feb-26 | 16-Feb-26 | 25-May-26 | 1,090.50 | 1,090.50 | 1.00 |
| DAM3-E-MA-EN-0030 | HDPE pipes for water supply system | 5 | 1,598.26 | 10-Feb-26 | 15-Feb-26 | 08-Feb-26 | 26-Feb-26 | 1,598.26 | 1,598.26 | 1.00 |
| DAM3-E-MA-EN-0040 | Directly buried gate valve for water system | 5 | 2,414.78 | 12-Feb-26 | 17-Feb-26 | 16-Feb-26 | 25-May-26 | 2,414.78 | 2,414.78 | 1.00 |
| DAM3-E-MA-EN-0050 | Air valve | 5 | 1,963.06 | 15-Feb-26 | 21-Feb-26 | 18-Feb-26 | 26-Feb-26 | 1,963.06 | 1,963.06 | 1.00 |
| DAM3-E-MA-EN-0060 | Washout valve | 5 | 2,302.04 | 17-Feb-26 | 24-Feb-26 | 18-Feb-26 | 14-Jun-26 | 2,302.04 | 2,302.04 | 1.00 |
| DAM3-E-MA-EN-0070 | Gate valve | 5 | 6,398.75 | 19-Feb-26 | 26-Feb-26 | 18-Feb-26 | 14-Jun-26 | 6,398.75 | 6,398.75 | 1.00 |
| DAM3-E-MA-EN-0080 | UPVC pipes | 5 | 20,218.26 | 23-Feb-26 | 01-Mar-26 | 08-Feb-26 | 26-Feb-26 | 20,218.26 | 20,218.26 | 1.00 |
| **METHOD STATEMENTS** | | 125 | 0.00 | 29-Jan-26 | 23-Apr-26 | 07-Feb-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| **PREPARATION AND SUBMITTAL** | | 112 | 0.00 | 29-Jan-26 | 25-Mar-26 | 07-Feb-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-C-0010 | Method Statement for Structural Works | 7 | 0.00 | 29-Jan-26 | 05-Feb-26 | 07-Feb-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-A-0020 | Method Statement for Architectural Works | 7 | 0.00 | 07-Feb-26 | 14-Feb-26 | 05-Mar-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-M-0030 | Method Statement for Mechanical Works | 7 | 0.00 | 15-Feb-26 | 24-Feb-26 | 10-May-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |

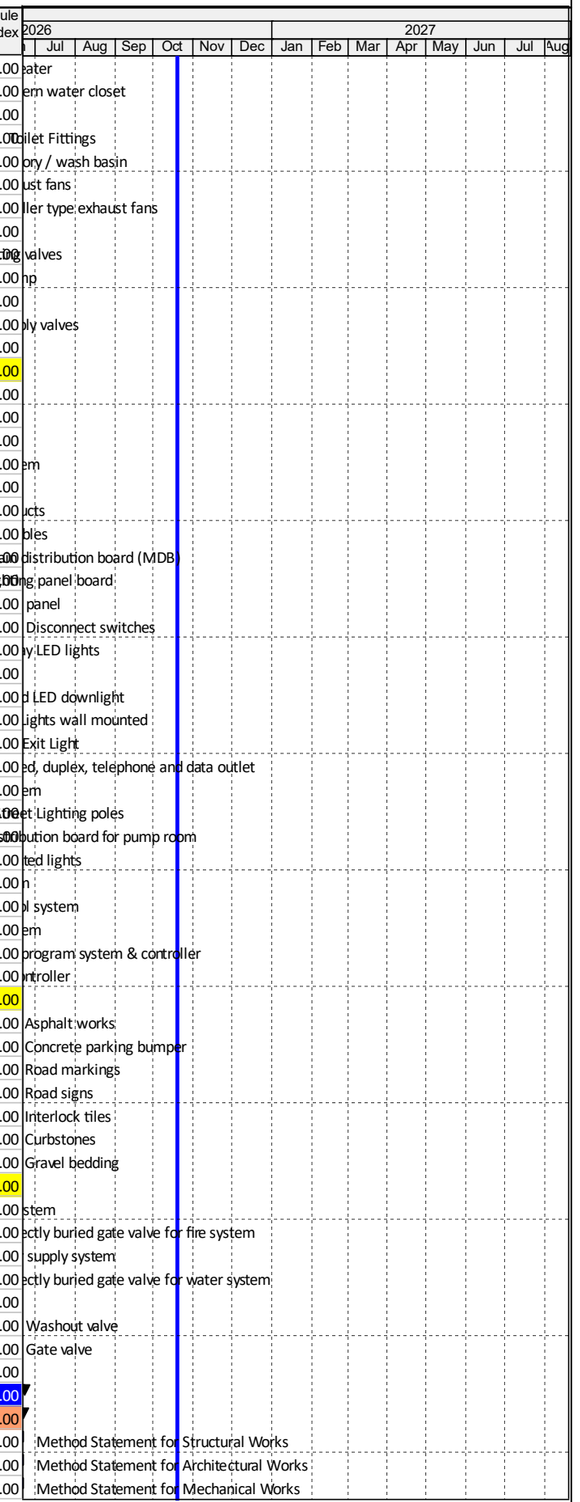





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-E-MT-E-0040 | Method Statement for Electrical Works | 7 | 0.00 | 24-Feb-26 | 04-Mar-26 | 10-May-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-EX-0050 | Method Statement for External Works | 7 | 0.00 | 05-Mar-26 | 12-Mar-26 | 21-Jun-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-ENV-0060 | Method Statement for Environmental Works | 8 | 0.00 | 14-Mar-26 | 25-Mar-26 | 21-Jun-26 | 22-Jun-26 | 0.00 | 0.00 | 0.00 |
| **REVIEW AND APPROVAL** | | 51 | 0.00 | 07-Feb-26 | 22-Apr-26 | 07-Feb-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-C-1010 | Method Statement for Structural Works | 10 | 0.00 | 07-Feb-26 | 17-Feb-26 | 07-Feb-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-A-1020 | Method Statement for Architectural Works | 10 | 0.00 | 18-Feb-26 | 03-Mar-26 | 05-Mar-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-M-1030 | Method Statement for Mechanical Works | 10 | 0.00 | 04-Mar-26 | 15-Mar-26 | 10-May-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-E-1040 | Method Statement for Electrical Works | 10 | 0.00 | 16-Mar-26 | 30-Mar-26 | 10-May-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-EX-1050 | Method Statement for External Works | 10 | 0.00 | 31-Mar-26 | 11-Apr-26 | 21-Jun-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-ENV-1060 | Method Statement for Environmental Works | 10 | 0.00 | 12-Apr-26 | 22-Apr-26 | 21-Jun-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| **STAGING** | | 42 | 0.00 | 18-Feb-26 | 23-Apr-26 | 09-Feb-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-C-2010 | Method Statement for Structural Works | 1 | 0.00 | 18-Feb-26 | 19-Feb-26 | 09-Feb-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-A-2020 | Method Statement for Architectural Works | 4 | 0.00 | 04-Mar-26 | 08-Mar-26 | 21-Jun-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-M-2030 | Method Statement for Mechanical Works | 1 | 0.00 | 16-Mar-26 | 16-Mar-26 | 10-May-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-E-2040 | Method Statement for Electrical Works | 1 | 0.00 | 31-Mar-26 | 31-Mar-26 | 10-May-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-EX-2050 | Method Statement for External Works | 1 | 0.00 | 12-Apr-26 | 12-Apr-26 | 21-Jun-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MT-ENV-2060 | Method Statement for Environmental Works | 1 | 0.00 | 23-Apr-26 | 23-Apr-26 | 21-Jun-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| **PROCUREMENT (20%)** | | 258 | 19,199,305.00 | 04-Feb-26 | 15-Nov-26 | 14-Jan-26 | 27-Sep-26 | 18,821,263.50 | 19,199,305.00 | 1.02 |
| **LONG LEAD MATERIALS** | | 245 | 9,350,010.31 | 09-Feb-26 | 15-Nov-26 | 14-Jan-26 | 27-Sep-26 | 8,971,968.81 | 9,350,010.31 | 1.04 |
| **ARCHITECTURAL** | | 145 | 6,184,977.93 | 18-Feb-26 | 06-Jul-26 | 14-Jan-26 | 20-Aug-26 | 6,184,977.93 | 6,184,977.93 | 1.00 |
| **PO ISSUE** | | 90 | 0.00 | 18-Feb-26 | 28-Feb-26 | 14-Jan-26 | 22-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-180 | Doors | 5 | 0.00 | 18-Feb-26 | 25-Feb-26 | 18-Mar-26 | 18-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-A-1700 | PES -Steel Structure | 5 | 0.00 | 18-Feb-26 | 25-Feb-26 | 14-Jan-26 | 14-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-190 | Windows | 5 | 0.00 | 21-Feb-26 | 28-Feb-26 | 22-Mar-26 | 22-Mar-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 99 | 0.00 | 25-Feb-26 | 20-Jun-26 | 14-Jan-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-180 | Doors | 90 | 0.00 | 25-Feb-26 | 17-Jun-26 | 21-Mar-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-A-1700 | PES -Steel Structure | 45 | 0.00 | 25-Feb-26 | 22-Apr-26 | 14-Jan-26 | 25-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-190 | Windows | 90 | 0.00 | 01-Mar-26 | 20-Jun-26 | 25-Mar-26 | 23-Jun-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY TO SITE** | | 59 | 6,184,977.93 | 23-Apr-26 | 04-Jul-26 | 31-May-26 | 20-Aug-26 | 6,184,977.93 | 6,184,977.93 | 1.00 |
| DAM3-P-DL-A-1700 | PES -Steel Structure -1 | 7 | 2,369,269.97 | 23-Apr-26 | 30-Apr-26 | 31-May-26 | 31-May-26 | 2,369,269.97 | 2,369,269.97 | 1.00 |
| DAM3-P-DL-A-1770 | PES -Steel Structure -2 | 7 | 740,740.74 | 02-May-26 | 09-May-26 | 10-Jun-26 | 14-Jun-26 | 740,740.74 | 740,740.74 | 1.00 |
| DAM3-P-DL-A-180 | Doors | 7 | 502,577.07 | 18-Jun-26 | 25-Jun-26 | 18-Aug-26 | 20-Aug-26 | 502,577.07 | 502,577.07 | 1.00 |
| DAM3-P-DL-A-1780 | PES -Steel Structure -3 | 7 | 740,740.74 | 18-Jun-26 | 25-Jun-26 | 14-Jun-26 | 14-Jul-26 | 740,740.74 | 740,740.74 | 1.00 |
| DAM3-P-DL-A-190 | Windows | 7 | 350,167.93 | 21-Jun-26 | 28-Jun-26 | 19-Aug-26 | 20-Aug-26 | 350,167.93 | 350,167.93 | 1.00 |
| DAM3-P-DL-A-1790 | PES -Steel Structure -4 | 7 | 1,481,481.48 | 27-Jun-26 | 04-Jul-26 | 01-Jul-26 | 01-Jul-26 | 1,481,481.48 | 1,481,481.48 | 1.00 |
| **STAGING TIME** | | 38 | 0.00 | 02-May-26 | 06-Jul-26 | 21-Jul-26 | 20-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-A-1700 | PES -Steel Structure | 2 | 0.00 | 02-May-26 | 03-May-26 | 21-Jul-26 | 22-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-180 | Doors | 7 | 0.00 | 27-Jun-26 | 04-Jul-26 | 18-Aug-26 | 20-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-190 | Windows | 7 | 0.00 | 29-Jun-26 | 06-Jul-26 | 19-Aug-26 | 20-Aug-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 187 | 2,332,207.26 | 01-Mar-26 | 15-Nov-26 | 24-Mar-26 | 27-Sep-26 | 1,954,165.75 | 2,332,207.26 | 1.19 |
| **PO ISSUE** | | 60 | 0.00 | 01-Mar-26 | 14-May-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-190 | Main distribution board (MDB) | 5 | 0.00 | 01-Mar-26 | 07-Mar-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-190 | Lighting panel board | 5 | 0.00 | 07-Mar-26 | 12-Mar-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-200 | PP-AC panel | 5 | 0.00 | 12-Mar-26 | 22-Mar-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-200 | Suspended High Bay LED lights | 5 | 0.00 | 24-Mar-26 | 29-Mar-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-210 | Flood lights | 5 | 0.00 | 30-Mar-26 | 04-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-220 | Recessed mounted LED downlight | 5 | 0.00 | 05-Apr-26 | 09-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-0230 | CCTV System | 5 | 0.00 | 07-Apr-26 | 12-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-0240 | Access control system | 5 | 0.00 | 09-Apr-26 | 14-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-230 | LED Emergency Lights wall mounted | 5 | 0.00 | 11-Apr-26 | 15-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-0250 | Solar system | 5 | 0.00 | 12-Apr-26 | 16-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-0260 | Main program system & controller | 5 | 0.00 | 14-Apr-26 | 19-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-240 | LED Emergency Exit Light | 5 | 0.00 | 16-Apr-26 | 21-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-0270 | PLC controller | 5 | 0.00 | 16-Apr-26 | 21-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-250 | Fire alarm system | 5 | 0.00 | 22-Apr-26 | 27-Apr-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-260 | Street Lighting poles | 5 | 0.00 | 28-Apr-26 | 03-May-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-270 | Distribution board for pump room | 5 | 0.00 | 04-May-26 | 09-May-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-280 | Surface mounted lights | 5 | 0.00 | 10-May-26 | 14-May-26 | 24-Mar-26 | 24-Mar-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 187 | 0.00 | 07-Mar-26 | 29-Oct-26 | 01-Apr-26 | 27-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-190 | Main distribution board (MDB) | 90 | 0.00 | 07-Mar-26 | 27-Jun-26 | 01-Apr-26 | 22-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-190 | Lighting panel board | 90 | 0.00 | 12-Mar-26 | 02-Jul-26 | 07-Apr-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-200 | PP-AC panel | 90 | 0.00 | 22-Mar-26 | 08-Jul-26 | 13-Apr-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |

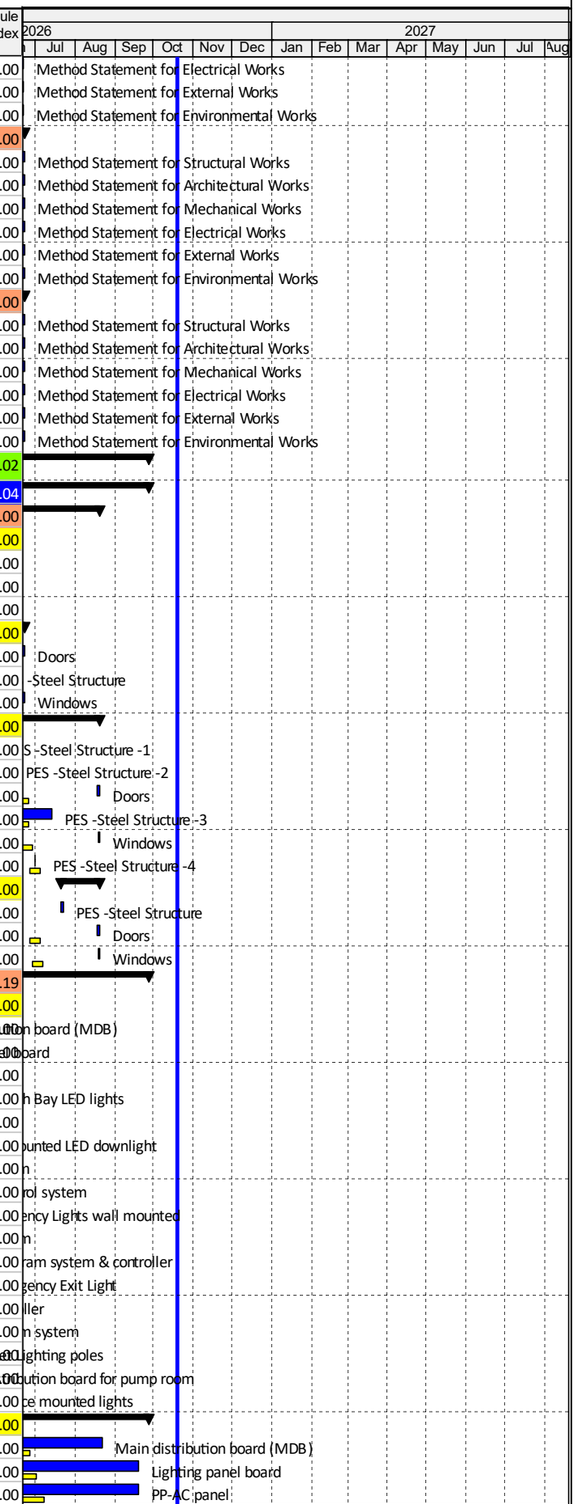




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-MF-E-200 | Suspended High Bay LED lights | 90 | 0.00 | 30-Mar-26 | 15-Jul-26 | 20-Apr-26 | 27-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-210 | Flood lights | 90 | 0.00 | 05-Apr-26 | 21-Jul-26 | 28-Apr-26 | 27-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-220 | Recessed mounted LED downlight | 90 | 0.00 | 11-Apr-26 | 27-Jul-26 | 04-May-26 | 27-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-0230 | CCTV System | 120 | 0.00 | 13-Apr-26 | 02-Sep-26 | 25-Apr-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-0240 | Access control system | 150 | 0.00 | 15-Apr-26 | 11-Oct-26 | 16-Apr-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-230 | LED Emergency Lights wall mounted | 90 | 0.00 | 16-Apr-26 | 02-Aug-26 | 10-May-26 | 27-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-0250 | Solar system | 150 | 0.00 | 18-Apr-26 | 13-Oct-26 | 25-Apr-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-0260 | Main program system & controller | 155 | 0.00 | 20-Apr-26 | 21-Oct-26 | 29-Apr-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-240 | LED Emergency Exit Light | 90 | 0.00 | 22-Apr-26 | 08-Aug-26 | 16-May-26 | 27-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-0270 | PLC controller | 160 | 0.00 | 22-Apr-26 | 29-Oct-26 | 02-May-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-250 | Fire alarm system | 130 | 0.00 | 28-Apr-26 | 30-Sep-26 | 21-May-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-260 | Street Lighting poles | 90 | 0.00 | 04-May-26 | 19-Aug-26 | 31-May-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-270 | Distribution board for pump room | 90 | 0.00 | 10-May-26 | 25-Aug-26 | 06-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-280 | Surface mounted lights | 90 | 0.00 | 16-May-26 | 31-Aug-26 | 11-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY TO SITE** | | 33 | 2,332,207.26 | 27-Jun-26 | 07-Nov-26 | 24-Aug-26 | 21-Sep-26 | 1,954,165.75 | 2,332,207.26 | 1.19 |
| DAM3-P-DL-E-190 | Main distribution board (MDB) | 7 | 106,626.87 | 27-Jun-26 | 05-Jul-26 | 24-Aug-26 | 24-Aug-26 | 106,626.87 | 106,626.87 | 1.00 |
| DAM3-P-DL-E-1900 | Lighting panel board | 7 | 60,429.51 | 02-Jul-26 | 11-Jul-26 | 01-Sep-26 | 21-Sep-26 | 60,429.51 | 60,429.51 | 1.00 |
| DAM3-P-DL-E-2000 | PP-AC panel | 7 | 71,084.56 | 08-Jul-26 | 16-Jul-26 | 01-Sep-26 | 21-Sep-26 | 71,084.56 | 71,084.56 | 1.00 |
| DAM3-P-DL-E-200 | Suspended High Bay LED lights | 7 | 99,586.79 | 16-Jul-26 | 23-Jul-26 | 29-Aug-26 | 29-Aug-26 | 99,586.79 | 99,586.79 | 1.00 |
| DAM3-P-DL-E-210 | Flood lights | 7 | 15,121.21 | 22-Jul-26 | 29-Jul-26 | 29-Aug-26 | 29-Aug-26 | 15,121.21 | 15,121.21 | 1.00 |
| DAM3-P-DL-E-220 | Recessed mounted LED downlight | 7 | 133,874.22 | 28-Jul-26 | 04-Aug-26 | 29-Aug-26 | 29-Aug-26 | 133,874.22 | 133,874.22 | 1.00 |
| DAM3-P-DL-E-230 | LED Emergency Lights wall mounted | 7 | 27,627.07 | 03-Aug-26 | 10-Aug-26 | 29-Aug-26 | 29-Aug-26 | 27,627.07 | 27,627.07 | 1.00 |
| DAM3-P-DL-E-240 | LED Emergency Exit Light | 7 | 7,634.17 | 09-Aug-26 | 16-Aug-26 | 29-Aug-26 | 29-Aug-26 | 7,634.17 | 7,634.17 | 1.00 |
| DAM3-P-DL-E-260 | Street Lighting poles | 7 | 70,168.75 | 20-Aug-26 | 27-Aug-26 | 19-Sep-26 | 21-Sep-26 | 70,168.75 | 70,168.75 | 1.00 |
| DAM3-P-DL-E-270 | Distribution board for pump room | 7 | 73,351.39 | 26-Aug-26 | 02-Sep-26 | 19-Sep-26 | 20-Sep-26 | 73,351.39 | 73,351.39 | 1.00 |
| DAM3-P-DL-E-280 | Surface mounted lights | 7 | 73,792.16 | 01-Sep-26 | 08-Sep-26 | 29-Aug-26 | 29-Aug-26 | 73,792.16 | 73,792.16 | 1.00 |
| DAM3-P-DL-E-0230 | CCTV System | 7 | 250,698.98 | 03-Sep-26 | 10-Sep-26 | 06-Sep-26 | 21-Sep-26 | 250,698.98 | 250,698.98 | 1.00 |
| DAM3-P-DL-E-250 | Fire alarm system | 7 | 279,467.41 | 01-Oct-26 | 08-Oct-26 | 02-Sep-26 | 21-Sep-26 | 279,467.41 | 279,467.41 | 1.00 |
| DAM3-P-DL-E-0240 | Access control system | 7 | 90,682.24 | 12-Oct-26 | 19-Oct-26 | 19-Sep-26 | 21-Sep-26 | 90,682.24 | 90,682.24 | 1.00 |
| DAM3-P-DL-E-0250 | Solar system | 7 | 831,628.60 | 14-Oct-26 | 21-Oct-26 | 09-Sep-26 | 21-Sep-26 | 594,020.43 | 831,628.60 | 1.40 |
| DAM3-P-DL-E-0260 | Main program system & controller | 7 | 83,856.79 | 22-Oct-26 | 29-Oct-26 | 06-Sep-26 | 21-Sep-26 | 0.00 | 83,856.79 | 0.00 |
| DAM3-P-DL-E-0270 | PLC controller | 7 | 56,576.55 | 31-Oct-26 | 07-Nov-26 | 07-Sep-26 | 21-Sep-26 | 0.00 | 56,576.55 | 0.00 |
| **STAGING TIME** | | 38 | 0.00 | 05-Jul-26 | 15-Nov-26 | 24-Aug-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-190 | Main distribution board (MDB) | 7 | 0.00 | 05-Jul-26 | 13-Jul-26 | 24-Aug-26 | 24-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-190 | Lighting panel board | 7 | 0.00 | 11-Jul-26 | 19-Jul-26 | 01-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-200 | PP-AC panel | 7 | 0.00 | 16-Jul-26 | 25-Jul-26 | 01-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-200 | Suspended High Bay LED lights | 7 | 0.00 | 25-Jul-26 | 01-Aug-26 | 29-Aug-26 | 29-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-210 | Flood lights | 7 | 0.00 | 30-Jul-26 | 06-Aug-26 | 29-Aug-26 | 29-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-220 | Recessed mounted LED downlight | 7 | 0.00 | 05-Aug-26 | 12-Aug-26 | 29-Aug-26 | 29-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-230 | LED Emergency Lights wall mounted | 7 | 0.00 | 11-Aug-26 | 18-Aug-26 | 29-Aug-26 | 29-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-240 | LED Emergency Exit Light | 7 | 0.00 | 17-Aug-26 | 24-Aug-26 | 29-Aug-26 | 29-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-260 | Street Lighting poles | 7 | 0.00 | 29-Aug-26 | 05-Sep-26 | 19-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-270 | Distribution board for pump room | 7 | 0.00 | 03-Sep-26 | 10-Sep-26 | 19-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-280 | Surface mounted lights | 7 | 0.00 | 09-Sep-26 | 16-Sep-26 | 29-Aug-26 | 29-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-0230 | CCTV System | 7 | 0.00 | 12-Sep-26 | 19-Sep-26 | 06-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-250 | Fire alarm system | 7 | 0.00 | 10-Oct-26 | 17-Oct-26 | 02-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-0240 | Access control system | 7 | 0.00 | 20-Oct-26 | 27-Oct-26 | 19-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-0250 | Solar system | 7 | 0.00 | 22-Oct-26 | 29-Oct-26 | 09-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-0260 | Main program system & controller | 7 | 0.00 | 31-Oct-26 | 07-Nov-26 | 06-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-0270 | PLC controller | 7 | 0.00 | 08-Nov-26 | 15-Nov-26 | 07-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 216 | 832,825.12 | 09-Feb-26 | 13-Oct-26 | 01-Mar-26 | 20-Sep-26 | 832,825.12 | 832,825.12 | 1.00 |
| **PO ISSUE** | | 84 | 0.00 | 09-Feb-26 | 29-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-340 | Seamless black steel or ERW pipes | 5 | 0.00 | 09-Feb-26 | 14-Feb-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-350 | Fire hose cabinet | 5 | 0.00 | 24-Feb-26 | 02-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-360 | Western water closet | 5 | 0.00 | 25-Mar-26 | 31-Mar-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-370 | Wall propeller type exhaust fans | 5 | 0.00 | 06-Apr-26 | 12-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-380 | Fire pumps | 5 | 0.00 | 12-Apr-26 | 18-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-400 | Booster pump | 5 | 0.00 | 18-Apr-26 | 23-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-410 | GRP tank | 5 | 0.00 | 23-Apr-26 | 29-Apr-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 211 | 0.00 | 15-Feb-26 | 27-Sep-26 | 02-Mar-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-340 | Seamless black steel or ERW pipes | 120 | 0.00 | 15-Feb-26 | 13-Jul-26 | 02-Mar-26 | 29-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-350 | Fire hose cabinet | 120 | 0.00 | 03-Mar-26 | 27-Jul-26 | 02-Mar-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |

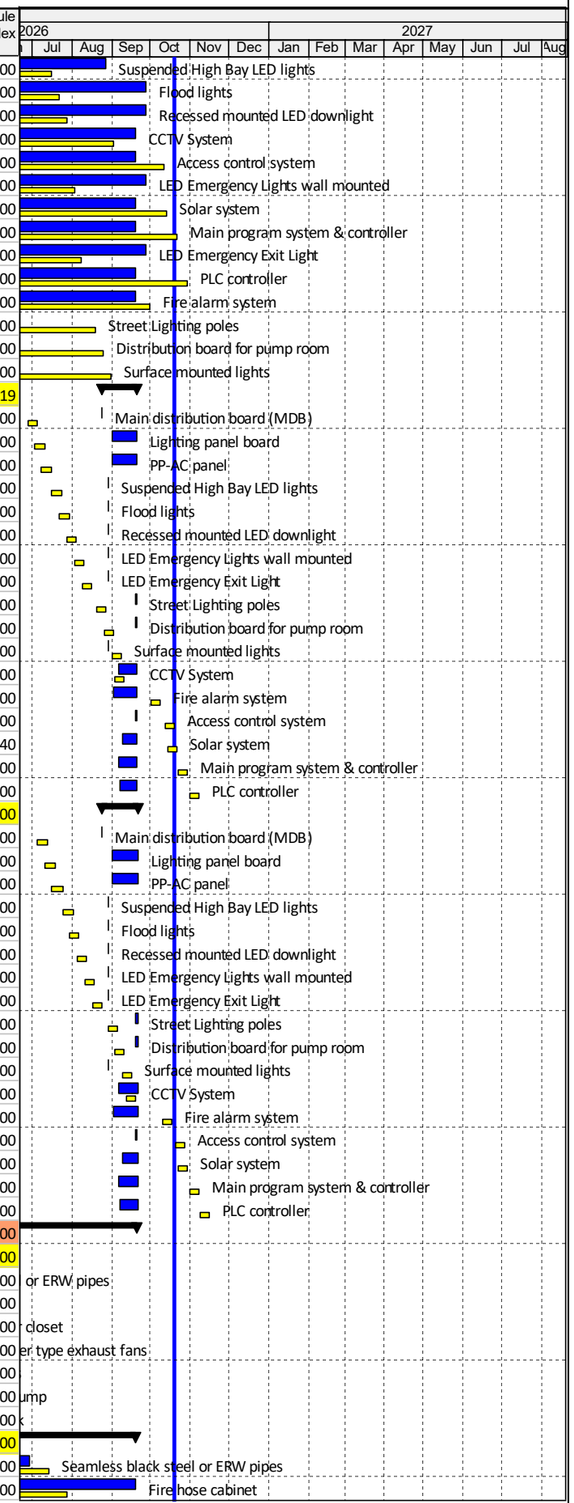





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-MF-M-360 | Western water closet | 150 | 0.00 | 31-Mar-26 | 27-Sep-26 | 02-Mar-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-370 | Wall propeller type exhaust fans | 100 | 0.00 | 12-Apr-26 | 10-Aug-26 | 02-Mar-26 | 09-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-380 | Fire pumps | 120 | 0.00 | 18-Apr-26 | 08-Sep-26 | 02-Mar-26 | 17-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-400 | Booster pump | 110 | 0.00 | 23-Apr-26 | 02-Sep-26 | 02-Mar-26 | 06-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-410 | GRP tank | 100 | 0.00 | 29-Apr-26 | 27-Aug-26 | 02-Mar-26 | 25-Aug-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY TO SITE** | | 72 | 832,825.12 | 14-Jul-26 | 05-Oct-26 | 01-Jul-26 | 20-Sep-26 | 832,825.12 | 832,825.12 | 1.00 |
| DAM3-P-DL-M-340 | Seamless black steel or ERW pipes | 7 | 237,714.11 | 14-Jul-26 | 21-Jul-26 | 01-Jul-26 | 11-Aug-26 | 237,714.11 | 237,714.11 | 1.00 |
| DAM3-P-DL-M-350 | Fire hose cabinet | 7 | 49,774.39 | 28-Jul-26 | 04-Aug-26 | 19-Sep-26 | 20-Sep-26 | 49,774.39 | 49,774.39 | 1.00 |
| DAM3-P-DL-M-370 | Wall propeller type exhaust fans | 7 | 153,775.51 | 10-Aug-26 | 18-Aug-26 | 10-Aug-26 | 20-Sep-26 | 153,775.51 | 153,775.51 | 1.00 |
| DAM3-P-DL-M-410 | GRP tank | 7 | 209,853.09 | 27-Aug-26 | 05-Sep-26 | 29-Aug-26 | 31-Aug-26 | 209,853.09 | 209,853.09 | 1.00 |
| DAM3-P-DL-M-400 | Booster pump | 7 | 12,924.47 | 02-Sep-26 | 10-Sep-26 | 07-Sep-26 | 07-Sep-26 | 12,924.47 | 12,924.47 | 1.00 |
| DAM3-P-DL-M-380 | Fire pumps | 7 | 103,368.93 | 08-Sep-26 | 16-Sep-26 | 20-Sep-26 | 20-Sep-26 | 103,368.93 | 103,368.93 | 1.00 |
| DAM3-P-DL-M-360 | Western water closet | 7 | 65,414.62 | 27-Sep-26 | 05-Oct-26 | 19-Sep-26 | 20-Sep-26 | 65,414.62 | 65,414.62 | 1.00 |
| **STAGING TIME** | | 86 | 0.00 | 22-Jul-26 | 13-Oct-26 | 01-Jul-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-340 | Seamless black steel or ERW pipes | 7 | 0.00 | 22-Jul-26 | 29-Jul-26 | 01-Jul-26 | 11-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-350 | Fire hose cabinet | 7 | 0.00 | 05-Aug-26 | 12-Aug-26 | 19-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-370 | Wall propeller type exhaust fans | 7 | 0.00 | 18-Aug-26 | 26-Aug-26 | 10-Aug-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-410 | GRP tank | 7 | 0.00 | 05-Sep-26 | 13-Sep-26 | 29-Aug-26 | 31-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-400 | Booster pump | 7 | 0.00 | 10-Sep-26 | 19-Sep-26 | 07-Sep-26 | 07-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-380 | Fire pumps | 7 | 0.00 | 16-Sep-26 | 26-Sep-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-360 | Western water closet | 7 | 0.00 | 05-Oct-26 | 13-Oct-26 | 19-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| **SHORT LEAD MATERIALS** | | 258 | 9,849,294.69 | 04-Feb-26 | 14-Oct-26 | 14-Jan-26 | 21-Sep-26 | 9,849,294.69 | 9,849,294.69 | 1.00 |
| **STRUCTURAL** | | 74 | 3,207,417.90 | 04-Feb-26 | 15-Apr-26 | 20-Jan-26 | 29-Apr-26 | 3,207,417.90 | 3,207,417.90 | 1.00 |
| **PO ISSUE** | | 28 | 0.00 | 04-Feb-26 | 15-Feb-26 | 20-Jan-26 | 25-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-C-50 | Anti termite | 2 | 0.00 | 04-Feb-26 | 05-Feb-26 | 25-Mar-26 | 25-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-C-60 | Concrete mix | 2 | 0.00 | 07-Feb-26 | 08-Feb-26 | 20-Jan-26 | 20-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-C-70 | Polyethylene sheet | 2 | 0.00 | 09-Feb-26 | 10-Feb-26 | 01-Mar-26 | 01-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-C-80 | Bitumen paint | 2 | 0.00 | 11-Feb-26 | 12-Feb-26 | 09-Mar-26 | 09-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-C-90 | Rebar | 2 | 0.00 | 14-Feb-26 | 15-Feb-26 | 01-Feb-26 | 01-Feb-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 38 | 0.00 | 07-Feb-26 | 02-Mar-26 | 21-Jan-26 | 07-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-C-50 | Anti termite | 12 | 0.00 | 07-Feb-26 | 21-Feb-26 | 26-Mar-26 | 07-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-C-60 | Concrete mix | 17 | 0.00 | 09-Feb-26 | 02-Mar-26 | 21-Jan-26 | 01-Feb-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-C-70 | Polyethylene sheet | 10 | 0.00 | 09-Feb-26 | 21-Feb-26 | 02-Mar-26 | 10-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-C-80 | Bitumen paint | 10 | 0.00 | 14-Feb-26 | 26-Feb-26 | 10-Mar-26 | 07-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-C-90 | Rebar | 7 | 0.00 | 16-Feb-26 | 25-Feb-26 | 02-Feb-26 | 15-Feb-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY** | | 59 | 3,207,417.90 | 21-Feb-26 | 15-Apr-26 | 12-Mar-26 | 29-Apr-26 | 3,207,417.90 | 3,207,417.90 | 1.00 |
| DAM3-P-DL-C-50 | Anti termite | 2 | 130,309.59 | 21-Feb-26 | 24-Feb-26 | 12-Mar-26 | 29-Apr-26 | 130,309.59 | 130,309.59 | 1.00 |
| DAM3-P-DL-C-70 | Polyethylene sheet | 2 | 86,906.55 | 21-Feb-26 | 24-Feb-26 | 12-Mar-26 | 29-Apr-26 | 86,906.55 | 86,906.55 | 1.00 |
| DAM3-P-DL-C-90 | Rebar-1 | 2 | 218,896.43 | 25-Feb-26 | 28-Feb-26 | 31-Mar-26 | 29-Apr-26 | 218,896.43 | 218,896.43 | 1.00 |
| DAM3-P-DL-C-80 | Bitumen paint | 2 | 192,960.68 | 26-Feb-26 | 01-Mar-26 | 31-Mar-26 | 29-Apr-26 | 192,960.68 | 192,960.68 | 1.00 |
| DAM3-P-DL-C-60 | Concrete mix -1 | 2 | 196,863.16 | 03-Mar-26 | 04-Mar-26 | 12-Mar-26 | 14-Apr-26 | 196,863.16 | 196,863.16 | 1.00 |
| DAM3-P-DL-C-100 | Concrete mix -2 | 2 | 740,740.74 | 12-Apr-26 | 13-Apr-26 | 16-Apr-26 | 29-Apr-26 | 740,740.74 | 740,740.74 | 1.00 |
| DAM3-P-DL-C-120 | Rebar-2 | 2 | 450,000.00 | 12-Apr-26 | 13-Apr-26 | 16-Apr-26 | 29-Apr-26 | 450,000.00 | 450,000.00 | 1.00 |
| DAM3-P-DL-C-110 | Concrete mix -3 | 2 | 740,740.74 | 14-Apr-26 | 15-Apr-26 | 16-Apr-26 | 29-Apr-26 | 740,740.74 | 740,740.74 | 1.00 |
| DAM3-P-DL-C-130 | Rebar-3 | 2 | 450,000.00 | 14-Apr-26 | 15-Apr-26 | 16-Apr-26 | 29-Apr-26 | 450,000.00 | 450,000.00 | 1.00 |
| **STAGING TIME** | | 16 | 0.00 | 24-Feb-26 | 05-Mar-26 | 12-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-C-50 | Anti termite | 1 | 0.00 | 24-Feb-26 | 25-Feb-26 | 12-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-C-70 | Polyethylene sheet | 1 | 0.00 | 24-Feb-26 | 25-Feb-26 | 12-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-C-90 | Rebar | 1 | 0.00 | 01-Mar-26 | 01-Mar-26 | 31-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-C-80 | Bitumen paint | 1 | 0.00 | 02-Mar-26 | 02-Mar-26 | 31-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-C-60 | Concrete mix | 1 | 0.00 | 05-Mar-26 | 05-Mar-26 | 12-Mar-26 | 29-Apr-26 | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 107 | 2,031,043.96 | 09-Feb-26 | 19-Jul-26 | 14-Jan-26 | 20-Sep-26 | 2,031,043.96 | 2,031,043.96 | 1.00 |
| **PO ISSUE** | | 86 | 0.00 | 09-Feb-26 | 28-Mar-26 | 14-Jan-26 | 24-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-200 | Concrete masonry unit (CMU) | 5 | 0.00 | 09-Feb-26 | 14-Feb-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-210 | Steel ladder | 5 | 0.00 | 15-Feb-26 | 21-Feb-26 | 14-Jan-26 | 18-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-220 | Steel gratings | 5 | 0.00 | 21-Feb-26 | 28-Feb-26 | 02-Apr-26 | 02-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-280 | Ceramic tiles | 5 | 0.00 | 24-Feb-26 | 02-Mar-26 | 07-Apr-26 | 07-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-230 | Steel rails | 5 | 0.00 | 01-Mar-26 | 05-Mar-26 | 24-May-26 | 24-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-310 | Epoxy paint | 5 | 0.00 | 01-Mar-26 | 07-Mar-26 | 24-May-26 | 24-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-290 | Granite strip | 5 | 0.00 | 03-Mar-26 | 08-Mar-26 | 12-May-26 | 12-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-A-320 | Internl paint | 5 | 0.00 | 07-Mar-26 | 12-Mar-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-A-1750 | Steel fence and gates | 5 | 0.00 | 11-Mar-26 | 16-Mar-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |

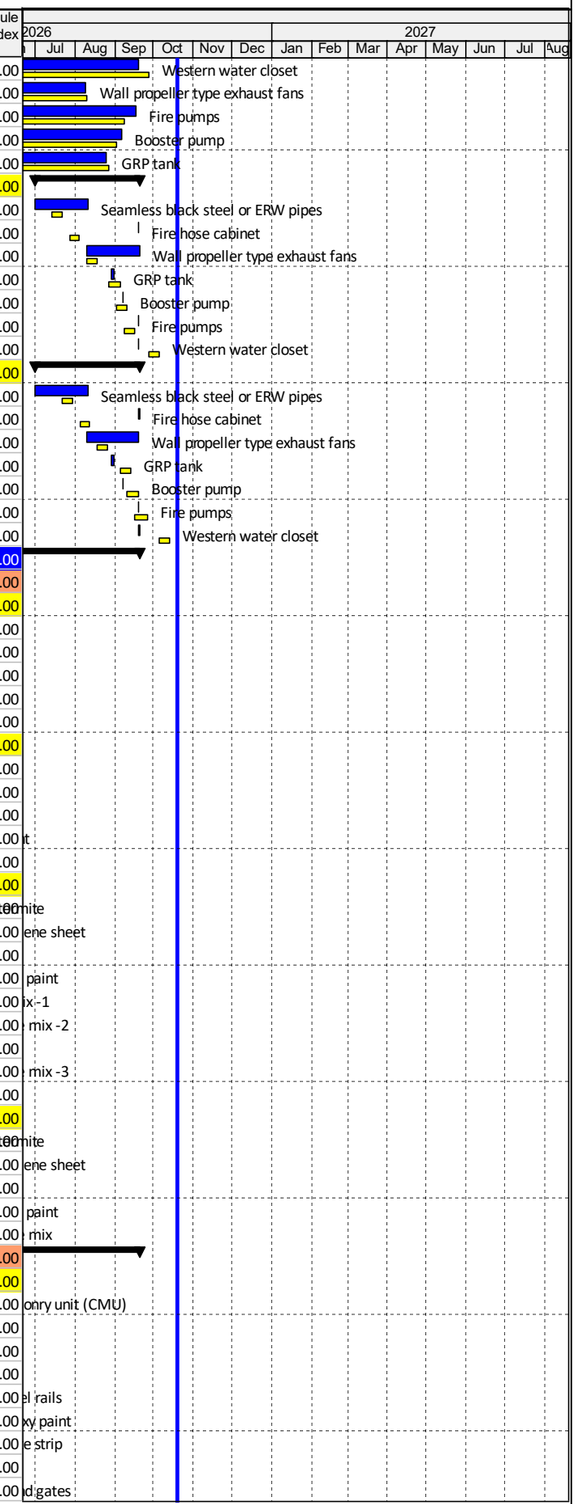


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-PO-A-330 | Gypsum board | 5 | 0.00 | 12-Mar-26 | 22-Mar-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-A-1760 | Identification sign; ID01 & ID02 | 5 | 0.00 | 21-Mar-26 | 25-Mar-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-A-1720 | Aluminum Composite Panel | 5 | 0.00 | 22-Mar-26 | 28-Mar-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 100 | 0.00 | 15-Feb-26 | 02-Jul-26 | 14-Jan-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-200 | Concrete masonry unit (CMU) | 50 | 0.00 | 15-Feb-26 | 19-Apr-26 | 06-Apr-26 | 08-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-210 | Steel ladder | 80 | 0.00 | 21-Feb-26 | 02-Jun-26 | 14-Jan-26 | 22-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-220 | Steel gratings | 80 | 0.00 | 01-Mar-26 | 08-Jun-26 | 06-Apr-26 | 02-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-280 | Ceramic tiles | 80 | 0.00 | 03-Mar-26 | 10-Jun-26 | 06-Apr-26 | 09-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-230 | Steel rails | 80 | 0.00 | 07-Mar-26 | 14-Jun-26 | 06-Apr-26 | 02-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-310 | Epoxy paint | 80 | 0.00 | 07-Mar-26 | 15-Jun-26 | 06-Apr-26 | 20-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-290 | Granite strip | 80 | 0.00 | 09-Mar-26 | 16-Jun-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-320 | Internl paint | 80 | 0.00 | 12-Mar-26 | 21-Jun-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-A-1750 | Steel fence and gates | 80 | 0.00 | 21-Mar-26 | 24-Jun-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-A-330 | Gypsum board | 80 | 0.00 | 22-Mar-26 | 27-Jun-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-A-1760 | Identification sign; ID01 & ID02 | 80 | 0.00 | 26-Mar-26 | 30-Jun-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-A-1720 | Aluminum Composite Panel | 80 | 0.00 | 28-Mar-26 | 02-Jul-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY** | | 59 | 2,031,043.96 | 20-Apr-26 | 11-Jul-26 | 10-Jun-26 | 20-Sep-26 | 2,031,043.96 | 2,031,043.96 | 1.00 |
| DAM3-P-DL-A-200 | Concrete masonry unit (CMU) | 7 | 418,802.40 | 20-Apr-26 | 27-Apr-26 | 10-Jun-26 | 14-Jun-26 | 418,802.40 | 418,802.40 | 1.00 |
| DAM3-P-DL-A-210 | Steel ladder | 7 | 32,307.70 | 03-Jun-26 | 10-Jun-26 | 28-Jul-26 | 28-Jul-26 | 32,307.70 | 32,307.70 | 1.00 |
| DAM3-P-DL-A-220 | Steel gratings | 7 | 21,196.03 | 09-Jun-26 | 16-Jun-26 | 05-Jul-26 | 05-Jul-26 | 21,196.03 | 21,196.03 | 1.00 |
| DAM3-P-DL-A-280 | Ceramic tiles | 7 | 241,008.42 | 11-Jun-26 | 18-Jun-26 | 11-Jun-26 | 15-Jun-26 | 241,008.42 | 241,008.42 | 1.00 |
| DAM3-P-DL-A-230 | Steel rails | 7 | 5,036.93 | 15-Jun-26 | 22-Jun-26 | 28-Jul-26 | 28-Jul-26 | 5,036.93 | 5,036.93 | 1.00 |
| DAM3-P-DL-A-310 | Epoxy paint | 7 | 378,990.27 | 15-Jun-26 | 23-Jun-26 | 23-Jul-26 | 25-Jul-26 | 378,990.27 | 378,990.27 | 1.00 |
| DAM3-P-DL-A-290 | Granite strip | 7 | 2,203.66 | 17-Jun-26 | 24-Jun-26 | 20-Sep-26 | 20-Sep-26 | 2,203.66 | 2,203.66 | 1.00 |
| DAM3-P-DL-A-320 | Internl paint | 7 | 145,026.96 | 21-Jun-26 | 29-Jun-26 | 02-Sep-26 | 20-Sep-26 | 145,026.96 | 145,026.96 | 1.00 |
| DAM3-P-DL-A-1750 | Steel fence and gates | 7 | 23,657.36 | 25-Jun-26 | 02-Jul-26 | 20-Sep-26 | 20-Sep-26 | 23,657.36 | 23,657.36 | 1.00 |
| DAM3-P-DL-A-330 | Gypsum board | 7 | 153,646.35 | 27-Jun-26 | 05-Jul-26 | 14-Sep-26 | 20-Sep-26 | 153,646.35 | 153,646.35 | 1.00 |
| DAM3-P-DL-A-1760 | Identification sign; ID01 & ID02 | 7 | 31,622.71 | 01-Jul-26 | 08-Jul-26 | 20-Sep-26 | 20-Sep-26 | 31,622.71 | 31,622.71 | 1.00 |
| DAM3-P-DL-A-1720 | Aluminum Composite Panel | 7 | 577,545.17 | 02-Jul-26 | 11-Jul-26 | 07-Sep-26 | 20-Sep-26 | 577,545.17 | 577,545.17 | 1.00 |
| **STAGING TIME** | | 58 | 0.00 | 28-Apr-26 | 19-Jul-26 | 15-Jun-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-200 | Concrete masonry unit (CMU) | 7 | 0.00 | 28-Apr-26 | 05-May-26 | 15-Jun-26 | 15-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-210 | Steel ladder | 7 | 0.00 | 11-Jun-26 | 18-Jun-26 | 28-Jul-26 | 28-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-220 | Steel gratings | 7 | 0.00 | 17-Jun-26 | 24-Jun-26 | 05-Jul-26 | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-280 | Ceramic tiles | 7 | 0.00 | 20-Jun-26 | 27-Jun-26 | 15-Jun-26 | 15-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-230 | Steel rails | 7 | 0.00 | 23-Jun-26 | 30-Jun-26 | 28-Jul-26 | 28-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-310 | Epoxy paint | 7 | 0.00 | 23-Jun-26 | 01-Jul-26 | 23-Jul-26 | 25-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-290 | Granite strip | 7 | 0.00 | 25-Jun-26 | 02-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-320 | Internl paint | 7 | 0.00 | 29-Jun-26 | 07-Jul-26 | 02-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-A-1750 | Steel fence and gates | 7 | 0.00 | 04-Jul-26 | 11-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-A-330 | Gypsum board | 7 | 0.00 | 05-Jul-26 | 13-Jul-26 | 14-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-A-1760 | Identification sign; ID01 & ID02 | 7 | 0.00 | 09-Jul-26 | 16-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-A-1720 | Aluminum Composite Panel | 7 | 0.00 | 11-Jul-26 | 19-Jul-26 | 07-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 174 | 1,190,075.32 | 11-Feb-26 | 14-Oct-26 | 05-Apr-26 | 20-Sep-26 | 1,190,075.32 | 1,190,075.32 | 1.00 |
| **PO ISSUE** | | 60 | 0.00 | 11-Feb-26 | 12-May-26 | 05-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-480 | PPR pipes | 5 | 0.00 | 11-Feb-26 | 16-Feb-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-600 | HVAC duct | 5 | 0.00 | 17-Feb-26 | 24-Feb-26 | 05-Apr-26 | 05-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-610 | Flexible duct | 5 | 0.00 | 24-Feb-26 | 02-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-620 | Exhaust diffuser | 5 | 0.00 | 03-Mar-26 | 08-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-490 | Ball valve | 5 | 0.00 | 07-Mar-26 | 11-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-430 | U/G HDPE pipes | 5 | 0.00 | 09-Mar-26 | 14-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-500 | Capped connection | 5 | 0.00 | 12-Mar-26 | 21-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-660 | Warning tapes | 5 | 0.00 | 15-Mar-26 | 23-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-510 | UPVC pipes | 5 | 0.00 | 22-Mar-26 | 26-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-440 | Automatic air release valve | 5 | 0.00 | 24-Mar-26 | 29-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-520 | Roof vent caps | 5 | 0.00 | 28-Mar-26 | 01-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-450 | OS & Y gate valve | 5 | 0.00 | 30-Mar-26 | 04-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-570 | Toilet Fittings | 5 | 0.00 | 30-Mar-26 | 05-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-530 | Floor drain | 5 | 0.00 | 02-Apr-26 | 07-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-460 | Fire alarm check valve | 5 | 0.00 | 05-Apr-26 | 09-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-540 | Gully trap | 5 | 0.00 | 08-Apr-26 | 13-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-550 | Electric water heater | 5 | 0.00 | 14-Apr-26 | 19-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-420 | Water supply valves | 5 | 0.00 | 18-Apr-26 | 23-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |

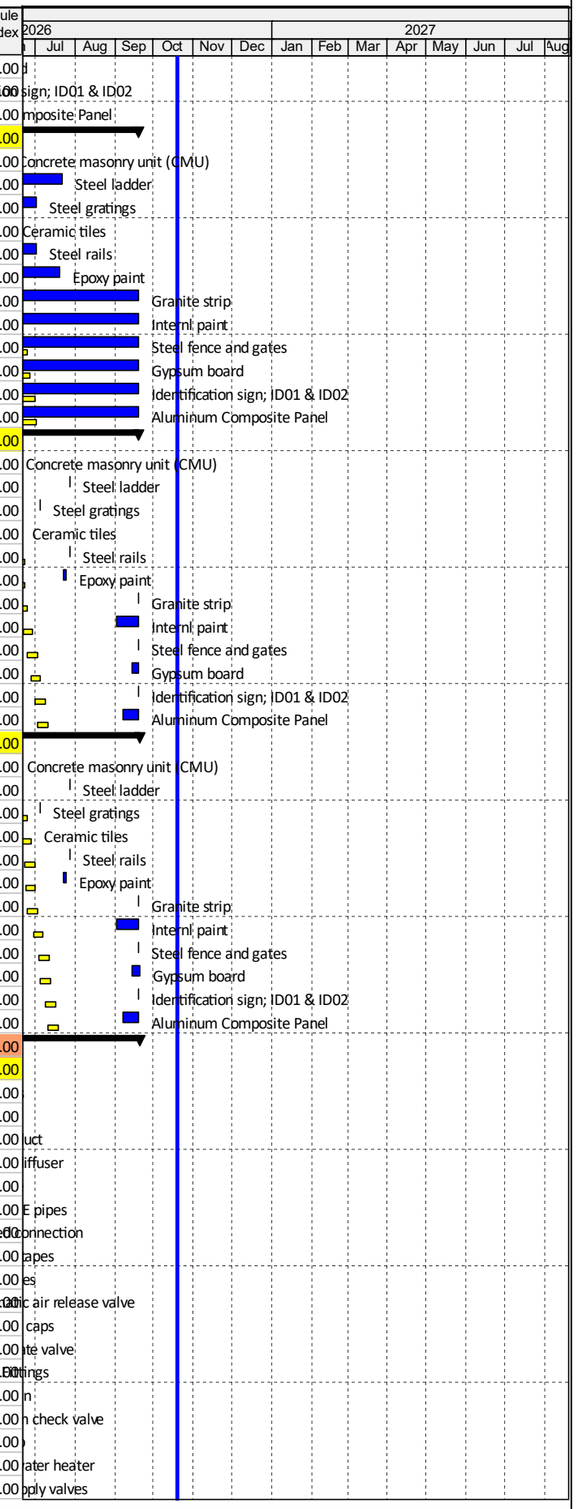




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-PO-M-560 | Bib tap | 5 | 0.00 | 20-Apr-26 | 25-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-M-3410 | Water tap | 5 | 0.00 | 21-Apr-26 | 26-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-580 | Lavatory / wash basin | 5 | 0.00 | 26-Apr-26 | 30-Apr-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-590 | Inline exhaust fans | 5 | 0.00 | 02-May-26 | 06-May-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-M-390 | Fire fighting valves | 5 | 0.00 | 07-May-26 | 12-May-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 169 | 0.00 | 17-Feb-26 | 28-Sep-26 | 06-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-480 | PPR pipes | 80 | 0.00 | 17-Feb-26 | 30-May-26 | 27-Apr-26 | 03-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-600 | HVAC duct | 80 | 0.00 | 24-Feb-26 | 04-Jun-26 | 06-Apr-26 | 01-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-610 | Flexible duct | 80 | 0.00 | 03-Mar-26 | 10-Jun-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-620 | Exhaust diffuser | 80 | 0.00 | 09-Mar-26 | 16-Jun-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-490 | Ball valve | 80 | 0.00 | 12-Mar-26 | 20-Jun-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-430 | U/G HDPE pipes | 80 | 0.00 | 15-Mar-26 | 22-Jun-26 | 27-Apr-26 | 02-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-500 | Capped connection | 80 | 0.00 | 22-Mar-26 | 25-Jun-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-660 | Warning tapes | 80 | 0.00 | 24-Mar-26 | 28-Jun-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-510 | UPVC pipes | 80 | 0.00 | 28-Mar-26 | 01-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-440 | Automatic air release valve | 80 | 0.00 | 30-Mar-26 | 04-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-520 | Roof vent caps | 80 | 0.00 | 02-Apr-26 | 07-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-450 | OS & Y gate valve | 80 | 0.00 | 05-Apr-26 | 09-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-570 | Toilet Fittings | 5 | 0.00 | 05-Apr-26 | 11-Apr-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-530 | Floor drain | 80 | 0.00 | 08-Apr-26 | 13-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-460 | Fire alarm check valve | 80 | 0.00 | 11-Apr-26 | 15-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-540 | Gully trap | 80 | 0.00 | 14-Apr-26 | 19-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-550 | Electric water heater | 120 | 0.00 | 20-Apr-26 | 09-Sep-26 | 27-Apr-26 | 13-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-420 | Water supply valves | 80 | 0.00 | 23-Apr-26 | 29-Jul-26 | 27-Apr-26 | 02-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-560 | Bib tap | 80 | 0.00 | 26-Apr-26 | 30-Jul-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-M-3410 | Water tap | 80 | 0.00 | 27-Apr-26 | 01-Aug-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-580 | Lavatory / wash basin | 80 | 0.00 | 02-May-26 | 05-Aug-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-590 | Inline exhaust fans | 120 | 0.00 | 07-May-26 | 28-Sep-26 | 27-Apr-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-M-390 | Fire fighting valves | 80 | 0.00 | 13-May-26 | 17-Aug-26 | 27-Apr-26 | 09-Aug-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY** | | 60 | 1,190,075.32 | 11-Apr-26 | 06-Oct-26 | 10-May-26 | 20-Sep-26 | 1,190,075.32 | 1,190,075.32 | 1.00 |
| DAM3-P-DL-M-570 | Toilet Fittings | 5 | 75,460.88 | 11-Apr-26 | 16-Apr-26 | 15-Sep-26 | 20-Sep-26 | 75,460.88 | 75,460.88 | 1.00 |
| DAM3-P-DL-M-480 | PPR pipes | 7 | 76,567.93 | 31-May-26 | 07-Jun-26 | 05-Jul-26 | 15-Sep-26 | 76,567.93 | 76,567.93 | 1.00 |
| DAM3-P-DL-M-600 | HVAC duct | 7 | 490,860.48 | 06-Jun-26 | 13-Jun-26 | 04-Jun-26 | 14-Jun-26 | 490,860.48 | 490,860.48 | 1.00 |
| DAM3-P-DL-M-610 | Flexible duct | 7 | 69,629.67 | 11-Jun-26 | 18-Jun-26 | 16-Sep-26 | 20-Sep-26 | 69,629.67 | 69,629.67 | 1.00 |
| DAM3-P-DL-M-620 | Exhaust diffuser | 7 | 7,040.00 | 17-Jun-26 | 24-Jun-26 | 20-Sep-26 | 20-Sep-26 | 7,040.00 | 7,040.00 | 1.00 |
| DAM3-P-DL-M-490 | Ball valve | 7 | 14,232.16 | 21-Jun-26 | 28-Jun-26 | 18-Jul-26 | 18-Jul-26 | 14,232.16 | 14,232.16 | 1.00 |
| DAM3-P-DL-M-430 | U/G HDPE pipes | 7 | 49,971.54 | 23-Jun-26 | 30-Jun-26 | 01-Aug-26 | 20-Sep-26 | 49,971.54 | 49,971.54 | 1.00 |
| DAM3-P-DL-M-500 | Capped connection | 7 | 913.27 | 27-Jun-26 | 04-Jul-26 | 05-Jul-26 | 14-Sep-26 | 913.27 | 913.27 | 1.00 |
| DAM3-P-DL-M-660 | Warning tapes | 7 | 14,077.01 | 29-Jun-26 | 06-Jul-26 | 05-Jul-26 | 05-Jul-26 | 14,077.01 | 14,077.01 | 1.00 |
| DAM3-P-DL-M-510 | UPVC pipes | 7 | 126,693.12 | 02-Jul-26 | 09-Jul-26 | 10-May-26 | 19-May-26 | 126,693.12 | 126,693.12 | 1.00 |
| DAM3-P-DL-M-440 | Automatic air release valve | 7 | 1,769.50 | 05-Jul-26 | 12-Jul-26 | 20-Sep-26 | 20-Sep-26 | 1,769.50 | 1,769.50 | 1.00 |
| DAM3-P-DL-M-520 | Roof vent caps | 7 | 3,044.27 | 08-Jul-26 | 15-Jul-26 | 20-Sep-26 | 20-Sep-26 | 3,044.27 | 3,044.27 | 1.00 |
| DAM3-P-DL-M-450 | OS & Y gate valve | 7 | 11,631.51 | 11-Jul-26 | 18-Jul-26 | 15-Jul-26 | 20-Sep-26 | 11,631.51 | 11,631.51 | 1.00 |
| DAM3-P-DL-M-530 | Floor drain | 7 | 74,093.27 | 14-Jul-26 | 21-Jul-26 | 16-Sep-26 | 20-Sep-26 | 74,093.27 | 74,093.27 | 1.00 |
| DAM3-P-DL-M-460 | Fire alarm check valve | 7 | 26,656.72 | 16-Jul-26 | 23-Jul-26 | 20-Sep-26 | 20-Sep-26 | 26,656.72 | 26,656.72 | 1.00 |
| DAM3-P-DL-M-540 | Gully trap | 7 | 15,982.56 | 20-Jul-26 | 27-Jul-26 | 06-Sep-26 | 20-Sep-26 | 15,982.56 | 15,982.56 | 1.00 |
| DAM3-P-DL-M-420 | Water supply valves | 7 | 3,114.56 | 29-Jul-26 | 06-Aug-26 | 05-Jul-26 | 15-Sep-26 | 3,114.56 | 3,114.56 | 1.00 |
| DAM3-P-DL-M-560 | Bib tap | 7 | 6,240.96 | 01-Aug-26 | 08-Aug-26 | 20-Sep-26 | 20-Sep-26 | 6,240.96 | 6,240.96 | 1.00 |
| DAM3-P-DL-M-3410 | Water tap | 7 | 9,437.47 | 02-Aug-26 | 09-Aug-26 | 20-Sep-26 | 20-Sep-26 | 9,437.47 | 9,437.47 | 1.00 |
| DAM3-P-DL-M-580 | Lavatory / wash basin | 7 | 70,323.44 | 06-Aug-26 | 13-Aug-26 | 16-Sep-26 | 20-Sep-26 | 70,323.44 | 70,323.44 | 1.00 |
| DAM3-P-DL-M-390 | Fire fighting valves | 7 | 8,885.58 | 18-Aug-26 | 25-Aug-26 | 10-Aug-26 | 10-Aug-26 | 8,885.58 | 8,885.58 | 1.00 |
| DAM3-P-DL-M-550 | Electric water heater | 7 | 5,974.50 | 10-Sep-26 | 17-Sep-26 | 16-Sep-26 | 16-Sep-26 | 5,974.50 | 5,974.50 | 1.00 |
| DAM3-P-DL-M-590 | Inline exhaust fans | 7 | 27,474.92 | 29-Sep-26 | 06-Oct-26 | 05-Sep-26 | 20-Sep-26 | 27,474.92 | 27,474.92 | 1.00 |
| **STAGING TIME** | | 67 | 0.00 | 16-Apr-26 | 14-Oct-26 | 10-May-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-570 | Toilet Fittings | 5 | 0.00 | 16-Apr-26 | 22-Apr-26 | 15-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-480 | PPR pipes | 7 | 0.00 | 08-Jun-26 | 15-Jun-26 | 05-Jul-26 | 15-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-600 | HVAC duct | 7 | 0.00 | 14-Jun-26 | 21-Jun-26 | 04-Jun-26 | 14-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-610 | Flexible duct | 7 | 0.00 | 20-Jun-26 | 27-Jun-26 | 16-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-620 | Exhaust diffuser | 7 | 0.00 | 25-Jun-26 | 02-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-490 | Ball valve | 7 | 0.00 | 29-Jun-26 | 06-Jul-26 | 18-Jul-26 | 18-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-430 | U/G HDPE pipes | 7 | 0.00 | 01-Jul-26 | 08-Jul-26 | 01-Aug-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-500 | Capped connection | 7 | 0.00 | 05-Jul-26 | 12-Jul-26 | 05-Jul-26 | 14-Sep-26 | 0.00 | 0.00 | 0.00 |

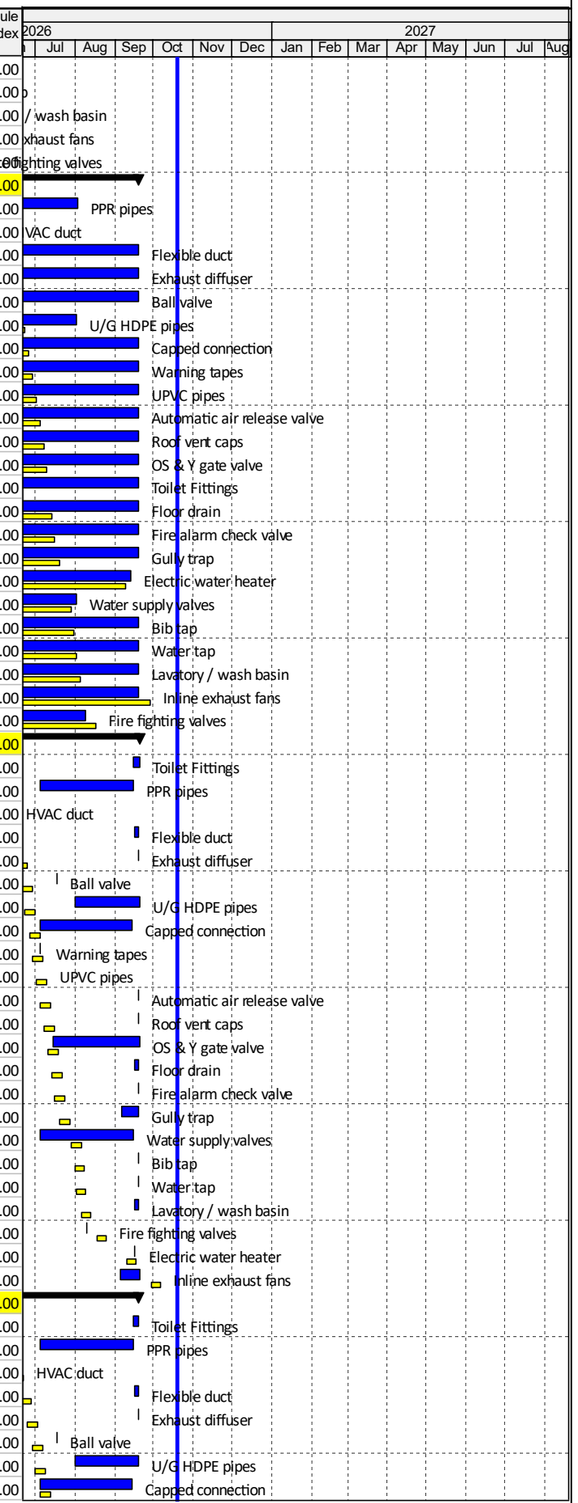





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-ST-M-660 | Warning tapes | 7 | 0.00 | 07-Jul-26 | 14-Jul-26 | 05-Jul-26 | 05-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-510 | UPVC pipes | 7 | 0.00 | 11-Jul-26 | 18-Jul-26 | 10-May-26 | 19-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-440 | Automatic air release valve | 7 | 0.00 | 13-Jul-26 | 20-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-520 | Roof vent caps | 7 | 0.00 | 16-Jul-26 | 23-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-450 | OS & Y gate valve | 7 | 0.00 | 19-Jul-26 | 26-Jul-26 | 15-Jul-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-530 | Floor drain | 7 | 0.00 | 22-Jul-26 | 29-Jul-26 | 16-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-460 | Fire alarm check valve | 7 | 0.00 | 25-Jul-26 | 01-Aug-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-540 | Gully trap | 7 | 0.00 | 28-Jul-26 | 04-Aug-26 | 06-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-420 | Water supply valves | 7 | 0.00 | 06-Aug-26 | 15-Aug-26 | 05-Jul-26 | 15-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-560 | Bib tap | 7 | 0.00 | 09-Aug-26 | 16-Aug-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-M-3410 | Water tap | 7 | 0.00 | 10-Aug-26 | 17-Aug-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-580 | Lavatory / wash basin | 7 | 0.00 | 15-Aug-26 | 22-Aug-26 | 16-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-390 | Fire fighting valves | 7 | 0.00 | 26-Aug-26 | 02-Sep-26 | 10-Aug-26 | 10-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-550 | Electric water heater | 7 | 0.00 | 19-Sep-26 | 27-Sep-26 | 16-Sep-26 | 16-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-M-590 | Inline exhaust fans | 7 | 0.00 | 07-Oct-26 | 14-Oct-26 | 05-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 147 | 819,995.13 | 11-Feb-26 | 01-Aug-26 | 10-Mar-26 | 20-Sep-26 | 819,995.13 | 819,995.13 | 1.00 |
| **PO ISSUE** | | 68 | 0.00 | 11-Feb-26 | 09-Apr-26 | 10-Mar-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-310 | PVC conduits | 5 | 0.00 | 11-Feb-26 | 16-Feb-26 | 10-Mar-26 | 10-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-320 | Wires | 5 | 0.00 | 17-Feb-26 | 24-Feb-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-PO-E-210 | Cable Tray | 5 | 0.00 | 24-Feb-26 | 02-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-340 | Grounding system | 5 | 0.00 | 03-Mar-26 | 08-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-350 | Wiring devices | 5 | 0.00 | 09-Mar-26 | 14-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-370 | HDPE ducts | 5 | 0.00 | 15-Mar-26 | 23-Mar-26 | 26-Apr-26 | 26-Apr-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-290 | Low Voltage cables | 5 | 0.00 | 24-Mar-26 | 29-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-300 | Disconnect switches | 5 | 0.00 | 30-Mar-26 | 04-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-E-330 | Wall mounted, duplex, telephone and data outlet | 5 | 0.00 | 05-Apr-26 | 09-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 142 | 0.00 | 17-Feb-26 | 15-Jul-26 | 11-Mar-26 | 16-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-310 | PVC conduits | 60 | 0.00 | 17-Feb-26 | 03-May-26 | 11-Mar-26 | 02-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-320 | Wires | 80 | 0.00 | 24-Feb-26 | 04-Jun-26 | 28-Jun-26 | 16-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-MF-E-210 | Cable Tray | 80 | 0.00 | 03-Mar-26 | 10-Jun-26 | 04-Jul-26 | 16-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-340 | Grounding system | 80 | 0.00 | 09-Mar-26 | 16-Jun-26 | 27-Apr-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-350 | Wiring devices | 80 | 0.00 | 15-Mar-26 | 22-Jun-26 | 09-Jul-26 | 16-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-370 | HDPE ducts | 80 | 0.00 | 24-Mar-26 | 28-Jun-26 | 27-Apr-26 | 03-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-290 | Low Voltage cables | 80 | 0.00 | 30-Mar-26 | 04-Jul-26 | 15-Jul-26 | 22-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-300 | Disconnect switches | 80 | 0.00 | 05-Apr-26 | 09-Jul-26 | 21-Jul-26 | 22-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-E-330 | Wall mounted, duplex, telephone and data outlet | 80 | 0.00 | 11-Apr-26 | 15-Jul-26 | 27-Jul-26 | 16-Sep-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY** | | 65 | 819,995.13 | 04-May-26 | 23-Jul-26 | 03-May-26 | 20-Sep-26 | 819,995.13 | 819,995.13 | 1.00 |
| DAM3-P-DL-E-310 | PVC conduits | 7 | 15,738.66 | 04-May-26 | 11-May-26 | 03-May-26 | 20-May-26 | 15,738.66 | 15,738.66 | 1.00 |
| DAM3-P-DL-E-320 | Wires | 7 | 7,379.37 | 06-Jun-26 | 13-Jun-26 | 20-Sep-26 | 20-Sep-26 | 7,379.37 | 7,379.37 | 1.00 |
| DAM3-P-DL-E-2100 | Cable Tray | 7 | 1,063.80 | 11-Jun-26 | 18-Jun-26 | 20-Sep-26 | 20-Sep-26 | 1,063.80 | 1,063.80 | 1.00 |
| DAM3-P-DL-E-340 | Grounding system | 7 | 65,141.26 | 17-Jun-26 | 24-Jun-26 | 10-May-26 | 19-May-26 | 65,141.26 | 65,141.26 | 1.00 |
| DAM3-P-DL-E-350 | Wiring devices | 7 | 66,414.34 | 23-Jun-26 | 30-Jun-26 | 17-Sep-26 | 20-Sep-26 | 66,414.34 | 66,414.34 | 1.00 |
| DAM3-P-DL-E-370 | HDPE ducts | 7 | 176,019.75 | 29-Jun-26 | 06-Jul-26 | 10-May-26 | 19-May-26 | 176,019.75 | 176,019.75 | 1.00 |
| DAM3-P-DL-E-290 | Low Voltage cables | 7 | 299,034.47 | 05-Jul-26 | 12-Jul-26 | 23-Jul-26 | 25-Jul-26 | 299,034.47 | 299,034.47 | 1.00 |
| DAM3-P-DL-E-300 | Disconnect switches | 7 | 100,576.04 | 11-Jul-26 | 18-Jul-26 | 23-Jul-26 | 25-Jul-26 | 100,576.04 | 100,576.04 | 1.00 |
| DAM3-P-DL-E-330 | Wall mounted, duplex, telephone and data outlet | 7 | 88,627.44 | 16-Jul-26 | 23-Jul-26 | 17-Sep-26 | 20-Sep-26 | 88,627.44 | 88,627.44 | 1.00 |
| **STAGING TIME** | | 75 | 0.00 | 12-May-26 | 01-Aug-26 | 03-May-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-310 | PVC conduits | 7 | 0.00 | 12-May-26 | 19-May-26 | 03-May-26 | 20-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-320 | Wires | 7 | 0.00 | 14-Jun-26 | 21-Jun-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-E-ST-E-210 | Cable Tray | 7 | 0.00 | 20-Jun-26 | 27-Jun-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-340 | Grounding system | 7 | 0.00 | 25-Jun-26 | 02-Jul-26 | 10-May-26 | 19-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-350 | Wiring devices | 7 | 0.00 | 01-Jul-26 | 08-Jul-26 | 17-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-370 | HDPE ducts | 7 | 0.00 | 07-Jul-26 | 14-Jul-26 | 10-May-26 | 19-May-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-290 | Low Voltage cables | 7 | 0.00 | 13-Jul-26 | 20-Jul-26 | 25-Jul-26 | 25-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-300 | Disconnect switches | 7 | 0.00 | 19-Jul-26 | 26-Jul-26 | 25-Jul-26 | 25-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-E-330 | Wall mounted, duplex, telephone and data outlet | 7 | 0.00 | 25-Jul-26 | 01-Aug-26 | 17-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 119 | 2,215,885.18 | 07-Apr-26 | 03-Sep-26 | 02-Mar-26 | 21-Sep-26 | 2,215,885.18 | 2,215,885.18 | 1.00 |
| **PO ISSUE** | | 23 | 0.00 | 07-Apr-26 | 28-Apr-26 | 02-Mar-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EX-80 | Asphalt works | 5 | 0.00 | 07-Apr-26 | 12-Apr-26 | 02-Mar-26 | 02-Mar-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EX-90 | Concrete parking bumper | 5 | 0.00 | 08-Apr-26 | 14-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EX-100 | Road markings | 5 | 0.00 | 11-Apr-26 | 16-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EX-110 | Road signs | 5 | 0.00 | 13-Apr-26 | 19-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |

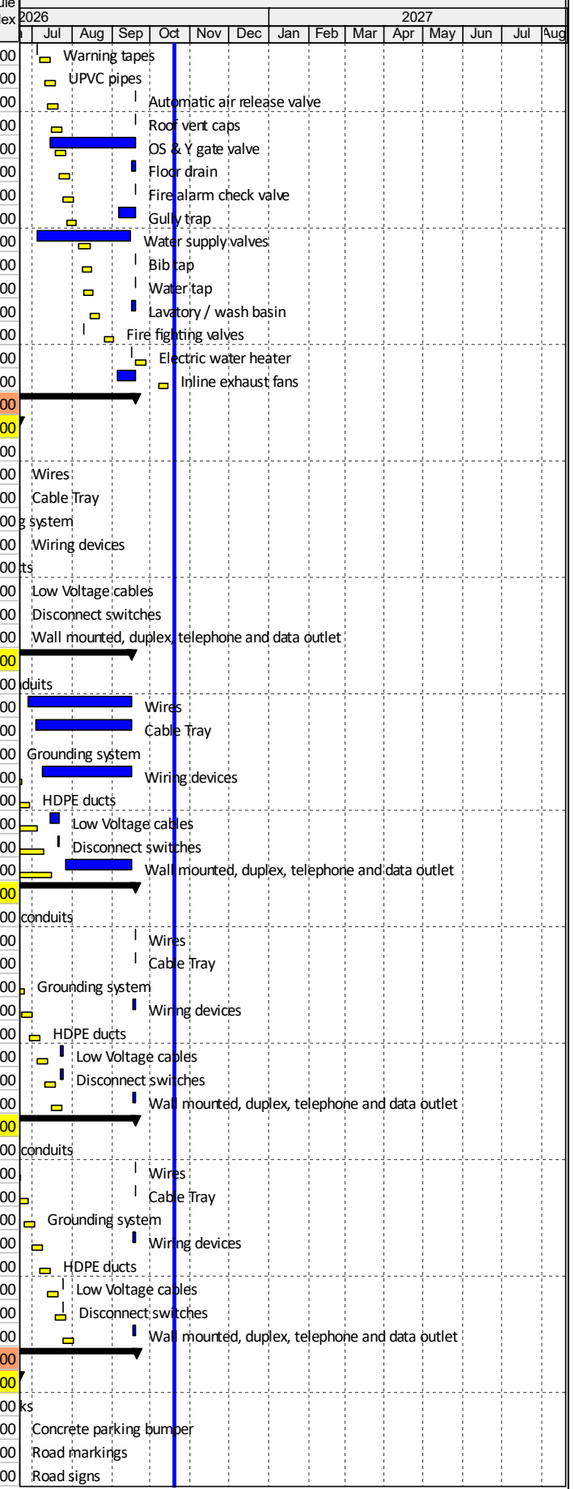




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-PO-EX-140 | Curbstones | 5 | 0.00 | 18-Apr-26 | 23-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EX-150 | Gravel bedding | 5 | 0.00 | 21-Apr-26 | 26-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EX-130 | Interlock tiles | 5 | 0.00 | 22-Apr-26 | 28-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 111 | 0.00 | 13-Apr-26 | 15-Aug-26 | 03-Mar-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-80 | Asphalt works | 100 | 0.00 | 13-Apr-26 | 10-Aug-26 | 03-Mar-26 | 07-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-90 | Concrete parking bumper | 90 | 0.00 | 14-Apr-26 | 01-Aug-26 | 28-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-100 | Road markings | 90 | 0.00 | 16-Apr-26 | 03-Aug-26 | 28-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-110 | Road signs | 90 | 0.00 | 19-Apr-26 | 05-Aug-26 | 28-Jun-26 | 17-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-140 | Curbstones | 90 | 0.00 | 23-Apr-26 | 10-Aug-26 | 28-Jun-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-150 | Gravel bedding | 90 | 0.00 | 27-Apr-26 | 12-Aug-26 | 28-Jun-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EX-130 | Interlock tiles | 90 | 0.00 | 28-Apr-26 | 15-Aug-26 | 21-Jul-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY** | | 27 | 2,215,885.18 | 01-Aug-26 | 23-Aug-26 | 08-Jun-26 | 21-Sep-26 | 2,215,885.18 | 2,215,885.18 | 1.00 |
| DAM3-P-DL-EX-90 | Concrete parking bumper | 7 | 9,558.14 | 01-Aug-26 | 09-Aug-26 | 21-Sep-26 | 21-Sep-26 | 9,558.14 | 9,558.14 | 1.00 |
| DAM3-P-DL-EX-100 | Road markings | 7 | 11,308.91 | 03-Aug-26 | 11-Aug-26 | 21-Sep-26 | 21-Sep-26 | 11,308.91 | 11,308.91 | 1.00 |
| DAM3-P-DL-EX-110 | Road signs | 7 | 31,028.59 | 05-Aug-26 | 13-Aug-26 | 20-Sep-26 | 20-Sep-26 | 31,028.59 | 31,028.59 | 1.00 |
| DAM3-P-DL-EX-140 | Curbstones | 7 | 86,912.40 | 10-Aug-26 | 18-Aug-26 | 17-Sep-26 | 20-Sep-26 | 86,912.40 | 86,912.40 | 1.00 |
| DAM3-P-DL-EX-80 | Asphalt works | 7 | 1,868,985.04 | 11-Aug-26 | 18-Aug-26 | 08-Jun-26 | 17-Jun-26 | 1,868,985.04 | 1,868,985.04 | 1.00 |
| DAM3-P-DL-EX-150 | Gravel bedding | 7 | 66,111.93 | 13-Aug-26 | 20-Aug-26 | 17-Sep-26 | 21-Sep-26 | 66,111.93 | 66,111.93 | 1.00 |
| DAM3-P-DL-EX-130 | Interlock tiles | 7 | 141,980.16 | 15-Aug-26 | 23-Aug-26 | 17-Sep-26 | 20-Sep-26 | 141,980.16 | 141,980.16 | 1.00 |
| **STAGING TIME** | | 41 | 0.00 | 09-Aug-26 | 03-Sep-26 | 08-Jun-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-90 | Concrete parking bumper | 7 | 0.00 | 09-Aug-26 | 17-Aug-26 | 21-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-100 | Road markings | 7 | 0.00 | 11-Aug-26 | 19-Aug-26 | 21-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-110 | Road signs | 7 | 0.00 | 13-Aug-26 | 22-Aug-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-80 | Asphalt works | 7 | 0.00 | 19-Aug-26 | 26-Aug-26 | 08-Jun-26 | 08-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-150 | Gravel bedding | 7 | 0.00 | 22-Aug-26 | 29-Aug-26 | 17-Sep-26 | 21-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-130 | Interlock tiles | 7 | 0.00 | 23-Aug-26 | 31-Aug-26 | 17-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EX-140 | Curbstones | 7 | 0.00 | 27-Aug-26 | 03-Sep-26 | 17-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| **ENVIRONMENTAL** | | 151 | 384,877.22 | 11-Feb-26 | 06-Aug-26 | 21-Jun-26 | 20-Sep-26 | 384,877.22 | 384,877.22 | 1.00 |
| **PO ISSUE** | | 40 | 0.00 | 11-Feb-26 | 04-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-100 | HDPE pipes for fire system | 5 | 0.00 | 11-Feb-26 | 16-Feb-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-110 | Directly buried gate valve for fire system | 5 | 0.00 | 17-Feb-26 | 24-Feb-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-120 | HDPE pipes for water supply system | 5 | 0.00 | 24-Feb-26 | 02-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-130 | Directly buried gate valve for water system | 5 | 0.00 | 03-Mar-26 | 08-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-140 | Air valve | 5 | 0.00 | 09-Mar-26 | 14-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-150 | Washout valve | 5 | 0.00 | 15-Mar-26 | 23-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-160 | Gate valve | 5 | 0.00 | 24-Mar-26 | 29-Mar-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-PO-EN-170 | UPVC pipes | 5 | 0.00 | 30-Mar-26 | 04-Apr-26 | 21-Jun-26 | 21-Jun-26 | 0.00 | 0.00 | 0.00 |
| **MANUFACTURING** | | 133 | 0.00 | 17-Feb-26 | 21-Jul-26 | 22-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-100 | HDPE pipes for fire system | 90 | 0.00 | 17-Feb-26 | 10-Jun-26 | 28-Jun-26 | 23-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-110 | Directly buried gate valve for fire system | 90 | 0.00 | 24-Feb-26 | 16-Jun-26 | 04-Jul-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-120 | HDPE pipes for water supply system | 90 | 0.00 | 03-Mar-26 | 22-Jun-26 | 22-Jun-26 | 15-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-130 | Directly buried gate valve for water system | 90 | 0.00 | 09-Mar-26 | 28-Jun-26 | 22-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-140 | Air valve | 90 | 0.00 | 15-Mar-26 | 04-Jul-26 | 22-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-150 | Washout valve | 90 | 0.00 | 24-Mar-26 | 09-Jul-26 | 22-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-160 | Gate valve | 90 | 0.00 | 30-Mar-26 | 15-Jul-26 | 22-Jun-26 | 19-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-MF-EN-170 | UPVC pipes | 90 | 0.00 | 05-Apr-26 | 21-Jul-26 | 22-Jun-26 | 25-Jul-26 | 0.00 | 0.00 | 0.00 |
| **DELIVERY** | | 107 | 384,877.22 | 11-Jun-26 | 29-Jul-26 | 25-Jul-26 | 20-Sep-26 | 384,877.22 | 384,877.22 | 1.00 |
| DAM3-P-DL-EN-100 | HDPE pipes for fire system | 7 | 144,972.85 | 11-Jun-26 | 18-Jun-26 | 25-Jul-26 | 26-Jul-26 | 144,972.85 | 144,972.85 | 1.00 |
| DAM3-P-DL-EN-110 | Directly buried gate valve for fire system | 7 | 7,270.01 | 17-Jun-26 | 24-Jun-26 | 20-Sep-26 | 20-Sep-26 | 7,270.01 | 7,270.01 | 1.00 |
| DAM3-P-DL-EN-120 | HDPE pipes for water supply system | 7 | 10,655.04 | 23-Jun-26 | 30-Jun-26 | 17-Aug-26 | 17-Aug-26 | 10,655.04 | 10,655.04 | 1.00 |
| DAM3-P-DL-EN-130 | Directly buried gate valve for water system | 7 | 16,098.52 | 29-Jun-26 | 06-Jul-26 | 20-Sep-26 | 20-Sep-26 | 16,098.52 | 16,098.52 | 1.00 |
| DAM3-P-DL-EN-140 | Air valve | 7 | 13,087.07 | 05-Jul-26 | 12-Jul-26 | 20-Sep-26 | 20-Sep-26 | 13,087.07 | 13,087.07 | 1.00 |
| DAM3-P-DL-EN-150 | Washout valve | 7 | 15,346.94 | 11-Jul-26 | 18-Jul-26 | 20-Sep-26 | 20-Sep-26 | 15,346.94 | 15,346.94 | 1.00 |
| DAM3-P-DL-EN-160 | Gate valve | 7 | 42,658.36 | 16-Jul-26 | 23-Jul-26 | 05-Sep-26 | 20-Sep-26 | 42,658.36 | 42,658.36 | 1.00 |
| DAM3-P-DL-EN-170 | UPVC pipes | 7 | 134,788.44 | 22-Jul-26 | 29-Jul-26 | 26-Jul-26 | 26-Jul-26 | 134,788.44 | 134,788.44 | 1.00 |
| **STAGING TIME** | | 107 | 0.00 | 20-Jun-26 | 06-Aug-26 | 25-Jul-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-100 | HDPE pipes for fire system | 7 | 0.00 | 20-Jun-26 | 27-Jun-26 | 25-Jul-26 | 26-Jul-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-110 | Directly buried gate valve for fire system | 7 | 0.00 | 25-Jun-26 | 02-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-120 | HDPE pipes for water supply system | 7 | 0.00 | 01-Jul-26 | 08-Jul-26 | 17-Aug-26 | 17-Aug-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-130 | Directly buried gate valve for water system | 7 | 0.00 | 07-Jul-26 | 14-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-140 | Air valve | 7 | 0.00 | 13-Jul-26 | 20-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-150 | Washout valve | 7 | 0.00 | 19-Jul-26 | 26-Jul-26 | 20-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |

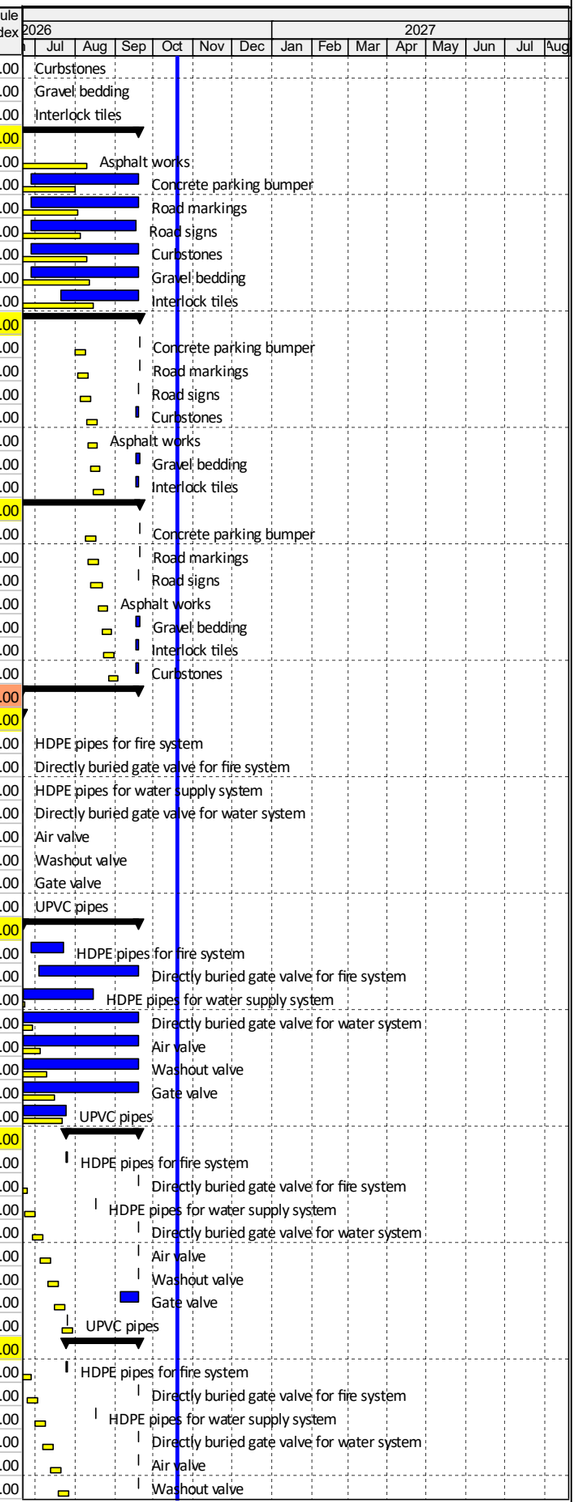





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-P-ST-EN-160 | Gate valve | 7 | 0.00 | 25-Jul-26 | 01-Aug-26 | 05-Sep-26 | 20-Sep-26 | 0.00 | 0.00 | 0.00 |
| DAM3-P-ST-EN-170 | UPVC pipes | 7 | 0.00 | 30-Jul-26 | 06-Aug-26 | 26-Jul-26 | 26-Jul-26 | 0.00 | 0.00 | 0.00 |
| **CONSTRUCTION (67%)** | | 321 | 64,317,671.75 | 27-Jan-26 | 21-Feb-27 | 14-Jan-26 | | 40,977,321.22 | 40,781,573.10 | 1.00 |
| **RBF 900 SQM FACTORIES** | | 321 | 55,841,646.40 | 27-Jan-26 | 16-Feb-27 | 14-Jan-26 | | 38,968,435.06 | 38,012,958.67 | 0.98 |
| **SITE WORKS** | | 16 | 10,892.39 | 27-Jan-26 | 25-Feb-26 | 14-Jan-26 | 31-Jan-26 | 10,892.39 | 10,892.39 | 1.00 |
| DAM3-C-GEN-10 | Initial Site Survey and Setting out | 12 | 0.00 | 27-Jan-26 | 09-Feb-26 | 19-Jan-26 | 24-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-C-GEN-88 | Demolition of the existing pavement | 12 | 10,892.39 | 10-Feb-26 | 25-Feb-26 | 14-Jan-26 | 31-Jan-26 | 10,892.39 | 10,892.39 | 1.00 |
| **BLOCK B6** | | 264 | 5,075,523.09 | 10-Feb-26 | 23-Nov-26 | 15-Feb-26 | | 4,056,159.13 | 3,289,562.29 | 0.81 |
| **STRUCTURAL** | | 201 | 1,389,042.53 | 10-Feb-26 | 07-Jul-26 | 15-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 74 | 597,655.16 | 10-Feb-26 | 25-Mar-26 | 15-Feb-26 | 10-May-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B6-S-160 | Excavation for footings | 8 | 89,859.61 | 10-Feb-26 | 19-Feb-26 | 15-Feb-26 | 24-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B6-S-6143 | Soil replacement - rock fill | 6 | 179,061.91 | 19-Feb-26 | 28-Feb-26 | 02-Apr-26 | 04-Apr-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B6-S-6153 | Engineering fill | 6 | 46,046.19 | 01-Mar-26 | 07-Mar-26 | 12-Apr-26 | 13-Apr-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B6-S-777 | Anti Termite Below Footings | 1 | 11,905.55 | 08-Mar-26 | 08-Mar-26 | 22-Apr-26 | 22-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B6-S-687 | Vapour Barrier for Footings | 1 | 7,940.10 | 09-Mar-26 | 09-Mar-26 | 22-Apr-26 | 22-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B6-S-537 | Lean Concrete Below Footings | 2 | 8,229.34 | 10-Mar-26 | 11-Mar-26 | 22-Apr-26 | 22-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B6-S-587 | Rebar for Footings | 4 | 101,844.98 | 12-Mar-26 | 16-Mar-26 | 02-May-26 | 05-May-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B6-S-597 | Formwork for Footings | 4 | 25,461.25 | 21-Mar-26 | 24-Mar-26 | 04-May-26 | 09-May-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B6-S-547 | Pouring Concrete for Footings | 1 | 127,306.23 | 25-Mar-26 | 25-Mar-26 | 10-May-26 | 10-May-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 12 | 120,554.54 | 26-Mar-26 | 11-Apr-26 | 05-May-26 | 01-Jun-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B6-S-637 | Rebar for column neck | 2 | 14,919.19 | 26-Mar-26 | 28-Mar-26 | 05-May-26 | 09-May-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B6-S-647 | Formwork for column neck | 2 | 9,946.13 | 29-Mar-26 | 30-Mar-26 | 12-May-26 | 16-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B6-S-627 | Pouring Concrete for column neck | 1 | 24,865.31 | 31-Mar-26 | 31-Mar-26 | 17-May-26 | 17-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B6-S-677 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 01-Apr-26 | 02-Apr-26 | 18-May-26 | 19-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B6-S-737 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 04-Apr-26 | 11-Apr-26 | 24-May-26 | 01-Jun-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 17 | 171,632.86 | 12-Apr-26 | 28-Apr-26 | 04-Jun-26 | 22-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B6-S-787 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 12-Apr-26 | 12-Apr-26 | 04-Jun-26 | 04-Jun-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B6-S-707 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 13-Apr-26 | 14-Apr-26 | 04-Jun-26 | 04-Jun-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B6-S-557 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 15-Apr-26 | 16-Apr-26 | 04-Jun-26 | 04-Jun-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B6-S-607 | Rebar for Grade Beams | 5 | 27,194.46 | 18-Apr-26 | 22-Apr-26 | 08-Jun-26 | 09-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B6-S-617 | Formwork for Grade Beams | 2 | 6,798.61 | 23-Apr-26 | 25-Apr-26 | 10-Jun-26 | 14-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B6-S-767 | Anchor bolts installation | 2 | 57,238.83 | 23-Apr-26 | 25-Apr-26 | 11-Jun-26 | 13-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B6-S-567 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 26-Apr-26 | 26-Apr-26 | 15-Jun-26 | 15-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B6-S-717 | Damp proof /Bitumin paint on Grade Beams | 2 | 24,777.73 | 27-Apr-26 | 28-Apr-26 | 20-Jun-26 | 22-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 100 | 397,232.98 | 29-Apr-26 | 07-Jul-26 | 28-Jun-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B6-S-747 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 29-Apr-26 | 06-May-26 | 28-Jun-26 | 06-Jul-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B6-S-697 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 07-May-26 | 07-May-26 | 18-Aug-26 | 23-Aug-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B6-S-727 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 09-May-26 | 10-May-26 | 18-Aug-26 | 23-Aug-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B6-S-577 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 11-May-26 | 14-May-26 | 18-Aug-26 | 23-Aug-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B6-S-757 | Concrete pad | 7 | 907.11 | 30-Jun-26 | 07-Jul-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 65 | 101,966.98 | 07-May-26 | 07-Jun-26 | 08-Jun-26 | 06-Oct-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B6-S-5101 | Rebar for column | 5 | 20,144.05 | 07-May-26 | 12-May-26 | 18-Jul-26 | 20-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B6-S-5102 | Formwork for column | 4 | 5,036.01 | 13-May-26 | 17-May-26 | 23-Jul-26 | 11-Aug-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B6-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 18-May-26 | 18-May-26 | 26-Jul-26 | 13-Aug-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B6-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 19-May-26 | 23-May-26 | 08-Jun-26 | 13-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B6-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 24-May-26 | 25-May-26 | 11-Jun-26 | 14-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B6-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 30-May-26 | 30-May-26 | 15-Jun-26 | 15-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B6-S-6113 | Rebar for Beams | 4 | 13,379.11 | 31-May-26 | 03-Jun-26 | 21-Sep-26 | 22-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B6-S-6123 | Formwork for Beams | 2 | 3,344.77 | 04-Jun-26 | 06-Jun-26 | 28-Sep-26 | 04-Oct-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B6-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 07-Jun-26 | 07-Jun-26 | 01-Oct-26 | 06-Oct-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 81 | 1,566,668.48 | 16-May-26 | 12-Jul-26 | 06-Jul-26 | | 1,566,668.48 | 1,539,773.29 | 0.98 |
| DAM3-C-B6-SS-150 | Installation of columns | 3 | 217,507.55 | 16-May-26 | 18-May-26 | 06-Jul-26 | 06-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B6-SS-160 | Installation of raft and purlins | 5 | 326,261.32 | 19-May-26 | 24-May-26 | 06-Jul-26 | 07-Jul-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B6-SS-1020 | Intumescent paint to steel works | 7 | 317,759.56 | 25-May-26 | 04-Jun-26 | 25-Jul-26 | 17-Aug-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B6-SS-1030 | Steel members for office area | 7 | 115,805.20 | 25-May-26 | 04-Jun-26 | 11-Oct-26 | 12-Oct-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B6-SS-1040 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 06-Jun-26 | 13-Jun-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B6-SS-1050 | Steel members for external platform | 7 | 18,670.78 | 08-Jun-26 | 15-Jun-26 | 30-Aug-26 | 31-Aug-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B6-SS-1060 | Epoxy paint for external platform | 5 | 3,734.16 | 16-Jun-26 | 21-Jun-26 | | | 3,734.16 | 0.00 | 0.00 |
| DAM3-C-B6-SS-180 | Installation of wall sandwich panel | 5 | 326,261.32 | 30-Jun-26 | 05-Jul-26 | 11-Oct-26 | 13-Oct-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B6-SS-190 | Installation of roof sheet | 5 | 217,507.55 | 07-Jul-26 | 12-Jul-26 | 24-Aug-26 | 30-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| **ARCHITECTURAL** | | 101 | 900,244.66 | 25-May-26 | 03-Nov-26 | 15-Aug-26 | | 753,533.00 | 133,999.53 | 0.18 |
| **MASONARY WORKS** | | 35 | 78,954.21 | 25-May-26 | 07-Jul-26 | 29-Aug-26 | 15-Sep-26 | 78,954.21 | 78,954.21 | 1.00 |

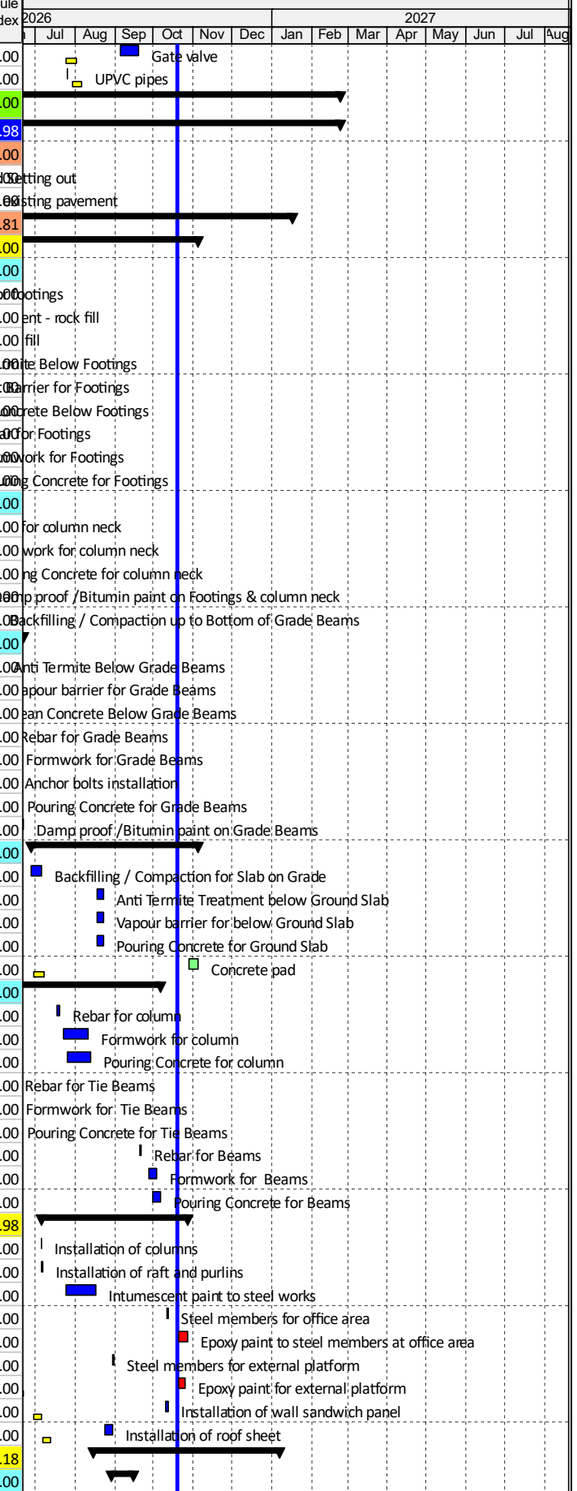





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B6-A-170 | Block work at factory area | 10 | 58,338.72 | 25-May-26 | 08-Jun-26 | 29-Aug-26 | 07-Sep-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B6-A-200 | Block work at office area | 7 | 6,179.18 | 22-Jun-26 | 29-Jun-26 | 30-Aug-26 | 09-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B6-A-620 | Block work at toilet area | 7 | 14,436.31 | 30-Jun-26 | 07-Jul-26 | 31-Aug-26 | 15-Sep-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 37 | 92,757.47 | 08-Jul-26 | 06-Oct-26 | 15-Oct-26 | | 92,757.47 | 48,590.16 | 0.52 |
| DAM3-C-B6-A-630 | Internal Wall Plaster | 15 | 48,590.16 | 08-Jul-26 | 25-Jul-26 | 15-Oct-26 | 19-Oct-26 | 48,590.16 | 48,590.16 | 1.00 |
| DAM3-C-B6-A-680 | Paint to Plaster (Primer, Putty & First Coat) | 7 | 44,167.30 | 29-Sep-26 | 06-Oct-26 | | | 44,167.30 | 0.00 | 0.00 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 20-Sep-26 | 26-Sep-26 | | | 46,792.30 | 0.00 | 0.00 |
| DAM3-C-B6-A-690 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 20-Sep-26 | 26-Sep-26 | | | 46,792.30 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 41 | 189,488.90 | 13-Aug-26 | 03-Nov-26 | | | 74,069.14 | 0.00 | 0.00 |
| DAM3-C-B6-A-670 | Tiles for Toilet | 7 | 46,530.71 | 13-Aug-26 | 20-Aug-26 | | | 46,530.71 | 0.00 | 0.00 |
| DAM3-C-B6-A-700 | Tiles for Office Area | 2 | 26,867.31 | 27-Sep-26 | 28-Sep-26 | | | 26,867.31 | 0.00 | 0.00 |
| DAM3-C-B6-A-830 | Granite strip | 2 | 671.12 | 29-Sep-26 | 30-Sep-26 | | | 671.12 | 0.00 | 0.00 |
| DAM3-C-B6-A-850 | Epoxy paint | 5 | 115,419.76 | 27-Oct-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 16 | 248,575.06 | 07-Jul-26 | 08-Aug-26 | | | 248,575.06 | 0.00 | 0.00 |
| DAM3-C-B6-A-1010 | Window (CW1) | 7 | 94,173.21 | 07-Jul-26 | 14-Jul-26 | | | 94,173.21 | 0.00 | 0.00 |
| DAM3-C-B6-A-640 | Roll up Shutter Door | 1 | 68,619.20 | 15-Jul-26 | 15-Jul-26 | | | 68,619.20 | 0.00 | 0.00 |
| DAM3-C-B6-A-650 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 16-Jul-26 | 16-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B6-A-710 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 18-Jul-26 | 18-Jul-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B6-A-720 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 19-Jul-26 | 19-Jul-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B6-A-940 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 20-Jul-26 | 20-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B6-A-950 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 30-Jul-26 | 30-Jul-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B6-A-960 | Skylight fixtures installation | 3 | 6,489.89 | 01-Aug-26 | 08-Aug-26 | | | 6,489.89 | 0.00 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 09-Aug-26 | 12-Aug-26 | | | 4,879.02 | 0.00 | 0.00 |
| DAM3-C-B6-A-810 | Waterproofing membrane for toilets | 4 | 4,879.02 | 09-Aug-26 | 12-Aug-26 | | | 4,879.02 | 0.00 | 0.00 |
| **METAL WORKS** | | 21 | 193,717.06 | 01-Oct-26 | 15-Oct-26 | 15-Aug-26 | | 193,717.06 | 6,455.16 | 0.03 |
| DAM3-C-B6-A-740 | Steel Ladder | 2 | 9,839.16 | 01-Oct-26 | 03-Oct-26 | | | 9,839.16 | 0.00 | 0.00 |
| DAM3-C-B6-A-840 | Steel railing works | 4 | 1,533.98 | 04-Oct-26 | 07-Oct-26 | | | 1,533.98 | 0.00 | 0.00 |
| DAM3-C-B6-A-760 | Aluminium composite panel | 5 | 175,888.76 | 08-Oct-26 | 13-Oct-26 | | | 175,888.76 | 0.00 | 0.00 |
| DAM3-C-B6-A-750 | Galvanised Steel Gratings | 2 | 6,455.16 | 14-Oct-26 | 15-Oct-26 | 15-Aug-26 | 15-Aug-26 | 6,455.16 | 6,455.16 | 1.00 |
| **SPECIALTIES** | | 9 | 45,080.66 | 17-Oct-26 | 26-Oct-26 | | | 13,788.76 | 0.00 | 0.00 |
| DAM3-C-B6-A-770 | Installation of fittings | 5 | 22,981.27 | 17-Oct-26 | 21-Oct-26 | | | 13,788.76 | 0.00 | 0.00 |
| DAM3-C-B6-A-1000 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 22-Oct-26 | 25-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-A-790 | Furniture Installation | 1 | 12,468.83 | 26-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 138 | 467,522.66 | 29-Apr-26 | 03-Nov-26 | 14-Jul-26 | | 231,656.03 | 156,280.78 | 0.67 |
| **HVAC** | | 17 | 233,183.33 | 15-Oct-26 | 31-Oct-26 | | | 31,354.38 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 22-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-450 | Installation of HVAC Ducts | 2 | 149,489.33 | 22-Oct-26 | 24-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-480 | Installation of Duct insulation | 2 | 21,205.40 | 25-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **SECOND STAGE** | | 17 | 62,488.60 | 15-Oct-26 | 31-Oct-26 | | | 31,354.38 | 0.00 | 0.00 |
| DAM3-C-B6-M-440 | Installation of Exhaust Fans | 2 | 7,938.56 | 15-Oct-26 | 17-Oct-26 | | | 7,938.56 | 0.00 | 0.00 |
| DAM3-C-B6-M-470 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 18-Oct-26 | 21-Oct-26 | | | 23,415.82 | 0.00 | 0.00 |
| DAM3-C-B6-M-460 | Installation of Diffuser | 2 | 2,144.00 | 27-Oct-26 | 28-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-650 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 29-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 20 | 102,458.78 | 07-Oct-26 | 03-Nov-26 | 11-Oct-26 | | 82,154.27 | 84,594.16 | 1.03 |
| **FIRST STAGE** | | 12 | 84,594.16 | 07-Oct-26 | 20-Oct-26 | 11-Oct-26 | 15-Oct-26 | 82,154.27 | 84,594.16 | 1.03 |
| DAM3-C-B6-M-610 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 07-Oct-26 | 14-Oct-26 | 11-Oct-26 | 15-Oct-26 | 72,394.75 | 72,394.75 | 1.00 |
| DAM3-C-B6-M-620 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 15-Oct-26 | 20-Oct-26 | 11-Oct-26 | 15-Oct-26 | 9,759.52 | 12,199.40 | 1.25 |
| **SECOND STAGE** | | 20 | 17,864.62 | 21-Oct-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-630 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 21-Oct-26 | 24-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-680 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 01-Nov-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 120 | 90,009.74 | 29-Apr-26 | 27-Oct-26 | 14-Jul-26 | | 76,276.56 | 30,093.94 | 0.39 |
| **FIRST STAGE** | | 106 | 41,149.90 | 29-Apr-26 | 29-Aug-26 | 14-Jul-26 | | 41,149.90 | 30,093.94 | 0.73 |
| DAM3-C-B6-M-510 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 29-Apr-26 | 03-May-26 | 14-Jul-26 | 18-Jul-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B6-M-530 | Installation of Floor Drain | 2 | 11,055.96 | 22-Aug-26 | 23-Aug-26 | | | 11,055.96 | 0.00 | 0.00 |
| DAM3-C-B6-M-690 | Installation of Trench drain | 5 | 11,508.80 | 24-Aug-26 | 29-Aug-26 | 15-Jul-26 | 18-Jul-26 | 11,508.80 | 11,508.80 | 1.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 28-Sep-26 | 27-Oct-26 | | | 35,126.66 | 0.00 | 0.00 |
| DAM3-C-B6-M-490 | Installation of Electric Water Heater | 2 | 1,819.51 | 28-Sep-26 | 29-Sep-26 | | | 1,819.51 | 0.00 | 0.00 |
| DAM3-C-B6-M-500 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 13-Oct-26 | 18-Oct-26 | | | 19,921.72 | 0.00 | 0.00 |
| DAM3-C-B6-M-520 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 18-Oct-26 | 20-Oct-26 | | | 13,385.43 | 0.00 | 0.00 |
| DAM3-C-B6-M-580 | Installation of Bib Tap | 2 | 1,900.66 | 20-Oct-26 | 22-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-540 | Installation of Water Tap | 2 | 2,874.14 | 22-Oct-26 | 25-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-M-550 | Installation of Roof Vent Cap | 2 | 927.12 | 25-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |

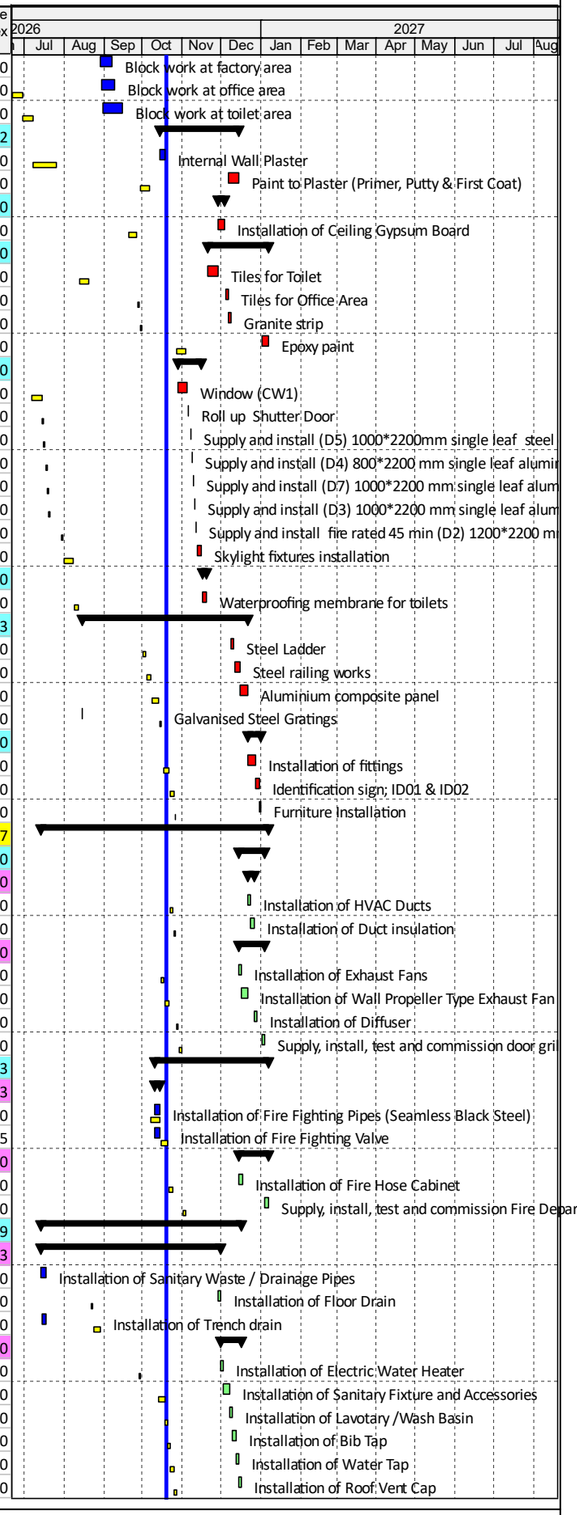


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| WATER SUPPLY SYSTEM | | 8 | 41,870.81 | 07-Oct-26 | 19-Oct-26 | 03-Oct-26 | | 41,870.81 | 41,592.68 | 0.99 |
| FIRST STAGE | | 6 | 41,592.68 | 07-Oct-26 | 13-Oct-26 | 03-Oct-26 | 07-Oct-26 | 41,592.68 | 41,592.68 | 1.00 |
| DAM3-C-B6-M-600 | Installation of Water Supply Pipes | 4 | 23,318.41 | 07-Oct-26 | 11-Oct-26 | 03-Oct-26 | 07-Oct-26 | 23,318.41 | 23,318.41 | 1.00 |
| DAM3-C-B6-M-590 | Installation of Water Supply Valve | 2 | 18,274.27 | 12-Oct-26 | 13-Oct-26 | 03-Oct-26 | 07-Oct-26 | 18,274.27 | 18,274.27 | 1.00 |
| SECOND STAGE | | 3 | 278.13 | 14-Oct-26 | 19-Oct-26 | | | 278.13 | 0.00 | 0.00 |
| DAM3-C-B6-M-640 | Capped connection | 3 | 278.13 | 14-Oct-26 | 19-Oct-26 | | | 278.13 | 0.00 | 0.00 |
| ELECTRICAL | | 165 | 752,044.76 | 20-May-26 | 23-Nov-26 | 08-Jun-26 | | 115,259.09 | 71,373.28 | 0.62 |
| FIRST STAGE | | 161 | 86,114.12 | 20-May-26 | 05-Nov-26 | 08-Jun-26 | | 60,725.20 | 27,642.87 | 0.46 |
| DAM3-C-B6-E-413 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 20-May-26 | 01-Jun-26 | 08-Jun-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B6-E-343 | Installation of Earthing and Grounding | 4 | 19,646.47 | 04-Jul-26 | 07-Jul-26 | 08-Jun-26 | | 19,646.47 | 17,681.82 | 0.90 |
| DAM3-C-B6-E-453 | Installation of LV Cables | 4 | 36,389.98 | 21-Jul-26 | 25-Jul-26 | | | 36,389.98 | 0.00 | 0.00 |
| DAM3-C-B6-E-373 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 14-Oct-26 | 18-Oct-26 | 09-Jun-26 | | 1,768.31 | 884.15 | 0.50 |
| DAM3-C-B6-E-393 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 28-Oct-26 | 01-Nov-26 | 01-Oct-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B6-E-463 | Installation of Wires | 4 | 16,925.94 | 02-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| SECOND STAGE | | 80 | 665,930.64 | 07-Oct-26 | 23-Nov-26 | 10-Oct-26 | | 54,533.89 | 43,730.41 | 0.80 |
| DAM3-C-B6-E-403 | Installation of Wiring Devices | 4 | 19,435.09 | 07-Oct-26 | 11-Oct-26 | | | 19,435.09 | 0.00 | 0.00 |
| DAM3-C-B6-E-433 | Installation of Disconnect Switches | 2 | 30,235.95 | 12-Oct-26 | 13-Oct-26 | | | 30,235.95 | 0.00 | 0.00 |
| DAM3-C-B6-E-353 | Installation of Fire Alarm Control Panel | 3 | 19,451.37 | 19-Oct-26 | 22-Oct-26 | | | 4,862.84 | 0.00 | 0.00 |
| DAM3-C-B6-E-363 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 24-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-503 | Installation of Access Control System | 4 | 27,616.86 | 28-Oct-26 | 01-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-730 | Installation of Solar power plant | 7 | 253,268.71 | 31-Oct-26 | 07-Nov-26 | 12-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| DAM3-C-B6-E-513 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 02-Nov-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-523 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 04-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-533 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 04-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-383 | Installation of Lighting fixtures | 2 | 76,166.74 | 07-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-423 | Installation of Main Distribution Board | 2 | 32,472.73 | 11-Nov-26 | 12-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-473 | Installation of LP-1 Panel | 2 | 18,403.54 | 14-Nov-26 | 15-Nov-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B6-E-483 | Installation of PP-AC panel | 2 | 21,648.48 | 16-Nov-26 | 17-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-443 | Installation of Telephone Cabinet | 2 | 26,991.08 | 18-Nov-26 | 19-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B6-E-720 | Installation of CCTV System | 3 | 76,349.24 | 18-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| BLOCK B5 | | 242 | 5,075,523.09 | 19-Feb-26 | 23-Nov-26 | 16-Feb-26 | | 4,820,713.04 | 3,378,514.23 | 0.70 |
| STRUCTURAL | | 188 | 1,389,042.53 | 19-Feb-26 | 25-Jul-26 | 16-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| FOOTING | | 44 | 597,655.16 | 19-Feb-26 | 25-Mar-26 | 16-Feb-26 | 05-May-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B5-S-250 | Excavation for footings | 4 | 89,859.61 | 19-Feb-26 | 25-Feb-26 | 16-Feb-26 | 18-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B5-S-6163 | Soil replacement - rock fill | 4 | 179,061.91 | 25-Feb-26 | 02-Mar-26 | 30-Mar-26 | 02-Apr-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B5-S-6173 | Engineering fill | 4 | 46,046.19 | 03-Mar-26 | 07-Mar-26 | 07-Apr-26 | 13-Apr-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B5-S-1297 | Anti Termite Below Footings | 1 | 11,905.55 | 08-Mar-26 | 08-Mar-26 | 21-Apr-26 | 21-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B5-S-1207 | Vapour Barrier for Footings | 1 | 7,940.10 | 09-Mar-26 | 09-Mar-26 | 21-Apr-26 | 21-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B5-S-1057 | Lean Concrete Below Footings | 2 | 8,229.34 | 10-Mar-26 | 11-Mar-26 | 21-Apr-26 | 21-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B5-S-1107 | Rebar for Footings | 4 | 101,844.98 | 12-Mar-26 | 16-Mar-26 | 28-Apr-26 | 29-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B5-S-1117 | Formwork for Footings | 4 | 25,461.25 | 21-Mar-26 | 24-Mar-26 | 02-May-26 | 03-May-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B5-S-1067 | Pouring Concrete for Footings | 1 | 127,306.23 | 25-Mar-26 | 25-Mar-26 | 05-May-26 | 05-May-26 | 127,306.23 | 127,306.23 | 1.00 |
| COLUMN NECK | | 20 | 120,554.54 | 26-Mar-26 | 11-Apr-26 | 03-May-26 | 24-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B5-S-1157 | Rebar for column neck | 2 | 14,919.19 | 26-Mar-26 | 28-Mar-26 | 03-May-26 | 05-May-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B5-S-1167 | Formwork for column neck | 2 | 9,946.13 | 29-Mar-26 | 30-Mar-26 | 06-May-26 | 09-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B5-S-1147 | Pouring Concrete for column neck | 1 | 24,865.31 | 31-Mar-26 | 31-Mar-26 | 10-May-26 | 10-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B5-S-1197 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 01-Apr-26 | 02-Apr-26 | 11-May-26 | 12-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B5-S-1257 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 04-Apr-26 | 11-Apr-26 | 20-May-26 | 24-May-26 | 46,046.19 | 46,046.19 | 1.00 |
| GRADE BEAM | | 13 | 171,632.86 | 12-Apr-26 | 28-Apr-26 | 01-Jun-26 | 18-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B5-S-1307 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 12-Apr-26 | 12-Apr-26 | 01-Jun-26 | 01-Jun-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B5-S-1227 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 13-Apr-26 | 14-Apr-26 | 01-Jun-26 | 01-Jun-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B5-S-1077 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 15-Apr-26 | 16-Apr-26 | 01-Jun-26 | 01-Jun-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B5-S-1127 | Rebar for Grade Beams | 5 | 27,194.46 | 18-Apr-26 | 22-Apr-26 | 03-Jun-26 | 04-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B5-S-1137 | Formwork for Grade Beams | 2 | 6,798.61 | 23-Apr-26 | 25-Apr-26 | 03-Jun-26 | 07-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B5-S-1287 | Anchor bolts installation | 2 | 57,238.83 | 23-Apr-26 | 25-Apr-26 | 02-Jun-26 | 04-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B5-S-1087 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 26-Apr-26 | 26-Apr-26 | 11-Jun-26 | 11-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B5-S-1237 | Damp proof /Bitumin paint on Grade Beams | 2 | 24,777.73 | 27-Apr-26 | 28-Apr-26 | 14-Jun-26 | 18-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| SLAB ON GRADE | | 109 | 397,232.98 | 29-Apr-26 | 29-Jun-26 | 21-Jun-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B5-S-1267 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 29-Apr-26 | 06-May-26 | 21-Jun-26 | 24-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B5-S-1217 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 07-May-26 | 07-May-26 | 01-Aug-26 | 04-Aug-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B5-S-1247 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 09-May-26 | 10-May-26 | 01-Aug-26 | 04-Aug-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B5-S-1097 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 11-May-26 | 14-May-26 | 01-Aug-26 | 04-Aug-26 | 344,195.21 | 344,195.21 | 1.00 |

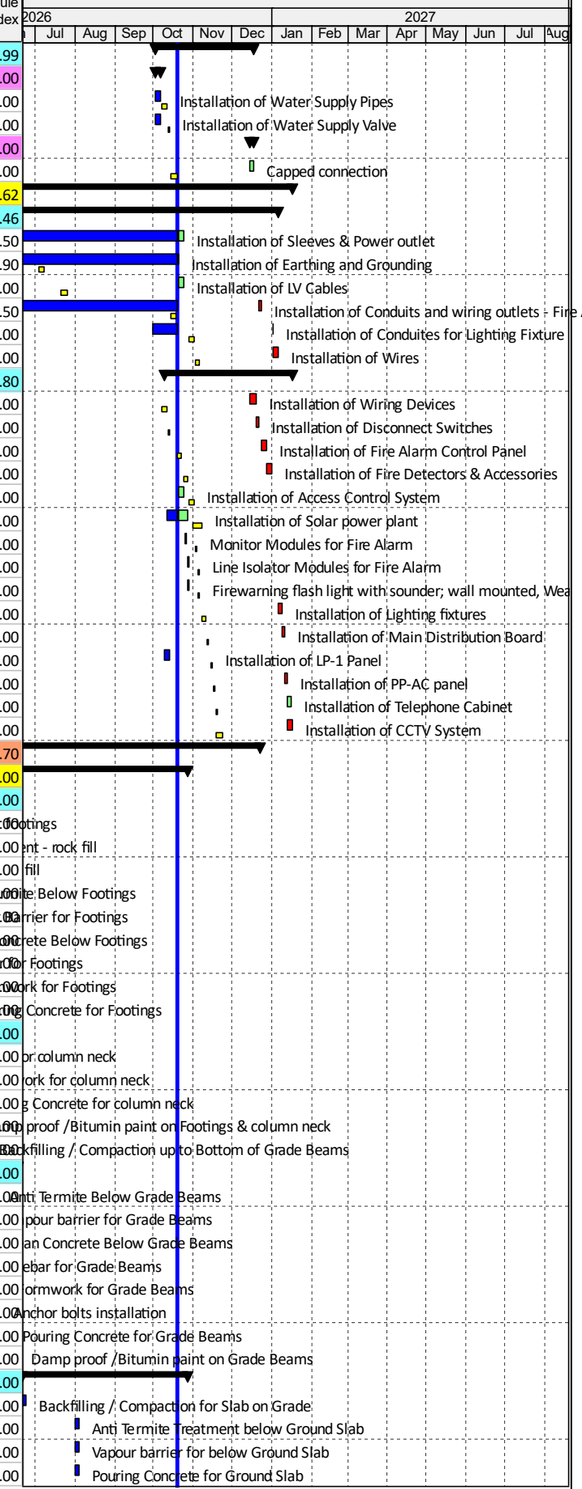




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B5-S-1277 | Concrete pad | 7 | 907.11 | 22-Jun-26 | 29-Jun-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 77 | 101,966.98 | 07-May-26 | 25-Jul-26 | 03-Jun-26 | 22-Sep-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B5-S-5101 | Rebar for column | 5 | 20,144.05 | 07-May-26 | 12-May-26 | 14-Jul-26 | 16-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B5-S-5102 | Formwork for column | 4 | 5,036.01 | 13-May-26 | 17-May-26 | 16-Jul-26 | 20-Jul-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B5-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 18-May-26 | 18-May-26 | 18-Jul-26 | 21-Jul-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B5-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 19-May-26 | 23-May-26 | 03-Jun-26 | 09-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B5-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 24-May-26 | 25-May-26 | 04-Jun-26 | 10-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B5-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 30-May-26 | 30-May-26 | 11-Jun-26 | 11-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B5-S-6113 | Rebar for Beams | 4 | 13,379.11 | 16-Jul-26 | 21-Jul-26 | 07-Sep-26 | 15-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B5-S-6123 | Formwork for Beams | 2 | 3,344.77 | 21-Jul-26 | 23-Jul-26 | 15-Sep-26 | 20-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B5-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 23-Jul-26 | 25-Jul-26 | 17-Sep-26 | 22-Sep-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 93 | 1,566,668.48 | 16-May-26 | 30-Jul-26 | 02-Jul-26 | | 1,566,668.48 | 1,539,773.29 | 0.98 |
| DAM3-C-B5-SS-270 | Installation of columns | 3 | 217,507.55 | 16-May-26 | 18-May-26 | 02-Jul-26 | 05-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B5-SS-280 | Installation of raft and purlins | 5 | 326,261.32 | 19-May-26 | 24-May-26 | 02-Jul-26 | 06-Jul-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B5-SS-1840 | Intumescent paint to steel works | 7 | 317,759.56 | 25-May-26 | 04-Jun-26 | 12-Jul-26 | 20-Jul-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B5-SS-1850 | Steel members for office area | 7 | 115,805.20 | 06-Jun-26 | 13-Jun-26 | 05-Oct-26 | 06-Oct-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B5-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 14-Jun-26 | 21-Jun-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B5-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 14-Jun-26 | 21-Jun-26 | 31-Aug-26 | 01-Sep-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B5-SS-300 | Installation of wall sandwich panel | 5 | 326,261.32 | 22-Jun-26 | 27-Jun-26 | 04-Oct-26 | 08-Oct-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B5-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 22-Jun-26 | 27-Jun-26 | | | 3,734.16 | 0.00 | 0.00 |
| DAM3-C-B5-SS-310 | Installation of roof sheet | 5 | 217,507.55 | 25-Jul-26 | 30-Jul-26 | 29-Jul-26 | 08-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| **ARCHITECTURAL** | | 102 | 900,244.66 | 25-May-26 | 21-Sep-26 | 08-Aug-26 | | 900,244.66 | 222,951.47 | 0.25 |
| **MASONARY WORKS** | | 26 | 78,954.21 | 25-May-26 | 29-Jun-26 | 09-Aug-26 | 09-Sep-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B5-A-290 | Block work at factory area | 10 | 58,338.72 | 25-May-26 | 08-Jun-26 | 09-Aug-26 | 12-Aug-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B5-A-320 | Block work at office area | 7 | 6,179.18 | 14-Jun-26 | 21-Jun-26 | 13-Aug-26 | 09-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B5-A-1440 | Block work at toilet area | 7 | 14,436.31 | 22-Jun-26 | 29-Jun-26 | 15-Aug-26 | 09-Sep-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 25 | 92,757.47 | 09-Jul-26 | 24-Aug-26 | 26-Sep-26 | | 92,757.47 | 86,132.37 | 0.93 |
| DAM3-C-B5-A-1450 | Internal Wall Plaster | 15 | 48,590.16 | 09-Jul-26 | 26-Jul-26 | 26-Sep-26 | 11-Oct-26 | 48,590.16 | 48,590.16 | 1.00 |
| DAM3-C-B5-A-1500 | Paint to Plaster (Primer, Putty & First Coat) | 7 | 44,167.30 | 17-Aug-26 | 24-Aug-26 | 11-Oct-26 | | 44,167.30 | 37,542.21 | 0.85 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 09-Aug-26 | 13-Aug-26 | | | 46,792.30 | 0.00 | 0.00 |
| DAM3-C-B5-A-1510 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 09-Aug-26 | 13-Aug-26 | | | 46,792.30 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 40 | 189,488.90 | 01-Aug-26 | 21-Sep-26 | 11-Oct-26 | | 189,488.90 | 46,530.71 | 0.25 |
| DAM3-C-B5-A-1490 | Tiles for Toilet | 7 | 46,530.71 | 01-Aug-26 | 08-Aug-26 | 11-Oct-26 | 13-Oct-26 | 46,530.71 | 46,530.71 | 1.00 |
| DAM3-C-B5-A-1520 | Tiles for Office Area | 2 | 26,867.31 | 15-Aug-26 | 16-Aug-26 | | | 26,867.31 | 0.00 | 0.00 |
| DAM3-C-B5-A-1650 | Granite strip | 2 | 671.12 | 17-Aug-26 | 18-Aug-26 | | | 671.12 | 0.00 | 0.00 |
| DAM3-C-B5-A-1670 | Epoxy paint | 7 | 115,419.76 | 14-Sep-26 | 21-Sep-26 | | | 115,419.76 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 14 | 248,575.06 | 28-Jun-26 | 13-Jul-26 | | | 248,575.06 | 0.00 | 0.00 |
| DAM3-C-B5-A-1830 | Window (CW1) | 7 | 94,173.21 | 28-Jun-26 | 05-Jul-26 | | | 94,173.21 | 0.00 | 0.00 |
| DAM3-C-B5-A-1460 | Roll up Shutter Door | 1 | 68,619.20 | 06-Jul-26 | 06-Jul-26 | | | 68,619.20 | 0.00 | 0.00 |
| DAM3-C-B5-A-1470 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 07-Jul-26 | 07-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B5-A-1530 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 08-Jul-26 | 08-Jul-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B5-A-1540 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 09-Jul-26 | 09-Jul-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B5-A-1760 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 11-Jul-26 | 11-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B5-A-1770 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 12-Jul-26 | 12-Jul-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B5-A-1780 | Skylight fixtures installation | 1 | 6,489.89 | 13-Jul-26 | 13-Jul-26 | | | 6,489.89 | 0.00 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 27-Jul-26 | 30-Jul-26 | 14-Oct-26 | 17-Oct-26 | 4,879.02 | 4,879.02 | 1.00 |
| DAM3-C-B5-A-1630 | Waterproofing membrane for toilets | 4 | 4,879.02 | 27-Jul-26 | 30-Jul-26 | 14-Oct-26 | 17-Oct-26 | 4,879.02 | 4,879.02 | 1.00 |
| **METAL WORKS** | | 18 | 193,717.06 | 19-Aug-26 | 02-Sep-26 | 08-Aug-26 | | 193,717.06 | 6,455.16 | 0.03 |
| DAM3-C-B5-A-1560 | Steel Ladder | 2 | 9,839.16 | 19-Aug-26 | 20-Aug-26 | | | 9,839.16 | 0.00 | 0.00 |
| DAM3-C-B5-A-1660 | Steel railing works | 4 | 1,533.98 | 22-Aug-26 | 25-Aug-26 | | | 1,533.98 | 0.00 | 0.00 |
| DAM3-C-B5-A-1580 | Aluminium composite panel | 5 | 175,888.76 | 26-Aug-26 | 31-Aug-26 | | | 175,888.76 | 0.00 | 0.00 |
| DAM3-C-B5-A-1570 | Galvanised Steel Gratings | 2 | 6,455.16 | 01-Sep-26 | 02-Sep-26 | 08-Aug-26 | 08-Aug-26 | 6,455.16 | 6,455.16 | 1.00 |
| **SPECIALTIES** | | 9 | 45,080.66 | 03-Sep-26 | 13-Sep-26 | | | 45,080.66 | 0.00 | 0.00 |
| DAM3-C-B5-A-1590 | Installation of fittings | 5 | 22,981.27 | 03-Sep-26 | 08-Sep-26 | | | 22,981.27 | 0.00 | 0.00 |
| DAM3-C-B5-A-1820 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 09-Sep-26 | 12-Sep-26 | | | 9,630.56 | 0.00 | 0.00 |
| DAM3-C-B5-A-1610 | Furniture Installation | 1 | 12,468.83 | 13-Sep-26 | 13-Sep-26 | | | 12,468.83 | 0.00 | 0.00 |
| **MECHANICAL** | | 119 | 467,522.66 | 29-Apr-26 | 13-Sep-26 | 08-Jul-26 | | 467,522.66 | 156,280.78 | 0.33 |
| **HVAC** | | 14 | 233,183.33 | 25-Aug-26 | 09-Sep-26 | | | 233,183.33 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 01-Sep-26 | 05-Sep-26 | | | 170,694.73 | 0.00 | 0.00 |
| DAM3-C-B5-M-1070 | Installation of HVAC Ducts | 2 | 149,489.33 | 01-Sep-26 | 02-Sep-26 | | | 149,489.33 | 0.00 | 0.00 |
| DAM3-C-B5-M-1100 | Installation of Duct insulation | 2 | 21,205.40 | 03-Sep-26 | 05-Sep-26 | | | 21,205.40 | 0.00 | 0.00 |
| **SECOND STAGE** | | 14 | 62,488.60 | 25-Aug-26 | 09-Sep-26 | | | 62,488.60 | 0.00 | 0.00 |

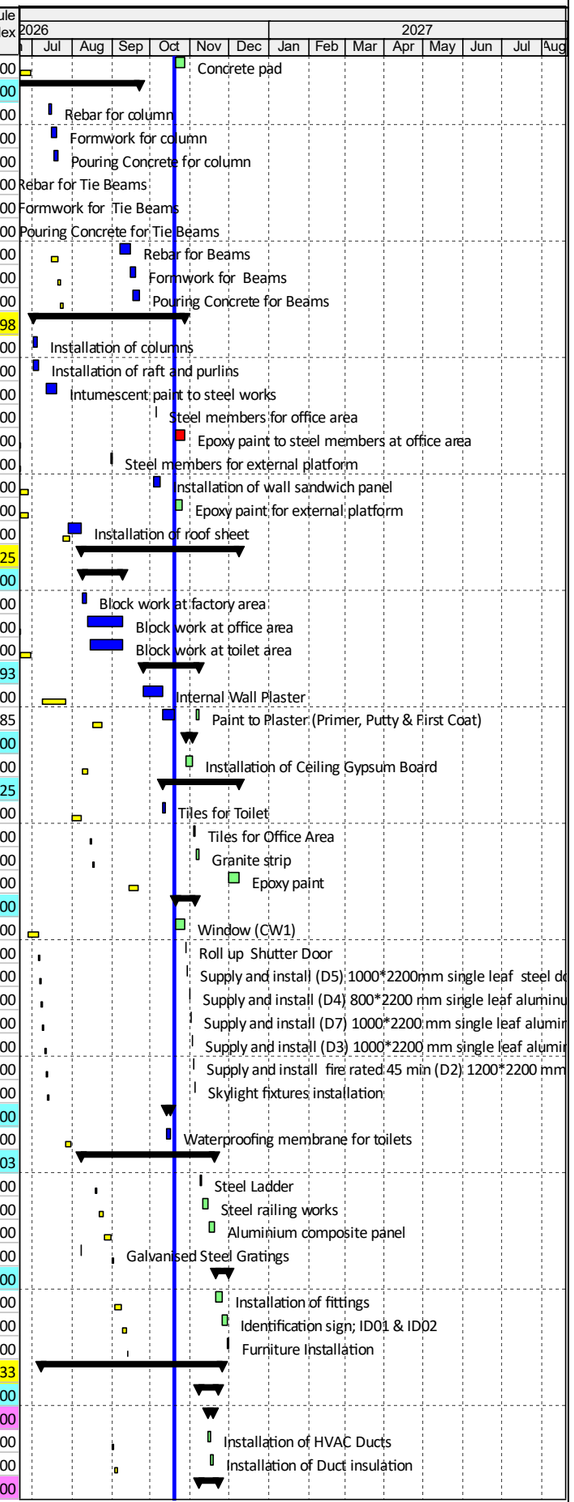




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B5-M-1060 | Installation of Exhaust Fans | 2 | 7,938.56 | 25-Aug-26 | 26-Aug-26 | | | 7,938.56 | 0.00 | 0.00 |
| DAM3-C-B5-M-1090 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 27-Aug-26 | 31-Aug-26 | | | 46,831.64 | 0.00 | 0.00 |
| DAM3-C-B5-M-1080 | Installation of Diffuser | 2 | 2,144.00 | 06-Sep-26 | 07-Sep-26 | | | 2,144.00 | 0.00 | 0.00 |
| DAM3-C-B5-M-1270 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 08-Sep-26 | 09-Sep-26 | | | 5,574.40 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 17 | 102,458.78 | 25-Aug-26 | 13-Sep-26 | 11-Oct-26 | | 102,458.78 | 84,594.16 | 0.83 |
| **FIRST STAGE** | | 12 | 84,594.16 | 25-Aug-26 | 07-Sep-26 | 11-Oct-26 | 13-Oct-26 | 84,594.16 | 84,594.16 | 1.00 |
| DAM3-C-B5-M-1230 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 25-Aug-26 | 01-Sep-26 | 11-Oct-26 | 13-Oct-26 | 72,394.75 | 72,394.75 | 1.00 |
| DAM3-C-B5-M-1240 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 02-Sep-26 | 07-Sep-26 | 11-Oct-26 | 13-Oct-26 | 12,199.40 | 12,199.40 | 1.00 |
| **SECOND STAGE** | | 17 | 17,864.62 | 08-Sep-26 | 13-Sep-26 | | | 17,864.62 | 0.00 | 0.00 |
| DAM3-C-B5-M-1250 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 08-Sep-26 | 10-Sep-26 | | | 15,158.56 | 0.00 | 0.00 |
| DAM3-C-B5-M-1300 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 10-Sep-26 | 13-Sep-26 | | | 2,706.06 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 100 | 90,009.74 | 29-Apr-26 | 01-Sep-26 | 08-Jul-26 | | 90,009.74 | 30,093.94 | 0.33 |
| **FIRST STAGE** | | 86 | 41,149.90 | 29-Apr-26 | 16-Aug-26 | 08-Jul-26 | | 41,149.90 | 30,093.94 | 0.73 |
| DAM3-C-B5-M-1130 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 29-Apr-26 | 03-May-26 | 08-Jul-26 | 12-Jul-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B5-M-1150 | Installation of Floor Drain | 2 | 11,055.96 | 09-Aug-26 | 10-Aug-26 | | | 11,055.96 | 0.00 | 0.00 |
| DAM3-C-B5-M-1310 | Installation of Trench drain | 5 | 11,508.80 | 11-Aug-26 | 16-Aug-26 | 11-Jul-26 | 14-Jul-26 | 11,508.80 | 11,508.80 | 1.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 17-Aug-26 | 01-Sep-26 | | | 48,859.84 | 0.00 | 0.00 |
| DAM3-C-B5-M-1110 | Installation of Electric Water Heater | 2 | 1,819.51 | 17-Aug-26 | 18-Aug-26 | | | 1,819.51 | 0.00 | 0.00 |
| DAM3-C-B5-M-1120 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 19-Aug-26 | 23-Aug-26 | | | 19,921.72 | 0.00 | 0.00 |
| DAM3-C-B5-M-1140 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 24-Aug-26 | 25-Aug-26 | | | 21,416.68 | 0.00 | 0.00 |
| DAM3-C-B5-M-1200 | Installation of Bib Tap | 2 | 1,900.66 | 26-Aug-26 | 27-Aug-26 | | | 1,900.66 | 0.00 | 0.00 |
| DAM3-C-B5-M-1160 | Installation of Water Tap | 2 | 2,874.14 | 29-Aug-26 | 30-Aug-26 | | | 2,874.14 | 0.00 | 0.00 |
| DAM3-C-B5-M-1170 | Installation of Roof Vent Cap | 2 | 927.12 | 31-Aug-26 | 01-Sep-26 | | | 927.12 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 24 | 41,870.81 | 25-Aug-26 | 06-Sep-26 | 29-Sep-26 | | 41,870.81 | 41,592.68 | 0.99 |
| **FIRST STAGE** | | 6 | 41,592.68 | 25-Aug-26 | 31-Aug-26 | 29-Sep-26 | 03-Oct-26 | 41,592.68 | 41,592.68 | 1.00 |
| DAM3-C-B5-M-1220 | Installation of Water Supply Pipes | 4 | 23,318.41 | 25-Aug-26 | 29-Aug-26 | 29-Sep-26 | 03-Oct-26 | 23,318.41 | 23,318.41 | 1.00 |
| DAM3-C-B5-M-1210 | Installation of Water Supply Valve | 2 | 18,274.27 | 30-Aug-26 | 31-Aug-26 | 29-Sep-26 | 03-Oct-26 | 18,274.27 | 18,274.27 | 1.00 |
| **SECOND STAGE** | | 5 | 278.13 | 01-Sep-26 | 06-Sep-26 | | | 278.13 | 0.00 | 0.00 |
| DAM3-C-B5-M-1260 | Capped connection | 5 | 278.13 | 01-Sep-26 | 06-Sep-26 | | | 278.13 | 0.00 | 0.00 |
| **ELECTRICAL** | | 118 | 752,044.76 | 30-Jun-26 | 23-Nov-26 | 04-Jun-26 | | 497,234.70 | 71,373.28 | 0.14 |
| **FIRST STAGE** | | 118 | 86,114.12 | 30-Jun-26 | 13-Oct-26 | 04-Jun-26 | | 86,114.12 | 27,642.87 | 0.32 |
| DAM3-C-B5-E-873 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 30-Jun-26 | 08-Jul-26 | 04-Jun-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B5-E-833 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 01-Sep-26 | 05-Sep-26 | 04-Jun-26 | | 1,768.31 | 884.15 | 0.50 |
| DAM3-C-B5-E-853 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 15-Sep-26 | 19-Sep-26 | 20-Sep-26 | | 8,462.97 | 7,616.67 | 0.90 |
| DAM3-C-B5-E-923 | Installation of Wires | 4 | 16,925.94 | 20-Sep-26 | 24-Sep-26 | | | 16,925.94 | 0.00 | 0.00 |
| DAM3-C-B5-E-803 | Installation of Earthing and Grounding | 4 | 19,646.47 | 10-Oct-26 | 13-Oct-26 | 04-Jun-26 | | 19,646.47 | 17,681.82 | 0.90 |
| DAM3-C-B5-E-913 | Installation of LV Cables | 4 | 36,389.98 | 10-Oct-26 | 13-Oct-26 | | | 36,389.98 | 0.00 | 0.00 |
| **SECOND STAGE** | | 52 | 665,930.64 | 25-Aug-26 | 23-Nov-26 | 10-Oct-26 | | 411,120.59 | 43,730.41 | 0.11 |
| DAM3-C-B5-E-863 | Installation of Wiring Devices | 4 | 19,435.09 | 25-Aug-26 | 29-Aug-26 | | | 19,435.09 | 0.00 | 0.00 |
| DAM3-C-B5-E-893 | Installation of Disconnect Switches | 2 | 30,235.95 | 30-Aug-26 | 31-Aug-26 | | | 30,235.95 | 0.00 | 0.00 |
| DAM3-C-B5-E-813 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 06-Sep-26 | 09-Sep-26 | | | 19,451.37 | 0.00 | 0.00 |
| DAM3-C-B5-E-823 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 10-Sep-26 | 14-Sep-26 | | | 56,740.37 | 0.00 | 0.00 |
| DAM3-C-B5-E-843 | Installation of Lighting fixtures | 4 | 76,166.74 | 26-Sep-26 | 29-Sep-26 | | | 76,166.74 | 0.00 | 0.00 |
| DAM3-C-B5-E-883 | Installation of Main Distribution Board | 2 | 32,472.73 | 30-Sep-26 | 01-Oct-26 | | | 32,472.73 | 0.00 | 0.00 |
| DAM3-C-B5-E-933 | Installation of LP-1 Panel | 2 | 18,403.54 | 03-Oct-26 | 04-Oct-26 | 10-Oct-26 | 14-Oct-26 | 18,403.54 | 18,403.54 | 1.00 |
| DAM3-C-B5-E-943 | Installation of PP-AC panel | 2 | 21,648.48 | 05-Oct-26 | 06-Oct-26 | | | 21,648.48 | 0.00 | 0.00 |
| DAM3-C-B5-E-903 | Installation of Telephone Cabinet | 2 | 26,991.08 | 07-Oct-26 | 08-Oct-26 | | | 26,991.08 | 0.00 | 0.00 |
| DAM3-C-B5-E-1340 | Installation of CCTV System | 7 | 76,349.24 | 07-Oct-26 | 14-Oct-26 | | | 76,349.24 | 0.00 | 0.00 |
| DAM3-C-B5-E-963 | Installation of Access Control System | 4 | 27,616.86 | 10-Oct-26 | 13-Oct-26 | | | 27,616.86 | 0.00 | 0.00 |
| DAM3-C-B5-E-973 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 14-Oct-26 | 15-Oct-26 | | | 3,882.38 | 0.00 | 0.00 |
| DAM3-C-B5-E-983 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 17-Oct-26 | 18-Oct-26 | | | 185.40 | 0.00 | 0.00 |
| DAM3-C-B5-E-993 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 19-Oct-26 | 20-Oct-26 | | | 1,541.35 | 0.00 | 0.00 |
| DAM3-C-B5-E-1350 | Installation of Solar power plant | 14 | 253,268.71 | 08-Nov-26 | 23-Nov-26 | 11-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **BLOCK B4** | | 242 | 5,075,523.09 | 25-Feb-26 | 01-Dec-26 | 17-Feb-26 | | 4,583,200.88 | 3,378,514.23 | 0.74 |
| **STRUCTURAL** | | 198 | 1,389,042.53 | 25-Feb-26 | 21-Jul-26 | 17-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 36 | 597,655.16 | 25-Feb-26 | 30-Mar-26 | 17-Feb-26 | 30-Apr-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B4-S-210 | Excavation for footings | 4 | 89,859.61 | 25-Feb-26 | 02-Mar-26 | 17-Feb-26 | 24-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B4-S-6183 | Soil replacement - rock fill | 4 | 179,061.91 | 03-Mar-26 | 07-Mar-26 | 26-Mar-26 | 29-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B4-S-6193 | Engineering fill | 4 | 46,046.19 | 08-Mar-26 | 11-Mar-26 | 02-Apr-26 | 05-Apr-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B4-S-1037 | Anti Termite Below Footings | 1 | 11,905.55 | 12-Mar-26 | 12-Mar-26 | 15-Apr-26 | 15-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B4-S-947 | Vapour Barrier for Footings | 1 | 7,940.10 | 14-Mar-26 | 14-Mar-26 | 15-Apr-26 | 15-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B4-S-797 | Lean Concrete Below Footings | 2 | 8,229.34 | 15-Mar-26 | 16-Mar-26 | 15-Apr-26 | 15-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |

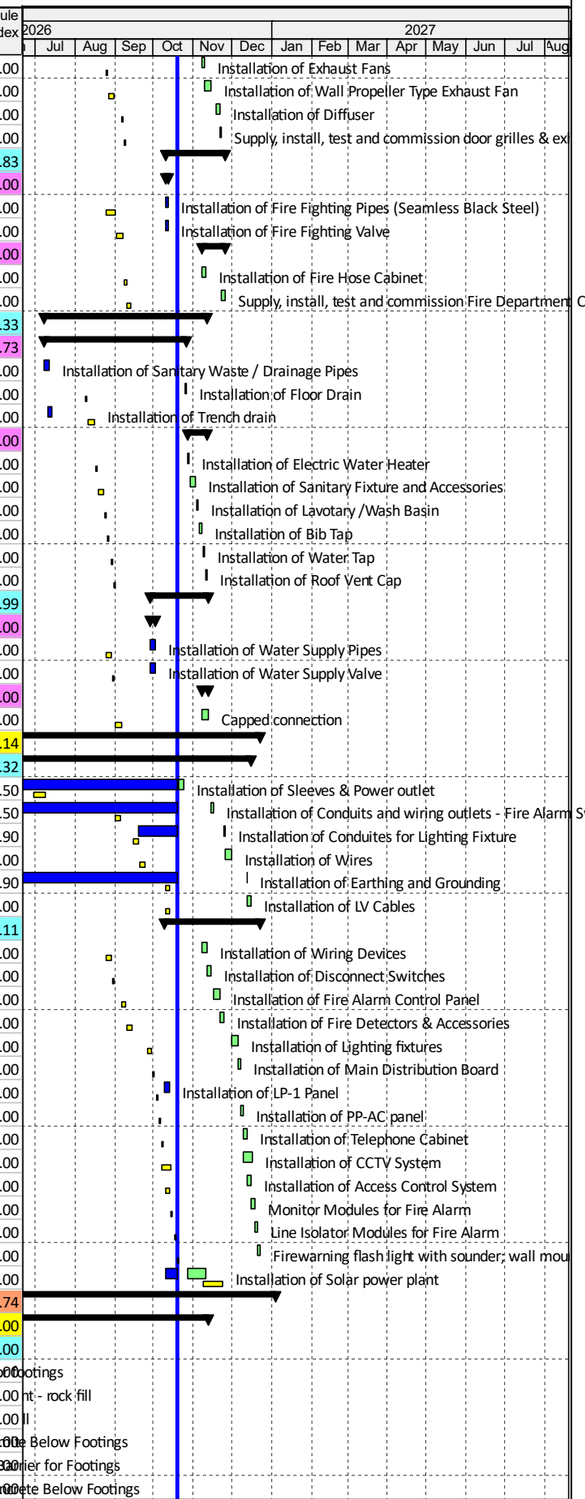




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B4-S-847 | Rebar for Footings | 4 | 101,844.98 | 21-Mar-26 | 24-Mar-26 | 23-Apr-26 | 28-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B4-S-857 | Formwork for Footings | 4 | 25,461.25 | 25-Mar-26 | 29-Mar-26 | 20-Apr-26 | 22-Apr-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B4-S-807 | Pouring Concrete for Footings | 1 | 127,306.23 | 30-Mar-26 | 30-Mar-26 | 30-Apr-26 | 30-Apr-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 17 | 120,554.54 | 31-Mar-26 | 15-Apr-26 | 23-Apr-26 | 19-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B4-S-897 | Rebar for column neck | 2 | 14,919.19 | 31-Mar-26 | 01-Apr-26 | 23-Apr-26 | 28-Apr-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B4-S-907 | Formwork for column neck | 2 | 9,946.13 | 02-Apr-26 | 04-Apr-26 | 03-May-26 | 05-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B4-S-887 | Pouring Concrete for column neck | 1 | 24,865.31 | 05-Apr-26 | 05-Apr-26 | 05-May-26 | 05-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B4-S-937 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 06-Apr-26 | 07-Apr-26 | 07-May-26 | 10-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B4-S-997 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 08-Apr-26 | 15-Apr-26 | 13-May-26 | 19-May-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 17 | 171,632.86 | 16-Apr-26 | 06-May-26 | 20-May-26 | 09-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B4-S-1047 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 16-Apr-26 | 16-Apr-26 | 20-May-26 | 20-May-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B4-S-967 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 18-Apr-26 | 19-Apr-26 | 20-May-26 | 20-May-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B4-S-817 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 20-Apr-26 | 21-Apr-26 | 20-May-26 | 20-May-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B4-S-867 | Rebar for Grade Beams | 5 | 27,194.46 | 22-Apr-26 | 27-Apr-26 | 21-May-26 | 24-May-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B4-S-877 | Formwork for Grade Beams | 2 | 6,798.61 | 28-Apr-26 | 29-Apr-26 | 24-May-26 | 02-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B4-S-1027 | Anchor bolts installation | 2 | 57,238.83 | 28-Apr-26 | 29-Apr-26 | 31-May-26 | 01-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B4-S-827 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 30-Apr-26 | 30-Apr-26 | 03-Jun-26 | 03-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B4-S-977 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 02-May-26 | 06-May-26 | 07-Jun-26 | 09-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 128 | 397,232.98 | 07-May-26 | 21-Jul-26 | 14-Jun-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B4-S-1007 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 07-May-26 | 14-May-26 | 14-Jun-26 | 22-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B4-S-957 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 16-May-26 | 16-May-26 | 29-Jul-26 | 01-Aug-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B4-S-987 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 17-May-26 | 18-May-26 | 29-Jul-26 | 01-Aug-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B4-S-837 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 19-May-26 | 23-May-26 | 29-Jul-26 | 01-Aug-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B4-S-1017 | Concrete pad | 7 | 907.11 | 14-Jul-26 | 21-Jul-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 61 | 101,966.98 | 16-May-26 | 15-Jun-26 | 21-May-26 | 14-Sep-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B4-S-5101 | Rebar for column | 5 | 20,144.05 | 16-May-26 | 20-May-26 | 22-Jun-26 | 02-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B4-S-5102 | Formwork for column | 4 | 5,036.01 | 21-May-26 | 25-May-26 | 29-Jun-26 | 05-Jul-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B4-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 30-May-26 | 30-May-26 | 09-Jul-26 | 12-Jul-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B4-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 31-May-26 | 03-Jun-26 | 21-May-26 | 24-May-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B4-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 04-Jun-26 | 06-Jun-26 | 24-May-26 | 02-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B4-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 07-Jun-26 | 07-Jun-26 | 03-Jun-26 | 03-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B4-S-6113 | Rebar for Beams | 4 | 13,379.11 | 08-Jun-26 | 11-Jun-26 | 30-Aug-26 | 01-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B4-S-6123 | Formwork for Beams | 2 | 3,344.77 | 13-Jun-26 | 14-Jun-26 | 02-Sep-26 | 08-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B4-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 15-Jun-26 | 15-Jun-26 | 08-Sep-26 | 14-Sep-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 98 | 1,566,668.48 | 25-May-26 | 19-Jul-26 | 24-Jun-26 | | 1,566,668.48 | 1,539,773.29 | 0.98 |
| DAM3-C-B4-A-210 | Installation of columns | 3 | 217,507.55 | 25-May-26 | 31-May-26 | 24-Jun-26 | 24-Jun-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B4-A-220 | Installation of raft and purlins | 5 | 326,261.32 | 01-Jun-26 | 06-Jun-26 | 25-Jun-26 | 25-Jun-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B4-A-1430 | Intumescent paint to steel works | 7 | 317,759.56 | 07-Jun-26 | 14-Jun-26 | 08-Jul-26 | 14-Jul-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B4-A-1440 | Steel members for office area | 7 | 115,805.20 | 15-Jun-26 | 22-Jun-26 | 01-Oct-26 | 04-Oct-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B4-A-250 | Installation of roof sheet | 5 | 217,507.55 | 21-Jun-26 | 25-Jun-26 | 26-Jul-26 | 30-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B4-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 23-Jun-26 | 30-Jun-26 | 01-Sep-26 | 02-Sep-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B4-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 28-Jun-26 | 05-Jul-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B4-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 01-Jul-26 | 06-Jul-26 | | | 3,734.16 | 0.00 | 0.00 |
| DAM3-C-B4-A-240 | Installation of wall sandwich panel | 5 | 326,261.32 | 14-Jul-26 | 19-Jul-26 | 03-Oct-26 | 20-Oct-26 | 326,261.32 | 326,261.32 | 1.00 |
| **ARCHITECTURAL** | | 113 | 900,244.66 | 09-Jun-26 | 17-Oct-26 | 03-Aug-26 | | 900,244.66 | 222,951.47 | 0.25 |
| **MASONARY WORKS** | | 30 | 78,954.21 | 09-Jun-26 | 21-Jul-26 | 05-Aug-26 | 01-Sep-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B4-A-230 | Block work at factory area | 10 | 58,338.72 | 09-Jun-26 | 20-Jun-26 | 05-Aug-26 | 10-Aug-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B4-A-260 | Block work at office area | 7 | 6,179.18 | 06-Jul-26 | 13-Jul-26 | 05-Aug-26 | 01-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B4-A-1030 | Block work at toilet area | 7 | 14,436.31 | 14-Jul-26 | 21-Jul-26 | 05-Aug-26 | 24-Aug-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 28 | 92,757.47 | 01-Aug-26 | 15-Sep-26 | 24-Sep-26 | | 92,757.47 | 86,132.37 | 0.93 |
| DAM3-C-B4-A-1040 | Internal Wall Plaster | 10 | 48,590.16 | 01-Aug-26 | 17-Aug-26 | 24-Sep-26 | 06-Oct-26 | 48,590.16 | 48,590.16 | 1.00 |
| DAM3-C-B4-A-1090 | Paint to Plaster (Primer, Putty & First Coat) | 7 | 44,167.30 | 08-Sep-26 | 15-Sep-26 | 07-Oct-26 | | 44,167.30 | 37,542.21 | 0.85 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 31-Aug-26 | 05-Sep-26 | | | 46,792.30 | 0.00 | 0.00 |
| DAM3-C-B4-A-1100 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 31-Aug-26 | 05-Sep-26 | | | 46,792.30 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 43 | 189,488.90 | 23-Aug-26 | 17-Oct-26 | 05-Oct-26 | | 189,488.90 | 46,530.71 | 0.25 |
| DAM3-C-B4-A-1080 | Tiles for Toilet | 7 | 46,530.71 | 23-Aug-26 | 30-Aug-26 | 05-Oct-26 | 10-Oct-26 | 46,530.71 | 46,530.71 | 1.00 |
| DAM3-C-B4-A-1110 | Tiles for Office Area | 2 | 26,867.31 | 06-Sep-26 | 07-Sep-26 | | | 26,867.31 | 0.00 | 0.00 |
| DAM3-C-B4-A-1240 | Granite strip | 2 | 671.12 | 08-Sep-26 | 09-Sep-26 | | | 671.12 | 0.00 | 0.00 |
| DAM3-C-B4-A-1260 | Epoxy paint | 7 | 115,419.76 | 10-Oct-26 | 17-Oct-26 | | | 115,419.76 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 14 | 248,575.06 | 20-Jul-26 | 04-Aug-26 | | | 248,575.06 | 0.00 | 0.00 |
| DAM3-C-B4-A-1420 | Window (CW1) | 7 | 94,173.21 | 20-Jul-26 | 27-Jul-26 | | | 94,173.21 | 0.00 | 0.00 |
| DAM3-C-B4-A-1050 | Roll up Shutter Door | 1 | 68,619.20 | 28-Jul-26 | 28-Jul-26 | | | 68,619.20 | 0.00 | 0.00 |

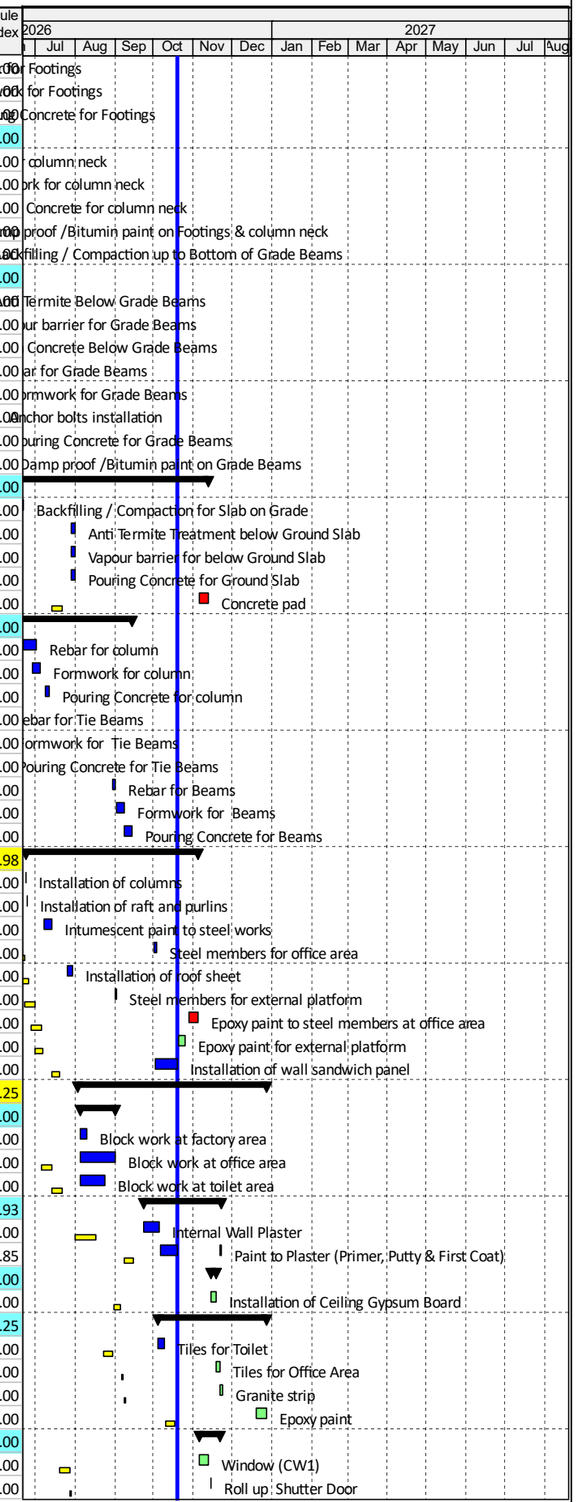




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B4-A-1060 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 29-Jul-26 | 29-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B4-A-1120 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 30-Jul-26 | 30-Jul-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B4-A-1130 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 01-Aug-26 | 01-Aug-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B4-A-1350 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 02-Aug-26 | 02-Aug-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B4-A-1360 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 03-Aug-26 | 03-Aug-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B4-A-1370 | Skylight fixtures installation | 1 | 6,489.89 | 04-Aug-26 | 04-Aug-26 | | | 6,489.89 | 0.00 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 18-Aug-26 | 22-Aug-26 | 18-Oct-26 | 20-Oct-26 | 4,879.02 | 4,879.02 | 1.00 |
| DAM3-C-B4-A-1220 | Waterproofing membrane for toilets | 4 | 4,879.02 | 18-Aug-26 | 22-Aug-26 | 18-Oct-26 | 20-Oct-26 | 4,879.02 | 4,879.02 | 1.00 |
| **METAL WORKS** | | 20 | 193,717.06 | 10-Sep-26 | 26-Sep-26 | 03-Aug-26 | | 193,717.06 | 6,455.16 | 0.03 |
| DAM3-C-B4-A-1150 | Steel Ladder | 2 | 9,839.16 | 10-Sep-26 | 12-Sep-26 | | | 9,839.16 | 0.00 | 0.00 |
| DAM3-C-B4-A-1250 | Steel railing works | 4 | 1,533.98 | 13-Sep-26 | 16-Sep-26 | | | 1,533.98 | 0.00 | 0.00 |
| DAM3-C-B4-A-1170 | Aluminium composite panel | 5 | 175,888.76 | 17-Sep-26 | 22-Sep-26 | | | 175,888.76 | 0.00 | 0.00 |
| DAM3-C-B4-A-1160 | Galvanised Steel Gratings | 2 | 6,455.16 | 24-Sep-26 | 26-Sep-26 | 03-Aug-26 | 03-Aug-26 | 6,455.16 | 6,455.16 | 1.00 |
| **SPECIALTIES** | | 11 | 45,080.66 | 27-Sep-26 | 08-Oct-26 | | | 45,080.66 | 0.00 | 0.00 |
| DAM3-C-B4-A-1180 | Installation of fittings | 7 | 22,981.27 | 27-Sep-26 | 04-Oct-26 | | | 22,981.27 | 0.00 | 0.00 |
| DAM3-C-B4-A-1410 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 05-Oct-26 | 07-Oct-26 | | | 9,630.56 | 0.00 | 0.00 |
| DAM3-C-B4-A-1200 | Furniture Installation | 1 | 12,468.83 | 08-Oct-26 | 08-Oct-26 | | | 12,468.83 | 0.00 | 0.00 |
| **MECHANICAL** | | 150 | 467,522.66 | 07-May-26 | 06-Oct-26 | 25-Jun-26 | | 467,522.66 | 156,280.78 | 0.33 |
| **HVAC** | | 14 | 233,183.33 | 16-Sep-26 | 03-Oct-26 | | | 233,183.33 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 24-Sep-26 | 28-Sep-26 | | | 170,694.73 | 0.00 | 0.00 |
| DAM3-C-B4-M-760 | Installation of HVAC Ducts | 2 | 149,489.33 | 24-Sep-26 | 26-Sep-26 | | | 149,489.33 | 0.00 | 0.00 |
| DAM3-C-B4-M-790 | Installation of Duct insulation | 2 | 21,205.40 | 27-Sep-26 | 28-Sep-26 | | | 21,205.40 | 0.00 | 0.00 |
| **SECOND STAGE** | | 14 | 62,488.60 | 16-Sep-26 | 03-Oct-26 | | | 62,488.60 | 0.00 | 0.00 |
| DAM3-C-B4-M-750 | Installation of Exhaust Fans | 2 | 7,938.56 | 16-Sep-26 | 17-Sep-26 | | | 7,938.56 | 0.00 | 0.00 |
| DAM3-C-B4-M-780 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 19-Sep-26 | 22-Sep-26 | | | 46,831.64 | 0.00 | 0.00 |
| DAM3-C-B4-M-770 | Installation of Diffuser | 2 | 2,144.00 | 29-Sep-26 | 30-Sep-26 | | | 2,144.00 | 0.00 | 0.00 |
| DAM3-C-B4-M-960 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 01-Oct-26 | 03-Oct-26 | | | 5,574.40 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 24 | 102,458.78 | 16-Sep-26 | 06-Oct-26 | 30-Sep-26 | | 102,458.78 | 84,594.16 | 0.83 |
| **FIRST STAGE** | | 12 | 84,594.16 | 16-Sep-26 | 30-Sep-26 | 30-Sep-26 | 04-Oct-26 | 84,594.16 | 84,594.16 | 1.00 |
| DAM3-C-B4-M-920 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 16-Sep-26 | 24-Sep-26 | 30-Sep-26 | 04-Oct-26 | 72,394.75 | 72,394.75 | 1.00 |
| DAM3-C-B4-M-930 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 26-Sep-26 | 30-Sep-26 | 30-Sep-26 | 04-Oct-26 | 12,199.40 | 12,199.40 | 1.00 |
| **SECOND STAGE** | | 17 | 17,864.62 | 01-Oct-26 | 06-Oct-26 | | | 17,864.62 | 0.00 | 0.00 |
| DAM3-C-B4-M-940 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 01-Oct-26 | 04-Oct-26 | | | 15,158.56 | 0.00 | 0.00 |
| DAM3-C-B4-M-990 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 04-Oct-26 | 06-Oct-26 | | | 2,706.06 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 133 | 90,009.74 | 07-May-26 | 24-Sep-26 | 25-Jun-26 | | 90,009.74 | 30,093.94 | 0.33 |
| **FIRST STAGE** | | 119 | 41,149.90 | 07-May-26 | 07-Sep-26 | 25-Jun-26 | | 41,149.90 | 30,093.94 | 0.73 |
| DAM3-C-B4-M-820 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 07-May-26 | 11-May-26 | 27-Jun-26 | 29-Jun-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B4-M-840 | Installation of Floor Drain | 2 | 11,055.96 | 31-Aug-26 | 01-Sep-26 | | | 11,055.96 | 0.00 | 0.00 |
| DAM3-C-B4-M-1000 | Installation of Trench drain | 5 | 11,508.80 | 02-Sep-26 | 07-Sep-26 | 25-Jun-26 | 28-Jun-26 | 11,508.80 | 11,508.80 | 1.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 08-Sep-26 | 24-Sep-26 | | | 48,859.84 | 0.00 | 0.00 |
| DAM3-C-B4-M-800 | Installation of Electric Water Heater | 2 | 1,819.51 | 08-Sep-26 | 09-Sep-26 | | | 1,819.51 | 0.00 | 0.00 |
| DAM3-C-B4-M-810 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 10-Sep-26 | 14-Sep-26 | | | 19,921.72 | 0.00 | 0.00 |
| DAM3-C-B4-M-830 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 15-Sep-26 | 16-Sep-26 | | | 21,416.68 | 0.00 | 0.00 |
| DAM3-C-B4-M-890 | Installation of Bib Tap | 2 | 1,900.66 | 17-Sep-26 | 19-Sep-26 | | | 1,900.66 | 0.00 | 0.00 |
| DAM3-C-B4-M-850 | Installation of Water Tap | 2 | 2,874.14 | 20-Sep-26 | 21-Sep-26 | | | 2,874.14 | 0.00 | 0.00 |
| DAM3-C-B4-M-860 | Installation of Roof Vent Cap | 2 | 927.12 | 22-Sep-26 | 24-Sep-26 | | | 927.12 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 18 | 41,870.81 | 16-Sep-26 | 29-Sep-26 | 22-Sep-26 | | 41,870.81 | 41,592.68 | 0.99 |
| **FIRST STAGE** | | 7 | 41,592.68 | 16-Sep-26 | 22-Sep-26 | 22-Sep-26 | 29-Sep-26 | 41,592.68 | 41,592.68 | 1.00 |
| DAM3-C-B4-M-910 | Installation of Water Supply Pipes | 4 | 23,318.41 | 16-Sep-26 | 20-Sep-26 | 22-Sep-26 | 29-Sep-26 | 23,318.41 | 23,318.41 | 1.00 |
| DAM3-C-B4-M-900 | Installation of Water Supply Valve | 2 | 18,274.27 | 21-Sep-26 | 22-Sep-26 | 24-Sep-26 | 29-Sep-26 | 18,274.27 | 18,274.27 | 1.00 |
| **SECOND STAGE** | | 5 | 278.13 | 24-Sep-26 | 29-Sep-26 | | | 278.13 | 0.00 | 0.00 |
| DAM3-C-B4-M-950 | Capped connection | 5 | 278.13 | 24-Sep-26 | 29-Sep-26 | | | 278.13 | 0.00 | 0.00 |
| **ELECTRICAL** | | 100 | 752,044.76 | 22-Jul-26 | 01-Dec-26 | 24-May-26 | | 259,722.55 | 71,373.28 | 0.27 |
| **FIRST STAGE** | | 99 | 86,114.12 | 22-Jul-26 | 28-Oct-26 | 24-May-26 | | 30,077.67 | 27,642.87 | 0.92 |
| DAM3-C-B4-E-643 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 22-Jul-26 | 30-Jul-26 | 24-May-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B4-E-603 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 24-Sep-26 | 28-Sep-26 | 24-May-26 | | 1,768.31 | 884.15 | 0.50 |
| DAM3-C-B4-E-623 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 08-Oct-26 | 12-Oct-26 | 12-Sep-26 | | 8,462.97 | 7,616.67 | 0.90 |
| DAM3-C-B4-E-693 | Installation of Wires | 4 | 16,925.94 | 13-Oct-26 | 17-Oct-26 | | | 16,925.94 | 0.00 | 0.00 |
| DAM3-C-B4-E-573 | Installation of Earthing and Grounding | 4 | 19,646.47 | 25-Oct-26 | 28-Oct-26 | 24-May-26 | | 0.00 | 17,681.82 | 0.00 |
| DAM3-C-B4-E-683 | Installation of LV Cables | 4 | 36,389.98 | 25-Oct-26 | 28-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **SECOND STAGE** | | 48 | 665,930.64 | 16-Sep-26 | 01-Dec-26 | 10-Oct-26 | | 229,644.88 | 43,730.41 | 0.19 |
| DAM3-C-B4-E-633 | Installation of Wiring Devices | 4 | 19,435.09 | 16-Sep-26 | 20-Sep-26 | | | 19,435.09 | 0.00 | 0.00 |

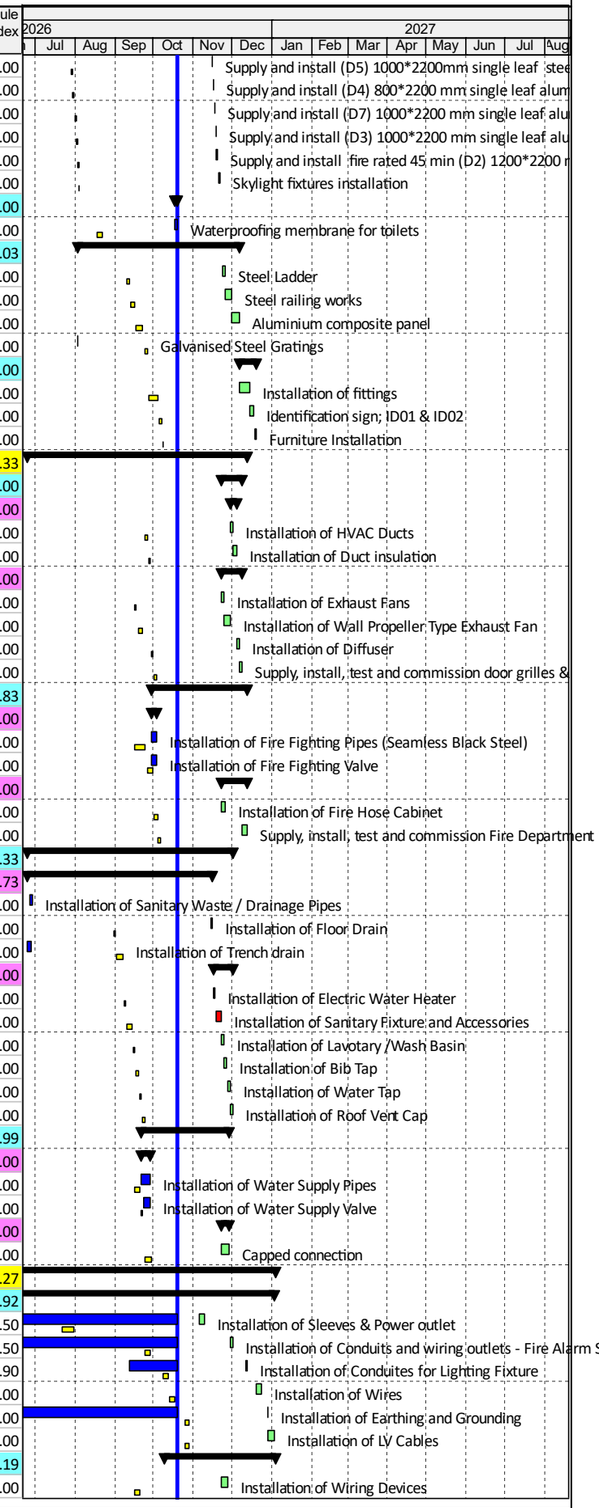


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B4-E-663 | Installation of Disconnect Switches | 2 | 30,235.95 | 21-Sep-26 | 22-Sep-26 | | | 30,235.95 | 0.00 | 0.00 |
| DAM3-C-B4-E-583 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 29-Sep-26 | 03-Oct-26 | | | 19,451.37 | 0.00 | 0.00 |
| DAM3-C-B4-E-593 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 04-Oct-26 | 07-Oct-26 | | | 56,740.37 | 0.00 | 0.00 |
| DAM3-C-B4-E-733 | Installation of Access Control System | 5 | 27,616.86 | 08-Oct-26 | 13-Oct-26 | | | 27,616.86 | 0.00 | 0.00 |
| DAM3-C-B4-E-743 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 14-Oct-26 | 15-Oct-26 | | | 3,882.38 | 0.00 | 0.00 |
| DAM3-C-B4-E-753 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 17-Oct-26 | 18-Oct-26 | | | 185.40 | 0.00 | 0.00 |
| DAM3-C-B4-E-613 | Installation of Lighting fixtures | 4 | 76,166.74 | 18-Oct-26 | 21-Oct-26 | | | 38,083.37 | 0.00 | 0.00 |
| DAM3-C-B4-E-653 | Installation of Main Distribution Board | 2 | 32,472.73 | 18-Oct-26 | 19-Oct-26 | | | 32,472.73 | 0.00 | 0.00 |
| DAM3-C-B4-E-763 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 19-Oct-26 | 20-Oct-26 | | | 1,541.35 | 0.00 | 0.00 |
| DAM3-C-B4-E-703 | Installation of LP-1 Panel | 2 | 18,403.54 | 20-Oct-26 | 21-Oct-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B4-E-1030 | Installation of CCTV System | 7 | 76,349.24 | 22-Oct-26 | 29-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B4-E-713 | Installation of PP-AC panel | 2 | 21,648.48 | 22-Oct-26 | 24-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B4-E-673 | Installation of Telephone Cabinet | 2 | 26,991.08 | 25-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B4-E-1040 | Installation of Solar power plant | 7 | 253,268.71 | 24-Nov-26 | 01-Dec-26 | 10-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **BLOCK B3** | | 303 | 5,075,523.09 | 03-Mar-26 | 28-Dec-26 | 17-Feb-26 | | 3,476,170.36 | 3,312,279.43 | 0.95 |
| **STRUCTURAL** | | 180 | 1,389,042.53 | 03-Mar-26 | 18-Jul-26 | 17-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 46 | 597,655.16 | 03-Mar-26 | 04-Apr-26 | 17-Feb-26 | 17-May-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B3-S-210 | Excavation for footings | 4 | 89,859.61 | 03-Mar-26 | 07-Mar-26 | 17-Feb-26 | 12-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B3-S-6203 | Soil replacement - rock fill | 4 | 179,061.91 | 08-Mar-26 | 11-Mar-26 | 17-Mar-26 | 24-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B3-S-6213 | Engineering fill | 4 | 46,046.19 | 12-Mar-26 | 16-Mar-26 | 28-Mar-26 | 07-Apr-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B3-S-1037 | Anti Termite Below Footings | 1 | 11,905.55 | 21-Mar-26 | 21-Mar-26 | 11-Apr-26 | 11-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B3-S-947 | Vapour Barrier for Footings | 1 | 7,940.10 | 22-Mar-26 | 22-Mar-26 | 11-Apr-26 | 11-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B3-S-797 | Lean Concrete Below Footings | 2 | 8,229.34 | 23-Mar-26 | 24-Mar-26 | 11-Apr-26 | 11-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B3-S-847 | Rebar for Footings | 4 | 101,844.98 | 25-Mar-26 | 29-Mar-26 | 06-May-26 | 11-May-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B3-S-857 | Formwork for Footings | 4 | 25,461.25 | 30-Mar-26 | 02-Apr-26 | 11-May-26 | 13-May-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B3-S-807 | Pouring Concrete for Footings | 1 | 127,306.23 | 04-Apr-26 | 04-Apr-26 | 17-May-26 | 17-May-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 12 | 120,554.54 | 05-Apr-26 | 20-Apr-26 | 11-May-26 | 09-Jun-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B3-S-897 | Rebar for column neck | 2 | 14,919.19 | 05-Apr-26 | 06-Apr-26 | 11-May-26 | 14-May-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B3-S-907 | Formwork for column neck | 2 | 9,946.13 | 07-Apr-26 | 08-Apr-26 | 21-May-26 | 23-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B3-S-887 | Pouring Concrete for column neck | 1 | 24,865.31 | 09-Apr-26 | 09-Apr-26 | 20-May-26 | 20-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B3-S-937 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 11-Apr-26 | 12-Apr-26 | 20-May-26 | 23-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B3-S-997 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 13-Apr-26 | 20-Apr-26 | 24-May-26 | 09-Jun-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 15 | 171,632.86 | 21-Apr-26 | 11-May-26 | 14-Jun-26 | 30-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B3-S-1047 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 21-Apr-26 | 21-Apr-26 | 14-Jun-26 | 14-Jun-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B3-S-967 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 22-Apr-26 | 23-Apr-26 | 14-Jun-26 | 14-Jun-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B3-S-817 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 25-Apr-26 | 26-Apr-26 | 14-Jun-26 | 14-Jun-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B3-S-867 | Rebar for Grade Beams | 5 | 27,194.46 | 27-Apr-26 | 02-May-26 | 16-Jun-26 | 20-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B3-S-877 | Formwork for Grade Beams | 2 | 6,798.61 | 03-May-26 | 04-May-26 | 18-Jun-26 | 22-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B3-S-1027 | Anchor bolts installation | 2 | 57,238.83 | 03-May-26 | 04-May-26 | 18-Jun-26 | 20-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B3-S-827 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 05-May-26 | 05-May-26 | 24-Jun-26 | 24-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B3-S-977 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 06-May-26 | 11-May-26 | 27-Jun-26 | 30-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 97 | 397,232.98 | 12-May-26 | 18-Jul-26 | 06-Jul-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B3-S-1007 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 12-May-26 | 19-May-26 | 06-Jul-26 | 09-Jul-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B3-S-957 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 20-May-26 | 20-May-26 | 11-Aug-26 | 15-Aug-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B3-S-987 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 21-May-26 | 23-May-26 | 11-Aug-26 | 15-Aug-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B3-S-837 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 24-May-26 | 31-May-26 | 11-Aug-26 | 15-Aug-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B3-S-1017 | Concrete pad | 7 | 907.11 | 11-Jul-26 | 18-Jul-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 59 | 101,966.98 | 20-May-26 | 20-Jun-26 | 16-Jun-26 | 05-Oct-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B3-S-5101 | Rebar for column | 5 | 20,144.05 | 20-May-26 | 25-May-26 | 22-Jul-26 | 25-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B3-S-5102 | Formwork for column | 4 | 5,036.01 | 30-May-26 | 02-Jun-26 | 27-Jul-26 | 02-Aug-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B3-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 03-Jun-26 | 03-Jun-26 | 29-Jul-26 | 03-Aug-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B3-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 04-Jun-26 | 08-Jun-26 | 16-Jun-26 | 20-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B3-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 09-Jun-26 | 10-Jun-26 | 18-Jun-26 | 22-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B3-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 11-Jun-26 | 11-Jun-26 | 24-Jun-26 | 24-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B3-S-6113 | Rebar for Beams | 4 | 13,379.11 | 13-Jun-26 | 16-Jun-26 | 08-Sep-26 | 15-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B3-S-6123 | Formwork for Beams | 2 | 3,344.77 | 17-Jun-26 | 18-Jun-26 | 23-Sep-26 | 29-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B3-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 20-Jun-26 | 20-Jun-26 | 26-Sep-26 | 05-Oct-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 86 | 1,566,668.48 | 07-Jun-26 | 15-Jul-26 | 15-Jul-26 | | 1,566,668.48 | 1,521,102.51 | 0.97 |
| DAM3-C-B3-A-210 | Installation of columns | 3 | 217,507.55 | 07-Jun-26 | 09-Jun-26 | 15-Jul-26 | 15-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B3-A-220 | Installation of raft and purlins | 5 | 326,261.32 | 10-Jun-26 | 15-Jun-26 | 15-Jul-26 | 16-Jul-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B3-A-1430 | Intumescent paint to steel works | 7 | 317,759.56 | 16-Jun-26 | 23-Jun-26 | 25-Jul-26 | 29-Jul-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B3-A-1440 | Steel members for office area | 7 | 115,805.20 | 24-Jun-26 | 01-Jul-26 | 07-Oct-26 | 20-Oct-26 | 115,805.20 | 115,805.20 | 1.00 |

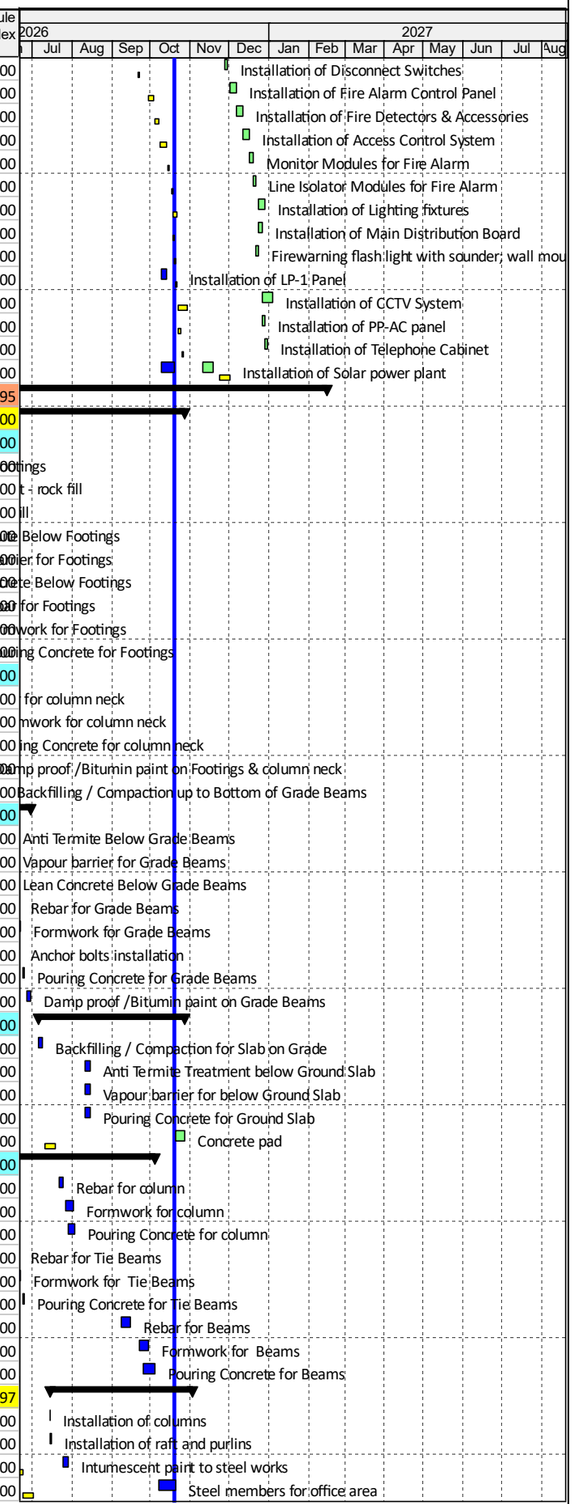




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B3-A-250 | Installation of roof sheet | 5 | 217,507.55 | 02-Jul-26 | 07-Jul-26 | 16-Aug-26 | 23-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B3-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 02-Jul-26 | 09-Jul-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B3-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 02-Jul-26 | 09-Jul-26 | | | 18,670.78 | 0.00 | 0.00 |
| DAM3-C-B3-A-240 | Installation of wall sandwich panel | 5 | 326,261.32 | 11-Jul-26 | 15-Jul-26 | 12-Oct-26 | 20-Oct-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B3-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 11-Jul-26 | 15-Jul-26 | | | 3,734.16 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 145 | 900,244.66 | 21-Jun-26 | 20-Dec-26 | 18-Aug-26 | | 427,529.16 | 175,387.45 | 0.41 |
| **MASONARY WORKS** | | 25 | 78,954.21 | 21-Jun-26 | 18-Jul-26 | 24-Aug-26 | 09-Sep-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B3-A-230 | Block work at factory area | 10 | 58,338.72 | 21-Jun-26 | 01-Jul-26 | 24-Aug-26 | 01-Sep-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B3-A-260 | Block work at office area | 7 | 6,179.18 | 02-Jul-26 | 09-Jul-26 | 25-Aug-26 | 09-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B3-A-1030 | Block work at toilet area | 7 | 14,436.31 | 11-Jul-26 | 18-Jul-26 | 25-Aug-26 | 03-Sep-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 70 | 92,757.47 | 28-Jul-26 | 19-Nov-26 | 12-Oct-26 | | 48,590.16 | 48,590.16 | 1.00 |
| DAM3-C-B3-A-1040 | Internal Wall Plaster | 10 | 48,590.16 | 28-Jul-26 | 13-Aug-26 | 12-Oct-26 | 20-Oct-26 | 48,590.16 | 48,590.16 | 1.00 |
| DAM3-C-B3-A-1090 | Paint to Plaster (Primer, Putty & First Coat) | 2 | 44,167.30 | 12-Nov-26 | 19-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 04-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1100 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 04-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 78 | 189,488.90 | 19-Aug-26 | 20-Dec-26 | 18-Oct-26 | | 46,530.71 | 34,898.03 | 0.75 |
| DAM3-C-B3-A-1080 | Tiles for Toilet | 7 | 46,530.71 | 19-Aug-26 | 26-Aug-26 | 18-Oct-26 | | 46,530.71 | 34,898.03 | 0.75 |
| DAM3-C-B3-A-1110 | Tiles for Office Area | 2 | 26,867.31 | 10-Nov-26 | 11-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1240 | Granite strip | 2 | 671.12 | 12-Nov-26 | 14-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1260 | Epoxy paint | 3 | 115,419.76 | 13-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 14 | 248,575.06 | 16-Jul-26 | 01-Aug-26 | 18-Oct-26 | | 248,575.06 | 6,489.89 | 0.03 |
| DAM3-C-B3-A-1420 | Window (CW1) | 7 | 94,173.21 | 16-Jul-26 | 23-Jul-26 | | | 94,173.21 | 0.00 | 0.00 |
| DAM3-C-B3-A-1050 | Roll up Shutter Door | 1 | 68,619.20 | 25-Jul-26 | 25-Jul-26 | | | 68,619.20 | 0.00 | 0.00 |
| DAM3-C-B3-A-1060 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 26-Jul-26 | 26-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B3-A-1120 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 27-Jul-26 | 27-Jul-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B3-A-1130 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 28-Jul-26 | 28-Jul-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B3-A-1350 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 29-Jul-26 | 29-Jul-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B3-A-1360 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 30-Jul-26 | 30-Jul-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B3-A-1370 | Skylight fixtures installation | 1 | 6,489.89 | 01-Aug-26 | 01-Aug-26 | 18-Oct-26 | 20-Oct-26 | 6,489.89 | 6,489.89 | 1.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 15-Aug-26 | 18-Aug-26 | | | 4,879.02 | 0.00 | 0.00 |
| DAM3-C-B3-A-1220 | Waterproofing membrane for toilets | 4 | 4,879.02 | 15-Aug-26 | 18-Aug-26 | | | 4,879.02 | 0.00 | 0.00 |
| **METAL WORKS** | | 21 | 193,717.06 | 15-Nov-26 | 29-Nov-26 | 18-Aug-26 | | 0.00 | 6,455.16 | 0.00 |
| DAM3-C-B3-A-1150 | Steel Ladder | 2 | 9,839.16 | 15-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1250 | Steel railing works | 4 | 1,533.98 | 17-Nov-26 | 21-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1170 | Aluminium composite panel | 5 | 175,888.76 | 22-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1160 | Galvanised Steel Gratings | 2 | 6,455.16 | 28-Nov-26 | 29-Nov-26 | 18-Aug-26 | 18-Aug-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 7 | 45,080.66 | 30-Nov-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1180 | Installation of fittings | 3 | 22,981.27 | 30-Nov-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1410 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 08-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-A-1200 | Furniture Installation | 1 | 12,468.83 | 12-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 162 | 467,522.66 | 12-May-26 | 09-Dec-26 | 30-Jul-26 | | 90,009.74 | 156,280.78 | 1.74 |
| **HVAC** | | 14 | 233,183.33 | 21-Nov-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 28-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-760 | Installation of HVAC Ducts | 2 | 149,489.33 | 28-Nov-26 | 29-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-790 | Installation of Duct insulation | 2 | 21,205.40 | 30-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SECOND STAGE** | | 14 | 62,488.60 | 21-Nov-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-750 | Installation of Exhaust Fans | 2 | 7,938.56 | 21-Nov-26 | 22-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-780 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 23-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-770 | Installation of Diffuser | 2 | 2,144.00 | 02-Dec-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-960 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 05-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 25 | 102,458.78 | 21-Nov-26 | 09-Dec-26 | 21-Sep-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 12 | 84,594.16 | 21-Nov-26 | 03-Dec-26 | 21-Sep-26 | 28-Sep-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B3-M-920 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 21-Nov-26 | 28-Nov-26 | 21-Sep-26 | 28-Sep-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B3-M-930 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 29-Nov-26 | 03-Dec-26 | 22-Sep-26 | 28-Sep-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 17 | 17,864.62 | 05-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-940 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 05-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-990 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 07-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 99 | 90,009.74 | 12-May-26 | 20-Sep-26 | 30-Jul-26 | | 90,009.74 | 30,093.94 | 0.33 |
| **FIRST STAGE** | | 85 | 41,149.90 | 12-May-26 | 03-Sep-26 | 30-Jul-26 | | 41,149.90 | 30,093.94 | 0.73 |
| DAM3-C-B3-M-820 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 12-May-26 | 16-May-26 | 30-Jul-26 | 03-Aug-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B3-M-840 | Installation of Floor Drain | 2 | 11,055.96 | 27-Aug-26 | 29-Aug-26 | | | 11,055.96 | 0.00 | 0.00 |
| DAM3-C-B3-M-1000 | Installation of Trench drain | 5 | 11,508.80 | 30-Aug-26 | 03-Sep-26 | 08-Aug-26 | 09-Aug-26 | 11,508.80 | 11,508.80 | 1.00 |

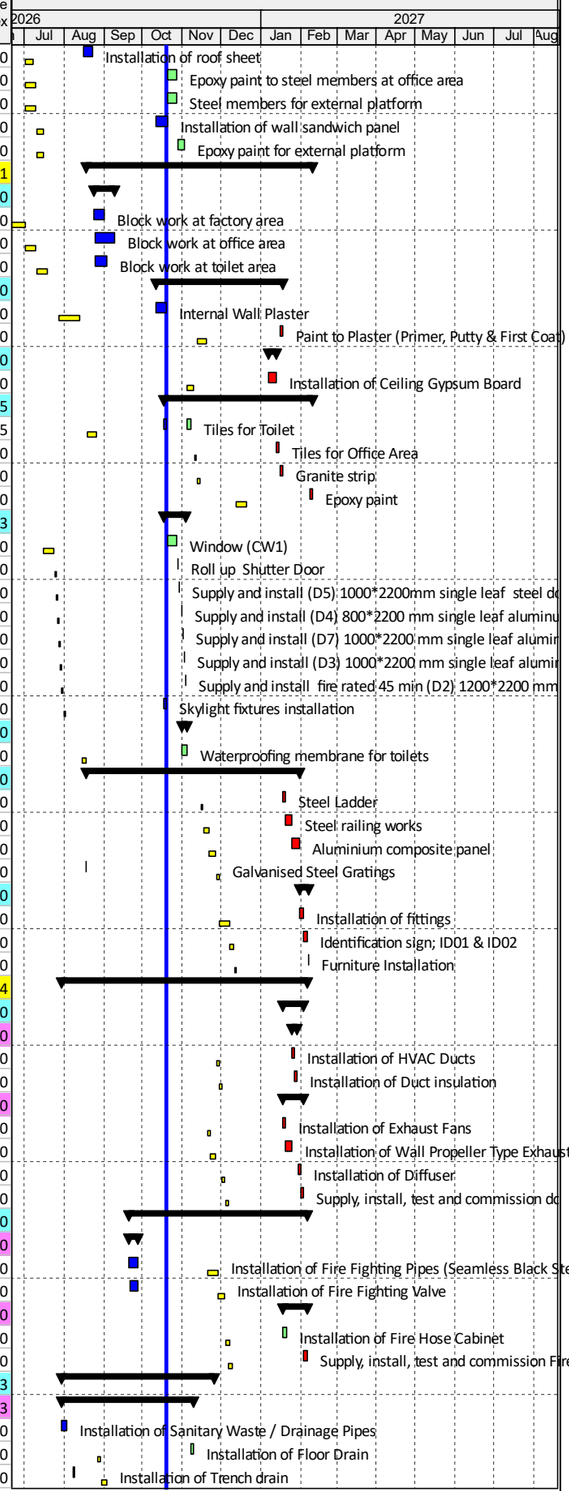


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| SECOND STAGE | | 14 | 48,859.84 | 05-Sep-26 | 20-Sep-26 | | | 48,859.84 | 0.00 | 0.00 |
| DAM3-C-B3-M-800 | Installation of Electric Water Heater | 2 | 1,819.51 | 05-Sep-26 | 06-Sep-26 | | | 1,819.51 | 0.00 | 0.00 |
| DAM3-C-B3-M-810 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 07-Sep-26 | 10-Sep-26 | | | 19,921.72 | 0.00 | 0.00 |
| DAM3-C-B3-M-830 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 12-Sep-26 | 13-Sep-26 | | | 21,416.68 | 0.00 | 0.00 |
| DAM3-C-B3-M-890 | Installation of Bib Tap | 2 | 1,900.66 | 14-Sep-26 | 15-Sep-26 | | | 1,900.66 | 0.00 | 0.00 |
| DAM3-C-B3-M-850 | Installation of Water Tap | 2 | 2,874.14 | 16-Sep-26 | 17-Sep-26 | | | 2,874.14 | 0.00 | 0.00 |
| DAM3-C-B3-M-860 | Installation of Roof Vent Cap | 2 | 927.12 | 19-Sep-26 | 20-Sep-26 | | | 927.12 | 0.00 | 0.00 |
| WATER SUPPLY SYSTEM | | 7 | 41,870.81 | 21-Nov-26 | 02-Dec-26 | 01-Oct-26 | | 0.00 | 41,592.68 | 0.00 |
| FIRST STAGE | | 6 | 41,592.68 | 21-Nov-26 | 26-Nov-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B3-M-910 | Installation of Water Supply Pipes | 4 | 23,318.41 | 21-Nov-26 | 24-Nov-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B3-M-900 | Installation of Water Supply Valve | 2 | 18,274.27 | 25-Nov-26 | 26-Nov-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 18,274.27 | 0.00 |
| SECOND STAGE | | 5 | 278.13 | 28-Nov-26 | 02-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-M-950 | Capped connection | 5 | 278.13 | 28-Nov-26 | 02-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| ELECTRICAL | | 166 | 752,044.76 | 19-Jul-26 | 28-Dec-26 | 17-Jun-26 | | 2,920.45 | 71,373.28 | 24.44 |
| FIRST STAGE | | 166 | 86,114.12 | 19-Jul-26 | 24-Dec-26 | 17-Jun-26 | | 2,920.45 | 27,642.87 | 9.47 |
| DAM3-C-B3-E-643 | Installation of Sleeves & Power outlet | 5 | 2,920.45 | 19-Jul-26 | 27-Jul-26 | 17-Jun-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B3-E-603 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 28-Nov-26 | 01-Dec-26 | 21-Jul-26 | | 0.00 | 884.15 | 0.00 |
| DAM3-C-B3-E-623 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 12-Dec-26 | 15-Dec-26 | 23-Sep-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B3-E-693 | Installation of Wires | 2 | 16,925.94 | 16-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-573 | Installation of Earthing and Grounding | 4 | 19,646.47 | 21-Dec-26 | 24-Dec-26 | 17-Jun-26 | | 0.00 | 17,681.82 | 0.00 |
| DAM3-C-B3-E-683 | Installation of LV Cables | 4 | 36,389.98 | 21-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| SECOND STAGE | | 80 | 665,930.64 | 21-Nov-26 | 28-Dec-26 | 10-Oct-26 | | 0.00 | 43,730.41 | 0.00 |
| DAM3-C-B3-E-633 | Installation of Wiring Devices | 4 | 19,435.09 | 21-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-663 | Installation of Disconnect Switches | 2 | 30,235.95 | 25-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-583 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 02-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-1040 | Installation of Solar power plant | 7 | 253,268.71 | 02-Dec-26 | 09-Dec-26 | 12-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| DAM3-C-B3-E-593 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 07-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-733 | Installation of Access Control System | 3 | 27,616.86 | 12-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-743 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 17-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-753 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 20-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-613 | Installation of Lighting fixtures | 4 | 76,166.74 | 21-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-653 | Installation of Main Distribution Board | 2 | 32,472.73 | 21-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-763 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 22-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-1030 | Installation of CCTV System | 3 | 76,349.24 | 23-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-703 | Installation of LP-1 Panel | 2 | 18,403.54 | 23-Dec-26 | 24-Dec-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B3-E-713 | Installation of PP-AC panel | 2 | 21,648.48 | 23-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B3-E-673 | Installation of Telephone Cabinet | 2 | 26,991.08 | 26-Dec-26 | 27-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| BLOCK B2 | | 273 | 5,075,523.09 | 08-Mar-26 | 02-Jan-27 | 17-Feb-26 | | 3,426,422.18 | 2,933,193.28 | 0.86 |
| STRUCTURAL | | 205 | 1,389,042.53 | 08-Mar-26 | 29-Sep-26 | 17-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| FOOTING | | 43 | 597,655.16 | 08-Mar-26 | 08-Apr-26 | 17-Feb-26 | 13-May-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B2-S-150 | Excavation for footings | 4 | 89,859.61 | 08-Mar-26 | 11-Mar-26 | 17-Feb-26 | 24-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B2-S-6223 | Soil replacement - rock fill | 4 | 179,061.91 | 12-Mar-26 | 16-Mar-26 | 17-Mar-26 | 24-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B2-S-6233 | Engineering fill | 4 | 46,046.19 | 21-Mar-26 | 24-Mar-26 | 28-Mar-26 | 06-Apr-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B2-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 25-Mar-26 | 25-Mar-26 | 13-Apr-26 | 13-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B2-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 26-Mar-26 | 26-Mar-26 | 13-Apr-26 | 13-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B2-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 28-Mar-26 | 29-Mar-26 | 13-Apr-26 | 13-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B2-S-104 | Rebar for Footings | 4 | 101,844.98 | 30-Mar-26 | 02-Apr-26 | 06-May-26 | 11-May-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B2-S-105 | Formwork for Footings | 4 | 25,461.25 | 04-Apr-26 | 07-Apr-26 | 10-May-26 | 12-May-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B2-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 08-Apr-26 | 08-Apr-26 | 13-May-26 | 13-May-26 | 127,306.23 | 127,306.23 | 1.00 |
| COLUMN NECK | | 16 | 120,554.54 | 09-Apr-26 | 27-Apr-26 | 10-May-26 | 09-Jun-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B2-S-257 | Rebar for column neck | 4 | 14,919.19 | 09-Apr-26 | 13-Apr-26 | 10-May-26 | 12-May-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B2-S-267 | Formwork for column neck | 2 | 9,946.13 | 14-Apr-26 | 15-Apr-26 | 14-May-26 | 16-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B2-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 16-Apr-26 | 16-Apr-26 | 17-May-26 | 18-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B2-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 18-Apr-26 | 19-Apr-26 | 19-May-26 | 20-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B2-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 20-Apr-26 | 27-Apr-26 | 24-May-26 | 09-Jun-26 | 46,046.19 | 46,046.19 | 1.00 |
| GRADE BEAM | | 16 | 171,632.86 | 28-Apr-26 | 18-May-26 | 13-Jun-26 | 25-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B2-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 28-Apr-26 | 28-Apr-26 | 13-Jun-26 | 13-Jun-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B2-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 29-Apr-26 | 30-Apr-26 | 13-Jun-26 | 13-Jun-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B2-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 02-May-26 | 03-May-26 | 13-Jun-26 | 13-Jun-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B2-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 04-May-26 | 09-May-26 | 15-Jun-26 | 18-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B2-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 10-May-26 | 11-May-26 | 17-Jun-26 | 21-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B2-S-341 | Anchor bolts installation | 2 | 57,238.83 | 10-May-26 | 11-May-26 | 18-Jun-26 | 20-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |

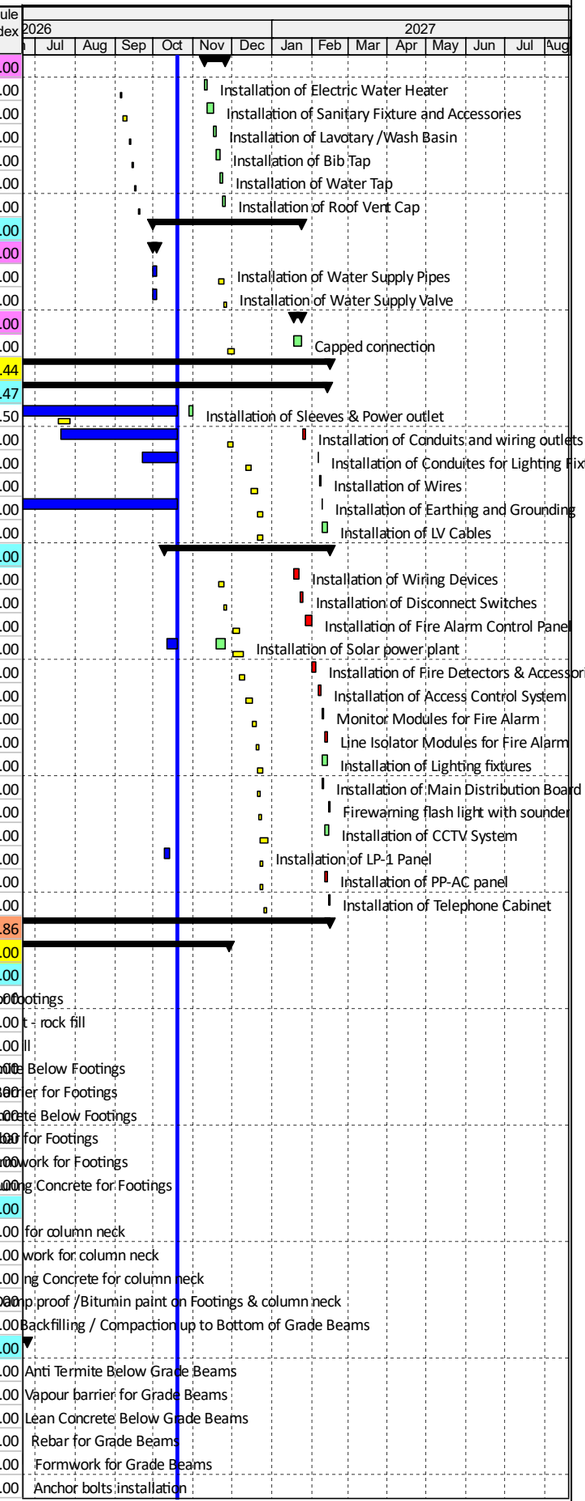





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B2-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 12-May-26 | 12-May-26 | 22-Jun-26 | 22-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B2-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 13-May-26 | 18-May-26 | 24-Jun-26 | 25-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 126 | 397,232.98 | 19-May-26 | 29-Sep-26 | 02-Jul-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B2-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 19-May-26 | 30-May-26 | 02-Jul-26 | 06-Jul-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B2-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 04-Jun-26 | 04-Jun-26 | 09-Aug-26 | 10-Aug-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B2-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 06-Jun-26 | 07-Jun-26 | 09-Aug-26 | 10-Aug-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B2-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 25-Jul-26 | 29-Jul-26 | 09-Aug-26 | 10-Aug-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B2-S-517 | Concrete pad | 7 | 907.11 | 20-Sep-26 | 29-Sep-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 66 | 101,966.98 | 31-May-26 | 29-Jun-26 | 15-Jun-26 | 04-Oct-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B2-S-5101 | Rebar for column | 5 | 20,144.05 | 31-May-26 | 04-Jun-26 | 22-Jul-26 | 30-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B2-S-5102 | Formwork for column | 4 | 5,036.01 | 06-Jun-26 | 09-Jun-26 | 11-Aug-26 | 18-Aug-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B2-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 10-Jun-26 | 10-Jun-26 | 13-Aug-26 | 22-Aug-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B2-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 11-Jun-26 | 15-Jun-26 | 15-Jun-26 | 18-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B2-S-6102 | Formwork for  Tie Beams | 2 | 1,815.91 | 16-Jun-26 | 17-Jun-26 | 17-Jun-26 | 21-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B2-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 21-Jun-26 | 21-Jun-26 | 22-Jun-26 | 22-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B2-S-6113 | Rebar for Beams | 4 | 13,379.11 | 22-Jun-26 | 25-Jun-26 | 17-Sep-26 | 20-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B2-S-6123 | Formwork for  Beams | 2 | 3,344.77 | 27-Jun-26 | 28-Jun-26 | 28-Sep-26 | 01-Oct-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B2-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 29-Jun-26 | 29-Jun-26 | 03-Oct-26 | 04-Oct-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 63 | 1,566,668.48 | 08-Aug-26 | 01-Oct-26 | 12-Jul-26 | | 1,566,668.48 | 1,176,914.38 | 0.75 |
| DAM3-C-B2-SS-0100 | Installation of columns | 3 | 217,507.55 | 08-Aug-26 | 10-Aug-26 | 12-Jul-26 | 13-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B2-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 11-Aug-26 | 16-Aug-26 | 12-Jul-26 | 14-Jul-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B2-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 26-Aug-26 | 03-Sep-26 | 30-Jul-26 | 01-Aug-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B2-SS-0140 | Installation of roof sheet | 5 | 217,507.55 | 03-Sep-26 | 09-Sep-26 | 06-Aug-26 | 13-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B2-SS-620 | Steel members for office area | 7 | 115,805.20 | 03-Sep-26 | 12-Sep-26 | | | 115,805.20 | 0.00 | 0.00 |
| DAM3-C-B2-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 12-Sep-26 | 20-Sep-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B2-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 12-Sep-26 | 20-Sep-26 | | | 18,670.78 | 0.00 | 0.00 |
| DAM3-C-B2-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 20-Sep-26 | 27-Sep-26 | | | 3,734.16 | 0.00 | 0.00 |
| DAM3-C-B2-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 26-Sep-26 | 01-Oct-26 | 18-Oct-26 | | 326,261.32 | 97,878.40 | 0.30 |
| **ARCHITECTURAL** | | 97 | 900,244.66 | 17-Aug-26 | 02-Jan-27 | 12-Aug-26 | | 357,493.20 | 140,489.42 | 0.39 |
| **MASONARY WORKS** | | 19 | 78,954.21 | 17-Aug-26 | 29-Sep-26 | 22-Aug-26 | 27-Sep-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B2-A-0120 | Block work at factory area | 8 | 58,338.72 | 17-Aug-26 | 27-Aug-26 | 22-Aug-26 | 25-Aug-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B2-A-0150 | Block work at office area | 7 | 6,179.18 | 12-Sep-26 | 20-Sep-26 | 22-Aug-26 | 08-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B2-A-170 | Block work at toilet area | 7 | 14,436.31 | 20-Sep-26 | 29-Sep-26 | 22-Aug-26 | 27-Sep-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 24 | 92,757.47 | 08-Oct-26 | 24-Nov-26 | 04-Oct-26 | | 29,963.93 | 48,590.16 | 1.62 |
| DAM3-C-B2-A-180 | Internal Wall Plaster | 15 | 48,590.16 | 08-Oct-26 | 26-Oct-26 | 04-Oct-26 | 15-Oct-26 | 29,963.93 | 48,590.16 | 1.62 |
| DAM3-C-B2-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 7 | 44,167.30 | 16-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 08-Nov-26 | 14-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-240 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 08-Nov-26 | 14-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 67 | 189,488.90 | 31-Oct-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-220 | Tiles for Toilet | 7 | 46,530.71 | 31-Oct-26 | 08-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-250 | Tiles for Office Area | 2 | 26,867.31 | 14-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-390 | Granite strip | 2 | 671.12 | 16-Nov-26 | 18-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-420 | Epoxy paint | 3 | 115,419.76 | 22-Dec-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 11 | 248,575.06 | 01-Oct-26 | 18-Oct-26 | 11-Oct-26 | | 248,575.06 | 6,489.89 | 0.03 |
| DAM3-C-B2-A-552 | Window (CW1) | 5 | 94,173.21 | 01-Oct-26 | 10-Oct-26 | | | 94,173.21 | 0.00 | 0.00 |
| DAM3-C-B2-A-553 | Roll up  Shutter Door | 1 | 68,619.20 | 10-Oct-26 | 11-Oct-26 | | | 68,619.20 | 0.00 | 0.00 |
| DAM3-C-B2-A-200 | Supply and install (D5) 1000*2200mm single leaf  steel door with do | 1 | 16,016.16 | 11-Oct-26 | 12-Oct-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B2-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 12-Oct-26 | 13-Oct-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B2-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 13-Oct-26 | 14-Oct-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B2-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 14-Oct-26 | 15-Oct-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B2-A-557 | Supply and install  fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 15-Oct-26 | 17-Oct-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B2-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 17-Oct-26 | 18-Oct-26 | 11-Oct-26 | 14-Oct-26 | 6,489.89 | 6,489.89 | 1.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 26-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 26-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **METAL WORKS** | | 27 | 193,717.06 | 18-Nov-26 | 03-Dec-26 | 12-Aug-26 | | 0.00 | 6,455.16 | 0.00 |
| DAM3-C-B2-A-290 | Steel Ladder | 2 | 9,839.16 | 18-Nov-26 | 21-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-291 | Steel railing works | 4 | 1,533.98 | 21-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-292 | Aluminium composite panel | 5 | 175,888.76 | 25-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 01-Dec-26 | 03-Dec-26 | 12-Aug-26 | 12-Aug-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 36 | 45,080.66 | 03-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-320 | Installation of fittings | 5 | 22,981.27 | 03-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 09-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |

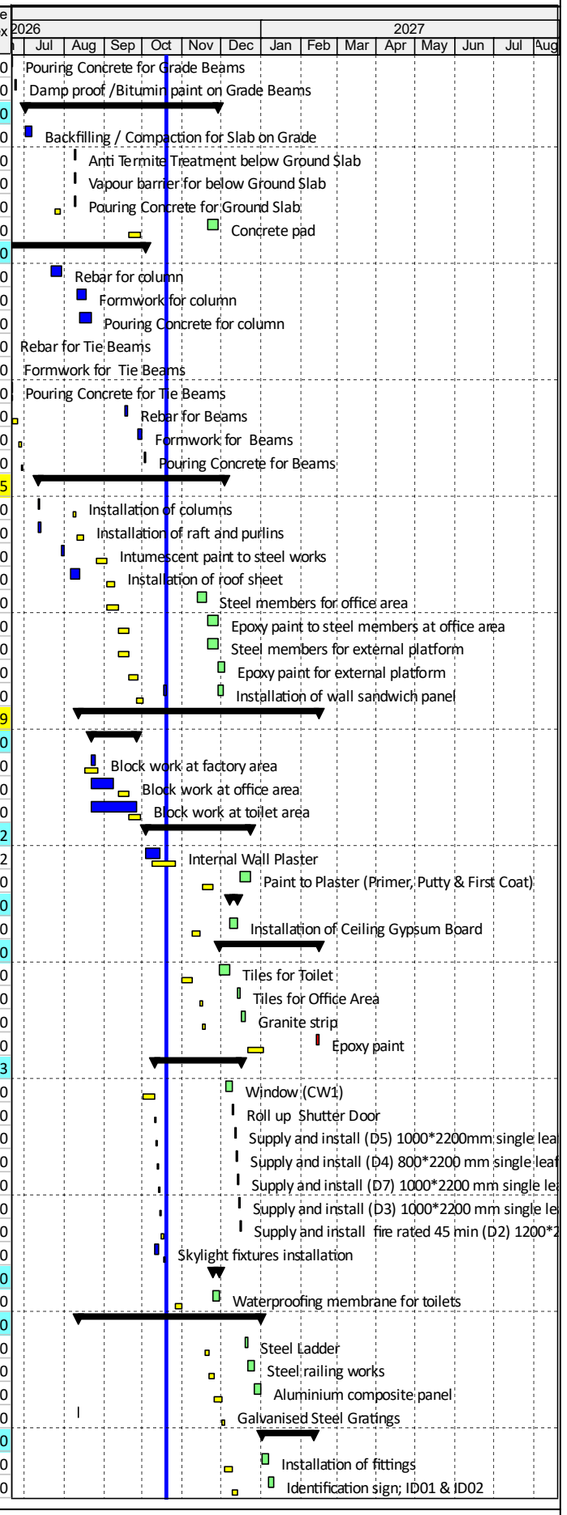


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B2-A-340 | Furniture Installation | 1 | 12,468.83 | 21-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 147 | 467,522.66 | 19-May-26 | 14-Dec-26 | 23-Jul-26 | | 18,585.14 | 156,280.78 | 8.41 |
| **HVAC** | | 14 | 233,183.33 | 24-Nov-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 01-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 01-Dec-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 03-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SECOND STAGE** | | 14 | 62,488.60 | 24-Nov-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 24-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-160 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 26-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-339 | Installation of Diffuser | 2 | 2,144.00 | 06-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 08-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 21 | 102,458.78 | 24-Nov-26 | 14-Dec-26 | 10-Sep-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 12 | 84,594.16 | 24-Nov-26 | 08-Dec-26 | 10-Sep-26 | 21-Sep-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B2-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 24-Nov-26 | 02-Dec-26 | 10-Sep-26 | 21-Sep-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B2-M-310 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 02-Dec-26 | 08-Dec-26 | 10-Sep-26 | 21-Sep-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 17 | 17,864.62 | 08-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 08-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 10-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 132 | 90,009.74 | 19-May-26 | 02-Dec-26 | 23-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| **FIRST STAGE** | | 127 | 41,149.90 | 19-May-26 | 16-Nov-26 | 23-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B2-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 19-May-26 | 23-May-26 | 23-Jul-26 | 27-Jul-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B2-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 08-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-380 | Installation of Trench drain | 5 | 11,508.80 | 10-Nov-26 | 16-Nov-26 | 03-Aug-26 | 04-Aug-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 16-Nov-26 | 02-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 16-Nov-26 | 18-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 18-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 23-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 25-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-428 | Installation of Water Tap | 2 | 2,874.14 | 28-Nov-26 | 30-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 30-Nov-26 | 02-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 17 | 41,870.81 | 24-Nov-26 | 07-Dec-26 | 01-Oct-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 6 | 41,592.68 | 24-Nov-26 | 01-Dec-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B2-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 24-Nov-26 | 29-Nov-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B2-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 29-Nov-26 | 01-Dec-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 18,274.27 | 0.00 |
| **SECOND STAGE** | | 5 | 278.13 | 01-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-M-330 | Capped connection | 5 | 278.13 | 01-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 59 | 752,044.76 | 29-Sep-26 | 21-Dec-26 | 17-Jun-26 | | 94,632.83 | 71,373.28 | 0.75 |
| **FIRST STAGE** | | 47 | 86,114.12 | 29-Sep-26 | 11-Nov-26 | 17-Jun-26 | | 18,441.09 | 27,642.87 | 1.50 |
| DAM3-C-B2-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 29-Sep-26 | 04-Oct-26 | 17-Jun-26 | | 1,768.31 | 884.15 | 0.50 |
| DAM3-C-B2-E-183 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 29-Sep-26 | 08-Oct-26 | 18-Jun-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B2-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 13-Oct-26 | 18-Oct-26 | 29-Sep-26 | | 8,462.97 | 7,616.67 | 0.90 |
| DAM3-C-B2-E-233 | Installation of Wires | 4 | 16,925.94 | 18-Oct-26 | 22-Oct-26 | | | 5,289.36 | 0.00 | 0.00 |
| DAM3-C-B2-E-223 | Installation of LV Cables | 4 | 36,389.98 | 01-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-113 | Installation of Earthing and Grounding | 5 | 19,646.47 | 05-Nov-26 | 11-Nov-26 | 18-Jun-26 | | 0.00 | 17,681.82 | 0.00 |
| **SECOND STAGE** | | 43 | 665,930.64 | 04-Oct-26 | 21-Dec-26 | 10-Oct-26 | | 76,191.74 | 43,730.41 | 0.57 |
| DAM3-C-B2-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 04-Oct-26 | 08-Oct-26 | | | 19,451.37 | 0.00 | 0.00 |
| DAM3-C-B2-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 08-Oct-26 | 13-Oct-26 | | | 56,740.37 | 0.00 | 0.00 |
| DAM3-C-B2-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 22-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 22-Oct-26 | 25-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-410 | Installation of CCTV System | 6 | 76,349.24 | 22-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 25-Oct-26 | 27-Oct-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B2-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 27-Oct-26 | 29-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 29-Oct-26 | 01-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-273 | Installation of Access Control System | 5 | 27,616.86 | 31-Oct-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 05-Nov-26 | 08-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 08-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 10-Nov-26 | 12-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-173 | Installation of Wiring Devices | 4 | 19,435.09 | 24-Nov-26 | 29-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 29-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B2-E-420 | Installation of Solar power plant | 10 | 253,268.71 | 10-Dec-26 | 21-Dec-26 | 13-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **BLOCK B1** | | 272 | 5,075,523.09 | 12-Mar-26 | 03-Jan-27 | 17-Mar-26 | | 3,354,324.53 | 2,896,750.65 | 0.86 |
| **STRUCTURAL** | | 204 | 1,389,042.53 | 12-Mar-26 | 21-Sep-26 | 17-Mar-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |

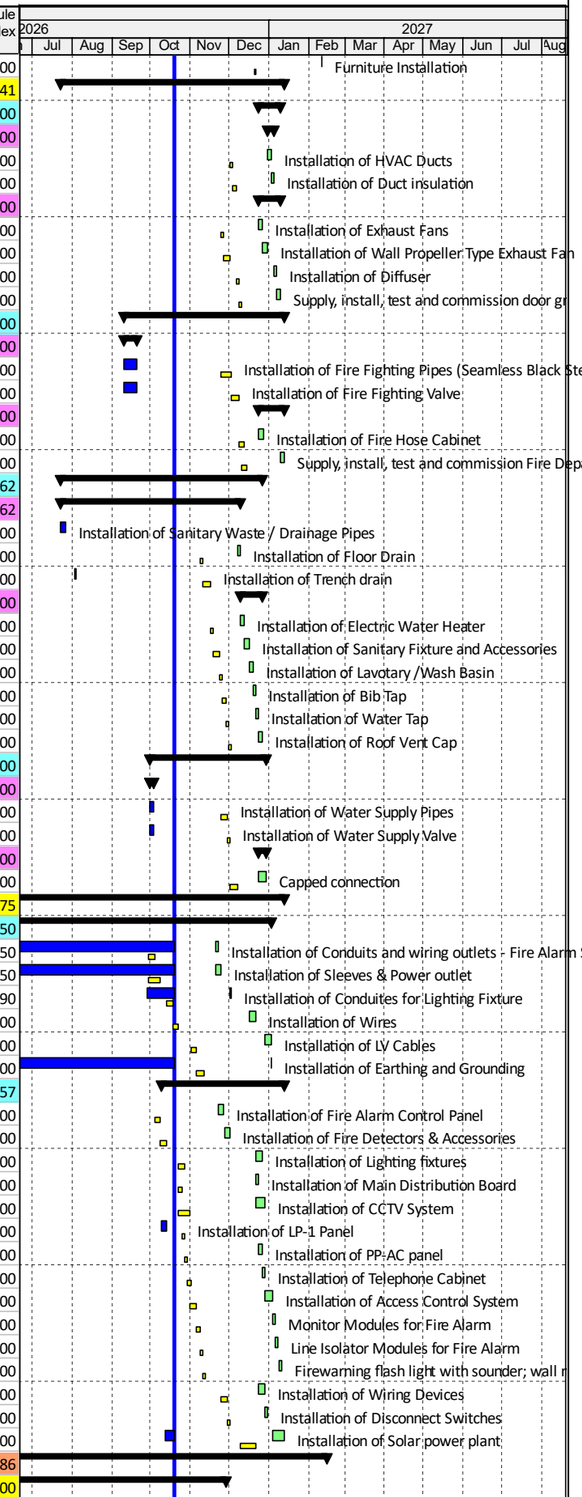




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| **FOOTING** | | 101 | 597,655.16 | 12-Mar-26 | 29-Apr-26 | 17-Mar-26 | 07-May-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B1-S-150 | Excavation for footings | 4 | 89,859.61 | 12-Mar-26 | 16-Mar-26 | 17-Mar-26 | 24-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B1-S-6243 | Soil replacement - rock fill | 4 | 179,061.91 | 21-Mar-26 | 24-Mar-26 | 17-Mar-26 | 24-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B1-S-6253 | Engineering fill | 4 | 46,046.19 | 25-Mar-26 | 29-Mar-26 | 07-Apr-26 | 13-Apr-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B1-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 30-Mar-26 | 30-Mar-26 | 25-Apr-26 | 25-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B1-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 31-Mar-26 | 31-Mar-26 | 25-Apr-26 | 25-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B1-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 13-Apr-26 | 14-Apr-26 | 25-Apr-26 | 25-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B1-S-104 | Rebar for Footings | 4 | 101,844.98 | 20-Apr-26 | 23-Apr-26 | 02-May-26 | 05-May-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B1-S-105 | Formwork for Footings | 4 | 25,461.25 | 25-Apr-26 | 28-Apr-26 | 05-May-26 | 06-May-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B1-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 29-Apr-26 | 29-Apr-26 | 07-May-26 | 07-May-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 10 | 120,554.54 | 30-Apr-26 | 18-May-26 | 05-May-26 | 01-Jun-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B1-S-257 | Rebar for column neck | 4 | 14,919.19 | 30-Apr-26 | 04-May-26 | 05-May-26 | 06-May-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B1-S-267 | Formwork for column neck | 2 | 9,946.13 | 05-May-26 | 06-May-26 | 11-May-26 | 12-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B1-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 07-May-26 | 07-May-26 | 13-May-26 | 13-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B1-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 09-May-26 | 10-May-26 | 16-May-26 | 17-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B1-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 11-May-26 | 18-May-26 | 21-May-26 | 01-Jun-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 11 | 171,632.86 | 19-May-26 | 11-Jun-26 | 06-Jun-26 | 25-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B1-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 19-May-26 | 19-May-26 | 06-Jun-26 | 06-Jun-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B1-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 20-May-26 | 21-May-26 | 06-Jun-26 | 06-Jun-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B1-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 23-May-26 | 24-May-26 | 06-Jun-26 | 06-Jun-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B1-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 25-May-26 | 02-Jun-26 | 08-Jun-26 | 09-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B1-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 03-Jun-26 | 04-Jun-26 | 11-Jun-26 | 15-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B1-S-341 | Anchor bolts installation | 2 | 57,238.83 | 03-Jun-26 | 04-Jun-26 | 11-Jun-26 | 13-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B1-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 06-Jun-26 | 06-Jun-26 | 17-Jun-26 | 17-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B1-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 07-Jun-26 | 11-Jun-26 | 23-Jun-26 | 25-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 119 | 397,232.98 | 13-Jun-26 | 21-Sep-26 | 27-Jun-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B1-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 13-Jun-26 | 20-Jun-26 | 27-Jun-26 | 05-Jul-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B1-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 21-Jun-26 | 21-Jun-26 | 06-Aug-26 | 08-Aug-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B1-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 22-Jun-26 | 23-Jun-26 | 06-Aug-26 | 08-Aug-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B1-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 24-Jun-26 | 28-Jun-26 | 06-Aug-26 | 08-Aug-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B1-S-517 | Concrete pad | 7 | 907.11 | 14-Sep-26 | 21-Sep-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 63 | 101,966.98 | 21-Jun-26 | 18-Jul-26 | 08-Jun-26 | 10-Oct-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B1-S-5101 | Rebar for column | 5 | 20,144.05 | 21-Jun-26 | 25-Jun-26 | 26-Jul-26 | 28-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B1-S-5102 | Formwork for column | 4 | 5,036.01 | 27-Jun-26 | 30-Jun-26 | 22-Aug-26 | 27-Aug-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B1-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 01-Jul-26 | 01-Jul-26 | 25-Aug-26 | 29-Aug-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B1-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 02-Jul-26 | 06-Jul-26 | 08-Jun-26 | 09-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B1-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 07-Jul-26 | 08-Jul-26 | 11-Jun-26 | 15-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B1-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 09-Jul-26 | 09-Jul-26 | 17-Jun-26 | 17-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B1-S-6113 | Rebar for Beams | 4 | 13,379.11 | 11-Jul-26 | 14-Jul-26 | 27-Sep-26 | 04-Oct-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B1-S-6123 | Formwork for Beams | 2 | 3,344.77 | 15-Jul-26 | 16-Jul-26 | 29-Sep-26 | 06-Oct-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B1-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 18-Jul-26 | 18-Jul-26 | 07-Oct-26 | 10-Oct-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 60 | 1,566,668.48 | 11-Aug-26 | 19-Sep-26 | 11-Jul-26 | | 1,566,668.48 | 1,176,914.38 | 0.75 |
| DAM3-C-B1-SS-0100 | Installation of columns | 3 | 217,507.55 | 11-Aug-26 | 13-Aug-26 | 11-Jul-26 | 11-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B1-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 15-Aug-26 | 19-Aug-26 | 11-Jul-26 | 13-Jul-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B1-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 20-Aug-26 | 27-Aug-26 | 25-Jul-26 | 28-Jul-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B1-SS-620 | Steel members for office area | 7 | 115,805.20 | 29-Aug-26 | 05-Sep-26 | | | 115,805.20 | 0.00 | 0.00 |
| DAM3-C-B1-SS-0140 | Installation of roof sheet | 5 | 217,507.55 | 01-Sep-26 | 06-Sep-26 | 04-Aug-26 | 11-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B1-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 06-Sep-26 | 13-Sep-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B1-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 06-Sep-26 | 13-Sep-26 | | | 18,670.78 | 0.00 | 0.00 |
| DAM3-C-B1-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 14-Sep-26 | 19-Sep-26 | 18-Oct-26 | | 326,261.32 | 97,878.40 | 0.30 |
| DAM3-C-B1-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 14-Sep-26 | 19-Sep-26 | | | 3,734.16 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 94 | 900,244.66 | 20-Aug-26 | 03-Jan-27 | 10-Aug-26 | | 327,518.07 | 104,046.80 | 0.32 |
| **MASONARY WORKS** | | 28 | 78,954.21 | 20-Aug-26 | 07-Oct-26 | 15-Aug-26 | 07-Sep-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B1-A-0120 | Block work at factory area | 10 | 58,338.72 | 20-Aug-26 | 31-Aug-26 | 15-Aug-26 | 23-Aug-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B1-A-0150 | Block work at office area | 7 | 6,179.18 | 06-Sep-26 | 13-Sep-26 | 23-Aug-26 | 06-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B1-A-170 | Block work at toilet area | 7 | 14,436.31 | 30-Sep-26 | 07-Oct-26 | 02-Sep-26 | 07-Sep-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 40 | 92,757.47 | 18-Oct-26 | 06-Dec-26 | 19-Oct-26 | | 6,478.69 | 12,147.54 | 1.88 |
| DAM3-C-B1-A-180 | Internal Wall Plaster | 10 | 48,590.16 | 18-Oct-26 | 03-Nov-26 | 19-Oct-26 | | 6,478.69 | 12,147.54 | 1.88 |
| DAM3-C-B1-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 3 | 44,167.30 | 29-Nov-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **CIELING FINISHES** | | 3 | 46,792.30 | 21-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-240 | Installation of Ceiling Gypsum Board | 3 | 46,792.30 | 21-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 48 | 189,488.90 | 11-Nov-26 | 03-Jan-27 | | | 0.00 | 0.00 | 0.00 |

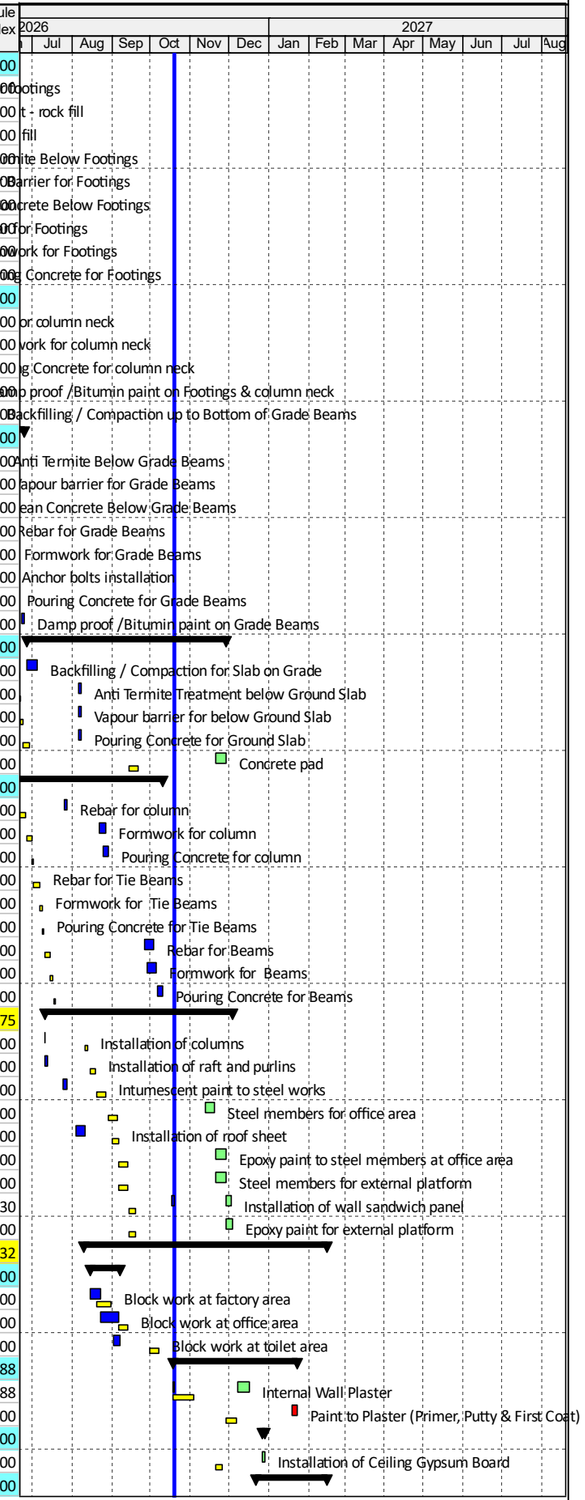


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B1-A-220 | Tiles for Toilet | 4 | 46,530.71 | 11-Nov-26 | 18-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-250 | Tiles for Office Area | 2 | 26,867.31 | 26-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-390 | Granite strip | 2 | 671.12 | 29-Nov-26 | 30-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-420 | Epoxy paint | 7 | 115,419.76 | 27-Dec-26 | 03-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 14 | 248,575.06 | 20-Sep-26 | 28-Oct-26 | 15-Oct-26 | | 242,085.17 | 6,489.89 | 0.03 |
| DAM3-C-B1-A-552 | Window (CW1) | 5 | 94,173.21 | 20-Sep-26 | 28-Sep-26 | | | 94,173.21 | 0.00 | 0.00 |
| DAM3-C-B1-A-553 | Roll up Shutter Door | 1 | 68,619.20 | 29-Sep-26 | 29-Sep-26 | | | 68,619.20 | 0.00 | 0.00 |
| DAM3-C-B1-A-200 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 30-Sep-26 | 30-Sep-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B1-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 01-Oct-26 | 01-Oct-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B1-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 03-Oct-26 | 03-Oct-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B1-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 04-Oct-26 | 04-Oct-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B1-A-557 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 05-Oct-26 | 05-Oct-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B1-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 27-Oct-26 | 28-Oct-26 | 15-Oct-26 | 17-Oct-26 | 0.00 | 6,489.89 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 07-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 07-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **METAL WORKS** | | 10 | 193,717.06 | 01-Dec-26 | 15-Dec-26 | 10-Aug-26 | | 0.00 | 6,455.16 | 0.00 |
| DAM3-C-B1-A-290 | Steel Ladder | 2 | 9,839.16 | 01-Dec-26 | 02-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-291 | Steel railing works | 2 | 1,533.98 | 03-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-292 | Aluminium composite panel | 3 | 175,888.76 | 08-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 14-Dec-26 | 15-Dec-26 | 10-Aug-26 | 10-Aug-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 7 | 45,080.66 | 16-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-320 | Installation of fittings | 3 | 22,981.27 | 16-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 22-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-A-340 | Furniture Installation | 1 | 12,468.83 | 26-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 173 | 467,522.66 | 13-Jun-26 | 26-Dec-26 | 18-Jul-26 | | 18,585.14 | 156,280.78 | 8.41 |
| **HVAC** | | 12 | 233,183.33 | 07-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 14-Dec-26 | 17-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 14-Dec-26 | 15-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 16-Dec-26 | 17-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SECOND STAGE** | | 12 | 62,488.60 | 07-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 07-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-160 | Installation of Wall Propeller Type Exhaust Fan | 2 | 46,831.64 | 09-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-339 | Installation of Diffuser | 2 | 2,144.00 | 19-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 21-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 16 | 102,458.78 | 07-Dec-26 | 26-Dec-26 | 06-Sep-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 10 | 84,594.16 | 07-Dec-26 | 20-Dec-26 | 06-Sep-26 | 09-Sep-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B1-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 07-Dec-26 | 14-Dec-26 | 06-Sep-26 | 09-Sep-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B1-M-310 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 15-Dec-26 | 20-Dec-26 | 08-Sep-26 | 09-Sep-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 15 | 17,864.62 | 21-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 21-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 23-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 151 | 90,009.74 | 13-Jun-26 | 13-Dec-26 | 18-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| **FIRST STAGE** | | 137 | 41,149.90 | 13-Jun-26 | 26-Nov-26 | 18-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B1-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 13-Jun-26 | 16-Jun-26 | 18-Jul-26 | 25-Jul-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B1-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 19-Nov-26 | 21-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-380 | Installation of Trench drain | 5 | 11,508.80 | 22-Nov-26 | 26-Nov-26 | 19-Jul-26 | 25-Jul-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 28-Nov-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 28-Nov-26 | 29-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 30-Nov-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 05-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 07-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-428 | Installation of Water Tap | 2 | 2,874.14 | 09-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 12-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 8 | 41,870.81 | 07-Dec-26 | 19-Dec-26 | 13-Oct-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 6 | 41,592.68 | 07-Dec-26 | 13-Dec-26 | 13-Oct-26 | 17-Oct-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B1-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 07-Dec-26 | 10-Dec-26 | 13-Oct-26 | 17-Oct-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B1-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 12-Dec-26 | 13-Dec-26 | 13-Oct-26 | 17-Oct-26 | 0.00 | 18,274.27 | 0.00 |
| **SECOND STAGE** | | 5 | 278.13 | 14-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-M-330 | Capped connection | 5 | 278.13 | 14-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 71 | 752,044.76 | 08-Oct-26 | 29-Dec-26 | 08-Jun-26 | | 52,510.32 | 71,373.28 | 1.36 |
| **FIRST STAGE** | | 48 | 86,114.12 | 08-Oct-26 | 22-Nov-26 | 08-Jun-26 | | 4,688.76 | 27,642.87 | 5.90 |
| DAM3-C-B1-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 08-Oct-26 | 12-Oct-26 | 09-Jun-26 | | 1,768.31 | 884.15 | 0.50 |

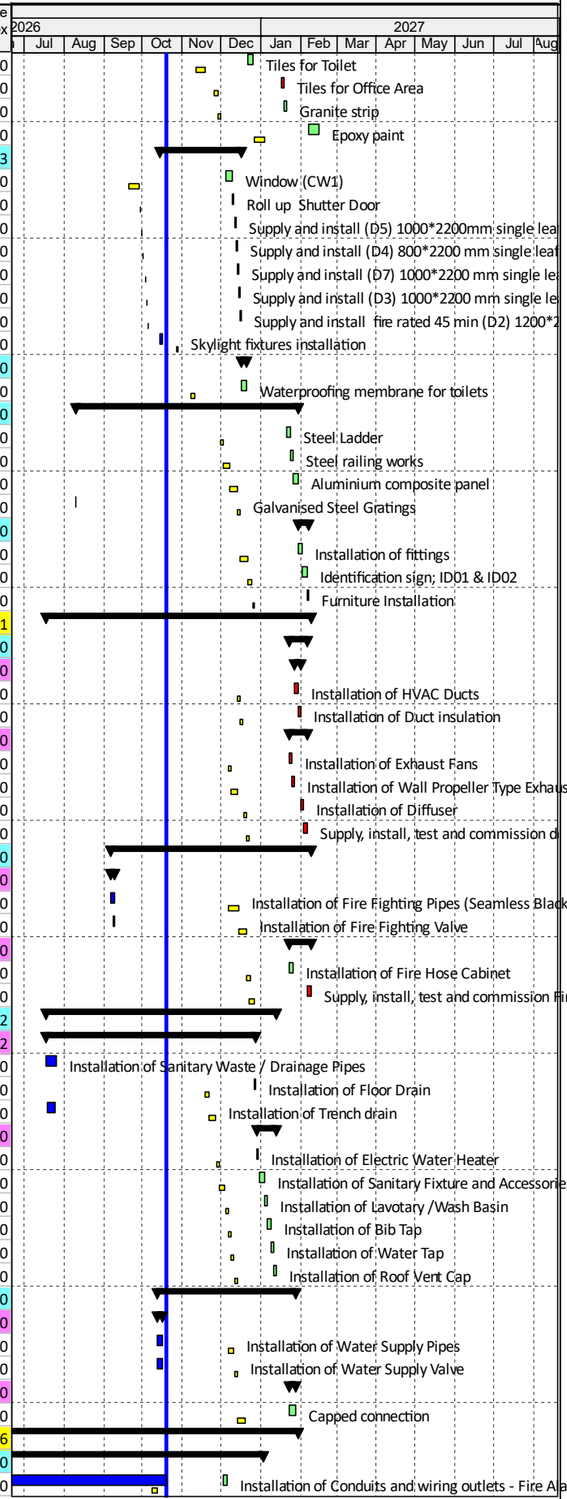




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B1-E-183 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 08-Oct-26 | 17-Oct-26 | 08-Jun-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B1-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 22-Oct-26 | 26-Oct-26 | 01-Oct-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B1-E-233 | Installation of Wires | 4 | 16,925.94 | 28-Oct-26 | 02-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-223 | Installation of LV Cables | 4 | 36,389.98 | 11-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-113 | Installation of Earthing and Grounding | 5 | 19,646.47 | 16-Nov-26 | 22-Nov-26 | 08-Jun-26 | | 0.00 | 17,681.82 | 0.00 |
| **SECOND STAGE** | | 47 | 665,930.64 | 13-Oct-26 | 29-Dec-26 | 10-Oct-26 | | 47,821.56 | 43,730.41 | 0.91 |
| DAM3-C-B1-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 13-Oct-26 | 17-Oct-26 | | | 19,451.37 | 0.00 | 0.00 |
| DAM3-C-B1-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 18-Oct-26 | 21-Oct-26 | | | 28,370.18 | 0.00 | 0.00 |
| DAM3-C-B1-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 02-Nov-26 | 07-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 02-Nov-26 | 04-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-410 | Installation of CCTV System | 7 | 76,349.24 | 02-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 04-Nov-26 | 07-Nov-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B1-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 07-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 09-Nov-26 | 11-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-273 | Installation of Access Control System | 5 | 27,616.86 | 10-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 16-Nov-26 | 18-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 18-Nov-26 | 21-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 21-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-173 | Installation of Wiring Devices | 4 | 19,435.09 | 07-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 12-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B1-E-420 | Installation of Solar power plant | 7 | 253,268.71 | 22-Dec-26 | 29-Dec-26 | 14-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **BLOCK B7** | | 273 | 5,075,523.09 | 10-Feb-26 | 06-Jan-27 | 16-Feb-26 | | 3,446,966.96 | 4,160,544.65 | 1.21 |
| **STRUCTURAL** | | 212 | 1,389,042.53 | 10-Feb-26 | 26-Sep-26 | 16-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 32 | 597,655.16 | 10-Feb-26 | 25-Mar-26 | 16-Feb-26 | 11-Apr-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B7-S-150 | Excavation for footings | 8 | 89,859.61 | 10-Feb-26 | 19-Feb-26 | 16-Feb-26 | 19-Feb-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B7-S-6263 | Soil replacement - rock fill | 6 | 179,061.91 | 19-Feb-26 | 28-Feb-26 | 21-Feb-26 | 26-Feb-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B7-S-6273 | Engineering fill | 6 | 46,046.19 | 01-Mar-26 | 07-Mar-26 | 05-Mar-26 | 11-Mar-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B7-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 08-Mar-26 | 08-Mar-26 | 25-Mar-26 | 25-Mar-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B7-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 09-Mar-26 | 09-Mar-26 | 25-Mar-26 | 25-Mar-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B7-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 10-Mar-26 | 11-Mar-26 | 25-Mar-26 | 25-Mar-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B7-S-104 | Rebar for Footings | 4 | 101,844.98 | 12-Mar-26 | 16-Mar-26 | 05-Apr-26 | 09-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B7-S-105 | Formwork for Footings | 4 | 25,461.25 | 21-Mar-26 | 24-Mar-26 | 06-Apr-26 | 09-Apr-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B7-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 25-Mar-26 | 25-Mar-26 | 11-Apr-26 | 11-Apr-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 19 | 120,554.54 | 26-Mar-26 | 13-Apr-26 | 09-Apr-26 | 10-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B7-S-257 | Rebar for column neck | 4 | 14,919.19 | 26-Mar-26 | 30-Mar-26 | 09-Apr-26 | 11-Apr-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B7-S-267 | Formwork for column neck | 2 | 9,946.13 | 31-Mar-26 | 01-Apr-26 | 15-Apr-26 | 15-Apr-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B7-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 02-Apr-26 | 02-Apr-26 | 16-Apr-26 | 16-Apr-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B7-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 04-Apr-26 | 05-Apr-26 | 20-Apr-26 | 23-Apr-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B7-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 06-Apr-26 | 13-Apr-26 | 02-May-26 | 10-May-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 14 | 171,632.86 | 14-Apr-26 | 04-May-26 | 13-May-26 | 31-May-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B7-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 14-Apr-26 | 14-Apr-26 | 13-May-26 | 13-May-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B7-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 15-Apr-26 | 16-Apr-26 | 13-May-26 | 13-May-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B7-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 18-Apr-26 | 19-Apr-26 | 13-May-26 | 13-May-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B7-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 20-Apr-26 | 25-Apr-26 | 16-May-26 | 18-May-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B7-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 26-Apr-26 | 27-Apr-26 | 18-May-26 | 19-May-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B7-S-341 | Anchor bolts installation | 2 | 57,238.83 | 26-Apr-26 | 27-Apr-26 | 16-May-26 | 18-May-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B7-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 28-Apr-26 | 28-Apr-26 | 20-May-26 | 20-May-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B7-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 29-Apr-26 | 04-May-26 | 23-May-26 | 31-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 143 | 397,232.98 | 05-May-26 | 26-Sep-26 | 01-Jun-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B7-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 05-May-26 | 12-May-26 | 01-Jun-26 | 08-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B7-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 13-May-26 | 13-May-26 | 08-Jul-26 | 12-Jul-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B7-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 14-May-26 | 16-May-26 | 08-Jul-26 | 12-Jul-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B7-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 17-May-26 | 20-May-26 | 08-Jul-26 | 12-Jul-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B7-S-517 | Concrete pad | 7 | 907.11 | 17-Sep-26 | 26-Sep-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 58 | 101,966.98 | 13-May-26 | 13-Jun-26 | 11-May-26 | 29-Aug-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B7-S-5101 | Rebar for column | 5 | 20,144.05 | 13-May-26 | 18-May-26 | 25-Jun-26 | 02-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B7-S-5102 | Formwork for column | 4 | 5,036.01 | 19-May-26 | 23-May-26 | 01-Jun-26 | 07-Jul-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B7-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 24-May-26 | 24-May-26 | 05-Jul-26 | 22-Jul-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B7-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 25-May-26 | 01-Jun-26 | 11-May-26 | 12-May-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B7-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 02-Jun-26 | 03-Jun-26 | 13-May-26 | 13-May-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B7-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 04-Jun-26 | 04-Jun-26 | 14-May-26 | 14-May-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B7-S-6113 | Rebar for Beams | 4 | 13,379.11 | 06-Jun-26 | 09-Jun-26 | 16-Aug-26 | 19-Aug-26 | 13,379.11 | 13,379.11 | 1.00 |

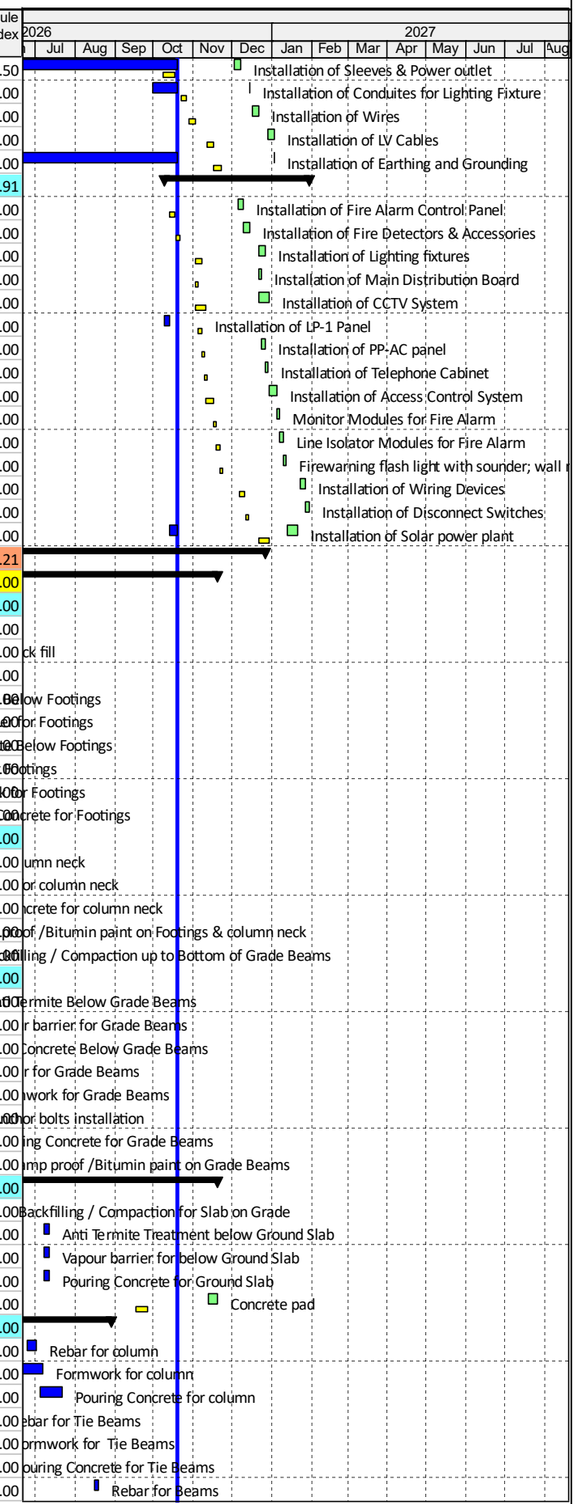




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B7-S-6123 | Formwork for Beams | 2 | 3,344.77 | 10-Jun-26 | 11-Jun-26 | 20-Aug-26 | 26-Aug-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B7-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 13-Jun-26 | 13-Jun-26 | 26-Aug-26 | 29-Aug-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 41 | 1,566,668.48 | 15-Aug-26 | 22-Sep-26 | 13-Jun-26 | | 1,566,668.48 | 1,539,773.29 | 0.98 |
| DAM3-C-B7-SS-0100 | Installation of columns | 3 | 217,507.55 | 15-Aug-26 | 17-Aug-26 | 13-Jun-26 | 13-Jun-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B7-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 18-Aug-26 | 23-Aug-26 | 14-Jun-26 | 15-Jun-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B7-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 24-Aug-26 | 31-Aug-26 | 14-Jun-26 | 21-Jun-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B7-SS-620 | Steel members for office area | 7 | 115,805.20 | 01-Sep-26 | 08-Sep-26 | 21-Sep-26 | 24-Sep-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B7-SS-0140 | Installation of roof sheet | 5 | 217,507.55 | 05-Sep-26 | 09-Sep-26 | 07-Jul-26 | 25-Jul-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B7-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 09-Sep-26 | 16-Sep-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B7-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 09-Sep-26 | 16-Sep-26 | 24-Aug-26 | 19-Sep-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B7-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 17-Sep-26 | 22-Sep-26 | 01-Sep-26 | 24-Sep-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B7-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 17-Sep-26 | 22-Sep-26 | | | 3,734.16 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 75 | 900,244.66 | 24-Aug-26 | 19-Dec-26 | 01-Jul-26 | | 366,401.40 | 581,675.79 | 1.59 |
| **MASONARY WORKS** | | 23 | 78,954.21 | 24-Aug-26 | 26-Sep-26 | 22-Jul-26 | 17-Aug-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B7-A-0120 | Block work at factory area | 10 | 58,338.72 | 24-Aug-26 | 03-Sep-26 | 22-Jul-26 | 26-Jul-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B7-A-0150 | Block work at office area | 7 | 6,179.18 | 09-Sep-26 | 16-Sep-26 | 25-Jul-26 | 17-Aug-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B7-A-170 | Block work at toilet area | 7 | 14,436.31 | 17-Sep-26 | 26-Sep-26 | 26-Jul-26 | 17-Aug-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 15 | 92,757.47 | 06-Oct-26 | 21-Nov-26 | 03-Sep-26 | | 38,872.13 | 86,132.37 | 2.22 |
| DAM3-C-B7-A-180 | Internal Wall Plaster | 15 | 48,590.16 | 06-Oct-26 | 22-Oct-26 | 03-Sep-26 | 24-Sep-26 | 38,872.13 | 48,590.16 | 1.25 |
| DAM3-C-B7-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 4 | 44,167.30 | 14-Nov-26 | 21-Nov-26 | 28-Sep-26 | | 0.00 | 37,542.21 | 0.00 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 05-Nov-26 | 10-Nov-26 | 04-Oct-26 | 15-Oct-26 | 0.00 | 46,792.30 | 0.00 |
| DAM3-C-B7-A-240 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 05-Nov-26 | 10-Nov-26 | 04-Oct-26 | 15-Oct-26 | 0.00 | 46,792.30 | 0.00 |
| **FLOOR FINISHES** | | 29 | 189,488.90 | 28-Oct-26 | 19-Dec-26 | 19-Sep-26 | | 0.00 | 66,681.19 | 0.00 |
| DAM3-C-B7-A-220 | Tiles for Toilet | 7 | 46,530.71 | 28-Oct-26 | 04-Nov-26 | 19-Sep-26 | 28-Sep-26 | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B7-A-250 | Tiles for Office Area | 2 | 26,867.31 | 11-Nov-26 | 12-Nov-26 | 19-Oct-26 | | 0.00 | 20,150.48 | 0.00 |
| DAM3-C-B7-A-390 | Granite strip | 2 | 671.12 | 14-Nov-26 | 15-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-A-420 | Epoxy paint | 7 | 115,419.76 | 12-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 8 | 248,575.06 | 24-Sep-26 | 10-Oct-26 | 21-Sep-26 | | 248,575.06 | 159,864.98 | 0.64 |
| DAM3-C-B7-A-552 | Window (CW1) | 7 | 94,173.21 | 24-Sep-26 | 01-Oct-26 | 05-Oct-26 | | 94,173.21 | 84,755.89 | 0.90 |
| DAM3-C-B7-A-553 | Roll up Shutter Door | 1 | 68,619.20 | 03-Oct-26 | 03-Oct-26 | 18-Oct-26 | 20-Oct-26 | 68,619.20 | 68,619.20 | 1.00 |
| DAM3-C-B7-A-200 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 04-Oct-26 | 04-Oct-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B7-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 05-Oct-26 | 05-Oct-26 | | | 22,737.85 | 0.00 | 0.00 |
| DAM3-C-B7-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 06-Oct-26 | 06-Oct-26 | | | 7,811.07 | 0.00 | 0.00 |
| DAM3-C-B7-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 07-Oct-26 | 07-Oct-26 | | | 16,016.16 | 0.00 | 0.00 |
| DAM3-C-B7-A-557 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 08-Oct-26 | 08-Oct-26 | | | 16,711.52 | 0.00 | 0.00 |
| DAM3-C-B7-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 10-Oct-26 | 10-Oct-26 | 21-Sep-26 | 26-Sep-26 | 6,489.89 | 6,489.89 | 1.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 24-Oct-26 | 27-Oct-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 4,879.02 | 0.00 |
| DAM3-C-B7-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 24-Oct-26 | 27-Oct-26 | 01-Oct-26 | 04-Oct-26 | 0.00 | 4,879.02 | 0.00 |
| **METAL WORKS** | | 25 | 193,717.06 | 16-Nov-26 | 30-Nov-26 | 01-Jul-26 | | 0.00 | 138,371.73 | 0.00 |
| DAM3-C-B7-A-290 | Steel Ladder | 2 | 9,839.16 | 16-Nov-26 | 17-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-A-291 | Steel railing works | 4 | 1,533.98 | 18-Nov-26 | 22-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-A-292 | Aluminium composite panel | 5 | 175,888.76 | 23-Nov-26 | 28-Nov-26 | 30-Sep-26 | | 0.00 | 131,916.57 | 0.00 |
| DAM3-C-B7-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 29-Nov-26 | 30-Nov-26 | 01-Jul-26 | 01-Jul-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 9 | 45,080.66 | 01-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-A-320 | Installation of fittings | 5 | 22,981.27 | 01-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 07-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-A-340 | Furniture Installation | 1 | 12,468.83 | 10-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 178 | 467,522.66 | 05-May-26 | 10-Dec-26 | 10-Jun-26 | | 18,585.14 | 328,795.02 | 17.69 |
| **HVAC** | | 22 | 233,183.33 | 22-Nov-26 | 07-Dec-26 | 05-Oct-26 | | 0.00 | 170,694.73 | 0.00 |
| **FIRST STAGE** | | 6 | 170,694.73 | 29-Nov-26 | 02-Dec-26 | 05-Oct-26 | 11-Oct-26 | 0.00 | 170,694.73 | 0.00 |
| DAM3-C-B7-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 29-Nov-26 | 30-Nov-26 | 05-Oct-26 | 11-Oct-26 | 0.00 | 149,489.33 | 0.00 |
| DAM3-C-B7-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 01-Dec-26 | 02-Dec-26 | 06-Oct-26 | 11-Oct-26 | 0.00 | 21,205.40 | 0.00 |
| **SECOND STAGE** | | 9 | 62,488.60 | 22-Nov-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 22-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-160 | Installation of Wall Propeller Type Exhaust Fan | 3 | 46,831.64 | 24-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-339 | Installation of Diffuser | 2 | 2,144.00 | 03-Dec-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 06-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 40 | 102,458.78 | 22-Nov-26 | 10-Dec-26 | 29-Jul-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 17 | 84,594.16 | 22-Nov-26 | 05-Dec-26 | 29-Jul-26 | 12-Aug-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B7-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 22-Nov-26 | 29-Nov-26 | 29-Jul-26 | 10-Aug-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B7-M-310 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 30-Nov-26 | 05-Dec-26 | 09-Aug-26 | 12-Aug-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 12 | 17,864.62 | 06-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |

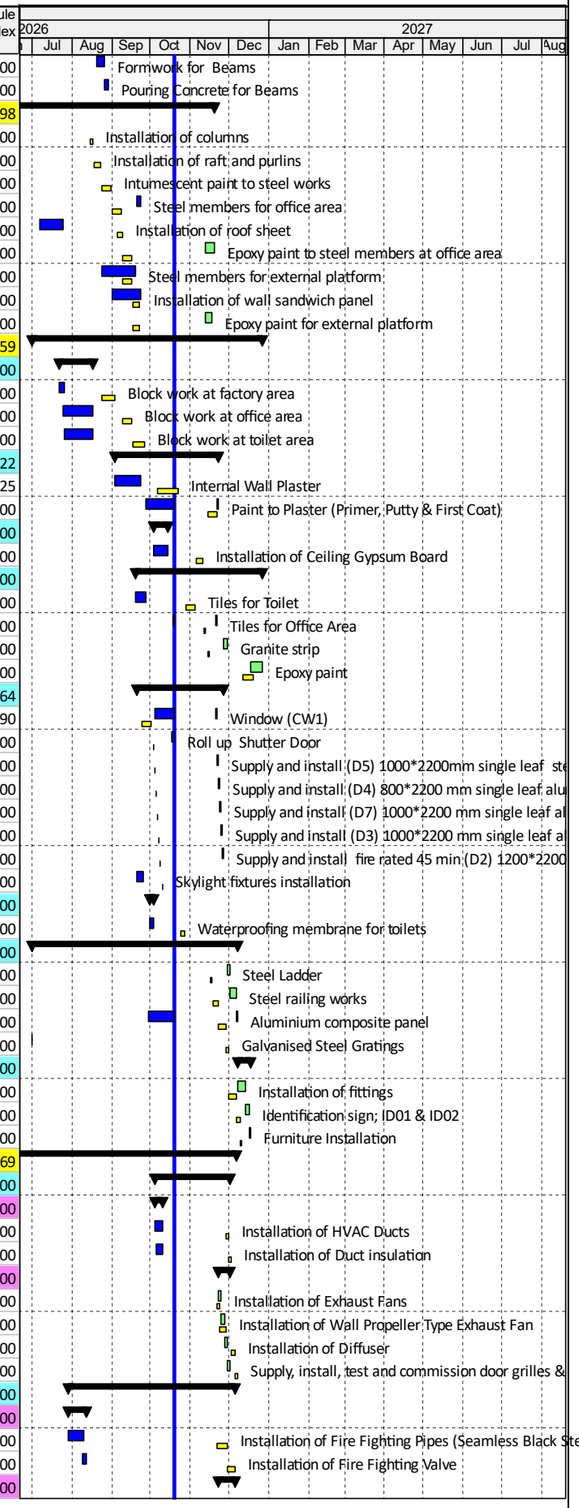




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B7-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 06-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 08-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 153 | 90,009.74 | 05-May-26 | 29-Nov-26 | 10-Jun-26 | | 18,585.14 | 31,913.45 | 1.72 |
| **FIRST STAGE** | | 153 | 41,149.90 | 05-May-26 | 12-Nov-26 | 10-Jun-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B7-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 05-May-26 | 09-May-26 | 10-Jun-26 | 14-Jun-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B7-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 05-Nov-26 | 07-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-380 | Installation of Trench drain | 5 | 11,508.80 | 08-Nov-26 | 12-Nov-26 | 16-Jun-26 | 18-Jun-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 12 | 48,859.84 | 14-Nov-26 | 29-Nov-26 | 17-Oct-26 | | 0.00 | 1,819.51 | 0.00 |
| DAM3-C-B7-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 14-Nov-26 | 15-Nov-26 | 17-Oct-26 | 18-Oct-26 | 0.00 | 1,819.51 | 0.00 |
| DAM3-C-B7-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 16-Nov-26 | 19-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 21-Nov-26 | 22-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 23-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-428 | Installation of Water Tap | 2 | 2,874.14 | 25-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 28-Nov-26 | 29-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 44 | 41,870.81 | 22-Nov-26 | 03-Dec-26 | 30-Aug-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 9 | 41,592.68 | 22-Nov-26 | 28-Nov-26 | 30-Aug-26 | 03-Sep-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B7-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 22-Nov-26 | 25-Nov-26 | 30-Aug-26 | 03-Sep-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B7-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 26-Nov-26 | 28-Nov-26 | 31-Aug-26 | 03-Sep-26 | 0.00 | 18,274.27 | 0.00 |
| **SECOND STAGE** | | 5 | 278.13 | 29-Nov-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-M-330 | Capped connection | 5 | 278.13 | 29-Nov-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 67 | 752,044.76 | 27-Sep-26 | 06-Jan-27 | 16-May-26 | | 106,269.41 | 322,165.14 | 3.03 |
| **FIRST STAGE** | | 63 | 86,114.12 | 27-Sep-26 | 08-Nov-26 | 16-May-26 | | 30,077.67 | 27,642.87 | 0.92 |
| DAM3-C-B7-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 27-Sep-26 | 30-Sep-26 | 16-May-26 | | 1,768.31 | 884.15 | 0.50 |
| DAM3-C-B7-E-183 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 27-Sep-26 | 05-Oct-26 | 18-May-26 | | 2,920.45 | 1,460.23 | 0.50 |
| DAM3-C-B7-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 11-Oct-26 | 14-Oct-26 | 06-Sep-26 | | 8,462.97 | 7,616.67 | 0.90 |
| DAM3-C-B7-E-233 | Installation of Wires | 4 | 16,925.94 | 15-Oct-26 | 19-Oct-26 | | | 16,925.94 | 0.00 | 0.00 |
| DAM3-C-B7-E-223 | Installation of LV Cables | 4 | 36,389.98 | 29-Oct-26 | 02-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-113 | Installation of Earthing and Grounding | 5 | 19,646.47 | 03-Nov-26 | 08-Nov-26 | 16-May-26 | | 0.00 | 17,681.82 | 0.00 |
| **SECOND STAGE** | | 67 | 665,930.64 | 01-Oct-26 | 06-Jan-27 | 21-Sep-26 | | 76,191.74 | 294,522.27 | 3.87 |
| DAM3-C-B7-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 01-Oct-26 | 05-Oct-26 | | | 19,451.37 | 0.00 | 0.00 |
| DAM3-C-B7-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 06-Oct-26 | 10-Oct-26 | | | 56,740.37 | 0.00 | 0.00 |
| DAM3-C-B7-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 20-Oct-26 | 24-Oct-26 | 21-Sep-26 | | 0.00 | 22,850.02 | 0.00 |
| DAM3-C-B7-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 20-Oct-26 | 21-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-410 | Installation of CCTV System | 7 | 76,349.24 | 20-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 22-Oct-26 | 24-Oct-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B7-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 25-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 27-Oct-26 | 28-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-273 | Installation of Access Control System | 5 | 27,616.86 | 28-Oct-26 | 02-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 03-Nov-26 | 04-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 05-Nov-26 | 07-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 08-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-173 | Installation of Wiring Devices | 4 | 19,435.09 | 22-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 26-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B7-E-420 | Installation of Solar power plant | 7 | 253,268.71 | 30-Dec-26 | 06-Jan-27 | 04-Oct-26 | 06-Oct-26 | 0.00 | 253,268.71 | 0.00 |
| **BLOCK B8** | | 288 | 5,075,523.09 | 19-Feb-26 | 14-Jan-27 | 17-Feb-26 | | 3,108,677.89 | 3,872,447.51 | 1.25 |
| **STRUCTURAL** | | 208 | 1,389,042.53 | 19-Feb-26 | 17-Oct-26 | 17-Feb-26 | | 1,389,042.53 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 58 | 597,655.16 | 19-Feb-26 | 13-May-26 | 17-Feb-26 | 16-Apr-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B8-S-150 | Excavation for footings | 4 | 89,859.61 | 19-Feb-26 | 25-Feb-26 | 17-Feb-26 | 21-Feb-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B8-S-6283 | Soil replacement - rock fill | 4 | 179,061.91 | 25-Feb-26 | 02-Mar-26 | 28-Feb-26 | 02-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B8-S-6293 | Engineering fill | 4 | 46,046.19 | 03-Mar-26 | 07-Mar-26 | 08-Mar-26 | 16-Mar-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B8-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 08-Mar-26 | 08-Mar-26 | 28-Mar-26 | 28-Mar-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B8-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 09-Mar-26 | 09-Mar-26 | 28-Mar-26 | 28-Mar-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B8-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 10-Mar-26 | 11-Mar-26 | 28-Mar-26 | 28-Mar-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B8-S-104 | Rebar for Footings | 4 | 101,844.98 | 12-Mar-26 | 16-Mar-26 | 11-Apr-26 | 13-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B8-S-105 | Formwork for Footings | 4 | 25,461.25 | 09-May-26 | 12-May-26 | 13-Apr-26 | 14-Apr-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B8-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 13-May-26 | 13-May-26 | 16-Apr-26 | 16-Apr-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 17 | 120,554.54 | 14-May-26 | 04-Jun-26 | 14-Apr-26 | 12-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B8-S-257 | Rebar for column neck | 4 | 14,919.19 | 14-May-26 | 18-May-26 | 14-Apr-26 | 15-Apr-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B8-S-267 | Formwork for column neck | 2 | 9,946.13 | 19-May-26 | 20-May-26 | 22-Apr-26 | 25-Apr-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B8-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 21-May-26 | 21-May-26 | 23-Apr-26 | 25-Apr-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B8-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 23-May-26 | 24-May-26 | 27-Apr-26 | 30-Apr-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B8-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 25-May-26 | 04-Jun-26 | 05-May-26 | 12-May-26 | 46,046.19 | 46,046.19 | 1.00 |

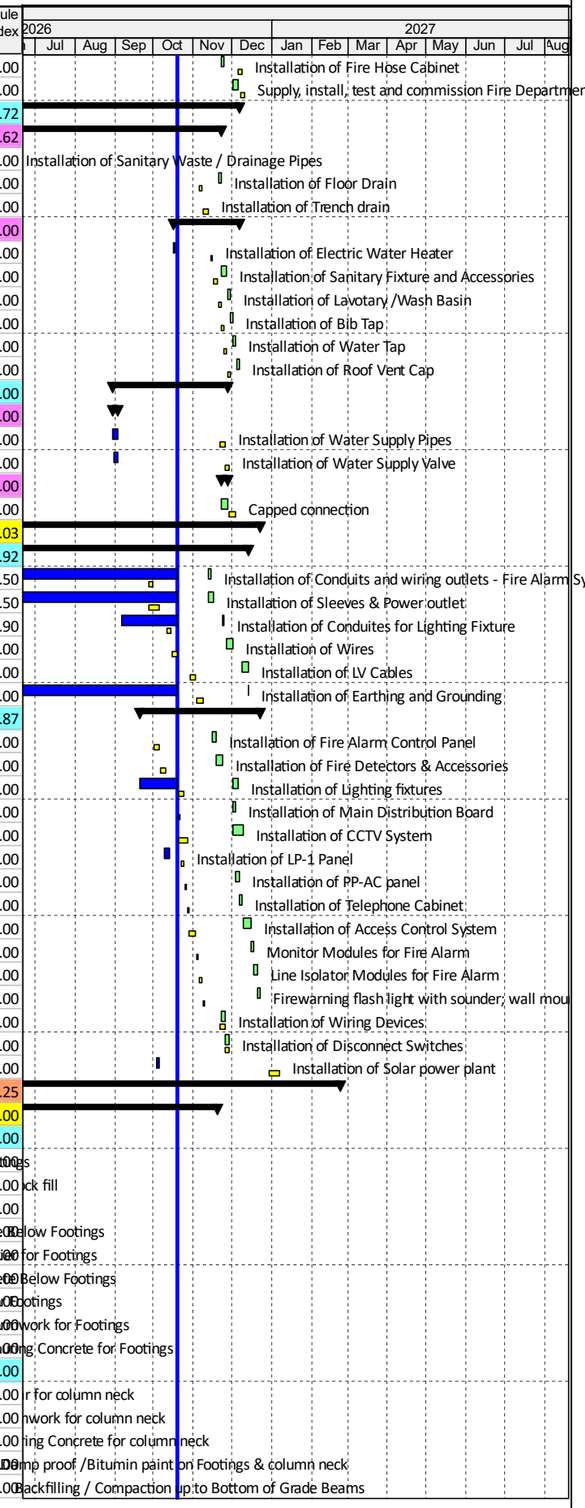




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| **GRADE BEAM** | | 24 | 171,632.86 | 20-Jun-26 | 09-Jul-26 | 13-May-26 | 03-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B8-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 20-Jun-26 | 20-Jun-26 | 13-May-26 | 13-May-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B8-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 21-Jun-26 | 22-Jun-26 | 13-May-26 | 13-May-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B8-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 23-Jun-26 | 24-Jun-26 | 13-May-26 | 13-May-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B8-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 25-Jun-26 | 30-Jun-26 | 16-May-26 | 20-May-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B8-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 01-Jul-26 | 02-Jul-26 | 20-May-26 | 23-May-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B8-S-341 | Anchor bolts installation | 2 | 57,238.83 | 01-Jul-26 | 02-Jul-26 | 17-May-26 | 20-May-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B8-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 04-Jul-26 | 04-Jul-26 | 24-May-26 | 25-May-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B8-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 05-Jul-26 | 09-Jul-26 | 31-May-26 | 03-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 25 | 397,232.98 | 11-Jul-26 | 17-Oct-26 | 04-Jun-26 | | 397,232.98 | 396,325.87 | 1.00 |
| DAM3-C-B8-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 11-Jul-26 | 18-Jul-26 | 04-Jun-26 | 09-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B8-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 19-Jul-26 | 19-Jul-26 | 13-Jul-26 | 16-Jul-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B8-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 20-Jul-26 | 21-Jul-26 | 13-Jul-26 | 16-Jul-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B8-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 22-Jul-26 | 26-Jul-26 | 13-Jul-26 | 16-Jul-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B8-S-517 | Concrete pad | 7 | 907.11 | 10-Oct-26 | 17-Oct-26 | | | 907.11 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 34 | 101,966.98 | 27-Jul-26 | 29-Aug-26 | 16-May-26 | 03-Sep-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B8-S-5101 | Rebar for column | 5 | 20,144.05 | 27-Jul-26 | 01-Aug-26 | 02-Jul-26 | 11-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B8-S-5102 | Formwork for column | 4 | 5,036.01 | 02-Aug-26 | 05-Aug-26 | 07-Jul-26 | 25-Jul-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B8-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 08-Aug-26 | 08-Aug-26 | 13-Jul-26 | 26-Jul-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B8-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 09-Aug-26 | 12-Aug-26 | 16-May-26 | 23-May-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B8-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 13-Aug-26 | 15-Aug-26 | 16-May-26 | 24-May-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B8-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 19-Aug-26 | 20-Aug-26 | 16-May-26 | 25-May-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B8-S-6113 | Rebar for Beams | 4 | 13,379.11 | 20-Aug-26 | 25-Aug-26 | 23-Aug-26 | 26-Aug-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B8-S-6123 | Formwork for Beams | 2 | 3,344.77 | 25-Aug-26 | 27-Aug-26 | 29-Aug-26 | 01-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B8-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 27-Aug-26 | 29-Aug-26 | 01-Sep-26 | 03-Sep-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 44 | 1,566,668.48 | 05-Sep-26 | 14-Oct-26 | 14-Jun-26 | | 1,566,668.48 | 1,539,773.29 | 0.98 |
| DAM3-C-B8-SS-0100 | Installation of columns | 3 | 217,507.55 | 05-Sep-26 | 07-Sep-26 | 14-Jun-26 | 15-Jun-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B8-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 08-Sep-26 | 13-Sep-26 | 15-Jun-26 | 16-Jun-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B8-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 14-Sep-26 | 21-Sep-26 | 17-Jun-26 | 24-Jun-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B8-SS-620 | Steel members for office area | 4 | 115,805.20 | 22-Sep-26 | 30-Sep-26 | 26-Sep-26 | 28-Sep-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B8-SS-0140 | Installation of roof sheet | 5 | 217,507.55 | 27-Sep-26 | 01-Oct-26 | 19-Jul-26 | 01-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B8-SS-1020 | Epoxy paint to steel members at office area | 4 | 23,161.04 | 01-Oct-26 | 08-Oct-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B8-SS-1030 | Steel members for external platform | 4 | 18,670.78 | 01-Oct-26 | 08-Oct-26 | 20-Sep-26 | 21-Sep-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B8-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 10-Oct-26 | 14-Oct-26 | 02-Sep-26 | 22-Sep-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B8-SS-1040 | Epoxy paint for external platform | 3 | 3,734.16 | 10-Oct-26 | 14-Oct-26 | | | 3,734.16 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 89 | 900,244.66 | 14-Sep-26 | 13-Jan-27 | 18-Jul-26 | | 132,767.47 | 544,370.51 | 4.10 |
| **MASONARY WORKS** | | 18 | 78,954.21 | 14-Sep-26 | 17-Oct-26 | 23-Jul-26 | 23-Aug-26 | 78,954.21 | 78,954.21 | 1.00 |
| DAM3-C-B8-A-0120 | Block work at factory area | 5 | 58,338.72 | 14-Sep-26 | 26-Sep-26 | 23-Jul-26 | 27-Jul-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B8-A-0150 | Block work at office area | 5 | 6,179.18 | 01-Oct-26 | 08-Oct-26 | 23-Jul-26 | 23-Aug-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B8-A-170 | Block work at toilet area | 3 | 14,436.31 | 10-Oct-26 | 17-Oct-26 | 27-Jul-26 | 22-Aug-26 | 14,436.31 | 14,436.31 | 1.00 |
| **WALL FINISHES** | | 59 | 92,757.47 | 27-Oct-26 | 12-Dec-26 | 10-Sep-26 | | 0.00 | 86,132.37 | 0.00 |
| DAM3-C-B8-A-180 | Internal Wall Plaster | 10 | 48,590.16 | 27-Oct-26 | 12-Nov-26 | 10-Sep-26 | 28-Sep-26 | 0.00 | 48,590.16 | 0.00 |
| DAM3-C-B8-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 4 | 44,167.30 | 05-Dec-26 | 12-Dec-26 | 01-Oct-26 | | 0.00 | 37,542.21 | 0.00 |
| **CIELING FINISHES** | | 3 | 46,792.30 | 26-Nov-26 | 01-Dec-26 | 15-Oct-26 | 20-Oct-26 | 0.00 | 46,792.30 | 0.00 |
| DAM3-C-B8-A-240 | Installation of Ceiling Gypsum Board | 3 | 46,792.30 | 26-Nov-26 | 01-Dec-26 | 15-Oct-26 | 20-Oct-26 | 0.00 | 46,792.30 | 0.00 |
| **FLOOR FINISHES** | | 38 | 189,488.90 | 18-Nov-26 | 13-Jan-27 | 30-Sep-26 | | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B8-A-220 | Tiles for Toilet | 4 | 46,530.71 | 18-Nov-26 | 25-Nov-26 | 30-Sep-26 | 04-Oct-26 | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B8-A-250 | Tiles for Office Area | 2 | 26,867.31 | 02-Dec-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-390 | Granite strip | 2 | 671.12 | 05-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-420 | Epoxy paint | 2 | 115,419.76 | 06-Jan-27 | 13-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 9 | 248,575.06 | 15-Oct-26 | 31-Oct-26 | 27-Sep-26 | | 53,813.26 | 142,710.18 | 2.65 |
| DAM3-C-B8-A-552 | Window (CW1) | 7 | 94,173.21 | 15-Oct-26 | 22-Oct-26 | 08-Oct-26 | | 53,813.26 | 84,755.89 | 1.58 |
| DAM3-C-B8-A-553 | Roll up Shutter Door | 1 | 68,619.20 | 24-Oct-26 | 24-Oct-26 | 19-Oct-26 | | 0.00 | 51,464.40 | 0.00 |
| DAM3-C-B8-A-200 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 25-Oct-26 | 25-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 26-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 27-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 28-Oct-26 | 28-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-557 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 29-Oct-26 | 29-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 31-Oct-26 | 31-Oct-26 | 27-Sep-26 | 30-Sep-26 | 0.00 | 6,489.89 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 14-Nov-26 | 17-Nov-26 | 05-Oct-26 | 08-Oct-26 | 0.00 | 4,879.02 | 0.00 |
| DAM3-C-B8-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 14-Nov-26 | 17-Nov-26 | 05-Oct-26 | 08-Oct-26 | 0.00 | 4,879.02 | 0.00 |
| **METAL WORKS** | | 27 | 193,717.06 | 07-Dec-26 | 21-Dec-26 | 18-Jul-26 | | 0.00 | 138,371.73 | 0.00 |

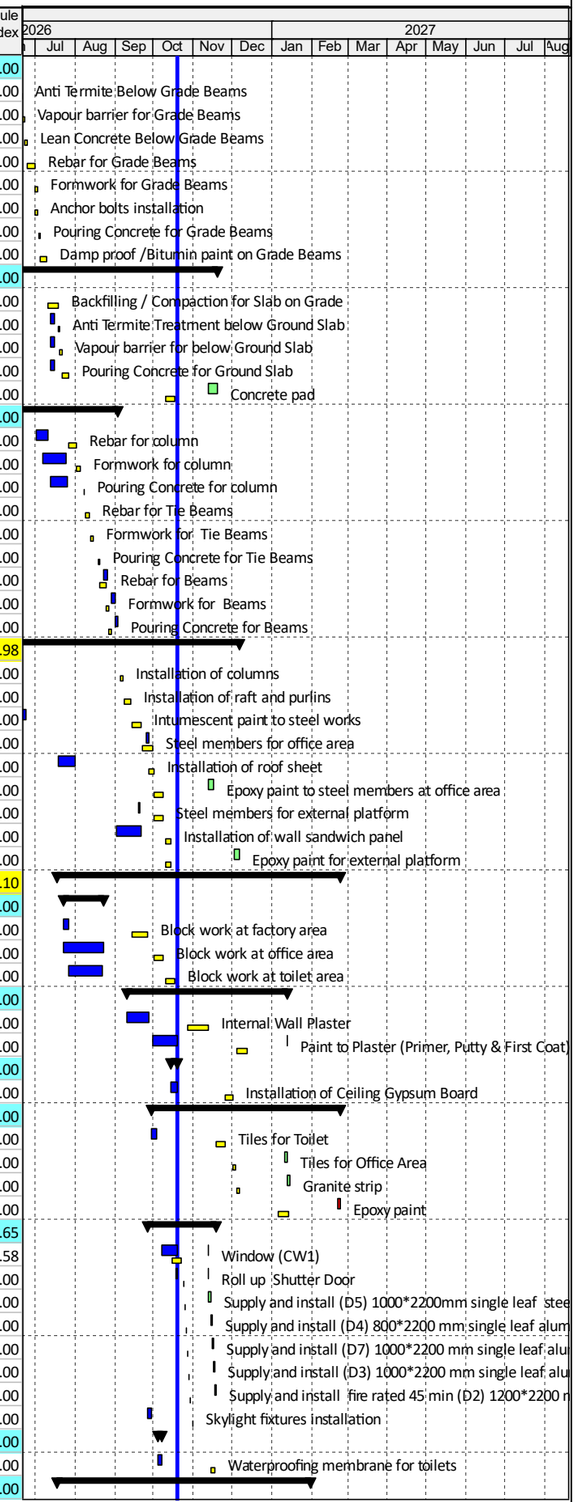




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B8-A-290 | Steel Ladder | 2 | 9,839.16 | 07-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-291 | Steel railing works | 4 | 1,533.98 | 09-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-292 | Aluminium composite panel | 3 | 175,888.76 | 14-Dec-26 | 19-Dec-26 | 06-Oct-26 | | 0.00 | 131,916.57 | 0.00 |
| DAM3-C-B8-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 20-Dec-26 | 21-Dec-26 | 18-Jul-26 | 18-Jul-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 7 | 45,080.66 | 27-Dec-26 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-320 | Installation of fittings | 3 | 22,981.27 | 27-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 02-Jan-27 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-A-340 | Furniture Installation | 1 | 12,468.83 | 05-Jan-27 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 107 | 467,522.66 | 11-Jul-26 | 05-Jan-27 | 15-Jun-26 | | 18,585.14 | 328,795.02 | 17.69 |
| **HVAC** | | 10 | 233,183.33 | 13-Dec-26 | 28-Dec-26 | 11-Oct-26 | | 0.00 | 170,694.73 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 20-Dec-26 | 23-Dec-26 | 11-Oct-26 | 15-Oct-26 | 0.00 | 170,694.73 | 0.00 |
| DAM3-C-B8-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 20-Dec-26 | 21-Dec-26 | 11-Oct-26 | 15-Oct-26 | 0.00 | 149,489.33 | 0.00 |
| DAM3-C-B8-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 22-Dec-26 | 23-Dec-26 | 11-Oct-26 | 15-Oct-26 | 0.00 | 21,205.40 | 0.00 |
| **SECOND STAGE** | | 10 | 62,488.60 | 13-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 13-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-160 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 15-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-339 | Installation of Diffuser | 2 | 2,144.00 | 24-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 27-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 21 | 102,458.78 | 13-Dec-26 | 05-Jan-27 | 12-Aug-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 11 | 84,594.16 | 13-Dec-26 | 26-Dec-26 | 12-Aug-26 | 16-Aug-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B8-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 4 | 72,394.75 | 13-Dec-26 | 20-Dec-26 | 12-Aug-26 | 16-Aug-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B8-M-310 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 21-Dec-26 | 26-Dec-26 | 15-Aug-26 | 16-Aug-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 21 | 17,864.62 | 29-Dec-26 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 29-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 03-Jan-27 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 91 | 90,009.74 | 11-Jul-26 | 20-Dec-26 | 15-Jun-26 | | 18,585.14 | 31,913.45 | 1.72 |
| **FIRST STAGE** | | 91 | 41,149.90 | 11-Jul-26 | 03-Dec-26 | 15-Jun-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B8-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 11-Jul-26 | 14-Jul-26 | 15-Jun-26 | 20-Jun-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B8-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 26-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-380 | Installation of Trench drain | 5 | 11,508.80 | 29-Nov-26 | 03-Dec-26 | 20-Jun-26 | 21-Jun-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 16 | 48,859.84 | 05-Dec-26 | 20-Dec-26 | 12-Oct-26 | | 0.00 | 1,819.51 | 0.00 |
| DAM3-C-B8-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 05-Dec-26 | 06-Dec-26 | 12-Oct-26 | 14-Oct-26 | 0.00 | 1,819.51 | 0.00 |
| DAM3-C-B8-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 07-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 12-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 14-Dec-26 | 15-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-428 | Installation of Water Tap | 2 | 2,874.14 | 16-Dec-26 | 17-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 19-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 13 | 41,870.81 | 13-Dec-26 | 24-Dec-26 | 05-Sep-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 8 | 41,592.68 | 13-Dec-26 | 19-Dec-26 | 05-Sep-26 | 09-Sep-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B8-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 13-Dec-26 | 16-Dec-26 | 05-Sep-26 | 08-Sep-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B8-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 17-Dec-26 | 19-Dec-26 | 06-Sep-26 | 09-Sep-26 | 0.00 | 18,274.27 | 0.00 |
| **SECOND STAGE** | | 3 | 278.13 | 20-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-M-330 | Capped connection | 3 | 278.13 | 20-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 61 | 752,044.76 | 18-Oct-26 | 14-Jan-27 | 19-May-26 | | 1,614.27 | 71,373.28 | 44.21 |
| **FIRST STAGE** | | 61 | 86,114.12 | 18-Oct-26 | 29-Nov-26 | 19-May-26 | | 1,614.27 | 27,642.87 | 17.12 |
| DAM3-C-B8-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 18-Oct-26 | 21-Oct-26 | 20-May-26 | | 884.15 | 884.15 | 1.00 |
| DAM3-C-B8-E-183 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 18-Oct-26 | 26-Oct-26 | 20-May-26 | | 730.11 | 1,460.23 | 2.00 |
| DAM3-C-B8-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 01-Nov-26 | 04-Nov-26 | 07-Sep-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B8-E-233 | Installation of Wires | 4 | 16,925.94 | 05-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-223 | Installation of LV Cables | 2 | 36,389.98 | 19-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-113 | Installation of Earthing and Grounding | 3 | 19,646.47 | 24-Nov-26 | 29-Nov-26 | 19-May-26 | | 0.00 | 17,681.82 | 0.00 |
| **SECOND STAGE** | | 42 | 665,930.64 | 22-Oct-26 | 14-Jan-27 | 05-Oct-26 | | 0.00 | 43,730.41 | 0.00 |
| DAM3-C-B8-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 22-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 27-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 10-Nov-26 | 14-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 10-Nov-26 | 11-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-410 | Installation of CCTV System | 3 | 76,349.24 | 10-Nov-26 | 17-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 12-Nov-26 | 14-Nov-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B8-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 15-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 17-Nov-26 | 18-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-273 | Installation of Access Control System | 3 | 27,616.86 | 18-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 24-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |

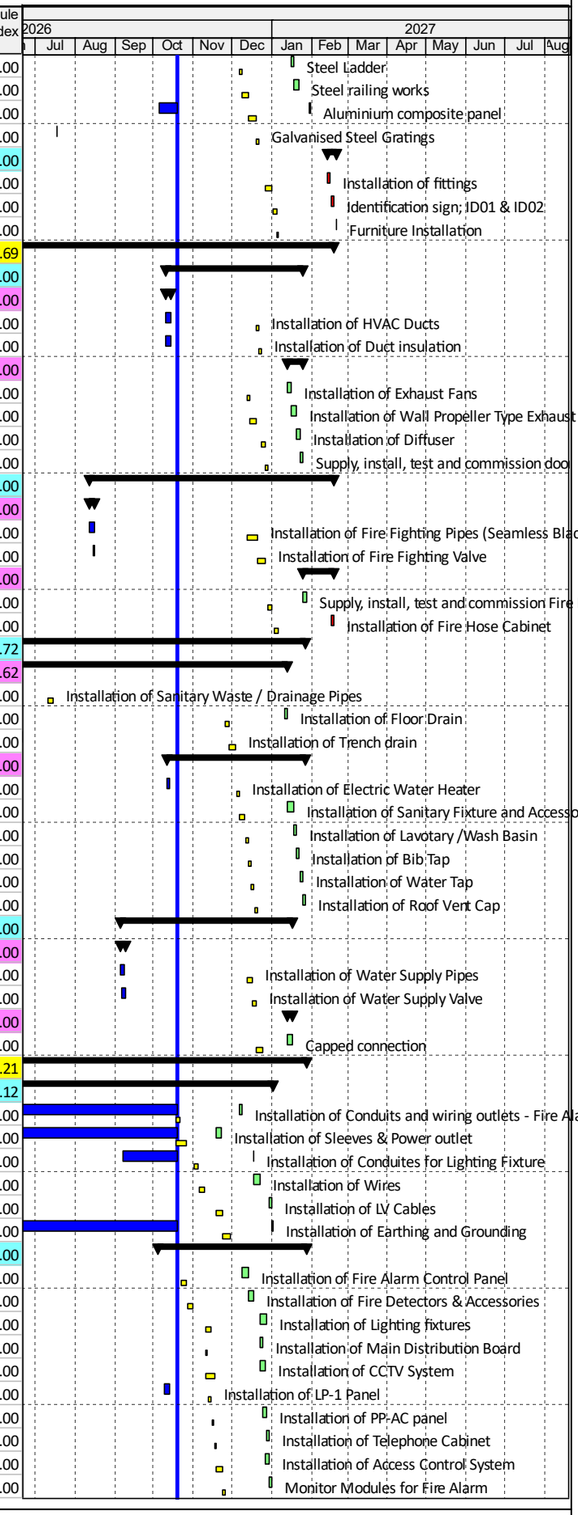




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B8-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 26-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 29-Nov-26 | 30-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-173 | Installation of Wiring Devices | 3 | 19,435.09 | 13-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 17-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B8-E-420 | Installation of Solar power plant | 7 | 253,268.71 | 07-Jan-27 | 14-Jan-27 | 05-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **BLOCK B9** | | 287 | 5,075,523.09 | 25-Feb-26 | 31-Jan-27 | 17-Feb-26 | | 3,064,511.75 | 3,804,037.02 | 1.24 |
| **STRUCTURAL** | | 210 | 1,389,042.53 | 25-Feb-26 | 20-Oct-26 | 17-Feb-26 | | 1,388,912.94 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 96 | 597,655.16 | 25-Feb-26 | 13-May-26 | 17-Feb-26 | 23-Apr-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B9-S-150 | Excavation for footings | 4 | 89,859.61 | 25-Feb-26 | 02-Mar-26 | 17-Feb-26 | 21-Feb-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B9-S-6303 | Soil replacement - rock fill | 4 | 179,061.91 | 03-Mar-26 | 07-Mar-26 | 03-Mar-26 | 07-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B9-S-6313 | Engineering fill | 4 | 46,046.19 | 08-Mar-26 | 11-Mar-26 | 09-Mar-26 | 17-Mar-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B9-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 12-Mar-26 | 12-Mar-26 | 29-Mar-26 | 29-Mar-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B9-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 14-Mar-26 | 14-Mar-26 | 29-Mar-26 | 29-Mar-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B9-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 15-Mar-26 | 16-Mar-26 | 30-Mar-26 | 30-Mar-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B9-S-104 | Rebar for Footings | 4 | 101,844.98 | 04-May-26 | 07-May-26 | 18-Apr-26 | 20-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B9-S-105 | Formwork for Footings | 4 | 25,461.25 | 09-May-26 | 12-May-26 | 19-Apr-26 | 21-Apr-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B9-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 13-May-26 | 13-May-26 | 23-Apr-26 | 23-Apr-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 14 | 120,554.54 | 14-May-26 | 04-Jun-26 | 21-Apr-26 | 14-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B9-S-257 | Rebar for column neck | 4 | 14,919.19 | 14-May-26 | 18-May-26 | 21-Apr-26 | 22-Apr-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B9-S-267 | Formwork for column neck | 2 | 9,946.13 | 19-May-26 | 20-May-26 | 22-Apr-26 | 23-Apr-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B9-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 21-May-26 | 21-May-26 | 28-Apr-26 | 28-Apr-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B9-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 23-May-26 | 24-May-26 | 02-May-26 | 02-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B9-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 25-May-26 | 04-Jun-26 | 09-May-26 | 14-May-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 41 | 171,632.86 | 06-Jun-26 | 01-Jul-26 | 18-May-26 | 07-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B9-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 06-Jun-26 | 06-Jun-26 | 18-May-26 | 18-May-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B9-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 07-Jun-26 | 08-Jun-26 | 18-May-26 | 18-May-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B9-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 09-Jun-26 | 10-Jun-26 | 18-May-26 | 18-May-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B9-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 17-Jun-26 | 22-Jun-26 | 20-May-26 | 21-May-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B9-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 23-Jun-26 | 24-Jun-26 | 21-May-26 | 24-May-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B9-S-341 | Anchor bolts installation | 2 | 57,238.83 | 23-Jun-26 | 24-Jun-26 | 20-May-26 | 23-May-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B9-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 25-Jun-26 | 25-Jun-26 | 25-May-26 | 25-May-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B9-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 27-Jun-26 | 01-Jul-26 | 02-Jun-26 | 07-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 81 | 397,232.98 | 15-Jul-26 | 20-Oct-26 | 09-Jun-26 | | 397,103.40 | 396,325.87 | 1.00 |
| DAM3-C-B9-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 15-Jul-26 | 22-Jul-26 | 09-Jun-26 | 13-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B9-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 23-Jul-26 | 23-Jul-26 | 22-Jul-26 | 25-Jul-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B9-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 25-Jul-26 | 26-Jul-26 | 22-Jul-26 | 25-Jul-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B9-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 27-Jul-26 | 30-Jul-26 | 22-Jul-26 | 25-Jul-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B9-S-517 | Concrete pad | 7 | 907.11 | 13-Oct-26 | 20-Oct-26 | | | 777.53 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 74 | 101,966.98 | 23-Jul-26 | 19-Aug-26 | 21-May-26 | 12-Sep-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B9-S-5101 | Rebar for column | 5 | 20,144.05 | 23-Jul-26 | 28-Jul-26 | 11-Jul-26 | 14-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B9-S-5102 | Formwork for column | 4 | 5,036.01 | 29-Jul-26 | 02-Aug-26 | 14-Jul-26 | 28-Jul-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B9-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 03-Aug-26 | 03-Aug-26 | 15-Jul-26 | 29-Jul-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B9-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 04-Aug-26 | 08-Aug-26 | 21-May-26 | 07-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B9-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 09-Aug-26 | 10-Aug-26 | 23-May-26 | 08-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B9-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 11-Aug-26 | 11-Aug-26 | 25-May-26 | 09-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B9-S-6113 | Rebar for Beams | 4 | 13,379.11 | 12-Aug-26 | 16-Aug-26 | 23-Aug-26 | 26-Aug-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B9-S-6123 | Formwork for Beams | 2 | 3,344.77 | 17-Aug-26 | 18-Aug-26 | 01-Sep-26 | 05-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B9-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 19-Aug-26 | 19-Aug-26 | 08-Sep-26 | 12-Sep-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 48 | 1,566,668.48 | 08-Sep-26 | 18-Oct-26 | 16-Jun-26 | | 1,566,668.48 | 1,539,773.29 | 0.98 |
| DAM3-C-B9-SS-0100 | Installation of columns | 3 | 217,507.55 | 08-Sep-26 | 10-Sep-26 | 16-Jun-26 | 17-Jun-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B9-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 12-Sep-26 | 16-Sep-26 | 18-Jun-26 | 22-Jun-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B9-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 17-Sep-26 | 26-Sep-26 | 05-Jul-26 | 07-Jul-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B9-SS-620 | Steel members for office area | 2 | 115,805.20 | 27-Sep-26 | 04-Oct-26 | 27-Sep-26 | 29-Sep-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B9-SS-0140 | Installation of roof sheet | 5 | 217,507.55 | 30-Sep-26 | 05-Oct-26 | 22-Jul-26 | 01-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B9-SS-1020 | Epoxy paint to steel members at office area | 7 | 23,161.04 | 05-Oct-26 | 12-Oct-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B9-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 05-Oct-26 | 12-Oct-26 | 21-Sep-26 | 26-Sep-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B9-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 13-Oct-26 | 18-Oct-26 | 03-Sep-26 | 05-Oct-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B9-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 13-Oct-26 | 18-Oct-26 | | | 3,734.16 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 88 | 900,244.66 | 17-Sep-26 | 12-Jan-27 | 27-Jul-26 | | 90,345.19 | 475,960.02 | 5.27 |
| **MASONARY WORKS** | | 19 | 78,954.21 | 17-Sep-26 | 20-Oct-26 | 28-Jul-26 | 29-Aug-26 | 76,891.88 | 78,954.21 | 1.03 |
| DAM3-C-B9-A-0120 | Block work at factory area | 10 | 58,338.72 | 17-Sep-26 | 29-Sep-26 | 28-Jul-26 | 30-Jul-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B9-A-0150 | Block work at office area | 5 | 6,179.18 | 05-Oct-26 | 12-Oct-26 | 30-Jul-26 | 27-Aug-26 | 6,179.18 | 6,179.18 | 1.00 |

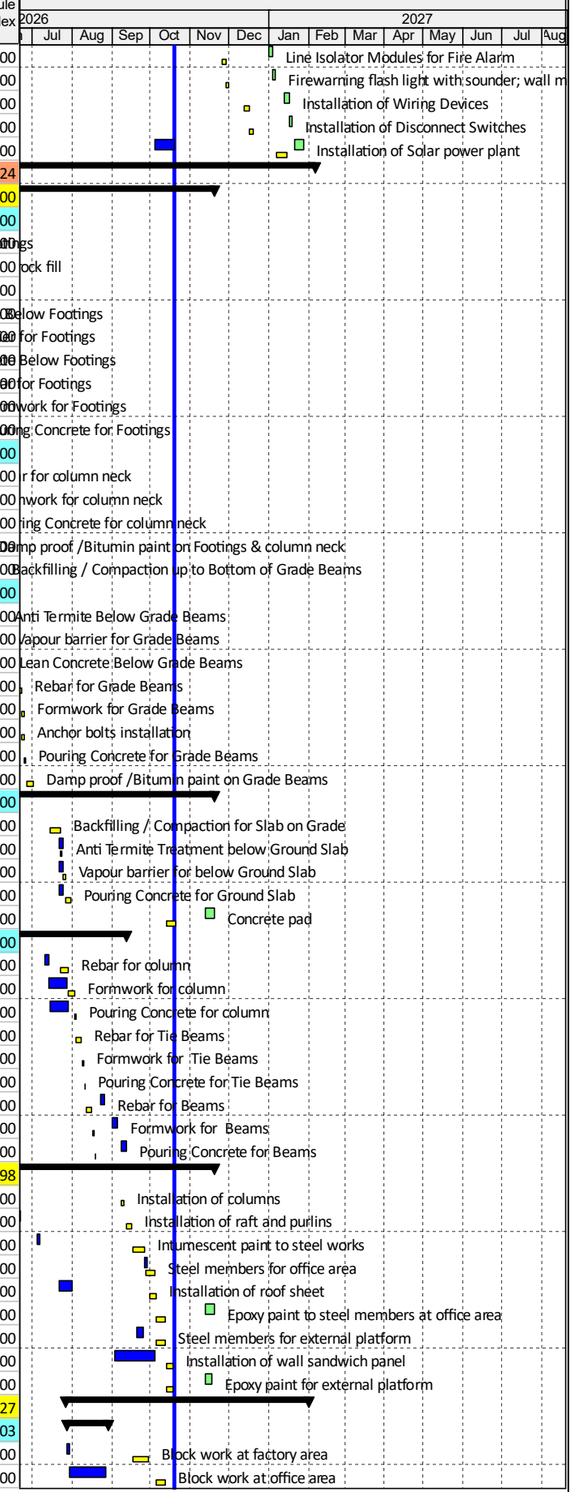




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B9-A-170 | Block work at toilet area | 5 | 14,436.31 | 13-Oct-26 | 20-Oct-26 | 02-Aug-26 | 29-Aug-26 | 12,373.98 | 14,436.31 | 1.17 |
| **WALL FINISHES** | | 27 | 92,757.47 | 31-Oct-26 | 15-Dec-26 | 17-Sep-26 | | 0.00 | 86,132.37 | 0.00 |
| DAM3-C-B9-A-180 | Internal Wall Plaster | 5 | 48,590.16 | 31-Oct-26 | 16-Nov-26 | 17-Sep-26 | 05-Oct-26 | 0.00 | 48,590.16 | 0.00 |
| DAM3-C-B9-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 4 | 44,167.30 | 08-Dec-26 | 15-Dec-26 | 03-Oct-26 | | 0.00 | 37,542.21 | 0.00 |
| **CIELING FINISHES** | | 3 | 46,792.30 | 30-Nov-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-240 | Installation of Ceiling Gypsum Board | 3 | 46,792.30 | 30-Nov-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 56 | 189,488.90 | 22-Nov-26 | 12-Jan-27 | 01-Oct-26 | | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B9-A-220 | Tiles for Toilet | 4 | 46,530.71 | 22-Nov-26 | 29-Nov-26 | 01-Oct-26 | 07-Oct-26 | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B9-A-250 | Tiles for Office Area | 2 | 26,867.31 | 06-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-390 | Granite strip | 2 | 671.12 | 08-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-420 | Epoxy paint | 4 | 115,419.76 | 05-Jan-27 | 12-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 18 | 248,575.06 | 19-Oct-26 | 03-Nov-26 | 30-Sep-26 | | 13,453.32 | 77,119.80 | 5.73 |
| DAM3-C-B9-A-552 | Window (CW1) | 7 | 94,173.21 | 19-Oct-26 | 26-Oct-26 | 10-Oct-26 | | 13,453.32 | 70,629.91 | 5.25 |
| DAM3-C-B9-A-553 | Roll up Shutter Door | 1 | 68,619.20 | 27-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-200 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 28-Oct-26 | 28-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 29-Oct-26 | 29-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 31-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 01-Nov-26 | 01-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-557 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 02-Nov-26 | 02-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 03-Nov-26 | 03-Nov-26 | 30-Sep-26 | 04-Oct-26 | 0.00 | 6,489.89 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 17-Nov-26 | 21-Nov-26 | 10-Oct-26 | 13-Oct-26 | 0.00 | 4,879.02 | 0.00 |
| DAM3-C-B9-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 17-Nov-26 | 21-Nov-26 | 10-Oct-26 | 13-Oct-26 | 0.00 | 4,879.02 | 0.00 |
| **METAL WORKS** | | 65 | 193,717.06 | 10-Dec-26 | 24-Dec-26 | 27-Jul-26 | | 0.00 | 182,343.92 | 0.00 |
| DAM3-C-B9-A-290 | Steel Ladder | 2 | 9,839.16 | 10-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-291 | Steel railing works | 3 | 1,533.98 | 13-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-292 | Aluminium composite panel | 3 | 175,888.76 | 17-Dec-26 | 22-Dec-26 | 29-Sep-26 | | 0.00 | 175,888.76 | 0.00 |
| DAM3-C-B9-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 23-Dec-26 | 24-Dec-26 | 27-Jul-26 | 27-Jul-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 7 | 45,080.66 | 26-Dec-26 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-320 | Installation of fittings | 3 | 22,981.27 | 26-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 31-Dec-26 | 03-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-A-340 | Furniture Installation | 1 | 12,468.83 | 04-Jan-27 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 158 | 467,522.66 | 02-Jul-26 | 04-Jan-27 | 21-Jun-26 | | 18,585.14 | 328,795.02 | 17.69 |
| **HVAC** | | 11 | 233,183.33 | 16-Dec-26 | 31-Dec-26 | 15-Oct-26 | | 0.00 | 170,694.73 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 23-Dec-26 | 27-Dec-26 | 15-Oct-26 | 18-Oct-26 | 0.00 | 170,694.73 | 0.00 |
| DAM3-C-B9-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 23-Dec-26 | 24-Dec-26 | 15-Oct-26 | 18-Oct-26 | 0.00 | 149,489.33 | 0.00 |
| DAM3-C-B9-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 26-Dec-26 | 27-Dec-26 | 15-Oct-26 | 18-Oct-26 | 0.00 | 21,205.40 | 0.00 |
| **SECOND STAGE** | | 10 | 62,488.60 | 16-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 16-Dec-26 | 17-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-160 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 19-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-339 | Installation of Diffuser | 2 | 2,144.00 | 28-Dec-26 | 29-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 30-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 18 | 102,458.78 | 16-Dec-26 | 04-Jan-27 | 17-Aug-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 10 | 84,594.16 | 16-Dec-26 | 29-Dec-26 | 17-Aug-26 | 23-Aug-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B9-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 5 | 72,394.75 | 16-Dec-26 | 23-Dec-26 | 17-Aug-26 | 22-Aug-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B9-M-310 | Installation of Fire Fighting Valve | 5 | 12,199.40 | 24-Dec-26 | 29-Dec-26 | 17-Aug-26 | 23-Aug-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 13 | 17,864.62 | 30-Dec-26 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 30-Dec-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 02-Jan-27 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 158 | 90,009.74 | 02-Jul-26 | 23-Dec-26 | 21-Jun-26 | | 18,585.14 | 31,913.45 | 1.72 |
| **FIRST STAGE** | | 158 | 41,149.90 | 02-Jul-26 | 07-Dec-26 | 21-Jun-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B9-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 02-Jul-26 | 06-Jul-26 | 21-Jun-26 | 24-Jun-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B9-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 30-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-380 | Installation of Trench drain | 5 | 11,508.80 | 02-Dec-26 | 07-Dec-26 | 22-Jun-26 | 24-Jun-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 12 | 48,859.84 | 08-Dec-26 | 23-Dec-26 | 18-Oct-26 | | 0.00 | 1,819.51 | 0.00 |
| DAM3-C-B9-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 08-Dec-26 | 09-Dec-26 | 18-Oct-26 | 19-Oct-26 | 0.00 | 1,819.51 | 0.00 |
| DAM3-C-B9-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 10-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 15-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 17-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-428 | Installation of Water Tap | 2 | 2,874.14 | 20-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 22-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 12 | 41,870.81 | 16-Dec-26 | 28-Dec-26 | 14-Sep-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 4 | 41,592.68 | 16-Dec-26 | 22-Dec-26 | 14-Sep-26 | 19-Sep-26 | 0.00 | 41,592.68 | 0.00 |

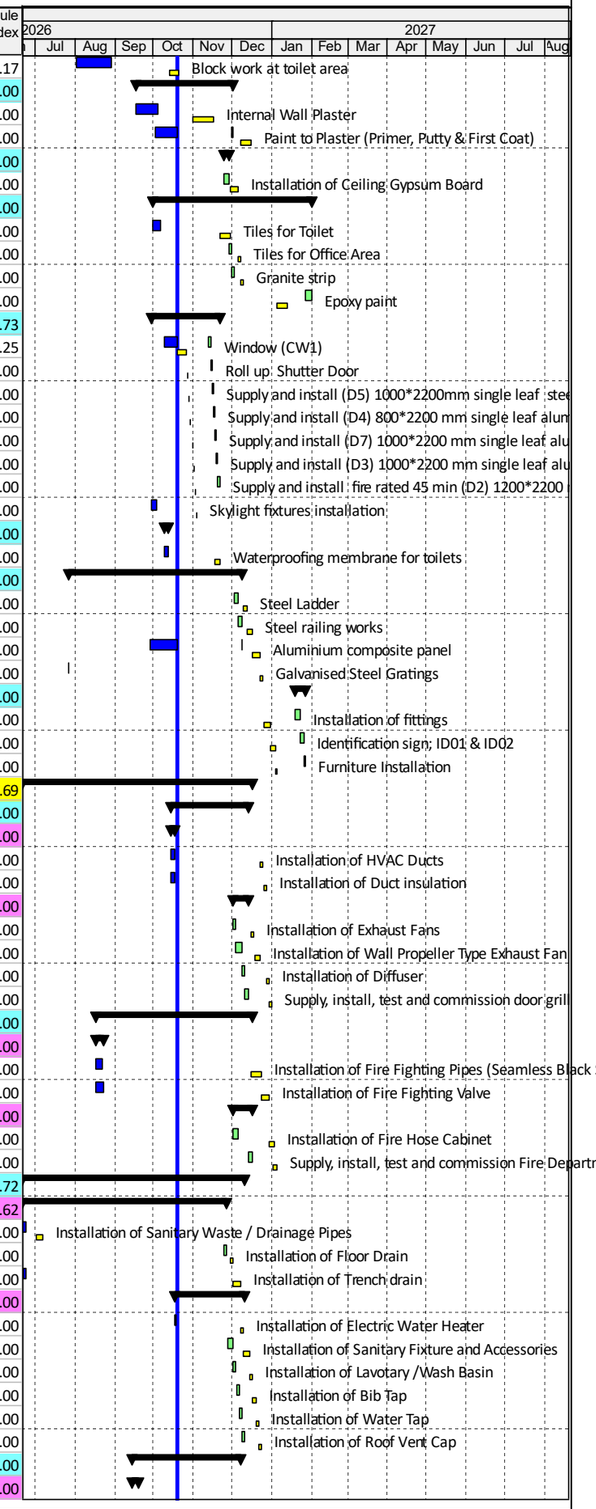




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B9-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 16-Dec-26 | 20-Dec-26 | 14-Sep-26 | 19-Sep-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B9-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 21-Dec-26 | 22-Dec-26 | 15-Sep-26 | 19-Sep-26 | 0.00 | 18,274.27 | 0.00 |
| SECOND STAGE | | 5 | 278.13 | 23-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-M-330 | Capped connection | 5 | 278.13 | 23-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| ELECTRICAL | | 77 | 752,044.76 | 21-Oct-26 | 31-Jan-27 | 20-May-26 | | 0.00 | 71,373.28 | 0.00 |
| FIRST STAGE | | 77 | 86,114.12 | 21-Oct-26 | 02-Dec-26 | 20-May-26 | | 0.00 | 27,642.87 | 0.00 |
| DAM3-C-B9-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 21-Oct-26 | 25-Oct-26 | 21-May-26 | | 0.00 | 884.15 | 0.00 |
| DAM3-C-B9-E-183 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 21-Oct-26 | 29-Oct-26 | 21-May-26 | | 0.00 | 1,460.23 | 0.00 |
| DAM3-C-B9-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 04-Nov-26 | 08-Nov-26 | 08-Sep-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B9-E-233 | Installation of Wires | 4 | 16,925.94 | 09-Nov-26 | 12-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-223 | Installation of LV Cables | 4 | 36,389.98 | 23-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-113 | Installation of Earthing and Grounding | 3 | 19,646.47 | 28-Nov-26 | 02-Dec-26 | 20-May-26 | | 0.00 | 17,681.82 | 0.00 |
| SECOND STAGE | | 64 | 665,930.64 | 26-Oct-26 | 31-Jan-27 | 06-Oct-26 | | 0.00 | 43,730.41 | 0.00 |
| DAM3-C-B9-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 26-Oct-26 | 29-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 31-Oct-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 14-Nov-26 | 17-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 14-Nov-26 | 15-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-410 | Installation of CCTV System | 5 | 76,349.24 | 14-Nov-26 | 21-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 16-Nov-26 | 17-Nov-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B9-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 18-Nov-26 | 19-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 21-Nov-26 | 22-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-273 | Installation of Access Control System | 5 | 27,616.86 | 22-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 28-Nov-26 | 29-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 30-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 02-Dec-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-173 | Installation of Wiring Devices | 4 | 19,435.09 | 16-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 21-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B9-E-420 | Installation of Solar power plant | 8 | 253,268.71 | 16-Jan-27 | 31-Jan-27 | 06-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| BLOCK B10 | | 293 | 5,075,523.09 | 03-Mar-26 | 08-Feb-27 | 18-Feb-26 | | 2,912,484.49 | 3,639,038.61 | 1.25 |
| STRUCTURAL | | 208 | 1,389,042.53 | 03-Mar-26 | 24-Oct-26 | 18-Feb-26 | | 1,388,524.18 | 1,388,135.41 | 1.00 |
| FOOTING | | 55 | 597,655.16 | 03-Mar-26 | 04-Apr-26 | 18-Feb-26 | 28-Apr-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B10-S-150 | Excavation for footings | 4 | 89,859.61 | 03-Mar-26 | 07-Mar-26 | 18-Feb-26 | 03-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B10-S-6323 | Soil replacement - rock fill | 4 | 179,061.91 | 08-Mar-26 | 11-Mar-26 | 07-Mar-26 | 11-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B10-S-6333 | Engineering fill | 4 | 46,046.19 | 12-Mar-26 | 16-Mar-26 | 18-Mar-26 | 31-Mar-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B10-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 21-Mar-26 | 21-Mar-26 | 01-Apr-26 | 01-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B10-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 22-Mar-26 | 22-Mar-26 | 01-Apr-26 | 01-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B10-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 23-Mar-26 | 24-Mar-26 | 01-Apr-26 | 01-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B10-S-104 | Rebar for Footings | 4 | 101,844.98 | 25-Mar-26 | 29-Mar-26 | 23-Apr-26 | 23-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B10-S-105 | Formwork for Footings | 4 | 25,461.25 | 30-Mar-26 | 02-Apr-26 | 23-Apr-26 | 25-Apr-26 | 25,461.25 | 25,461.25 | 1.00 |
| DAM3-C-B10-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 04-Apr-26 | 04-Apr-26 | 28-Apr-26 | 28-Apr-26 | 127,306.23 | 127,306.23 | 1.00 |
| COLUMN NECK | | 17 | 120,554.54 | 05-Apr-26 | 22-Apr-26 | 26-Apr-26 | 20-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B10-S-257 | Rebar for column neck | 4 | 14,919.19 | 05-Apr-26 | 08-Apr-26 | 26-Apr-26 | 27-Apr-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B10-S-267 | Formwork for column neck | 2 | 9,946.13 | 09-Apr-26 | 11-Apr-26 | 27-Apr-26 | 04-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B10-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 12-Apr-26 | 12-Apr-26 | 02-May-26 | 05-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B10-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 13-Apr-26 | 14-Apr-26 | 05-May-26 | 09-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B10-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 15-Apr-26 | 22-Apr-26 | 13-May-26 | 20-May-26 | 46,046.19 | 46,046.19 | 1.00 |
| GRADE BEAM | | 16 | 171,632.86 | 23-Apr-26 | 13-May-26 | 25-May-26 | 15-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B10-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 23-Apr-26 | 23-Apr-26 | 25-May-26 | 25-May-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B10-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 25-Apr-26 | 26-Apr-26 | 25-May-26 | 25-May-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B10-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 27-Apr-26 | 28-Apr-26 | 25-May-26 | 25-May-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B10-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 29-Apr-26 | 04-May-26 | 31-May-26 | 03-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B10-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 05-May-26 | 06-May-26 | 07-Jun-26 | 09-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B10-S-341 | Anchor bolts installation | 2 | 57,238.83 | 05-May-26 | 06-May-26 | 02-Jun-26 | 03-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B10-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 07-May-26 | 07-May-26 | 09-Jun-26 | 09-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B10-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 09-May-26 | 13-May-26 | 14-Jun-26 | 15-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| SLAB ON GRADE | | 121 | 397,232.98 | 14-May-26 | 24-Oct-26 | 16-Jun-26 | | 396,714.63 | 396,325.87 | 1.00 |
| DAM3-C-B10-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 14-May-26 | 21-May-26 | 16-Jun-26 | 22-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B10-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 23-May-26 | 23-May-26 | 18-Jul-26 | 21-Jul-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B10-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 24-May-26 | 25-May-26 | 18-Jul-26 | 21-Jul-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B10-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 30-May-26 | 02-Jun-26 | 18-Jul-26 | 21-Jul-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B10-S-517 | Concrete pad | 7 | 907.11 | 17-Oct-26 | 24-Oct-26 | | | 388.76 | 0.00 | 0.00 |
| COLUMNS & BEAMS | | 55 | 101,966.98 | 23-May-26 | 22-Jun-26 | 01-Jun-26 | 16-Sep-26 | 101,966.98 | 101,966.98 | 1.00 |

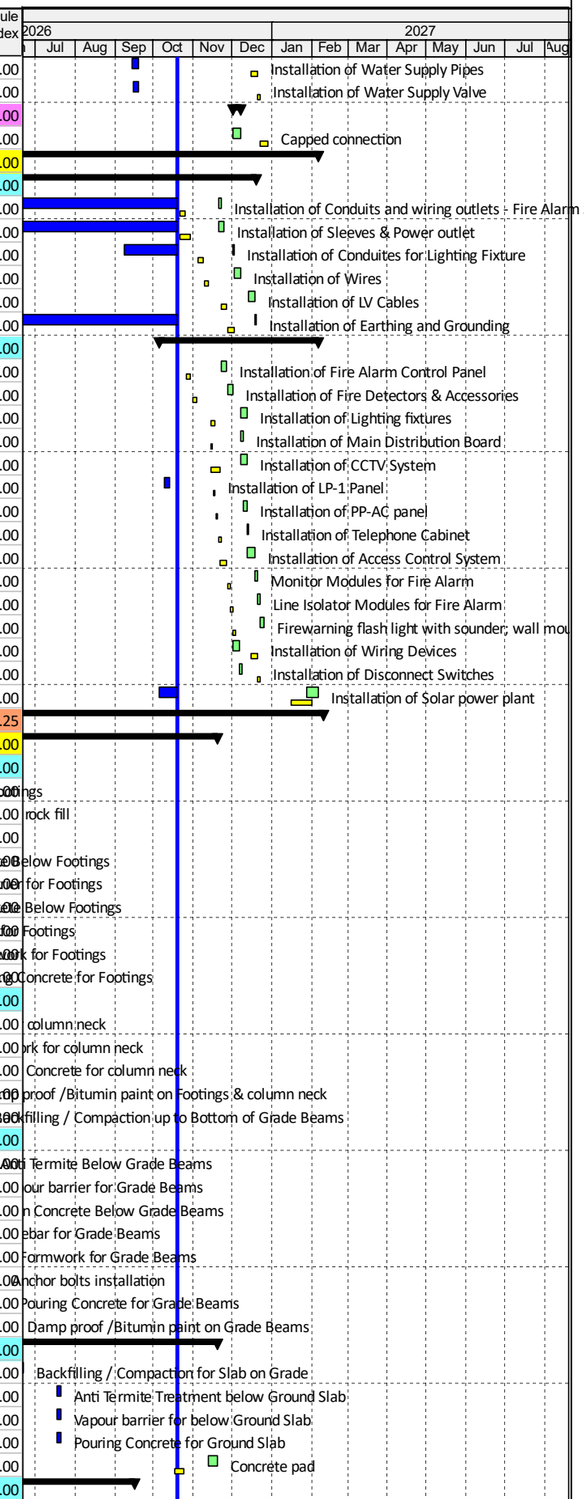




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B10-S-5101 | Rebar for column | 5 | 20,144.05 | 23-May-26 | 31-May-26 | 12-Jul-26 | 16-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B10-S-5102 | Formwork for column | 4 | 5,036.01 | 01-Jun-26 | 04-Jun-26 | 04-Aug-26 | 06-Aug-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B10-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 06-Jun-26 | 06-Jun-26 | 05-Aug-26 | 09-Aug-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B10-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 07-Jun-26 | 10-Jun-26 | 01-Jun-26 | 03-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B10-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 11-Jun-26 | 13-Jun-26 | 07-Jun-26 | 08-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B10-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 14-Jun-26 | 14-Jun-26 | 09-Jun-26 | 09-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B10-S-6113 | Rebar for Beams | 4 | 13,379.11 | 15-Jun-26 | 18-Jun-26 | 31-Aug-26 | 02-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B10-S-6123 | Formwork for Beams | 2 | 3,344.77 | 20-Jun-26 | 21-Jun-26 | 08-Sep-26 | 15-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B10-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 22-Jun-26 | 22-Jun-26 | 12-Sep-26 | 16-Sep-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 48 | 1,566,668.48 | 12-Sep-26 | 21-Oct-26 | 25-Jun-26 | | 1,434,670.29 | 1,539,773.29 | 1.07 |
| DAM3-C-B10-SS-0100 | Installation of columns | 3 | 217,507.55 | 12-Sep-26 | 14-Sep-26 | 25-Jun-26 | 25-Jun-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B10-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 15-Sep-26 | 20-Sep-26 | 25-Jun-26 | 28-Jun-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B10-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 21-Sep-26 | 29-Sep-26 | 07-Jul-26 | 11-Aug-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B10-SS-620 | Steel members for office area | 4 | 115,805.20 | 30-Sep-26 | 07-Oct-26 | 29-Sep-26 | 30-Sep-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B10-SS-0140 | Installation of roof sheet | 3 | 217,507.55 | 04-Oct-26 | 08-Oct-26 | 13-Aug-26 | 16-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B10-SS-1020 | Epoxy paint to steel members at office area | 4 | 23,161.04 | 08-Oct-26 | 15-Oct-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B10-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 08-Oct-26 | 15-Oct-26 | 26-Sep-26 | 06-Oct-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B10-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 17-Oct-26 | 21-Oct-26 | 03-Sep-26 | 30-Sep-26 | 195,756.79 | 326,261.32 | 1.67 |
| DAM3-C-B10-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 17-Oct-26 | 21-Oct-26 | | | 2,240.49 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 85 | 900,244.66 | 21-Sep-26 | 16-Jan-27 | 23-Jul-26 | | 70,704.89 | 312,781.12 | 4.42 |
| **MASONARY WORKS** | | 20 | 78,954.21 | 21-Sep-26 | 24-Oct-26 | 02-Aug-26 | 03-Sep-26 | 70,704.89 | 78,954.21 | 1.12 |
| DAM3-C-B10-A-0120 | Block work at factory area | 3 | 58,338.72 | 21-Sep-26 | 03-Oct-26 | 02-Aug-26 | 23-Aug-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B10-A-0150 | Block work at office area | 4 | 6,179.18 | 08-Oct-26 | 15-Oct-26 | 08-Aug-26 | 01-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B10-A-170 | Block work at toilet area | 5 | 14,436.31 | 17-Oct-26 | 24-Oct-26 | 11-Aug-26 | 03-Sep-26 | 6,186.99 | 14,436.31 | 2.33 |
| **WALL FINISHES** | | 31 | 92,757.47 | 03-Nov-26 | 19-Dec-26 | 21-Sep-26 | | 0.00 | 86,132.37 | 0.00 |
| DAM3-C-B10-A-180 | Internal Wall Plaster | 5 | 48,590.16 | 03-Nov-26 | 19-Nov-26 | 21-Sep-26 | 12-Oct-26 | 0.00 | 48,590.16 | 0.00 |
| DAM3-C-B10-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 5 | 44,167.30 | 12-Dec-26 | 19-Dec-26 | 08-Oct-26 | | 0.00 | 37,542.21 | 0.00 |
| **CIELING FINISHES** | | 4 | 46,792.30 | 03-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-240 | Installation of Ceiling Gypsum Board | 4 | 46,792.30 | 03-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 22 | 189,488.90 | 25-Nov-26 | 16-Jan-27 | 11-Oct-26 | | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B10-A-220 | Tiles for Toilet | 5 | 46,530.71 | 25-Nov-26 | 02-Dec-26 | 11-Oct-26 | 18-Oct-26 | 0.00 | 46,530.71 | 0.00 |
| DAM3-C-B10-A-250 | Tiles for Office Area | 2 | 26,867.31 | 09-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-390 | Granite strip | 2 | 671.12 | 12-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-420 | Epoxy paint | 3 | 115,419.76 | 09-Jan-27 | 16-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 19 | 248,575.06 | 22-Oct-26 | 07-Nov-26 | 04-Oct-26 | | 0.00 | 77,119.80 | 0.00 |
| DAM3-C-B10-A-552 | Window (CW1) | 7 | 94,173.21 | 22-Oct-26 | 29-Oct-26 | 14-Oct-26 | | 0.00 | 70,629.91 | 0.00 |
| DAM3-C-B10-A-553 | Roll up Shutter Door | 1 | 68,619.20 | 31-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-200 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 01-Nov-26 | 01-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 02-Nov-26 | 02-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 03-Nov-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 04-Nov-26 | 04-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-557 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 05-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 07-Nov-26 | 07-Nov-26 | 04-Oct-26 | 06-Oct-26 | 0.00 | 6,489.89 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 21-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 21-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **METAL WORKS** | | 65 | 193,717.06 | 14-Dec-26 | 28-Dec-26 | 23-Jul-26 | | 0.00 | 24,044.04 | 0.00 |
| DAM3-C-B10-A-290 | Steel Ladder | 2 | 9,839.16 | 14-Dec-26 | 15-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-291 | Steel railing works | 3 | 1,533.98 | 16-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-292 | Aluminium composite panel | 3 | 175,888.76 | 21-Dec-26 | 26-Dec-26 | 14-Oct-26 | | 0.00 | 17,588.88 | 0.00 |
| DAM3-C-B10-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 27-Dec-26 | 28-Dec-26 | 23-Jul-26 | 23-Jul-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 7 | 45,080.66 | 29-Dec-26 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-320 | Installation of fittings | 3 | 22,981.27 | 29-Dec-26 | 03-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 04-Jan-27 | 06-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-A-340 | Furniture Installation | 1 | 12,468.83 | 07-Jan-27 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 168 | 467,522.66 | 14-May-26 | 07-Jan-27 | 01-Jul-26 | | 18,585.14 | 326,975.51 | 17.59 |
| **HVAC** | | 10 | 233,183.33 | 20-Dec-26 | 04-Jan-27 | 18-Oct-26 | | 0.00 | 170,694.73 | 0.00 |
| **FIRST STAGE** | | 2 | 170,694.73 | 27-Dec-26 | 30-Dec-26 | 18-Oct-26 | 20-Oct-26 | 0.00 | 170,694.73 | 0.00 |
| DAM3-C-B10-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 27-Dec-26 | 28-Dec-26 | 18-Oct-26 | 20-Oct-26 | 0.00 | 149,489.33 | 0.00 |
| DAM3-C-B10-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 29-Dec-26 | 30-Dec-26 | 18-Oct-26 | 20-Oct-26 | 0.00 | 21,205.40 | 0.00 |
| **SECOND STAGE** | | 10 | 62,488.60 | 20-Dec-26 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 20-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-160 | Installation of Wall Propeller Type Exhaust Fan | 4 | 46,831.64 | 22-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |

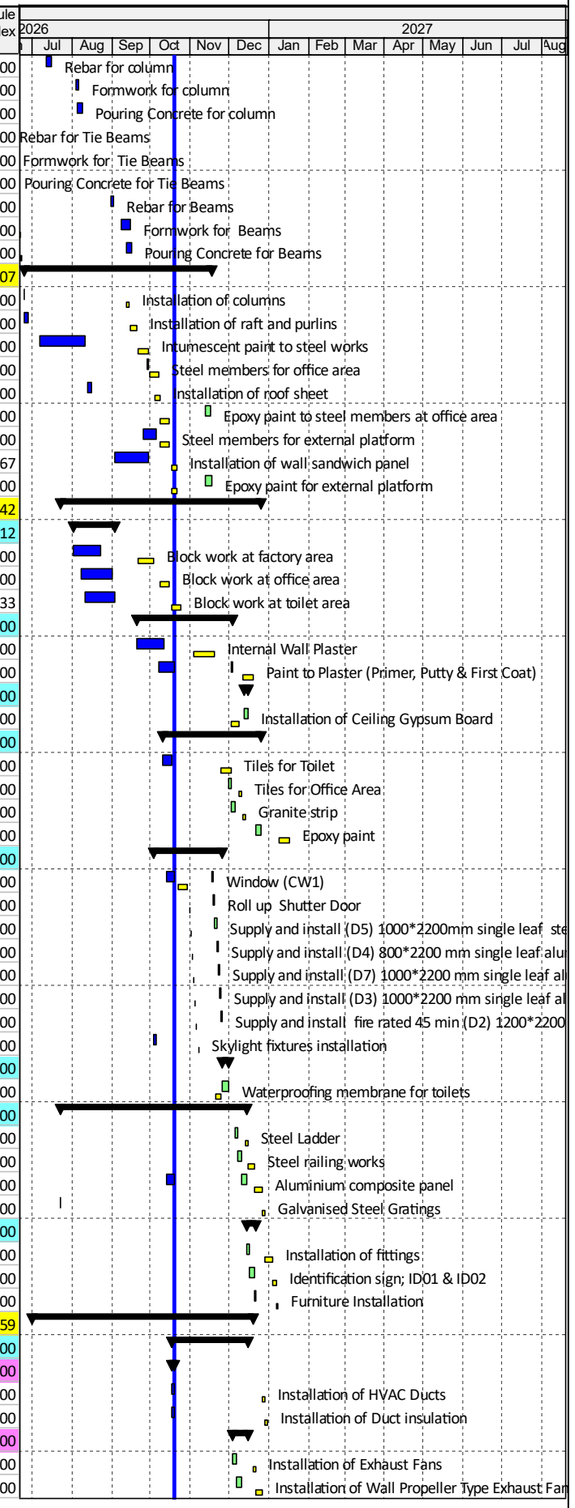




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B10-M-339 | Installation of Diffuser | 2 | 2,144.00 | 31-Dec-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 03-Jan-27 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 19 | 102,458.78 | 20-Dec-26 | 07-Jan-27 | 23-Aug-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 8 | 84,594.16 | 20-Dec-26 | 02-Jan-27 | 23-Aug-26 | 29-Aug-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B10-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 7 | 72,394.75 | 20-Dec-26 | 27-Dec-26 | 23-Aug-26 | 27-Aug-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B10-M-310 | Installation of Fire Fighting Valve | 3 | 12,199.40 | 28-Dec-26 | 02-Jan-27 | 25-Aug-26 | 29-Aug-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 13 | 17,864.62 | 03-Jan-27 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 03-Jan-27 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 05-Jan-27 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 168 | 90,009.74 | 14-May-26 | 27-Dec-26 | 01-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| **FIRST STAGE** | | 168 | 41,149.90 | 14-May-26 | 10-Dec-26 | 01-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B10-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 14-May-26 | 18-May-26 | 01-Jul-26 | 06-Jul-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B10-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 03-Dec-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-380 | Installation of Trench drain | 5 | 11,508.80 | 06-Dec-26 | 10-Dec-26 | 07-Jul-26 | 09-Jul-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 12-Dec-26 | 27-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 12-Dec-26 | 13-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 14-Dec-26 | 17-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 19-Dec-26 | 20-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 21-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-428 | Installation of Water Tap | 2 | 2,874.14 | 23-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 26-Dec-26 | 27-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 18 | 41,870.81 | 20-Dec-26 | 31-Dec-26 | 17-Sep-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 6 | 41,592.68 | 20-Dec-26 | 26-Dec-26 | 17-Sep-26 | 21-Sep-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B10-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 20-Dec-26 | 23-Dec-26 | 17-Sep-26 | 21-Sep-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B10-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 24-Dec-26 | 26-Dec-26 | 17-Sep-26 | 21-Sep-26 | 0.00 | 18,274.27 | 0.00 |
| **SECOND STAGE** | | 5 | 278.13 | 27-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-M-330 | Capped connection | 5 | 278.13 | 27-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 90 | 752,044.76 | 25-Oct-26 | 08-Feb-27 | 02-Jun-26 | | 0.00 | 71,373.28 | 0.00 |
| **FIRST STAGE** | | 82 | 86,114.12 | 25-Oct-26 | 06-Dec-26 | 02-Jun-26 | | 0.00 | 27,642.87 | 0.00 |
| DAM3-C-B10-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 25-Oct-26 | 28-Oct-26 | 03-Jun-26 | | 0.00 | 884.15 | 0.00 |
| DAM3-C-B10-E-183 | Installation of Sleeves & Power outlet | 4 | 2,920.45 | 25-Oct-26 | 02-Nov-26 | 03-Jun-26 | | 0.00 | 1,460.23 | 0.00 |
| DAM3-C-B10-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 08-Nov-26 | 11-Nov-26 | 21-Sep-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B10-E-233 | Installation of Wires | 4 | 16,925.94 | 12-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-223 | Installation of LV Cables | 4 | 36,389.98 | 26-Nov-26 | 30-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-113 | Installation of Earthing and Grounding | 5 | 19,646.47 | 01-Dec-26 | 06-Dec-26 | 02-Jun-26 | | 0.00 | 17,681.82 | 0.00 |
| **SECOND STAGE** | | 76 | 665,930.64 | 29-Oct-26 | 08-Feb-27 | 07-Oct-26 | | 0.00 | 43,730.41 | 0.00 |
| DAM3-C-B10-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 29-Oct-26 | 02-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 03-Nov-26 | 07-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 17-Nov-26 | 21-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 17-Nov-26 | 18-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-410 | Installation of CCTV System | 7 | 76,349.24 | 17-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 19-Nov-26 | 21-Nov-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B10-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 22-Nov-26 | 23-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 24-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-273 | Installation of Access Control System | 5 | 27,616.86 | 25-Nov-26 | 30-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 01-Dec-26 | 02-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 03-Dec-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 06-Dec-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-173 | Installation of Wiring Devices | 4 | 19,435.09 | 20-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 24-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B10-E-420 | Installation of Solar power plant | 5 | 253,268.71 | 01-Feb-27 | 08-Feb-27 | 07-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **BLOCK B11** | | 288 | 5,075,523.09 | 08-Mar-26 | 16-Feb-27 | 18-Feb-26 | | 2,707,911.45 | 3,337,184.36 | 1.23 |
| **STRUCTURAL** | | 202 | 1,389,042.53 | 08-Mar-26 | 27-Oct-26 | 18-Feb-26 | | 1,388,135.41 | 1,388,135.41 | 1.00 |
| **FOOTING** | | 36 | 597,655.16 | 08-Mar-26 | 08-Apr-26 | 18-Feb-26 | 02-May-26 | 597,655.16 | 597,655.16 | 1.00 |
| DAM3-C-B11-S-150 | Excavation for footings | 4 | 89,859.61 | 08-Mar-26 | 11-Mar-26 | 18-Feb-26 | 08-Mar-26 | 89,859.61 | 89,859.61 | 1.00 |
| DAM3-C-B11-S-6343 | Soil replacement - rock fill | 4 | 179,061.91 | 12-Mar-26 | 16-Mar-26 | 08-Mar-26 | 16-Mar-26 | 179,061.91 | 179,061.91 | 1.00 |
| DAM3-C-B11-S-6353 | Engineering fill | 4 | 46,046.19 | 21-Mar-26 | 24-Mar-26 | 26-Mar-26 | 31-Mar-26 | 46,046.19 | 46,046.19 | 1.00 |
| DAM3-C-B11-S-101 | Anti Termite Below Footings | 1 | 11,905.55 | 25-Mar-26 | 25-Mar-26 | 02-Apr-26 | 02-Apr-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B11-S-102 | Vapour Barrier for Footings | 1 | 7,940.10 | 26-Mar-26 | 26-Mar-26 | 02-Apr-26 | 02-Apr-26 | 7,940.10 | 7,940.10 | 1.00 |
| DAM3-C-B11-S-103 | Lean Concrete Below Footings | 2 | 8,229.34 | 28-Mar-26 | 29-Mar-26 | 02-Apr-26 | 02-Apr-26 | 8,229.34 | 8,229.34 | 1.00 |
| DAM3-C-B11-S-104 | Rebar for Footings | 4 | 101,844.98 | 30-Mar-26 | 02-Apr-26 | 25-Apr-26 | 28-Apr-26 | 101,844.98 | 101,844.98 | 1.00 |
| DAM3-C-B11-S-105 | Formwork for Footings | 4 | 25,461.25 | 04-Apr-26 | 07-Apr-26 | 28-Apr-26 | 29-Apr-26 | 25,461.25 | 25,461.25 | 1.00 |

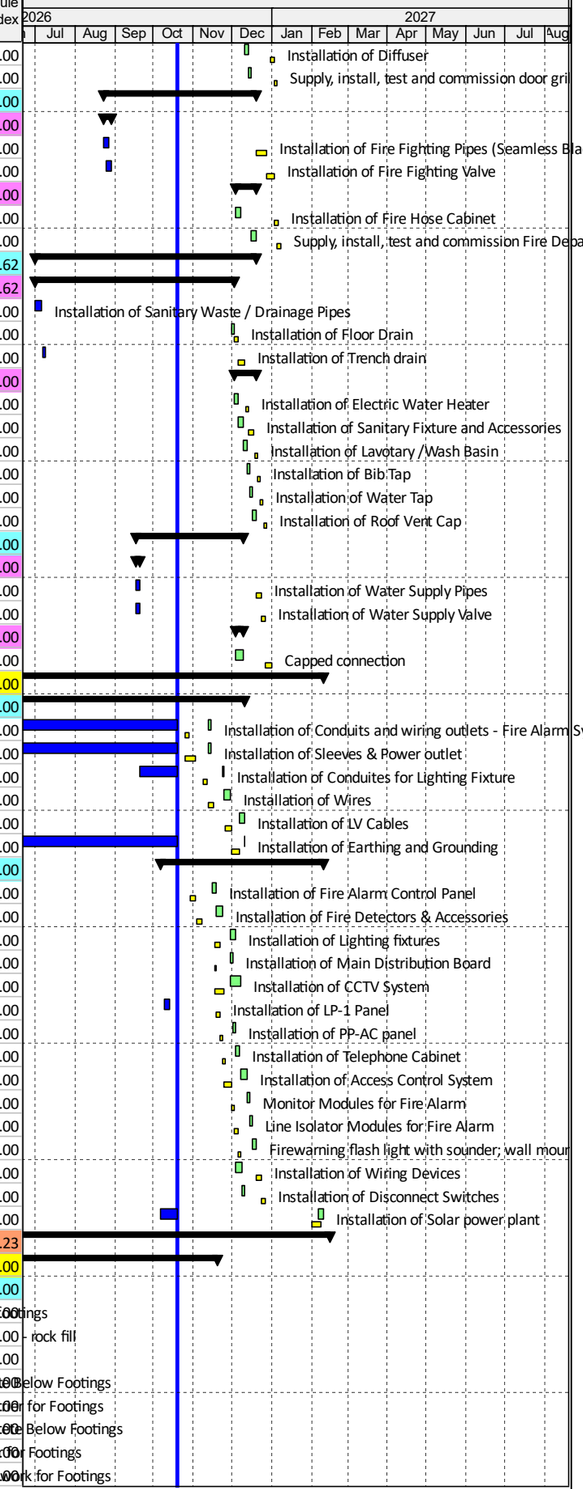





© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B11-S-106 | Pouring Concrete for Footings | 1 | 127,306.23 | 08-Apr-26 | 08-Apr-26 | 02-May-26 | 02-May-26 | 127,306.23 | 127,306.23 | 1.00 |
| **COLUMN NECK** | | 19 | 120,554.54 | 09-Apr-26 | 27-Apr-26 | 27-Apr-26 | 20-May-26 | 120,554.54 | 120,554.54 | 1.00 |
| DAM3-C-B11-S-257 | Rebar for column neck | 4 | 14,919.19 | 09-Apr-26 | 13-Apr-26 | 27-Apr-26 | 28-Apr-26 | 14,919.19 | 14,919.19 | 1.00 |
| DAM3-C-B11-S-267 | Formwork for column neck | 2 | 9,946.13 | 14-Apr-26 | 15-Apr-26 | 05-May-26 | 06-May-26 | 9,946.13 | 9,946.13 | 1.00 |
| DAM3-C-B11-S-297 | Pouring Concrete for column neck | 1 | 24,865.31 | 16-Apr-26 | 16-Apr-26 | 07-May-26 | 07-May-26 | 24,865.31 | 24,865.31 | 1.00 |
| DAM3-C-B11-S-307 | Damp proof /Bitumin paint on Footings & column neck | 2 | 24,777.73 | 18-Apr-26 | 19-Apr-26 | 11-May-26 | 13-May-26 | 24,777.73 | 24,777.73 | 1.00 |
| DAM3-C-B11-S-367 | Backfilling / Compaction up to Bottom of Grade Beams | 7 | 46,046.19 | 20-Apr-26 | 27-Apr-26 | 17-May-26 | 20-May-26 | 46,046.19 | 46,046.19 | 1.00 |
| **GRADE BEAM** | | 18 | 171,632.86 | 28-Apr-26 | 18-May-26 | 24-May-26 | 13-Jun-26 | 171,632.86 | 171,632.86 | 1.00 |
| DAM3-C-B11-S-527 | Anti Termite Below Grade Beams | 1 | 11,905.55 | 28-Apr-26 | 28-Apr-26 | 24-May-26 | 24-May-26 | 11,905.55 | 11,905.55 | 1.00 |
| DAM3-C-B11-S-337 | Vapour barrier for Grade Beams | 2 | 5,293.40 | 29-Apr-26 | 30-Apr-26 | 24-May-26 | 24-May-26 | 5,293.40 | 5,293.40 | 1.00 |
| DAM3-C-B11-S-338 | Lean Concrete Below Grade Beams | 2 | 4,431.19 | 02-May-26 | 03-May-26 | 24-May-26 | 24-May-26 | 4,431.19 | 4,431.19 | 1.00 |
| DAM3-C-B11-S-339 | Rebar for Grade Beams | 5 | 27,194.46 | 04-May-26 | 09-May-26 | 01-Jun-26 | 03-Jun-26 | 27,194.46 | 27,194.46 | 1.00 |
| DAM3-C-B11-S-340 | Formwork for Grade Beams | 2 | 6,798.61 | 10-May-26 | 11-May-26 | 02-Jun-26 | 06-Jun-26 | 6,798.61 | 6,798.61 | 1.00 |
| DAM3-C-B11-S-341 | Anchor bolts installation | 2 | 57,238.83 | 10-May-26 | 11-May-26 | 02-Jun-26 | 03-Jun-26 | 57,238.83 | 57,238.83 | 1.00 |
| DAM3-C-B11-S-342 | Pouring Concrete for Grade Beams | 1 | 33,993.09 | 12-May-26 | 12-May-26 | 06-Jun-26 | 06-Jun-26 | 33,993.09 | 33,993.09 | 1.00 |
| DAM3-C-B11-S-347 | Damp proof /Bitumin paint on Grade Beams | 5 | 24,777.73 | 13-May-26 | 18-May-26 | 11-Jun-26 | 13-Jun-26 | 24,777.73 | 24,777.73 | 1.00 |
| **SLAB ON GRADE** | | 134 | 397,232.98 | 19-May-26 | 27-Oct-26 | 15-Jun-26 | | 396,325.87 | 396,325.87 | 1.00 |
| DAM3-C-B11-S-377 | Backfilling / Compaction for Slab on Grade | 7 | 23,023.09 | 19-May-26 | 30-May-26 | 15-Jun-26 | 21-Jun-26 | 23,023.09 | 23,023.09 | 1.00 |
| DAM3-C-B11-S-378 | Anti Termite Treatment below Ground Slab | 1 | 15,874.08 | 31-May-26 | 31-May-26 | 26-Jul-26 | 28-Jul-26 | 15,874.08 | 15,874.08 | 1.00 |
| DAM3-C-B11-S-379 | Vapour barrier for below Ground Slab | 2 | 13,233.49 | 01-Jun-26 | 02-Jun-26 | 26-Jul-26 | 28-Jul-26 | 13,233.49 | 13,233.49 | 1.00 |
| DAM3-C-B11-S-382 | Pouring Concrete for Ground Slab | 4 | 344,195.21 | 03-Jun-26 | 07-Jun-26 | 26-Jul-26 | 28-Jul-26 | 344,195.21 | 344,195.21 | 1.00 |
| DAM3-C-B11-S-517 | Concrete pad | 7 | 907.11 | 20-Oct-26 | 27-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **COLUMNS & BEAMS** | | 81 | 101,966.98 | 31-May-26 | 27-Jun-26 | 02-Jun-26 | 01-Oct-26 | 101,966.98 | 101,966.98 | 1.00 |
| DAM3-C-B11-S-5101 | Rebar for column | 5 | 20,144.05 | 31-May-26 | 04-Jun-26 | 13-Jul-26 | 16-Jul-26 | 20,144.05 | 20,144.05 | 1.00 |
| DAM3-C-B11-S-5102 | Formwork for column | 4 | 5,036.01 | 06-Jun-26 | 09-Jun-26 | 08-Aug-26 | 11-Aug-26 | 5,036.01 | 5,036.01 | 1.00 |
| DAM3-C-B11-S-5103 | Pouring Concrete for column | 1 | 25,180.06 | 10-Jun-26 | 10-Jun-26 | 09-Aug-26 | 12-Aug-26 | 25,180.06 | 25,180.06 | 1.00 |
| DAM3-C-B11-S-6101 | Rebar for Tie Beams | 4 | 7,263.64 | 11-Jun-26 | 15-Jun-26 | 02-Jun-26 | 08-Jun-26 | 7,263.64 | 7,263.64 | 1.00 |
| DAM3-C-B11-S-6102 | Formwork for Tie Beams | 2 | 1,815.91 | 16-Jun-26 | 17-Jun-26 | 03-Jun-26 | 08-Jun-26 | 1,815.91 | 1,815.91 | 1.00 |
| DAM3-C-B11-S-6103 | Pouring Concrete for Tie Beams | 1 | 9,079.54 | 18-Jun-26 | 18-Jun-26 | 06-Jun-26 | 09-Jun-26 | 9,079.54 | 9,079.54 | 1.00 |
| DAM3-C-B11-S-6113 | Rebar for Beams | 4 | 13,379.11 | 20-Jun-26 | 23-Jun-26 | 01-Sep-26 | 03-Sep-26 | 13,379.11 | 13,379.11 | 1.00 |
| DAM3-C-B11-S-6123 | Formwork for Beams | 2 | 3,344.77 | 24-Jun-26 | 25-Jun-26 | 21-Sep-26 | 26-Sep-26 | 3,344.77 | 3,344.77 | 1.00 |
| DAM3-C-B11-S-6133 | Pouring Concrete for Beams | 1 | 16,723.88 | 27-Jun-26 | 27-Jun-26 | 28-Sep-26 | 01-Oct-26 | 16,723.88 | 16,723.88 | 1.00 |
| **STRUCTURAL STEEL** | | 44 | 1,566,668.48 | 15-Sep-26 | 25-Oct-26 | 25-Jun-26 | | 1,236,673.00 | 1,539,773.29 | 1.25 |
| DAM3-C-B11-SS-0100 | Installation of columns | 3 | 217,507.55 | 15-Sep-26 | 17-Sep-26 | 25-Jun-26 | 28-Jun-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B11-SS-0110 | Installation of raft and purlins | 5 | 326,261.32 | 19-Sep-26 | 24-Sep-26 | 30-Jun-26 | 01-Jul-26 | 326,261.32 | 326,261.32 | 1.00 |
| DAM3-C-B11-SS-610 | Intumescent paint to steel works | 7 | 317,759.56 | 26-Sep-26 | 03-Oct-26 | 19-Jul-26 | 25-Jul-26 | 317,759.56 | 317,759.56 | 1.00 |
| DAM3-C-B11-SS-620 | Steel members for office area | 7 | 115,805.20 | 04-Oct-26 | 11-Oct-26 | 27-Sep-26 | 30-Sep-26 | 115,805.20 | 115,805.20 | 1.00 |
| DAM3-C-B11-SS-0140 | Installation of roof sheet | 5 | 217,507.55 | 07-Oct-26 | 12-Oct-26 | 01-Aug-26 | 08-Aug-26 | 217,507.55 | 217,507.55 | 1.00 |
| DAM3-C-B11-SS-1020 | Epoxy paint to steel members at office area | 4 | 23,161.04 | 12-Oct-26 | 19-Oct-26 | | | 23,161.04 | 0.00 | 0.00 |
| DAM3-C-B11-SS-1030 | Steel members for external platform | 7 | 18,670.78 | 12-Oct-26 | 19-Oct-26 | 04-Oct-26 | 07-Oct-26 | 18,670.78 | 18,670.78 | 1.00 |
| DAM3-C-B11-SS-0130 | Installation of wall sandwich panel | 5 | 326,261.32 | 20-Oct-26 | 25-Oct-26 | 03-Sep-26 | 30-Sep-26 | 0.00 | 326,261.32 | 0.00 |
| DAM3-C-B11-SS-1040 | Epoxy paint for external platform | 5 | 3,734.16 | 20-Oct-26 | 25-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| **ARCHITECTURAL** | | 88 | 900,244.66 | 26-Sep-26 | 19-Jan-27 | 30-Jul-26 | | 64,517.90 | 181,621.60 | 2.82 |
| **MASONARY WORKS** | | 21 | 78,954.21 | 26-Sep-26 | 27-Oct-26 | 06-Aug-26 | 06-Sep-26 | 64,517.90 | 78,954.21 | 1.22 |
| DAM3-C-B11-A-0120 | Block work at factory area | 5 | 58,338.72 | 26-Sep-26 | 06-Oct-26 | 06-Aug-26 | 11-Aug-26 | 58,338.72 | 58,338.72 | 1.00 |
| DAM3-C-B11-A-0150 | Block work at office area | 3 | 6,179.18 | 12-Oct-26 | 19-Oct-26 | 10-Aug-26 | 06-Sep-26 | 6,179.18 | 6,179.18 | 1.00 |
| DAM3-C-B11-A-170 | Block work at toilet area | 4 | 14,436.31 | 20-Oct-26 | 27-Oct-26 | 13-Aug-26 | 06-Sep-26 | 0.00 | 14,436.31 | 0.00 |
| **WALL FINISHES** | | 11 | 92,757.47 | 07-Nov-26 | 22-Dec-26 | 27-Sep-26 | | 0.00 | 48,590.16 | 0.00 |
| DAM3-C-B11-A-180 | Internal Wall Plaster | 10 | 48,590.16 | 07-Nov-26 | 23-Nov-26 | 27-Sep-26 | 15-Oct-26 | 0.00 | 48,590.16 | 0.00 |
| DAM3-C-B11-A-230 | Paint to Plaster (Primer, Putty & First Coat) | 4 | 44,167.30 | 15-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **CIELING FINISHES** | | 5 | 46,792.30 | 07-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-240 | Installation of Ceiling Gypsum Board | 5 | 46,792.30 | 07-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FLOOR FINISHES** | | 17 | 189,488.90 | 29-Nov-26 | 19-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-220 | Tiles for Toilet | 5 | 46,530.71 | 29-Nov-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-250 | Tiles for Office Area | 2 | 26,867.31 | 13-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-390 | Granite strip | 2 | 671.12 | 15-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-420 | Epoxy paint | 7 | 115,419.76 | 12-Jan-27 | 19-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **DOORS & WINDOWS** | | 16 | 248,575.06 | 26-Oct-26 | 10-Nov-26 | 06-Oct-26 | | 0.00 | 30,033.19 | 0.00 |
| DAM3-C-B11-A-552 | Window (CW1) | 7 | 94,173.21 | 26-Oct-26 | 02-Nov-26 | 20-Oct-26 | | 0.00 | 23,543.30 | 0.00 |
| DAM3-C-B11-A-553 | Roll up Shutter Door | 1 | 68,619.20 | 03-Nov-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-200 | Supply and install (D5) 1000*2200mm single leaf steel door with do | 1 | 16,016.16 | 04-Nov-26 | 04-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-554 | Supply and install (D4) 800*2200 mm single leaf aluminum door wit | 1 | 22,737.85 | 05-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |

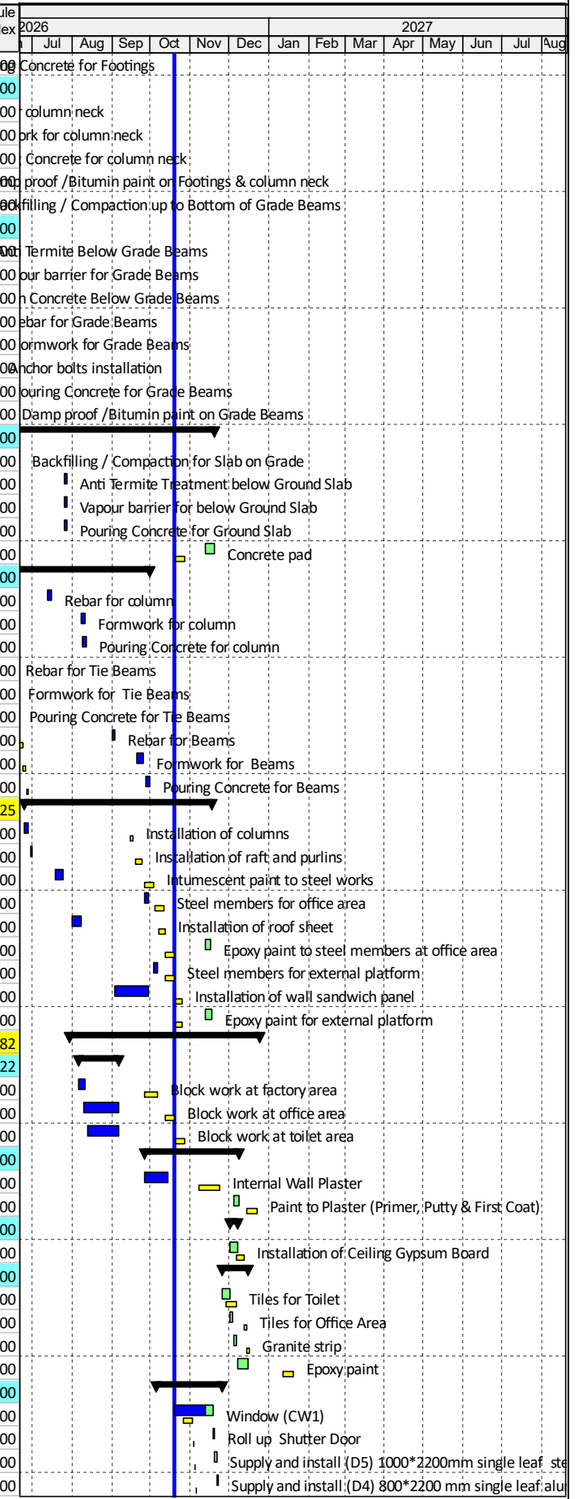




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B11-A-555 | Supply and install (D7) 1000*2200 mm single leaf aluminum door wi | 1 | 7,811.07 | 07-Nov-26 | 07-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-556 | Supply and install (D3) 1000*2200 mm single leaf aluminum door wi | 1 | 16,016.16 | 08-Nov-26 | 08-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-557 | Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf | 1 | 16,711.52 | 09-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-558 | Skylight fixtures installation | 1 | 6,489.89 | 10-Nov-26 | 10-Nov-26 | 06-Oct-26 | 08-Oct-26 | 0.00 | 6,489.89 | 0.00 |
| **WATER PROOFING WORKS** | | 4 | 4,879.02 | 24-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-370 | Waterproofing membrane for toilets | 4 | 4,879.02 | 24-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| **METAL WORKS** | | 67 | 193,717.06 | 17-Dec-26 | 31-Dec-26 | 30-Jul-26 | | 0.00 | 24,044.04 | 0.00 |
| DAM3-C-B11-A-290 | Steel Ladder | 2 | 9,839.16 | 17-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-291 | Steel railing works | 4 | 1,533.98 | 20-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-292 | Aluminium composite panel | 3 | 175,888.76 | 24-Dec-26 | 29-Dec-26 | 15-Oct-26 | | 0.00 | 17,588.88 | 0.00 |
| DAM3-C-B11-A-300 | Galvanised Steel Gratings | 2 | 6,455.16 | 30-Dec-26 | 31-Dec-26 | 30-Jul-26 | 30-Jul-26 | 0.00 | 6,455.16 | 0.00 |
| **SPECIALTIES** | | 7 | 45,080.66 | 02-Jan-27 | 11-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-320 | Installation of fittings | 3 | 22,981.27 | 02-Jan-27 | 06-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-570 | Identification sign; ID01 & ID02 | 3 | 9,630.56 | 07-Jan-27 | 10-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-A-340 | Furniture Installation | 1 | 12,468.83 | 11-Jan-27 | 11-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **MECHANICAL** | | 182 | 467,522.66 | 19-May-26 | 11-Jan-27 | 05-Jul-26 | | 18,585.14 | 156,280.78 | 8.41 |
| **HVAC** | | 13 | 233,183.33 | 23-Dec-26 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **FIRST STAGE** | | 4 | 170,694.73 | 30-Dec-26 | 03-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-140 | Installation of HVAC Ducts | 2 | 149,489.33 | 30-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-170 | Installation of Duct insulation | 2 | 21,205.40 | 02-Jan-27 | 03-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **SECOND STAGE** | | 13 | 62,488.60 | 23-Dec-26 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-130 | Installation of Exhaust Fans | 2 | 7,938.56 | 23-Dec-26 | 24-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-160 | Installation of Wall Propeller Type Exhaust Fan | 3 | 46,831.64 | 26-Dec-26 | 29-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-339 | Installation of Diffuser | 2 | 2,144.00 | 04-Jan-27 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-340 | Supply, install, test and commission door grilles & exhaust louvers | 2 | 5,574.40 | 06-Jan-27 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **FIRE FIGHTING SYSTEM** | | 20 | 102,458.78 | 23-Dec-26 | 11-Jan-27 | 29-Aug-26 | | 0.00 | 84,594.16 | 0.00 |
| **FIRST STAGE** | | 8 | 84,594.16 | 23-Dec-26 | 05-Jan-27 | 29-Aug-26 | 07-Sep-26 | 0.00 | 84,594.16 | 0.00 |
| DAM3-C-B11-M-300 | Installation of Fire Fighting Pipes (Seamless Black Steel) | 5 | 72,394.75 | 23-Dec-26 | 30-Dec-26 | 29-Aug-26 | 05-Sep-26 | 0.00 | 72,394.75 | 0.00 |
| DAM3-C-B11-M-310 | Installation of Fire Fighting Valve | 3 | 12,199.40 | 31-Dec-26 | 05-Jan-27 | 30-Aug-26 | 07-Sep-26 | 0.00 | 12,199.40 | 0.00 |
| **SECOND STAGE** | | 16 | 17,864.62 | 06-Jan-27 | 11-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-320 | Installation of Fire Hose Cabinet | 3 | 15,158.56 | 06-Jan-27 | 09-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-370 | Supply, install, test and commission Fire Department Connection(FDC) | 3 | 2,706.06 | 09-Jan-27 | 11-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **SEWER AND DRAINAGE SYSTEM** | | 182 | 90,009.74 | 19-May-26 | 30-Dec-26 | 05-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| **FIRST STAGE** | | 182 | 41,149.90 | 19-May-26 | 14-Dec-26 | 05-Jul-26 | | 18,585.14 | 30,093.94 | 1.62 |
| DAM3-C-B11-M-200 | Installation of Sanitary Waste / Drainage Pipes | 4 | 18,585.14 | 19-May-26 | 23-May-26 | 05-Jul-26 | 08-Jul-26 | 18,585.14 | 18,585.14 | 1.00 |
| DAM3-C-B11-M-220 | Installation of Floor Drain | 2 | 11,055.96 | 07-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-380 | Installation of Trench drain | 5 | 11,508.80 | 09-Dec-26 | 14-Dec-26 | 06-Jul-26 | 08-Jul-26 | 0.00 | 11,508.80 | 0.00 |
| **SECOND STAGE** | | 14 | 48,859.84 | 15-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-180 | Installation of Electric Water Heater | 2 | 1,819.51 | 15-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-190 | Installation of Sanitary Fixture and Accessories | 4 | 19,921.72 | 17-Dec-26 | 21-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-210 | Installation of Lavotary /Wash Basin | 2 | 21,416.68 | 22-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-270 | Installation of Bib Tap | 2 | 1,900.66 | 24-Dec-26 | 26-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-428 | Installation of Water Tap | 2 | 2,874.14 | 27-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-429 | Installation of Roof Vent Cap | 2 | 927.12 | 29-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **WATER SUPPLY SYSTEM** | | 20 | 41,870.81 | 23-Dec-26 | 04-Jan-27 | 01-Oct-26 | | 0.00 | 41,592.68 | 0.00 |
| **FIRST STAGE** | | 6 | 41,592.68 | 23-Dec-26 | 29-Dec-26 | 01-Oct-26 | 05-Oct-26 | 0.00 | 41,592.68 | 0.00 |
| DAM3-C-B11-M-290 | Installation of Water Supply Pipes | 4 | 23,318.41 | 23-Dec-26 | 27-Dec-26 | 01-Oct-26 | 05-Oct-26 | 0.00 | 23,318.41 | 0.00 |
| DAM3-C-B11-M-280 | Installation of Water Supply Valve | 2 | 18,274.27 | 28-Dec-26 | 29-Dec-26 | 01-Oct-26 | 05-Oct-26 | 0.00 | 18,274.27 | 0.00 |
| **SECOND STAGE** | | 5 | 278.13 | 30-Dec-26 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-M-330 | Capped connection | 5 | 278.13 | 30-Dec-26 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 125 | 752,044.76 | 28-Oct-26 | 16-Feb-27 | 01-Jun-26 | | 0.00 | 71,373.28 | 0.00 |
| **FIRST STAGE** | | 79 | 86,114.12 | 28-Oct-26 | 09-Dec-26 | 01-Jun-26 | | 0.00 | 27,642.87 | 0.00 |
| DAM3-C-B11-E-143 | Installation of Conduits and wiring outlets - Fire Alarm System | 4 | 1,768.31 | 28-Oct-26 | 01-Nov-26 | 02-Jun-26 | | 0.00 | 884.15 | 0.00 |
| DAM3-C-B11-E-183 | Installation of Sleeves & Power outlet | 8 | 2,920.45 | 28-Oct-26 | 05-Nov-26 | 02-Jun-26 | | 0.00 | 1,460.23 | 0.00 |
| DAM3-C-B11-E-163 | Installation of Conduites for Lighting Fixture | 4 | 8,462.97 | 11-Nov-26 | 15-Nov-26 | 27-Sep-26 | | 0.00 | 7,616.67 | 0.00 |
| DAM3-C-B11-E-233 | Installation of Wires | 4 | 16,925.94 | 16-Nov-26 | 19-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-223 | Installation of LV Cables | 4 | 36,389.98 | 30-Nov-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-113 | Installation of Earthing and Grounding | 3 | 19,646.47 | 05-Dec-26 | 09-Dec-26 | 01-Jun-26 | | 0.00 | 17,681.82 | 0.00 |
| **SECOND STAGE** | | 66 | 665,930.64 | 02-Nov-26 | 16-Feb-27 | 08-Oct-26 | | 0.00 | 43,730.41 | 0.00 |
| DAM3-C-B11-E-123 | Installation of Fire Alarm Control Panel | 4 | 19,451.37 | 02-Nov-26 | 05-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-133 | Installation of Fire Detectors & Accessories | 4 | 56,740.37 | 07-Nov-26 | 10-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-153 | Installation of Lighting fixtures | 4 | 76,166.74 | 21-Nov-26 | 24-Nov-26 | | | 0.00 | 0.00 | 0.00 |

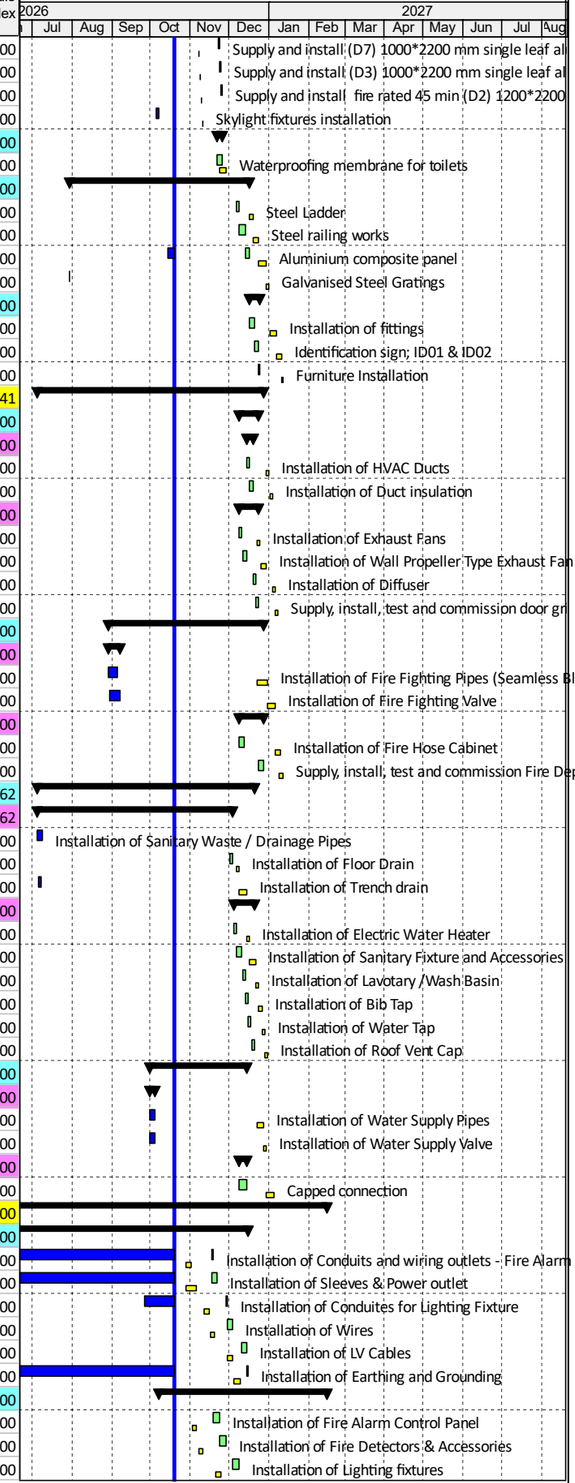




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-B11-E-193 | Installation of Main Distribution Board | 2 | 32,472.73 | 21-Nov-26 | 22-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-410 | Installation of CCTV System | 5 | 76,349.24 | 21-Nov-26 | 28-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-243 | Installation of LP-1 Panel | 2 | 18,403.54 | 23-Nov-26 | 24-Nov-26 | 10-Oct-26 | 14-Oct-26 | 0.00 | 18,403.54 | 0.00 |
| DAM3-C-B11-E-253 | Installation of PP-AC panel | 2 | 21,648.48 | 25-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-213 | Installation of Telephone Cabinet | 2 | 26,991.08 | 28-Nov-26 | 29-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-273 | Installation of Access Control System | 5 | 27,616.86 | 29-Nov-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-283 | Monitor Modules for Fire Alarm | 2 | 3,882.38 | 05-Dec-26 | 06-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-293 | Line Isolator Modules for Fire Alarm | 2 | 185.40 | 07-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-303 | Firewarning flash light with sounder; wall mounted, Weather proof | 2 | 3,082.69 | 09-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-173 | Installation of Wiring Devices | 4 | 19,435.09 | 23-Dec-26 | 27-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-203 | Installation of Disconnect Switches | 2 | 30,235.95 | 28-Dec-26 | 29-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-B11-E-420 | Installation of Solar power plant | 4 | 253,268.71 | 09-Feb-27 | 16-Feb-27 | 08-Oct-26 | | 0.00 | 25,326.87 | 0.00 |
| **SITE INFRASTRUCTURE** | | 282 | 8,476,025.35 | 10-Feb-26 | 21-Feb-27 | 19-Jan-26 | | 2,008,886.17 | 2,768,614.43 | 1.38 |
| **SITE WORKS** | | 23 | 197,690.88 | 10-Feb-26 | 10-Mar-26 | 19-Jan-26 | 28-Feb-26 | 197,690.88 | 197,690.88 | 1.00 |
| DAM3-C-GEN-180 | Initial Site Survey and Setting out | 3 | 0.00 | 10-Feb-26 | 12-Feb-26 | 19-Jan-26 | 24-Jan-26 | 0.00 | 0.00 | 0.00 |
| DAM3-C-GEN-190 | Excavation to the target grading level | 20 | 197,690.88 | 14-Feb-26 | 10-Mar-26 | 10-Feb-26 | 28-Feb-26 | 197,690.88 | 197,690.88 | 1.00 |
| **NETWORKS** | | 84 | 1,901,944.63 | 07-Sep-26 | 23-Dec-26 | 01-Aug-26 | | 919,729.18 | 1,318,470.60 | 1.43 |
| **INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UNITS)** | | 42 | 571,716.96 | 07-Sep-26 | 21-Oct-26 | 01-Aug-26 | | 565,935.31 | 497,845.16 | 0.88 |
| DAM3-C-ENV-F-212 | Excavation for External Fire Fighting Works | 7 | 40,471.58 | 07-Sep-26 | 14-Sep-26 | 01-Aug-26 | | 40,471.58 | 36,424.43 | 0.90 |
| DAM3-C-ENV-F-172 | Installation of HDPE PN16 Pipes (200 Dia) | 10 | 364,244.28 | 15-Sep-26 | 27-Sep-26 | 02-Aug-26 | | 364,244.28 | 327,819.85 | 0.90 |
| DAM3-C-ENV-F-202 | Warning Tapes | 2 | 40,471.58 | 28-Sep-26 | 29-Sep-26 | 03-Aug-26 | | 40,471.58 | 32,377.27 | 0.80 |
| DAM3-C-ENV-F-192 | Installation of Valves | 5 | 86,057.93 | 30-Sep-26 | 05-Oct-26 | 02-Aug-26 | | 86,057.93 | 68,846.34 | 0.80 |
| DAM3-C-ENV-F-222 | Backfilling for External Fire Fighting Works | 14 | 40,471.58 | 06-Oct-26 | 21-Oct-26 | 05-Aug-26 | | 34,689.93 | 32,377.27 | 0.93 |
| **WATER SUPPLY SYSTEM** | | 37 | 290,579.64 | 15-Sep-26 | 23-Dec-26 | 04-Oct-26 | | 182,365.84 | 137,507.78 | 0.75 |
| DAM3-C-ENV-WS-786 | Excavation for Water Suppy Works | 7 | 13,950.39 | 15-Sep-26 | 22-Sep-26 | 12-Oct-26 | | 13,950.39 | 6,975.20 | 0.50 |
| DAM3-C-ENV-WS-746 | Installation of HDPE PN16 Pipes for Cold Water Supply | 7 | 125,553.50 | 24-Sep-26 | 05-Oct-26 | 17-Oct-26 | | 125,553.50 | 62,776.75 | 0.50 |
| DAM3-C-ENV-WS-806 | Construction of Washout Chamber | 7 | 17,314.15 | 06-Oct-26 | 13-Oct-26 | 04-Oct-26 | | 17,314.15 | 13,851.32 | 0.80 |
| DAM3-C-ENV-WS-776 | Warning Tape | 2 | 13,950.39 | 14-Oct-26 | 15-Oct-26 | 18-Oct-26 | | 13,950.39 | 6,975.20 | 0.50 |
| DAM3-C-ENV-WS-846 | Construction of Air Valve Chamber | 7 | 16,236.37 | 14-Oct-26 | 21-Oct-26 | 04-Oct-26 | | 11,597.40 | 12,989.09 | 1.12 |
| DAM3-C-ENV-WS-766 | Installation of Valves | 5 | 53,930.05 | 16-Nov-26 | 21-Nov-26 | 17-Oct-26 | | 0.00 | 26,965.03 | 0.00 |
| DAM3-C-ENV-WS-796 | Backfilling for Water Supply | 14 | 13,950.39 | 22-Nov-26 | 07-Dec-26 | 18-Oct-26 | | 0.00 | 6,975.20 | 0.00 |
| DAM3-C-ENV-WS-826 | Supply and install Service connection -HDPE | 14 | 35,694.38 | 08-Dec-26 | 23-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **SEWER & DRAINAGE SYSTEM** | | 36 | 772,226.27 | 06-Oct-26 | 08-Dec-26 | 22-Aug-26 | | 133,571.67 | 683,117.66 | 5.11 |
| DAM3-C-ENV-SW-516 | Excavation for Sewer Works | 7 | 22,261.94 | 06-Oct-26 | 13-Oct-26 | 22-Aug-26 | 04-Oct-26 | 22,261.94 | 22,261.94 | 1.00 |
| DAM3-C-ENV-SW-486 | Installation of UPVC Pipes for Sewer | 4 | 222,619.45 | 14-Oct-26 | 25-Oct-26 | 16-Sep-26 | 05-Oct-26 | 111,309.72 | 222,619.45 | 2.00 |
| DAM3-C-ENV-SW-536 | Construction of Manhole | 7 | 166,049.07 | 26-Oct-26 | 02-Nov-26 | 22-Aug-26 | 10-Sep-26 | 0.00 | 166,049.07 | 0.00 |
| DAM3-C-ENV-SW-496 | Construction of inspection chambers | 7 | 249,925.25 | 03-Nov-26 | 10-Nov-26 | 22-Aug-26 | 03-Oct-26 | 0.00 | 249,925.25 | 0.00 |
| DAM3-C-ENV-SW-526 | Backfilling for Sewer Drainage | 14 | 22,261.94 | 03-Nov-26 | 18-Nov-26 | 17-Sep-26 | 06-Oct-26 | 0.00 | 22,261.94 | 0.00 |
| DAM3-C-ENV-SW-506 | Gully trap | 10 | 53,541.58 | 19-Nov-26 | 30-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-546 | UPVC pipe service connection | 7 | 35,567.03 | 01-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **IRRIGATION SYSTEM** | | 48 | 267,421.77 | 06-Oct-26 | 22-Dec-26 | | | 37,856.36 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-556 | Excavation for HDPE pipes | 7 | 6,309.39 | 06-Oct-26 | 13-Oct-26 | | | 6,309.39 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-566 | Installation of HDPE Pipes | 10 | 63,093.94 | 14-Oct-26 | 25-Oct-26 | | | 31,546.97 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-586 | Construction of Washout valve chamber | 5 | 3,247.85 | 26-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-576 | Construction of Air valve chamber | 5 | 3,786.75 | 26-Oct-26 | 31-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-596 | Backfilling for HDPE pipes | 14 | 6,309.39 | 01-Nov-26 | 16-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-606 | Installation of valves | 5 | 84,556.00 | 09-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-SW-616 | Main program system and controller for irrigation system | 7 | 100,118.45 | 15-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **EXTERNAL WORKS** | | 74 | 3,338,525.71 | 15-Sep-26 | 25-Jan-27 | 01-Jul-26 | | 891,466.10 | 1,252,452.95 | 1.40 |
| **MECHANICAL** | | 36 | 1,375,655.38 | 26-Oct-26 | 10-Jan-27 | 01-Jul-26 | | 0.00 | 1,252,452.95 | 0.00 |
| DAM3-C-ENV-M-1371 | Installation of GRP Tanks | 10 | 585,839.88 | 30-Nov-26 | 10-Dec-26 | 08-Aug-26 | 08-Oct-26 | 0.00 | 585,839.88 | 0.00 |
| DAM3-C-ENV-M-1381 | Valves for GRP Tank | 3 | 58,583.98 | 12-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-M-1391 | Access Ladder for GRP Tank | 2 | 58,583.98 | 15-Dec-26 | 16-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-M-1341 | Installation of Booster Pump | 5 | 38,967.27 | 26-Dec-26 | 30-Dec-26 | 07-Oct-26 | 07-Oct-26 | 0.00 | 38,967.27 | 0.00 |
| DAM3-C-ENV-M-1301 | Installation of Fire Fighting Pump | 4 | 345,880.31 | 31-Dec-26 | 04-Jan-27 | 22-Sep-26 | 22-Sep-26 | 0.00 | 345,880.31 | 0.00 |
| DAM3-C-ENV-M-1351 | Valves for Water Supply Pump | 2 | 4,329.70 | 03-Jan-27 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-M-1311 | CO2 fire extinguisher | 1 | 217.29 | 05-Jan-27 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-M-1361 | Powder fire extinguisher | 1 | 188.33 | 06-Jan-27 | 06-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **GRP Tank Foundation** | | 31 | 180,037.46 | 31-Oct-26 | 29-Nov-26 | 27-Jul-26 | 27-Aug-26 | 0.00 | 180,037.46 | 0.00 |
| DAM3-C-GRP-S-0101 | Excavation for Foundation | 4 | 9,001.87 | 31-Oct-26 | 03-Nov-26 | 27-Jul-26 | 27-Jul-26 | 0.00 | 9,001.87 | 0.00 |
| DAM3-C-GRP-S-0102 | Vapour Barrier for Foundation | 2 | 9,001.87 | 04-Nov-26 | 05-Nov-26 | 06-Aug-26 | 06-Aug-26 | 0.00 | 9,001.87 | 0.00 |
| DAM3-C-GRP-S-0103 | Lean Concrete Below Foundation | 2 | 18,003.75 | 07-Nov-26 | 08-Nov-26 | 06-Aug-26 | 06-Aug-26 | 0.00 | 18,003.75 | 0.00 |

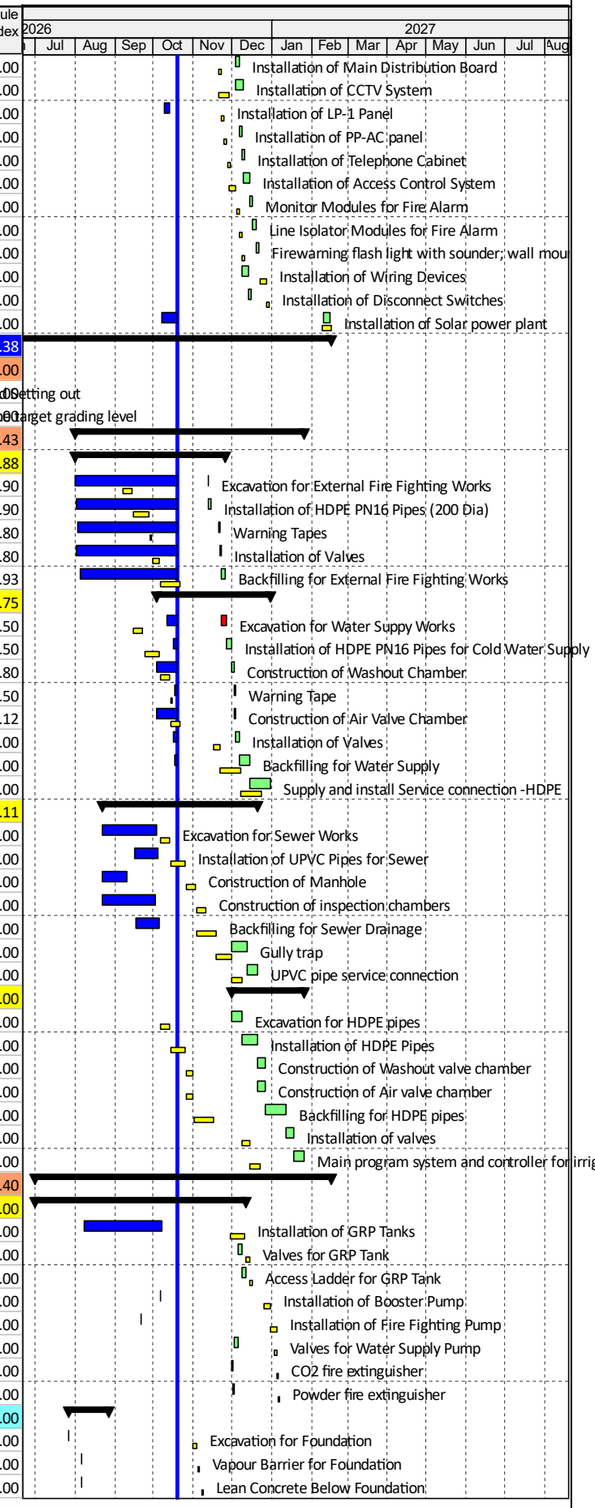




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-GRP-S-0104 | Rebar for Foundation | 4 | 36,007.49 | 09-Nov-26 | 12-Nov-26 | 11-Aug-26 | 16-Aug-26 | 0.00 | 36,007.49 | 0.00 |
| DAM3-C-GRP-S-0105 | Formwork for Foundation | 4 | 18,003.75 | 14-Nov-26 | 17-Nov-26 | 12-Aug-26 | 23-Aug-26 | 0.00 | 18,003.75 | 0.00 |
| DAM3-C-GRP-S-0106 | Pouring Concrete for Foundation | 1 | 63,013.11 | 18-Nov-26 | 18-Nov-26 | 18-Aug-26 | 23-Aug-26 | 0.00 | 63,013.11 | 0.00 |
| DAM3-C-GRP-S-0107 | Damp proof /Bitumin paint on Foundation | 2 | 9,001.87 | 19-Nov-26 | 21-Nov-26 | 24-Aug-26 | 25-Aug-26 | 0.00 | 9,001.87 | 0.00 |
| DAM3-C-GRP-S-0108 | Backfilling / Compaction Around Foundation | 7 | 18,003.75 | 22-Nov-26 | 29-Nov-26 | 26-Aug-26 | 27-Aug-26 | 0.00 | 18,003.75 | 0.00 |
| **Pump Shed** | | 36 | 103,027.17 | 26-Oct-26 | 10-Jan-27 | 01-Jul-26 | | 0.00 | 101,728.03 | 0.00 |
| DAM3-C-PR-S-108 | Excavation for Footings | 4 | 649.57 | 26-Oct-26 | 29-Oct-26 | 01-Jul-26 | 02-Jul-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-308 | Vapour Barrier for Footings | 2 | 649.57 | 31-Oct-26 | 01-Nov-26 | 23-Jul-26 | 23-Jul-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-138 | Lean Concrete Below Footings | 2 | 649.57 | 02-Nov-26 | 03-Nov-26 | 23-Jul-26 | 23-Jul-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-198 | Rebar for Footings | 4 | 1,299.14 | 04-Nov-26 | 08-Nov-26 | 25-Jul-26 | 25-Jul-26 | 0.00 | 1,299.14 | 0.00 |
| DAM3-C-PR-S-208 | Formwork for Footings | 4 | 649.57 | 09-Nov-26 | 12-Nov-26 | 25-Jul-26 | 25-Jul-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-148 | Pouring Concrete for Footings | 1 | 5,846.13 | 14-Nov-26 | 14-Nov-26 | 26-Jul-26 | 26-Jul-26 | 0.00 | 5,846.13 | 0.00 |
| DAM3-C-PR-S-298 | Damp proof /Bitumin paint on Footing Sides | 2 | 649.57 | 15-Nov-26 | 16-Nov-26 | 28-Jul-26 | 28-Jul-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-378 | Backfilling / Compaction Around Footings to Bottom of Grade Beams | 5 | 1,299.14 | 17-Nov-26 | 22-Nov-26 | 29-Jul-26 | 03-Aug-26 | 0.00 | 1,299.14 | 0.00 |
| DAM3-C-PR-S-328 | Vapour barrier for Grade Beams | 2 | 649.57 | 23-Nov-26 | 24-Nov-26 | 04-Aug-26 | 04-Aug-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-158 | Lean Concrete Below Grade Beams | 2 | 649.57 | 25-Nov-26 | 26-Nov-26 | 04-Aug-26 | 04-Aug-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-218 | Rebar for Grade Beams | 2 | 1,299.14 | 28-Nov-26 | 29-Nov-26 | 15-Aug-26 | 15-Aug-26 | 0.00 | 1,299.14 | 0.00 |
| DAM3-C-PR-S-188 | Pedestal including anchor bolts | 1 | 1,299.14 | 30-Nov-26 | 30-Nov-26 | 17-Aug-26 | 17-Aug-26 | 0.00 | 1,299.14 | 0.00 |
| DAM3-C-PR-S-228 | Formwork for Grade Beams | 2 | 649.57 | 30-Nov-26 | 01-Dec-26 | 16-Aug-26 | 17-Aug-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-168 | Pouring Concrete for Grade Beams | 1 | 3,247.85 | 02-Dec-26 | 02-Dec-26 | 18-Aug-26 | 18-Aug-26 | 0.00 | 3,247.85 | 0.00 |
| DAM3-C-PR-S-338 | Damp proof /Bitumin paint on Grade Beams | 2 | 649.57 | 03-Dec-26 | 05-Dec-26 | 20-Aug-26 | 22-Aug-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-388 | Backfilling / Compaction for Slab on Grade | 5 | 1,299.14 | 06-Dec-26 | 10-Dec-26 | 23-Aug-26 | 24-Aug-26 | 0.00 | 1,299.14 | 0.00 |
| DAM3-C-PR-S-318 | Anti Termite Treatment below Ground Slab | 1 | 649.57 | 12-Dec-26 | 12-Dec-26 | 24-Aug-26 | 24-Aug-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-348 | Vapour barrier for below Ground Slab | 2 | 649.57 | 13-Dec-26 | 14-Dec-26 | 24-Aug-26 | 24-Aug-26 | 0.00 | 649.57 | 0.00 |
| DAM3-C-PR-S-268 | Rebar for Ground Slab | 4 | 12,070.63 | 15-Dec-26 | 19-Dec-26 | 25-Aug-26 | 26-Aug-26 | 0.00 | 12,070.63 | 0.00 |
| DAM3-C-PR-S-278 | Formwork for Ground Slab | 4 | 8,263.60 | 20-Dec-26 | 23-Dec-26 | 26-Aug-26 | 26-Aug-26 | 0.00 | 8,263.60 | 0.00 |
| DAM3-C-PR-S-178 | Pouring Concrete for Ground Slab | 1 | 20,334.24 | 24-Dec-26 | 24-Dec-26 | 27-Aug-26 | 27-Aug-26 | 0.00 | 20,334.24 | 0.00 |
| DAM3-C-PR-S-288 | Concrete Pad | 5 | 1,299.14 | 26-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-PR-S-128 | Installation of Columns | 3 | 7,794.85 | 31-Dec-26 | 03-Jan-27 | 30-Aug-26 | 30-Aug-26 | 0.00 | 7,794.85 | 0.00 |
| DAM3-C-PR-S-358 | Installation of Raft & Purlins | 4 | 11,042.69 | 04-Jan-27 | 07-Jan-27 | 30-Aug-26 | 30-Aug-26 | 0.00 | 11,042.69 | 0.00 |
| DAM3-C-PR-S-368 | Installation of Roof Sheet | 2 | 19,487.12 | 09-Jan-27 | 10-Jan-27 | 31-Aug-26 | 31-Aug-26 | 0.00 | 19,487.12 | 0.00 |
| **ELECTRICAL** | | 17 | 236,867.32 | 31-Dec-26 | 25-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-176 | Installation of Main MCC | 2 | 13,498.43 | 31-Dec-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-186 | Installation of Earthing and Grounding | 3 | 1,399.38 | 03-Jan-27 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-236 | Installation of panel boards | 2 | 5,953.91 | 05-Jan-27 | 06-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-1321 | Installation of wiring devices | 5 | 5,632.31 | 07-Jan-27 | 12-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-1341 | Installation of Cable tray | 5 | 3,563.73 | 07-Jan-27 | 12-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-206 | Installation of Conduites for Lighting Fixture | 4 | 798.20 | 09-Jan-27 | 12-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-216 | Installation of LV Cables | 5 | 7,709.71 | 13-Jan-27 | 18-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-226 | Installation of Wires | 2 | 1,596.40 | 13-Jan-27 | 14-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-196 | Installation of Lighting fixtures | 2 | 7,183.81 | 16-Jan-27 | 17-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-1331 | Installation of Programmable Logis Controller | 4 | 189,531.43 | 18-Jan-27 | 25-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **EXTERNAL ELECTRICAL WORKS** | | 56 | 1,711,707.92 | 15-Sep-26 | 01-Dec-26 | | | 891,466.10 | 0.00 | 0.00 |
| DAM3-C-ENV-E-400 | Installation of UPVC Pipe | 5 | 76,356.22 | 15-Sep-26 | 20-Sep-26 | | | 76,356.22 | 0.00 | 0.00 |
| DAM3-C-ENV-E-410 | Construction of Concrete encased duct bank | 8 | 687,205.97 | 21-Sep-26 | 03-Oct-26 | | | 687,205.97 | 0.00 | 0.00 |
| DAM3-C-ENV-E-420 | Installation of Sleeves for lighting poles | 5 | 19,588.78 | 04-Oct-26 | 08-Oct-26 | | | 19,588.78 | 0.00 | 0.00 |
| DAM3-C-ENV-E-390 | Installation of Telecom manhole | 4 | 120,350.16 | 10-Oct-26 | 20-Oct-26 | | | 108,315.14 | 0.00 | 0.00 |
| DAM3-C-ENV-E-450 | Foundation for Lighting poles | 5 | 19,588.78 | 21-Oct-26 | 26-Oct-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-440 | Installation of Lighting poles | 5 | 156,710.21 | 27-Oct-26 | 03-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-430 | Installation of Lighting Fixture | 5 | 39,177.55 | 04-Nov-26 | 09-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-380 | Installation of LV Cables | 7 | 98,914.91 | 10-Nov-26 | 17-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-460 | Electrical Manhole | 7 | 253,329.40 | 18-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-470 | Installation of Earthing and Grounding | 5 | 19,643.55 | 26-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-E-480 | Installation of Street Lighting Feeder pillars & KWH meter | 5 | 220,842.40 | 26-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| **FENCES AND GATES** | | 37 | 14,295.10 | 10-Nov-26 | 10-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1374 | Excavation for Fence | 2 | 597.56 | 10-Nov-26 | 17-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1354 | Vapour Barrier for Fence | 4 | 298.78 | 18-Nov-26 | 22-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1274 | Lean Concrete Below Fence | 4 | 597.56 | 23-Nov-26 | 26-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1304 | Rebar for Footings | 7 | 1,195.12 | 28-Nov-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1314 | Formwork for Footings | 4 | 597.56 | 06-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1284 | Pouring Concrete for Footings | 2 | 1,792.67 | 10-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1344 | Damp proof /Bitumin paint on Footing Sides | 2 | 298.78 | 13-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |

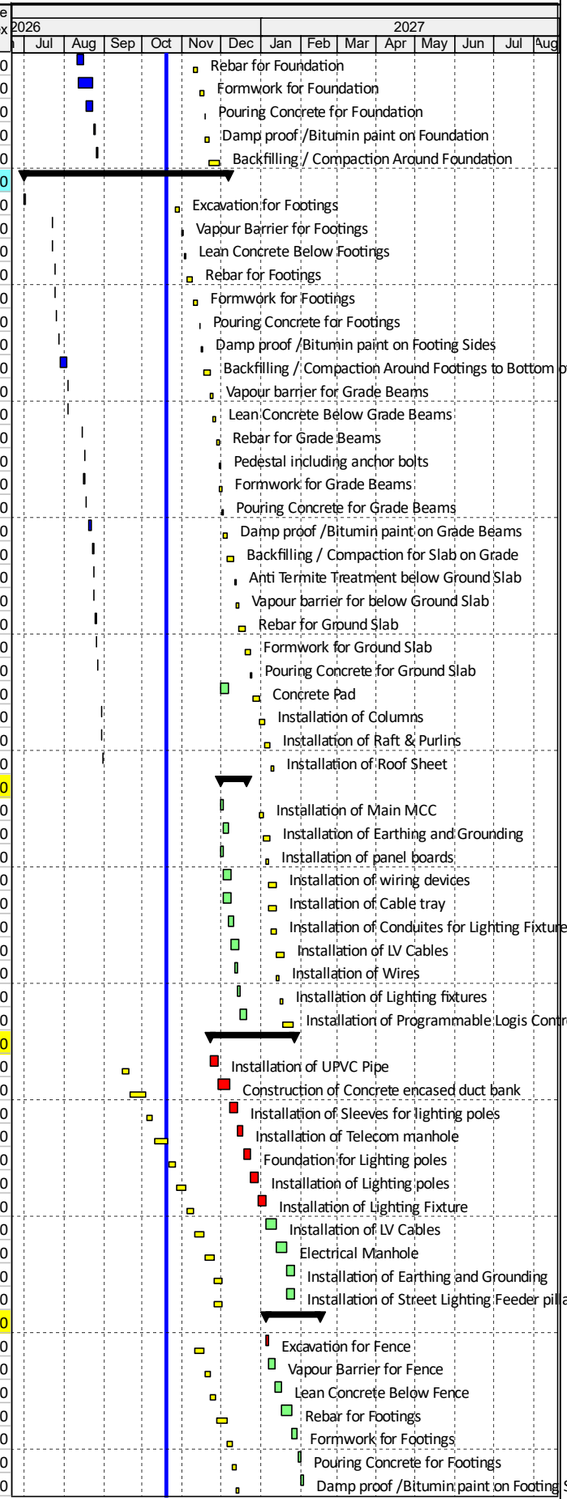




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| DAM3-C-ENV-S-1364 | Backfilling / Compaction Around Footings | 4 | 597.56 | 15-Dec-26 | 22-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1334 | Installation of base plate | 2 | 1,195.12 | 23-Dec-26 | 28-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1324 | Installation of steel members | 2 | 2,390.24 | 29-Dec-26 | 05-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1294 | Installation of steel fence | 2 | 2,390.24 | 06-Jan-27 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-S-1384 | Installation of steel gates | 2 | 2,343.91 | 09-Jan-27 | 10-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **ROAD WORKS** | | 34 | 2,873,764.57 | 23-Nov-26 | 21-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1390 | SubGrade Preparation & Compaction | 5 | 319,796.23 | 23-Nov-26 | 03-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1400 | Aggregate Base Course Layer | 5 | 262,382.32 | 05-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1460 | Curb Stones | 4 | 291,156.54 | 13-Dec-26 | 04-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1480 | Interlock Tiles | 3 | 475,633.54 | 05-Jan-27 | 27-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-890 | Supply and install geotextile sheet | 2 | 47,639.01 | 28-Jan-27 | 30-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1490 | Gravel Bedding | 2 | 57,375.45 | 31-Jan-27 | 01-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1500 | Road Signs | 3 | 103,945.80 | 02-Feb-27 | 07-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1450 | Prime Coat | 1 | 71,708.03 | 08-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1410 | Asphalt Concrete Base Course Layer | 2 | 645,372.33 | 09-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1470 | Tack Coat | 1 | 52,885.08 | 11-Feb-27 | 11-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1420 | Asphalt Concrete Wearing Course Layer | 2 | 475,965.66 | 13-Feb-27 | 14-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1430 | Retroreflective Thermoplastic White Traffic lines | 2 | 37,884.84 | 15-Feb-27 | 16-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1440 | Installation of Concrete wheel bumper | 2 | 32,019.76 | 17-Feb-27 | 21-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **LANDSCAPING** | | 12 | 164,099.55 | 02-Feb-27 | 15-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1510 | Planting of trees | 5 | 110,131.54 | 02-Feb-27 | 07-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-C-ENV-R-1520 | Planting of shrubs | 7 | 53,968.01 | 08-Feb-27 | 15-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **TESTING AND COMMISSIONING (10%)** | | 183 | 9,599,652.50 | 24-May-26 | 18-Feb-27 | 17-Jun-26 | | 7,246,921.51 | 7,280,531.96 | 1.00 |
| **TESTING AND COMMISSIONING 900 Sq.m-2** | | 183 | 1,943,587.85 | 24-May-26 | 18-Feb-27 | 28-Jun-26 | | 63,346.56 | 66,035.08 | 1.04 |
| **MECHANICAL** | | 182 | 617,124.79 | 24-May-26 | 17-Jan-27 | 28-Jun-26 | | 63,346.56 | 66,035.08 | 1.04 |
| P001-C-TC-M-3406 | Testing & Commissioning of Sewer & Drainage Pipes | 7 | 63,346.56 | 24-May-26 | 03-Jun-26 | 28-Jun-26 | 08-Oct-26 | 63,346.56 | 63,346.56 | 1.00 |
| P001-C-TC-M-3416 | Testing and Commissioning of Electric Water Heater | 7 | 2,987.25 | 18-Nov-26 | 26-Nov-26 | 19-Oct-26 | | 0.00 | 2,688.52 | 0.00 |
| P001-C-TC-M-3426 | Testing and Commissioning of Sanitary Fixtures | 7 | 32,707.31 | 23-Nov-26 | 01-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-M3446 | Testing and Commissioning of Exhaust Fan | 7 | 13,737.46 | 26-Nov-26 | 05-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-M-3396 | Testing & Commissioning of Water Supply Pipes | 7 | 38,283.97 | 29-Nov-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-M-3456 | Testing and Commissioning of Wall propeller type exhaust fans | 7 | 76,887.76 | 01-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-M-3376 | Testing and Commissioning of Fire Fighting Pipes | 7 | 118,857.06 | 02-Dec-26 | 10-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-M-3436 | Testing and Commissioning of HVAC Duct | 7 | 245,430.24 | 03-Dec-26 | 12-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-M-3386 | Testing and Commissioning of Fire Hose Cabinet | 3 | 24,887.19 | 10-Jan-27 | 17-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| **ELECTRICAL** | | 28 | 1,326,463.06 | 29-Nov-26 | 18-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3506 | Testing and Commissioning of Wiring Devices | 7 | 33,207.17 | 29-Nov-26 | 07-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3496 | Testing and Commissioning of Fire Alarm System | 2 | 139,733.70 | 07-Dec-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3546 | Testing and Commissioning of Access Control System | 2 | 45,341.12 | 17-Dec-26 | 19-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3456 | Testing and Commissioning of Main Distribution Board | 3 | 53,313.44 | 23-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3446 | Testing and Commissioning of LV cables | 2 | 149,517.23 | 26-Dec-26 | 27-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3486 | Testing and Commissioning of Grounding | 2 | 32,570.63 | 26-Dec-26 | 27-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3526 | Testing and Commissioning of PP-AC panel | 2 | 35,542.28 | 26-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3536 | Testing and Commissioning of Telephone and data system | 2 | 44,313.72 | 28-Dec-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3566 | Testing and Commissioning of CCTV System | 2 | 125,349.49 | 29-Dec-26 | 30-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3466 | Testing and Commissioning of Disconnect Switches | 7 | 50,288.02 | 30-Dec-26 | 06-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3516 | Testing and Commissioning of LP panel board | 2 | 30,214.76 | 31-Dec-26 | 02-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3476 | Testing and Commissioning of Lighting Fixtures | 1 | 171,257.21 | 18-Jan-27 | 18-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| P001-C-TC-E-3556 | Testing and Commissioning of Solar power plant | 2 | 415,814.30 | 17-Feb-27 | 18-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **TESTING AND COMMISSIONING SITE INFRASTRUCTURE** | | 85 | 530,478.84 | 06-Oct-26 | 06-Feb-27 | 13-Oct-26 | | 57,989.14 | 130,687.36 | 2.25 |
| **PUMP ROOM SHED** | | 19 | 306,247.54 | 12-Dec-26 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-M-3596 | Testing & Commissioning of GRP tank | 3 | 104,926.55 | 12-Dec-26 | 14-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-M-3586 | Testing & Commissioning of Booster pump | 7 | 6,462.23 | 31-Dec-26 | 07-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-M-3576 | Testing & Commissioning of Fire Fighting pump | 5 | 51,684.47 | 05-Jan-27 | 10-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-E-3616 | Testing and Commissioning of Panel Board | 2 | 36,675.69 | 07-Jan-27 | 09-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-E-3636 | Testing and Commissioning of Grounding | 5 | 208.86 | 09-Jan-27 | 13-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-E-3646 | Testing and Commissioning of Wiring devices | 2 | 193.73 | 13-Jan-27 | 14-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-E-3626 | Testing and Commissioning of Lighting Fixtures | 2 | 1,429.61 | 18-Jan-27 | 19-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-E-3621 | Testing and Commissioning of LV cables | 3 | 76,378.12 | 19-Jan-27 | 24-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-E-3656 | Testing and Commissioning of Programmable Logic Controller | 2 | 28,288.27 | 26-Jan-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **EXTERNAL** | | 26 | 52,779.67 | 18-Nov-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-EX-E-3626 | Testing and Commissioning of LV cables | 7 | 14,763.42 | 18-Nov-26 | 25-Nov-26 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-EX-E-3646 | Testing and Commissioning of Street Lighting pole | 15 | 35,084.37 | 22-Nov-26 | 08-Dec-26 | | | 0.00 | 0.00 | 0.00 |

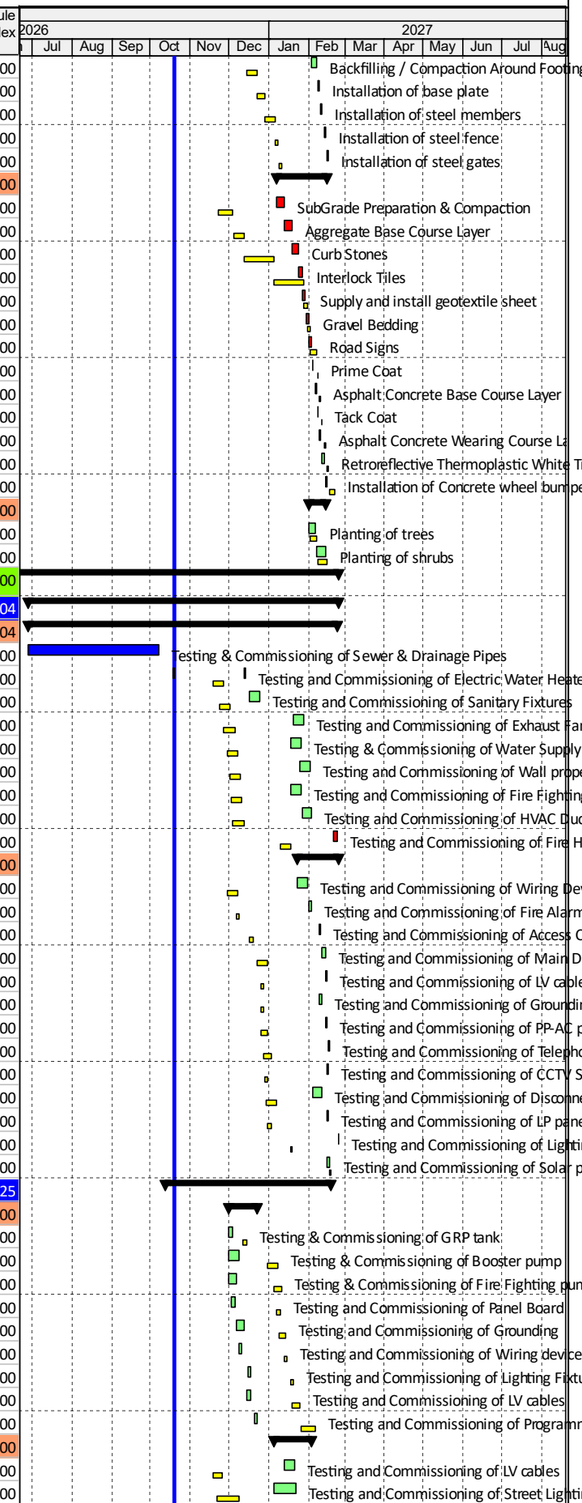


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone




TASK filter: All Activities

© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| S001-C-TC-EX-E-3656 | Testing and Commissioning of Grounding | 7 | 2,931.87 | 02-Dec-26 | 09-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| ENVIRONMENTAL | | 85 | 171,451.64 | 06-Oct-26 | 19-Jan-27 | 13-Oct-26 | | 57,989.14 | 130,687.36 | 2.25 |
| S001-C-TC-ENV-F-1051 | Testing & Commissioning of External Fire Fighting System 200 Dia | 15 | 72,486.43 | 06-Oct-26 | 22-Oct-26 | 13-Oct-26 | | 57,989.14 | 65,237.78 | 1.13 |
| S001-C-TC-ENV-WS-11 | Testing & Commissioning of Water Supply System | 15 | 5,327.52 | 22-Nov-26 | 08-Dec-26 | 19-Oct-26 | | 0.00 | 4,794.77 | 0.00 |
| S001-C-TC-ENV-SW-70 | Testing & Commissioning of Irrigaiton System | 15 | 11,300.41 | 15-Dec-26 | 31-Dec-26 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-ENV-3666 | Testing and Commissioning of Main program system & controller | 10 | 14,943.05 | 23-Dec-26 | 09-Jan-27 | | | 0.00 | 0.00 | 0.00 |
| S001-C-TC-ENV-SW-60 | Testing & Commissioning of Sewer & Drainage System | 3 | 67,394.23 | 03-Jan-27 | 19-Jan-27 | 13-Oct-26 | | 0.00 | 60,654.81 | 0.00 |
| SNAGG WORKS | | 79 | 7,125,585.81 | 10-Jun-26 | 16-Jul-26 | 17-Jun-26 | | 7,125,585.81 | 7,083,809.52 | 0.99 |
| S001-C-TC-M-100 | Mechanical Snagg works | 5 | 1,206,604.05 | 10-Jun-26 | 15-Jun-26 | 05-Jul-26 | 06-Jul-26 | 1,206,604.05 | 1,206,604.05 | 1.00 |
| S001-C-TC-E-3676 | External Snagg works | 5 | 3,231,301.32 | 02-Jul-26 | 07-Jul-26 | 22-Jun-26 | 05-Jul-26 | 3,231,301.32 | 3,231,301.32 | 1.00 |
| S001-C-TC-C-80 | Civil & Architectural Snagg works-1 | 5 | 1,520,575.29 | 05-Jul-26 | 11-Jul-26 | 17-Jun-26 | 20-Jun-26 | 1,520,575.29 | 1,520,575.29 | 1.00 |
| S001-C-TC-E-3606 | Electrical Snagg works | 5 | 167,105.15 | 08-Jul-26 | 13-Jul-26 | 05-Jul-26 | | 167,105.15 | 125,328.86 | 0.75 |
| S001-C-TC-A-90 | Civil & Architectural Snagg works-2 | 5 | 1,000,000.00 | 11-Jul-26 | 16-Jul-26 | 21-Jun-26 | 22-Jun-26 | 1,000,000.00 | 1,000,000.00 | 1.00 |
| PREOJECT CLOSEOUT | | 25 | 0.00 | 02-Feb-27 | 06-Mar-27 | | | 0.00 | 0.00 | 0.00 |
| ENGINEERING | | 8 | 0.00 | 02-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| AS BUILT DRAWINGS | | 6 | 0.00 | 02-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| CIVIL DRAWINGS | | 2 | 0.00 | 02-Feb-27 | 03-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 02-Feb-27 | 03-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1010 | Civil drawings | 2 | 0.00 | 02-Feb-27 | 03-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVALS | | 2 | 0.00 | 02-Feb-27 | 03-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1053 | Civil drawings | 2 | 0.00 | 02-Feb-27 | 03-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| ARCHITECTURAL DRAWINGS | | 4 | 0.00 | 04-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1011 | Architectural drawings | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVALS | | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1023 | Architectural drawings | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| MECHANICAL DRAWINGS | | 4 | 0.00 | 04-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1013 | Mechanical drawings | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVALS | | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1033 | Mechanical drawings | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| ELECTRICAL DRAWINGS | | 4 | 0.00 | 04-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1012 | Electrical drawings | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVALS | | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1043 | Electrical drawings | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| EXTERNAL WORKS DRAWINGS | | 4 | 0.00 | 04-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1054 | External works drawings | 2 | 0.00 | 04-Feb-27 | 06-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVALS | | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-AB-1055 | External works drawings | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| WARRANTIES AND GUARANTEES | | 4 | 0.00 | 07-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| SYSTEM | | 4 | 0.00 | 07-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1010 | Warraties and Guarantees For Mechanical Equipments | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1011 | Warraties and Guarantees For Electrical Systems | 2 | 0.00 | 07-Feb-27 | 08-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVAL | | 2 | 0.00 | 09-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1012 | Warraties and Guarantees For Mechanical Equipments | 2 | 0.00 | 09-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1013 | Warraties and Guarantees For Electrical Systems | 2 | 0.00 | 09-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| TRAINING AND MANUALS | | 10 | 0.00 | 11-Feb-27 | 23-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| TRAINING | | 6 | 0.00 | 11-Feb-27 | 17-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| SYSTEM | | 6 | 0.00 | 11-Feb-27 | 17-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| PREPARATION AND SUBMITTALS | | 2 | 0.00 | 11-Feb-27 | 13-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1014 | The Proposed Coursework For Mechanical Equipment | 2 | 0.00 | 11-Feb-27 | 13-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1015 | The Proposed Coursework For Electircal systems | 2 | 0.00 | 11-Feb-27 | 13-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| REVIEW AND APPROVAL | | 2 | 0.00 | 14-Feb-27 | 15-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1016 | The Proposed Coursework For Mechanical Equipment | 2 | 0.00 | 14-Feb-27 | 15-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1017 | The Proposed Coursework For Electircal systems | 2 | 0.00 | 14-Feb-27 | 15-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DELIVERY | | 2 | 0.00 | 16-Feb-27 | 17-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1018 | The Proposed Coursework For Mechanical Equipment | 2 | 0.00 | 16-Feb-27 | 17-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1019 | The Proposed Coursework For Electircal systems | 2 | 0.00 | 16-Feb-27 | 17-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| MANUALS | | 4 | 0.00 | 18-Feb-27 | 23-Feb-27 | | | 0.00 | 0.00 | 0.00 |

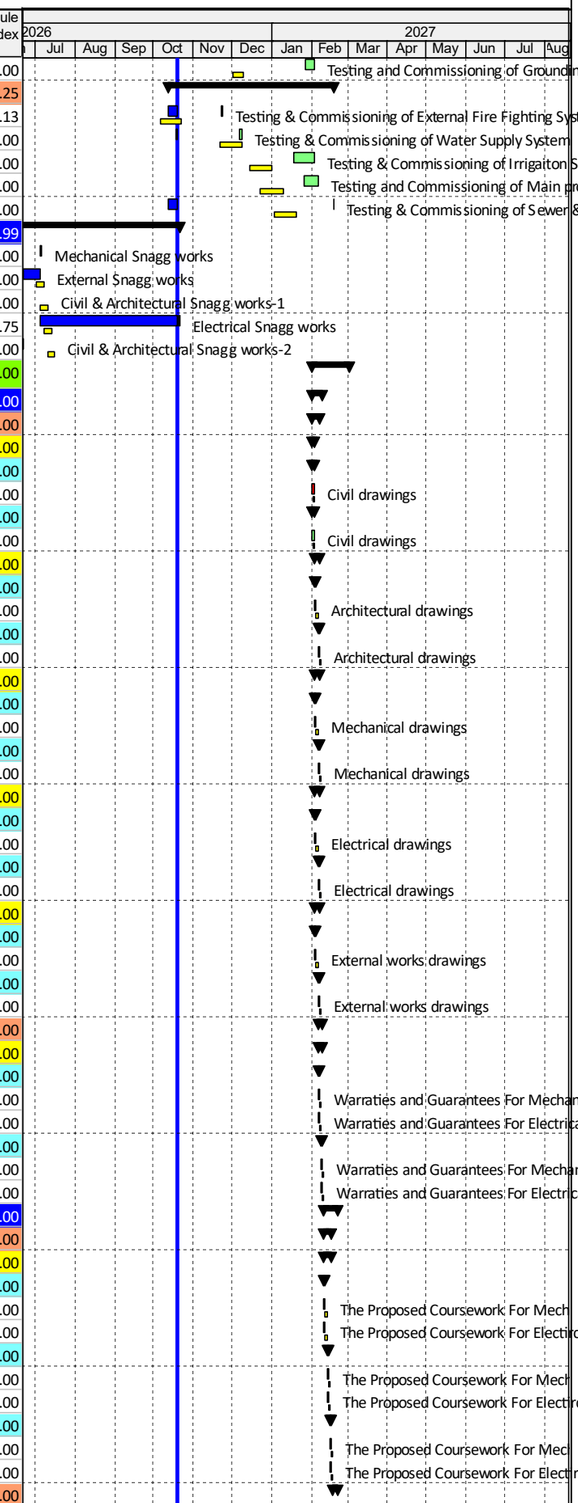




© Oracle Corporation

# 44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

| Activity ID | Activity Name | Original Duration | Budgeted Total Cost | BL Project Start | BL Project Finish | Actual Start | Actual Finish | Planned Value Cost | Earned Value Cost | Schedule Performance Index |
|---|---|---|---|---|---|---|---|---|---|---|
| **SYSTEM** | | 4 | 0.00 | 18-Feb-27 | 23-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **PREPARATION AND SUBMITTALS** | | 2 | 0.00 | 18-Feb-27 | 20-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1020 | Manual and Catalogue For Mechanical Equipment | 2 | 0.00 | 18-Feb-27 | 20-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1021 | Manual and Catalogue For For Electircal systems | 2 | 0.00 | 18-Feb-27 | 20-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **REVIEW AND APPROVAL** | | 2 | 0.00 | 21-Feb-27 | 23-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1022 | Manual and Catalogue For Mechanical Equipment | 2 | 0.00 | 21-Feb-27 | 23-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-WG-1023 | Manual and Catalogue For For Electircal systems | 2 | 0.00 | 21-Feb-27 | 23-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **DEMOBILIZATION** | | 13 | 0.00 | 09-Feb-27 | 24-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-D.MOB-1013 | Demobilization of manpower | 2 | 0.00 | 09-Feb-27 | 10-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-D.MOB-1020 | Demobilization of equipment | 2 | 0.00 | 11-Feb-27 | 13-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-D.MOB-1010 | Dismantling and removal offices | 1 | 0.00 | 24-Feb-27 | 24-Feb-27 | | | 0.00 | 0.00 | 0.00 |
| **FINAL HANDOVER** | | 5 | 0.00 | 23-Feb-27 | 06-Mar-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-FH-1000 | Snag List Rectification | 3 | 0.00 | 23-Feb-27 | 03-Mar-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-FH-1010 | Handover Letter | 1 | 0.00 | 04-Mar-27 | 04-Mar-27 | | | 0.00 | 0.00 | 0.00 |
| DAM3-FH-1020 | Intial Handingover | 1 | 0.00 | 06-Mar-27 | 06-Mar-27 | | | 0.00 | 0.00 | 0.00 |

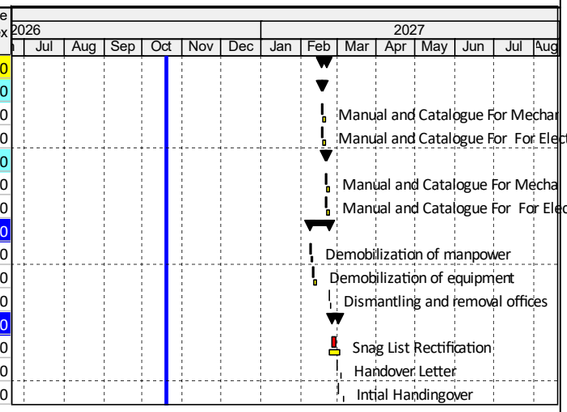



© Oracle Corporation
