

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		114	12-Feb-26	06-Mar-27	09-Jun-26 A	02-Mar-27	131
PROJECT MILESTONES		114	12-Feb-26	06-Mar-27	20-Oct-26	02-Mar-27	2
CONTRACTUAL MILESTONES		114	12-Feb-26	06-Mar-27	20-Oct-26	02-Mar-27	2
DAM3-PMS-MMS-0100	Project Completion Date	0		06-Mar-27		02-Mar-27	1
DAM3-PMS-MMS-0070	Completion of Site levelling, local roads & parkings	0		12-Feb-26		20-Oct-26	1
CONSTRUCTION (67%)		108	06-Jun-26	07-Feb-27	09-Jun-26 A	23-Feb-27	103
RBF 900 SQM FACTORIES		108	06-Jun-26	13-Jan-27	09-Jun-26 A	23-Feb-27	87
BLOCK B6		76	06-Jun-26	23-Nov-26	09-Jun-26 A	17-Jan-27	34
STRUCTURAL STEEL		7	06-Jun-26	21-Jun-26	20-Oct-26	27-Oct-26	2
DAM3-C-B6-SS-1040	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	20-Oct-26	27-Oct-26	1
DAM3-C-B6-SS-1060	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	20-Oct-26	25-Oct-26	1
ARCHITECTURAL		61	07-Jul-26	03-Nov-26	28-Oct-26	06-Jan-27	21
WALL FINISHES		7	29-Sep-26	06-Oct-26	07-Dec-26	14-Dec-26	1
DAM3-C-B6-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	29-Sep-26	06-Oct-26	07-Dec-26	14-Dec-26	1
CIELING FINISHES		5	20-Sep-26	26-Sep-26	29-Nov-26	03-Dec-26	1
DAM3-C-B6-A-690	Installation of Ceiling Gypsum Board	5	20-Sep-26	26-Sep-26	29-Nov-26	03-Dec-26	1
FLOOR FINISHES		41	13-Aug-26	03-Nov-26	21-Nov-26	06-Jan-27	4
DAM3-C-B6-A-670	Tiles for Toilet	7	13-Aug-26	20-Aug-26	21-Nov-26	28-Nov-26	1
DAM3-C-B6-A-700	Tiles for Office Area	2	27-Sep-26	28-Sep-26	05-Dec-26	06-Dec-26	1
DAM3-C-B6-A-830	Granite strip	2	29-Sep-26	30-Sep-26	07-Dec-26	08-Dec-26	1
DAM3-C-B6-A-850	Epoxy paint	5	27-Oct-26	03-Nov-26	02-Jan-27	06-Jan-27	1
DOORS & WINDOWS		16	07-Jul-26	08-Aug-26	28-Oct-26	15-Nov-26	8
DAM3-C-B6-A-640	Roll up Shutter Door	1	15-Jul-26	15-Jul-26	05-Nov-26	05-Nov-26	1
DAM3-C-B6-A-650	Supply and install (D5) 1000*2200mm single leaf steel door v	1	16-Jul-26	16-Jul-26	07-Nov-26	07-Nov-26	1
DAM3-C-B6-A-710	Supply and install (D4) 800*2200 mm single leaf aluminum dc	1	18-Jul-26	18-Jul-26	08-Nov-26	08-Nov-26	1
DAM3-C-B6-A-720	Supply and install (D7) 1000*2200 mm single leaf aluminum c	1	19-Jul-26	19-Jul-26	09-Nov-26	09-Nov-26	1
DAM3-C-B6-A-940	Supply and install (D3) 1000*2200 mm single leaf aluminum c	1	20-Jul-26	20-Jul-26	10-Nov-26	10-Nov-26	1
DAM3-C-B6-A-950	Supply and install fire rated 45 min (D2) 1200*2200 mm singl	1	30-Jul-26	30-Jul-26	11-Nov-26	11-Nov-26	1
DAM3-C-B6-A-960	Skylight fixtures installation	3	01-Aug-26	08-Aug-26	12-Nov-26	15-Nov-26	1
DAM3-C-B6-A-1010	Window (CW1)	7	07-Jul-26	14-Jul-26	28-Oct-26	04-Nov-26	1
WATER PROOFING WORKS		4	09-Aug-26	12-Aug-26	16-Nov-26	19-Nov-26	1
DAM3-C-B6-A-810	Waterproofing membrane for toilets	4	09-Aug-26	12-Aug-26	16-Nov-26	19-Nov-26	1
METAL WORKS		11	01-Oct-26	13-Oct-26	09-Dec-26	21-Dec-26	3
DAM3-C-B6-A-740	Steel Ladder	2	01-Oct-26	03-Oct-26	09-Dec-26	10-Dec-26	1
DAM3-C-B6-A-760	Aluminium composite panel	5	08-Oct-26	13-Oct-26	16-Dec-26	21-Dec-26	1
DAM3-C-B6-A-840	Steel railing works	4	04-Oct-26	07-Oct-26	12-Dec-26	15-Dec-26	1
SPECIALTIES		9	17-Oct-26	26-Oct-26	22-Dec-26	31-Dec-26	3
DAM3-C-B6-A-770	Installation of fittings	5	17-Oct-26	21-Oct-26	22-Dec-26	27-Dec-26	1
DAM3-C-B6-A-790	Furniture Installation	1	26-Oct-26	26-Oct-26	31-Dec-26	31-Dec-26	1
DAM3-C-B6-A-1000	Identification sign; ID01 & ID02	3	22-Oct-26	25-Oct-26	28-Dec-26	30-Dec-26	1
ELECTRICAL		47	07-Oct-26	23-Nov-26	09-Jun-26 A	17-Jan-27	11
FIRST STAGE		43	14-Oct-26	05-Nov-26	09-Jun-26 A	06-Jan-27	3
DAM3-C-B6-E-463	Installation of Wires	4	02-Nov-26	05-Nov-26	02-Jan-27	06-Jan-27	1
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm System	4	14-Oct-26	18-Oct-26	09-Jun-26 A	23-Dec-26	1
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	01-Oct-26 A	02-Jan-27	1
SECOND STAGE		28	07-Oct-26	23-Nov-26	15-Dec-26	17-Jan-27	8
DAM3-C-B6-E-353	Installation of Fire Alarm Control Panel	3	19-Oct-26	22-Oct-26	24-Dec-26	27-Dec-26	1
DAM3-C-B6-E-363	Installation of Fire Detectors & Accessories	4	24-Oct-26	27-Oct-26	28-Dec-26	31-Dec-26	1

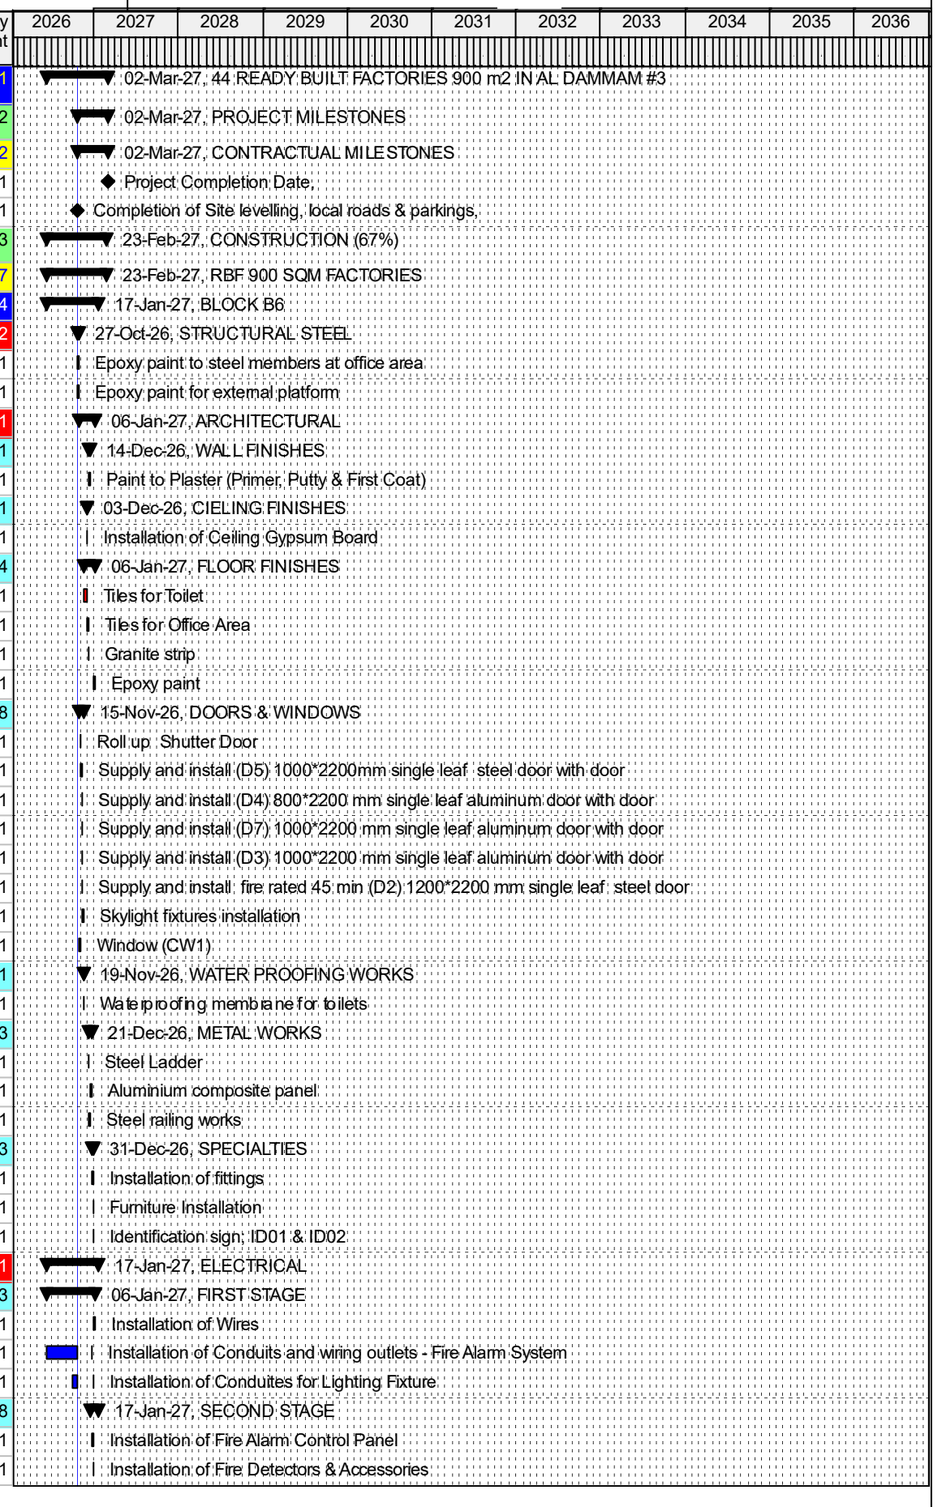

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-26	WEEKLY REPORT#34		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
DAM3-C-B6-E-383	Installation of Lighting fixtures	2	07-Nov-26	10-Nov-26	06-Jan-27	09-Jan-27	1
DAM3-C-B6-E-403	Installation of Wiring Devices	4	07-Oct-26	11-Oct-26	15-Dec-26	19-Dec-26	1
DAM3-C-B6-E-423	Installation of Main Distribution Board	2	11-Nov-26	12-Nov-26	09-Jan-27	11-Jan-27	1
DAM3-C-B6-E-433	Installation of Disconnect Switches	2	12-Oct-26	13-Oct-26	20-Dec-26	21-Dec-26	1
DAM3-C-B6-E-720	Installation of CCTV System	3	18-Nov-26	23-Nov-26	13-Jan-27	17-Jan-27	1
DAM3-C-B6-E-483	Installation of PP-AC panel	2	16-Nov-26	17-Nov-26	11-Jan-27	13-Jan-27	1
BLOCK B5		7	14-Jun-26	21-Jun-26	20-Oct-26	27-Oct-26	1
STRUCTURAL STEEL		7	14-Jun-26	21-Jun-26	20-Oct-26	27-Oct-26	1
DAM3-C-B5-SS-1020	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	20-Oct-26	27-Oct-26	1
BLOCK B4		22	28-Jun-26	14-Sep-26	28-Oct-26	22-Nov-26	5
STRUCTURAL		7	14-Jul-26	21-Jul-26	05-Nov-26	12-Nov-26	1
SLAB ON GRADE		7	14-Jul-26	21-Jul-26	05-Nov-26	12-Nov-26	1
DAM3-C-B4-S-1017	Concrete pad	7	14-Jul-26	21-Jul-26	05-Nov-26	12-Nov-26	1
STRUCTURAL STEEL		7	28-Jun-26	05-Jul-26	28-Oct-26	04-Nov-26	1
DAM3-C-B4-SS-1020	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	28-Oct-26	04-Nov-26	1
MECHANICAL		8	31-Aug-26	14-Sep-26	14-Nov-26	22-Nov-26	3
SEWER AND DRAINAGE SYSTEM		8	31-Aug-26	14-Sep-26	14-Nov-26	22-Nov-26	3
FIRST STAGE		2	31-Aug-26	01-Sep-26	14-Nov-26	15-Nov-26	1
DAM3-C-B4-M-840	Installation of Floor Drain	2	31-Aug-26	01-Sep-26	14-Nov-26	15-Nov-26	1
SECOND STAGE		6	08-Sep-26	14-Sep-26	16-Nov-26	22-Nov-26	2
DAM3-C-B4-M-800	Installation of Electric Water Heater	2	08-Sep-26	09-Sep-26	16-Nov-26	17-Nov-26	1
DAM3-C-B4-M-810	Installation of Sanitary Fixture and Accessories	4	10-Sep-26	14-Sep-26	18-Nov-26	22-Nov-26	1
BLOCK B3		34	04-Nov-26	27-Dec-26	21-Jul-26 A	15-Feb-27	31
ARCHITECTURAL		30	04-Nov-26	20-Dec-26	07-Jan-27	10-Feb-27	11
WALL FINISHES		2	12-Nov-26	19-Nov-26	16-Jan-27	17-Jan-27	1
DAM3-C-B3-A-1090	Paint to Plaster (Primer, Putty & First Coat)	2	12-Nov-26	19-Nov-26	16-Jan-27	17-Jan-27	1
CIELING FINISHES		5	04-Nov-26	09-Nov-26	07-Jan-27	12-Jan-27	1
DAM3-C-B3-A-1100	Installation of Ceiling Gypsum Board	5	04-Nov-26	09-Nov-26	07-Jan-27	12-Jan-27	1
FLOOR FINISHES		25	10-Nov-26	20-Dec-26	13-Jan-27	10-Feb-27	3
DAM3-C-B3-A-1110	Tiles for Office Area	2	10-Nov-26	11-Nov-26	13-Jan-27	14-Jan-27	1
DAM3-C-B3-A-1240	Granite strip	2	12-Nov-26	14-Nov-26	16-Jan-27	17-Jan-27	1
DAM3-C-B3-A-1260	Epoxy paint	3	13-Dec-26	20-Dec-26	08-Feb-27	10-Feb-27	1
METAL WORKS		11	15-Nov-26	26-Nov-26	18-Jan-27	30-Jan-27	3
DAM3-C-B3-A-1150	Steel Ladder	2	15-Nov-26	16-Nov-26	18-Jan-27	19-Jan-27	1
DAM3-C-B3-A-1170	Aluminium composite panel	5	22-Nov-26	26-Nov-26	25-Jan-27	30-Jan-27	1
DAM3-C-B3-A-1250	Steel railing works	4	17-Nov-26	21-Nov-26	20-Jan-27	24-Jan-27	1
SPECIALTIES		7	30-Nov-26	12-Dec-26	31-Jan-27	07-Feb-27	3
DAM3-C-B3-A-1180	Installation of fittings	3	30-Nov-26	07-Dec-26	31-Jan-27	02-Feb-27	1
DAM3-C-B3-A-1200	Furniture Installation	1	12-Dec-26	12-Dec-26	07-Feb-27	07-Feb-27	1
DAM3-C-B3-A-1410	Identification sign; ID01 & ID02	3	08-Dec-26	10-Dec-26	03-Feb-27	06-Feb-27	1
MECHANICAL		17	21-Nov-26	09-Dec-26	18-Jan-27	06-Feb-27	7
HVAC		14	21-Nov-26	06-Dec-26	18-Jan-27	02-Feb-27	6
FIRST STAGE		4	28-Nov-26	01-Dec-26	25-Jan-27	28-Jan-27	2
DAM3-C-B3-M-760	Installation of HVAC Ducts	2	28-Nov-26	29-Nov-26	25-Jan-27	26-Jan-27	1
DAM3-C-B3-M-790	Installation of Duct insulation	2	30-Nov-26	01-Dec-26	27-Jan-27	28-Jan-27	1
SECOND STAGE		14	21-Nov-26	06-Dec-26	18-Jan-27	02-Feb-27	4
DAM3-C-B3-M-750	Installation of Exhaust Fans	2	21-Nov-26	22-Nov-26	18-Jan-27	19-Jan-27	1
DAM3-C-B3-M-770	Installation of Diffuser	2	02-Dec-26	03-Dec-26	30-Jan-27	31-Jan-27	1
DAM3-C-B3-M-780	Installation of Wall Propeller Type Exhaust Fan	4	23-Nov-26	26-Nov-26	20-Jan-27	24-Jan-27	1

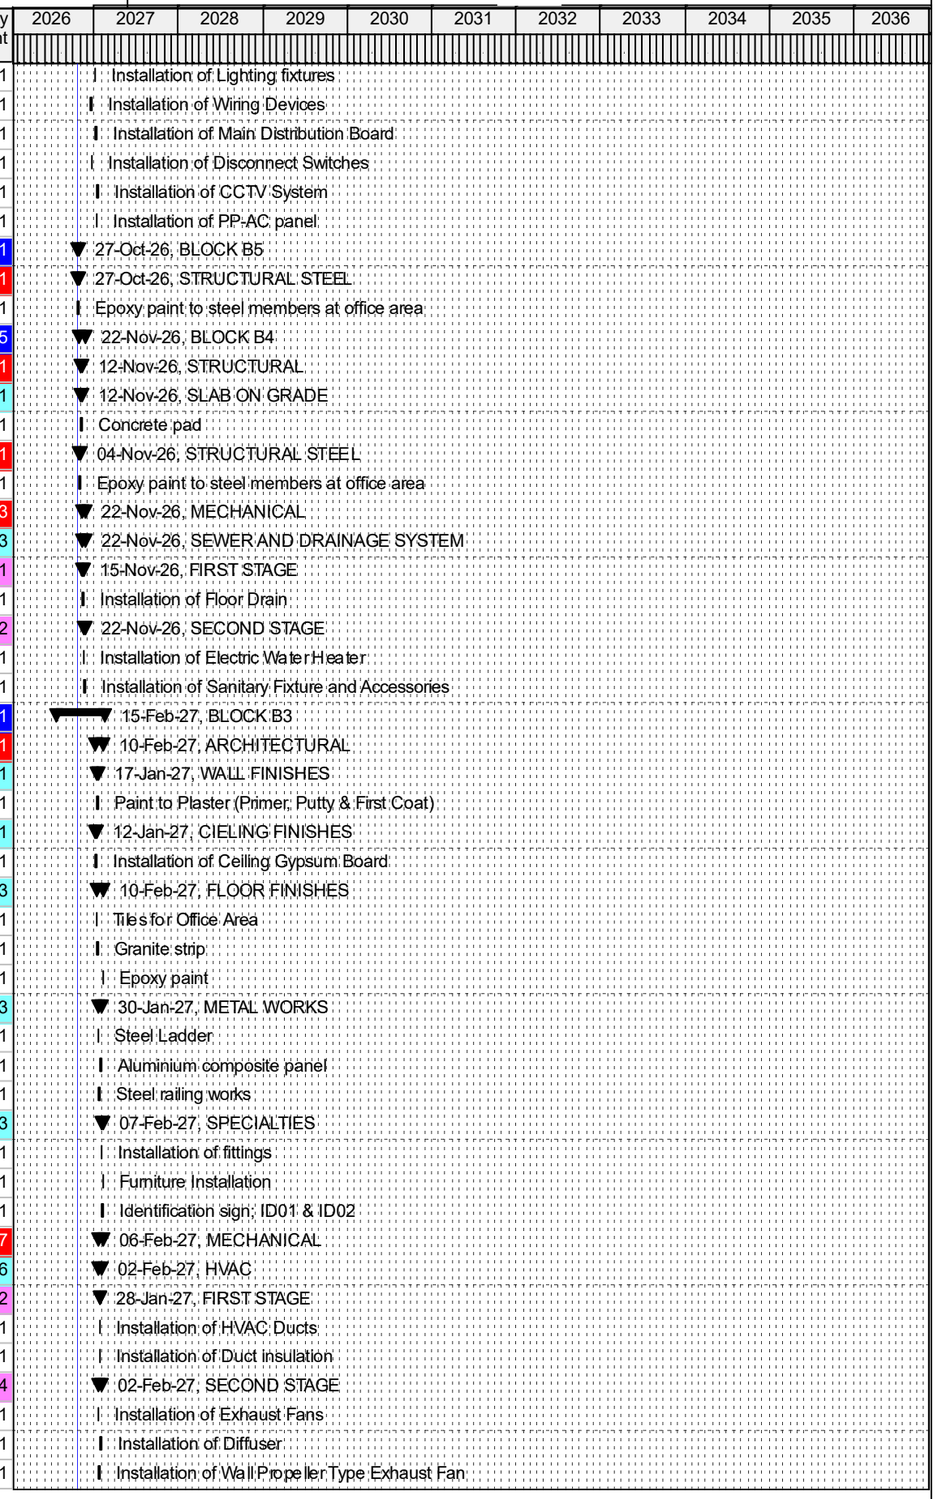

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-26	WEEKLY REPORT#34		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
DAM3-C-B3-M-960	Supply, install, test and commission door grilles & exhaust lou	2	05-Dec-26	06-Dec-26	01-Feb-27	02-Feb-27	1
FIRE FIGHTING SYSTEM		3	07-Dec-26	09-Dec-26	03-Feb-27	06-Feb-27	1
SECOND STAGE		3	07-Dec-26	09-Dec-26	03-Feb-27	06-Feb-27	1
DAM3-C-B3-M-990	Supply, install, test and commission Fire Department Connect	3	07-Dec-26	09-Dec-26	03-Feb-27	06-Feb-27	1
ELECTRICAL		28	21-Nov-26	27-Dec-26	21-Jul-26 A	15-Feb-27	13
FIRST STAGE		22	28-Nov-26	20-Dec-26	21-Jul-26 A	08-Feb-27	2
DAM3-C-B3-E-693	Installation of Wires	2	16-Dec-26	20-Dec-26	07-Feb-27	08-Feb-27	1
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	28-Nov-26	01-Dec-26	21-Jul-26 A	26-Jan-27	1
SECOND STAGE		25	21-Nov-26	27-Dec-26	18-Jan-27	15-Feb-27	11
DAM3-C-B3-E-583	Installation of Fire Alarm Control Panel	4	02-Dec-26	06-Dec-26	27-Jan-27	31-Jan-27	1
DAM3-C-B3-E-593	Installation of Fire Detectors & Accessories	4	07-Dec-26	10-Dec-26	01-Feb-27	04-Feb-27	1
DAM3-C-B3-E-633	Installation of Wiring Devices	4	21-Nov-26	24-Nov-26	18-Jan-27	21-Jan-27	1
DAM3-C-B3-E-653	Installation of Main Distribution Board	2	21-Dec-26	22-Dec-26	09-Feb-27	10-Feb-27	1
DAM3-C-B3-E-663	Installation of Disconnect Switches	2	25-Nov-26	26-Nov-26	23-Jan-27	24-Jan-27	1
DAM3-C-B3-E-673	Installation of Telephone Cabinet	2	26-Dec-26	27-Dec-26	14-Feb-27	15-Feb-27	1
DAM3-C-B3-E-713	Installation of PP-AC panel	2	23-Dec-26	24-Dec-26	11-Feb-27	13-Feb-27	1
DAM3-C-B3-E-733	Installation of Access Control System	3	12-Dec-26	16-Dec-26	06-Feb-27	08-Feb-27	1
DAM3-C-B3-E-743	Monitor Modules for Fire Alarm	2	17-Dec-26	19-Dec-26	09-Feb-27	10-Feb-27	1
DAM3-C-B3-E-753	Line Isolator Modules for Fire Alarm	2	20-Dec-26	21-Dec-26	11-Feb-27	13-Feb-27	1
DAM3-C-B3-E-763	Firewarning flash light with sounder; wall mounted, Weather pr	2	22-Dec-26	23-Dec-26	14-Feb-27	15-Feb-27	1
BLOCK B2		4	21-Dec-26	02-Jan-27	11-Feb-27	15-Feb-27	2
ARCHITECTURAL		4	21-Dec-26	02-Jan-27	11-Feb-27	15-Feb-27	2
FLOOR FINISHES		3	22-Dec-26	02-Jan-27	13-Feb-27	15-Feb-27	1
DAM3-C-B2-A-420	Epoxy paint	3	22-Dec-26	02-Jan-27	13-Feb-27	15-Feb-27	1
SPECIALTIES		1	21-Dec-26	21-Dec-26	11-Feb-27	11-Feb-27	1
DAM3-C-B2-A-340	Furniture Installation	1	21-Dec-26	21-Dec-26	11-Feb-27	11-Feb-27	1
BLOCK B1		20	26-Nov-26	26-Dec-26	17-Jan-27	09-Feb-27	9
ARCHITECTURAL		5	26-Nov-26	06-Dec-26	17-Jan-27	23-Jan-27	2
WALL FINISHES		3	29-Nov-26	06-Dec-26	19-Jan-27	23-Jan-27	1
DAM3-C-B1-A-230	Paint to Plaster (Primer, Putty & First Coat)	3	29-Nov-26	06-Dec-26	19-Jan-27	23-Jan-27	1
FLOOR FINISHES		2	26-Nov-26	28-Nov-26	17-Jan-27	19-Jan-27	1
DAM3-C-B1-A-250	Tiles for Office Area	2	26-Nov-26	28-Nov-26	17-Jan-27	19-Jan-27	1
MECHANICAL		15	07-Dec-26	26-Dec-26	23-Jan-27	09-Feb-27	7
HVAC		12	07-Dec-26	22-Dec-26	23-Jan-27	06-Feb-27	6
FIRST STAGE		4	14-Dec-26	17-Dec-26	27-Jan-27	01-Feb-27	2
DAM3-C-B1-M-140	Installation of HVAC Ducts	2	14-Dec-26	15-Dec-26	27-Jan-27	30-Jan-27	1
DAM3-C-B1-M-170	Installation of Duct insulation	2	16-Dec-26	17-Dec-26	30-Jan-27	01-Feb-27	1
SECOND STAGE		12	07-Dec-26	22-Dec-26	23-Jan-27	06-Feb-27	4
DAM3-C-B1-M-130	Installation of Exhaust Fans	2	07-Dec-26	08-Dec-26	23-Jan-27	25-Jan-27	1
DAM3-C-B1-M-339	Installation of Diffuser	2	19-Dec-26	20-Dec-26	01-Feb-27	03-Feb-27	1
DAM3-C-B1-M-160	Installation of Wall Propeller Type Exhaust Fan	2	09-Dec-26	13-Dec-26	25-Jan-27	27-Jan-27	1
DAM3-C-B1-M-340	Supply, install, test and commission door grilles & exhaust lou	2	21-Dec-26	22-Dec-26	03-Feb-27	06-Feb-27	1
FIRE FIGHTING SYSTEM		3	23-Dec-26	26-Dec-26	06-Feb-27	09-Feb-27	1
SECOND STAGE		3	23-Dec-26	26-Dec-26	06-Feb-27	09-Feb-27	1
DAM3-C-B1-M-370	Supply, install, test and commission Fire Department Connect	3	23-Dec-26	26-Dec-26	06-Feb-27	09-Feb-27	1
BLOCK B8		9	27-Dec-26	13-Jan-27	13-Feb-27	23-Feb-27	5
ARCHITECTURAL		9	27-Dec-26	13-Jan-27	13-Feb-27	23-Feb-27	4
FLOOR FINISHES		2	06-Jan-27	13-Jan-27	21-Feb-27	23-Feb-27	1
DAM3-C-B8-A-420	Epoxy paint	2	06-Jan-27	13-Jan-27	21-Feb-27	23-Feb-27	1

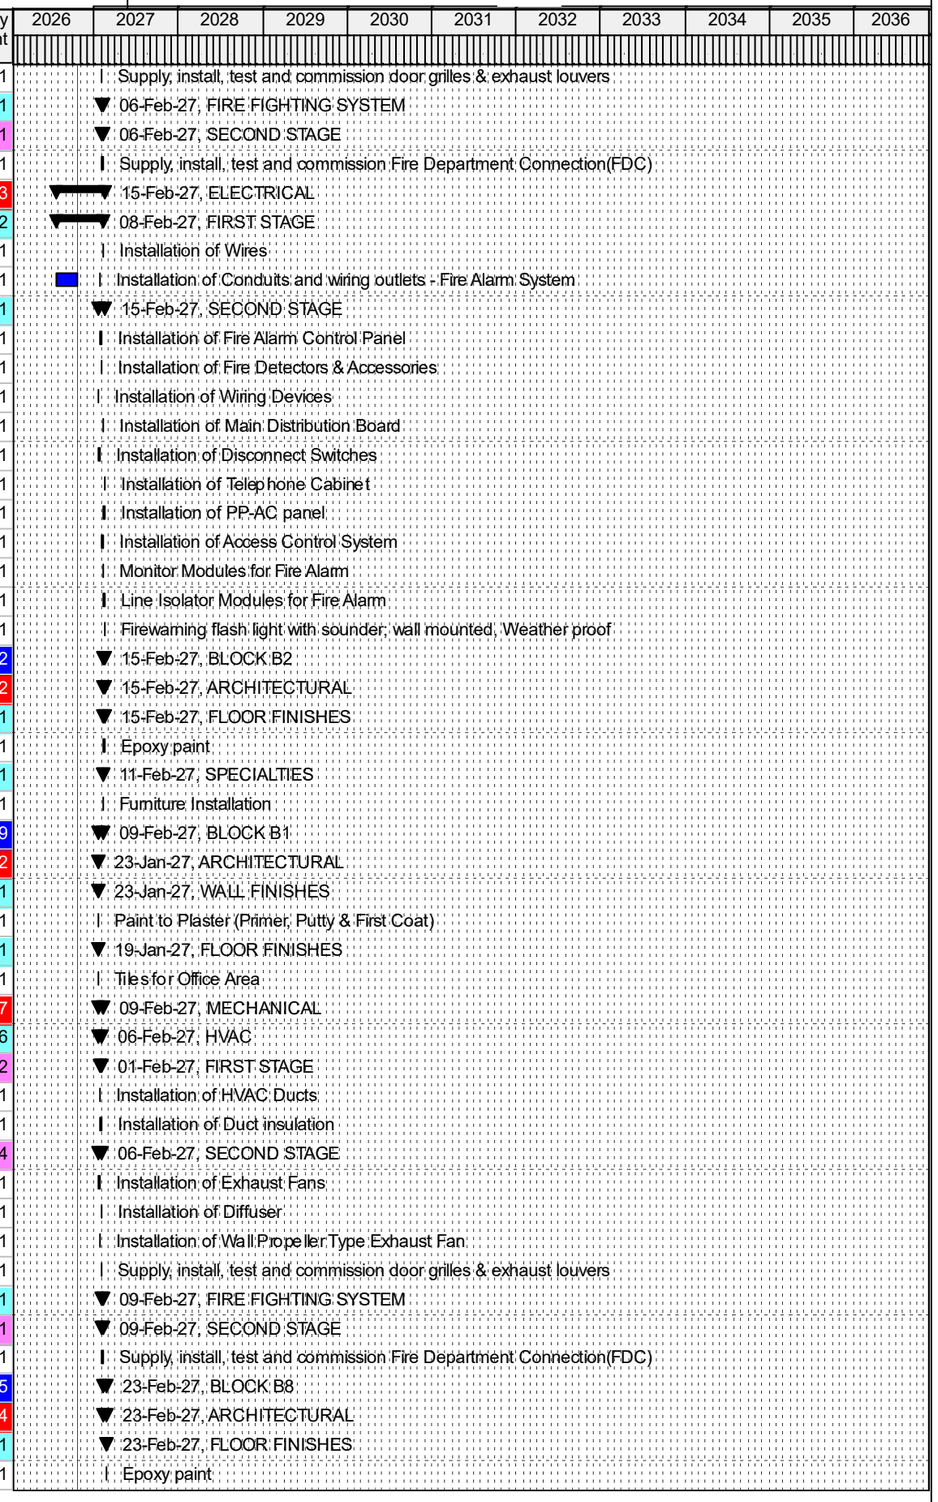

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-26	WEEKLY REPORT#34		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
SPECIALTIES		7	27-Dec-26	05-Jan-27	13-Feb-27	20-Feb-27	3
DAM3-C-B8-A-320	Installation of fittings	3	27-Dec-26	31-Dec-26	13-Feb-27	15-Feb-27	1
DAM3-C-B8-A-340	Furniture Installation	1	05-Jan-27	05-Jan-27	20-Feb-27	20-Feb-27	1
DAM3-C-B8-A-570	Identification sign; ID01 & ID02	3	02-Jan-27	04-Jan-27	16-Feb-27	18-Feb-27	1
MECHANICAL		3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
FIRE FIGHTING SYSTEM		3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
SECOND STAGE		3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
DAM3-C-B8-M-320	Installation of Fire Hose Cabinet	3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
SITE INFRASTRUCTURE		64	15-Sep-26	07-Feb-27	12-Oct-26 A	03-Feb-27	16
NETWORKS		7	15-Sep-26	22-Sep-26	12-Oct-26 A	26-Nov-26	1
WATER SUPPLY SYSTEM		7	15-Sep-26	22-Sep-26	12-Oct-26 A	26-Nov-26	1
DAM3-C-ENV-WS-786	Excavation for Water Suppy Works	7	15-Sep-26	22-Sep-26	12-Oct-26 A	26-Nov-26	1
EXTERNAL WORKS		39	15-Sep-26	17-Nov-26	23-Nov-26	06-Jan-27	8
EXTERNAL ELECTRICAL WORKS		37	15-Sep-26	09-Nov-26	23-Nov-26	04-Jan-27	7
DAM3-C-ENV-E-390	Installation of Telecom manhole	4	10-Oct-26	20-Oct-26	14-Dec-26	17-Dec-26	1
DAM3-C-ENV-E-400	Installation of UPVC Pipe	5	15-Sep-26	20-Sep-26	23-Nov-26	28-Nov-26	1
DAM3-C-ENV-E-410	Construction of Concrete encased duct bank	8	21-Sep-26	03-Oct-26	29-Nov-26	07-Dec-26	1
DAM3-C-ENV-E-420	Installation of Sleeves for lighting poles	5	04-Oct-26	08-Oct-26	08-Dec-26	13-Dec-26	1
DAM3-C-ENV-E-430	Installation of Lighting Fixture	5	04-Nov-26	09-Nov-26	30-Dec-26	04-Jan-27	1
DAM3-C-ENV-E-440	Installation of Lighting poles	5	27-Oct-26	03-Nov-26	24-Dec-26	29-Dec-26	1
DAM3-C-ENV-E-450	Foundation for Lighting poles	5	21-Oct-26	26-Oct-26	19-Dec-26	23-Dec-26	1
FENCES AND GATES		2	10-Nov-26	17-Nov-26	05-Jan-27	06-Jan-27	1
DAM3-C-ENV-S-1374	Excavation for Fence	2	10-Nov-26	17-Nov-26	05-Jan-27	06-Jan-27	1
ROAD WORKS		24	23-Nov-26	07-Feb-27	07-Jan-27	03-Feb-27	7
DAM3-C-ENV-R-890	Supply and install geotextile sheet	2	28-Jan-27	30-Jan-27	27-Jan-27	28-Jan-27	1
DAM3-C-ENV-R-1390	SubGrade Preparation & Compaction	5	23-Nov-26	03-Dec-26	07-Jan-27	12-Jan-27	1
DAM3-C-ENV-R-1400	Aggregate Base Course Layer	5	05-Dec-26	12-Dec-26	13-Jan-27	18-Jan-27	1
DAM3-C-ENV-R-1460	Curb Stones	4	13-Dec-26	04-Jan-27	19-Jan-27	23-Jan-27	1
DAM3-C-ENV-R-1480	Interlock Tiles	3	05-Jan-27	27-Jan-27	24-Jan-27	26-Jan-27	1
DAM3-C-ENV-R-1490	Gravel Bedding	2	31-Jan-27	01-Feb-27	30-Jan-27	31-Jan-27	1
DAM3-C-ENV-R-1500	Road Signs	3	02-Feb-27	07-Feb-27	01-Feb-27	03-Feb-27	1
TESTING AND COMMISSIONING (10%)		7	28-Dec-26	19-Jan-27	13-Oct-26 A	24-Feb-27	4
TESTING AND COMMISSIONING 900 Sq.m-2		7	28-Dec-26	18-Jan-27	16-Feb-27	24-Feb-27	3
MECHANICAL		3	10-Jan-27	17-Jan-27	20-Feb-27	23-Feb-27	1
P001-C-TC-M-3386	Testing and Commissioning of Fire Hose Cabinet	3	10-Jan-27	17-Jan-27	20-Feb-27	23-Feb-27	1
ELECTRICAL		7	28-Dec-26	18-Jan-27	16-Feb-27	24-Feb-27	2
P001-C-TC-E-3476	Testing and Commissioning of Lighting Fixtures	1	18-Jan-27	18-Jan-27	24-Feb-27	24-Feb-27	1
P001-C-TC-E-3536	Testing and Commissioning of Telephone and data system	2	28-Dec-26	02-Jan-27	16-Feb-27	17-Feb-27	1
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		3	03-Jan-27	19-Jan-27	13-Oct-26 A	18-Feb-27	1
ENVIRONMENTAL		3	03-Jan-27	19-Jan-27	13-Oct-26 A	18-Feb-27	1
S001-C-TC-ENV-SW-60	Testing & Commissioning of Sewer & Drainage System	3	03-Jan-27	19-Jan-27	13-Oct-26 A	18-Feb-27	1
PREOJECT CLOSEOUT		25	02-Feb-27	06-Mar-27	01-Feb-27	02-Mar-27	22

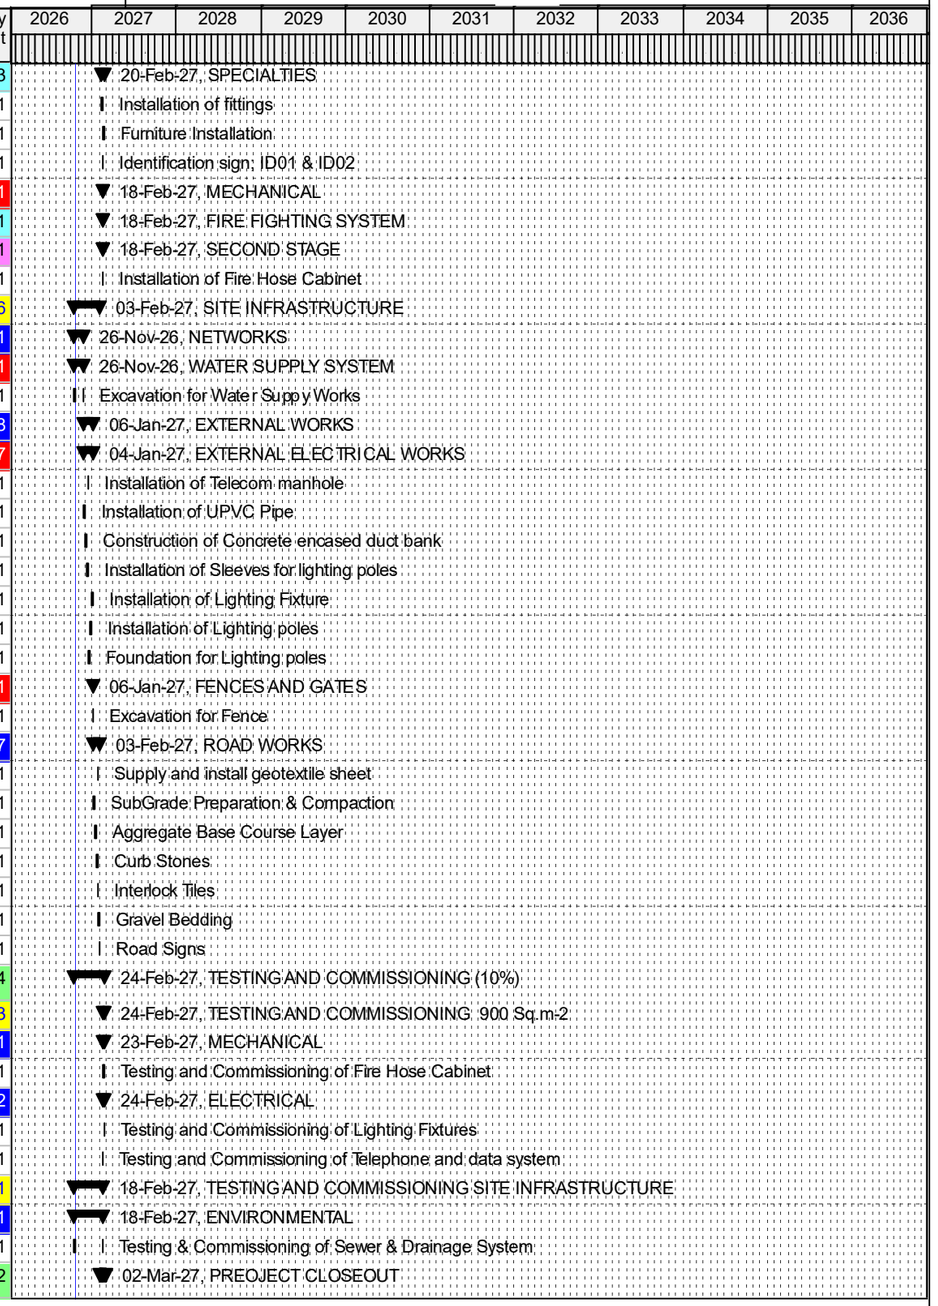

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-26	WEEKLY REPORT#34		
