
egis | ENJAZCO شركة الانجاز للتجارة والمقاولات AlEnjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 20 Oct 2026
2 Week Look Ahead

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-R-UP-Land Developmen		147	23-Mar-26	05-May-27	16-May-26 A	02-Jan-27	0.00	6,036,481.48	8,765,791.23	0%	68.86%	102
Key Milestones		0	23-Mar-26	22-Sep-26	20-Oct-26	20-Oct-26	0.00	0.00	0.00	0%	0%	-23
Contractual Milestone		0	23-Mar-26	22-Sep-26	20-Oct-26	20-Oct-26	0.00	0.00	0.00	0%	0%	-23
Construction		0	23-Mar-26	22-Sep-26	20-Oct-26	20-Oct-26	0.00	0.00	0.00	0%	0%	-23
JDH4-02-007-M	Completion of Road Works	0		22-Sep-26		20-Oct-26	0.00	0.00	0.00	100%	0%	-23
JDH4-02-007-M	Completion of Earthworks & Site Gra	0		23-Mar-26		20-Oct-26	0.00	0.00	0.00	100%	0%	-177
Construction		147	10-Nov-26	02-May-27	16-May-26 A	29-Dec-26	0.00	4,972,257.88	6,309,890.61	0%	78.8%	102
Roads		12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
Road 01		12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
Road Works (Roundabout)		12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
Finishing Works		12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
Traffic Signage		12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
JDH4-02-00	Installation of Traffic Signs [Road 01]	12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
Sewage Lift Station		147	12-Dec-26	02-May-27	17-Sep-26 A	29-Dec-26	0.00	1,175,990.79	1,969,140.70	0%	59.72%	102
Mechanical Works		66	12-Dec-26	10-Jan-27	23-Sep-26 A	01-Nov-26	0.00	764,786.08	1,116,429.99	0%	68.5%	60
Anti Water Hammer Equipment		4	12-Dec-26	15-Dec-26	01-Oct-26 A	25-Oct-26	0.00	706,441.58	883,051.97	0%	80%	44
JDH4-02-007-	Installation of Anti-Water Hammer Ec	4	12-Dec-26	15-Dec-26	01-Oct-26 A	25-Oct-26	0.00	706,441.58	883,051.97	0%	80%	44
Pumps		6	04-Jan-27	10-Jan-27	23-Sep-26 A	01-Nov-26	0.00	58,344.51	233,378.02	0%	25%	60
JDH4-02-007-	Installation of Submersible pump [Se	6	04-Jan-27	10-Jan-27	23-Sep-26 A	01-Nov-26	0.00	58,344.51	233,378.02	0%	25%	60
Electrical Works		141	12-Dec-26	02-May-27	17-Sep-26 A	29-Dec-26	0.00	411,204.71	852,710.71	0%	48.22%	102
Main Distribution Board		14	12-Dec-26	27-Dec-26	03-Oct-26 A	05-Nov-26	0.00	52,036.99	104,073.98	0%	50%	44
JDH4-02-007-	Installation of Panel Board [Sewage I	7	20-Dec-26	27-Dec-26	03-Oct-26 A	05-Nov-26	0.00	14,191.91	28,383.81	0%	50%	44
JDH4-02-007-	Installation of Main Distribution Board	7	12-Dec-26	19-Dec-26	03-Oct-26 A	28-Oct-26	0.00	37,845.09	75,690.17	0%	50%	44
Local Control Panel		25	20-Dec-26	27-Jan-27	04-Oct-26 A	21-Nov-26	0.00	53,613.87	107,227.74	0%	50%	58
JDH4-02-007-	Installation of MCP-LP-01 [Sewage L	10	20-Dec-26	30-Dec-26	04-Oct-26 A	09-Nov-26	0.00	12,615.03	25,230.06	0%	50%	44
JDH4-02-007-	Installation of FP-CP [Sewage Lift Sta	5	23-Jan-27	27-Jan-27	04-Oct-26 A	21-Nov-26	0.00	14,191.91	28,383.81	0%	50%	58
JDH4-02-007-	Installation of OD-CP [Sewage Lift St	5	06-Jan-27	11-Jan-27	04-Oct-26 A	16-Nov-26	0.00	14,191.91	28,383.81	0%	50%	49
JDH4-02-007-	Installation of MCP-LP-02 [Sewage L	5	31-Dec-26	05-Jan-27	04-Oct-26 A	15-Nov-26	0.00	12,615.03	25,230.06	0%	50%	44
Power Factor Correction Capacitor Bank		7	12-Jan-27	19-Jan-27	05-Oct-26 A	17-Nov-26	0.00	11,038.15	22,076.30	0%	50%	54
JDH4-02-007-	Installation of Power Factor Correctio	7	12-Jan-27	19-Jan-27	05-Oct-26 A	17-Nov-26	0.00	11,038.15	22,076.30	0%	50%	54
Low-Voltage Electrical Power Conductors and Cable		9	20-Jan-27	30-Jan-27	29-Sep-26 A	28-Nov-26	0.00	8,767.60	17,535.20	0%	50%	54
JDH4-02-007-	Installation of Low Voltage Cables [Se	9	20-Jan-27	30-Jan-27	29-Sep-26 A	28-Nov-26	0.00	8,767.60	17,535.20	0%	50%	54
Enclosed Switches and Circuit Breakers		5	12-Jan-27	17-Jan-27	14-Oct-26 A	15-Nov-26	0.00	5,033.40	8,830.52	0%	57%	54
JDH4-02-007-	Installation of Enclosed Switches and	5	12-Jan-27	17-Jan-27	14-Oct-26 A	15-Nov-26	0.00	5,033.40	8,830.52	0%	57%	54
Programmable Logic Controllers		14	31-Mar-27	15-Apr-27	04-Oct-26 A	20-Dec-26	0.00	126,150.28	252,300.56	0%	50%	96
JDH4-02-007-	Installation of Programmable Logic C	14	31-Mar-27	15-Apr-27	04-Oct-26 A	20-Dec-26	0.00	126,150.28	252,300.56	0%	50%	96
Process Control Wiring		4	17-Apr-27	20-Apr-27	18-Oct-26 A	24-Dec-26	0.00	63,075.14	157,687.85	0%	40%	96
JDH4-02-007-	Installation of Process Control Wiring	4	17-Apr-27	20-Apr-27	18-Oct-26 A	24-Dec-26	0.00	63,075.14	157,687.85	0%	40%	96
Instrumentation for Process Systems		8	21-Apr-27	02-May-27	17-Sep-26 A	29-Dec-26	0.00	91,489.28	182,978.56	0%	50%	102
JDH4-02-007-	Installation of Process System [Sewa	8	21-Apr-27	02-May-27	17-Sep-26 A	29-Dec-26	0.00	91,489.28	182,978.56	0%	50%	102
Plot Backfilling 2		20	14-Jan-27	06-Feb-27	25-Jul-26 A	02-Nov-26	0.00	1,672,617.57	2,027,415.24	0%	82.5%	82
JDH4-02-007-CI	Plots backfilling Stage 7 [Plots]	10	26-Jan-27	06-Feb-27	30-Jul-26 A	02-Nov-26	0.00	760,280.72	1,013,707.62	0%	75%	82
JDH4-02-007-CI	Plots backfilling Stage 6 [Plots]	10	14-Jan-27	25-Jan-27	25-Jul-26 A	27-Oct-26	0.00	912,336.86	1,013,707.62	0%	90%	78
Additional Works		30	25-Mar-27	24-Apr-27	16-May-26 A	08-Nov-26	0.00	2,115,880.70	2,287,438.60	0%	92.5%	140
JDH4-02-007-CI	Road Work	25	27-Mar-27	24-Apr-27	16-May-26 A	02-Nov-26	0.00	1,029,347.37	1,143,719.30	0%	90%	145
JDH4-02-007-CI	Electrical Works	25	25-Mar-27	22-Apr-27	28-Jun-26 A	08-Nov-26	0.00	1,086,533.33	1,143,719.30	0%	95%	139
Testing & Commissioning		78	20-Dec-26	05-May-27	09-Jun-26 A	02-Jan-27	0.00	1,064,223.60	2,455,900.62	0%	43.33%	102
JDH4-02-007-TC	Test for Road Works	3	30-Mar-27	01-Apr-27	09-Jun-26 A	07-Nov-26	0.00	654,906.83	818,633.54	0%	80%	121
JDH4-02-007-TC	Test for Sewage Lift Station	3	03-May-27	05-May-27	17-Jun-26 A	02-Jan-27	0.00	163,726.71	818,633.54	0%	20%	102
JDH4-02-007-TC	Test for Electrical Network	3	20-Dec-26	22-Dec-26	08-Sep-26 A	07-Nov-26	0.00	245,590.06	818,633.54	0%	30%	39

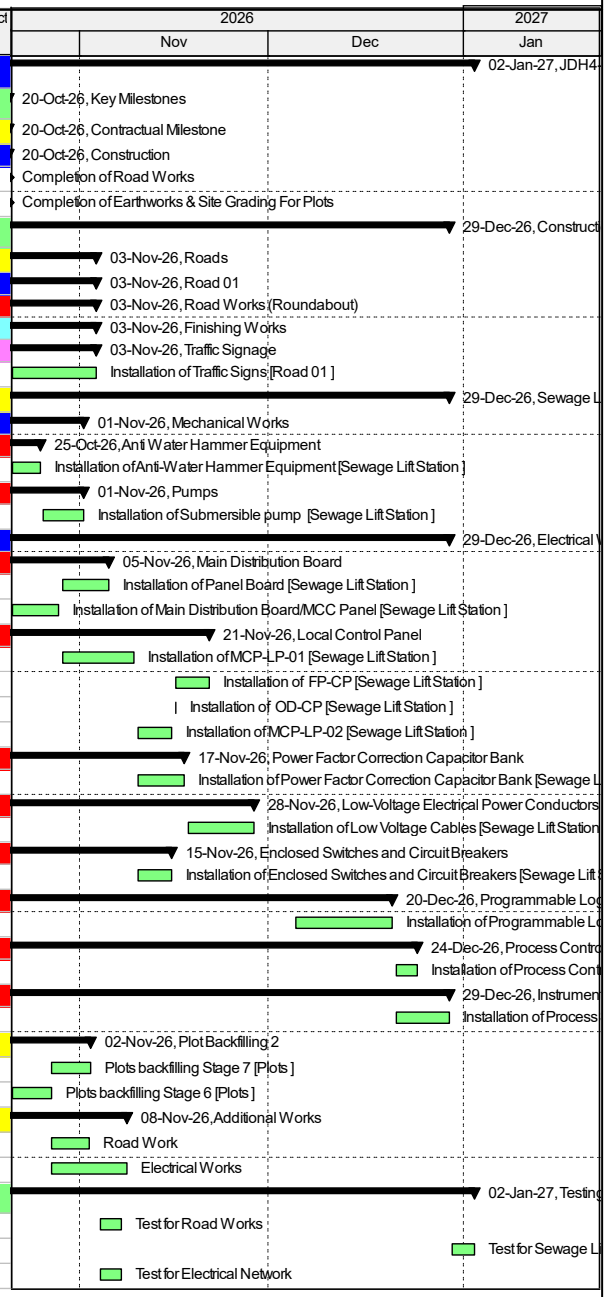

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis | ENJAZCO شركة الانجاز للتجارة والمقاولات AL Enjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 20 Oct 2026
2 Week Look Ahead

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Project Hand Over & Close-out		5	23-Dec-26	29-Apr-27	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	0%	140
As-Built DWGs		5	23-Dec-26	29-Apr-27	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	0%	140
As-Built DWGs Submittal		5	23-Dec-26	29-Apr-27	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	0%	140
JDH4-02-007-A	As-Built DWGs Submittal for Road W	5	25-Apr-27	29-Apr-27	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	35%	140
JDH4-02-007-A	As-Built DWGs Submittal for Electrica	5	23-Dec-26	28-Dec-26	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	35%	39



Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved
