
egis

ENJAZCO
شركة الانجاز للتجارة والمقاولات
ALEnjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 27 Oct 2026 Remaining Work

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-R-UP-Land Developmen		147	23-Mar-26	23-May-27	16-May-26 A	21-Jan-27	0.00	4,698,324.71	5,896,225.88	0%	79.68%	96
Key Milestones		74	23-Mar-26	23-May-27	27-Oct-26	21-Jan-27	0.00	0.00	0.00	0%	0%	96
General Milestone		0	23-May-27	23-May-27	21-Jan-27	21-Jan-27	0.00	0.00	0.00	0%	0%	96
JDH4-02-007-MS	Project Completion Date	0		23-May-27		21-Jan-27	0.00	0.00	0.00	0%	0%	96
Contractual Milestone		61	23-Mar-26	23-May-27	27-Oct-26	06-Jan-27	0.00	0.00	0.00	0%	0%	109
Construction		61	23-Mar-26	23-May-27	27-Oct-26	06-Jan-27	0.00	0.00	0.00	0%	0%	109
JDH4-02-007-M	Completion of Earthworks & Site Gra	0		23-Mar-26		27-Oct-26	0.00	0.00	0.00	100%	0%	-183
JDH4-02-007-M	Completion of Road Works	0		22-Sep-26		27-Oct-26	0.00	0.00	0.00	100%	0%	-29
JDH4-02-007-M	Completion of Electrical Networks	0		04-Jan-27		03-Nov-26	0.00	0.00	0.00	0%	0%	53
JDH4-02-007-M	Completion of Entire Project	0		23-May-27		06-Jan-27	0.00	0.00	0.00	0%	0%	109
Construction		147	12-Dec-26	02-May-27	16-May-26 A	05-Jan-27	0.00	4,289,007.94	5,077,592.34	0%	84.47%	96
Sewage Lift Station		147	12-Dec-26	02-May-27	17-Sep-26 A	05-Jan-27	0.00	1,311,475.76	1,776,446.12	0%	73.83%	96
Mechanical Works		4	12-Dec-26	15-Dec-26	01-Oct-26 A	01-Nov-26	0.00	706,441.58	883,051.97	0%	80%	38
Anti Water Hammer Equipment		4	12-Dec-26	15-Dec-26	01-Oct-26 A	01-Nov-26	0.00	706,441.58	883,051.97	0%	80%	38
JDH4-02-007-	Installation of Anti-Water Hammer Ec	4	12-Dec-26	15-Dec-26	01-Oct-26 A	01-Nov-26	0.00	706,441.58	883,051.97	0%	80%	38
Electrical Works		141	12-Dec-26	02-May-27	17-Sep-26 A	05-Jan-27	0.00	605,034.19	893,394.15	0%	67.72%	96
Main Distribution Board		14	12-Dec-26	27-Dec-26	03-Oct-26 A	12-Nov-26	0.00	72,851.79	104,073.98	0%	70%	38
JDH4-02-007-	Installation of Main Distribution Board	7	12-Dec-26	19-Dec-26	03-Oct-26 A	04-Nov-26	0.00	52,983.12	75,690.17	0%	70%	38
JDH4-02-007-	Installation of Panel Board [Sewage I	7	20-Dec-26	27-Dec-26	03-Oct-26 A	12-Nov-26	0.00	19,868.67	28,383.81	0%	70%	38
Local Control Panel		25	20-Dec-26	27-Jan-27	04-Oct-26 A	28-Nov-26	0.00	75,059.42	107,227.74	0%	70%	52
JDH4-02-007-	Installation of MCP-LP-01 [Sewage L	10	20-Dec-26	30-Dec-26	04-Oct-26 A	16-Nov-26	0.00	17,661.04	25,230.06	0%	70%	38
JDH4-02-007-	Installation of MCP-LP-02 [Sewage L	5	31-Dec-26	05-Jan-27	04-Oct-26 A	22-Nov-26	0.00	17,661.04	25,230.06	0%	70%	38
JDH4-02-007-	Installation of OD-CP [Sewage Lift St	5	06-Jan-27	11-Jan-27	04-Oct-26 A	23-Nov-26	0.00	19,868.67	28,383.81	0%	70%	43
JDH4-02-007-	Installation of FP-CP [Sewage Lift Sta	5	23-Jan-27	27-Jan-27	04-Oct-26 A	28-Nov-26	0.00	19,868.67	28,383.81	0%	70%	52
Power Factor Correction Capacitor Bank		7	12-Jan-27	19-Jan-27	05-Oct-26 A	24-Nov-26	0.00	15,453.41	22,076.30	0%	70%	48
JDH4-02-007-	Installation of Power Factor Correctio	7	12-Jan-27	19-Jan-27	05-Oct-26 A	24-Nov-26	0.00	15,453.41	22,076.30	0%	70%	48
Low-Voltage Electrical Power Conductors and Cable		9	20-Jan-27	30-Jan-27	29-Sep-26 A	05-Dec-26	0.00	12,274.64	17,535.20	0%	70%	48
JDH4-02-007-	Installation of Low Voltage Cables [Se	9	20-Jan-27	30-Jan-27	29-Sep-26 A	05-Dec-26	0.00	12,274.64	17,535.20	0%	70%	48
Enclosed Switches and Circuit Breakers		5	12-Jan-27	17-Jan-27	14-Oct-26 A	22-Nov-26	0.00	6,181.36	8,830.52	0%	70%	48
JDH4-02-007-	Installation of Enclosed Switches and	5	12-Jan-27	17-Jan-27	14-Oct-26 A	22-Nov-26	0.00	6,181.36	8,830.52	0%	70%	48
Grounding and Bonding for Electrical Systems		6	25-Jan-27	31-Jan-27	24-Oct-26 A	29-Nov-26	0.00	3,721.43	18,607.15	0%	20%	54
JDH4-02-007-	Installation of Grounding Links [Sewa	6	25-Jan-27	31-Jan-27	24-Oct-26 A	29-Nov-26	0.00	3,721.43	18,607.15	0%	20%	54
ICT (Data& telephone System)		16	20-Feb-27	14-Mar-27	24-Oct-26 A	23-Dec-26	0.00	4,415.26	22,076.29	0%	20%	65
JDH4-02-007-	Installationof Single data/Telephone	5	20-Feb-27	25-Feb-27	24-Oct-26 A	10-Dec-26	0.00	252.30	1,261.50	0%	20%	65
JDH4-02-007-	Installation of Data Switch (24 Port) [S	5	27-Feb-27	03-Mar-27	25-Oct-26 A	16-Dec-26	0.00	3,784.51	18,922.54	0%	20%	65
JDH4-02-007-	Installation of Fiber optic cable (12 Cc	6	04-Mar-27	14-Mar-27	24-Oct-26 A	23-Dec-26	0.00	378.45	1,892.25	0%	20%	65
Programmable Logic Controllers		14	31-Mar-27	15-Apr-27	04-Oct-26 A	27-Dec-26	0.00	176,610.39	252,300.56	0%	70%	90
JDH4-02-007-	Installation of Programmable Logic C	14	31-Mar-27	15-Apr-27	04-Oct-26 A	27-Dec-26	0.00	176,610.39	252,300.56	0%	70%	90
Process Control Wiring		4	17-Apr-27	20-Apr-27	18-Oct-26 A	31-Dec-26	0.00	110,381.50	157,687.85	0%	70%	90
JDH4-02-007-	Installation of Process Control Wiring	4	17-Apr-27	20-Apr-27	18-Oct-26 A	31-Dec-26	0.00	110,381.50	157,687.85	0%	70%	90
Instrumentation for Process Systems		8	21-Apr-27	02-May-27	17-Sep-26 A	05-Jan-27	0.00	128,084.99	182,978.56	0%	70%	96
JDH4-02-007-	Installation of Process System [Sewa	8	21-Apr-27	02-May-27	17-Sep-26 A	05-Jan-27	0.00	128,084.99	182,978.56	0%	70%	96
Plot Backfilling 2		10	26-Jan-27	06-Feb-27	30-Jul-26 A	03-Nov-26	0.00	861,651.48	1,013,707.62	0%	85%	82
JDH4-02-007-CI	Plots backfilling Stage 7 [Plots]	10	26-Jan-27	06-Feb-27	30-Jul-26 A	03-Nov-26	0.00	861,651.48	1,013,707.62	0%	85%	82
Additional Works		30	25-Mar-27	24-Apr-27	16-May-26 A	08-Nov-26	0.00	2,115,880.70	2,287,438.60	0%	92.5%	139
JDH4-02-007-CI	Electrical Works	25	25-Mar-27	22-Apr-27	28-Jun-26 A	08-Nov-26	0.00	1,086,533.33	1,143,719.30	0%	95%	138
JDH4-02-007-CI	Road Work	25	27-Mar-27	24-Apr-27	16-May-26 A	02-Nov-26	0.00	1,029,347.37	1,143,719.30	0%	90%	144
Testing & Commissioning		3	03-May-27	05-May-27	17-Jun-26 A	09-Jan-27	0.00	409,316.77	818,633.54	0%	50%	96
JDH4-02-007-TC	Test for Sewage Lift Station	3	03-May-27	05-May-27	17-Jun-26 A	09-Jan-27	0.00	409,316.77	818,633.54	0%	50%	96

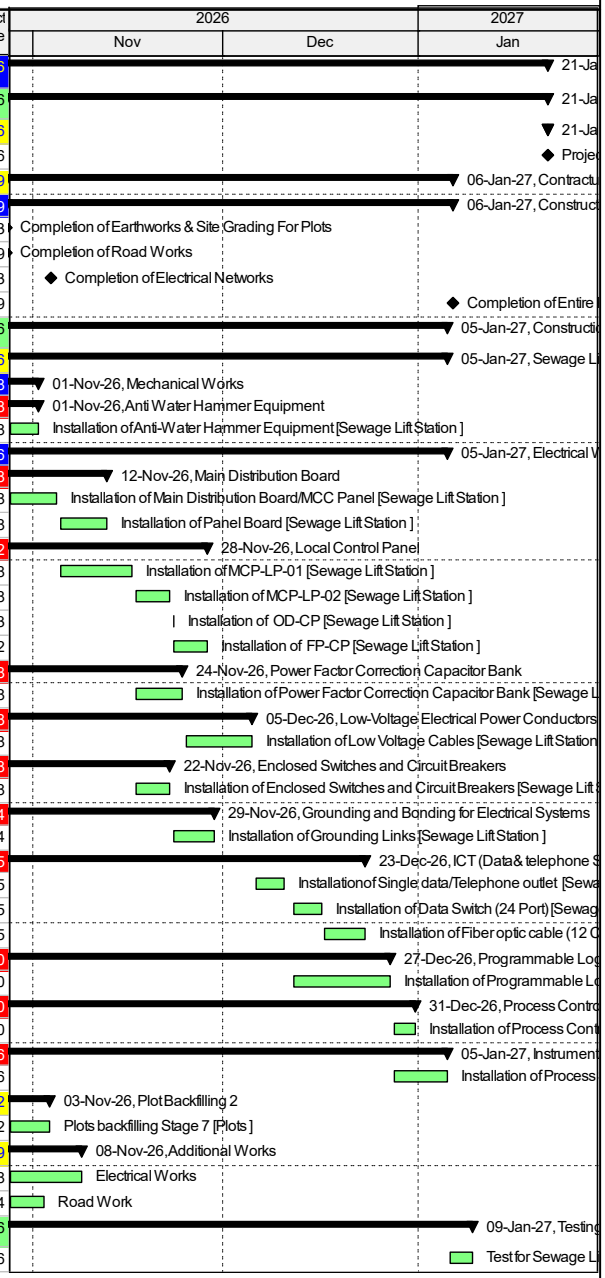

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Project Hand Over & Close-out		74	29-Dec-26	23-May-27	08-Oct-26 A	21-Jan-27	0.00	0.00	0.00	0%	0%	96
As-Built DWGs		74	29-Dec-26	23-May-27	14-Oct-26 A	21-Jan-27	0.00	0.00	0.00	0%	0%	96
As-Built DWGs Submittal		59	25-Apr-27	11-May-27	14-Oct-26 A	14-Jan-27	0.00	0.00	0.00	0%	0%	96
JDH4-02-007-A	As-Built DWGs Submittal for Sewage	5	06-May-27	11-May-27	10-Jan-27	14-Jan-27	0.00	0.00	0.00	0%	0%	96
JDH4-02-007-A	As-Built DWGs Submittal for Road W	5	25-Apr-27	29-Apr-27	14-Oct-26 A	08-Nov-26	0.00	0.00	0.00	0%	90%	144
As-Built DWGs Approval		74	29-Dec-26	23-May-27	17-Oct-26 A	21-Jan-27	0.00	0.00	0.00	0%	0%	96
JDH4-02-007-A	As- Built DWGs Approval for Electrica	6	29-Dec-26	04-Jan-27	28-Oct-26	03-Nov-26	0.00	0.00	0.00	0%	0%	53
JDH4-02-007-A	As- Built DWGs Approval for Sewage	6	12-May-27	23-May-27	16-Jan-27	21-Jan-27	0.00	0.00	0.00	0%	0%	96
JDH4-02-007-A	As- Built DWGs Approval for Road W	6	01-May-27	06-May-27	17-Oct-26 A	15-Nov-26	0.00	0.00	0.00	0%	70%	144
Demobilization		50	08-May-27	23-May-27	08-Oct-26 A	06-Jan-27	0.00	0.00	0.00	0%	0%	109
JDH4-02-007-DI	Demobilization of Manpower	5	08-May-27	12-May-27	08-Oct-26 A	09-Nov-26	0.00	0.00	0.00	0%	30%	154
JDH4-02-007-DI	Removal of Equipment from Site	5	08-May-27	12-May-27	15-Oct-26 A	14-Nov-26	0.00	0.00	0.00	0%	30%	150
JDH4-02-007-DI	Site Clean Up	5	08-May-27	12-May-27	15-Oct-26 A	14-Nov-26	0.00	0.00	0.00	0%	20%	150
JDH4-02-007-DI	Removal of Site Offices and Structure	5	08-May-27	12-May-27	22-Oct-26 A	14-Nov-26	0.00	0.00	0.00	0%	5%	150
JDH4-02-007-DI	Restoration of Ground Surfaces	5	13-May-27	23-May-27	02-Jan-27	06-Jan-27	0.00	0.00	0.00	0%	0%	109

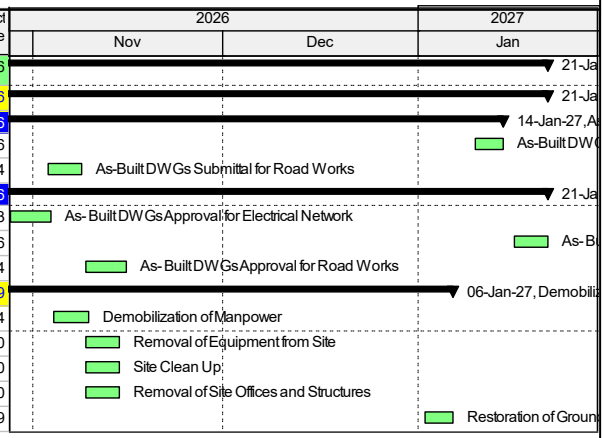

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
