Land Development of Jeddah Oasis

مشروع تطوير اراضي بواحة جدة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Enjaz Trading and Contracting Co.	EGIS	Mohammed Alshunaifi	24-Nov-2025	23-May-2027

Scope: roads, storm water piping with catch basins, manholes, box culvert and channels, sewerage network with a sewage lift station, potable water and TSE networks with fire hydrants, 36 kV medium-voltage cables with ring main units, and street lighting. Contract duration 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 97.2% against 79.0% planned under the revised plan, the project is 18.2% ahead. This week it gained 0.69% against 1.21% planned. The earthworks-for-plots and road-works milestones, now forecast for 27-Oct-2026, are still open.

PHYSICAL % COMPLETE

97.2% / 79.0% plan

▲ SPI 1.23 +18.2%

PROGRESS THIS WEEK

+0.69% / +1.21% plan

▼ 0.52% below the weekly plan

CONTRACT TIME ELAPSED

61.8% · day 337 of 545

● Forecast finish 27-Dec-2026

INVOICED TO DATE (GROSS)

80.3% · 46.0M SAR

10 invoices, last period ends 18-Oct-2026

Well ahead overall, but two milestones slipped again and this week fell short of plan.

The earthworks-for-plots and road-works milestones, forecast last week for 13-Oct-2026, are now forecast for 27-Oct-2026, and the P6 update (data date 27-Oct-2026) still shows both as not started on that date. Project completion is now forecast for 27-Dec-2026 in both the weekly report and P6, 147 days before the contract date of 23-May-2027; the Remaining Work schedule print gives 21-Jan-2027.

Site photos this week

Four photos from the Weekly Photos sheet of the 27-Oct-2026 weekly report, time-stamped 25-Oct-2026 where the stamp is visible. Select a photo to view it larger, then use the arrows to move between photos.




Road marking, Tent Road

Fresh lane markings on the curved Tent Road. No date stamp.



Guard rail work, Tent Road

Crew fixing the guard rail along Tent Road. Stamped 25-Oct-2026, 08:26.

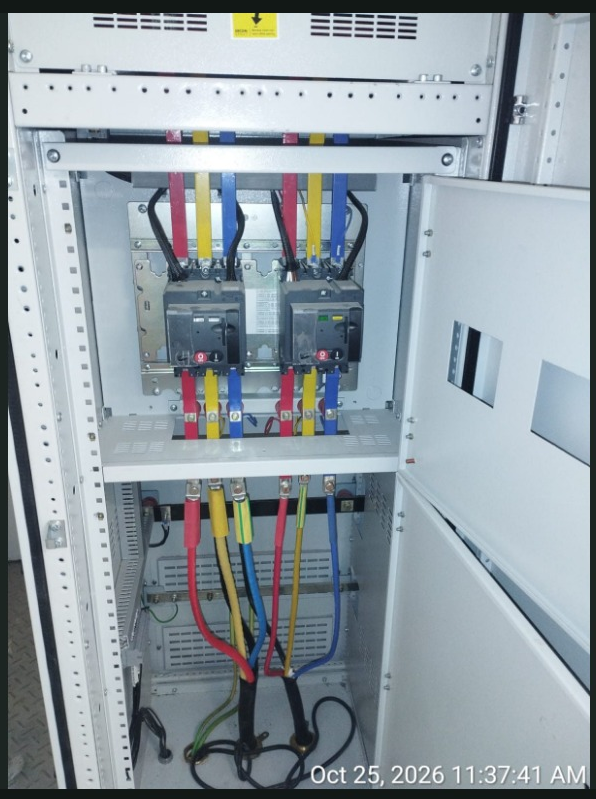

Termination work, lift station

Cable terminations in a lift station panel. Stamped 25-Oct-2026, 11:37.




Rock filling, Plot 6

Rollers and trucks on the rock fill of Plot 6. GPS-stamped 25-Oct-2026, 16:08.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet; the October point is the to-date value of 27-Oct-2026.

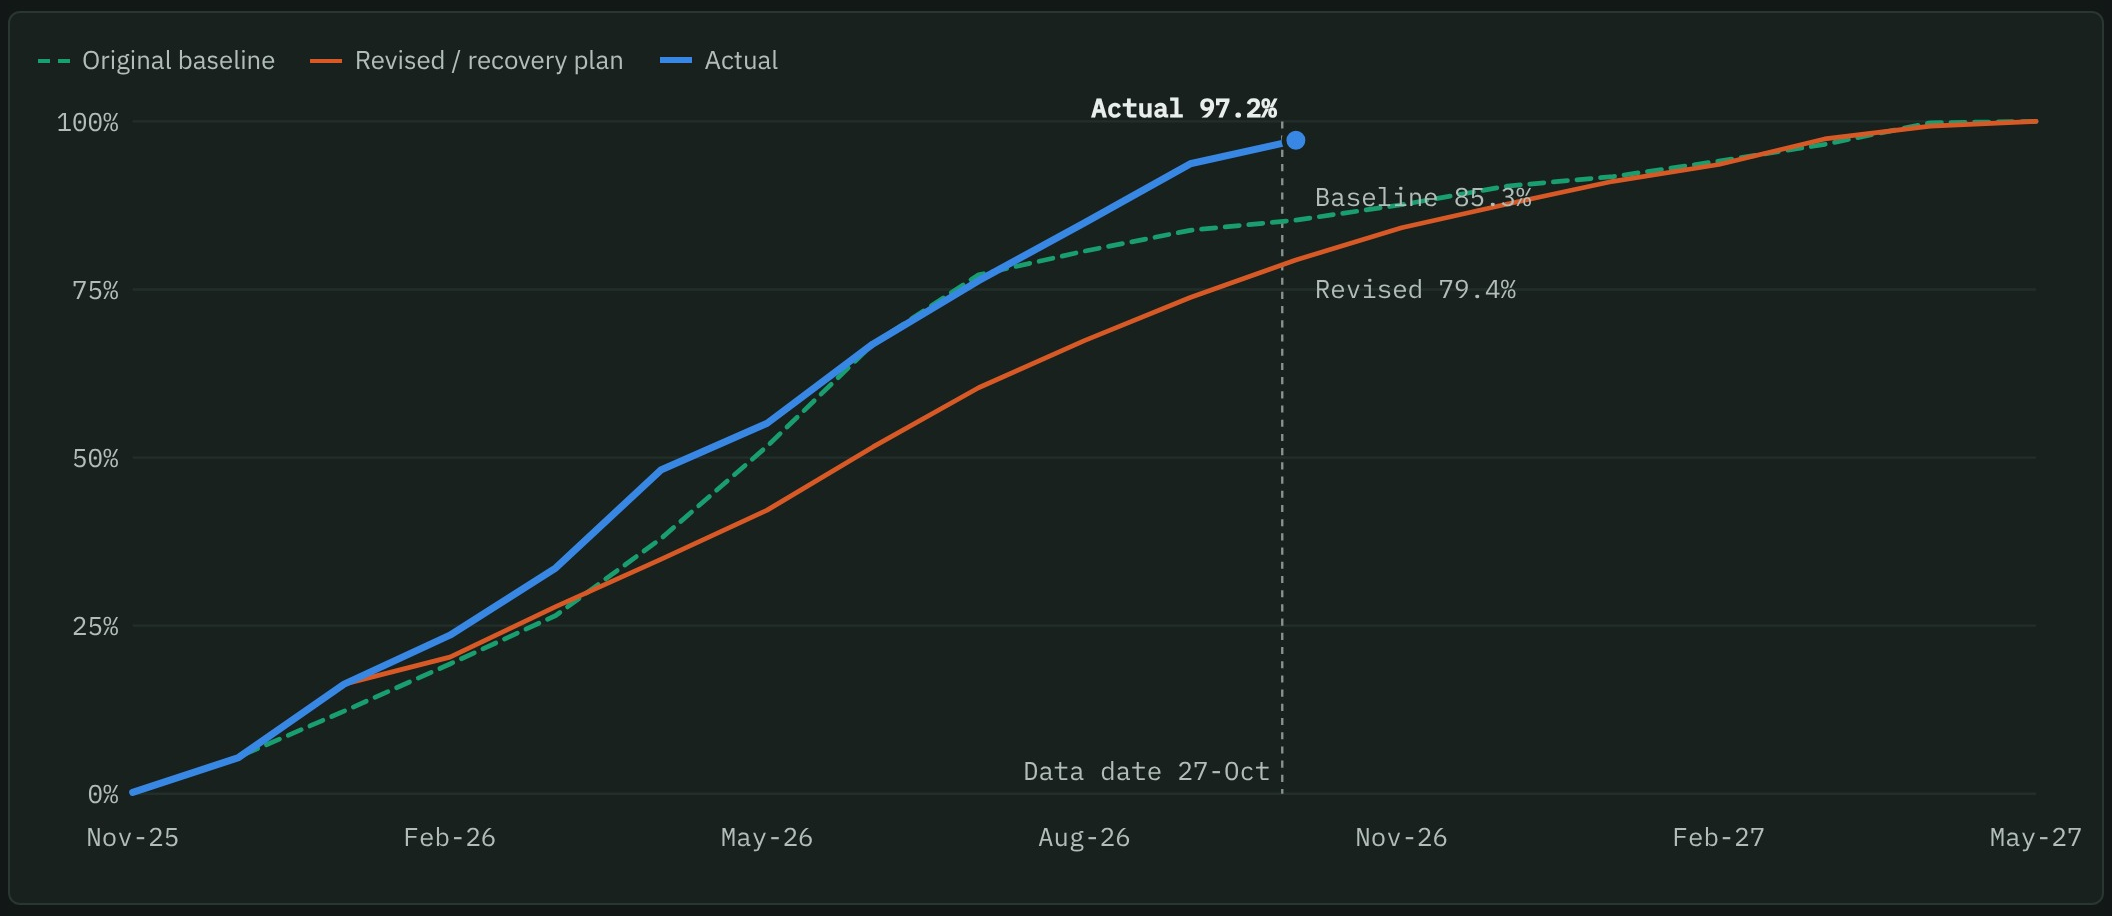

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	76.4	96.1	+19.7%	–	1.26
20-Oct-2026	77.8	96.5	+18.7%	+0.36%	1.24
27-Oct-2026	**79.0**	**97.2**	**+18.2%**	**+0.69%**	**1.23**

Weekly values from the Progress (2) sheets of the 20-Oct and 27-Oct-2026 reports, which give this week's and last week's cumulative man-hours. Planned values follow the revised / recovery plan; the original baseline called for 85.3% by the end of October.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Preliminaries	2.1%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	20.2%	98.9%	102.2%	+3.3%	1.03	▲ Ahead
Road works	13.1%	76.8%	106.5%	+29.7%	1.39	▲ Ahead
Electrical works	14.4%	42.6%	84.0%	+41.4%	1.97	▲ Ahead
Demolition works	3.6%	109.5%	109.5%	0.0%	1.00	✓ Complete
Storm water network	7.2%	93.6%	102.8%	+9.1%	1.10	▲ Ahead
Plots	3.1%	82.5%	113.9%	+31.4%	1.38	▲ Ahead
Sewer network	6.0%	84.2%	84.2%	0.0%	1.00	● On plan
TSE network	9.7%	87.8%	94.1%	+6.2%	1.07	▲ Ahead
Potable water network	7.7%	76.1%	86.8%	+10.7%	1.14	▲ Ahead
Sewage lift station	3.8%	15.9%	92.6%	+76.6%	5.81	▲ Ahead

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Box culvert	0.5%	114.3%	114.3%	0.0%	1.00	✓ Complete
Open drain channel	1.2%	128.1%	128.1%	0.0%	1.00	✓ Complete
Underpass	0.3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Testing & commissioning	2.4%	13.1%	85.5%	+72.5%	6.54	▲ Ahead
Total	100%	**79.0%**	**97.2%**	**+18.2%**	**1.23**	▲ Ahead

Eight phases report more earned man-hours than budgeted (above 100%). The P6 update (data date 27-Oct-2026) has 1,218 activities: 1,182 completed, 28 in progress and 8 not started; 17 of the activities in progress are installations at the sewage lift station. Its scheduled finish is 27-Dec-2026, 147 days before the contract date.

Scope of work: quantities

Total quantity, quantity finished to date and quantity remaining for the main BOQ items, from the Major Quantities sheet of the 27-Oct-2026 weekly report. "This week" is the change from the 20-Oct-2026 report; only plot backfilling moved.



SCOPE ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Road backfilling	m³	329,707	329,707	0	0	100.0%
Plots backfilling	m³	718,628	692,513	+38,199	26,115	96.4%
Subgrade	m³	30,812	30,812	0	0	100.0%

SCOPE ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Aggregate base course	m³	19,162	19,162	0	0	100.0%
Bituminous base course	m³	7,129	7,129	0	0	100.0%
Bituminous wearing course	m³	4,052	4,052	0	0	100.0%
Precast curb (K1)	m³	22,496	22,496	0	0	100.0%
Interlocking pavers	m²	12,677	12,677	0	0	100.0%
Potable water HDPE pipes	m	4,025	4,025	0	0	100.0%
TSE HDPE pipes	m	4,209	4,209	0	0	100.0%
Valves	nr	77	77	0	0	100.0%
Sewer GRP pipes	m	2,735	2,735	0	0	100.0%
Sewer manholes	nr	45	45	0	0	100.0%
Storm water GRP pipes	m	3,971	3,971	0	0	100.0%
Storm water manholes	nr	42	42	0	0	100.0%
Catch basins	nr	77	77	0	0	100.0%
MV cable 15 kV	m²	5,632	5,632	0	0	100.0%
LV cables	m	6,457	6,457	0	0	100.0%
Lighting poles	nr	258	258	0	0	100.0%
Telecom ducts, 6-way 50 mm	m	6,424	6,424	0	0	100.0%
Telecom ducts, 2 × 32 mm	m	4,604	4,604	0	0	100.0%
Submersible pumps	nr	2	0	0	2	0.0%
CCTV cameras	nr	7	1	0	6	14.3%
Fibre-optic cable	m	20	1	0	19	5.0%

Networks: all lengths installed

The Progress Summary sheet shows every network fully installed: roads 5,657 m, MV 13,171 m, street lighting 9,910 m, telecom 11,025 m, potable water 4,025 m, TSE 4,209 m, sewer 2,735 m and storm water 3,791 m.

Still open

Plot backfilling rose by 38,199 m³ this week to 96.4% (26,115 m³ remaining). At the lift station, the 2 submersible pumps are still reported as not installed, 1 of 7 CCTV cameras is in place and 1 of 20 m of fibre-optic cable.

Milestones

The weekly report and the P6 schedule update give different forecasts for some milestones.
Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	24-Nov-2025	24-Nov-2025	24-Nov-2025 (actual)	–	✓ Done
Complete mobilisation	23-Dec-2025	23-Dec-2025	23-Dec-2025 (actual)	–	✓ Done
Long-lead items ordered	21-Nov-2026	14-Jul-2026	–	–	✓ Done
Sewerage network	22-Jul-2026	–	26-Aug-2026 (actual)	–	✓ Done
TSE network	23-Nov-2026	–	30-Aug-2026 (actual)	–	✓ Done

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Potable water network	23-Nov-2026	02-Nov-2026	05-Sep-2026 (actual)	–	? Forecasts disagree
Delivery of all equipment and materials	31-Dec-2026	06-Oct-2026	–	–	? Conflicts with procurement log
Earthworks and site grading for plots	23-Mar-2026	27-Oct-2026	27-Oct-2026	118	▼ Late
Road works	22-Sep-2026	27-Oct-2026	27-Oct-2026	154	▼ Late
Electrical (MV) networks	06-May-2027	27-Oct-2026 (actual)	03-Nov-2026	154	? Forecasts disagree
All works complete, ready for initial handover	23-May-2027	27-Dec-2026	27-Dec-2026	118	● On time
Project completion / demobilisation	23-May-2027	27-Dec-2026	27-Dec-2026	118	● On time

Earthworks for plots and road works slipped from 13-Oct to 27-Oct-2026 and are still open.

P6 again places both on the data date of 27-Oct-2026 as not started. The weekly report now marks the electrical networks complete on 27-Oct-2026, while P6 plans them for 03-Nov-2026. For potable water it is the other way round: the weekly report no longer marks it done and forecasts 02-Nov-2026, while P6 shows it complete on 05-Sep-2026. Baseline dates are from the weekly report's Milestones sheet; the sewerage and TSE baselines are the P6 baseline finishes.

Procurement of key materials

Long-lead materials on site by discipline. Source: Procurement Summary, weekly report 27-Oct-2026.



Lift station equipment: 9 items still "under manufacturing"


Pumps, MCCB (VFD), local control panels, generator, capacitor bank, PLC, process instrumentation, flow meter and ATS. Most were due on site by 15-Sep-2026. P6 shows the installation of these items at the lift station 70% complete, so the log, unchanged since last week, may not be up to date.

Enclosed switches and circuit breakers: 4 of 7

The only item below 100% in the procurement log; it is marked as in progress. The other 26 items are completed.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

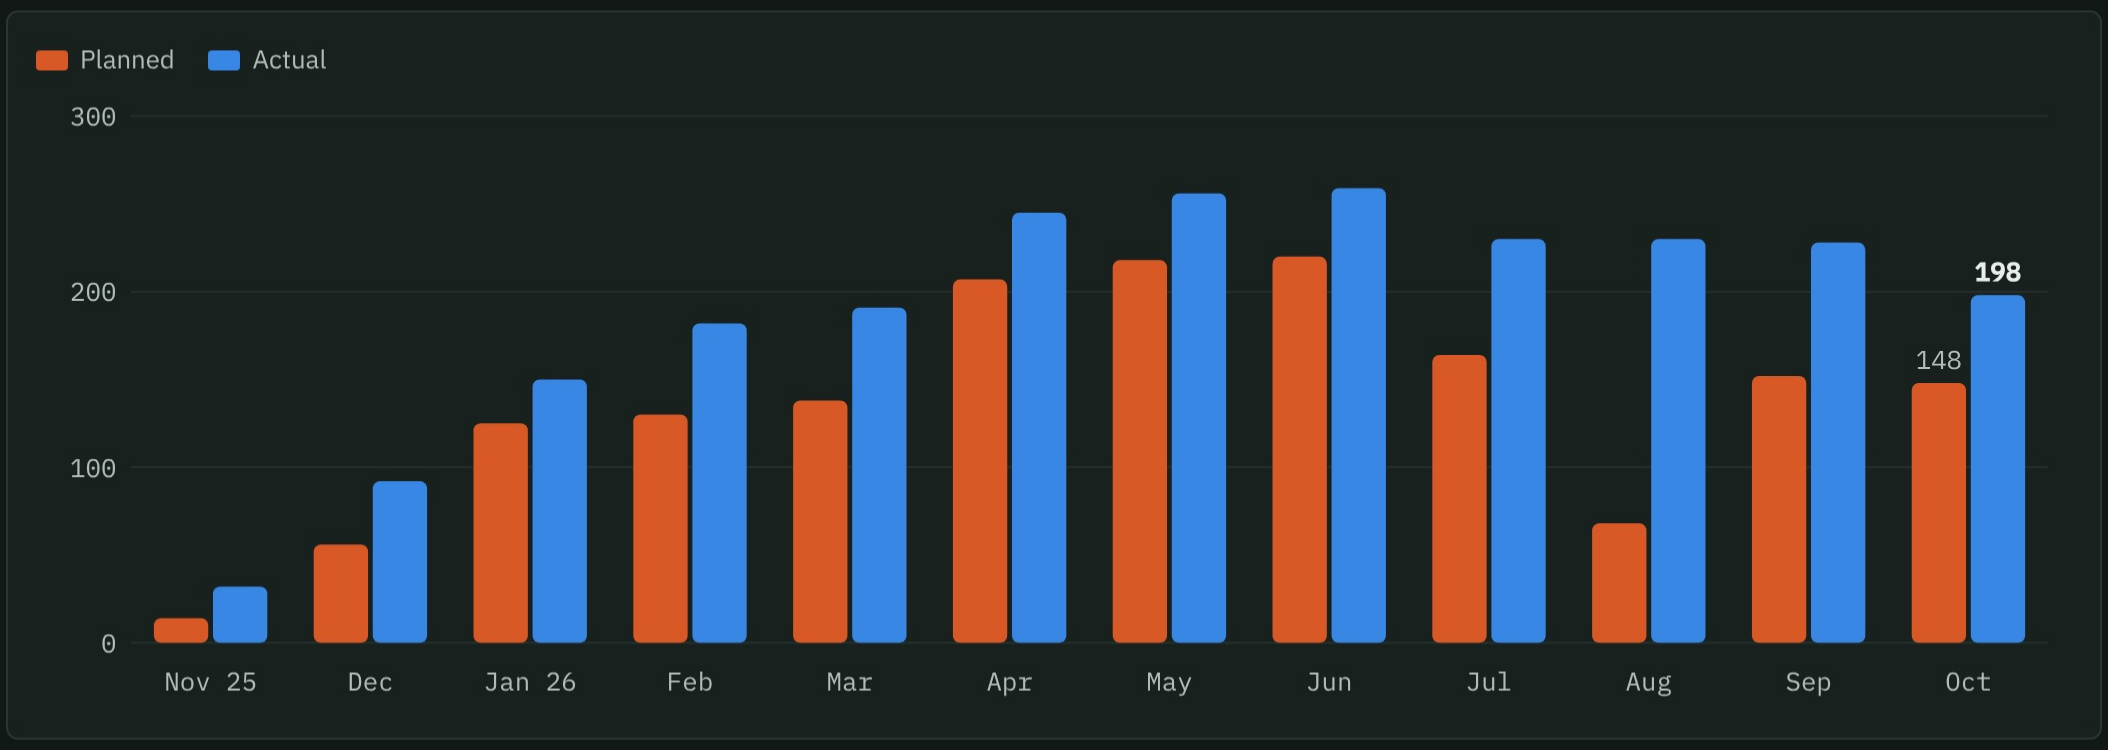

October head count is 198 (49 non-manual, 149 manual) against 148 planned. Equipment on site in October: 82 against 75 planned.

Cost and invoicing

Contract value

Road works	31,180,897
Electrical and telecom network	8,774,396
Storm water network	5,894,425
Lift station	3,284,426
TSE network	2,885,131
Sewage network	2,756,313
Potable water network	2,528,760
BOQ total (excl. VAT)	**57,304,348**
Contract value incl. 15% VAT	65,900,000
Change orders	0

All values in SAR. Breakdown from the Progress Summary sheet. No change orders or potential changes are registered.

Invoices

Invoices submitted	10
Gross value	45,992,129
Net incl. VAT	52,890,948
Approved by MODON PM (7)	33,617,268
Paid to date	27,469,389
Retention / deductions	0 / 0
FIR value to date	56,768,603

Gross invoicing is 80.3% of the contract value against 97.2% physical progress. No invoice was added this week. Invoices 8 to 10 are not yet approved by MODON, and the amount paid equals invoices 1 to 6.

Health, safety and quality

Safety Score 0.88

Safe man-hours (cumulative)	515,278
Man-hours this week	10,512
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	81 / 44

These statistics are identical to the 20-Oct-2026 report; the cumulative man-hours did not grow.

Quality Score 0.85

FIRs issued / closed (cumulative)	1,571 / 1,551
FIRs pending	20
NCRs issued / closed	43 / 43
Site instructions issued / closed	10 / 10
MIRs issued / closed	116 / 116
Shop drawings processed	394
Materials approved	146

The last pending shop drawing (road works) was approved this week. Network tests are complete for sewerage, potable water, storm water and TSE. Road testing is at 10%, and P6 shows the lift station test at 50%.

Open issues and risks

ISSUE	STATUS	DETAIL
Scope reduction, Road No. 6	Closed 25-Jan-2026	Road No. 6 and its utility networks were removed from the scope; a new scope of work covering all ongoing activities was issued.
Rock protection, wadi channel and box culvert	Closed 25-Jan-2026	The scope had no rock protection at the culvert inlet and outlet or along the wadi; a decision on grouted riprap was needed.
Wadi channel vs culvert width	Closed 30-Dec-2025	The 15 m wadi bed is much wider than the 6.7 m culvert CU-02; the IFC drawings are followed.
Existing underpasses	Closed 25-Jan-2026	To avoid leakage and odour, the underpass concrete is removed completely and backfilled.
MV network materials and quantities	Closed 30-Apr-2026	Approval of MV materials and quantities by SEC and MODON.
Safety: deep openings, heat stress, traffic	Closed	Hard barriers, summer work break, flagmen and signboards in place.

Every item in the issue log (8 issues) and the risk register (7 risks) is closed; both are unchanged from last week. What remains open, from the other sheets: the earthworks-for-plots and road-works milestones, the lift station equipment and installation, 20 pending FIRs, and the road and lift station tests.

Data notes

- The weekly report's headline, the summary sheet and the "work done this week" files label a cost-based progress figure as "actual". This report uses physical % complete (man-hours) only.
- Week number: the Milestones sheet states "Current Contract Weeks: 49 of 79", which is used here. Counting whole weeks from site handover (24-Nov-2025 to 27-Oct-2026, 337 days) gives week 48.
- The Physical-Chart Data sheet shows 97.7% for October (396,939 man-hours), while the progress sheets give 97.2% to date (394,817 man-hours). This report uses 97.2%.
- Earned man-hours exceed the budget in eight phases (up to 128% for the open drain channel), and planned man-hours also exceed the budget in three of them. The baseline and revised plans use different totals (406,229 and 406,774 man-hours).
- Milestones disagree between the weekly report and P6: electrical networks are marked complete on 27-Oct-2026 in the report but not started (03-Nov-2026) in P6; potable water was marked complete on 05-Sep-2026 last week but is now forecast for 02-Nov-2026, while P6 still shows it complete.
- Completion dates differ between files: 27-Dec-2026 (weekly report and P6 XER), 21-Jan-2027 for project completion and 06-Jan-2027 for the entire project in the Remaining Work print, 23-Nov-2026 as the expected end in the "work done this week" files, and 23-May-2026 as the contract end in one of them (the contract end is 23-May-2027).
- The Schedule sheet counts 1,176 completed, 28 in progress and 8 not started activities (1,212 in total), while the P6 XER has 1,182 completed (1,218 in total). Several open lift-station and additional-works activities in P6 finish between January and April 2027, after the 27-Dec-2026 project finish.
- Several files and sheets are unchanged from last week: the Tracking Progress file is identical, as are the procurement log, the issue log, the risk register, the invoice log, the HSE statistics and the inspection counts (FIR, NCR, MIR).
- The milestone "Complete delivery of all equipment and materials" is marked achieved on 06-Oct-2026, but the procurement log has 9 items "under manufacturing" and one at 4 of 7, and the Procurement Summary has 27 of 34 materials on site.

- FIR amounts for this week differ: 2,421,817 in the FIR summary and 1,886,072 for week 49 in the FIR log. The Testing sheet's planned dates changed from last week (for example, the road works test moved from 30-Mar-2027 to 12-Jul-2026), and its road works forecast finish is marked actual at only 10% complete.
- Scope quantities disagree between sheets: storm water 3,791 m (Progress Summary) vs 3,971 m of GRP pipe (Major Quantities); MV network 13,171 m vs 5,632 of 15 kV cable. The Major Quantities sheet gives curbs in m³ and MV cable in m². Shop drawing totals are 394 on the dashboard and 703 on the Quality-Stat sheet.
- Manpower for October: the dashboard shows 61 planned and 181 actual manual workers (by trade), the Manpower sheet 136 and 149; last week's report gave 156 actual for October.
- The "work done this week" files give the PM as Abdullah Alshunaifi and place the project in the central sector. The invoice summary counts 3 paid invoices, but the paid amount equals invoices 1 to 6. Several cells show #REF ! (issue owners, EAC).

Compiled 01-Nov-2026 from the weekly report for the week ending 27-Oct-2026 (W04 upload), with the 20-Oct-2026 report for this-week values.
