
Development of the Technology City in Dammam Project
BL-Update28-09-2026
WBS Summary Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Schedule % Complete	Performance % Complete	Budgeted Total Cost	Planned Value Cost	Earned Value Cost
Development of the Technology City in Dhahran Project Reco		3632.00	06-Jan-26 A	08-Jul-27	37.26%	24.76%	93,061,973	34,795,176	23,121,817
Key Milestones		3632.00	06-Jan-26 A	08-Jul-27	0%	0%	0	0	0
Preliminaries and Mobilization Works		632.00	06-Jan-26 A	11-Apr-26 A	0%	0%	0	0	0
Mobilization Works		632.00	06-Jan-26 A	11-Apr-26 A	0%	0%	0	0	0
Project Main Documents From The Contractor		224.00	06-Jan-26 A	05-Feb-26 A	0%	0%	0	0	0
Engineering Works		2080.00	06-Jan-26 A	15-Nov-26	0%	0%	0	0	0
Shop Drawings		216.00	06-Jan-26 A	04-Feb-26 A	0%	0%	0	0	0
Method Statements		104.00	18-Jan-26 A	31-Jan-26 A	0%	0%	0	0	0
Material Submittals and Approvals		2080.00	06-Jan-26 A	15-Nov-26	0%	0%	0	0	0
Procurement Cycle		2696.00	02-May-26 A	13-Jun-27	0%	0%	0	0	0
Short Lead Time Items		2400.00	02-May-26 A	25-Apr-27	0%	0%	0	0	0
Long Lead Time Items		1456.00	04-Nov-26	13-Jun-27	0%	0%	0	0	0
Construction Works		3054.00	10-Mar-26 A	16-Jun-27	37.26%	24.76%	93,061,973	34,795,176	23,121,817
Infrastructure Networks		3038.00	10-Mar-26 A	14-Jun-27	55.97%	23.46%	57,696,530	32,291,178	13,535,825
Internal		3038.00	10-Mar-26 A	14-Jun-27	51.19%	9.4%	32,508,953	16,641,136	3,055,456
Alignment-RD-01		2902.00	10-Mar-26 A	25-May-27	53.82%	20.1%	15,199,337	8,180,211	3,055,456
Alignment-RD-02		1392.00	15-Nov-26	14-Jun-27	50.61%	0%	7,655,882	3,874,904	0
Alignment-RD-03-1		1368.00	19-Oct-26	09-May-27	37%	0%	3,448,486	1,276,024	0
Alignment-RD-03-2		1536.00	21-Oct-26	10-Jun-27	55.96%	0%	3,959,670	2,215,741	0
Alignment-RD-03-3		1320.00	02-Nov-26	22-May-27	48.73%	0%	2,245,578	1,094,256	0
External		2672.00	01-Apr-26 A	04-May-27	62.13%	41.61%	25,187,577	15,650,043	10,480,369
External Road - 1 - 1		2664.00	01-Apr-26 A	03-May-27	62.19%	49.95%	5,221,714	3,247,135	2,608,226
External Road - 1 - 2		2560.00	18-Apr-26 A	04-May-27	62.3%	23.4%	7,651,591	4,767,067	1,790,191
External Road - 2		2416.00	09-May-26 A	04-May-27	62.12%	35.19%	3,781,297	2,348,995	1,330,763
External Road - 3		2416.00	09-May-26 A	04-May-27	61.96%	55.68%	8,532,974	5,286,846	4,751,189
Superstructure Work		1760.00	01-Aug-26 A	16-Jun-27	7.02%	26.86%	35,365,443	2,503,998	9,585,992
Utility Buildings		1760.00	29-Aug-26 A	16-Jun-27	11.44%	12.35%	8,083,982	924,668	998,693
Softscape and Planting Works		280.00	24-Apr-27	08-Jun-27	0%	0%	3,915,193	0	0
Storm Drainage Ponds		440.00	01-Oct-26 A	28-Apr-27	0%	45%	8,820,044	0	3,969,020
Boundary Fence and Gaurd Room		1488.00	01-Aug-26 A	06-Jun-27	10.62%	31.05%	14,546,224	1,579,329	4,618,279

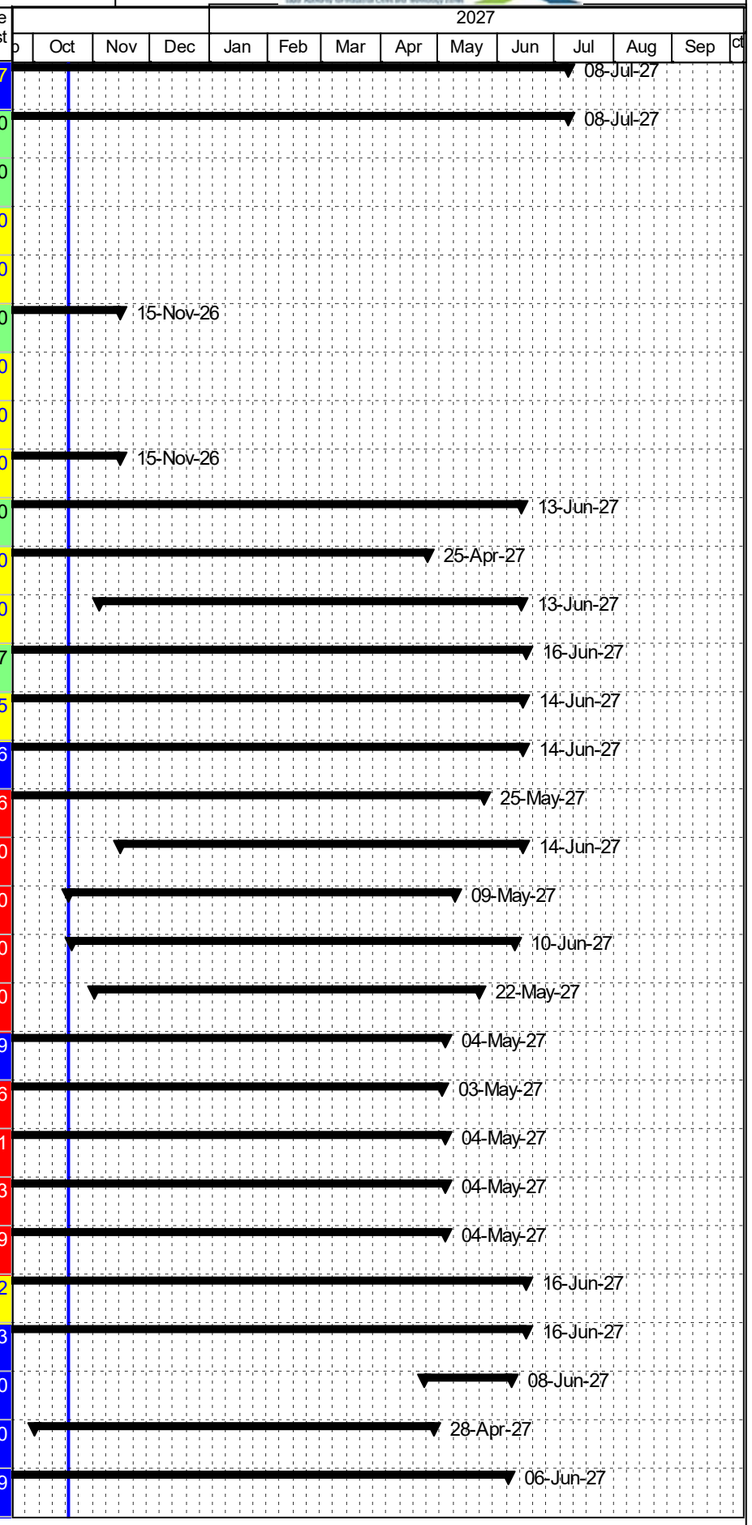


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
28-Sep-26	Third Industrial City		

Development of the Technology City in Dammam Project
BL-Update28-09-2026
WBS Summary Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Schedule % Complete	Performance % Complete	Budgeted Total Cost	Planned Value Cost	Earned Value Cost
Testing and Comissioning		200.00	07-Jun-27	05-Jul-27	0%	0%	0	0	0
Infrastructure Networks		136.00	12-Jun-27	30-Jun-27	0%	0%	0	0	0
Utility Buildings		200.00	07-Jun-27	05-Jul-27	0%	0%	0	0	0
Handing over and close out		192.00	12-Jun-27	08-Jul-27	0%	0%	0	0	0

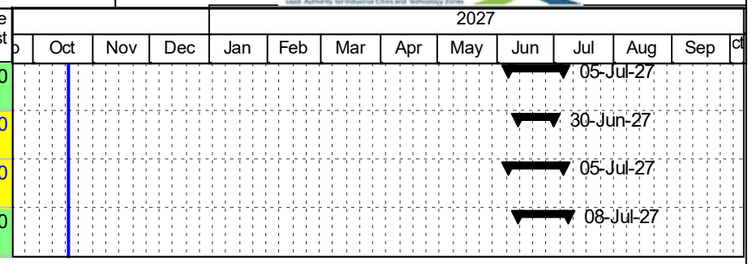

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
28-Sep-26	Third Industrial City		
