Development of the Technology City in Dhahran

تطوير المناطق التقنية - الظهران

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ANSAB Contracting	EGIS	Eng. Afat Elanzey	06-Jan-2026	05-Mar-2027

Scope: collector and local roads; potable water, sewage, storm drainage, irrigation, TSE, medium-voltage, street lighting and telecom networks; a sewage pump station and storm drainage ponds; boundary fence, guard room and utility buildings.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 26-Oct-2026 data date the project is 20.8% complete against 36.4% planned in the baseline (SPI 0.57), and against 32.1% in the contractor's recovery plan (SPI 0.65). This week added 0.34% against 0.54% planned.

PHYSICAL % COMPLETE

20.8% / 36.4% plan

▼ SPI 0.57 −15.6%

PROGRESS THIS WEEK

+0.34% / +0.54% plan

▼ 0.20% below the weekly plan

CONTRACT TIME ELAPSED

69.3% · day 293 of 423

▼ P6 finish 15-Jul-2027

INVOICED TO DATE (GROSS)

11.3% · 10.5M SAR

4 invoices, last period ends 15-Oct-2026

The schedule update finishes the project more than four months late.

The P6 update with data date 26-Oct-2026 schedules project completion on 15-Jul-2027, 132 days after the contract completion date of 05-Mar-2027. The weekly report still forecasts 05-Mar-2027 with no change to any milestone. Finishing on time needs about 4.4% physical progress a week for the 18 weeks left, against 0.34% this week.

Site photos this week

Four photos embedded in the 26-Oct-2026 weekly report workbook. None carries a date or GPS stamp. Select a photo to view it larger, then use the arrows to move between photos.




Trench excavation

Excavator opening a pipe trench in sandy ground.




Lean concrete

Worker levelling lean concrete in a footing pit, with starter bars in place.

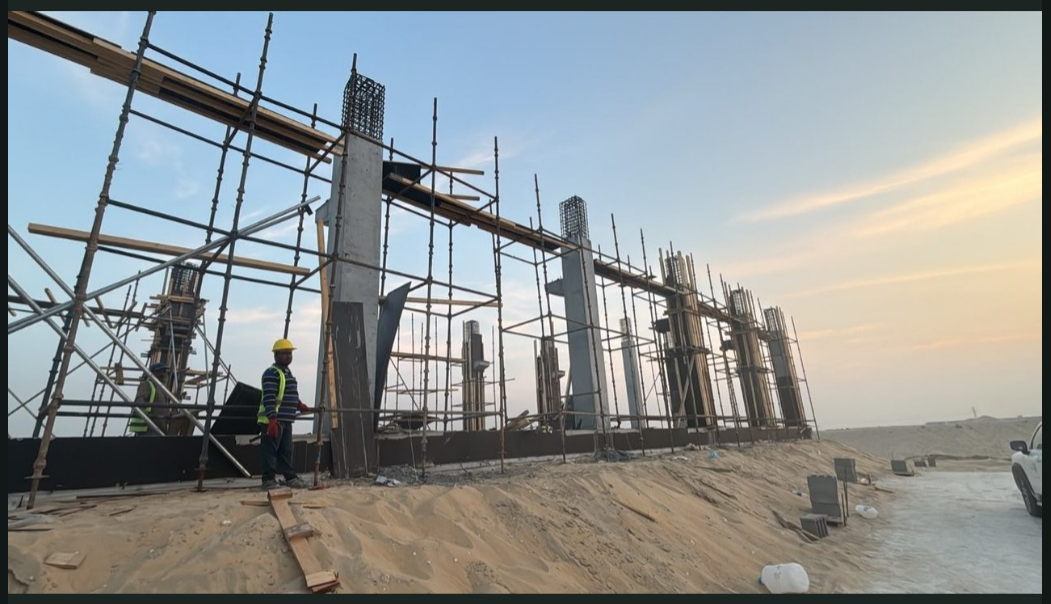

Columns and scaffolding

Reinforced concrete columns cast along a wall line, with scaffolding.

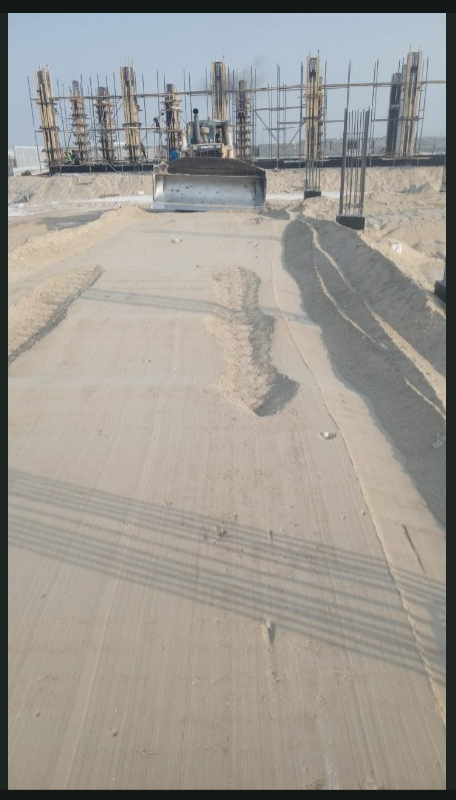


Embankment works

Dozer spreading and levelling fill, with the column line behind.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

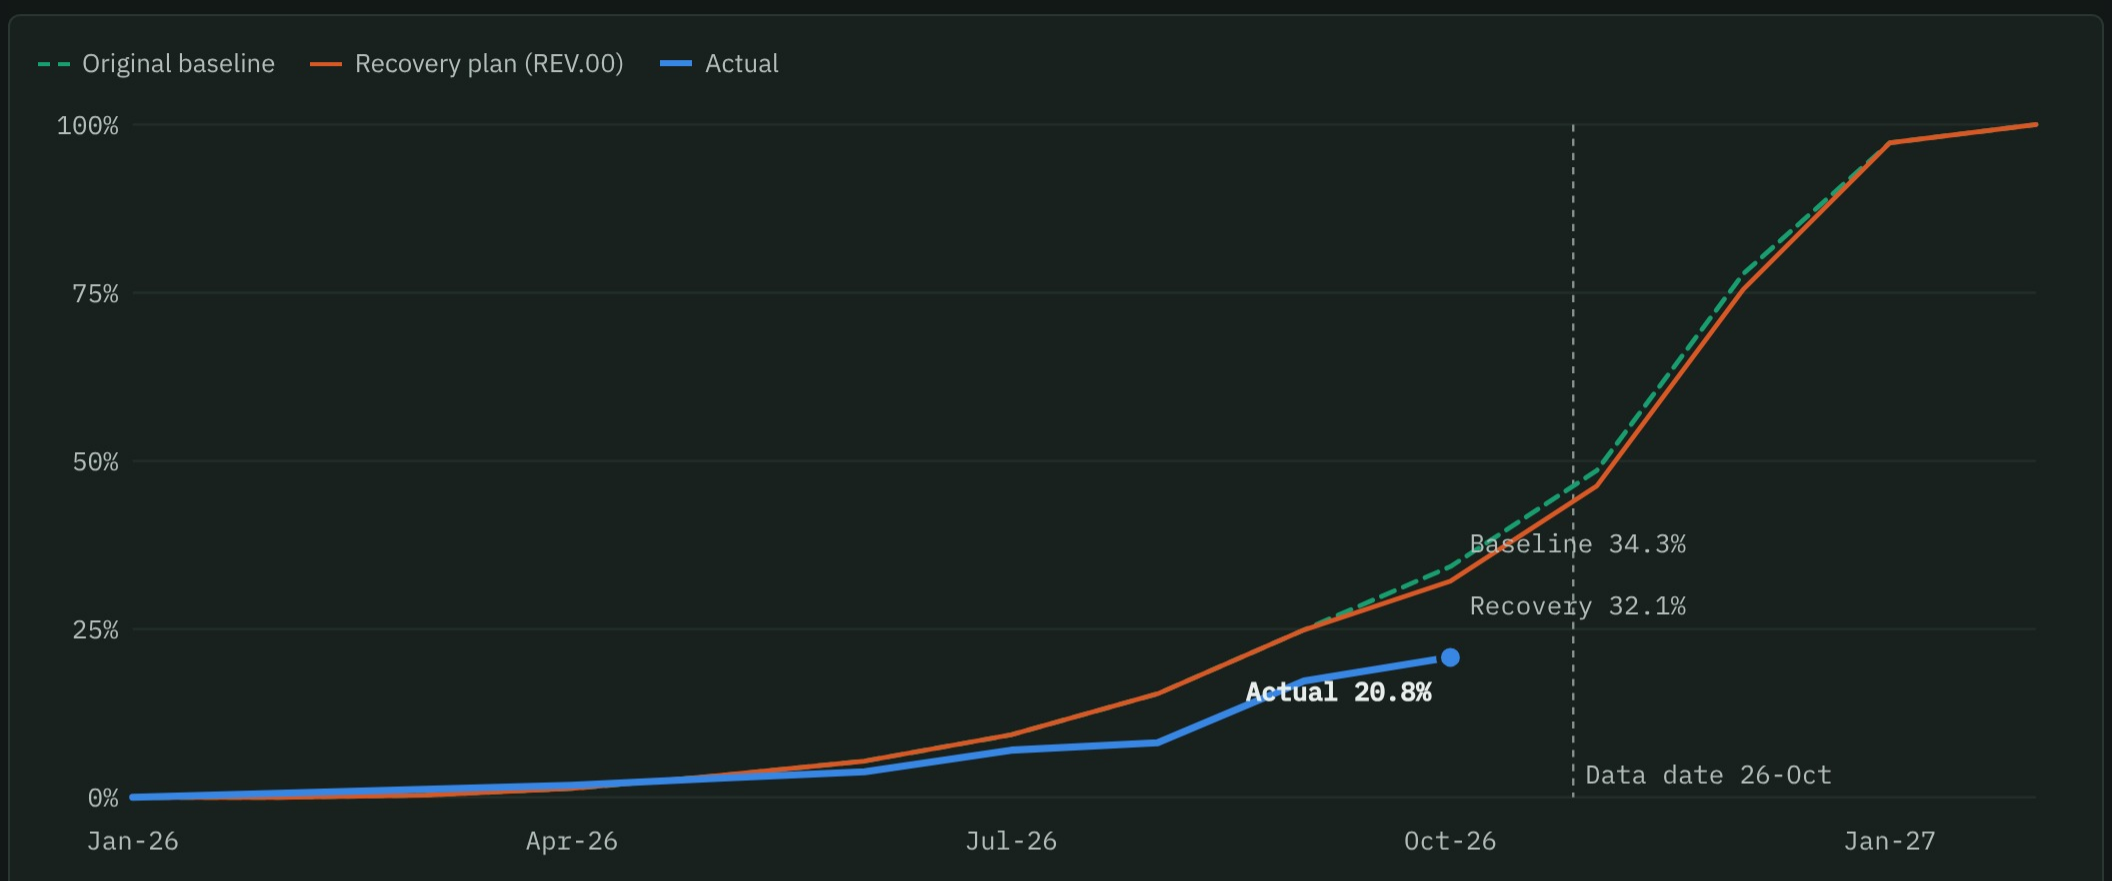

MONTH	PLANNED %	ACTUAL %	VARIANCE	GAINED IN MONTH	SPI
May-2026	3.2	2.8	−0.5%	+1.0%	0.86
Jun-2026	5.4	3.8	−1.6%	+1.0%	0.70
Jul-2026	9.3	7.0	−2.3%	+3.2%	0.75
Aug-2026	15.4	8.1	−7.3%	+1.1%	0.52
Sep-2026	24.9	17.3	−7.5%	+9.2%	0.70
26-Oct-2026	**36.4***	**20.8**	**−15.6%**	**+3.5%**	**0.57**

Planned values are the original baseline. No earlier weekly reports were uploaded, so the table is monthly; this week's gain (+0.34%) comes from the weekly columns of the report. * The progress summary gives 36.4% planned to date; the monthly chart data gives 34.3% for October. The recovery plan matches the baseline until September and gives 32.1% for October.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (131,328 in total). All man-hours sit under construction; engineering, procurement and testing carry none.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Boundary fence and guard room	28.5%	56.3%	51.1%	−5.2%	0.91	▼ Slightly behind
Roads network	17.2%	0.0%	0.8%	+0.8%	–	▲ Started early
Utility buildings	14.1%	59.6%	28.8%	−30.8%	0.48	▼ Behind
Storm drainage network	10.6%	80.4%	19.3%	−61.0%	0.24	▼ Behind
Softscape	5.3%	0.0%	0.0%	0.0%	–	● Not yet due
Low-voltage network	5.0%	0.0%	0.0%	0.0%	–	● Not yet due
Potable water network	4.1%	10.4%	0.0%	−10.4%	0.00	▼ Not started
Sewage network	3.1%	65.4%	0.0%	−65.4%	0.00	▼ Not started
Street lighting network	3.0%	0.0%	0.0%	0.0%	–	● Not yet due
TSE network	2.6%	19.7%	0.0%	−19.7%	0.00	▼ Not started
Irrigation network	2.2%	4.2%	0.0%	−4.2%	0.00	▼ Not started
CCTV	1.6%	0.0%	0.0%	0.0%	–	● Not yet due
Medium-voltage network	1.3%	23.9%	0.0%	−23.9%	0.00	▼ Not started
Telecom network	1.2%	0.0%	0.0%	0.0%	–	● Not yet due
Furnishing	0.2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**36.4%**	**20.8%**	**−15.6%**	**0.57**	▼ Behind

Planned is the original baseline. Against the recovery plan (32.1% to date) the SPI is 0.65; the recovery plan moves sewage, potable water, TSE and irrigation work earlier and storm drainage, utility buildings and MV work later. The P6 update (data date 26-Oct-2026) has 1,065 activities: 302 completed, 21 in progress and 742 not started.

Scope of work: quantities

Total quantity, quantity finished and quantity remaining for the main items, from the Major Quantities sheet of the 26-Oct-2026 weekly report. No earlier weekly report was uploaded, so the "This week" column cannot be filled yet.

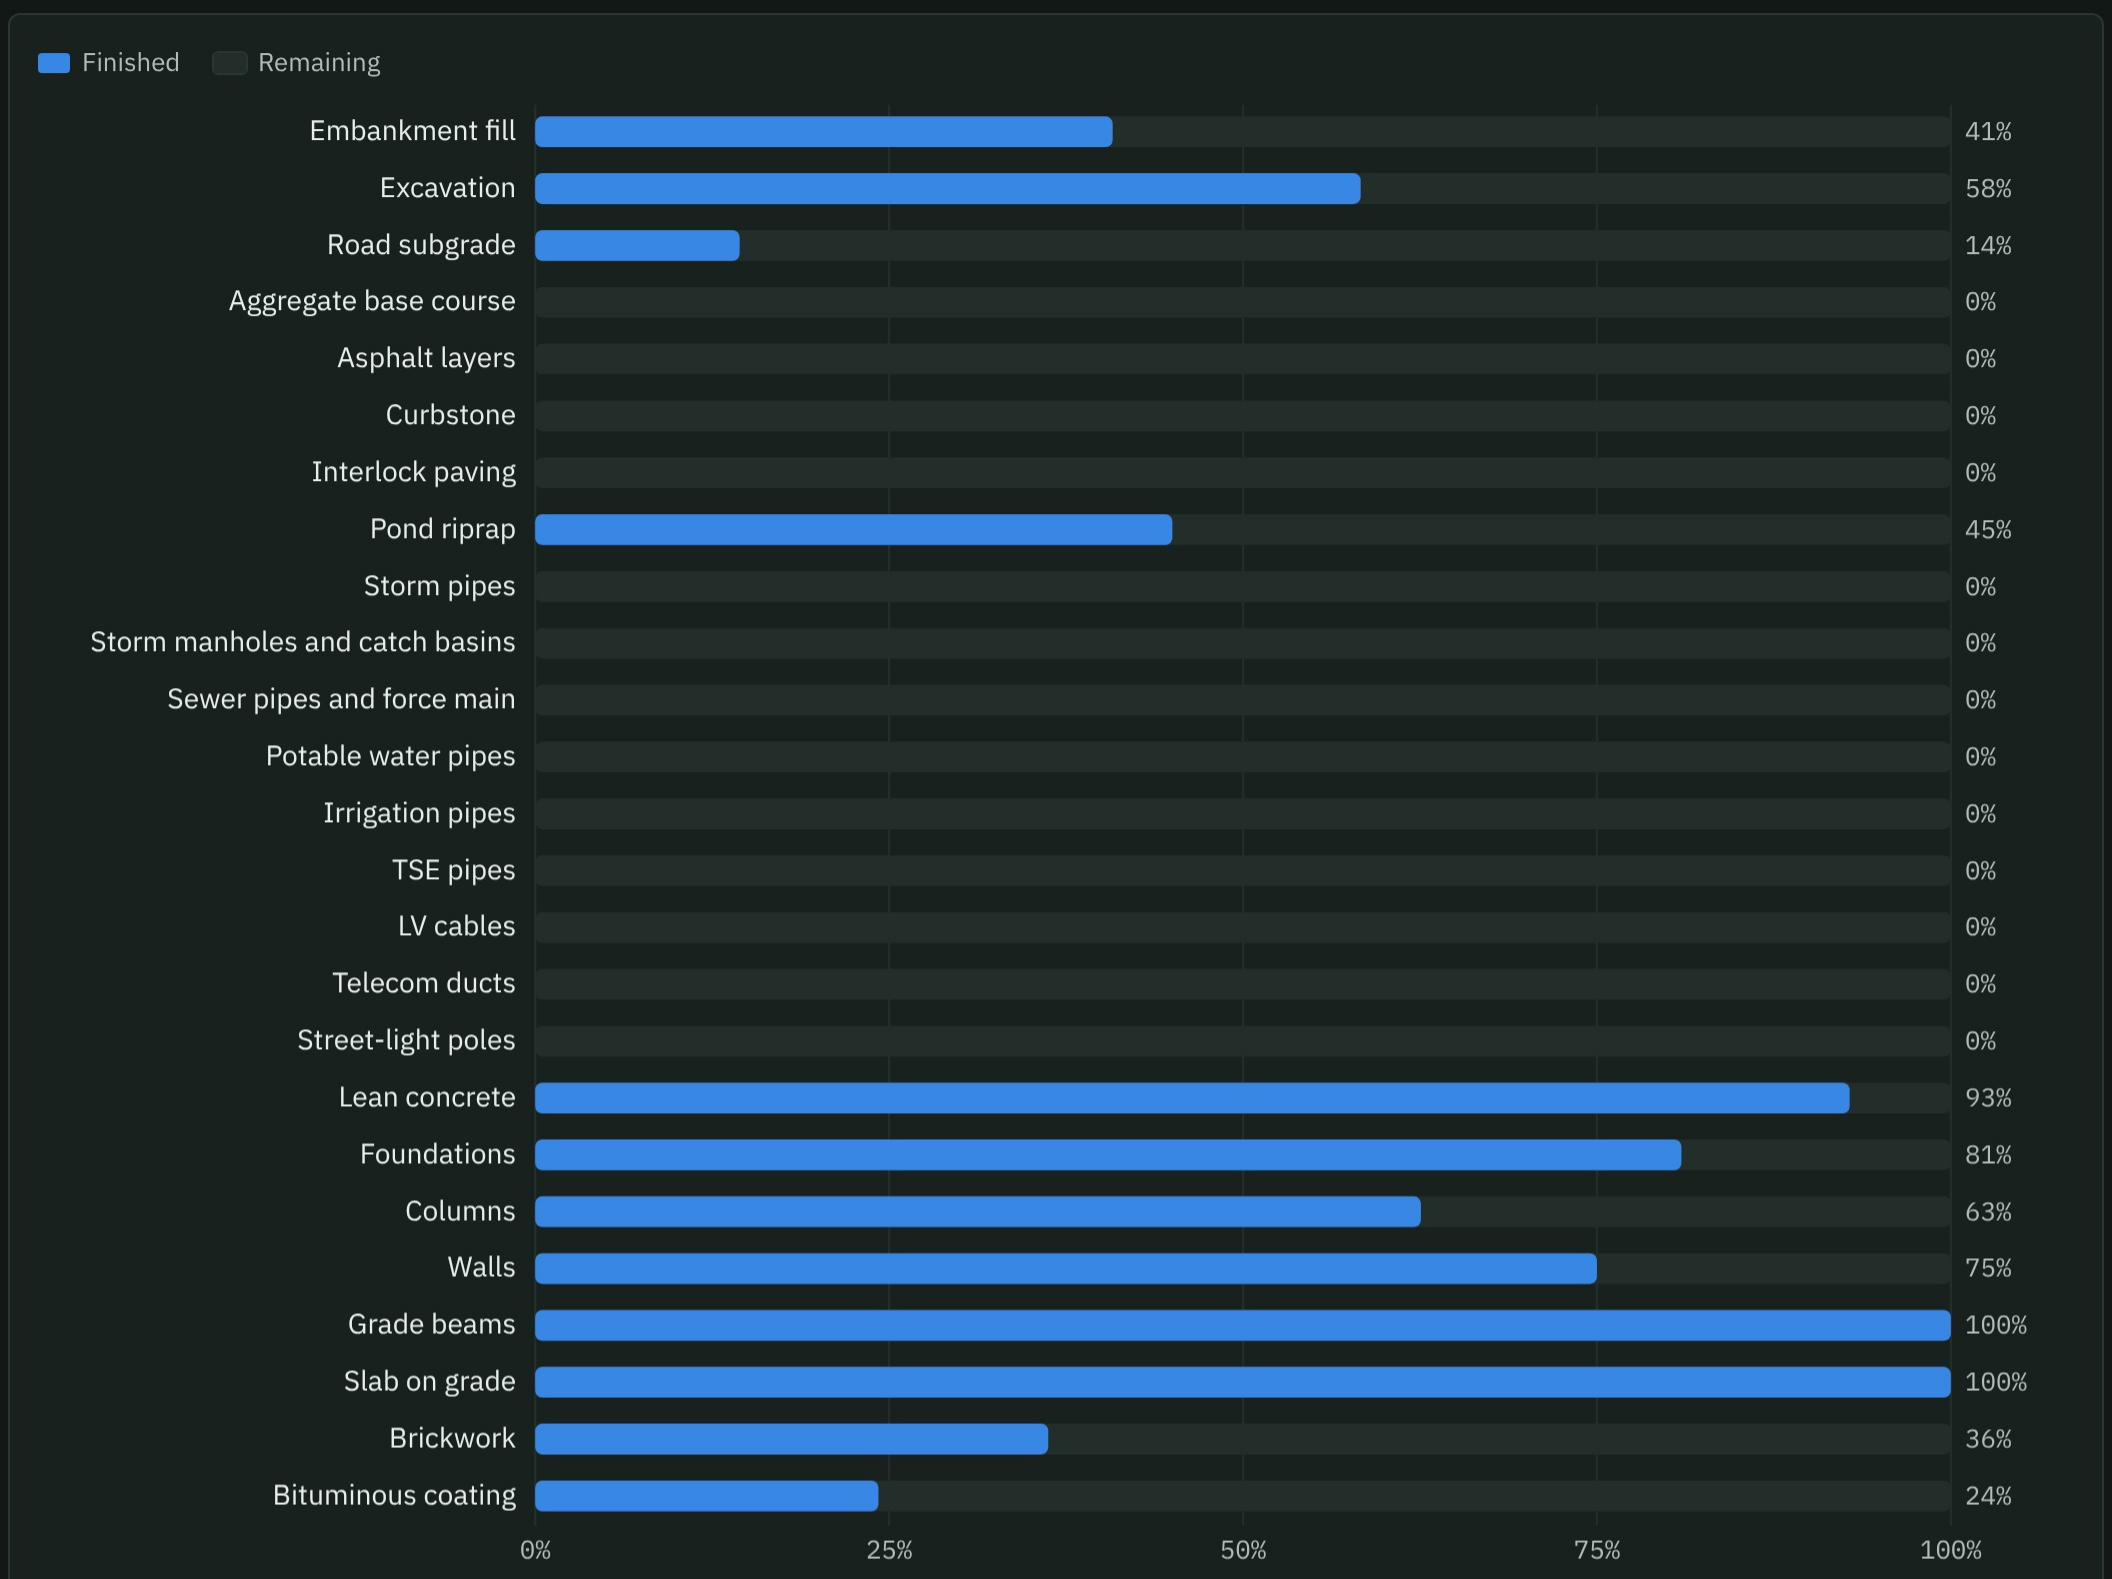

SCOPE ITEM	AREA	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Embankment fill	Site	m³	1,050,000	428,344	–	621,656	40.8%
Excavation	Site	m³	61,715	35,987	–	25,728	58.3%
Road subgrade	Roads	m³	45,731	6,605	–	39,126	14.4%
Aggregate base course	Roads	m³	22,866	0	–	22,866	0.0%
Asphalt layers	Roads	m³	15,254	0	–	15,254	0.0%
Curbstone	Roads	LM	46,423	0	–	46,423	0.0%
Interlock paving	Roads	m²	90,979	0	–	90,979	0.0%
Pond riprap	Storm ponds	m²	7,985	3,594	–	4,391	45.0%
Storm pipes	Networks	LM	7,221	0	–	7,221	0.0%
Storm manholes and catch basins	Networks	EA	283	0	–	283	0.0%
Sewer pipes and force main	Networks	LM	3,897	0	–	3,897	0.0%
Potable water pipes	Networks	LM	4,183	0	–	4,183	0.0%
Irrigation pipes	Networks	LM	8,954	0	–	8,954	0.0%

SCOPE ITEM	AREA	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
TSE pipes	Networks	LM	5,421	0	–	5,421	0.0%
LV cables	Networks	LM	13,353	0	–	13,353	0.0%
Telecom ducts	Networks	LM	5,770	0	–	5,770	0.0%
Street-light poles	Networks	EA	139	0	–	139	0.0%
Lean concrete	Fence and guard room	m³	1,933	1,914	–	19	99.0%
	Utility buildings	m³	248	111	–	137	44.8%
	Total	m³	**2,181**	**2,025**	**–**	**156**	**92.8%**
Foundations	Fence and guard room	m³	2,119	2,102	–	17	99.2%
	Utility buildings	m³	781	246	–	535	31.5%
	Total	m³	**2,900**	**2,348**	**–**	**552**	**81.0%**
Columns	Fence and guard room	m³	440	328	–	112	74.5%
	Utility buildings	m³	137	33	–	104	24.1%
	Total	m³	**577**	**361**	**–**	**216**	**62.6%**
Walls	Fence and guard room	m³	1,328	996	–	332	75.0%
Grade beams	Utility buildings	m³	460	460	–	0	100.0%
Slab on grade	Utility buildings	m³	119	119	–	0	100.0%
Brickwork	Fence and guard room	m²	11,754	4,260	–	7,494	36.2%
Bituminous coating	Fence and guard room	m²	51,678	12,532	–	39,146	24.3%

Buildings and earthworks

Fence and guard room foundations are almost complete and walls are at 75%. Utility building grade beams and slabs are complete, but their columns are at 24%. Embankment fill is at 41% and road subgrade at 14%; the storm pond riprap is at 45%.

No network installed yet

No pipes, manholes, cables or ducts are recorded as installed for any network. The sheet plans 5,698 m of storm pipes and 1,768 m of sewer pipes by this date, and none of the road pavement layers has started.

Milestones

The weekly report keeps every milestone on its baseline date, while the P6 update moves most of them by three to nine months. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 VS BASELINE (DAYS)	STATUS
Site handover	06-Jan-2026	06-Jan-2026	06-Jan-2026 (actual)	0	✓ Done
Execution plan and baseline schedule	05-Feb-2026	05-Feb-2026	05-Feb-2026 (actual)	0	✓ Done
Shop drawing and material approval	16-Feb-2026	16-Feb-2026	22-Nov-2026	+279	▼ Late
Mobilisation	08-Mar-2026	08-Mar-2026	07-Mar-2026 (actual)	−1	✓ Done
Potable water network	14-Dec-2026	14-Dec-2026	12-May-2027	+149	▼ Late
Irrigation network	27-Dec-2026	27-Dec-2026	12-May-2027	+136	▼ Late

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 VS BASELINE (DAYS)	STATUS
Medium-voltage network	07-Jan-2027	07-Jan-2027	17-Apr-2027	+100	▼ Late
Telecom network	11-Jan-2027	11-Jan-2027	12-May-2027	+121	▼ Late
Storm drainage network	13-Jan-2027	13-Jan-2027	11-May-2027	+118	▼ Late
Sewage network	26-Jan-2027	26-Jan-2027	04-Mar-2027	+37	▼ At risk
TSE network	26-Jan-2027	26-Jan-2027	05-Jun-2027	+130	▼ Late
Street lighting network	09-Feb-2027	09-Feb-2027	11-May-2027	+91	▼ Late
Road works	–	–	12-May-2027	–	▼ After contract date
Storm drainage ponds	–	–	05-May-2027	–	▼ After contract date
Sewage and water pump stations	–	–	23-Jun-2027	–	▼ After contract date
Control room	–	–	12-Jul-2027	–	▼ After contract date
Project completion	05-Mar-2027	05-Mar-2027	15-Jul-2027	+132	▼ Late

The weekly report and the P6 update disagree on every open milestone.

The weekly report shows all milestones on their baseline dates with zero days of change, including shop drawing and material approval (16-Feb-2026), which is still open. The P6 update moves every network past its baseline and finishes the project on 15-Jul-2027. The P6 file gives no total float values, so float is not shown.

Procurement of key materials

Share of total quantity delivered to site. Source: Procurement sheet, weekly report 26-Oct-2026.



Only pipes have started to arrive


Potable water, TSE and storm pipes are 14–26% delivered. Sewage pipes, all manholes, catch basins, covers, valves and fire hydrants, and all 107 material lines for the buildings and tanks are still at 0%.

Deliveries due in the next weeks

Storm manholes are due between 28-Oct and 08-Nov-2026, storm pipes and sewage pipes by 25 and 28-Nov-2026, and storm catch basins by 01-Dec-2026.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

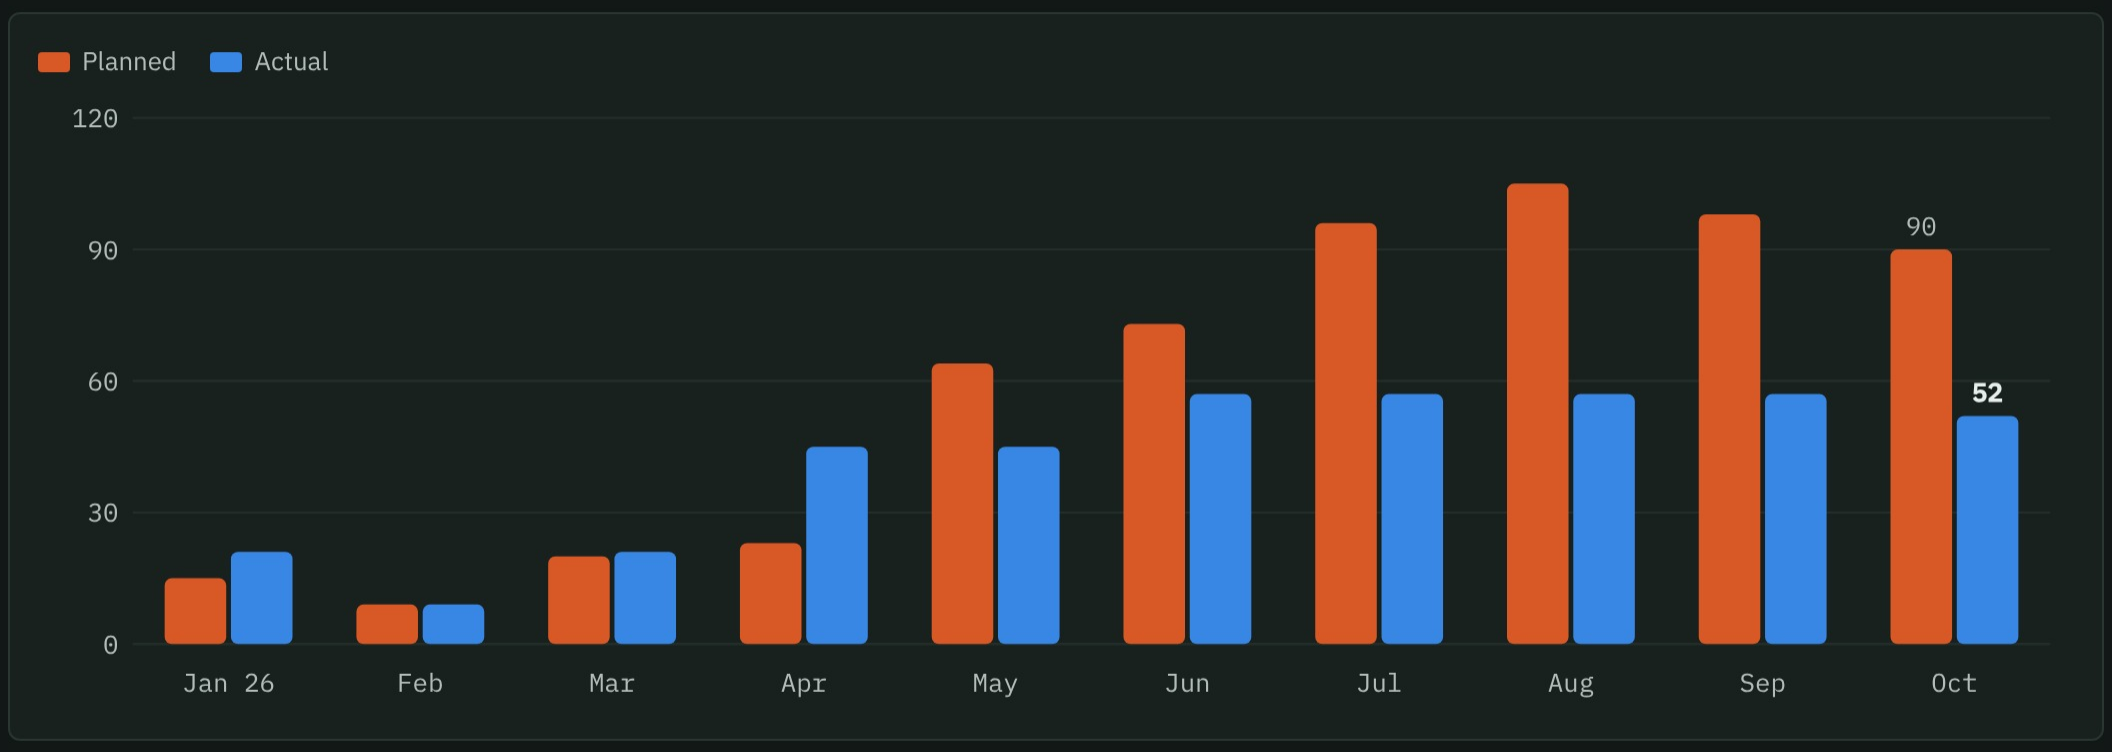

October head count is 52 against 90 planned (−42%): 30 manual workers against 81 planned, and 22 staff against 9 planned. Planned manual labour peaks at 96 in August 2026.

Cost and invoicing

Contract value

Original contract value	93,388,079
Change orders	0
Potential changes	0
Advance payment (10%)	9,338,808

All values in SAR. The contract summary in the same workbook gives 93,388,697 including VAT.

Invoices

Invoices submitted	4
Gross value	10,524,342
Retention	0
Deductions and penalties	165,500
Net amount	10,358,842
PM-approved / paid	0 / 0

Invoicing is 11.3% of the contract value against 20.8% physical progress. None of the four invoices is recorded as approved by the PM or paid.

Health, safety and quality

Safety Score 0.89

Safe man-hours (cumulative)	123,030
Man-hours this week	3,900
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	9 / 28

Quality Score 0.84

NCRs issued / open	4 / 4
Site instructions open	5
FIRs issued / closed	3 / 3
MIRs issued	0
Shop drawings submitted	53
Material submittals	19
Material submittals with consultant	5

Three NCRs have been open for 31–60 days. The scores come from a QC checklist dated 14-Apr-2026 and an HSE inspection covering 27-Jan to 03-Feb-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Advance payment and invoices	Client	Risk score 25 of 25. The P6 update still shows receipt of the advance payment as not started, and none of the four invoices is approved or paid.
Testing of executed works	Contractor	Risk score 20. Delays in testing, or failed tests, could lead to rework and delay handover.
Tie-in to existing networks	Client / Consultant	Risk score 16. The existing infrastructure may not be ready for connection, delaying commissioning.
Groundwater	Contractor	Risk score 16. Excavations may need continuous dewatering, which would slow trench and foundation works.
Material supply	Contractor	Risk score 15. Most network materials are still undelivered while installation is planned to be well advanced.

Source: Risk Log sheet. Both items in the issue log (site debris and the advance payment) are marked closed. The risk log also lists an opportunity: possible BOQ savings after re-measurement of quantities.

Data notes

- Only one weekly report has been uploaded for this project (W04 folder), so week-on-week figures such as quantities executed this week cannot be computed yet.
- The Milestones sheet states contract week 42 of 60, used as the report week. Whole weeks from site handover to the data date give 41.
- Planned progress to date is 36.4% in the progress summary but 34.3% for October in the monthly chart data.
- The weekly report forecasts completion on 05-Mar-2027 with zero variance, while the P6 update and the WBS summary PDF dated 26-Oct-2026 both finish on 15-Jul-2027. The recovery plan summary in the chart data finishes on 06-Mar-2027.
- In the dashboard's progress overview, the Roads and CCTV rows have their names swapped; the Progress sheet was used instead.
- The Conclusion sheet and the dashboard label cost-based progress as "actual" progress; it is not used in this report.
- The Conclusion sheet is headed "Dammam", reports 260,000 m³ of earthworks against 428,344 m³ in the Major Quantities sheet, and gives network lengths that differ from the Procurement sheet (for example storm pipes 4,838 m against 4,672 m).
- The invoice summary says 3 invoices were submitted, but the invoice log lists 4 with a total of 10,524,342 SAR. The log also shows a revised contract value of 21,100,000 and an EAC of 20,900,000, which do not match this contract.
- Several sheets carry other projects' identifiers or old dates: the QC checklist and FIR summary use project DHRT-02-001, the risk register uses DAMT-01-002 (Dammam), and the HSE inspection covers 27-Jan to 03-Feb-2026.
- The issue log closes the advance payment issue, but the P6 update and the risk log both show it as still open.
- The dashboard's resources panel shows January head counts (9.9 planned, 12 actual) instead of October.
- The Schedule sheet counts 1,271 activities; the uploaded P6 file has 1,065.
- The physical forecast curve ends at 100.4% in February 2027.
- The Procurement sheet marks the potable water pipe delivery finish of 09-Jan-2027 as actual, although the date is in the future.
- The uploaded PowerPoint is the MODON report guide with an older data snapshot (contract week 35 of 60, 95,730 man-hours); it was not used for figures.
