
egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14

WBS L5

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-004-Road Development for		383	25-Jun-26	24-Aug-27	25-Jun-26A	14-Oct-27	6,317,560.67	11,020,157.62	33,040,004.00	19.12%	33.35%	-43
Key Milestones		383	25-Jun-26	24-Aug-27	25-Jun-26A	14-Oct-27	0.00	0.00	0.00	0%	0%	-43
General Milestone		383	25-Jun-26	24-Aug-27	25-Jun-26A	14-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-KI	Project Commencement Date	0	25-Jun-26		25-Jun-26A		0.00	0.00	0.00	100%	100%	0
MKH2-02-004-KI	Project Completion Date	0		24-Aug-27		14-Oct-27	0.00	0.00	0.00	0%	0%	-43
Contractual Milestone		377	12-Jul-26	24-Aug-27	12-Jul-26A	14-Oct-27	0.00	0.00	0.00	0%	0%	-43
Engineering & Mobilization		64	12-Jul-26	23-Aug-26	12-Jul-26A	19-Sep-26A	0.00	0.00	0.00	0%	0%	-23
MKH2-02-004-I	Completion of Mobilization	0		23-Jul-26		15-Aug-26A	0.00	0.00	0.00	100%	100%	-18
MKH2-02-004-I	Submission of the Work Plan (Basel	0		12-Jul-26		12-Jul-26A	0.00	0.00	0.00	100%	100%	1
MKH2-02-004-I	Submission and Approval of Drawing	0		23-Aug-26		19-Sep-26A	0.00	0.00	0.00	100%	100%	-23
Construction		156	24-Feb-27	24-Aug-27	10-Apr-27	14-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-I	Completion of Road Works	0		24-Apr-27		15-Jun-27	0.00	0.00	0.00	0%	0%	-41
MKH2-02-004-I	Completion of Storm Water Drainag	0		24-Feb-27		10-Apr-27	0.00	0.00	0.00	0%	0%	-35
MKH2-02-004-I	Completion of Entire Project	0		24-Aug-27		14-Oct-27	0.00	0.00	0.00	0%	0%	-43
Mobilization		40	25-Jun-26	23-Jul-26	25-Jun-26A	17-Aug-26A	0.00	0.00	0.00	0%	0%	-21
Site Facilities & Offices		40	25-Jun-26	23-Jul-26	25-Jun-26A	17-Aug-26A	0.00	0.00	0.00	0%	0%	-21
MKH2-02-004-M	Site Layout Plan	5	25-Jun-26	30-Jun-26	25-Jun-26A	30-Jun-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-M	Clear & Grub for Offices & Access Ro	4	01-Jul-26	05-Jul-26	01-Jul-26A	05-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-M	Construct Site Access Roads	3	01-Jul-26	04-Jul-26	01-Jul-26A	04-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-M	Construct Temporary Fence	7	06-Jul-26	13-Jul-26	06-Jul-26A	13-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-M	Construct Site Offices & Storage	17	05-Jul-26	23-Jul-26	05-Jul-26A	15-Aug-26A	0.00	0.00	0.00	100%	100%	-19
MKH2-02-004-M	Install Project Signs	10	05-Jul-26	15-Jul-26	12-Aug-26A	17-Aug-26A	0.00	0.00	0.00	100%	100%	-28
MKH2-02-004-M	Install Site Facilities	4	14-Jul-26	18-Jul-26	14-Jul-26A	16-Aug-26A	0.00	0.00	0.00	100%	100%	-25
MKH2-02-004-M	Electrical Works & Connections	7	14-Jul-26	21-Jul-26	14-Jul-26A	16-Aug-26A	0.00	0.00	0.00	100%	100%	-22
MKH2-02-004-M	Construct Parking Sheds	7	14-Jul-26	21-Jul-26	14-Jul-26A	16-Aug-26A	0.00	0.00	0.00	100%	100%	-22
MKH2-02-004-M	Mobilization of Equipment	7	16-Jul-26	23-Jul-26	25-Jun-26A	04-Jul-26A	0.00	0.00	0.00	100%	100%	17
MKH2-02-004-M	Mobilization of Manpower	5	19-Jul-26	23-Jul-26	25-Jun-26A	30-Jun-26A	0.00	0.00	0.00	100%	100%	20
Topographic Survey		20	25-Jun-26	18-Jul-26	25-Jun-26A	18-Jul-26A	0.00	0.00	0.00	0%	0%	0
MKH2-02-004-M	Site Survey Works	20	25-Jun-26	18-Jul-26	25-Jun-26A	18-Jul-26A	0.00	0.00	0.00	100%	100%	0
Permit's and Authority Approvals		20	25-Jun-26	18-Jul-26	25-Jun-26A	18-Jul-26A	0.00	0.00	0.00	0%	0%	0
MKH2-02-004-M	Excavation & Backfilling Permit	20	25-Jun-26	18-Jul-26	25-Jun-26A	18-Jul-26A	0.00	0.00	0.00	100%	100%	0
Preliminary Submittals		16	05-Jul-26	23-Jul-26	05-Jul-26A	19-Jul-26A	0.00	0.00	0.00	0%	0%	4
Preparation and Submittal by Contractor's		13	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	0%	0%	0
MKH2-02-004-I	Preparation and Submittal of Detaile	7	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-I	Preparation and Submittal of Project	7	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-I	Preparation and Submittal of Quality	7	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-I	Preparation and Submittal of Safety I	7	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-I	Preparation and Submittal of Organi	7	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	100%	100%	0
MKH2-02-004-I	Preparation and Submittal of Comm	7	05-Jul-26	12-Jul-26	05-Jul-26A	12-Jul-26A	0.00	0.00	0.00	100%	100%	0
Approval by the Employer's		10	13-Jul-26	23-Jul-26	13-Jul-26A	19-Jul-26A	0.00	0.00	0.00	0%	0%	4
MKH2-02-004-I	Approval of Detailed Work Order Pro	10	13-Jul-26	23-Jul-26	13-Jul-26A	13-Jul-26A	0.00	0.00	0.00	100%	100%	9
MKH2-02-004-I	Approval of Project Execution Plan	10	13-Jul-26	23-Jul-26	13-Jul-26A	15-Jul-26A	0.00	0.00	0.00	100%	100%	7
MKH2-02-004-I	Approval of Quality Management Pla	10	13-Jul-26	23-Jul-26	13-Jul-26A	19-Jul-26A	0.00	0.00	0.00	100%	100%	4
MKH2-02-004-I	Approval of Safety Management Plan	10	13-Jul-26	23-Jul-26	13-Jul-26A	14-Jul-26A	0.00	0.00	0.00	100%	100%	8
MKH2-02-004-I	Approval of Organization Chart	10	13-Jul-26	23-Jul-26	13-Jul-26A	14-Jul-26A	0.00	0.00	0.00	100%	100%	8
MKH2-02-004-I	Approval of Comminumcation Plan	10	13-Jul-26	23-Jul-26	13-Jul-26A	14-Jul-26A	0.00	0.00	0.00	100%	100%	8
Engineering		64	01-Jul-26	23-Aug-26	06-Jul-26A	19-Sep-26A	0.00	0.00	0.00	0%	0%	-23
Shop Drawings		64	19-Jul-26	17-Aug-26	06-Jul-26A	19-Sep-26A	0.00	0.00	0.00	0%	0%	-28

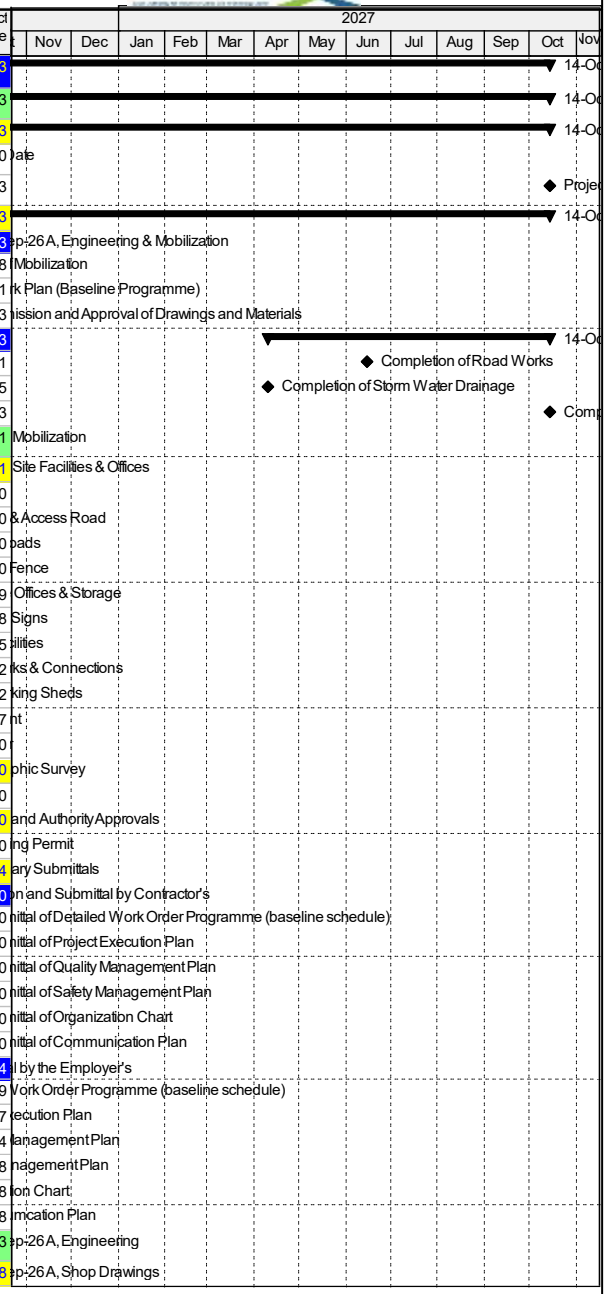

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14
WBS L5

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Shop Drawings Submittal		16	19-Jul-26	05-Aug-26	06-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	23
Shop Drawings Submittal for Road Works		16	19-Jul-26	05-Aug-26	06-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	23
MKH2-02-004-	Shop DWG Submittal for Topograph	8	19-Jul-26	27-Jul-26	06-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	15
MKH2-02-004-	Shop DWG Submittal for Road Layc	8	28-Jul-26	05-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	100%	100%	26
MKH2-02-004-	Shop DWG Submittal for Typical Cro	8	28-Jul-26	05-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	100%	100%	26
MKH2-02-004-	Shop DWG Submittal for Road Settir	8	28-Jul-26	05-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	100%	100%	26
MKH2-02-004-	Shop DWG Submittal for Road Profil	8	28-Jul-26	05-Aug-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	100%	100%	26
MKH2-02-004-	Shop DWG Submittal for Grading La	8	28-Jul-26	05-Aug-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	23
MKH2-02-004-	Shop DWG Submittal for Curb Settin	8	28-Jul-26	05-Aug-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	23
MKH2-02-004-	Shop DWG Submittal for Signing & M	8	28-Jul-26	05-Aug-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	23
MKH2-02-004-	Shop DWG Submittal for Standards	8	28-Jul-26	05-Aug-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	23
Shop Drawings Submittal for Stormwater Network		8	19-Jul-26	27-Jul-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	15
MKH2-02-004-	Shop DWG Submittal for Stormwate	8	19-Jul-26	27-Jul-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	15
MKH2-02-004-	Shop DWG Submittal for Stormwate	8	19-Jul-26	27-Jul-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	15
MKH2-02-004-	Shop DWG Submittal for Stormwate	8	19-Jul-26	27-Jul-26	09-Jul-26 A	09-Jul-26 A	0.00	0.00	0.00	100%	100%	15
Shop Drawings Approval		64	28-Jul-26	17-Aug-26	06-Jul-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%	-28
Shop Drawings Approval for Road Works		64	28-Jul-26	17-Aug-26	06-Jul-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%	-28
MKH2-02-004-	Shop DWG Approval for Topographi	10	28-Jul-26	08-Aug-26	03-Aug-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	4
MKH2-02-004-	Shop DWG Approval for Road Layo	10	06-Aug-26	17-Aug-26	06-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	100%	100%	34
MKH2-02-004-	Shop DWG Approval for Typical Cro	10	06-Aug-26	17-Aug-26	06-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	100%	100%	35
MKH2-02-004-	Shop DWG Approval for Road Settir	10	06-Aug-26	17-Aug-26	03-Aug-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-004-	Shop DWG Approval for Road Profil	10	06-Aug-26	17-Aug-26	06-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	100%	100%	34
MKH2-02-004-	Shop DWG Approval for Grading La	10	06-Aug-26	17-Aug-26	03-Aug-26 A	06-Aug-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-004-	Shop DWG Approval for Curb Settin	10	06-Aug-26	17-Aug-26	09-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	100%	100%	30
MKH2-02-004-	Shop DWG Approval for Signing & M	10	06-Aug-26	17-Aug-26	16-Sep-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%	-28
MKH2-02-004-	Shop DWG Approval for Standards I	10	06-Aug-26	17-Aug-26	09-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	100%	100%	17
Shop Drawings Approval for Storm Network		10	28-Jul-26	08-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	0%	0%	14
MKH2-02-004-	Shop DWG Approval for Stormwater	10	28-Jul-26	08-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%	14
MKH2-02-004-	Shop DWG Approval for Stormwater	10	28-Jul-26	08-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%	14
MKH2-02-004-	Shop DWG Approval for Stormwater	10	28-Jul-26	08-Aug-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%	14
Method Statements		34	01-Jul-26	11-Aug-26	11-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	18
Method Statements Submittal		24	01-Jul-26	30-Jul-26	11-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	11
MKH2-02-004-M	Preparation & Submission of Methoc	8	01-Jul-26	09-Jul-26	11-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	100%	100%	-3
MKH2-02-004-M	Preparation & Submission of Methoc	8	11-Jul-26	19-Jul-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	2
MKH2-02-004-M	Preparation & Submission of Methoc	10	20-Jul-26	30-Jul-26	16-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	100%	100%	11
Method Statements Approval		26	11-Jul-26	11-Aug-26	11-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	18
MKH2-02-004-M	Approval of Method Statement for Ea	10	11-Jul-26	21-Jul-26	11-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-004-M	Approval of Method Statement for Cc	10	20-Jul-26	30-Jul-26	16-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	100%	100%	8
MKH2-02-004-M	Approval of Method Statement for As	10	01-Aug-26	11-Aug-26	18-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	100%	100%	18
Pre-qualification and Material		52	06-Jul-26	23-Aug-26	11-Jul-26 A	29-Aug-26 A	0.00	0.00	0.00	0%	0%	-5
Pre-qualification		45	06-Jul-26	04-Aug-26	11-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	0%	0%	2
Road Works - Civil		45	19-Jul-26	04-Aug-26	11-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	0%	0%	2
Aggregate Base Course		15	19-Jul-26	04-Aug-26	11-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	0%	0%	17
MKH2-02-00	Pre-Qualification Submittal for Aggre	5	19-Jul-26	23-Jul-26	11-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-00	Pre-Qualification Approval for Aggre	10	25-Jul-26	04-Aug-26	11-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	100%	100%	17
Bituminous Base Course		15	19-Jul-26	04-Aug-26	28-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	0%	0%	2
MKH2-02-00	Pre-Qualification Submittal for Bitumi	5	19-Jul-26	23-Jul-26	28-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%	-8
MKH2-02-00	Pre-Qualification Approval for Bitumir	10	25-Jul-26	04-Aug-26	28-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%	2
Precast Concrete Kerb		26	19-Jul-26	04-Aug-26	11-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	0%	0%	17
MKH2-02-00	Pre-Qualification Submittal for Precas	5	19-Jul-26	23-Jul-26	11-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-00	Pre-Qualification Approval for Precas	10	25-Jul-26	04-Aug-26	11-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	100%	100%	17

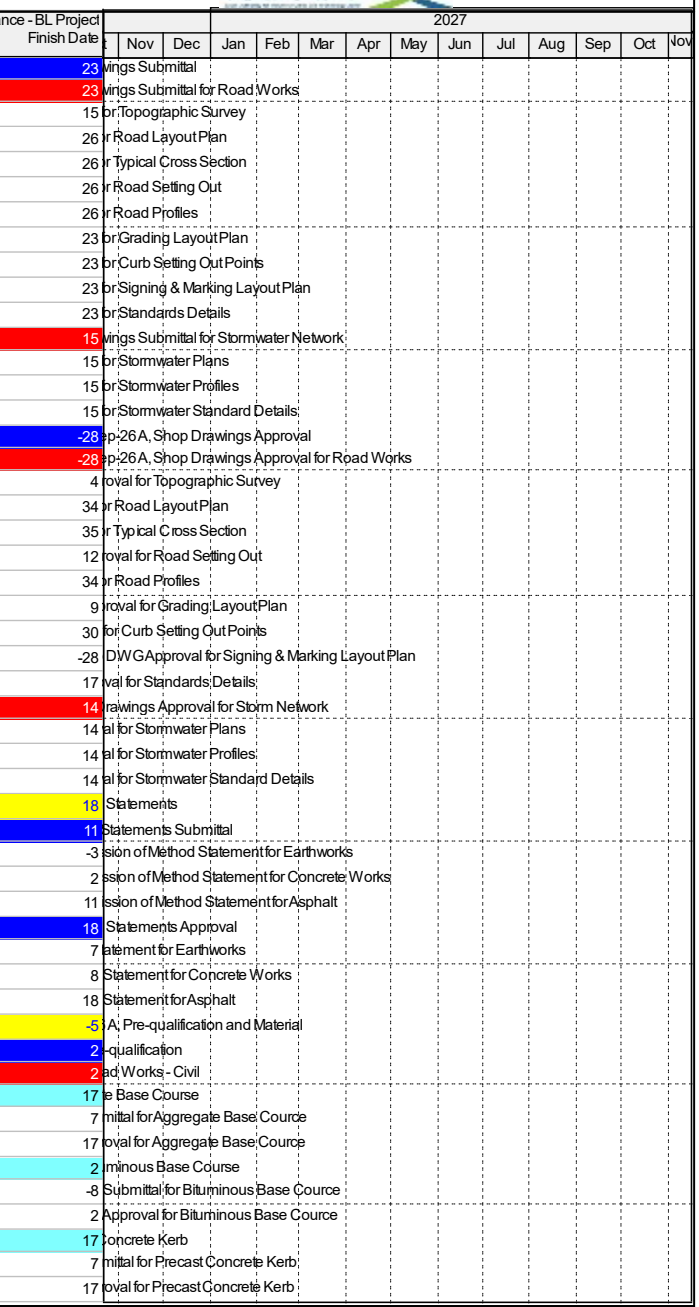

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14
WBS L5

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Interlocking Block Pavers		15	19-Jul-26	04-Aug-26	12-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	0%	0%	18
MKH2-02-00	Pre-Qualification Submittal for Interlo	5	19-Jul-26	23-Jul-26	12-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	100%	100%	8
MKH2-02-00	Pre-Qualification Approval for Interloc	10	25-Jul-26	04-Aug-26	12-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	100%	100%	18
Pavement Markings		15	19-Jul-26	04-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	0%	0%	16
MKH2-02-00	Pre-Qualification Submittal for Paven	5	19-Jul-26	23-Jul-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-00	Pre-Qualification Approval for Paver	10	25-Jul-26	04-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	16
Traffic Signs		15	19-Jul-26	04-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	0%	0%	16
MKH2-02-00	Pre-Qualification Submittal for Traffic S	5	19-Jul-26	23-Jul-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-00	Pre-Qualification Approval for Traffic S	10	25-Jul-26	04-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	16
Storm Network		20	06-Jul-26	28-Jul-26	11-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	0%	0%	12
GRP Pipes		15	06-Jul-26	22-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	10
MKH2-02-00	Pre-Qualification Submittal for GRP F	5	06-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-00	Pre-Qualification Approval for GRP P	10	12-Jul-26	22-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	100%	100%	10
Catch Basin		15	06-Jul-26	22-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	10
MKH2-02-00	Pre-Qualification Submittal for Catch	5	06-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-00	Pre-Qualification Approval for Catch I	10	12-Jul-26	22-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	100%	100%	10
Inlet Manholes		15	12-Jul-26	28-Jul-26	13-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	0%	0%	12
MKH2-02-00	Pre-Qualification Submittal for Inlet M	5	12-Jul-26	16-Jul-26	13-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	100%	100%	2
MKH2-02-00	Pre-Qualification Approval for Inlet Ma	10	18-Jul-26	28-Jul-26	13-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	100%	100%	12
Material Submittal		52	23-Jul-26	23-Aug-26	11-Jul-26 A	29-Aug-26 A	0.00	0.00	0.00	0%	0%	-5
Road Works - Civil		46	05-Aug-26	23-Aug-26	19-Jul-26 A	29-Aug-26 A	0.00	0.00	0.00	0%	0%	-5
Aggregate Base Course		28	05-Aug-26	23-Aug-26	05-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-4
MKH2-02-00	Design Submittal for Aggregate Base	6	05-Aug-26	11-Aug-26	05-Aug-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	5
MKH2-02-00	Design Approval for Aggregate Base	10	12-Aug-26	23-Aug-26	22-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	-4
Bituminous Base Course		16	05-Aug-26	23-Aug-26	28-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	0%	0%	18
MKH2-02-00	Design Submittal for Bituminous Bas	6	05-Aug-26	11-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-00	Design Approval for Bituminous Base	10	12-Aug-26	23-Aug-26	28-Jul-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%	18
Precast Concrete Kerb		16	05-Aug-26	23-Aug-26	22-Aug-26 A	23-Aug-26 A	0.00	0.00	0.00	0%	0%	0
MKH2-02-00	Material Submittal for Precast Concre	6	05-Aug-26	11-Aug-26	22-Aug-26 A	23-Aug-26 A	0.00	0.00	0.00	100%	100%	-10
MKH2-02-00	Material Approval for Precast Concre	10	12-Aug-26	23-Aug-26	22-Aug-26 A	23-Aug-26 A	0.00	0.00	0.00	100%	100%	0
Interlocking Block Pavers		16	05-Aug-26	23-Aug-26	22-Aug-26 A	23-Aug-26 A	0.00	0.00	0.00	0%	0%	0
MKH2-02-00	Material Submittal for Interlocking Blo	6	05-Aug-26	11-Aug-26	22-Aug-26 A	23-Aug-26 A	0.00	0.00	0.00	100%	100%	-10
MKH2-02-00	Material Approval for Interlocking Bloc	10	12-Aug-26	23-Aug-26	22-Aug-26 A	23-Aug-26 A	0.00	0.00	0.00	100%	100%	0
Pavement Markings		16	05-Aug-26	23-Aug-26	27-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	0%	0%	-5
MKH2-02-00	Material Submittal for Pavement Mark	6	05-Aug-26	11-Aug-26	27-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	-15
MKH2-02-00	Material Approval for Pavement Mark	10	12-Aug-26	23-Aug-26	27-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	-5
Traffic Signs		16	05-Aug-26	23-Aug-26	19-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	0%	0%	29
MKH2-02-00	Material Submittal for Traffic Signs	6	05-Aug-26	11-Aug-26	19-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	100%	100%	19
MKH2-02-00	Material Approval for Trafic Signs	10	12-Aug-26	23-Aug-26	19-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	100%	100%	29
Storm Network		28	23-Jul-26	15-Aug-26	11-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	21
GRP Pipes		15	23-Jul-26	09-Aug-26	11-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	24
MKH2-02-00	Material Submittal for GRP Pipe	5	23-Jul-26	28-Jul-26	11-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	100%	100%	14
MKH2-02-00	Material Approval for GRP Pipe	10	29-Jul-26	09-Aug-26	11-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	100%	100%	24
Catch Basin		22	23-Jul-26	09-Aug-26	19-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	16
MKH2-02-00	Material Submittal for Catch Basin	5	23-Jul-26	28-Jul-26	19-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	100%	100%	8
MKH2-02-00	Material Approval for Catch Basin	10	29-Jul-26	09-Aug-26	19-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	100%	100%	16
Inlet Manholes		22	29-Jul-26	15-Aug-26	19-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	21
MKH2-02-00	Material Submittal for Inlet Manholes	5	29-Jul-26	03-Aug-26	19-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-00	Material Approval for Inlet Manholes	10	04-Aug-26	15-Aug-26	19-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	100%	100%	21
Procurement		139	10-Aug-26	30-Nov-26	15-Jul-26 A	20-Jan-27	0.00	0.00	0.00	0%	0%	-44
Road Works - Civil		80	24-Aug-26	30-Nov-26	30-Sep-26 A	20-Jan-27	0.00	0.00	0.00	0%	0%	-44

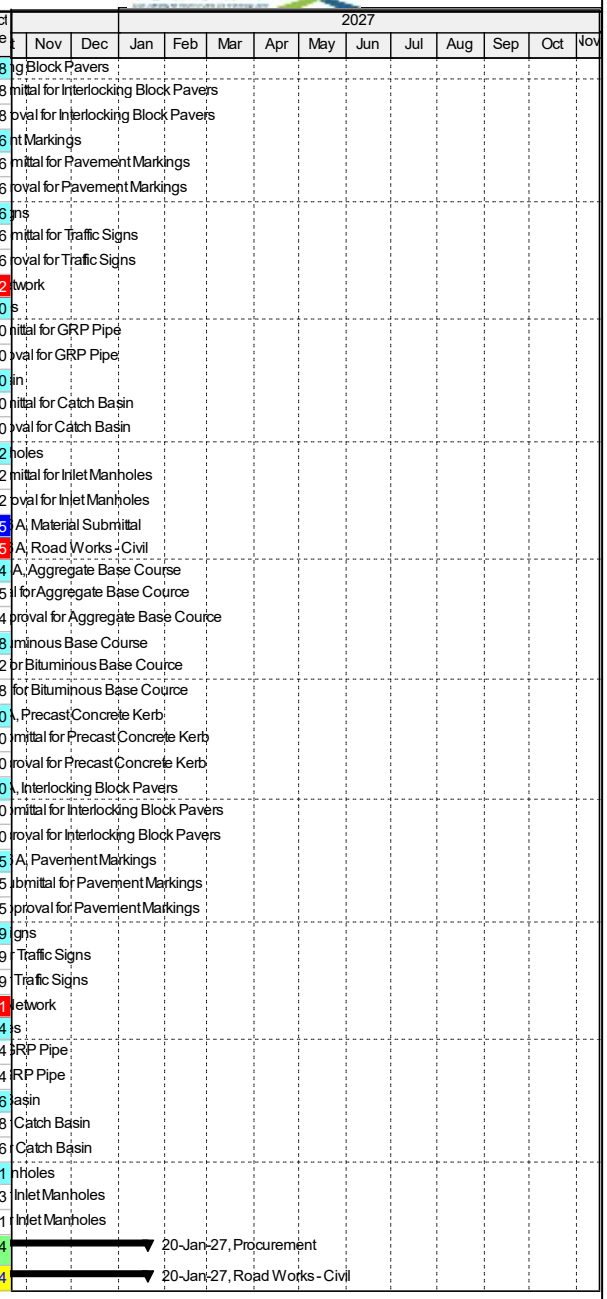

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14
WBS L5

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Aggregate Base Course		65	24-Aug-26	08-Nov-26	20-Oct-26	03-Jan-27	0.00	0.00	0.00	0%	0%	-48
MKH2-02-004-F	PO for Aggregate Base Course	5	24-Aug-26	29-Aug-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Aggregate Base	30	30-Aug-26	04-Oct-26	26-Oct-26	29-Nov-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Aggregate Base	30	05-Oct-26	08-Nov-26	30-Nov-26	03-Jan-27	0.00	0.00	0.00	43.33%	0%	-48
Bituminous Base Course		75	30-Aug-26	25-Nov-26	26-Oct-26	20-Jan-27	0.00	0.00	0.00	0%	0%	-48
MKH2-02-004-F	PO for Bituminous Base Course	5	30-Aug-26	03-Sep-26	26-Oct-26	31-Oct-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Bituminous Base	35	05-Sep-26	15-Oct-26	01-Nov-26	10-Dec-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Bituminous Base	35	17-Oct-26	25-Nov-26	12-Dec-26	20-Jan-27	0.00	0.00	0.00	8.57%	0%	-48
Precast Concrete Curb		65	05-Sep-26	19-Nov-26	01-Nov-26	14-Jan-27	0.00	0.00	0.00	0%	0%	-48
MKH2-02-004-F	PO for Precast Concrete Curb	5	05-Sep-26	09-Sep-26	01-Nov-26	05-Nov-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Fabrication for Precast Conc	30	10-Sep-26	15-Oct-26	07-Nov-26	10-Dec-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Precast Concret	30	17-Oct-26	19-Nov-26	12-Dec-26	14-Jan-27	0.00	0.00	0.00	10%	0%	-48
Interlocking Block Pavers		63	10-Sep-26	23-Nov-26	07-Nov-26	18-Jan-27	0.00	0.00	0.00	0%	0%	-48
MKH2-02-004-F	PO for Interlocking Block Pavers	3	10-Sep-26	13-Sep-26	07-Nov-26	09-Nov-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Fabrication for Interlocking B	30	14-Sep-26	19-Oct-26	10-Nov-26	14-Dec-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Interlocking Bloc	30	20-Oct-26	23-Nov-26	15-Dec-26	18-Jan-27	0.00	0.00	0.00	0%	0%	-48
Pavement Markings		54	14-Sep-26	16-Nov-26	10-Nov-26	11-Jan-27	0.00	0.00	0.00	0%	0%	-48
MKH2-02-004-F	PO for Pavement Markings	4	14-Sep-26	17-Sep-26	10-Nov-26	14-Nov-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Fabrication for Pavement Ma	25	19-Sep-26	18-Oct-26	15-Nov-26	13-Dec-26	0.00	0.00	0.00	100%	0%	-48
MKH2-02-004-F	Material Delivery for Pavement Marki	25	19-Oct-26	16-Nov-26	14-Dec-26	11-Jan-27	0.00	0.00	0.00	4%	0%	-48
Traffic Signs		62	19-Sep-26	30-Nov-26	30-Sep-26 A	12-Oct-26 A	0.00	0.00	0.00	0%	0%	42
MKH2-02-004-F	PO for Traffic Signs	6	19-Sep-26	26-Sep-26	30-Sep-26 A	04-Oct-26 A	0.00	0.00	0.00	100%	100%	-7
MKH2-02-004-F	Material Fabrication for Traffic Signs	28	27-Sep-26	28-Oct-26	05-Oct-26 A	10-Oct-26 A	0.00	0.00	0.00	71.43%	100%	16
MKH2-02-004-F	Material Delivery for Traffic Signs	28	29-Oct-26	30-Nov-26	11-Oct-26 A	12-Oct-26 A	0.00	0.00	0.00	0%	100%	42
Stormwater Utilities		93	10-Aug-26	16-Nov-26	15-Jul-26 A	21-Nov-26	0.00	0.00	0.00	0%	0%	-4
GRP Pipes		57	10-Aug-26	29-Oct-26	15-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%	33
MKH2-02-004-F	PO for GRP Pipes	5	10-Aug-26	15-Aug-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	100%	100%	26
MKH2-02-004-F	Material Fabrication for GRP Pipes	16	16-Aug-26	02-Sep-26	16-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	100%	100%	38
MKH2-02-004-F	Material Delivery for GRP Pipes-Stag	16	03-Sep-26	21-Sep-26	27-Jul-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	42
MKH2-02-004-F	Material Delivery for GRP Pipes-Stag	16	22-Sep-26	11-Oct-26	09-Sep-26 A	14-Sep-26 A	0.00	0.00	0.00	100%	100%	22
MKH2-02-004-F	Material Delivery for GRP Pipes-Stag	16	12-Oct-26	29-Oct-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	43.75%	100%	33
Catch Basins		81	10-Aug-26	16-Nov-26	15-Jul-26 A	21-Nov-26	0.00	0.00	0.00	0%	0%	-4
MKH2-02-004-F	PO for Catch Basins	4	10-Aug-26	13-Aug-26	15-Jul-26 A	15-Jul-26 A	0.00	0.00	0.00	100%	100%	25
MKH2-02-004-F	Material Fabrication for Catch Basins	20	15-Aug-26	06-Sep-26	09-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	100%	100%	-5
MKH2-02-004-F	Material Delivery for Catch Basins-St	20	07-Sep-26	30-Sep-26	13-Sep-26 A	07-Oct-26 A	0.00	0.00	0.00	100%	100%	-6
MKH2-02-004-F	Material Delivery for Catch Basins-St	20	01-Oct-26	24-Oct-26	08-Oct-26 A	28-Oct-26	0.00	0.00	0.00	80%	80%	-4
MKH2-02-004-F	Material Delivery for Catch Basins-St	20	25-Oct-26	16-Nov-26	29-Oct-26	21-Nov-26	0.00	0.00	0.00	0%	0%	-4
Inlet Manholes		49	16-Aug-26	31-Oct-26	13-Aug-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%	34
MKH2-02-004-F	PO for Inlet Manholes	5	16-Aug-26	20-Aug-26	13-Aug-26 A	13-Aug-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-004-F	Material Fabrication for Inlet Manhole	20	22-Aug-26	13-Sep-26	15-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	100%	100%	22
MKH2-02-004-F	Material Delivery for Inlet Manholes-S	20	14-Sep-26	07-Oct-26	22-Aug-26 A	05-Sep-26 A	0.00	0.00	0.00	100%	100%	27
MKH2-02-004-F	Material Delivery for Inlet Manholes-S	20	08-Oct-26	31-Oct-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	50%	100%	34
Construction		289	25-Jul-26	03-Jun-27	07-Jul-26 A	24-Jul-27	6,317,560.67	11,020,157.62	33,040,004.00	19.12%	33.35%	-43
Roads		289	25-Jul-26	03-Jun-27	07-Jul-26 A	24-Jul-27	6,317,560.67	11,020,157.62	33,040,004.00	19.12%	33.35%	-43
Local 17		228	25-Jul-26	01-Mar-27	07-Jul-26 A	09-May-27	3,667,192.09	1,651,772.40	8,900,038.48	41.2%	18.56%	-56
Road Works		228	25-Jul-26	01-Mar-27	07-Jul-26 A	09-May-27	2,099,874.00	1,651,772.40	5,304,527.65	39.59%	31.14%	-56
Earthworks & Site grading		152	25-Jul-26	01-Dec-26	07-Jul-26 A	04-Feb-27	2,099,874.00	1,651,772.40	2,708,208.00	77.54%	60.99%	-56
MKH2-02-00	Road excavation [Local 17]-Stage 1	18	25-Jul-26	13-Aug-26	07-Jul-26 A	20-Aug-26 A	768,636.00	768,636.00	768,636.00	100%	100%	-6
MKH2-02-00	Road excavation [Local 17]-Stage 2	18	15-Aug-26	03-Sep-26	20-Aug-26 A	31-Oct-26	768,614.00	461,168.40	768,614.00	100%	60%	-48
MKH2-02-00	Road backfilling [Local 17]-Stage 1	18	25-Jul-26	13-Aug-26	15-Jul-26 A	01-Aug-26 A	281,312.00	281,312.00	281,312.00	100%	100%	11

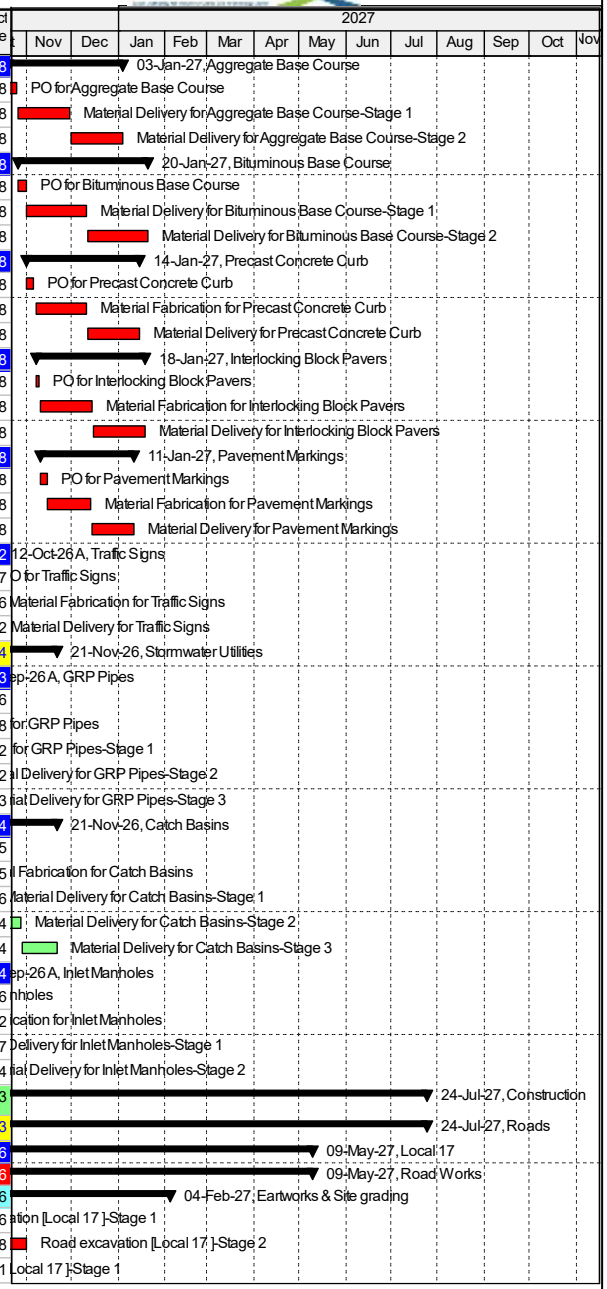

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14
WBS L5

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Road backfilling [Local 17]-Stage 2	18	15-Aug-26	03-Sep-26	01-Aug-26 A	05-Nov-26	281,312.00	140,656.00	281,312.00	100%	50%	-53
MKH2-02-00	Subgrade [Local 17]	15	28-Oct-26	14-Nov-26	02-Jan-27	18-Jan-27	0.00	0.00	236,170.00	0%	0%	-56
MKH2-02-00	Aggregate base course [Local 17]	15	15-Nov-26	01-Dec-26	19-Jan-27	04-Feb-27	0.00	0.00	372,164.00	0%	0%	-56
Asphalt Works		25	02-Dec-26	30-Dec-26	06-Feb-27	07-Mar-27	0.00	0.00	1,403,360.00	0%	0%	-56
MKH2-02-00	Prime Coat (MC1) [Local 17]	10	02-Dec-26	13-Dec-26	06-Feb-27	16-Feb-27	0.00	0.00	140,560.00	0%	0%	-56
MKH2-02-00	Bituminous base course [Local 17]	15	14-Dec-26	30-Dec-26	17-Feb-27	07-Mar-27	0.00	0.00	1,262,800.00	0%	0%	-56
Finishing Works		51	31-Dec-26	01-Mar-27	08-Mar-27	09-May-27	0.00	0.00	1,192,959.65	0%	0%	-56
Precast Concrete Curb		12	31-Dec-26	13-Jan-27	08-Mar-27	24-Mar-27	0.00	0.00	415,849.65	0%	0%	-56
MKH2-02-00	Installation of Precast Concrete curb	12	31-Dec-26	13-Jan-27	08-Mar-27	24-Mar-27	0.00	0.00	415,849.65	0%	0%	-56
Precast Interlocking block pavers		11	14-Jan-27	26-Jan-27	25-Mar-27	06-Apr-27	0.00	0.00	559,160.00	0%	0%	-56
MKH2-02-00	Installation of Interlocking block pave	11	14-Jan-27	26-Jan-27	25-Mar-27	06-Apr-27	0.00	0.00	559,160.00	0%	0%	-56
Pavement Markings		16	27-Jan-27	14-Feb-27	07-Apr-27	25-Apr-27	0.00	0.00	129,750.00	0%	0%	-56
MKH2-02-00	Pavement markings [Local 17]	8	27-Jan-27	04-Feb-27	07-Apr-27	15-Apr-27	0.00	0.00	69,750.00	0%	0%	-56
MKH2-02-00	(Speed Hump) with retroreflective The	8	06-Feb-27	14-Feb-27	17-Apr-27	25-Apr-27	0.00	0.00	60,000.00	0%	0%	-56
Traffic Signage		12	15-Feb-27	01-Mar-27	26-Apr-27	09-May-27	0.00	0.00	88,200.00	0%	0%	-56
MKH2-02-00	Installation of Traffic Signs [Local 17]	12	15-Feb-27	01-Mar-27	26-Apr-27	09-May-27	0.00	0.00	88,200.00	0%	0%	-56
Storm Water Drainage		109	15-Aug-26	02-Jan-27	20-Oct-26	24-Feb-27	1,567,318.09	0.00	3,595,510.83	43.59%	0%	-45
Pipe Works		63	15-Aug-26	27-Oct-26	20-Oct-26	31-Dec-26	1,300,008.43	0.00	1,368,373.77	95%	0%	-56
MKH2-02-00	Excavation & Compaction (FDT) [Lo	13	15-Aug-26	29-Aug-26	20-Oct-26	03-Nov-26	68,472.00	0.00	68,472.00	100%	0%	-56
MKH2-02-00	Excavation & Compaction (FDT) [Lo	13	30-Aug-26	13-Sep-26	04-Nov-26	18-Nov-26	68,365.34	0.00	68,365.34	100%	0%	-56
MKH2-02-00	Sand Bedding [Local 17]-Stage 1	8	30-Aug-26	07-Sep-26	04-Nov-26	12-Nov-26	68,472.00	0.00	68,472.00	100%	0%	-56
MKH2-02-00	Sand Bedding [Local 17]-Stage 2	8	14-Sep-26	22-Sep-26	19-Nov-26	28-Nov-26	68,365.34	0.00	68,365.34	100%	0%	-56
MKH2-02-00	Installation of GRP Pipe [Local 17]-S	14	08-Sep-26	24-Sep-26	14-Nov-26	29-Nov-26	342,360.11	0.00	342,360.11	100%	0%	-56
MKH2-02-00	Installation of GRP Pipe [Local 17]-S	14	26-Sep-26	11-Oct-26	30-Nov-26	15-Dec-26	341,826.84	0.00	341,826.84	100%	0%	-56
MKH2-02-00	Sand Cover & Warning Tape [Local	7	26-Sep-26	03-Oct-26	30-Nov-26	07-Dec-26	136,944.06	0.00	136,944.06	100%	0%	-56
MKH2-02-00	Sand Cover & Warning Tape [Local	7	12-Oct-26	19-Oct-26	16-Dec-26	23-Dec-26	136,730.75	0.00	136,730.75	100%	0%	-56
MKH2-02-00	Backfilling & Compaction [Local 17]-	7	04-Oct-26	11-Oct-26	08-Dec-26	15-Dec-26	68,472.00	0.00	68,472.00	100%	0%	-56
MKH2-02-00	Backfilling & Compaction [Local 17]-	7	20-Oct-26	27-Oct-26	24-Dec-26	31-Dec-26	0.00	0.00	68,365.34	0%	0%	-56
Manholes		35	08-Oct-26	17-Nov-26	30-Nov-26	09-Jan-27	235,763.89	0.00	778,020.83	30.3%	0%	-45
MKH2-02-00	Installation of Manholes [Local 17]-S	7	08-Oct-26	15-Oct-26	30-Nov-26	07-Dec-26	165,034.72	0.00	165,034.72	100%	0%	-45
MKH2-02-00	Installation of Manholes [Local 17]-S	7	17-Oct-26	24-Oct-26	08-Dec-26	15-Dec-26	70,729.17	0.00	165,034.72	42.86%	0%	-45
MKH2-02-00	Installation of Manholes [Local 17]-S	7	25-Oct-26	01-Nov-26	16-Dec-26	23-Dec-26	0.00	0.00	165,034.72	0%	0%	-45
MKH2-02-00	Installation of Manholes [Local 17]-S	7	02-Nov-26	09-Nov-26	24-Dec-26	31-Dec-26	0.00	0.00	165,034.72	0%	0%	-45
MKH2-02-00	Installation of Manholes [Local 17]-S	7	10-Nov-26	17-Nov-26	02-Jan-27	09-Jan-27	0.00	0.00	117,881.94	0%	0%	-45
Catch Basins		67	17-Oct-26	02-Jan-27	08-Dec-26	24-Feb-27	31,545.78	0.00	706,625.39	4.46%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	17-Oct-26	24-Oct-26	08-Dec-26	15-Dec-26	31,545.78	0.00	73,606.81	42.86%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	25-Oct-26	01-Nov-26	16-Dec-26	23-Dec-26	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	02-Nov-26	09-Nov-26	24-Dec-26	31-Dec-26	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	10-Nov-26	17-Nov-26	02-Jan-27	09-Jan-27	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	18-Nov-26	25-Nov-26	10-Jan-27	17-Jan-27	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	26-Nov-26	03-Dec-26	18-Jan-27	25-Jan-27	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	05-Dec-26	12-Dec-26	26-Jan-27	02-Feb-27	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	13-Dec-26	20-Dec-26	03-Feb-27	10-Feb-27	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	7	21-Dec-26	28-Dec-26	11-Feb-27	18-Feb-27	0.00	0.00	73,606.81	0%	0%	-45
MKH2-02-00	Construction of Catch basins [Local	4	29-Dec-26	02-Jan-27	20-Feb-27	24-Feb-27	0.00	0.00	44,164.09	0%	0%	-45
Concrete chambers Pipes		45	25-Oct-26	15-Dec-26	16-Dec-26	06-Feb-27	0.00	0.00	742,490.84	0%	0%	-45
MKH2-02-00	Excavation and Compaction (FDT) [	11	25-Oct-26	05-Nov-26	16-Dec-26	28-Dec-26	0.00	0.00	74,290.89	0%	0%	-45
MKH2-02-00	Excavation and Compaction (FDT) [	11	07-Nov-26	18-Nov-26	29-Dec-26	10-Jan-27	0.00	0.00	74,207.32	0%	0%	-45
MKH2-02-00	Installation of Pipes [Local 17]-Stage	12	07-Nov-26	19-Nov-26	29-Dec-26	11-Jan-27	0.00	0.00	222,872.57	0%	0%	-45
MKH2-02-00	Installation of Pipes [Local 17]-Stage	12	21-Nov-26	03-Dec-26	12-Jan-27	25-Jan-27	0.00	0.00	222,621.87	0%	0%	-45

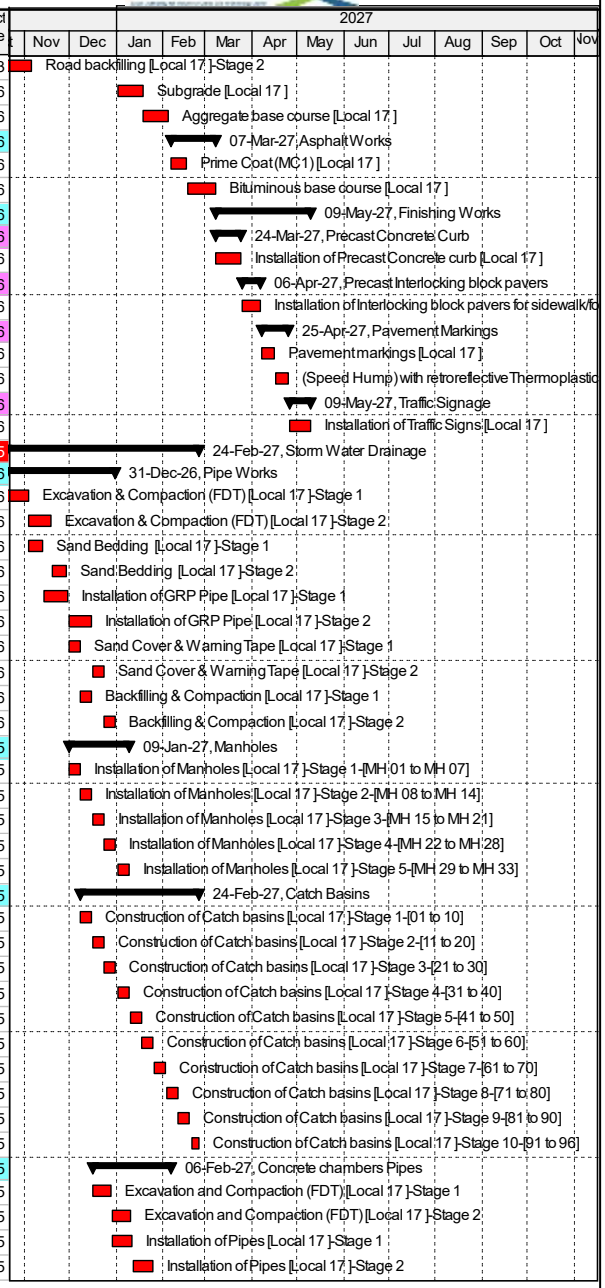

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Backfilling & Compaction [Local 17]-	10	21-Nov-26	01-Dec-26	12-Jan-27	23-Jan-27	0.00	0.00	74,290.89	0%	0%	-45
MKH2-02-00	Backfilling & Compaction [Local 17]-	10	05-Dec-26	15-Dec-26	26-Jan-27	06-Feb-27	0.00	0.00	74,207.32	0%	0%	-45
Local 11		192	05-Sep-26	28-Feb-27	05-Aug-26 A	06-May-27	1,485,474.61	2,271,649.82	5,488,541.48	27.07%	41.39%	-55
Road Works		192	05-Sep-26	28-Feb-27	05-Aug-26 A	06-May-27	1,307,556.00	1,176,180.00	3,300,493.47	39.62%	35.64%	-55
Eartworks & Site grading		127	05-Sep-26	14-Dec-26	05-Aug-26 A	15-Feb-27	1,307,556.00	1,176,180.00	1,686,316.00	77.54%	69.75%	-54
MKH2-02-00	Road excavation [Local 11]-Stage 1	11	05-Sep-26	16-Sep-26	05-Aug-26 A	03-Sep-26 A	478,610.00	478,610.00	478,610.00	100%	100%	11
MKH2-02-00	Road excavation [Local 11]-Stage 2	11	17-Sep-26	30-Sep-26	03-Sep-26 A	10-Oct-26 A	478,610.00	478,610.00	478,610.00	100%	100%	-8
MKH2-02-00	Road backfilling [Local 11]-Stage 1	11	05-Sep-26	16-Sep-26	09-Sep-26 A	24-Sep-26 A	175,168.00	175,168.00	175,168.00	100%	100%	-6
MKH2-02-00	Road backfilling [Local 11]-Stage 2	11	17-Sep-26	30-Sep-26	15-Oct-26 A	15-Nov-26	175,168.00	43,792.00	175,168.00	100%	25%	-39
MKH2-02-00	Subgrade [Local 11]	9	24-Nov-26	03-Dec-26	19-Jan-27	28-Jan-27	0.00	0.00	147,048.00	0%	0%	-48
MKH2-02-00	Aggregate base course [Local 11]	9	05-Dec-26	14-Dec-26	06-Feb-27	15-Feb-27	0.00	0.00	231,712.00	0%	0%	-54
Asphalt Works		22	15-Dec-26	09-Jan-27	17-Feb-27	18-Mar-27	0.00	0.00	873,600.00	0%	0%	-55
MKH2-02-00	Prime Coat (MC1) [Local 11]	10	15-Dec-26	26-Dec-26	17-Feb-27	01-Mar-27	0.00	0.00	87,360.00	0%	0%	-55
MKH2-02-00	Bituminous base course [Local 11]	12	27-Dec-26	09-Jan-27	02-Mar-27	18-Mar-27	0.00	0.00	786,240.00	0%	0%	-55
Finishing Works		42	10-Jan-27	28-Feb-27	20-Mar-27	06-May-27	0.00	0.00	740,577.47	0%	0%	-55
Precast Concrete Curb		11	10-Jan-27	21-Jan-27	20-Mar-27	31-Mar-27	0.00	0.00	258,972.47	0%	0%	-55
MKH2-02-0(	Installation of Precast Concrete curb	11	10-Jan-27	21-Jan-27	20-Mar-27	31-Mar-27	0.00	0.00	258,972.47	0%	0%	-55
Precast Interlocking block pavers		10	23-Jan-27	02-Feb-27	01-Apr-27	12-Apr-27	0.00	0.00	348,180.00	0%	0%	-55
MKH2-02-0(	Installation of Interlocking block pave	10	23-Jan-27	02-Feb-27	01-Apr-27	12-Apr-27	0.00	0.00	348,180.00	0%	0%	-55
Pavement Markings		14	03-Feb-27	18-Feb-27	13-Apr-27	28-Apr-27	0.00	0.00	79,425.00	0%	0%	-55
MKH2-02-0(	Pavement markings [Local 11]	7	03-Feb-27	10-Feb-27	13-Apr-27	20-Apr-27	0.00	0.00	43,425.00	0%	0%	-55
MKH2-02-0(	(Speed Hump) with retroreflective The	7	11-Feb-27	18-Feb-27	21-Apr-27	28-Apr-27	0.00	0.00	36,000.00	0%	0%	-55
Traffic Signage		7	20-Feb-27	28-Feb-27	29-Apr-27	06-May-27	0.00	0.00	54,000.00	0%	0%	-55
MKH2-02-0(	Installation of Traffic Signs [Local 11]	7	20-Feb-27	28-Feb-27	29-Apr-27	06-May-27	0.00	0.00	54,000.00	0%	0%	-55
Storm Water Drainage		43	01-Oct-26	19-Dec-26	17-Sep-26 A	26-Dec-26	177,918.61	1,095,469.82	2,188,048.01	8.13%	50.07%	-6
Pipe Works		39	01-Oct-26	23-Nov-26	17-Sep-26 A	15-Dec-26	177,918.61	737,108.71	909,760.58	19.56%	81.02%	-19
MKH2-02-00	Excavation & Compaction (FDT) [Lo	8	01-Oct-26	10-Oct-26	17-Sep-26 A	08-Oct-26 A	45,541.34	45,541.34	45,541.34	100%	100%	1
MKH2-02-00	Excavation & Compaction (FDT) [Lo	8	11-Oct-26	19-Oct-26	10-Oct-26 A	19-Nov-26	45,434.69	36,347.75	45,434.69	100%	80%	-27
MKH2-02-00	Sand Bedding [Local 11]-Stage 1	6	11-Oct-26	17-Oct-26	20-Sep-26 A	08-Oct-26 A	45,541.34	45,541.34	45,541.34	100%	100%	7
MKH2-02-00	Sand Bedding [Local 11]-Stage 2	6	20-Oct-26	26-Oct-26	12-Oct-26 A	23-Nov-26	0.00	27,260.81	45,434.69	0%	60%	-24
MKH2-02-00	Installation of GRP Pipe [Local 11]-St	11	18-Oct-26	29-Oct-26	01-Oct-26 A	11-Oct-26 A	41,401.24	227,706.80	227,706.80	18.18%	100%	16
MKH2-02-00	Installation of GRP Pipe [Local 11]-St	11	31-Oct-26	11-Nov-26	12-Oct-26 A	06-Dec-26	0.00	136,304.12	227,173.53	0%	60%	-21
MKH2-02-00	Sand Cover & Warning Tape [Local	5	31-Oct-26	04-Nov-26	11-Oct-26 A	17-Oct-26 A	0.00	91,082.73	91,082.73	0%	100%	16
MKH2-02-00	Sand Cover & Warning Tape [Local	5	12-Nov-26	17-Nov-26	18-Oct-26 A	09-Dec-26	0.00	54,521.65	90,869.42	0%	60%	-19
MKH2-02-00	Backfilling & Compaction [Local 11]-	5	05-Nov-26	10-Nov-26	12-Oct-26 A	17-Oct-26 A	0.00	45,541.34	45,541.34	0%	100%	21
MKH2-02-00	Backfilling & Compaction [Local 11]-	5	18-Nov-26	23-Nov-26	18-Oct-26 A	15-Dec-26	0.00	27,260.81	45,434.69	0%	60%	-19
Manholes		30	01-Nov-26	24-Nov-26	03-Oct-26 A	21-Nov-26	0.00	358,361.11	471,527.78	0%	76%	3
MKH2-02-00	Installation of Manholes [Local 11]-St	7	01-Nov-26	08-Nov-26	03-Oct-26 A	10-Oct-26 A	0.00	165,034.72	165,034.72	0%	100%	25
MKH2-02-00	Installation of Manholes [Local 11]-St	7	09-Nov-26	16-Nov-26	10-Oct-26 A	12-Oct-26 A	0.00	165,034.72	165,034.72	0%	100%	30
MKH2-02-00	Installation of Manholes [Local 11]-St	7	17-Nov-26	24-Nov-26	18-Oct-26 A	21-Nov-26	0.00	28,291.67	141,458.33	0%	20%	3
Catch Basins		35	09-Nov-26	19-Dec-26	16-Nov-26	26-Dec-26	0.00	0.00	368,034.06	0%	0%	-6
MKH2-02-00	Construction of Catch basins [Local	7	09-Nov-26	16-Nov-26	16-Nov-26	23-Nov-26	0.00	0.00	73,606.81	0%	0%	-6
MKH2-02-00	Construction of Catch basins [Local	7	17-Nov-26	24-Nov-26	24-Nov-26	01-Dec-26	0.00	0.00	73,606.81	0%	0%	-6
MKH2-02-00	Construction of Catch basins [Local	7	25-Nov-26	02-Dec-26	02-Dec-26	09-Dec-26	0.00	0.00	73,606.81	0%	0%	-6
MKH2-02-00	Construction of Catch basins [Local	7	03-Dec-26	10-Dec-26	10-Dec-26	17-Dec-26	0.00	0.00	73,606.81	0%	0%	-6
MKH2-02-00	Construction of Catch basins [Local	7	12-Dec-26	19-Dec-26	19-Dec-26	26-Dec-26	0.00	0.00	73,606.81	0%	0%	-6
Concrete chambers Pipes		25	17-Nov-26	15-Dec-26	24-Nov-26	22-Dec-26	0.00	0.00	438,725.60	0%	0%	-6
MKH2-02-00	Excavation and Compaction (FDT) [I	9	17-Nov-26	26-Nov-26	24-Nov-26	03-Dec-26	0.00	0.00	87,745.14	0%	0%	-6
MKH2-02-00	Installation of Pipes [Local 11]	7	28-Nov-26	05-Dec-26	05-Dec-26	12-Dec-26	0.00	0.00	263,235.32	0%	0%	-6
MKH2-02-00	Backfilling & Compaction [Local 11]	9	06-Dec-26	15-Dec-26	13-Dec-26	22-Dec-26	0.00	0.00	87,745.14	0%	0%	-6
Local 29		161	01-Oct-26	03-Mar-27	11-Aug-26 A	03-May-27	773,065.60	1,458,723.44	3,259,356.46	23.72%	44.75%	-49

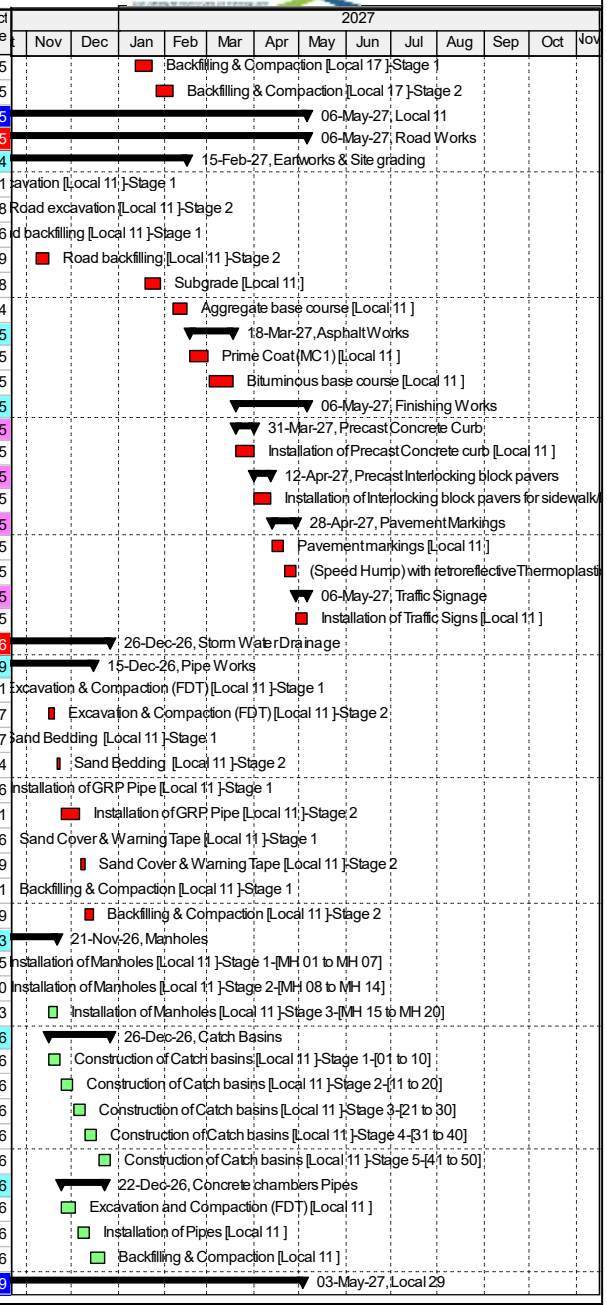

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14
WBS L5

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Road Works		161	01-Oct-26	03-Mar-27	11-Aug-26 A	03-May-27	718,352.00	689,482.40	1,818,912.70	39.49%	37.91%	-49
Eartworks & Site grading		113	01-Oct-26	05-Jan-27	11-Aug-26 A	04-Mar-27	718,352.00	689,482.40	926,432.00	77.54%	74.42%	-49
MKH2-02-00	Road excavation [Local 29]	10	01-Oct-26	12-Oct-26	11-Aug-26 A	22-Aug-26 A	525,888.00	525,888.00	525,888.00	100%	100%	43
MKH2-02-00	Road backfilling [Local 29]	10	01-Oct-26	12-Oct-26	12-Aug-26 A	21-Nov-26	192,464.00	163,594.40	192,464.00	100%	85%	-34
MKH2-02-00	Subgrade [Local 29]	14	05-Dec-26	20-Dec-26	30-Jan-27	14-Feb-27	0.00	0.00	80,784.00	0%	0%	-48
MKH2-02-00	Aggregate base course [Local 29]	14	21-Dec-26	05-Jan-27	16-Feb-27	04-Mar-27	0.00	0.00	127,296.00	0%	0%	-49
Asphalt Works		18	06-Jan-27	26-Jan-27	06-Mar-27	29-Mar-27	0.00	0.00	480,480.00	0%	0%	-49
MKH2-02-00	Prime Coat (MC1) [Local 29]	8	06-Jan-27	14-Jan-27	06-Mar-27	17-Mar-27	0.00	0.00	48,160.00	0%	0%	-49
MKH2-02-00	Bituminous base course [Local 29]	10	16-Jan-27	26-Jan-27	18-Mar-27	29-Mar-27	0.00	0.00	432,320.00	0%	0%	-49
Finishing Works		30	27-Jan-27	03-Mar-27	30-Mar-27	03-May-27	0.00	0.00	412,000.70	0%	0%	-49
Precast Concrete Curb		6	27-Jan-27	02-Feb-27	30-Mar-27	05-Apr-27	0.00	0.00	142,240.70	0%	0%	-49
MKH2-02-0(	Installation of Precast Concrete curb	6	27-Jan-27	02-Feb-27	30-Mar-27	05-Apr-27	0.00	0.00	142,240.70	0%	0%	-49
Precast Interlocking block pavers		6	03-Feb-27	09-Feb-27	06-Apr-27	12-Apr-27	0.00	0.00	191,310.00	0%	0%	-49
MKH2-02-0(	Installation of Interlocking block pave	6	03-Feb-27	09-Feb-27	06-Apr-27	12-Apr-27	0.00	0.00	191,310.00	0%	0%	-49
Pavement Markings		12	10-Feb-27	24-Feb-27	13-Apr-27	26-Apr-27	0.00	0.00	47,850.00	0%	0%	-49
MKH2-02-0(	Pavement markings [Local 29]	6	10-Feb-27	16-Feb-27	13-Apr-27	19-Apr-27	0.00	0.00	23,850.00	0%	0%	-49
MKH2-02-0(	(Speed Hump) with retroreflective Th	6	17-Feb-27	24-Feb-27	20-Apr-27	26-Apr-27	0.00	0.00	24,000.00	0%	0%	-49
Traffic Signage		6	25-Feb-27	03-Mar-27	27-Apr-27	03-May-27	0.00	0.00	30,600.00	0%	0%	-49
MKH2-02-0(	Installation of Traffic Signs [Local 29]	6	25-Feb-27	03-Mar-27	27-Apr-27	03-May-27	0.00	0.00	30,600.00	0%	0%	-49
Storm Water Drainage		38	13-Oct-26	20-Dec-26	14-Oct-26 A	07-Jan-27	54,713.60	769,241.04	1,440,443.75	3.8%	53.4%	-16
Pipe Works		32	13-Oct-26	18-Nov-26	14-Oct-26 A	07-Dec-26	54,713.60	472,178.54	547,136.20	10%	86.3%	-16
MKH2-02-00	Excavation & Compaction (FDT) [Lo	6	13-Oct-26	19-Oct-26	14-Oct-26 A	28-Nov-26	54,713.60	53,619.33	54,713.60	100%	98%	-34
MKH2-02-00	Sand Bedding [Local 29]	6	20-Oct-26	26-Oct-26	15-Oct-26 A	30-Nov-26	0.00	49,242.24	54,713.60	0%	90%	-30
MKH2-02-00	Installation of GRP Pipe [Local 29]	9	27-Oct-26	05-Nov-26	17-Oct-26 A	02-Dec-26	0.00	246,211.31	273,568.13	0%	90%	-23
MKH2-02-00	Sand Cover & Warning Tape [Local	5	07-Nov-26	11-Nov-26	18-Oct-26 A	05-Dec-26	0.00	82,070.45	109,427.26	0%	75%	-20
MKH2-02-00	Backfilling & Compaction [Local 29]	6	12-Nov-26	18-Nov-26	19-Oct-26 A	07-Dec-26	0.00	41,035.20	54,713.60	0%	75%	-16
Manholes		14	07-Nov-26	22-Nov-26	17-Oct-26 A	06-Dec-26	0.00	297,062.50	353,645.83	0%	84%	-12
MKH2-02-00	Installation of Manholes [Local 29]-S	7	07-Nov-26	14-Nov-26	17-Oct-26 A	19-Oct-26 A	0.00	165,034.72	165,034.72	0%	100%	22
MKH2-02-00	Installation of Manholes [Local 29]-S	7	15-Nov-26	22-Nov-26	19-Oct-26 A	06-Dec-26	0.00	132,027.78	188,611.11	0%	70%	-12
Catch Basins		25	15-Nov-26	13-Dec-26	03-Dec-26	31-Dec-26	0.00	0.00	257,623.84	0%	0%	-16
MKH2-02-00	Construction of Catch basins [Local 2	7	15-Nov-26	22-Nov-26	03-Dec-26	10-Dec-26	0.00	0.00	73,606.81	0%	0%	-16
MKH2-02-00	Construction of Catch basins [Local 2	7	23-Nov-26	30-Nov-26	12-Dec-26	19-Dec-26	0.00	0.00	73,606.81	0%	0%	-16
MKH2-02-00	Construction of Catch basins [Local 2	7	01-Dec-26	08-Dec-26	20-Dec-26	27-Dec-26	0.00	0.00	73,606.81	0%	0%	-16
MKH2-02-00	Construction of Catch basins [Local 2	4	09-Dec-26	13-Dec-26	28-Dec-26	31-Dec-26	0.00	0.00	36,803.41	0%	0%	-16
Concrete chambers Pipes		24	23-Nov-26	20-Dec-26	12-Dec-26	07-Jan-27	0.00	0.00	282,037.88	0%	0%	-16
MKH2-02-00	Excavation and Compaction (FDT) [	7	23-Nov-26	30-Nov-26	12-Dec-26	19-Dec-26	0.00	0.00	56,407.59	0%	0%	-16
MKH2-02-00	Installation of Pipes [Local 29]	9	01-Dec-26	10-Dec-26	20-Dec-26	29-Dec-26	0.00	0.00	169,222.70	0%	0%	-16
MKH2-02-00	Backfilling & Compaction [Local 29]	6	14-Dec-26	20-Dec-26	02-Jan-27	07-Jan-27	0.00	0.00	56,407.59	0%	0%	-16
Local 30		169	13-Oct-26	21-Mar-27	21-Jul-26 A	22-May-27	391,828.36	1,815,165.56	3,255,276.56	12.04%	55.76%	-49
Road Works		169	13-Oct-26	21-Mar-27	21-Jul-26 A	22-May-27	391,828.36	776,040.32	1,818,912.70	21.54%	42.67%	-49
Eartworks & Site grading		121	13-Oct-26	19-Jan-27	21-Jul-26 A	22-Mar-27	391,828.36	776,040.32	926,432.00	42.29%	83.77%	-49
MKH2-02-00	Road excavation [Local 30]	11	13-Oct-26	25-Oct-26	21-Jul-26 A	22-Aug-26 A	286,848.00	525,888.00	525,888.00	54.55%	100%	54
MKH2-02-00	Road backfilling [Local 30]	11	13-Oct-26	25-Oct-26	22-Jul-26 A	26-Nov-26	104,980.36	169,368.32	192,464.00	54.55%	88%	-28
MKH2-02-00	Subgrade [Local 30]	14	21-Dec-26	05-Jan-27	19-Sep-26 A	10-Oct-26 A	0.00	80,784.00	80,784.00	0%	100%	75
MKH2-02-00	Aggregate base course [Local 30]	12	06-Jan-27	19-Jan-27	06-Mar-27	22-Mar-27	0.00	0.00	127,296.00	0%	0%	-49
Asphalt Works		18	20-Jan-27	09-Feb-27	23-Mar-27	12-Apr-27	0.00	0.00	480,480.00	0%	0%	-49
MKH2-02-00	Prime Coat (MC1) [Local 30]	8	20-Jan-27	28-Jan-27	23-Mar-27	31-Mar-27	0.00	0.00	48,160.00	0%	0%	-49
MKH2-02-00	Bituminous base course [Local 30]	10	30-Jan-27	09-Feb-27	01-Apr-27	12-Apr-27	0.00	0.00	432,320.00	0%	0%	-49
Finishing Works		30	10-Feb-27	21-Mar-27	13-Apr-27	22-May-27	0.00	0.00	412,000.70	0%	0%	-49
Precast Concrete Curb		6	10-Feb-27	16-Feb-27	13-Apr-27	19-Apr-27	0.00	0.00	142,240.70	0%	0%	-49
MKH2-02-0(	Installation of Precast Concrete curb	6	10-Feb-27	16-Feb-27	13-Apr-27	19-Apr-27	0.00	0.00	142,240.70	0%	0%	-49

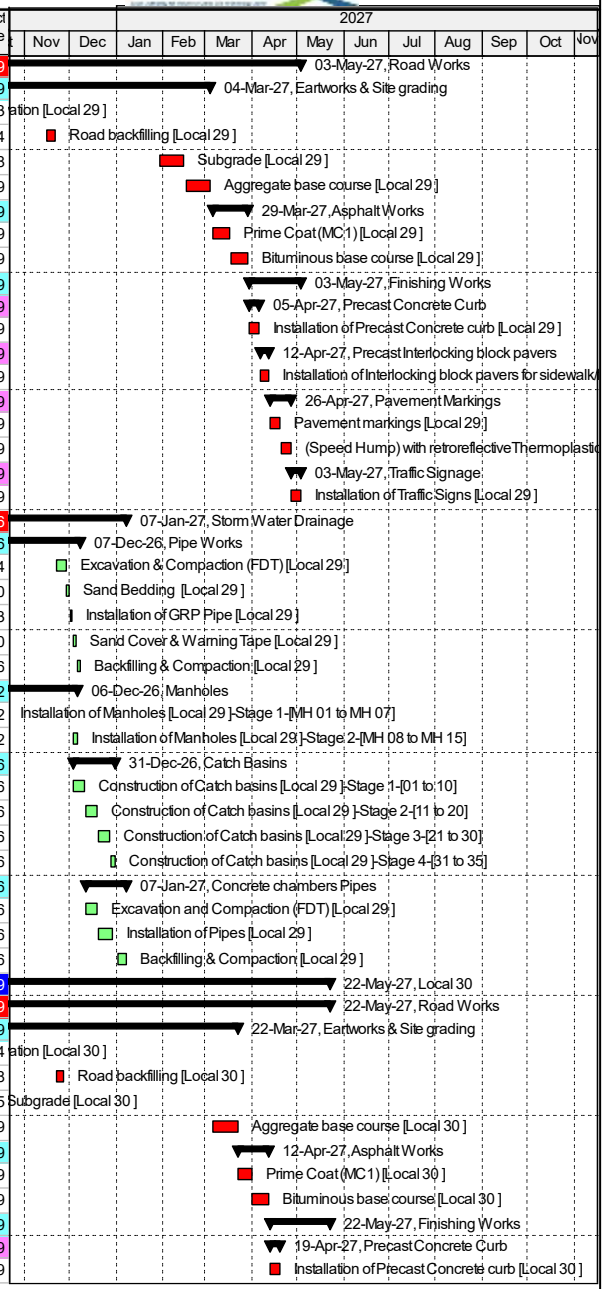

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Precast Interlocking block pavers		6	17-Feb-27	24-Feb-27	20-Apr-27	26-Apr-27	0.00	0.00	191,310.00	0%	0%	-49
MKH2-02-0(	Installation of Interlocking block pave	6	17-Feb-27	24-Feb-27	20-Apr-27	26-Apr-27	0.00	0.00	191,310.00	0%	0%	-49
Pavement Markings		12	25-Feb-27	14-Mar-27	27-Apr-27	10-May-27	0.00	0.00	47,850.00	0%	0%	-49
MKH2-02-0(	Pavement markings [Local 30]	6	25-Feb-27	03-Mar-27	27-Apr-27	03-May-27	0.00	0.00	23,850.00	0%	0%	-49
MKH2-02-0(	(Speed Hump) with retroreflective The	6	04-Mar-27	14-Mar-27	04-May-27	10-May-27	0.00	0.00	24,000.00	0%	0%	-49
Traffic Signage		6	15-Mar-27	21-Mar-27	11-May-27	22-May-27	0.00	0.00	30,600.00	0%	0%	-49
MKH2-02-0(	Installation of Traffic Signs [Local 30]	6	15-Mar-27	21-Mar-27	11-May-27	22-May-27	0.00	0.00	30,600.00	0%	0%	-49
Storm Water Drainage		106	26-Oct-26	12-Jan-27	26-Aug-26 A	04-Mar-27	0.00	1,039,125.24	1,436,363.86	0%	72.34%	-43
Pipe Works		39	26-Oct-26	09-Dec-26	26-Aug-26 A	19-Sep-26 A	0.00	620,727.62	620,727.62	0%	100%	69
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	6	26-Oct-26	01-Nov-26	26-Aug-26 A	16-Sep-26 A	0.00	62,072.74	62,072.74	0%	100%	38
MKH2-02-00(	Sand Bedding [Local 30]	6	02-Nov-26	08-Nov-26	29-Aug-26 A	17-Sep-26 A	0.00	62,072.74	62,072.74	0%	100%	43
MKH2-02-00(	Installation of GRP Pipe [Local 30]	10	09-Nov-26	19-Nov-26	29-Aug-26 A	19-Sep-26 A	0.00	310,363.84	310,363.84	0%	100%	52
MKH2-02-00(	Sand Cover & Warning Tape [Local	5	21-Nov-26	25-Nov-26	03-Sep-26 A	19-Sep-26 A	0.00	124,145.55	124,145.55	0%	100%	57
MKH2-02-00(	Backfilling & Compaction [Local 30]	12	26-Nov-26	09-Dec-26	03-Sep-26 A	19-Sep-26 A	0.00	62,072.74	62,072.74	0%	100%	69
Manholes		24	21-Nov-26	22-Dec-26	03-Sep-26 A	21-Sep-26 A	0.00	330,069.44	330,069.44	0%	100%	78
MKH2-02-00(	Installation of Manholes [Local 30]-S	14	21-Nov-26	06-Dec-26	03-Sep-26 A	17-Sep-26 A	0.00	165,034.72	165,034.72	0%	100%	67
MKH2-02-00(	Installation of Manholes [Local 30]-S	14	07-Dec-26	22-Dec-26	19-Sep-26 A	21-Sep-26 A	0.00	165,034.72	165,034.72	0%	100%	78
Catch Basins		20	07-Dec-26	11-Jan-27	18-Oct-26 A	19-Dec-26	0.00	88,328.17	228,181.11	0%	38.71%	20
MKH2-02-00(	Construction of Catch basins [Local 3	10	07-Dec-26	17-Dec-26	18-Oct-26 A	19-Oct-26 A	0.00	73,606.81	73,606.81	0%	100%	51
MKH2-02-00(	Construction of Catch basins [Local 3	10	19-Dec-26	29-Dec-26	19-Oct-26 A	06-Dec-26	0.00	14,721.36	73,606.81	0%	20%	20
MKH2-02-00(	Construction of Catch basins [Local 3	11	30-Dec-26	11-Jan-27	07-Dec-26	19-Dec-26	0.00	0.00	80,967.49	0%	0%	20
Concrete chambers Pipes		22	19-Dec-26	12-Jan-27	07-Feb-27	04-Mar-27	0.00	0.00	257,385.68	0%	0%	-43
MKH2-02-00(	Excavation and Compaction (FDT) [I	7	19-Dec-26	26-Dec-26	07-Feb-27	14-Feb-27	0.00	0.00	51,477.15	0%	0%	-43
MKH2-02-00(	Installation of Pipes [Local 30]	9	27-Dec-26	05-Jan-27	15-Feb-27	25-Feb-27	0.00	0.00	154,431.38	0%	0%	-43
MKH2-02-00(	Backfilling & Compaction [Local 30]	6	06-Jan-27	12-Jan-27	27-Feb-27	04-Mar-27	0.00	0.00	51,477.15	0%	0%	-43
Local 31		194	26-Oct-26	06-May-27	29-Jul-26 A	30-Jun-27	0.00	948,352.00	4,767,621.35	0%	19.89%	-43
Road Works		194	26-Oct-26	06-May-27	29-Jul-26 A	30-Jun-27	0.00	948,352.00	2,945,668.71	0%	32.19%	-43
Eartworks & Site grading		130	26-Oct-26	16-Feb-27	29-Jul-26 A	12-Apr-27	0.00	948,352.00	1,503,724.00	0%	63.07%	-43
MKH2-02-00(	Road excavation [Local 31]-Stage 1	12	26-Oct-26	08-Nov-26	29-Jul-26 A	14-Oct-26 A	0.00	426,756.00	426,756.00	0%	100%	21
MKH2-02-00(	Road excavation [Local 31]-Stage 2	12	09-Nov-26	22-Nov-26	15-Oct-26 A	10-Dec-26	0.00	256,053.60	426,756.00	0%	60%	-16
MKH2-02-00(	Road backfilling [Local 31]-Stage 1	12	26-Oct-26	08-Nov-26	05-Sep-26 A	19-Sep-26 A	0.00	156,208.00	156,208.00	0%	100%	42
MKH2-02-00(	Road backfilling [Local 31]-Stage 2	12	09-Nov-26	22-Nov-26	01-Oct-26 A	10-Dec-26	0.00	109,334.40	156,192.00	0%	70%	-16
MKH2-02-00(	Subgrade [Local 31]	18	06-Jan-27	26-Jan-27	15-Feb-27	08-Mar-27	0.00	0.00	131,164.00	0%	0%	-34
MKH2-02-00(	Aggregate base course [Local 31]	18	27-Jan-27	16-Feb-27	23-Mar-27	12-Apr-27	0.00	0.00	206,648.00	0%	0%	-43
Asphalt Works		19	17-Feb-27	15-Mar-27	13-Apr-27	04-May-27	0.00	0.00	777,280.00	0%	0%	-43
MKH2-02-00(	Prime Coat (MC1) [Local 31]	9	17-Feb-27	28-Feb-27	13-Apr-27	22-Apr-27	0.00	0.00	77,280.00	0%	0%	-43
MKH2-02-00(	Bituminous base course [Local 31]	10	01-Mar-27	15-Mar-27	24-Apr-27	04-May-27	0.00	0.00	700,000.00	0%	0%	-43
Finishing Works		45	16-Mar-27	06-May-27	05-May-27	30-Jun-27	0.00	0.00	664,664.71	0%	0%	-43
Precast Concrete Curb		10	16-Mar-27	27-Mar-27	05-May-27	20-May-27	0.00	0.00	230,894.71	0%	0%	-43
MKH2-02-0(	Installation of Precast Concrete curb	10	16-Mar-27	27-Mar-27	05-May-27	20-May-27	0.00	0.00	230,894.71	0%	0%	-43
Precast Interlocking block pavers		9	28-Mar-27	06-Apr-27	22-May-27	31-May-27	0.00	0.00	310,380.00	0%	0%	-43
MKH2-02-0(	Installation of Interlocking block pave	9	28-Mar-27	06-Apr-27	22-May-27	31-May-27	0.00	0.00	310,380.00	0%	0%	-43
Pavement Markings		18	07-Apr-27	27-Apr-27	01-Jun-27	21-Jun-27	0.00	0.00	74,790.00	0%	0%	-43
MKH2-02-0(	Pavement markings [Local 31]	9	07-Apr-27	17-Apr-27	01-Jun-27	10-Jun-27	0.00	0.00	38,790.00	0%	0%	-43
MKH2-02-0(	(Speed Hump) with retroreflective The	9	18-Apr-27	27-Apr-27	12-Jun-27	21-Jun-27	0.00	0.00	36,000.00	0%	0%	-43
Traffic Signage		8	28-Apr-27	06-May-27	22-Jun-27	30-Jun-27	0.00	0.00	48,600.00	0%	0%	-43
MKH2-02-0(	Installation of Traffic Signs [Local 31]	8	28-Apr-27	06-May-27	22-Jun-27	30-Jun-27	0.00	0.00	48,600.00	0%	0%	-43
Storm Water Drainage		99	09-Nov-26	02-Feb-27	28-Nov-26	27-Mar-27	0.00	0.00	1,821,952.64	0%	0%	-41
Pipe Works		46	09-Nov-26	31-Dec-26	28-Nov-26	19-Jan-27	0.00	0.00	634,592.67	0%	0%	-16
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	8	09-Nov-26	17-Nov-26	28-Nov-26	06-Dec-26	0.00	0.00	31,782.95	0%	0%	-16
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	8	18-Nov-26	26-Nov-26	07-Dec-26	15-Dec-26	0.00	0.00	31,676.30	0%	0%	-16

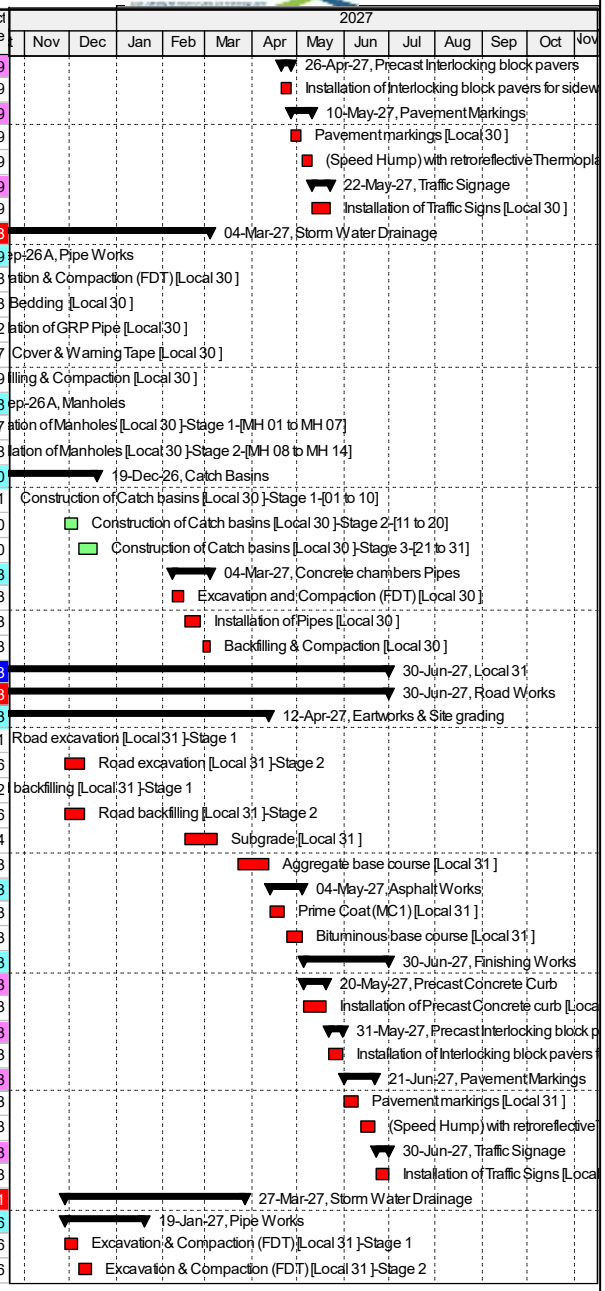

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Sand Bedding [Local 31]-Stage 1	10	18-Nov-26	29-Nov-26	07-Dec-26	17-Dec-26	0.00	0.00	31,782.95	0%	0%	-16
MKH2-02-00	Sand Bedding [Local 31]-Stage 2	10	30-Nov-26	10-Dec-26	19-Dec-26	29-Dec-26	0.00	0.00	31,676.30	0%	0%	-16
MKH2-02-00	Installation of GRP Pipe [Local 31]-S	8	30-Nov-26	08-Dec-26	19-Dec-26	27-Dec-26	0.00	0.00	158,914.82	0%	0%	-16
MKH2-02-00	Installation of GRP Pipe [Local 31]-S	8	12-Dec-26	20-Dec-26	30-Dec-26	07-Jan-27	0.00	0.00	158,381.55	0%	0%	-16
MKH2-02-00	Sand Cover & Warning Tape [Local	5	09-Dec-26	14-Dec-26	28-Dec-26	02-Jan-27	0.00	0.00	63,565.93	0%	0%	-16
MKH2-02-00	Sand Cover & Warning Tape [Local	5	21-Dec-26	26-Dec-26	09-Jan-27	13-Jan-27	0.00	0.00	63,352.62	0%	0%	-16
MKH2-02-00	Backfilling & Compaction [Local 31]-	5	15-Dec-26	20-Dec-26	03-Jan-27	07-Jan-27	0.00	0.00	31,782.95	0%	0%	-16
MKH2-02-00	Backfilling & Compaction [Local 31]-	5	27-Dec-26	31-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	31,676.30	0%	0%	-16
Manholes		40	09-Dec-26	24-Jan-27	28-Dec-26	11-Feb-27	0.00	0.00	471,527.78	0%	0%	-16
MKH2-02-00	Installation of Manholes [Local 31]-S	14	09-Dec-26	24-Dec-26	28-Dec-26	12-Jan-27	0.00	0.00	165,034.72	0%	0%	-16
MKH2-02-00	Installation of Manholes [Local 31]-S	14	26-Dec-26	10-Jan-27	13-Jan-27	28-Jan-27	0.00	0.00	165,034.72	0%	0%	-16
MKH2-02-00	Installation of Manholes [Local 31]-S	12	11-Jan-27	24-Jan-27	30-Jan-27	11-Feb-27	0.00	0.00	141,458.33	0%	0%	-16
Catch Basins		51	26-Dec-26	23-Jan-27	13-Jan-27	17-Mar-27	0.00	0.00	360,673.37	0%	0%	-42
MKH2-02-00	Construction of Catch basins [Local 3	5	26-Dec-26	30-Dec-26	13-Jan-27	18-Jan-27	0.00	0.00	73,606.81	0%	0%	-16
MKH2-02-00	Construction of Catch basins [Local 3	5	31-Dec-26	05-Jan-27	19-Jan-27	24-Jan-27	0.00	0.00	73,606.81	0%	0%	-16
MKH2-02-00	Construction of Catch basins [Local 3	5	06-Jan-27	11-Jan-27	25-Feb-27	02-Mar-27	0.00	0.00	73,606.81	0%	0%	-42
MKH2-02-00	Construction of Catch basins [Local 3	5	12-Jan-27	17-Jan-27	03-Mar-27	08-Mar-27	0.00	0.00	73,606.81	0%	0%	-42
MKH2-02-00	Construction of Catch basins [Local 3	5	18-Jan-27	23-Jan-27	09-Mar-27	17-Mar-27	0.00	0.00	66,246.13	0%	0%	-42
Concrete chambers Pipes		54	31-Dec-26	02-Feb-27	19-Jan-27	27-Mar-27	0.00	0.00	355,158.82	0%	0%	-41
MKH2-02-00	Excavation and Compaction (FDT) [I	9	31-Dec-26	10-Jan-27	19-Jan-27	28-Jan-27	0.00	0.00	71,031.78	0%	0%	-16
MKH2-02-00	Installation of Pipes [Local 31]	12	11-Jan-27	24-Jan-27	30-Jan-27	11-Feb-27	0.00	0.00	213,095.26	0%	0%	-16
MKH2-02-00	Backfilling & Compaction [Local 31]	8	25-Jan-27	02-Feb-27	18-Mar-27	27-Mar-27	0.00	0.00	71,031.78	0%	0%	-41
Local 28		206	09-Nov-26	03-Jun-27	05-Aug-26 A	24-Jul-27	0.00	2,398,345.59	4,985,962.53	0%	48.1%	-43
Road Works		206	09-Nov-26	03-Jun-27	05-Aug-26 A	24-Jul-27	0.00	1,188,599.90	2,941,183.79	0%	40.41%	-43
Eartworks & Site grading		136	09-Nov-26	08-Mar-27	05-Aug-26 A	28-Apr-27	0.00	1,188,599.90	1,500,412.00	0%	79.22%	-41
MKH2-02-00	Road excavation [Local 28]-Stage 1	12	09-Nov-26	22-Nov-26	05-Aug-26 A	03-Sep-26 A	0.00	425,854.00	425,854.00	0%	100%	68
MKH2-02-00	Road excavation [Local 28]-Stage 2	12	23-Nov-26	06-Dec-26	22-Aug-26 A	14-Sep-26 A	0.00	425,832.00	425,832.00	0%	100%	71
MKH2-02-00	Road backfilling [Local 28]-Stage 1	12	09-Nov-26	22-Nov-26	08-Aug-26 A	22-Aug-26 A	0.00	155,856.00	155,856.00	0%	100%	78
MKH2-02-00	Road backfilling [Local 28]-Stage 2	12	23-Nov-26	06-Dec-26	22-Aug-26 A	06-Dec-26	0.00	109,099.20	155,856.00	0%	70%	0
MKH2-02-00	Subgrade [Local 28]	16	01-Feb-27	18-Feb-27	17-Oct-26 A	30-Mar-27	0.00	71,958.70	130,834.00	0%	55%	-30
MKH2-02-00	Aggregate base course [Local 28]	14	20-Feb-27	08-Mar-27	13-Apr-27	28-Apr-27	0.00	0.00	206,180.00	0%	0%	-41
Asphalt Works		18	09-Mar-27	01-Apr-27	29-Apr-27	24-May-27	0.00	0.00	777,280.00	0%	0%	-41
MKH2-02-00	Prime Coat (MC1) [Local 28]	8	09-Mar-27	21-Mar-27	29-Apr-27	08-May-27	0.00	0.00	77,840.00	0%	0%	-41
MKH2-02-00	Bituminous base course [Local 28]	10	22-Mar-27	01-Apr-27	09-May-27	24-May-27	0.00	0.00	699,440.00	0%	0%	-41
Finishing Works		52	03-Apr-27	03-Jun-27	25-May-27	24-Jul-27	0.00	0.00	663,491.79	0%	0%	-43
Precast Concrete Curb		10	03-Apr-27	13-Apr-27	25-May-27	05-Jun-27	0.00	0.00	230,416.79	0%	0%	-41
MKH2-02-0(	Installation of Precast Concrete curb	10	03-Apr-27	13-Apr-27	25-May-27	05-Jun-27	0.00	0.00	230,416.79	0%	0%	-41
Precast Interlocking block pavers		9	14-Apr-27	24-Apr-27	06-Jun-27	15-Jun-27	0.00	0.00	309,820.00	0%	0%	-41
MKH2-02-0(	Installation of Interlocking block pave	9	14-Apr-27	24-Apr-27	06-Jun-27	15-Jun-27	0.00	0.00	309,820.00	0%	0%	-41
Pavement Markings		19	28-Apr-27	24-May-27	22-Jun-27	13-Jul-27	0.00	0.00	74,655.00	0%	0%	-43
MKH2-02-0(	Pavement markings [Local 28]	10	28-Apr-27	09-May-27	22-Jun-27	03-Jul-27	0.00	0.00	38,655.00	0%	0%	-43
MKH2-02-0(	(Speed Hump) with retroreflective Th	9	10-May-27	24-May-27	04-Jul-27	13-Jul-27	0.00	0.00	36,000.00	0%	0%	-43
Traffic Signage		9	25-May-27	03-Jun-27	14-Jul-27	24-Jul-27	0.00	0.00	48,600.00	0%	0%	-43
MKH2-02-0(	Installation of Traffic Signs [Local 28]	9	25-May-27	03-Jun-27	14-Jul-27	24-Jul-27	0.00	0.00	48,600.00	0%	0%	-43
Storm Water Drainage		103	07-Dec-26	24-Feb-27	09-Sep-26 A	10-Apr-27	0.00	1,209,745.69	2,044,778.74	0%	59.16%	-35
Pipe Works		30	07-Dec-26	31-Jan-27	09-Sep-26 A	26-Dec-26	0.00	738,217.92	790,307.84	0%	93.41%	31
MKH2-02-00	Excavation & Compaction (FDT) [Lo	10	07-Dec-26	17-Dec-26	09-Sep-26 A	17-Sep-26 A	0.00	39,568.71	39,568.71	0%	100%	77
MKH2-02-00	Excavation & Compaction (FDT) [Lo	10	19-Dec-26	29-Dec-26	23-Sep-26 A	07-Oct-26 A	0.00	39,462.05	39,462.05	0%	100%	71
MKH2-02-00	Sand Bedding [Local 28]-Stage 1	8	19-Dec-26	27-Dec-26	10-Sep-26 A	19-Sep-26 A	0.00	39,568.71	39,568.71	0%	100%	84
MKH2-02-00	Sand Bedding [Local 28]-Stage 2	8	30-Dec-26	07-Jan-27	26-Sep-26 A	12-Dec-26	0.00	38,672.81	39,462.05	0%	98%	23
MKH2-02-00	Installation of GRP Pipe [Local 28]-S	10	28-Dec-26	07-Jan-27	12-Sep-26 A	24-Sep-26 A	0.00	197,843.62	197,843.62	0%	100%	90

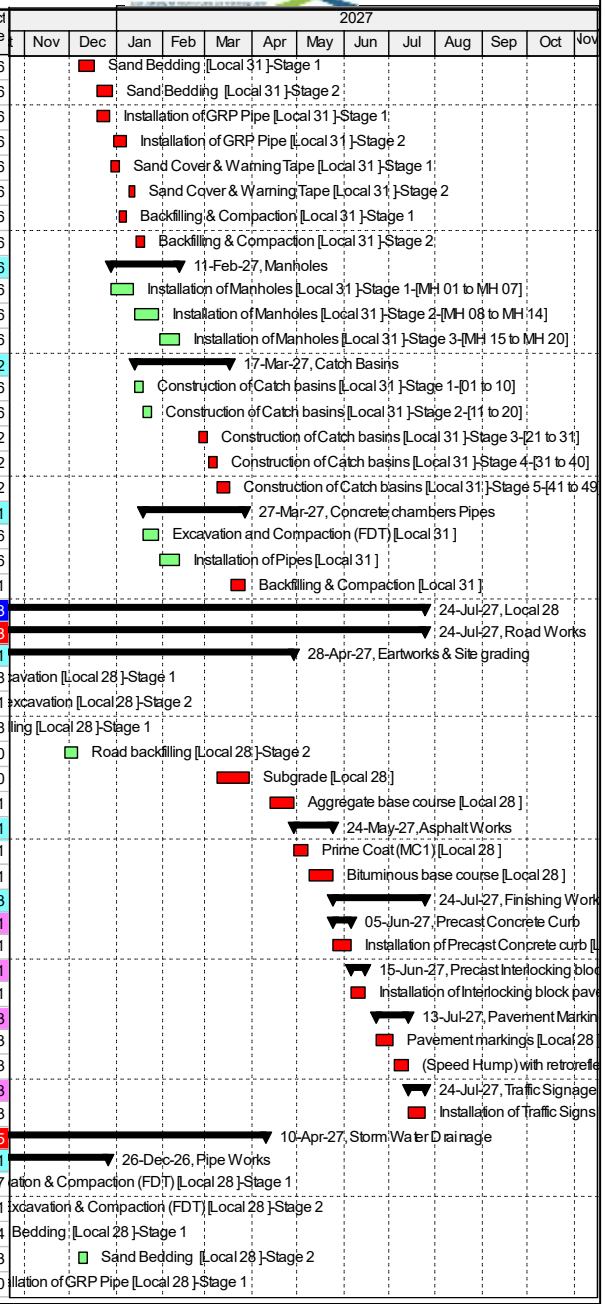

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Installation of GRP Pipe [Local 28]-S	10	09-Jan-27	19-Jan-27	27-Sep-26 A	19-Dec-26	0.00	193,364.14	197,310.34	0%	98%	27
MKH2-02-00	Sand Cover & Warning Tape [Local	5	09-Jan-27	13-Jan-27	26-Sep-26 A	27-Sep-26 A	0.00	79,137.45	79,137.45	0%	100%	93
MKH2-02-00	Sand Cover & Warning Tape [Local	5	20-Jan-27	25-Jan-27	30-Sep-26 A	22-Dec-26	0.00	47,354.49	78,924.15	0%	60%	29
MKH2-02-00	Backfilling & Compaction [Local 28]-	5	14-Jan-27	19-Jan-27	27-Sep-26 A	28-Sep-26 A	0.00	39,568.71	39,568.71	0%	100%	97
MKH2-02-00	Backfilling & Compaction [Local 28]-	5	26-Jan-27	31-Jan-27	03-Oct-26 A	26-Dec-26	0.00	23,677.23	39,462.05	0%	60%	31
Manholes		35	20-Jan-27	06-Feb-27	13-Sep-26 A	19-Oct-26 A	0.00	471,527.78	471,527.78	0%	100%	94
MKH2-02-00	Installation of Manholes [Local 28]-S	5	20-Jan-27	25-Jan-27	13-Sep-26 A	23-Sep-26 A	0.00	165,034.72	165,034.72	0%	100%	106
MKH2-02-00	Installation of Manholes [Local 28]-S	5	26-Jan-27	31-Jan-27	24-Sep-26 A	28-Sep-26 A	0.00	165,034.72	165,034.72	0%	100%	107
MKH2-02-00	Installation of Manholes [Local 28]-S	5	01-Feb-27	06-Feb-27	30-Sep-26 A	19-Oct-26 A	0.00	141,458.33	141,458.33	0%	100%	94
Catch Basins		25	20-Jan-27	17-Feb-27	20-Dec-26	17-Jan-27	0.00	0.00	368,034.06	0%	0%	27
MKH2-02-00	Construction of Catch basins [Local 2	5	20-Jan-27	25-Jan-27	20-Dec-26	24-Dec-26	0.00	0.00	73,606.81	0%	0%	27
MKH2-02-00	Construction of Catch basins [Local 2	5	26-Jan-27	31-Jan-27	26-Dec-26	30-Dec-26	0.00	0.00	73,606.81	0%	0%	27
MKH2-02-00	Construction of Catch basins [Local 2	5	01-Feb-27	06-Feb-27	31-Dec-26	05-Jan-27	0.00	0.00	73,606.81	0%	0%	27
MKH2-02-00	Construction of Catch basins [Local 2	5	07-Feb-27	11-Feb-27	06-Jan-27	11-Jan-27	0.00	0.00	73,606.81	0%	0%	27
MKH2-02-00	Construction of Catch basins [Local 2	5	13-Feb-27	17-Feb-27	12-Jan-27	17-Jan-27	0.00	0.00	73,606.81	0%	0%	27
Concrete chambers Pipes		25	26-Jan-27	24-Feb-27	09-Mar-27	10-Apr-27	0.00	0.00	414,909.06	0%	0%	-35
MKH2-02-00	Excavation and Compaction (FDT) [I	8	26-Jan-27	03-Feb-27	09-Mar-27	21-Mar-27	0.00	0.00	82,981.83	0%	0%	-35
MKH2-02-00	Installation of Pipes [Local 28]	10	04-Feb-27	15-Feb-27	22-Mar-27	01-Apr-27	0.00	0.00	248,945.40	0%	0%	-35
MKH2-02-00	Backfilling & Compaction [Local 28]	7	16-Feb-27	24-Feb-27	03-Apr-27	10-Apr-27	0.00	0.00	82,981.83	0%	0%	-35
Local 10		165	07-Dec-26	08-May-27	07-Jul-26 A	29-Jun-27	0.00	309,953.01	1,363,235.86	0%	22.74%	-41
Road Works		153	07-Dec-26	08-May-27	07-Jul-26 A	29-Jun-27	0.00	287,715.60	809,336.29	0%	35.55%	-41
Eartworks & Site grading		117	07-Dec-26	27-Mar-27	07-Jul-26 A	13-May-27	0.00	287,715.60	412,312.00	0%	69.78%	-41
MKH2-02-00	Road excavation [Local 10]	6	07-Dec-26	13-Dec-26	07-Jul-26 A	09-Dec-26	0.00	210,632.40	234,036.00	0%	90%	3
MKH2-02-00	Road backfilling [Local 10]	6	07-Dec-26	13-Dec-26	15-Jul-26 A	09-Dec-26	0.00	77,083.20	85,648.00	0%	90%	3
MKH2-02-00	Subgrade [Local 10]	7	09-Mar-27	20-Mar-27	29-Apr-27	06-May-27	0.00	0.00	35,948.00	0%	0%	-41
MKH2-02-00	Aggregate base course [Local 10]	6	21-Mar-27	27-Mar-27	08-May-27	13-May-27	0.00	0.00	56,680.00	0%	0%	-41
Asphalt Works		8	28-Mar-27	05-Apr-27	19-May-27	27-May-27	0.00	0.00	213,360.00	0%	0%	-41
MKH2-02-00	Prime Coat (MC1) [Local 10]	4	28-Mar-27	31-Mar-27	19-May-27	23-May-27	0.00	0.00	21,280.00	0%	0%	-41
MKH2-02-00	Bituminous base course [Local 10]	4	01-Apr-27	05-Apr-27	24-May-27	27-May-27	0.00	0.00	192,080.00	0%	0%	-41
Finishing Works		21	14-Apr-27	08-May-27	06-Jun-27	29-Jun-27	0.00	0.00	183,664.29	0%	0%	-41
Precast Concrete Curb		6	14-Apr-27	20-Apr-27	06-Jun-27	12-Jun-27	0.00	0.00	63,324.29	0%	0%	-41
MKH2-02-0(	Installation of Precast Concrete curb	6	14-Apr-27	20-Apr-27	06-Jun-27	12-Jun-27	0.00	0.00	63,324.29	0%	0%	-41
Precast Interlocking block pavers		5	21-Apr-27	26-Apr-27	13-Jun-27	17-Jun-27	0.00	0.00	85,120.00	0%	0%	-41
MKH2-02-0(	Installation of Interlocking block pave	5	21-Apr-27	26-Apr-27	13-Jun-27	17-Jun-27	0.00	0.00	85,120.00	0%	0%	-41
Pavement Markings		7	27-Apr-27	04-May-27	19-Jun-27	26-Jun-27	0.00	0.00	22,620.00	0%	0%	-41
MKH2-02-0(	Pavement markings [Local 10]	4	27-Apr-27	01-May-27	19-Jun-27	22-Jun-27	0.00	0.00	10,620.00	0%	0%	-41
MKH2-02-0(	(Speed Hump) with retroreflective Th	3	02-May-27	04-May-27	23-Jun-27	26-Jun-27	0.00	0.00	12,000.00	0%	0%	-41
Traffic Signage		3	05-May-27	08-May-27	27-Jun-27	29-Jun-27	0.00	0.00	12,600.00	0%	0%	-41
MKH2-02-0(	Installation of Traffic Signs [Local 10]	3	05-May-27	08-May-27	27-Jun-27	29-Jun-27	0.00	0.00	12,600.00	0%	0%	-41
Storm Water Drainage		31	14-Dec-26	18-Jan-27	10-Sep-26 A	14-Jan-27	0.00	22,237.41	553,899.57	0%	4.01%	3
Pipe Works		17	14-Dec-26	02-Jan-27	10-Sep-26 A	29-Dec-26	0.00	22,237.41	148,249.38	0%	15%	3
MKH2-02-00	Excavation & Compaction (FDT) [Lo	4	14-Dec-26	17-Dec-26	10-Sep-26 A	14-Dec-26	0.00	4,447.48	14,824.93	0%	30%	3
MKH2-02-00	Sand Bedding [Local 10]	3	19-Dec-26	21-Dec-26	12-Sep-26 A	17-Dec-26	0.00	2,964.99	14,824.93	0%	20%	3
MKH2-02-00	Installation of GRP Pipe [Local 10]	5	22-Dec-26	27-Dec-26	12-Sep-26 A	23-Dec-26	0.00	14,824.94	74,124.70	0%	20%	3
MKH2-02-00	Sand Cover & Warning Tape [Local	2	28-Dec-26	29-Dec-26	24-Dec-26	26-Dec-26	0.00	0.00	29,649.88	0%	0%	3
MKH2-02-00	Backfilling & Compaction [Local 10]	3	30-Dec-26	02-Jan-27	27-Dec-26	29-Dec-26	0.00	0.00	14,824.93	0%	0%	3
Manholes		10	28-Dec-26	07-Jan-27	24-Dec-26	04-Jan-27	0.00	0.00	259,340.28	0%	0%	3
MKH2-02-00	Installation of Manholes [Local 10]-S	5	28-Dec-26	02-Jan-27	24-Dec-26	29-Dec-26	0.00	0.00	165,034.72	0%	0%	3
MKH2-02-00	Installation of Manholes [Local 10]-S	5	03-Jan-27	07-Jan-27	30-Dec-26	04-Jan-27	0.00	0.00	94,305.56	0%	0%	3
Catch Basins		4	03-Jan-27	06-Jan-27	30-Dec-26	03-Jan-27	0.00	0.00	73,606.81	0%	0%	3
MKH2-02-00	Construction of Catch basins [Local 1	4	03-Jan-27	06-Jan-27	30-Dec-26	03-Jan-27	0.00	0.00	73,606.81	0%	0%	3

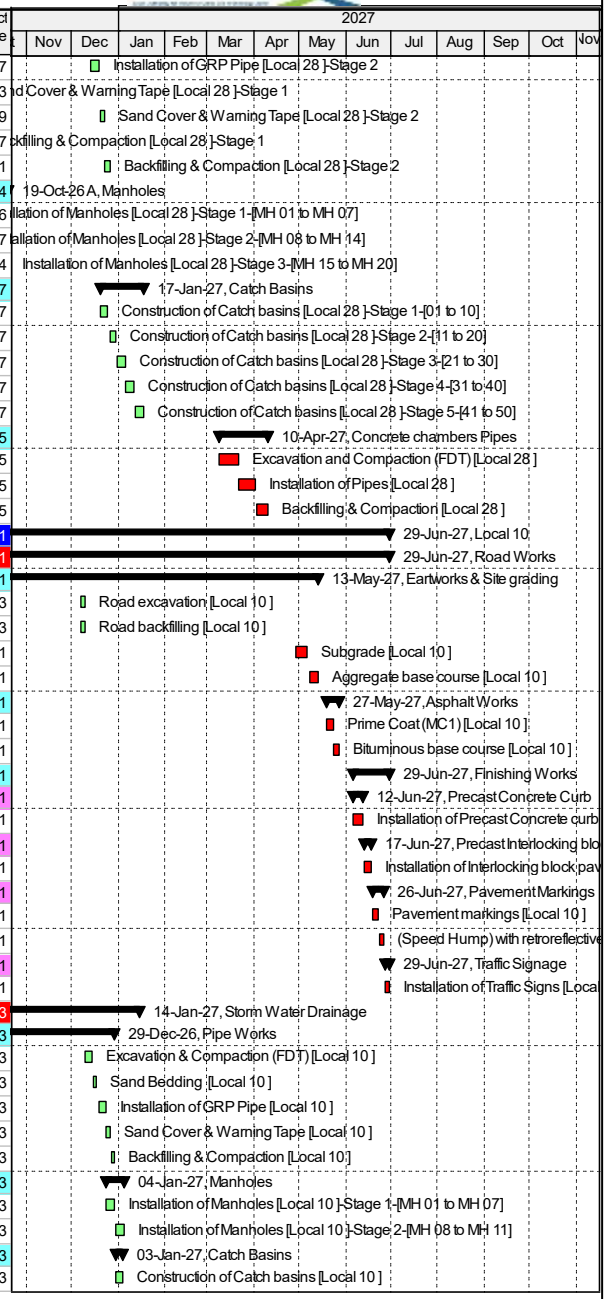

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved


egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 14

WBS L5

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Concrete chambers Pipes		10	07-Jan-27	18-Jan-27	04-Jan-27	14-Jan-27	0.00	0.00	72,703.10	0%	0%	3
MKH2-02-00	Excavation and Compaction (FDT) [L	3	07-Jan-27	10-Jan-27	04-Jan-27	06-Jan-27	0.00	0.00	14,540.62	0%	0%	3
MKH2-02-00	Installation of Pipes [Local 10]	4	11-Jan-27	14-Jan-27	07-Jan-27	11-Jan-27	0.00	0.00	43,621.85	0%	0%	3
MKH2-02-00	Backfilling & Compaction [Local 10]	3	16-Jan-27	18-Jan-27	12-Jan-27	14-Jan-27	0.00	0.00	14,540.62	0%	0%	3
Collector 02		166	14-Dec-26	12-May-27	21-Jul-26 A	04-Jul-27	0.00	166,195.80	1,019,971.28	0%	16.29%	-41
Road Works		153	14-Dec-26	12-May-27	21-Jul-26 A	04-Jul-27	0.00	166,195.80	472,918.82	0%	35.14%	-41
Eartworks & Site grading		125	14-Dec-26	10-Apr-27	21-Jul-26 A	01-Jun-27	0.00	166,195.80	238,138.00	0%	69.79%	-41
MKH2-02-00	Road excavation [Collector 02]	6	14-Dec-26	20-Dec-26	21-Jul-26 A	13-Dec-26	0.00	121,671.00	135,190.00	0%	90%	6
MKH2-02-00	Road backfilling [Collector 02]	6	14-Dec-26	20-Dec-26	22-Jul-26 A	13-Dec-26	0.00	44,524.80	49,472.00	0%	90%	6
MKH2-02-00	Subgrade [Collector 02]	6	28-Mar-27	03-Apr-27	19-May-27	25-May-27	0.00	0.00	20,768.00	0%	0%	-41
MKH2-02-00	Aggregate base course [Collector 02	6	04-Apr-27	10-Apr-27	26-May-27	01-Jun-27	0.00	0.00	32,708.00	0%	0%	-41
Asphalt Works		12	11-Apr-27	24-Apr-27	02-Jun-27	15-Jun-27	0.00	0.00	123,760.00	0%	0%	-41
MKH2-02-00	Prime Coat (MC1) [Collector 02]	6	11-Apr-27	17-Apr-27	02-Jun-27	08-Jun-27	0.00	0.00	12,320.00	0%	0%	-41
MKH2-02-00	Bituminous base course [Collector 0	6	18-Apr-27	24-Apr-27	09-Jun-27	15-Jun-27	0.00	0.00	111,440.00	0%	0%	-41
Finishing Works		16	25-Apr-27	12-May-27	16-Jun-27	04-Jul-27	0.00	0.00	111,020.82	0%	0%	-41
Precast Concrete Curb		4	25-Apr-27	28-Apr-27	16-Jun-27	20-Jun-27	0.00	0.00	36,560.82	0%	0%	-41
MKH2-02-0(	Installation of Precast Concrete curb	4	25-Apr-27	28-Apr-27	16-Jun-27	20-Jun-27	0.00	0.00	36,560.82	0%	0%	-41
Precast Interlocking block pavers		3	29-Apr-27	02-May-27	21-Jun-27	23-Jun-27	0.00	0.00	49,140.00	0%	0%	-41
MKH2-02-0(	Installation of Interlocking block pave	3	29-Apr-27	02-May-27	21-Jun-27	23-Jun-27	0.00	0.00	49,140.00	0%	0%	-41
Pavement Markings		6	03-May-27	09-May-27	24-Jun-27	30-Jun-27	0.00	0.00	18,120.00	0%	0%	-41
MKH2-02-0(	Pavement markings [Collector 02]	3	03-May-27	05-May-27	24-Jun-27	27-Jun-27	0.00	0.00	6,120.00	0%	0%	-41
MKH2-02-0(	(Speed Hump) with retroreflectiveThe	3	06-May-27	09-May-27	28-Jun-27	30-Jun-27	0.00	0.00	12,000.00	0%	0%	-41
Traffic Signage		3	10-May-27	12-May-27	01-Jul-27	04-Jul-27	0.00	0.00	7,200.00	0%	0%	-41
MKH2-02-0(	Installation of Traffic Signs [Collector (	3	10-May-27	12-May-27	01-Jul-27	04-Jul-27	0.00	0.00	7,200.00	0%	0%	-41
Storm Water Drainage		72	21-Dec-26	21-Jan-27	14-Dec-26	08-Mar-27	0.00	0.00	547,052.46	0%	0%	-38
Pipe Works		21	21-Dec-26	13-Jan-27	14-Dec-26	06-Jan-27	0.00	0.00	270,901.74	0%	0%	6
MKH2-02-00	Excavation & Compaction (FDT) [Co	4	21-Dec-26	24-Dec-26	14-Dec-26	17-Dec-26	0.00	0.00	27,090.17	0%	0%	6
MKH2-02-00	Sand Bedding [Collector 02]	3	26-Dec-26	28-Dec-26	19-Dec-26	21-Dec-26	0.00	0.00	27,090.17	0%	0%	6
MKH2-02-00	Installation of GRP Pipe [Collector 02	5	29-Dec-26	03-Jan-27	22-Dec-26	27-Dec-26	0.00	0.00	135,450.88	0%	0%	6
MKH2-02-00	Sand Cover & Warning Tape [Collec	3	04-Jan-27	06-Jan-27	28-Dec-26	30-Dec-26	0.00	0.00	54,180.36	0%	0%	6
MKH2-02-00	Backfilling & Compaction [Collector (	6	07-Jan-27	13-Jan-27	31-Dec-26	06-Jan-27	0.00	0.00	27,090.17	0%	0%	6
Manholes		12	04-Jan-27	17-Jan-27	28-Dec-26	10-Jan-27	0.00	0.00	259,340.28	0%	0%	6
MKH2-02-00	Installation of Manholes [Collector 02	6	04-Jan-27	10-Jan-27	28-Dec-26	03-Jan-27	0.00	0.00	165,034.72	0%	0%	6
MKH2-02-00	Installation of Manholes [Collector 02	6	11-Jan-27	17-Jan-27	04-Jan-27	10-Jan-27	0.00	0.00	94,305.56	0%	0%	6
Catch Basins		3	11-Jan-27	13-Jan-27	25-Feb-27	28-Feb-27	0.00	0.00	14,721.36	0%	0%	-38
MKH2-02-00	Construction of Catch basins [Collec	3	11-Jan-27	13-Jan-27	25-Feb-27	28-Feb-27	0.00	0.00	14,721.36	0%	0%	-38
Concrete chambers Pipes		7	14-Jan-27	21-Jan-27	01-Mar-27	08-Mar-27	0.00	0.00	2,089.08	0%	0%	-38
MKH2-02-00	Excavation and Compaction (FDT) [I	2	14-Jan-27	16-Jan-27	01-Mar-27	02-Mar-27	0.00	0.00	417.83	0%	0%	-38
MKH2-02-00	Installation of Pipes [Collector 02]	3	17-Jan-27	19-Jan-27	03-Mar-27	06-Mar-27	0.00	0.00	1,253.50	0%	0%	-38
MKH2-02-00	Backfilling & Compaction [Collector (	2	20-Jan-27	21-Jan-27	07-Mar-27	08-Mar-27	0.00	0.00	417.74	0%	0%	-38
Testing and Commissioning		106	25-Feb-27	27-Jun-27	11-Apr-27	16-Aug-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-T&	Test for Stormwater Utilities	20	25-Feb-27	23-Mar-27	11-Apr-27	03-May-27	0.00	0.00	0.00	0%	0%	-35
MKH2-02-004-T&	Test for Road Works	20	05-Jun-27	27-Jun-27	25-Jul-27	16-Aug-27	0.00	0.00	0.00	0%	0%	-43
Project Hand Over & Close-out		136	24-Mar-27	24-Aug-27	04-May-27	14-Oct-27	0.00	0.00	0.00	0%	0%	-43
As-Built DWGs		116	24-Mar-27	01-Aug-27	04-May-27	20-Sep-27	0.00	0.00	0.00	0%	0%	-43
As-Built DWGs Submittal		101	24-Mar-27	14-Jul-27	04-May-27	02-Sep-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-A	As-Built DWGs Submittal for Stormw	15	24-Mar-27	10-Apr-27	04-May-27	25-May-27	0.00	0.00	0.00	0%	0%	-35
MKH2-02-004-A	As-Built DWGs Submittal for Road W	15	28-Jun-27	14-Jul-27	17-Aug-27	02-Sep-27	0.00	0.00	0.00	0%	0%	-43
As-Built DWGs Approval		101	11-Apr-27	01-Aug-27	26-May-27	20-Sep-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-A	As-Built DWGs Approval for Stormw	10	11-Apr-27	21-Apr-27	26-May-27	06-Jun-27	0.00	0.00	0.00	0%	0%	-35
MKH2-02-004-A	As-Built DWGs Approval for Road W	15	15-Jul-27	01-Aug-27	04-Sep-27	20-Sep-27	0.00	0.00	0.00	0%	0%	-43

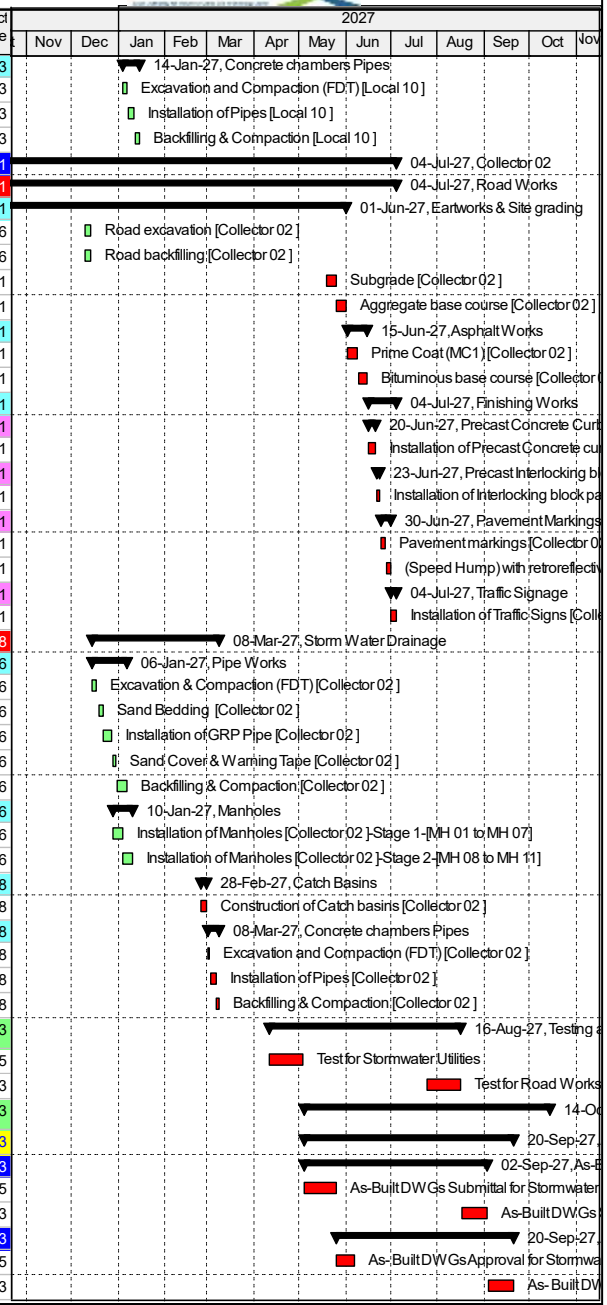

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Demobilization		20	02-Aug-27	24-Aug-27	21-Sep-27	14-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-D	Demobilization of Manpower	10	02-Aug-27	12-Aug-27	21-Sep-27	03-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-D	Removal of Equipment from Site	10	02-Aug-27	12-Aug-27	21-Sep-27	03-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-D	Site Clean Up	10	02-Aug-27	12-Aug-27	21-Sep-27	03-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-D	Removal of Site Offices and Structure	10	02-Aug-27	12-Aug-27	21-Sep-27	03-Oct-27	0.00	0.00	0.00	0%	0%	-43
MKH2-02-004-D	Restoration of Ground Surfaces	10	14-Aug-27	24-Aug-27	04-Oct-27	14-Oct-27	0.00	0.00	0.00	0%	0%	-43



Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
