Road Development for the Support Services Area, Second Industrial City in Makkah (Al-Akayshiyah)

تطوير الطرق لمنطقة الخدمات المساندة بالمدينة الصناعية الثانية بمكة المكرمة (العكيشية)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Trading & Contracting Co.	EGIS	Abdallah Aljulaifi	25-Jun-2026	24-Aug-2027

Scope: road works and the storm water drainage network for the support services area of the Second Industrial City in Makkah, Al-Akayshiyah. Contract value 33.04M SAR excluding VAT, 14 months from site handover.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 20-Oct-2026 the project is 45.2% complete against 32.6% planned, 12.6% ahead of plan, after gaining 4.3% this week against 4.1% planned.

PHYSICAL % COMPLETE
45.2% / 32.6% plan
▲ SPI 1.39 +12.6%

PROGRESS THIS WEEK
+4.3% / +4.1% plan
▲ 0.2% above the weekly plan

CONTRACT TIME ELAPSED
27.5% · day 117 of 425
▼ P6 finish 14-Oct-2027

INVOICED TO DATE (GROSS)
20.4% · 6.75M SAR
3 invoices, last period ends 27-Sep-2026

Progress is ahead of plan, but the schedule finishes 51 days late.

The P6 update (UP 14, data date 20-Oct-2026) schedules project completion on 14-Oct-2027, 51 days after the contract completion date of 24-Aug-2027, with −43 days of total float. The weekly report gives the same forecast. Earthworks are well ahead of plan, but pavement layers, kerbs and interlock have not started and their materials have no purchase orders yet.

Site photos this week

Four photos from the Weekly Photos sheet of the 20-Oct-2026 weekly report, each stamped 18-Oct-2026 with time and altitude (no GPS coordinates are shown). Select a photo to view it larger, then use the arrows to move between photos.




Cutting works, Local Road 17

Stamped 18-Oct-2026, 08:46, altitude 187.3 m.



Subgrade works, Local Road 28

Stamped 18-Oct-2026, 11:33, altitude 164.2 m.

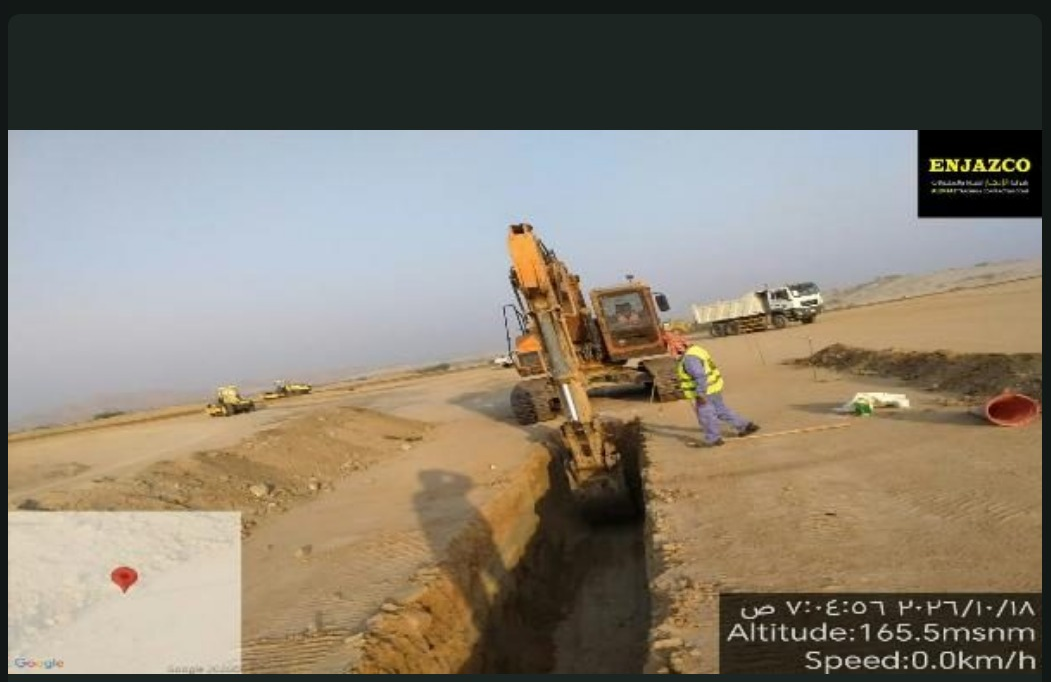

Storm drainage excavation, Local Road 29

Stamped 18-Oct-2026, 07:04, altitude 165.5 m.



Manhole installation, Local Road 29

Stamped 18-Oct-2026, 07:03, altitude 168.3 m.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values. Source: Physical-Chart Data sheet.



WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	28.5	41.0	+12.4%	–	1.44
20-Oct-2026	**32.6**	**45.2**	**+12.6%**	**+4.3**	**1.39**

Only this week's report was used. The 13-Oct-2026 row is the "CM Last Week" figure stated in this week's Progress (2) sheet; earlier weeks are not shown.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (218,590 in total). Source: Weekly Progress Report sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.6%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	2.7%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	2.2%	77.0%	59.4%	−17.6%	0.77	▼ Behind
Road works	54.3%	31.9%	50.1%	+18.2%	1.57	▲ Ahead
Storm water drainage	35.6%	20.5%	29.3%	+8.8%	1.43	▲ Ahead
Testing & commissioning	1.1%	0.0%	0.0%	0.0%	–	Not due yet
Handover & close-out	0.4%	0.0%	0.0%	0.0%	–	Not due yet
Total	100%	**32.6%**	**45.2%**	**+12.6%**	**1.39**	▲ Ahead

The P6 update (UP 14, data date 20-Oct-2026) has 381 activities: 148 completed, 34 in progress and 199 not started. Its scheduled finish is 14-Oct-2027 with −43 days of total float. Critical-path activities fell from 183 to 168 this week; failed starts rose from 25 to 29.

Scope of work: quantities

Total scope and quantity finished for the items under way, from the Major Quantities sheet of the 20-Oct-2026 weekly report. "This week" is the quantity listed in this week's summary of works executed during the week.

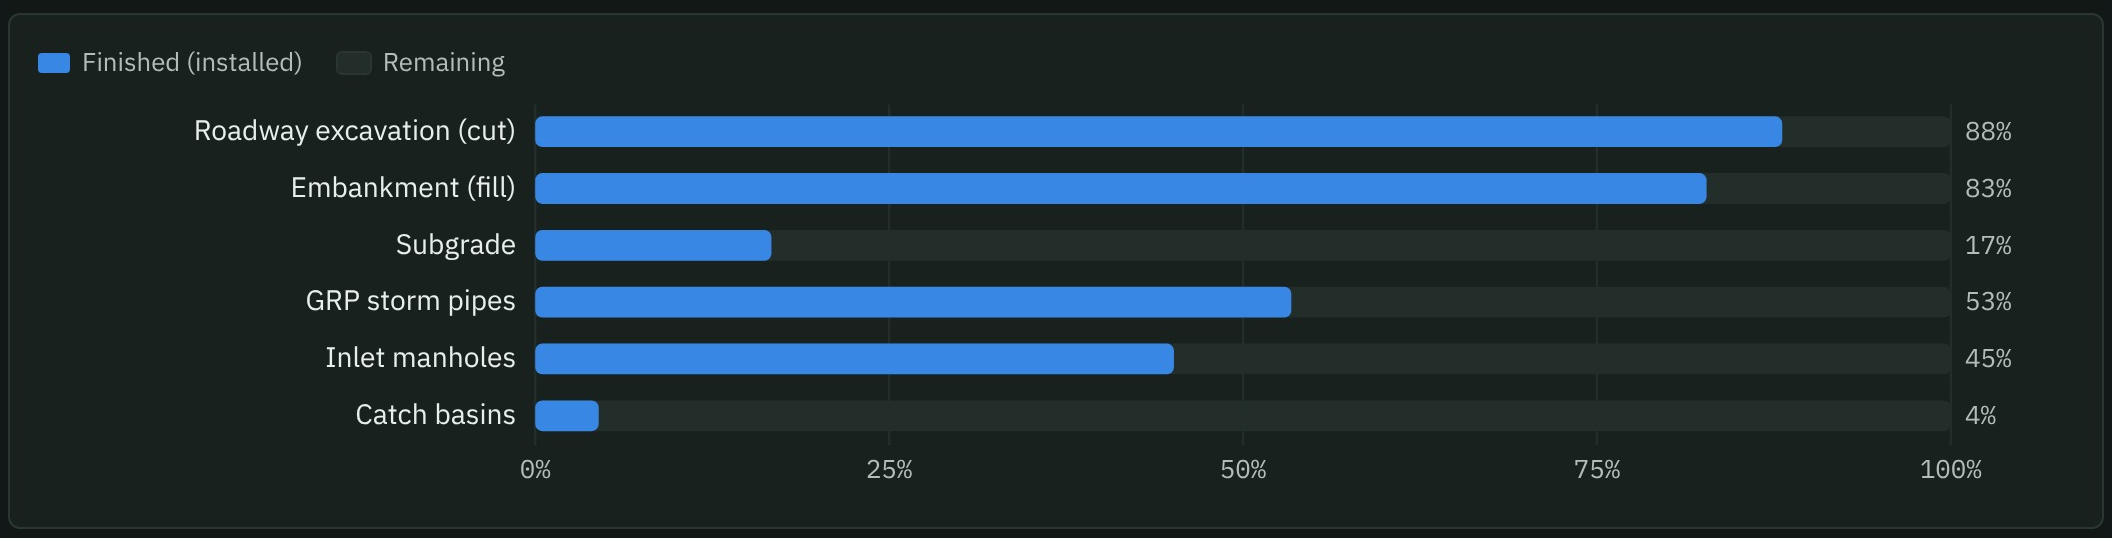

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Roadway excavation (cut)	All roads	m³	252,115	222,090	+7,110	30,025	88.1%	–
Embankment (fill)	All roads	m³	221,841	183,569	+4,140	38,272	82.7%	–
Subgrade	All roads	m³	39,250	6,550	+1,968	32,700	16.7%	–
GRP storm pipes	All roads	LM	5,855	3,127	+941	2,728	53.4%	–
Inlet manholes	All roads	EA	82	37	+10	45	45.1%	–
Catch basins	All roads	EA	156	7	+7	149	4.5%	–

Earthworks well ahead of plan

Cut is 222,090 m³ against 148,344 m³ planned to date, and fill is 183,569 m³ against 130,531 m³ planned. This week: cut on Local Roads 17 and 31, fill on Local Road 31 and subgrade on Local Road 28.

Not yet started

Aggregate base course, bituminous base and wearing courses, precast kerbs, interlock paving, pavement markings and traffic signs are all at 0%. Of the 156 catch basins, 7 are installed, all of them this week.

Milestones

The weekly report and the P6 update give the same forecast dates. The weekly report shows the slip in calendar days; the P6 column shows total float.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	25-Jun-2026	25-Jun-2026	25-Jun-2026 (actual)	–	✓ Done
Baseline programme submission	12-Jul-2026	12-Jul-2026	12-Jul-2026 (actual)	–	✓ Done
Completion of mobilisation	23-Jul-2026	15-Aug-2026 (+23 d)	15-Aug-2026 (actual)	–	✓ Done late
Approval of drawings and materials	23-Aug-2026	19-Sep-2026 (+27 d)	19-Sep-2026 (actual)	–	✓ Done late
Storm water drainage complete	24-Feb-2027	10-Apr-2027 (+45 d)	10-Apr-2027	−20	▼ Late
Road works complete	24-Apr-2027	15-Jun-2027 (+52 d)	15-Jun-2027	−26	▼ Late
Project completion	24-Aug-2027	14-Oct-2027 (+51 d)	14-Oct-2027	−43	▼ Late

The finish is late even though progress is ahead.

Physical progress is 12.6% ahead of plan, yet both the weekly report and P6 forecast completion 51 days after the contract date. Negative float runs through the pavement and storm-drainage work still to come: subgrade on Local Roads 17, 11 and 29 is at −42 to −43 days, and procurement of the pavement materials is at −17 days.

Procurement of key materials

Procurement completion rate per material. Source: Procurement sheet, weekly report 20-Oct-2026.



Pavement materials: no purchase orders


Aggregate base course, bituminous base, precast kerbs, interlock pavers and pavement markings have no purchase order, although the required order dates (29-Aug to 17-Sep-2026) have passed. Aggregate base is needed on site by 15-Nov-2026 and bituminous base by 14-Dec-2026.

Storm drainage materials

GRP pipes (5,855 m), inlet manholes (82) and traffic signs (171) are fully procured. Catch basins are at 110 of 164 (67%).

Manpower

Monthly average head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

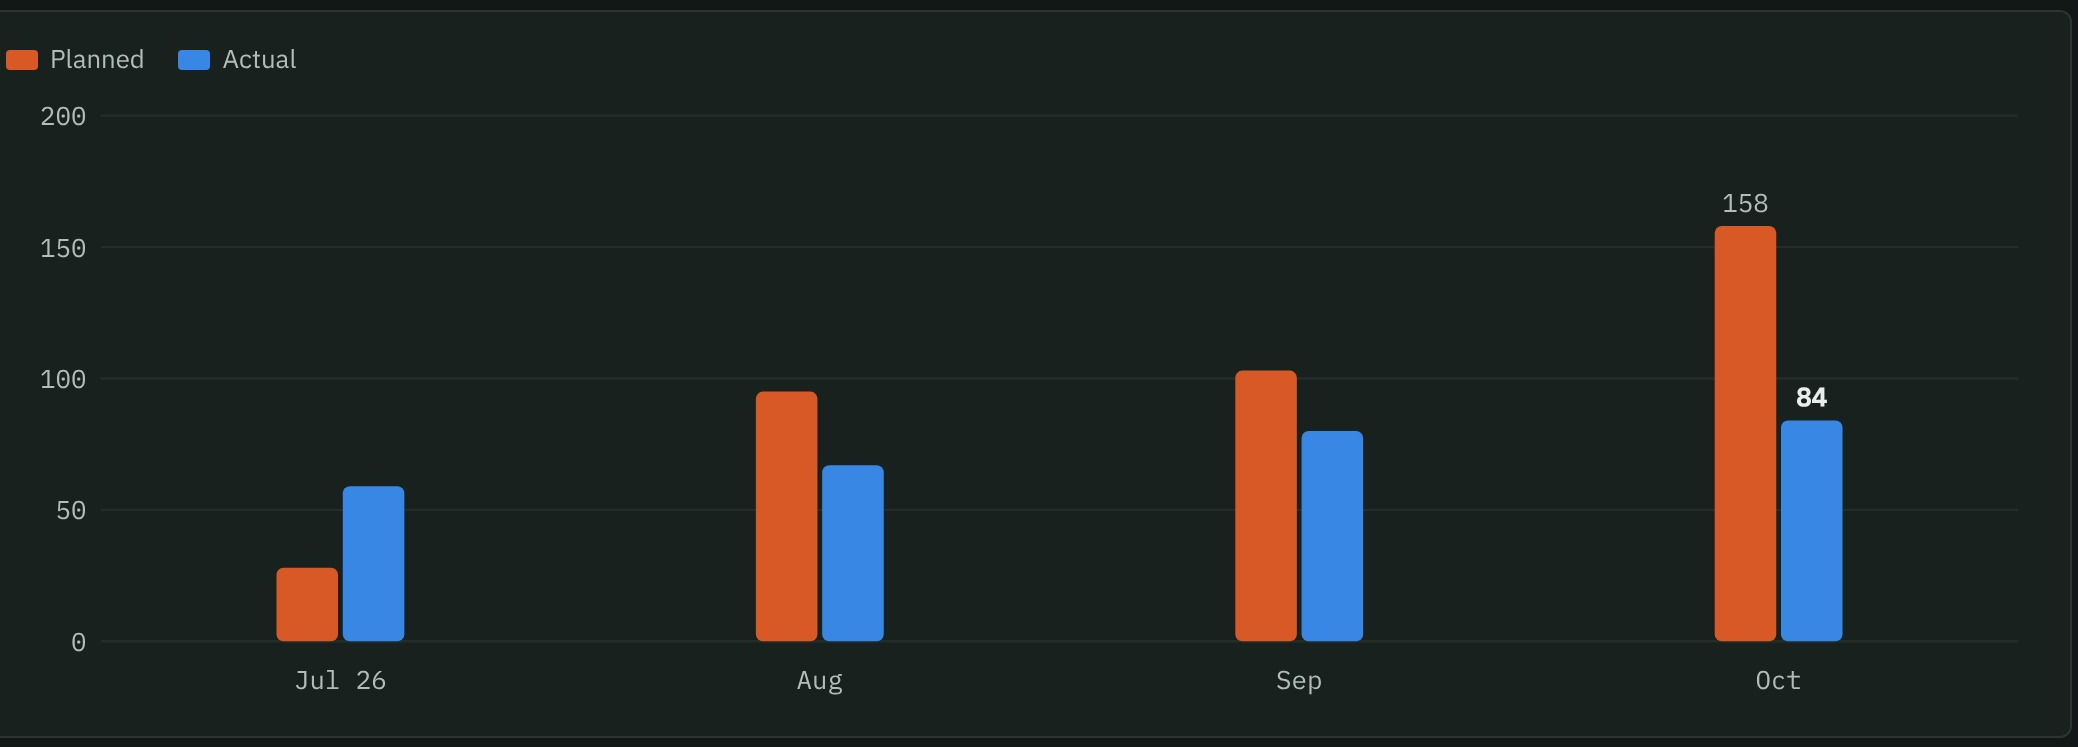

October head count is 84 against 158 planned (−47%): 68 manual workers against 145 planned, and 16 staff against 13. Equipment on site is 62 against 80 planned. The plan peaks at 182 in November 2026.

Cost and invoicing

Contract value

Road works	19,411,954
Storm water drainage	13,628,050
BOQ total (excl. VAT)	**33,040,004**
Contract value incl. 15% VAT	37,996,005
Change orders	0

All values in SAR. Road works are 58.8% of the BOQ and storm water drainage 41.2%. No change orders are registered.

Invoices

Invoices submitted	3
Gross value	6,754,935
Deductions and penalties	2,000
Net incl. VAT	7,770,175
Paid (2 invoices)	3,778,785
FIR value to date	9,511,215

Invoicing is 20.4% of the contract value against 45.2% physical progress. Invoice 3 (26-Aug to 27-Sep-2026) was approved by accounts on 08-Oct-2026 and is not yet paid. There is no advance payment or retention.

Health, safety and quality

Safety Score 0.88

Safe man-hours (cumulative)	36,989
Man-hours this week	2,976
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	1
Property damage	0
Inductions / toolbox talks	4 / 18

Quality Score 0.89

FIRs issued (cumulative)	204
FIRs closed / pending	175 / 29
MIRs issued / closed	42 / 42
NCRs issued	0
Site instructions (closed)	1
Shop drawings approved	22 / 23
Material submittals approved	40 / 42

Consultant quality and safety inspections of 20-Oct-2026.

Open issues and risks

RISK	OWNER	DETAIL
Falls into excavations	Contractor	Unstable soil and missing barricades. Barricades, warning signs and a supervisor at excavations. Rated high (H20, H16 after treatment).
Traffic management	Contractor	Vehicle accidents from inadequate traffic diversion. Diversion signs, barriers and traffic marshals. Rated high (H16).
Operator competence	Contractor	Accidents from insufficient training and supervision of operators. Training, competency checks and supervision. Rated high (H16).
Oil spills	Contractor	Soil contamination from equipment leaks or poor handling of oil. Spill response plan, maintenance and containment. Rated medium (M9).

The issue log and the top-issues panel of the weekly report are empty, and the weekly summary sheets state no delay reasons or challenges.

Data notes

- The summary sheets (works executed and progress files, Progress Summary sheet) label a cost-based figure as "actual" progress. This report uses physical (man-hour) progress only.
- The progress file and the works-executed file show this week's progress with opposite signs.
- The works-executed file gives a project start of 24-Nov-2025 and a contract end of 23-May-2026. The weekly report gives site handover on 25-Jun-2026 and completion on 24-Aug-2027.
- The MODON PM is written as الجليفي in the progress file and as الشنيفي in the works-executed file.

- The weekly physical progress panel shows 8.2% planned and 8.53% earned this week. These add each row twice (17,924 and 18,642 man-hours); the correct figures are 4.10% and 4.26%.
- The Progress sheet uses a budget of 181,410 man-hours, which gives 39.3% planned and 54.5% earned. The Weekly Progress Report sheet and the P6 update use 218,590 man-hours (32.6% and 45.2%), which this report follows.
- Week number: the report states week 17 (Report No. 17 and the Milestones sheet). Whole weeks from site handover to the data date give 16.
- The weekly report shows the completion slip as −51 days, while P6 total float is −43 days. The lower part of the Milestones sheet lists activities and dates of project MKH2-02-003. The Progress Summary gives road works completion as 27-Apr-2027 instead of 24-Apr-2027.
- The forecast in the Physical-Chart Data sheet reaches 100% on 31-Aug-2027, but P6 finishes on 14-Oct-2027.
- The baseline schedule approval is dated 13-Jul-2025, before the contract award of 11-May-2026.
- Major Quantities lists several items twice with different totals (aggregate base 14,403 and 26,167 m³; bituminous base 7,129 and 9,160 m³; subgrade 21,604 and 39,250 m³; interlock 18,500 and 29,206 m²), and electrical items (MV cable, substation, RMU, lighting poles) that are not in this project's roads and storm-drainage scope.
- GRP pipe installed is 3,127 m in Major Quantities but 1,778 m in the Progress Summary.
- Catch basins are 110 of 164 in the Procurement sheet and 110 of 156 in the Progress Summary. Pavement markings are 5,688 m² and 5,668 m².
- "This week" quantities come from the list of works executed this week. The subbase layer on Local Road 28 (1,968 m³) is shown under subgrade, the item its inspection request refers to.
- The manpower summary panel shows 28 planned and 94 actual, while the Manpower sheet gives 158 planned and 84 actual for October.
- The invoice summary shows 0 submitted invoices and 7,768,175 SAR, while the invoice log lists 3 invoices with 7,770,175 SAR net. Potential changes are 0 in the summary and 200,000 SAR in the invoice log.
- The risk register marks the four project risks as Closed while their treatment status is Open; it also holds rows for project MKH2-02-003 and rows without a project.
- Several summary panels in the weekly report workbook show #REF! errors.
- The site photos are the images embedded in the weekly report workbook, about 600 px wide. No separate photo files were uploaded.

Compiled 28-Oct-2026 from weekly report No. 17 (data date 20-Oct-2026) only.
