
egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-004-Road Development for		345	15-Aug-26	24-Aug-27	07-Jul-26 A	21-Oct-27	3,664,638.32	3,916,569.16	24,920,770.91	14.71%	15.72%	-49
Key Milestones		156	24-Feb-27	24-Aug-27	17-Apr-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49
General Milestone		0	24-Aug-27	24-Aug-27	21-Oct-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-KI	Project Completion Date	0		24-Aug-27		21-Oct-27	0.00	0.00	0.00	0%	0%	-49
Contractual Milestone		156	24-Feb-27	24-Aug-27	17-Apr-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49
Construction		156	24-Feb-27	24-Aug-27	17-Apr-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-I	Completion of Road Works	0		24-Apr-27		22-Jun-27	0.00	0.00	0.00	0%	0%	-47
MKH2-02-004-I	Completion of Storm Water Drainag	0		24-Feb-27		17-Apr-27	0.00	0.00	0.00	0%	0%	-41
MKH2-02-004-I	Completion of Entire Project	0		24-Aug-27		21-Oct-27	0.00	0.00	0.00	0%	0%	-49
Procurement		80	24-Aug-26	25-Nov-26	08-Oct-26 A	27-Jan-27	0.00	0.00	0.00	0%	0%	-54
Road Works - Civil		80	24-Aug-26	25-Nov-26	27-Oct-26	27-Jan-27	0.00	0.00	0.00	0%	0%	-54
Aggregate Base Course		65	24-Aug-26	08-Nov-26	27-Oct-26	10-Jan-27	0.00	0.00	0.00	0%	0%	-54
MKH2-02-004-I	PO for Aggregate Base Course	5	24-Aug-26	29-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	100%	0%	-54
MKH2-02-004-I	Material Delivery for Aggregate Base	30	30-Aug-26	04-Oct-26	02-Nov-26	06-Dec-26	0.00	0.00	0.00	100%	0%	-54
MKH2-02-004-I	Material Delivery for Aggregate Base	30	05-Oct-26	08-Nov-26	07-Dec-26	10-Jan-27	0.00	0.00	0.00	63.33%	0%	-54
Bituminous Base Course		75	30-Aug-26	25-Nov-26	02-Nov-26	27-Jan-27	0.00	0.00	0.00	0%	0%	-54
MKH2-02-004-I	PO for Bituminous Base Course	5	30-Aug-26	03-Sep-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	100%	0%	-54
MKH2-02-004-I	Material Delivery for Bituminous Base	35	05-Sep-26	15-Oct-26	08-Nov-26	17-Dec-26	0.00	0.00	0.00	100%	0%	-54
MKH2-02-004-I	Material Delivery for Bituminous Base	35	17-Oct-26	25-Nov-26	19-Dec-26	27-Jan-27	0.00	0.00	0.00	25.71%	0%	-54
Precast Concrete Curb		65	05-Sep-26	19-Nov-26	08-Nov-26	21-Jan-27	0.00	0.00	0.00	0%	0%	-54
MKH2-02-004-I	PO for Precast Concrete Curb	5	05-Sep-26	09-Sep-26	08-Nov-26	12-Nov-26	0.00	0.00	0.00	100%	0%	-54
MKH2-02-004-I	Material Fabrication for Precast Conc	30	10-Sep-26	15-Oct-26	14-Nov-26	17-Dec-26	0.00	0.00	0.00	100%	0%	-54
MKH2-02-004-I	Material Delivery for Precast Concret	30	17-Oct-26	19-Nov-26	19-Dec-26	21-Jan-27	0.00	0.00	0.00	30%	0%	-54
Interlocking Block Pavers		60	14-Sep-26	23-Nov-26	14-Nov-26	21-Jan-27	0.00	0.00	0.00	0%	0%	-51
MKH2-02-004-I	Material Fabrication for Interlocking B	30	14-Sep-26	19-Oct-26	14-Nov-26	17-Dec-26	0.00	0.00	0.00	100%	0%	-51
MKH2-02-004-I	Material Delivery for Interlocking Bloc	30	20-Oct-26	23-Nov-26	19-Dec-26	21-Jan-27	0.00	0.00	0.00	20%	0%	-51
Pavement Markings		54	14-Sep-26	16-Nov-26	14-Nov-26	14-Jan-27	0.00	0.00	0.00	0%	0%	-51
MKH2-02-004-I	PO for Pavement Markings	4	14-Sep-26	17-Sep-26	14-Nov-26	17-Nov-26	0.00	0.00	0.00	100%	0%	-51
MKH2-02-004-I	Material Fabrication for Pavement Ma	25	19-Sep-26	18-Oct-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	100%	0%	-51
MKH2-02-004-I	Material Delivery for Pavement Marki	25	19-Oct-26	16-Nov-26	17-Dec-26	14-Jan-27	0.00	0.00	0.00	28%	0%	-51
Stormwater Utilities		20	01-Oct-26	16-Nov-26	08-Oct-26 A	28-Nov-26	0.00	0.00	0.00	0%	0%	-10
Catch Basins		20	01-Oct-26	16-Nov-26	08-Oct-26 A	28-Nov-26	0.00	0.00	0.00	0%	0%	-10
MKH2-02-004-I	Material Delivery for Catch Basins-St	20	01-Oct-26	24-Oct-26	08-Oct-26 A	04-Nov-26	0.00	0.00	0.00	100%	80%	-10
MKH2-02-004-I	Material Delivery for Catch Basins-St	20	25-Oct-26	16-Nov-26	05-Nov-26	28-Nov-26	0.00	0.00	0.00	10%	0%	-10
Construction		275	15-Aug-26	03-Jun-27	07-Jul-26 A	31-Jul-27	3,664,638.32	3,916,569.16	24,920,770.91	14.71%	15.72%	-49
Roads		275	15-Aug-26	03-Jun-27	07-Jul-26 A	31-Jul-27	3,664,638.32	3,916,569.16	24,920,770.91	14.71%	15.72%	-49
Local 17		214	15-Aug-26	01-Mar-27	01-Aug-26 A	20-May-27	2,893,900.28	601,824.40	7,850,090.48	36.86%	7.67%	-62
Road Works		214	15-Aug-26	01-Mar-27	01-Aug-26 A	20-May-27	1,049,926.00	601,824.40	4,254,579.65	24.68%	14.15%	-62
Earthworks & Site grading		138	15-Aug-26	01-Dec-26	01-Aug-26 A	11-Feb-27	1,049,926.00	601,824.40	1,658,260.00	63.31%	36.29%	-62
MKH2-02-00	Road excavation [Local 17]-Stage 2	18	15-Aug-26	03-Sep-26	20-Aug-26 A	07-Nov-26	768,614.00	461,168.40	768,614.00	100%	60%	-54
MKH2-02-00	Road backfilling [Local 17]-Stage 2	18	15-Aug-26	03-Sep-26	01-Aug-26 A	12-Nov-26	281,312.00	140,656.00	281,312.00	100%	50%	-59
MKH2-02-00	Subgrade [Local 17]	15	28-Oct-26	14-Nov-26	09-Jan-27	25-Jan-27	0.00	0.00	236,170.00	0%	0%	-62
MKH2-02-00	Aggregate base course [Local 17]	15	15-Nov-26	01-Dec-26	26-Jan-27	11-Feb-27	0.00	0.00	372,164.00	0%	0%	-62
Asphalt Works		25	02-Dec-26	30-Dec-26	13-Feb-27	17-Mar-27	0.00	0.00	1,403,360.00	0%	0%	-62
MKH2-02-00	Prime Coat (MC1) [Local 17]	10	02-Dec-26	13-Dec-26	13-Feb-27	24-Feb-27	0.00	0.00	140,560.00	0%	0%	-62
MKH2-02-00	Bituminous base course [Local 17]	15	14-Dec-26	30-Dec-26	25-Feb-27	17-Mar-27	0.00	0.00	1,262,800.00	0%	0%	-62
Finishing Works		51	31-Dec-26	01-Mar-27	18-Mar-27	20-May-27	0.00	0.00	1,192,959.65	0%	0%	-62
Precast Concrete Curb		12	31-Dec-26	13-Jan-27	18-Mar-27	31-Mar-27	0.00	0.00	415,849.65	0%	0%	-62
MKH2-02-00	Installation of Precast Concrete curb	12	31-Dec-26	13-Jan-27	18-Mar-27	31-Mar-27	0.00	0.00	415,849.65	0%	0%	-62

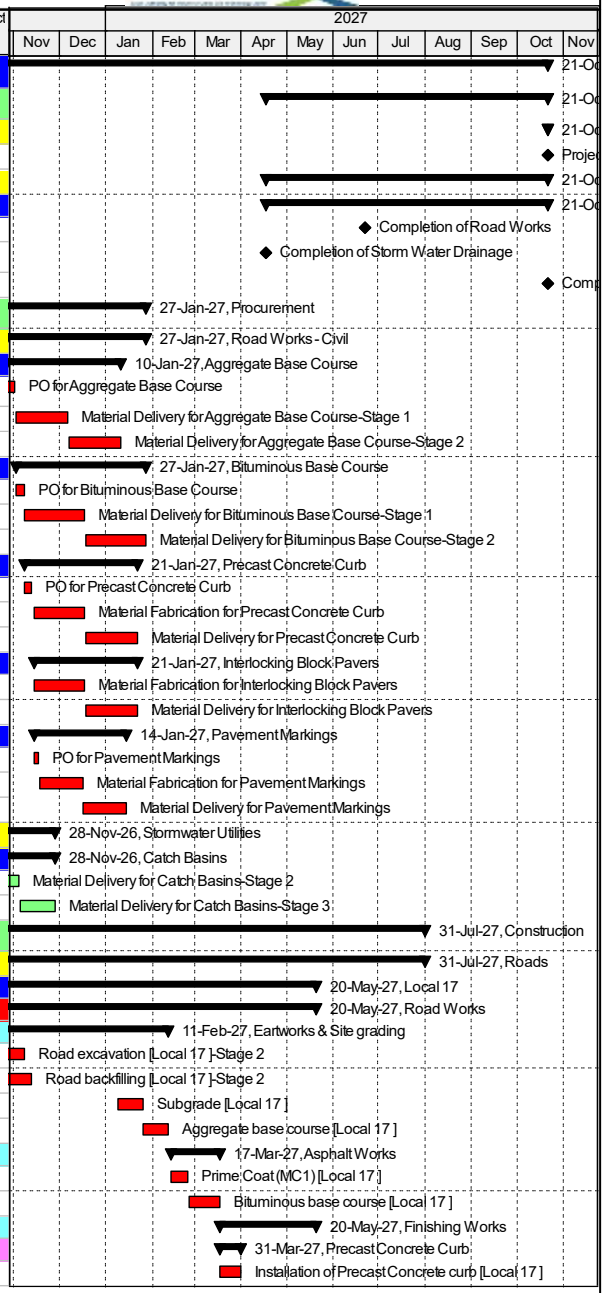

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Precast Interlocking block pavers		11	14-Jan-27	26-Jan-27	01-Apr-27	13-Apr-27	0.00	0.00	559,160.00	0%	0%	-62
MKH2-02-0(	Installation of Interlocking block pave	11	14-Jan-27	26-Jan-27	01-Apr-27	13-Apr-27	0.00	0.00	559,160.00	0%	0%	-62
Pavement Markings		16	27-Jan-27	14-Feb-27	14-Apr-27	02-May-27	0.00	0.00	129,750.00	0%	0%	-62
MKH2-02-0(	Pavement markings [Local 17]	8	27-Jan-27	04-Feb-27	14-Apr-27	22-Apr-27	0.00	0.00	69,750.00	0%	0%	-62
MKH2-02-0(	(Speed Hump) with retroreflective The	8	06-Feb-27	14-Feb-27	24-Apr-27	02-May-27	0.00	0.00	60,000.00	0%	0%	-62
Traffic Signage		12	15-Feb-27	01-Mar-27	03-May-27	20-May-27	0.00	0.00	88,200.00	0%	0%	-62
MKH2-02-0(	Installation of Traffic Signs [Local 17]	12	15-Feb-27	01-Mar-27	03-May-27	20-May-27	0.00	0.00	88,200.00	0%	0%	-62
Storm Water Drainage		109	15-Aug-26	02-Jan-27	27-Oct-26	03-Mar-27	1,843,974.28	0.00	3,595,510.83	51.29%	0%	-51
Pipe Works		63	15-Aug-26	27-Oct-26	27-Oct-26	07-Jan-27	1,358,607.29	0.00	1,368,373.77	99.29%	0%	-62
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	13	15-Aug-26	29-Aug-26	27-Oct-26	10-Nov-26	68,472.00	0.00	68,472.00	100%	0%	-62
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	13	30-Aug-26	13-Sep-26	11-Nov-26	25-Nov-26	68,365.34	0.00	68,365.34	100%	0%	-62
MKH2-02-00(	Sand Bedding [Local 17]-Stage 1	8	30-Aug-26	07-Sep-26	11-Nov-26	19-Nov-26	68,472.00	0.00	68,472.00	100%	0%	-62
MKH2-02-00(	Sand Bedding [Local 17]-Stage 2	8	14-Sep-26	22-Sep-26	26-Nov-26	05-Dec-26	68,365.34	0.00	68,365.34	100%	0%	-62
MKH2-02-00(	Installation of GRP Pipe [Local 17]-S	14	08-Sep-26	24-Sep-26	21-Nov-26	06-Dec-26	342,360.11	0.00	342,360.11	100%	0%	-62
MKH2-02-00(	Installation of GRP Pipe [Local 17]-S	14	26-Sep-26	11-Oct-26	07-Dec-26	22-Dec-26	341,826.84	0.00	341,826.84	100%	0%	-62
MKH2-02-00(	Sand Cover & Warning Tape [Local	7	26-Sep-26	03-Oct-26	07-Dec-26	14-Dec-26	136,944.06	0.00	136,944.06	100%	0%	-62
MKH2-02-00(	Sand Cover & Warning Tape [Local	7	12-Oct-26	19-Oct-26	23-Dec-26	30-Dec-26	136,730.75	0.00	136,730.75	100%	0%	-62
MKH2-02-00(	Backfilling & Compaction [Local 17]-	7	04-Oct-26	11-Oct-26	15-Dec-26	22-Dec-26	68,472.00	0.00	68,472.00	100%	0%	-62
MKH2-02-00(	Backfilling & Compaction [Local 17]-	7	20-Oct-26	27-Oct-26	31-Dec-26	07-Jan-27	58,598.86	0.00	68,365.34	85.71%	0%	-62
Manholes		35	08-Oct-26	17-Nov-26	07-Dec-26	16-Jan-27	377,222.22	0.00	778,020.83	48.48%	0%	-51
MKH2-02-00(	Installation of Manholes [Local 17]-S	7	08-Oct-26	15-Oct-26	07-Dec-26	14-Dec-26	165,034.72	0.00	165,034.72	100%	0%	-51
MKH2-02-00(	Installation of Manholes [Local 17]-S	7	17-Oct-26	24-Oct-26	15-Dec-26	22-Dec-26	165,034.72	0.00	165,034.72	100%	0%	-51
MKH2-02-00(	Installation of Manholes [Local 17]-S	7	25-Oct-26	01-Nov-26	23-Dec-26	30-Dec-26	47,152.78	0.00	165,034.72	28.57%	0%	-51
MKH2-02-00(	Installation of Manholes [Local 17]-S	7	02-Nov-26	09-Nov-26	31-Dec-26	07-Jan-27	0.00	0.00	165,034.72	0%	0%	-51
MKH2-02-00(	Installation of Manholes [Local 17]-S	7	10-Nov-26	17-Nov-26	09-Jan-27	16-Jan-27	0.00	0.00	117,881.94	0%	0%	-51
Catch Basins		67	17-Oct-26	02-Jan-27	15-Dec-26	03-Mar-27	94,637.33	0.00	706,625.39	13.39%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	17-Oct-26	24-Oct-26	15-Dec-26	22-Dec-26	73,606.81	0.00	73,606.81	100%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	25-Oct-26	01-Nov-26	23-Dec-26	30-Dec-26	21,030.52	0.00	73,606.81	28.57%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	02-Nov-26	09-Nov-26	31-Dec-26	07-Jan-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	10-Nov-26	17-Nov-26	09-Jan-27	16-Jan-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	18-Nov-26	25-Nov-26	17-Jan-27	24-Jan-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	26-Nov-26	03-Dec-26	25-Jan-27	01-Feb-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	05-Dec-26	12-Dec-26	02-Feb-27	09-Feb-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	13-Dec-26	20-Dec-26	10-Feb-27	17-Feb-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	7	21-Dec-26	28-Dec-26	18-Feb-27	27-Feb-27	0.00	0.00	73,606.81	0%	0%	-51
MKH2-02-00(	Construction of Catch basins [Local '	4	29-Dec-26	02-Jan-27	28-Feb-27	03-Mar-27	0.00	0.00	44,164.09	0%	0%	-51
Concrete chambers Pipes		45	25-Oct-26	15-Dec-26	23-Dec-26	13-Feb-27	13,507.43	0.00	742,490.84	1.82%	0%	-51
MKH2-02-00(	Excavation and Compaction (FDT) [I	11	25-Oct-26	05-Nov-26	23-Dec-26	04-Jan-27	13,507.43	0.00	74,290.89	18.18%	0%	-51
MKH2-02-00(	Excavation and Compaction (FDT) [I	11	07-Nov-26	18-Nov-26	05-Jan-27	17-Jan-27	0.00	0.00	74,207.32	0%	0%	-51
MKH2-02-00(	Installation of Pipes [Local 17]-Stage	12	07-Nov-26	19-Nov-26	05-Jan-27	18-Jan-27	0.00	0.00	222,872.57	0%	0%	-51
MKH2-02-00(	Installation of Pipes [Local 17]-Stage	12	21-Nov-26	03-Dec-26	19-Jan-27	01-Feb-27	0.00	0.00	222,621.87	0%	0%	-51
MKH2-02-00(	Backfilling & Compaction [Local 17]-	10	21-Nov-26	01-Dec-26	19-Jan-27	30-Jan-27	0.00	0.00	74,290.89	0%	0%	-51
MKH2-02-00(	Backfilling & Compaction [Local 17]-	10	05-Dec-26	15-Dec-26	02-Feb-27	13-Feb-27	0.00	0.00	74,207.32	0%	0%	-51
Local 11		158	17-Sep-26	28-Feb-27	10-Oct-26 A	13-May-27	266,037.38	353,778.82	3,570,670.47	7.45%	9.91%	-61
Road Works		158	17-Sep-26	28-Feb-27	15-Oct-26 A	13-May-27	175,168.00	43,792.00	2,168,105.47	8.08%	2.02%	-61
Eartworks & Site grading		93	17-Sep-26	14-Dec-26	15-Oct-26 A	23-Feb-27	175,168.00	43,792.00	553,928.00	31.62%	7.91%	-60
MKH2-02-00(	Road backfilling [Local 11]-Stage 2	11	17-Sep-26	30-Sep-26	15-Oct-26 A	22-Nov-26	175,168.00	43,792.00	175,168.00	100%	25%	-45
MKH2-02-00(	Subgrade [Local 11]	9	24-Nov-26	03-Dec-26	26-Jan-27	04-Feb-27	0.00	0.00	147,048.00	0%	0%	-54
MKH2-02-00(	Aggregate base course [Local 11]	9	05-Dec-26	14-Dec-26	13-Feb-27	23-Feb-27	0.00	0.00	231,712.00	0%	0%	-60
Asphalt Works		22	15-Dec-26	09-Jan-27	25-Feb-27	25-Mar-27	0.00	0.00	873,600.00	0%	0%	-61

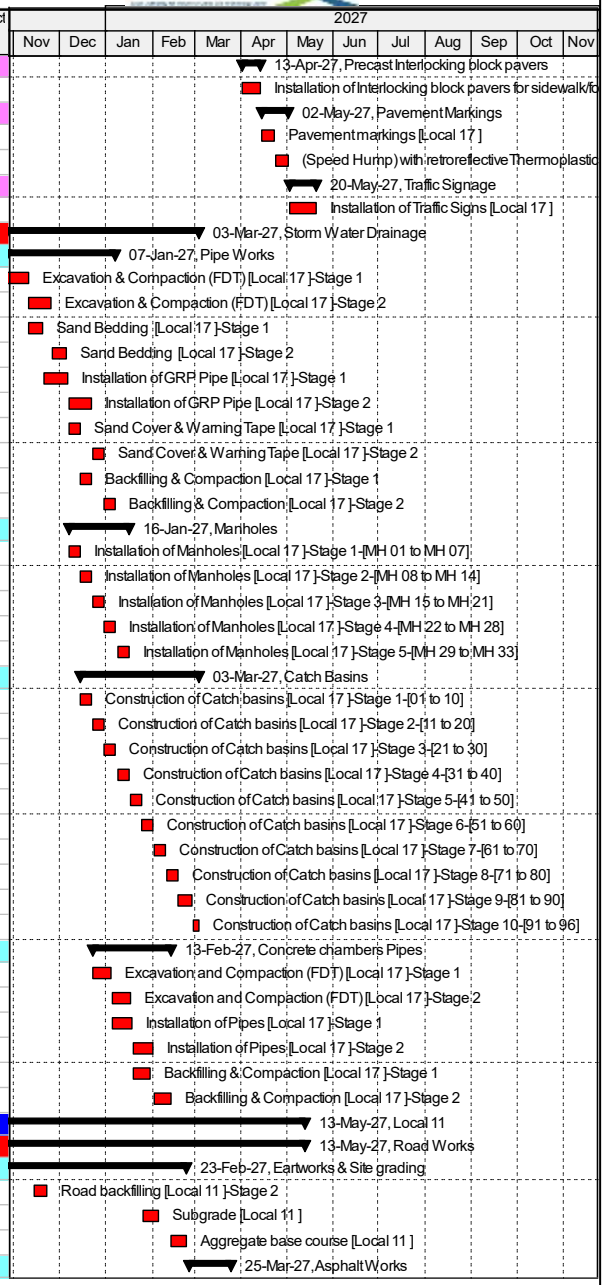

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Prime Coat (MC1) [Local 11]	10	15-Dec-26	26-Dec-26	25-Feb-27	08-Mar-27	0.00	0.00	87,360.00	0%	0%	-61
MKH2-02-00	Bituminous base course [Local 11]	12	27-Dec-26	09-Jan-27	09-Mar-27	25-Mar-27	0.00	0.00	786,240.00	0%	0%	-61
Finishing Works		42	10-Jan-27	28-Feb-27	27-Mar-27	13-May-27	0.00	0.00	740,577.47	0%	0%	-61
Precast Concrete Curb		11	10-Jan-27	21-Jan-27	27-Mar-27	07-Apr-27	0.00	0.00	258,972.47	0%	0%	-61
MKH2-02-0(	Installation of Precast Concrete curb [	11	10-Jan-27	21-Jan-27	27-Mar-27	07-Apr-27	0.00	0.00	258,972.47	0%	0%	-61
Precast Interlocking block pavers		10	23-Jan-27	02-Feb-27	08-Apr-27	19-Apr-27	0.00	0.00	348,180.00	0%	0%	-61
MKH2-02-0(	Installation of Interlocking block pave	10	23-Jan-27	02-Feb-27	08-Apr-27	19-Apr-27	0.00	0.00	348,180.00	0%	0%	-61
Pavement Markings		14	03-Feb-27	18-Feb-27	20-Apr-27	05-May-27	0.00	0.00	79,425.00	0%	0%	-61
MKH2-02-0(	Pavement markings [Local 11]	7	03-Feb-27	10-Feb-27	20-Apr-27	27-Apr-27	0.00	0.00	43,425.00	0%	0%	-61
MKH2-02-0(	(Speed Hump) with retroreflective Th	7	11-Feb-27	18-Feb-27	28-Apr-27	05-May-27	0.00	0.00	36,000.00	0%	0%	-61
Traffic Signage		7	20-Feb-27	28-Feb-27	06-May-27	13-May-27	0.00	0.00	54,000.00	0%	0%	-61
MKH2-02-0(	Installation of Traffic Signs [Local 11]	7	20-Feb-27	28-Feb-27	06-May-27	13-May-27	0.00	0.00	54,000.00	0%	0%	-61
Storm Water Drainage		38	11-Oct-26	19-Dec-26	10-Oct-26 A	02-Jan-27	90,869.38	309,986.82	1,402,565.00	6.48%	22.1%	-12
Pipe Works		28	11-Oct-26	23-Nov-26	10-Oct-26 A	22-Dec-26	90,869.38	281,695.15	454,347.02	20%	62%	-25
MKH2-02-00	Excavation & Compaction (FDT) [Lo	8	11-Oct-26	19-Oct-26	10-Oct-26 A	26-Nov-26	45,434.69	36,347.75	45,434.69	100%	80%	-33
MKH2-02-00	Sand Bedding [Local 11]-Stage 2	6	20-Oct-26	26-Oct-26	12-Oct-26 A	30-Nov-26	45,434.69	27,260.81	45,434.69	100%	60%	-30
MKH2-02-00	Installation of GRP Pipe [Local 11]-St	11	31-Oct-26	11-Nov-26	12-Oct-26 A	13-Dec-26	0.00	136,304.12	227,173.53	0%	60%	-27
MKH2-02-00	Sand Cover & Warning Tape [Local	5	12-Nov-26	17-Nov-26	18-Oct-26 A	16-Dec-26	0.00	54,521.65	90,869.42	0%	60%	-25
MKH2-02-00	Backfilling & Compaction [Local 11]-	5	18-Nov-26	23-Nov-26	18-Oct-26 A	22-Dec-26	0.00	27,260.81	45,434.69	0%	60%	-25
Manholes		7	17-Nov-26	24-Nov-26	18-Oct-26 A	28-Nov-26	0.00	28,291.67	141,458.33	0%	20%	-3
MKH2-02-00	Installation of Manholes [Local 11]-St	7	17-Nov-26	24-Nov-26	18-Oct-26 A	28-Nov-26	0.00	28,291.67	141,458.33	0%	20%	-3
Catch Basins		35	09-Nov-26	19-Dec-26	23-Nov-26	02-Jan-27	0.00	0.00	368,034.06	0%	0%	-12
MKH2-02-00	Construction of Catch basins [Local	7	09-Nov-26	16-Nov-26	23-Nov-26	30-Nov-26	0.00	0.00	73,606.81	0%	0%	-12
MKH2-02-00	Construction of Catch basins [Local	7	17-Nov-26	24-Nov-26	01-Dec-26	08-Dec-26	0.00	0.00	73,606.81	0%	0%	-12
MKH2-02-00	Construction of Catch basins [Local	7	25-Nov-26	02-Dec-26	09-Dec-26	16-Dec-26	0.00	0.00	73,606.81	0%	0%	-12
MKH2-02-00	Construction of Catch basins [Local	7	03-Dec-26	10-Dec-26	17-Dec-26	24-Dec-26	0.00	0.00	73,606.81	0%	0%	-12
MKH2-02-00	Construction of Catch basins [Local	7	12-Dec-26	19-Dec-26	26-Dec-26	02-Jan-27	0.00	0.00	73,606.81	0%	0%	-12
Concrete chambers Pipes		25	17-Nov-26	15-Dec-26	01-Dec-26	29-Dec-26	0.00	0.00	438,725.60	0%	0%	-12
MKH2-02-00	Excavation and Compaction (FDT) [	9	17-Nov-26	26-Nov-26	01-Dec-26	10-Dec-26	0.00	0.00	87,745.14	0%	0%	-12
MKH2-02-00	Installation of Pipes [Local 11]	7	28-Nov-26	05-Dec-26	12-Dec-26	19-Dec-26	0.00	0.00	263,235.32	0%	0%	-12
MKH2-02-00	Backfilling & Compaction [Local 11]	9	06-Dec-26	15-Dec-26	20-Dec-26	29-Dec-26	0.00	0.00	87,745.14	0%	0%	-12
Local 29		167	01-Oct-26	03-Mar-27	12-Aug-26 A	10-May-27	301,891.21	699,787.88	2,379,822.62	12.69%	29.41%	-55
Road Works		167	01-Oct-26	03-Mar-27	12-Aug-26 A	10-May-27	192,464.00	163,594.40	1,293,024.70	14.88%	12.65%	-55
Eartworks & Site grading		119	01-Oct-26	05-Jan-27	12-Aug-26 A	15-Mar-27	192,464.00	163,594.40	400,544.00	48.05%	40.84%	-55
MKH2-02-00	Road backfilling [Local 29]	10	01-Oct-26	12-Oct-26	12-Aug-26 A	28-Nov-26	192,464.00	163,594.40	192,464.00	100%	85%	-40
MKH2-02-00	Subgrade [Local 29]	14	05-Dec-26	20-Dec-26	06-Feb-27	21-Feb-27	0.00	0.00	80,784.00	0%	0%	-54
MKH2-02-00	Aggregate base course [Local 29]	14	21-Dec-26	05-Jan-27	24-Feb-27	15-Mar-27	0.00	0.00	127,296.00	0%	0%	-55
Asphalt Works		18	06-Jan-27	26-Jan-27	16-Mar-27	05-Apr-27	0.00	0.00	480,480.00	0%	0%	-55
MKH2-02-00	Prime Coat (MC1) [Local 29]	8	06-Jan-27	14-Jan-27	16-Mar-27	24-Mar-27	0.00	0.00	48,160.00	0%	0%	-55
MKH2-02-00	Bituminous base course [Local 29]	10	16-Jan-27	26-Jan-27	25-Mar-27	05-Apr-27	0.00	0.00	432,320.00	0%	0%	-55
Finishing Works		30	27-Jan-27	03-Mar-27	06-Apr-27	10-May-27	0.00	0.00	412,000.70	0%	0%	-55
Precast Concrete Curb		6	27-Jan-27	02-Feb-27	06-Apr-27	12-Apr-27	0.00	0.00	142,240.70	0%	0%	-55
MKH2-02-0(	Installation of Precast Concrete curb [	6	27-Jan-27	02-Feb-27	06-Apr-27	12-Apr-27	0.00	0.00	142,240.70	0%	0%	-55
Precast Interlocking block pavers		6	03-Feb-27	09-Feb-27	13-Apr-27	19-Apr-27	0.00	0.00	191,310.00	0%	0%	-55
MKH2-02-0(	Installation of Interlocking block pave	6	03-Feb-27	09-Feb-27	13-Apr-27	19-Apr-27	0.00	0.00	191,310.00	0%	0%	-55
Pavement Markings		12	10-Feb-27	24-Feb-27	20-Apr-27	03-May-27	0.00	0.00	47,850.00	0%	0%	-55
MKH2-02-0(	Pavement markings [Local 29]	6	10-Feb-27	16-Feb-27	20-Apr-27	26-Apr-27	0.00	0.00	23,850.00	0%	0%	-55
MKH2-02-0(	(Speed Hump) with retroreflective Th	6	17-Feb-27	24-Feb-27	27-Apr-27	03-May-27	0.00	0.00	24,000.00	0%	0%	-55
Traffic Signage		6	25-Feb-27	03-Mar-27	04-May-27	10-May-27	0.00	0.00	30,600.00	0%	0%	-55
MKH2-02-0(	Installation of Traffic Signs [Local 29]	6	25-Feb-27	03-Mar-27	04-May-27	10-May-27	0.00	0.00	30,600.00	0%	0%	-55
Storm Water Drainage		44	13-Oct-26	20-Dec-26	14-Oct-26 A	14-Jan-27	109,427.21	536,193.48	1,086,797.92	10.07%	49.34%	-22

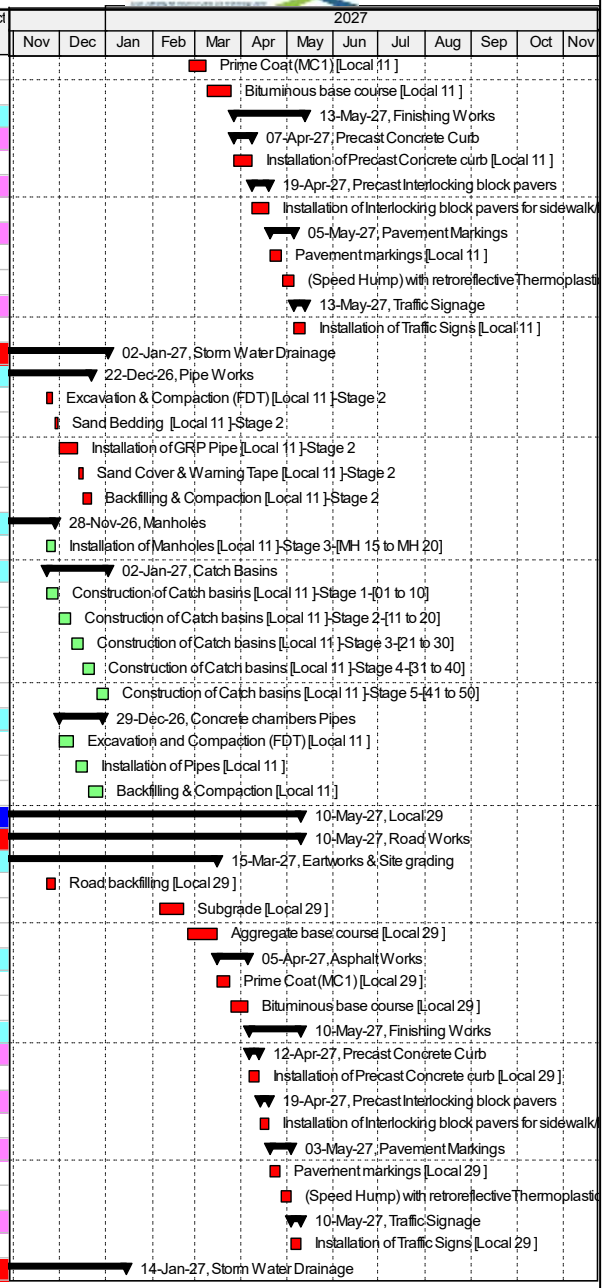

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Pipe Works		32	13-Oct-26	18-Nov-26	14-Oct-26 A	14-Dec-26	109,427.21	536,193.48	547,136.20	20%	98%	-22
MKH2-02-00	Excavation & Compaction (FDT) [Lo	6	13-Oct-26	19-Oct-26	14-Oct-26 A	05-Dec-26	54,713.60	53,619.33	54,713.60	100%	98%	-40
MKH2-02-00	Sand Bedding [Local 29]	6	20-Oct-26	26-Oct-26	15-Oct-26 A	07-Dec-26	54,713.60	53,619.33	54,713.60	100%	98%	-36
MKH2-02-00	Installation of GRP Pipe [Local 29]	9	27-Oct-26	05-Nov-26	17-Oct-26 A	09-Dec-26	0.00	268,096.76	273,568.13	0%	98%	-29
MKH2-02-00	Sand Cover & Warning Tape [Local	5	07-Nov-26	11-Nov-26	18-Oct-26 A	12-Dec-26	0.00	107,238.72	109,427.26	0%	98%	-26
MKH2-02-00	Backfilling & Compaction [Local 29]	6	12-Nov-26	18-Nov-26	19-Oct-26 A	14-Dec-26	0.00	53,619.33	54,713.60	0%	98%	-22
Catch Basins		25	15-Nov-26	13-Dec-26	10-Dec-26	07-Jan-27	0.00	0.00	257,623.84	0%	0%	-22
MKH2-02-00	Construction of Catch basins [Local 2	7	15-Nov-26	22-Nov-26	10-Dec-26	17-Dec-26	0.00	0.00	73,606.81	0%	0%	-22
MKH2-02-00	Construction of Catch basins [Local 2	7	23-Nov-26	30-Nov-26	19-Dec-26	26-Dec-26	0.00	0.00	73,606.81	0%	0%	-22
MKH2-02-00	Construction of Catch basins [Local 2	7	01-Dec-26	08-Dec-26	27-Dec-26	03-Jan-27	0.00	0.00	73,606.81	0%	0%	-22
MKH2-02-00	Construction of Catch basins [Local 2	4	09-Dec-26	13-Dec-26	04-Jan-27	07-Jan-27	0.00	0.00	36,803.41	0%	0%	-22
Concrete chambers Pipes		24	23-Nov-26	20-Dec-26	19-Dec-26	14-Jan-27	0.00	0.00	282,037.88	0%	0%	-22
MKH2-02-00	Excavation and Compaction (FDT) [	7	23-Nov-26	30-Nov-26	19-Dec-26	26-Dec-26	0.00	0.00	56,407.59	0%	0%	-22
MKH2-02-00	Installation of Pipes [Local 29]	9	01-Dec-26	10-Dec-26	27-Dec-26	05-Jan-27	0.00	0.00	169,222.70	0%	0%	-22
MKH2-02-00	Backfilling & Compaction [Local 29]	6	14-Dec-26	20-Dec-26	09-Jan-27	14-Jan-27	0.00	0.00	56,407.59	0%	0%	-22
Local 30		175	13-Oct-26	21-Mar-27	22-Jul-26 A	29-May-27	202,809.46	878,061.80	2,090,354.00	9.7%	42.01%	-55
Road Works		175	13-Oct-26	21-Mar-27	22-Jul-26 A	29-May-27	192,464.00	169,368.32	1,212,240.70	15.88%	13.97%	-55
Eartworks & Site grading		127	13-Oct-26	19-Jan-27	22-Jul-26 A	29-Mar-27	192,464.00	169,368.32	319,760.00	60.19%	52.97%	-55
MKH2-02-00	Road backfilling [Local 30]	11	13-Oct-26	25-Oct-26	22-Jul-26 A	03-Dec-26	192,464.00	169,368.32	192,464.00	100%	88%	-34
MKH2-02-00	Aggregate base course [Local 30]	12	06-Jan-27	19-Jan-27	16-Mar-27	29-Mar-27	0.00	0.00	127,296.00	0%	0%	-55
Asphalt Works		18	20-Jan-27	09-Feb-27	30-Mar-27	19-Apr-27	0.00	0.00	480,480.00	0%	0%	-55
MKH2-02-00	Prime Coat (MC1) [Local 30]	8	20-Jan-27	28-Jan-27	30-Mar-27	07-Apr-27	0.00	0.00	48,160.00	0%	0%	-55
MKH2-02-00	Bituminous base course [Local 30]	10	30-Jan-27	09-Feb-27	08-Apr-27	19-Apr-27	0.00	0.00	432,320.00	0%	0%	-55
Finishing Works		30	10-Feb-27	21-Mar-27	20-Apr-27	29-May-27	0.00	0.00	412,000.70	0%	0%	-55
Precast Concrete Curb		6	10-Feb-27	16-Feb-27	20-Apr-27	26-Apr-27	0.00	0.00	142,240.70	0%	0%	-55
MKH2-02-0(	Installation of Precast Concrete curb	6	10-Feb-27	16-Feb-27	20-Apr-27	26-Apr-27	0.00	0.00	142,240.70	0%	0%	-55
Precast Interlocking block pavers		6	17-Feb-27	24-Feb-27	27-Apr-27	03-May-27	0.00	0.00	191,310.00	0%	0%	-55
MKH2-02-0(	Installation of Interlocking block pave	6	17-Feb-27	24-Feb-27	27-Apr-27	03-May-27	0.00	0.00	191,310.00	0%	0%	-55
Pavement Markings		12	25-Feb-27	14-Mar-27	04-May-27	22-May-27	0.00	0.00	47,850.00	0%	0%	-55
MKH2-02-0(	Pavement markings [Local 30]	6	25-Feb-27	03-Mar-27	04-May-27	10-May-27	0.00	0.00	23,850.00	0%	0%	-55
MKH2-02-0(	(Speed Hump) with retroreflective Th	6	04-Mar-27	14-Mar-27	11-May-27	22-May-27	0.00	0.00	24,000.00	0%	0%	-55
Traffic Signage		6	15-Mar-27	21-Mar-27	23-May-27	29-May-27	0.00	0.00	30,600.00	0%	0%	-55
MKH2-02-0(	Installation of Traffic Signs [Local 30]	6	15-Mar-27	21-Mar-27	23-May-27	29-May-27	0.00	0.00	30,600.00	0%	0%	-55
Storm Water Drainage		106	26-Oct-26	12-Jan-27	26-Aug-26 A	03-Mar-27	10,345.46	708,693.48	878,113.30	1.18%	80.71%	-42
Pipe Works		39	26-Oct-26	09-Dec-26	26-Aug-26 A	12-Dec-26	10,345.46	608,313.07	620,727.62	1.67%	98%	-2
MKH2-02-00	Excavation & Compaction (FDT) [Lo	6	26-Oct-26	01-Nov-26	26-Aug-26 A	05-Dec-26	10,345.46	60,831.29	62,072.74	16.67%	98%	-29
MKH2-02-00	Sand Bedding [Local 30]	6	02-Nov-26	08-Nov-26	29-Aug-26 A	06-Dec-26	0.00	60,831.29	62,072.74	0%	98%	-24
MKH2-02-00	Installation of GRP Pipe [Local 30]	10	09-Nov-26	19-Nov-26	29-Aug-26 A	08-Dec-26	0.00	304,156.56	310,363.84	0%	98%	-16
MKH2-02-00	Sand Cover & Warning Tape [Local	5	21-Nov-26	25-Nov-26	03-Sep-26 A	09-Dec-26	0.00	121,662.64	124,145.55	0%	98%	-12
MKH2-02-00	Backfilling & Compaction [Local 30]	12	26-Nov-26	09-Dec-26	03-Sep-26 A	12-Dec-26	0.00	60,831.29	62,072.74	0%	98%	-2
Concrete chambers Pipes		16	19-Dec-26	12-Jan-27	21-Oct-26 A	03-Mar-27	0.00	100,380.41	257,385.68	0%	39%	-42
MKH2-02-00	Excavation and Compaction (FDT) [	7	19-Dec-26	26-Dec-26	21-Oct-26 A	16-Feb-27	0.00	30,886.29	51,477.15	0%	60%	-45
MKH2-02-00	Installation of Pipes [Local 30]	9	27-Dec-26	05-Jan-27	24-Oct-26 A	24-Feb-27	0.00	69,494.12	154,431.38	0%	45%	-42
MKH2-02-00	Backfilling & Compaction [Local 30]	6	06-Jan-27	12-Jan-27	25-Feb-27	03-Mar-27	0.00	0.00	51,477.15	0%	0%	-42
Local 31		192	09-Nov-26	06-May-27	01-Oct-26 A	07-Jul-27	0.00	252,123.08	3,535,420.63	0%	7.13%	-49
Road Works		192	09-Nov-26	06-May-27	01-Oct-26 A	07-Jul-27	0.00	109,334.40	1,935,948.71	0%	5.65%	-49
Eartworks & Site grading		128	09-Nov-26	16-Feb-27	01-Oct-26 A	19-Apr-27	0.00	109,334.40	494,004.00	0%	22.13%	-49
MKH2-02-00	Road backfilling [Local 31]-Stage 2	12	09-Nov-26	22-Nov-26	01-Oct-26 A	17-Dec-26	0.00	109,334.40	156,192.00	0%	70%	-22
MKH2-02-00	Subgrade [Local 31]	18	06-Jan-27	26-Jan-27	23-Feb-27	18-Mar-27	0.00	0.00	131,164.00	0%	0%	-40
MKH2-02-00	Aggregate base course [Local 31]	18	27-Jan-27	16-Feb-27	30-Mar-27	19-Apr-27	0.00	0.00	206,648.00	0%	0%	-49
Asphalt Works		19	17-Feb-27	15-Mar-27	20-Apr-27	11-May-27	0.00	0.00	777,280.00	0%	0%	-49

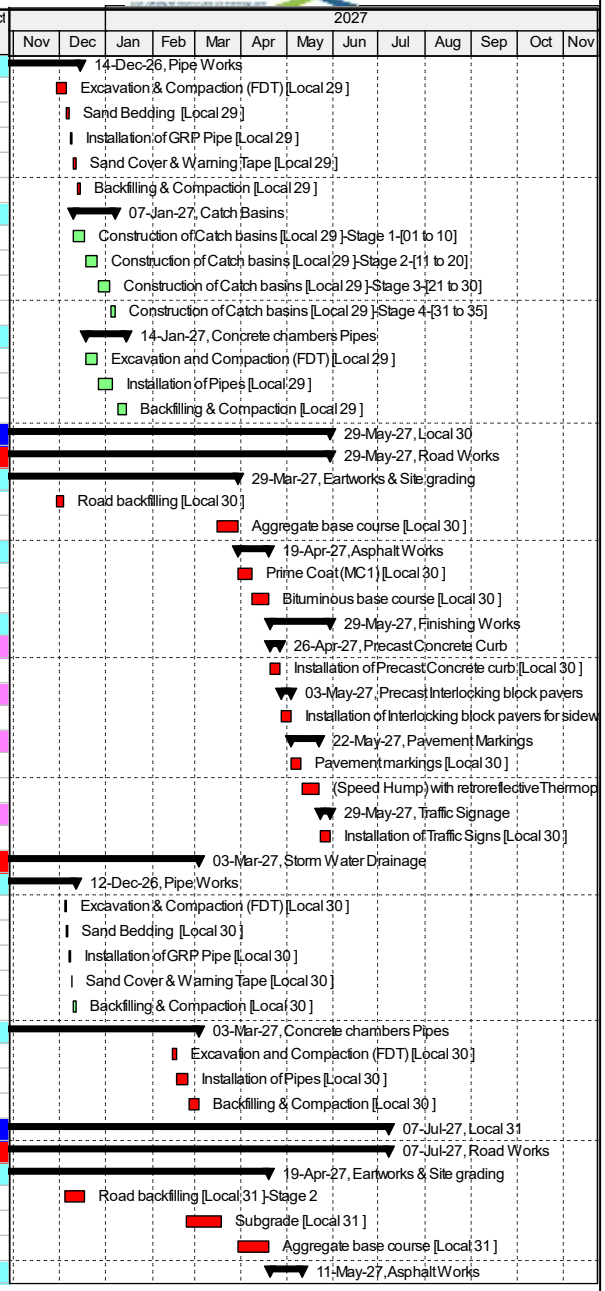

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Prime Coat (MC1) [Local 31]	9	17-Feb-27	28-Feb-27	20-Apr-27	29-Apr-27	0.00	0.00	77,280.00	0%	0%	-49
MKH2-02-00	Bituminous base course [Local 31]	10	01-Mar-27	15-Mar-27	01-May-27	11-May-27	0.00	0.00	700,000.00	0%	0%	-49
Finishing Works		45	16-Mar-27	06-May-27	12-May-27	07-Jul-27	0.00	0.00	664,664.71	0%	0%	-49
Precast Concrete Curb		10	16-Mar-27	27-Mar-27	12-May-27	27-May-27	0.00	0.00	230,894.71	0%	0%	-49
MKH2-02-0(	Installation of Precast Concrete curb	10	16-Mar-27	27-Mar-27	12-May-27	27-May-27	0.00	0.00	230,894.71	0%	0%	-49
Precast Interlocking block pavers		9	28-Mar-27	06-Apr-27	29-May-27	07-Jun-27	0.00	0.00	310,380.00	0%	0%	-49
MKH2-02-0(	Installation of Interlocking block pave	9	28-Mar-27	06-Apr-27	29-May-27	07-Jun-27	0.00	0.00	310,380.00	0%	0%	-49
Pavement Markings		18	07-Apr-27	27-Apr-27	08-Jun-27	28-Jun-27	0.00	0.00	74,790.00	0%	0%	-49
MKH2-02-0(	Pavement markings [Local 31]	9	07-Apr-27	17-Apr-27	08-Jun-27	17-Jun-27	0.00	0.00	38,790.00	0%	0%	-49
MKH2-02-0(	(Speed Hump) with retroreflective The	9	18-Apr-27	27-Apr-27	19-Jun-27	28-Jun-27	0.00	0.00	36,000.00	0%	0%	-49
Traffic Signage		8	28-Apr-27	06-May-27	29-Jun-27	07-Jul-27	0.00	0.00	48,600.00	0%	0%	-49
MKH2-02-0(	Installation of Traffic Signs [Local 31]	8	28-Apr-27	06-May-27	29-Jun-27	07-Jul-27	0.00	0.00	48,600.00	0%	0%	-49
Storm Water Drainage		99	18-Nov-26	02-Feb-27	24-Oct-26 A	03-Apr-27	0.00	142,788.68	1,599,471.91	0%	8.93%	-47
Pipe Works		29	18-Nov-26	31-Dec-26	24-Oct-26 A	16-Jan-27	0.00	142,788.68	412,111.95	0%	34.65%	-13
MKH2-02-00	Excavation & Compaction (FDT) [Lo	8	18-Nov-26	26-Nov-26	24-Oct-26 A	17-Dec-26	0.00	12,670.52	31,676.30	0%	40%	-18
MKH2-02-00	Sand Bedding [Local 31]-Stage 2	10	30-Nov-26	10-Dec-26	25-Oct-26 A	29-Dec-26	0.00	9,502.89	31,676.30	0%	30%	-16
MKH2-02-00	Installation of GRP Pipe [Local 31]-S	8	12-Dec-26	20-Dec-26	25-Oct-26 A	04-Jan-27	0.00	47,514.46	158,381.55	0%	30%	-13
MKH2-02-00	Sand Cover & Warning Tape [Local	5	09-Dec-26	14-Dec-26	25-Oct-26 A	07-Dec-26	0.00	50,852.75	63,565.93	0%	80%	6
MKH2-02-00	Sand Cover & Warning Tape [Local	5	21-Dec-26	26-Dec-26	05-Jan-27	10-Jan-27	0.00	0.00	63,352.62	0%	0%	-13
MKH2-02-00	Backfilling & Compaction [Local 31]-	5	15-Dec-26	20-Dec-26	26-Oct-26 A	10-Dec-26	0.00	22,248.07	31,782.95	0%	70%	8
MKH2-02-00	Backfilling & Compaction [Local 31]-	5	27-Dec-26	31-Dec-26	11-Jan-27	16-Jan-27	0.00	0.00	31,676.30	0%	0%	-13
Manholes		40	09-Dec-26	24-Jan-27	05-Dec-26	19-Jan-27	0.00	0.00	471,527.78	0%	0%	4
MKH2-02-00	Installation of Manholes [Local 31]-S	14	09-Dec-26	24-Dec-26	05-Dec-26	20-Dec-26	0.00	0.00	165,034.72	0%	0%	4
MKH2-02-00	Installation of Manholes [Local 31]-S	14	26-Dec-26	10-Jan-27	21-Dec-26	05-Jan-27	0.00	0.00	165,034.72	0%	0%	4
MKH2-02-00	Installation of Manholes [Local 31]-S	12	11-Jan-27	24-Jan-27	06-Jan-27	19-Jan-27	0.00	0.00	141,458.33	0%	0%	4
Catch Basins		77	26-Dec-26	23-Jan-27	21-Dec-26	24-Mar-27	0.00	0.00	360,673.37	0%	0%	-48
MKH2-02-00	Construction of Catch basins [Local 3	5	26-Dec-26	30-Dec-26	21-Dec-26	26-Dec-26	0.00	0.00	73,606.81	0%	0%	4
MKH2-02-00	Construction of Catch basins [Local 3	5	31-Dec-26	05-Jan-27	03-Jan-27	07-Jan-27	0.00	0.00	73,606.81	0%	0%	-2
MKH2-02-00	Construction of Catch basins [Local 3	5	06-Jan-27	11-Jan-27	04-Mar-27	09-Mar-27	0.00	0.00	73,606.81	0%	0%	-48
MKH2-02-00	Construction of Catch basins [Local 3	5	12-Jan-27	17-Jan-27	14-Mar-27	18-Mar-27	0.00	0.00	73,606.81	0%	0%	-48
MKH2-02-00	Construction of Catch basins [Local 3	5	18-Jan-27	23-Jan-27	20-Mar-27	24-Mar-27	0.00	0.00	66,246.13	0%	0%	-48
Concrete chambers Pipes		80	31-Dec-26	02-Feb-27	27-Dec-26	03-Apr-27	0.00	0.00	355,158.82	0%	0%	-47
MKH2-02-00	Excavation and Compaction (FDT) [I	9	31-Dec-26	10-Jan-27	27-Dec-26	05-Jan-27	0.00	0.00	71,031.78	0%	0%	4
MKH2-02-00	Installation of Pipes [Local 31]	12	11-Jan-27	24-Jan-27	06-Jan-27	19-Jan-27	0.00	0.00	213,095.26	0%	0%	4
MKH2-02-00	Backfilling & Compaction [Local 31]	8	25-Jan-27	02-Feb-27	25-Mar-27	03-Apr-27	0.00	0.00	71,031.78	0%	0%	-47
Local 28		202	23-Nov-26	03-Jun-27	22-Aug-26 A	31-Jul-27	0.00	584,254.27	3,111,205.56	0%	18.78%	-49
Road Works		202	23-Nov-26	03-Jun-27	22-Aug-26 A	31-Jul-27	0.00	200,683.00	1,933,641.79	0%	10.38%	-49
Eartworks & Site grading		132	23-Nov-26	08-Mar-27	22-Aug-26 A	05-May-27	0.00	200,683.00	492,870.00	0%	40.72%	-47
MKH2-02-00	Road backfilling [Local 28]-Stage 2	12	23-Nov-26	06-Dec-26	22-Aug-26 A	13-Dec-26	0.00	109,099.20	155,856.00	0%	70%	-6
MKH2-02-00	Subgrade [Local 28]	16	01-Feb-27	18-Feb-27	17-Oct-26 A	06-Apr-27	0.00	91,583.80	130,834.00	0%	70%	-36
MKH2-02-00	Aggregate base course [Local 28]	14	20-Feb-27	08-Mar-27	20-Apr-27	05-May-27	0.00	0.00	206,180.00	0%	0%	-47
Asphalt Works		18	09-Mar-27	01-Apr-27	06-May-27	31-May-27	0.00	0.00	777,280.00	0%	0%	-47
MKH2-02-00	Prime Coat (MC1) [Local 28]	8	09-Mar-27	21-Mar-27	06-May-27	19-May-27	0.00	0.00	77,840.00	0%	0%	-47
MKH2-02-00	Bituminous base course [Local 28]	10	22-Mar-27	01-Apr-27	20-May-27	31-May-27	0.00	0.00	699,440.00	0%	0%	-47
Finishing Works		52	03-Apr-27	03-Jun-27	01-Jun-27	31-Jul-27	0.00	0.00	663,491.79	0%	0%	-49
Precast Concrete Curb		10	03-Apr-27	13-Apr-27	01-Jun-27	12-Jun-27	0.00	0.00	230,416.79	0%	0%	-47
MKH2-02-0(	Installation of Precast Concrete curb	10	03-Apr-27	13-Apr-27	01-Jun-27	12-Jun-27	0.00	0.00	230,416.79	0%	0%	-47
Precast Interlocking block pavers		9	14-Apr-27	24-Apr-27	13-Jun-27	22-Jun-27	0.00	0.00	309,820.00	0%	0%	-47
MKH2-02-0(	Installation of Interlocking block pave	9	14-Apr-27	24-Apr-27	13-Jun-27	22-Jun-27	0.00	0.00	309,820.00	0%	0%	-47
Pavement Markings		19	28-Apr-27	24-May-27	29-Jun-27	20-Jul-27	0.00	0.00	74,655.00	0%	0%	-49
MKH2-02-0(	Pavement markings [Local 28]	10	28-Apr-27	09-May-27	29-Jun-27	10-Jul-27	0.00	0.00	38,655.00	0%	0%	-49

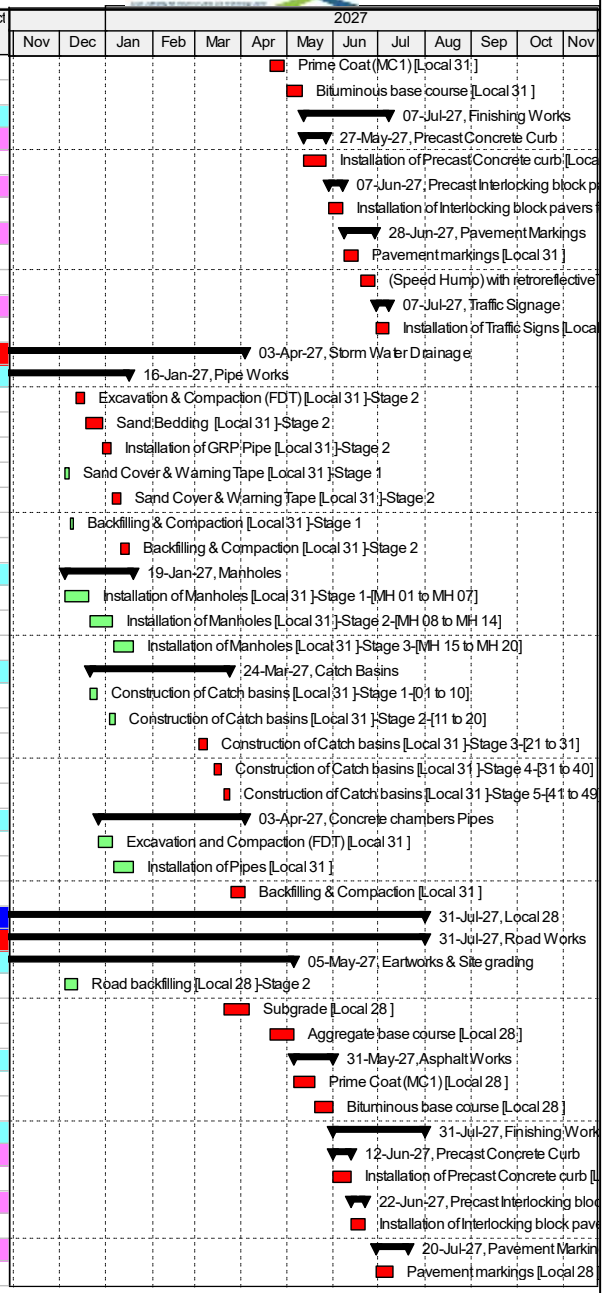

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-0(	(Speed Hump) with retroreflective The	9	10-May-27	24-May-27	11-Jul-27	20-Jul-27	0.00	0.00	36,000.00	0%	0%	-49
Traffic Signage		9	25-May-27	03-Jun-27	21-Jul-27	31-Jul-27	0.00	0.00	48,600.00	0%	0%	-49
MKH2-02-0(	Installation of Traffic Signs [Local 28]	9	25-May-27	03-Jun-27	21-Jul-27	31-Jul-27	0.00	0.00	48,600.00	0%	0%	-49
Storm Water Drainage		107	19-Dec-26	24-Feb-27	23-Sep-26 A	17-Apr-27	0.00	383,571.27	1,177,563.77	0%	32.57%	-41
Pipe Works		28	19-Dec-26	31-Jan-27	23-Sep-26 A	02-Jan-27	0.00	383,571.27	394,620.65	0%	97.2%	25
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	10	19-Dec-26	29-Dec-26	23-Sep-26 A	14-Dec-26	0.00	35,515.85	39,462.05	0%	90%	14
MKH2-02-00(	Sand Bedding [Local 28]-Stage 2	8	30-Dec-26	07-Jan-27	26-Sep-26 A	19-Dec-26	0.00	38,672.81	39,462.05	0%	98%	17
MKH2-02-00(	Installation of GRP Pipe [Local 28]-S	10	09-Jan-27	19-Jan-27	27-Sep-26 A	26-Dec-26	0.00	193,364.14	197,310.34	0%	98%	21
MKH2-02-00(	Sand Cover & Warning Tape [Local	5	20-Jan-27	25-Jan-27	30-Sep-26 A	29-Dec-26	0.00	77,345.66	78,924.15	0%	98%	23
MKH2-02-00(	Backfilling & Compaction [Local 28]-	5	26-Jan-27	31-Jan-27	03-Oct-26 A	02-Jan-27	0.00	38,672.81	39,462.05	0%	98%	25
Catch Basins		25	20-Jan-27	17-Feb-27	27-Dec-26	24-Jan-27	0.00	0.00	368,034.06	0%	0%	21
MKH2-02-00(	Construction of Catch basins [Local 2	5	20-Jan-27	25-Jan-27	27-Dec-26	31-Dec-26	0.00	0.00	73,606.81	0%	0%	21
MKH2-02-00(	Construction of Catch basins [Local 2	5	26-Jan-27	31-Jan-27	02-Jan-27	06-Jan-27	0.00	0.00	73,606.81	0%	0%	21
MKH2-02-00(	Construction of Catch basins [Local 2	5	01-Feb-27	06-Feb-27	07-Jan-27	12-Jan-27	0.00	0.00	73,606.81	0%	0%	21
MKH2-02-00(	Construction of Catch basins [Local 2	5	07-Feb-27	11-Feb-27	13-Jan-27	18-Jan-27	0.00	0.00	73,606.81	0%	0%	21
MKH2-02-00(	Construction of Catch basins [Local 2	5	13-Feb-27	17-Feb-27	19-Jan-27	24-Jan-27	0.00	0.00	73,606.81	0%	0%	21
Concrete chambers Pipes		25	26-Jan-27	24-Feb-27	20-Mar-27	17-Apr-27	0.00	0.00	414,909.06	0%	0%	-41
MKH2-02-00(	Excavation and Compaction (FDT) [I	8	26-Jan-27	03-Feb-27	20-Mar-27	28-Mar-27	0.00	0.00	82,981.83	0%	0%	-41
MKH2-02-00(	Installation of Pipes [Local 28]	10	04-Feb-27	15-Feb-27	29-Mar-27	08-Apr-27	0.00	0.00	248,945.40	0%	0%	-41
MKH2-02-00(	Backfilling & Compaction [Local 28]	7	16-Feb-27	24-Feb-27	10-Apr-27	17-Apr-27	0.00	0.00	82,981.83	0%	0%	-41
Local 10		171	07-Dec-26	08-May-27	07-Jul-26 A	06-Jul-27	0.00	354,695.61	1,363,235.86	0%	26.02%	-47
Road Works		159	07-Dec-26	08-May-27	07-Jul-26 A	06-Jul-27	0.00	332,458.20	809,336.29	0%	41.08%	-47
Eartworks & Site grading		123	07-Dec-26	27-Mar-27	07-Jul-26 A	25-May-27	0.00	332,458.20	412,312.00	0%	80.63%	-47
MKH2-02-00(	Road excavation [Local 10]	6	07-Dec-26	13-Dec-26	07-Jul-26 A	16-Dec-26	0.00	222,334.20	234,036.00	0%	95%	-3
MKH2-02-00(	Road backfilling [Local 10]	6	07-Dec-26	13-Dec-26	15-Jul-26 A	16-Dec-26	0.00	81,365.60	85,648.00	0%	95%	-3
MKH2-02-00(	Subgrade [Local 10]	7	09-Mar-27	20-Mar-27	22-May-27 A	13-May-27	0.00	28,758.40	35,948.00	0%	80%	-47
MKH2-02-00(	Aggregate base course [Local 10]	6	21-Mar-27	27-Mar-27	19-May-27	25-May-27	0.00	0.00	56,680.00	0%	0%	-47
Asphalt Works		8	28-Mar-27	05-Apr-27	26-May-27	03-Jun-27	0.00	0.00	213,360.00	0%	0%	-47
MKH2-02-00(	Prime Coat (MC1) [Local 10]	4	28-Mar-27	31-Mar-27	26-May-27	30-May-27	0.00	0.00	21,280.00	0%	0%	-47
MKH2-02-00(	Bituminous base course [Local 10]	4	01-Apr-27	05-Apr-27	31-May-27	03-Jun-27	0.00	0.00	192,080.00	0%	0%	-47
Finishing Works		21	14-Apr-27	08-May-27	13-Jun-27	06-Jul-27	0.00	0.00	183,664.29	0%	0%	-47
Precast Concrete Curb		6	14-Apr-27	20-Apr-27	13-Jun-27	19-Jun-27	0.00	0.00	63,324.29	0%	0%	-47
MKH2-02-0(	Installation of Precast Concrete curb	6	14-Apr-27	20-Apr-27	13-Jun-27	19-Jun-27	0.00	0.00	63,324.29	0%	0%	-47
Precast Interlocking block pavers		5	21-Apr-27	26-Apr-27	20-Jun-27	24-Jun-27	0.00	0.00	85,120.00	0%	0%	-47
MKH2-02-0(	Installation of Interlocking block pave	5	21-Apr-27	26-Apr-27	20-Jun-27	24-Jun-27	0.00	0.00	85,120.00	0%	0%	-47
Pavement Markings		7	27-Apr-27	04-May-27	26-Jun-27	03-Jul-27	0.00	0.00	22,620.00	0%	0%	-47
MKH2-02-0(	Pavement markings [Local 10]	4	27-Apr-27	01-May-27	26-Jun-27	29-Jun-27	0.00	0.00	10,620.00	0%	0%	-47
MKH2-02-0(	(Speed Hump) with retroreflective The	3	02-May-27	04-May-27	30-Jun-27	03-Jul-27	0.00	0.00	12,000.00	0%	0%	-47
Traffic Signage		3	05-May-27	08-May-27	04-Jul-27	06-Jul-27	0.00	0.00	12,600.00	0%	0%	-47
MKH2-02-0(	Installation of Traffic Signs [Local 10]	3	05-May-27	08-May-27	04-Jul-27	06-Jul-27	0.00	0.00	12,600.00	0%	0%	-47
Storm Water Drainage		37	14-Dec-26	18-Jan-27	10-Sep-26 A	21-Jan-27	0.00	22,237.41	553,899.57	0%	4.01%	-3
Pipe Works		23	14-Dec-26	02-Jan-27	10-Sep-26 A	05-Jan-27	0.00	22,237.41	148,249.38	0%	15%	-3
MKH2-02-00(	Excavation & Compaction (FDT) [Lo	4	14-Dec-26	17-Dec-26	10-Sep-26 A	21-Dec-26	0.00	4,447.48	14,824.93	0%	30%	-3
MKH2-02-00(	Sand Bedding [Local 10]	3	19-Dec-26	21-Dec-26	12-Sep-26 A	24-Dec-26	0.00	2,964.99	14,824.93	0%	20%	-3
MKH2-02-00(	Installation of GRP Pipe [Local 10]	5	22-Dec-26	27-Dec-26	12-Sep-26 A	30-Dec-26	0.00	14,824.94	74,124.70	0%	20%	-3
MKH2-02-00(	Sand Cover & Warning Tape [Local	2	28-Dec-26	29-Dec-26	31-Dec-26	02-Jan-27	0.00	0.00	29,649.88	0%	0%	-3
MKH2-02-00(	Backfilling & Compaction [Local 10]	3	30-Dec-26	02-Jan-27	03-Jan-27	05-Jan-27	0.00	0.00	14,824.93	0%	0%	-3
Manholes		10	28-Dec-26	07-Jan-27	31-Dec-26	11-Jan-27	0.00	0.00	259,340.28	0%	0%	-3
MKH2-02-00(	Installation of Manholes [Local 10]-S	5	28-Dec-26	02-Jan-27	31-Dec-26	05-Jan-27	0.00	0.00	165,034.72	0%	0%	-3
MKH2-02-00(	Installation of Manholes [Local 10]-S	5	03-Jan-27	07-Jan-27	06-Jan-27	11-Jan-27	0.00	0.00	94,305.56	0%	0%	-3
Catch Basins		4	03-Jan-27	06-Jan-27	06-Jan-27	10-Jan-27	0.00	0.00	73,606.81	0%	0%	-3

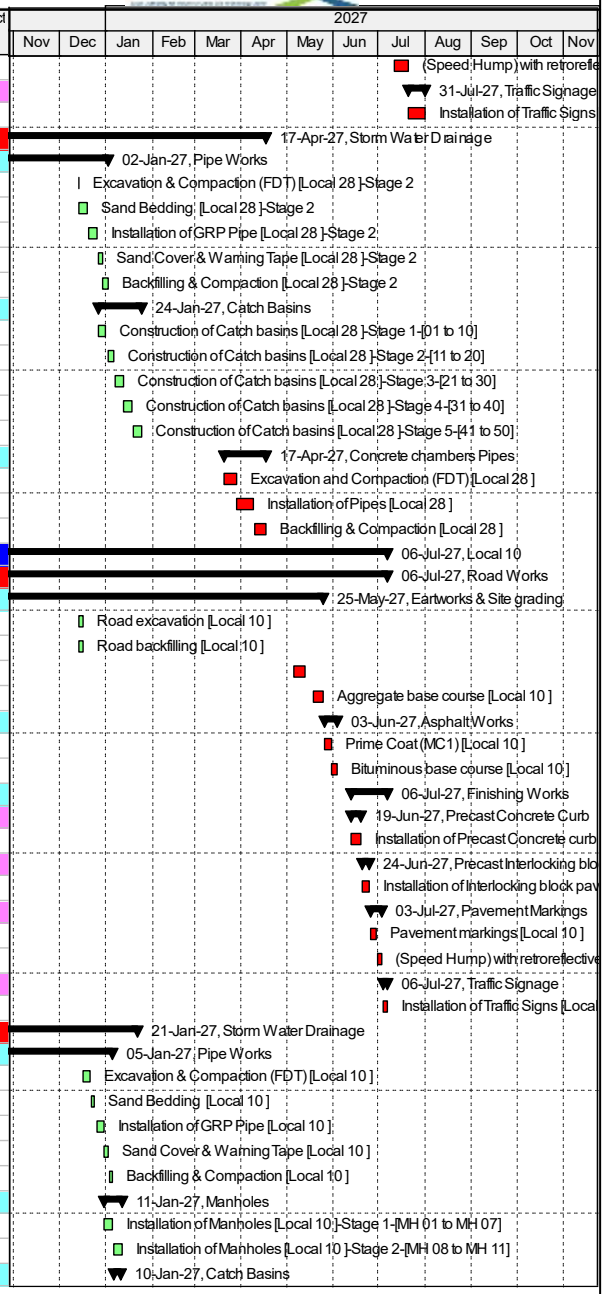

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-00	Construction of Catch basins [Local 1	4	03-Jan-27	06-Jan-27	06-Jan-27	10-Jan-27	0.00	0.00	73,606.81	0%	0%	-3
Concrete chambers Pipes		10	07-Jan-27	18-Jan-27	11-Jan-27	21-Jan-27	0.00	0.00	72,703.10	0%	0%	-3
MKH2-02-00	Excavation and Compaction (FDT) [L	3	07-Jan-27	10-Jan-27	11-Jan-27	13-Jan-27	0.00	0.00	14,540.62	0%	0%	-3
MKH2-02-00	Installation of Pipes [Local 10]	4	11-Jan-27	14-Jan-27	14-Jan-27	18-Jan-27	0.00	0.00	43,621.85	0%	0%	-3
MKH2-02-00	Backfilling & Compaction [Local 10]	3	16-Jan-27	18-Jan-27	19-Jan-27	21-Jan-27	0.00	0.00	14,540.62	0%	0%	-3
Collector 02		166	14-Dec-26	12-May-27	21-Jul-26 A	11-Jul-27	0.00	192,043.30	1,019,971.28	0%	18.83%	-47
Road Works		159	14-Dec-26	12-May-27	21-Jul-26 A	11-Jul-27	0.00	192,043.30	472,918.82	0%	40.61%	-47
Eartworks & Site grading		131	14-Dec-26	10-Apr-27	21-Jul-26 A	08-Jun-27	0.00	192,043.30	238,138.00	0%	80.64%	-47
MKH2-02-00	Road excavation [Collector 02]	6	14-Dec-26	20-Dec-26	21-Jul-26 A	20-Dec-26	0.00	128,430.50	135,190.00	0%	95%	0
MKH2-02-00	Road backfilling [Collector 02]	6	14-Dec-26	20-Dec-26	22-Jul-26 A	20-Dec-26	0.00	46,998.40	49,472.00	0%	95%	0
MKH2-02-00	Subgrade [Collector 02]	6	28-Mar-27	03-Apr-27	22-Oct-26 A	01-Jun-27	0.00	16,614.40	20,768.00	0%	80%	-47
MKH2-02-00	Aggregate base course [Collector 02	6	04-Apr-27	10-Apr-27	02-Jun-27	08-Jun-27	0.00	0.00	32,708.00	0%	0%	-47
Asphalt Works		12	11-Apr-27	24-Apr-27	09-Jun-27	22-Jun-27	0.00	0.00	123,760.00	0%	0%	-47
MKH2-02-00	Prime Coat (MC1) [Collector 02]	6	11-Apr-27	17-Apr-27	09-Jun-27	15-Jun-27	0.00	0.00	12,320.00	0%	0%	-47
MKH2-02-00	Bituminous base course [Collector 0	6	18-Apr-27	24-Apr-27	16-Jun-27	22-Jun-27	0.00	0.00	111,440.00	0%	0%	-47
Finishing Works		16	25-Apr-27	12-May-27	23-Jun-27	11-Jul-27	0.00	0.00	111,020.82	0%	0%	-47
Precast Concrete Curb		4	25-Apr-27	28-Apr-27	23-Jun-27	27-Jun-27	0.00	0.00	36,560.82	0%	0%	-47
MKH2-02-0(	Installation of Precast Concrete curb	4	25-Apr-27	28-Apr-27	23-Jun-27	27-Jun-27	0.00	0.00	36,560.82	0%	0%	-47
Precast Interlocking block pavers		3	29-Apr-27	02-May-27	28-Jun-27	30-Jun-27	0.00	0.00	49,140.00	0%	0%	-47
MKH2-02-0(	Installation of Interlocking block pave	3	29-Apr-27	02-May-27	28-Jun-27	30-Jun-27	0.00	0.00	49,140.00	0%	0%	-47
Pavement Markings		6	03-May-27	09-May-27	01-Jul-27	07-Jul-27	0.00	0.00	18,120.00	0%	0%	-47
MKH2-02-0(	Pavement markings [Collector 02]	3	03-May-27	05-May-27	01-Jul-27	04-Jul-27	0.00	0.00	6,120.00	0%	0%	-47
MKH2-02-0(	(Speed Hump) with retroreflective The	3	06-May-27	09-May-27	05-Jul-27	07-Jul-27	0.00	0.00	12,000.00	0%	0%	-47
Traffic Signage		3	10-May-27	12-May-27	08-Jul-27	11-Jul-27	0.00	0.00	7,200.00	0%	0%	-47
MKH2-02-0(	Installation of Traffic Signs [Collector (	3	10-May-27	12-May-27	08-Jul-27	11-Jul-27	0.00	0.00	7,200.00	0%	0%	-47
Storm Water Drainage		72	21-Dec-26	21-Jan-27	21-Dec-26	18-Mar-27	0.00	0.00	547,052.46	0%	0%	-44
Pipe Works		21	21-Dec-26	13-Jan-27	21-Dec-26	13-Jan-27	0.00	0.00	270,901.74	0%	0%	0
MKH2-02-00	Excavation & Compaction (FDT) [Co	4	21-Dec-26	24-Dec-26	21-Dec-26	24-Dec-26	0.00	0.00	27,090.17	0%	0%	0
MKH2-02-00	Sand Bedding [Collector 02]	3	26-Dec-26	28-Dec-26	26-Dec-26	28-Dec-26	0.00	0.00	27,090.17	0%	0%	0
MKH2-02-00	Installation of GRP Pipe [Collector 02	5	29-Dec-26	03-Jan-27	29-Dec-26	03-Jan-27	0.00	0.00	135,450.88	0%	0%	0
MKH2-02-00	Sand Cover & Warning Tape [Collec	3	04-Jan-27	06-Jan-27	04-Jan-27	06-Jan-27	0.00	0.00	54,180.36	0%	0%	0
MKH2-02-00	Backfilling & Compaction [Collector (	6	07-Jan-27	13-Jan-27	07-Jan-27	13-Jan-27	0.00	0.00	27,090.17	0%	0%	0
Manholes		12	04-Jan-27	17-Jan-27	04-Jan-27	17-Jan-27	0.00	0.00	259,340.28	0%	0%	0
MKH2-02-00	Installation of Manholes [Collector 02	6	04-Jan-27	10-Jan-27	04-Jan-27	10-Jan-27	0.00	0.00	165,034.72	0%	0%	0
MKH2-02-00	Installation of Manholes [Collector 02	6	11-Jan-27	17-Jan-27	11-Jan-27	17-Jan-27	0.00	0.00	94,305.56	0%	0%	0
Catch Basins		3	11-Jan-27	13-Jan-27	04-Mar-27	07-Mar-27	0.00	0.00	14,721.36	0%	0%	-44
MKH2-02-00	Construction of Catch basins [Collec	3	11-Jan-27	13-Jan-27	04-Mar-27	07-Mar-27	0.00	0.00	14,721.36	0%	0%	-44
Concrete chambers Pipes		7	14-Jan-27	21-Jan-27	08-Mar-27	18-Mar-27	0.00	0.00	2,089.08	0%	0%	-44
MKH2-02-00	Excavation and Compaction (FDT) [L	2	14-Jan-27	16-Jan-27	08-Mar-27	09-Mar-27	0.00	0.00	417.83	0%	0%	-44
MKH2-02-00	Installation of Pipes [Collector 02]	3	17-Jan-27	19-Jan-27	14-Mar-27	16-Mar-27	0.00	0.00	1,253.50	0%	0%	-44
MKH2-02-00	Backfilling & Compaction [Collector (	2	20-Jan-27	21-Jan-27	17-Mar-27	18-Mar-27	0.00	0.00	417.74	0%	0%	-44
Testing and Commissioning		106	25-Feb-27	27-Jun-27	18-Apr-27	23-Aug-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-T&	Test for Stormwater Utilities	20	25-Feb-27	23-Mar-27	18-Apr-27	10-May-27	0.00	0.00	0.00	0%	0%	-41
MKH2-02-004-T&	Test for Road Works	20	05-Jun-27	27-Jun-27	01-Aug-27	23-Aug-27	0.00	0.00	0.00	0%	0%	-49
Project Hand Over & Close-out		136	24-Mar-27	24-Aug-27	11-May-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49
As-Built DWGs		116	24-Mar-27	01-Aug-27	11-May-27	28-Sep-27	0.00	0.00	0.00	0%	0%	-49
As-Built DWGs Submittal		101	24-Mar-27	14-Jul-27	11-May-27	09-Sep-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-A	As-Built DWGs Submittal for Stormw	15	24-Mar-27	10-Apr-27	11-May-27	01-Jun-27	0.00	0.00	0.00	0%	0%	-41
MKH2-02-004-A	As-Built DWGs Submittal for Road W	15	28-Jun-27	14-Jul-27	24-Aug-27	09-Sep-27	0.00	0.00	0.00	0%	0%	-49
As-Built DWGs Approval		101	11-Apr-27	01-Aug-27	02-Jun-27	28-Sep-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-A	As- Built DWGs Approval for Stormw	10	11-Apr-27	21-Apr-27	02-Jun-27	13-Jun-27	0.00	0.00	0.00	0%	0%	-41

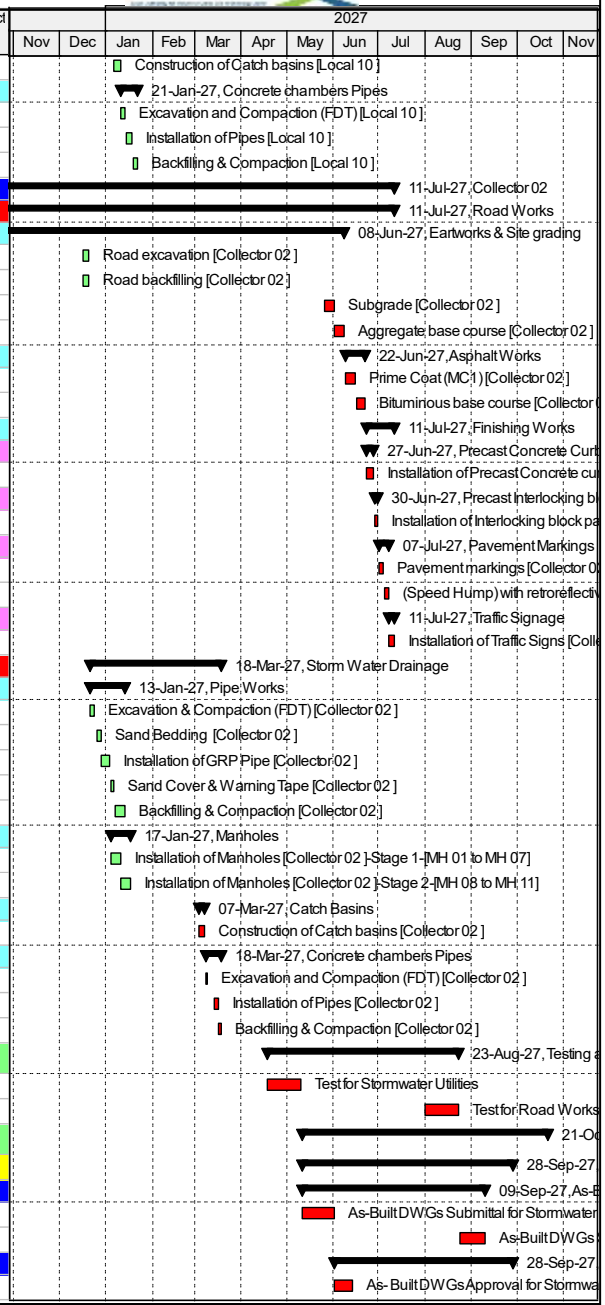

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-004-Road Development for the Support Services Area at the Second Indust City in Makkah UP 15
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-004-A	As-Built DWGs Approval for Road W	15	15-Jul-27	01-Aug-27	11-Sep-27	28-Sep-27	0.00	0.00	0.00	0%	0%	-49
Demobilization		20	02-Aug-27	24-Aug-27	29-Sep-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-D	Demobilization of Manpower	10	02-Aug-27	12-Aug-27	29-Sep-27	10-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-D	Removal of Equipment from Site	10	02-Aug-27	12-Aug-27	29-Sep-27	10-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-D	Site Clean Up	10	02-Aug-27	12-Aug-27	29-Sep-27	10-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-D	Removal of Site Offices and Structure	10	02-Aug-27	12-Aug-27	29-Sep-27	10-Oct-27	0.00	0.00	0.00	0%	0%	-49
MKH2-02-004-D	Restoration of Ground Surfaces	10	14-Aug-27	24-Aug-27	11-Oct-27	21-Oct-27	0.00	0.00	0.00	0%	0%	-49



Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
