Road Development for the Support Services Area, Second Industrial City in Makkah (Al-Akayshiyah)

تطوير الطرق لمنطقة الخدمات المساندة بالمدينة الصناعية الثانية بمكة المكرمة (العكيشية)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Trading & Contracting Co.	EGIS	Abdallah Aljulaifi	25-Jun-2026	24-Aug-2027

Scope: road works and the storm water drainage network for the support services area of the Second Industrial City in Makkah, Al-Akayshiyah. Contract value 33.04M SAR excluding VAT, 14 months from site handover.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 27-Oct-2026 the project is 48.3% complete against 35.7% planned, 12.6% ahead of plan. This week it gained 3.0%, in line with the 3.0% planned for the week.

PHYSICAL % COMPLETE
48.3% / 35.7% plan
▲ SPI 1.35 +12.6%

PROGRESS THIS WEEK
+3.0% / +3.0% plan
● In line with the weekly plan

CONTRACT TIME ELAPSED
29.2% · day 124 of 425
▼ P6 finish 21-Oct-2027

INVOICED TO DATE (GROSS)
20.4% · 6.75M SAR
3 invoices, all paid; last period ends 27-Sep-2026

Progress is ahead of plan, but the forecast finish slipped another week: now 58 days late.

The P6 update (UP 15, data date 27-Oct-2026) schedules project completion on 21-Oct-2027, 58 days after the contract completion date of 24-Aug-2027, with −49 days of total float (−43 last week). The weekly report gives the same forecast. Pavement materials still have no purchase orders, and 35 activities have failed to start on time, up from 29.

Site photos this week

Four photos from the Weekly Photos sheet of the 27-Oct-2026 weekly report, each stamped 26-Oct-2026 with time and altitude (no GPS coordinates are shown). Select a photo to view it larger, then use the arrows to move between photos.



Cutting works, Local Road 17

Stamped 26-Oct-2026, 09:56, altitude 185.0 m.




Subgrade works, Local Road 11

Stamped 26-Oct-2026, 10:51, altitude 173.3 m.



Storm drainage excavation, Local Road 17

Stamped 26-Oct-2026, 11:17, altitude 183.1 m.

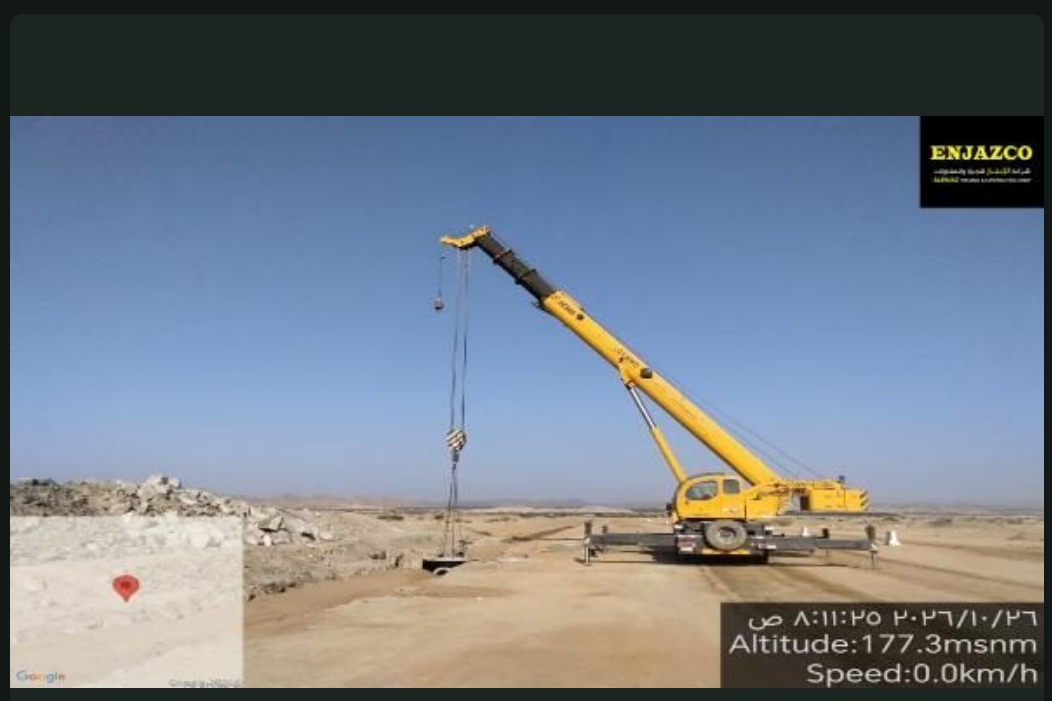

Manhole installation, Local Road 31

Stamped 26-Oct-2026, 08:11, altitude 177.3 m.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values. Source: Physical-Chart Data sheet.



WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	28.5	41.0	+12.4%	–	1.44
20-Oct-2026	32.6	45.2	+12.6%	+4.3	1.39
27-Oct-2026	**35.7**	**48.3**	**+12.6%**	**+3.0**	**1.35**

Rows from weekly reports No. 17 and No. 18. The 13-Oct-2026 row is the "CM Last Week" figure stated in report No. 17; earlier weeks were not uploaded.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (218,590 in total). Source: Weekly Progress Report sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.6%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	2.7%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	2.2%	84.2%	59.8%	−24.3%	0.71	▼ Behind
Road works	54.3%	34.9%	51.7%	+16.8%	1.48	▲ Ahead
Storm water drainage	35.6%	23.9%	35.2%	+11.3%	1.47	▲ Ahead
Testing & commissioning	1.1%	0.0%	0.0%	0.0%	–	Not due yet
Handover & close-out	0.4%	0.0%	0.0%	0.0%	–	Not due yet
Total	100%	**35.7%**	**48.3%**	**+12.6%**	**1.35**	▲ Ahead

The schedule (P6 UP 15, data date 27-Oct-2026) has 381 activities: 150 completed, 46 in progress and 185 not started. Its scheduled finish is 21-Oct-2027 with −49 days of total float. Critical-path activities went from 168 to 166 this week; failed starts rose from 29 to 35.

Scope of work: quantities

Total scope and quantity finished for the items under way, from the Major Quantities sheet of the 27-Oct-2026 weekly report. "This week" is this week's cumulative quantity minus the 20-Oct-2026 report's.

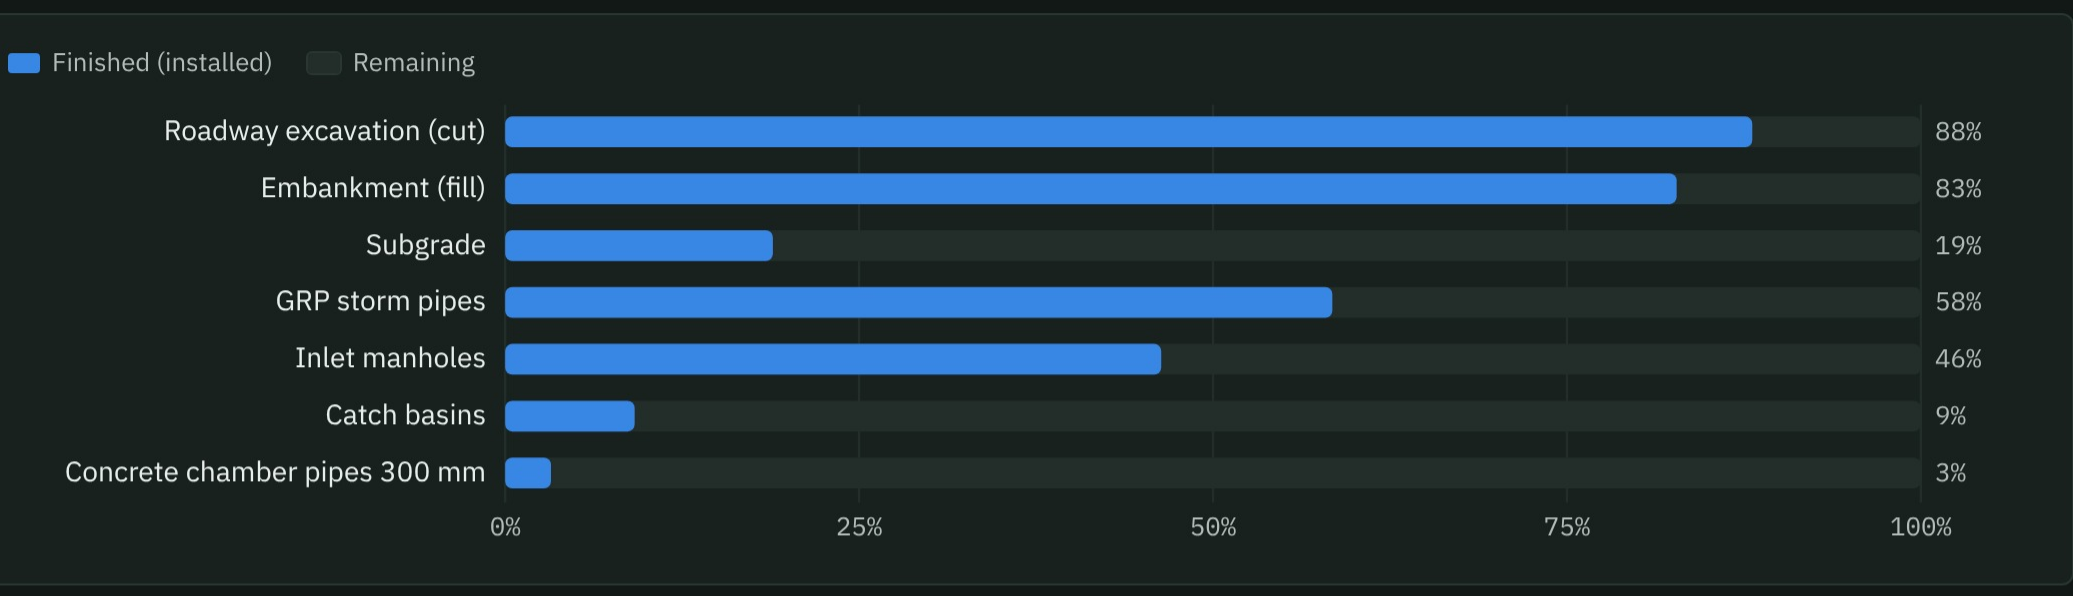

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Roadway excavation (cut)	All roads	m³	252,115	222,090	0	30,025	88.1%	–
Embankment (fill)	All roads	m³	221,841	183,569	0	38,272	82.7%	–
Subgrade	All roads	m³	39,250	7,422	+872	31,828	18.9%	–
GRP storm pipes	All roads	LM	5,855	3,421	+293.7	2,434	58.4%	–
Inlet manholes	All roads	EA	82	38	+1	44	46.3%	–
Catch basins	All roads	EA	164	15	+8	149	9.1%	–
Concrete chamber pipes 300 mm	All roads	LM	5,410	175	+175	5,235	3.2%	–

Earthworks well ahead of plan

Cut is 222,090 m³ against 160,673 m³ planned to date, and fill is 183,569 m³ against 141,379 m³ planned. The cut and fill totals did not change this week, although the list of works executed reports 6,510 m³ of cut on Local Roads 17 and 31.

Not yet started

Aggregate base course, bituminous base and wearing courses, precast kerbs, interlock paving, pavement markings and traffic signs are all at 0%. Catch basins reached 15 of 164 (8 this week), and 175 m of 300 mm concrete chamber pipes appear for the first time.

Milestones

The weekly report and the P6 update give the same forecast dates. The weekly report shows the slip in calendar days. No P6 XER file was uploaded this week, so float is available only for the whole project.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	25-Jun-2026	25-Jun-2026	25-Jun-2026 (actual)	–	✓ Done
Baseline programme submission	12-Jul-2026	12-Jul-2026	12-Jul-2026 (actual)	–	✓ Done
Completion of mobilisation	23-Jul-2026	15-Aug-2026 (+23 d)	15-Aug-2026 (actual)	–	✓ Done late
Approval of drawings and materials	23-Aug-2026	19-Sep-2026 (+27 d)	19-Sep-2026 (actual)	–	✓ Done late
Storm water drainage complete	24-Feb-2027	17-Apr-2027 (+52 d)	17-Apr-2027	–	▼ Late
Road works complete	24-Apr-2027	22-Jun-2027 (+59 d)	22-Jun-2027	–	▼ Late
Project completion	24-Aug-2027	21-Oct-2027 (+58 d)	21-Oct-2027	−49	▼ Late

All three construction milestones slipped 7 days this week.

Storm drainage moved from 10-Apr to 17-Apr-2027, road works from 15-Jun to 22-Jun-2027 and project completion from 14-Oct to 21-Oct-2027. Negative float now covers every road: Local Road 28 at −49 days, Local Road 30 at −41, Local Road 17 at −40, Local Road 11 at −38 and Local Road 29 at −35; procurement is at −16 days.

Procurement of key materials

Procurement completion rate per material. Source: Procurement Log, weekly report 27-Oct-2026.



Pavement materials: still no purchase orders


Aggregate base course, bituminous base, precast kerbs, interlock pavers and pavement markings have no purchase order, although the required order dates (29-Aug to 17-Sep-2026) have passed. The failed-start list now plans the aggregate base order for 27-Oct-2026 and the bituminous base order for 02-Nov-2026. Aggregate base is needed on site by 15-Nov-2026.

Storm drainage materials

GRP pipes (5,855 m), inlet manholes (82) and traffic signs (171) are fully procured. Catch basins are still at 110 of 164 (67%); the third delivery is planned for 05-Nov-2026.

Manpower

Monthly average head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

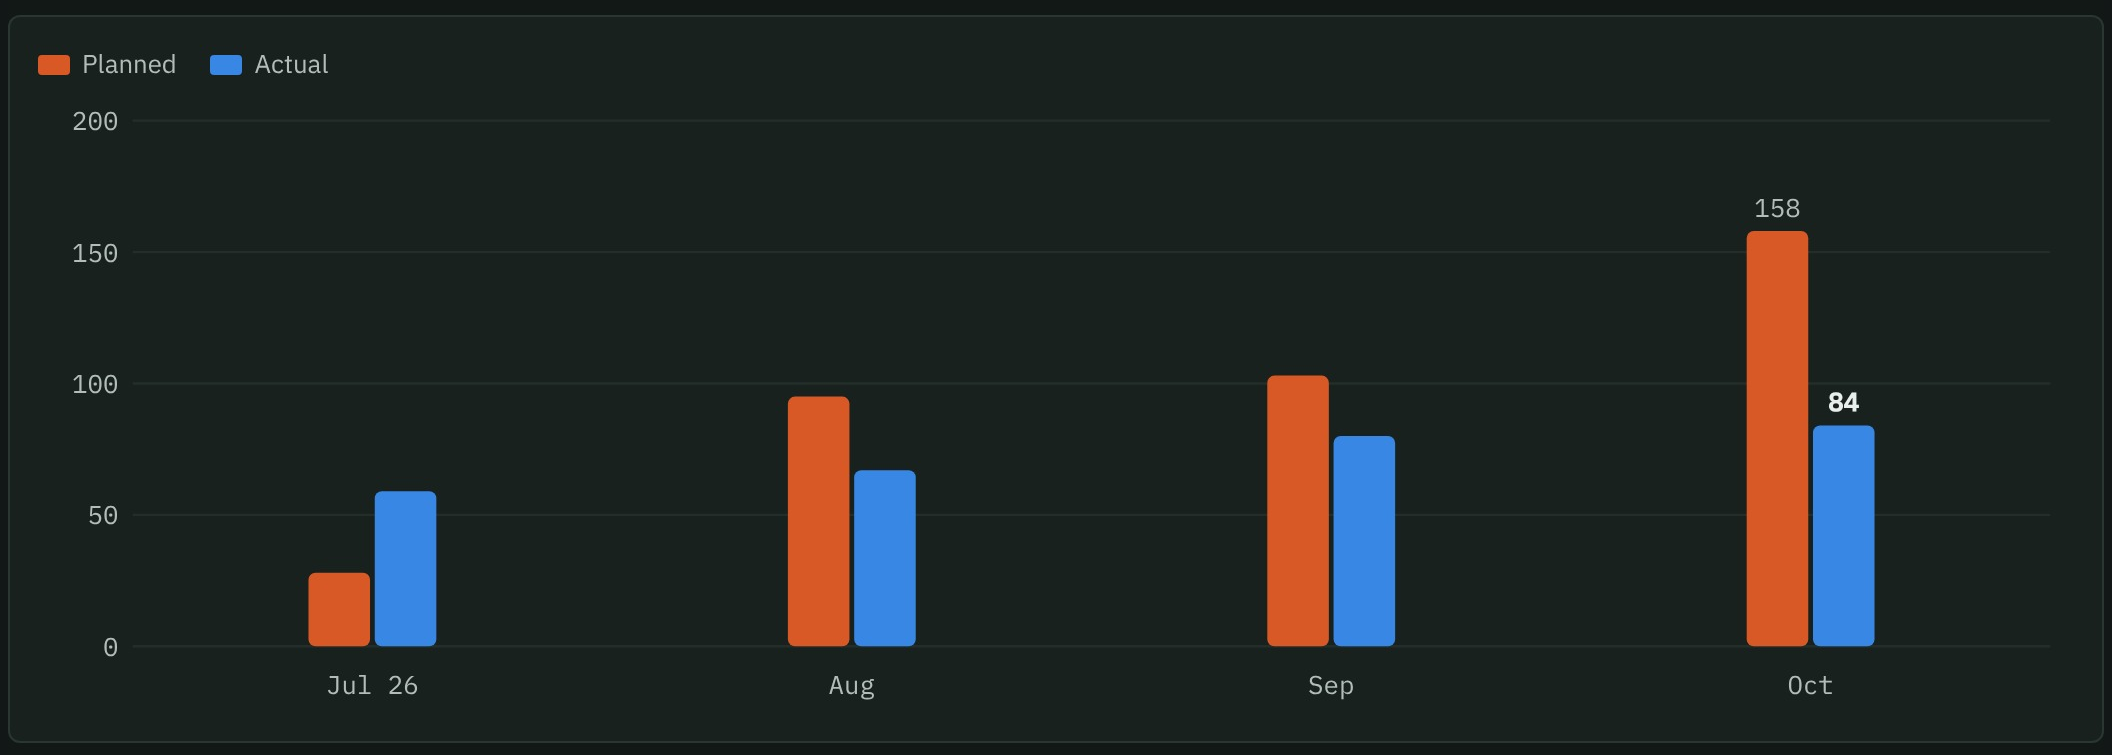

October head count is 84 against 158 planned (−47%): 68 manual workers against 145 planned, and 16 staff against 13. Equipment on site is 62 against 80 planned. The plan peaks at 182 in November 2026.

Cost and invoicing

Contract value

Road works	19,411,954
Storm water drainage	13,628,050
BOQ total (excl. VAT)	**33,040,004**
Contract value incl. 15% VAT	37,996,005
Change orders	0

All values in SAR. Road works are 58.8% of the BOQ and storm water drainage 41.2%. No change orders are registered.

Invoices

Invoices submitted	3
Gross value	6,754,935
Deductions and penalties	2,000
Net incl. VAT	7,770,175
Paid (3 invoices)	7,770,175
FIR value to date	9,917,485

Invoicing is 20.4% of the contract value against 48.3% physical progress. Invoice 3 (26-Aug to 27-Sep-2026) was paid on 25-Oct-2026, so nothing is pending. No new invoice has been submitted since. There is no advance payment or retention.

Health, safety and quality

Safety Score 0.89

Safe man-hours (cumulative)	39,965
Man-hours this week	2,976
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	1
Property damage	0
Inductions / toolbox talks	4 / 19

Quality Score 0.89

FIRs issued (cumulative)	252
FIRs closed / pending	222 / 30
MIRs issued / closed	42 / 42
NCRs issued	0
Site instructions (closed)	1
Shop drawings approved	22 / 23
Material submittals approved	40 / 42

Consultant quality and safety inspections of 27-Oct-2026. 48 FIRs were issued this week.

Open issues and risks

RISK	OWNER	DETAIL
Falls into excavations	Contractor	Unstable soil and missing barricades. Barricades, warning signs and a supervisor at excavations. Rated high (H20, H16 after treatment).
Traffic management	Contractor	Vehicle accidents from inadequate traffic diversion. Diversion signs, barriers and traffic marshals. Rated high (H16).
Operator competence	Contractor	Accidents from insufficient training and supervision of operators. Training, competency checks and supervision. Rated high (H16).
Oil spills	Contractor	Soil contamination from equipment leaks or poor handling of oil. Spill response plan, maintenance and containment. Rated medium (M9).

The risk register is unchanged from last week. The issue log and the top-issues panel of the weekly report are empty, and the weekly summary sheets state no delay reasons or challenges.

Data notes

- The summary sheets (works executed and progress files, Progress Summary) label a cost-based figure as "actual" progress. This report uses physical (man-hour) progress only.
- The progress file and the works-executed file again show this week's progress with opposite signs.

- The works-executed file still gives a project start of 24-Nov-2025 and a contract end of 23-May-2026, against site handover on 25-Jun-2026 and completion on 24-Aug-2027 in the weekly report.
- The MODON PM is written as الجليفي in the progress file and as الشنيفي in the works-executed file.
- The weekly physical progress panel shows 6.08% planned and 6.09% earned this week. These add each row twice (13,288 and 13,312 man-hours); the correct figures are 3.04% and 3.05%.
- The Progress sheet uses a budget of 181,410 man-hours, which gives 43.0% planned and 58.2% earned. The Weekly Progress Report sheet and the schedule use 218,590 man-hours (35.7% and 48.3%), which this report follows.
- Week number: the report states contract week 18 of 61 (Milestones sheet). Whole weeks from site handover to the data date give 17.
- No P6 XER file was uploaded this week. Project float (–49 days) is taken from the Progress (2) sheet; the P6 PDF shows –47 and –41 days against the road works and storm drainage milestones as variance to the baseline finish, not as float.
- Cut and fill to date are unchanged in Major Quantities (222,090 and 183,569 m³), while the list of works executed reports 4,410 m³ of cut on Local Road 17 and 2,100 m³ on Local Road 31 this week.
- The catch basin total changed from 156 to 164 in Major Quantities; the Progress Summary still shows 156.
- The Progress Summary gives the same executed length, 2,101 m, for roads (of 5,708 m) and for storm drainage (of 5,855 m); Major Quantities gives 3,421 m of GRP pipe.
- The Failed Start List carries the title, contractor line and date (13-Oct-2026) of project MKH2-02-003, although its activities belong to this project.
- The forecast in the Physical-Chart Data sheet reaches 100% on 31-Aug-2027, but the schedule finishes on 21-Oct-2027.
- The baseline schedule approval is dated 13-Jul-2025, before the contract award of 11-May-2026.
- Major Quantities lists several items twice with different totals (aggregate base 14,403 and 26,167 m³; bituminous base 7,129 and 9,160 m³; subgrade 21,604 and 39,250 m³; interlock 18,500 and 29,206 m²), and electrical items that are not in this project's roads and storm-drainage scope.
- The manpower summary panel shows 28 planned and 94 actual, while the Manpower sheet gives 158 planned and 84 actual for October.
- The invoice summary shows 0 submitted invoices, while the invoice log lists 3. Potential changes are 0 in the summary and 200,000 SAR in the invoice log.
- The risk register marks the four project risks as Closed while their treatment status is Open; it also holds rows for project MKH2-02-003 and rows without a project.
- Several summary panels in the weekly report workbook show #REF! errors.
- The site photos are the images embedded in the weekly report workbook, 594 to 599 px wide. No separate photo files were uploaded.
