MODON - Weekly Progress Report - Construction Projects

Data Date 26-Oct-26

Contract General Information

Project Name	Construction of Passenger Station for SAR Railway Sudair Industrial City		
Project ID	SUD1-05-018	Stage	Construction
Contractor	Technical Development Co. "TDC"	Status	Active
Consultant	Saudi Arabia Consulting Engineering Company "EGIS"	Modon PM	Engr.Zyad Al Shabat

Key Dates

Contract Award	31-Mar-26	Contract Award (Hijri)	10/12/1447	Revised Completion	07-Apr-26	
Contract Sign	31-Mar-26	Contract Sign (Hijri)	10/12/1447	Committed Completion	06-Aug-27	
Site Handover	07-Apr-26	Site Handover (Hijri)	11/19/1447	Forecast Completion	06-Aug-27	
Original Completion	06-Aug-27	Original Completion (Hijri)	03/03/1449	Variance	0	

Cost Summary (SR)

Original Contract Value	33,090,825	O&M Value	0
Revised Contract Value	0	Revised O&M Value	0
Estimate At Completion Value	33,090,825	Submitted Invoices (Gross Value)	3,048,399
Potential Changes	0	Total Deduction	(2,000)

Performance Summary

Plan Value	20.54%	Phys. Plan Value	39.96%	Quality Score	88.7%
Earn Value	22.24%	Phys. Earn Value	27.29%		
Variance	1.70%	Variance	(12.66%)	Safety Score	83.3%
SPI	1.08	SPI	0.68		

Project Scope


Civil Work , Storm Water Drainage , Sewer , Portable , Electrical , CCTV

Progress Overview


Earned Value Progress (SAR) / Physical Progress (Effort)

WBS	BOQ Value (SAR)	% Wt.	Weekly (SAR) Planned	Weekly (SAR) Earned	To Date (SAR) Original Plan	To Date (SAR) Cum. Planned	To Date (SAR) Cum.Earned	Original Plan %	Cum. Planned %	Cum.Earned %	Variance	SPI	Budgeted (Manhours)	% Wt.	Weekly Physical Progress Planned	Weekly Physical Progress Earned	Plan %	Earned %	To Date Physical Progress Planned	To Date Physical Progress Earned	Plan %	Earned %	Variance	SPI
	-	0.0%	-	-	-	29,068	-	0.0%	0.0%	0.0%	0.0%		-	0.0%	-	-	0.0%	0.0%		-	0.0%	0.0%	0.0%	
Milestones	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%		-	0.0%	-	-	0.0%	0.0%	19,793	19,793	0.0%	0.0%	0.0%	
Mobilization	-	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%		19154.00	3.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	
Engineering	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%		31923.40	5.0%	-	-	0.0%	0.0%	32,988	31,339	103.3%	98.2%	-5.2%	0.95
Procurement	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%		89,386	14.0%	3,175	-	3.6%	0.0%	71,522	17,130	80.0%	19.2%	-60.9%	0.24
Construction	33,090,852	100.0%	495,271	265,487	-	6,797,078	7,361,029	0.0%	20.5%	22.2%	1.7%	1.08	478,851	75.0%	8,970	7,758	1.9%	1.6%	130,821	106,004	27.3%	22.1%	-5.2%	0.81
Package-1	22,502,032	68.0%	461,728	265,487	-	6,348,360	7,361,029	0.0%	28.2%	32.7%	4.5%	1.16	345,776	54.2%	8,700	7,758	2.5%	2.2%	118,362	106,004	34.2%	30.7%	-3.6%	0.90
ROAD WORKS 1	17,704,263	53.5%	319,944	121,193	-	5,686,305	6,621,766	0.0%	32.1%	37.4%	5.3%	1.16	168,660	26.4%	17,222	192	10.2%	0.1%	75,962	79,097	45.0%	46.9%	1.9%	1.04
ROAD - 01	10,400,905	31.4%	174,074	121,193	-	3,325,062	4,261,259	0.0%	41.0%	41.0%	0.0%	1.00	96,630	15.1%	1,006	192	1.0%	0.2%	59,746	62,852	61.8%	65.0%	3.2%	1.05
ROAD - 02	7,303,358	22.1%	145,870	-	-	2,361,243	2,360,507						72,030	11.3%	1,406	-	2.0%	0.0%	16,216	16,245	22.5%	22.6%	0.0%	1.00
ELECTRICAL WORKS	3,415,753	10.3%	79,057	26,802	-	326,029	89,432						103,222	16.2%	-	-	0.0%	0.0%	21,481	5,989	20.8%	5.8%	-15.0%	0.28
MV Network	1,577,890	4.8%	19,352	-	-	54,830	-						37,659	5.9%	1,619	-	4.3%	0.0%	1,619	-	4.3%	0.0%	-4.3%	0.00
Earthing System	4,795	0.0%	-	-	-	-	-						173	0.0%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
Street Lighting Network	1,454,545	4.4%		22,684	-	186,446	29,066						51,051	8.0%	10,989	1,937	21.5%	3.8%	14,997	2,452	29.4%	4.8%	-24.6%	0.16
TELECOMMUNICATIONS WORKS	378,522	1.1%		4,119	-	84,753	60,366						14,340	2.2%	4,864	301	33.9%	2.1%	4,864	3,538	33.9%	24.7%	-9.2%	0.73
LOW VOLTAGE	86,942	0.3%		-	-	-	4,927						6,638	1.0%	66	329	1.0%	5.0%	66	651	1.0%	9.8%	8.8%	9.86
ROAD - 01	28,981	0.1%	-	-	-	398,560	2,029	0.0%	7.0%	7.0%	0.0%	1.00	2,072	0.3%	66	-	3.2%	0.0%	2,450	322	118.2%	15.5%	-102.7%	0.13
ROAD - 02	57,961	0.2%		869									4,566	0.7%						328				
PORTABLE WATER	379,700	1.1%		225,657									46,755	7.3%										
ROAD - 01	189,850	0.6%		(76,185)									20,132	3.2%										
ROAD - 02	189,850	0.6%		-									26,623	4.2%										
SEWARAGE NETWORK	621,335	1.9%		57,350									19,752	3.1%										
ROAD - 01	372,801	1.1%											12,695	2.0%										
ROAD - 02	248,534	0.8%											7,057	1.1%										
STORM WATER	294,040	0.9%											749	0.1%										
ROAD N...	294,040	0.9%											749	0.1%										
Package-3	10,588,820	32.0%											133,075	20.8%										
Site Works	21,090	0.1%											1,836	0.3%										
Earthworks	21,090	0.1%											1,836	0.3%										
Platform Works	6,003,782	18.1%											68,965	10.8%										
Platform Substructure	5,037,344	15.2%	-	-	-	398,560	-	0.0%	0.0%	0.0%	0.0%		47,411	7.4%	-	-	0.0%	0.0%	2,450	-	5.2%	0.0%	-5.2%	0.00
Finishes & Architectural Works	966,437	2.9%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%		21,152	3.3%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
Total	**33,090,825**	**100.0%**	**522,331**	**265,487**	**-**	**6,797,078**	**7,361,029**	**0.00%**	**20.54%**	**22.24%**	**1.70%**	**1.08**	**638,468**	**100.0%**	**12,145**	**7,758**	**1.90%**	**1.22%**	**255,124**	**174,266**	**39.96%**	**27.29%**	**-12.66%**	**0.68**


Earned Value Progress (%)

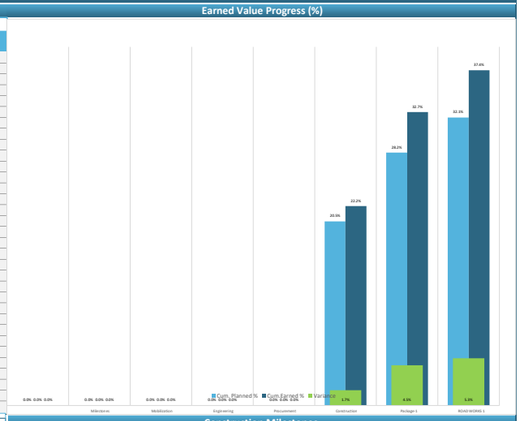

Earned Value - Cost

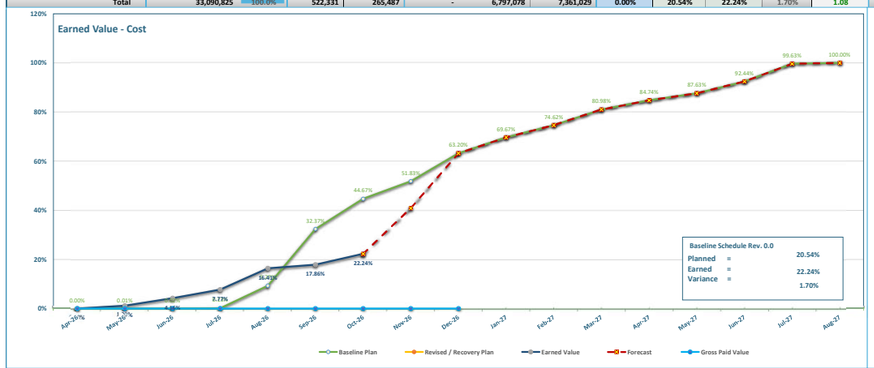

Physical Progress - Effort

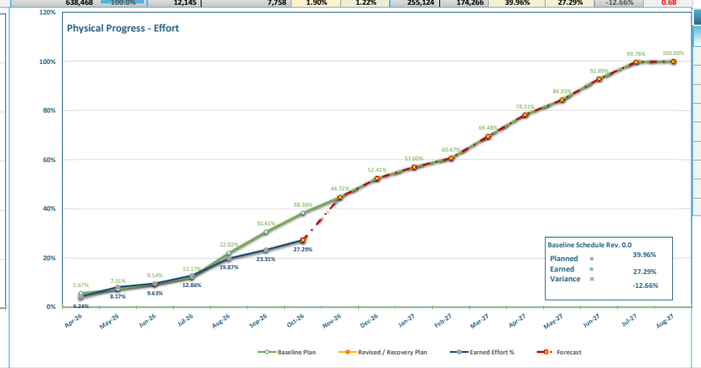


Construction Milestones

Item No.	Milestones	Original (Baseline)	Latest Plan	Forecast	Status	Days Change
1	Project Start Milstone	07-Apr-26	07-Apr-26	07-Apr-26	Finish	0
2	Mobilization Finish Milestone	06-May-26	06-May-26	06-May-26	Finish	0
3	Work Plan and Timeline Milestone	06-May-26	16-Aug-26	16-Aug-26	UP	(102)
4	Completion of MV Work	22-May-27	05-May-27	05-May-27	UP	17
5	Completion of road and paving works Milestone	06-Dec-26	31-Dec-26	31-Dec-26	UP	(25)
6	Completion of site and platform work Milestone	20-Jul-27	05-Aug-27	05-Aug-27	UP	(16)
7	Completion of finishing works and general site works	20-Jul-27	06-Aug-27	06-Aug-27	UP	(17)
8	Engineering Phase Finish Milestone	06-May-26	21-Sep-26	21-Sep-26	UP	(138)
9	Procurment Phase Finish Milestone	15-Apr-27	09-Jun-27	09-Jun-27	UP	(55)

Project Status Score



Actual Invoices



Performance overview

Submittals Status

Shop Drawings

Item Per WBS	Total	Total Submitted Drawings A	B	C	D	Processed	Remaining	Pending	Total Submittals
Roadwork	90	69	10	0	0	79	0	11	79
wet network(sewer,,potable)	47	13	34	0	0	47	0	0	47
Telecom	15	15	0	0	0	15	0	0	15
Lighting	28	13	1	0	0	14	0	14	14
Electrical	24	12	12	0	0	24	0	0	24
TOTAL	204	122	57	0	0	179	0	25	179

Material Approval

Item Per WBS	Total	Total Submitted Material A	B	C	D	Processed	Remaining to approve	Pending	Total Submittals
Civil /Structural /Architectural	22	0	21	1	0	22	0	0	22
Electrical	16	1	13	2	0	16	0	0	16
Mechanical	7	0	7	0	0	7	0	0	7
TOTAL	45	1	41	3	0	45	0	0	45

Procurement Summary

Item Per WBS	Total Materials	Total Number of P.O.	Actual P.O. To Date	Remaining P.O	Material on Site	Remaining Materials	Material Delivery Completion (Date)
Civil /Structural /Architectural	3	2	2	1	0	3	-
Electrical	18	15	15	3	6	6	-
Mechanical	6	5	5	1	3	3	-
TOTAL	27	22	22	5	9	12	00-Jan-00

Primavera P6 Schedule Status

Project Activities Overview

Schedule Statistics: Total Act.	Not Started	In Progress	Completed	%	Active Schedule Activities: Active	Ahead	On	Behind	Flag	0
855	557	51	247	28.89%	2	2	0	1	1	

Critical Path Activities: Last Week	This Week	Diff	Free Float Management (Total): Greater Than 14 Days Last Week	This Week	Less Than 14 Days Last Week	This Week	Failed Start Activities: Last Week	This Week	Flag	0
0	0	0	172	287	570	552	2	1	1	

Quality

Quality Reports

Quality Reports	Issued	Closed	Pending	Avg. Closing (Days)	Pending 0-10 Days	11-20 Days	21-30 Days	31-60 Days	> 60 Days
Non Conformance (NCR)	4	4	0	0	0	-	-	-	-
Site Instruction (SIR)	0	0	0	0	-	0	0	0	0
Material Inspection (MIR)	15	15	0	0	0	0	0	0	0
Field Inspection (FIR)	157	152	5	0	5	0	0	0	0

Key Submittals Approval Status

1 Quality Plan Approval	11-May-26	6 Baseline Approval	02-Aug-26
2 Quality Plan Last Up	11-May-26	7 No of Approved Version of Schedule	-
3 Safety Plan Approval	06-May-26	8 Last Approved Schedule	-
4 Safety Plan Last Up	30-Apr-26	9 BOQ Approval Date	-
5 Construction Plan Approval	-	10 No of Approved Version of BOQ	-

Invoices Summary

Total Submitted Invoices	2	Submitted Invoices (SAR)	3,048,399
PM Approved Invoices	0	PM Approved Invoices (SAR)	0
No of Paid Invoices	0	Paid Invoices (SAR)	0
No of Pending Invoices	2	Last Submitted Period	00-Jan-00
Advance Payment %	0%	Advance Payment (SAR)	0
Retention %	0%	Retention (SAR)	0
Deduction / Penalties %	0%	Deduction / Penalties (SAR)	(2,000)



Resources at Site

Head Count - Manual: Planned	Actual	Next Month Forecast	Saudi Staff	Head Count - Non Manual: Planned	Actual	Next Month Forecast	Saudi Staff	Total Head Count: Total Plan	Total Actual	Variance
40	65	0	0	20	22	0	3	60	87	27

Manpower Breakdown by Trade: Key Trade	Planned	Actual
Engineer	2	10
Doc. Controller	1	1
Proc. Team	1	1
Foreman	2	3
Draftman	1	1
Driver	5	31
Un-Skilled Labor	15	20
Total	40	87



Major Equipment: Type	Planned	Actual	Idle
Pick Up/Car	1	2	0
Bus	1	2	0
Dump Truck	10	12	0
Boom Truck	0	2	0
Generator	1	1	0
CRANE	0	1	0
Shovel	0	1	0
Total	13	21	0

Safety


Safety Statistics

Category	Item	This Week	This Month	Year to Date	Cumulative
General	Total Hours Worked	5,100	14,640	82,150	82,150
	Safe Hours Worked	5,100	14,640	82,150	82,150
Reactive	0	0	0	23	0
	0	0	0	0	0
	0	0	0	21	0
	0	0	0	0	0
	0	0	0	0	0
	0	0	0	0	0
	0	0	0	0	0
	0	0	0	0	0
Proactive	0	0	0	0	0
	No.of Internal Training	1	4	23	23
	No.of Internal Audit	0	0	0	0
	No. of Toolbox Talks	1	4	21	21
	Safety Awards/Incentives	0	0	0	0

Proactive Vs Reactive Actions Taken



Total Hours Worked Vs Safe Hours Worked



Latest Contract Change Order Log

CCO No.	Date Added	Description of Change	Status	Cost	Sch Impact (Months)	Date Approved	Duration
-	-	-	-	-	-	-	-

Major Quantity Trackers

BOQ NO.	Item Description	Total Qty	Measu Unit	Plan to Date	Act to Date	Remaining	Variance
B1.32 11 13.01	Subgrade	20530	m3	0.00	18182.25	2347.75	0.00
B1.32 11 23.01	Aggregate base course	16375.94	m3	0.00	21459.19	-5083.25	0.00
B1.32 12 16.01	Asphalt	13360	m3	0.00	573.00	12787.00	0.00
B1.32 14 13.13.0	Interlock	27900	m2	0.00	0.00	27900.00	0.00
B1.32 16 13.23.0	Curbstone	20555	m2	0.00	282.00	20273.00	0.00

Testing And Commissioning

Item	Planned Start Date	Planned Finish Date	Forecast Start Date	Forecast Finish Date	Actual Start Date	Actual Finish Date	% Completed	Open Comments	Closed Comments
Civil Works	09-May-27	31-May-27	06-Jun-27	23-Jun-27			0%	0	0
Storm Water Drainaae Network	19-Jan-27	06-Feb-27	18-Mar-27	05-Apr-27			0%	0	0
Sewerage Network	14-Mar-27	31-Mar-27	25-Jan-27	13-Feb-27			0%	0	0
Portable Water	22-Mar-27	08-Apr-27	28-Mar-27	14-Apr-27			0%	0	0
Electrical Works	18-Jul-27	03-Aug-27	08-Jul-27	26-Jul-27			0%	0	0
CCTV Works	22-Jul-27	06-Aug-27	12-Jul-27	27-Jul-27			0%	0	0

Top Issues and Risks

Top 5 Issues

Issue No	Date Identified	Issue Description	Responsible	Action Taken	Mitigation	Current Status	Expected/Actual Closure	Duration Elapsed
3120-13	11/Oct/26	Observe site without mandatory PPE complaince	Contractor/HSE Team	Wear the mandatory PPE all the time when present on site		Close	2	1
3120-14	18/Oct/26	Observe dust created at temporary vehicles roads due insuffient dust control measures.	Contractor/HSE Team	Ensure dust control by regular spraying of water on vehicles routes		Close	2	1
3120-15	17/Oct/26	Observe non complaince of mandatory PPE by equipment operators	Contractor/HSE Team	Wear the mandatory PPE all the time by equipment operators when present on site		Close	2	1
3120-16	25/Oct/26	Observe some shallow excavations areas with edge protection.	Contractor/HSE Team	Provide proper barricade and warning signages		Close	2	1
3120-17	25/Oct/26	Observe non complaince of mandatory PPE by equipment operators	Contractor/HSE Team	Wear the mandatory PPE all the time by equipment operators when present on site		Close	2	1

Data sensitivity - Internal

Weekly Progress Report - Construction Projects

Data Date	26-Oct-26

Contract General Information

Project Name	Construction of Passenger Station for SAR Railway Sudair Industrial City
Project ID	SUD1-05-018
Contractor	Technical Dvelopment Co. "TDC"
Consultant	Saudi Arabia Consulting Engineering Company "EGIS"
Stage	Construction
Status	Active
Modon PM	Engr.Zyad Al Shabat

Key Dates

Contract Award Date	31-Mar-26
Contract Sign Date	31-Mar-26
Site Handover Date	07-Apr-26
Original Completion	06-Aug-27
Contract Award Date (Hijri)	10/12/1447
Contract Sign Date (Hijri)	10/12/1447
Site Handover Date (Hijri)	11/19/1447
Original Completion (Hijri)	03/03/1449
Revised Completion Date	07-Apr-26
Committed Completion Date	06-Aug-27
Forecast Completion	06-Aug-27
Variance	0

Key Project Submittals	Submission Date	Days taken to approve orginal plan from site handover date
Quality Plan submission	30-Apr-26	23
Quality Plan approval	11-May-26	
Quality Plan Last Update	11-May-26	
Safety Plan submission	30-Apr-26	23
Safety Plan approval	6-May-26	
Safety Plan Last Update	30-Apr-26	
Risk Management Plan submission	20-Apr-26	13
Risk Management Plan approval	30-Apr-26	
Risk Management Plan Last Update	30-Apr-26	
Baseline Schedule submission	7-May-26	30
Baseline Schedule approval	2-Aug-26	
No of Schedule Versions	-	
Last Revised Schedule Approval Date	-	
BOQ submission	-	-
BOQ approval	-	
No of Approved Version of BOQ	-	
Execution Plan submission	30-Apr-26	23
Execution Plan Approval	-	

Data sensitivity - Internal

Project Scope Statement	Construction of Passenger Station for SAR Railway Sudair Industrial City


Earned Value Progress (SAR)								Physical Progress (Effort)					
WBS	BOQ Value (SAR)	% Wt.	Weekly (SAR)			To Date (SAR)		Budgeted	% Wt.	Weekly Physical Progress		To Date Physical Progress	
			Planned	Earned	Original Plan	Planned	Earned	(Manhours)		Planned	Earned	Planned	Earned
Milestones						-	-	-	0.0%			-	-
Mobilization	-					-	-	19,154	3.0%	-	-	19793	19793
Engineering	**-**	**0.00%**	**-**	**-**	**-**	**-**	**-**	**31923.4**	**5.0%**	**-**	**-**	32988	31339
Procurement	**-**	**0.00%**	**-**	**-**	**-**	**-**	**-**	**89385.5**	**14.0%**	**3,175**	**-**	71522	17130
Construction	**33,090,852.00**	**100.00%**	**495,271**	**265,487**	**-**	6,797,077.99	7,361,028.85	**478850.8**	**75.0%**	**8,970**	**7,758**	130821	106004
Package-1	22,502,032.00	68.00%	461,728	265,487	-	6,348,359.62	7,361,028.85	345775.5	54.2%	8,700	7,758	118362	106004
ROAD WORKS 1	17,704,263.00	53.50%	319,944	121,193	-	5,686,304.89	6,621,766.13	168659.6	26.4%	17,222	192	75962	79097
ROAD - 01	10,400,905.00	31.43%	174,074	121,193	-	3,325,061.62	4,261,258.80	96629.6	15.1%	1,006	192	59746	62852
ROAD - 02	7,303,358.00	22.07%	145,870	-		2,361,243.28	2,360,507.33	72030.1	11.3%	1,406	-	16216	16245
ELECTRICAL WORKS	3,415,753.00	10.32%	79,057	26,802		326,029.21	89,431.83	103222.1	16.2%		-	21481	5989
MV Network	1,577,890.00	4.77%	19,352	-		54,830.44	0	37659	5.9%	1,619	-	1619	0
Earthing System	4,795.00	0.01%	-	-		0	0	172.8	0.0%	-	-	0	0
Street Lighting Network	1,454,545.00	4.40%	39,995	22,684		186,445.64	29,066.10	51050.8	8.0%	10,989	1,937	14997	2452
TELECOMMUNICATIONS WORKS	378,522.00	1.14%	19,710	4,119		84,753.13	60,365.73	14339.6	2.2%	4,864	301	4864	3538
LOW VOLTAGE	86,942.00	0.26%	416	-		415.99	4,926.72	6638.4	1.0%	66	329	66	651
ROAD - 01	28,981.00	0.09%	416	-		415.99	2,028.65	2072.2	0.3%	66	-	66	322
ROAD - 02	57,961.00	0.18%	-	869		0	2,898.07	4566.2	0.7%	(11,285)	-	0	328
PORTABLE WATER	379,700.00	1.15%	9,785	225,657		76,026.95	228,555.12	46755	7.3%	8,631	6,032	13377	13227
ROAD - 01	189,850.00	0.57%	4,447	(76,185)		35,282.66	137,133.08	20132.1	3.2%	(823)	3,470	5716	8349
ROAD - 02	189,850.00	0.57%	5,338	-		40,744.29	91,422.05	26622.9	4.2%	1,122	-	7661	4879
SEWARAGE NETWORK	621,335.00	1.88%	106,560	57,350		141,966.48	148,772.44	19751.7	3.1%	2,851	3,815	7298	6453
ROAD - 01	372,801.00	1.13%	(39,790)	7,329		87,455.66	115,594.86	12694.5	2.0%	3,315	4,010	5172	4422
ROAD - 02	248,534.00	0.75%	(24,854)	15,133		54,510.81	33,177.58	7057.2	1.1%	1,970	1,619	2126	2031
STORM WATER	294,040.00	0.89%	69,736	249,532		117,616.10	267,576.62	748.6	0.1%	21	359	177	587
ROAD N...	294,040.00	0.89%	37,805	61,748		117,616.10	267,576.62	748.6	0.1%	21	587	177	587
Package-3	10,588,820.00	32.00%	33,543	-		448,718.37	0	133075.3	20.8%	269	-	12459	0
Site Works	21,090.00	0.06%	(394,085)	-		21,090.02	0	1835.5	0.3%	-	-	9506	0
Earthworks	21,090.00	0.06%	-	-		21,090.02	0	1835.5	0.3%	-	-	9506	0
Platform Works	6,003,782.00	18.14%	27,060	-	-	398,560.32	0	68964.6	10.8%	114	-	2450	0
Platform Substructure	5,037,344.00	15.22%	27,060	-	-	398,560.32	0	47410.5	7.4%	2,450	-	2450	0
Finishes & Architectural Works	966,437.00	2.92%	-	-		0	0	21151.7	3.3%	-	-	0	0
Platform Electrical Works	-	0.00%				0	0	402	0.1%			0	0
Canopy works	3,863,605.00	11.68%				29,068.02	0	33,381	5.2%			503	0
Civil and Architectural Works	166,440.00	0.50%				13,888.01	0	1,831	0.3%			304	0
Metals	3,697,165.00	11.17%				15,180.01	0	31,550	4.9%			199	0
Electrical Works	700,343.00	2.12%				0	0	28,894	4.5%			0	0
Low-Voltage Electrical Power Conductors and Cables	36,000.00	0.11%				0	0	676	0.1%			0	0
Ondoor Lighting Points	62,010.00	0.19%				0	0	390	0.1%			0	0
Outdoor Lighting Fixtures	152,490.00	0.46%				0	0	16,411	2.6%			0	0
CCTV	327,218.00	0.99%				0	0	4,076	0.6%			0	0
Voice Evacuation System	122,624.00	0.37%				0	0	7,342	1.1%			0	0
Testing and Comissioning	**0**	**0%**				0	0	**12737.5**	2.0%			0	0
Close Out	**0**	**0%**				0	0	**6416.6**	1.0%			0	0
Total	33,090,825.00	**100.0%**	**522,331**	**265,487**	**-**	**6,797,078**	**7,361,029**	**638,468**	**100.0%**	**12,145**	**7,758**	**255,124**	**174,266**
						20.54%	22.24%					39.96%	27.29%

Data sensitivity - Internal

WEEKLY PROGRESS PHOTOS

Data Date 26-Oct-26

Bituminous base course MC-01 at Road 1

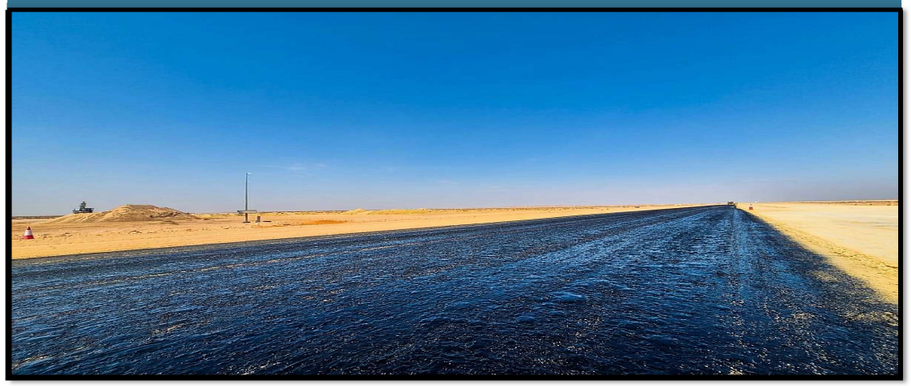

backfiling filing for roundabout at MC20 with road 1



Compaction For Aggregate Base course layer works at road 1From st 1+500 to st 1+850



Aggregate Base course layer works at road 1From st 1+500 to st 1+850



Grading for second layer of subgrade at Road no.1 From st 00+950 to 1+200 - Right side



Compaction for 5th layer at parking at Road no.1



Data sensitivity - Internal

Quality -Stat

Quality Reports

Item	Issued	Closed	Pending	Avg. Closing (Days)	Pending				
					0-10 Days	11-20 Days	21-30 Days	31-60 Days	> 60 Days
Non Conforomance Report (NCR)	4	4	0			-	-	-	-
Site Instruction (SI)	0	0	0		-	-	-	-	-
Material Inspection Report (MIR)	15	15	0		-	-	-	-	-
Field Inspection Request (FIR)	157	152	5		5	-	-	-	-

Shop Drawings

Item Per WBS	Total	Total Drawings Submitted					Remaining Drawings	Pending Submittals With Consultant	Total Submittals
		A	B	C	D	Processed(A+B+C+D)			
Road work	90	69	10	0	0	79	-	11	79
wet network(sewer,potable,Storm)	47	13	34	0	0	47	-	0	47
Telecom	15	15	0	0	0	15	-	0	15
Lighting	28	13	1	0	0	14	-	14	14
Electrical	24	12	12	0	0	24	-	0	24
TOTAL	**204**	**122**	**57**	**-**	**-**	**179**	**-**	**25**	**179**

Material Approval

Item Per WBS	Total	Total Materials Submitted					Remaining to approve	Pending Submittals With Consultant	Total Submittals
		A	B	C	D	Processed(A+B+C+D)			
Civil /Structural /Architectural	22	-	21	1	-	22	-	0	22
Electrical	16	1	13	2	-	16	-	0	16
Mechanical/STR	7	-	7	0	-	7	-	0	7
TOTAL	**45**	**1**	**41**	**3**	**-**	**45**	**-**	**-**	**45**

Procurement Summary

Item Per WBS	Total Materials	Total Number of P.O.	Actual P.O. To Date	Remaining P.O	Actual Material on Site	Remaining Materials	Material Delivery Completion (Date)
Civil /Structural /Architectural	3	2	2	1	-	3	-
Electrical	18	15	15	3	6	6	-
Mechanical	6	5	5	1	3	3	-
TOTAL	**27**	**22**	**22**	**5**	**9**	**12**	

Data sensitivity - Internal

QC OBSERVATIONS CHECKLIST

Project No.	**SUD1-05-018**	**OBS No.**		**Inspection Day:**	**October 26, 2026**
Project	**Construction of Passenger Station for SAR Railway Sudair Industrial City**	**Contractor: Consultant:**	**Technical Development Company** **Egis Engineering cunsultancy**		

4	Excellent	Quality Management System is being practiced and applies to MODON System	**90 - 100**	**QC Overall Score**	**88.7%**
3	**Good**	Evidence of compliance with plans and procedures.	**80 - 89**		
2	Average	Indication level of compliance with standards but there is room for improvement	**70 - 79**		
1	Improve	Quality and Control is NOT being managed effectively. Needs Improvement	**≤ 69**		
0	N/A	Item was not applicable or this item was not reviewed during the inspection.	**Zero**		

No.	Topic	E (4)	G (3)	A (2)	I (1)	N/A (0)
1	Control of Access to Site/Office		G			
2	Document Control Administration		G			
3	Project Documents and Progress		G			
4	Contractor's Quality Plan/CM (Updated and Reviewed)		G			
5	MS Log and Paperwork		G			
6	RFI, FIR, & MIR Procedure		G			
7	RFI, FIR, & MIR Inventory system		G			
8	NCRs Control & Procedure		G			
9	NCR Log		G			
10	MODON Standard*			G		
11	Project Risk Plan/Management*				G	
12	Monthly Quality Reports*				G	
13	ITP			G		
14	MODON Weekly Report				G	
15	Design Change Official Paperwork*					G
16	Design Change was Applied*					G
17	Material List		G			
18	Pending Material Status		G			
19	Lifting Plan*				G	
20	DWG Log				G	
21	Invoice Status				G	
22	Site Handover Letter	G				
23	Material Testing Results & Certification				G	
24	As Build Drawings Status*					G
25	Calibrated Lab Tools & Equipment		G			
26	Storage Inventory System		G			
27	Logistics Plan		G			
28	Project Progress Planview			G		
29	Sufficient Number of QC Inspectors			G		

No.	Topic	E (4)	G (3)	A (2)	I (1)	N/A (0)
30	QC of Excavation		G			
31	QC of Roads/Round about		G			
32	QC of Interlock & Curbstone		G			
33	Layers/Backfilling Sampling		G			
34	Pump Stations Units					G
35	Quality of Form Work					
36	Design Change List					G
37	Quality of Concrete Placing					G
38	Concrete Surface Finishing					G
39	Pedestals/Columns/Beams Alignment					G
40	Siporex Lifting & Unloading					G
41	Siporex Quality Pre-installation					G
42	Siporex Finishing Quality					G
43	Roads / Parking Markings		G			
44	QC of Finishing Outdoors					G
45	Quality of Finishing Indoors					G
46	Stairs Quality					G
47	Tanks Method Statement Work					G
48	Electric Rooms					G
49	QC of MCC/ATS Plant Units					G
50	Qualified Subcontractor		G			
51	Scaffold/Ladders/Slope/Bridge Compliance					G
52	Protection Applied to Completed Work					G
53	Storage Management in/out Control					G
54	Material Control		G			
55	Manholes Storing and Quality					G
56	Reinforced Steel Quality					G
57	Safety Overview		G			
58	Waste Management Control		G			

Prepared by:	**Sarvar Ahmad**

Issued to PM:	**Engr.Zyad Al Shabat**

*QC Observations refer only to the practices and documentation observed at time of inspection. The responsibility of the CM and Contractor is to ensure that aspects of Quality are suitably managed.
*Scores are a reflection of the general site conditions based upon the findings at the time of the walk through
*If Applicable

Data sensitivity - Internal

Safety Statistics					
Category	Item	This Week	This Month	Year to Date	Cumulative
Category	Total Hours Worked	5,100	14,640	82,150	82,150
	Safe Hours Worked	5,100	14,640	82,150	82,150
	No.of Internal Training	1	4	23	23
	No.of Internal Audit				
	No. of Toolbox Talks	1	4	21	21
	Safety Awards/Incentives				

Category	Item	This Week	This Month	Year to Dat	Cumulative
Overall Average	83.33%				
This Week Score	83%				

Consultant Safety Inspection (Weekly Basis)						
Week Number	Date of Audit	Date Issued	Numbers Of Comments	Overall Score	Date Closed	Closure Duration
Week-1			0	76%		0
Week-2			0	76%		0
Week-3			0	83%		0
Week-4			0	77%		0
Week-5			0	83%		0
Week-6			0	83%		0
Week-7			0	83%		0
Week-8			0	83%		0
Week-9			0	83%		0
Week-10	17-Aug-26	17-Aug-26	0	83%	17-Aug-26	0
Week-11	24-Aug-26	24-Aug-26	0	83%	24-Aug-26	0
Week-12	31-Aug-26	31-Aug-26	0	83%	31-Aug-26	0
Week-13	7-Sep-26	7-Sep-26	0	83%	7-Sep-26	0
Week-14	14-Sep-26	14-Sep-26	0	83%	14-Sep-26	0
Week-15	21-Sep-26	21-Sep-26	0	83%	21-Sep-26	0
Week-16	28-Sep-26	28-Sep-26	0	83%	28-Sep-26	0
Week-17	5-Oct-26	5-Oct-26	0	83%	5-Oct-26	0
Week-18	12-Oct-26	12-Oct-26	0	83%	12-Oct-26	0
Week-19	19-Oct-26	19-Oct-26	0	83%	19-Oct-26	0
Week-20	26-Oct-26	26-Oct-26	0	83%	26-Oct-26	0
Week-21			0	0%		0
Week-22			0	0%		0
Week-23			0	0%		0
Week-24			0	0%		0
Week-25			0	0%		0
Week-26			0	0%		0
Week-27			0	0%		0
Week-28			0	0%		0
Week-29			0	0%		0

Data sensitivity - Internal

MODON HSE Site Inspection Report

Date	26-Oct-26	Inspected By:	Engr Ayman Sabry		
Project ID.	SUD1-02-011	Report No.		MODON PM Name	Engr.Ziyad Al Shabbat
Project Name:	Construction of Passenger Station for SAR Railway Sudair Industrial City	Contractor:	TECHNICAL DEVELOPMENT CONTRACTING CO.	Safety Performance	83.33%

Inspections are a snapshot in time and refer only to the practices and documentation observed at the time of the Inspection. It remains the responsibility of the Consultant and Contractor to ensure that all aspects of Health & Safety are suitably managed.

	Good Practice		Need Improvement		Fail (Life Threatening Activity) / Comliance with Plan & Procedures	N/A	Atcitty Not Applicable for this Site Inspection Report

No.	Topic	HSE Compliance
1	Access and Egress - (General access to site, segregated from vehicles, / Overhead protection, while entering into the building /Adequate lighting provided when dark or overnight work)	
2	Traffic Management - (Loading/unloading/sheeting/temp. routes/speed/parking/competence)	
3	Site Signage - (Project Notice Board & General Signage)	
4	PPE Compliance - (Use, storage, stock, handling & checks - Head, Foot, Eye, Hearing)	
5	Housekeeping - (Material correctly stored/Rubbish cleaned & removed daily/slips & trips hazards)	
6	Storage of Materials - (Transporting, storage, training and use - Combustible / Flammable / Hazardous substances (COSHH)	
7	Site Waste Management - (Hazardous waste /Combustible waste / Human waste / Construction waste - asphalt, cable, timber, paving roof sheeting tiles, plastic & bricks)	
8	Health Surveillance - (Expose to excessive noise/vibration/dust/silica/CO/cement/radiation/extreme weather condition)	
9	Electrical Safety - (Electrical qualified /RCD/GFCI/Industrial Cocket/LOTO/Cable-overhung or buried/Cords in good condition/current inspection tag)	
10	Tools & Equipment - (Includes, powered, hydraulic & pneumatic/Guards in place/Properly stored/RCD Protection/Earthed/Good condition & tagged)	
11	Manual Handling - (Lifting/loading/pulling/pushing/twisting/awkward posture/repetitive task/frequent and prolong physical effort/Reasonable practicable use of mechanical aid)	
12	Vehicle and mobile equipment / Plant - (dumpers; excavators, cranes, piling rigs, grader, roller, loaders/condition/KSA License/certification)	
13	Lifting Operations & Rigging - (Lifting Plan/Lifting devices & gears/PTW/Condition/3rd party certification/bank-man/rigger/slingers/man-basket/inspection record/tagged)	N/A
14	Work at Height - (PPE/Fall Protection(Same level, above and blow) / Training / Fall restraint / competency /Safe access & egress to and from work at height / Ladders / Openings (floor/shafts/Provision of emergency rescue)	N/A
15	Scaffolding - (Temp. Scaffolding Work-platform (All types) - qualified scaffolder / Inspection / Tagged / Safe Access/egress / PTW/Falsework & Formwork)	N/A
16	Mobile Elevated Work platform (MEWP) - (PTW/competence requirements/conditions/inspections/tagged/training/Full-body harness)	N/A
17	Excavation & Trenches - (PTW/Edge protection/buffer zone/Slope/Benching/Shoring/Geo-tech report/Atmospheric hazards/Acess&egress/Emergency management / MS&RA/H.E)	
18	Confined Space - (PTW/Training/competence/Emergency Management/MS & RA/Safe access/egress)	N/A
19	Fire Protection - (Flammable/Oxy. LPG /Combustible separated/FE's/Flashback arrestor/Sparks & slags/Smoking area/PTW/Generators/MS & RA/Emergency Management)	
20	Health & Welfare - (Adequate drinking water/shaded - eating & rest area/washing & sanitary facilities/Certified FA/FA Box & Stock/adequate toilets/Ambulance)	
21	Environmental Incident Measures - (Spill/ Leakage / Concrete wash / vehicle & eqpts. wash / waste disposal/Sewers and drains/emissions/Emergency Management/Training/site run-off water)	
22	HSE Communications & Meetings - (Schedule HSE Meetings/Safety Committee meetings/Alerts / Lesson learned/Safety Bulletin contains latest HSE KPI)	
23	HSE Plan & Associated Procedures - (Approved updated HSE Plan/ CEMP/HAZComm/Procedures/Standards/Project Safety Risk Register)	
24	Health, Safety & Environment Incident reporting - (Review of HSE Statistics, Reporting of Unsafe Act & Conditions/ Reporting of Near Miss incident/Reporting of FA cases/Record MT cases)	
25	HSE Awareness, Training & Competence - (Policy /Objective & targets/Information, training/Climatic condition awareness/Reponses in emergency situation/ Safety Behavior Observation)	
26	Project Leadership Site Tours - (Provide evidence of proactive safety performance/Deficient discovered discussed/Positive feedback/Workers resolving safety issues)	

Prepared by:	**Abdul kalim**	**Sent to MODON PM:**	**Engr.Ziyad Al Shabbat**

Safety Results

	7		14		0

Data sensitivity - Internal

MAJOR QUANTITIES

BOQ Number	Description of Item	Total Quantity	Unit of Measurement	Actual To Date	Excecuted on site	Remaining Total
B1.32 11 13.01	Subgrade	20530	m3	18,182	3,182.25	2,348
B1.32 11 23.01	Aggregate base course	16375.94	m3	21,459	11,583.25	-5,083
B4.33 31 23.01	HDPE pipe	5,808	m	5,808		0
B1.32 12 16.01	Asphalt	13,360	m3	573		12,787
B1.32 14 13.13.01	Interlock	27,900	m2	0		27,900
B1.32 16 13.23.01	Curbstone	20,555	m2	282	282	20,273
B2.31 23 00.01	Medium Voltage cables	7,120	m	0		7,120
B2.33 71 00 02.01	Low Voltage Cables, Copper & Aluminum,	7,500	m	7,500		0
31 00 00	Canopy	4,000	m	0		4,000
03 00 00	Platform	4,000	m2	0		4,000
B4.05 52 00.01	Metal Handrail	440	m	0		440
B2.26 56 19.01	Lighting Luminaire	116	Unit	0		116

Data sensitivity - Internal

Weekly Progress Report - Invoice Log

Project Value

Original Contract Value	33,090,825.00	O&M Value	0
Revised Contract Value	0.00	Revised O&M Value	0
Estimate At Completion Value	33,090,825.00	Submitted Invoices (Gross Value)	3,048,399
Potential Changes	0.00	Total Deduction	(2,000)

Payment Status

Advance Payment %	0%	Advance Payment (SAR)	0
Retention %	0%	Retention (SAR)	0
Penalties and deduction %	-0.006%	AP Recovery (SAR)	0
Penalties and deduction (SAR)	(2,000)	Retention Cumulative (SAR)	0

Invoices Summary

No of Submitted Invoices	2	Submitted Invoices (SAR)	3,048,399.33
No of Approved Invoices (CM)	0	Approved Invoices (CM) (SAR)	0
No of Approved Invoices (PM)	0	Approved Invoices (PM) (SAR)	0
No of Paid Invoices	0	Paid Invoices (SAR)	0

Submitted Invoice Peroid

Invoice Submitted Compared to Contract Value

Invoice Reference				Invoice Value						Period Covered		CM / PgM Approval Timeline				Modon PM & Accounts Approval							Payment Status			
#	Invoice No.	Doc Control reference	Submittal Rev. #	Gross Value	AP Recovery	Retention	VAT 5%/15%	Deduction / Penalties	Amount (net)	Start Date	End Date	Date to CM / PgM	CM / PgM Approval (Yes/No)	CM / PgM Reply Date	Days Elapsed	Date to PM	PM Approval (Yes/No)	PM Reply Date	Date to Accounts	Accounts Approval (Yes/No)	Accounts Approval Date	Days Elapsed	Date Paid	Amount Paid	Paid %	Payment Period (d)
1	1	SUD1-05-018-TDC-TS9-1-IPC-0001-00	0	2,573,925.60	0.00		386,088.84	(2,000.00)	2,958,014.44	07-Apr-26	18-Jul-26															
9	2	SUD1-05-018-TDC-TS9-1-IPC-0002-00		474,473.73			71,171.06	0.00	545,644.79	19-Jul-26	30-Aug-26															
10																										
11																										
12																										
13																										
14																										
15																										
16																										
17																										
18																										
19																										
20																										
21																										
22																										
23																										
24																										
25																										
26																										
27																										
28																										
29																										
30																										
31																										
32																										
33																										
34																										
35																										
36																										
37																										
38																										
39																										
40																										
41																										
42																										
43																										
44																										
45																										
46																										
47																										
48																										
49																										
50																										
			TOTAL	3,048,399.33	0.00	0.00		(2,000.00)	3,503,659.23															0.00		

Data sensitivity - Internal

Project Name	Construction of Passenger Station for SAR Railway Sudair Industrial City				
Project ID	SUD1-02-011	Project Budget	33,090,825		
Date Paried	Start Date	07/Apr/26	To	Data Date	26/Oct/26

SL NO	BOQ Item #	BOQ Description	Date	FIR #	FIR Description	Unit Rate	Current Period Quantity	% Claim	Unite rate as per claim	Total (SR)
	Description									3,646,338.73
1	B1 .31 23 23.01	Earth works & Embankment	15-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0014-01	Check Coordinates level and Compaction F.D.T for Embankment 1st Layer for Station Road RD-01 , STA: 1+350 to STA: 1+700	24.00	5,835.38	100%	24.00	140,049.12
2	B1 .31 23 23.01	Earth works & Embankment	11-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0015-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 0+850 to STA: 1+000 (Bottom subgrade)	24.00	1,733.54	100%	24.00	41,604.96
3	B1 .31 23 23.01	Earth works & Embankment	16-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0016-01	Check Coordinates level and Compaction F.D.T for Embankment 1st Layer for Station Road RD-01 , STA: 0+120 to STA: 0+500	24.00	5,229.11	100%	24.00	125,498.64
4	B1 .31 23 23.01	Earth works & Embankment	15-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0018-00	Check Coordinates level and Compaction F.D.T for Embankment 1st Layer for Station Road RD-01 , STA: 0+500 to STA: 1+000	24.00	6,588.40	100%	24.00	158,121.60
5	B1 .31 23 23.01	Earth works & Embankment	15-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0021-00	Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-02, STA: 1+000 to STA:1+239.64	24.00	3,557.97	100%	24.00	85,391.28
6	B1 .31 23 23.01	Earth works & Embankment	15-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0022-00	Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-01, STA: 1+000 to STA:1+350	24.00	6,159.64	100%	24.00	147,831.36
7	B1.312323.01	Earth works & Embankment	16-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0023-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+350 to STA:1+530	24.00	2,536.83	100%	24.00	60,883.92
8	B1 .31 23 23.01	Earth works & Embankment	17-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0026-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 0+120 to STA:0+300	24.00	3,205.93	100%	24.00	76,942.32
9	B1 .31 23 23.01	Earth works & Embankment	20-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0027-01	Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-02, STA: 0+840 to STA:1+000	24.00	2,713.88	100%	24.00	65,133.12
10	B1 .31 23 23.01	Earth works & Embankment	20-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0028-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+200 to STA:1+350	24.00	2,471.63	100%	24.00	59,319.12
11	B1.31 23.23.01	Earth works & Embankment	21-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0029-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd Layer for Station Road RD-01, STA: 0+300 to STA:0+500	24.00	3,412.82	100%	24.00	81,907.68
12	B1 .31 23 23.01	Earth works & Embankment	21-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0030-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd Layer for Station Road RD-01, STA: 0+500 to STA:0+700	24.00	3,411.28	100%	24.00	81,870.72
13	B1 .31 23 23.01	Earth works & Embankment	21-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0031-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+000 to STA:1+200	24.00	3,279.64	100%	24.00	78,711.36
14	B1 .31 23 23.01	Earth works & Embankment	21-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0032-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 0+600 to STA:0+700	24.00	1,118.04	100%	24.00	26,832.96
15	B1 .31 23 23.01	Earth works & Embankment	23-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0033-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 0+860 to STA:1+000	24.00	1,963.02	100%	24.00	47,112.48
16	B1 .31 23 23.01	Earth works & Embankment	22-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0034-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 0+700 to STA:0+850	24.00	2,675.56	100%	24.00	64,213.44
17	B1 .31 23 23.01	Earth works & Embankment	22-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0035-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 0+850 to STA:1+000	24.00	2,465.69	100%	24.00	59,176.56
18	B1 .31 23 23.01	Earth works & Embankment	22-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0036-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 1+000 to STA:1+239.64	24.00	3,622.31	100%	24.00	86,935.44
19	B1 .31 23 23.01	Earth works & Embankment	23-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0037-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+120 to STA:0+300	24.00	3,301.84	100%	24.00	79,244.16
20	B1 .31 23 23.01	Earth works & Embankment	23-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0038-00	Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-02, STA: 0+550 to STA:0+700	24.00	2,146.37	100%	24.00	51,512.88
21	B1 .31 23 23.01	Earth works & Embankment	24-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0039-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+300 to STA:0+500	24.00	3,181.05	100%	24.00	76,345.20
22	B1 .31 23 23.01	Earth works & Embankment	24-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0040-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+850 to STA:1+000	24.00	2,363.84	100%	24.00	56,732.16
23	B1 .31 23 23.01	Earth works & Embankment	25-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0041-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+120 to STA:0+300	24.00	3,035.56	100%	24.00	72,853.44
24	B1 .31 23 23.01	Earth works & Embankment	25-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0042-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+200 to STA:1+350	24.00	1,819.60	100%	24.00	43,670.40
25	B1 .31 23 23.01	Earth works & Embankment	27-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0043-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+380 to STA:1+530	24.00	1,600.68	100%	24.00	38,416.32
26	B1 .31 23 23.01	Earth works & Embankment	20-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0044-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 0+570 to STA:0+600	24.00	422.84	100%	24.00	10,148.16
27	B1 .31 23 23.01	Earth works & Embankment	14-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0045-01	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+350 to STA:1+380	24.00	459.23	100%	24.00	11,021.52
28	B1 .31 23 23.01	Earth works & Embankment	27-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0046-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+000 to STA:1+200	24.00	3,121.83	100%	24.00	74,923.92
29	B1 .31 23 23.01	Earth works & Embankment	28-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0047-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+300 to STA:0+500	24.00	2,984.00	100%	24.00	71,616.00
30	B1 .31 23 23.01	Earth works & Embankment	28-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0048-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+530 to STA:1+700 (Bottom Subgrade)	24.00	2,264.12	100%	24.00	54,338.88
31	B1 .31 23 23.01	Earth works & Embankment	29-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0049-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+500 to STA:0+700	24.00	3,745.61	100%	24.00	89,894.64
32	B1 .31 23 23.01	Earth works & Embankment	30-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0050-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+700 to STA:0+850	24.00	2,120.15	100%	24.00	50,883.60
33	B1 .31 23 23.01	Earth works & Embankment	30-Jun-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0051-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 1+000 to STA:1+239.64	24.00	2,901.29	100%	24.00	69,630.96
34	B1.31 23 16.01	Excavation (all types of soil)	8-Sep-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0052-02	Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgarde of road at Station Road RD-02, STA: 0+340 to STA:0+500	24.00	118.65	25%	6.00	711.90
35	B1 .31 23 23.01	Earth works & Embankment	1-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0053-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+850 to STA: 1+000	24.00	2,143.65	100%	24.00	51,447.60
36	B1 .31 23 23.01	Earth works & Embankment	4-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0055-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 1+000 to STA:1+200	24.00	2,569.79	100%	24.00	61,674.96
37	B1 .31 23 23.01	Earth works & Embankment	4-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0056-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 1+200 to STA:1+350	24.00	1,024.89	100%	24.00	24,597.36
38	B1 .31 23 23.01	Earth works & Embankment	22-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0057-00	Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road \ Carriage-way RD-02, STA: 0+730 to STA:0+840 (Bottom subgrade)	24.00	234.51	100%	24.00	5,628.24
39	B1 .31 23 23.01	Earth works & Embankment	4-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0058-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 0+600 to STA:0+700	24.00	1,290.07	100%	24.00	30,961.68

Data sensitivity - Internal

SL NO	BOQ Item #	BOQ Description	Date	FIR #	FIR Description	Unit Rate	Current Period Quantity	% Claim	Unite rate as per claim	Total (SR)
40	B1 .31 23 23.01	Earth works & Embankment	4-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0059-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 0+120 to STA: 0+300 (Bottom Subgrade)	24.00	2,301.88	100%	24.00	55,245.12
41	B1 .31 23 23.01	Earth works & Embankment	5-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0060-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 0+880 to STA:1+000	24.00	938.22	100%	24.00	22,517.28
42	B1 .31 23 23.01	Earth works & Embankment	6-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0061-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 0+300 to STA: 0+500 (Bottom Subgrade)	24.00	2,334.35	100%	24.00	56,024.40
43	B1 .31 23 23.01	Earth works & Embankment	6-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0062-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+500 to STA:0+700 (Bottom Subgrade)	24.00	3,250.21	100%	24.00	78,005.04
44	B1 .31 23 16.01	Earth works & Excavation / Cutting	6-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0063-00	Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgarde for Station Road RD-02, STA: 0+000 to STA:0+160	24.00	1,335.84	100%	24.00	32,060.16
45	B1 .31 23 23.01	Earth works & Embankment	7-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0064-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+700 to STA:0+850 (Bottom Subgrade)	24.00	2,062.86	100%	24.00	49,508.64
46	B1 .31 23 16.01	Earth works & Excavation/cutting (all types of soil)	22-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0065-00	Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade for Station Road\ Carriage-way RD-02, STA: 0+730 to STA:0+840	24.00	515.37	25%	6.00	3,092.22
47	B1 .31 23 23.01	Earth works & Embankment	7-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0066-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 1+000 to STA: 1+200 (Bottom Subgrade)	24.00	2,348.09	100%	24.00	56,354.16
48	B1 .31 23 23.01	Earth works & Embankment	8-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0067-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 1+200 to STA: 1+350 (Bottom Subgrade)	24.00	1,209.65	100%	24.00	29,031.60
49	B1 .31 23 23.01	Earth works & Embankment	13-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0068-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 1+110 to STA:1+239.64 (Bottom sub grade)	24.00	1,033.00	100%	24.00	24,792.00
50	B1 .31 23 23.01	Earth works & Embankment	13-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0069-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 1+000 to STA:1+110	24.00	1,219.05	100%	24.00	29,257.20
51	B1 .31 23 23.01	Earth works & Embankment	13-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0070-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 0+880 to STA:1+000	24.00	1,443.25	100%	24.00	34,638.00
52	B1 .31 23 16.01	Earthwork & Excavation / Cutting	23-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0072-00	Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade for shoulders (left and right side) at Station Road RD-02, STA: 0+730 to STA:0+840	24.00	276.36	100%	24.00	6,632.64
53	B1 .31 23 16.01	Earth works & Embankment	23-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0073-00	Check Coordinates and bottom level Road Filling and compaction test of bottom Sub-Grade of shoulders (left and right side) at Road # RD-02 STA: 0+730	24.00	1,024.52	100%	24.00	24,588.48
54	B1 .31 23 23.01	Earth works & Embankment	27-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0074-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-02, STA: 1+030 to STA:1+110 (Bottom Sub grade)	24.00	739.52	100%	24.00	17,748.48
55	B1 .31 23 23.01	Earth works & Embankment	28-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0075-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer (Road and shoulders) for Station Road RD-02, STA: 0+880 to STA:1+030	24.00	1,687.63	100%	24.00	40,503.12
56	B1 .31 23 16.01	Earth works & Embankment	29-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0076-00	Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade of road at Station Road RD-02, STA: 0+160 to STA:0+340	24.00	183.94	100%	24.00	4,414.56
57	B1 .31 23 23.01	Earth works & Embankment	29-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0077-00	Check Coordinates and bottom level Road Filling and compaction test of bottom Sub-Grade of Road/Carriageway at Road # RD-02 STA: 0+160 to STA: 0+340	24.00	420.30	100%	24.00	10,087.20
58	B1 .31 23 16.01	Earth works & Embankment	29-Jul-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0078-00	Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade of road at Station Road RD-01, STA: 1+850 to STA:1+914.20	24.00	327.47	100%	24.00	7,859.28
59	B1 .31 23 23.01	Earth works & Embankment	1-Aug-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0080-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 0+840 to STA:0+880	24.00	475.30	100%	24.00	11,407.20
60	B1 .31 23 23.01	Earth works & Embankment	5-Aug-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0081-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 0+600 to STA:0+700	24.00	1,191.58	100%	24.00	28,597.92
61	B1 .31 23 23.01	Earth works & Embankment	5-Aug-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0083-00	Check Coordinates level and Compaction F.D.T for Embankment Bottom Subgrade layer for Station Road RD-01, STA: 1+700 to STA:1+850	24.00	3,527.28	100%	24.00	84,654.72
62	B1 .31 23 23.01	Earth works & Embankment	5-Aug-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0084-00	Check Coordinates level and Compaction F.D.T for Embankment3rd layer for Station Road RD-02, STA: 0+510 to STA:0+600	24.00	1,181.28	100%	24.00	28,350.72
63	B1 .31 23 23.01	Earth works & Embankment	10-Aug-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0090-00	Check Coordinates level and Compaction F.D.T for Embankment 6th layer (Road and shoulders) for Station Road RD-02, STA: 0+840 to STA:1+030 (Botto	24.00	1,632.57	100%	24.00	39,181.68
64	B1 .31 23 23.01	Earth works & Embankment	15-Aug-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0096-00	Check Coordinates level and Compaction F.D.T for Embankment Bottom Subgrade layer for Station Road RD-02, STA: 0+500 to STA:0+730	24.00	2,707.85	100%	24.00	64,988.40
65	B1 .31 23 23.01	Earth works & Embankment/Fill	3-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0099-02	Check Coordinates and bottom level Road Filling and compaction test of bottom Sub-Grade of Road/Carriageway at Road # RD-02 STA: 0+340 to STA: 0+	18.00	761.53	10%	1.80	1,370.75
66	B1 33 71 00 02 01	Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm)	22-Aug-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0100-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 05 To Manhole 06 for Street Lightin	1,617.00	57.90	25%	404.25	23,406.08
67	B1 33 71 00 02 01	Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm)	22-Aug-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0101-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 03 To Manhole 04 for Street Lightin	1,617.00	13.00	25%	404.25	5,255.25
68	B1 33 71 00 02 01	Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm)	22-Aug-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0102-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 07 To Manhole 08 for Street Lightin	1,617.00	13.00	25%	404.25	5,255.25
69	B2.33 71 00 02.02	Road Crossing Duct for Street Lighting cables UPVC (4xØ110mm)	23-Aug-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0105-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (4X110mm) from Manhole 01 To Manhole 02 for Street Lightin	525.00	9.05	25%	131.25	1,187.81
70	B2.33 71 00 02.02	Road Crossing Duct for Street Lighting cables UPVC (4xØ110mm)	23-Aug-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0106-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (4X110mm) from Manhole 09 To Manhole 10 for Street Lightin	525.00	9.05	25%	131.25	1,187.81
71	B2.33 71 00 02.01	Road Crossing Duct for Street Lighting cables UPVC (4xØ110mm)	23-Aug-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0107-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 11 To Manhole 12 for Street Lightin	327.00	15.90	45%	147.15	2,339.69
72	B2.1.33 81 26.06	Road crossing ducts, (6*50mm) HDPE	23-Aug-26	SUD1-05-018-TDC-TS9-1-TEL-FIR-0108-00	Check levels, Laying polyethylene sheet, Form work and concrete pouring for TELECOMMUNICATIONS Works Duct Bank for HDPE Pipe 3(2X50mm) From	124.00	40.61	25%	31.00	1,258.91
73	B3.33 14 13.01	Potable Water Network: 75mm Diameter (Depth: 0.0m - 1.5m)	31-Aug-26	SUD1-05-018-TDC-TS9-1-PW-FIR-0109-00	Check Coordinates level and Excavation width Bottom level and compaction for potable water pipeline from Station ST: 0+250 to ST: 1+900 #RD-02	106.00	1,650.00	5%	5.30	8,745.00
74	B4.33 31 23.01	Sewarage Network: HDPE force main110 mm diameter (Depth: 0- 1.5m)	27-Aug-26	SUD1-05-018-TDC-TS9-1-SEW-FIR-0110-00	Check Coordinates level and Excavation width Bottom level and compaction for Sewerage pipeline trench from Station ST: 1+060 to ST: 2+625 #RD-01	143.00	1,565.00	10%	14.30	22,379.50
75	B5.33.42.13.01	Storm Water Network: Concrete pipe culverts (900mm) Diameter	6-Sep-26	SUD1-05-018-TDC-TS9-1-STR-FIR-0111-00	Check Coordinates level and Excavation width Bottom level and compaction for Precast concrete pipe culvert (900mm) diameter at #RD-01	1,018.00	195.00	10%	101.80	19,851.00
76	B1.31 23 23.01	Earth works & Embankment/Fill	14-Sep-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0114-00	Check Coordinates and bottom level Road Filling and compaction test of Median Island 1st layer at Road # RD-01 STA: 1+500 to STA: 1+850	24.00	285.60	10%	2.40	685.44
77	B1.31 23 23.01	Earth works & Embankment	14-Sep-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0115-00	Check Coordinates level and Compaction F.D.T for Embankment 1st layer from St:0+000 to 0+062.93 Parking Station Road	24.00	4,750.08	100%	24.00	114,001.92
78	B1.31 23 23.01	Earth works & Embankment	19-Sep-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0116-00	Check Coordinates level and Compaction F.D.T for Embankment 2nd layer from St:0+000 to 0+062.93 Parking Station Road	24.00	1,105.46	100%	24.00	26,531.04

Data sensitivity - Internal

SL NO	BOQ Item #	BOQ Description	Date	FIR #	FIR Description	Unit Rate	Current Pariod Quantity	% Claim	Unite rate as per claim	Total (SR)
79	B5.33 42 13.01	Storm Water Network: Concrete pipe culverts (900mm) Diameter	24-Sep-26	SUD1-05-018-TDC-TS9-1-STR-FIR-0117-00	Check Pipe installation of Precast concrete pipe culvert (900mm) diameter at #RD-01	1,018.00	195.00	30%	305.40	59,553.00
80	B1 31 23 23 01	Check Installation Manhole MH-18 for TELECOMMUNICATIONS Works in Road COL-MC10	29-Sep-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0123-00	Check Coordinates level and Compaction F.D.T for Embankment 3rd layer from St:0+000 to 0+062.93 Parking Station Road	5,939.00	1,185.51	0%	-	-
81	B2.1.33 81 26.04	Earth works & Embankment	7-Oct-26	SUD1-05-018-TDC-TS9-1-TEL-FIR-0124-01	Check Installation Manhole MH-18 for TELECOMMUNICATIONS Works in Road COL-MC10	24.00	1.00	100%	24.00	24.00
82	B2.1.33 81 26.03	Check Installation Manhole MH-11 & MH-12 & MH-15 & MH-16 & MH-17 for TELECOMMUNICATIONS Works in Road COL-MC10	30-Sep-26	SUD1-05-018-TDC-TS9-1-TEL-FIR-0125-00	Check Installation Manhole MH-11 & MH-12 & MH-15 & MH-16 & MH-17 for TELECOMMUNICATIONS Works in Road COL-MC10 & RD-01	5,811.00	5.00	30%	1,743.30	8,716.50
83	B1 32 11 13 01	Subgrade	30-Sep-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0127-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+150 to STA: 0+650(Left side)	36.00	1,312.50	10%	3.60	4,725.00
84	B2.26 05 19.01	4Cx 6mm2 + 1Cx6mm2 Cu/XLPE/SWA/PVC	30-Sep-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0128-00	Check Sand Bedding and Laying of U/G LV Cables (4Cx6+6E) for Bollard Lighting Network in landscape Area near Modon Office	24.00	2,200.00	45%	10.80	23,760.00
85	B5.33 42 13.05	Storm Water Network: Concrete pipe culverts	4-Oct-26	SUD1-05-018-TDC-TS9-1-STR-FIR-0131-00	Check Steel Reinforcement and concrete pouring for Base slab	29,950.00	2.00	25%	7,487.50	14,975.00
86	B1.31 23 23.01	Earth works & Embankment	5-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0134-00	Check Coordinates level and Compaction F.D.T for Embankment 4th layer from St:0+000 to 0+062.93 Parking Station Road	24.00	1,236.30	100%	24.00	29,671.20
87	B1.32 11 13.01	Subgrade	6-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0135-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+650 to STA: 0+900 (left side)	36.00	656.25	10%	3.60	2,362.50
88	B1.32 11 13.01	Subgrade	6-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0137-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+900 to STA: 1+200 (left side)	36.00	787.50	10%	3.60	2,835.00
89	B2.1.33 81 26.03	Manhole Type 1	7-Oct-26	SUD1-05-018-TDC-TS9-1-TEL-FIR-0138-00	Check Installation Manhole MH-03 & MH-04 & MH-07 & MH-08 & MH-09 & MH-10 for TELECOMMUNICATIONS Works in Road RD-01& RD-02	5,811.00	6.00	25%	1,452.75	8,716.50
90	B2.1.33 81 26.04	Manhole Type 2	8-Oct-26	SUD1-05-018-TDC-TS9-1-TEL-FIR-0139-00	Check Installation Manhole MH-02 & MH-05 & MH-06 & MH-14 for TELECOMMUNICATIONS Works in Road COL-MC10 & RD-02	5,939.00	4.00	25%	1,484.75	5,939.00
91	B1.32 11 13.01	Subgrade	10-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0140-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 1+200 to STA: 1+500 (Left side)	36.00	787.50	10%	3.60	2,835.00
92	B1.32 11 13.01	Subgrade	10-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0141-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 1+500 to STA: 1+850 (Left side)	36.00	918.75	10%	3.60	3,307.50
93	B1.32 11 23.01	Aggregate Base Courses	11-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0142-01	Check Coordinates level and compaction F.D.T for (Aggregate base course) at Road /Carriageway# RD-01 STA: 0+170 to STA: 0+650(Left Side)	66.00	840.00	10%	6.60	5,544.00
94	B1.31 23 23.01	Earth works & Embankment	12-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0143-00	Check Coordinates level and Compaction F.D.T for Embankment 5th layer from St:0+000 to 0+062.93 Parking Station Road	24.00	1,515.03	100%	24.00	36,360.72
95	B5.33 42 13.01	Storm Water Network: Concrete pipe culverts (900mm) Diameter	14-Oct-26	SUD1-05-018-TDC-TS9-1-STR-FIR-0144-00	Check Concrete pouring on top of Precast concrete pipe culvert (900mm) diameter at #RD-01	1,018.00	195.00	25%	254.50	49,627.50
96	B5.33 42 13.05	Storm Water Network: Concrete pipe culverts	14-Oct-26	SUD1-05-018-TDC-TS9-1-STR-FIR-0145-00	Check Steel Reinforcement and concrete pouring for wing walls, and headwall of Outlet and inlet structures	29,950.00	2.00	25%	7,487.50	14,975.00
97	B1.32 11 23.01	Aggregate Base Courses	14-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0148-00	Check Coordinates level and compaction F.D.T for (Aggregate base course) at Road /Carriageway# RD-01 STA: 0+650 to STA: 1+200(Left Side)	66.00	962.50	10%	6.60	6,352.50
98	B1.32 11 13.01	Subgrade	14-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0149-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+160 to STA: 0+650 (Right side)	36.00	1,312.50	10%	3.60	4,725.00
99	B3.33 14 13.01	Potable Water Network: 75mm Diameter (Depth: 0.0m - 1.5m)	17-Oct-26	SUD1-05-018-TDC-TS9-1-PW-FIR-0150-00	Check Coordinates level and Excavation width Bottom level and compaction for potable water pipeline from Station ST: 2+350 to ST: 2+725 #RD-02	106.00	375.00	5%	5.30	1,987.50
100	B1.32 11 26.01	BITUMINOUS BASE COURSE	17-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0151-00	Check Coordinates, level, thickness, Compaction and Testing for Bituminous base course 1st layer (80mm) on Road /Carriageway from STA:0+170 to STA	533.00	266.00	10%	53.30	14,177.80
101	B1.32 11 13.01	Subgrade	18-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0152-00	Check Compaction F.D.T for (Subgrade) 1st layer at Road /Carriageway # RD-02 STA: 0+760 to STA: 1+240 (Right & left side)	36.00		10%	3.60	-
102	B1.32 11 13.01	Subgrade	19-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0153-00	Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway# RD-01 STA: 0+650 to STA: 0+950 (Right side)	36.00	787.50	10%	3.60	2,835.00
103	B3.33 14 13.01	Potable Water Network: 75mm Diameter (Depth: 0.0m - 1.5m)	20-Oct-26	SUD1-05-018-TDC-TS9-1-PW-FIR-0154-00	Check Sand bedding and pipe installation of potable water HDPEPipes (Diameter 75mm) from Station ST: 0+275 to ST: 1+900 #RD-01	106.00	1,625.00	5%	5.30	8,612.50
104	B1.31 23 23.01	Earth works & Embankment	21-Oct-26	SUD1-05-018-TDC-TS9-1-ROD-FIR-0155-00	Check Coordinates level and Compaction F.D.T for Embankment 6th layer from St:0+000 to 0+062.93 Parking Station Road	24.00	1,009.58	100%	24.00	24,229.92
105	B5.33 42 13.01	Storm Water Network: Concrete pipe culverts (900mm) Diameter	7-Oct-26	SUD1-05-018-TDC-TS9-1-STR-FIR-0156-00	Installation of polyethylene sheet beneath the reinforcement prior to Concrete casting of pipe culvert	1,018.00		25%	254.50	-
106	B1 33 71 00 02 01	Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm)	20-Oct-26	SUD1-05-018-TDC-TS9-1-LIT-FIR-0157-00	Application for Bituminous coating for concrete encased duct bank prior to Backfilling at # RD-02	1,617.00		25%	404.25	-
									-	-
									-	-
									-	-
										3,923,633.37

Data sensitivity - Internal

PROCUREMENT

Sr. NO.	Project ID	ACT#inP6	Item Description	Discipline	(Long \Short) Lead Items	BOQ. No.	Unit	Quantity	Proc. Qty	Required P.O Date	Method of Shipping	Required on Job	E.D.A. to Site	A.D.A. to Site	Lead Time	Approval Status	The Impact (BOQ Cost)	Completion Rate	Remarks
1	SUD1-05-018	SDR-ST-PRO-S-1010	Waterproofing (Thermal & moisture Protection)	Civil	Short Lead Items	07 00 00	m2	910	910	10-Aug-26	Local trancport	Civil	4-Sep-26	4-Nov-26	25	Approved	-	-	
2	SUD1-05-018	SDR-ST-PRO-S-1030	Interlock	Civil	Short Lead Items	33 42 16	m2	27900	27900	2-Sep-26	Local trancport	Civil	28-Sep-26	19-Nov-26	26	Approved	-	-	on going
3	SUD1-05-018	SDR-ST-PRO-S-1060	Kerbstone	Civil	Short Lead Items	32 11 26	m	20555	20555	3-Sep-26	Local trancport	Civil	17-Sep-26	17-Nov-26	14	Approved	-	1.40	on going
4	SUD1-05-018	SDR-ST-PRO-S-1260	Steel Bars	Civil	Short Lead Items	05 12 00	Unit	1	1	1-Jun-26	Local trancport	Civil	22-Jul-26	20-Sep-26	51	Approved	-	90%	on going
5	SUD1-05-018	SDR-ST-PRO-S-1270	Asphalt	Civil	Short Lead Items	32 12 16	m3	3420	3420	27-Oct-26	Local trancport	Civil	10-Nov-26	9-Feb-27	14	Approved	-	4.30%	on going
6	SUD1-05-018	SDR-ST-PRO-S-1140	LOW VOLTAGE CABLES	Electrical	Short Lead Items	33 71 00 02	m	695	695	31-Aug-26	Local trancport	Civil	11-Sep-26	11-Oct-26	11	Approved	-	100%	Delivered
7	SUD1-05-018	SDR-ST-PRO-S-1150	LOW VOLTAGE DISTRIBUTION Panel	Electrical	Short Lead Items	33 71 26	Unit	1	1	28-Aug-26	Local trancport	Civil	18-Sep-26	18-Nov-26	32	Approved	-	-	on going
8	SUD1-05-018	SDR-ST-PRO-S-1160	STREET LIGHTING FEEDER Panel	Electrical	Short Lead Items	33 71 26 03	Unit	2	2	7-Sep-26	Local trancport	Civil	21-Sep-26	1-Nov-26	14	Approved	-	-	on going
9	SUD1-05-018	SDR-ST-PRO-S-1170	STREET LIGHTING CABLES	Electrical	Short Lead Items	33 71 00 01	Unit	6800	6800	31-Aug-26	Local trancport	Civil	14-Sep-26	14-Nov-26	14	Approved	-	100%	Delivered
10	SUD1-05-018	SDR-ST-PRO-S-1200	ROAD CROSSING DUCTS Ø110mm	Electrical	Short Lead Items	33 81 26	Unit	104	104	18-Aug-26	Local trancport	Civil	28-Sep-26	2-Nov-26	19	Approved	-	100%	Delivered
12	SUD1-05-018	SDR-ST-PRO-S-1230	CCTV :5MP IP PoE Bullet Camera	Electrical	Short Lead Items	B2.28.20.00.01	unit	16	16	1-Sep-26	Local trancport	Electrical	17-Sep-26	28-Oct-26	16	Approved	-	-	on going
13	SUD1-05-018	SDR-ST-PRO-S-1240	CCTV :Pole mounted Filed Equipment cabinet (FE	Electrical	Short Lead Items	B2.28.20.00.02	unit	4	4	26-Oct-26	Local trancport	Electrical	6-Nov-26	5-Jan-27	11	Approved	-	-	on going
14	SUD1-05-018	SDR-ST-PRO-S-1250	VOICE EVACUATION SYSTEM	Electrical	Short Lead Items	27 40 00	Unit	32	32	29-Oct-26	Local trancport	Electrical	11-Nov-26	10-Jan-27	13	Approved	-	-	on going
15	SUD1-05-018	SDR-ST-PRO-S-1040	HDPE PIPES & FITTINGS	Mechanical	Short Lead Items	33 31 23	m	2946	2946	24-Aug-26	Local trancport	Electrical	18-Sep-26	18-Nov-26	25	Approved	-	100%	Delivered
16	SUD1-05-018	SDR-ST-PRO-S-1050	CONCRETE PIPES AND FITTINGS	Mechanical	Short Lead Items	33 42 13	m	230	230	7-Sep-26	Local trancport	Electrical	18-Sep-26	7-Dec-26	11	Approved	-	100%	Delivered
19	SUD1-05-018	SDR-ST-PRO-S-1090	MANHOLE, CATCH BASIN & VALVE BOX COVER	Mechanical	Short Lead Items	33 81 26	Unit	16	16	14-Sep-26	Local trancport	Electrical	28-Sep-26	7-Dec-26	14	Approved	-	-	
20	SUD1-05-018	SDR-ST-PRO-S-1000	Metal railing for platform	Civil	Long Lead Items	05 52 00	m	440	440	25-Aug-26	Local trancport	Electrical	28-Oct-26	2-Feb-27	64	Not submitted	-	-	
21	SUD1-05-018	SDR-ST-PRO-S-1020	Canopy	Civil	Long Lead Items	03 30 00/03 53 00	560	m2	m2	19-Nov-26	Local trancport	Mechanical	22-Dec-26	8-Apr-27	33	Not submitted	-	-	
22	SUD1-05-018	SDR-ST-PRO-S-1110	MEDIUM VOLTAGE CABLES DUCT BANKS	Electrical	Long Lead Items	33 71 00	m	105	105	12-Oct-26	Local trancport	Mechanical	29-Oct-26	14-Feb-27	17	Not submitted	-	-	
23	SUD1-05-018	SDR-ST-PRO-S-1120	MEDIUM VOLTAGE CABLES	Electrical	Long Lead Items	33 71 49.23	Unit	7120	7120	12-Oct-26	Local trancport	Mechanical	30-Oct-26	15-Feb-27	18	Not submitted	-	-	
24	SUD1-05-018	SDR-ST-PRO-S-1130	SUB-STATION	Electrical	Long Lead Items	33 73 00	unit	2	2	19-Oct-26	Local trancport	Mechanical	3-Dec-26	4-Mar-27	45	Not submitted	-	-	
25	SUD1-05-018	SDR-ST-PRO-S-1180	LIGHTING POLES	Electrical	Long Lead Items	33 71 16	m	143	143	19-Oct-26	Local trancport	Mechanical	5-Nov-26	27-Feb-27	17	Not submitted	-	-	
26	SUD1-05-018	SDR-ST-PRO-S-1190	STREET LIGHTING LUMINAIRE	Electrical	Long Lead Items	26 56 19	Unit	276	276	10-Nov-26	Local trancport	Civil	18-Dec-26	25-Mar-27	38	Not submitted	-	-	
27	SUD1-05-018	SDR-ST-PRO-S-1220	Outdoor Lighting Fixtures	Electrical	Long Lead Items	26 56 00	Unit	390	390	23-Nov-26	Local trancport	Civil	10-Dec-26	11-Apr-27	17	Not submitted	-	-	
28	SUD1-05-018	SDR-ST-PRO-S-1100	WASHOUT & AIR VALVE, GATE VALVE, BUTTERFLY VALVE	Mechanical	Long Lead Items	33 14 19	Unit	5	5	26-Oct-26	Local trancport	Electrical	8-Dec-26	25-Mar-27	43	Approved	-	-	on going


Data sensitivity - Internal

Head-Count (Non Manual)

MONTHS	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26	Oct-26	Nov-26	Dec-26	Jan-27	Feb-27	Mar-27	Apr-27	May-27	Jun-27	Jul-27	Aug-27
Plan - Monthly	12	16	20	29	30	30	32	32	32	30	28	24	21	20	19	21	15
Planned - Cumulative	12	24	40	60	89	119	149	181	213	245	275	303	327	348	368	387	408
Actual - Monthly	12	16	16	16	22	16	22										
Actual Cumulative	12	28	44	60	82	98	120										
Forecast - Monthly																	
Saudi Monthly - Actual																	

Head-Count (Manual)

MONTHS	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26	Oct-26	Nov-26	Dec-26	Jan-27	Feb-27	Mar-27	Apr-27	May-27	Jun-27	Jul-27	Aug-27
Plan - Monthly	18	30	36	41	47	123	185	200	231	226	219	204	203	136	137	106	7
Planned - Cumulative	18	48	84	125	172	295	480	680	911	1137	1356	1560	1762	1898	2036	2141	2148
Actual - Monthly	41	48	62	65	31	31	65										
Actual Cumulative	41	89	151	216	247	278	343										
Forecast - Monthly																	
Saudi - Actual																	

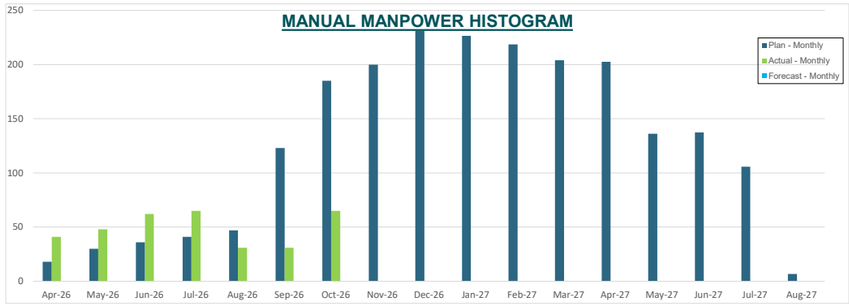

0

Head-Count (Non-Manual)				
Planned	Actual	Variance	Forecast Next Month	Saudi Staff
20	22	2	0	3

Head-Count (Manual)				
Planned	Actual	Variance	Forecast Next Month	Saudi Staff
40	65	25	0	0


Month	Oct-26	Nov-26

Man Power by Trade										
Key Trade	Engineer	Doc. Controller	Proc. Team	Foreman	Draftman	Driver	UnSkilled Labor	Skiled labour	Others	**Total**
Plan	2	1	1	2	1	5	15	8	5	40
Actual	10	1	1	3	1	31	20	10	10	87

Equipment

MONTHS	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26	Oct-26	Nov-26	Dec-26	Jan-27	Feb-27	Mar-27	Apr-27	May-27	Jun-27	Jul-27	Aug-27
Plan - Monthly	0	6	6	22	29	48	57	62	46	31	15	14	10	9	8	0	0
Planned - Cumulative	0	6	13	19	41	70	118	174	236	282	314	329	342	352	361	369	369
Actual - Monthly	0	6	14	17	32	18	32										
Actual Cumulative	0	6	20	37	69	87	119										
Forecast - Monthly																	

Equipment Count				
Planned	Actual	Idle	Variance	Forecast Next Month
29	32	0	3	0

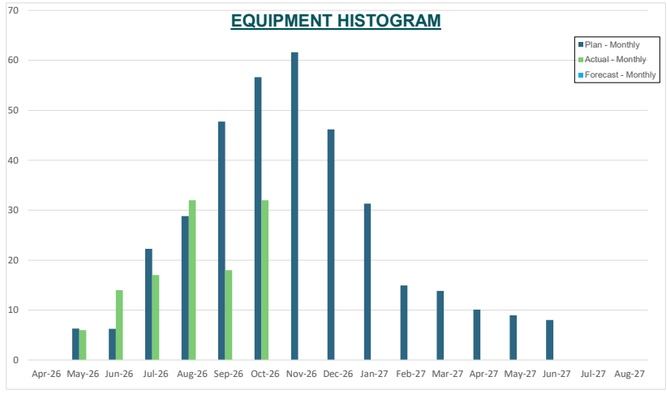

Type	Pick Up/Car	Bus	Dump Truck	Boom Truck	Generator	CRANE	Showel	Grader	Truck	Water Tank	Finisher	Bobcat	Forklift	JCB	Loader	Boom Truck	Road Marker	Total
Plan	1	1	10	0	1	0	0	6	0	0	0	0	0	0	1	2	0	22
Actual	2	1	10	0	1	1	1	5	0	2	0	0	0	0	0	0	0	23
Idle																		0

Data sensitivity - Internal

Issue Log

Issue ID	Parent Project ID	Contract / Project ID	Project Name	City	Region	Fund Source	Phase	PM / Owner	Contractor / Designer	Current Status	Description	Priority	Action Required	Date Raised	Status	Duration Elapsed	Expected/Actual Closure	Target Date
3120-1	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Access & Permits	Egis / MODON	Technical Development Company for	Close	Noticed a signboard that is fallen and improperly positioned on the ground	Contractor	Assess the damage: Evaluate whether the sign can be repaired and	2-Sep-26	Closed	1	2	2-Sep-26
3120-2	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Design / Engineering	Egis / MODON	Technical Development Company for	Close	Waste plastic bottles were scattered on-site, resulting in poor housekeeping.	Contractor	Informed the workgroup about the concern to clean up the area immediately,	4-Sep-26	Closed	1	2	4-Sep-26
3120-3	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	A new water filter was installed to ensure clean drinking water.	Contractor	GOOD PRACTICE	6-Sep-26	Closed	1	2	6-Sep-26
3120-4	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	It was observed that the subcontractor was carrying out pipe-shifting activities using a wheel loader.	Contractor	Stop Work: Issue an immediate Stop Work Order to halt the pipe-	8-Sep-26	Closed	1	2	8-Sep-26
3120-5	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Concrete barriers were misplaced in the area	Contractor/HSE Team	Use appropriate heavy lifting equipment (such as a Boomtruck) to move the	9-Sep-26	Closed	1	2	9-Sep-26
3120-6	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Dust created by vehicles moving on project routes	Contractor	Water spraying on vehiceles routes on regular basis	20-Sep-26	Closed	1	2	20-Sep-26
3120-7	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Unavaiilibilty of shaded cold water station	Contractor/HSE Team	Provision of shaded cold water station to the site workers.	20-Sep-26	Closed	1	2	20-Sep-26
3120-8	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Shallow excavation found without safety and warning signages	Contractor/HSE Team	posting warning and safety signages to increase the visibility and awareness	24-Sep-26	Closed	1	2	24-Sep-26
3120-9	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Workers found in equipment working zone	Contractor/HSE Team	Stop movement in man machine/ equioment interface and segrete	24-Sep-26	Closed	1	2	24-Sep-26
3120-10	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Directional signages along with concrete jersey barriers and warning signages and tape were found missing	Contractor HSE team	Directional signages along with concrete jersey barriers and warning tape	3-Oct-26	Closed	1	2	3-Oct-26
3120-11	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Equipment operator found working zone with Non-compalince to site mandatory PPE.	Contractor consruction /HSE Team	it was ensure to wear the mandatory PPE all the time when present on site	3-Oct-26	Closed	1	2	3-Oct-26
3120-12	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Observe Hot Work activity without proper control measure Fire safety	Contractor HSE team	Provide Fire Extinguisher and other requirements as per Hot work requirements.	10-Oct-26	Closed	1	2	10-Oct-26
3120-13	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Observe site without mandatory PPE complaince	Contractor consruction /HSE Team	Wear the mandatory PPE all the time when present on site	11-Oct-26	Closed	1	2	11-Oct-26
3120-14	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Observe dust created at temporary vehicles roads due insuffient dust control measures.	Contractor HSE team	Ensure dust control by regular spraying of water on vehicles routes	18-Oct-26	Closed	1	2	18-Oct-26
3120-15	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Observe non complaince of mandatory PPE by equipment operators	Contractor consruction /HSE Team	Wear the mandatory PPE all the time by equipment operators when present on site	17-Oct-26	Closed	1	2	17-Oct-26
3120-16	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Observe some shallow excavations areas with edge protection.	Contractor HSE team	Provide proper barricade and warning signages	25-Oct-26	Closed	1	2	25-Oct-26
3120-17	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for	Close	Observe non complaince of mandatory PPE by equipment operators	Contractor consruction /HSE Team	Wear the mandatory PPE all the time by equipment operators when present on	25-Oct-26	Closed	1	2	25-Oct-26

Data sensitivity - Internal

Risk Log

Risk ID	Parent Project ID	Contract / Project ID	Project Name	City	Region	Fund Source	Phase	PM / Owner	Contractor / Designer	Current Status	Category	Risk Title	Description	Evidence / Data	Probability (1-5)	Impact (1-5)	Score	Rating	Mitigation Plan	Date Identified	Status	Target Date	Notes / Updates	Source
3120-1	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Access & Permits	Egis / MODON	Technical Development Company for Contracting	Open	Permits/Stakeholder	Pending SAR Fence Permission Affecting Platform and Canopy Works	The required SAR/fence permission to commence the works inside the designated platform area is still pending. As a result, the Contractor is unable to commence the platform and associated	Canopy and platform design/details not received from Client; related shop drawings cannot be finalized; associated procurement and construction activities are dependent on the required	5	5	25	Very High	Expedite the SAR/fence permission through the Client and relevant authorities. Escalate the matter to project	16/9/2026	Open		SAR/fence permission remains outstanding. Platform and canopy works cannot commence until the required permission is obtained. Continued delay may affect the planned	SAR/Fence Permission Correspondence, Client Instructions, RFI/Approval Register, Site Records, Project
3120-2	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Design / Engineering	Egis / MODON	Technical Development Company for Contracting	Open	Design/Technical	Outstanding Canopy and Platform Design Affecting Shop Drawing, Procurement and Construction	The required design/details for the canopy and platform have not yet been provided by the Client. The outstanding design	Canopy and platform design/details not received from Client; related shop drawings cannot be finalized; associated procurement and	5	5	25	Very High	Immediately escalate the outstanding design requirement to the Client/Consultant	16/9/2026	Open		Project is currently ahead of schedule; however, the Client's outstanding canopy and platform design is affecting the finalization of	Client/Consultant Correspondence, RFI, Design/Submittal Register, Shop
3120-3	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Open	Interface/Utilities	Delay in Client Approval for MV Duct Crossings Affecting MV Cable Installation	Client approval is required for the proposed MV duct crossings. If approval is not obtained within the desired	MV duct crossing proposal/submission pending Client approval; MV cable installation is dependent on	4	4	16	High	Expedite Client review and approval of the MV duct crossing proposal.	16/9/2026	Open		Project is currently ahead of schedule. However, pending Client approval for MV duct crossings may	MV Duct Crossing Proposal / Client Correspondence / RFI or Technical
3120-4	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Open	Authorities / Permits	Delay is receviengSAR Permit	Affecting Geo technical Report ,Shop Drawing and Backfilling work	Delay in completion date	4	4	16	High		2026-05-05	Close	2026-06-05		
3120-5	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Open	Authorities / Permits	Delay is receviengTender drawing for platform	Structure Drawing for Platform	Delay in completion date	3	3	12	M12		2026-05-05	Close	2026-06-05		
3120-6	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Visibility is low due to strong winds and dust.	Vehicle and machinery collisions, falls from high places, and breathing problems.	Severe site hazards, including vehicle and machinery collisions, respiratory damage from inhaled particles, and	3	3	12	M12		2026-08-04	Close	2026-08-04	Suspending high-risk tasks, controlling vehicle movement, and protecting workers.	
3120-7	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Found a damaged fire extinguisher in the site office area.	May fail during a fire, can leak harmful chemicals or gas, and it can burst or fly apart.	Complete equipment failure during a fire, sudden rupture or explosion of the pressurized metal container, and delayed evacuation or severe personal injury	2	2	10	L4		2026-08-05	Close	2026-08-05	Finding a damaged fire extinguisher requires immediate removal, clear tagging, and professional servicing	
3120-8	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	It was observed that diesel is being stored in plastic containers.	Chemical Breakdown and Leaks, Fuel Contamination, Environmental Spills and Exposure. Fire hazard	Health Risks, Equipment Failure	2	2	10	L4		2026-09-08	Close	2026-09-08	Immediate transfer of the diesel into approved containers and the systematic neutralization of microbial risks	
3120-9	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Due to sand storm dust accumulated and poor visibility on site	Visibility & Safety Hazards, Acute Health Risks, Equipment & Asset Damage	Immediate On-Site Consequences (Due to Poor Visibility), Physical Consequences (Due to Accumulated Dust, Health Hazards for Site Personnel,	2	2	10	L4		2026-09-09	Close	2026-09-09	Halt All Mobile Operations: Order an immediate stop to all heavy equipment operation, crane lifting, and vehicle transit. Poor visibility makes navigating the site blind and	
3120-10	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Dust created by vehicles moving on project routes	Visibility & Safety Hazards, Acute Health Risks, Equipment & Asset Damage	Health Issues (repiratory), Equipment collision due low visibility	3	3	12	M8		2026-09-20	Close	2026-09-20	Regular water spraying on vehicle routes	
3120-11	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Shade not available for drinking water	Heat Stress to workers on site due improper arrangement of cold water stations.	Heat stress and heat stroke to workers as workers	3	3	12	M8		2026-09-20	Close	2026-09-20	Shaded water station so that water remains cold for long duration for site workers.	
3120-12	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Shallow excavation found without safety and warning signages	Visibility & Safety Hazards which could lead in workers and equipment fall in to excavation.	Peronsal injuries and equipment damages	4	4	25	Very High		2026-09-24	Close	2026-09-24	posting warning and safety signages to increase the visibility and awareness about riks.	
3120-13	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Workers found in equipment working zone	Workers working in machine /equipment working zone are exposed to hit/ struck by the moving machine/ equipment.	Peronal injuries from minor to critical injuries and fatalities	5	5	25	Very High		2026-09-24	Close	2026-09-24	Stop movement in man machine/ equiomnt interface and segrete equipment and man working areas.	
3120-14	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	directional signages along with concrete jersey barriers and warning signages and tape were missing	Information signages incrrease Visibility & absence expose workers and equipment to Safety Hazards which could lead in workers and equipment collision and	Information signages incrrease Visibility & absence expose workers and equipment to Safety Hazards which could lead in workers and equipment collision and	5	5	25	Very High		2026-10-03	Close	2026-10-03	Directional signages along with concrete jersey barriers and warning tape with rope have been provided – New Diversion Road,to ensure safe traffic	
3120-15	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Found equipment operators without PPE complaince	Mandatory PPE non complaince could to several injuries from minor to major.	Mandatory PPE non complaince could to several injuries from minor to major.	3	3	12	M12		2026-10-03	Close	2026-10-03	Wear the mandatory PPE all the time when present on site	
3120-16	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Observe Hot Work activity without proper control measure Fire safety	High risk of uncontrolled fire resulted from unavialablity of fire extinguisher	Peronsal injuries and equipment damages	5	5	25	Very High		2026-10-10	Close	2026-10-10	Peronsal injuries and equipment damages	
3120-17	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Observe site without mandatory PPE complaince	Mandatory PPE non complaince could to several injuries from minor to major.	minor and major injuries	3	3	12	M12		2026-10-11	Close	2026-10-11	minor and major injuries	
3120-18	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Observe dust created at temporary vehicles roads due insuffient dust control measures.	Risk of low visibility and respiratory diseases to workers working around	Peronsal injuries and equipment damages	5	5	25	Very High		2026-10-18	Close	2026-10-18	Peronsal injuries and equipment damages	
3120-19	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Observe site without mandatory PPE complaince by equipment operator	Mandatory PPE non complaince could to several injuries from minor to major.	minor and major injuries	5	5	25	Very High		2026-10-17	Close	2026-10-17	minor and major injuries	
3120-20	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Observe some shallow excavations areas with edge protection.	Risk of fall of person and equipment into the excavations.	Peronsal injuries and equipment damages	5	5	25	Very High		2026-10-25	Close	26-Oct-26	Peronsal injuries and equipment damages	
3120-21	3120	3196	Construction of Passenger Station for SAR Railway Sudair Industrial City	Sudair	Riyadh Region	Government Funded	Construction / Civil Works	Egis / MODON	Technical Development Company for Contracting	Close	Safety / Quality	Observe site without mandatory PPE complaince by equipment operator	Mandatory PPE non complaince could to several injuries from minor to major.	minor and major injuries	5	5	25	Very High		2026-10-25	Close	26-Oct-26	minor and major injuries	

Post Treatment

Project Name						
Item No.	Milestones	Original (Baseline)	Latest	Forecast		Days Change
	Contract Duration **Current Contract Weeks : 29 of 69**		**69**	**69**		**0**
1	Project Start Milstone	07-Apr-26	07-Apr-26	07-Apr-26	Finish	**0**
2	Mobilization Finish Milestone	06-May-26	06-May-26	06-May-26	Finish	**0**
3	Work Plan and Timeline Milestone	06-May-26	06-May-26	16-Aug-26	UP	**(102)**
4	Completion of MV Work	12-May-27	22-May-27	05-May-27	UP	**17**
5	Completion of road and paving works Milestone	06-Dec-26	06-Dec-26	31-Dec-26	UP	**(25)**
6	Completion of site and platform work Milestone	20-Jul-27	20-Jul-27	05-Aug-27	UP	**(16)**
7	Completion of finishing works and general site works	20-Jul-27	20-Jul-27	06-Aug-27	UP	**(17)**
8	Engineering Phase Finish Milestone	06-May-26	06-May-26	21-Sep-26	UP	**(138)**
9	Procurment Phase Finish Milestone	15-Apr-27	15-Apr-27	09-Jun-27	UP	**(55)**
10	Project Finish Milstone	06-Aug-27	06-Aug-27	06-Aug-27	-	**0**

Data sensitivity - Internal

Primavera P6 Schedule Status									
Project Activities Overview									
Schedule Statistics					Active Schedule Activities				
Total Act.	Not Started	In Progress	Completed	%	Active	Ahead	On	Behind	Flag
855	557	51	247	28.89%	2	2	0	1	1
Critical Path Activities			Free Float Management (Total)				Failed Start Activities		
			Greater Than 14 Days		Less Than 14 Days				
Last Week	This Week	Diff	Last Week	This Week	Last Week	This Week	Last Week	This Week	Flag
0	0	0	172	287	570	552	2	1	1

Data Date 26-Oct-26

Data sensitivity - Internal

	Baseline Plan			Revised / Recovery Plan			Earned Value			Gross Paid Value			Forecast			Actual/Fcst vs Plan	
Month	Monthly	Cum	%	Monthly	Cum	%	Monthly	Cum	%	Monthly	Cum	%	Monthly	C um		Month	Cum
Apr-26		0.00	0.00%				0.00	0.0	0.00%	-	0.00	0.00%	0.00	0.00			0.00
May-26	2034	2,034.00	0.01%				397,090.00	397,090.00	1.20%	-	0.00	0.00%	397,090.00	397,090.00		395,056.00	395,056.00
Jun-26	4,767.00	6,801.00	0.02%				980,202.00	1,377,292.0	4.16%	-	0.00	0.00%	980,202.00	1,377,292.0		975,435.00	975,435.00
Jul-26	36,612.00	43,413.00	0.13%				1,192,785.00	2,570,077.00	7.77%	-	0.00	0.00%	1,192,785.00	2,570,077.00		1,156,173.00	1,156,173.00
Aug-26	3,025,382.00	3,068,795.00	9.27%				2,859,151.79	5,429,228.79	16.41%	-	0.00	0.00%	2,859,151.79	5,429,228.79		(166,230.21)	(166,230.21)
Sep-26	7,642,106.00	10,710,901.00	32.37%				482,348.68	5,911,577.47	17.86%	-	0.00	0.00%	482,348.68	5,911,577.47		(7,159,757.32)	(7,159,757.32)
Oct-26	4,071,913.00	14,782,814.00	44.67%				1,449,451.38	7,361,028.85	22.24%	-	0.00	0.00%	1,449,451.38	7,361,028.85	22.24%	(2,622,461.62)	(2,622,461.62)
Nov-26	2,368,425.00	17,151,239.00	51.83%				0.00			-	0.00	0.00%	6,161,534.80	13,522,563.65	40.86%	3,793,109.80	3,793,109.80
Dec-26	3,761,619.00	20,912,858.00	63.20%				0.00			-	0.00	0.00%	7,390,294.35	20,912,858.00	63.20%	3,628,675.35	3,628,675.35
Jan-27	2,141,463.00	23,054,321.00	69.67%				0.00						2,141,463.00	23,054,321.00	69.67%	0.00	0.00
Feb-27	1,637,344.00	24,691,665.00	74.62%				0.00						1,637,344.00	24,691,665.00	74.62%	0.00	0.00
Mar-27	2,104,692.00	26,796,357.00	80.98%				0.00						2,104,692.00	26,796,357.00	80.98%	0.00	0.00
Apr-27	1,246,419.00	28,042,776.00	84.74%				0.00						1,246,419.00	28,042,776.00	84.74%	0.00	0.00
May-27	955,808.00	28,998,584.00	87.63%				0.00						955,808.00	28,998,584.00	87.63%	0.00	0.00
Jun-27	1,588,983.00	30,587,567.00	92.44%				0.00						1,588,983.00	30,587,567.00	92.44%	0.00	0.00
Jul-27	2,381,575.00	32,969,142.00	99.63%				0.00						2,381,575.00	32,969,142.00	99.63%	0.00	0.00
Aug-27	121,711.00	33,090,853.00	100.00%				0.00						121,711.00	33,090,853.00	100.00%	0.00	0.00

Actuals thru previous month

Forecast current and future months

UPDATE ONLY YELLOW PORTION FROM PRIMAVERA EXPORT, IF NEEDED, EXTEND YELLOW PORTION BASED ON SCHEDULE.

Data sensitivity - Internal

	Baseline Plan			Revised / Recovery Plan			Earned Effort %			Forecast			Achieved/Fcst vs Plan	
Week	Monthly Effort	Cum Effort	Plan Wt.%	MonthlyEffort	Cum Effort	Plan Wt.%	Monthly Wt.	Cum Wt.	Achieved Wt.%	Monthly Wt.	Cum Wt.	Wt.%	Monthly Wt.	Cum Wt.
Apr-26	36,221	36,221	5.67%				22,574	22,574.00	4.24%	22,574	22,574.00		(13,647.30)	(13,647.30)
May-26	10,471	46,693	7.31%				11,000	33,574.00	8.17%	11,000	33,574.00		528.70	(13,118.60)
Jun-26	14,208	60,900	9.54%				27,880	61,454.00	9.63%	27,880	61,454.00		13,672.40	553.80
Jul-26	16,821	77,721	12.17%				20,650	82,104.00	12.86%	20,650	82,104.00		3,829.20	4,383.00
Aug-26	62,842	140,563	22.02%				44,752	126,856.00	19.87%	44,752	126,856.00		(18,090.30)	(13,707.30)
Sep-26	54,899	195,462	30.61%				21,939	148,795.00	23.31%	21,939	148,795.00		(32,959.50)	(46,666.80)
Oct-26	49,442	244,904	38.36%				25,471	174,266.00	27.29%	25,471	174,266.00	27.29%	(23,971.20)	(70,638.00)
Nov-26	40,628	285,532	44.72%				-			111,266	285,531.80	44.72%	70,638.00	0.00
Dec-26	49,100	334,632	52.41%				-			49,100	334,632.20	52.41%	0.00	0.00
Jan-27	29,292	363,925	57.00%				-			29,292	363,924.50	57.00%	0.00	0.00
Feb-27	23,424	387,349	60.67%							23,424	387,348.90	60.67%	0.00	0.00
Mar-27	56,271	443,620	69.48%							56,271	443,620.00	69.48%	0.00	0.00
Apr-27	56,367	499,987	78.31%							56,367	499,987.40	78.31%	0.00	0.00
May-27	38,590	538,578	84.35%							38,590	538,577.50	84.35%	0.00	0.00
Jun-27	54,479	593,056	92.89%							54,479	593,056.20	92.89%	0.00	0.00
Jul-27	44,014	637,070	99.78%							44,014	637,069.80	99.78%	0.00	0.00
Aug-27	1,398	638,468	100.00%							1,398	638,468	100.00%	(0.00)	(0.00)

Actuals thru previous month

Forecast current and future months

UPDATE ONLY YELLOW PORTION FROM PRIMAVERA EXPORT, IF NEEDED, EXTEND YELLOW PORTION BASED ON SCHEDULE.

Data sensitivity - Internal

Testing and Commissioning

Item	Planned Start Date	Planned Finish Date	Forecast Start Date	Forecast Finish Date	Actual Start Date	Actual Finish Date	% Completed	Open Comments	Closed Comments
Package 1	19-Jan-27	06-Aug-27	25-Jan-27	27-Jul-27			0%	0	0
Testing and Comissioning	19-Jan-27	06-Aug-27	25-Jan-27	27-Jul-27			0%	0	0
Civil Works	9-May-27	31-May-27	6-Jun-27	23-Jun-27			0%	0.00	0.00
Storm Water Drainage Network	19-Jan-27	6-Feb-27	18-Mar-27	5-Apr-27			0%	0.00	0.00
Sewerage Network	14-Mar-27	31-Mar-27	25-Jan-27	13-Feb-27			0%	0.00	0.00
Portable Water	22-Mar-27	8-Apr-27	28-Mar-27	14-Apr-27			0%	0.00	0.00
Electrical Works	18-Jul-27	3-Aug-27	8-Jul-27	26-Jul-27			0%	0.00	0.00
CCTV Works	22-Jul-27	6-Aug-27	12-Jul-27	27-Jul-27			0%	0.00	0.00
Package 3	19-Jan-27	06-Aug-27	25-Jan-27	27-Jul-27			0%	0	0
Testing and Comissioning	19-Jan-27	06-Aug-27	25-Jan-27	27-Jul-27			0%	0	0
Civil Works	9-May-27	31-May-27	6-Jun-27	23-Jun-27			0%	0.00	0.00
Storm Water Drainage Network	19-Jan-27	6-Feb-27	18-Mar-27	5-Apr-27			0%	0.00	0.00
Sewerage Network	14-Mar-27	31-Mar-27	25-Jan-27	13-Feb-27			0%	0.00	0.00
Portable Water	22-Mar-27	8-Apr-27	28-Mar-27	14-Apr-27			0%	0.00	0.00
Electrical Works	18-Jul-27	3-Aug-27	8-Jul-27	26-Jul-27			0%	0.00	0.00
CCTV Works	22-Jul-27	6-Aug-27	12-Jul-27	27-Jul-27			0%	0.00	0.00
Total							0	0	0

Data sensitivity - Internal
