
Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Project:PASSENGER STATION FOI	15-Apr-26	15-Feb-27	01-Jul-26 A	21-Mar-27	17.53%	33.7%	SAR570,426.68	SAR1,096,542.42
Milestone	06-May-26	06-May-26	27-Oct-26	27-Oct-26	0%	0%	SAR0.00	SAR0.00
Major Milestone					0%	0%	SAR0.00	SAR0.00
Contractual Milestone					0%	0%	SAR0.00	SAR0.00
Phases Milestone	06-May-26	06-May-26	27-Oct-26	27-Oct-26	0%	0%	SAR0.00	SAR0.00
Engineering Phase Finish Milestone		06-May-26		27-Oct-26	100%	0%	SAR0.00	SAR0.00
Mobilization					0%	0%	SAR0.00	SAR0.00
Office Site Prepare					0%	0%	SAR0.00	SAR0.00
Access Roads					0%	0%	SAR0.00	SAR0.00
Offices Installation					0%	0%	SAR0.00	SAR0.00
Offices MEP Works					0%	0%	SAR0.00	SAR0.00
Manpower Mobilization					0%	0%	SAR0.00	SAR0.00
Equipment Mobilization					0%	0%	SAR0.00	SAR0.00
Project Signage					0%	0%	SAR0.00	SAR0.00
Preliminary Submittals					0%	0%	SAR0.00	SAR0.00
HSSE Plan					0%	0%	SAR0.00	SAR0.00
Quality Control Plan					0%	0%	SAR0.00	SAR0.00
Communications Plan					0%	0%	SAR0.00	SAR0.00
Risk Managment Plan					0%	0%	SAR0.00	SAR0.00
Project Execution Plan					0%	0%	SAR0.00	SAR0.00
Project Schedule					0%	0%	SAR0.00	SAR0.00
Engineering	15-Apr-26	06-May-26	26-Jul-26 A	04-Nov-26	0%	0%	SAR0.00	SAR0.00
Shop Drawings Stage	15-Apr-26	27-Apr-26	26-Oct-26	27-Oct-26	0%	0%	SAR0.00	SAR0.00
Submission					0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Sewerage Network					0%	0%	SAR0.00	SAR0.00
Portable Water					0%	0%	SAR0.00	SAR0.00
Electrical					0%	0%	SAR0.00	SAR0.00
Approvals	15-Apr-26	27-Apr-26	26-Oct-26	27-Oct-26	0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Sewerage Network					0%	0%	SAR0.00	SAR0.00
Portable Water					0%	0%	SAR0.00	SAR0.00
Electrical	15-Apr-26	27-Apr-26	26-Oct-26	27-Oct-26	0%	0%	SAR0.00	SAR0.00
Medium Voltage Network Approval	15-Apr-26	27-Apr-26	26-Oct-26	27-Oct-26	100%	0%	SAR0.00	SAR0.00
Standard Details Medium Voltage Approval	15-Apr-26	27-Apr-26	26-Oct-26	27-Oct-26	100%	0%	SAR0.00	SAR0.00
Materials	16-Apr-26	06-May-26	26-Jul-26 A	04-Nov-26	0%	0%	SAR0.00	SAR0.00
Materials Submission	16-Apr-26	23-Apr-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
Short Lead Items					0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Electrical					0%	0%	SAR0.00	SAR0.00
Mechanical					0%	0%	SAR0.00	SAR0.00
Long Lead Items	16-Apr-26	23-Apr-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Electrical	16-Apr-26	23-Apr-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
MEDIUM VOLTAGE CABLES DUCT BANKS	16-Apr-26	23-Apr-26	26-Oct-26	02-Nov-26	100%	0%	SAR0.00	SAR0.00
MEDIUM VOLTAGE CABLES	16-Apr-26	23-Apr-26	26-Oct-26	02-Nov-26	100%	0%	SAR0.00	SAR0.00

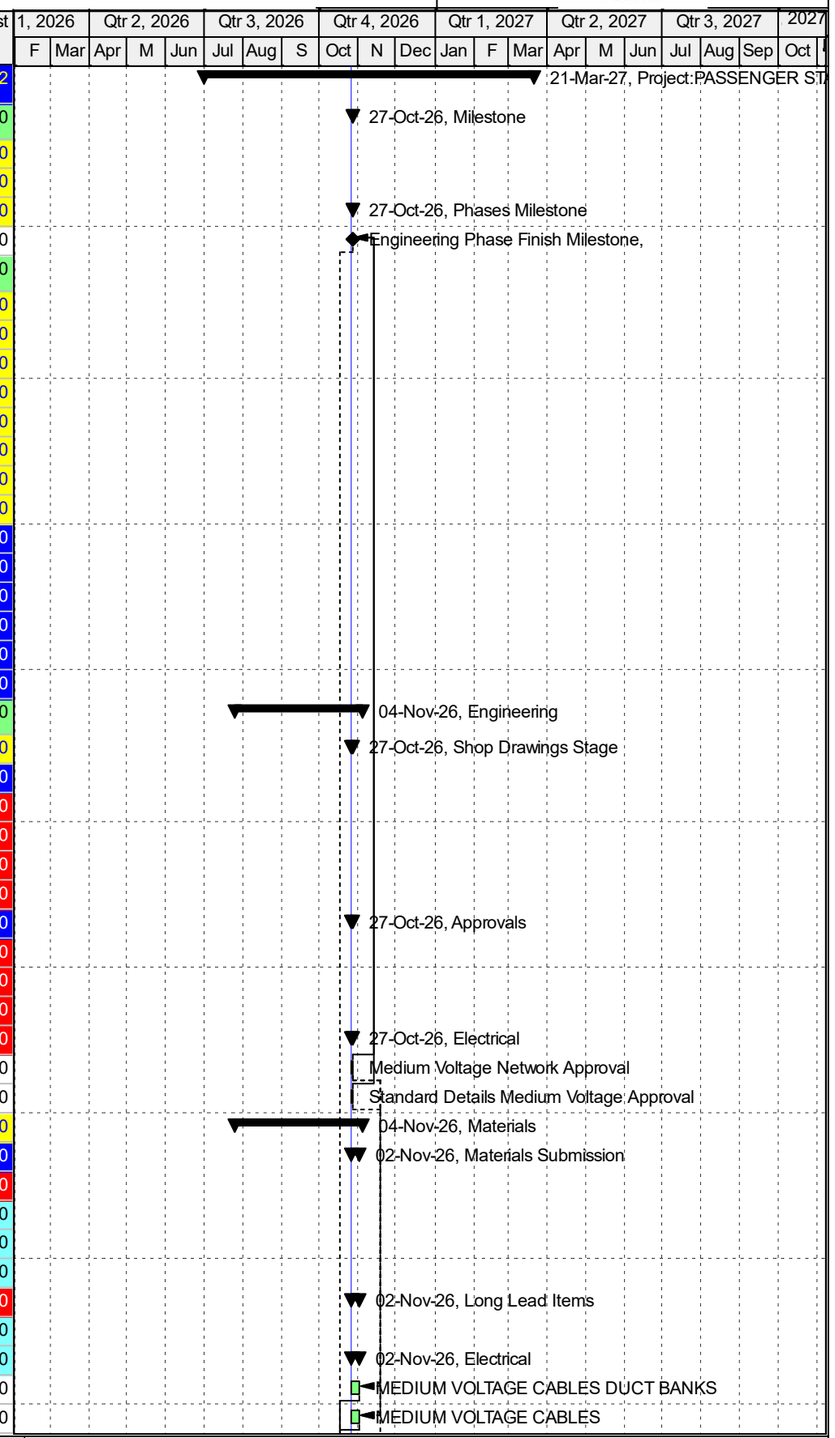

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
SUB-STATION	16-Apr-26	23-Apr-26	26-Oct-26	02-Nov-26	100%	0%	SAR0.00	SAR0.00
Mechanical					0%	0%	SAR0.00	SAR0.00
Materials Approval	25-Apr-26	06-May-26	26-Jul-26 A	04-Nov-26	0%	0%	SAR0.00	SAR0.00
Short Lead Items	25-Apr-26	06-May-26	26-Jul-26 A	01-Nov-26	0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Electrical	25-Apr-26	06-May-26	26-Jul-26 A	01-Nov-26	0%	0%	SAR0.00	SAR0.00
CCTV :5MP IP PoE Bullet Camera	25-Apr-26	06-May-26	26-Jul-26 A	01-Nov-26	100%	60%	SAR0.00	SAR0.00
CCTV :Pole mounted Filed Equipment cabinet	25-Apr-26	06-May-26	26-Jul-26 A	01-Nov-26	100%	60%	SAR0.00	SAR0.00
Mechanical					0%	0%	SAR0.00	SAR0.00
Long Lead Items	25-Apr-26	06-May-26	03-Nov-26	04-Nov-26	0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Electrical	25-Apr-26	06-May-26	03-Nov-26	04-Nov-26	0%	0%	SAR0.00	SAR0.00
MEDIUM VOLTAGE CABLES DUCT BANKS	25-Apr-26	06-May-26	03-Nov-26	04-Nov-26	100%	0%	SAR0.00	SAR0.00
MEDIUM VOLTAGE CABLES	25-Apr-26	06-May-26	03-Nov-26	03-Nov-26	100%	0%	SAR0.00	SAR0.00
SUB-STATION	25-Apr-26	06-May-26	03-Nov-26	04-Nov-26	100%	0%	SAR0.00	SAR0.00
Mechanical					0%	0%	SAR0.00	SAR0.00
Procurement	07-May-26	21-Dec-26	01-Jul-26 A	07-Feb-27	0%	0%	SAR0.00	SAR0.00
Purchase Order	07-May-26	21-Oct-26	01-Jul-26 A	24-Nov-26	0%	0%	SAR0.00	SAR0.00
Short Lead Items	07-May-26	22-Sep-26	01-Jul-26 A	12-Nov-26	0%	0%	SAR0.00	SAR0.00
Civil	07-May-26	16-Sep-26	28-Sep-26 A	10-Nov-26	0%	0%	SAR0.00	SAR0.00
Interlock	21-Jul-26	03-Aug-26	26-Oct-26	08-Nov-26	100%	0%	SAR0.00	SAR0.00
Steel Bars	07-May-26	18-May-26	28-Sep-26 A	26-Oct-26	100%	25%	SAR0.00	SAR0.00
Waterproofing (Thermal & moisture Protection)	10-Aug-26	01-Sep-26	19-Oct-26 A	10-Nov-26 A	100%	100%	SAR0.00	SAR0.00
Kerbstone	22-Jul-26	02-Aug-26	19-Oct-26 A	29-Oct-26 A	100%	100%	SAR0.00	SAR0.00
Asphalt	06-Sep-26	16-Sep-26	19-Oct-26 A	29-Oct-26 A	100%	100%	SAR0.00	SAR0.00
Electrical	15-Jul-26	22-Sep-26	01-Jul-26 A	12-Nov-26	0%	0%	SAR0.00	SAR0.00
Drawpits	15-Jul-26	26-Jul-26	26-Oct-26	05-Nov-26	100%	0%	SAR0.00	SAR0.00
CCTV :5MP IP PoE Bullet Camera	12-Sep-26	22-Sep-26	02-Nov-26	12-Nov-26	100%	0%	SAR0.00	SAR0.00
CCTV :Pole mounted Filed Equipment cabinet	21-Jul-26	01-Aug-26	02-Nov-26	12-Nov-26	100%	0%	SAR0.00	SAR0.00
VOICE EVACUATION SYSTEM	06-Sep-26	16-Sep-26	26-Oct-26	05-Nov-26	100%	0%	SAR0.00	SAR0.00
LOW VOLTAGE DISTRIBUTION Panel	30-Jul-26	10-Aug-26	01-Jul-26 A	26-Oct-26	100%	50%	SAR0.00	SAR0.00
STREET LIGHTING FEEDER Panel	21-Jul-26	01-Aug-26	01-Jul-26 A	26-Oct-26	100%	50%	SAR0.00	SAR0.00
STREET LIGHTING CABLES	04-Aug-26	16-Aug-26	25-Aug-26 A	26-Oct-26	100%	50%	SAR0.00	SAR0.00
Mechanical	23-Jul-26	12-Aug-26	26-Oct-26	05-Nov-26	0%	0%	SAR0.00	SAR0.00
GI GOOSENECK & VENT	23-Jul-26	03-Aug-26	26-Oct-26	05-Nov-26	100%	0%	SAR0.00	SAR0.00
MANHOLE, CATCH BASIN & VALVE BOX COV	02-Aug-26	12-Aug-26	26-Oct-26	05-Nov-26	100%	0%	SAR0.00	SAR0.00
Long Lead Items	13-Aug-26	21-Oct-26	01-Jul-26 A	24-Nov-26	0%	0%	SAR0.00	SAR0.00
Civil	13-Aug-26	15-Oct-26	26-Oct-26	24-Nov-26	0%	0%	SAR0.00	SAR0.00
Metal railing for platform	13-Aug-26	12-Sep-26	26-Oct-26	24-Nov-26	100%	0%	SAR0.00	SAR0.00
Canopy	30-Sep-26	15-Oct-26	26-Oct-26	10-Nov-26	100%	0%	SAR0.00	SAR0.00
Electrical	25-Aug-26	21-Oct-26	01-Jul-26 A	21-Nov-26	0%	0%	SAR0.00	SAR0.00
MEDIUM VOLTAGE CABLES DUCT BANKS	25-Aug-26	09-Sep-26	05-Nov-26	21-Nov-26	100%	0%	SAR0.00	SAR0.00
MEDIUM VOLTAGE CABLES	25-Aug-26	10-Sep-26	04-Nov-26	21-Nov-26	100%	0%	SAR0.00	SAR0.00
SUB-STATION	06-Oct-26	21-Oct-26	05-Nov-26	21-Nov-26	100%	0%	SAR0.00	SAR0.00
STREET LIGHTING LUMINAIRE	14-Sep-26	30-Sep-26	26-Oct-26	10-Nov-26	100%	0%	SAR0.00	SAR0.00
Outdoor Lighting Fixtures	12-Sep-26	28-Sep-26	26-Oct-26	10-Nov-26	100%	0%	SAR0.00	SAR0.00

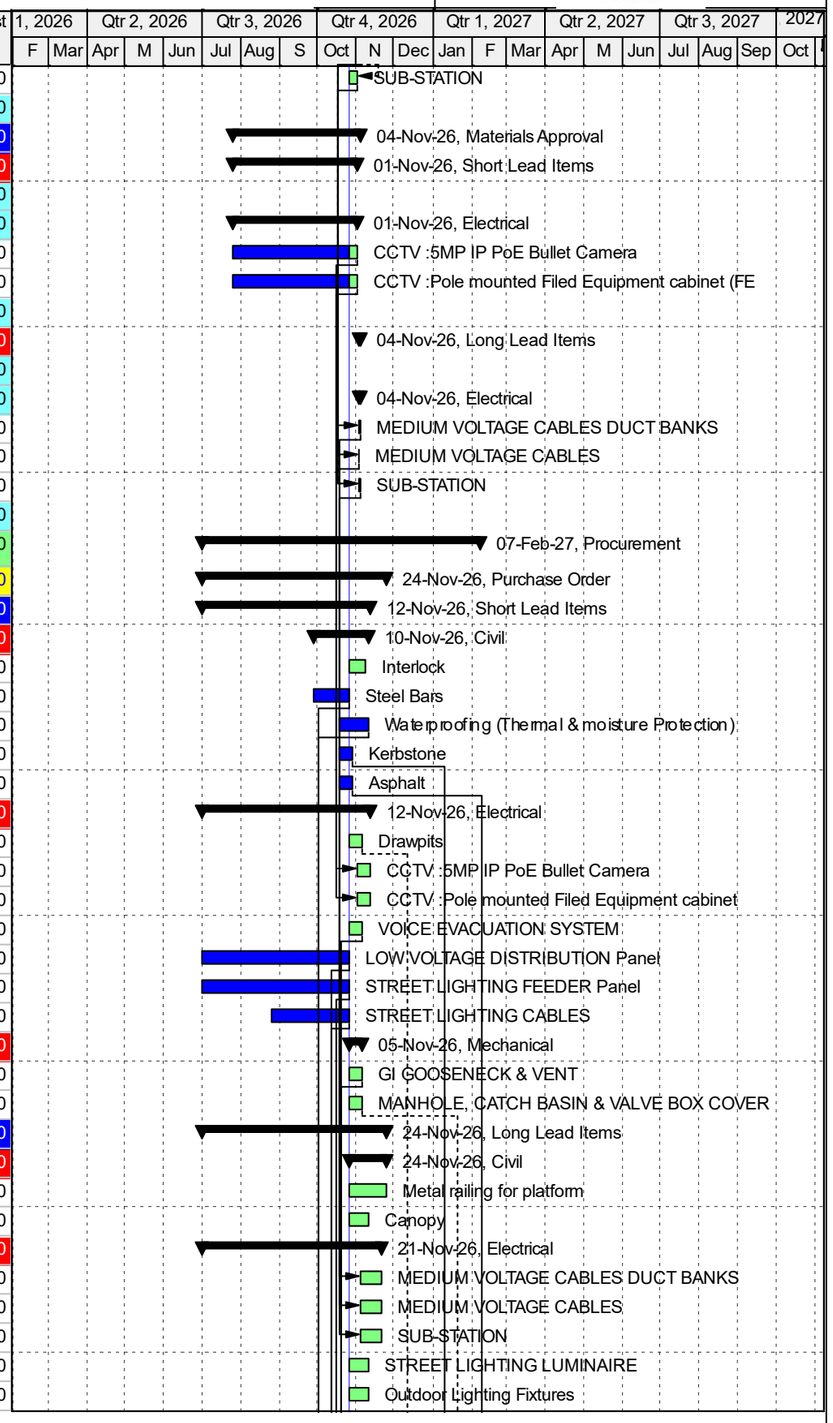

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
LIGHTING POLES	01-Sep-26	16-Sep-26	01-Jul-26 A	26-Oct-26	100%	50%	SAR0.00	SAR0.00
Mechanical	01-Sep-26	16-Sep-26	26-Oct-26	10-Nov-26	0%	0%	SAR0.00	SAR0.00
WASHOUT & AIR VALVE, GATE VALVE, BUTTE	01-Sep-26	16-Sep-26	26-Oct-26	10-Nov-26	100%	0%	SAR0.00	SAR0.00
Delivery to Site	25-Jun-26	17-Dec-26	02-Aug-26 A	07-Feb-27	0%	0%	SAR0.00	SAR0.00
Short Lead Items Delivery	25-Jun-26	19-Nov-26	02-Aug-26 A	23-Jan-27	0%	0%	SAR0.00	SAR0.00
Civil	25-Jun-26	02-Nov-26	19-Oct-26 A	23-Jan-27	0%	0%	SAR0.00	SAR0.00
Kerbstone	04-Aug-26	25-Sep-26	26-Oct-26	24-Dec-26	100%	0%	SAR0.00	SAR0.00
Asphalt	18-Sep-26	07-Oct-26	19-Oct-26 A	23-Jan-27	100%	10%	SAR0.00	SAR0.00
Steel Bars	25-Jun-26	23-Aug-26	19-Oct-26 A	24-Dec-26	100%	25%	SAR0.00	SAR0.00
Waterproofing (Thermal & moisture Protection)	02-Sep-26	02-Nov-26	19-Oct-26 A	24-Dec-26	86.89%	75%	SAR0.00	SAR0.00
Electrical	27-Jul-26	19-Nov-26	02-Aug-26 A	04-Jan-27	0%	0%	SAR0.00	SAR0.00
LOW VOLTAGE DISTRIBUTION Panel	14-Aug-26	25-Sep-26	29-Oct-26	07-Dec-26	100%	0%	SAR0.00	SAR0.00
STREET LIGHTING FEEDER Panel	09-Aug-26	18-Sep-26	02-Nov-26	11-Dec-26	100%	0%	SAR0.00	SAR0.00
STREET LIGHTING CABLES	20-Aug-26	14-Sep-26	29-Oct-26	02-Dec-26	100%	0%	SAR0.00	SAR0.00
ROAD CROSSING DUCTS 110-mm	27-Jul-26	12-Aug-26	26-Oct-26	23-Nov-26	100%	0%	SAR0.00	SAR0.00
Drawpits	27-Jul-26	27-Aug-26	26-Oct-26	24-Nov-26	100%	0%	SAR0.00	SAR0.00
VOICE EVACUATION SYSTEM	17-Sep-26	19-Nov-26	06-Nov-26	04-Jan-27	60.32%	0%	SAR0.00	SAR0.00
LOW VOLTAGE CABLES	27-Aug-26	28-Oct-26	02-Aug-26 A	15-Dec-26	95.16%	25%	SAR0.00	SAR0.00
Mechanical	04-Aug-26	22-Oct-26	26-Oct-26	03-Jan-27	0%	0%	SAR0.00	SAR0.00
GI GOOSENECK & VENT	04-Aug-26	02-Oct-26	06-Nov-26	02-Jan-27	100%	0%	SAR0.00	SAR0.00
MANHOLE, CATCH BASIN & VALVE BOX COV	13-Aug-26	22-Oct-26	26-Oct-26	03-Jan-27	100%	0%	SAR0.00	SAR0.00
Long Lead Items Delivery	17-Sep-26	17-Dec-26	26-Oct-26	07-Feb-27	0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Electrical	17-Sep-26	17-Dec-26	26-Oct-26	07-Feb-27	0%	0%	SAR0.00	SAR0.00
LIGHTING POLES	17-Sep-26	17-Dec-26	26-Oct-26	07-Feb-27	41.76%	0%	SAR0.00	SAR0.00
Mechanical	22-Sep-26	09-Oct-26	30-Oct-26	27-Jan-27	0%	0%	SAR0.00	SAR0.00
WASHOUT & AIR VALVE, GATE VALVE, BUTTE	22-Sep-26	09-Oct-26	30-Oct-26	27-Jan-27	100%	0%	SAR0.00	SAR0.00
Materials Staging Time	24-Aug-26	21-Dec-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
Short Lead Items Delivery	24-Aug-26	28-Oct-26	26-Oct-26	29-Oct-26	0%	0%	SAR0.00	SAR0.00
Civil	24-Aug-26	27-Aug-26	26-Oct-26	29-Oct-26	0%	0%	SAR0.00	SAR0.00
Steel Bars	24-Aug-26	27-Aug-26	26-Oct-26	29-Oct-26	100%	0%	SAR0.00	SAR0.00
Electrical					0%	0%	SAR0.00	SAR0.00
Mechanical	14-Sep-26	28-Oct-26	26-Oct-26	29-Oct-26	0%	0%	SAR0.00	SAR0.00
HDPE PIPES & FITTINGS	16-Oct-26	19-Oct-26	26-Oct-26	29-Oct-26	100%	0%	SAR0.00	SAR0.00
CONCRETE PIPES AND FITTINGS	25-Oct-26	28-Oct-26	26-Oct-26	29-Oct-26	25%	0%	SAR0.00	SAR0.00
WARNING TAPE	14-Sep-26	17-Sep-26	26-Oct-26	29-Oct-26	100%	0%	SAR0.00	SAR0.00
Long Lead Items Delivery	10-Oct-26	21-Dec-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Electrical	18-Dec-26	21-Dec-26	26-Oct-26	29-Oct-26	0%	0%	SAR0.00	SAR0.00
LIGHTING POLES	18-Dec-26	21-Dec-26	26-Oct-26	29-Oct-26	0%	0%	SAR0.00	SAR0.00
Mechanical	10-Oct-26	14-Oct-26	30-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
WASHOUT & AIR VALVE, GATE VALVE, BUTTE	10-Oct-26	14-Oct-26	30-Oct-26	02-Nov-26	100%	0%	SAR0.00	SAR0.00
Construction	07-Jul-26	15-Feb-27	03-Aug-26 A	21-Mar-27	17.53%	33.7%	SAR570,426.68	SAR1,096,542.42
Package-1	03-Aug-26	15-Feb-27	03-Aug-26 A	21-Mar-27	15.74%	34.44%	SAR501,336.62	SAR1,096,542.42
ROAD WORKS 1	13-Oct-26	01-Dec-26	07-Sep-26 A	30-Nov-26	10.89%	33.13%	SAR284,704.89	SAR865,955.32
ROAD - 01	13-Oct-26	01-Dec-26	10-Sep-26 A	29-Nov-26	5.41%	35.05%	SAR106,149.21	SAR688,135.58

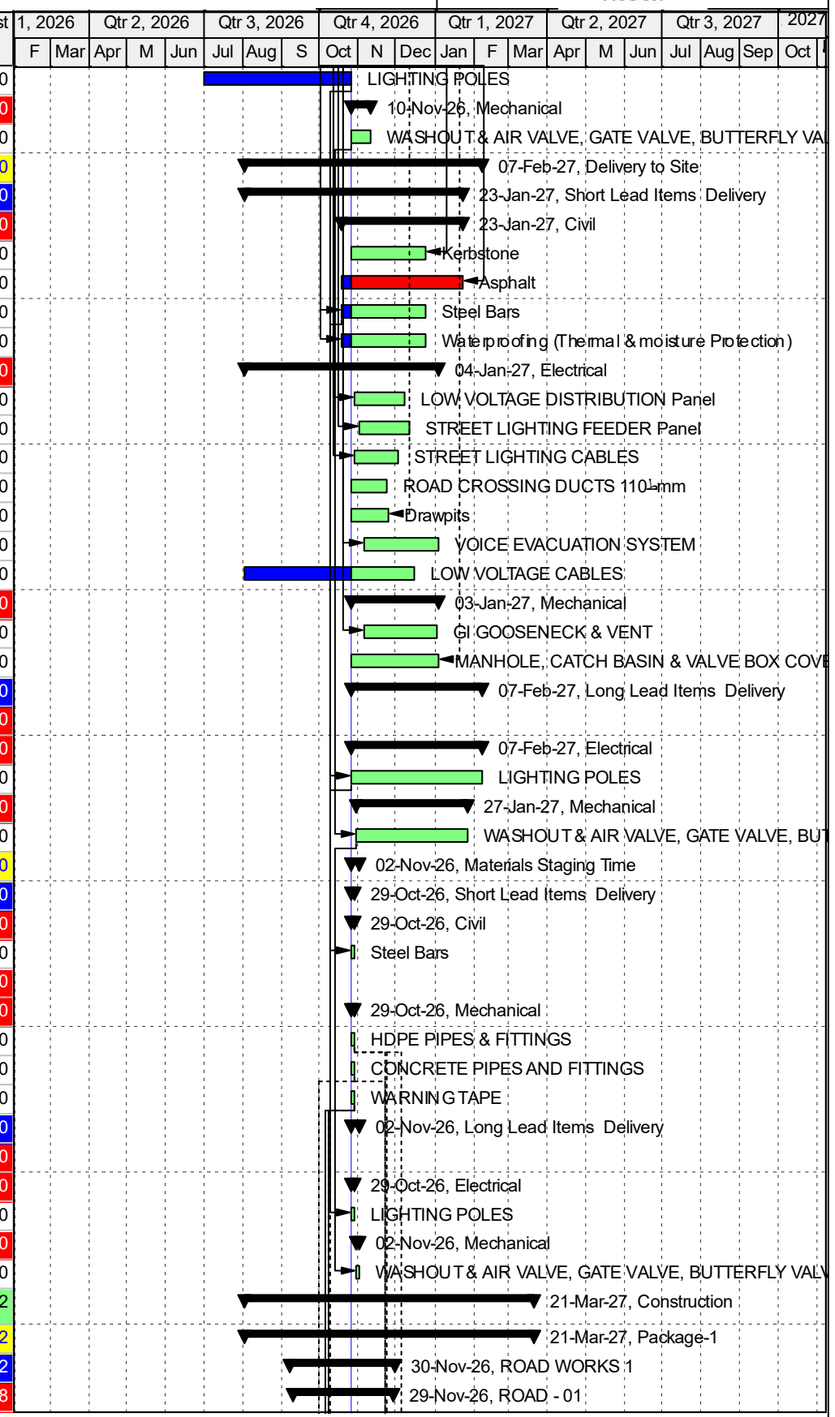

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
ROAD-01 From 0 to 470 m (3)	05-Nov-26	29-Nov-26	11-Oct-26 A	18-Nov-26	0%	54.78%	SAR0.00	SAR363,166.15
GENERAL WORKS					0%	0%	SAR0.00	SAR0.00
Cleaning and removal of organic materials ir					0%	0%	SAR0.00	SAR0.00
Surveying works Zone A					0%	0%	SAR0.00	SAR0.00
Earth Works Road					0%	0%	SAR0.00	SAR0.00
Backfilling Works					0%	0%	SAR0.00	SAR0.00
Subgrade					0%	0%	SAR0.00	SAR0.00
Base Course					0%	0%	SAR0.00	SAR0.00
Asphalt Works	21-Nov-26	29-Nov-26	11-Oct-26 A	01-Nov-26	0%	70%	SAR0.00	SAR363,166.15
Bituminous base course	21-Nov-26	29-Nov-26	11-Oct-26 A	01-Nov-26	0%	70%	SAR0.00	SAR363,166.15
Bituminous base course (Grading I - Class A 1	21-Nov-26	29-Nov-26	11-Oct-26 A	01-Nov-26	0%	70%	SAR0.00	SAR363,166.15
Bituminous concrete wearing course					0%	0%	SAR0.00	SAR0.00
Kerbstone Installation	05-Nov-26	29-Nov-26	26-Oct-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Precast Concrete Curbstone, Type A2	05-Nov-26	29-Nov-26	26-Oct-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Interlock Installation					0%	0%	SAR0.00	SAR0.00
Road Marking					0%	0%	SAR0.00	SAR0.00
Traffic Signage					0%	0%	SAR0.00	SAR0.00
Speed table					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 470 to 1125 m (6)	09-Nov-26	01-Dec-26	08-Oct-26 A	17-Nov-26	0%	10.41%	SAR0.00	SAR87,154.29
GENERAL WORKS					0%	0%	SAR0.00	SAR0.00
Cleaning and removal of organic materials ir					0%	0%	SAR0.00	SAR0.00
Surveying works Zone A					0%	0%	SAR0.00	SAR0.00
Earth Works Road					0%	0%	SAR0.00	SAR0.00
Backfilling Works					0%	0%	SAR0.00	SAR0.00
Subgrade					0%	0%	SAR0.00	SAR0.00
Base Course	09-Nov-26	21-Nov-26	08-Oct-26 A	05-Nov-26	0%	50%	SAR0.00	SAR87,154.29
Aggregate base course layer	09-Nov-26	21-Nov-26	08-Oct-26 A	05-Nov-26	0%	50%	SAR0.00	SAR87,154.29
Asphalt Works	22-Nov-26	28-Nov-26	07-Nov-26	12-Nov-26	0%	0%	SAR0.00	SAR0.00
Bituminous base course	22-Nov-26	28-Nov-26	07-Nov-26	12-Nov-26	0%	0%	SAR0.00	SAR0.00
Bituminous base course (Grading I - Class A 1	22-Nov-26	28-Nov-26	07-Nov-26	12-Nov-26	0%	0%	SAR0.00	SAR0.00
Bituminous concrete wearing course					0%	0%	SAR0.00	SAR0.00
Kerbstone Installation	09-Nov-26	01-Dec-26	26-Oct-26	17-Nov-26	0%	0%	SAR0.00	SAR0.00
Precast Concrete Curbstone, Type A2	09-Nov-26	01-Dec-26	26-Oct-26	17-Nov-26	0%	0%	SAR0.00	SAR0.00
Interlock Installation					0%	0%	SAR0.00	SAR0.00
Road Marking					0%	0%	SAR0.00	SAR0.00
Traffic Signage					0%	0%	SAR0.00	SAR0.00
Speed table					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 1125 to 1765 m (7)	13-Oct-26	22-Nov-26	10-Sep-26 A	29-Nov-26	22.92%	51.34%	SAR106,149.21	SAR237,815.14
GENERAL WORKS					0%	0%	SAR0.00	SAR0.00
Cleaning and removal of organic materials ir					0%	0%	SAR0.00	SAR0.00
Surveying works Zone A					0%	0%	SAR0.00	SAR0.00
Earth Works Road					0%	0%	SAR0.00	SAR0.00
Backfilling Works					0%	0%	SAR0.00	SAR0.00
Subgrade	13-Oct-26	29-Oct-26	10-Sep-26 A	05-Nov-26	73.33%	80%	SAR106,149.21	SAR115,799.14
Subgrade layer works	13-Oct-26	29-Oct-26	10-Sep-26 A	05-Nov-26	73.33%	80%	SAR106,149.21	SAR115,799.14
Base Course	31-Oct-26	16-Nov-26	17-Oct-26 A	16-Nov-26	0%	70%	SAR0.00	SAR122,016.01
Aggregate base course layer	31-Oct-26	16-Nov-26	17-Oct-26 A	16-Nov-26	0%	70%	SAR0.00	SAR122,016.01

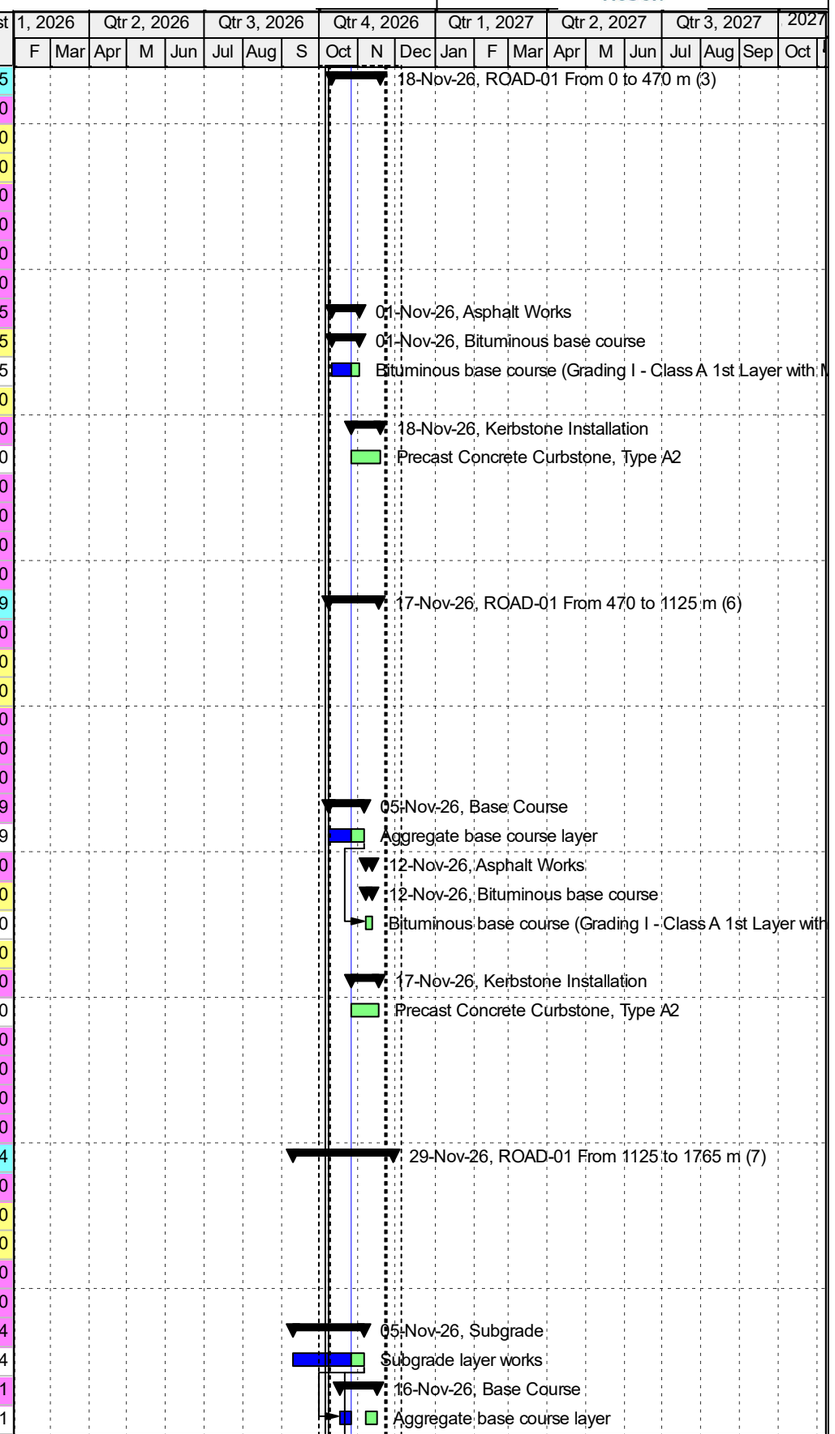

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Asphalt Works					0%	0%	SAR0.00	SAR0.00
Bituminous base course					0%	0%	SAR0.00	SAR0.00
Bituminous concrete wearing course					0%	0%	SAR0.00	SAR0.00
Kerbstone Installation	31-Oct-26	22-Nov-26	07-Nov-26	29-Nov-26	0%	0%	SAR0.00	SAR0.00
Precast Concrete Curbstone, Type A2	31-Oct-26	22-Nov-26	07-Nov-26	29-Nov-26	0%	0%	SAR0.00	SAR0.00
Interlock Installation					0%	0%	SAR0.00	SAR0.00
Road Marking					0%	0%	SAR0.00	SAR0.00
Traffic Signage					0%	0%	SAR0.00	SAR0.00
Speed table					0%	0%	SAR0.00	SAR0.00
ROAD - 02	15-Oct-26	26-Nov-26	07-Sep-26 A	30-Nov-26	27.44%	27.33%	SAR178,555.69	SAR177,819.74
ROAD-01 From 0 to 400 m (9)	15-Oct-26	29-Oct-26	07-Sep-26 A	09-Nov-26	69.23%	75%	SAR70,346.27	SAR76,208.46
GENERAL WORKS					0%	0%	SAR0.00	SAR0.00
Cleaning and removal of organic materials ir					0%	0%	SAR0.00	SAR0.00
Surveying works Zone A					0%	0%	SAR0.00	SAR0.00
Earth Works Road					0%	0%	SAR0.00	SAR0.00
Backfilling Works					0%	0%	SAR0.00	SAR0.00
Subgrade	15-Oct-26	29-Oct-26	07-Sep-26 A	09-Nov-26	69.23%	75%	SAR70,346.27	SAR76,208.46
Subgrade layer works	15-Oct-26	29-Oct-26	07-Sep-26 A	09-Nov-26	69.23%	75%	SAR70,346.27	SAR76,208.46
Base Course					0%	0%	SAR0.00	SAR0.00
Asphalt Works					0%	0%	SAR0.00	SAR0.00
Bituminous base course					0%	0%	SAR0.00	SAR0.00
Bituminous concrete wearing course					0%	0%	SAR0.00	SAR0.00
Kerbstone Installation					0%	0%	SAR0.00	SAR0.00
Interlock Installation					0%	0%	SAR0.00	SAR0.00
Road Marking					0%	0%	SAR0.00	SAR0.00
Traffic Signage					0%	0%	SAR0.00	SAR0.00
Speed table					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 400 to 900 m (10)	19-Oct-26	26-Nov-26	07-Sep-26 A	30-Nov-26	13.39%	15.62%	SAR43,547.69	SAR50,805.64
GENERAL WORKS					0%	0%	SAR0.00	SAR0.00
Cleaning and removal of organic materials ir					0%	0%	SAR0.00	SAR0.00
Surveying works Zone A					0%	0%	SAR0.00	SAR0.00
Earth Works Road					0%	0%	SAR0.00	SAR0.00
Backfilling Works					0%	0%	SAR0.00	SAR0.00
Subgrade	19-Oct-26	03-Nov-26	07-Sep-26 A	07-Nov-26	42.86%	50%	SAR43,547.69	SAR50,805.64
Subgrade layer works	19-Oct-26	03-Nov-26	07-Sep-26 A	07-Nov-26	42.86%	50%	SAR43,547.69	SAR50,805.64
Base Course	04-Nov-26	19-Nov-26	08-Nov-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Aggregate base course layer	04-Nov-26	19-Nov-26	08-Nov-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Asphalt Works					0%	0%	SAR0.00	SAR0.00
Bituminous base course					0%	0%	SAR0.00	SAR0.00
Bituminous concrete wearing course					0%	0%	SAR0.00	SAR0.00
Kerbstone Installation	04-Nov-26	26-Nov-26	08-Nov-26	30-Nov-26	0%	0%	SAR0.00	SAR0.00
Precast Concrete Curbstone, Type A2	04-Nov-26	26-Nov-26	08-Nov-26	30-Nov-26	0%	0%	SAR0.00	SAR0.00
Interlock Installation					0%	0%	SAR0.00	SAR0.00
Road Marking					0%	0%	SAR0.00	SAR0.00
Traffic Signage					0%	0%	SAR0.00	SAR0.00
Speed table					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11)	18-Oct-26	09-Nov-26	07-Sep-26 A	11-Nov-26	28.87%	22.68%	SAR64,661.72	SAR50,805.64

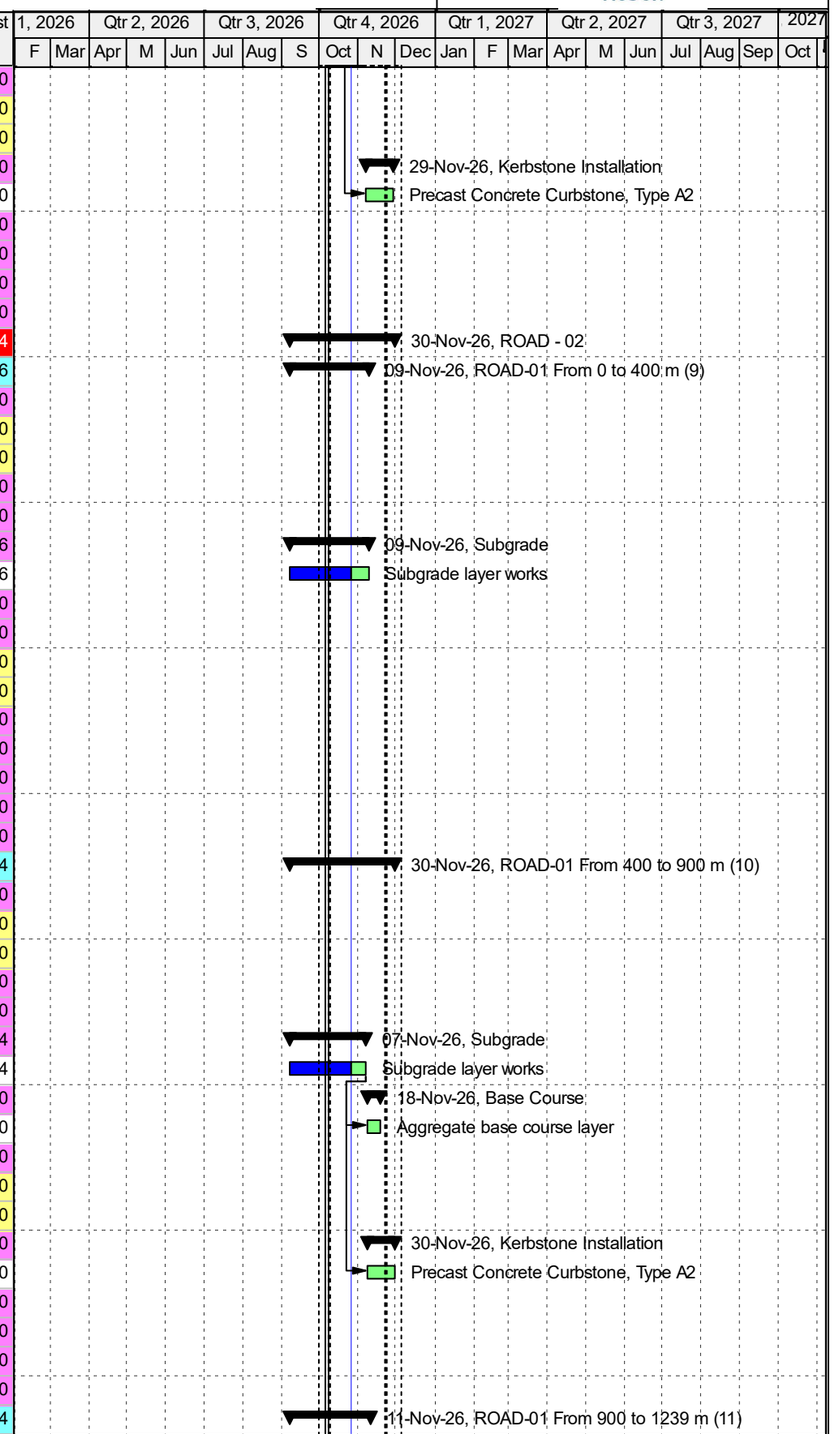

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
GENERAL WORKS					0%	0%	SAR0.00	SAR0.00
Cleaning and removal of organic materials i					0%	0%	SAR0.00	SAR0.00
Surveying works Zone A					0%	0%	SAR0.00	SAR0.00
Earth Works Road					0%	0%	SAR0.00	SAR0.00
Backfilling Works					0%	0%	SAR0.00	SAR0.00
Subgrade	18-Oct-26	29-Oct-26	07-Sep-26 A	03-Nov-26	63.64%	50%	SAR64,661.72	SAR50,805.64
Subgrade layer works	18-Oct-26	29-Oct-26	07-Sep-26 A	03-Nov-26	63.64%	50%	SAR64,661.72	SAR50,805.64
Base Course	31-Oct-26	09-Nov-26	04-Nov-26	11-Nov-26	0%	0%	SAR0.00	SAR0.00
Aggregate base course layer	31-Oct-26	09-Nov-26	04-Nov-26	11-Nov-26	0%	0%	SAR0.00	SAR0.00
Asphalt Works					0%	0%	SAR0.00	SAR0.00
Bituminous base course					0%	0%	SAR0.00	SAR0.00
Bituminous concrete wearing course					0%	0%	SAR0.00	SAR0.00
Kerbstone Installation					0%	0%	SAR0.00	SAR0.00
Interlock Installation					0%	0%	SAR0.00	SAR0.00
Road Marking					0%	0%	SAR0.00	SAR0.00
Traffic Signage					0%	0%	SAR0.00	SAR0.00
Speed table					0%	0%	SAR0.00	SAR0.00
ELECTRICAL WORKS	03-Aug-26	24-Dec-26	03-Aug-26 A	19-Jan-27	81.24%	11.22%	SAR150,806.71	SAR20,830.62
MV Network	28-Sep-26	29-Oct-26	26-Oct-26	26-Nov-26	90.67%	0%	SAR40,876.31	SAR0.00
ROAD - 01	28-Sep-26	29-Oct-26	26-Oct-26	26-Nov-26	90.67%	0%	SAR40,876.31	SAR0.00
ROAD-01 From 1125 to 1765 m (7)	28-Sep-26	21-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR22,541.29	SAR0.00
Excavation	28-Sep-26	21-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR22,541.29	SAR0.00
Excavation Works Part 1	28-Sep-26	21-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR22,541.29	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 470 to 1125 m (6)	06-Oct-26	29-Oct-26	03-Nov-26	26-Nov-26	81.34%	0%	SAR18,335.02	SAR0.00
Excavation	06-Oct-26	29-Oct-26	03-Nov-26	26-Nov-26	81.34%	0%	SAR18,335.02	SAR0.00
Excavation Works Part 1	06-Oct-26	29-Oct-26	03-Nov-26	26-Nov-26	80.95%	0%	SAR18,335.02	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD-01 N 03					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD-01 N 01					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD - 02					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 0 to 400 m (9) 2 Way 150 mm					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00

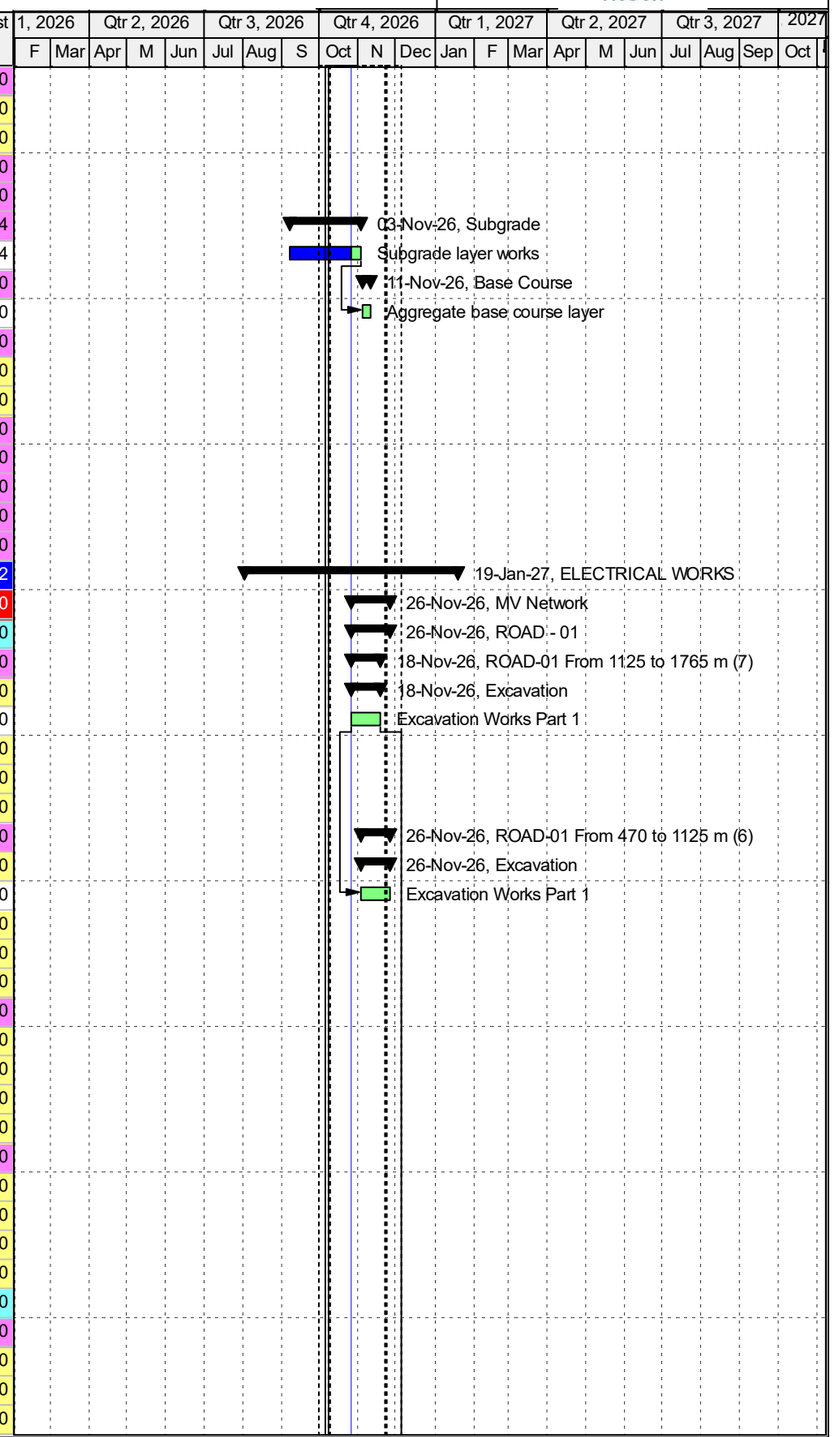

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 400 to 900 m (10) 2 Way 150 r					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11) 2 Way 150					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Earthing System					0%	0%	SAR0.00	SAR0.00
Street Lighting Network	03-Aug-26	28-Nov-26	03-Aug-26 A	21-Nov-26	85.56%	7%	SAR78,058.01	SAR6,382.50
ROAD - 01	03-Aug-26	28-Nov-26	03-Aug-26 A	21-Nov-26	77.75%	10.78%	SAR46,046.99	SAR6,382.50
ROAD-01 From 470 to 1125 m (6)	03-Aug-26	18-Oct-26	03-Aug-26 A	18-Nov-26	100%	16.67%	SAR15,318.00	SAR2,553.00
Excavation	03-Aug-26	18-Oct-26	03-Aug-26 A	18-Nov-26	100%	16.67%	SAR15,318.00	SAR2,553.00
Excavation for LV Cable trench Section 2	30-Aug-26	22-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 3	24-Sep-26	18-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 1	03-Aug-26	26-Aug-26	03-Aug-26 A	17-Nov-26	100%	50%	SAR5,106.00	SAR2,553.00
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 1125 to 1765 m (7)	27-Aug-26	20-Sep-26	03-Aug-26 A	17-Nov-26	100%	50%	SAR5,106.00	SAR2,553.00
Excavation	27-Aug-26	20-Sep-26	03-Aug-26 A	17-Nov-26	100%	50%	SAR5,106.00	SAR2,553.00
Excavation for LV Cable trench Section 1	27-Aug-26	20-Sep-26	03-Aug-26 A	17-Nov-26	100%	50%	SAR5,106.00	SAR2,553.00
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 0 to 470 m (3)	27-Aug-26	09-Nov-26	05-Sep-26 A	18-Nov-26	79.37%	8.33%	SAR12,157.14	SAR1,276.50
Excavation	27-Aug-26	09-Nov-26	05-Sep-26 A	18-Nov-26	79.37%	8.33%	SAR12,157.14	SAR1,276.50
Excavation for LV Cable trench Section 2	21-Sep-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 3	17-Oct-26	09-Nov-26	26-Oct-26	18-Nov-26	38.1%	0%	SAR1,945.14	SAR0.00
Excavation for LV Cable trench Section 1	27-Aug-26	20-Sep-26	05-Sep-26 A	18-Nov-26	100%	25%	SAR5,106.00	SAR1,276.50
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
ROAD-01 N (1)	27-Aug-26	11-Nov-26	26-Oct-26	21-Nov-26	76.19%	0%	SAR11,305.51	SAR0.00
Excavation	27-Aug-26	11-Nov-26	26-Oct-26	21-Nov-26	76.19%	0%	SAR11,305.51	SAR0.00
Excavation for LV Cable trench Section 2	24-Sep-26	18-Oct-26	28-Oct-26	21-Nov-26	100%	0%	SAR4,946.16	SAR0.00
Excavation for LV Cable trench Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR4,946.16	SAR0.00
Excavation for LV Cable trench Section 3	19-Oct-26	11-Nov-26	28-Oct-26	21-Nov-26	28.57%	0%	SAR1,413.19	SAR0.00
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
Road Crossing & Drawpits	27-Aug-26	28-Nov-26	26-Oct-26	18-Nov-26	25%	0%	SAR2,160.34	SAR0.00
ROAD - 01	27-Aug-26	28-Nov-26	26-Oct-26	18-Nov-26	25%	0%	SAR2,160.34	SAR0.00
ROAD-01 From 470 to 1125 m (6)	02-Nov-26	16-Nov-26	26-Oct-26	09-Nov-26	0%	0%	SAR0.00	SAR0.00

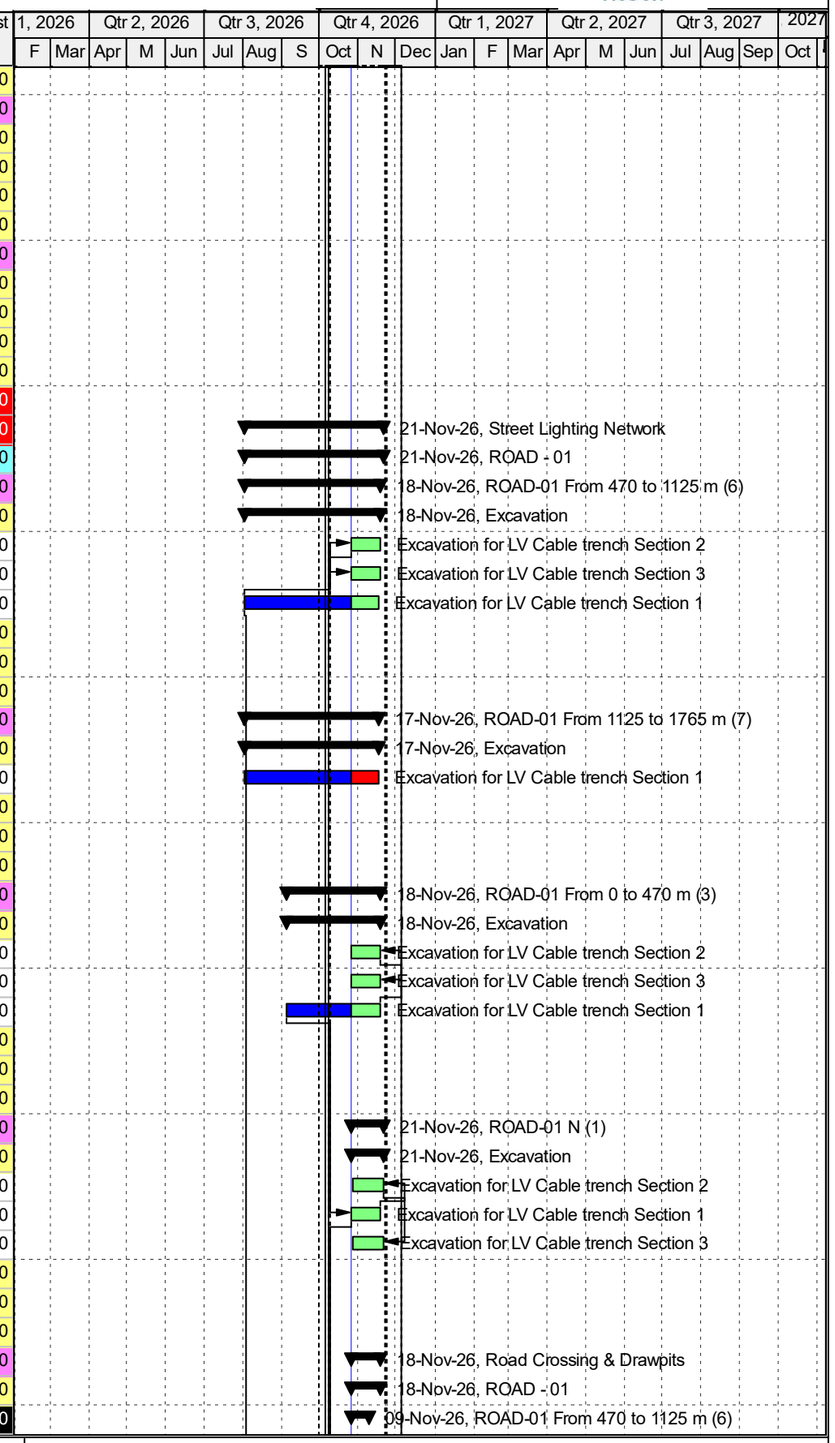

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Road crossing Ducts & Drawpits	02-Nov-26	16-Nov-26	26-Oct-26	09-Nov-26	0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing	02-Nov-26	09-Nov-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
Testing ST GRP Pipes	02-Nov-26	09-Nov-26	26-Oct-26	02-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling	10-Nov-26	16-Nov-26	03-Nov-26	09-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling ST GRP Pipes	10-Nov-26	16-Nov-26	03-Nov-26	09-Nov-26	0%	0%	SAR0.00	SAR0.00
ROAD-01 From 1125 to 1765 m (7)					0%	0%	SAR0.00	SAR0.00
Road crossing Ducts & Drawpits					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 0 to 470 m (3)	01-Nov-26	28-Nov-26	26-Oct-26	14-Nov-26	0%	0%	SAR0.00	SAR0.00
Road crossing Ducts & Drawpits	01-Nov-26	28-Nov-26	26-Oct-26	14-Nov-26	0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing	01-Nov-26	11-Nov-26	26-Oct-26	01-Nov-26	0%	0%	SAR0.00	SAR0.00
Testing ST GRP Pipes	01-Nov-26	11-Nov-26	26-Oct-26	01-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling	14-Nov-26	28-Nov-26	03-Nov-26	14-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling ST GRP Pipes	14-Nov-26	28-Nov-26	03-Nov-26	14-Nov-26	0%	0%	SAR0.00	SAR0.00
ROAD-01 N (1)	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Road crossing Ducts & Drawpits	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation for GRP Pipes Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Ring Main Unit					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
Feeder Pillars					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
KWH Frame					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
Street Lighting Sub-station					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00

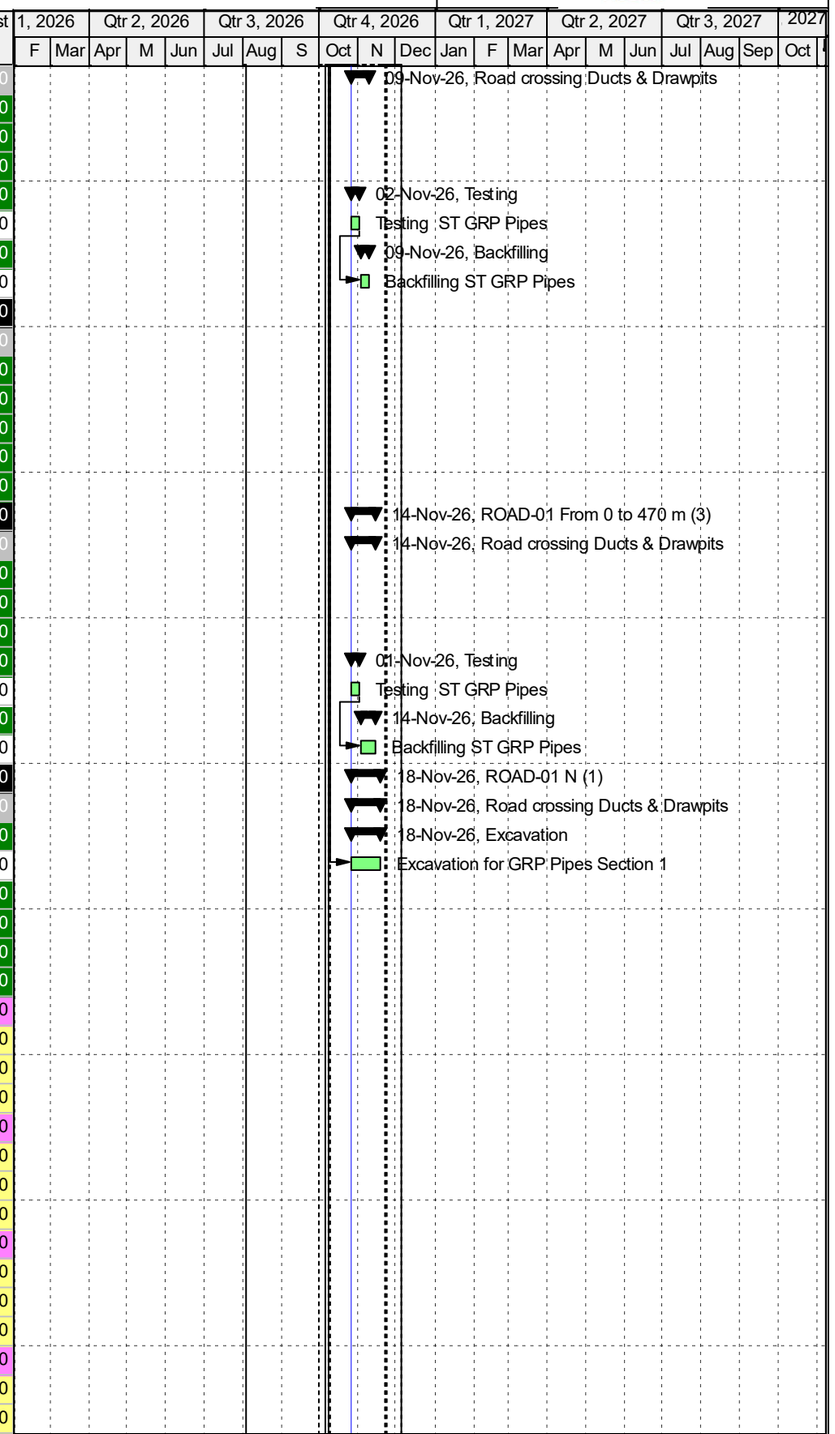

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Installation					0%	0%	SAR0.00	SAR0.00
ROAD - 02	13-Aug-26	07-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR32,011.02	SAR0.00
ROAD-01 From 0 to 400 m (9) 2 Way 110 mm	15-Aug-26	31-Aug-26	26-Oct-26	11-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation	15-Aug-26	31-Aug-26	26-Oct-26	11-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 1	15-Aug-26	31-Aug-26	26-Oct-26	11-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 400 to 900 m (10) 4 Way 110 r	13-Aug-26	07-Oct-26	26-Oct-26	11-Nov-26	100%	0%	SAR15,318.00	SAR0.00
Excavation	13-Aug-26	07-Oct-26	26-Oct-26	11-Nov-26	100%	0%	SAR15,318.00	SAR0.00
Excavation for LV Cable trench Section 2	02-Sep-26	19-Sep-26	26-Oct-26	11-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 1	13-Aug-26	30-Aug-26	26-Oct-26	11-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 3	20-Sep-26	07-Oct-26	26-Oct-26	11-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11) 2 Way 110	27-Aug-26	12-Sep-26	26-Oct-26	10-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation	27-Aug-26	12-Sep-26	26-Oct-26	10-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Excavation for LV Cable trench Section 1	27-Aug-26	12-Sep-26	26-Oct-26	10-Nov-26	100%	0%	SAR5,106.00	SAR0.00
Install Footings					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Install pole					0%	0%	SAR0.00	SAR0.00
Road Crossing & Drawpits	13-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR6,481.02	SAR0.00
ROAD - 02	13-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR6,481.02	SAR0.00
ROAD-01 From 0 to 400 m (9) 2 Way 110 mi	15-Aug-26	07-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Road crossing Ducts & Drawpits	15-Aug-26	07-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation	15-Aug-26	07-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation for GRP Pipes Section 1	15-Aug-26	07-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 400 to 900 m (10) 4 Way 11(	13-Aug-26	06-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Road crossing Ducts & Drawpits	13-Aug-26	06-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation	13-Aug-26	06-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation for GRP Pipes Section 1	13-Aug-26	06-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11) 2 Way 11	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Road crossing Ducts & Drawpits	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
Excavation for GRP Pipes Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,160.34	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00

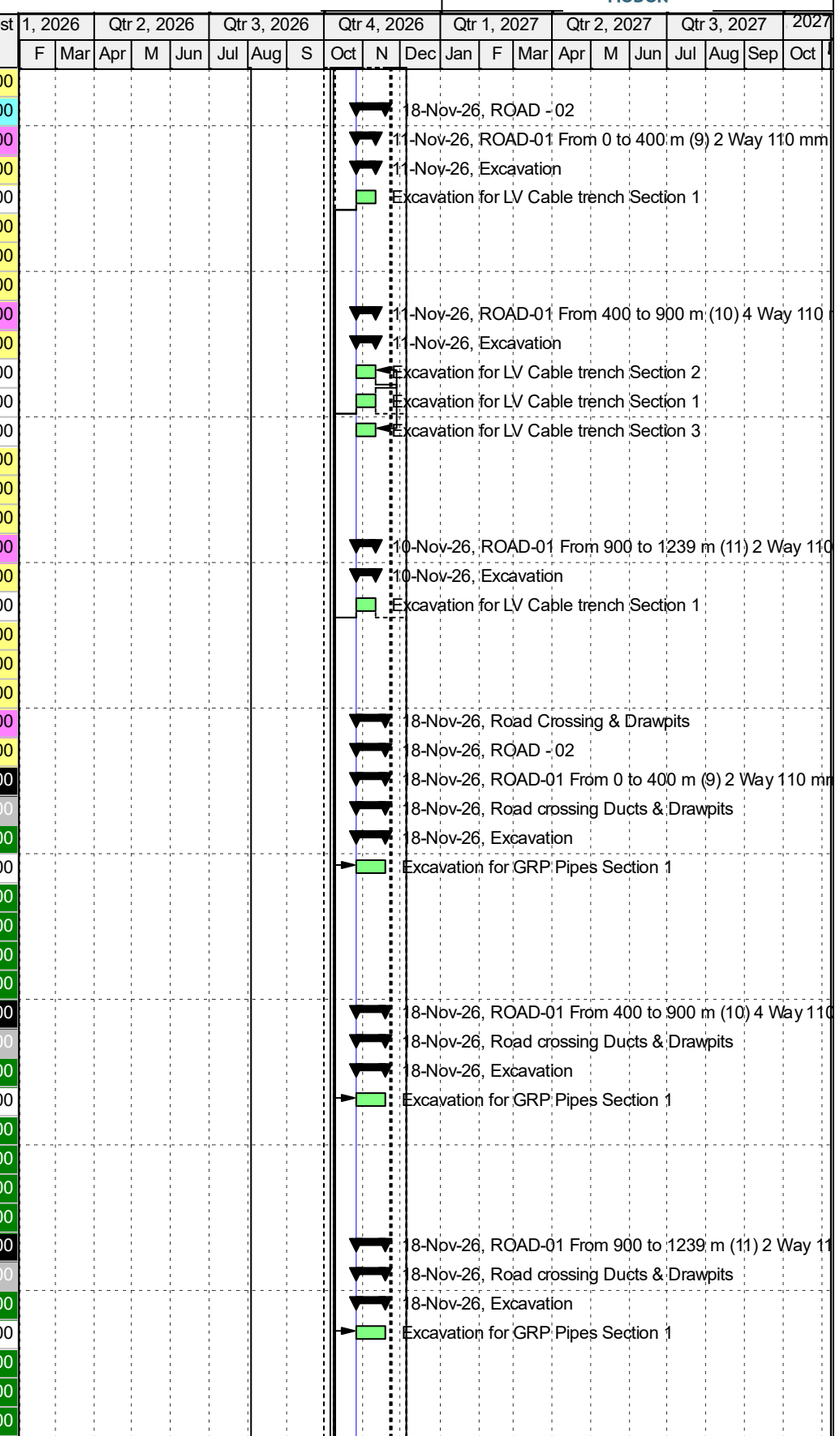

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Backfilling					0%	0%	SAR0.00	SAR0.00
Ring Main Unit					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
Feeder Pillars					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
KWH Frame					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
Street Lighting Sub-station					0%	0%	SAR0.00	SAR0.00
Leveling					0%	0%	SAR0.00	SAR0.00
Lean Concrete					0%	0%	SAR0.00	SAR0.00
Installation					0%	0%	SAR0.00	SAR0.00
TELECOMMUNICATIONS WORKS	13-Aug-26	24-Dec-26	05-Oct-26 A	19-Jan-27	64.62%	29.29%	SAR31,872.38	SAR14,448.12
ROAD - 01	27-Aug-26	24-Dec-26	05-Oct-26 A	19-Jan-27	50.36%	38.57%	SAR9,695.63	SAR7,426.92
ROAD-01 N 1 (2X3)X50 mm MH-15 to MH-16	27-Aug-26	24-Dec-26	26-Oct-26	18-Nov-26	60.04%	0%	SAR2,028.61	SAR0.00
Ducts	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation for telecom trench Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes	02-Dec-26	24-Dec-26	26-Oct-26	17-Nov-26	0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Bedding Work					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testting	02-Dec-26	24-Dec-26	26-Oct-26	17-Nov-26	0%	0%	SAR0.00	SAR0.00
Telecom Manhole finishing works	02-Dec-26	24-Dec-26	26-Oct-26	17-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 0 to 470 m (3) (2X3)X50 mm M	21-Sep-26	30-Nov-26	05-Oct-26 A	19-Jan-27	34.49%	70.95%	SAR3,609.80	SAR7,426.92
Ducts	21-Sep-26	15-Oct-26	19-Oct-26 A	18-Nov-26	100%	20%	SAR2,028.61	SAR405.72
Excavation	21-Sep-26	15-Oct-26	19-Oct-26 A	18-Nov-26	100%	20%	SAR2,028.61	SAR405.72
Excavation for telecom trench Section 2	21-Sep-26	15-Oct-26	19-Oct-26 A	18-Nov-26	100%	20%	SAR2,028.61	SAR405.72
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes	21-Sep-26	30-Nov-26	05-Oct-26 A	19-Jan-27	18.74%	83.2%	SAR1,581.19	SAR7,021.20
Excavation	21-Sep-26	15-Oct-26	05-Oct-26 A	05-Dec-26	100%	70%	SAR1,012.67	SAR708.87
Excavation for Telecom Manhole Section 2	21-Sep-26	15-Oct-26	05-Oct-26 A	05-Dec-26	100%	70%	SAR1,012.67	SAR708.87
Bedding Work	17-Oct-26	07-Nov-26	07-Oct-26 A	27-Dec-26	42.11%	85%	SAR568.52	SAR1,147.70
Sand bedding for Telecom Manhole	17-Oct-26	07-Nov-26	07-Oct-26 A	27-Dec-26	42.11%	85%	SAR568.52	SAR1,147.70
Install Manholes	08-Nov-26	30-Nov-26	13-Oct-26 A	19-Jan-27	0%	85%	SAR0.00	SAR5,164.63
Installation of Telecom Manhole	08-Nov-26	30-Nov-26	13-Oct-26 A	19-Jan-27	0%	85%	SAR0.00	SAR5,164.63

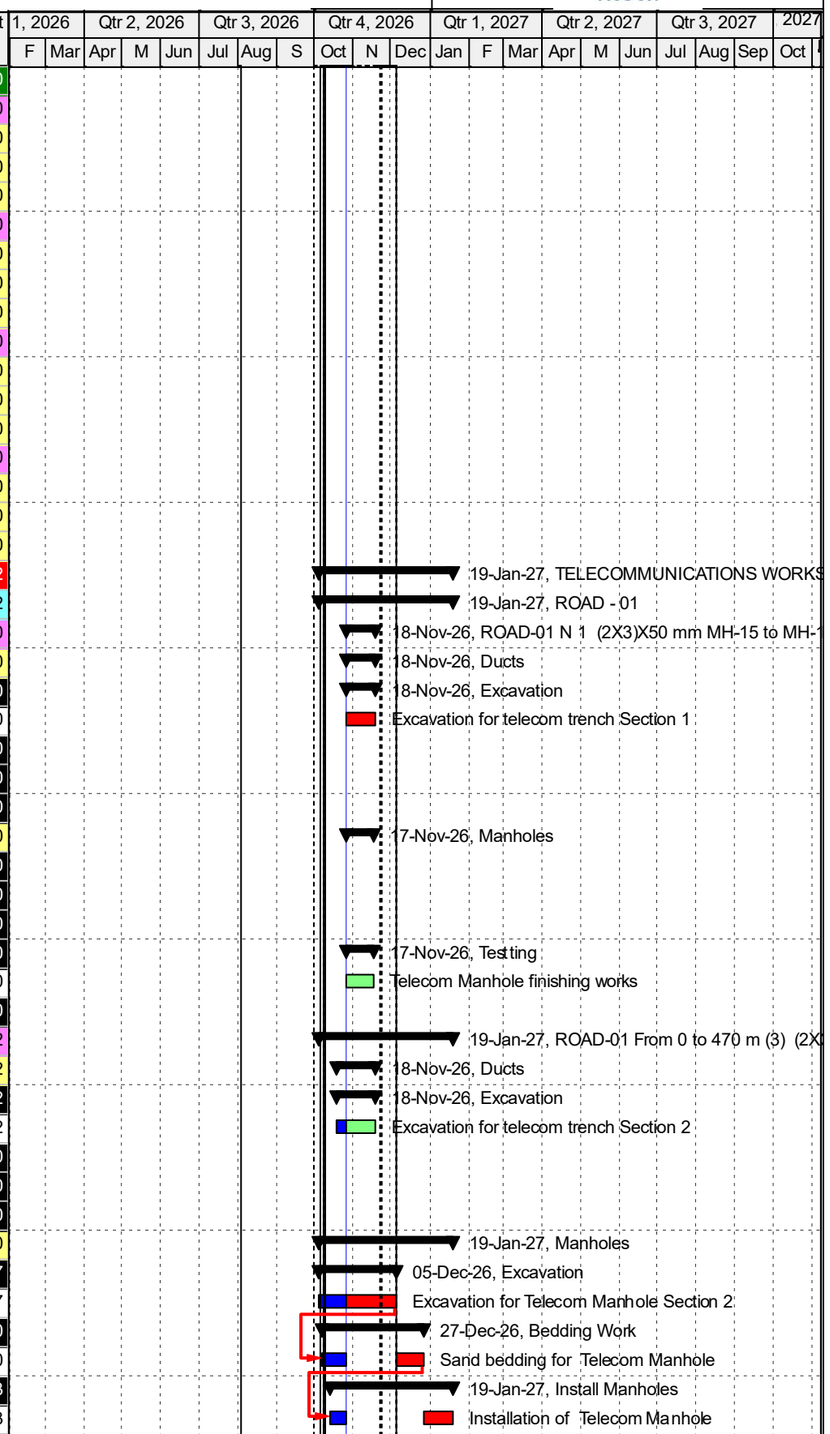

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Testting					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 470 to 1125 m (6) (2X3)X50 m	08-Sep-26	03-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Ducts	08-Sep-26	03-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation	08-Sep-26	03-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation for telecom trench Section 2	08-Sep-26	03-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Bedding Work					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testting					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 1125 to 1765 m (7) (2X3)X50 m	21-Sep-26	21-Dec-26	26-Oct-26	18-Nov-26	60.04%	0%	SAR2,028.61	SAR0.00
Ducts	21-Sep-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation	21-Sep-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation for telecom trench Section 2	21-Sep-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes	01-Dec-26	21-Dec-26	26-Oct-26	15-Nov-26	0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Bedding Work					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testting	01-Dec-26	21-Dec-26	26-Oct-26	15-Nov-26	0%	0%	SAR0.00	SAR0.00
Telecom Manhole finishing works	01-Dec-26	21-Dec-26	26-Oct-26	15-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD - 02	13-Aug-26	14-Dec-26	07-Oct-26 A	03-Jan-27	73.75%	23.35%	SAR22,176.76	SAR7,021.20
ROAD-01 From 0 to 400 m (9) (2X3)X50 mm M	15-Aug-26	14-Dec-26	26-Oct-26	18-Nov-26	84.3%	0%	SAR11,398.88	SAR0.00
Ducts	15-Aug-26	27-Oct-26	26-Oct-26	18-Nov-26	93.65%	0%	SAR11,398.88	SAR0.00
Excavation	15-Aug-26	03-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR4,057.22	SAR0.00
Excavation for telecom trench Section 2	08-Sep-26	03-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation for telecom trench Section 1	15-Aug-26	07-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Pipe laying	04-Oct-26	27-Oct-26	26-Oct-26	18-Nov-26	90.48%	0%	SAR7,341.66	SAR0.00
HDPE Pipes for Telecom Installation	04-Oct-26	27-Oct-26	26-Oct-26	18-Nov-26	90.48%	0%	SAR7,341.66	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes	21-Nov-26	14-Dec-26	26-Oct-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
Bedding Work					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testting	21-Nov-26	14-Dec-26	26-Oct-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Telecom Manhole finishing works	21-Nov-26	14-Dec-26	26-Oct-26	18-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 400 to 900 m (10) (2X3)X50 m	13-Aug-26	16-Nov-26	07-Oct-26 A	03-Jan-27	53.81%	56.19%	SAR6,723.92	SAR7,021.20

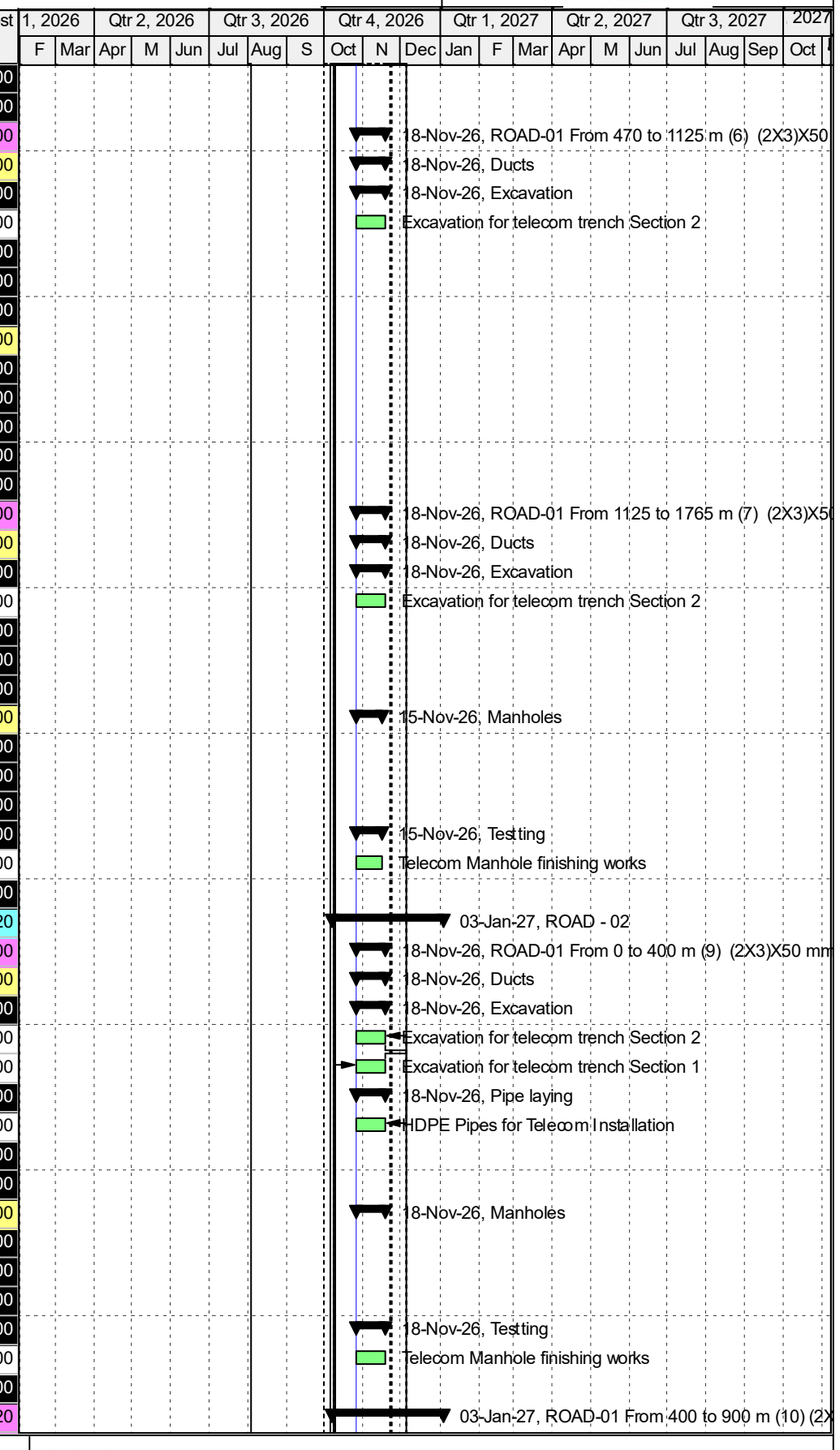

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Ducts	13-Aug-26	01-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR4,057.22	SAR0.00
Excavation	13-Aug-26	01-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR4,057.22	SAR0.00
Excavation for telecom trench Section 2	07-Sep-26	01-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation for telecom trench Section 1	13-Aug-26	06-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes	07-Sep-26	16-Nov-26	07-Oct-26 A	03-Jan-27	31.6%	83.2%	SAR2,666.70	SAR7,021.20
Excavation	07-Sep-26	01-Oct-26	07-Oct-26 A	18-Nov-26	100%	70%	SAR1,012.67	SAR708.87
Excavation for Telecom Manhole Section 2	07-Sep-26	01-Oct-26	07-Oct-26 A	18-Nov-26	100%	70%	SAR1,012.67	SAR708.87
Bedding Work	03-Oct-26	24-Oct-26	10-Oct-26 A	10-Dec-26	100%	85%	SAR1,350.23	SAR1,147.70
Sand bedding for Telecom Manhole	03-Oct-26	24-Oct-26	10-Oct-26 A	10-Dec-26	100%	85%	SAR1,350.23	SAR1,147.70
Install Manholes	25-Oct-26	16-Nov-26	13-Oct-26 A	03-Jan-27	5%	85%	SAR303.80	SAR5,164.63
Installation of Telecom Manhole	25-Oct-26	16-Nov-26	13-Oct-26 A	03-Jan-27	5%	85%	SAR303.80	SAR5,164.63
Testting					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11) (2)X32 mm	27-Aug-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR4,053.95	SAR0.00
Ducts	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Excavation for telecom trench Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,028.61	SAR0.00
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
Manholes	27-Aug-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,025.34	SAR0.00
Excavation	27-Aug-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,025.34	SAR0.00
Excavation for Telecom Manhole Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,012.67	SAR0.00
Excavation for Telecom Manhole Section 2	21-Sep-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,012.67	SAR0.00
Bedding Work					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testting					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
LOW VOLTAGE	22-Oct-26	01-Dec-26	20-Aug-26 A	18-Nov-26	4.78%	56.67%	SAR415.99	SAR4,926.72
ROAD - 01	22-Oct-26	15-Nov-26	20-Aug-26 A	18-Nov-26	14.35%	70%	SAR415.99	SAR2,028.65
ROAD-01 From 470 to 1125 m (6)	22-Oct-26	15-Nov-26	20-Aug-26 A	18-Nov-26	14.35%	70%	SAR415.99	SAR2,028.65
Excavation	22-Oct-26	15-Nov-26	20-Aug-26 A	18-Nov-26	14.35%	70%	SAR415.99	SAR2,028.65
Excavation Works Part 1	22-Oct-26	15-Nov-26	20-Aug-26 A	18-Nov-26	14.29%	70%	SAR415.99	SAR2,028.65
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD - 02	31-Oct-26	01-Dec-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR2,898.07
ROAD-01 From 400 to 900 m (10)	31-Oct-26	23-Nov-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR1,449.04
Excavation	31-Oct-26	23-Nov-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR1,449.04
Excavation Works Part 1	31-Oct-26	23-Nov-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR1,449.04
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11)	08-Nov-26	01-Dec-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR1,449.04

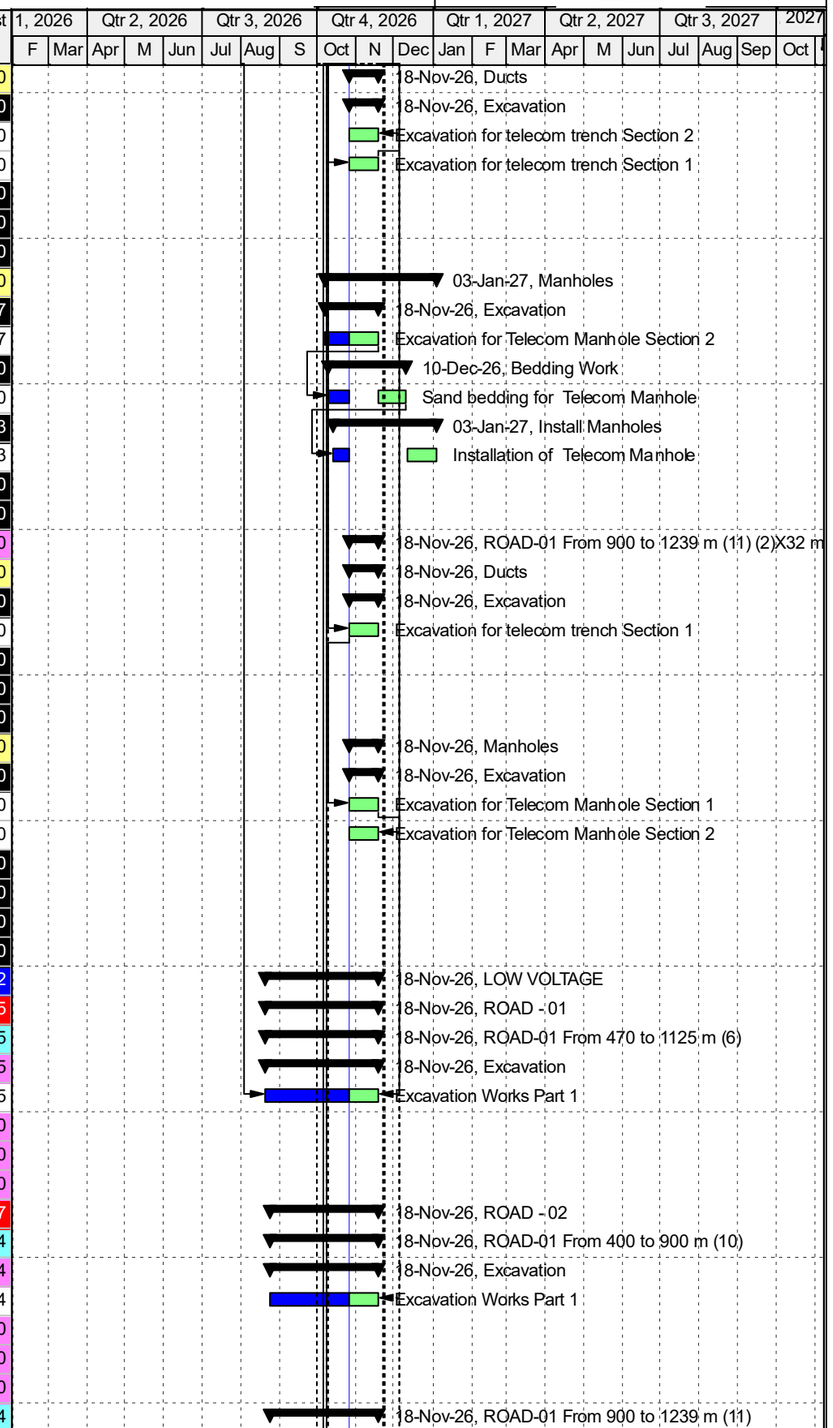

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Excavation	08-Nov-26	01-Dec-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR1,449.04
Excavation Works Part 1	08-Nov-26	01-Dec-26	24-Aug-26 A	18-Nov-26	0%	50%	SAR0.00	SAR1,449.04
Pipe laying					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Pulling Cable					0%	0%	SAR0.00	SAR0.00
PORTABLE WATER	07-Sep-26	15-Feb-27	22-Sep-26 A	21-Mar-27	8.48%	61.28%	SAR10,543.38	SAR76,185.06
ROAD - 01	12-Sep-26	15-Feb-27	22-Oct-26 A	21-Mar-27	10.95%	44.52%	SAR3,747.99	SAR15,237.02
ROAD-01 From 0 to 470 m (3)	22-Sep-26	09-Feb-27	22-Oct-26 A	23-Nov-26	10.95%	44.52%	SAR1,249.33	SAR5,079.01
Pipes Work	17-Jan-27	09-Feb-27	22-Oct-26 A	23-Nov-26	0%	50%	SAR0.00	SAR5,079.01
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling	17-Jan-27	09-Feb-27	22-Oct-26 A	23-Nov-26	0%	50%	SAR0.00	SAR5,079.01
Backfilling of PW HDPE Pipe 315 mm.	17-Jan-27	09-Feb-27	22-Oct-26 A	23-Nov-26	0%	50%	SAR0.00	SAR5,079.01
Valve Chambers & Valves & Fire Hydrant	22-Sep-26	17-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation	22-Sep-26	17-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation for Valve Chambers Section 1	22-Sep-26	17-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Chambers & Valves & Fire Hydrant					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 470 to 1125 m (6)	12-Sep-26	28-Jan-27	25-Oct-26 A	23-Nov-26	10.95%	44.52%	SAR1,249.33	SAR5,079.01
Pipes Work	05-Jan-27	28-Jan-27	25-Oct-26 A	23-Nov-26	0%	50%	SAR0.00	SAR5,079.01
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling	05-Jan-27	28-Jan-27	25-Oct-26 A	23-Nov-26	0%	50%	SAR0.00	SAR5,079.01
Backfilling of PW HDPE Pipe 315 mm.	05-Jan-27	28-Jan-27	25-Oct-26 A	23-Nov-26	0%	50%	SAR0.00	SAR5,079.01
Valve Chambers & Valves & Fire Hydrant	12-Sep-26	06-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation	12-Sep-26	06-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation for Valve Chambers Section 1	12-Sep-26	06-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Chambers & Valves & Fire Hydrant					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 1125 to 1765 m (7)	13-Sep-26	15-Feb-27	25-Oct-26 A	21-Mar-27	10.95%	44.52%	SAR1,249.33	SAR5,079.01
Pipes Work	23-Jan-27	15-Feb-27	25-Oct-26 A	21-Mar-27	0%	50%	SAR0.00	SAR5,079.01
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling	23-Jan-27	15-Feb-27	25-Oct-26 A	21-Mar-27	0%	50%	SAR0.00	SAR5,079.01
Backfilling of PW HDPE Pipe 315 mm.	23-Jan-27	15-Feb-27	25-Oct-26 A	21-Mar-27	0%	50%	SAR0.00	SAR5,079.01
Valve Chambers & Valves & Fire Hydrant	13-Sep-26	07-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation	13-Sep-26	07-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00

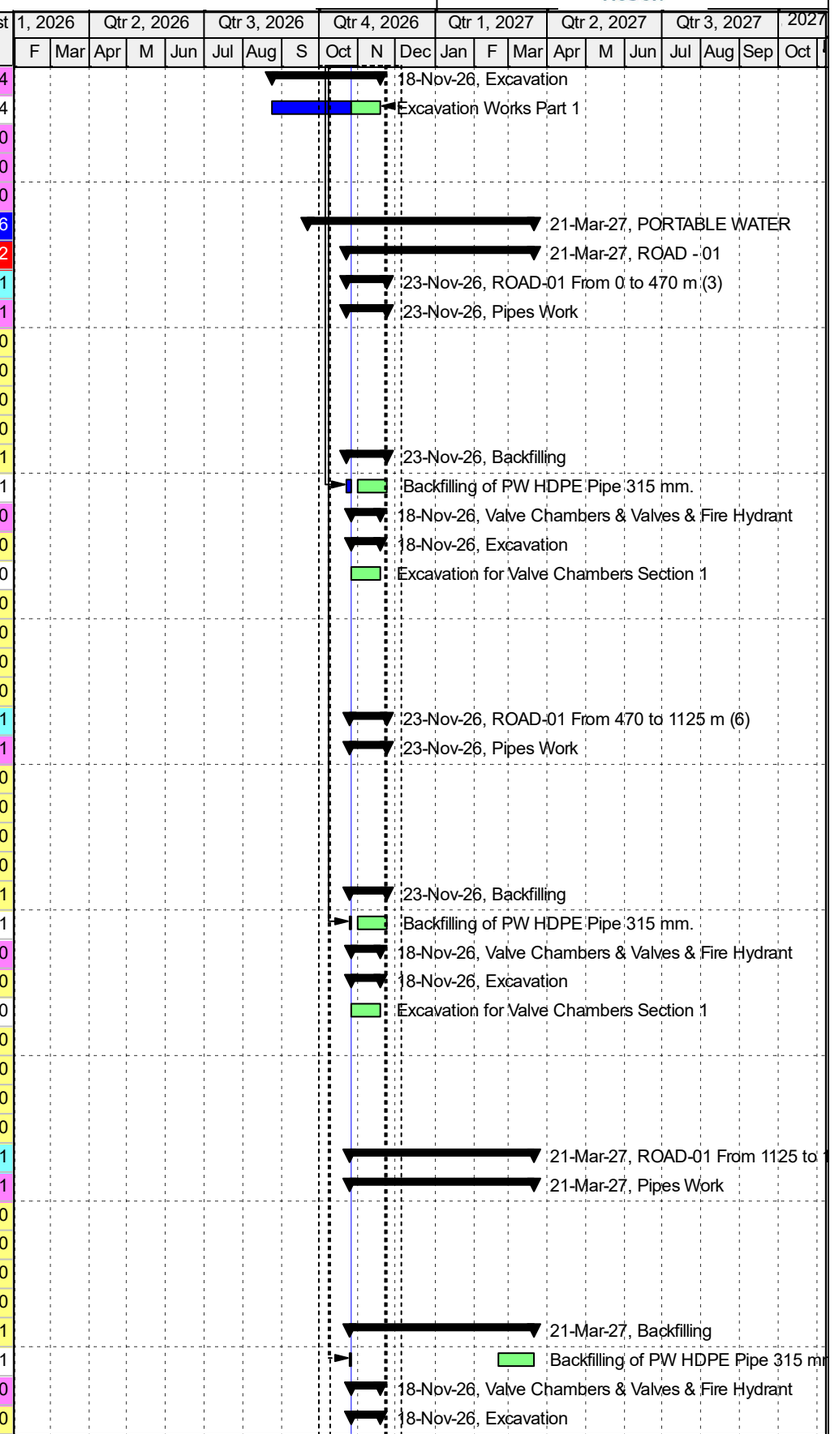

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Excavation for Valve Chambers Section 1	13-Sep-26	07-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,249.33	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Chambers & Valves & Fire Hydrant					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD - 02	07-Sep-26	14-Dec-26	22-Sep-26 A	23-Nov-26	7.54%	67.65%	SAR6,795.39	SAR60,948.05
ROAD-01 From 0 to 400 m (9)	07-Sep-26	14-Dec-26	22-Sep-26 A	18-Nov-26	4.69%	76.25%	SAR1,249.33	SAR20,316.02
Pipes Work	27-Oct-26	14-Dec-26	22-Sep-26 A	18-Nov-26	0%	80%	SAR0.00	SAR20,316.02
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works	27-Oct-26	19-Nov-26	22-Sep-26 A	18-Nov-26	0%	80%	SAR0.00	SAR2,031.60
Sand bedding for PW HDPE Pipes 315 mm	27-Oct-26	19-Nov-26	22-Sep-26 A	18-Nov-26	0%	80%	SAR0.00	SAR2,031.60
Pipes Laying	21-Nov-26	14-Dec-26	24-Sep-26 A	18-Nov-26	0%	80%	SAR0.00	SAR18,284.42
Install PW 315 mm HDPE Pipe	21-Nov-26	14-Dec-26	24-Sep-26 A	18-Nov-26	0%	80%	SAR0.00	SAR18,284.42
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Valve Chambers & Valves & Fire Hydrant	07-Sep-26	30-Sep-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation	07-Sep-26	30-Sep-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation for Valve Chambers Section 1	07-Sep-26	30-Sep-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Chambers & Valves & Fire Hydrant					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 400 to 900 m (10)	08-Sep-26	30-Nov-26	22-Sep-26 A	23-Nov-26	7.94%	64.04%	SAR2,519.08	SAR20,316.02
Pipes Work	19-Oct-26	30-Nov-26	22-Sep-26 A	23-Nov-26	4.17%	66.67%	SAR1,269.75	SAR20,316.02
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works	19-Oct-26	01-Nov-26	22-Sep-26 A	08-Nov-26	50%	80%	SAR1,269.75	SAR2,031.60
Sand bedding for PW HDPE Pipes 315 mm	19-Oct-26	01-Nov-26	22-Sep-26 A	08-Nov-26	50%	80%	SAR1,269.75	SAR2,031.60
Pipes Laying	02-Nov-26	14-Nov-26	24-Sep-26 A	07-Nov-26	0%	80%	SAR0.00	SAR18,284.42
Install PW 315 mm HDPE Pipe	02-Nov-26	14-Nov-26	24-Sep-26 A	07-Nov-26	0%	80%	SAR0.00	SAR18,284.42
Testing	15-Nov-26	30-Nov-26	08-Nov-26	23-Nov-26	0%	0%	SAR0.00	SAR0.00
Testing of PW HDPE Pipe 315 mm.	15-Nov-26	30-Nov-26	08-Nov-26	23-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Valve Chambers & Valves & Fire Hydrant	08-Sep-26	01-Oct-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation	08-Sep-26	01-Oct-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation for Valve Chambers Section 1	08-Sep-26	01-Oct-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Chambers & Valves & Fire Hydrant					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11)	09-Sep-26	25-Nov-26	22-Sep-26 A	22-Nov-26	9.54%	64.04%	SAR3,026.98	SAR20,316.02
Pipes Work	18-Oct-26	25-Nov-26	22-Sep-26 A	22-Nov-26	5.83%	66.67%	SAR1,777.65	SAR20,316.02
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works	18-Oct-26	28-Oct-26	22-Sep-26 A	05-Nov-26	70%	80%	SAR1,777.65	SAR2,031.60
Sand bedding for PW HDPE Pipes 315 mm	18-Oct-26	28-Oct-26	22-Sep-26 A	05-Nov-26	70%	80%	SAR1,777.65	SAR2,031.60
Pipes Laying	29-Oct-26	09-Nov-26	24-Sep-26 A	05-Nov-26	0%	80%	SAR0.00	SAR18,284.42
Install PW 315 mm HDPE Pipe	29-Oct-26	09-Nov-26	24-Sep-26 A	05-Nov-26	0%	80%	SAR0.00	SAR18,284.42
Testing	10-Nov-26	25-Nov-26	07-Nov-26	22-Nov-26	0%	0%	SAR0.00	SAR0.00

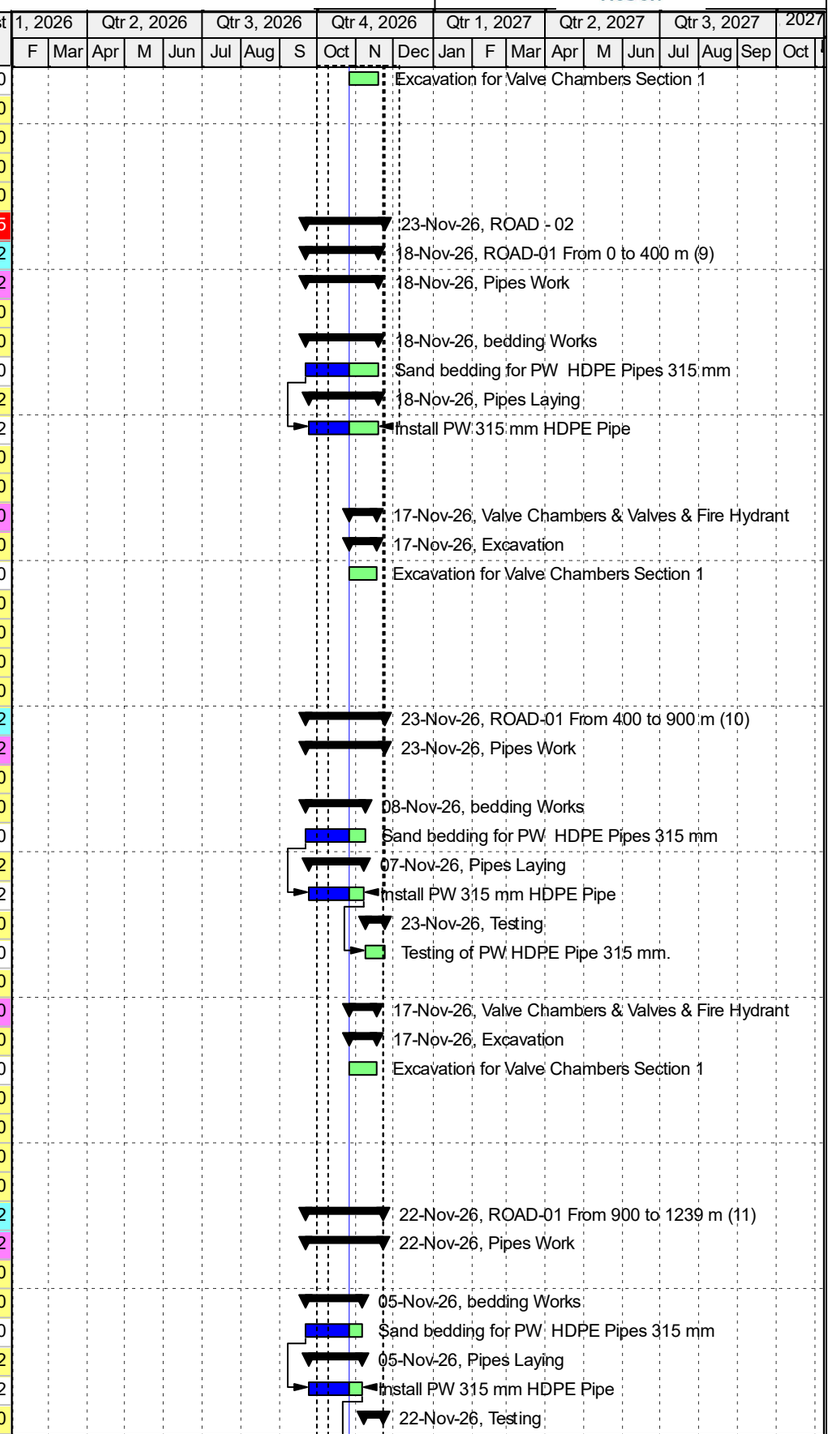

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Testing of PW HDPE Pipe 315 mm.	10-Nov-26	25-Nov-26	07-Nov-26	22-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Valve Chambers & Valves & Fire Hydrant	09-Sep-26	03-Oct-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation	09-Sep-26	03-Oct-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
Excavation for Valve Chambers Section 1	09-Sep-26	03-Oct-26	26-Oct-26	17-Nov-26	100%	0%	SAR1,249.33	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Chambers & Valves & Fire Hydrant					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
SEWARAGE NETWORK	27-Aug-26	16-Dec-26	07-Sep-26 A	19-Dec-26	33.6%	40.97%	SAR54,865.65	SAR66,896.26
ROAD - 01	27-Aug-26	16-Dec-26	07-Sep-26 A	19-Dec-26	23.08%	33.95%	SAR32,471.90	SAR47,764.48
ROAD-01 From 0 to 470 m (3) 110 mm HDPE	14-Oct-26	16-Dec-26	22-Sep-26 A	30-Nov-26	5.56%	50%	SAR3,538.11	SAR31,842.98
Pipes Work	14-Oct-26	16-Dec-26	22-Sep-26 A	30-Nov-26	5.56%	50%	SAR3,538.11	SAR31,842.98
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works	14-Oct-26	31-Oct-26	22-Sep-26 A	11-Nov-26	66.67%	60%	SAR3,538.11	SAR3,184.30
Sand bedding for GRP Pipe 200mm Diamete	14-Oct-26	31-Oct-26	22-Sep-26 A	11-Nov-26	66.67%	60%	SAR3,538.11	SAR3,184.30
Pipes Laying	01-Nov-26	23-Nov-26	24-Sep-26 A	05-Nov-26	0%	60%	SAR0.00	SAR28,658.69
200 mm GRP Pipe Laying	01-Nov-26	23-Nov-26	24-Sep-26 A	05-Nov-26	0%	60%	SAR0.00	SAR28,658.69
Testing	24-Nov-26	16-Dec-26	07-Nov-26	30-Nov-26	0%	0%	SAR0.00	SAR0.00
Testing of 200 mm GRP Pipe.	24-Nov-26	16-Dec-26	07-Nov-26	30-Nov-26	0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Manholes					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 470 to 1125 m (6) 110 mm HDF	19-Sep-26	18-Nov-26	07-Sep-26 A	19-Dec-26	24.5%	16.67%	SAR15,600.92	SAR10,614.33
Pipes Work	19-Sep-26	18-Nov-26	07-Sep-26 A	19-Dec-26	24.5%	16.67%	SAR15,600.92	SAR10,614.33
Excavation	19-Sep-26	08-Oct-26	07-Sep-26 A	14-Nov-26	100%	50%	SAR10,614.33	SAR5,307.17
Excavation for GRP Pipe 200mm Diameter S	19-Sep-26	08-Oct-26	07-Sep-26 A	14-Nov-26	100%	50%	SAR10,614.33	SAR5,307.17
bedding Works	10-Oct-26	26-Oct-26	17-Oct-26 A	01-Dec-26	93.96%	10%	SAR4,986.59	SAR530.72
Sand bedding for GRP Pipe 200mm Diamete	10-Oct-26	26-Oct-26	17-Oct-26 A	01-Dec-26	93.33%	10%	SAR4,986.59	SAR530.72
Pipes Laying	29-Oct-26	18-Nov-26	17-Oct-26 A	19-Dec-26	0%	10%	SAR0.00	SAR4,776.45
200 mm GRP Pipe Laying	29-Oct-26	18-Nov-26	17-Oct-26 A	19-Dec-26	0%	10%	SAR0.00	SAR4,776.45
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Manholes					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 1125 to 1765 m (7) 110 mm HD	27-Aug-26	15-Oct-26	07-Sep-26 A	18-Nov-26	100%	39.81%	SAR13,332.87	SAR5,307.17
Pipes Work	20-Sep-26	10-Oct-26	07-Sep-26 A	14-Nov-26	100%	50%	SAR10,614.33	SAR5,307.17
Excavation	20-Sep-26	10-Oct-26	07-Sep-26 A	14-Nov-26	100%	50%	SAR10,614.33	SAR5,307.17
Excavation for GRP Pipe 200mm Diameter S	20-Sep-26	10-Oct-26	07-Sep-26 A	14-Nov-26	100%	50%	SAR10,614.33	SAR5,307.17

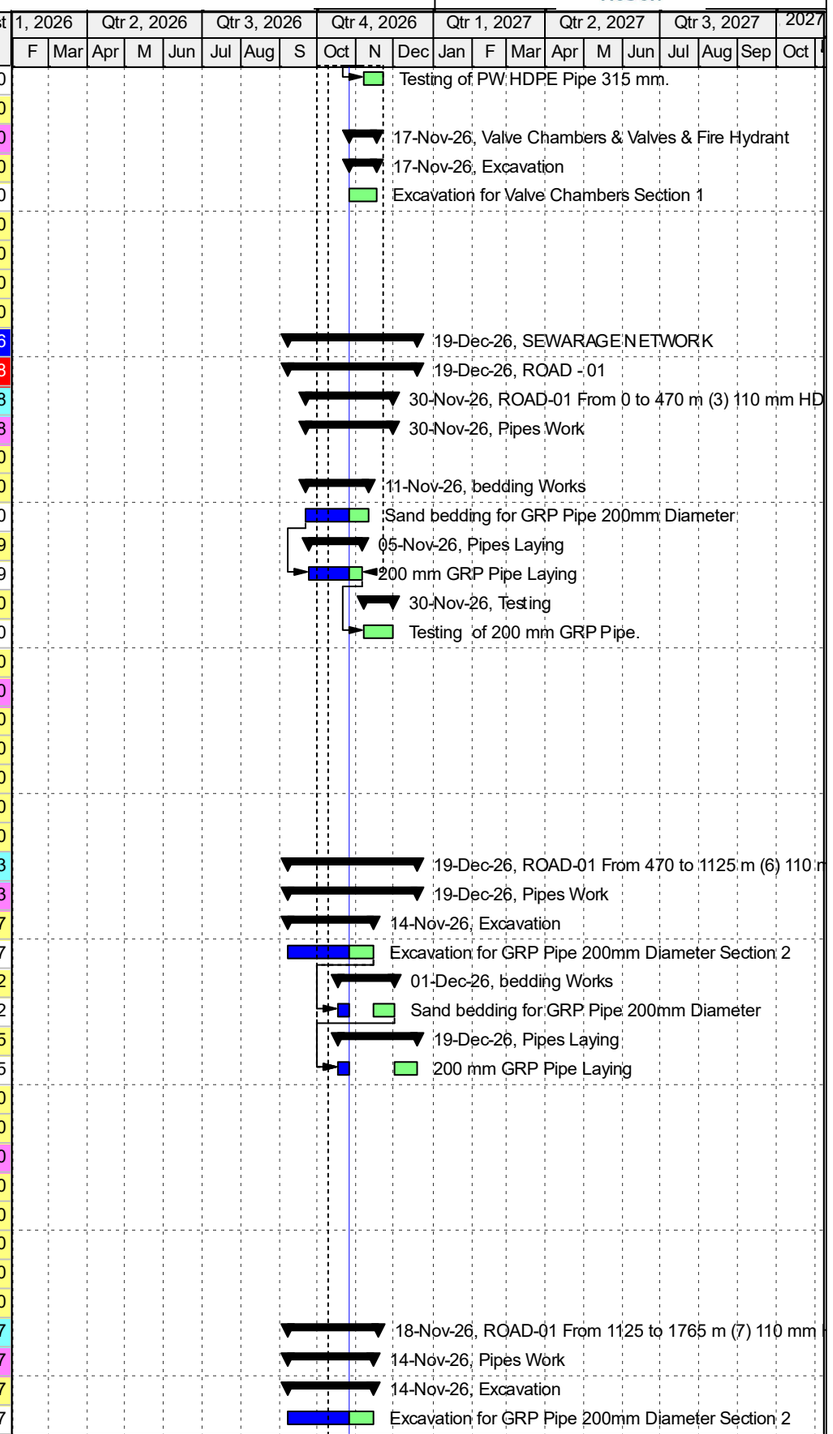

Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Manholes	27-Aug-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,718.54	SAR0.00
Excavation	27-Aug-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR2,718.54	SAR0.00
Excavation for manhole. Section 2	21-Sep-26	15-Oct-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,359.27	SAR0.00
Excavation for manhole. Section 1	27-Aug-26	20-Sep-26	26-Oct-26	18-Nov-26	100%	0%	SAR1,359.27	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD - 02	30-Aug-26	28-Oct-26	07-Sep-26 A	18-Nov-26	99.14%	84.7%	SAR22,393.75	SAR19,131.78
ROAD-01 From 400 to 900 m (10) 110 mm HDF	30-Aug-26	17-Sep-26	07-Sep-26 A	07-Nov-26	100%	90%	SAR10,614.33	SAR9,552.90
Pipes Work	30-Aug-26	17-Sep-26	07-Sep-26 A	07-Nov-26	100%	90%	SAR10,614.33	SAR9,552.90
Excavation	30-Aug-26	17-Sep-26	07-Sep-26 A	07-Nov-26	100%	90%	SAR10,614.33	SAR9,552.90
Excavation for GRP Pipe 200mm Diameter S	30-Aug-26	17-Sep-26	07-Sep-26 A	07-Nov-26	100%	90%	SAR10,614.33	SAR9,552.90
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Manholes					0%	0%	SAR0.00	SAR0.00
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
ROAD-01 From 900 to 1239 m (11) 110 mm HD	09-Sep-26	28-Oct-26	07-Sep-26 A	18-Nov-26	98.38%	80%	SAR11,779.42	SAR9,578.88
Pipes Work	09-Sep-26	28-Sep-26	07-Sep-26 A	07-Nov-26	100%	80%	SAR10,614.33	SAR8,491.46
Excavation	09-Sep-26	28-Sep-26	07-Sep-26 A	07-Nov-26	100%	80%	SAR10,614.33	SAR8,491.46
Excavation for GRP Pipe 200mm Diameter S	09-Sep-26	28-Sep-26	07-Sep-26 A	07-Nov-26	100%	80%	SAR10,614.33	SAR8,491.46
bedding Works					0%	0%	SAR0.00	SAR0.00
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
Manholes	05-Oct-26	28-Oct-26	25-Oct-26 A	18-Nov-26	85.71%	80%	SAR1,165.09	SAR1,087.42
Excavation	05-Oct-26	28-Oct-26	25-Oct-26 A	18-Nov-26	85.71%	80%	SAR1,165.09	SAR1,087.42
Excavation for manhole. Section 2	05-Oct-26	28-Oct-26	25-Oct-26 A	18-Nov-26	85.71%	80%	SAR1,165.09	SAR1,087.42
bedding Works					0%	0%	SAR0.00	SAR0.00
Install Manholes					0%	0%	SAR0.00	SAR0.00
Testing					0%	0%	SAR0.00	SAR0.00
Backfilling					0%	0%	SAR0.00	SAR0.00
STORM WATER	16-Nov-26	19-Jan-27	25-Oct-26 A	07-Mar-27	0%	70%	SAR0.00	SAR61,748.45
ROAD N...	16-Nov-26	19-Jan-27	25-Oct-26 A	07-Mar-27	0%	70%	SAR0.00	SAR61,748.45
Pipes Works	16-Nov-26	19-Jan-27	25-Oct-26 A	07-Mar-27	0%	70%	SAR0.00	SAR61,748.45
Excavation					0%	0%	SAR0.00	SAR0.00
bedding Works					0%	0%	SAR0.00	SAR0.00

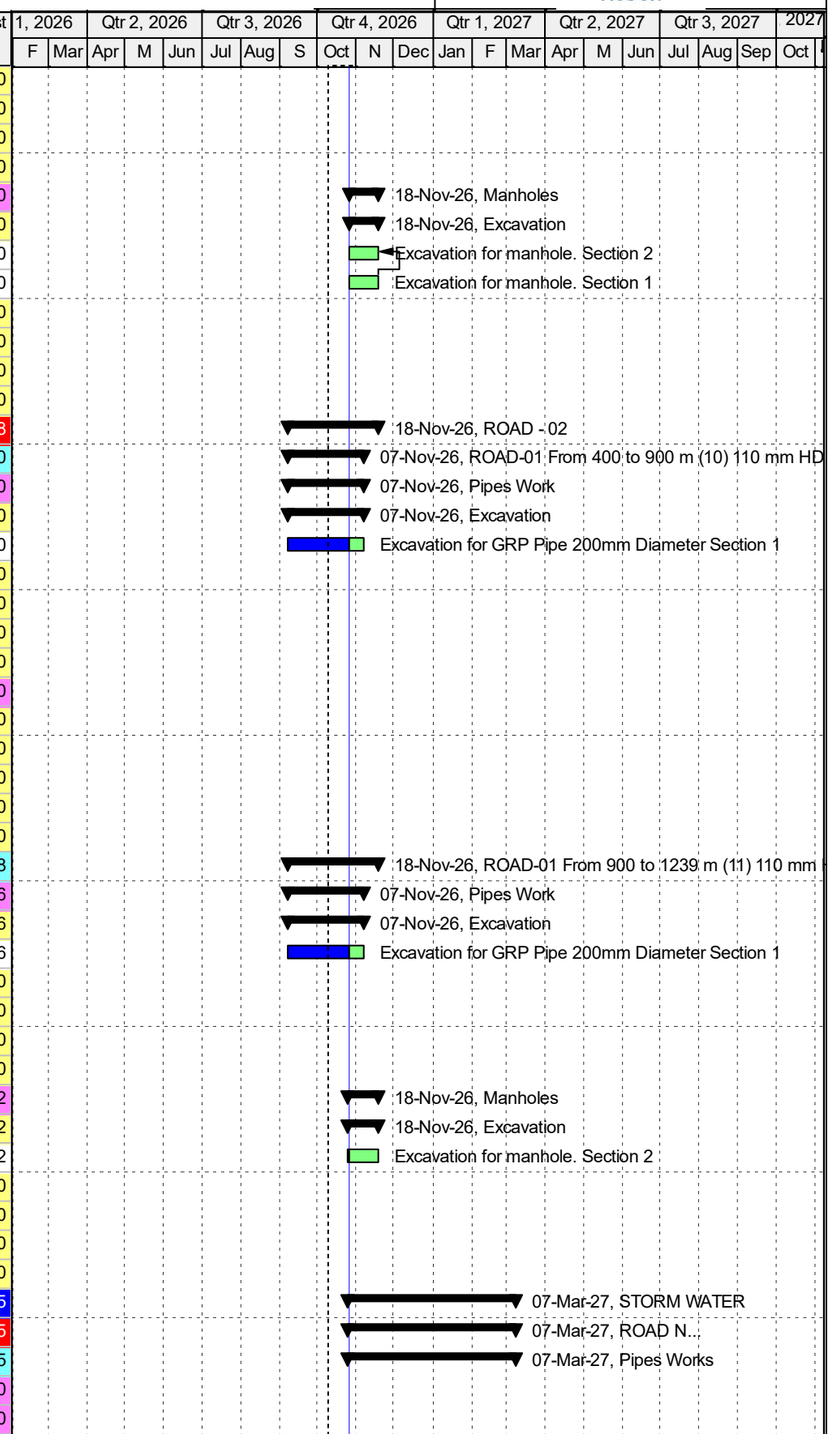

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Pipes Laying					0%	0%	SAR0.00	SAR0.00
Testing	16-Nov-26	09-Dec-26	25-Oct-26 A	19-Dec-26	0%	70%	SAR0.00	SAR20,582.81
Testing ST GRP Pipes	16-Nov-26	09-Dec-26	25-Oct-26 A	19-Dec-26	0%	70%	SAR0.00	SAR20,582.81
Backfilling	28-Dec-26	19-Jan-27	26-Oct-26 A	07-Mar-27	0%	70%	SAR0.00	SAR41,165.64
Backfilling ST GRP Pipes	28-Dec-26	19-Jan-27	26-Oct-26 A	07-Mar-27	0%	70%	SAR0.00	SAR41,165.64
Package-3	07-Jul-26	03-Sep-26	26-Oct-26	17-Nov-26	100%	0%	SAR69,090.06	SAR0.00
Site Works	07-Jul-26	16-Aug-26	26-Oct-26	17-Nov-26	100%	0%	SAR21,090.02	SAR0.00
Earthworks	07-Jul-26	16-Aug-26	26-Oct-26	17-Nov-26	100%	0%	SAR21,090.02	SAR0.00
Excavation	07-Jul-26	29-Jul-26	26-Oct-26	17-Nov-26	100%	0%	SAR13,800.01	SAR0.00
Excavation in all types of soil to the required dep	07-Jul-26	29-Jul-26	26-Oct-26	17-Nov-26	100%	0%	SAR13,800.01	SAR0.00
Fill	30-Jul-26	16-Aug-26	26-Oct-26	11-Nov-26	100%	0%	SAR7,290.01	SAR0.00
Backfilling with improved and select fill material f	30-Jul-26	16-Aug-26	26-Oct-26	11-Nov-26	100%	0%	SAR7,290.01	SAR0.00
Platform Works	17-Aug-26	03-Sep-26	26-Oct-26	12-Nov-26	100%	0%	SAR48,000.04	SAR0.00
Platform	17-Aug-26	03-Sep-26	26-Oct-26	12-Nov-26	100%	0%	SAR48,000.04	SAR0.00
Earthworks	17-Aug-26	03-Sep-26	26-Oct-26	12-Nov-26	100%	0%	SAR48,000.04	SAR0.00
Excavation	17-Aug-26	03-Sep-26	26-Oct-26	12-Nov-26	100%	0%	SAR48,000.04	SAR0.00
Excavation in all types of soil to the required de	17-Aug-26	03-Sep-26	26-Oct-26	12-Nov-26	100%	0%	SAR48,000.04	SAR0.00
Fill					0%	0%	SAR0.00	SAR0.00
Concrete Works					0%	0%	SAR0.00	SAR0.00
Foundations					0%	0%	SAR0.00	SAR0.00
Footings					0%	0%	SAR0.00	SAR0.00
Substructure					0%	0%	SAR0.00	SAR0.00
Basement					0%	0%	SAR0.00	SAR0.00
Tank					0%	0%	SAR0.00	SAR0.00
Retaining Walls					0%	0%	SAR0.00	SAR0.00
Waterproofing Vertical					0%	0%	SAR0.00	SAR0.00
Neck Walls					0%	0%	SAR0.00	SAR0.00
Preparation for Slab					0%	0%	SAR0.00	SAR0.00
Slab on Grade					0%	0%	SAR0.00	SAR0.00
Finishes					0%	0%	SAR0.00	SAR0.00
Troweled Finish					0%	0%	SAR0.00	SAR0.00
Exposed Aggregate Finish					0%	0%	SAR0.00	SAR0.00
Finishes & Architectural Works					0%	0%	SAR0.00	SAR0.00
Platform Electrical Works					0%	0%	SAR0.00	SAR0.00
Canopy works					0%	0%	SAR0.00	SAR0.00
Civil and Architectural Works					0%	0%	SAR0.00	SAR0.00
Concrete					0%	0%	SAR0.00	SAR0.00
Metals					0%	0%	SAR0.00	SAR0.00
Structural Steel Framing					0%	0%	SAR0.00	SAR0.00
Aluminum Cladding Panels					0%	0%	SAR0.00	SAR0.00
Steel Subframe Installation					0%	0%	SAR0.00	SAR0.00
Aluminum Cladding Installation					0%	0%	SAR0.00	SAR0.00
THERMAL & MOISTURE PROTECTION					0%	0%	SAR0.00	SAR0.00
Bituminous Sheet Waterproofing					0%	0%	SAR0.00	SAR0.00
Electrical Works					0%	0%	SAR0.00	SAR0.00
Low-Voltage Electrical Power Conductors and C					0%	0%	SAR0.00	SAR0.00
Ondoor Lighting Points					0%	0%	SAR0.00	SAR0.00

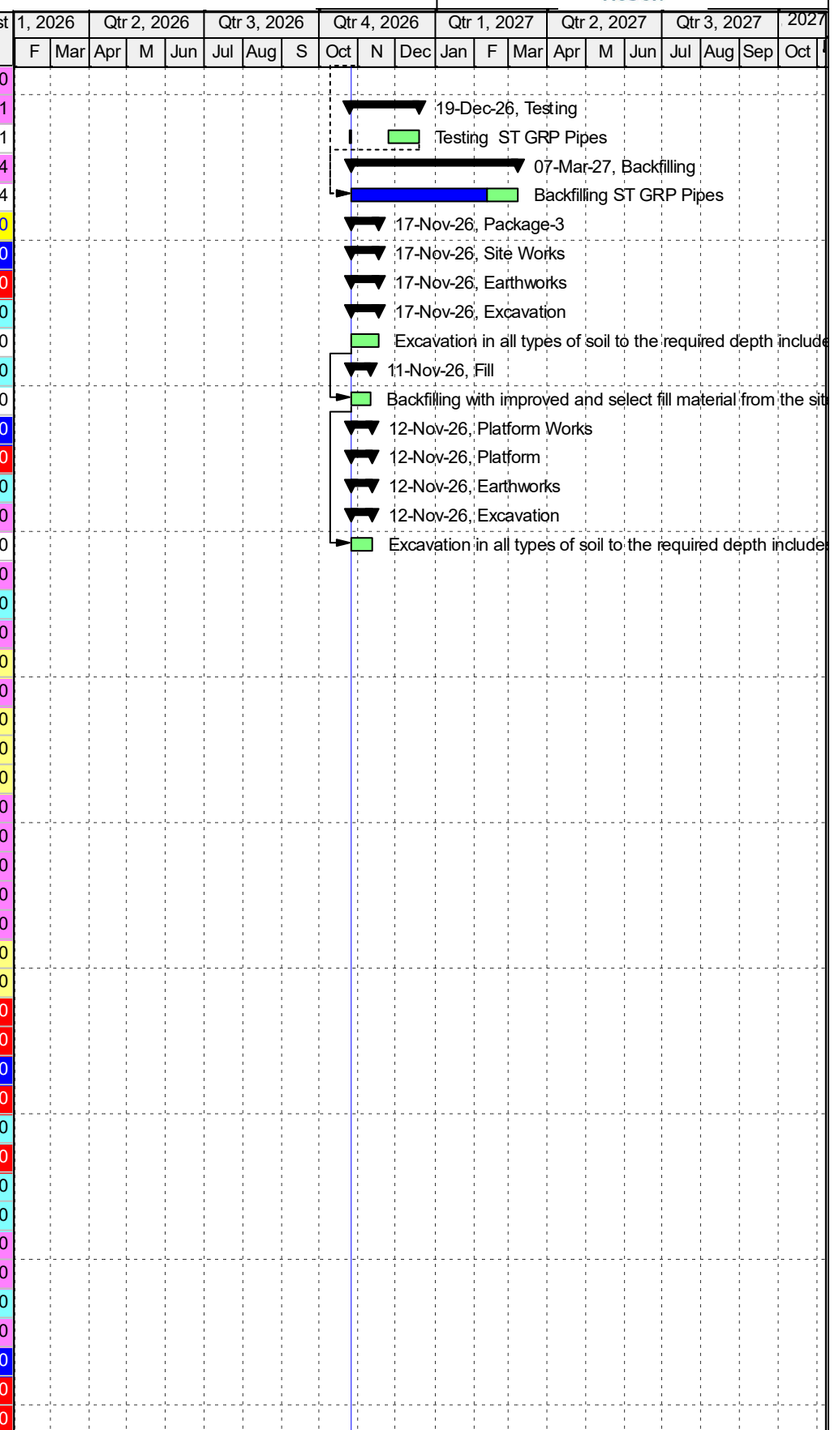

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity Name	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
Outdoor Lighting Fixtures					0%	0%	SAR0.00	SAR0.00
CCTV					0%	0%	SAR0.00	SAR0.00
Voice Evacuation System					0%	0%	SAR0.00	SAR0.00
Testing and Comissioning					0%	0%	SAR0.00	SAR0.00
Civil Works					0%	0%	SAR0.00	SAR0.00
Storm Water Drainage Network					0%	0%	SAR0.00	SAR0.00
Sewerage Network					0%	0%	SAR0.00	SAR0.00
Portable Water					0%	0%	SAR0.00	SAR0.00
Electrical Works					0%	0%	SAR0.00	SAR0.00
CCTV Works					0%	0%	SAR0.00	SAR0.00
Close Out					0%	0%	SAR0.00	SAR0.00
As Built Drawings					0%	0%	SAR0.00	SAR0.00
Civil					0%	0%	SAR0.00	SAR0.00
Mechanical					0%	0%	SAR0.00	SAR0.00
Electrical					0%	0%	SAR0.00	SAR0.00
Training and Manuals					0%	0%	SAR0.00	SAR0.00
Demobilize Manpower					0%	0%	SAR0.00	SAR0.00
Demobilize Equipment					0%	0%	SAR0.00	SAR0.00
Removal of Site Offices and Structures					0%	0%	SAR0.00	SAR0.00
Handover					0%	0%	SAR0.00	SAR0.00

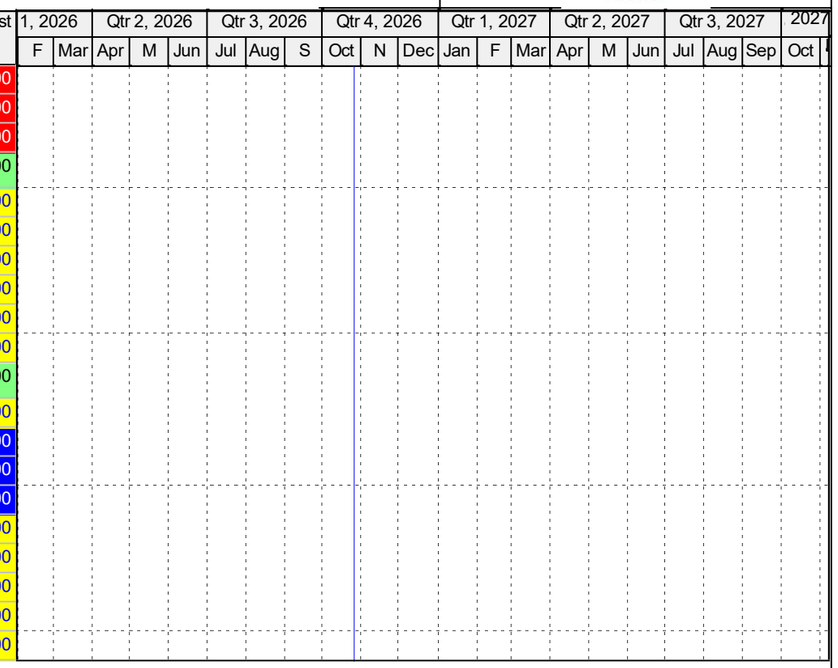

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation
