
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026		176	25-Jun-26	16-Dec-26	01-Jul-26 A	03-Feb-27	10,787,048.80	6,538,014.17	19,460,014.61	55.43%	33.6%	-36
MILESTONES		176	25-Jun-2	16-Dec-26	01-Jul-26 A	03-Feb-27	0.00	0.00	0.00	0%	0%	-36
GENERAL MILESTONES		176	25-Jun-2	16-Dec-26	01-Jul-26 A	03-Feb-27	0.00	0.00	0.00	0%	0%	-36
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-2	15-Dec-26	01-Jul-26 A	27-Dec-26	0.00	0.00	0.00	56.95%	50%	-5
PG-GN-MS-20	Project Completion Date	0		16-Dec-26		03-Feb-27	0.00	0.00	0.00	0%	0%	0
CONTRACUAL MILESTONES		63	28-Oct-2	16-Dec-26	22-Nov-26	03-Feb-27	0.00	0.00	0.00	0%	0%	-21
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26		22-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-50	Completion of Playground Works	0		07-Dec-26		09-Dec-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-40	Completion of Landscape Works	0		16-Dec-26		24-Jan-27	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-60	Substantial Completion - All Works	0		16-Dec-26		03-Feb-27	0.00	0.00	0.00	0%	0%	0
QASSIM		150	25-Jun-2	16-Dec-26	30-Jul-26 A	24-Jan-27	5,074,058.71	2,939,813.05	8,894,848.39	57.04%	33.05%	-3
ENGINEERING		35	25-Jun-2	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-21
SHOP DRAWINGS SUBMITTALS		35	25-Jun-2	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-21
MECHANICAL DRAWINGS		18	25-Jun-2	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-38
AIR DOME		18	25-Jun-2	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-38
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-2	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	100%	90%	-38
ELECTRICAL DRAWINGS		17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-39
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-39
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	03-Oct-26	0.00	0.00	0.00	100%	90%	-45
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	100%	90%	-41
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	100%	90%	-39
PROCUREMENT		80	25-Jun-2	27-Aug-26	14-Aug-26 A	17-Nov-26	2,540,171.64	1,459,417.35	2,540,171.64	100%	57.45%	-26
LONG LEAD ITEMS		80	25-Jun-2	27-Aug-26	14-Aug-26 A	17-Nov-26	2,386,452.70	1,372,173.92	2,386,452.70	100%	57.5%	-26
MANUFACTURE / FABRICATION		25	25-Jun-2	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-2	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-2	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		80	07-Jul-26	27-Aug-26	14-Aug-26 A	17-Nov-26	2,386,452.70	1,372,173.92	2,386,452.70	100%	57.5%	-36
EXTERNAL / LANDSCAPE WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-28
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-28
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	11-Oct-26	2,119,264.56	1,155,873.24	2,119,264.56	100%	54.54%	-13
PG-Q-PR-LL-SP-DL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	04-Oct-26	26,778.60	24,100.74	26,778.60	100%	90%	-28
PG-Q-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	46,985.40	42,286.86	46,985.40	100%	90%	-28
PG-Q-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	10,152.00	9,136.80	10,152.00	100%	90%	-28
PG-Q-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	156,686.40	141,017.76	156,686.40	100%	90%	-28
PG-Q-PR-LL-SP-DL-50	Air Dome Materials	10	12-Aug-2	23-Aug-26	25-Aug-26 A	11-Oct-26	1,878,662.16	939,331.08	1,878,662.16	100%	50%	-30
METAL WORK		15	25-Jul-26	10-Aug-26	01-Nov-26	17-Nov-26	3,427.65	0.00	3,427.65	100%	0%	0
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26	10-Aug-26	01-Nov-26	17-Nov-26	3,427.65	0.00	3,427.65	100%	0%	0
PLUMBING WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	7,810.43	7,029.38	7,810.43	100%	90%	-28
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	7,810.43	7,029.38	7,810.43	100%	90%	-28
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	03-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-28
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	03-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-28
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	05-Oct-26	221,065.50	176,852.40	221,065.50	100%	80%	-19
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	1,785.24	1,428.19	1,785.24	100%	80%	-33
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-2	27-Aug-26	14-Aug-26 A	05-Oct-26	3,124.17	2,499.34	3,124.17	100%	80%	-29
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-2	27-Aug-26	14-Aug-26 A	05-Oct-26	182,755.44	146,204.35	182,755.44	100%	80%	-29
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-2	27-Aug-26	14-Aug-26 A	05-Oct-26	8,081.83	6,465.46	8,081.83	100%	80%	-29
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-2	27-Aug-26	27-Aug-26 A	05-Oct-26	6,326.40	5,061.12	6,326.40	100%	80%	-18
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-2	27-Aug-26	27-Aug-26 A	05-Oct-26	6,170.09	4,936.08	6,170.09	100%	80%	-18
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-2	27-Aug-26	27-Aug-26 A	05-Oct-26	7,811.37	6,249.10	7,811.37	100%	80%	-18
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-2	27-Aug-26	27-Aug-26 A	05-Oct-26	5,010.96	4,008.77	5,010.96	100%	80%	-18
SHORT LEAD ITEMS		49	25-Jun-2	12-Jul-26	14-Aug-26 A	11-Oct-26	153,718.94	87,243.43	153,718.94	100%	56.76%	-34
DELIVERY TO SITE		49	25-Jun-2	12-Jul-26	14-Aug-26 A	11-Oct-26	153,718.94	87,243.43	153,718.94	100%	56.76%	-34
EXTERNAL / LANDSCAPE WORK		12	25-Jun-2	08-Jul-26	27-Aug-26 A	11-Oct-26	78,553.04	38,992.68	78,553.04	100%	49.64%	-26
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-2	08-Jul-26	27-Aug-26 A	11-Oct-26	1,892.27	662.29	1,892.27	100%	35%	-26
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-2	08-Jul-26	27-Aug-26 A	08-Oct-26	714.10	357.05	714.10	100%	50%	-24
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-2	08-Jul-26	27-Aug-26 A	08-Oct-26	34,366.68	17,183.34	34,366.68	100%	50%	-24
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-2	08-Jul-26	27-Aug-26 A	08-Oct-26	41,580.00	20,790.00	41,580.00	100%	50%	-24
METAL WORK		12	25-Jun-2	08-Jul-26	26-Sep-26 A	08-Oct-26	1,724.00	862.00	1,724.00	100%	50%	0
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-2	08-Jul-26	26-Sep-26 A	08-Oct-26	1,302.70	651.35	1,302.70	100%	50%	0
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-2	08-Jul-26	26-Sep-26 A	08-Oct-26	112.75	56.38	112.75	100%	50%	0
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-2	08-Jul-26	26-Sep-26 A	08-Oct-26	308.56	154.28	308.56	100%	50%	0
IRRIGATION WORK		18	25-Jun-2	08-Jul-26	14-Aug-26 A	07-Oct-26	71,118.65	46,227.12	71,118.65	100%	65%	-33
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-2	08-Jul-26	14-Aug-26 A	07-Oct-26	7,186.00	4,670.90	7,186.00	100%	65%	-33
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-2	08-Jul-26	20-Aug-26 A	07-Oct-26	63,932.65	41,556.22	63,932.65	100%	65%	-28
ELECTRICAL WORK		15	25-Jun-2	12-Jul-26	26-Sep-26 A	11-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	2
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-2	12-Jul-26	26-Sep-26 A	11-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	2
FIRE FIGHTING WORK		12	25-Jun-2	08-Jul-26	26-Sep-26 A	08-Oct-26	122.63	61.32	122.63	100%	50%	0
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-2	08-Jul-26	26-Sep-26 A	08-Oct-26	122.63	61.32	122.63	100%	50%	0
CONSTRUCTION STAGE		127	05-Jul-26	16-Dec-26	06-Aug-26 A	18-Jan-27	2,533,887.07	1,208,563.83	4,653,535.37	54.45%	25.97%	1
PLAYGROUND AND LANDSCAPING WORKS		127	05-Jul-26	16-Dec-26	06-Aug-26 A	18-Jan-27	894,802.68	930,423.39	1,629,217.98	54.92%	57.11%	1
PLAYGROUND WORKS		96	11-Aug-2	02-Dec-26	06-Aug-26 A	09-Dec-26	83,996.71	226,095.54	325,784.34	25.78%	69.4%	-10
FOOTBALL PLAYGROUND WORKS		53	19-Aug-2	17-Nov-26	14-Aug-26 A	29-Oct-26	48,027.00	69,070.08	109,254.66	43.96%	63.22%	13
PG-Q-CON-EX-FB-120	Installation of Lighting System	12	19-Aug-2	01-Sep-26	20-Aug-26 A	04-Oct-26	24,360.00	20,706.00	24,360.00	100%	85%	-26
PG-Q-CON-EX-FB-90	Tufing / Seeding Works	10	02-Sep-2	13-Sep-26	14-Aug-26 A	06-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-35

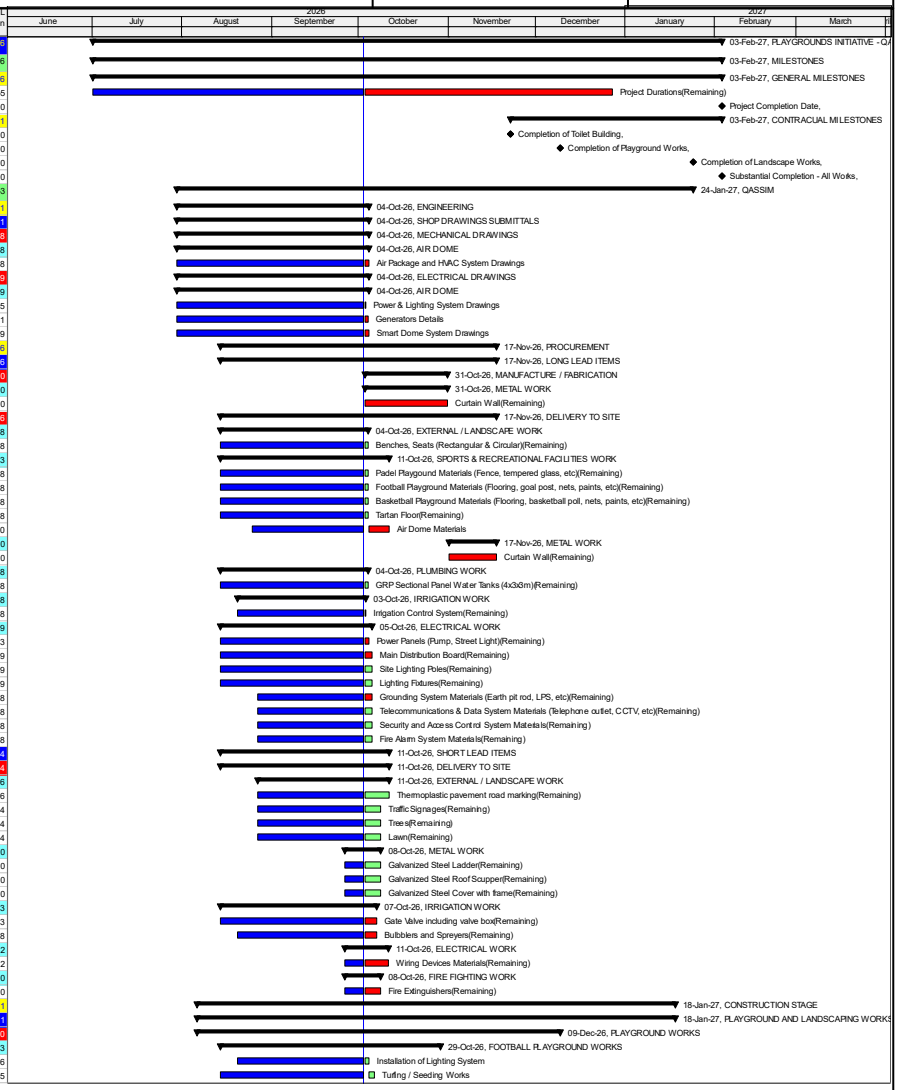

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EX-FB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	10-Oct-26	0.00	28,400.40	35,500.50	0%	80%	-22
PG-Q-CON-EX-FB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	20-Oct-26	0.00	1,030.08	2,060.16	0%	50%	-28
PG-Q-CON-EX-FB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	20-Oct-26	29-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		64	31-Aug-26	17-Nov-26	20-Aug-26 A	05-Nov-26	24,013.23	33,324.48	43,200.72	55.59%	77.14%	2
PG-Q-CON-EX-BB-80	Court Line Marking	15	31-Aug-26	16-Sep-26	20-Aug-26 A	07-Oct-26	13,091.76	10,473.41	13,091.76	100%	80%	-26
PG-Q-CON-EX-BB-60	Basketball Pole Installation & Alignment	17	17-Sep-26	07-Oct-26	20-Aug-26 A	11-Oct-26	10,921.47	12,377.66	15,472.08	70.59%	80%	-27
PG-Q-CON-EX-BB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	01-Oct-26 A	15-Oct-26	0.00	10,473.41	13,091.76	0%	80%	5
PG-Q-CON-EX-BB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	15-Oct-26	05-Nov-26	0.00	0.00	1,545.12	0%	0%	0
PADEL PLAYGROUND WORKS		86	11-Aug-26	02-Dec-26	06-Aug-26 A	09-Dec-26	11,956.48	123,700.98	173,328.96	6.9%	71.37%	-10
PG-Q-CON-EX-PD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26	31-Aug-26	20-Aug-26 A	10-Oct-26	3,534.96	2,474.47	3,534.96	100%	70%	-25
PG-Q-CON-EX-PD-60	Chain Link Fence & Gates Installation	16	01-Sep-26	19-Sep-26	20-Aug-26 A	15-Oct-26	5,302.44	3,711.71	5,302.44	100%	70%	-32
PG-Q-CON-EX-PD-50	Tempered Glass Installation	17	20-Sep-26	10-Oct-26	15-Oct-26	04-Nov-26	3,119.08	0.00	5,302.44	58.82%	0%	0
PG-Q-CON-EX-PD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	04-Nov-26	0.00	117,514.80	130,572.00	0%	90%	-61
PG-Q-CON-EX-PD-70	Court Accessories Installation	15	29-Oct-26	15-Nov-26	04-Nov-26	22-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-Q-CON-EX-PD-80	Install Playground Benches	15	16-Nov-26	02-Dec-26	22-Nov-26	09-Dec-26	0.00	0.00	1,545.12	0%	0%	0
GENERAL SITE WORKS		127	05-Jul-26	16-Dec-26	14-Aug-26 A	18-Jan-27	767,563.74	523,600.87	838,805.34	91.51%	62.42%	8
FENCE WORKS		58	02-Aug-26	13-Sep-26	20-Aug-26 A	29-Oct-26	19,745.64	7,240.07	19,745.64	100%	36.67%	-22
PG-Q-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-26	15-Aug-26	20-Aug-26 A	04-Oct-26	6,581.88	5,594.60	6,581.88	100%	85%	-26
PG-Q-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-26	01-Sep-26	27-Sep-26 A	18-Oct-26	6,581.88	1,645.47	6,581.88	100%	25%	-2
PG-Q-CON-EX-GN-FN-50	Installation of Gates	10	02-Sep-26	13-Sep-26	18-Oct-26	29-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		58	05-Jul-26	18-Aug-26	20-Aug-26 A	01-Nov-26	349,080.54	238,538.34	349,080.54	100%	68.33%	-22
STORM WATER AND UTILITY WORK		56	05-Jul-26	16-Aug-26	20-Aug-26 A	29-Oct-26	21,060.00	11,894.40	21,060.00	100%	56.48%	-22
PG-Q-CON-EX-GN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	04-Oct-26	4,128.00	3,302.40	4,128.00	100%	80%	-31
PG-Q-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	05-Oct-26	10,740.00	8,592.00	10,740.00	100%	80%	-32
PG-Q-CON-EX-GN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	05-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	13-Oct-26	20-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-26	16-Aug-26	22-Oct-26	29-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		5	03-Aug-26	09-Aug-26	20-Aug-26 A	22-Oct-26	327,702.60	226,643.94	327,702.60	100%	69.16%	-47
PG-Q-CON-EX-GN-M-90	Installation of Irrigation Control System	3	03-Aug-26	05-Aug-26	20-Aug-26 A	20-Oct-26	90,915.00	72,732.00	90,915.00	100%	80%	-49
PG-Q-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-26	09-Aug-26	27-Aug-26 A	22-Oct-26	236,787.60	153,911.94	236,787.60	100%	65%	-44
FIRE PROTECTION SYSTEM		2	17-Aug-26	18-Aug-26	29-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-Q-CON-EX-GN-M-110	Fire Extinguisher Installation	2	17-Aug-26	18-Aug-26	29-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		72	13-Aug-26	01-Nov-26	20-Aug-26 A	29-Dec-26	398,737.56	275,813.66	450,291.36	88.55%	61.25%	-43
POWER, LIGHTING & GROUNDING		37	13-Aug-26	20-Sep-26	20-Aug-26 A	18-Nov-26	393,221.16	275,813.66	393,221.16	100%	70.14%	-43
PG-Q-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-26	17-Aug-26	20-Aug-26 A	29-Oct-26	162,449.28	129,959.42	162,449.28	100%	80%	-56
PG-Q-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	29-Aug-26	31-Aug-26	27-Aug-26 A	01-Nov-26	8,265.00	6,612.00	8,265.00	100%	80%	-53
PG-Q-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	01-Sep-26	02-Sep-26	01-Nov-26	03-Nov-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-Q-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	03-Sep-26	08-Sep-26	03-Nov-26	09-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-Q-CON-EX-GN-E-60	Site Lighting Poles Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	10-Nov-26	174,052.80	139,242.24	174,052.80	100%	80%	-66
PG-Q-CON-EX-GN-E-70	Wiring Works	3	13-Sep-26	15-Sep-26	10-Nov-26	14-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-Q-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	16-Sep-26	20-Sep-26	14-Nov-26	18-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-26	20-Oct-26	18-Nov-26	17-Dec-26	4,028.70	0.00	43,146.00	9.34%	0%	0
PG-Q-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	21-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-Q-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	26-Sep-26	28-Sep-26	22-Nov-26	25-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-Q-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	29-Sep-26	03-Oct-26	25-Nov-26	30-Nov-26	2,789.10	0.00	3,718.80	75%	0%	0
PG-Q-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26	07-Oct-26	30-Nov-26	05-Dec-26	0.00	0.00	15,249.12	0%	0%	0
PG-Q-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	08-Oct-26	12-Oct-26	05-Dec-26	09-Dec-26	0.00	0.00	1,446.48	0%	0%	0
PG-Q-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	13-Oct-26	17-Oct-26	09-Dec-26	14-Dec-26	0.00	0.00	6,612.00	0%	0%	0
PG-Q-CON-EX-GN-E-150	IP Camera Installation	3	18-Oct-26	20-Oct-26	14-Dec-26	17-Dec-26	0.00	0.00	14,880.00	0%	0%	0
FIRE ALARM SYSTEM		32	26-Sep-26	01-Nov-26	22-Nov-26	29-Dec-26	1,487.70	0.00	13,924.20	10.68%	0%	0
PG-Q-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	26-Sep-26	04-Oct-26	22-Nov-26	01-Dec-26	1,487.70	0.00	1,983.60	75%	0%	0
PG-Q-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26	13-Oct-26	01-Dec-26	10-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-Q-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26	22-Oct-26	10-Dec-26	20-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-Q-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	24-Oct-26	01-Nov-26	20-Dec-26	29-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		5	04-Nov-26	09-Nov-26	23-Dec-26	29-Dec-26	0.00	0.00	14,479.80	0%	0%	0
PG-Q-CON-EX-GN-PR-30	Marking & Signages	5	04-Nov-26	09-Nov-26	23-Dec-26	29-Dec-26	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		26	19-Nov-26	16-Dec-26	14-Aug-26 A	18-Jan-27	0.00	2,008.80	5,208.00	0%	38.57%	-109
PG-Q-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-26	28-Nov-26	14-Aug-26 A	30-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-109
PG-Q-CON-EX-GN-SC-30	Connection to City Network	8	29-Nov-26	07-Dec-26	30-Dec-26	09-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-Q-CON-EX-GN-SC-40	Backfilling	8	08-Dec-26	16-Dec-26	09-Jan-27	18-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		55	30-Sep-26	14-Dec-26	20-Aug-26 A	09-Dec-26	8,529.23	180,726.98	429,915.30	1.98%	42.04%	-29
HARDSCAPE WORK		55	30-Sep-26	14-Dec-26	20-Aug-26 A	09-Dec-26	8,529.23	94,101.98	123,489.30	6.91%	76.2%	-29
PG-Q-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-26	14-Oct-26	27-Aug-26 A	31-Oct-26	8,529.23	47,124.00	55,440.00	15.38%	85%	-42
PG-Q-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-26	02-Dec-26	20-Aug-26 A	28-Nov-26	0.00	46,977.98	62,637.30	0%	75%	-74
PG-Q-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-26	14-Dec-26	28-Nov-26	09-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		30	15-Oct-26	21-Nov-26	27-Aug-26 A	24-Nov-26	0.00	86,625.00	306,426.00	0%	28.27%	-44
PG-Q-CON-EX-LS-SS-20_R	Lawn Area Reparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	04-Nov-26	0.00	86,625.00	115,500.00	0%	75%	-44
PG-Q-CON-EX-LS-SS-10	Planting Trees	17	02-Nov-26	21-Nov-26	04-Nov-26	24-Nov-26	0.00	0.00	190,926.00	0%	0%	0
TANK WORKS		8	11-Aug-26	19-Aug-26	04-Oct-26	13-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
WATER STORAGE TANK		8	11-Aug-26	19-Aug-26	04-Oct-26	13-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-Q-CON-EX-TW-IR-40	GRP Water Tank Installation	8	11-Aug-26	19-Aug-26	04-Oct-26	13-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		95	17-Aug-26	26-Nov-26	27-Aug-26 A	04-Jan-27	1,628,173.87	250,488.29	2,967,347.81	54.87%	8.44%	-24
CIVIL WORK		18	22-Aug-26	10-Sep-26	04-Oct-26	25-Oct-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-Q-CON-EX-AD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26	01-Sep-26	04-Oct-26	15-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EX-AD-CL-80	Installation of Membrane System	8	02-Sep-26	10-Sep-26	15-Oct-26	25-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
ARCHITECTURAL WORK		27	27-Oct-25	26-Nov-26	27-Aug-26 A	04-Jan-27	0.00	125,244.14	712,953.22	0%	17.57%	-84
PG-Q-CON-EX-AD-AR-10	Installation of Thermal Insulation System	8	27-Oct-25	04-Nov-26	27-Aug-26 A	13-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-84
PG-Q-CON-EX-AD-AR-40	Final Fixing of Accessories & Finishes	8	05-Nov-26	14-Nov-26	13-Dec-26	22-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EX-AD-AR-20	Installation of Doors & Access Systems	6	15-Nov-26	21-Nov-26	22-Dec-26	29-Dec-26	0.00	0.00	250,488.29	0%	0%	0
PG-Q-CON-EX-AD-AR-30	Installation of Logo	5	22-Nov-26	26-Nov-26	29-Dec-26	04-Jan-27	0.00	0.00	3,236.40	0%	0%	0
MECHANICAL WORK		16	12-Sep-26	30-Sep-26	25-Oct-26	12-Nov-26	667,968.77	0.00	667,968.77	100%	0%	0
PG-Q-CON-EX-AD-ME-10	Installation of Main Air Package Units	5	12-Sep-26	16-Sep-26	25-Oct-26	31-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EX-AD-ME-20	Installation of Backup Air Package Unit	5	17-Sep-26	22-Sep-26	31-Oct-26	05-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EX-AD-ME-30	Installation of Complete HVAC System	6	24-Sep-26	30-Sep-26	05-Nov-26	12-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
ELECTRICAL WORK		72	17-Aug-26	26-Oct-26	27-Aug-26 A	08-Dec-26	459,228.53	125,244.14	1,085,449.25	42.31%	11.54%	-28
PG-Q-CON-EX-AD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26	30-Aug-26	27-Aug-26 A	08-Oct-26	208,740.24	125,244.14	208,740.24	100%	60%	-24
PG-Q-CON-EX-AD-EL-20	Installation of Lighting System	12	31-Aug-26	13-Sep-26	08-Oct-26	22-Oct-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EX-AD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	01-Oct-26	06-Oct-26	12-Nov-26	18-Nov-26	41,748.05	0.00	208,740.24	20%	0%	0
PG-Q-CON-EX-AD-EL-40	Installation of Backup Generator	6	07-Oct-26	13-Oct-26	18-Nov-26	25-Nov-26	0.00	0.00	208,740.24	0%	0%	0
PG-Q-CON-EX-AD-EL-50	Installation of Smart Dome System	11	14-Oct-26	26-Oct-26	25-Nov-26	08-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		41	20-Aug-26	20-Oct-26	20-Aug-26 A	22-Nov-26	10,910.52	27,652.16	56,969.58	19.15%	48.54%	-27
CIVIL WORK		33	06-Oct-26	19-Oct-26	20-Aug-26 A	21-Nov-26	0.00	24,890.46	45,922.80	0%	54.2%	-67
ARCHITECTURAL WORK		33	06-Oct-26	19-Oct-26	20-Aug-26 A	21-Nov-26	0.00	24,890.46	45,922.80	0%	54.2%	-67
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	21-Nov-26	0.00	13,067.46	20,825.40	0%	62.75%	-63
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	14-Oct-26	0.00	9,291.66	13,273.80	0%	70%	-36
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	19-Sep-26 A	21-Nov-26	0.00	3,775.80	7,551.60	0%	50%	-49
WET AREA FINISHES		5	08-Oct-26	13-Oct-26	01-Oct-26 A	15-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-7
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	01-Oct-26 A	15-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-7
ROOF FINISHES		33	06-Oct-26	19-Oct-26	20-Aug-26 A	21-Nov-26	0.00	9,142.20	19,735.80	0%	46.32%	-67
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	13-Oct-26	0.00	9,142.20	10,158.00	0%	90%	-40
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26	19-Oct-26	19-Nov-26	21-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		39	20-Aug-26	20-Oct-26	01-Oct-26 A	22-Nov-26	10,910.52	2,761.70	11,046.78	98.77%	25%	8
MECANICAL WORKS		39	20-Aug-26	20-Oct-26	01-Oct-26 A	22-Nov-26	10,910.52	2,761.70	11,046.78	98.77%	25%	8
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	01-Oct-26 A	22-Nov-26	0.00	34.07	136.26	0%	25%	-43
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	01-Oct-26 A	22-Nov-26	0.00	34.07	136.26	0%	25%	-43
SEWER AND DRAINAGE SYSTEM		2	01-Sep-26	02-Sep-26	01-Oct-26 A	12-Oct-26	3,225.72	806.43	3,225.72	100%	25%	-8
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	01-Oct-26 A	12-Oct-26	3,225.72	806.43	3,225.72	100%	25%	-8
HVAC SYSTEM		3	20-Aug-26	23-Aug-26	01-Oct-26 A	05-Oct-26	7,684.80	1,921.20	7,684.80	100%	25%	0
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installtion	3	20-Aug-26	23-Aug-26	01-Oct-26 A	05-Oct-26	7,684.80	1,921.20	7,684.80	100%	25%	0
PROJECT CLOSOUT		36	15-Nov-26	16-Dec-26	06-Aug-26 A	24-Jan-27	0.00	271,831.87	1,701,141.38	0%	15.98%	-118
PG-Q-PCL-20	As-Built Drawings	15	15-Nov-26	02-Dec-26	23-Sep-26 A	12-Jan-27	0.00	35,075.08	175,375.40	0%	20%	-79
PG-Q-PCL-10_R	Testing, Commessioning for All Systems(Remaining)	11	15-Nov-26	26-Nov-26	06-Aug-26 A	04-Jan-27	0.00	236,756.79	473,513.58	0%	50%	-118
PG-Q-PCL-30	Snag list Submission	3	28-Nov-26	30-Nov-26	04-Jan-27	07-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-40	Snag list Closeout	10	01-Dec-26	12-Dec-26	07-Jan-27	19-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-50	Issuing Approvals	3	13-Dec-26	15-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	175,375.40	0%	0%	0
PG-Q-PCL-60	Handing Over	1	16-Dec-26	16-Dec-26	23-Jan-27	24-Jan-27	0.00	0.00	175,375.40	0%	0%	0
HAIL		130	25-Jun-26	16-Dec-26	09-Jul-26 A	16-Jan-27	1,880,511.70	1,621,207.24	3,264,064.16	57.61%	49.67%	-14
PROCUREMENT		59	25-Jun-26	26-Aug-26	06-Aug-26 A	03-Nov-26	516,988.47	460,355.44	516,988.47	100%	89.05%	-21
LONG LEAD ITEMS		59	25-Jun-26	26-Aug-26	06-Aug-26 A	03-Nov-26	423,859.72	388,815.28	423,859.72	100%	91.73%	-21
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
PG-HPR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		59	25-Jul-26	26-Aug-26	06-Aug-26 A	03-Nov-26	423,859.72	388,815.28	423,859.72	100%	91.73%	-46
EXTERNAL / LANDSCAPE WORK		29	25-Jul-26	06-Aug-26	06-Aug-26 A	04-Oct-26	72,919.30	66,425.88	72,919.30	100%	91.1%	-38
PG-HPR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	20-Aug-26 A	04-Oct-26	28,474.61	24,203.41	28,474.61	100%	85%	-26
PG-HPR-LL-LS-DL-10_R	Bike and Walk Path Matetals(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	03-Oct-26	44,444.70	42,222.46	44,444.70	100%	95%	-37
SPORTS & RECREATIONAL FACILITIES WORK		12	25-Jul-26	06-Aug-26	06-Aug-26 A	04-Oct-26	163,721.25	150,559.76	163,721.25	100%	91.96%	-37
PG-HPR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	06-Aug-26 A	03-Oct-26	64,212.75	61,002.11	64,212.75	100%	95%	-37
PG-HPR-LL-SPDL-20_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	04-Oct-26	99,508.50	89,557.65	99,508.50	100%	90%	-37
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	03-Nov-26	4,801.84	3,841.47	4,801.84	100%	80%	-45
PG-HPR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	05-Oct-26	688.66	550.93	688.66	100%	80%	-20
PG-HPR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	03-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-45
PLUMBING WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	05-Oct-26	9,372.51	7,498.01	9,372.51	100%	80%	-20
PG-HPR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	05-Oct-26	9,372.51	7,498.01	9,372.51	100%	80%	-20
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	04-Oct-26	173,044.81	160,490.15	173,044.81	100%	92.74%	-14
PG-HPR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	04-Oct-26	3,124.17	2,655.54	3,124.17	100%	85%	-23
PG-HPR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	04-Oct-26	2,499.34	2,124.44	2,499.34	100%	85%	-23
PG-HPR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	04-Oct-26	6,326.40	5,377.44	6,326.40	100%	85%	-23
PG-HPR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	03-Oct-26	134,020.66	127,319.62	134,020.66	100%	95%	-25
PG-HPR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	04-Oct-26	8,081.83	6,869.55	8,081.83	100%	85%	-26
PG-HPR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	04-Oct-26	6,170.09	5,244.58	6,170.09	100%	85%	-20
PG-HPR-LL-EL-DL-70_R	Security and Access Control System Matetals(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	04-Oct-26	7,811.37	6,639.66	7,811.37	100%	85%	-20
PG-HPR-LL-EL-DL-80_R	Fire Alarm System Matetals(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	04-Oct-26	5,010.96	4,259.31	5,010.96	100%	85%	-20
SHORT LEAD ITEMS		39	04-Jul-26	16-Jul-26	20-Aug-26 A	15-Oct-26	93,128.75	71,540.16	93,128.75	100%	76.82%	-36
DELIVERY TO SITE		39	04-Jul-26	16-Jul-26	20-Aug-26 A	15-Oct-26	93,128.75	71,540.16	93,128.75	100%	76.82%	-36
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	59,572.42	44,679.32	59,572.42	100%	75%	-21
PG-HPR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	3,311.47	2,483.60	3,311.47	100%	75%	-21
PG-HPR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	1,249.67	937.25	1,249.67	100%	75%	-21
PG-HPR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	30,441.29	22,830.96	30,441.29	100%	75%	-21
PG-HPR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	24,570.00	18,427.50	24,570.00	100%	75%	-21




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
IRRIGATION WORK		17	04-Jul-26	16-Jul-26	20-Aug-26 A	04-Oct-26	30,845.88	26,219.00	30,845.88	100%	85%	-26
PG-HPR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26	16-Jul-26	20-Aug-26 A	04-Oct-26	3,403.35	2,892.85	3,403.35	100%	85%	-26
PG-HPR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	04-Oct-26	27,442.53	23,326.15	27,442.53	100%	85%	-20
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	26-Sep-26 A	08-Oct-26	2,567.38	641.84	2,567.38	100%	25%	0
PG-HPR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26 A	08-Oct-26	2,567.38	641.84	2,567.38	100%	25%	0
FIRE FIGHTING WORK		12	04-Jul-26	16-Jul-26	03-Oct-26	15-Oct-26	143.07	0.00	143.07	100%	0%	0
PG-HPR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26	16-Jul-26	03-Oct-26	15-Oct-26	143.07	0.00	143.07	100%	0%	0
CONSTRUCTION STAGE		130	25-Jun-2	26-Nov-26	09-Jul-26 A	16-Jan-27	1,363,523.23	1,105,653.13	2,086,054.45	65.36%	53%	-30
PLAYGROUND AND LANDSCAPING WORKS		127	25-Jun-2	26-Nov-26	09-Jul-26 A	16-Jan-27	1,232,637.07	1,032,818.08	1,917,464.23	64.28%	53.86%	-30
PLAYGROUND WORKS		65	29-Jul-26	17-Nov-26	06-Aug-26 A	07-Nov-26	406,003.50	413,232.06	516,185.40	78.65%	80.05%	16
FOOTBALL PLAYGROUND WORKS		65	29-Jul-26	17-Nov-26	06-Aug-26 A	07-Nov-26	406,003.50	413,232.06	516,185.40	78.65%	80.05%	16
PG-HCON-EX-FB-50	Goal Post Foundation	17	29-Jul-26	17-Aug-26	20-Aug-26 A	07-Oct-26	35,500.50	26,625.38	35,500.50	100%	75%	-23
PG-HCON-EX-FB-120	Installation of Lighting System	13	18-Aug-2	01-Sep-26	27-Aug-26 A	12-Oct-26	48,720.00	31,668.00	48,720.00	100%	65%	-26
PG-HCON-EX-FB-90	Tufing / Seeding Works	12	02-Sep-2	15-Sep-26	14-Aug-26 A	15-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-40
PG-HCON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-2	04-Oct-26	06-Aug-26 A	15-Oct-26	298,116.00	309,582.00	343,980.00	86.67%	90%	-44
PG-HCON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-2	19-Oct-26	20-Aug-26 A	20-Oct-26	0.00	23,075.33	35,500.50	0%	65%	-39
PG-HCON-EX-FB-110	Install Playground Benches	15	20-Oct-2	05-Nov-26	27-Aug-26 A	26-Oct-26	0.00	3,347.76	5,150.40	0%	65%	-36
PG-HCON-EX-FB-100	Markings and Signages	10	07-Nov-2	17-Nov-26	27-Oct-26	07-Nov-26	0.00	0.00	23,667.00	0%	0%	0
GENERAL SITE WORKS		127	25-Jun-2	26-Nov-26	14-Aug-26 A	16-Jan-27	715,583.29	315,556.85	854,072.29	83.78%	36.95%	1
FENCE WORKS		37	23-Jul-26	16-Aug-26	27-Aug-26 A	13-Oct-26	39,491.28	13,163.76	39,491.28	100%	33.33%	-18
PG-HCON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26	02-Aug-26	27-Aug-26 A	04-Oct-26	13,163.76	10,531.01	13,163.76	100%	80%	-23
PG-HCON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-2	11-Aug-26	27-Sep-26 A	08-Oct-26	13,163.76	2,632.75	13,163.76	100%	20%	-1
PG-HCON-EX-GN-FN-50	Installation of Gates	4	12-Aug-2	16-Aug-26	08-Oct-26	13-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
MECHANICAL WORK		63	25-Jun-2	06-Aug-26	14-Aug-26 A	28-Oct-26	344,669.34	151,389.96	344,669.34	100%	43.92%	-27
STORM WATER AND UTILITY WORK		61	25-Jun-2	04-Aug-26	14-Aug-26 A	26-Oct-26	23,124.00	4,747.20	23,124.00	100%	20.53%	-27
PG-HCON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-2	06-Jul-26	14-Aug-26 A	04-Oct-26	1,032.00	877.20	1,032.00	100%	85%	-33
PG-HCON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	05-Oct-26	5,160.00	3,870.00	5,160.00	100%	75%	-28
PG-HCON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	05-Oct-26	10-Oct-26	10,740.00	0.00	10,740.00	100%	0%	0
PG-HCON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	10-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-HCON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	13-Oct-26	17-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-HCON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-2	04-Aug-26	21-Oct-26	26-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		34	21-Jul-26	30-Jul-26	14-Aug-26 A	21-Oct-26	321,227.40	146,642.76	321,227.40	100%	45.65%	-50
PG-HCON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	17-Oct-26	108,345.60	92,093.76	108,345.60	100%	85%	-51
PG-HCON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	18-Oct-26	90,915.00	54,549.00	90,915.00	100%	60%	-42
PG-HCON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	18-Oct-26	21-Oct-26	121,966.80	0.00	121,966.80	100%	0%	0
FIRE PROTECTION SYSTEM		2	05-Aug-2	06-Aug-26	26-Oct-26	28-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-HCON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-2	06-Aug-26	26-Oct-26	28-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		80	05-Aug-2	20-Oct-26	20-Aug-26 A	31-Dec-26	331,422.67	83,390.63	360,557.47	91.92%	23.13%	-49
POWER, LIGHTING & GROUNDING		45	05-Aug-2	08-Sep-26	20-Aug-26 A	21-Nov-26	303,487.27	83,390.63	303,487.27	100%	27.48%	-49
PG-HCON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-2	09-Aug-26	20-Aug-26 A	27-Oct-26	119,129.47	83,390.63	119,129.47	100%	70%	-55
PG-HCON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-2	19-Aug-26	28-Oct-26	01-Nov-26	8,265.00	0.00	8,265.00	100%	0%	0
PG-HCON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-2	22-Aug-26	01-Nov-26	03-Nov-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-HCON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-2	27-Aug-26	03-Nov-26	09-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-HCON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-2	31-Aug-26	09-Nov-26	12-Nov-26	127,638.72	0.00	127,638.72	100%	0%	0
PG-HCON-EX-GN-E-70	Wiring Works	3	01-Sep-2	03-Sep-26	12-Nov-26	16-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-HCON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-2	08-Sep-26	16-Nov-26	21-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-2	08-Oct-26	21-Nov-26	20-Dec-26	23,307.00	0.00	43,146.00	54.02%	0%	0
PG-HCON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-2	12-Sep-26	21-Nov-26	24-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-HCON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-2	15-Sep-26	24-Nov-26	28-Nov-26	619.80	0.00	619.80	100%	0%	0
PG-HCON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-2	20-Sep-26	28-Nov-26	02-Dec-26	3,718.80	0.00	3,718.80	100%	0%	0
PG-HCON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-2	26-Sep-26	02-Dec-26	07-Dec-26	15,249.12	0.00	15,249.12	100%	0%	0
PG-HCON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-2	30-Sep-26	07-Dec-26	12-Dec-26	1,446.48	0.00	1,446.48	100%	0%	0
PG-HCON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-2	05-Oct-26	12-Dec-26	16-Dec-26	1,653.00	0.00	6,612.00	25%	0%	0
PG-HCON-EX-GN-E-150	IP Camera Installation	3	06-Oct-2	08-Oct-26	16-Dec-26	20-Dec-26	0.00	0.00	14,880.00	0%	0%	0
FIRE ALARM SYSTEM		32	13-Sep-2	20-Oct-26	24-Nov-26	31-Dec-26	4,628.40	0.00	13,924.20	33.24%	0%	0
PG-HCON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-2	21-Sep-26	24-Nov-26	03-Dec-26	1,983.60	0.00	1,983.60	100%	0%	0
PG-HCON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-2	01-Oct-26	03-Dec-26	13-Dec-26	2,644.80	0.00	2,644.80	100%	0%	0
PG-HCON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-2	11-Oct-26	13-Dec-26	22-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-HCON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-2	20-Oct-26	22-Dec-26	31-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		27	10-Oct-2	20-Oct-26	20-Aug-26 A	31-Dec-26	0.00	64,822.50	104,146.20	0%	62.24%	-104
PG-HCON-EX-GN-PR-10	Installlation of Parking Accessories	5	10-Oct-2	14-Oct-26	20-Aug-26 A	22-Dec-26	0.00	64,822.50	86,430.00	0%	75%	-100
PG-HCON-EX-GN-PR-30	Marking & Signages	5	15-Oct-2	20-Oct-26	26-Dec-26	31-Dec-26	0.00	0.00	17,716.20	0%	0%	0
SERVICE CONNECTION		28	31-Oct-2	26-Nov-26	20-Aug-26 A	16-Jan-27	0.00	2,790.00	5,208.00	0%	53.57%	-102
PG-HCON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-2	08-Nov-26	20-Aug-26 A	03-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-107
PG-HCON-EX-GN-SC-30	Connection to City Network	8	09-Nov-2	17-Nov-26	03-Jan-27	12-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-HCON-EX-GN-SC-40	Backfilling	8	18-Nov-2	26-Nov-26	27-Aug-26 A	16-Jan-27	0.00	892.80	1,488.00	0%	60%	-112
LANDSCAPING WORKS		47	20-Sep-2	09-Nov-26	09-Jul-26 A	07-Dec-26	70,560.00	300,409.25	506,716.26	13.92%	59.29%	-66
HARDSCAPE WORK		47	20-Sep-2	09-Nov-26	09-Jul-26 A	07-Dec-26	70,560.00	259,459.25	355,477.26	19.85%	72.99%	-86
PG-HCON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-2	05-Oct-26	27-Aug-26 A	08-Nov-26	41,580.00	37,837.80	54,054.00	76.92%	70%	-48
PG-HCON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-2	07-Oct-26	30-Jul-26 A	08-Nov-26	28,980.00	39,123.00	43,470.00	66.67%	90%	-70
PG-HCON-EX-LS-HS-40_R	Bike Path and Walking Path Constructon(Remaining)	8	08-Oct-2	17-Oct-26	09-Jul-26 A	19-Nov-26	0.00	140,741.55	148,149.00	0%	95%	-105
PG-HCON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-2	28-Oct-26	30-Jul-26 A	25-Nov-26	0.00	41,756.90	104,392.26	0%	40%	-91
PG-HCON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	29-Oct-2	09-Nov-26	25-Nov-26	07-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		22	06-Oct-2	09-Nov-26	27-Aug-26 A	07-Dec-26	0.00	40,950.00	151,239.00	0%	27.08%	-57
PG-HCON-EX-LS-SS-10	Planting Trees	10	06-Oct-2	17-Oct-26	08-Nov-26	19-Nov-26	0.00	0.00	96,639.00	0%	0%	0

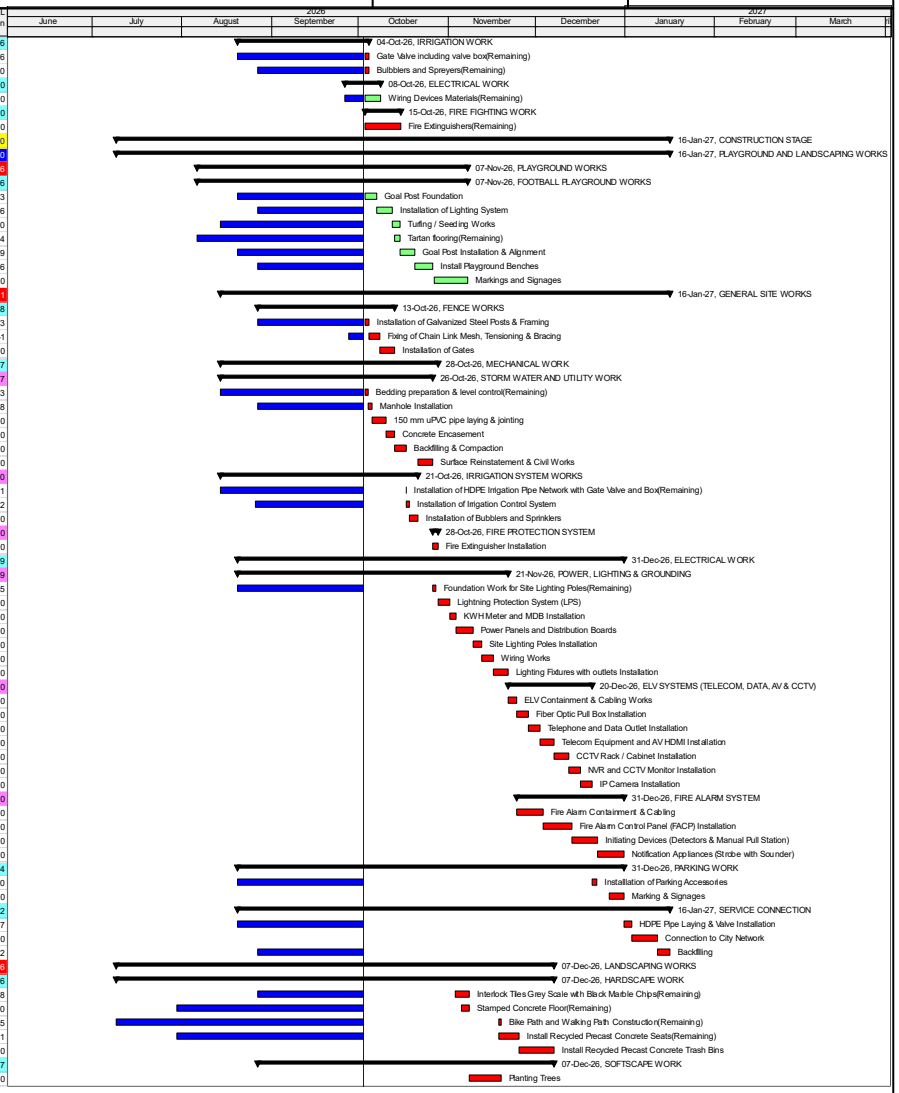

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00


PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-2	09-Nov-26	27-Aug-26 A	07-Dec-26	0.00	40,950.00	54,600.00	0%	75%	-80
TANK WORKS		67	02-Jul-26	19-Sep-26	14-Aug-26 A	03-Nov-26	40,490.28	3,619.92	40,490.28	100%	8.94%	0
SEPTIC TANK		62	02-Jul-26	31-Aug-26	14-Aug-26 A	28-Oct-26	5,777.28	3,619.92	5,777.28	100%	62.66%	-11
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26	09-Jul-26	14-Aug-26 A	05-Oct-26	2,757.60	1,930.32	2,757.60	100%	70%	-36
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26	18-Jul-26	27-Aug-26 A	07-Oct-26	2,599.38	1,689.60	2,599.38	100%	65%	-28
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-2	24-Aug-26	13-Oct-26	21-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-2	31-Aug-26	21-Oct-26	28-Oct-26	168.12	0.00	168.12	100%	0%	0
WATER STORAGE TANK		5	14-Sep-2	19-Sep-26	28-Oct-26	03-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-H-CON-EX-TW-IR-40	GRP Water Tank Installation	5	14-Sep-2	19-Sep-26	28-Oct-26	03-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
TOILET BUILDING WORKS		78	03-Aug-2	06-Oct-26	30-Jul-26 A	12-Nov-26	130,886.16	72,835.04	168,590.22	77.64%	43.2%	-34
CIVIL WORK		44	09-Sep-2	05-Oct-26	20-Aug-26 A	11-Nov-26	64,120.20	25,152.12	101,688.00	63.06%	24.73%	-48
ARCHITECTURAL WORK		44	09-Sep-2	05-Oct-26	20-Aug-26 A	11-Nov-26	64,120.20	25,152.12	101,688.00	63.06%	24.73%	-48
GENERAL FINISHES		26	09-Sep-2	05-Oct-26	20-Aug-26 A	11-Nov-26	48,463.80	11,553.78	72,432.60	66.91%	15.95%	-48
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-2	12-Sep-26	20-Aug-26 A	10-Oct-26	2,958.00	2,070.60	2,958.00	100%	70%	-40
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-2	20-Sep-26	20-Aug-26 A	12-Oct-26	273.60	191.52	273.60	100%	70%	-38
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-2	27-Sep-26	27-Aug-26 A	14-Oct-26	13,273.80	9,291.66	13,273.80	100%	70%	-36
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-2	05-Oct-26	03-Nov-26	11-Nov-26	31,958.40	0.00	55,927.20	57.14%	0%	0
WET AREA FINISHES		4	01-Oct-2	05-Oct-26	27-Aug-26 A	12-Oct-26	1,340.40	3,485.04	5,361.60	25%	65%	-34
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-2	05-Oct-26	27-Aug-26 A	12-Oct-26	1,340.40	3,485.04	5,361.60	25%	65%	-34
ROOF FINISHES		44	19-Sep-2	05-Oct-26	20-Aug-26 A	11-Nov-26	14,316.00	10,113.30	23,893.80	59.92%	42.33%	-56
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-2	22-Sep-26	20-Aug-26 A	12-Oct-26	4,158.00	2,494.80	4,158.00	100%	60%	-41
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-2	26-Sep-26	27-Aug-26 A	12-Oct-26	10,158.00	7,618.50	10,158.00	100%	75%	-37
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-2	05-Oct-26	09-Nov-26	11-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		78	03-Aug-2	06-Oct-26	30-Jul-26 A	12-Nov-26	66,765.96	47,682.92	66,902.22	99.8%	71.27%	-34
MECANICAL WORKS		78	03-Aug-2	06-Oct-26	30-Jul-26 A	12-Nov-26	50,502.24	33,858.76	50,638.50	99.73%	66.86%	-34
FIRE FIGHTING SYSTEM		1	06-Oct-2	06-Oct-26	11-Nov-26	12-Nov-26	0.00	0.00	136.26	0%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-2	06-Oct-26	11-Nov-26	12-Nov-26	0.00	0.00	136.26	0%	0%	0
SEWER AND DRAINAGE SYSTEM		47	03-Aug-2	23-Aug-26	30-Jul-26 A	07-Oct-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-40
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-2	04-Aug-26	30-Jul-26 A	03-Oct-26	3,225.72	2,741.86	3,225.72	100%	85%	-52
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-2	23-Aug-26	05-Oct-26	07-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-2	15-Aug-26	26-Sep-26 A	04-Oct-26	7,684.80	3,842.40	7,684.80	100%	50%	-5
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-2	15-Aug-26	26-Sep-26 A	04-Oct-26	7,684.80	3,842.40	7,684.80	100%	50%	-5
WATER SUPPLY SYSTEM		3	18-Aug-2	20-Aug-26	27-Aug-26 A	05-Oct-26	36,366.00	27,274.50	36,366.00	100%	75%	-29
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-2	20-Aug-26	27-Aug-26 A	05-Oct-26	36,366.00	27,274.50	36,366.00	100%	75%	-29
ELECTRICAL WORKS		11	27-Aug-2	08-Sep-26	20-Aug-26 A	08-Oct-26	16,263.72	13,824.16	16,263.72	100%	85%	-31
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-2	29-Aug-26	20-Aug-26 A	07-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-39
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-2	01-Sep-26	20-Aug-26 A	07-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-38
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-2	05-Sep-26	20-Aug-26 A	08-Oct-26	4,959.00	4,215.15	4,959.00	100%	85%	-38
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-2	08-Sep-26	20-Aug-26 A	08-Oct-26	7,337.52	6,236.89	7,337.52	100%	85%	-39
PROJECT CLOSOUT		37	02-Nov-2	16-Dec-26	06-Aug-26 A	09-Jan-27	0.00	55,198.68	681,021.24	0%	8.35%	-95
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-2	14-Nov-26	06-Aug-26 A	07-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-95
PG-H-PCL-20	As-Built Drawings	18	14-Nov-2	05-Dec-26	07-Dec-26	28-Dec-26	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-30	Snag list Submission	8	14-Nov-2	23-Nov-26	07-Dec-26	16-Dec-26	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-40	Snag list Closeout	14	23-Nov-2	09-Dec-26	16-Dec-26	02-Jan-27	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-50	Issuing Approvals	3	09-Dec-2	13-Dec-26	02-Jan-27	05-Jan-27	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-60	Handing Over	3	13-Dec-2	16-Dec-26	05-Jan-27	09-Jan-27	0.00	0.00	68,146.52	0%	0%	0
TABUK		158	25-Jun-2	16-Dec-26	12-Jul-26 A	03-Feb-27	3,832,478.39	1,976,993.88	7,301,102.06	52.49%	27.08%	-27
PROCUREMENT		63	25-Jun-2	27-Aug-26	06-Aug-26 A	21-Oct-26	2,157,429.76	1,184,097.22	2,157,429.76	100%	54.88%	-9
LONG LEAD ITEMS		54	01-Jul-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,118,427.42	1,150,173.89	2,118,427.42	100%	54.29%	-15
MANUFACTURE / FABRICATION		26	18-Jul-26	16-Aug-26	27-Aug-26 A	14-Oct-26	0.00	0.00	0.00	0%	0%	-14
SPORTS & RECREATIONAL FACILITIES WORK		26	18-Jul-26	16-Aug-26	27-Aug-26 A	14-Oct-26	0.00	0.00	0.00	0%	0%	-14
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26	16-Aug-26	27-Aug-26 A	14-Oct-26	0.00	0.00	0.00	100%	60%	-14
DELIVERY TO SITE		54	01-Jul-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,118,427.42	1,150,173.89	2,118,427.42	100%	54.29%	-15
EXTERNAL / LANDSCAPE WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-30
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-30
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,013,812.01	1,060,965.95	2,013,812.01	100%	52.68%	-34
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	58,731.75	52,858.58	58,731.75	100%	90%	-30
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	10,152.00	9,136.80	10,152.00	100%	90%	-30
PG-T-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	26,778.60	24,100.74	26,778.60	100%	90%	-30
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	04-Oct-26	39,487.50	35,538.75	39,487.50	100%	90%	-37
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-2	27-Aug-26	20-Aug-26 A	21-Oct-26	1,878,662.16	939,331.08	1,878,662.16	100%	50%	-42
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	08-Oct-26	4,001.54	2,401.70	4,001.54	100%	60.02%	-23
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	04-Oct-26	573.89	516.50	573.89	100%	90%	-19
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	08-Oct-26	3,427.65	1,885.21	3,427.65	100%	55%	-23
PLUMBING WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-30
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-30
IRRIGATION WORK		4	01-Jul-26	06-Jul-26	20-Aug-26 A	03-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-32
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	06-Jul-26	20-Aug-26 A	03-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-32
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	05-Oct-26	64,072.19	53,918.72	64,072.19	100%	84.15%	-16
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	03-Oct-26	3,615.08	3,072.82	3,615.08	100%	85%	-38
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	1,785.24	1,517.45	1,785.24	100%	85%	-31
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	1,428.19	1,213.96	1,428.19	100%	85%	-31
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	41,772.67	35,506.77	41,772.67	100%	85%	-31
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	4,618.19	3,925.46	4,618.19	100%	85%	-31
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-2	24-Aug-26	27-Aug-26 A	05-Oct-26	3,525.77	2,820.61	3,525.77	100%	80%	-20

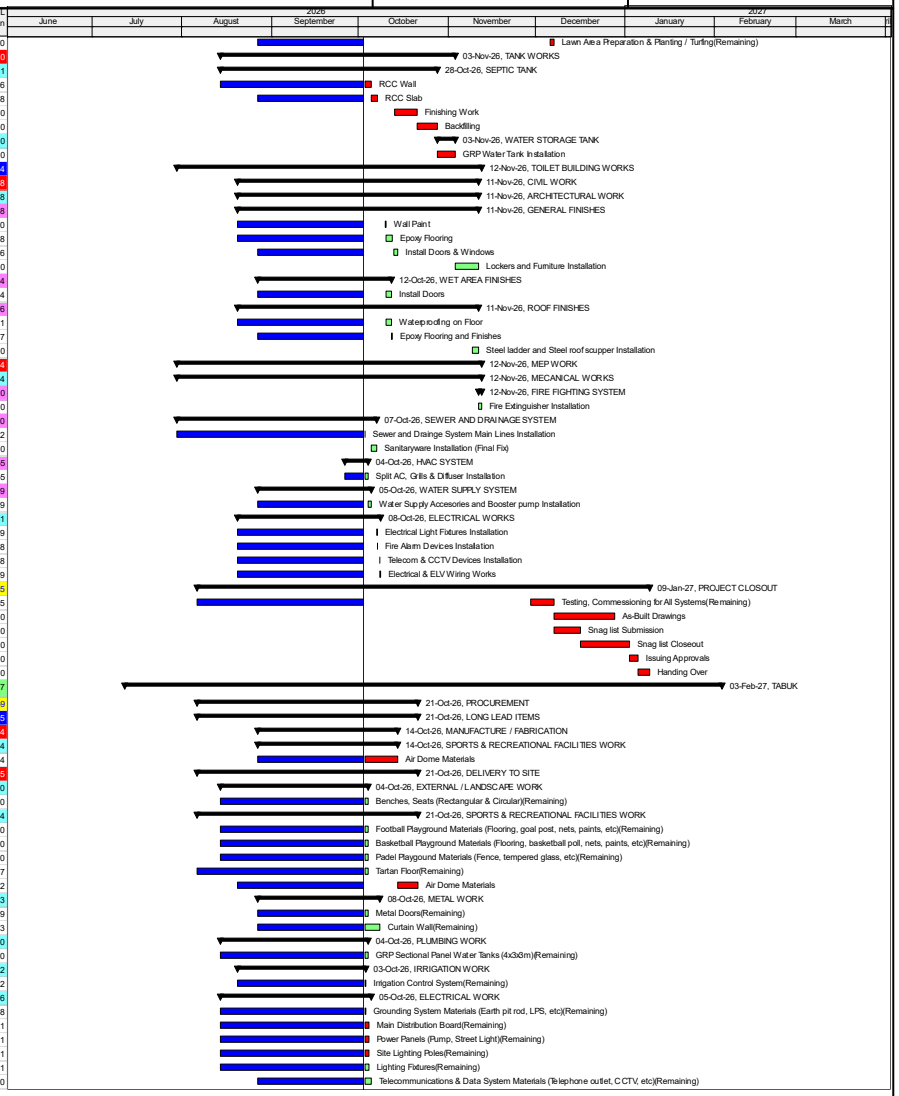

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-26	24-Aug-26	27-Aug-26 A	05-Oct-26	4,463.64	3,570.91	4,463.64	100%	80%	-20
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-26	24-Aug-26	27-Aug-26 A	05-Oct-26	2,863.40	2,290.72	2,863.40	100%	80%	-20
SHORT LEAD ITEMS		52	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Oct-26	39,002.34	33,923.33	39,002.34	100%	86.98%	-29
DELIVERY TO SITE		52	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Oct-26	39,002.34	33,923.33	39,002.34	100%	86.98%	-29
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	19,978.06	17,980.25	19,978.06	100%	90%	-21
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	714.10	642.69	714.10	100%	90%	-21
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	8,301.96	7,471.76	8,301.96	100%	90%	-21
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	10,962.00	9,865.80	10,962.00	100%	90%	-21
METAL WORK		12	25-Jun-26	08-Jul-26	23-Sep-26 A	08-Oct-26	1,724.00	862.00	1,724.00	100%	50%	-1
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	23-Sep-26 A	08-Oct-26	1,302.70	651.35	1,302.70	100%	50%	-1
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	08-Oct-26	112.75	56.38	112.75	100%	50%	-1
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	08-Oct-26	308.56	154.28	308.56	100%	50%	-1
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	03-Oct-26	14,977.04	13,479.33	14,977.04	100%	90%	-39
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	03-Oct-26	1,859.76	1,673.78	1,859.76	100%	90%	-39
PG-T-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	03-Oct-26	13,117.28	11,805.55	13,117.28	100%	90%	-28
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	19-Sep-26 A	06-Oct-26	2,200.61	1,540.43	2,200.61	100%	70%	-3
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	19-Sep-26 A	06-Oct-26	2,200.61	1,540.43	2,200.61	100%	70%	-3
FIRE FIGHTING WORK		9	30-Jun-26	09-Jul-26	27-Sep-26 A	07-Oct-26	122.63	61.32	122.63	100%	50%	-1
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26	09-Jul-26	27-Sep-26 A	07-Oct-26	122.63	61.32	122.63	100%	50%	-1
CONSTRUCTION STAGE		150	25-Jun-26	14-Dec-26	12-Jul-26 A	24-Jan-27	1,675,048.63	616,850.75	4,041,965.60	41.44%	15.26%	-21
PLAYGROUND AND LANDSCAPING WORKS		150	25-Jun-26	14-Dec-26	12-Jul-26 A	24-Jan-27	555,971.67	588,291.30	1,012,265.62	54.92%	58.12%	-21
PLAYGROUND WORKS		77	08-Aug-26	07-Dec-26	14-Aug-26 A	23-Nov-26	82,062.54	126,192.44	221,537.34	37.04%	56.96%	18
FOOTBALL PLAYGROUND WORKS		55	19-Aug-26	17-Nov-26	14-Aug-26 A	27-Oct-26	48,027.00	68,855.79	109,254.66	43.96%	63.02%	15
PG-T-CONEX-FB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	05-Oct-26	24,360.00	19,488.00	24,360.00	100%	80%	-26
PG-T-CONEX-FB-90	Tufing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	06-Oct-26	23,667.00	21,300.30	23,667.00	100%	90%	-33
PG-T-CONEX-FB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	11-Oct-26	0.00	26,625.38	35,500.50	0%	75%	-29
PG-T-CONEX-FB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	15-Oct-26	0.00	1,442.11	2,080.16	0%	70%	-29
PG-T-CONEX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	15-Oct-26	27-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		51	31-Aug-26	17-Nov-26	20-Aug-26 A	02-Nov-26	22,546.92	24,819.01	43,200.72	52.19%	57.45%	4
PG-T-CONEX-BB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	06-Oct-26	13,091.76	11,128.00	13,091.76	100%	85%	-24
PG-T-CONEX-BB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	11-Oct-26	9,455.16	12,377.66	15,472.08	61.11%	80%	-25
PG-T-CONEX-BB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	11-Oct-26	31-Oct-26	0.00	0.00	13,091.76	0%	0%	0
PG-T-CONEX-BB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	02-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-41
PADEL PLAYGROUND WORKS		63	08-Aug-26	07-Dec-26	20-Aug-26 A	23-Nov-26	11,488.62	32,517.64	69,081.96	16.63%	47.07%	23
PG-T-CONEX-PD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	07-Oct-26	3,534.96	3,004.72	3,534.96	100%	85%	-20
PG-T-CONEX-PD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	10-Oct-26	5,302.44	4,507.07	5,302.44	100%	85%	-25
PG-T-CONEX-PD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	10-Oct-26	31-Oct-26	2,651.22	0.00	5,302.44	50%	0%	0
PG-T-CONEX-PD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	02-Nov-26	0.00	23,692.50	26,325.00	0%	90%	-46
PG-T-CONEX-PD-70	Court Accessories Installation	16	02-Nov-26	19-Nov-26	02-Nov-26	21-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-T-CONEX-PD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	23-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-60
GENERAL SITE WORKS		150	25-Jun-26	14-Dec-26	12-Jul-26 A	24-Jan-27	409,193.37	278,888.83	497,741.02	82.21%	56.03%	-21
FENCE WORKS		45	27-Jul-26	17-Aug-26	20-Aug-26 A	14-Oct-26	19,745.64	8,227.35	19,745.64	100%	41.67%	-28
PG-T-CONEX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26	03-Aug-26	20-Aug-26 A	04-Oct-26	6,581.88	5,594.60	6,581.88	100%	85%	-30
PG-T-CONEX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-26	10-Aug-26	20-Sep-26 A	07-Oct-26	6,581.88	2,632.75	6,581.88	100%	40%	-9
PG-T-CONEX-GN-FN-50	Installation of Gates	6	11-Aug-26	17-Aug-26	07-Oct-26	14-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		72	01-Jul-26	10-Aug-26	12-Jul-26 A	25-Oct-26	206,336.28	167,571.01	206,336.28	100%	81.21%	-55
STORM WATER AND UTILITY WORK		49	01-Jul-26	04-Aug-26	20-Aug-26 A	19-Oct-26	22,092.00	9,498.00	22,092.00	100%	42.99%	-21
PG-T-CONEX-GN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	03-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-32
PG-T-CONEX-GN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	05-Oct-26	10,740.00	5,370.00	10,740.00	100%	50%	-9
PG-T-CONEX-GN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	06-Oct-26	08-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CONEX-GN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	10-Oct-26	12-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CONEX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	14-Oct-26	19-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	14-Oct-26	183,926.34	158,073.01	183,926.34	100%	85.94%	-66
PG-T-CONEX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	12-Oct-26	34,712.34	31,241.11	34,712.34	100%	90%	-75
PG-T-CONEX-GN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	13-Oct-26	90,915.00	77,277.75	90,915.00	100%	85%	-40
PG-T-CONEX-GN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	14-Oct-26	58,299.00	49,554.15	58,299.00	100%	85%	-42
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	19-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-T-CONEX-GN-M-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	19-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		114	25-Jun-26	07-Nov-26	20-Aug-26 A	03-Jan-27	183,111.45	90,258.87	239,107.30	76.58%	37.75%	-1
POWER, LIGHTING & GROUNDING		79	25-Jun-26	27-Sep-26	20-Aug-26 A	24-Nov-26	182,037.10	81,629.67	182,037.10	100%	44.84%	-1
PG-T-CONEX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	07-Oct-26	55,696.90	44,557.52	55,696.90	100%	80%	-19
PG-T-CONEX-GN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	26-Oct-26	8,265.00	7,025.25	8,265.00	100%	85%	-49
PG-T-CONEX-GN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	01-Nov-26	4,586.70	458.67	4,586.70	100%	10%	-32
PG-T-CONEX-GN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	08-Nov-26	17,397.90	1,739.79	17,397.90	100%	10%	-37
PG-T-CONEX-GN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	12-Nov-26	69,621.12	27,848.45	69,621.12	100%	40%	-41
PG-T-CONEX-GN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	12-Nov-26	17-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-T-CONEX-GN-E-80	Lighting Fixtures with outlets Installation	6	20-Sep-26	27-Sep-26	17-Nov-26	24-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	17-Dec-26	826.40	8,629.20	43,146.00	1.92%	20%	-48
PG-T-CONEX-GN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	26-Nov-26	619.80	123.96	619.80	100%	20%	-53
PG-T-CONEX-GN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	30-Nov-26	206.60	123.96	619.80	33.33%	20%	-55
PG-T-CONEX-GN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	03-Dec-26	0.00	743.76	3,718.80	0%	20%	-57
PG-T-CONEX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	07-Dec-26	0.00	3,049.82	15,249.12	0%	20%	-60
PG-T-CONEX-GN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	10-Dec-26	0.00	289.30	1,446.48	0%	20%	-64
PG-T-CONEX-GN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	14-Dec-26	0.00	1,322.40	6,612.00	0%	20%	-67
PG-T-CONEX-GN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	17-Dec-26	0.00	2,976.00	14,880.00	0%	20%	-70




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
FIRE ALARM SYSTEM		32	01-Oct-26	07-Nov-26	26-Nov-26	03-Jan-27	247.95	0.00	13,924.20	1.78%	0%	0
PG-T-CONEX-GN-E160	Fire Alarm Containment & Cabling	8	01-Oct-26	10-Oct-26	26-Nov-26	06-Dec-26	247.95	0.00	1,983.60	12.5%	0%	0
PG-T-CONEX-GN-E170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26	19-Oct-26	06-Dec-26	15-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-T-CONEX-GN-E180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26	28-Oct-26	15-Dec-26	24-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-T-CONEX-GN-E190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26	07-Nov-26	24-Dec-26	03-Jan-27	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		17	27-Oct-26	11-Nov-26	20-Aug-26 A	03-Jan-27	0.00	10,934.40	27,343.80	0%	39.99%	-102
PG-T-CONEX-GN-PR-10	Installation of Parking Accessories	7	27-Oct-26	03-Nov-26	20-Aug-26 A	19-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-95
PG-T-CONEX-GN-PR-30	Marking & Signages	7	04-Nov-26	11-Nov-26	26-Dec-26	03-Jan-27	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		27	12-Nov-26	14-Dec-26	14-Aug-26 A	24-Jan-27	0.00	1,897.20	5,208.00	0%	36.43%	-111
PG-T-CONEX-GN-SC-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	03-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-111
PG-T-CONEX-GN-SC-30	Connection to City Network	10	24-Nov-26	05-Dec-26	03-Jan-27	14-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-T-CONEX-GN-SC-40	Backfilling	8	06-Dec-26	14-Dec-26	14-Jan-27	24-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		38	28-Sep-26	22-Nov-26	12-Jul-26 A	02-Dec-26	24,393.60	182,106.99	252,665.10	9.65%	72.07%	-74
HARDSCAPE WORK		38	28-Sep-26	22-Nov-26	30-Jul-26 A	02-Dec-26	24,393.60	146,435.79	170,003.10	14.35%	86.14%	-58
PG-T-CONEX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	09-Nov-26	24,393.60	51,836.40	60,984.00	40%	85%	-53
PG-T-CONEX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26	20-Oct-26	30-Jul-26 A	09-Nov-26	0.00	39,123.00	43,470.00	0%	90%	-77
PG-T-CONEX-LS-HS-60_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	23-Nov-26	0.00	54,123.39	60,137.10	0%	90%	-89
PG-T-CONEX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	02-Dec-26	0.00	1,353.00	5,412.00	0%	25%	-49
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	35,671.20	82,662.00	0%	43.15%	-84
PG-T-CONEX-LS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	22-Nov-26	0.00	4,612.20	46,122.00	0%	10%	-40
PG-T-CONEX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	31,059.00	36,540.00	0%	85%	-116
TANK WORKS		71	07-Jul-26	27-Sep-26	14-Aug-26 A	08-Nov-26	40,322.16	1,103.04	40,322.16	100%	2.74%	-2
SEPTIC TANK		66	07-Jul-26	26-Aug-26	14-Aug-26 A	02-Nov-26	5,609.16	1,103.04	5,609.16	100%	19.66%	-23
PG-T-CONEX-TW-ST-40	RCC Wall	9	07-Jul-26	16-Jul-26	14-Aug-26 A	08-Oct-26	2,757.60	1,103.04	2,757.60	100%	40%	-37
PG-T-CONEX-TW-ST-50	RCC Slab	13	18-Jul-26	01-Aug-26	08-Oct-26	24-Oct-26	2,599.38	0.00	2,599.38	100%	0%	0
PG-T-CONEX-TW-ST-60	Finishing Work	8	18-Aug-26	26-Aug-26	24-Oct-26	02-Nov-26	252.18	0.00	252.18	100%	0%	0
WATER STORAGE TANK		5	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-T-CONEX-TW-IR-40	GRP Water Tank Installation	5	21-Sep-26	27-Sep-26	02-Nov-26	08-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		85	26-Aug-26	03-Dec-26	14-Oct-26	21-Jan-27	1,079,485.24	0.00	2,967,347.81	36.38%	0%	0
CIVIL WORK		17	26-Aug-26	14-Sep-26	14-Oct-26	03-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-T-CONEX-AD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-26	05-Sep-26	14-Oct-26	25-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CONEX-AD-CL-80	Installation of Membrane System	8	06-Sep-26	14-Sep-26	25-Oct-26	03-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		25	05-Nov-26	03-Dec-26	23-Dec-26	21-Jan-27	0.00	0.00	712,953.22	0%	0%	0
PG-T-CONEX-AD-AR-10	Installation of Thermal Insulation System	7	05-Nov-26	12-Nov-26	23-Dec-26	31-Dec-26	0.00	0.00	250,488.29	0%	0%	0
PG-T-CONEX-AD-AR-40	Final Fixing of Accessories & Finishes	7	14-Nov-26	21-Nov-26	31-Dec-26	09-Jan-27	0.00	0.00	208,740.24	0%	0%	0
PG-T-CONEX-AD-AR-20	Installation of Doors & Access Systems	6	22-Nov-26	28-Nov-26	09-Jan-27	16-Jan-27	0.00	0.00	250,488.29	0%	0%	0
PG-T-CONEX-AD-AR-30	Installation of Logo	5	29-Nov-26	03-Dec-26	16-Jan-27	21-Jan-27	0.00	0.00	3,236.40	0%	0%	0
MECHANICAL WORK		23	15-Sep-26	12-Oct-26	03-Nov-26	30-Nov-26	459,228.53	0.00	667,968.77	68.75%	0%	0
PG-T-CONEX-AD-ME-10	Installation of Main Air Package Units	5	15-Sep-26	20-Sep-26	03-Nov-26	09-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CONEX-AD-ME-20	Installation of Backup Air Package Unit	5	21-Sep-26	27-Sep-26	09-Nov-26	15-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CONEX-AD-ME-30	Installation of Complete HVAC System	6	06-Oct-26	12-Oct-26	23-Nov-26	30-Nov-26	0.00	0.00	208,740.24	0%	0%	0
ELECTRICAL WORK		33	28-Sep-26	04-Nov-26	15-Nov-26	23-Dec-26	119,280.14	0.00	1,085,449.25	10.99%	0%	0
PG-T-CONEX-AD-EL-10	Installation of Electrical Boxes & MDBs	7	28-Sep-26	05-Oct-26	15-Nov-26	23-Nov-26	119,280.14	0.00	208,740.24	57.14%	0%	0
PG-T-CONEX-AD-EL-20	Installation of Lighting System	7	06-Oct-26	13-Oct-26	23-Nov-26	01-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CONEX-AD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	14-Oct-26	19-Oct-26	01-Dec-26	07-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CONEX-AD-EL-40	Installation of Backup Generator	6	20-Oct-26	26-Oct-26	07-Dec-26	14-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CONEX-AD-EL-50	Installation of Smart Dome System	8	27-Oct-26	04-Nov-26	14-Dec-26	23-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		16	31-Aug-26	28-Oct-26	19-Sep-26 A	13-Oct-26	39,591.72	28,559.45	62,352.18	63.5%	45.8%	30
CIVIL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	6,033.03	14,939.40	0%	40.38%	-5
ARCHITECTURAL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	6,033.03	14,939.40	0%	40.38%	-5
WET AREA FINISHES		2	11-Oct-26	12-Oct-26	23-Sep-26 A	11-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-12
PG-T-CONB-AR-WF-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	11-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-12
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-16
PG-T-CONB-AR-RF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-16
MEP WORK		16	31-Aug-26	28-Oct-26	20-Sep-26 A	13-Oct-26	39,591.72	22,526.42	47,412.78	83.5%	47.51%	31
MECANICAL WORKS		16	31-Aug-26	28-Oct-26	20-Sep-26 A	13-Oct-26	39,591.72	22,526.42	47,412.78	83.5%	47.51%	31
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	13-Oct-26	0.00	40.88	136.26	0%	30%	-14
PG-T-CONB-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	13-Oct-26	0.00	40.88	136.26	0%	30%	-14
SEWER AND DRAINAGE SYSTEM		2	03-Sep-26	05-Sep-26	23-Sep-26 A	10-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-11
PG-T-CONB-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-26	05-Sep-26	23-Sep-26 A	10-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-11
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	11-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-15
PG-T-CONB-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	11-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-15
WATER SUPPLY SYSTEM		3	31-Aug-26	02-Sep-26	23-Sep-26 A	08-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-9
PG-T-CONB-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-26	02-Sep-26	23-Sep-26 A	08-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-9
PROJECT CLOSOUT		154	22-Nov-26	16-Dec-26	06-Aug-26 A	03-Feb-27	0.00	176,045.92	1,101,706.70	0%	15.98%	-133
PG-T-PCL-20	As-Built Drawings	15	22-Nov-26	09-Dec-26	23-Sep-26 A	28-Jan-27	0.00	22,715.60	113,578.01	0%	20%	-94
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-26	03-Dec-26	06-Aug-26 A	21-Jan-27	0.00	153,330.31	306,660.63	0%	50%	-133
PG-T-PCL-30	Snag list Submission	2	05-Dec-26	06-Dec-26	21-Jan-27	24-Jan-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-40	Snag list Closeout	7	07-Dec-26	14-Dec-26	24-Jan-27	01-Feb-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-50	Issuing Approvals	1	15-Dec-26	15-Dec-26	01-Feb-27	02-Feb-27	0.00	0.00	113,578.01	0%	0%	0
PG-T-PCL-60	Handing Over	1	16-Dec-26	16-Dec-26	02-Feb-27	03-Feb-27	0.00	0.00	113,578.01	0%	0%	0

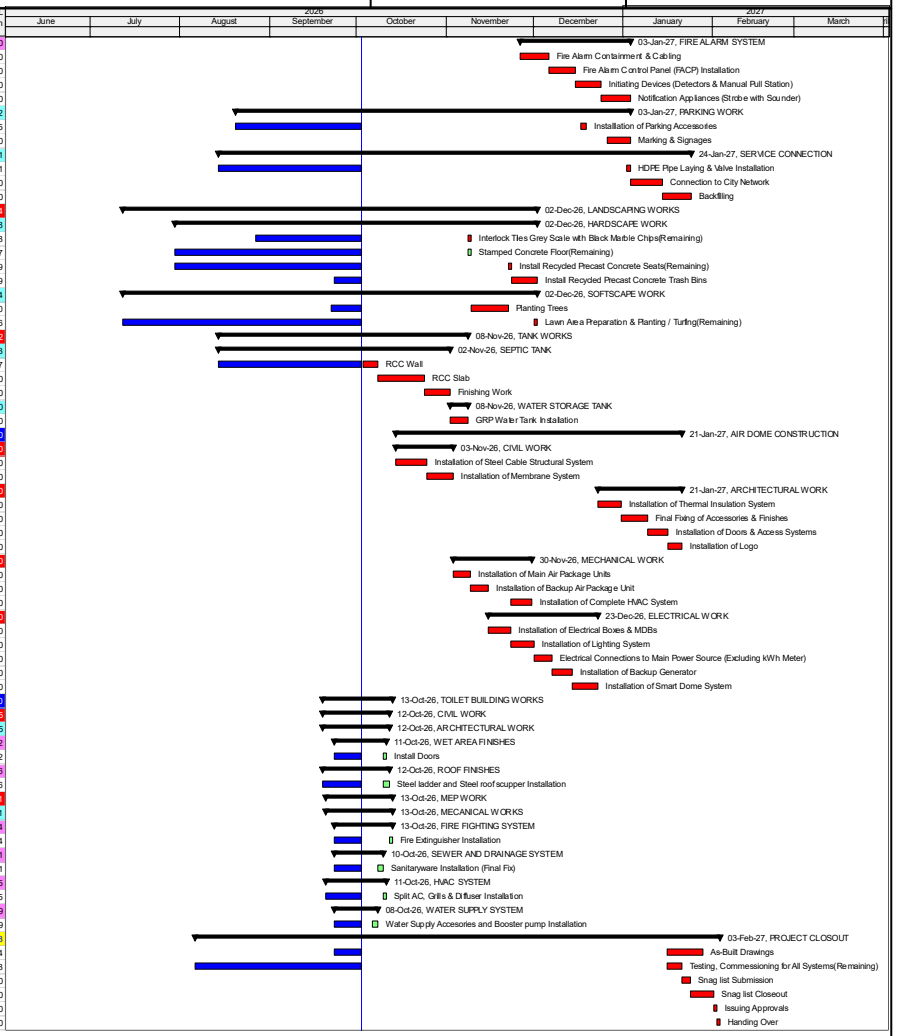

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
