
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026		162	25-Jun-26	15-Dec-26	01-Jul-26 A	04-Feb-27	9,126,881.72	7,148,966.98	11,849,909.26	77.02%	60.33%	-40
MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	03-Jan-27	0.00	0.00	0.00	0%	0%	-11
GENERAL MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	03-Jan-27	0.00	0.00	0.00	0%	0%	-11
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	03-Jan-27	0.00	0.00	0.00	61.02%	50%	-11
QASSIM		132	25-Jun-26	02-Dec-26	30-Jul-26 A	19-Jan-27	4,362,411.96	3,198,545.01	5,682,934.93	76.76%	56.28%	-10
ENGINEERING		35	25-Jun-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-27
SHOP DRAWINGS SUBMITTALS		35	25-Jun-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-27
MECHANICAL DRAWINGS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-44
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-44
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	100%	90%	-44
ELECTRICAL DRAWINGS		17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-45
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-45
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	10-Oct-26	0.00	0.00	0.00	100%	90%	-51
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	100%	90%	-47
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	100%	90%	-45
PROCUREMENT		71	25-Jun-26	27-Aug-26	14-Aug-26 A	07-Nov-26	2,536,743.99	1,701,749.04	2,536,743.99	100%	67.08%	-17
LONG LEAD ITEMS		71	25-Jun-26	27-Aug-26	14-Aug-26 A	07-Nov-26	2,383,025.05	1,594,567.33	2,383,025.05	100%	66.91%	-17
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		66	07-Jul-26	27-Aug-26	14-Aug-26 A	15-Oct-26	2,383,025.05	1,594,567.33	2,383,025.05	100%	66.91%	-8
EXTERNAL / LANDSCAPE WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	11-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-34
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	11-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-34
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	15-Oct-26	2,119,264.56	1,355,769.58	2,119,264.56	100%	63.97%	-17
PG-Q-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	46,985.40	44,636.13	46,985.40	100%	95%	-33
PG-Q-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	10,152.00	9,644.40	10,152.00	100%	95%	-33
PG-Q-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	10-Oct-26	26,778.60	25,439.67	26,778.60	100%	95%	-33
PG-Q-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	156,686.40	148,852.08	156,686.40	100%	95%	-33
PG-Q-PR-LL-SPDL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	25-Aug-26 A	15-Oct-26	1,878,662.16	1,127,197.30	1,878,662.16	100%	60%	-34
PLUMBING WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	7,810.43	7,419.90	7,810.43	100%	95%	-33
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	7,810.43	7,419.90	7,810.43	100%	95%	-33
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	10-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-34
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	10-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-34
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	11-Oct-26	221,065.50	198,958.95	221,065.50	100%	90%	-24
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	11-Oct-26	3,124.17	2,811.75	3,124.17	100%	90%	-34
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	1,785.24	1,606.72	1,785.24	100%	90%	-38
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	11-Oct-26	182,755.44	164,479.90	182,755.44	100%	90%	-34
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	11-Oct-26	8,081.83	7,273.65	8,081.83	100%	90%	-34
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	6,326.40	5,693.76	6,326.40	100%	90%	-23
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	6,170.09	5,553.08	6,170.09	100%	90%	-23
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	7,811.37	7,030.23	7,811.37	100%	90%	-23
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	5,010.96	4,509.86	5,010.96	100%	90%	-23
SHORT LEAD ITEMS		49	25-Jun-26	12-Jul-26	14-Aug-26 A	15-Oct-26	153,718.94	107,181.71	153,718.94	100%	69.73%	-38
DELIVERY TO SITE		49	25-Jun-26	12-Jul-26	14-Aug-26 A	15-Oct-26	153,718.94	107,181.71	153,718.94	100%	69.73%	-38
EXTERNAL / LANDSCAPE WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	14-Oct-26	78,553.04	54,797.90	78,553.04	100%	69.76%	-29
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	14-Oct-26	1,892.27	1,135.36	1,892.27	100%	60%	-29
PG-Q-PR-SL-LS-DL-60_R	Tiaffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	13-Oct-26	714.10	499.87	714.10	100%	70%	-28
PG-Q-PR-SL-LS-DL-70_R	Tiees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	13-Oct-26	34,366.68	24,056.68	34,366.68	100%	70%	-28
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	13-Oct-26	41,580.00	29,106.00	41,580.00	100%	70%	-28
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	1,724.00	1,206.80	1,724.00	100%	70%	-4
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	1,302.70	911.89	1,302.70	100%	70%	-4
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	112.75	78.93	112.75	100%	70%	-4
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	308.56	215.99	308.56	100%	70%	-4
IRRIGATION WORK		18	25-Jun-26	08-Jul-26	14-Aug-26 A	13-Oct-26	71,118.65	49,783.05	71,118.65	100%	70%	-39
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	13-Oct-26	7,186.00	5,030.20	7,186.00	100%	70%	-39
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	13-Oct-26	63,932.65	44,752.86	63,932.65	100%	70%	-34
ELECTRICAL WORK		15	25-Jun-26	12-Jul-26	26-Sep-26 A	15-Oct-26	2,200.61	1,320.36	2,200.61	100%	60%	-3
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26 A	15-Oct-26	2,200.61	1,320.36	2,200.61	100%	60%	-3
FIRE FIGHTING WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	14-Oct-26	122.63	73.58	122.63	100%	60%	-5
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	14-Oct-26	122.63	73.58	122.63	100%	60%	-5
CONSTRUCTION STAGE		110	05-Jul-26	02-Dec-26	06-Aug-26 A	06-Jan-27	1,825,667.97	1,224,964.10	2,497,301.96	73.11%	49.05%	-1
PLAYGROUND AND LANDSCAPING WORKS		110	05-Jul-26	02-Dec-26	06-Aug-26 A	06-Jan-27	887,494.32	944,443.84	1,280,964.84	69.28%	73.73%	-1
PLAYGROUND WORKS		96	11-Aug-26	17-Nov-26	06-Aug-26 A	09-Nov-26	105,389.08	227,449.85	297,167.22	35.46%	76.54%	4
FOOTBALL PLAYGROUND WORKS		58	19-Aug-26	17-Nov-26	14-Aug-26 A	03-Nov-26	62,227.20	69,276.10	109,254.66	56.96%	63.41%	8
PG-Q-CON-EXFB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	25-Oct-26	03-Nov-26	0.00	0.00	23,667.00	0%	0%	0
PG-Q-CON-EXFB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	25-Oct-26	0.00	1,236.10	2,060.16	0%	60%	-33
PG-Q-CON-EXFB-120	Installation of Lighting System	12	19-Aug-26	01-Sep-26	20-Aug-26 A	11-Oct-26	24,360.00	20,706.00	24,360.00	100%	85%	-32
PG-Q-CON-EXFB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	17-Oct-26	14,200.20	28,400.40	35,500.50	40%	80%	-28
PG-Q-CON-EXFB-90	Turfing / Seeding Works	10	02-Sep-26	13-Sep-26	14-Aug-26 A	13-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-41
BASKETBALL PLAYGROUND WORKS		70	31-Aug-26	17-Nov-26	20-Aug-26 A	03-Nov-26	29,333.94	33,942.53	43,200.72	67.9%	78.57%	4
PG-Q-CON-EXBB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	27-Sep-26 A	03-Nov-26	0.00	618.05	1,545.12	0%	40%	-14
PG-Q-CON-EXBB-60	Basketball Pole Installation & Alignment	17	17-Sep-26	07-Oct-26	20-Aug-26 A	18-Oct-26	15,472.08	12,377.66	15,472.08	100%	80%	-32
PG-Q-CON-EXBB-80	Court Line Marking	15	31-Aug-26	16-Sep-26	20-Aug-26 A	13-Oct-26	13,091.76	10,473.41	13,091.76	100%	80%	-31

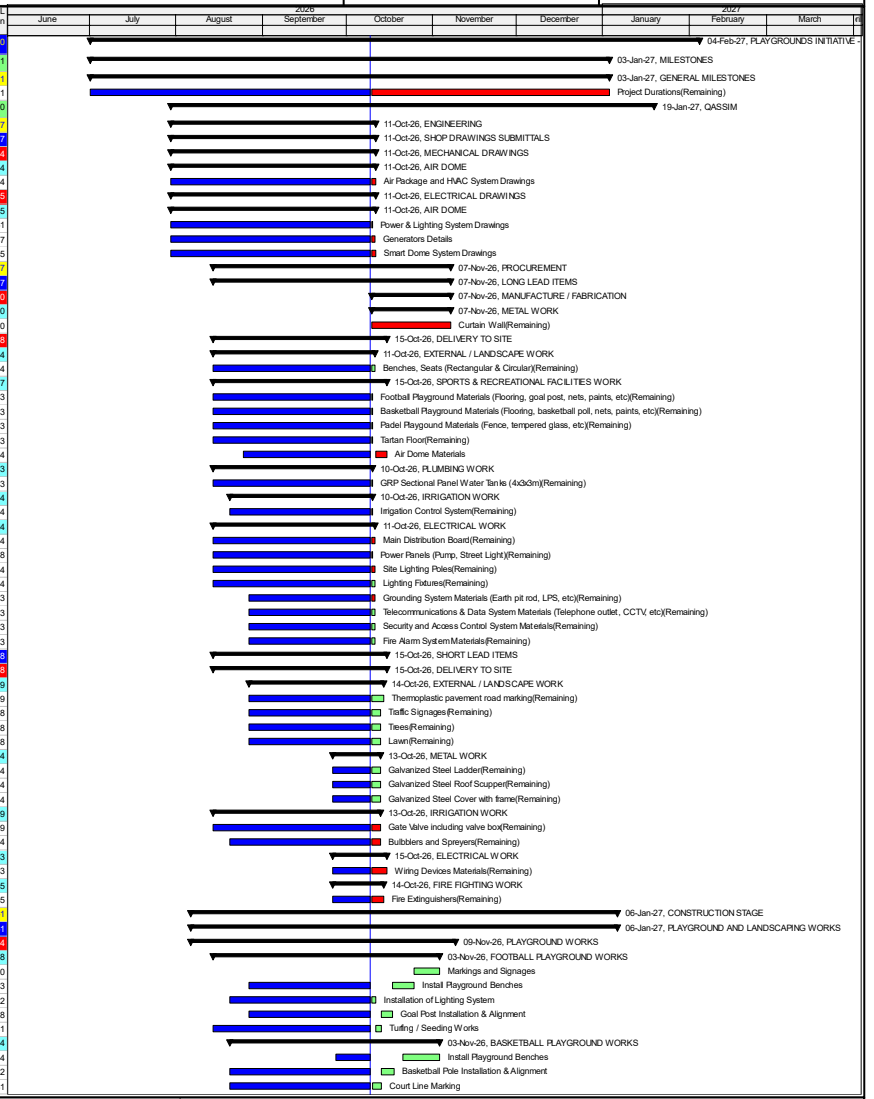

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EXBB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	01-Oct-26 A	21-Oct-26	770.10	10,473.41	13,091.76	5.88%	80%	0
PADEL PLAYGROUND WORKS		86	11-Aug-26	28-Oct-26	06-Aug-26 A	09-Nov-26	13,827.93	124,231.22	144,711.84	9.56%	85.85%	-13
PG-Q-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	09-Nov-26	0.00	117,514.80	130,572.00	0%	90%	-64
PG-Q-CON-EXPD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26	31-Aug-26	20-Aug-26 A	17-Oct-26	3,534.96	2,474.47	3,534.96	100%	70%	-30
PG-Q-CON-EXPD-50	Tempered Glass Installation	17	20-Sep-26	10-Oct-26	20-Oct-26	09-Nov-26	4,990.53	0.00	5,302.44	94.12%	0%	0
PG-Q-CON-EXPD-60	Chain Link Fence & Gates Installation	16	01-Sep-26	19-Sep-26	20-Aug-26 A	20-Oct-26	5,302.44	4,241.95	5,302.44	100%	80%	-35
GENERAL SITE WORKS		110	05-Jul-26	28-Nov-26	14-Aug-26 A	06-Jan-27	713,275.32	524,588.15	715,507.32	99.69%	73.32%	2
FENCE WORKS		62	02-Aug-26	13-Sep-26	20-Aug-26 A	02-Nov-26	19,745.64	8,227.35	19,745.64	100%	41.67%	-26
PG-Q-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-26	15-Aug-26	20-Aug-26 A	11-Oct-26	6,581.88	5,594.60	6,581.88	100%	85%	-32
PG-Q-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-26	01-Sep-26	27-Sep-26 A	21-Oct-26	6,581.88	2,632.75	6,581.88	100%	40%	-6
PG-Q-CON-EXGN-FN-50	Installation of Gates	10	02-Sep-26	13-Sep-26	21-Oct-26	02-Nov-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		62	05-Jul-26	16-Aug-26	20-Aug-26 A	05-Nov-26	348,762.60	238,538.34	348,762.60	100%	68.4%	-28
STORM WATER AND UTILITY WORK		62	05-Jul-26	16-Aug-26	20-Aug-26 A	05-Nov-26	21,060.00	11,894.40	21,060.00	100%	56.48%	-28
PG-Q-CON-EXGN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	11-Oct-26	4,128.00	3,302.40	4,128.00	100%	80%	-37
PG-Q-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	12-Oct-26	10,740.00	8,592.00	10,740.00	100%	80%	-38
PG-Q-CON-EXGN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	12-Oct-26	20-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	20-Oct-26	27-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-26	16-Aug-26	29-Oct-26	05-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		5	03-Aug-26	09-Aug-26	20-Aug-26 A	29-Oct-26	327,702.60	226,643.94	327,702.60	100%	69.16%	-53
PG-Q-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-26	09-Aug-26	27-Aug-26 A	29-Oct-26	236,787.60	153,911.94	236,787.60	100%	65%	-50
PG-Q-CON-EXGN-M-90	Installation of Irrigation Control System	3	03-Aug-26	05-Aug-26	20-Aug-26 A	27-Oct-26	90,915.00	72,732.00	90,915.00	100%	80%	-55
ELECTRICAL WORK		25	13-Aug-26	12-Sep-26	20-Aug-26 A	17-Nov-26	344,767.08	275,813.66	344,767.08	100%	80%	-49
POWER, LIGHTING & GROUNDING		25	13-Aug-26	12-Sep-26	20-Aug-26 A	17-Nov-26	344,767.08	275,813.66	344,767.08	100%	80%	-49
PG-Q-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-26	17-Aug-26	20-Aug-26 A	05-Nov-26	162,449.28	129,959.42	162,449.28	100%	80%	-62
PG-Q-CON-EXGN-E-30	Lightning Protection System (LPS)	3	29-Aug-26	31-Aug-26	27-Aug-26 A	08-Nov-26	8,265.00	6,612.00	8,265.00	100%	80%	-59
PG-Q-CON-EXGN-E-60	Site Lighting Poles Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	17-Nov-26	174,052.80	139,242.24	174,052.80	100%	80%	-72
SERVICE CONNECTION		8	19-Nov-26	28-Nov-26	14-Aug-26 A	06-Jan-27	0.00	2,008.80	2,232.00	0%	90%	-115
PG-Q-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-26	28-Nov-26	14-Aug-26 A	06-Jan-27	0.00	2,008.80	2,232.00	0%	90%	-115
LANDSCAPING WORKS		54	30-Sep-26	02-Dec-26	20-Aug-26 A	30-Nov-26	34,116.92	192,405.84	233,577.30	14.61%	82.37%	-31
HARDSCAPE WORK		54	30-Sep-26	02-Dec-26	20-Aug-26 A	30-Nov-26	34,116.92	100,005.84	118,077.30	28.89%	84.7%	-31
PG-Q-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-26	14-Oct-26	27-Aug-26 A	04-Nov-26	34,116.92	49,896.00	55,440.00	61.54%	90%	-45
PG-Q-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-26	02-Dec-26	20-Aug-26 A	30-Nov-26	0.00	50,109.84	62,637.30	0%	80%	-76
SOFTSCAPE WORK		15	15-Oct-26	01-Nov-26	27-Aug-26 A	08-Nov-26	0.00	92,400.00	115,500.00	0%	80%	-46
PG-Q-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	08-Nov-26	0.00	92,400.00	115,500.00	0%	80%	-46
TANK WORKS		8	11-Aug-26	19-Aug-26	10-Oct-26	19-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
WATER STORAGE TANK		8	11-Aug-26	19-Aug-26	10-Oct-26	19-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-Q-CON-EXTW-IR-40	GRP Water Tank Installation	8	11-Aug-26	19-Aug-26	10-Oct-26	19-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		76	17-Aug-26	04-Nov-26	27-Aug-26 A	20-Dec-26	918,457.06	250,488.29	1,168,945.34	78.57%	21.43%	-30
CIVIL WORK		18	22-Aug-26	10-Sep-26	11-Oct-26	01-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-Q-CON-EXAD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26	01-Sep-26	11-Oct-26	22-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXAD-CL-80	Installation of Membrane System	8	02-Sep-26	10-Sep-26	22-Oct-26	01-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		8	27-Oct-26	04-Nov-26	27-Aug-26 A	20-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-90
PG-Q-CON-EXAD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	20-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-90
ELECTRICAL WORK		38	17-Aug-26	13-Sep-26	27-Aug-26 A	29-Oct-26	417,480.48	125,244.14	417,480.48	100%	30%	-30
PG-Q-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26	30-Aug-26	27-Aug-26 A	15-Oct-26	208,740.24	125,244.14	208,740.24	100%	60%	-30
PG-Q-CON-EXAD-EL-20	Installation of Lighting System	12	31-Aug-26	13-Sep-26	15-Oct-26	29-Oct-26	208,740.24	0.00	208,740.24	100%	0%	0
TOILET BUILDING WORKS		39	20-Aug-26	20-Oct-26	20-Aug-26 A	28-Nov-26	19,716.60	30,031.97	47,391.78	41.6%	63.37%	-33
CIVIL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	26-Nov-26	8,806.08	26,717.94	36,345.00	24.23%	73.51%	-72
ARCHITECTURAL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	26-Nov-26	8,806.08	26,717.94	36,345.00	24.23%	73.51%	-72
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	26-Nov-26	2,654.76	13,822.62	20,825.40	12.75%	66.37%	-68
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	19-Oct-26	2,654.76	9,291.66	13,273.80	20%	70%	-40
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	19-Sep-26 A	26-Nov-26	0.00	4,530.96	7,551.60	0%	60%	-54
WET AREA FINISHES		5	08-Oct-26	13-Oct-26	01-Oct-26 A	19-Oct-26	1,072.32	3,753.12	5,361.60	20%	70%	-10
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	01-Oct-26 A	19-Oct-26	1,072.32	3,753.12	5,361.60	20%	70%	-10
ROOF FINISHES		6	06-Oct-26	12-Oct-26	20-Aug-26 A	18-Oct-26	5,079.00	9,142.20	10,158.00	50%	90%	-44
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	18-Oct-26	5,079.00	9,142.20	10,158.00	50%	90%	-44
MEP WORK		39	20-Aug-26	20-Oct-26	01-Oct-26 A	28-Nov-26	10,910.52	3,314.03	11,046.78	98.77%	30%	2
MECANICAL WORKS		39	20-Aug-26	20-Oct-26	01-Oct-26 A	28-Nov-26	10,910.52	3,314.03	11,046.78	98.77%	30%	2
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	01-Oct-26 A	28-Nov-26	0.00	40.88	136.26	0%	30%	-49
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	01-Oct-26 A	28-Nov-26	0.00	40.88	136.26	0%	30%	-49
SEWER AND DRAINAGE SYSTEM		2	01-Sep-26	02-Sep-26	01-Oct-26 A	18-Oct-26	3,225.72	967.72	3,225.72	100%	30%	-12
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	01-Oct-26 A	18-Oct-26	3,225.72	967.72	3,225.72	100%	30%	-12
HVAC SYSTEM		3	20-Aug-26	23-Aug-26	01-Oct-26 A	12-Oct-26	7,684.80	2,305.44	7,684.80	100%	30%	-6
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26	23-Aug-26	01-Oct-26 A	12-Oct-26	7,684.80	2,305.44	7,684.80	100%	30%	-6
PROJECT CLOSOUT		18	15-Nov-26	02-Dec-26	06-Aug-26 A	19-Jan-27	0.00	271,831.87	648,888.98	0%	41.89%	-126
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	15-Nov-26	26-Nov-26	06-Aug-26 A	11-Jan-27	0.00	236,756.79	473,513.58	0%	50%	-124
PG-Q-PCL-20	As-Built Drawings	15	15-Nov-26	02-Dec-26	23-Sep-26 A	19-Jan-27	0.00	35,075.08	175,375.40	0%	20%	-85
HAIL		113	25-Jun-26	26-Nov-26	09-Jul-26 A	21-Jan-27	1,763,447.41	1,717,346.97	2,379,610.32	74.11%	72.17%	-36
PROCUREMENT		65	25-Jun-26	26-Aug-26	06-Aug-26 A	10-Nov-26	516,988.47	464,851.03	516,988.47	100%	89.92%	-27
LONG LEAD ITEMS		65	25-Jun-26	26-Aug-26	06-Aug-26 A	10-Nov-26	423,859.72	386,426.43	423,859.72	100%	91.17%	-27
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	100%	0%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
DELIVERY TO SITE		59	25-Jul-26	26-Aug-26	06-Aug-26 A	10-Nov-26	423,859.72	386,426.43	423,859.72	100%	91.17%	-52
EXTERNAL / LANDSCAPE WORK		29	25-Jul-26	05-Aug-26	06-Aug-26 A	11-Oct-26	72,919.30	67,849.61	72,919.30	100%	93.05%	-43
PG-H-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	05-Aug-26	06-Aug-26 A	10-Oct-26	44,444.70	42,222.46	44,444.70	100%	95%	-43
PG-H-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	05-Aug-26	20-Aug-26 A	11-Oct-26	28,474.61	25,627.14	28,474.61	100%	90%	-31
SPORTS & RECREATIONAL FACILITIES WORK		12	25-Jul-26	05-Aug-26	06-Aug-26 A	11-Oct-26	163,721.25	150,559.76	163,721.25	100%	91.96%	-43
PG-H-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	05-Aug-26	06-Aug-26 A	10-Oct-26	64,212.75	61,002.11	64,212.75	100%	95%	-43
PG-H-PR-LL-SP-DL-20_R	Tartan Floor(Remaining)	12	25-Jul-26	05-Aug-26	06-Aug-26 A	11-Oct-26	99,508.50	89,557.65	99,508.50	100%	90%	-43
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	10-Nov-26	4,801.84	3,841.47	4,801.84	100%	80%	-51
PG-H-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	12-Oct-26	688.66	550.93	688.66	100%	80%	-26
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	10-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-51
PLUMBING WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	11-Oct-26	9,372.51	8,435.26	9,372.51	100%	90%	-25
PG-H-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	11-Oct-26	9,372.51	8,435.26	9,372.51	100%	90%	-25
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	11-Oct-26	173,044.81	155,740.33	173,044.81	100%	90%	-19
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	10-Oct-26	3,124.17	2,811.75	3,124.17	100%	90%	-29
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	10-Oct-26	2,499.34	2,249.40	2,499.34	100%	90%	-29
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	11-Oct-26	134,020.66	120,618.59	134,020.66	100%	90%	-31
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	11-Oct-26	8,081.83	7,273.65	8,081.83	100%	90%	-31
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	10-Oct-26	6,326.40	5,693.76	6,326.40	100%	90%	-29
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	11-Oct-26	6,170.09	5,553.08	6,170.09	100%	90%	-25
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	11-Oct-26	7,811.37	7,030.23	7,811.37	100%	90%	-25
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	11-Oct-26	5,010.96	4,509.86	5,010.96	100%	90%	-25
SHORT LEAD ITEMS		45	04-Jul-26	16-Jul-26	20-Aug-26 A	20-Oct-26	93,128.75	78,424.60	93,128.75	100%	84.21%	-40
DELIVERY TO SITE		45	04-Jul-26	16-Jul-26	20-Aug-26 A	20-Oct-26	93,128.75	78,424.60	93,128.75	100%	84.21%	-40
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	59,572.42	50,636.56	59,572.42	100%	85%	-26
PG-H-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	3,311.47	2,814.75	3,311.47	100%	85%	-26
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	1,249.67	1,062.22	1,249.67	100%	85%	-26
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	30,441.29	25,875.09	30,441.29	100%	85%	-26
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	24,570.00	20,884.50	24,570.00	100%	85%	-26
IRRIGATION WORK		17	04-Jul-26	16-Jul-26	20-Aug-26 A	11-Oct-26	30,845.88	26,219.00	30,845.88	100%	85%	-32
PG-H-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26	16-Jul-26	20-Aug-26 A	11-Oct-26	3,403.35	2,892.85	3,403.35	100%	85%	-32
PG-H-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	27,442.53	23,326.15	27,442.53	100%	85%	-26
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	26-Sep-26 A	14-Oct-26	2,567.38	1,540.43	2,567.38	100%	60%	-5
PG-H-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26 A	14-Oct-26	2,567.38	1,540.43	2,567.38	100%	60%	-5
FIRE FIGHTING WORK		12	04-Jul-26	16-Jul-26	03-Oct-26 A	20-Oct-26	143.07	28.61	143.07	100%	20%	-4
PG-H-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26	16-Jul-26	03-Oct-26 A	20-Oct-26	143.07	28.61	143.07	100%	20%	-4
CONSTRUCTION STAGE		113	25-Jun-26	26-Nov-26	09-Jul-26 A	21-Jan-27	1,246,458.95	1,197,297.26	1,678,626.25	74.25%	71.33%	-36
PLAYGROUND AND LANDSCAPING WORKS		110	25-Jun-26	26-Nov-26	09-Jul-26 A	21-Jan-27	1,087,582.79	1,096,246.43	1,519,750.09	71.56%	72.13%	-36
PLAYGROUND WORKS		67	29-Jul-26	17-Nov-26	06-Aug-26 A	09-Nov-26	462,790.73	422,169.15	516,185.40	89.66%	81.79%	14
FOOTBALL PLAYGROUND WORKS		67	29-Jul-26	17-Nov-26	06-Aug-26 A	09-Nov-26	462,790.73	422,169.15	516,185.40	89.66%	81.79%	14
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	28-Oct-26	09-Nov-26	0.00	0.00	23,667.00	0%	0%	0
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	28-Oct-26	0.00	3,862.80	5,150.40	0%	75%	-38
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26	01-Sep-26	27-Aug-26 A	17-Oct-26	48,720.00	36,540.00	48,720.00	100%	75%	-30
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26	04-Oct-26	06-Aug-26 A	20-Oct-26	343,980.00	309,582.00	343,980.00	100%	90%	-48
PG-H-CON-EX-FB-50	Goal Post Foundation	17	29-Jul-26	17-Aug-26	20-Aug-26 A	13-Oct-26	35,500.50	28,400.40	35,500.50	100%	80%	-28
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	24-Oct-26	10,923.23	24,850.35	35,500.50	30.77%	70%	-42
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26	15-Sep-26	14-Aug-26 A	20-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-44
GENERAL SITE WORKS		110	25-Jun-26	26-Nov-26	14-Aug-26 A	21-Jan-27	502,972.15	346,033.93	593,122.15	84.8%	58.34%	-5
FENCE WORKS		41	23-Jul-26	16-Aug-26	27-Aug-26 A	17-Oct-26	39,491.28	22,378.39	39,491.28	100%	56.67%	-22
PG-H-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26	02-Aug-26	27-Aug-26 A	10-Oct-26	13,163.76	11,847.38	13,163.76	100%	90%	-28
PG-H-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-26	11-Aug-26	27-Sep-26 A	12-Oct-26	13,163.76	10,531.01	13,163.76	100%	80%	-5
PG-H-CON-EX-GN-FN-50	Installation of Gates	4	12-Aug-26	16-Aug-26	12-Oct-26	17-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
MECHANICAL WORK		66	25-Jun-26	04-Aug-26	14-Aug-26 A	02-Nov-26	344,351.40	160,739.46	344,351.40	100%	46.68%	-32
STORM WATER AND UTILITY WORK		66	25-Jun-26	04-Aug-26	14-Aug-26 A	02-Nov-26	23,124.00	5,005.20	23,124.00	100%	21.65%	-32
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	11-Oct-26	1,032.00	877.20	1,032.00	100%	85%	-39
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	12-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-34
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	12-Oct-26	17-Oct-26	10,740.00	0.00	10,740.00	100%	0%	0
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	17-Oct-26	20-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	20-Oct-26	24-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	28-Oct-26	02-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		40	21-Jul-26	30-Jul-26	14-Aug-26 A	28-Oct-26	321,227.40	155,734.26	321,227.40	100%	48.48%	-55
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	25-Oct-26	28-Oct-26	121,966.80	0.00	121,966.80	100%	0%	0
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	24-Oct-26	108,345.60	92,093.76	108,345.60	100%	85%	-57
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	25-Oct-26	90,915.00	63,640.50	90,915.00	100%	70%	-47
ELECTRICAL WORK		4	05-Aug-26	09-Aug-26	20-Aug-26 A	03-Nov-26	119,129.47	95,303.58	119,129.47	100%	80%	-60
POWER, LIGHTING & GROUNDING		4	05-Aug-26	09-Aug-26	20-Aug-26 A	03-Nov-26	119,129.47	95,303.58	119,129.47	100%	80%	-60
PG-H-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-26	09-Aug-26	20-Aug-26 A	03-Nov-26	119,129.47	95,303.58	119,129.47	100%	80%	-60
PARKING WORK		5	10-Oct-26	14-Oct-26	20-Aug-26 A	28-Dec-26	0.00	64,822.50	86,430.00	0%	75%	-106
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	28-Dec-26	0.00	64,822.50	86,430.00	0%	75%	-106
SERVICE CONNECTION		11	31-Oct-26	26-Nov-26	20-Aug-26 A	21-Jan-27	0.00	2,790.00	3,720.00	0%	75%	-108
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	09-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-113
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26	26-Nov-26	27-Aug-26 A	21-Jan-27	0.00	892.80	1,488.00	0%	60%	-118
LANDSCAPING WORKS		43	20-Sep-26	09-Nov-26	09-Jul-26 A	08-Dec-26	116,042.63	324,017.71	404,665.26	28.68%	80.07%	-87
HARDSCAPE WORK		33	20-Sep-26	28-Oct-26	09-Jul-26 A	26-Nov-26	116,042.63	280,337.71	350,065.26	33.15%	80.08%	-87

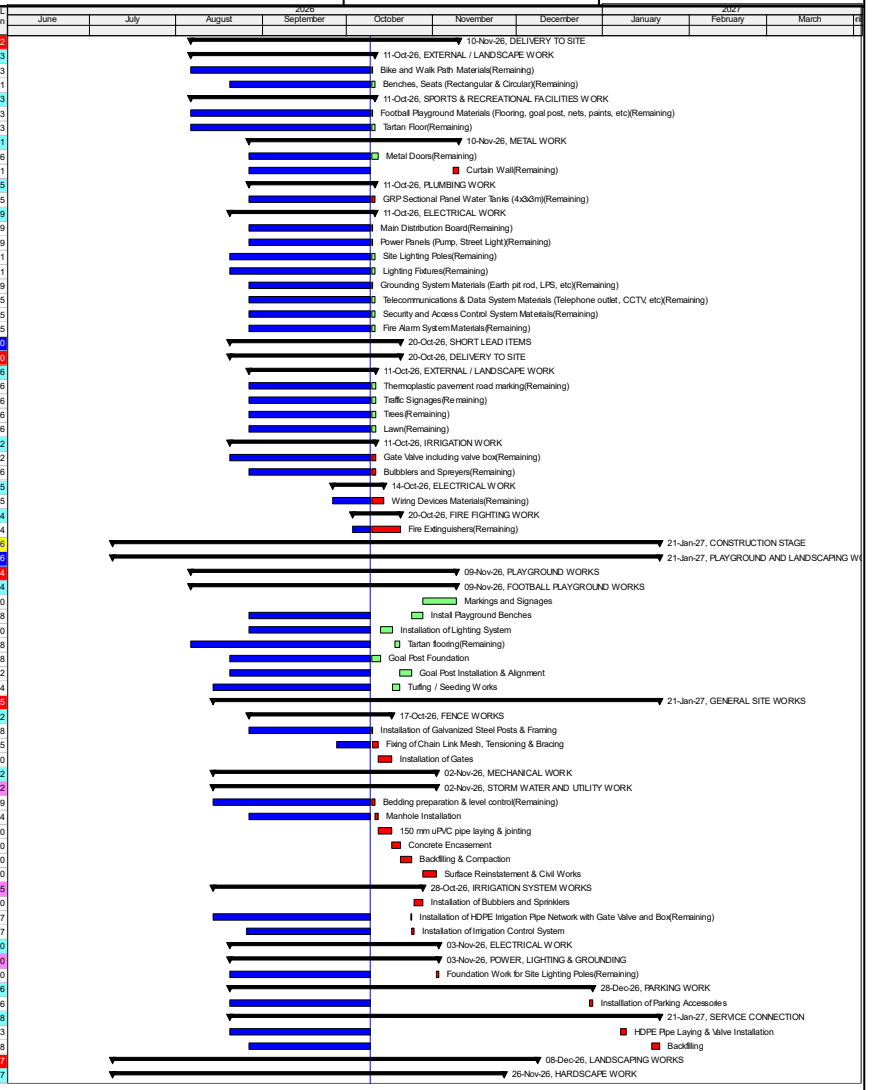

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00


PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-2	05-Oct-26	27-Aug-26 A	11-Nov-26	54,054.00	37,837.80	54,054.00	100%	70%	-51
PG-H-CON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-2	07-Oct-26	30-Jul-26 A	11-Nov-26	43,470.00	39,123.00	43,470.00	100%	90%	-73
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	23-Nov-26	18,518.63	140,741.55	148,149.00	12.5%	95%	-108
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	26-Nov-26	0.00	62,635.36	104,392.26	0%	60%	-92
SOFTSCAPE WORK		7	02-Nov-2	09-Nov-26	27-Aug-26 A	08-Dec-26	0.00	43,680.00	54,600.00	0%	80%	-82
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Ranting / Turfing(Remaining)	7	02-Nov-2	09-Nov-26	27-Aug-26 A	08-Dec-26	0.00	43,680.00	54,600.00	0%	80%	-82
TANK WORKS		65	02-Jul-26	31-Aug-26	14-Aug-26 A	01-Nov-26	5,777.28	4,025.65	5,777.28	100%	69.68%	-15
SEPTIC TANK		65	02-Jul-26	31-Aug-26	14-Aug-26 A	01-Nov-26	5,777.28	4,025.65	5,777.28	100%	69.68%	-15
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26	09-Jul-26	14-Aug-26 A	11-Oct-26	2,757.60	2,206.08	2,757.60	100%	80%	-41
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26	18-Jul-26	27-Aug-26 A	13-Oct-26	2,599.38	1,819.57	2,599.38	100%	70%	-33
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-2	24-Aug-26	17-Oct-26	25-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-2	31-Aug-26	25-Oct-26	01-Nov-26	168.12	0.00	168.12	100%	0%	0
TOILET BUILDING WORKS		83	03-Aug-2	05-Oct-26	30-Jul-26 A	15-Nov-26	158,876.16	101,050.82	158,876.16	100%	63.6%	-38
CIVIL WORK		50	09-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	92,110.20	50,781.12	92,110.20	100%	55.13%	-52
ARCHITECTURAL WORK		50	09-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	92,110.20	50,781.12	92,110.20	100%	55.13%	-52
GENERAL FINISHES		32	09-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	72,432.60	35,575.20	72,432.60	100%	49.11%	-52
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-2	12-Sep-26	20-Aug-26 A	17-Oct-26	2,958.00	2,366.40	2,958.00	100%	80%	-45
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-2	20-Sep-26	20-Aug-26 A	18-Oct-26	273.60	218.88	273.60	100%	80%	-42
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-2	27-Sep-26	27-Aug-26 A	19-Oct-26	13,273.80	10,619.04	13,273.80	100%	80%	-39
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-2	05-Oct-26	04-Oct-26 A	15-Nov-26	55,927.20	22,370.88	55,927.20	100%	40%	-30
WET AREA FINISHES		4	01-Oct-26	05-Oct-26	27-Aug-26 A	18-Oct-26	5,361.60	3,753.12	5,361.60	100%	70%	-39
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26	05-Oct-26	27-Aug-26 A	18-Oct-26	5,361.60	3,753.12	5,361.60	100%	70%	-39
ROOF FINISHES		36	19-Sep-2	26-Sep-26	20-Aug-26 A	18-Oct-26	14,316.00	11,452.80	14,316.00	100%	80%	-43
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-2	22-Sep-26	20-Aug-26 A	17-Oct-26	4,158.00	3,326.40	4,158.00	100%	80%	-45
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-2	26-Sep-26	27-Aug-26 A	18-Oct-26	10,158.00	8,126.40	10,158.00	100%	80%	-41
MEP WORK		62	03-Aug-2	08-Sep-26	30-Jul-26 A	15-Oct-26	66,765.96	50,269.70	66,765.96	100%	75.29%	-33
MECANICAL WORKS		54	03-Aug-2	23-Aug-26	30-Jul-26 A	13-Oct-26	50,502.24	36,445.54	50,502.24	100%	72.17%	-46
SEWER AND DRAINAGE SYSTEM		53	03-Aug-2	23-Aug-26	30-Jul-26 A	13-Oct-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-46
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-2	04-Aug-26	30-Jul-26 A	10-Oct-26	3,225.72	2,741.86	3,225.72	100%	85%	-58
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-2	23-Aug-26	11-Oct-26	13-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-2	15-Aug-26	26-Sep-26 A	11-Oct-26	7,684.80	4,610.88	7,684.80	100%	60%	-10
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-2	15-Aug-26	26-Sep-26 A	11-Oct-26	7,684.80	4,610.88	7,684.80	100%	60%	-10
WATER SUPPLY SYSTEM		3	18-Aug-2	20-Aug-26	27-Aug-26 A	11-Oct-26	36,366.00	29,092.80	36,366.00	100%	80%	-35
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-2	20-Aug-26	27-Aug-26 A	11-Oct-26	36,366.00	29,092.80	36,366.00	100%	80%	-35
ELECTRICAL WORKS		11	27-Aug-2	08-Sep-26	20-Aug-26 A	15-Oct-26	16,263.72	13,824.16	16,263.72	100%	85%	-36
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-2	29-Aug-26	20-Aug-26 A	14-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-44
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-2	01-Sep-26	20-Aug-26 A	14-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-44
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-2	05-Sep-26	20-Aug-26 A	14-Oct-26	4,959.00	4,215.15	4,959.00	100%	85%	-44
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-2	08-Sep-26	20-Aug-26 A	15-Oct-26	7,337.52	6,236.89	7,337.52	100%	85%	-44
PROJECT CLOSOUT		10	02-Nov-2	14-Nov-26	06-Aug-26 A	08-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-96
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-2	14-Nov-26	06-Aug-26 A	08-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-96
TABUK		144	25-Jun-26	09-Dec-26	12-Jul-26 A	04-Feb-27	3,001,022.35	2,233,075.02	3,787,364.00	79.24%	58.96%	-36
PROCUREMENT		63	25-Jun-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,157,429.76	1,375,963.21	2,157,429.76	100%	63.78%	-13
LONG LEAD ITEMS		54	01-Jul-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,118,427.42	1,341,415.10	2,118,427.42	100%	63.32%	-19
MANUFACTURE / FABRICATION		26	18-Jul-26	16-Aug-26	27-Aug-26 A	21-Oct-26	0.00	0.00	0.00	0%	0%	-20
SPORTS & RECREATIONAL FACILITIES WORK		26	18-Jul-26	16-Aug-26	27-Aug-26 A	21-Oct-26	0.00	0.00	0.00	0%	0%	-20
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26	16-Aug-26	27-Aug-26 A	21-Oct-26	0.00	0.00	0.00	100%	60%	-20
DELIVERY TO SITE		54	01-Jul-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,118,427.42	1,341,415.10	2,118,427.42	100%	63.32%	-19
EXTERNAL / LANDSCAPE WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-36
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-36
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,013,812.01	1,248,832.16	2,013,812.01	100%	62.01%	-38
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	58,731.75	52,858.58	58,731.75	100%	90%	-36
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	10,152.00	9,136.80	10,152.00	100%	90%	-36
PG-T-PR-LL-SPDL-30_R	Padel Playground Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	26,778.60	24,100.74	26,778.60	100%	90%	-36
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	11-Oct-26	39,487.50	35,538.75	39,487.50	100%	90%	-43
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-2	27-Aug-26	20-Aug-26 A	26-Oct-26	1,878,662.16	1,127,197.30	1,878,662.16	100%	60%	-46
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	14-Oct-26	4,001.54	2,573.09	4,001.54	100%	64.3%	-29
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	11-Oct-26	573.89	516.50	573.89	100%	90%	-25
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	14-Oct-26	3,427.65	2,056.59	3,427.65	100%	60%	-29
PLUMBING WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-36
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-36
IRRIGATION WORK		4	01-Jul-26	06-Jul-26	20-Aug-26 A	10-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-38
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	06-Jul-26	20-Aug-26 A	10-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-38
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	11-Oct-26	64,072.19	57,122.33	64,072.19	100%	89.15%	-22
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	1,785.24	1,606.72	1,785.24	100%	90%	-36
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	1,428.19	1,285.37	1,428.19	100%	90%	-36
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	41,772.67	37,595.40	41,772.67	100%	90%	-36
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	4,618.19	4,156.37	4,618.19	100%	90%	-36
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	10-Oct-26	3,615.08	3,253.58	3,615.08	100%	90%	-43
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV	12	11-Aug-2	24-Aug-26	27-Aug-26 A	11-Oct-26	3,525.77	2,996.90	3,525.77	100%	85%	-26
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	11-Oct-26	4,463.64	3,794.09	4,463.64	100%	85%	-26
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	11-Oct-26	2,863.40	2,433.89	2,863.40	100%	85%	-26
SHORT LEAD ITEMS		52	25-Jun-26	22-Jul-26	07-Aug-26 A	14-Oct-26	39,002.34	34,548.11	39,002.34	100%	88.58%	-34

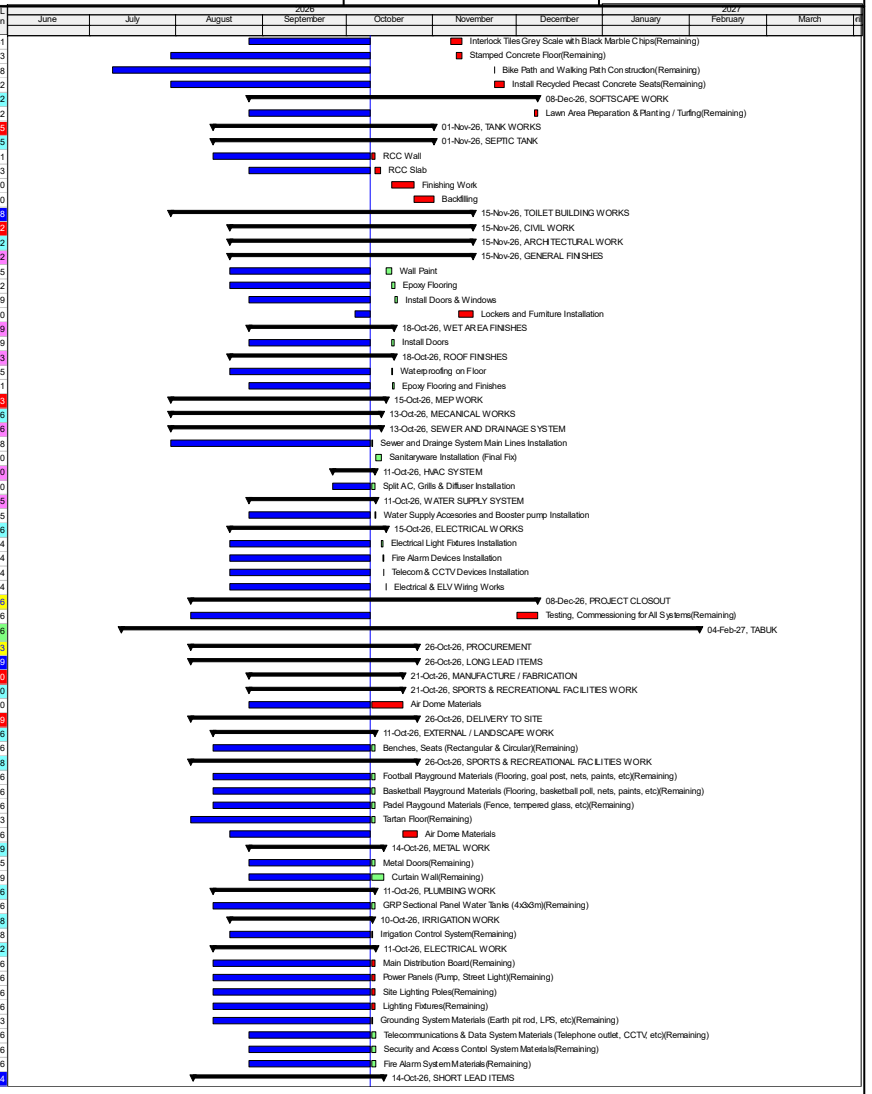


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
DELIVERY TO SITE		52	25-Jun-26	22-Jul-26	07-Aug-26 A	14-Oct-26	39,002.34	34,548.11	39,002.34	100%	88.58%	-34
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	19,978.06	17,980.25	19,978.06	100%	90%	-27
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	714.10	642.69	714.10	100%	90%	-27
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	8,301.96	7,471.76	8,301.96	100%	90%	-27
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	10,962.00	9,865.80	10,962.00	100%	90%	-27
METAL WORK		12	25-Jun-26	08-Jul-26	23-Sep-26 A	14-Oct-26	1,724.00	1,034.40	1,724.00	100%	60%	-6
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	23-Sep-26 A	14-Oct-26	1,302.70	781.62	1,302.70	100%	60%	-6
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	14-Oct-26	112.75	67.65	112.75	100%	60%	-6
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	14-Oct-26	308.56	185.13	308.56	100%	60%	-6
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	10-Oct-26	14,977.04	13,479.33	14,977.04	100%	90%	-45
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	10-Oct-26	1,859.76	1,673.78	1,859.76	100%	90%	-45
PG-T-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	10-Oct-26	13,117.28	11,805.55	13,117.28	100%	90%	-34
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	19-Sep-26 A	11-Oct-26	2,200.61	1,980.55	2,200.61	100%	90%	-6
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	19-Sep-26 A	11-Oct-26	2,200.61	1,980.55	2,200.61	100%	90%	-6
FIRE FIGHTING WORK		9	30-Jun-26	09-Jul-26	27-Sep-26 A	13-Oct-26	122.63	73.58	122.63	100%	60%	-6
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26	09-Jul-26	27-Sep-26 A	13-Oct-26	122.63	73.58	122.63	100%	60%	-6
CONSTRUCTION STAGE		132	25-Jun-26	07-Dec-26	12-Jul-26 A	31-Dec-26	843,592.58	681,065.89	1,209,695.60	69.74%	56.3%	-6
PLAYGROUND AND LANDSCAPING WORKS		132	25-Jun-26	07-Dec-26	12-Jul-26 A	31-Dec-26	553,512.58	645,408.09	896,855.14	61.72%	71.96%	-6
PLAYGROUND WORKS		68	08-Aug-26	07-Dec-26	14-Aug-26 A	29-Nov-26	96,087.48	129,656.60	194,465.34	49.41%	66.67%	13
FOOTBALL PLAYGROUND WORKS		59	19-Aug-26	17-Nov-26	14-Aug-26 A	31-Oct-26	55,127.10	72,054.83	109,254.66	50.46%	65.95%	11
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	19-Oct-26	31-Oct-26	0.00	0.00	23,667.00	0%	0%	0
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	19-Oct-26	0.00	1,648.13	2,060.16	0%	80%	-33
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	11-Oct-26	24,360.00	20,706.00	24,360.00	100%	85%	-31
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	17-Oct-26	7,100.10	28,400.40	35,500.50	20%	80%	-33
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	13-Oct-26	23,667.00	21,300.30	23,667.00	100%	90%	-38
BASKETBALL PLAYGROUND WORKS		57	31-Aug-26	17-Nov-26	20-Aug-26 A	09-Nov-26	27,704.28	24,819.01	43,200.72	64.13%	57.45%	-2
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	09-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-47
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	18-Oct-26	14,612.52	12,377.66	15,472.08	94.44%	80%	-31
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	13-Oct-26	13,091.76	11,128.00	13,091.76	100%	85%	-30
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	18-Oct-26	07-Nov-26	0.00	0.00	13,091.76	0%	0%	0
PADEL PLAYGROUND WORKS		54	08-Aug-26	07-Dec-26	20-Aug-26 A	29-Nov-26	13,256.10	32,782.76	42,009.96	31.55%	78.04%	18
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	08-Nov-26	0.00	23,692.50	26,325.00	0%	90%	-51
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	14-Oct-26	3,534.96	3,004.72	3,534.96	100%	85%	-26
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	17-Oct-26	05-Nov-26	4,418.70	0.00	5,302.44	83.33%	0%	0
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	15-Oct-26	5,302.44	4,772.20	5,302.44	100%	90%	-30
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	29-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-65
GENERAL SITE WORKS		132	25-Jun-26	23-Nov-26	12-Jul-26 A	31-Dec-26	390,831.94	311,646.94	444,115.54	88%	70.17%	-18
FENCE WORKS		48	27-Jul-26	17-Aug-26	20-Aug-26 A	18-Oct-26	19,745.64	11,189.20	19,745.64	100%	56.67%	-31
PG-T-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26	03-Aug-26	20-Aug-26 A	10-Oct-26	6,581.88	5,923.69	6,581.88	100%	90%	-36
PG-T-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-26	10-Aug-26	20-Sep-26 A	11-Oct-26	6,581.88	5,265.50	6,581.88	100%	80%	-12
PG-T-CON-EXGN-FN-50	Installation of Gates	6	11-Aug-26	17-Aug-26	11-Oct-26	18-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		77	01-Jul-26	10-Aug-26	12-Jul-26 A	01-Nov-26	206,336.28	168,645.01	206,336.28	100%	81.73%	-60
STORM WATER AND UTILITY WORK		55	01-Jul-26	04-Aug-26	20-Aug-26 A	26-Oct-26	22,092.00	10,572.00	22,092.00	100%	47.85%	-26
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	10-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-38
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	12-Oct-26	10,740.00	6,444.00	10,740.00	100%	60%	-14
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	12-Oct-26	15-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	15-Oct-26	19-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	21-Oct-26	26-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	21-Oct-26	183,926.34	158,073.01	183,926.34	100%	85.94%	-71
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	21-Oct-26	58,299.00	49,554.15	58,299.00	100%	85%	-47
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	19-Oct-26	34,712.34	31,241.11	34,712.34	100%	90%	-81
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	20-Oct-26	90,915.00	77,277.75	90,915.00	100%	85%	-46
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	26-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	26-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		99	25-Jun-26	26-Oct-26	20-Aug-26 A	12-Dec-26	164,750.02	118,981.14	202,937.62	81.18%	58.63%	8
POWER, LIGHTING & GROUNDING		79	25-Jun-26	19-Sep-26	20-Aug-26 A	15-Nov-26	159,791.62	106,037.34	159,791.62	100%	66.36%	1
PG-T-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	14-Oct-26	55,696.90	44,557.52	55,696.90	100%	80%	-25
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	02-Nov-26	8,265.00	7,025.25	8,265.00	100%	85%	-54
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	04-Nov-26	4,586.70	2,293.35	4,586.70	100%	50%	-36
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	09-Nov-26	17,397.90	8,698.95	17,397.90	100%	50%	-37
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	11-Nov-26	69,621.12	41,772.67	69,621.12	100%	60%	-41
PG-T-CON-EXGN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	04-Oct-26 A	15-Nov-26	4,224.00	1,689.60	4,224.00	100%	40%	-32
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	12-Dec-26	4,958.40	12,943.80	43,146.00	11.49%	30%	-44
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	26-Nov-26	619.80	185.94	619.80	100%	30%	-52
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	30-Nov-26	3,718.80	1,115.64	3,718.80	100%	30%	-54
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	03-Dec-26	0.00	4,574.74	15,249.12	0%	30%	-57
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	06-Dec-26	0.00	433.94	1,446.48	0%	30%	-60
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	09-Dec-26	0.00	1,983.60	6,612.00	0%	30%	-63
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	12-Dec-26	0.00	4,464.00	14,880.00	0%	30%	-66
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	24-Nov-26	619.80	185.94	619.80	100%	30%	-50
PARKING WORK		7	27-Oct-26	03-Nov-26	20-Aug-26 A	13-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-91
PG-T-CON-EXGN-PR-10	Installation of Parking Accessories	7	27-Oct-26	03-Nov-26	20-Aug-26 A	13-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-91
SERVICE CONNECTION		10	12-Nov-26	23-Nov-26	14-Aug-26 A	31-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-108

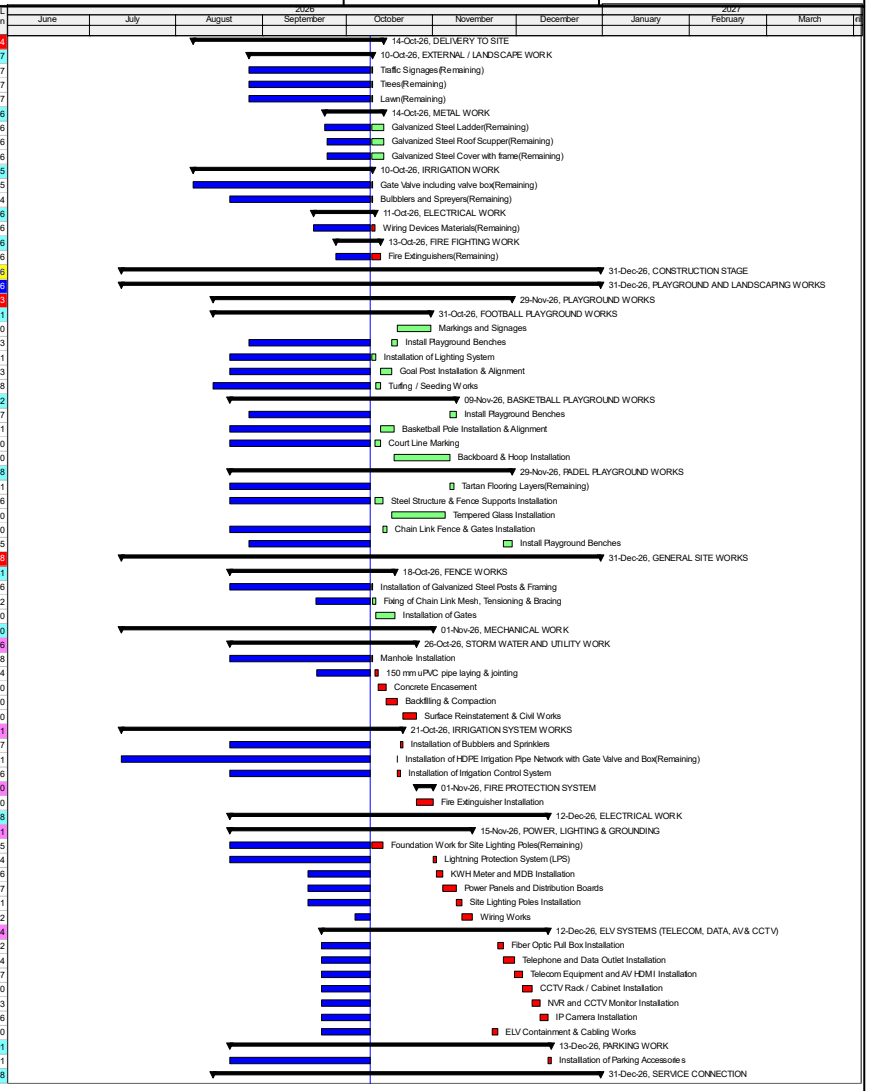


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-2	23-Nov-26	14-Aug-26 A	31-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-108
LANDSCAPING WORKS		38	28-Sep-2	22-Nov-26	12-Jul-26 A	28-Nov-26	60,984.00	202,449.99	252,665.10	24.14%	80.13%	-70
HARDSCAPE WORK		38	28-Sep-2	22-Nov-26	30-Jul-26 A	28-Nov-26	60,984.00	148,329.99	170,003.10	35.87%	87.25%	-54
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-2	08-Oct-26	27-Aug-26 A	15-Nov-26	60,984.00	51,836.40	60,984.00	100%	85%	-57
PG-T-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26	20-Oct-26	30-Jul-26 A	15-Nov-26	0.00	39,123.00	43,470.00	0%	90%	-81
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	23-Nov-26	0.00	54,123.39	60,137.10	0%	90%	-88
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-2	22-Nov-26	23-Sep-26 A	28-Nov-26	0.00	3,247.20	5,412.00	0%	60%	-45
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	28-Nov-26	0.00	54,120.00	82,662.00	0%	65.47%	-80
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	22-Nov-26	0.00	23,061.00	46,122.00	0%	50%	-39
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-2	22-Nov-26	12-Jul-26 A	28-Nov-26	0.00	31,059.00	36,540.00	0%	85%	-112
TANK WORKS		70	07-Jul-26	26-Aug-26	14-Aug-26 A	07-Nov-26	5,609.16	1,654.56	5,609.16	100%	29.5%	-28
SEPTIC TANK		70	07-Jul-26	26-Aug-26	14-Aug-26 A	07-Nov-26	5,609.16	1,654.56	5,609.16	100%	29.5%	-28
PG-T-CON-EXTW-ST-40	RCC Wall	9	07-Jul-26	16-Jul-26	14-Aug-26 A	13-Oct-26	2,757.60	1,654.56	2,757.60	100%	60%	-42
PG-T-CON-EXTW-ST-50	RCC Slab	13	18-Jul-26	01-Aug-26	13-Oct-26	28-Oct-26	2,599.38	0.00	2,599.38	100%	0%	0
PG-T-CON-EXTW-ST-60	Finishing Work	8	18-Aug-2	26-Aug-26	28-Oct-26	07-Nov-26	252.18	0.00	252.18	100%	0%	0
AIR DOME CONSTRUCTION		9	26-Aug-2	05-Sep-26	21-Oct-26	01-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
CIVIL WORK		9	26-Aug-2	05-Sep-26	21-Oct-26	01-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-2	05-Sep-26	21-Oct-26	01-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
TOILET BUILDING WORKS		16	31-Aug-2	28-Oct-26	19-Sep-26 A	18-Oct-26	39,591.72	35,657.80	62,352.18	63.5%	57.19%	26
CIVIL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	8,005.86	14,939.40	0%	53.59%	-9
ARCHITECTURAL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	8,005.86	14,939.40	0%	53.59%	-9
WET AREA FINISHES		2	11-Oct-26	12-Oct-26	23-Sep-26 A	13-Oct-26	0.00	3,216.96	5,361.60	0%	60%	-15
PG-T-CON-BAR-WF-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	13-Oct-26	0.00	3,216.96	5,361.60	0%	60%	-15
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	4,788.90	9,577.80	0%	50%	-20
PG-T-CON-BAR-RF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	4,788.90	9,577.80	0%	50%	-20
MEP WORK		16	31-Aug-2	28-Oct-26	20-Sep-26 A	18-Oct-26	39,591.72	27,651.94	47,412.78	83.5%	58.32%	27
MECANICAL WORKS		16	31-Aug-2	28-Oct-26	20-Sep-26 A	18-Oct-26	39,591.72	27,651.94	47,412.78	83.5%	58.32%	27
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	18-Oct-26	0.00	54.50	136.26	0%	40%	-19
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	18-Oct-26	0.00	54.50	136.26	0%	40%	-19
SEWER AND DRAINAGE SYSTEM		2	03-Sep-2	05-Sep-26	23-Sep-26 A	13-Oct-26	3,225.72	1,935.43	3,225.72	100%	60%	-14
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-2	05-Sep-26	23-Sep-26 A	13-Oct-26	3,225.72	1,935.43	3,225.72	100%	60%	-14
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	14-Oct-26	0.00	3,842.40	7,684.80	0%	50%	-18
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	14-Oct-26	0.00	3,842.40	7,684.80	0%	50%	-18
WATER SUPPLY SYSTEM		3	31-Aug-2	02-Sep-26	23-Sep-26 A	12-Oct-26	36,366.00	21,819.60	36,366.00	100%	60%	-12
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-2	02-Sep-26	23-Sep-26 A	12-Oct-26	36,366.00	21,819.60	36,366.00	100%	60%	-12
PROJECT CLOSOUT		140	22-Nov-2	09-Dec-26	06-Aug-26 A	04-Feb-27	0.00	176,045.92	420,238.64	0%	41.89%	-141
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-2	03-Dec-26	06-Aug-26 A	28-Jan-27	0.00	153,330.31	306,660.63	0%	50%	-139
PG-T-PCL-20	As-Built Drawings	15	22-Nov-2	09-Dec-26	23-Sep-26 A	04-Feb-27	0.00	22,715.60	113,578.01	0%	20%	-100

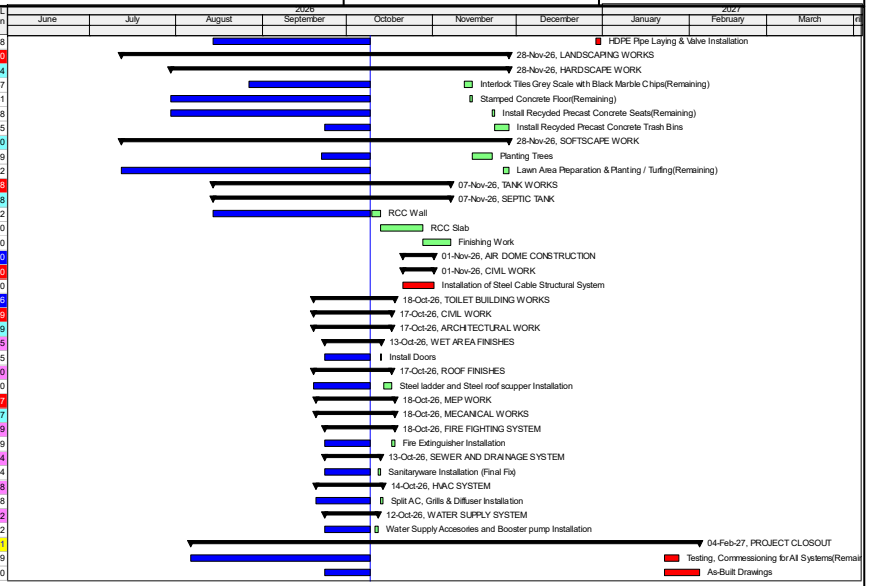

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
