
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026		182	25-Jun-26	16-Dec-26	01-Jul-26 A	10-Feb-27	11,632,169.13	7,148,966.98	19,460,014.61	59.77%	36.74%	-42
MILESTONES		182	25-Jun-26	16-Dec-26	01-Jul-26 A	10-Feb-27	0.00	0.00	0.00	0%	0%	-42
GENERAL MILESTONES		182	25-Jun-26	16-Dec-26	01-Jul-26 A	10-Feb-27	0.00	0.00	0.00	0%	0%	-42
PG-GN-MS-20	Project Completion Date	0		16-Dec-26		10-Feb-27	0.00	0.00	0.00	0%	0%	0
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	03-Jan-27	0.00	0.00	0.00	61.02%	50%	-11
CONTRACUAL MILESTONES		64	28-Oct-26	16-Dec-26	28-Nov-26	10-Feb-27	0.00	0.00	0.00	0%	0%	-22
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26		28-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-40	Completion of Landscape Works	0		16-Dec-26		25-Jan-27	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-50	Completion of Playground Works	0		07-Dec-26		14-Dec-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-60	Substantial Completion - All Works	0		16-Dec-26		10-Feb-27	0.00	0.00	0.00	0%	0%	0
QASSIM		156	25-Jun-26	16-Dec-26	30-Jul-26 A	31-Jan-27	5,384,775.86	3,198,545.01	8,894,848.39	60.54%	35.96%	-9
ENGINEERING		35	25-Jun-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-27
SHOP DRAWINGS SUBMITTALS		35	25-Jun-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-27
MECHANICAL DRAWINGS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-44
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-44
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	100%	90%	-44
ELECTRICAL DRAWINGS		17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-45
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-45
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	10-Oct-26	0.00	0.00	0.00	100%	90%	-51
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	100%	90%	-47
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	100%	90%	-45
PROCUREMENT		86	25-Jun-26	27-Aug-26	14-Aug-26 A	24-Nov-26	2,540,171.64	1,701,749.04	2,540,171.64	100%	66.99%	-32
LONG LEAD ITEMS		86	25-Jun-26	27-Aug-26	14-Aug-26 A	24-Nov-26	2,386,452.70	1,594,567.33	2,386,452.70	100%	66.82%	-32
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		86	07-Jul-26	27-Aug-26	14-Aug-26 A	24-Nov-26	2,386,452.70	1,594,567.33	2,386,452.70	100%	66.82%	-42
EXTERNAL / LANDSCAPE WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	11-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-34
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	11-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-34
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	15-Oct-26	2,119,264.56	1,355,769.58	2,119,264.56	100%	63.97%	-17
PG-Q-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	46,985.40	44,636.13	46,985.40	100%	95%	-33
PG-Q-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	10,152.00	9,644.40	10,152.00	100%	95%	-33
PG-Q-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	10-Oct-26	26,778.60	25,439.67	26,778.60	100%	95%	-33
PG-Q-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	156,686.40	148,852.08	156,686.40	100%	95%	-33
PG-Q-PR-LL-SPDL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	25-Aug-26 A	15-Oct-26	1,878,662.16	1,127,197.30	1,878,662.16	100%	60%	-34
METAL WORK		15	25-Jul-26	10-Aug-26	08-Nov-26	24-Nov-26	3,427.65	0.00	3,427.65	100%	0%	0
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26	10-Aug-26	08-Nov-26	24-Nov-26	3,427.65	0.00	3,427.65	100%	0%	0
PLUMBING WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	7,810.43	7,419.90	7,810.43	100%	95%	-33
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	7,810.43	7,419.90	7,810.43	100%	95%	-33
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	10-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-34
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	10-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-34
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	11-Oct-26	221,065.50	198,958.95	221,065.50	100%	90%	-24
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	11-Oct-26	3,124.17	2,811.75	3,124.17	100%	90%	-34
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	10-Oct-26	1,785.24	1,606.72	1,785.24	100%	90%	-38
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	11-Oct-26	182,755.44	164,479.90	182,755.44	100%	90%	-34
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	11-Oct-26	8,081.83	7,273.65	8,081.83	100%	90%	-34
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	6,326.40	5,693.76	6,326.40	100%	90%	-23
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	6,170.09	5,553.08	6,170.09	100%	90%	-23
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	7,811.37	7,030.23	7,811.37	100%	90%	-23
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	11-Oct-26	5,010.96	4,509.86	5,010.96	100%	90%	-23
SHORT LEAD ITEMS		49	25-Jun-26	12-Jul-26	14-Aug-26 A	15-Oct-26	153,718.94	107,181.71	153,718.94	100%	69.73%	-38
DELIVERY TO SITE		49	25-Jun-26	12-Jul-26	14-Aug-26 A	15-Oct-26	153,718.94	107,181.71	153,718.94	100%	69.73%	-38
EXTERNAL / LANDSCAPE WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	14-Oct-26	78,553.04	54,797.90	78,553.04	100%	69.76%	-29
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	14-Oct-26	1,892.27	1,135.36	1,892.27	100%	60%	-29
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	13-Oct-26	714.10	499.87	714.10	100%	70%	-28
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	13-Oct-26	34,366.68	24,056.68	34,366.68	100%	70%	-28
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	13-Oct-26	41,580.00	29,106.00	41,580.00	100%	70%	-28
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	1,724.00	1,206.80	1,724.00	100%	70%	-4
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	1,302.70	911.89	1,302.70	100%	70%	-4
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	112.75	78.93	112.75	100%	70%	-4
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	13-Oct-26	308.56	215.99	308.56	100%	70%	-4
IRRIGATION WORK		18	25-Jun-26	08-Jul-26	14-Aug-26 A	13-Oct-26	71,118.65	49,783.05	71,118.65	100%	70%	-39
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	13-Oct-26	7,186.00	5,030.20	7,186.00	100%	70%	-39
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	13-Oct-26	63,932.65	44,752.86	63,932.65	100%	70%	-34
ELECTRICAL WORK		15	25-Jun-26	12-Jul-26	26-Sep-26 A	15-Oct-26	2,200.61	1,320.36	2,200.61	100%	60%	-3
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26 A	15-Oct-26	2,200.61	1,320.36	2,200.61	100%	60%	-3
FIRE FIGHTING WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	14-Oct-26	122.63	73.58	122.63	100%	60%	-5
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	14-Oct-26	122.63	73.58	122.63	100%	60%	-5
CONSTRUCTION STAGE		133	05-Jul-26	16-Dec-26	06-Aug-26 A	25-Jan-27	2,844,604.22	1,224,964.10	4,853,535.37	61.13%	26.32%	-5
PLAYGROUND AND LANDSCAPING WORKS		133	05-Jul-26	16-Dec-26	06-Aug-26 A	25-Jan-27	960,141.48	944,443.84	1,629,217.98	58.93%	57.97%	-5
PLAYGROUND WORKS		97	11-Aug-26	02-Dec-26	06-Aug-26 A	14-Dec-26	105,389.08	227,449.85	325,784.34	32.35%	69.82%	-13
FOOTBALL PLAYGROUND WORKS		58	19-Aug-26	17-Nov-26	14-Aug-26 A	03-Nov-26	62,227.20	69,276.10	109,254.66	56.96%	63.41%	8
PG-Q-CON-EX-FB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	25-Oct-26	03-Nov-26	0.00	0.00	23,667.00	0%	0%	0

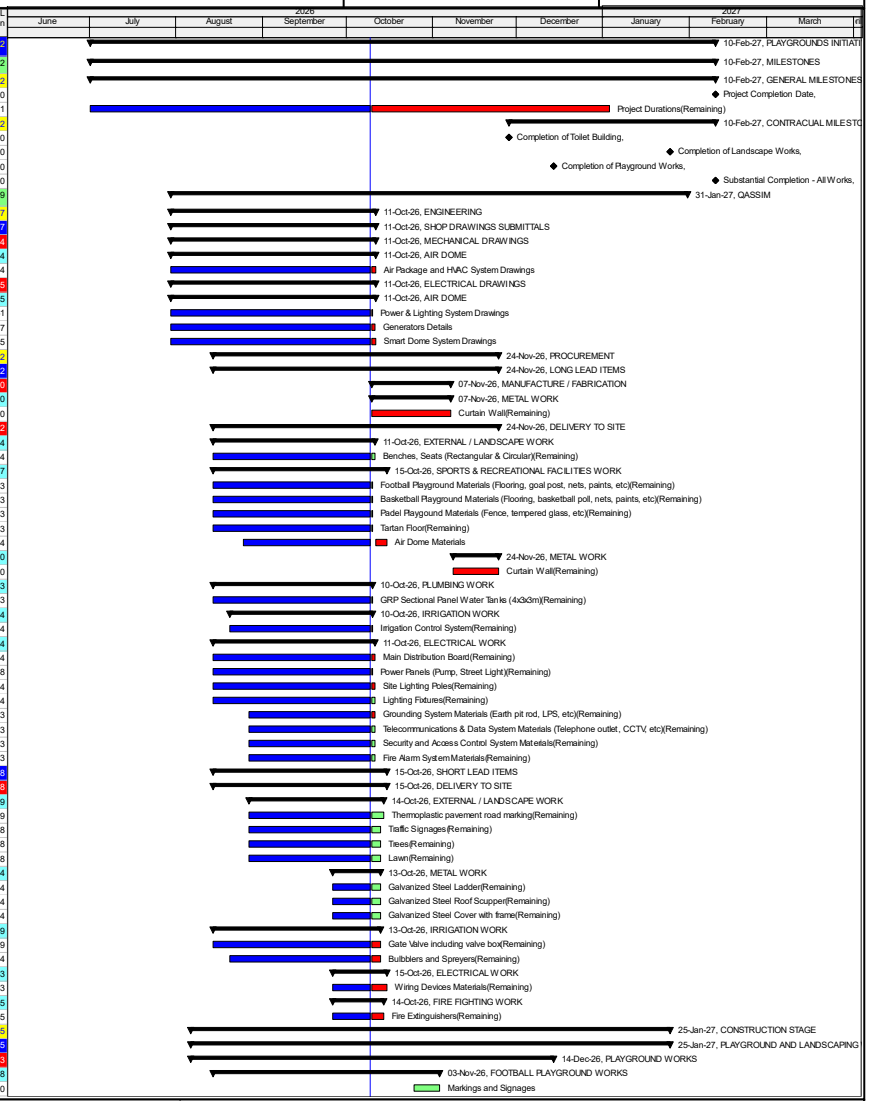

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EXFB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	25-Oct-26	0.00	1,236.10	2,060.16	0%	60%	-33
PG-Q-CON-EXFB-120	Installation of Lighting System	12	19-Aug-2	01-Sep-26	20-Aug-26 A	11-Oct-26	24,360.00	20,706.00	24,360.00	100%	85%	-32
PG-Q-CON-EXFB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	17-Oct-26	14,200.20	28,400.40	35,500.50	40%	80%	-28
PG-Q-CON-EXFB-90	Turfing / Seeding Works	10	02-Sep-2	13-Sep-26	14-Aug-26 A	13-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-41
BASKETBALL PLAYGROUND WORKS		70	31-Aug-2	17-Nov-26	20-Aug-26 A	03-Nov-26	29,333.94	33,942.53	43,200.72	67.9%	78.57%	4
PG-Q-CON-EXBB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	27-Sep-26 A	03-Nov-26	0.00	618.05	1,545.12	0%	40%	-14
PG-Q-CON-EXBB-60	Basketball Pole Installation & Alignment	17	17-Sep-2	07-Oct-26	20-Aug-26 A	18-Oct-26	15,472.08	12,377.66	15,472.08	100%	80%	-32
PG-Q-CON-EXBB-80	Court Line Marking	15	31-Aug-2	16-Sep-26	20-Aug-26 A	13-Oct-26	13,091.76	10,473.41	13,091.76	100%	80%	-31
PG-Q-CON-EXBB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	01-Oct-26 A	21-Oct-26	770.10	10,473.41	13,091.76	5.88%	80%	0
PADEL PLAYGROUND WORKS		87	11-Aug-2	02-Dec-26	06-Aug-26 A	14-Dec-26	13,827.93	124,231.22	173,326.96	7.98%	71.67%	-13
PG-Q-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	09-Nov-26	0.00	117,514.80	130,572.00	0%	90%	-64
PG-Q-CON-EXPD-40	Steel Structure & Fence Supports Installation	18	11-Aug-2	31-Aug-26	20-Aug-26 A	17-Oct-26	3,534.96	2,474.47	3,534.96	100%	70%	-30
PG-Q-CON-EXPD-50	Tempered Glass Installation	17	20-Sep-2	10-Oct-26	20-Oct-26	09-Nov-26	4,990.53	0.00	5,302.44	94.12%	0%	0
PG-Q-CON-EXPD-60	Chain Link Fence & Gates Installation	16	01-Sep-2	19-Sep-26	20-Aug-26 A	20-Oct-26	5,302.44	4,241.95	5,302.44	100%	80%	-35
PG-Q-CON-EXPD-70	Court Accessories Installation	15	29-Oct-26	15-Nov-26	09-Nov-26	26-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-Q-CON-EXPD-80	Install Playground Benches	15	16-Nov-2	02-Dec-26	26-Nov-26	14-Dec-26	0.00	0.00	1,545.12	0%	0%	0
GENERAL SITE WORKS		133	05-Jul-26	16-Dec-26	14-Aug-26 A	25-Jan-27	785,922.48	524,568.15	838,805.34	93.7%	62.54%	2
FENCE WORKS		62	02-Aug-2	13-Sep-26	20-Aug-26 A	02-Nov-26	19,745.64	8,227.35	19,745.64	100%	41.67%	-26
PG-Q-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-2	15-Aug-26	20-Aug-26 A	11-Oct-26	6,581.88	5,594.60	6,581.88	100%	85%	-32
PG-Q-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-2	01-Sep-26	27-Sep-26 A	21-Oct-26	6,581.88	2,632.75	6,581.88	100%	40%	-6
PG-Q-CON-EXGN-FN-50	Installation of Gates	10	02-Sep-2	13-Sep-26	21-Oct-26	02-Nov-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		64	05-Jul-26	18-Aug-26	20-Aug-26 A	08-Nov-26	349,080.54	238,538.34	349,080.54	100%	68.33%	-28
STORM WATER AND UTILITY WORK		62	05-Jul-26	16-Aug-26	20-Aug-26 A	05-Nov-26	21,060.00	11,894.40	21,060.00	100%	56.48%	-28
PG-Q-CON-EXGN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	11-Oct-26	4,128.00	3,302.40	4,128.00	100%	80%	-37
PG-Q-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	12-Oct-26	10,740.00	8,592.00	10,740.00	100%	80%	-38
PG-Q-CON-EXGN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	12-Oct-26	20-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	20-Oct-26	27-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-2	16-Aug-26	29-Oct-26	05-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		5	03-Aug-2	09-Aug-26	20-Aug-26 A	29-Oct-26	327,702.60	226,643.94	327,702.60	100%	69.16%	-53
PG-Q-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-2	09-Aug-26	27-Aug-26 A	29-Oct-26	236,787.60	153,911.94	236,787.60	100%	65%	-50
PG-Q-CON-EXGN-M-90	Installation of Irrigation Control System	3	03-Aug-2	05-Aug-26	20-Aug-26 A	27-Oct-26	90,915.00	72,732.00	90,915.00	100%	80%	-55
FIRE PROTECTION SYSTEM		2	17-Aug-2	18-Aug-26	05-Nov-26	08-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-Q-CON-EXGN-M-110	Fire Extinguisher Installation	2	17-Aug-2	18-Aug-26	05-Nov-26	08-Nov-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		78	13-Aug-2	01-Nov-26	20-Aug-26 A	05-Jan-27	417,096.30	275,813.66	450,291.36	92.63%	61.25%	-49
POWER, LIGHTING & GROUNDING		43	13-Aug-2	20-Sep-26	20-Aug-26 A	25-Nov-26	393,221.16	275,813.66	393,221.16	100%	70.14%	-49
PG-Q-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-2	17-Aug-26	20-Aug-26 A	05-Nov-26	162,449.28	129,959.42	162,449.28	100%	80%	-62
PG-Q-CON-EXGN-E-30	Lightning Protection System (LPS)	3	29-Aug-2	31-Aug-26	27-Aug-26 A	08-Nov-26	8,265.00	6,612.00	8,265.00	100%	80%	-59
PG-Q-CON-EXGN-E-40	KWH Meter and MDB Installation	2	01-Sep-2	02-Sep-26	08-Nov-26	10-Nov-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-Q-CON-EXGN-E-50	Power Panels and Distribution Boards	5	03-Sep-2	08-Sep-26	10-Nov-26	16-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-Q-CON-EXGN-E-60	Site Lighting Poles Installation	3	09-Sep-2	12-Sep-26	20-Aug-26 A	17-Nov-26	174,052.80	139,242.24	174,052.80	100%	80%	-72
PG-Q-CON-EXGN-E-70	Wiring Works	3	13-Sep-2	15-Sep-26	17-Nov-26	21-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-Q-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	4	16-Sep-2	20-Sep-26	21-Nov-26	25-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-2	20-Oct-26	25-Nov-26	24-Dec-26	20,569.14	0.00	43,146.00	47.67%	0%	0
PG-Q-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	26-Sep-2	28-Sep-26	29-Nov-26	02-Dec-26	619.80	0.00	619.80	100%	0%	0
PG-Q-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	29-Sep-2	03-Oct-26	02-Dec-26	07-Dec-26	3,718.80	0.00	3,718.80	100%	0%	0
PG-Q-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26	07-Oct-26	07-Dec-26	12-Dec-26	15,249.12	0.00	15,249.12	100%	0%	0
PG-Q-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	08-Oct-26	12-Oct-26	12-Dec-26	16-Dec-26	361.62	0.00	1,446.48	25%	0%	0
PG-Q-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	13-Oct-26	17-Oct-26	16-Dec-26	21-Dec-26	0.00	0.00	6,612.00	0%	0%	0
PG-Q-CON-EXGN-E-150	IP Camera Installation	3	18-Oct-26	20-Oct-26	21-Dec-26	24-Dec-26	0.00	0.00	14,880.00	0%	0%	0
PG-Q-CON-EXGN-E-90	ELV Containment & Cabling Works	3	21-Sep-2	24-Sep-26	25-Nov-26	29-Nov-26	619.80	0.00	619.80	100%	0%	0
FIRE ALARM SYSTEM		32	26-Sep-2	01-Nov-26	29-Nov-26	05-Jan-27	3,306.00	0.00	13,924.20	23.74%	0%	0
PG-Q-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	26-Sep-2	04-Oct-26	29-Nov-26	08-Dec-26	1,983.60	0.00	1,983.60	100%	0%	0
PG-Q-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26	13-Oct-26	08-Dec-26	17-Dec-26	1,322.40	0.00	2,644.80	50%	0%	0
PG-Q-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26	22-Oct-26	17-Dec-26	27-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-Q-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	24-Oct-26	01-Nov-26	27-Dec-26	05-Jan-27	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		5	04-Nov-2	09-Nov-26	30-Dec-26	05-Jan-27	0.00	0.00	14,479.80	0%	0%	0
PG-Q-CON-EXGN-PR-30	Marking & Signages	5	04-Nov-2	09-Nov-26	30-Dec-26	05-Jan-27	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		32	19-Nov-2	16-Dec-26	14-Aug-26 A	25-Jan-27	0.00	2,008.80	5,208.00	0%	38.57%	-115
PG-Q-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-2	28-Nov-26	14-Aug-26 A	06-Jan-27	0.00	2,008.80	2,232.00	0%	90%	-115
PG-Q-CON-EXGN-SC-30	Connection to City Network	8	29-Nov-2	07-Dec-26	06-Jan-27	16-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-Q-CON-EXGN-SC-40	Backfilling	8	08-Dec-2	16-Dec-26	16-Jan-27	25-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		57	30-Sep-2	14-Dec-26	20-Aug-26 A	12-Dec-26	34,116.92	192,405.84	429,915.30	7.94%	44.75%	-31
HARDSCAPE WORK		57	30-Sep-2	14-Dec-26	20-Aug-26 A	12-Dec-26	34,116.92	100,005.84	123,489.30	27.63%	80.98%	-31
PG-Q-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-2	14-Oct-26	27-Aug-26 A	04-Nov-26	34,116.92	49,896.00	55,440.00	61.54%	90%	-45
PG-Q-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-2	02-Dec-26	20-Aug-26 A	30-Nov-26	0.00	50,109.84	62,637.30	0%	80%	-76
PG-Q-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-2	14-Dec-26	30-Nov-26	12-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		32	15-Oct-26	21-Nov-26	27-Aug-26 A	28-Nov-26	0.00	92,400.00	306,426.00	0%	30.15%	-46
PG-Q-CON-EXLS-SS-10	Planting Trees	17	02-Nov-2	21-Nov-26	08-Nov-26	28-Nov-26	0.00	0.00	190,926.00	0%	0%	0
PG-Q-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	08-Nov-26	0.00	92,400.00	115,500.00	0%	80%	-46
TANK WORKS		8	11-Aug-2	19-Aug-26	10-Oct-26	19-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
WATER STORAGE TANK		8	11-Aug-2	19-Aug-26	10-Oct-26	19-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-Q-CON-EX-TW-IR-40	GRP Water Tank Installation	8	11-Aug-2	19-Aug-26	10-Oct-26	19-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		101	17-Aug-2	26-Nov-26	27-Aug-26 A	11-Jan-27	1,864,746.14	250,488.29	2,967,347.81	62.84%	8.44%	-30




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
CIVIL WORK		18	22-Aug-26	10-Sep-26	11-Oct-26	01-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-Q-CON-EXAD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26	01-Sep-26	11-Oct-26	22-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXAD-CL-80	Installation of Membrane System	8	02-Sep-26	10-Sep-26	22-Oct-26	01-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		33	27-Oct-26	26-Nov-26	27-Aug-26 A	11-Jan-27	0.00	125,244.14	712,953.22	0%	17.57%	-90
PG-Q-CON-EXAD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	20-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-90
PG-Q-CON-EXAD-AR-20	Installation of Doors & Access Systems	6	15-Nov-26	21-Nov-26	29-Dec-26	05-Jan-27	0.00	0.00	250,488.29	0%	0%	0
PG-Q-CON-EXAD-AR-30	Installation of Logo	5	22-Nov-26	26-Nov-26	05-Jan-27	11-Jan-27	0.00	0.00	3,236.40	0%	0%	0
PG-Q-CON-EXAD-AR-40	Final Fixing of Accessories & Finishes	8	05-Nov-26	14-Nov-26	20-Dec-26	29-Dec-26	0.00	0.00	208,740.24	0%	0%	0
MECHANICAL WORK		10	12-Sep-26	30-Sep-26	01-Nov-26	19-Nov-26	667,968.77	0.00	667,968.77	100%	0%	0
PG-Q-CON-EXAD-ME-10	Installation of Main Air Package Units	5	12-Sep-26	16-Sep-26	01-Nov-26	07-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXAD-ME-20	Installation of Backup Air Package Unit	5	17-Sep-26	22-Sep-26	07-Nov-26	12-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXAD-ME-30	Installation of Complete HVAC System	6	24-Sep-26	30-Sep-26	12-Nov-26	19-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
ELECTRICAL WORK		78	17-Aug-26	26-Oct-26	27-Aug-26 A	15-Dec-26	695,800.80	125,244.14	1,085,449.25	64.1%	11.54%	-34
PG-Q-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26	30-Aug-26	27-Aug-26 A	15-Oct-26	208,740.24	125,244.14	208,740.24	100%	60%	-30
PG-Q-CON-EXAD-EL-20	Installation of Lighting System	12	31-Aug-26	13-Sep-26	15-Oct-26	29-Oct-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXAD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	01-Oct-26	06-Oct-26	19-Nov-26	25-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXAD-EL-40	Installation of Backup Generator	6	07-Oct-26	13-Oct-26	25-Nov-26	02-Dec-26	69,580.08	0.00	208,740.24	33.33%	0%	0
PG-Q-CON-EXAD-EL-50	Installation of Smart Dome System	11	14-Oct-26	26-Oct-26	02-Dec-26	15-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		47	20-Aug-26	20-Oct-26	20-Aug-26 A	28-Nov-26	19,716.60	30,031.97	56,969.58	34.61%	52.72%	-33
CIVIL WORK		38	06-Oct-26	19-Oct-26	20-Aug-26 A	26-Nov-26	8,806.08	26,717.94	45,922.80	19.18%	58.18%	-72
ARCHITECTURAL WORK		38	06-Oct-26	19-Oct-26	20-Aug-26 A	26-Nov-26	8,806.08	26,717.94	45,922.80	19.18%	58.18%	-72
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	26-Nov-26	2,654.76	13,822.62	20,825.40	12.75%	66.37%	-68
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	19-Oct-26	2,654.76	9,291.66	13,273.80	20%	70%	-40
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	19-Sep-26 A	26-Nov-26	0.00	4,530.96	7,551.60	0%	60%	-54
WET AREA FINISHES		5	08-Oct-26	13-Oct-26	01-Oct-26 A	19-Oct-26	1,072.32	3,753.12	5,361.60	20%	70%	-10
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	01-Oct-26 A	19-Oct-26	1,072.32	3,753.12	5,361.60	20%	70%	-10
ROOF FINISHES		38	06-Oct-26	19-Oct-26	20-Aug-26 A	26-Nov-26	5,079.00	9,142.20	19,735.80	25.73%	46.32%	-72
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	18-Oct-26	5,079.00	9,142.20	10,158.00	50%	90%	-44
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26	19-Oct-26	26-Nov-26	26-Nov-26	0.00	0.00	9,577.80	0%	0%	0
MEP WORK		39	20-Aug-26	20-Oct-26	01-Oct-26 A	28-Nov-26	10,910.52	3,314.03	11,046.78	98.77%	30%	2
MECANICAL WORKS		39	20-Aug-26	20-Oct-26	01-Oct-26 A	28-Nov-26	10,910.52	3,314.03	11,046.78	98.77%	30%	2
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	01-Oct-26 A	28-Nov-26	0.00	40.88	136.26	0%	30%	-49
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	01-Oct-26 A	28-Nov-26	0.00	40.88	136.26	0%	30%	-49
SEWER AND DRAINAGE SYSTEM		2	01-Sep-26	02-Sep-26	01-Oct-26 A	18-Oct-26	3,225.72	967.72	3,225.72	100%	30%	-12
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	01-Oct-26 A	18-Oct-26	3,225.72	967.72	3,225.72	100%	30%	-12
HVAC SYSTEM		3	20-Aug-26	23-Aug-26	01-Oct-26 A	12-Oct-26	7,684.80	2,305.44	7,684.80	100%	30%	-6
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26	23-Aug-26	01-Oct-26 A	12-Oct-26	7,684.80	2,305.44	7,684.80	100%	30%	-6
PROJECT CLOSOUT		42	15-Nov-26	16-Dec-26	06-Aug-26 A	31-Jan-27	0.00	271,831.87	1,701,141.38	0%	15.98%	-124
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	15-Nov-26	26-Nov-26	06-Aug-26 A	11-Jan-27	0.00	236,756.79	473,513.58	0%	50%	-124
PG-Q-PCL-20	As-Built Drawings	15	15-Nov-26	02-Dec-26	23-Sep-26 A	19-Jan-27	0.00	35,075.08	175,375.40	0%	20%	-85
PG-Q-PCL-30	Snag list Submission	3	28-Nov-26	30-Nov-26	11-Jan-27	14-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-40	Snag list Closeout	10	01-Dec-26	12-Dec-26	14-Jan-27	26-Jan-27	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-50	Issuing Approvals	3	13-Dec-26	15-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	175,375.40	0%	0%	0
PG-Q-PCL-60	Handing Over	1	16-Dec-26	16-Dec-26	30-Jan-27	31-Jan-27	0.00	0.00	175,375.40	0%	0%	0
HAIL		136	25-Jun-26	16-Dec-26	09-Jul-26 A	21-Jan-27	2,075,389.51	1,717,346.97	3,264,064.16	63.58%	52.61%	-19
PROCUREMENT		65	25-Jun-26	26-Aug-26	06-Aug-26 A	10-Nov-26	516,988.47	464,851.03	516,988.47	100%	89.92%	-27
LONG LEAD ITEMS		65	25-Jun-26	26-Aug-26	06-Aug-26 A	10-Nov-26	423,859.72	386,426.43	423,859.72	100%	91.17%	-27
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	10-Oct-26	07-Nov-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		59	25-Jul-26	26-Aug-26	06-Aug-26 A	10-Nov-26	423,859.72	386,426.43	423,859.72	100%	91.17%	-52
EXTERNAL / LANDSCAPE WORK		29	25-Jul-26	06-Aug-26	06-Aug-26 A	11-Oct-26	72,919.30	67,849.61	72,919.30	100%	93.05%	-43
PG-H-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	10-Oct-26	44,444.70	42,222.46	44,444.70	100%	95%	-43
PG-H-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	20-Aug-26 A	11-Oct-26	28,474.61	25,627.14	28,474.61	100%	90%	-31
SPORTS & RECREATIONAL FACILITIES WORK		12	25-Jul-26	06-Aug-26	06-Aug-26 A	11-Oct-26	163,721.25	150,559.76	163,721.25	100%	91.96%	-43
PG-H-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	06-Aug-26 A	10-Oct-26	64,212.75	61,002.11	64,212.75	100%	95%	-43
PG-H-PR-LL-SP-DL-20_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	11-Oct-26	99,508.50	89,557.65	99,508.50	100%	90%	-43
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	10-Nov-26	4,801.84	3,841.47	4,801.84	100%	80%	-51
PG-H-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	12-Oct-26	688.66	550.93	688.66	100%	80%	-26
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	10-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-51
PLUMBING WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	11-Oct-26	9,372.51	8,435.26	9,372.51	100%	90%	-25
PG-H-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	11-Oct-26	9,372.51	8,435.26	9,372.51	100%	90%	-25
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	11-Oct-26	173,044.81	155,740.33	173,044.81	100%	90%	-19
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	10-Oct-26	3,124.17	2,811.75	3,124.17	100%	90%	-29
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	10-Oct-26	2,499.34	2,249.40	2,499.34	100%	90%	-29
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	11-Oct-26	134,020.66	120,618.59	134,020.66	100%	90%	-31
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	11-Oct-26	8,081.83	7,273.65	8,081.83	100%	90%	-31
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	10-Oct-26	6,326.40	5,693.76	6,326.40	100%	90%	-29
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	11-Oct-26	6,170.09	5,553.08	6,170.09	100%	90%	-25
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	11-Oct-26	7,811.37	7,030.23	7,811.37	100%	90%	-25
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	11-Oct-26	5,010.96	4,509.86	5,010.96	100%	90%	-25
SHORT LEAD ITEMS		45	04-Jul-26	16-Jul-26	20-Aug-26 A	20-Oct-26	93,128.75	78,424.60	93,128.75	100%	84.21%	-40
DELIVERY TO SITE		45	04-Jul-26	16-Jul-26	20-Aug-26 A	20-Oct-26	93,128.75	78,424.60	93,128.75	100%	84.21%	-40

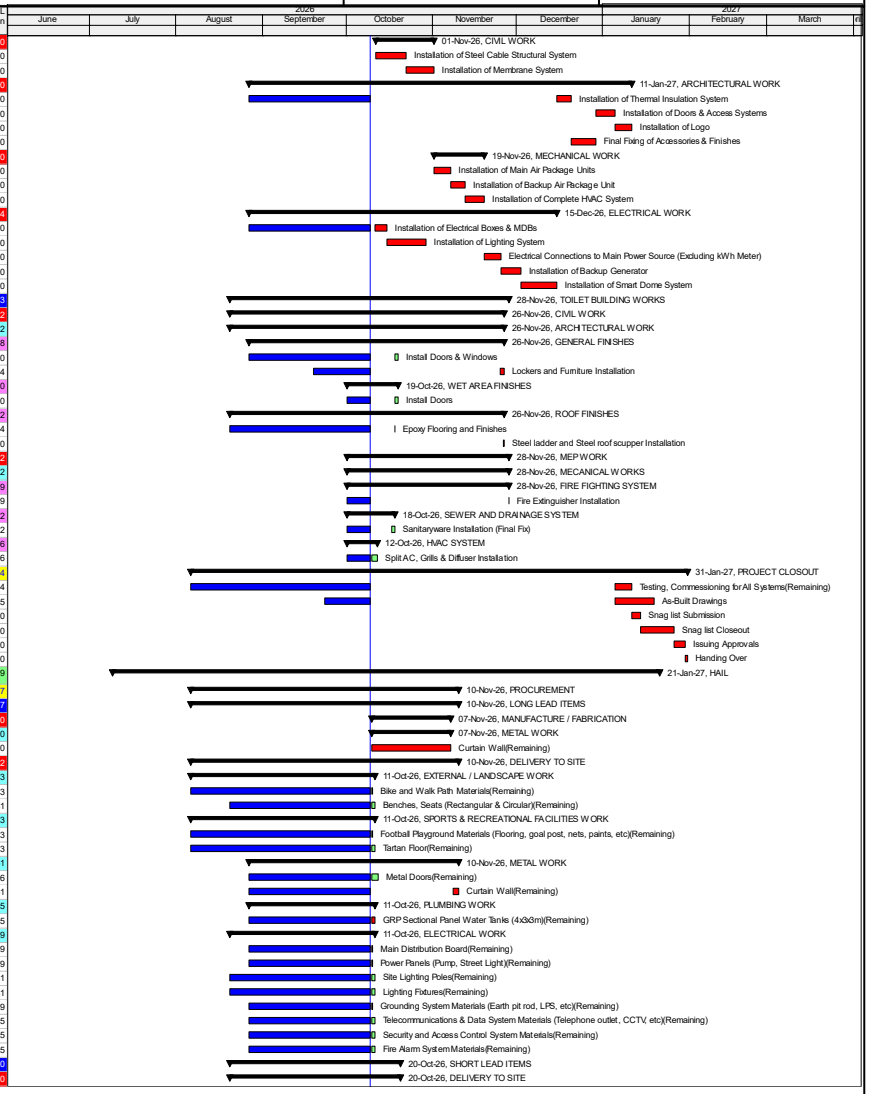


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	59,572.42	50,636.56	59,572.42	100%	85%	-26
PG-H-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	3,311.47	2,814.75	3,311.47	100%	85%	-26
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	1,249.67	1,062.22	1,249.67	100%	85%	-26
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	30,441.29	25,875.09	30,441.29	100%	85%	-26
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	24,570.00	20,884.50	24,570.00	100%	85%	-26
IRRIGATION WORK		17	04-Jul-26	16-Jul-26	20-Aug-26 A	11-Oct-26	30,845.88	26,219.00	30,845.88	100%	85%	-32
PG-H-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26	16-Jul-26	20-Aug-26 A	11-Oct-26	3,403.35	2,892.85	3,403.35	100%	85%	-32
PG-H-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	11-Oct-26	27,442.53	23,326.15	27,442.53	100%	85%	-26
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	26-Sep-26 A	14-Oct-26	2,567.38	1,540.43	2,567.38	100%	60%	-5
PG-H-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26 A	14-Oct-26	2,567.38	1,540.43	2,567.38	100%	60%	-5
FIRE FIGHTING WORK		12	04-Jul-26	16-Jul-26	03-Oct-26 A	20-Oct-26	143.07	28.61	143.07	100%	20%	-4
PG-H-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26	16-Jul-26	03-Oct-26 A	20-Oct-26	143.07	28.61	143.07	100%	20%	-4
CONSTRUCTION STAGE		136	25-Jun-26	26-Nov-26	09-Jul-26 A	21-Jan-27	1,558,401.05	1,197,297.26	2,086,054.45	74.71%	57.4%	-36
PLAYGROUND AND LANDSCAPING WORKS		133	25-Jun-26	26-Nov-26	09-Jul-26 A	21-Jan-27	1,389,810.83	1,096,246.43	1,917,464.23	72.48%	57.17%	-36
PLAYGROUND WORKS		67	29-Jul-26	17-Nov-26	06-Aug-26 A	09-Nov-26	462,790.73	422,169.15	516,185.40	89.66%	81.79%	14
FOOTBALL PLAYGROUND WORKS		67	29-Jul-26	17-Nov-26	06-Aug-26 A	09-Nov-26	462,790.73	422,169.15	516,185.40	89.66%	81.79%	14
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	28-Oct-26	09-Nov-26	0.00	0.00	23,667.00	0%	0%	0
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	28-Oct-26	0.00	3,862.80	5,150.40	0%	75%	-38
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26	01-Sep-26	27-Aug-26 A	17-Oct-26	48,720.00	36,540.00	48,720.00	100%	75%	-30
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26	04-Oct-26	06-Aug-26 A	20-Oct-26	343,980.00	309,582.00	343,980.00	100%	90%	-48
PG-H-CON-EX-FB-50	Goal Post Foundation	17	29-Jul-26	17-Aug-26	20-Aug-26 A	13-Oct-26	35,500.50	28,400.40	35,500.50	100%	80%	-28
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	24-Oct-26	10,923.23	24,850.35	35,500.50	30.77%	70%	-42
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26	15-Sep-26	14-Aug-26 A	20-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-44
GENERAL SITE WORKS		133	25-Jun-26	26-Nov-26	14-Aug-26 A	21-Jan-27	741,495.49	346,033.93	854,072.29	86.82%	40.52%	-5
FENCE WORKS		41	23-Jul-26	16-Aug-26	27-Aug-26 A	17-Oct-26	39,491.28	22,378.39	39,491.28	100%	56.67%	-22
PG-H-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26	02-Aug-26	27-Aug-26 A	10-Oct-26	13,163.76	11,847.38	13,163.76	100%	90%	-28
PG-H-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-26	11-Aug-26	27-Sep-26 A	12-Oct-26	13,163.76	10,531.01	13,163.76	100%	80%	-5
PG-H-CON-EX-GN-FN-50	Installation of Gates	4	12-Aug-26	16-Aug-26	12-Oct-26	17-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
MECHANICAL WORK		68	25-Jun-26	06-Aug-26	14-Aug-26 A	04-Nov-26	344,669.34	160,739.46	344,669.34	100%	46.64%	-32
STORM WATER AND UTILITY WORK		66	25-Jun-26	04-Aug-26	14-Aug-26 A	02-Nov-26	23,124.00	5,005.20	23,124.00	100%	21.65%	-32
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	11-Oct-26	1,032.00	877.20	1,032.00	100%	85%	-39
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	12-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-34
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	12-Oct-26	17-Oct-26	10,740.00	0.00	10,740.00	100%	0%	0
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	17-Oct-26	20-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	20-Oct-26	24-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	28-Oct-26	02-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		40	21-Jul-26	30-Jul-26	14-Aug-26 A	28-Oct-26	321,227.40	155,734.26	321,227.40	100%	48.48%	-55
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	25-Oct-26	28-Oct-26	121,966.80	0.00	121,966.80	100%	0%	0
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	24-Oct-26	108,345.60	92,093.76	108,345.60	100%	85%	-57
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	25-Oct-26	90,915.00	63,640.50	90,915.00	100%	70%	-47
FIRE PROTECTION SYSTEM		2	05-Aug-26	05-Aug-26	02-Nov-26	04-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-H-CON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-26	05-Aug-26	02-Nov-26	04-Nov-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		85	05-Aug-26	20-Oct-26	20-Aug-26 A	07-Jan-27	357,334.87	95,303.58	360,557.47	99.11%	26.43%	-54
POWER, LIGHTING & GROUNDING		50	05-Aug-26	08-Sep-26	20-Aug-26 A	28-Nov-26	303,487.27	95,303.58	303,487.27	100%	31.4%	-54
PG-H-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-26	09-Aug-26	20-Aug-26 A	03-Nov-26	119,129.47	95,303.58	119,129.47	100%	80%	-60
PG-H-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-26	19-Aug-26	04-Nov-26	08-Nov-26	8,265.00	0.00	8,265.00	100%	0%	0
PG-H-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-26	22-Aug-26	08-Nov-26	10-Nov-26	4,586.70	0.00	4,586.70	100%	0%	0
PG-H-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-26	27-Aug-26	10-Nov-26	16-Nov-26	17,397.90	0.00	17,397.90	100%	0%	0
PG-H-CON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-26	31-Aug-26	16-Nov-26	19-Nov-26	127,638.72	0.00	127,638.72	100%	0%	0
PG-H-CON-EX-GN-E-70	Wiring Works	3	01-Sep-26	03-Sep-26	19-Nov-26	23-Nov-26	4,224.00	0.00	4,224.00	100%	0%	0
PG-H-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-26	08-Sep-26	23-Nov-26	28-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-26	08-Oct-26	28-Nov-26	27-Dec-26	43,146.00	0.00	43,146.00	100%	0%	0
PG-H-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-26	15-Sep-26	01-Dec-26	05-Dec-26	619.80	0.00	619.80	100%	0%	0
PG-H-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-26	20-Sep-26	05-Dec-26	09-Dec-26	3,718.80	0.00	3,718.80	100%	0%	0
PG-H-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-26	26-Sep-26	09-Dec-26	14-Dec-26	15,249.12	0.00	15,249.12	100%	0%	0
PG-H-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-26	30-Sep-26	14-Dec-26	19-Dec-26	1,446.48	0.00	1,446.48	100%	0%	0
PG-H-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-26	05-Oct-26	19-Dec-26	23-Dec-26	6,612.00	0.00	6,612.00	100%	0%	0
PG-H-CON-EX-GN-E-150	IP Camera Installation	3	06-Oct-26	08-Oct-26	23-Dec-26	27-Dec-26	14,880.00	0.00	14,880.00	100%	0%	0
PG-H-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-26	12-Sep-26	28-Nov-26	01-Dec-26	619.80	0.00	619.80	100%	0%	0
FIRE ALARM SYSTEM		32	13-Sep-26	20-Oct-26	01-Dec-26	07-Jan-27	10,701.60	0.00	13,924.20	76.86%	0%	0
PG-H-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-26	21-Sep-26	01-Dec-26	10-Dec-26	1,983.60	0.00	1,983.60	100%	0%	0
PG-H-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-26	01-Oct-26	10-Dec-26	20-Dec-26	2,644.80	0.00	2,644.80	100%	0%	0
PG-H-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-26	11-Oct-26	20-Dec-26	29-Dec-26	6,073.20	0.00	8,097.60	75%	0%	0
PG-H-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-26	20-Oct-26	29-Dec-26	07-Jan-27	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		32	10-Oct-26	20-Oct-26	20-Aug-26 A	07-Jan-27	0.00	64,822.50	104,146.20	0%	62.24%	-109
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	28-Dec-26	0.00	64,822.50	86,430.00	0%	75%	-106
PG-H-CON-EX-GN-PR-30	Marking & Signages	5	15-Oct-26	20-Oct-26	02-Jan-27	07-Jan-27	0.00	0.00	17,716.20	0%	0%	0
SERVICE CONNECTION		33	31-Oct-26	26-Nov-26	20-Aug-26 A	21-Jan-27	0.00	2,790.00	5,208.00	0%	53.57%	-108
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	09-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-113
PG-H-CON-EX-GN-SC-30	Connection to City Network	8	09-Nov-26	17-Nov-26	09-Jan-27	18-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26	26-Nov-26	27-Aug-26 A	21-Jan-27	0.00	892.80	1,488.00	0%	60%	-118
LANDSCAPING WORKS		48	20-Sep-26	09-Nov-26	09-Jul-26 A	08-Dec-26	145,034.33	324,017.71	506,716.26	28.62%	63.94%	-87
HARDSCAPE WORK		48	20-Sep-26	09-Nov-26	09-Jul-26 A	08-Dec-26	116,042.63	280,337.71	355,477.26	32.64%	78.86%	-87

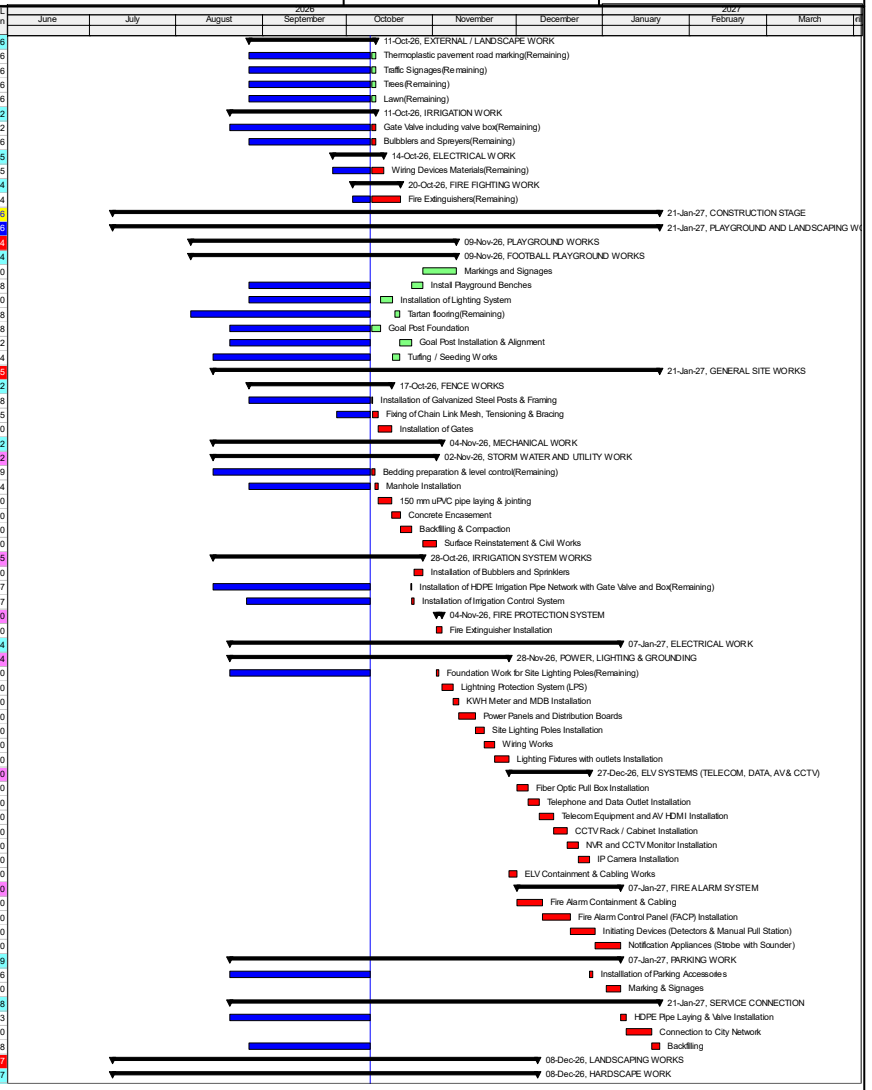


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-2	05-Oct-26	27-Aug-26 A	11-Nov-26	54,054.00	37,837.80	54,054.00	100%	70%	-51
PG-H-CON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-2	07-Oct-26	30-Jul-26 A	11-Nov-26	43,470.00	39,123.00	43,470.00	100%	90%	-73
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	23-Nov-26	18,518.63	140,741.55	148,149.00	12.5%	95%	-108
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	26-Nov-26	0.00	62,635.36	104,392.26	0%	60%	-92
PG-H-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	29-Oct-26	09-Nov-26	28-Nov-26	08-Dec-26	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		18	06-Oct-26	09-Nov-26	27-Aug-26 A	08-Dec-26	28,991.70	43,680.00	151,239.00	19.17%	28.88%	-58
PG-H-CON-EX-LS-SS-10	Planting Trees	10	06-Oct-26	17-Oct-26	11-Nov-26	23-Nov-26	28,991.70	0.00	96,639.00	30%	0%	0
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-2	09-Nov-26	27-Aug-26 A	08-Dec-26	0.00	43,680.00	54,600.00	0%	80%	-82
TANK WORKS		70	02-Jul-26	19-Sep-26	14-Aug-26 A	07-Nov-26	40,490.28	4,025.65	40,490.28	100%	9.94%	-4
SEPTIC TANK		65	02-Jul-26	31-Aug-26	14-Aug-26 A	01-Nov-26	5,777.28	4,025.65	5,777.28	100%	69.68%	-15
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26	09-Jul-26	14-Aug-26 A	11-Oct-26	2,757.60	2,206.08	2,757.60	100%	80%	-41
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26	18-Jul-26	27-Aug-26 A	13-Oct-26	2,599.38	1,819.57	2,599.38	100%	70%	-33
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-2	24-Aug-26	17-Oct-26	25-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-2	31-Aug-26	25-Oct-26	01-Nov-26	168.12	0.00	168.12	100%	0%	0
WATER STORAGE TANK		5	14-Sep-2	19-Sep-26	01-Nov-26	07-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-H-CON-EX-TW-IR-40	GRP Water Tank Installation	5	14-Sep-2	19-Sep-26	01-Nov-26	07-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
TOILET BUILDING WORKS		83	03-Aug-2	06-Oct-26	30-Jul-26 A	16-Nov-26	168,590.22	101,050.82	168,590.22	100%	59.94%	-38
CIVIL WORK		50	09-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	101,688.00	50,781.12	101,688.00	100%	49.94%	-52
ARCHITECTURAL WORK		50	09-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	101,688.00	50,781.12	101,688.00	100%	49.94%	-52
GENERAL FINISHES		32	09-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	72,432.60	35,575.20	72,432.60	100%	49.11%	-52
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-2	12-Sep-26	20-Aug-26 A	17-Oct-26	2,958.00	2,366.40	2,958.00	100%	80%	-45
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-2	20-Sep-26	20-Aug-26 A	18-Oct-26	273.60	218.88	273.60	100%	80%	-42
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-2	27-Sep-26	27-Aug-26 A	19-Oct-26	13,273.80	10,619.04	13,273.80	100%	80%	-39
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-2	05-Oct-26	04-Oct-26 A	15-Nov-26	55,927.20	22,370.88	55,927.20	100%	40%	-30
WET AREA FINISHES		4	01-Oct-26	05-Oct-26	27-Aug-26 A	18-Oct-26	5,361.60	3,753.12	5,361.60	100%	70%	-39
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26	05-Oct-26	27-Aug-26 A	18-Oct-26	5,361.60	3,753.12	5,361.60	100%	70%	-39
ROOF FINISHES		47	19-Sep-2	05-Oct-26	20-Aug-26 A	15-Nov-26	23,893.80	11,452.80	23,893.80	100%	47.93%	-60
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-2	22-Sep-26	20-Aug-26 A	17-Oct-26	4,158.00	3,326.40	4,158.00	100%	80%	-45
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-2	26-Sep-26	27-Aug-26 A	18-Oct-26	10,158.00	8,126.40	10,158.00	100%	80%	-41
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-26	05-Oct-26	12-Nov-26	15-Nov-26	9,577.80	0.00	9,577.80	100%	0%	0
MEP WORK		82	03-Aug-2	06-Oct-26	30-Jul-26 A	16-Nov-26	66,902.22	50,269.70	66,902.22	100%	75.14%	-38
MECANICAL WORKS		82	03-Aug-2	06-Oct-26	30-Jul-26 A	16-Nov-26	50,638.50	36,445.54	50,638.50	100%	71.97%	-38
FIRE FIGHTING SYSTEM		1	06-Oct-26	06-Oct-26	15-Nov-26	16-Nov-26	136.26	0.00	136.26	100%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-26	06-Oct-26	15-Nov-26	16-Nov-26	136.26	0.00	136.26	100%	0%	0
SEWER AND DRAINAGE SYSTEM		53	03-Aug-2	23-Aug-26	30-Jul-26 A	13-Oct-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-46
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-2	04-Aug-26	30-Jul-26 A	10-Oct-26	3,225.72	2,741.86	3,225.72	100%	85%	-58
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-2	23-Aug-26	11-Oct-26	13-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-2	15-Aug-26	26-Sep-26 A	11-Oct-26	7,684.80	4,610.88	7,684.80	100%	60%	-10
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-2	15-Aug-26	26-Sep-26 A	11-Oct-26	7,684.80	4,610.88	7,684.80	100%	60%	-10
WATER SUPPLY SYSTEM		3	18-Aug-2	20-Aug-26	27-Aug-26 A	11-Oct-26	36,366.00	29,092.80	36,366.00	100%	80%	-35
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-2	20-Aug-26	27-Aug-26 A	11-Oct-26	36,366.00	29,092.80	36,366.00	100%	80%	-35
ELECTRICAL WORKS		11	27-Aug-2	08-Sep-26	20-Aug-26 A	15-Oct-26	16,263.72	13,824.16	16,263.72	100%	85%	-36
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-2	29-Aug-26	20-Aug-26 A	14-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-44
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-2	01-Sep-26	20-Aug-26 A	14-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-44
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-2	05-Sep-26	20-Aug-26 A	14-Oct-26	4,959.00	4,215.15	4,959.00	100%	85%	-44
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-2	08-Sep-26	20-Aug-26 A	15-Oct-26	7,337.52	6,236.89	7,337.52	100%	85%	-44
PROJECT CLOSOUT		38	02-Nov-2	16-Dec-26	06-Aug-26 A	10-Jan-27	0.00	55,198.68	661,021.24	0%	8.35%	-96
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-2	14-Nov-26	06-Aug-26 A	08-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-96
PG-H-PCL-20	As-Built Drawings	18	14-Nov-2	05-Dec-26	09-Dec-26	29-Dec-26	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-30	Snag list Submission	8	14-Nov-2	23-Nov-26	09-Dec-26	17-Dec-26	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-40	Snag list Closeout	14	23-Nov-2	09-Dec-26	19-Dec-26	03-Jan-27	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-50	Issuing Approvals	3	09-Dec-2	13-Dec-26	04-Jan-27	06-Jan-27	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-60	Handing Over	3	13-Dec-2	16-Dec-26	07-Jan-27	10-Jan-27	0.00	0.00	68,146.52	0%	0%	0
TABUK		164	25-Jun-26	16-Dec-26	12-Jul-26 A	10-Feb-27	4,172,003.75	2,233,075.02	7,301,102.06	57.14%	30.59%	-33
PROCUREMENT		63	25-Jun-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,157,429.76	1,375,963.21	2,157,429.76	100%	63.78%	-13
LONG LEAD ITEMS		54	01-Jul-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,118,427.42	1,341,415.10	2,118,427.42	100%	63.32%	-19
MANUFACTURE / FABRICATION		26	18-Jul-26	16-Aug-26	27-Aug-26 A	21-Oct-26	0.00	0.00	0.00	0%	0%	-20
SPORTS & RECREATIONAL FACILITIES WORK		26	18-Jul-26	16-Aug-26	27-Aug-26 A	21-Oct-26	0.00	0.00	0.00	0%	0%	-20
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26	16-Aug-26	27-Aug-26 A	21-Oct-26	0.00	0.00	0.00	100%	60%	-20
DELIVERY TO SITE		54	01-Jul-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,118,427.42	1,341,415.10	2,118,427.42	100%	63.32%	-19
EXTERNAL / LANDSCAPE WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-36
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-36
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	26-Oct-26	2,013,812.01	1,248,832.16	2,013,812.01	100%	62.01%	-38
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	58,731.75	52,858.58	58,731.75	100%	90%	-36
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	10,152.00	9,136.80	10,152.00	100%	90%	-36
PG-T-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	26,778.60	24,100.74	26,778.60	100%	90%	-36
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	11-Oct-26	39,487.50	35,538.75	39,487.50	100%	90%	-43
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-2	27-Aug-26	20-Aug-26 A	26-Oct-26	1,878,662.16	1,127,197.30	1,878,662.16	100%	60%	-46
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	14-Oct-26	4,001.54	2,573.09	4,001.54	100%	64.3%	-29
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	11-Oct-26	573.89	516.50	573.89	100%	90%	-25
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	14-Oct-26	3,427.65	2,056.59	3,427.65	100%	60%	-29
PLUMBING WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-36
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	11-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-36

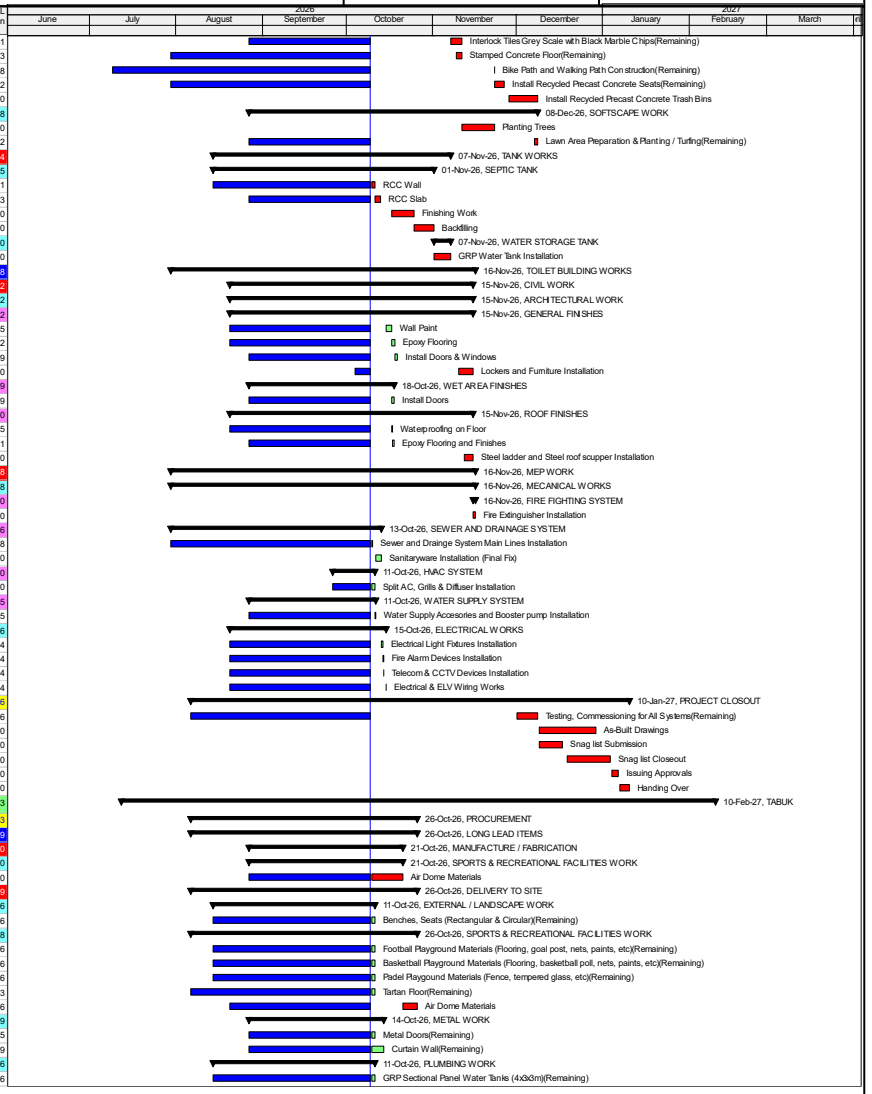


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
IRRIGATION WORK		4	01-Jul-26	05-Jul-26	20-Aug-26 A	10-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-38
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	05-Jul-26	20-Aug-26 A	10-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-38
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	11-Oct-26	64,072.19	57,122.33	64,072.19	100%	89.15%	-22
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	1,785.24	1,606.72	1,785.24	100%	90%	-36
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	1,428.19	1,285.37	1,428.19	100%	90%	-36
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	41,772.67	37,595.40	41,772.67	100%	90%	-36
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	11-Oct-26	4,618.19	4,156.37	4,618.19	100%	90%	-36
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	10-Oct-26	3,615.08	3,253.58	3,615.08	100%	90%	-43
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-2	24-Aug-26	27-Aug-26 A	11-Oct-26	3,525.77	2,996.90	3,525.77	100%	85%	-26
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	11-Oct-26	4,463.64	3,794.09	4,463.64	100%	85%	-26
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	11-Oct-26	2,863.40	2,433.89	2,863.40	100%	85%	-26
SHORT LEAD ITEMS		52	25-Jun-26	22-Jul-26	07-Aug-26 A	14-Oct-26	39,002.34	34,548.11	39,002.34	100%	88.58%	-34
DELIVERY TO SITE		52	25-Jun-26	22-Jul-26	07-Aug-26 A	14-Oct-26	39,002.34	34,548.11	39,002.34	100%	88.58%	-34
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	19,978.06	17,980.25	19,978.06	100%	90%	-27
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	714.10	642.69	714.10	100%	90%	-27
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	8,301.96	7,471.76	8,301.96	100%	90%	-27
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	10-Oct-26	10,962.00	9,865.80	10,962.00	100%	90%	-27
METAL WORK		12	25-Jun-26	08-Jul-26	23-Sep-26 A	14-Oct-26	1,724.00	1,034.40	1,724.00	100%	60%	-6
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	23-Sep-26 A	14-Oct-26	1,302.70	781.62	1,302.70	100%	60%	-6
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	14-Oct-26	112.75	67.65	112.75	100%	60%	-6
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	14-Oct-26	308.56	185.13	308.56	100%	60%	-6
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	10-Oct-26	14,977.04	13,479.33	14,977.04	100%	90%	-45
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	10-Oct-26	1,859.76	1,673.78	1,859.76	100%	90%	-45
PG-T-PR-SL-IR-DL-20_R	Bulbblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	10-Oct-26	13,117.28	11,805.55	13,117.28	100%	90%	-34
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	19-Sep-26 A	11-Oct-26	2,200.61	1,980.55	2,200.61	100%	90%	-6
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	19-Sep-26 A	11-Oct-26	2,200.61	1,980.55	2,200.61	100%	90%	-6
FIRE FIGHTING WORK		9	30-Jun-26	09-Jul-26	27-Sep-26 A	13-Oct-26	122.63	73.58	122.63	100%	60%	-6
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26	09-Jul-26	27-Sep-26 A	13-Oct-26	122.63	73.58	122.63	100%	60%	-6
CONSTRUCTION STAGE		153	25-Jun-26	14-Dec-26	12-Jul-26 A	28-Jan-27	2,014,573.99	681,065.89	4,041,965.60	49.84%	16.85%	-24
PLAYGROUND AND LANDSCAPING WORKS		147	25-Jun-26	14-Dec-26	12-Jul-26 A	21-Jan-27	612,206.71	645,408.09	1,012,265.62	60.48%	63.76%	-18
PLAYGROUND WORKS		82	08-Aug-2	07-Dec-26	14-Aug-26 A	29-Nov-26	96,087.48	129,656.60	221,537.34	43.37%	58.53%	13
FOOTBALL PLAYGROUND WORKS		59	19-Aug-2	17-Nov-26	14-Aug-26 A	31-Oct-26	55,127.10	72,054.83	109,254.66	50.46%	65.95%	11
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-2	17-Nov-26	19-Oct-26	31-Oct-26	0.00	0.00	23,667.00	0%	0%	0
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	19-Oct-26	0.00	1,648.13	2,060.16	0%	80%	-33
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-2	02-Sep-26	20-Aug-26 A	11-Oct-26	24,360.00	20,706.00	24,360.00	100%	85%	-31
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	17-Oct-26	7,100.10	28,400.40	35,500.50	20%	80%	-33
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-2	16-Sep-26	14-Aug-26 A	13-Oct-26	23,667.00	21,300.30	23,667.00	100%	90%	-38
BASKETBALL PLAYGROUND WORKS		57	31-Aug-2	17-Nov-26	20-Aug-26 A	09-Nov-26	27,704.28	24,819.01	43,200.72	64.13%	57.45%	-2
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	09-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-47
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-2	10-Oct-26	20-Aug-26 A	18-Oct-26	14,612.52	12,377.66	15,472.08	94.44%	80%	-31
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-2	17-Sep-26	20-Aug-26 A	13-Oct-26	13,091.76	11,128.00	13,091.76	100%	85%	-30
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	18-Oct-26	07-Nov-26	0.00	0.00	13,091.76	0%	0%	0
PADEL PLAYGROUND WORKS		68	08-Aug-2	07-Dec-26	20-Aug-26 A	29-Nov-26	13,256.10	32,782.76	69,081.96	19.19%	47.45%	18
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	08-Nov-26	0.00	23,692.50	26,325.00	0%	90%	-51
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-2	30-Aug-26	20-Aug-26 A	14-Oct-26	3,534.96	3,004.72	3,534.96	100%	85%	-26
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-2	12-Oct-26	17-Oct-26	05-Nov-26	4,418.70	0.00	5,302.44	83.33%	0%	0
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-2	20-Sep-26	20-Aug-26 A	15-Oct-26	5,302.44	4,772.20	5,302.44	100%	90%	-30
PG-T-CON-EXPD-70	Court Accessories Installation	16	02-Nov-2	19-Nov-26	08-Nov-26	26-Nov-26	0.00	0.00	27,072.00	0%	0%	0
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-2	07-Dec-26	27-Aug-26 A	29-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-65
GENERAL SITE WORKS		147	25-Jun-26	14-Dec-26	12-Jul-26 A	21-Jan-27	414,813.07	311,846.94	497,741.02	83.34%	62.61%	-18
FENCE WORKS		48	27-Jul-26	17-Aug-26	20-Aug-26 A	18-Oct-26	19,745.64	11,189.20	19,745.64	100%	56.67%	-31
PG-T-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26	03-Aug-26	20-Aug-26 A	10-Oct-26	6,581.88	5,923.69	6,581.88	100%	90%	-36
PG-T-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-2	10-Aug-26	20-Sep-26 A	11-Oct-26	6,581.88	5,265.50	6,581.88	100%	80%	-12
PG-T-CON-EXGN-FN-50	Installation of Gates	6	11-Aug-2	17-Aug-26	11-Oct-26	18-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		77	01-Jul-26	10-Aug-26	12-Jul-26 A	01-Nov-26	206,336.28	168,645.01	206,336.28	100%	81.73%	-60
STORM WATER AND UTILITY WORK		55	01-Jul-26	04-Aug-26	20-Aug-26 A	26-Oct-26	22,092.00	10,572.00	22,092.00	100%	47.85%	-26
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	10-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-38
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	12-Oct-26	10,740.00	6,444.00	10,740.00	100%	60%	-14
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	12-Oct-26	15-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	15-Oct-26	19-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-2	04-Aug-26	21-Oct-26	26-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	21-Oct-26	183,926.34	158,073.01	183,926.34	100%	85.94%	-71
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	21-Oct-26	58,299.00	49,554.15	58,299.00	100%	85%	-47
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	19-Oct-26	34,712.34	31,241.11	34,712.34	100%	90%	-81
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	20-Oct-26	90,915.00	77,277.75	90,915.00	100%	85%	-46
FIRE PROTECTION SYSTEM		5	05-Aug-2	10-Aug-26	26-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-2	10-Aug-26	26-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		111	25-Jun-26	07-Nov-26	20-Aug-26 A	31-Dec-26	188,731.15	118,981.14	239,107.30	78.93%	49.76%	2
POWER, LIGHTING & GROUNDING		79	25-Jun-26	27-Sep-26	20-Aug-26 A	22-Nov-26	182,037.10	106,037.34	182,037.10	100%	58.25%	1
PG-T-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	14-Oct-26	55,696.90	44,557.52	55,696.90	100%	80%	-25
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-2	19-Aug-26	20-Aug-26 A	02-Nov-26	8,265.00	7,025.25	8,265.00	100%	85%	-54
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-2	30-Aug-26	17-Sep-26 A	04-Nov-26	4,586.70	2,293.35	4,586.70	100%	50%	-36
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-2	07-Sep-26	17-Sep-26 A	09-Nov-26	17,397.90	8,698.95	17,397.90	100%	50%	-37

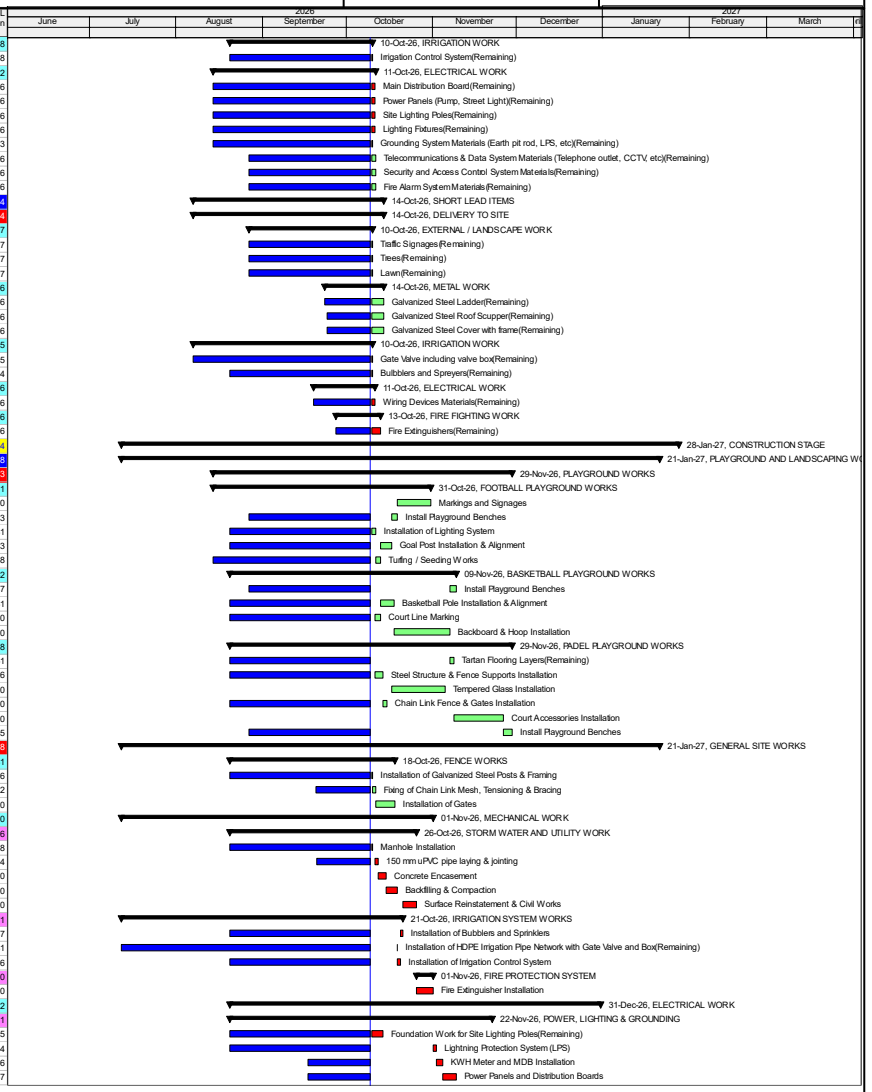

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	11-Nov-26	69,621.12	41,772.67	69,621.12	100%	60%	-41
PG-T-CON-EXGN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	04-Oct-26 A	15-Nov-26	4,224.00	1,689.60	4,224.00	100%	40%	-32
PG-T-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	6	20-Sep-26	27-Sep-26	15-Nov-26	22-Nov-26	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	12-Dec-26	4,958.40	12,943.80	43,146.00	11.49%	30%	-44
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	26-Nov-26	619.80	185.94	619.80	100%	30%	-52
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	30-Nov-26	3,718.80	1,115.64	3,718.80	100%	30%	-54
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	03-Dec-26	0.00	4,574.74	15,249.12	0%	30%	-57
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	06-Dec-26	0.00	433.94	1,446.48	0%	30%	-60
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	09-Dec-26	0.00	1,983.60	6,612.00	0%	30%	-63
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	12-Dec-26	0.00	4,464.00	14,880.00	0%	30%	-66
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	24-Nov-26	619.80	185.94	619.80	100%	30%	-50
FIRE ALARM SYSTEM		32	01-Oct-26	07-Nov-26	24-Nov-26	31-Dec-26	1,735.65	0.00	13,924.20	12.46%	0%	0
PG-T-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	01-Oct-26	10-Oct-26	24-Nov-26	03-Dec-26	1,735.65	0.00	1,983.60	87.5%	0%	0
PG-T-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26	19-Oct-26	03-Dec-26	13-Dec-26	0.00	0.00	2,644.80	0%	0%	0
PG-T-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26	28-Oct-26	13-Dec-26	22-Dec-26	0.00	0.00	8,097.60	0%	0%	0
PG-T-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26	07-Nov-26	22-Dec-26	31-Dec-26	0.00	0.00	1,198.20	0%	0%	0
PARKING WORK		15	27-Oct-26	11-Nov-26	20-Aug-26 A	31-Dec-26	0.00	10,934.40	27,343.80	0%	39.99%	-99
PG-T-CON-EXGN-PR-10	Installation of Parking Accessories	7	27-Oct-26	03-Nov-26	20-Aug-26 A	13-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-91
PG-T-CON-EXGN-PR-30	Marking & Signages	7	04-Nov-26	11-Nov-26	23-Dec-26	31-Dec-26	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		25	12-Nov-26	14-Dec-26	14-Aug-26 A	21-Jan-27	0.00	1,897.20	5,208.00	0%	36.43%	-108
PG-T-CON-EXGN-S-C-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	31-Dec-26	0.00	1,897.20	2,232.00	0%	85%	-108
PG-T-CON-EXGN-S-C-30	Connection to City Network	10	24-Nov-26	05-Dec-26	31-Dec-26	12-Jan-27	0.00	0.00	1,488.00	0%	0%	0
PG-T-CON-EXGN-S-C-40	Backfilling	8	06-Dec-26	14-Dec-26	12-Jan-27	21-Jan-27	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		38	28-Sep-26	22-Nov-26	12-Jul-26 A	28-Nov-26	60,984.00	202,449.99	252,665.10	24.14%	80.13%	-70
HARDSCAPE WORK		38	28-Sep-26	22-Nov-26	30-Jul-26 A	28-Nov-26	60,984.00	148,329.99	170,003.10	35.87%	87.25%	-54
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	15-Nov-26	60,984.00	51,836.40	60,984.00	100%	85%	-57
PG-T-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26	20-Oct-26	30-Jul-26 A	15-Nov-26	0.00	39,123.00	43,470.00	0%	90%	-81
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	23-Nov-26	0.00	54,123.39	60,137.10	0%	90%	-88
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	28-Nov-26	0.00	3,247.20	5,412.00	0%	60%	-45
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	28-Nov-26	0.00	54,120.00	82,662.00	0%	65.47%	-80
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	22-Nov-26	0.00	23,061.00	46,122.00	0%	50%	-39
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-26	22-Nov-26	12-Jul-26 A	28-Nov-26	0.00	31,059.00	36,540.00	0%	85%	-112
TANK WORKS		75	07-Jul-26	27-Sep-26	14-Aug-26 A	12-Nov-26	40,322.16	1,654.56	40,322.16	100%	4.1%	-7
SEPTIC TANK		70	07-Jul-26	26-Aug-26	14-Aug-26 A	07-Nov-26	5,609.16	1,654.56	5,609.16	100%	29.5%	-28
PG-T-CON-EXTW-ST-40	RCC Wall	9	07-Jul-26	16-Jul-26	14-Aug-26 A	13-Oct-26	2,757.60	1,654.56	2,757.60	100%	60%	-42
PG-T-CON-EXTW-ST-50	RCC Slab	13	18-Jul-26	01-Aug-26	13-Oct-26	28-Oct-26	2,599.38	0.00	2,599.38	100%	0%	0
PG-T-CON-EXTW-ST-60	Finishing Work	8	18-Aug-26	26-Aug-26	28-Oct-26	07-Nov-26	252.18	0.00	252.18	100%	0%	0
WATER STORAGE TANK		5	21-Sep-26	27-Sep-26	07-Nov-26	12-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-T-CON-EXTW-WR-40	GRP Water Tank Installation	5	21-Sep-26	27-Sep-26	07-Nov-26	12-Nov-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		85	26-Aug-26	03-Dec-26	21-Oct-26	28-Jan-27	1,362,775.57	0.00	2,967,347.81	45.93%	0%	0
CIVIL WORK		17	26-Aug-26	14-Sep-26	21-Oct-26	10-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-26	05-Sep-26	21-Oct-26	01-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-80	Installation of Membrane System	8	06-Sep-26	14-Sep-26	01-Nov-26	10-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		25	05-Nov-26	03-Dec-26	30-Dec-26	28-Jan-27	0.00	0.00	712,953.22	0%	0%	0
PG-T-CON-EXAD-AR-10	Installation of Thermal Insulation System	7	05-Nov-26	12-Nov-26	30-Dec-26	07-Jan-27	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-20	Installation of Doors & Access Systems	6	22-Nov-26	28-Nov-26	16-Jan-27	23-Jan-27	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-30	Installation of Logo	5	29-Nov-26	03-Dec-26	23-Jan-27	28-Jan-27	0.00	0.00	3,236.40	0%	0%	0
PG-T-CON-EXAD-AR-40	Final Fixing of Accessories & Finishes	7	14-Nov-26	21-Nov-26	07-Jan-27	16-Jan-27	0.00	0.00	208,740.24	0%	0%	0
MECHANICAL WORK		23	15-Sep-26	12-Oct-26	10-Nov-26	07-Dec-26	563,598.65	0.00	667,368.77	84.38%	0%	0
PG-T-CON-EXAD-ME-10	Installation of Main Air Package Units	5	15-Sep-26	20-Sep-26	10-Nov-26	16-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-ME-20	Installation of Backup Air Package Unit	5	21-Sep-26	27-Sep-26	16-Nov-26	22-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CON-EXAD-ME-30	Installation of Complete HVAC System	6	06-Oct-26	12-Oct-26	30-Nov-26	07-Dec-26	104,370.12	0.00	208,740.24	50%	0%	0
ELECTRICAL WORK		33	28-Sep-26	04-Nov-26	22-Nov-26	30-Dec-26	298,200.34	0.00	1,085,449.25	27.47%	0%	0
PG-T-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	7	28-Sep-26	05-Oct-26	22-Nov-26	30-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CON-EXAD-EL-20	Installation of Lighting System	7	06-Oct-26	13-Oct-26	30-Nov-26	08-Dec-26	89,460.10	0.00	208,740.24	42.86%	0%	0
PG-T-CON-EXAD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	14-Oct-26	19-Oct-26	08-Dec-26	14-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-40	Installation of Backup Generator	6	20-Oct-26	26-Oct-26	14-Dec-26	21-Dec-26	0.00	0.00	208,740.24	0%	0%	0
PG-T-CON-EXAD-EL-50	Installation of Smart Dome System	8	27-Oct-26	04-Nov-26	21-Dec-26	30-Dec-26	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		16	31-Aug-26	28-Oct-26	19-Sep-26 A	18-Oct-26	39,591.72	35,657.80	62,352.18	63.5%	57.19%	26
CIVIL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	8,005.86	14,939.40	0%	53.59%	-9
ARCHITECTURAL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	8,005.86	14,939.40	0%	53.59%	-9
WET AREA FINISHES		2	11-Oct-26	12-Oct-26	23-Sep-26 A	13-Oct-26	0.00	3,216.96	5,361.60	0%	60%	-15
PG-T-CON-B-AR-WF-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	13-Oct-26	0.00	3,216.96	5,361.60	0%	60%	-15
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	4,788.90	9,577.80	0%	50%	-20
PG-T-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	17-Oct-26	0.00	4,788.90	9,577.80	0%	50%	-20
MEP WORK		16	31-Aug-26	28-Oct-26	20-Sep-26 A	18-Oct-26	39,591.72	27,651.94	47,412.78	83.5%	58.32%	27
MECANICAL WORKS		16	31-Aug-26	28-Oct-26	20-Sep-26 A	18-Oct-26	39,591.72	27,651.94	47,412.78	83.5%	58.32%	27
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	18-Oct-26	0.00	54.50	136.26	0%	40%	-19
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	18-Oct-26	0.00	54.50	136.26	0%	40%	-19
SEWER AND DRAINAGE SYSTEM		2	03-Sep-26	05-Sep-26	23-Sep-26 A	13-Oct-26	3,225.72	1,935.43	3,225.72	100%	60%	-14
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-26	05-Sep-26	23-Sep-26 A	13-Oct-26	3,225.72	1,935.43	3,225.72	100%	60%	-14
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	14-Oct-26	0.00	3,842.40	7,684.80	0%	50%	-18
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	14-Oct-26	0.00	3,842.40	7,684.80	0%	50%	-18




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
WATER SUPPLY SYSTEM		3	31-Aug-26	02-Sep-26	23-Sep-26 A	12-Oct-26	36,366.00	21,819.60	36,366.00	100%	60%	-12
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-26	02-Sep-26	23-Sep-26 A	12-Oct-26	36,366.00	21,819.60	36,366.00	100%	60%	-12
PROJECT CLOSOUT		160	22-Nov-26	16-Dec-26	06-Aug-26 A	10-Feb-27	0.00	176,045.92	1,101,706.70	0%	15.98%	-139
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-26	03-Dec-26	06-Aug-26 A	28-Jan-27	0.00	153,330.31	306,660.63	0%	50%	-139
PG-T-PCL-20	As-Built Drawings	15	22-Nov-26	09-Dec-26	23-Sep-26 A	04-Feb-27	0.00	22,715.60	113,578.01	0%	20%	-100
PG-T-PCL-30	Snag list Submission	2	05-Dec-26	06-Dec-26	28-Jan-27	31-Jan-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-40	Snag list Closeout	7	07-Dec-26	14-Dec-26	31-Jan-27	08-Feb-27	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-50	Issuing Approvals	1	15-Dec-26	15-Dec-26	08-Feb-27	09-Feb-27	0.00	0.00	113,578.01	0%	0%	0
PG-T-PCL-60	Handing Over	1	16-Dec-26	16-Dec-26	09-Feb-27	10-Feb-27	0.00	0.00	113,578.01	0%	0%	0



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
