
| Activity ID | Activity Name | BL Project Duration | BL Project Start | BL Project Finish | Actual % | Planned % |
|---|---|---|---|---|---|---|
| Dammam 3rd Industrial City Gates and Fence - B1 | | 75 | 06-May-26 | 05-Aug-26 | 91.81% | 100% |
| Key Milestones | | 75 | 06-May-26 | 05-Aug-26 | 0% | 0% |
| Mobilization | | 18 | 06-May-26 | 31-May-26 | 0% | 0% |
| Preliminary Submittals | | 17 | 06-May-26 | 25-May-26 | 0% | 0% |
| Engineering | | 49 | 18-May-26 | 18-Jul-26 | 100% | 100% |
| Procurement | | 55 | 02-Jun-26 | 04-Aug-26 | 100% | 100% |
| Construction | | 62 | 21-May-26 | 05-Aug-26 | 99.57% | 100% |
| | SITE WORKS | 61 | 21-May-26 | 05-Aug-26 | 100% | 100% |
| | MASONRY UNIT | 3 | 02-Jul-26 | 06-Jul-26 | 100% | 100% |
| | THERMAL & MOISTURE PROTECTION | 14 | 14-Jul-26 | 30-Jul-26 | 100% | 100% |
| | ROOFING SYSTEM | 11 | 18-Jul-26 | 30-Jul-26 | 100% | 100% |
| | FINISHES | 27 | 06-Jul-26 | 05-Aug-26 | 100% | 100% |
| | SPECIAL CONSTRUCTION- STRUCTURAL STEEL (Fence Type 2) | 30 | 02-Jul-26 | 05-Aug-26 | 99.17% | 100% |
| | MECHANICAL WORKS | 52 | 07-Jun-26 | 05-Aug-26 | 100% | 100% |
| | ELECTRICAL WORKS | 52 | 07-Jun-26 | 05-Aug-26 | 99.55% | 100% |
| | METALS | 2 | 04-Aug-26 | 05-Aug-26 | 100% | 100% |
| | WOODS AND PLASTICS | 3 | 03-Aug-26 | 05-Aug-26 | 100% | 100% |
| | DOORS & WINDOWS | 7 | 29-Jul-26 | 05-Aug-26 | 100% | 100% |
| | SPECIALTIES | 2 | 04-Aug-26 | 05-Aug-26 | 100% | 100% |
| | FURNISHINGS | 1 | 05-Aug-26 | 05-Aug-26 | 100% | 100% |
| Testing & Commissioning | | 4 | 02-Aug-26 | 05-Aug-26 | 85% | 100% |
| Handing Over | | 6 | 30-Jul-26 | 05-Aug-26 | 12.2% | 100% |




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

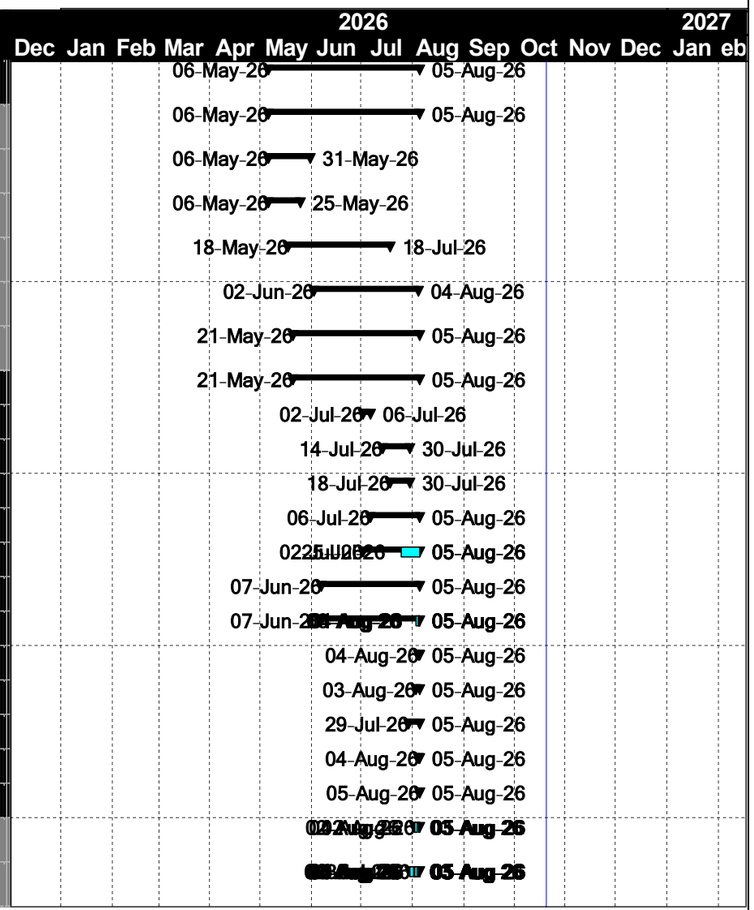

TASK filter: All Activities

© Oracle Corporation
